

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010

APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU0337
1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other <input type="checkbox"/> Single Zone <input checked="" type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator EOG RESOURCES, INC.		7. If Unit or CA Agreement, Name and No. CHAPITA WELLS UNI
Contact: MARY A. MAESTAS E-Mail: mary_maestas@eogresources.com		8. Lease Name and Well No. CHAPITA WELLS UNIT 728-29
3a. Address 1060 EAST HIGHWAY 40 VERNAL, UT 84078	3b. Phone No. (include area code) Ph: 303-824-5526	9. API Well No. 43047-39724
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NENE 608FNL 513FEL 40.01259 N Lat, 109.34314 W Lon At proposed prod. zone 641469X 4430267 Y 40.012658 -109.342447		10. Field and Pool, or Exploratory NATURAL BUTTES/WASATCH
14. Distance in miles and direction from nearest town or post office* 52.3 MILES SOUTH OF VERNAL, UTAH		11. Sec., T., R., M., or Blk. and Survey or Area Sec 29 T9S R23E Mer SLB NENE
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 513' LEASE LINE	16. No. of Acres in Lease 2344.00	12. County or Parish UINTAH
18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 70'	19. Proposed Depth 6890 MD	13. State UT
21. Elevations (Show whether DF, KB, RT, GL, etc.) 5189 GL	22. Approximate date work will start	17. Spacing Unit dedicated to this well
		20. BLM/BIA Bond No. on file NM2308
		23. Estimated duration 45 DAYS

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- | | |
|---|--|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature (Electronic Submission) 	Name (Printed/Typed) MARY A. MAESTAS Ph: 303-824-5526	Date 10/18/2007
Title REGULATORY ASSISTANT		
Approved by (Signature) 	Name (Printed/Typed) BRADLEY G. HILL	Date 10-23-07
Title ENVIRONMENTAL MANAGER		

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Electronic Submission #56806 verified by the BLM Well Information System
For EOG RESOURCES, INC., sent to the Vernal

RECEIVED


OCT 22 2007

DIV. OF OIL, GAS & MINING

Federal Approval of this
Action is Necessary

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **

T9S, R23E, S.L.B.&M.

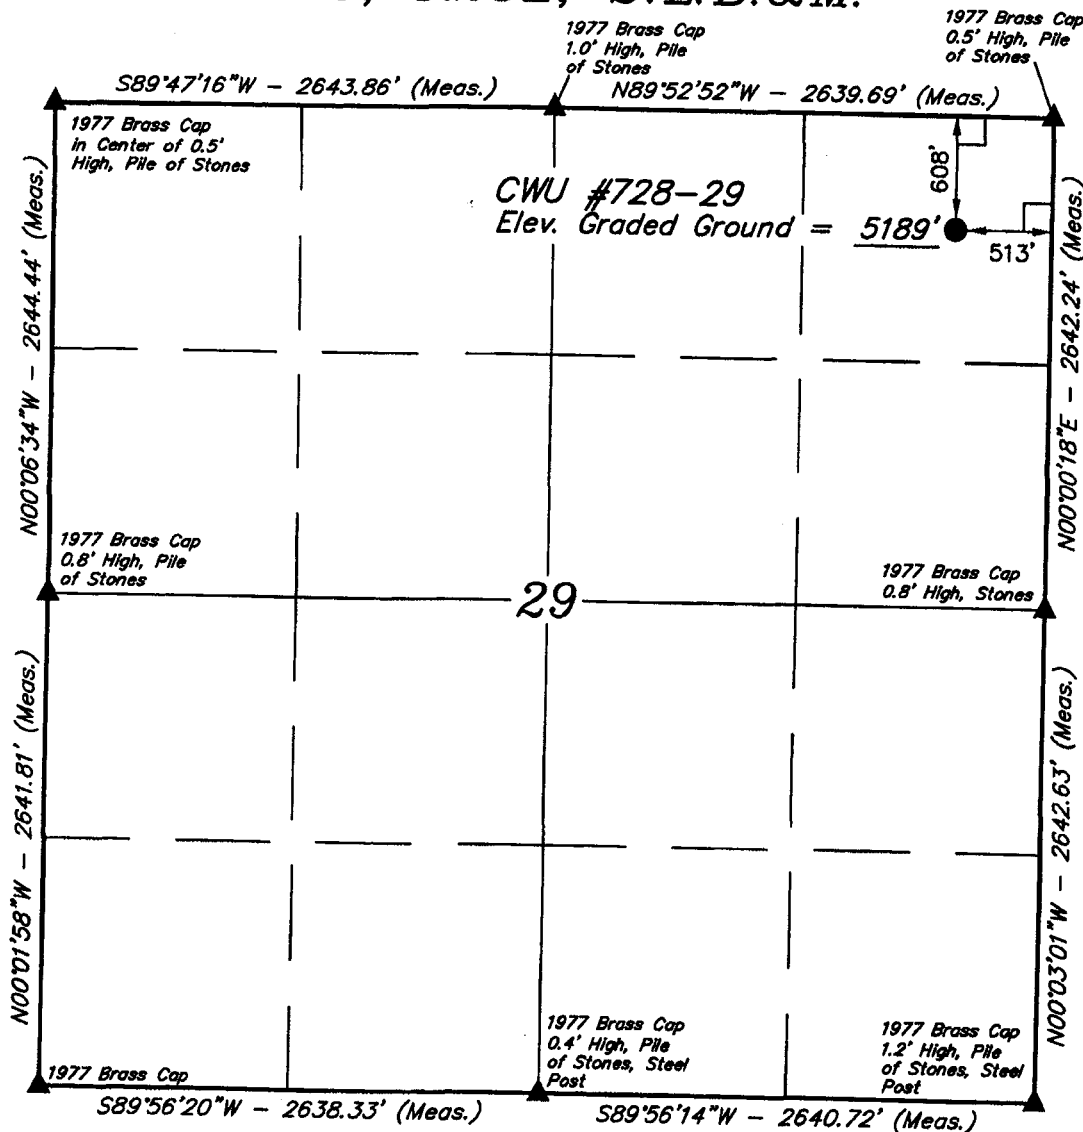

LEGEND:

— = 90° SYMBOL

● = PROPOSED WELL HEAD.

▲ = SECTION CORNERS LOCATED.

(NAD 83)
 LATITUDE = 40°00'45.33" (40.012592)
 LONGITUDE = 109°20'35.32" (109.343144)
 (NAD 27)
 LATITUDE = 40°00'45.45" (40.012625)
 LONGITUDE = 109°20'32.88" (109.342467)

EOG RESOURCES, INC.


Well location, CWU #728-29, located as shown in the NE 1/4 NE 1/4 of Section 29, T9S, R23E, S.L.B.&M., Uintah County, Utah.

BASIS OF ELEVATION


BENCHMARK 58 EAM (1965) LOCATED IN THE NE 1/4 OF SECTION 30, T9S, R23E, S.L.B.&M. TAKEN FROM THE RED WASH SE, QUADRANGLE, UTAH, UTAH COUNTY 7.5 MINUTE QUAD. (TOPOGRAPHIC MAP) PUBLISHED BY THE UNITED STATES DEPARTMENT OF THE INTERIOR, GEOLOGICAL SURVEY. SAID ELEVATION IS MARKED AS BEING 5132 FEET.

BASIS OF BEARINGS

BASIS OF BEARINGS IS A G.P.S. OBSERVATION.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.



UINTAH ENGINEERING & LAND SURVEYING
 85 SOUTH 200 EAST - VERNAL, UTAH 84078
 (435) 789-1017

SCALE 1" = 1000'	DATE SURVEYED: 09-06-07	DATE DRAWN: 09-27-07
PARTY C.R. C.P. L.K.	REFERENCES G.L.O. PLAT	
WEATHER WARM	FILE EOG RESOURCES, INC.	

EIGHT POINT PLAN

CHAPITA WELLS UNIT 728-29 NE/NE, SEC. 29, T9S, R23E, S.L.B.&M.. UINTAH COUNTY, UTAH

1. & 2. ESTIMATED TOPS & ANTICIPATED OIL, GAS, & WATER ZONES:

FORMATION	TVD-RKB (ft)	Objective	Lithology	
Green River	1,612		Shale	
Wasatch	4,560	Primary	Sandstone	Gas
Chapita Wells	5,122	Primary	Sandstone	Gas
Buck Canyon	5,788	Primary	Sandstone	Gas
North Horn	6,389	Primary	Sandstone	Gas
KMV Price River	6,685		Sandstone	
TD	6,890			

Estimated TD: 6,890' or 200'± below Sego top

Anticipated BHP: 3,762 Psig

1. Fresh Waters may exist in the upper, approximately 1,000 ft ± of the Green River Formation, with top at about 2,000 ft ±.
2. Cement isolation is installed to surface of the well isolating all zones by cement.

3. PRESSURE CONTROL EQUIPMENT:

Production Hole – 5000 Psig
BOP schematic diagrams attached.

4. CASING PROGRAM:

CASING	Hole Size	Length	Size	WEIGHT	Grade	Thread	Rating Collapse	Factor Burst	Tensile
Conductor	17 1/2"	0 – 45'	13 3/8"	48.0#	H-40	STC	770 PSI	1730 PSI	322,000#
Surface	12 1/4"	0 – 2,300' KB±	9-5/8"	36.0#	J-55	STC	2020 PSI	3520 Psi	394,000#
Production	7-7/8"	Surface – TD	4-1/2"	11.6#	N-80	LTC	6350 PSI	7780 Psi	233,000#

Note: 12-1/4" surface hole will be drilled to a total depth of 200'± below the base of the Green River lost circulation zone and cased w/9-5/8" as shown to that depth. Drilled depth may be shallower or deeper than the 2300' shown above depending on the actual depth of the loss zone.

All casing will be new or inspected.

EIGHT POINT PLAN
CHAPITA WELLS UNIT 728-29
NE/NE, SEC. 29, T9S, R23E, S.L.B.&M..
UINTAH COUNTY, UTAH

5. Float Equipment:

Surface Hole Procedure (0' - 2300'±)

Guide Shoe

Insert Float Collar (PDC drillable)

Centralizers: 1-5' above shoe, top of jts. #2 and #3 then every 5th joint to surface. (15 total)

Production Hole Procedure (2300'± - TD):

Float shoe, 1 joint casing, float collar and balance of casing to surface. 4-½", 11.6#, N-80 or equivalent marker collars or short casing joints to be placed at top of Price River and 400' above top of Wasatch. Centralizers to be placed 5' above shoe on joint #1, top of joint #2, and every 2nd joint to 400' above Wasatch Island top. Thread lock float shoe, top and bottom of float collar, and top of 2nd joint.

6. MUD PROGRAM

Surface Hole Procedure (Surface - 2300'±):

Air/air mist or aerated water.

Production Hole Procedure (2300'± - TD): Anticipated mud weight 9.5 – 10.5 ppg depending on actual wellbore conditions encountered while drilling.

2300'± - TD A closed mud system will be utilized. A bentonite gelled water mud system will be used to control viscosity w/PHPA polymer used for supplemental viscosity and clay encapsulation/inhibition. Water loss will be maintained at <15cc's using white starch or PAC. Bactericides will be used as needed. Anticipated pH will range from 9.0-10.0. Mud weight will be adjusted as necessary for well control. Deflocculants/thinners will be used as necessary to maintain mud quality. LCM sweeps will be utilized as necessary to control lost circulation and mud loss. CO2 contamination, if encountered, will be treated with lime and gypsum.

7. VARIANCE REQUESTS:

Reference: Onshore Oil and Gas Order No. 2 – Item E: Special Drilling Operations

EOG Resources, Inc. requests a variance to regulations requiring the blooie line to be 100' in length. Due to reduce location excavation, the blooie line will be approximately 75' in length

EIGHT POINT PLAN
CHAPITA WELLS UNIT 728-29
NE/NE, SEC. 29, T9S, R23E, S.L.B.&M..
UINTAH COUNTY, UTAH

8. EVALUATION PROGRAM:

Logs: Mud log from base of surface casing to TD.
Cased-hole Logs: Cased-hole logs will be run in lieu of open-hole logs consisting of the following:
Cement Bond / Casing Collar Locator and Pulsed Neutron

9. CEMENT PROGRAM:

Surface Hole Procedure (Surface - 2300'±):

Lead: 185 sks Class "G" cement with 16% Gel, 10 #/sx Gilsonite, 3% Salt, 2% CaCl₂, 3 lb/sx GR3 ¼ #/sx Flocele mixed at 11 ppg, 3.82 ft³/sk. yield, 23 gps water.

Tail: 207 sks Class "G" cement with 2% CaCl₂, ¼#/sk Flocele mixed at 15.6 ppg, 1.18 ft³/sk., 5.2 gps water.

Top Out: As necessary with Class "G" cement with 2% CaCl₂, ¼#/sk Flocele mixed at 15.6 ppg, 1.18 ft³/sk., 5.2 gps water.

Note: Cement volumes will be calculated to bring lead cement to surface and tail cement to 500' above the casing shoe.

Production Hole Procedure (2300'± - TD)

Lead: 130 sks: Hi-Lift "G" w/12% D20 (Bentonite), 1% D79 (Extender), 5% D44 (Salt), 0.2% D46 (Antifoam), 0.25% D112 (Fluid Loss Additive), 0.25 pps D29 (cello flakes) mixed at 11.0 ppg, 3.91 ft³/sk., 24.5 gps water.

Tail: 492 sks: 50:50 Poz "G" w/ 2% D20 (Bentonite), 0.1% D46 (Antifoam), 0.075% D13 (Retarder), 0.2% D167 (Fluid Loss Additive), 0.2% D65 (Dispersant), mixed at 14.1 ppg, 1.28 ft³/sk., 5.9gps water.

Note: The above number of sacks is based on gauge-hole calculation.
Lead volume to be calculated to bring cement to 200'± above 9-5/8" casing shoe.
Tail volume to be calculated to bring cement to 400'± above top of Wasatch.

Final Cement volumes will be based upon gauge-hole plus 45% excess.

EIGHT POINT PLAN
CHAPITA WELLS UNIT 728-29
NE/NE, SEC. 29, T9S, R23E, S.L.B.&M..
UINTAH COUNTY, UTAH

10. ABNORMAL CONDITIONS:

Surface Hole (Surface - 2300'±):

Lost circulation

Production Hole (2300'± - TD):

Sloughing shales, lost circulation and key seat development are possible in the Wasatch Formation.

11. STANDARD REQUIRED EQUIPMENT:

- A. Choke Manifold
- B. Upper and Lower Kelly Cock
- C. Stabbing Valve
- D. Visual Mud Monitoring


12. HAZARDOUS CHEMICALS:

No chemicals subject to reporting under SARA title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling of this well.

(Attachment: BOP Schematic Diagram)


**EOG RESOURCES 11" 5,000 PSI W.P. BOP
CONFIGURATION**

PAGE 1 OF 2

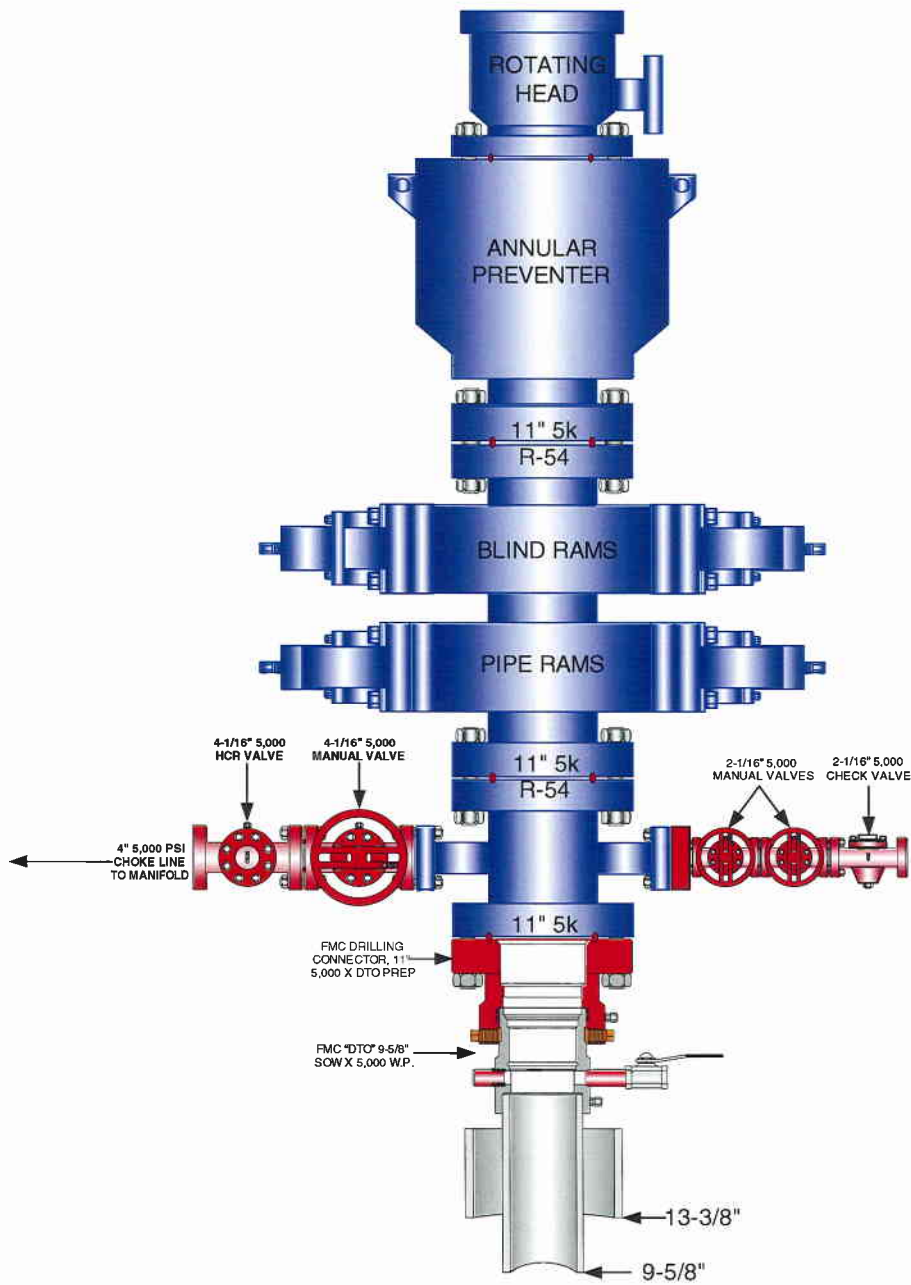

EOG RESOURCES CHOKE MANIFOLD CONFIGURATION W/ 5,000 PSI WP VALVES

PAGE 2 OF 2

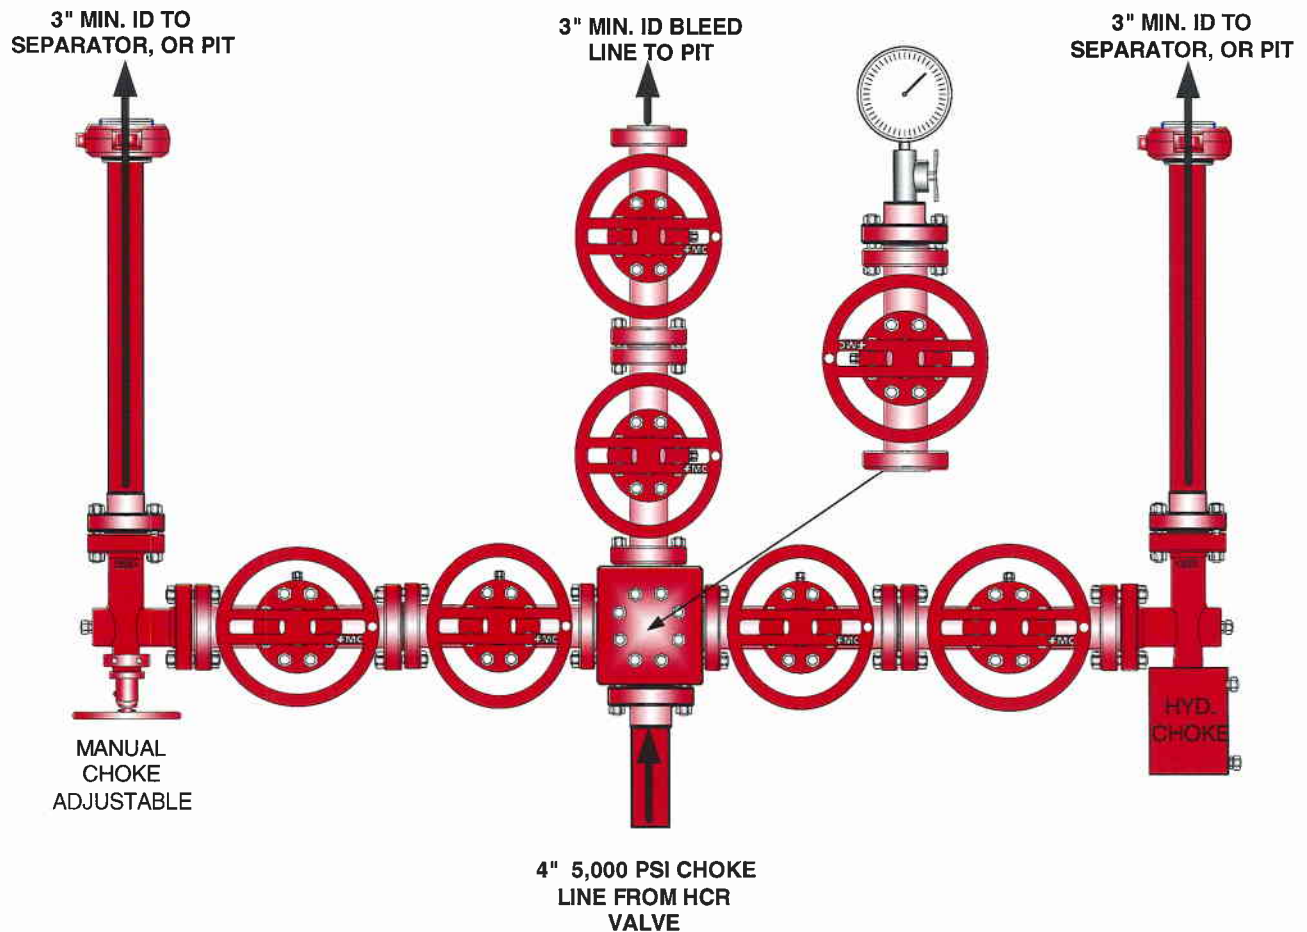

Testing Procedure:

1. BOP will be tested with a professional tester to conform to Onshore Order #2.
2. Blind and Pipe rams will be tested to rated working pressure, 5,000 psi.
3. Annular Preventer will be tested to 50% working pressure, 2,500 psi.
Casing will be tested to 0.22 psi / ft. or 1,500 psi. Not to exceed 70% of burst strength, **whichever is greater.**
4. All lines subject to well pressure will be tested to the same pressure as blind and pipe rams.
5. All BOPE specifications and configurations will meet Onshore Order #2 requirements.



***Chapita Wells Unit 728-29
NENE, Section 29, T9S, R23E
Uintah County, Utah***

SURFACE USE PLAN

The well pad is approximately 345 feet long with a 261-foot width, containing 2.07 acres more or less. New surface disturbance associated with the well pad is estimated to be 2.07 acres.

1. EXISTING ROADS:

- A. See attached Plats showing directional reference stakes on location, and attached TOPO Map "B" showing access to location from existing roads.
- B. The proposed well site is located approximately 52.3 miles south of Vernal, Utah – See attached TOPO Map "A".
- C. Refer to attached Topographic Map "A" showing labeled access route to location.
- D. Existing roads will be maintained and repaired as necessary.

2. PLANNED ACCESS ROAD:

- A. The existing access road for the Chapita Wells Unit 1099-29 will be used to access the proposed location. No new road will be required.
- B. No additional storage areas will be needed for storing equipment, stockpiling, or vehicle parking.

All travel will be confined to existing access road rights-of-way.

Traveling off the 40-foot right-of-way will not be allowed. The access road and associated drainage structures will be constructed and maintained in accordance with road guidelines contained in the joint BLM/USFS publication: Surface Operating Standards for Oil and Gas Exploration and Development, Fourth Edition, and/or BLM Manual Section 9113 concerning road construction standards on projects subject to federal jurisdiction. During the drilling and production phase of operations, the road surface and shoulders will be kept in a safe and useable condition and drainage ditches and culverts will be kept clear and free flowing.

3. LOCATION OF EXISTING WELLS WITHIN A ONE-MILE RADIUS:

See attached TOPO map "C" for the location of wells within a one-mile radius.

4. LOCATION OF EXISTING AND/OR PROPOSED PRODUCTION FACILITIES:

A. On Well Pad

1. Production facilities will be set on location if the well is successfully completed for production. Facilities will consist of wellhead valves, combo separator-dehy unit with meter, two (2) 400-bbl vertical tanks and attaching piping.
2. Gas gathering lines – A 4" gathering line will be buried from dehy to the edge of the location.

B. Off Well Pad

1. No new off-pad pipeline will be required. Existing pipeline for the Chapita Wells Unit 1099-29 will be used to transport gas from the proposed location.

All permanent (on site for six months or longer) structures constructed or installed (including pumping units) will be painted a flat, non-reflective, earthtone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within 6 months of installation. **All facilities will be painted with Carlsbad Canyon or Covert Green.** Facilities required to comply with O.S.H.A. (Occupational Safety and Health Act) will be excluded.

5. LOCATION AND TYPE OF WATER SUPPLY:

- A. Water supply will be from Ouray Municipal Water Plant at Ouray, Utah, and/or Bonanza Power Plant water source in Sec 26, T8S, R23E, Uintah County, UT (State Water Right # 49-225(A31368)). Water will be hauled by a licensed trucking company.
- B. Water will be hauled by a licensed trucking company.
- C. No water well will be drilled on lease.

6. SOURCE OF CONSTRUCTION MATERIALS:

- A. All construction material for this pipeline will be of native borrow and soil accumulated during the construction of the location.
- B. No mineral materials will be required.

7. METHODS OF HANDLING WASTE DISPOSAL:

A. METHODS AND LOCATION

1. Cuttings will be confined in the reserve pit.

2. A portable toilet will be provided for human waste during the drilling and completion of the well. Disposal will be at the Vernal sewage disposal plant.
 3. Burning will not be allowed. Trash and other waste material will be contained in a wire mesh cage and disposed of at the Uintah County Landfill.
 4. Produced wastewater will be confined to a lined pit or storage tank for a period not to exceed 90 days after initial production. After the 90 day period, the produced water will be contained in a tank on location and then disposed of at one of the following locations: Natural Buttes Unit 21-20B SWD, Ace Disposal, CWU 550-30N SWD or EOG Resources, Inc. drilling operations (Chapita Wells Unit, Natural Buttes Unit & Stagecoach Unit).
 5. All chemicals will be disposed of at an authorized disposal site. Drip pans and absorbent pads will be used on the drilling rig to avoid leakage of oil to the pit.
- B. Water from drilling fluids and recovered during testing operations will be disposed of by either evaporating in the reserve pit, through natural or artificial methods, or removed and disposed of at an authorized disposal site. Introduction of well bore hydrocarbons to the reserve pit will be avoided by flaring them off in the flare pit at the time of recovery.

The reserve pit will be constructed so as not to leak, break, or allow discharge. If the reserve pit requires padding prior to lining (due to rocky conditions) felt padding will be used.

The reserve pit shall be lined with felt, and a 16-millimeter plastic liner. Sufficient bedding (i.e. weed free straw, or hay; felt; polyswell or soil) will be used to cover any rocks. The liner will overlap the pit walls and be covered with dirt and/or rocks to hold it in place. No trash, scrap pipe, etc., that could puncture the liner will be disposed of in the pit. More stringent protective requirements may be deemed necessary by the A.O.

EOG Resources, Inc. maintains a file, per 29 CFR 1910.1200 (g) containing current Material Safety Data Sheets (MSDS) for all chemicals, compounds, and/or substances which are used during the course of construction, drilling, completion, and production operations for this project. Hazardous materials (substances) which may be found at the site may include drilling mud and cementing products which are primarily inhalation hazards, fuels (flammable and/or combustible), materials that may be necessary for well completion/ stimulation activities such as flammable or combustible substances and acids/gels (corrosives). The opportunity for Superfund Amendments and Reauthorization Act (SARA) listed Extremely Hazardous Substances (EHS) at the site is generally limited to proprietary treating chemicals. All hazardous and EHS and commercial preparations will be handled in an appropriate manner to minimize the potential for leaks or spills to the environment.

No chemicals subject to reporting under SARA Title III (hazardous materials) in an amount greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completion of the well. Furthermore, extremely hazardous substances, as defined in 40 CFR 355, in threshold

planning quantities, will not be used, produced, stored, transported, or disposed of in association with the drilling, testing or completion of the well.

8. ANCILLARY FACILITIES:

None anticipated.

9. WELL SITE LAYOUT:

- A. Refer to attached well site plat for related topography cuts and fills and cross sections.
- B. Refer to attached well site plat for rig layout and soil material stockpile location as approved on On-site.
- C. Refer to attached well site plat for rig orientation, parking areas, and access road.

The reserve pit will be located on the southeast corner of the location. The flare pit will be located downwind of the prevailing wind direction on the south side of the location, a minimum of 100 feet from the wellhead and 30 feet from the reserve pit fence.

The stockpiled pit topsoil (first six inches) will be stored separate from the location topsoil southwest of pit corner B. The stockpiled location topsoil will be stored in a location providing easy access for interim reclamation and protection of the topsoil. Upon completion of construction, the stockpiled topsoil from the location will be broadcast seeded with the approved seed mixture from this location and then walked down with a Caterpillar tractor.

Access to the well pad will be from the northeast.

The corners of the well pad will be rounded off as needed to minimize excavation.

FENCING REQUIREMENTS:

All pits will be fenced according to the following minimum standards:

- A. Thirty-nine inch net wire shall be used with at least one strand of barbed wire on top of the net wire. (Barbed wire is not necessary if pipe or some type of reinforcement rod is attached to the top of the entire fence.)
- B. The net wire shall be no more than 2 inches above the ground. The barbed wire strand shall be 3 inches above the net wire. Total height of the fence shall be at least 42 inches.
- C. Corner posts shall be cemented and/or braced in such a manner as to keep the fence tight at all times.
- D. Standard steel, wood, or pipe posts shall be used between the corner braces. Maximum distances between any two posts shall be no greater than 16 feet.

- E. All wire shall be stretched by using a stretching device before it is attached to the corner posts.

The reserve pit fencing will be on the three sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until clean-up.

Each existing fence to be crossed by the access road shall be braced and tied off before cutting so as to prevent slacking of the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and, upon completion of construction, the fence shall be repaired to BLM or SMA specifications. A cattleguard with an adjacent 16 foot gate shall be installed in any fence where a road is regularly traveled. If the well is a producer, the cattleguards (shall/shall not) be permanently counted on concrete bases. Prior to crossing any fence located on Federal land, or any fence between Federal land and private land, the operator will contact the BLM, who will in turn contact the grazing permittee or owner of said fence and offer him/her the opportunity to be present when the fence is cut in order to satisfy himself/herself that the fence is adequately braced and tied off.

10. PLANS FOR RECLAMATION OF THE SURFACE:

A. Interim Reclamation (Producing Location)

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, materials, trash, and junk not required for production.

Immediately upon well completion, any hydrocarbons on the pit shall be removed in accordance with CFR 3162.7-1.

If a plastic nylon reinforced liner is used, it shall be torn and perforated before backfilling of the reserve pit.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximate natural contours—see attached Figure #3. The reserve pit will be reclaimed within 90 days from the date of the well completion, or as soon as environmental conditions allow. Before any dirt takes place, the reserve pit must be completely dry and free of all foreign obstacles.

The stockpiled pit topsoil will then be spread over the pit area and broadcast seeded with the prescribed seed mixture for this location. The seeded area will then be walked down with a cat.

Seed Mixture	Drilled Rate (lbs./acre PLS*)
HyCrest Wheatgrass	9.0
Prostrate Kochia	3.0

*Pure live seed (PLS) formula: percent of purity of seed mixture times percent germination of seed mixture equals portion of seed mixture that is PLS.

B. Dry Hole/Abandoned Location

At such time as the well is plugged and abandoned, the operator will submit a subsequent report of abandonment and the BLM will attach the appropriated surface rehabilitation conditions of approval.

Seed Mixture	Drilled Rate (lbs./acre PLS*)
Wyoming Big Sage	3.0
Shadscale	3.0
Needle and Threadgrass	3.0
HyCrest Wheatgrass	1.0
Scarlet Globe Mallow	1.0

*Pure live seed (PLS) formula: percent of purity of seed mixture times percent germination of seed mixture equals portion of seed mixture that is PLS.

11. SURFACE OWNERSHIP:

Surface ownership of the proposed well site, access road, and pipeline route is as follows:

Bureau of Land Management

12. OTHER INFORMATION:

A. EOG Resources, Inc. will inform all persons in the area who are associated with this project that they are subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, the operator will immediately stop work that might further disturb such materials, and contact the Authorized Officer. Within five working days the Authorized Officer will inform the operator as to:

- Whether the materials appear eligible for the National Register of Historic Places;
- The mitigation measures the operator will likely have to undertake before the site can be used.

- A time frame for the Authorized Officer to complete an expedited review under 36 CFR 800.11 to confirm, through the State Historic Preservation Officer, that the findings of the Authorized Officer are correct and that mitigation is appropriate.

If the operator wished, at any time, to relocate activities to avoid the expense of mitigation and/or the delays associated with this process, the Authorized Officer will assume responsibility for whatever recordation and stabilization of the exposed materials that may be required. Otherwise, the operator will be responsible for mitigation costs. The Authorized Officer will provide technical and procedural guidelines for the conduct of mitigation. Upon verification from the Authorized Officer that required mitigation has been completed, the operator will then be allowed to resume construction.

- B. As operator, EOG Resources, Inc. will control noxious weeds along Right-of-Ways for roads, pipelines, well sites, or other applicable facilities. A list of noxious weeds will be obtained from the BLM administered land, a Pesticide Use proposal shall be submitted, and given approval, prior to the application of herbicides or other pesticides or possible hazardous chemicals.
- C. Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on BLM lands after the conclusion of drilling operations or at any other time without BLM authorization. However, if BLM authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities. (The BLM does not seek to compete with private industry. There are commercial facilities available for stacking and storing drilling rigs.)
- D. The drilling rig and ancillary equipment will be removed from the location prior to commencement of completion operations. Completion operations will be conducted utilizing a completion/workover rig.

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws, regulations, Onshore Oil and Gas Orders, the approved Plan of Operations, and any applicable Notice of Lessees. The operator is fully responsible for the actions of its subcontractors. A complete copy of the approved "Application for Permit to Drill" will be furnished to the field representative(s) to ensure compliance and shall be on location during all construction and drilling operations.

Construction activity will not be conducted using frozen or saturated soils material or during periods when watershed damage is likely to occur.

If the existing access road, proposed access road, and proposed pad are dry during construction, drilling, and completion activities, water will be applied to help facilitate compaction during construction and to minimize soil loss as a result of wind erosion.

A block cultural resources survey for Section 29, T9S, R23E was conducted and submitted by Montgomery Archaeological Consultants on 5/11/2007. A paleontological survey was conducted and will be submitted by Intermountain Paleo.

Additional Surface Stipulations:

None.

LESSEE OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:

PERMITTING AGENT

Mary A. Maestas
EOG Resources, Inc.
1060 East Highway 40
Vernal, UT 84078
(435) 781-9111

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws, regulations, Onshore Oil and Gas Orders, the approved plan of operations, and any applicable Notice to Lessees. The operator is fully responsible for the actions of his subcontractors. A copy of these conditions will be furnished to the field representative to insure compliance.

The operator or his/her contractor shall contact the BLM office at (435) 781-4400 forty-eight (48) hours prior to construction activities.


CERTIFICATION:

I hereby certify that I, or persons under my direct supervision, have inspected the proposed drill site and access route; that I am familiar with the conditions which currently exist; that the statements made in this plan are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed by EOG Resources, Inc. and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

Please be advised that EOG Resources, Inc. is considered to be the operator of the Chapita Wells Unit 728-29 Well, located in the NENE, of Section 29, T9S, R23E, Uintah County, Utah; Federal land and minerals; and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond Coverage is under Bond # NM 2308.

October 18, 2007

Date


Mary A. Maestas, Regulatory Assistant


Date of onsite: October 4, 2007

EOG RESOURCES, INC.

LOCATION LAYOUT FOR



CWU #728-29
SECTION 29, T9S, R23E, S.L.B.&M.
608' FNL 513' FEL

FIGURE #1



SCALE: 1" = 50'
DATE: 09-27-07
Drawn By: L.K.

NOTE:
Flare Pit is to
be located a min.
of 100' from the
Well Head.

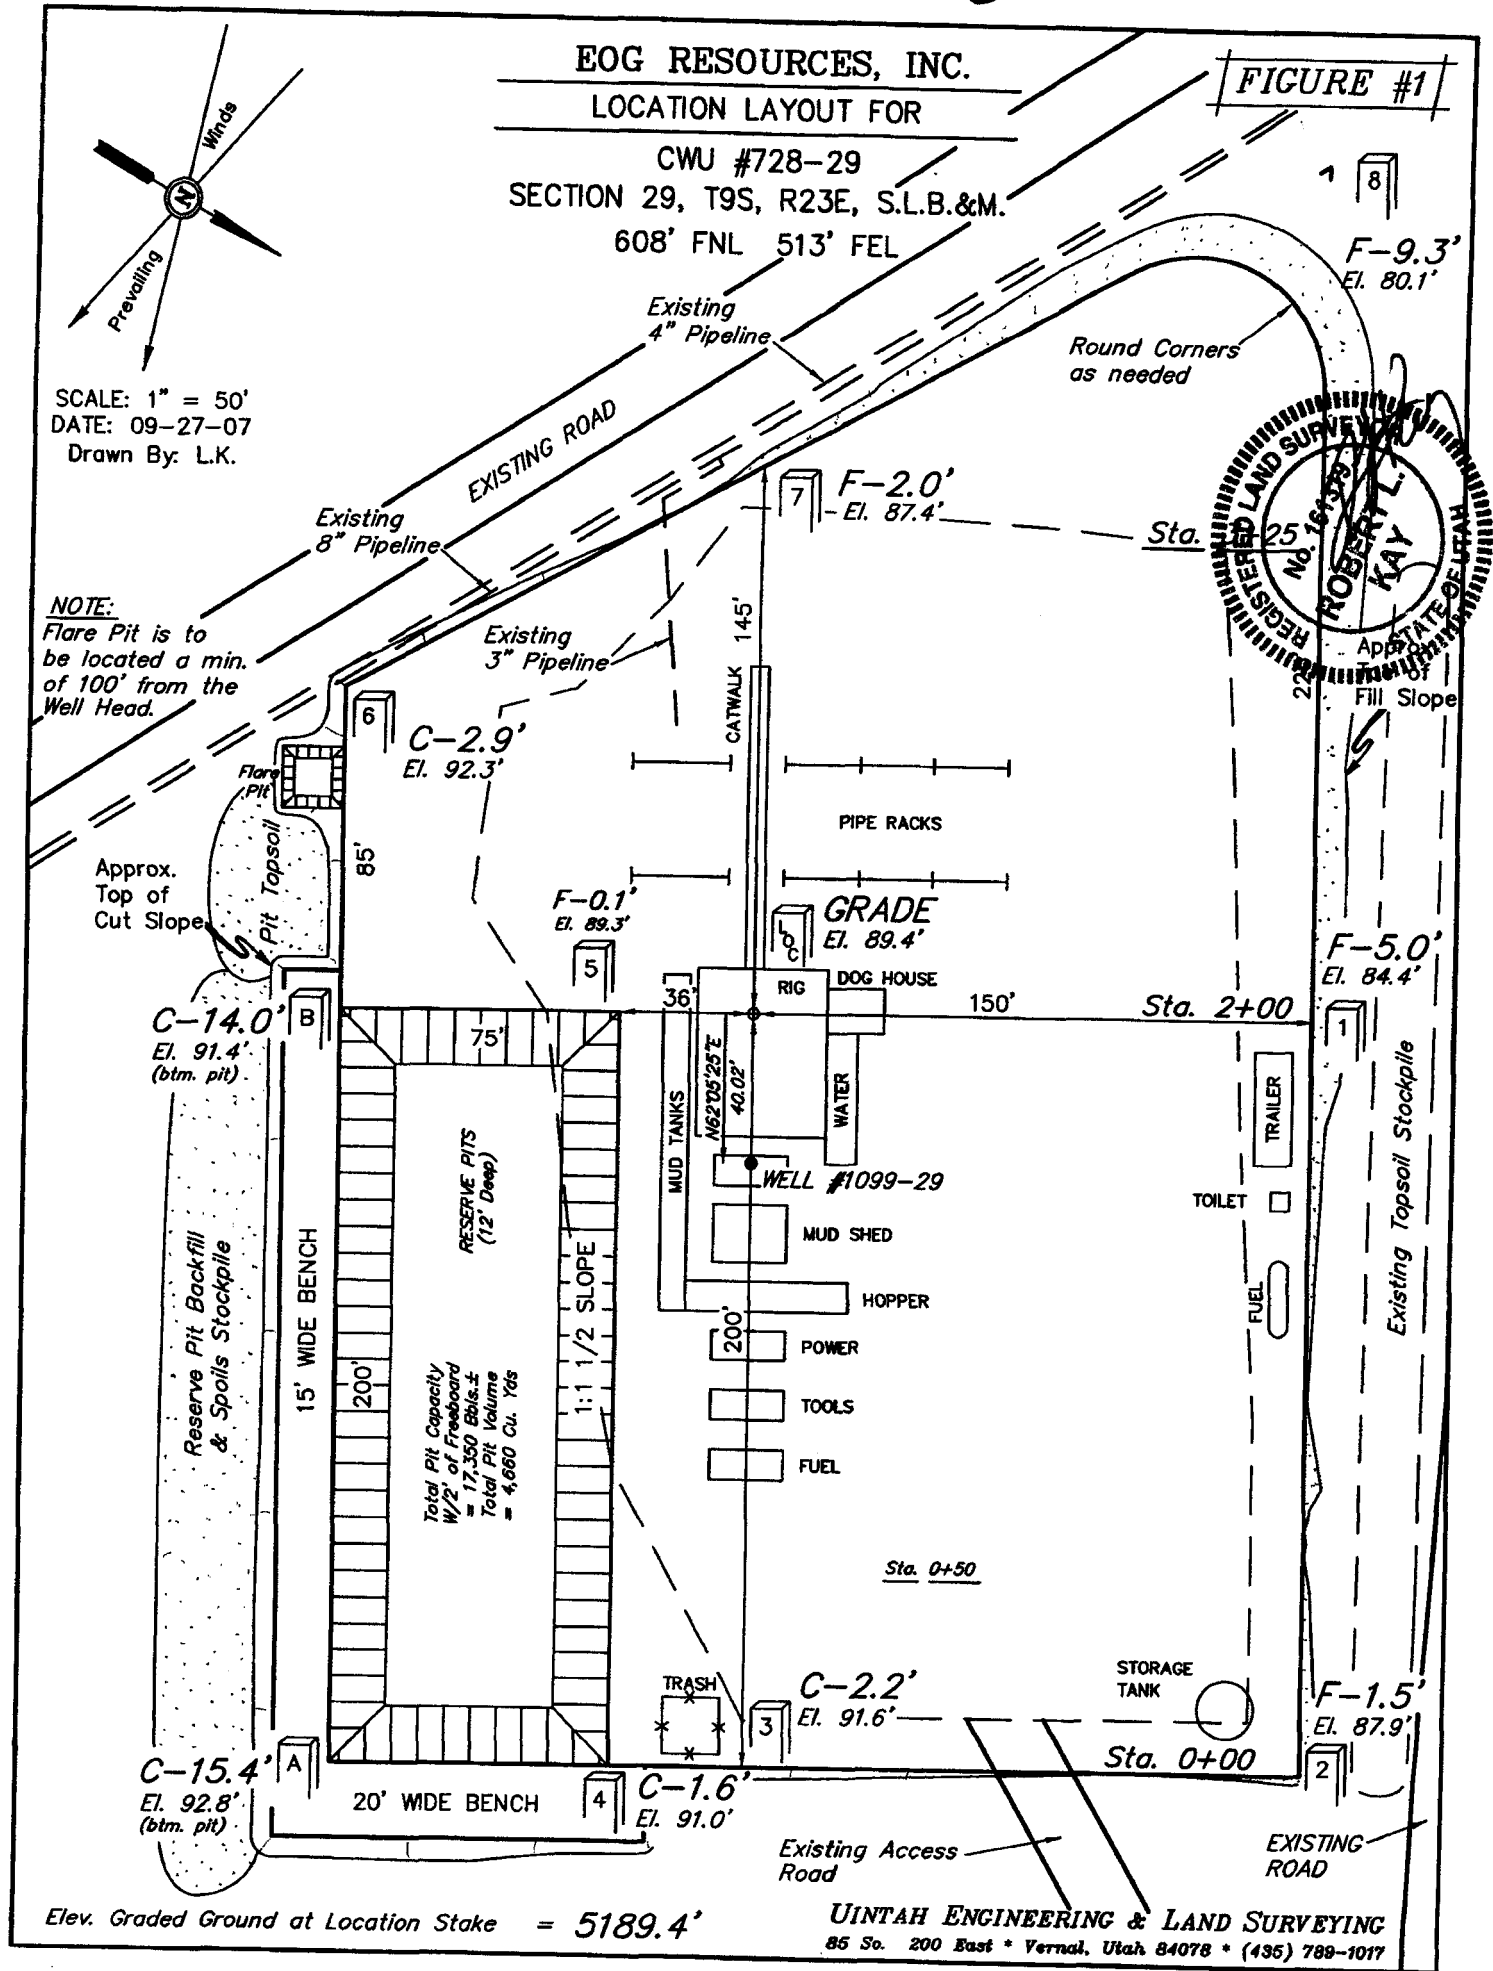

Elev. Graded Ground at Location Stake = 5189.4'

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East * Vernal, Utah 84078 * (435) 789-1017

EOG RESOURCES, INC.

TYPICAL CROSS SECTIONS FOR


CWU #728-29

SECTION 29, T9S, R23E, S.L.B.&M.

608' FNL 513' FEL

FIGURE #2

1" = 20'
X-Section
Scale
1" = 50'
DATE: 09-27-07
Drawn By: L.K.

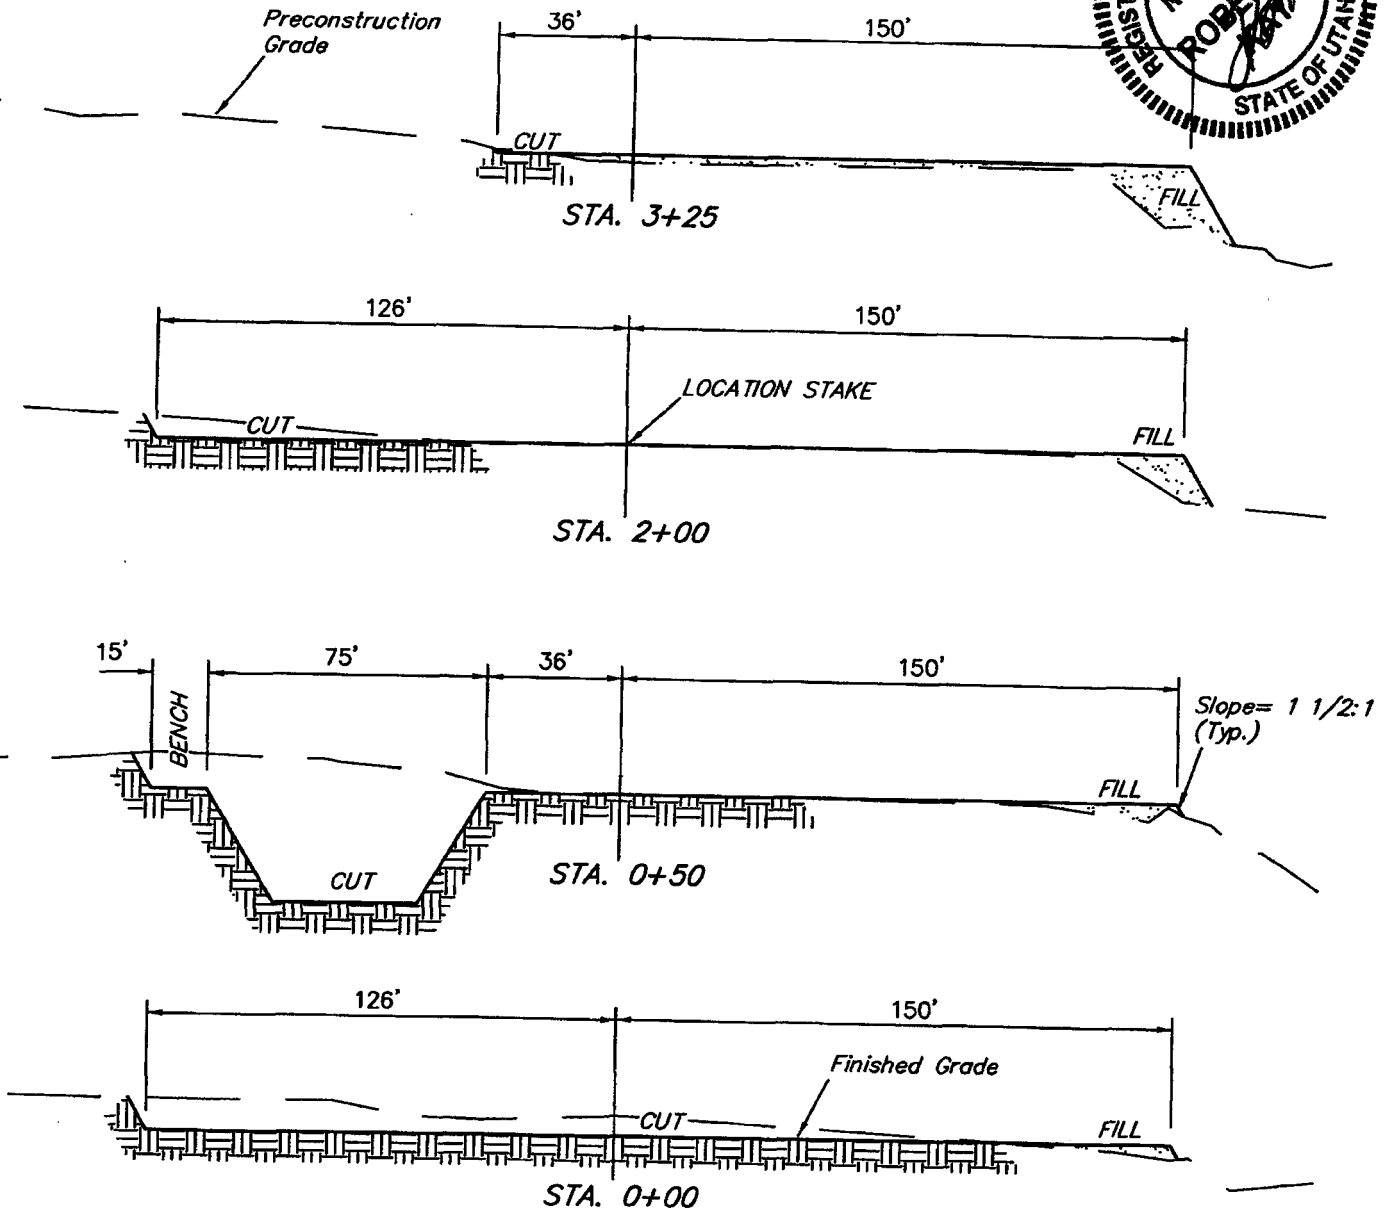

* NOTE:
FILL QUANTITY INCLUDES
5% FOR COMPACTION

APPROXIMATE YARDAGES

(6") Topsoil Stripping = 920 Cu. Yds.
(New Construction Only)
Remaining Location = 6,760 Cu. Yds.

TOTAL CUT = 7,680 CU.YDS.
FILL = 3,580 CU.YDS.

EXCESS MATERIAL = 4,100 Cu. Yds.
Topsoil & Pit Backfill = 3,250 Cu. Yds.
(1/2 Pit Vol.)
EXCESS UNBALANCE = 850 Cu. Yds.
(After Interim Rehabilitation)

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East • Vernal, Utah 84078 • (435) 789-1017



EOG RESOURCES, INC.
PRODUCTION FACILITY LAYOUT FOR

CWU #728-29
SECTION 29, T9S, R23E, S.L.B.&M.
608' FNL 513' FEL

FIGURE #3

1

SCALE: 1" = 50'
DATE: 09-27-07
Drawn By: L.K.

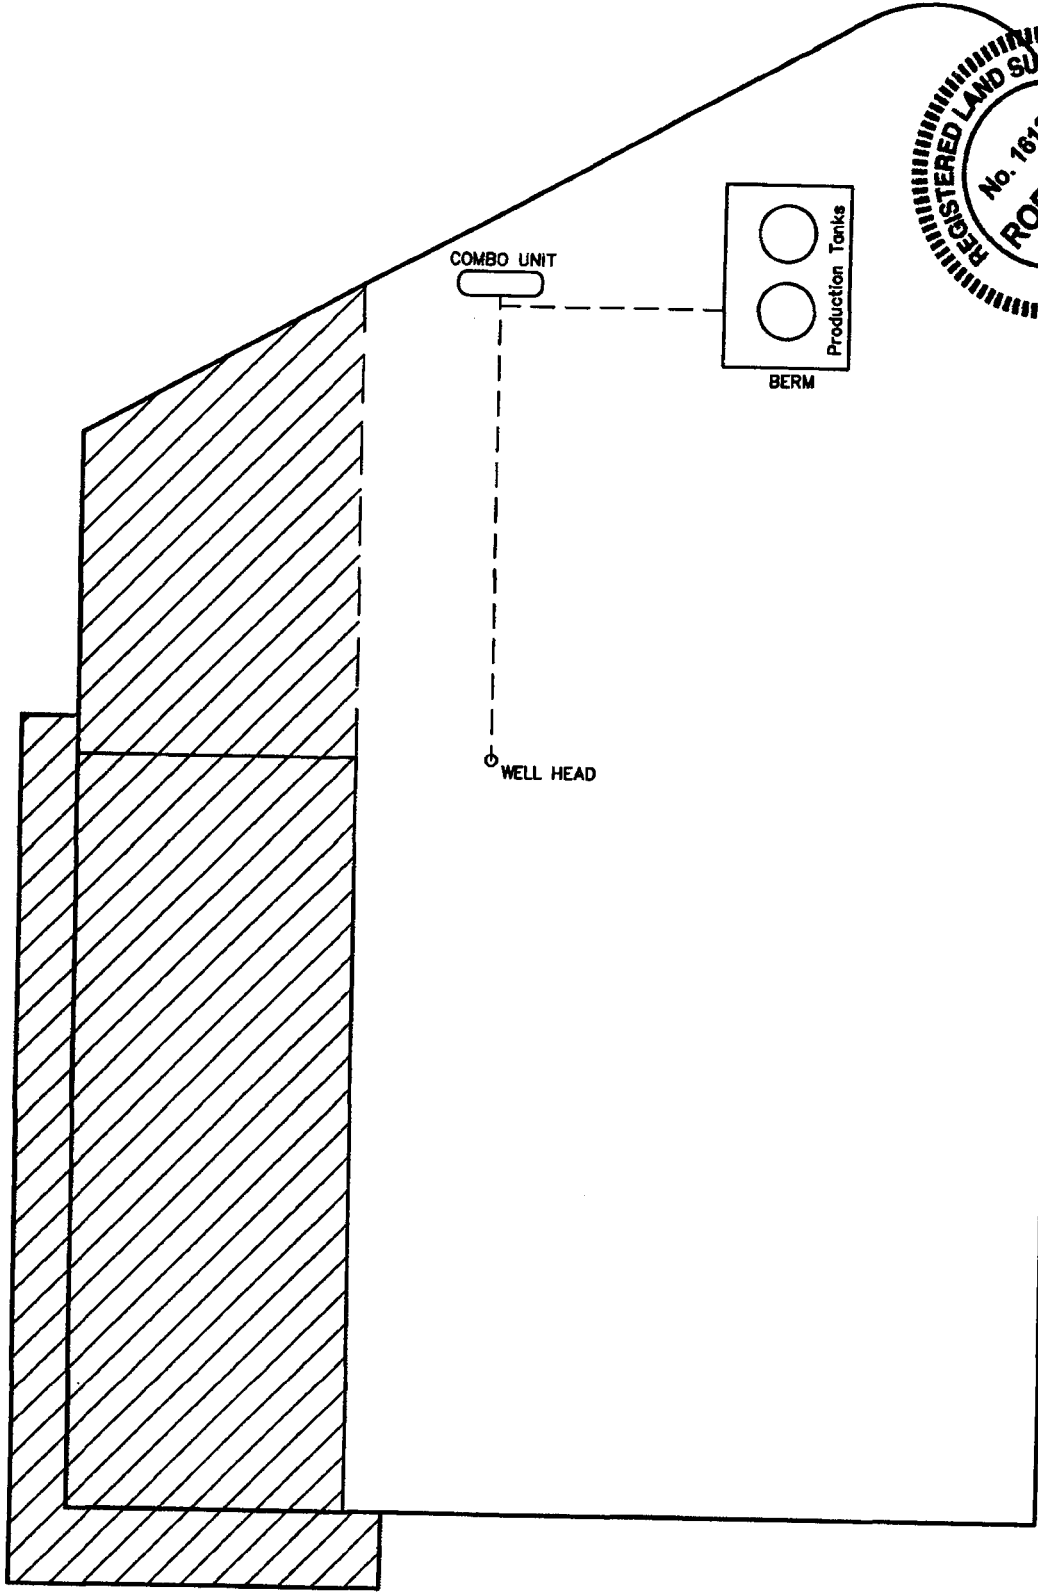

 RE-HABED AREA

EOG RESOURCES, INC.

CWU #728-29

LOCATED IN UTAH COUNTY, UTAH
SECTION 29, T9S, R23E, S.L.B.&M.



PHOTO: VIEW FROM CORNER #5 TO LOCATION STAKE

CAMERA ANGLE: NORTHWESTERLY

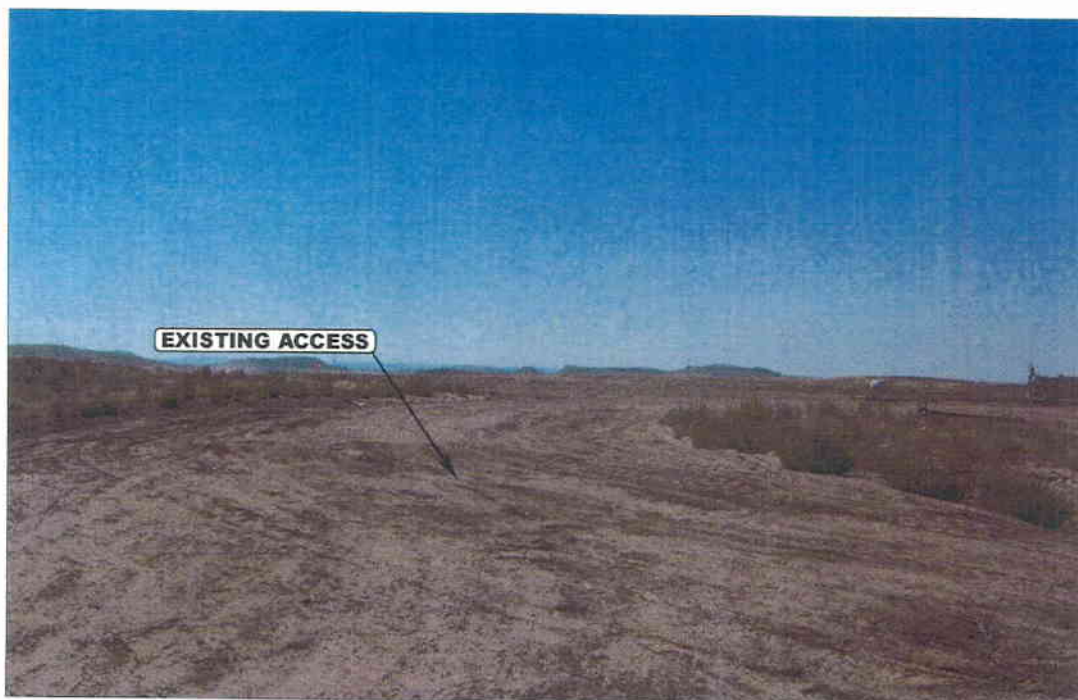


PHOTO: VIEW OF EXISTING ACCESS

CAMERA ANGLE: SOUTHWESTERLY



UELS

Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
435-789-1017 uels@uelsinc.com

LOCATION PHOTOS


09 18 07
MONTH DAY YEAR

PHOTO

TAKEN BY: C.R.

DRAWN BY: Z.L.

REVISED: 00-00-00

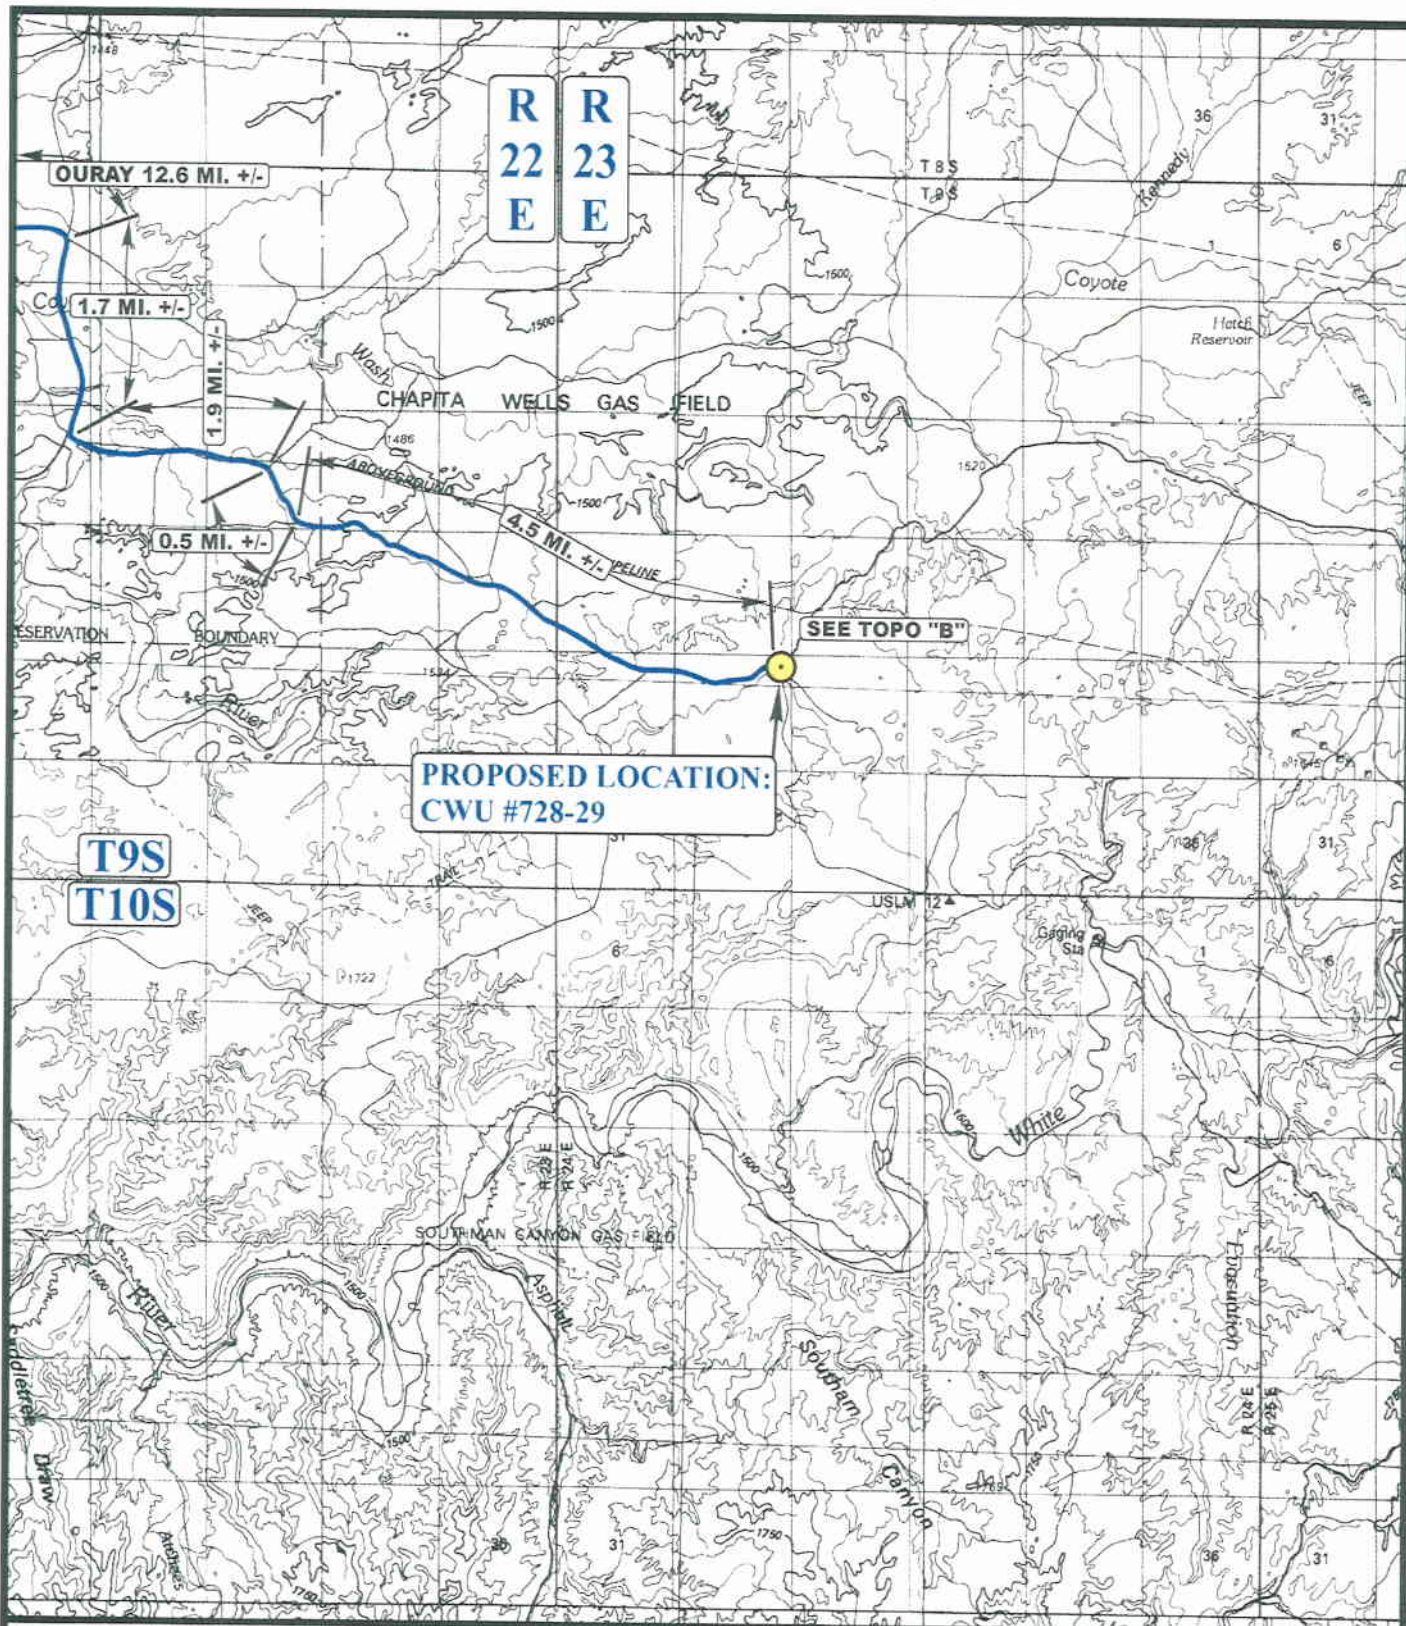

LEGEND:

● PROPOSED LOCATION

EOG RESOURCES, INC.

CWU #728-29

SECTION 29, T9S, R23E, S.L.B.&M.

608' FNL 513' FEL



Utah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813



TOPOGRAPHIC
MAP


09 18 07
MONTH DAY YEAR

SCALE: 1:100,000

DRAWN BY: Z.L.

REVISED: 00-00-00



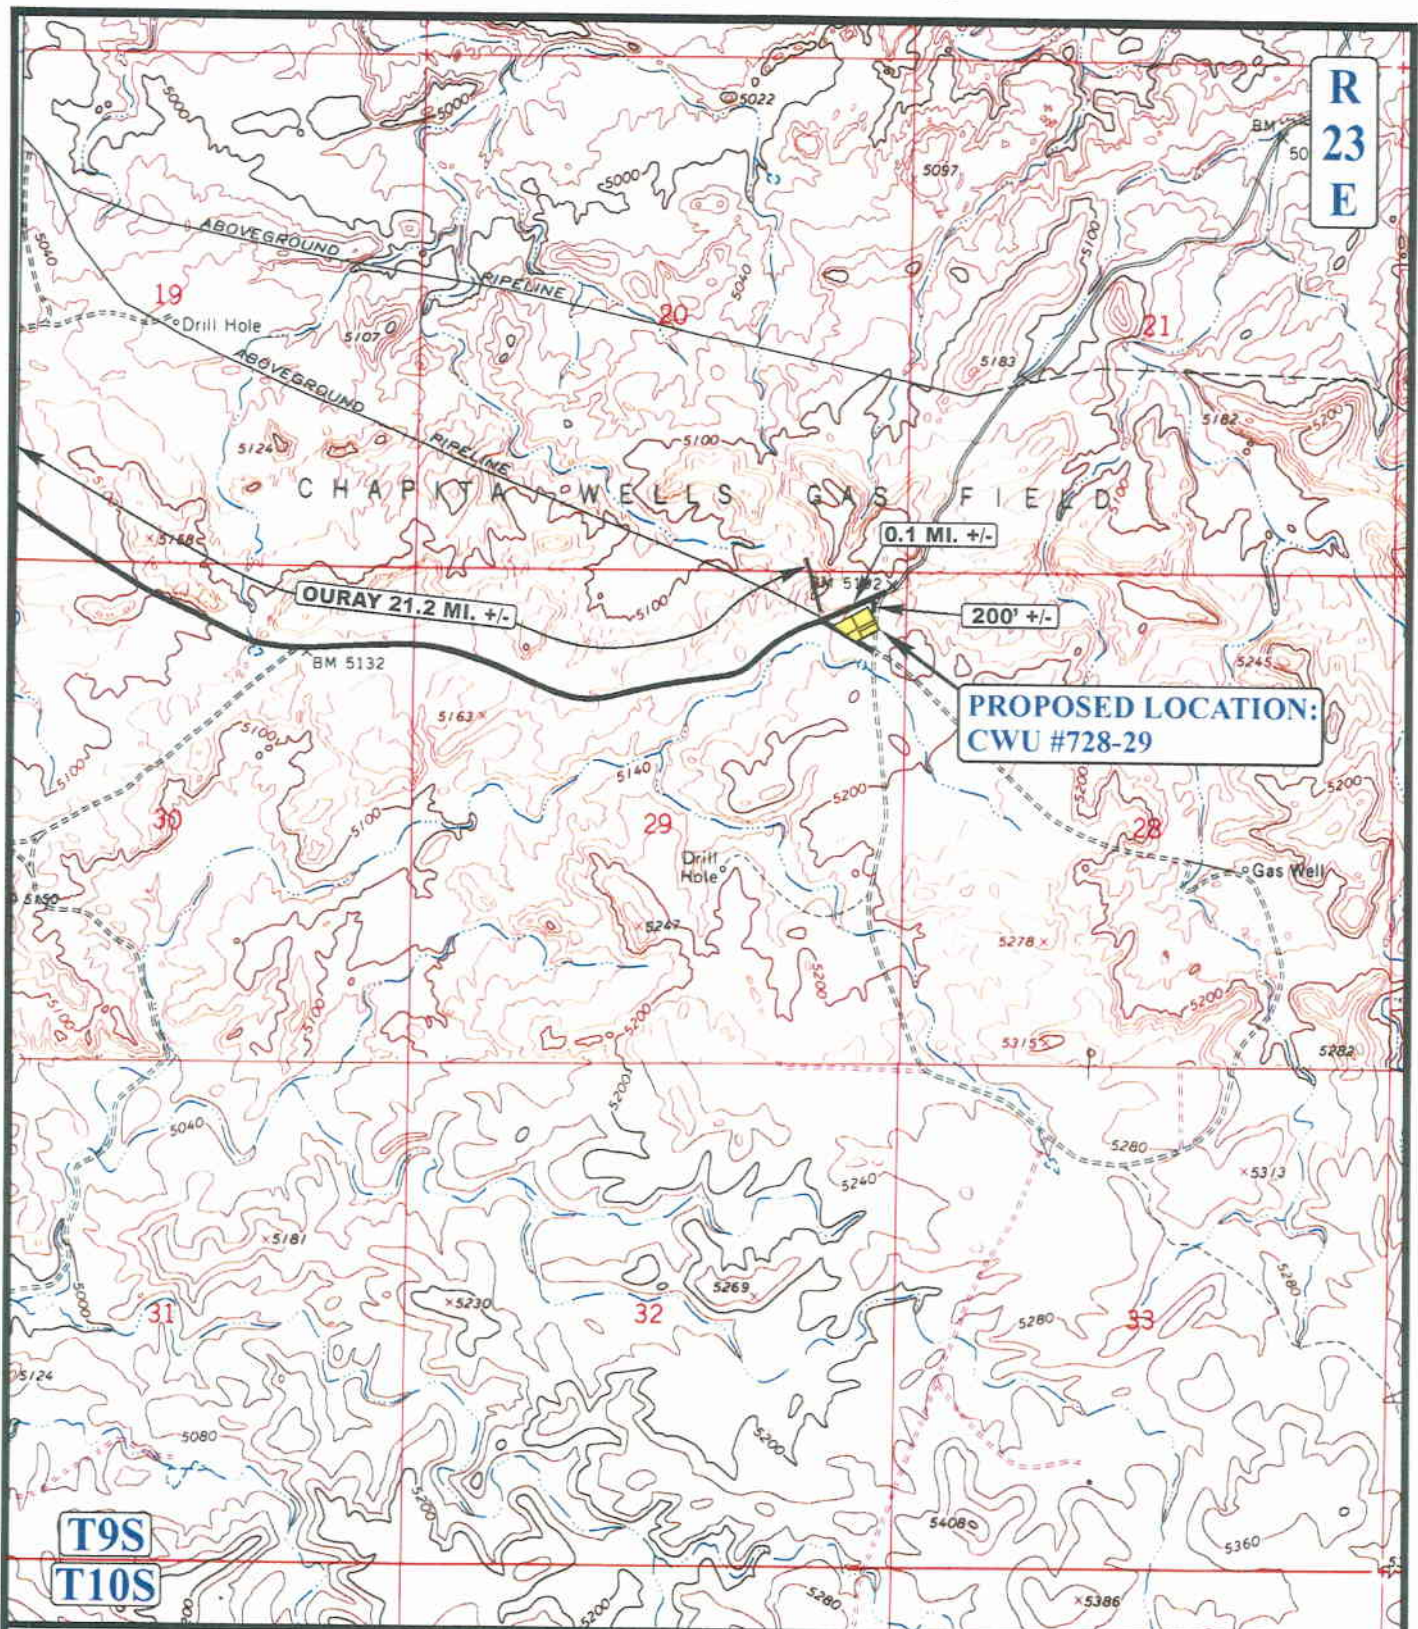

**R
23
E**

**T9S
T10S**

LEGEND:

EXISTING ROAD

N

EOG RESOURCES, INC.

**CWU #728-29
SECTION 29, T9S, R23E, S.L.B.&M.
608' FNL 513' FEL**

**U
E
L
S**

Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813

**TOPOGRAPHIC
MAP**

09 18 07
MONTH DAY YEAR

SCALE: 1" = 2000' DRAWN BY: Z.L. REVISED: 00-00-00

**B
TOPO**

**R
23
E**

**PROPOSED LOCATION:
CWU #728-29**

T9S

LEGEND:

- | | |
|-------------------|-------------------------|
| ○ DISPOSAL WELLS | ○ WATER WELLS |
| ● PRODUCING WELLS | ● ABANDONED WELLS |
| ● SHUT IN WELLS | ● TEMPORARILY ABANDONED |



Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813



EOG RESOURCES, INC.

CWU #728-29
SECTION 29, T9S, R23E, S.L.B.&M.
608' FNL 513' FEL

TOPOGRAPHIC MAP **09 18 07**
MONTH DAY YEAR
SCALE: 1" = 2000' DRAWN BY: Z.L. REV: 10-08-07 Z.L.



WORKSHEET
APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 10/22/2007

API NO. ASSIGNED: 43-047-39724

WELL NAME: CWU 728-29

OPERATOR: EOG RESOURCES INC (N9550)

PHONE NUMBER: 303-824-5526

CONTACT: MARY MAESTAS

PROPOSED LOCATION:

NENE 29 090S 230E

SURFACE: 0608 FNL 0513 FEL

BOTTOM: 0608 FNL 0513 FEL

COUNTY: UINTAH

LATITUDE: 40.01265 LONGITUDE: -109.3425

UTM SURF EASTINGS: 641469 NORTHINGS: 4430267

FIELD NAME: NATURAL BUTTES (630)

INSPECT LOCATN BY: / /		
Tech Review	Initials	Date
Engineering		
Geology		
Surface		

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU0337

SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: WSTC

COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:


☒ Plat
☒ Bond: Fed[1] Ind[] Sta[] Fee[]
(No. NM2308)
☒ Potash (Y/N)
☒ Oil Shale 190-5 (B) or 190-3 or 190-13
☒ Water Permit
(No. 49-225)
☒ RDCC Review (Y/N)
(Date:)
☒ Fee Surf Agreement (Y/N)
☒ Intent to Commingle (Y/N)

LOCATION AND SITING:

☐ R649-2-3.
Unit: CHAPITA WELLS
☐ R649-3-2. General
Siting: 460 From Qtr/Qtr & 920' Between Wells
☐ R649-3-3. Exception
☒ Drilling Unit
Board Cause No: 179-8
Eff Date: 8-10-1749
Siting: Disseminated Gas Siting
☐ R649-3-11. Directional Drill

COMMENTS: _____

STIPULATIONS: 1- Sealed Approval

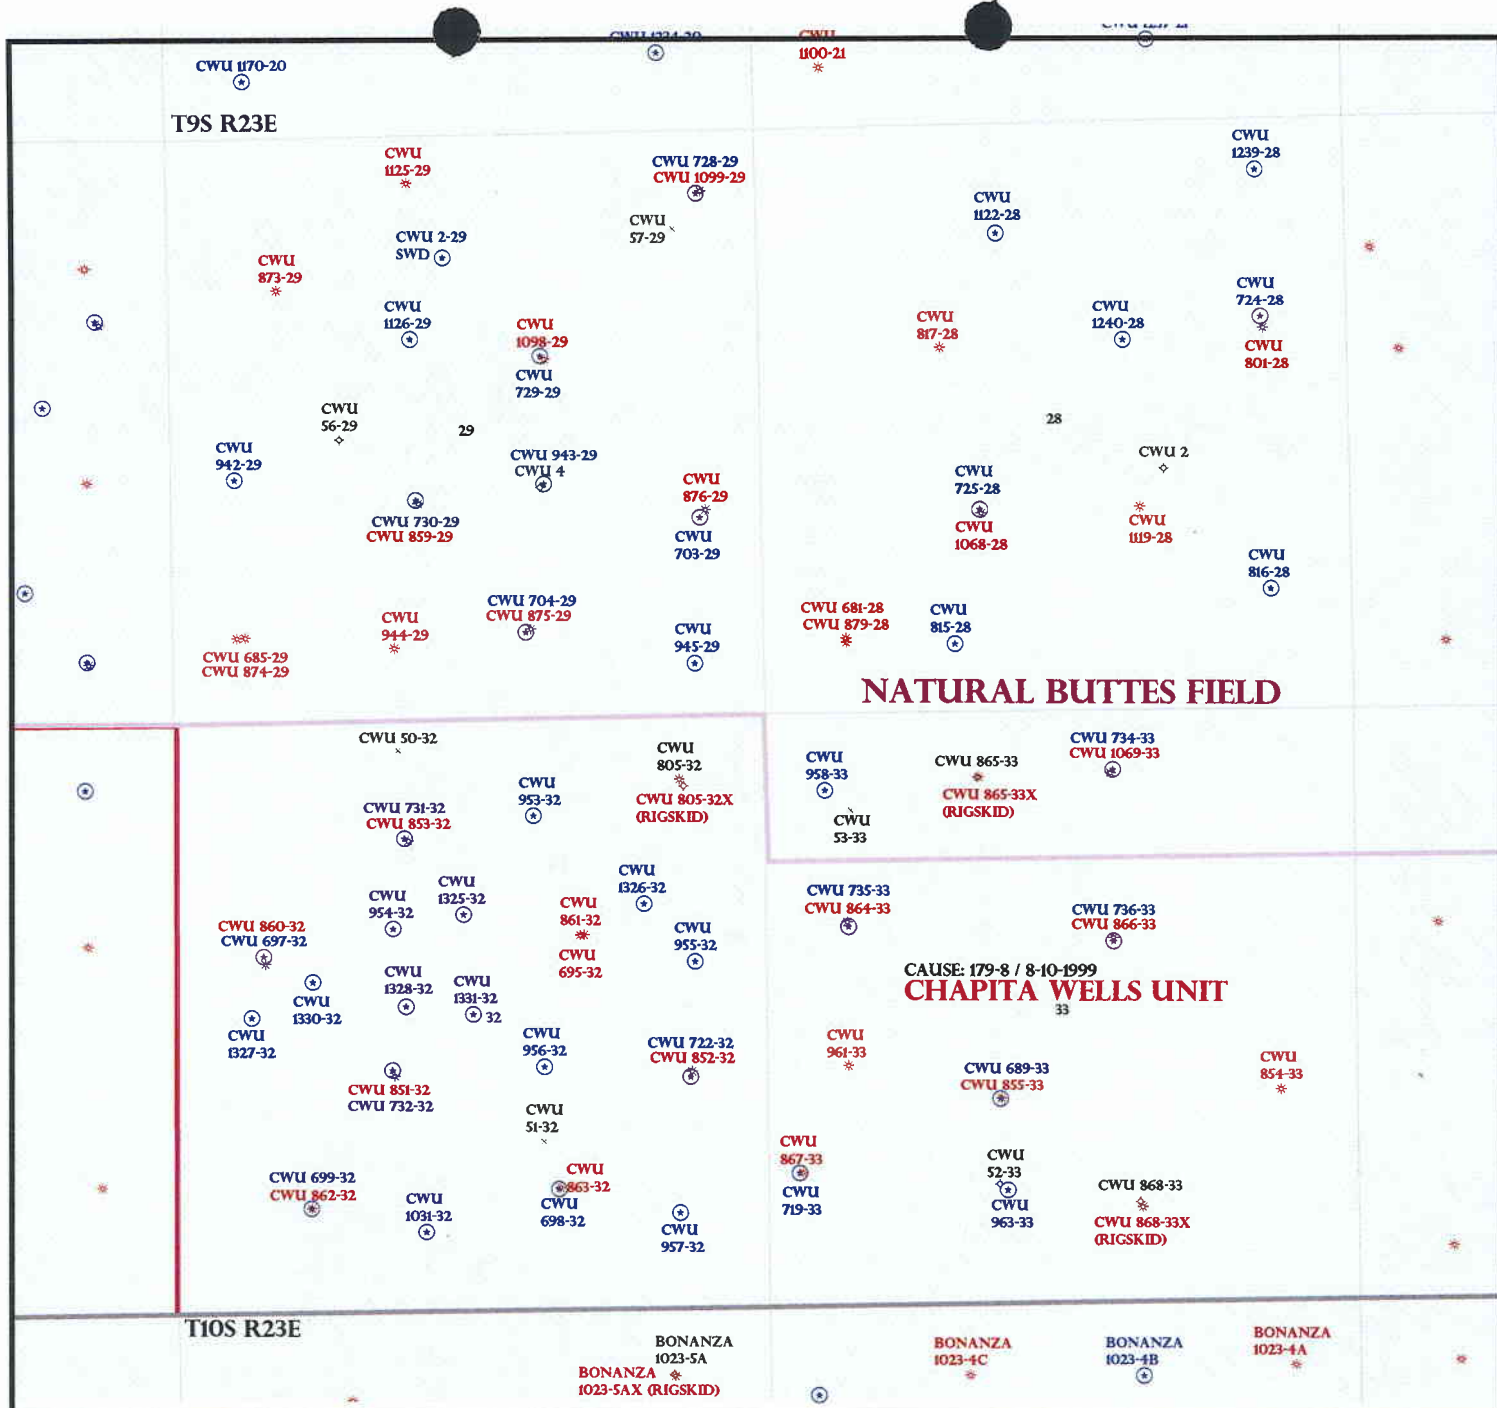

OPERATOR: EOG RESOURCES INC (N9550)

SEC: 29,33 T.9S R. 23E

FIELD: NATURAL BUTTES (630)

COUNTY: UINTAH

CAUSE: 179-8 / 8-10-1999



OIL, GAS & MINING



PREPARED BY: DIANA MASON
DATE: 23-OCTOBER-2007

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office
P.O. Box 45155
Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:
3160
(UT-922)

October 23, 2007

Memorandum

To: Assistant District Manager Minerals, Vernal District
From: Michael Coulthard, Petroleum Engineer
Subject: 2007 Plan of Development Chapita Wells Unit
Uintah County, Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2007 within the Chapita Wells Unit, Uintah County, Utah.

API #	WELL NAME	LOCATION
-------	-----------	----------

(Proposed PZ Wasatch)

43-047-39723	CWU 730-29 Sec 29 T09S R23E 1972 FSL 2201 FWL	
43-047-39724	CWU 728-29 Sec 29 T09S R23E 0608 FNL 0513 FEL	
43-047-39725	CWU 734-33 Sec 33 T09S R23E 0512 FNL 2158 FEL	

This office has no objection to permitting the wells at this time.

/s/ Michael L. Coulthard

bcc: File - Chapita Wells Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:10-23-07



JON M. HUNTSMAN, JR.
Governor

GARY R. HERBERT
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil Gas and Mining

JOHN R. BAZA
Division Director

October 23, 2007

EOG Resources, Inc.
1060 East Highway 40
Vernal, UT 84078

Re: Chapita Wells Unit 728-29 Well, 608' FNL, 513' FEL, NE NE, Sec. 29, T. 9 South,
R. 23 East, Uintah County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-047-39724.

Sincerely,

Gil Hunt
Associate Director

pab
Enclosures

cc: Uintah County Assessor
Bureau of Land Management, Vernal Office

Operator: EOG Resources, Inc.

Well Name & Number Chapita Wells Unit 728-29

API Number: 43-047-39724

Lease: UTU0337

Location: NE NE Sec. 29 T. 9 South R. 23 East

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

2. Notification Requirements

Notify the Division with 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dustin Doucet at (801) 538-5281 office (801) 733-0983 home

3. Reporting Requirements

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTFORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010

RECEIVED

OCT 18 2007

BLM

APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU0337
1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other <input type="checkbox"/> Single Zone <input checked="" type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator EOG RESOURCES INC		7. If Unit or CA Agreement, Name and No. UTU63013X
Contact: MARY A. MAESTAS E-Mail: mary_maestas@eogresources.com		8. Lease Name and Well No. CWU 728-29
3a. Address 1060 EAST HIGHWAY 40 VERNAL, UT 84078	3b. Phone No. (include area code) Ph: 303-824-5526 Fx: 303-824-5527	9. API Well No. 43 047 39724
4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NENE 608FNL 513FEL 40.01259 N Lat, 109.34314 W Lon At proposed prod. zone NENE 608FNL 513FEL 40.01259 N Lat, 109.34314 W Lon		10. Field and Pool, or Exploratory NATURAL BUTTES
14. Distance in miles and direction from nearest town or post office* 52.3 MILES SOUTH OF VERNAL, UTAH		11. Sec., T., R., M., or Blk. and Survey or Area Sec 29 T9S R23E Mer SLB SME: BLM
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 513' LEASE LINE	16. No. of Acres in Lease 2,344.080	12. County or Parish UINTAH
18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 70'	19. Proposed Depth 6890 MD	13. State UT
21. Elevations (Show whether DF, KB, RT, GL, etc.) 5189 GL	22. Approximate date work will start	17. Spacing Unit dedicated to this well
23. Estimated duration 45 DAYS		20. BLM/BIA Bond No. on file NM2308
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- | | |
|---|--|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature (Electronic Submission)	Name (Printed/Typed) MARY A. MAESTAS Ph: 303-824-5526	Date 10/18/2007
Title REGULATORY ASSISTANT		
Approved by (Signature) 	Name (Printed/Typed) Steve Kencella	Date 5-15-2008
Title Assistant Field Manager	Office VERNAL FIELD OFFICE	

Application for approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Electronic Submission #56806 verified by the BLM Well Information System
For EOG RESOURCES INC, sent to the Vernal
Committed to AFMSS for processing by CINDY SEVERSON on 10/18/2007 (08CX50015AE)

NOTICE OF APPROVAL

CONDITIONS OF APPROVAL ATTACHED
RECEIVED

MAY 19 2008

** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED ** BLM REVISED

DIV OF OIL, GAS & MINING

NOS 10/3/07
08GXJ0063AE



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE
170 South 500 East VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: E.O.G. Resources Inc.
Well No: CWU 728-29
API No: 43-047-39724

Location: NENE, Sec. 29, T9S, R23E
Lease No: UTU-0337
Agreement: Chapita Wells Unit

Title	Name	Office Phone Number	Cell Phone Number
Petroleum Engineer:	Matt Baker	(435) 781-4490	(435) 828-4470
Petroleum Engineer:	Michael Lee	(435) 781-4432	(435) 828-7875
Petroleum Engineer:	James Ashley	(435) 781-4470	(435) 828-7874
Petroleum Engineer:	Ryan Angus	(435) 781-4430	(435) 828-7368
Supervisory Petroleum Technician:	Jamie Sparger	(435) 781-4502	(435) 828-3913
NRS/Enviro Scientist:		(435) 781-4475	(435) 828-4029
NRS/Enviro Scientist:	Karl Wright	(435) 781-4484	(435) 828-7381
NRS/Enviro Scientist:	Holly Villa	(435) 781-4404	(435) 828-3544
NRS/Enviro Scientist:		(435) 781-4476	
NRS/Enviro Scientist:	Chuck Macdonald	(435) 781-4441	(435) 828-7482
NRS/Enviro Scientist:		(435) 781-3400	(435) 828-3544
NRS/Enviro Scientist:	Michael Cutler	(435) 781-3401	(435) 828-3546
NRS/Enviro Scientist:	Anna Figueroa	(435) 781-3407	(435) 828-3548
NRS/Enviro Scientist:	Verlyn Pindell	(435) 781-3402	(435) 828-3547
NRS/Enviro Scientist:	Darren Williams	(435) 781-4447	(435) 828-4029
NRS/Enviro Scientist:	Nathan Packer	(435) 781-3405	(435) 828-3545

Fax: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	- Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	- Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings.
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.
- Bury pipeline at all low water crossings.
- Permission from an authorized BLM representative would be required if construction or other operations occur during wet conditions that would lead to excessive rutting.
- Permission to clear all wildlife stipulations would only be approved by the BLM wildlife biologist during the specific timing for the species potentially affected by this action.
- Culverts and gravel may be installed as needed.
- Fill from pad construction will be kept off of the adjacent county road.

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- A surface casing shoe integrity test shall be performed.
- A variance is granted for Onshore Order #2-Drilling Operations III. E. "Blooie line discharge 100 feet from well bore and securely anchored" Blooie line can be 75 feet.
- Production casing cement shall be at a minimum 200 feet inside the surface casing. A CBL shall be run from TD to top of cement and a field copy shall be sent to this field office.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB

or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid,

and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: March 31, 2007

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE- Other instructions on reverse side.

5. Lease Serial No.
Multiple (See Attached)
6. If Indian, Allottee or Tribe Name

7. If Unit or CA/Agreement, Name and/or No.
Chapita Wells Unit

8. Well Name and No.
Multiple (See Attached)

9. API Well No.
Multiple (See Attached)

10. Field and Pool, or Exploratory Area
Natural Buttes

11. County or Parish, State
Uintah County, Utah

1. Type of Well
☐ Oil Well ☒ Gas Well ☐ Other

2. Name of Operator
EOG Resources, Inc.

3a. Address
1060 E. HWY 40 Vernal, UT 84078

3b. Phone No. (include area code)
435-789-0790

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
Multiple (See Attached)
43 047 3972A
CWU 728-29
95 23E 29

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other Air Drilling Variance
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Request
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

EOG Resources, Inc. respectfully requests authorization for air drilling operations, see attached.

COPY SENT TO OPERATOR

Date: 10.14.2008

Initials: KS

RECEIVED

SEP 22 2008

DIV. OF OIL, GAS & MINING

14. I hereby certify that the foregoing is true and correct
Name (Printed/Typed)

Mickenzie Thacker

Title **Operations Clerk**

Signature

Mickenzie Thacker

Date

09/17/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

[Signature]

Title

Pet. Eng.

Date

10/7/08

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

DOGm

Federal Approval Of This Action Is Necessary

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

API #	Lease #	Well Name	Footages	¼-¼ Legal Description
43-047-38495	UTU-0281	CWU 541-03	712' FSL 2088' FWL	SESW Sec. 3 T9S R22E
43-047-39902	UTU-29535	CWU 705-29	1354' FNL 957' FWL	SWNW Sec. 29 T9S R23E
43-047-39054	UTU-0343	CWU 715-07	650' FNL 1950' FEL	NWNE Sec. 7 T9S R23E
43-047-39896	UTU-0337	CWU 727-29	473' FNL 2136' FWL	NENW Sec. 29 T9S R23E
43-047-39724	UTU-0337	CWU 728-29	608' FNL 513' FEL	NENE Sec. 29 T9S R23E
43-047-39617	UTU-0337	CWU 729-29	2039' FNL 1944' FEL	SWNE Sec. 29 T9S R23E
43-047-39723	UTU-0337	CWU 730-29	1972' FSL 2201' FWL	NESW Sec. 29 T9S R23E
43-047-39789	UTU-0336	CWU 733-33	576' FNL 1880' FWL	NENW Sec. 33 T9S R23E
43-047-39725	UTU-0336	CWU 734-33	512' FNL 2158' FEL	NWNE Sec. 33 T9S R23E
43-047-39684	UTU-0336	CWU 735-33	1884' FNL 729' FWL	SWNW Sec. 33 T9S R23E
43-047-39682	UTU-0336	CWU 736-33	2050' FNL 2182' FEL	SWNE Sec. 33 T9S R23E
43-047-39924	UTU-0281	CWU 752-10	882' FSL 350' FWL	SWSW Sec. 10 T9S R22E
43-047-39933	UTU-0285-A	CWU 758-25	2075' FNL 534' FEL	SENE Sec. 25 T9S R22E
43-047-39909	UTU-0285-A	CWU 760-25	1990' FNL 2009' FWL	SENE Sec. 25 T9S R22E
43-047-39904	UTU-0282	CWU 763-14	2531' FNL 1649' FEL	SWNE Sec. 14 T9S R22E
43-047-39690	UTU-010956	CWU 935-25	762' FSL 1453' FWL	SESW Sec. 25 T9S R22E
43-047-39654	UTU-0283-A	CWU 1020-15	2110' FSL 1814' FEL	NWSE Sec. 15 T9S R22E
43-047-39594	UTU-0282	CWU 1062-14	1756' FSL 1853' FWL	NESW Sec. 14 T9S R22E
43-047-39912	UTU-0336-A	CWU 1072-28	2165' FSL 534' FWL	NWSW Sec. 28 T9S R23E
43-047-39186	UTU-010956	CWU 1075-25	627' FSL 412' FEL	SESE Sec. 25 T9S R22E
43-047-39689	UTU-010956	CWU 1080-25	460' FSL 1822' FWL	SESW Sec. 25 T9S R22E
43-047-39678	UTU-010956	CWU 1081-25	461' FSL 445' FWL	SWSW Sec. 25 T9S R22E
43-047-39640	UTU-0337	CWU 1126-29	1864' FNL 2171' FWL	SENE Sec. 29 T9S R23E

Air Drilling Operations:

1. Main Air Compressors are 1250 CFM 350 psi with 2000 psi Boosters and are rig mounted.
2. Secondary Air Compressors are 1170 CFM 350 psi with 2000 psi Boosters and are rig mounted.
3. Minimum setting depth of conductor casing will be 60' GL or 10'± into competent formation, whichever is deeper, as determined by the EOG person in charge. Exceptions must be approved by an EOG drilling superintendent or manager.
4. The diameter of the diverter flow line will be a minimum of 10" to help reduce back pressure on the well bore during uncontrolled flow.
5. Rat and Mouse hole drilling will occur only after surface casing has been set and cemented.
6. EOG Resources, Inc. will use a properly maintained and lubricated stripper head.

VARIANCE REQUESTS:

Reference: Onshore Oil and Gas Order No. 1

Onshore Oil and Gas Order No. 2 – Section E: Special Drilling Operations

1. EOG Resources, Inc. requests a variance to regulations requiring a straight run blooie line to be 100' in length. (Where possible, a straight run blooie line will be used).
2. EOG Resources, Inc. requests a variance to regulations requiring the blooie line to be 100' in length. To reduce location excavation, the blooie line will be approximately 75' in length.
3. EOG Resources, Inc. requests a variance to regulations, during air drilling operations only, requiring dedusting equipment. Dust during air drilling operations is controlled by water mist.
4. EOG Resources, Inc. requests a variance to regulations, during air drilling operations only, requiring an automatic igniter or continuous pilot light on the blooie line. (Not required on aerated water system).
5. EOG Resources, Inc. requests a variance that compressors are located in the opposite direction from the blooie line a minimum of 100 feet from the well bore. (Air Compressors are rig mounted).

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 9

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL OIL WELL ☐ GAS WELL ☒ OTHER _____

2. NAME OF OPERATOR:
EOG Resources, Inc.

3. ADDRESS OF OPERATOR:
1060 East Highway 40 CITY Vernal STATE UT ZIP 84078 PHONE NUMBER: (435) 789-0790

5. LEASE DESIGNATION AND SERIAL NUMBER:
UTU-0337

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:
Chapita Wells Unit

8. WELL NAME and NUMBER:
Chapita Wells Unit 728-29

9. API NUMBER:
43-047-39724

10. FIELD AND POOL, OR WILDCAT:
Natural Buttes

4. LOCATION OF WELL

FOOTAGES AT SURFACE: 608' FNL & 513' FEL 40.012592 LAT 109.343144 LON

COUNTY: Uintah

QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: NENE 29 9S 23E S.L.B. & M.

STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will start: _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLARE
<input type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of work completion: _____	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/RESUME)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: <u>APD EXTENSION REQUEST</u>
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

EOG Resources, Inc. respectfully requests the APD for the referenced well be extended for one year.

Approved by the
Utah Division of
Oil, Gas and Mining

Date: 09-30-08
By: [Signature]

NAME (PLEASE PRINT) Mickenzie Thacker

TITLE Operations Clerk

SIGNATURE

Mickenzie Thacker

DATE 9/22/2008

(This space for State use only)

COPY SENT TO OPERATOR

Date: 10.2.2008

Initials: KS

(5/2000)

(See Instructions on Reverse Side)

RECEIVED

SEP 25 2008

DIV. OF OIL, GAS & MINING

**Application for Permit to Drill
Request for Permit Extension
Validation**

(this form should accompany the Sundry Notice requesting permit extension)

API: 43-047-39724
Well Name: Chapita Wells Unit 728-29
Location: 608 FNL & 513 FEL (NENE), SECTION 29, T9S, R23E S.L.B.&M
Company Permit Issued to: EOG RESOURCES, INC.
Date Original Permit Issued: 10/23/2007

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision.

Following is a checklist of some items related to the application, which should be verified.

If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes ☐ No ☐

Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes ☐ No ☒

Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes ☐ No ☒

Have there been any changes to the access route including ownership, or right-of-way, which could affect the proposed location? Yes ☐ No ☒

Has the approved source of water for drilling changed? Yes ☐ No ☒

Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes ☐ No ☒

Is bonding still in place, which covers this proposed well? Yes ☒ No ☐

Mickie Thacker
Signature

9/22/2008
Date

Title: Operations Clerk

Representing: EOG Resources, Inc.

RECEIVED

SEP 25 2008

DIV. OF OIL, GAS & MINING

DIVISION OF OIL, GAS AND MINING

SPUDDING INFORMATION

Name of Company: EOG RESOURCES INC

Well Name: CWU 728-29

Api No: 43-047-39724 Lease Type: FEDERAL

Section 29 Township 09S Range 23E County UINTAH

Drilling Contractor ROCKY MOUNTAIN DRLG RIG # RATHOLE

SPUDDED:

Date 11/212008

Time 2:30 PM

How DRY

Drilling will Commence: _____

Reported by JERRY BARNES

Telephone # (435) 828-1720

Date 11/24/08 Signed CHD

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 6

ENTITY ACTION FORM

Operator: EOG RESOURCES Operator Account Number: N 9550
Address: 1060 East Highway 40
city VERNAL
state UT zip 84078 Phone Number: (435) 781-9145

Well 1

API Number	Well Name		QQ	Sec	Twp	Rng	County
43-047-39724	CHAPITA WELLS UNIT 728-29		NENE	29	9S	23E	UINTAH
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
A	99999	17221	11/21/2008		11/25/08		
Comments: <u>WASATCH</u>							

Well 2

API Number	Well Name		QQ	Sec	Twp	Rng	County
43-047-40080	CHAPITA WELLS UNIT 1358-24		NWSW	24	9S	22E	UINTAH
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
<u>AB</u>	99999	13650	11/21/2008		11/25/08		
Comments: <u>MESAVERDE</u>							

Well 3

API Number	Well Name		QQ	Sec	Twp	Rng	County
43-047-39725	CHAPITA WELLS UNIT 734-33		NWNE	33	9S	23E	UINTAH
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
A	99999	17222	11/22/2008		11/25/08		
Comments: <u>WASATCH</u>							

ACTION CODES:

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (Explain in 'comments' section)

Mickenzie Thacker

Name (Please Print)

Mickenzie Thacker

Signature

Operations Clerk

11/24/2008

Title

Date

RECEIVED

NOV 24 2008

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0135
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU0337

6. If Indian, Allottee or Tribe Name

7. If Unit or CA/Agreement, Name and/or No.
CHAPITA WELLS

8. Well Name and No.
CHAPITA WELLS UNIT 728-29

9. API Well No.
43-047-39724

10. Field and Pool, or Exploratory
NATURAL BUTTES

11. County or Parish, and State
UINTAH COUNTY, UT

SUBMIT IN TRIPLICATE - Other instructions on reverse side.

1. Type of Well

☐ Oil Well ☒ Gas Well ☐ Other

2. Name of Operator

EOG RESOURCES, INC.

Contact: MICKENZIE THACKER
E-Mail: MICKENZIE_THACKER@EOGRESOURCES.COM

3a. Address

1060 E. HWY 40
VERNAL, UT 84078

3b. Phone No. (include area code)

Ph: 435-781-9145

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Sec 29 T9S R23E NENE 608FNL 513FEL
40.01259 N Lat, 109.34314 W Lon

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Well Spud
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

The referenced well was spud on 11/21/2008.

14. I hereby certify that the foregoing is true and correct.

**Electronic Submission #65036 verified by the BLM Well Information System
For EOG RESOURCES, INC., sent to the Vernal**

Name (Printed/Typed) MICKENZIE THACKER

Title OPERATIONS CLERK

Signature

Mickenzie Thacker

Date 11/24/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved By

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

RECEIVED

**** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ****

NOV 26 2008

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTFORM APPROVED
OMB NO. 1004-0135
Expires: July 31, 2010**SUNDRY NOTICES AND REPORTS ON WELLS****Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.**5. Lease Serial No.
UTU0337

6. If Indian, Allottee or Tribe Name

7. If Unit or CA/Agreement, Name and/or No.
CHAPITA WELLS8. Well Name and No.
CHAPITA WELLS UNIT 728-299. API Well No.
43-047-3972410. Field and Pool, or Exploratory
NATURAL BUTTES11. County or Parish, and State
UINTAH COUNTY, UT**SUBMIT IN TRIPLICATE - Other instructions on reverse side.**

1. Type of Well

☐ Oil Well ☒ Gas Well ☐ Other2. Name of Operator
EOG RESOURCES, INC.Contact: MICKENZIE THACKER
E-Mail: MICKENZIE_THACKER@EOGRESOURCES.COM3a. Address
1060 E. HWY 40
VERNAL, UT 840783b. Phone No. (include area code)
Ph: 453-781-9145

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Sec 29 T9S R23E NENE 608FNL 513FEL
40.01259 N Lat, 109.34314 W Lon

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other Drilling Operations
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

The referenced well reached TD on 2/27/2009, waiting on completion operations to begin.

14. I hereby certify that the foregoing is true and correct.

**Electronic Submission #68186 verified by the BLM Well Information System
For EOG RESOURCES, INC., sent to the Vernal**

Name (Printed/Typed) MICKENZIE THACKER

Title OPERATIONS CLERK

Signature



Date 03/18/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved By

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

**** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ******RECEIVED**
MAR 23 2009

DIV. OF OIL, GAS & MINING

WELL CHRONOLOGY REPORT

Report Generated On: 03-16-2009

Well Name	CWU 728-29	Well Type	DEVG	Division	DENVER
Field	NATURAL BUTTES	API #	43-047-39724	Well Class	COMP
County, State	UINTAH, UT	Spud Date	02-25-2009	Class Date	
Tax Credit	N	TVD / MD	6,890/ 6,890	Property #	061773
Water Depth	0	Last CSG	4.5	Shoe TVD / MD	6,888/ 6,888
KB / GL Elev	5,202/ 5,189				
Location	Section 29, T9S, R23E, NENE, 608 FNL & 513 FEL				

Event No	1.0	Description	DRILL & COMPLETE
Operator	EOG RESOURCES, INC	WI %	0.0
		NRI %	0.0

AFE No	304812	AFE Total	1,231,365	DHC / CWC	553,365/ 678,000
---------------	--------	------------------	-----------	------------------	------------------

Rig Contr	ELENBURG	Rig Name	ELENBURG #28	Start Date	10-30-2007	Release Date	02-28-2009
10-30-2007	Reported By	SHARON CAUDILL					

Daily Costs: Drilling	\$62,040	Completion	\$0	Daily Total	\$62,040
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	0	TVD	0	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0			Perf :			PKR Depth : 0.0				

Activity at Report Time: LOCATION DATA

Start	End	Hrs	Activity Description
--------------	------------	------------	-----------------------------

06:00	06:00	24.0	LOCATION DATA
			608' FNL & 513' FEL (NE/NE)
			SECTION 29, T9S, R23E
			UINTAH COUNTY, UTAH

LAT 40.012592, LONG 109.343144 (NAD 83)
LAT 40.012625, LONG 109.342467 (NAD 27)

ELENBURG #28
OBJECTIVE: 6890' MD/TD, WASATCH
DW/GAS
OBJECTIVE: CHAPITA WELLS PROSPECT
DD&A: NATURAL BUTTES
NATURAL BUTTES FIELD

LEASE: UTU0337
ELEVATION: 5189.4' NAT GL, 5189' PREP GL (DUE TO ROUNDING PREP GL IS 5189'), 5202' KB ('13)

EOG WI %, NRI %

11-24-2008	Reported By	JERRY BARNES
------------	--------------------	--------------

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0		Perf :	PKR Depth : 0.0	

Activity at Report Time: SPUD/WO LOCATION BUILD

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKY MOUNTAIN DRILLING SPUD A 20" HOLE ON 11/21/08 @ 2:30 PM. SET 60' OF 14" CONDUCTOR. CEMENT TO SURFACE WITH READY MIX. JERRY BARNES NOTIFIED CAROL DANIELS W/UDOGM AND MICHAEL LEE W/BLM OF THE SPUD 11/21/08 @ 1:30 PM.

11-25-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0		Perf :	PKR Depth : 0.0	

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	STOCK PILING TOP SOIL AND PUSHING ON LOCATION.

11-26-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0		Perf :	PKR Depth : 0.0	

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION. 30% COMPLETE.

12-01-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0		Perf :	PKR Depth : 0.0	

Activity at Report Time: WO AIR RIG

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION 40% COMPLETE.

12-02-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0		Perf :	PKR Depth : 0.0	

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION. 45% COMPLETE.

12-03-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-04-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-05-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: WO AIR RIG

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT.

12-06-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-09-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-10-2008 Reported By TERRY CSERE

DailyCosts: Drilling \$0 Completion \$0 Daily Total \$0
 Cum Costs: Drilling \$62,040 Completion \$0 Well Total \$62,040
 MD 60 TVD 60 Progress 0 Days 0 MW 0.0 Visc 0.0
 Formation : PBTD : 0.0 Perf : PKR Depth : 0.0
 Activity at Report Time: BUILD LOCATION

Start End Hrs Activity Description
 06:00 06:00 24.0 ROCKED OUT. DRILLING ROCK.

12-11-2008 Reported By TERRY CSERE

DailyCosts: Drilling \$0 Completion \$0 Daily Total \$0
 Cum Costs: Drilling \$62,040 Completion \$0 Well Total \$62,040
 MD 60 TVD 60 Progress 0 Days 0 MW 0.0 Visc 0.0
 Formation : PBTD : 0.0 Perf : PKR Depth : 0.0
 Activity at Report Time: BUILD LOCATION

Start End Hrs Activity Description
 06:00 06:00 24.0 ROCKED OUT.

12-12-2008 Reported By TERRY CSERE

DailyCosts: Drilling \$0 Completion \$0 Daily Total \$0
 Cum Costs: Drilling \$62,040 Completion \$0 Well Total \$62,040
 MD 60 TVD 60 Progress 0 Days 0 MW 0.0 Visc 0.0
 Formation : PBTD : 0.0 Perf : PKR Depth : 0.0
 Activity at Report Time: BUILD LOCATION

Start End Hrs Activity Description
 06:00 06:00 24.0 SHOOTING TODAY.

12-15-2008 Reported By TERRY CSERE

DailyCosts: Drilling \$0 Completion \$0 Daily Total \$0
 Cum Costs: Drilling \$62,040 Completion \$0 Well Total \$62,040
 MD 60 TVD 60 Progress 0 Days 0 MW 0.0 Visc 0.0
 Formation : PBTD : 0.0 Perf : PKR Depth : 0.0
 Activity at Report Time: BUILD LOCATION

Start End Hrs Activity Description
 06:00 06:00 24.0 SHOT FRIDAY.

12-16-2008 Reported By TERRY CSERE

DailyCosts: Drilling \$0 Completion \$0 Daily Total \$0
 Cum Costs: Drilling \$62,040 Completion \$0 Well Total \$62,040
 MD 60 TVD 60 Progress 0 Days 0 MW 0.0 Visc 0.0
 Formation : PBTD : 0.0 Perf : PKR Depth : 0.0
 Activity at Report Time: BUILD LOCATION

Start End Hrs Activity Description
 06:00 06:00 24.0 SHOT FRIDAY.

12-17-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION.

12-18-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	LINE SATURDAY.

12-19-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	LINE SATURDAY.

12-22-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	LOCATION COMPLETE.

01-16-2009 Reported By DANNY FARNSWORTH

Daily Costs: Drilling	\$301,514	Completion	\$0	Daily Total	\$301,514
Cum Costs: Drilling	\$363,554	Completion	\$0	Well Total	\$363,554
MD	2,335	TVD	2,335	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0		

Activity at Report Time: WORT

Start	End	Hrs	Activity Description
-------	-----	-----	----------------------

06:00 06:00 24.0 MIRU CRAIGS DRILLING RIG #3 ON 01/08/2009. DRILLED 12-1/4" HOLE TO 2322' GL (2335' KB). ENCOUNTERED NO WATER. FLUID DRILLED HOLE FROM 1672'. LOST RETURNS @ 1900'. RAN 53 JTS (2314.98') OF 9-5/8", 36.0#, J-55, ST&C CASING WITH HALLIBURTON GUIDE SHOE AND FLOAT COLLAR. 8 CENTRALIZERS SPACED MIDDLE OF SHOE JOINT AND EVERY COLLAR TILL GONE. LANDED @ 2327' KB. RDMO CRAIGS RIG.

MIRU HALLIBURTON CEMENTERS. HELD SAFETY MEETING. PRESSURE TESTED LINES AND CEMENT VALVE TO 1150 PSIG. PUMPED 178 BBLS FRESH WATER & 20 BBLS GELLED WATER FLUSH AHEAD OF CEMENT. MIXED & PUMPED 400 SX (84 BBLS) OF PREMIUM CEMENT W/2 % CACL2. MIXED CEMENT @ 15.6 PPG W/YIELD OF 1.18 CF/SX. DISPLACED CEMENT W/175 BBLS FRESH WATER. BUMPED PLUG W/780# @ 8:23 AM, 1/14/2009. CHECKED FLOAT, FLOAT HELD. SHUT-IN CASING VALVE. NO RETURNS.

TOP JOB # 1: MIXED & PUMPED 100 SX (20.5 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. NO RETURNS. WOC 4 HRS 7 MINUTES.

TOP JOB # 2: MIXED & PUMPED 100 SX (20.5 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. NO RETURNS. WOC 2 HRS 10 MINUTES.

TOP JOB # 3: MIXED & PUMPED 75 SX (15.4 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. HOLE FILLED AND STOOD FULL. RDMO HALLIBURTON CEMENTERS

PREPARED LOCATION FOR ROTARY RIG. WORT. WILL DROP FROM REPORT UNTIL FURTHER ACTIVITY.

CRAIGS RIG 3 RAN SURVEYS @ 1200'= 0.25 DEGREE & 2100'= 1.5 DEGREE.

CONDUCTOR LEVEL RECORD: PS= 89.9 OPS= 89.9 VDS= 89.9 MS= 90.0.

9 5/8 CASING LEVEL RECORD: PS= 89.9 OPS= 89.9 VDS= 89.9 MS= 89.9

DAN FARNSWORTH EMAILED NOTIFICATION TO BLM OF THE SURFACE CASING & CEMENT JOB ON 01/09/2009 @ 11:30 AM.

02-25-2009		Reported By		DAVID FOREMAN							
Daily Costs: Drilling		\$86,659		Completion		\$578		Daily Total		\$87,237	
Cum Costs: Drilling		\$450,213		Completion		\$578		Well Total		\$450,791	
MD	2,335	TVD	2,335	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :			PBTD : 0.0			Perf :			PKR Depth : 0.0		

Activity at Report Time: PREPARE TO SPUD

Start	End	Hrs	Activity Description
06:00	10:00	4.0	SAFETY MEETING W/ ALL PERSONNEL.MOVE W/ HOWCROFT .8 MILE (ON THE CWU 723-28, INSTALL NIGHT CAP W/ FMC TRIP TO FMC OFFICE AND RETURN INSTALL NEW SEAL ASSEMBLY TEST TO 5000 PSI. GOOD TEST).
10:00	13:00	3.0	RIG UP ON NEW LOC. CWU 728-29 SET BOP TEST DTO HEAD TO 5000 PSI. W/ FMC LOCK DOWN BOP, CONTINUE RIGING UP.
13:00	17:00	4.0	NIPPLE UP BOP. FLARE LINES, FUNCTION TEST SAME. RIG ON DAY WORK @ 13:00 HRS, 2/24/09.
17:00	22:00	5.0	RIG UP B&C QUICK TEST & TEST BOP PIPE RAMS, BLIND RAMS, ALL KILL LINE VALVES, CHOKE LINE MANIFOLD VALVES, HCR,UPPER & LOWER TIW VALVES,SAFETY VALVE,DART VALVE,ALL TO 250 PSI LOW & 5000 PSI HIGH, ANNULAR 250 PSI LOW 2500 HIGH, SURFACE CSG.1500 PSI GOOD TEST. WITNESS BY BLM REP. CLADE RICH & ROBERT PICKERING B&C QUICK TEST. 2/24/09 NOTIFIED BLM. E-MAIL.

22:00 22:30 0.5 RIG DOWN B&C QUICK TEST. ACCIDENTLY OPENED SLIPS DROPPED TEST JT. IN HOLE.
 22:30 00:00 1.5 PICK UP DRILL PIPE TRIP IN HOLE F/ FISH TAG @ 2265'.
 00:00 01:00 1.5 FISHING. SCREW IN FISH. PRESSURE UP STOP PUMP. ROTATE DOWN TIGHTEN TOOL JT. CIRC. TAG BOTTOM!
 PRESSURE UP. PICK UP, BACK DOWN TAG TO CHECK FISH. TOOH W/ FISH L/D SAME.
 01:30 05:00 3.5 INSTALL WEAR BUSHING, P/U MOTOR M/U BIT TRIP IN W/ BHA & D/P. TAG @ 2299' INSTALL ROTATING
 HEAD.
 05:00 05:30 0.5 DRILL CEMENT/FLOAT EQUIP. F/ 2299' TO 2337' = 10' FORMATION.
 05:30 06:00 0.5 CIRC. & FIT TEST 260 PSI, 8.9 MWT = 11. EMW. GOOD TEST

BOILER 12 HRS.

MUD LOSS LAST 24 HRS. 0 BBLS.

ACCIDENTS NONE REPORTED
 TEST CROWN-O-MATIC.

SET & FUCTION

SAFETY MEETING: FALL ARREST: PPE.

CREWS FULL.

FUEL ON HAND: 5882 GALS. USED 518 GALS. REC. 6400.

FORMATION TOP: GREENRIVER.

02-26-2009 **Reported By** DAVID FOREMAN

Daily Costs: Drilling	\$26,262	Completion	\$0	Daily Total	\$26,262
Cum Costs: Drilling	\$476,476	Completion	\$578	Well Total	\$477,054

MD 5,574 **TVD** 5,574 **Progress** 3,239 **Days** 1 **MW** 8.7 **Visc** 33.0

Formation : **PBTD : 0.0** **Perf :** **PKR Depth : 0.0**

Activity at Report Time: DRILLING @ 5574'

Start	End	Hrs	Activity Description
06:00	10:00	4.0	DRILL ROTATE F/ 2335' TO 2902' 561' ROP 140' WOB 12/16 RPM 40/46 MUD WT. 9. VIS. 35. BOP DRILL 1 MIN.
10:00	10:30	0.5	SURVEY @ 2778' 1 1/2 DEG.
10:30	20:30	10.0	DRILL ROTATE F/ 2902' TO 4397' 1495' ROP 149.5' WOB 10/12 RPM 40/47 MUD WT. 9.2 VIS. 34.
20:30	21:00	0.5	CIRC. & SURVEY @ 4304' 2 3/4 DEG.
21:00	06:00	9.0	DRILL ROTATE F/ 4397' TO 5574' 1177' ROP 130.7' WOB 12/16 RPM 45/55 MUD WT. 9.7 VIS. 35.

BOILER 24 HRS.

ACCIDENTS NONE REPORTED

FUNCTION TEST CROWN-O-MATIC.

SAFETY MEETING: TEAM WORK : WORK AREA SAFETY.

CREWS FULL.

FUEL ON HAND: 4538 GALS. USED 1344 GALS.

FORMATION TOP: CHAPITA WELLS

06:00 SPUD 7 7/8" HOLE W/ROTARY TOOLS AT 06:00 HRS, 2/25/09.

02-27-2009 **Reported By** DAVID FOREMAN

Daily Costs: Drilling	\$41,922	Completion	\$472	Daily Total	\$42,394
Cum Costs: Drilling	\$518,399	Completion	\$1,050	Well Total	\$519,449

MD 6,890 **TVD** 6,890 **Progress** 1,316 **Days** 2 **MW** 10.3 **Visc** 35.0

Formation : PBTB : 0.0 Perf : PKR Depth : 0.0

Activity at Report Time: CIRCULATE

Start	End	Hrs	Activity Description
06:00	10:30	4.5	DRILL ROTATE F/ 5574' TO 5937' 563' ROP 90.75 WOB 16/20 RPM 45/30 MUD WT. 10.3 VIS. 33.
10:30	11:00	0.5	SERVICE RIG
11:00	03:00	16.0	DRILL ROTATE F/ 5937' TO 6890' 953' ROP 59.5' WOB 18/20 RPM 45/60 MUD WT. 10.8 VIS 36. REACHED TD AT @ 03:00 HRS, 2/27/09.
03:00	04:00	1.0	CIRC CLEAN F/ SHORT TRIP.
04:00	05:00	1.0	SHORT TRIP.
05:00	06:00	1.0	CIRC COND HOLE F/ CASING.

BOILER 24 HRS.

ACCIDENTS NONE REPORTED
CROWN-O-MATIC.

FICTION TEST

SAFETY MEETING: MIX CHEM. : TRIPS.

CREWS FULL.

FUEL ON HAND: 2836 GALS. USED 1700 GALS.

FORMATION TOP: PRICE RIVER/ TD

02-28-2009		Reported By		DAVID FOREMAN	
Daily Costs: Drilling	\$37,839	Completion	\$161,028	Daily Total	\$198,867
Cum Costs: Drilling	\$556,239	Completion	\$162,078	Well Total	\$718,317
MD	6,890	TVD	6,890	Progress	0
		Days	3	MW	0.0
		Visc	0.0		

Formation : PBTB : 0.0 Perf : PKR Depth : 0.0

Activity at Report Time: ND BOP

Start	End	Hrs	Activity Description
06:00	07:00	1.0	CIRC. CLEAN, SLUG PIPE, DROP SURVEY. NOTIFIED BLM F/ CASING RUN & CEMENTING 2/27/09.
07:00	14:00	7.0	LAY DOWN DRILL PIPE & BHA, PULL WEAR BUSHING. START L/D DP @ 07:00 2/27/09.
14:00	15:30	1.5	RIG UP CALIBER CSG. TO RUN CASING, & SAFETY MEETING W/ ALL PERSONNEL.
15:30	22:30	7.0	RUN CASING 4 1/2 RAN 156 JTS. P-110 LTC + 2 MARKER JT. 11.6# P-110 LTC & 1 PUP P-110 LTC. AS FOLLOWS: FLOAT SHOE, 1 JT CSG, FLOAT COLLAR, 13 JTS CSG, 1 MARKER JT, 47 JTSCSG, 1 MARKER JT, 95 JTS CSG, 1 PUP JT. DTO HANGER ASS. LANDING JT. FLOAT SHOE @ 6888', FLOAT COLLAR TOP @ 6841' MARKER JT. @ 6247' & @ 4172' CENTRALIZERS, 5 FT. ABOVE SHOE, TOP OF JT #2 & EVERY 3 TH. JT. TOTAL 15 .TAG @ 6890' LAY DOWN TAG JT. PICK UP HANGER SPACE OUT CIRC. CSG W/ RIG PUMP. RIG DOWN CALIBER CASING. LAND CSG. W/ FULL STRING WT. 74.000, WITNESS BY FMC REP.
22:30	00:00	1.5	CIRC. W/O HALLIBURTON. ARRIVED ON LOCATION AT 00:00 HR. HALLIBURTON WAS CALLED AT 09:00 AM. AND PUT ON STANDBY F/ CEMENT JOB, AND AT 14:00 PM. TO BE ON LOCATION AT 20:00 HR. CALLED AT 20:15 TO CONFIRM THE TIME TO BE ON LOCATION. SOME ONE DROPPED THE BALL NO CALL OUT ORDERS.
00:00	02:00	2.0	SAFETY MEETING W/ HALLIBURTON AND RIG UP TO PUMP CEMENT.

02:00 03:30 1.5 TEST LINES 3500 PSI. DROP BOTTOM PLUG PUMP 20 BBLs WATER SPACER & 20 BBLs. MUD FLUSH AHEAD. AND CEMENT 6890' 4 1/2 P-110 11.6# LTC CSG. LEAD 460 SKS. Highbond 75 WITH 4% BENTONITE, 0.3% VERSASET. 15# TURR FIBER IN FIRST 50 BBL MIXED @ 12. PPB. YIELD 1.84 FT³/SK H2O 9.86 GAL/SK. TAIL 730 SKS, EXTENDACEM WITH 0.125# POLYFLAKE/SK. @ 13.5 PPG. YIELD 1.47 FT³/SK H2O 6.88 GAL/SK. SHUTDOWN WASH OUT PUMPS & LINES DROP TOP PLUG & DISP. TO FLOAT COLLAR W/ FRESH WATER. 107 BBLs. AVG. DISP. RATE 7 BPM FULL RETURNS THROUGH OUT JOB. DROP PLUG @ 03:15 BUMPED PLUG @ 03:34 TO 3000 PSI. 1250 PSI. OVER LIFT PRESS. HOLD PRESS. F/2 MINS. 1.25 BBL. BACK, FLOAT HELD. @ 03:36 CEMENT IN PLACE. RIG DOWN HALLIBURTON LINES.

03:30 04:00 0.5 WAIT ON CEMENT & CLEAN PITS.

04:00 05:00 1.0 REMOVE CEMENT HEAD & LANDING JT. M/U & LAND PACKOFF TEST 5000 PSI. LOOSEN DTO LOCK DOWN BOLTS W/ FMC.

05:00 06:00 1.0 NIPPLE DOWN BOP & FINISH CLEAN PIT.

HOWCROFT TRUCKING TO BE ON LOCATION @ 07:00 2/28/09. & MOVE RIG .8 MILES TO NEW LOCATION CWU 729-29.

BOILER 24 HRS.

MUD MOVED 400 BBLs TO CWU 729-29.

ACCIDENTS NONE REPORTED.

FUNCTION TEST CROWN-O-MATIC.

SAFETY MEETING: RUN CSG. : PINCH POINTS.

CREWS FULL.

FUEL ON HAND: 1755 GALS. USED 1081 GALS.

03-01-2009 **Reported By** DAVID FOREMAN

Daily Costs: Drilling	\$11,439	Completion	\$0	Daily Total	\$11,439
Cum Costs: Drilling	\$567,678	Completion	\$162,078	Well Total	\$729,756

MD 6,890 **TVD** 6,890 **Progress** 0 **Days** 4 **MW** 0.0 **Visc** 0.0

Formation : **PBTD :** 0.0 **Perf :** **PKR Depth :** 0.0

Activity at Report Time: RDRT/WO COMPLETION

Start	End	Hrs	Activity Description
06:00	09:00	3.0	NIPPLE DOWN BOP, CLEAN PITS.
06:00			RELEASE RIG @ 09:00 HRS, 2/28/09.
			CASING POINT COST \$551,630

03-06-2009 **Reported By** SEARLE

Daily Costs: Drilling	\$0	Completion	\$36,300	Daily Total	\$36,300
Cum Costs: Drilling	\$567,678	Completion	\$198,378	Well Total	\$766,056

MD 6,890 **TVD** 6,890 **Progress** 0 **Days** 5 **MW** 0.0 **Visc** 0.0

Formation : **PBTD :** 6842.0 **Perf :** **PKR Depth :** 0.0

Activity at Report Time: PREP FOR FRACS

Start	End	Hrs	Activity Description
06:00			MIRU SCHLUMBERGER. LOG WITH RST/CBL/CCL/VDL/GR FROM PBTD TO 290'. EST CEMENT TOP @ 700'. RD SCHLUMBERGER.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0135
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU0337

6. If Indian, Allottee or Tribe Name

SUBMIT IN TRIPLICATE - Other instructions on reverse side.

7. If Unit or CA/Agreement, Name and/or No.
CHAPITA WELLS

8. Well Name and No.
CHAPITA WELLS UNIT 728-29

9. API Well No.
43-047-39724

10. Field and Pool, or Exploratory
NATURAL BUTTES

11. County or Parish, and State
UINTAH COUNTY, UT

1. Type of Well
☐ Oil Well ☒ Gas Well ☐ Other

2. Name of Operator
EOG RESOURCES, INC. Contact: MICKENZIE THACKER
E-Mail: MICKENZIE_THACKER@EOGRESOURCES.COM

3a. Address
1060 E. HWY 40
VERNAL, UT 84078

3b. Phone No. (include area code)
Ph: 453-781-9145

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
Sec 29 T9S R23E NENE 608FNL 513FEL
40.01259 N Lat, 109.34314 W Lon

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Drilling Operations
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

Waiting on completion operations. Please see the attached well chronology.

14. I hereby certify that the foregoing is true and correct.
**Electronic Submission #69602 verified by the BLM Well Information System
For EOG RESOURCES, INC., sent to the Vernal**

Name (Printed/Typed) MICKENZIE THACKER

Title OPERATIONS CLERK

Signature

Mickenzie Thacker

Date 04/29/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved By

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

**** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED**

RECEIVED

MAY 04 2009

DIV. OF OIL, GAS & MINING

WELL CHRONOLOGY REPORT

Report Generated On: 04-28-2009

Well Name	CWU 728-29	Well Type	DEVG	Division	DENVER
Field	NATURAL BUTTES	API #	43-047-39724	Well Class	COMP
County, State	UINTAH, UT	Spud Date	02-25-2009	Class Date	
Tax Credit	N	TVD / MD	6,890/ 6,890	Property #	061773
Water Depth	0	Last CSG	4.5	Shoe TVD / MD	6,888/ 6,888
KB / GL Elev	5,202/ 5,189				
Location	Section 29, T9S, R23E, NENE, 608 FNL & 513 FEL				

Event No	1.0	Description	DRILL & COMPLETE		
Operator	EOG RESOURCES, INC	WI %	100.0	NRI %	82.25

AFE No	304812	AFE Total	1,231,365	DHC / CWC	553,365/ 678,000
Rig Contr	ELENBURG	Rig Name	ELENBURG #28	Start Date	10-30-2007
10-30-2007	Reported By	SHARON CAUDILL			
Daily Costs: Drilling	\$62,040	Completion	\$0	Daily Total	\$62,040
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	0	TVD	0	Progress	0
Days	0	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0		Perf :	PKR Depth : 0.0	

Activity at Report Time: LOCATION DATA

Start	End	Hrs	Activity Description
06:00	06:00	24.0	LOCATION DATA
			608' FNL & 513' FEL (NE/NE)
			SECTION 29, T9S, R23E
			UINTAH COUNTY, UTAH
			LAT 40.012592, LONG 109.343144 (NAD 83)
			LAT 40.012625, LONG 109.342467 (NAD 27)
			ELENBURG #28
			OBJECTIVE: 6890' MD/TD, WASATCH
			DW/GAS
			OBJECTIVE: CHAPITA WELLS PROSPECT
			DD&A: NATURAL BUTTES
			NATURAL BUTTES FIELD
			LEASE: UTU0337
			ELEVATION: 5189.4' NAT GL, 5189' PREP GL (DUE TO ROUNDING PREP GL IS 5189'), 5202' KB ('13)
			EOG WI 100%, NRI 82.25%
			EOG APO WI 50%, NRI 43.50%

11-24-2008	Reported By	JERRY BARNES
-------------------	--------------------	--------------

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	SPUD/WO LOCATION BUILD				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKY MOUNTAIN DRILLING SPUD A 20" HOLE ON 11/21/08 @ 2:30 PM. SET 60' OF 14" CONDUCTOR. CEMENT TO SURFACE WITH READY MIX. JERRY BARNES NOTIFIED CAROL DANIELS W/UDOGM AND MICHAEL LEE W/BLM OF THE SPUD 11/21/08 @ 1:30 PM.

11-25-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	BUILD LOCATION				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	STOCK PILING TOP SOIL AND PUSHING ON LOCATION.

11-26-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	BUILD LOCATION				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION. 30% COMPLETE.

12-01-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	WO AIR RIG				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION 40% COMPLETE.

12-02-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	BUILD LOCATION				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION. 45% COMPLETE.

12-03-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTBTD : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: BUILD LOCATION											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.								

12-04-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTBTD : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: BUILD LOCATION											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.								

12-05-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTBTD : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: WO AIR RIG											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	ROCKED OUT.								

12-06-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTBTD : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: BUILD LOCATION											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.								

12-09-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTBTD : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: BUILD LOCATION											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.								

12-10-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
				Days	0
MW					0.0
Visc					0.0
Formation :	PBTB : 0.0			Perf :	PKR Depth : 0.0
Activity at Report Time: BUILD LOCATION					
Start	End	Hrs	Activity Description		
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.		

12-11-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
				Days	0
MW					0.0
Visc					0.0
Formation :	PBTB : 0.0			Perf :	PKR Depth : 0.0
Activity at Report Time: BUILD LOCATION					
Start	End	Hrs	Activity Description		
06:00	06:00	24.0	ROCKED OUT.		

12-12-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
				Days	0
MW					0.0
Visc					0.0
Formation :	PBTB : 0.0			Perf :	PKR Depth : 0.0
Activity at Report Time: BUILD LOCATION					
Start	End	Hrs	Activity Description		
06:00	06:00	24.0	SHOOTING TODAY.		

12-15-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
				Days	0
MW					0.0
Visc					0.0
Formation :	PBTB : 0.0			Perf :	PKR Depth : 0.0
Activity at Report Time: BUILD LOCATION					
Start	End	Hrs	Activity Description		
06:00	06:00	24.0	SHOT FRIDAY.		

12-16-2008 Reported By TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
				Days	0
MW					0.0
Visc					0.0
Formation :	PBTB : 0.0			Perf :	PKR Depth : 0.0
Activity at Report Time: BUILD LOCATION					
Start	End	Hrs	Activity Description		
06:00	06:00	24.0	SHOT FRIDAY.		

12-17-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTB : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: BUILD LOCATION											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	PUSHING ON LOCATION.								

12-18-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTB : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: BUILD LOCATION											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	LINE SATURDAY.								

12-19-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTB : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: BUILD LOCATION											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	LINE SATURDAY.								

12-22-2008		Reported By		TERRY CSERE							
DailyCosts: Drilling		\$0		Completion		\$0		Daily Total		\$0	
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040	
MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTB : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: BUILD LOCATION											
Start	End	Hrs	Activity Description								
06:00	06:00	24.0	LOCATION COMPLETE.								

01-16-2009		Reported By		DANNY FARNSWORTH							
DailyCosts: Drilling		\$301,514		Completion		\$0		Daily Total		\$301,514	
Cum Costs: Drilling		\$363,554		Completion		\$0		Well Total		\$363,554	
MD	2,335	TVD	2,335	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :		PBTB : 0.0				Perf :		PKR Depth : 0.0			
Activity at Report Time: WORT											
Start	End	Hrs	Activity Description								

06:00 06:00 24.0 MIRU CRAIGS DRILLING RIG #3 ON 01/08/2009. DRILLED 12-1/4" HOLE TO 2322' GL (2335' KB). ENCOUNTERED NO WATER. FLUID DRILLED HOLE FROM 1672'. LOST RETURNS @ 1900'. RAN 53 JTS (2314.08') OF 9-5/8", 36.0#, J-55, ST&C CASING WITH HALLIBURTON GUIDE SHOE AND FLOAT COLLAR. 8 CENTRALIZERS SPACED MIDDLE OF SHOE JOINT AND EVERY COLLAR TILL GONE. LANDED @ 2327' KB. RDMO CRAIGS RIG.

MIRU HALLIBURTON CEMENTERS. HELD SAFETY MEETING. PRESSURE TESTED LINES AND CEMENT VALVE TO 1150 PSIG. PUMPED 178 BBLS FRESH WATER & 20 BBLS GELLED WATER FLUSH AHEAD OF CEMENT. MIXED & PUMPED 400 SX (84 BBLS) OF PREMIUM CEMENT W/2 % CACL2. MIXED CEMENT @ 15.6 PPG W/YIELD OF 1.18 CF/SX. DISPLACED CEMENT W/175 BBLS FRESH WATER. BUMPED PLUG W/780# @ 8:23 AM, 1/14/2009. CHECKED FLOAT, FLOAT HELD. SHUT-IN CASING VALVE. NO RETURNS.

TOP JOB # 1: MIXED & PUMPED 100 SX (20.5 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. NO RETURNS. WOC 4 HRS 7 MINUTES.

TOP JOB # 2: MIXED & PUMPED 100 SX (20.5 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. NO RETURNS. WOC 2 HRS 10 MINUTES.

TOP JOB # 3: MIXED & PUMPED 75 SX (15.4 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. HOLE FILLED AND STOOD FULL. RDMO HALLIBURTON CEMENTERS

PREPARED LOCATION FOR ROTARY RIG. WORT. WILL DROP FROM REPORT UNTIL FURTHER ACTIVITY.

CRAIGS RIG 3 RAN SURVEYS @ 1200' = 0.25 DEGREE & 2100' = 1.5 DEGREE.

CONDUCTOR LEVEL RECORD: PS= 89.9 OPS= 89.9 VDS= 89.9 MS= 90.0.

9 5/8 CASING LEVEL RECORD: PS= 89.9 OPS= 89.9 VDS= 89.9 MS= 89.9

DAN FARNSWORTH EMAILED NOTIFICATION TO BLM OF THE SURFACE CASING & CEMENT JOB ON 01/09/2009 @ 11:30 AM.

02-25-2009 Reported By DAVID FOREMAN

Daily Costs: Drilling	\$86,659	Completion	\$578	Daily Total	\$87,237
Cum Costs: Drilling	\$450,213	Completion	\$578	Well Total	\$450,791

MD	2,335	TVD	2,335	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	-------	------------	-------	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: PREPARE TO SPUD

Start	End	Hrs	Activity Description
06:00	10:00	4.0	SAFETY MEETING W/ ALL PERSONNEL. MOVE W/ HOWCROFT .8 MILE (ON THE CWU 723-28, INSTALL NIGHT CAP W/ FMC TRIP TO FMC OFFICE AND RETURN INSTALL NEW SEAL ASSEMBLY TEST TO 5000 PSI. GOOD TEST).
10:00	13:00	3.0	RIG UP ON NEW LOC. CWU 728-29 SET BOP TEST DTO HEAD TO 5000 PSI. W/ FMC LOCK DOWN BOP, CONTINUE RIGGING UP.
13:00	17:00	4.0	NIPPLE UP BOP. FLARE LINES, FUNCTION TEST SAME. RIG ON DAY WORK @ 13:00 HRS, 2/24/09.
17:00	22:00	5.0	RIG UP B&C QUICK TEST & TEST BOP PIPE RAMS, BLIND RAMS, ALL KILL LINE VALVES, CHOKE LINE MANIFOLD VALVES, HCR, UPPER & LOWER TIW VALVES, SAFETY VALVE, DART VALVE, ALL TO 250 PSI LOW & 5000 PSI HIGH, ANNULAR 250 PSI LOW 2500 HIGH, SURFACE CSG. 1500 PSI GOOD TEST. WITNESS BY BLM REP. CLADE RICH & ROBERT PICKERING B&C QUICK TEST. 2/24/09 NOTIFIED BLM. E-MAIL.

22:00 22:30 0.5 RIG DOWN B&C QUICK TEST. ACCIDENTLY OPENED SLIPS DROPPED TEST JT. IN HOLE.
 22:30 00:00 1.5 PICK UP DRILL PIPE TRIP IN HOLE F/ FISH TAG @ 2265'.
 00:00 01:30 1.5 FISHING. SCREW IN FISH PRESSURE UP STOP PUMP. ROTATE DOWN TIGHTEN TOOL JT. ,CIRC.TAG BOTTOM PRESSURE UP. PICK UP,BACK DOWN TAG TO CHECK FISH.TOOH W/ FISH L/D SAME.
 01:30 05:00 3.5 INSTALL WEAR BUSHING, P/U MOTOR M/U BIT TRIP IN W/ BHA & D/P.TAG @ 2299' INSTALL ROTATING HEAD.
 05:00 05:30 0.5 DRILL CEMENT/FLOAT EQUIP.F/ 2299' TO 2337' = 10' FORMATION.
 05:30 06:00 0.5 CIRC. & FIT TEST 260 PSI, 8.9 MWT = 11. EMW. GOOD TEST

BOILER 12 HRS.

MUD LOSS LAST 24 HRS. 0 BBLs.

ACCIDENTS NONE REPORTED
 TEST CROWN-O-MATIC.

SET & FUCTION

SAFETY MEETING: FALL ARREST: PPE.

CREWS FULL.

FUEL ON HAND: 5882 GALS. USED 518 GALS.REC. 6400.

FORMATION TOP: GREENRIVER.

02-26-2009 **Reported By** DAVID FOREMAN

DailyCosts: Drilling	\$26,262	Completion	\$0	Daily Total	\$26,262
Cum Costs: Drilling	\$476,476	Completion	\$578	Well Total	\$477,054

MD 5,574 **TVD** 5,574 **Progress** 3,239 **Days** 1 **MW** 8.7 **Visc** 33.0

Formation : **PBTD : 0.0** **Perf :** **PKR Depth : 0.0**

Activity at Report Time: DRILLING @ 5574'

Start	End	Hrs	Activity Description
06:00	10:00	4.0	DRILL ROTATE F/ 2335' TO 2902' 561' ROP 140' WOB 12/16 RPM 40/46 MUD WT. 9. VIS. 35. BOP DRILL 1 MIN.
10:00	10:30	0.5	SURVEY @ 2778' 1 1/2 DEG.
10:30	20:30	10.0	DRILL ROTATE F/ 2902' TO 4397' 1495' ROP 149.5' WOB 10/12 RPM 40/47 MUD WT. 9.2 VIS. 34.
20:30	21:00	0.5	CIRC. & SURVEY @ 4304' 2 3/4 DEG.
21:00	06:00	9.0	DRILL ROTATE F/ 4397' TO 5574' 1177' ROP 130.7' WOB 12/16 RPM 45/55 MUD WT. 9.7 VIS. 35.

BOILER 24 HRS.

ACCIDENTS NONE REPORTED

FUNCTION TEST CROWN-O-MATIC.

SAFETY MEETING: TEAM WORK : WORK AREA SAFETY.

CREWS FULL.

FUEL ON HAND: 4538 GALS. USED 1344 GALS.

FORMATION TOP: CHAPITA WELLS

06:00 SPUD 7 7/8" HOLE W/ROTARY TOOLS AT 06:00 HRS, 2/25/09.

02-27-2009 **Reported By** DAVID FOREMAN

DailyCosts: Drilling	\$41,922	Completion	\$472	Daily Total	\$42,394
Cum Costs: Drilling	\$518,399	Completion	\$1,050	Well Total	\$519,449

MD 6,890 **TVD** 6,890 **Progress** 1,316 **Days** 2 **MW** 10.3 **Visc** 35.0

Formation : PBTB : 0.0 Perf : PKR Depth : 0.0

Activity at Report Time: CIRCULATE

Start	End	Hrs	Activity Description
06:00	10:30	4.5	DRILL ROTATE F/ 5574' TO 5937' 363' ROP 90.75 WOB 16/20 RPM 45/50 MUD WT. 10.3 VIS. 35.
10:30	11:00	0.5	SERVICE RIG
11:00	03:00	16.0	DRILL ROTATE F/ 5937' TO 6890' 953' ROP 59.5' WOB 18/20 RPM 45/60 MUD WT. 10.8 VIS 36. REACHED TD AT @ 03:00 HRS, 2/27/09.
03:00	04:00	1.0	CIRC CLEAN F/ SHORT TRIP.
04:00	05:00	1.0	SHORT TRIP.
05:00	06:00	1.0	CIRC COND HOLE F/ CASING.

BOILER 24 HRS.

ACCIDENTS NONE REPORTED
CROWN-O-MATIC.

FUCTION TEST

SAFETY MEETING: MIX CHEM. : TRIPS.

CREWS FULL.

FUEL ON HAND: 2836 GALS. USED 1700 GALS.

FORMATION TOP: PRICE RIVER/ TD

02-28-2009		Reported By		DAVID FOREMAN	
Daily Costs: Drilling	\$37,839	Completion	\$161,028	Daily Total	\$198,867
Cum Costs: Drilling	\$556,239	Completion	\$162,078	Well Total	\$718,317
MD	6,890	TVD	6,890	Progress	0
Days	3	MW	0.0	Visc	0.0

Formation : PBTB : 0.0 Perf : PKR Depth : 0.0

Activity at Report Time: ND BOP

Start	End	Hrs	Activity Description
06:00	07:00	1.0	CIRC. CLEAN, SLUG PIPE, DROP SURVEY. NOTIFIED BLM F/ CASING RUN & CEMENTING 2/27/09.
07:00	14:00	7.0	LAY DOWN DRILL PIPE & BHA, PULL WEAR BUSHING. START L/D DP @ 07:00 2/27/09.
14:00	15:30	1.5	RIG UP CALIBER CSG. TO RUN CASING, & SAFETY MEETING W/ ALL PERSONNEL.
15:30	22:30	7.0	RUN CASING 4 1/2 RAN 156 JTS.P-110 LTC + 2 MARKER JT. 11.6# P-110 LTC & 1 PUP P-110 LTC. AS FOLLOWS: FLOAT SHOE, 1 JT CSG, FLOAT COLLAR, 13 JTS CSG, 1 MARKER JT, 47 JTSCSG, 1 MARKER JT, 95 JTS CSG, 1 PUP JT. DTO HANGER ASS. LANDING JT. FLOAT SHOE @ 6888', FLOAT COLLAR TOP @ 6841' MARKER JT. @ 6247' & @ 4172' CENTRALIZERS, 5 FT. ABOVE SHOE, TOP OF JT #2 & EVERY 3 TH. JT. TOTAL 15 .TAG @ 6890' LAY DOWN TAG JT. PICK UP HANGER SPACE OUT CIRC. CSG W/ RIG PUMP. RIG DOWN CALIBER CASING. LAND CSG. W/ FULL STRING WT. 74.000, WITNESS BY FMC REP.
22:30	00:00	1.5	CIRC. W/O HALLIBURTON. ARRIVED ON LOCATION AT 00:00 HR. HALLIBURTON WAS CALLED AT 09:00 AM. AND PUT ON STANDBY F/ CEMENT JOB, AND AT 14:00 PM. TO BE ON LOCATION AT 20:00 HR. CALLED AT 20:15 TO CONFIRM THE TIME TO BE ON LOCATION. SOME ONE DROPPED THE BALL NO CALL OUT ORDERS.
00:00	02:00	2.0	SAFETY MEETING W/ HALLIBURTON AND RIG UP TO PUMP CEMENT.

02:00 03:30 1.5 TEST LINES 3500 PSI. DROP BOTTOM PLUG PUMP 20 BBLs WATER SPACER & 20 BBLs. MUD FLUSH AHEAD. AND CEMENT 6890' 4 1/2 P-110 11.6# LTC CSG. LEAD 460 SKS. HIGHBOND 75 WITH 4% BENTONITE, 0.3% VERSASET. 15# TURR FIBER IN FIRST 50 BBL MIXED @ 12. PPB. YIELD 1.84 FT³/SK H₂O 9.86 GAL/SK. TAIL 730 SKS, EXTENDACEM WITH 0.125# POLYFLAKE/SK. @ 13.5 PPG. YIELD 1.47 FT³/SK H₂O 6.88 GAL/SK. SHUTDOWN WASH OUT PUMPS & LINES DROP TOP PLUG & DISP. TO FLOAT COLLER W/ FRESH WATER. 107 BBLs. AVG. DISP. RATE 7 BPM FULL RETURNS THROUGH OUT JOB. DROP PLUG @ 03:15 BUMPED PLUG @ 03:34 TO 3000 PSI. 1250 PSI. OVER LIFT PRESS. HOLD PRESS. F/2 MINS. 1.25 BBL. BACK, FLOAT HELD. @ 03:36 CEMENT IN PLACE. RIG DOWN HALLIBURTON LINES.

03:30 04:00 0.5 WAIT ON CEMENT & CLEAN PITS.

04:00 05:00 1.0 REMOVE CEMENT HEAD & LANDING JT.M/U & LAND PACKOFF TEST 5000 PSI. LOOSEN DTO LOCK DOWN BOLTS W/ FMC.

05:00 06:00 1.0 NIPPLE DOWN BOP & FINISH CLEAN PIT.

HOWCROFT TRUCKING TO BE ON LOCATION @ 07:00 2/28/09. & MOVE RIG .8 MILES TO NEW LOCATION CWU 729-29.

BOILER 24 HRS.

MUD MOVED 400 BBLs TO CWU 729-29.

ACCIDENTS NONE REPORTED.

FUNCTION TEST CROWN-O-MATIC.

SAFETY MEETING: RUN CSG. : PINCH POINTS.

CREWS FULL.

FUEL ON HAND: 1755 GALS. USED 1081 GALS.

03-01-2009 Reported By DAVID FOREMAN

Daily Costs: Drilling	\$11,439	Completion	\$0	Daily Total	\$11,439
Cum Costs: Drilling	\$567,678	Completion	\$162,078	Well Total	\$729,756
MD	6,890	TVD	6,890	Progress	0
Days	4	MW	0.0	Visc	0.0
Formation :	PBTD : 0.0		Perf :	PKR Depth : 0.0	

Activity at Report Time: RDRT/NO COMPLETION

Start	End	Hrs	Activity Description
-------	-----	-----	----------------------

06:00	09:00	3.0	NIPPLE DOWN BOP, CLEAN PITS.
-------	-------	-----	------------------------------

06:00	RELEASE RIG @ 09:00 HRS, 2/28/09.		
-------	-----------------------------------	--	--

CASING POINT COST \$551,630

03-06-2009 Reported By SEARLE

Daily Costs: Drilling	\$0	Completion	\$36,300	Daily Total	\$36,300
Cum Costs: Drilling	\$567,678	Completion	\$198,378	Well Total	\$766,056
MD	6,890	TVD	6,890	Progress	0
Days	5	MW	0.0	Visc	0.0
Formation :	PBTD : 6842.0		Perf :	PKR Depth : 0.0	

Activity at Report Time: PREP FOR FRACS

Start	End	Hrs	Activity Description
-------	-----	-----	----------------------

06:00	06:00	24.0	MIRU SCHLUMBERGER. LOG WITH RST/CBL/CCL/VDL/GR FROM PBTD TO 290'. EST CEMENT TOP @ 700'. RD SCHLUMBERGER.
-------	-------	------	---

<div>STATE OF UTAH</div> <div>DEPARTMENT OF NATURAL RESOURCES</div> <div>DIVISION OF OIL, GAS, AND MINING</div>		<div>FORM 9</div> <div>5.LEASE DESIGNATION AND SERIAL NUMBER: UTU0337</div>	
<div>SUNDRY NOTICES AND REPORTS ON WELLS</div> <div>Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.</div>		<div>6. IF INDIAN, ALLOTTEE OR TRIBE NAME:</div> <div>7.UNIT or CA AGREEMENT NAME: CHAPITA WELLS</div>	
<div>1. TYPE OF WELL</div> <div>Gas Well</div>		<div>8. WELL NAME and NUMBER:</div> <div>CWU 728-29</div>	
<div>2. NAME OF OPERATOR:</div> <div>EOG Resources, Inc.</div>		<div>9. API NUMBER:</div> <div>43047397240000</div>	
<div>3. ADDRESS OF OPERATOR:</div> <div>1060 East Highway 40 , Vernal, UT, 84078</div>		<div>PHONE NUMBER:</div> <div>435 781-9111 Ext</div>	
<div>4. LOCATION OF WELL</div> <div>FOOTAGES AT SURFACE:</div> <div>0608 FNL 0513 FEL</div> <div>QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN:</div> <div>Qtr/Qtr: NENE Section: 29 Township: 09.0S Range: 23.0E Meridian: S</div>		<div>9. FIELD and POOL or WILDCAT:</div> <div>NATURAL BUTTES</div>	
		<div>COUNTY:</div> <div>UINTAH</div>	
		<div>STATE:</div> <div>UTAH</div>	
<div>11.</div> <div>CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA</div>			
<div>TYPE OF SUBMISSION</div>		<div>TYPE OF ACTION</div>	
<div><input type="checkbox"/> NOTICE OF INTENT</div> <div>Approximate date work will start:</div> <div><input type="checkbox"/> SUBSEQUENT REPORT</div> <div>Date of Work Completion:</div> <div><input type="checkbox"/> SPUD REPORT</div> <div>Date of Spud:</div> <div><input checked="" type="checkbox"/> DRILLING REPORT</div> <div>Report Date:</div> <div>5/29/2009</div>		<div><input type="checkbox"/> ACIDIZE</div> <div><input type="checkbox"/> CHANGE TO PREVIOUS PLANS</div> <div><input type="checkbox"/> CHANGE WELL STATUS</div> <div><input type="checkbox"/> DEEPEN</div> <div><input type="checkbox"/> OPERATOR CHANGE</div> <div><input type="checkbox"/> PRODUCTION START OR RESUME</div> <div><input type="checkbox"/> REPERFORATE CURRENT FORMATION</div> <div><input type="checkbox"/> TUBING REPAIR</div> <div><input type="checkbox"/> WATER SHUTOFF</div> <div><input type="checkbox"/> WILDCAT WELL DETERMINATION</div> <div><input type="checkbox"/> ALTER CASING</div> <div><input type="checkbox"/> CHANGE TUBING</div> <div><input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS</div> <div><input type="checkbox"/> FRACTURE TREAT</div> <div><input type="checkbox"/> PLUG AND ABANDON</div> <div><input type="checkbox"/> RECLAMATION OF WELL SITE</div> <div><input type="checkbox"/> SIDETRACK TO REPAIR WELL</div> <div><input type="checkbox"/> VENT OR FLARE</div> <div><input type="checkbox"/> SI TA STATUS EXTENSION</div> <div><input type="checkbox"/> OTHER</div> <div><input type="checkbox"/> CASING REPAIR</div> <div><input type="checkbox"/> CHANGE WELL NAME</div> <div><input type="checkbox"/> CONVERT WELL TYPE</div> <div><input type="checkbox"/> NEW CONSTRUCTION</div> <div><input type="checkbox"/> PLUG BACK</div> <div><input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION</div> <div><input type="checkbox"/> TEMPORARY ABANDON</div> <div><input type="checkbox"/> WATER DISPOSAL</div> <div><input type="checkbox"/> APD EXTENSION</div> <div>OTHER: </div>	
<div>12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.</div> <div>Completion operations are scheduled to begin on or about 6/9/2009.</div> <div>Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY</div> <div>June 01, 2009</div>			
<div>NAME (PLEASE PRINT)</div> <div>Kaylene Gardner</div>		<div>PHONE NUMBER</div> <div>435 781-9111</div>	
<div>SIGNATURE</div> <div>N/A</div>		<div>TITLE</div> <div>Regulatory Administrator</div>	
		<div>DATE</div> <div>5/29/2009</div>	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0337
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: EOG Resources, Inc.		7. UNIT or CA AGREEMENT NAME: CHAPITA WELLS
3. ADDRESS OF OPERATOR: 1060 East Highway 40 , Vernal, UT, 84078		8. WELL NAME and NUMBER: CWU 728-29
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0608 FNL 0513 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENE Section: 29 Township: 09.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047397240000
PHONE NUMBER: 435 781-9111 Ext		9. FIELD and POOL or WILDCAT: NATURAL BUTTES
COUNTY: UTAH		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 6/20/2009	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE TUBING	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER	
	OTHER:	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. The referenced well was turned to sales on 6/20/2009. Please see the attached operations summary report for drilling and completion operations performed on the subject well.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY June 29, 2009		
NAME (PLEASE PRINT) Mickenzie Thacker	PHONE NUMBER 435 781-9145	TITLE Operations Clerk
SIGNATURE N/A	DATE 6/26/2009	

WELL CHRONOLOGY REPORT

Report Generated On: 06-26-2009

Well Name	CWU 728-29	Well Type	DEVG	Division	DENVER
Field	CHAPITA WELLS UNIT	API #	43-047-39724	Well Class	1SA
County, State	UINTAH, UT	Spud Date	02-25-2009	Class Date	06-20-2009
Tax Credit	N	TVD / MD	6,890/ 6,890	Property #	061773
Water Depth	0	Last CSG	2.375	Shoe TVD / MD	0/ 0
KB / GL Elev	5,202/ 5,189				
Location	Section 29, T9S, R23E, NENE, 608 FNL & 513 FEL				

Event No	1.0	Description	DRILL & COMPLETE		
Operator	EOG RESOURCES, INC	WI %	100.0	NRI %	82.25

AFE No		304812		AFE Total		1,231,365		DHC / CWC		553,365/ 678,000													
Rig Contr		ELENBURG		Rig Name		ELENBURG #28		Start Date		10-30-2007		Release Date		02-28-2009									
10-30-2007		Reported By		SHARON CAUDILL																			
DailyCosts: Drilling		\$62,040		Completion		\$0		Daily Total		\$62,040													
Cum Costs: Drilling		\$62,040		Completion		\$0		Well Total		\$62,040													
MD		0		TVD		0		Progress		0		Days		0		MW		0.0		Visc		0.0	
Formation :				PBTD : 0.0				Perf :				PKR Depth : 0.0											

Activity at Report Time: LOCATION DATA

Start	End	Hrs	Activity Description
-------	-----	-----	----------------------

06:00	06:00	24.0	LOCATION DATA
-------	-------	------	---------------

608' FNL & 513' FEL (NE/NE)

SECTION 29, T9S, R23E

UINTAH COUNTY, UTAH

LAT 40.012592, LONG 109.343144 (NAD 83)

LAT 40.012625, LONG 109.342467 (NAD 27)

ELENBURG #28

OBJECTIVE: 6890' MD/TD, WASATCH

DW/GAS

OBJECTIVE: CHAPITA WELLS PROSPECT

DD&A: NATURAL BUTTES

NATURAL BUTTES FIELD

LEASE: UTU0337

ELEVATION: 5189.4' NAT GL, 5189' PREP GL (DUE TO ROUNDING PREP GL IS 5189'), 5202' KB ('13)

EOG WI 100%, NRI 82.25%

EOG APO WI 50%, NRI 43.50%

11-24-2008	Reported By	JERRY BARNES
------------	-------------	--------------

RECEIVED June 26, 2009

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	SPUD/WO LOCATION BUILD				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKY MOUNTAIN DRILLING SPUD A 20" HOLE ON 11/21/08 @ 2:30 PM. SET 60' OF 14" CONDUCTOR. CEMENT TO SURFACE WITH READY MIX. JERRY BARNES NOTIFIED CAROL DANIELS W/UDOGM AND MICHAEL LEE W/BLM OF THE SPUD 11/21/08 @ 1:30 PM.

11-25-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	BUILD LOCATION				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	STOCK PILING TOP SOIL AND PUSHING ON LOCATION.

11-26-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	BUILD LOCATION				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION. 30% COMPLETE.

12-01-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	WO AIR RIG				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION 40% COMPLETE.

12-02-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040
MD	60	TVD	60	Progress	0
Formation :		PBTD : 0.0		Perf :	
Activity at Report Time:	BUILD LOCATION				

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION. 45% COMPLETE.

12-03-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-04-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-05-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: WO AIR RIG

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT.

12-06-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-09-2008 **Reported By** TERRY CSERE

Daily Costs: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-10-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT. DRILLING ROCK.

12-11-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	ROCKED OUT.

12-12-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	SHOOTING TODAY.

12-15-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	SHOT FRIDAY.

12-16-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	SHOT FRIDAY.

12-17-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	PUSHING ON LOCATION.

12-18-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	LINE SATURDAY.

12-19-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	LINE SATURDAY.

12-22-2008 **Reported By** TERRY CSERE

DailyCosts: Drilling	\$0	Completion	\$0	Daily Total	\$0
Cum Costs: Drilling	\$62,040	Completion	\$0	Well Total	\$62,040

MD	60	TVD	60	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	----	------------	----	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: BUILD LOCATION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	LOCATION COMPLETE.

01-16-2009 **Reported By** DANNY FARNSWORTH

DailyCosts: Drilling	\$301,514	Completion	\$0	Daily Total	\$301,514
Cum Costs: Drilling	\$363,554	Completion	\$0	Well Total	\$363,554

MD	2,335	TVD	2,335	Progress	0	Days	0	MW	0.0	Visc	0.0
-----------	-------	------------	-------	-----------------	---	-------------	---	-----------	-----	-------------	-----

Formation :	PBTD : 0.0	Perf :	PKR Depth : 0.0
--------------------	-------------------	---------------	------------------------

Activity at Report Time: WORT

Start	End	Hrs	Activity Description
--------------	------------	------------	-----------------------------

06:00 06:00 24.0 MIRU CRAIGS DRILLING RIG #3 ON 01/08/2009. DRILLED 12-1/4" HOLE TO 2322' GL (2335' KB). ENCOUNTERED NO WATER. FLUID DRILLED HOLE FROM 1672'. LOST RETURNS @ 1900'. RAN 53 JTS (2314.08') OF 9-5/8", 36.0#, J-55, ST&C CASING WITH HALLIBURTON GUIDE SHOE AND FLOAT COLLAR. 8 CENTRALIZERS SPACED MIDDLE OF SHOE JOINT AND EVERY COLLAR TILL GONE. LANDED @ 2327' KB. RDMO CRAIGS RIG .

MIRU HALLIBURTON CEMENTERS. HELD SAFETY MEETING. PRESSURE TESTED LINES AND CEMENT VALVE TO 1150 PSIG. PUMPED 178 BBLS FRESH WATER & 20 BBLS GELLED WATER FLUSH AHEAD OF CEMENT. MIXED & PUMPED 400 SX (84 BBLS) OF PREMIUM CEMENT W/2 % CACL2. MIXED CEMENT @ 15.6 PPG W/YIELD OF 1.18 CF/SX. DISPLACED CEMENT W/175 BBLS FRESH WATER. BUMPED PLUG W/780# @ 8: 23 AM, 1/14/2009. CHECKED FLOAT, FLOAT HELD. SHUT-IN CASING VALVE. NO RETURNS.

TOP JOB # 1: MIXED & PUMPED 100 SX (20.5 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. NO RETURNS. WOC 4 HRS 7 MINUTES.

TOP JOB # 2: MIXED & PUMPED 100 SX (20.5 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. NO RETURNS. WOC 2 HRS 10 MINUTES.

TOP JOB # 3: MIXED & PUMPED 75 SX (15.4 BBLS) OF PREMIUM CEMENT W/3% CACL2. MIXED CEMENT @ 15.8 PPG W/YIELD OF 1.15 CF/SX. HOLE FILLED AND STOOD FULL. RDMO HALLIBURTON CEMENTERS

PREPARED LOCATION FOR ROTARY RIG. WORT. WILL DROP FROM REPORT UNTIL FURTHER ACTIVITY.

CRAIGS RIG 3 RAN SURVEYS @ 1200' = 0.25 DEGREE & 2100' = 1.5 DEGREE.

CONDUCTOR LEVEL RECORD: PS= 89.9 OPS= 89.9 VDS= 89.9 MS= 90.0.
9 5/8 CASING LEVEL RECORD: PS= 89.9 OPS= 89.9 VDS= 89.9 MS= 89.9

DAN FARNSWORTH EMAILED NOTIFICATION TO BLM OF THE SURFACE CASING & CEMENT JOB ON 01/09/2009 @ 11:30 AM.

02-25-2009		Reported By		DAVID FOREMAN							
Daily Costs: Drilling		\$86,659		Completion		\$578		Daily Total		\$87,237	
Cum Costs: Drilling		\$450,213		Completion		\$578		Well Total		\$450,791	
MD	2,335	TVD	2,335	Progress	0	Days	0	MW	0.0	Visc	0.0
Formation :			PBTD : 0.0			Perf :			PKR Depth : 0.0		
Activity at Report Time: PREPARE TO SPUD											
Start	End	Hrs	Activity Description								
06:00	10:00	4.0	SAFETY MEETING W/ ALL PERSONNEL.MOVE W/ HOWCROFT .8 MILE (ON THE CWU 723-28, INSTALL NIGHT CAP W/ FMC TRIP TO FMC OFFICE AND RETURN INSTALL NEW SEAL ASSEMBLY TEST TO 5000 PSI. GOOD TEST).								
10:00	13:00	3.0	RIG UP ON NEW LOC. CWU 728-29 SET BOP TEST DTO HEAD TO 5000 PSI. W/ FMC LOCK DOWN BOP, CONTINUE RIGING UP.								
13:00	17:00	4.0	NIPPLE UP BOP. FLARE LINES, FUNCTION TEST SAME. RIG ON DAY WORK @ 13:00 HRS, 2/24/09.								
17:00	22:00	5.0	RIG UP B&C QUICK TEST & TEST BOP PIPE RAMS, BLIND RAMS, ALL KILL LINE VALVES, CHOKE LINE MANIFOLD VALVES, HCR,UPPER & LOWER TIW VALVES,SAFETY VALVE,DART VALVE,ALL TO 250 PSI LOW & 5000 PSI HIGH, ANNULAR 250 PSI LOW 2500 HIGH, SURFACE CSG.1500 PSI GOOD TEST. WITNESS BY BLM REP. CLADE RICH & ROBERT PICKERING B&C QUICK TEST. 2/24/09 NOTIFIED BLM. E-MAIL.								

22:00	22:30	0.5 RIG DOWN B&C QUICK TEST. ACCIDENTLY OPENED SLIPS DROPPED TEST JT. IN HOLE.
22:30	00:00	1.5 PICK UP DRILL PIPE TRIP IN HOLE F/ FISH TAG @ 2265'.
00:00	01:30	1.5 FISHING. SCREW IN FISH PRESSURE UP STOP PUMP. ROTATE DOWN TIGHTEN TOOL JT. ,CIRC.TAG BOTTOM PRESSURE UP. PICK UP,BACK DOWN TAG TO CHECK FISH.TOOH W/ FISH L/D SAME.
01:30	05:00	3.5 INSTALL WEAR BUSHING, P/U MOTOR M/U BIT TRIP IN W/ BHA & D/P.TAG @ 2299' INSTALL ROTATING HEAD.
05:00	05:30	0.5 DRILL CEMENT/FLOAT EQUIP.F/ 2299' TO 2337' = 10' FORMATION.
05:30	06:00	0.5 CIRC. & FIT TEST 260 PSI, 8.9 MWT = 11. EMW. GOOD TEST

BOILER 12 HRS.

MUD LOSS LAST 24 HRS. 0 BBLs.

ACCIDENTS NONE REPORTED
TEST CROWN-O-MATIC.

SET & FUCTION

SAFETY MEETING: FALL ARREST: PPE.

CREWS FULL.

FUEL ON HAND: 5882 GALS. USED 518 GALS.REC. 6400.

FORMATION TOP: GREENRIVER.

02-26-2009	Reported By	DAVID FOREMAN									
DailyCosts: Drilling	\$26,262	Completion	\$0	Daily Total	\$26,262						
Cum Costs: Drilling	\$476,476	Completion	\$578	Well Total	\$477,054						
MD	5,574	TVD	5,574	Progress	3,239	Days	1	MW	8.7	Visc	33.0
Formation :	PBTD : 0.0			Perf :	PKR Depth : 0.0						
Activity at Report Time: DRILLING @ 5574'											

Start	End	Hrs	Activity Description
06:00	10:00	4.0	DRILL ROTATE F/ 2335' TO 2902' 561' ROP 140' WOB 12/16 RPM 40/46 MUD WT. 9. VIS. 35. BOP DRILL 1 MIN.
10:00	10:30	0.5	SURVEY @ 2778' 1 1/2 DEG.
10:30	20:30	10.0	DRILL ROTATE F/ 2902' TO 4397' 1495' ROP 149.5' WOB 10/12 RPM 40/47 MUD WT. 9.2 VIS. 34.
20:30	21:00	0.5	CIRC. & SURVEY @ 4304' 2 3/4 DEG.
21:00	06:00	9.0	DRILL ROTATE F/ 4397' TO 5574' 1177' ROP 130.7' WOB 12/16 RPM 45/55 MUD WT. 9.7 VIS. 35.

BOILER 24 HRS.

ACCIDENTS NONE REPORTED

FUNCTION TEST CROWN-O-MATIC.

SAFETY MEETING: TEAM WORK : WORK AREA SAFETY.

CREWS FULL.

FUEL ON HAND: 4538 GALS. USED 1344 GALS.

FORMATION TOP: CHAPITA WELLS

06:00	SPUD 7 7/8" HOLE W/ROTARY TOOLS AT 06:00 HRS, 2/25/09.
-------	--

02-27-2009	Reported By	DAVID FOREMAN									
DailyCosts: Drilling	\$41,922	Completion	\$472	Daily Total	\$42,394						
Cum Costs: Drilling	\$518,399	Completion	\$1,050	Well Total	\$519,449						
MD	6,890	TVD	6,890	Progress	1,316	Days	2	MW	10.3	Visc	35.0

Formation : **PBTD : 0.0** **Perf :** **PKR Depth : 0.0**

Activity at Report Time: CIRCULATE

Start	End	Hrs	Activity Description
06:00	10:30	4.5	DRILL ROTATE F/ 5574' TO 5937' 363' ROP 90.75 WOB 16/20 RPM 45/50 MUD WT. 10.3 VIS. 35.
10:30	11:00	0.5	SERVICE RIG
11:00	03:00	16.0	DRILL ROTATE F/ 5937' TO 6890' 953' ROP 59.5' WOB 18/20 RPM 45/60 MUD WT. 10.8 VIS 36. REACHED TD AT @ 03:00 HRS, 2/27/09.
03:00	04:00	1.0	CIRC CLEAN F/ SHORT TRIP.
04:00	05:00	1.0	SHORT TRIP.
05:00	06:00	1.0	CIRC COND HOLE F/ CASING.

BOILER 24 HRS.

ACCIDENTS NONE REPORTED
CROWN-O-MATIC.

FUCTION TEST

SAFETY MEETING: MIX CHEM. : TRIPS.

CREWS FULL.

FUEL ON HAND: 2836 GALS. USED 1700 GALS.

FORMATION TOP: PRICE RIVER/ TD

02-28-2009 **Reported By** DAVID FOREMAN

DailyCosts: Drilling \$37,839 **Completion** \$161,028 **Daily Total** \$198,867

Cum Costs: Drilling \$556,239 **Completion** \$162,078 **Well Total** \$718,317

MD 6,890 **TVD** 6,890 **Progress** 0 **Days** 3 **MW** 0.0 **Visc** 0.0

Formation : **PBTD : 0.0** **Perf :** **PKR Depth : 0.0**

Activity at Report Time: ND BOP

Start	End	Hrs	Activity Description
06:00	07:00	1.0	CIRC. CLEAN,SLUG PIPE, DROP SURVEY. NOTIFIED BLM F/ CASING RUN & CEMENTING 2/27/09.
07:00	14:00	7.0	LAY DOWN DRILL PIPE & BHA, PULL WEAR BUSHING. START L/D DP @ 07:00 2/27/09.
14:00	15:30	1.5	RIG UP CALIBER CSG. TO RUN CASING, & SAFETY MEETING W/ ALL PERSONNEL.
15:30	22:30	7.0	RUN CASING 4 1/2 RAN 156 JTS.P-110 LTC + 2 MARKER JT. 11.6# P-110 LTC & 1 PUP P-110 LTC. AS FOLLOWS: FLOAT SHOE, 1 JT CSG, FLOAT COLLAR, 13 JTS CSG, 1 MARKER JT, 47 JTSCSG, 1 MARKER JT, 95 JTS CSG, 1 PUP JT. DTO HANGER ASS. LANDING JT. FLOAT SHOE @ 6888', FLOAT COLLAR TOP @ 6841' MARKER JT. @ 6247' & @ 4172' CENTRALIZERS, 5 FT. ABOVE SHOE, TOP OF JT #2 & EVERY 3 TH. JT. TOTAL 15 .TAG @ 6890' LAY DOWN TAG JT. PICK UP HANGER SPACE OUT CIRC. CSG W/ RIG PUMP. RIG DOWN CALIBER CASING. LAND CSG. W/ FULL STRING WT. 74,000, WITNESS BY FMC REP.
22:30	00:00	1.5	CIRC. W/O HALLIBURTON.ARRIVED ON LOCATION AT 00:00 HR. HALLIBURTON WAS CALLED AT 09:00 AM. AND PUT ON STANDBY F/ CEMENT JOB, AND AT 14:00 PM. TO BE ON LOCATION AT 20:00 HR. CALLED AT 20:15 TO CONFIRM THE TIME TO BE ON LOCATION. SOME ONE DROPPED THE BALL NO CALL OUT ORDERS.
00:00	02:00	2.0	SAFETY MEETING W/ HALLIBURTON AND RIG UP TO PUMP CEMENT.

02:00 03:30 1.5 TEST LINES 3500 PSI. DROP BOTTOM PLUG PUMP 20 BBLs WATER SPACER & 20 BBLs. MUD FLUSH AHEAD. AND CEMENT 6890' 4 1/2 P-110 11.6# LTC CSG. LEAD 460 SKS. Highbond 75 WITH 4% BENTONITE, 0.3% VERSASET. 15# TURR FIBER IN FIRST 50 BBL MIXED @ 12. PPB. YIELD 1.84 FT³/SK H₂O 9.86 GAL/SK. TAIL 730 SKS, EXTENDACEM WITH 0.125# POLYFLAKE/SK. @ 13.5 PPG. YIELD 1.47 FT³/SK H₂O 6.88 GAL/SK. SHUTDOWN WASH OUT PUMPS & LINES DROP TOP PLUG & DISP. TO FLOAT COLLAR W/ FRESH WATER. 107 BBLs. AVG. DISP. RATE 7 BPM FULL RETURNS THROUGH OUT JOB. DROP PLUG @ 03:15 BUMPED PLUG @ 03:34 TO 3000 PSI. 1250 PSI. OVER LIFT PRESS. HOLD PRESS. F/2 MINS. 1.25 BBL. BACK, FLOAT HELD. @ 03:36 CEMENT IN PLACE. RIG DOWN HALLIBURTON LINES.

03:30 04:00 0.5 WAIT ON CEMENT & CLEAN PITS.

04:00 05:00 1.0 REMOVE CEMENT HEAD & LANDING JT. M/U & LAND PACKOFF TEST 5000 PSI. LOOSEN DTO LOCK DOWN BOLTS W/ FMC.

05:00 06:00 1.0 NIPPLE DOWN BOP & FINISH CLEAN PIT.

HOWCROFT TRUCKING TO BE ON LOCATION @ 07:00 2/28/09. & MOVE RIG .8 MILES TO NEW LOCATION CWU 729-29.

BOILER 24 HRS.

MUD MOVED 400 BBLs TO CWU 729-29.

ACCIDENTS NONE REPORTED.

FUNCTION TEST CROWN-O-MATIC.

SAFETY MEETING: RUN CSG. : PINCH POINTS.

CREWS FULL.

FUEL ON HAND: 1755 GALS. USED 1081 GALS.

03-01-2009 **Reported By** DAVID FOREMAN

Daily Costs: Drilling \$11,439 **Completion** \$0 **Daily Total** \$11,439

Cum Costs: Drilling \$567,678 **Completion** \$162,078 **Well Total** \$729,756

MD 6,890 **TVD** 6,890 **Progress** 0 **Days** 4 **MW** 0.0 **Visc** 0.0

Formation : **PBTD : 0.0** **Perf :** **PKR Depth : 0.0**

Activity at Report Time: RDRT/NO COMPLETION

Start **End** **Hrs** **Activity Description**

06:00 09:00 3.0 NIPPLE DOWN BOP, CLEAN PITS.

06:00 RELEASE RIG @ 09:00 HRS, 2/28/09.

CASING POINT COST \$551,630

03-06-2009 **Reported By** SEARLE

Daily Costs: Drilling \$0 **Completion** \$36,300 **Daily Total** \$36,300

Cum Costs: Drilling \$567,678 **Completion** \$198,378 **Well Total** \$766,056

MD 6,890 **TVD** 6,890 **Progress** 0 **Days** 5 **MW** 0.0 **Visc** 0.0

Formation : **PBTD : 6842.0** **Perf :** **PKR Depth : 0.0**

Activity at Report Time: PREP FOR FRACS

Start **End** **Hrs** **Activity Description**

06:00 06:00 24.0 MIRU SCHLUMBERGER. LOG WITH RST/CBL/CCL/VDL/GR FROM PBTD TO 290'. EST CEMENT TOP @ 700'. RD SCHLUMBERGER.

06-05-2009 **Reported By** MCCURDY

Daily Costs: Drilling \$0 **Completion** \$1,448 **Daily Total** \$1,448

Cum Costs: Drilling \$567,678 **Completion** \$199,826 **Well Total** \$767,504

MD 6,890 TVD 6,890 Progress 0 Days 6 MW 0.0 Visc 0.0

Formation : PBTD : 6842.0 Perf : PKR Depth : 0.0

Activity at Report Time: WO COMPLETION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	NU 10M FRAC TREE. PRESSURE TESTED FRAC TREE & CASING TO 6500 PSIG. WO COMPLETION.

06-09-2009 Reported By MCCURDY

Daily Costs: Drilling	\$0	Completion	\$668	Daily Total	\$668
Cum Costs: Drilling	\$567,678	Completion	\$200,494	Well Total	\$768,172

MD 6,890 TVD 6,890 Progress 0 Days 7 MW 0.0 Visc 0.0

Formation : WASATCH PBTD : 6842.0 Perf : 5949'-6670' PKR Depth : 0.0

Activity at Report Time: FRAC

Start	End	Hrs	Activity Description
06:00	06:00	24.0	RU CUTTERS WIRELINE & PERFORATE Ba/NORTH HORN FROM 6334'-35', 6390'-91', 6451'-52', 6506'-07', 6513'-14', 6545'-46', 6557'-60', 6572'-73', 6578'-79', 6669'-70' @ 3 SPF @ 1200 PHASING. RDWL. RU HALLIBURTON, FRAC DOWN CASING W/ 42 GAL K-87 MICROBIOCIDE, 165 GAL GYPTRON T-106, 8454 GAL 16# LINEAR W/11100# 20/40 SAND @ 1-1.5 PPG, 34801 GAL 16# DELTA 140 W/115900# 20/40 SAND @ 2-4 PPG. MTP 5650 PSIG. MTR 51.7 BPM. ATP 4462 PSIG. ATR 49.7 BPM. ISIP 2547 PSIG. RD HALLIBURTON.

RUWL. SET 6K CFP AT 6240'. PERFORATE Ba FROM 5949'-50', 5988'-89', 5996'-97', 6036'-37', 6061'-63', 6111'-12', 6133'-34', 6149'-50', 6174'-76', 6213'-14' @ 3 SPF @ 1200 PHASING. RDWL. RU HALLIBURTON, FRAC DOWN CASING W/42 GAL K-87 MICROBIOCIDE, 8522 GAL 16# LINEAR W/11160# 20/40 SAND @ 1-1.5 PPG, 22210 GAL 16# DELTA 140 W/71540# 20/40 SAND @ 2-4 PPG. MTP 6630 PSIG. MTR 52.5 BPM. ATP 4483 PSIG. ATR 49.5 BPM. ISIP 2595 PSIG. RD HALLIBURTON. SDFN.

06-10-2009 Reported By MCCURDY

Daily Costs: Drilling	\$0	Completion	\$117,491	Daily Total	\$117,491
Cum Costs: Drilling	\$567,678	Completion	\$317,985	Well Total	\$885,663

MD 6,890 TVD 6,890 Progress 0 Days 8 MW 0.0 Visc 0.0

Formation : WASATCH PBTD : 6842.0 Perf : 5068'-6670' PKR Depth : 0.0

Activity at Report Time: PREP TO MIRUSU

Start	End	Hrs	Activity Description
06:00	06:00	24.0	SICP 1430 PSIG. RUWL. SET 6K CFP AT 5880'. PERFORATE Ca/Ba FROM 5540'-43', 5591'-93', 5620'-21', 5632'-33', 5639'-40', 5687'-88', 5722'-23', 5768'-69', 5858'-59' @ 3 SPF @ 1200 PHASING. RDWL. RU HALLIBURTON, FRAC DOWN CASING W/ 42 GAL K-87 MICROBIOCIDE, 9547 GAL 16# LINEAR W/12700# 20/40 SAND @ 1-1.5 PPG, 19072 GAL 16# DELTA 140 W/61400# 20/40 SAND @ 2-4 PPG. MTP 4433 PSIG. MTR 52.3 BPM. ATP 3363 PSIG. ATR 48.6 BPM. ISIP 1450 PSIG. RD HALLIBURTON.

RUWL. SET 6K CFP AT 5380'. PERFORATE Pp/Ca FROM 5068'-70', 5077'-79', 5089'-90', 5097'-98', 5183'-85', 5188'-89', 5194'-95', 5232'-33', 5349'-50' @ 3 SPF @ 1200 PHASING. RDWL. RU HALLIBURTON, FRAC DOWN CASING W/42 GAL K-87 MICROBIOCIDE GAL 16# LINEAR W/3836# 20/40 SAND @ 1.5 PPG, 36150 GAL 16# DELTA 140 W/124700# 20/40 SAND @ 2-4 PPG. MTP 4292 PSIG. MTR 51.4 BPM. ATP 3444 PSIG. ATR 49.5 BPM. ISIP 1714 PSIG. RD HALLIBURTON.

RUWL. SET 6K CBP AT 5046'. RDWL.

06-16-2009 Reported By BAUSCH

Daily Costs: Drilling	\$0	Completion	\$61,759	Daily Total	\$61,759
Cum Costs: Drilling	\$567,678	Completion	\$379,744	Well Total	\$947,422

MD 6,890 TVD 6,890 Progress 0 Days 9 MW 0.0 Visc 0.0

Formation : WASATCH **PBTD :** 6842.0 **Perf :** 5068'-6670' **PKR Depth :** 0.0

Activity at Report Time: CLEAN OUT AFTER FRAC

Start	End	Hrs	Activity Description
07:00	15:00	8.0	MIRUSU. ND FRAC VALVES. NU BOP. RIH W/BIT & PUMP OFF BIT SUB TO CBP @ 4985'. RU TO DRILL OUT PLUGS. SDFN.

06-17-2009 **Reported By** BAUSCH

DailyCosts: Drilling	\$0	Completion	\$7,450	Daily Total	\$7,450						
Cum Costs: Drilling	\$567,678	Completion	\$387,194	Well Total	\$954,872						
MD	6,890	TVD	6,890	Progress	0	Days	10	MW	0.0	Visc	0.0

Formation : WASATCH **PBTD :** 6775.0 **Perf :** 5068'-6670' **PKR Depth :** 0.0

Activity at Report Time: FLOW TEST

Start	End	Hrs	Activity Description
07:00	06:00	23.0	CLEANED OUT & DRILLED OUT PLUGS @ 4985', 5380', 5880' & 6240'. RIH. CLEANED OUT TO 6775'. LANDED TBG AT 5033' KB. ND BOPE. NU TREE. PUMPED OFF BIT & SUB. RDMOSU.

FLOWED 14 HRS. NO CHOKE. FTP 0 PSIG. CP 0 PSIG. 13 BFPH. RECOVERED 214 BLW. 3728 BLWTR.

TUBING DETAIL LENGTH

PUMP OFF SUB 1.00'

1 JT 2-3/8" 4.7# N-80 TBG 32.69'

XN NIPPLE 1.30'

153 JTS 2-3/8 4.7# N-80 TBG 4984.52'

BELOW KB 13.00'

LANDED @ 5032.51' KB

06-18-2009 **Reported By** BAUSCH

DailyCosts: Drilling	\$0	Completion	\$1,800	Daily Total	\$1,800						
Cum Costs: Drilling	\$567,678	Completion	\$388,994	Well Total	\$956,672						
MD	6,890	TVD	6,890	Progress	0	Days	11	MW	0.0	Visc	0.0

Formation : WASATCH **PBTD :** 6775.0 **Perf :** 5068'-6670' **PKR Depth :** 0.0

Activity at Report Time: FLOW TEST

Start	End	Hrs	Activity Description
06:00	06:00	24.0	FLOWED 24 HRS ON 32/64" CHOKE. FTP 300 PSIG. SICP 1100 PSIG. 37 BFPH. RECOVERED 876 BLW. 2852 BLWTR.

06-19-2009 **Reported By** BAUSCH

DailyCosts: Drilling	\$0	Completion	\$1,800	Daily Total	\$1,800						
Cum Costs: Drilling	\$567,678	Completion	\$390,794	Well Total	\$958,472						
MD	6,890	TVD	6,890	Progress	0	Days	12	MW	0.0	Visc	0.0

Formation : WASATCH **PBTD :** 6775.0 **Perf :** 5068'-6670' **PKR Depth :** 0.0

Activity at Report Time: FLOW TEST

Start	End	Hrs	Activity Description
06:00	06:00	24.0	FLOWED 24 HRS. 32/64" CHOKE. FTP 350 PSIG. CP 1050 PSIG. 35 BFPH. RECOVERED 842 BLW. 2010 BLWTR.

06-20-2009 **Reported By** BAUSCH

DailyCosts: Drilling	\$0	Completion	\$1,800	Daily Total	\$1,800
Cum Costs: Drilling	\$567,678	Completion	\$392,594	Well Total	\$960,272
MD	6,890	TVD	6,890	Progress	0
Days	13	MW	0.0	Visc	0.0
Formation : WASATCH	PBTD : 6775.0	Perf : 5068'-6670'	PKR Depth : 0.0		

Activity at Report Time: ON SALES

Start	End	Hrs	Activity Description
06:00	06:00	24.0	FLOWED 24 HRS. 32/64 CHOKE. FTP 400 PSIG. CP 900 PSIG. 24 BFPH. RECOVERED 580 BLW. 1430 BLWTR. RD FLOW TESTERS. TURNED TO SALES.

FINAL COMPLETION DATE: 6/19/09

06-22-2009	Reported By	DUANE COOK
DailyCosts: Drilling	\$0	Completion
Cum Costs: Drilling	\$567,678	Completion
MD	6,890	TVD
Progress	0	Days
MW	0.0	Visc
Formation : WASATCH	PBTD : 6775.0	Perf : 5068'-6670'
PKR Depth : 0.0		

Activity at Report Time: INITIAL PRODUCTION

Start	End	Hrs	Activity Description
06:00	06:00	24.0	INITIAL PRODUCTION. OPENING PRESSURE: TP 1050 PSIG & CP 1150 PSIG. TURNED WELL OVER TO QUESTAR SALES AT 10:00 AM, 6/20/09. FLOWED 700 MCFD RATE ON 12/64" POS CHOKE. STATIC 280. QUESTAR METER #8114.

FLOWED 572 MCF, 0 BC & 10 BW IN 20 HRS ON 12/64" CHOKE, TP 1600 PSIG & CP 1650 PSIG. WELL DOWN LOST FUEL GAS.

06-23-2009	Reported By	DUANE COOK
DailyCosts: Drilling	\$0	Completion
Cum Costs: Drilling	\$567,678	Completion
MD	6,890	TVD
Progress	0	Days
MW	0.0	Visc
Formation : WASATCH	PBTD : 6775.0	Perf : 5068'-6670'
PKR Depth : 0.0		

Activity at Report Time: ON SALES

Start	End	Hrs	Activity Description
06:00	06:00	24.0	FLOWED 876 MCF, 33 BC & 20 BW IN 24 HRS ON 12/64" CHOKE, SITP 1450 PSIG & CP 1550 PSIG.

06-24-2009	Reported By	DUANE COOK
DailyCosts: Drilling	\$0	Completion
Cum Costs: Drilling	\$567,678	Completion
MD	6,890	TVD
Progress	0	Days
MW	0.0	Visc
Formation : WASATCH	PBTD : 6775.0	Perf : 5068'-6670'
PKR Depth : 0.0		

Activity at Report Time: ON SALES

Start	End	Hrs	Activity Description
06:00	06:00	24.0	FLOWED 767 MCF, 10 BC & 40 BW IN 24 HRS ON 16/64" CHOKE, TP 1400 PSIG, CP 1550 PSIG.

06-25-2009	Reported By	DUANE COOK
DailyCosts: Drilling	\$0	Completion
Cum Costs: Drilling	\$567,678	Completion
MD	6,890	TVD
Progress	0	Days
MW	0.0	Visc
Formation : WASATCH	PBTD : 6775.0	Perf : 5068'-6670'
PKR Depth : 0.0		

MD 6,890 **TVD** 6,890 **Progress** 0 **Days** 17 **MW** 0.0 **Visc** 0.0

Formation : WASATCH **PBTD :** 6775.0 **Perf :** 5068'-6670' **PKR Depth :** 0.0

Activity at Report Time: ON SALES

Start **End** **Hrs** **Activity Description**

06:00 06:00 24.0 FLOWED 762 MCF, 0 BC & 62 BW IN 24 HRS ON 12/64" CHOKE, TP 1375 PSIG, CP 1550 PSIG.

06-26-2009 **Reported By** DUANE COOK

Daily Costs: Drilling \$0 **Completion** \$0 **Daily Total** \$0

Cum Costs: Drilling \$567,678 **Completion** \$392,594 **Well Total** \$960,272

MD 6,890 **TVD** 6,890 **Progress** 0 **Days** 18 **MW** 0.0 **Visc** 0.0

Formation : WASATCH **PBTD :** 6775.0 **Perf :** 5068'-6670' **PKR Depth :** 0.0

Activity at Report Time: ON SALES

Start **End** **Hrs** **Activity Description**

06:00 06:00 24.0 FLOWED 290 MCF, 0 BC & 40 BW IN 8 HRS ON 12/64" CHOKE, TP 1550 PSIG, CP 1600 PSIG.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. Type of Well <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Dry <input type="checkbox"/> Other			5. Lease Serial No. UTU0337		
b. Type of Completion <input checked="" type="checkbox"/> New Well <input type="checkbox"/> Work Over <input type="checkbox"/> Deepen <input type="checkbox"/> Plug Back <input type="checkbox"/> Diff. Resvr. Other _____			6. If Indian, Allottee or Tribe Name		
2. Name of Operator EOG RESOURCES, INC.			7. Unit or CA Agreement Name and No. CHAPITA WELLS		
Contact: MICKENZIE THACKER E-Mail: MICKENZIE_THACKER@EOGRESOURCES.COM			8. Lease Name and Well No. CHAPITA WELLS UNIT 728-29		
3. Address 1060 EAST HIGHWAY 40 VERNAL, UT 84078			9. API Well No. 43-047-39724		
3a. Phone No. (include area code) Ph: 453-781-9145					
4. Location of Well (Report location clearly and in accordance with Federal requirements)* At surface NENE 608FNL 513FEL 40.01259 N Lat, 109.34314 W Lon At top prod interval reported below NENE 608FNL 513FEL 40.01259 N Lat, 109.34314 W Lon At total depth NENE 608FNL 513FEL 40.01259 N Lat, 109.34314 W Lon			10. Field and Pool, or Exploratory NATURAL BUTTES		
			11. Sec., T., R., M., or Block and Survey or Area Sec 29 T9S R23E Mer SLB		
			12. County or Parish UINTAH		13. State UT
14. Date Spudded 11/21/2008		15. Date T.D. Reached 02/27/2009	16. Date Completed <input type="checkbox"/> D & A <input checked="" type="checkbox"/> Ready to Prod. 06/20/2009		17. Elevations (DF, KB, RT, GL)* 5189 GL
18. Total Depth: MD TVD 6890		19. Plug Back T.D.: MD TVD 6775		20. Depth Bridge Plug Set: MD TVD 6775	
21. Type Electric & Other Mechanical Logs Run (Submit copy of each) <input checked="" type="checkbox"/> RST/CBL/CCL/VDL/GR			22. Was well cored? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Submit analysis) Was DST run? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Submit analysis) Directional Survey? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Submit analysis)		

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sks. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12.250	9.625 J-55	36.0		2327		675		0	
7.875	4.500 P-110	11.6		6888		1190		700	

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2.375	5033							

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) WASATCH	5068	6670	6334 TO 6670		3	
B)			5949 TO 6214		3	
C)			5540 TO 5859		3	
D)			5068 TO 5350		3	

27. Acid, Fracture, Treatment, Cement Squeeze, Etc.

Depth Interval	Amount and Type of Material
6334 TO 6670	43,420 GALS OF GELLED WATER & 127,000# 20/40 SAND
5949 TO 6214	30,774 GALS OF GELLED WATER & 82,700# 20/40 SAND
5540 TO 5859	28,661 GALS OF GELLED WATER & 74,100# 20/40 SAND
5068 TO 5350	36,192 GALS OF GELLED WATER & 128,536# 20/40 SAND

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
06/20/2009	06/24/2009	24	→	10.0	767.0	40.0			FLows FROM WELL
Choke Size	Tbg. Press. Flwg. 1400 SI	Csg. Press. 1550.0	24 Hr. Rate →	Oil BBL 10	Gas MCF 767	Water BBL 40	Gas:Oil Ratio	Well Status	PGW

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	

(See Instructions and spaces for additional data on reverse side)

ELECTRONIC SUBMISSION #72296 VERIFIED BY THE BLM WELL INFORMATION SYSTEM

**** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ****

RECEIVED
JUL 21 2009

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	

29. Disposition of Gas(*Sold, used for fuel, vented, etc.*)
SOLD

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
WASATCH	5068	6670		GREEN RIVER	1372
				BIRDS NEST	1689
				MAHOGANY	2293
				UTELAND BUTTE	4440
				WASATCH	4555
				CHAPITA WELLS	5115
				BUCK CANYON	5800
				PRICE RIVER	6680

32. Additional remarks (include plugging procedure):

RECEIVED

JUL 21 2009

33. Circle enclosed attachments:

- | | | | |
|---|--------------------|---------------|-----------------------|
| 1. Electrical/Mechanical Logs (1 full set req'd.) | 2. Geologic Report | 3. DST Report | 4. Directional Survey |
| 5. Sundry Notice for plugging and cement verification | 6. Core Analysis | 7 Other: | |

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions):

Electronic Submission #72296 Verified by the BLM Well Information System.
For EOG RESOURCES, INC., sent to the Vernal

Name (please print) MICKENZIE THACKER

Title OPERATIONS CLERK

Signature

Mickenzie Thacker

Date 07/17/2009

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

** ORIGINAL ** ORIGINAL ** ORIGINAL ** ORIGINAL ** ORIGINAL ** ORIGINAL ** ORIGINAL **

Chapita Wells Unit 728-29 - ADDITIONAL REMARKS (CONTINUED):

Perforated the Ba/North Horn from 6334'-35', 6390'-91', 6451'-52', 6506'-07', 6513'-14', 6545'-46', 6557'-60', 6572'-73', 6578'-79', 6669'-70' w/ 3 spf.

Perforated the Ba from 5949'-50', 5988'-89', 5996'-97', 6036'-37', 6061'-63', 6111'-12', 6133'-34', 6149'-50', 6174'-76', 6213'-14' w/ 3 spf.

Perforated the Ca/Ba from 5540'-43', 5591'-93', 5620'-21', 5632'-33', 5639'-40', 5687'-88', 5722'-23', 5768'-69', 5858'-59' w/ 3 spf.

Perforated the Pp/Ca from 5068'-70', 5077'-79', 5089'-90', 5097'-98', 5183'-85', 5188'-89', 5194'-95', 5232'-33', 5349'-50' w/ 3 spf.

RECEIVED

JUL 21 2009

DIV. OF OIL, GAS & MIN. AC.

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 7

REPORT OF WATER ENCOUNTERED DURING DRILLING

Well name and number: CWU 728-29

API number: 4304739724

Well Location: QQ NENE Section 29 Township 9S Range 23E County UINTAH

Well operator: EOG

Address: 1060 E HWY 40

city VERNAL state UT zip 84078

Phone: (435) 781-9111

Drilling contractor: CRAIGS ROUSTABOUT SERVICE

Address: PO BOX 41

city JENSEN state UT zip 84035

Phone: (435) 781-1366

Water encountered (attach additional pages as needed):

DEPTH		VOLUME (FLOW RATE OR HEAD)	QUALITY (FRESH OR SALTY)
FROM	TO		
		NO WATER	FLUID DRILLED

Formation tops:
(Top to Bottom)

1	_____	2	_____	3	_____
4	_____	5	_____	6	_____
7	_____	8	_____	9	_____
10	_____	11	_____	12	_____

If an analysis has been made of the water encountered, please attach a copy of the report to this form.

I hereby certify that this report is true and complete to the best of my knowledge.

NAME (PLEASE PRINT) Mickenzie Thacker

TITLE Operations Clerk

SIGNATURE Mickenzie Thacker

DATE 7/17/2009



United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office
P.O. Box 45155
Salt Lake City, UT 84145-0155
<http://www.blm.gov>



IN REPLY REFER TO:
3160
(UT922100)

AUG 06 2010

EOG Resources Inc.
600 Seventeenth Street
Suite 1000N
Denver, CO 80202

Re: Non-Paying Well Determination
CWU 728-29 Well, Chapita Wells Unit
Uintah County, Utah

Gentlemen:

Pursuant to your request of July 30, 2010, it has been determined by this office that under existing conditions the following well is not capable of producing unitized substances in paying quantities as defined in Section 9 of the unit agreement.

API Number	Well Name	Location	Comp. Date	Lease
4304739724	CWU 728-29	NENE 29 9.0 S 23.0 E SLB&M	06/20/2009	UTU03337

All past and future production from this well shall be handled and reported on a lease basis.

Sincerely,

/s/ Roger L. Bankert

Roger L. Bankert
Chief, Branch Minerals

RECEIVED

AUG 10 2010

DIV. OF OIL, GAS & MINING
