


STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT ☐

| | | | | | | | | | | | | | |
|---|------------------|--------------------|--|----------------|--|---|----------------------------|-----------------|--------------|------------------------------------|---------------|-----------------|--|
| APPLICATION FOR PERMIT TO DRILL | | | | | | 1. WELL NAME and NUMBER GMBU N-25-8-17 | | | | | | | |
| 2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/> | | | | | | 3. FIELD OR WILDCAT MONUMENT BUTTE | | | | | | | |
| 4. TYPE OF WELL Oil Well Coalbed Methane Well: NO | | | | | | 5. UNIT or COMMUNITIZATION AGREEMENT NAME GMBU (GRRV) | | | | | | | |
| 6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY | | | | | | 7. OPERATOR PHONE 435 646-4825 | | | | | | | |
| 8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052 | | | | | | 9. OPERATOR E-MAIL mcrozier@newfield.com | | | | | | | |
| 10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU-67845 | | | 11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/> | | | 12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/> | | | | | | | |
| 13. NAME OF SURFACE OWNER (if box 12 = 'fee') | | | | | | 14. SURFACE OWNER PHONE (if box 12 = 'fee') | | | | | | | |
| 15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee') | | | | | | 16. SURFACE OWNER E-MAIL (if box 12 = 'fee') | | | | | | | |
| 17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN') | | | 18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/> | | | 19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/> | | | | | | | |
| 20. LOCATION OF WELL | | FOOTAGES | | QTR-QTR | | SECTION | | TOWNSHIP | | RANGE | | MERIDIAN | |
| LOCATION AT SURFACE | | 2265 FSL 464 FWL | | NWSW | | 25 | | 8.0 S | | 17.0 E | | S | |
| Top of Uppermost Producing Zone | | 2640 FSL 1138 FWL | | NWSW | | 25 | | 8.0 S | | 17.0 E | | S | |
| At Total Depth | | 2366 FNL 1716 FWL | | SENW | | 25 | | 8.0 S | | 17.0 E | | S | |
| 21. COUNTY UINTAH | | | 22. DISTANCE TO NEAREST LEASE LINE (Feet) 2366 | | | 23. NUMBER OF ACRES IN DRILLING UNIT 20 | | | | | | | |
| | | | 25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 756 | | | 26. PROPOSED DEPTH MD: 6630 TVD: 6630 | | | | | | | |
| 27. ELEVATION - GROUND LEVEL 5015 | | | 28. BOND NUMBER WYB000493 | | | 29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 437478 | | | | | | | |
| Hole, Casing, and Cement Information | | | | | | | | | | | | | |
| String | Hole Size | Casing Size | Length | Weight | Grade & Thread | Max Mud Wt. | Cement | | Sacks | Yield | Weight | | |
| Surf | 12.25 | 8.625 | 0 - 300 | 24.0 | J-55 ST&C | 8.3 | Class G | | 138 | 1.17 | 15.8 | | |
| Prod | 7.875 | 5.5 | 0 - 6630 | 15.5 | J-55 LT&C | 8.3 | Premium Lite High Strength | | 320 | 3.26 | 11.0 | | |
| | | | | | | | 50/50 Poz | | 363 | 1.24 | 14.3 | | |
| ATTACHMENTS | | | | | | | | | | | | | |
| VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES | | | | | | | | | | | | | |
| <input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER | | | | | | <input checked="" type="checkbox"/> COMPLETE DRILLING PLAN | | | | | | | |
| <input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE) | | | | | | <input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER | | | | | | | |
| <input checked="" type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED) | | | | | | <input checked="" type="checkbox"/> TOPOGRAPHICAL MAP | | | | | | | |
| NAME Mandie Crozier | | | | | TITLE Regulatory Tech | | | | | PHONE 435 646-4825 | | | |
| SIGNATURE | | | | | DATE 06/06/2011 | | | | | EMAIL mcrozier@newfield.com | | | |
| API NUMBER ASSIGNED 43047516490000 | | | | | APPROVAL  Permit Manager | | | | | | | | |

NEWFIELD PRODUCTION COMPANY
GMBU N-25-8-17
AT SURFACE: NW/SW SECTION 25, T8S, R17E
UINTAH COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

| | |
|--------------------|--------------|
| Uinta | 0' – 1695' |
| Green River | 1695' |
| Wasatch | 6385' |
| Proposed TD | 6630' |

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil) 1695' – 6385'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

| | |
|--|---|
| Location & Sampled Interval | Date Sampled |
| Flow Rate | Temperature |
| Hardness | pH |
| Water Classification (State of Utah) | Dissolved Calcium (Ca) (mg/l) |
| Dissolved Iron (Fe) (ug/l) | Dissolved Sodium (Na) (mg/l) |
| Dissolved Magnesium (Mg) (mg/l) | Dissolved Carbonate (CO ₃) (mg/l) |
| Dissolved Bicarbonate (NaHCO ₃) (mg/l) | Dissolved Chloride (Cl) (mg/l) |
| Dissolved Sulfate (SO ₄) (mg/l) | Dissolved Total Solids (TDS) (mg/l) |

4. **PROPOSED CASING PROGRAM**

a. Casing Design: GMBU N-25-8-17

| Size | Interval | | Weight | Grade | Coupling | Design Factors | | |
|--------------------------|----------|--------|--------|-------|----------|----------------|----------------|------------------|
| | Top | Bottom | | | | Burst | Collapse | Tension |
| Surface casing 8-5/8" | 0' | 300' | 24.0 | J-55 | STC | 2,950 17.53 | 1,370 14.35 | 244,000 33.89 |
| Prod casing 5-1/2" | 0' | 6,630' | 15.5 | J-55 | LTC | 4,810 2.28 | 4,040 1.92 | 217,000 2.11 |

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg
 Pore pressure at surface casing shoe = 8.33 ppg
 Pore pressure at prod casing shoe = 8.33 ppg
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. Cementing Design: GMBU N-25-8-17

| Job | Fill | Description | Sacks | OH Excess* | Weight (ppg) | Yield (ft ³ /sk) |
|---------------------|--------|-------------------------------------|-----------------|---------------|-----------------|--------------------------------|
| | | | ft ³ | | | |
| Surface casing | 300' | Class G w/ 2% CaCl | 138 161 | 30% | 15.8 | 1.17 |
| Prod casing Lead | 4,630' | Prem Lite II w/ 10% gel + 3% KCl | 320 1043 | 30% | 11.0 | 3.26 |
| Prod casing Tail | 2,000' | 50/50 Poz w/ 2% gel + 3% KCl | 363 451 | 30% | 14.3 | 1.24 |

*Actual volume pumped will be 15% over the caliper log

- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ± 300 feet will be drilled with an air/mist system. The air rig is equipped with a 6 1/2" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ± 300 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated

bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.

10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the third quarter of 2011, and take approximately seven (7) days from spud to rig release.


T8S, R17E, S.L.B.&M.

N89°58'W - 79.90 (G.L.O.)

NEWFIELD EXPLORATION COMPANY

WELL LOCATION, N-25-8-17, LOCATED AS SHOWN IN THE NW 1/4 SW 1/4 OF SECTION 25, T8S, R17E, S.L.B.&M. UTAH COUNTY, UTAH.


TARGET BOTTOM HOLE, N-25-8-17, LOCATED AS SHOWN IN THE SE 1/4 NW 1/4 OF SECTION 25, T8S, R17E, S.L.B.&M. UTAH COUNTY, UTAH.

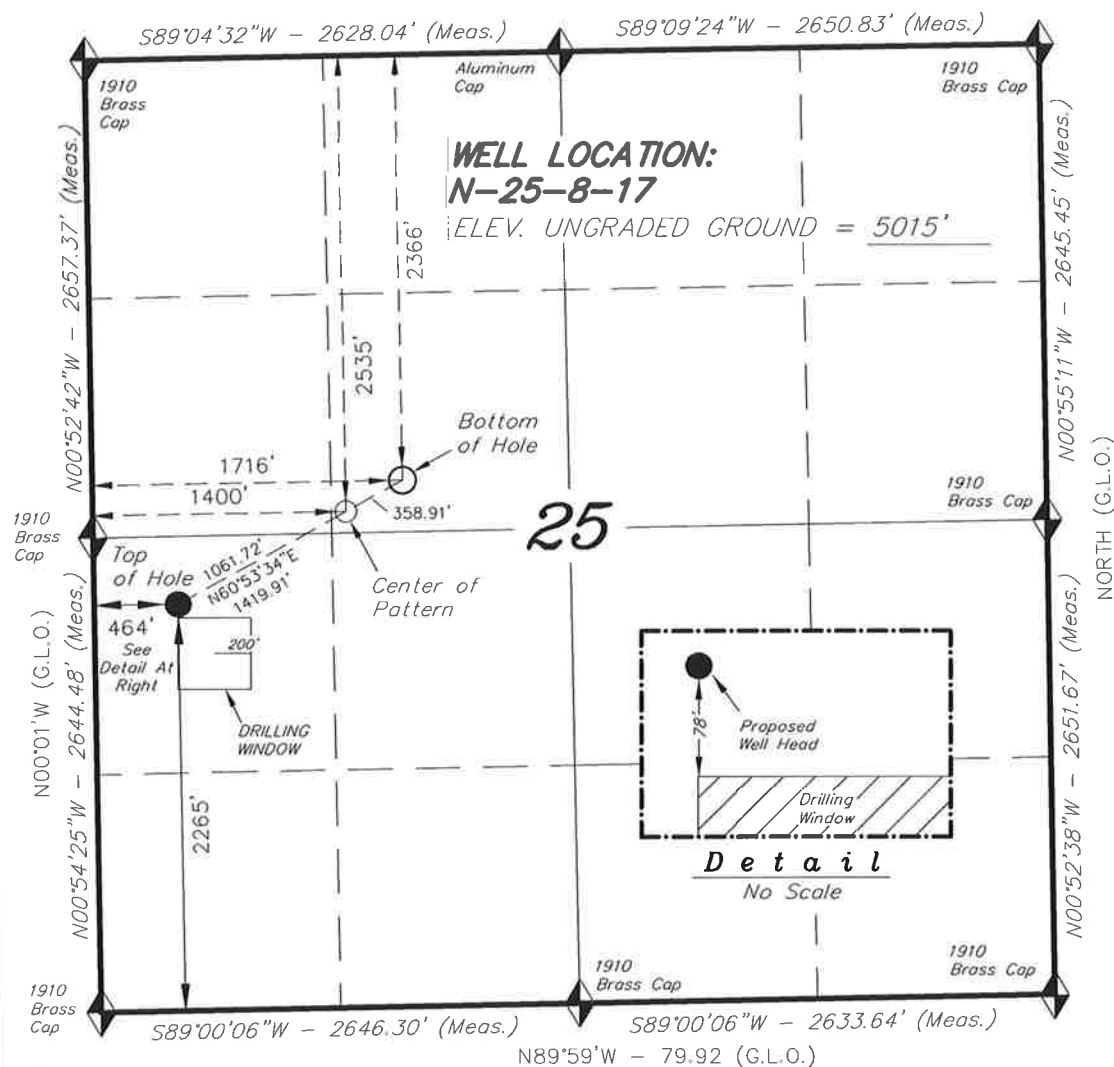

◆ = SECTION CORNERS LOCATED


BASIS OF ELEV; Elevations are base on LOCATION: an N.G.S. OPUS Correction.
LAT. 40°04'09.56" LONG. 110°00'43.28"
(Tristate Aluminum Cap) Elev. 5281.57'

N-25-8-17
(Surface Location) NAD 83
LATITUDE = 40° 05' 16.50"
LONGITUDE = 109° 57' 45.62"

**NOTES:**


1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.


THIS IS TO CERTIFY THAT THE ABOVE PLOT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.


**TRI STATE LAND SURVEYING & CONSULTING**


180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501


| | |
|----------------------------|-------------------|
| DATE SURVEYED: 10-09-10 | SURVEYED BY: D.G. |
| DATE DRAWN: 12-13-10 | DRAWN BY: M.W. |
| REVISED: | SCALE: 1" = 1000' |

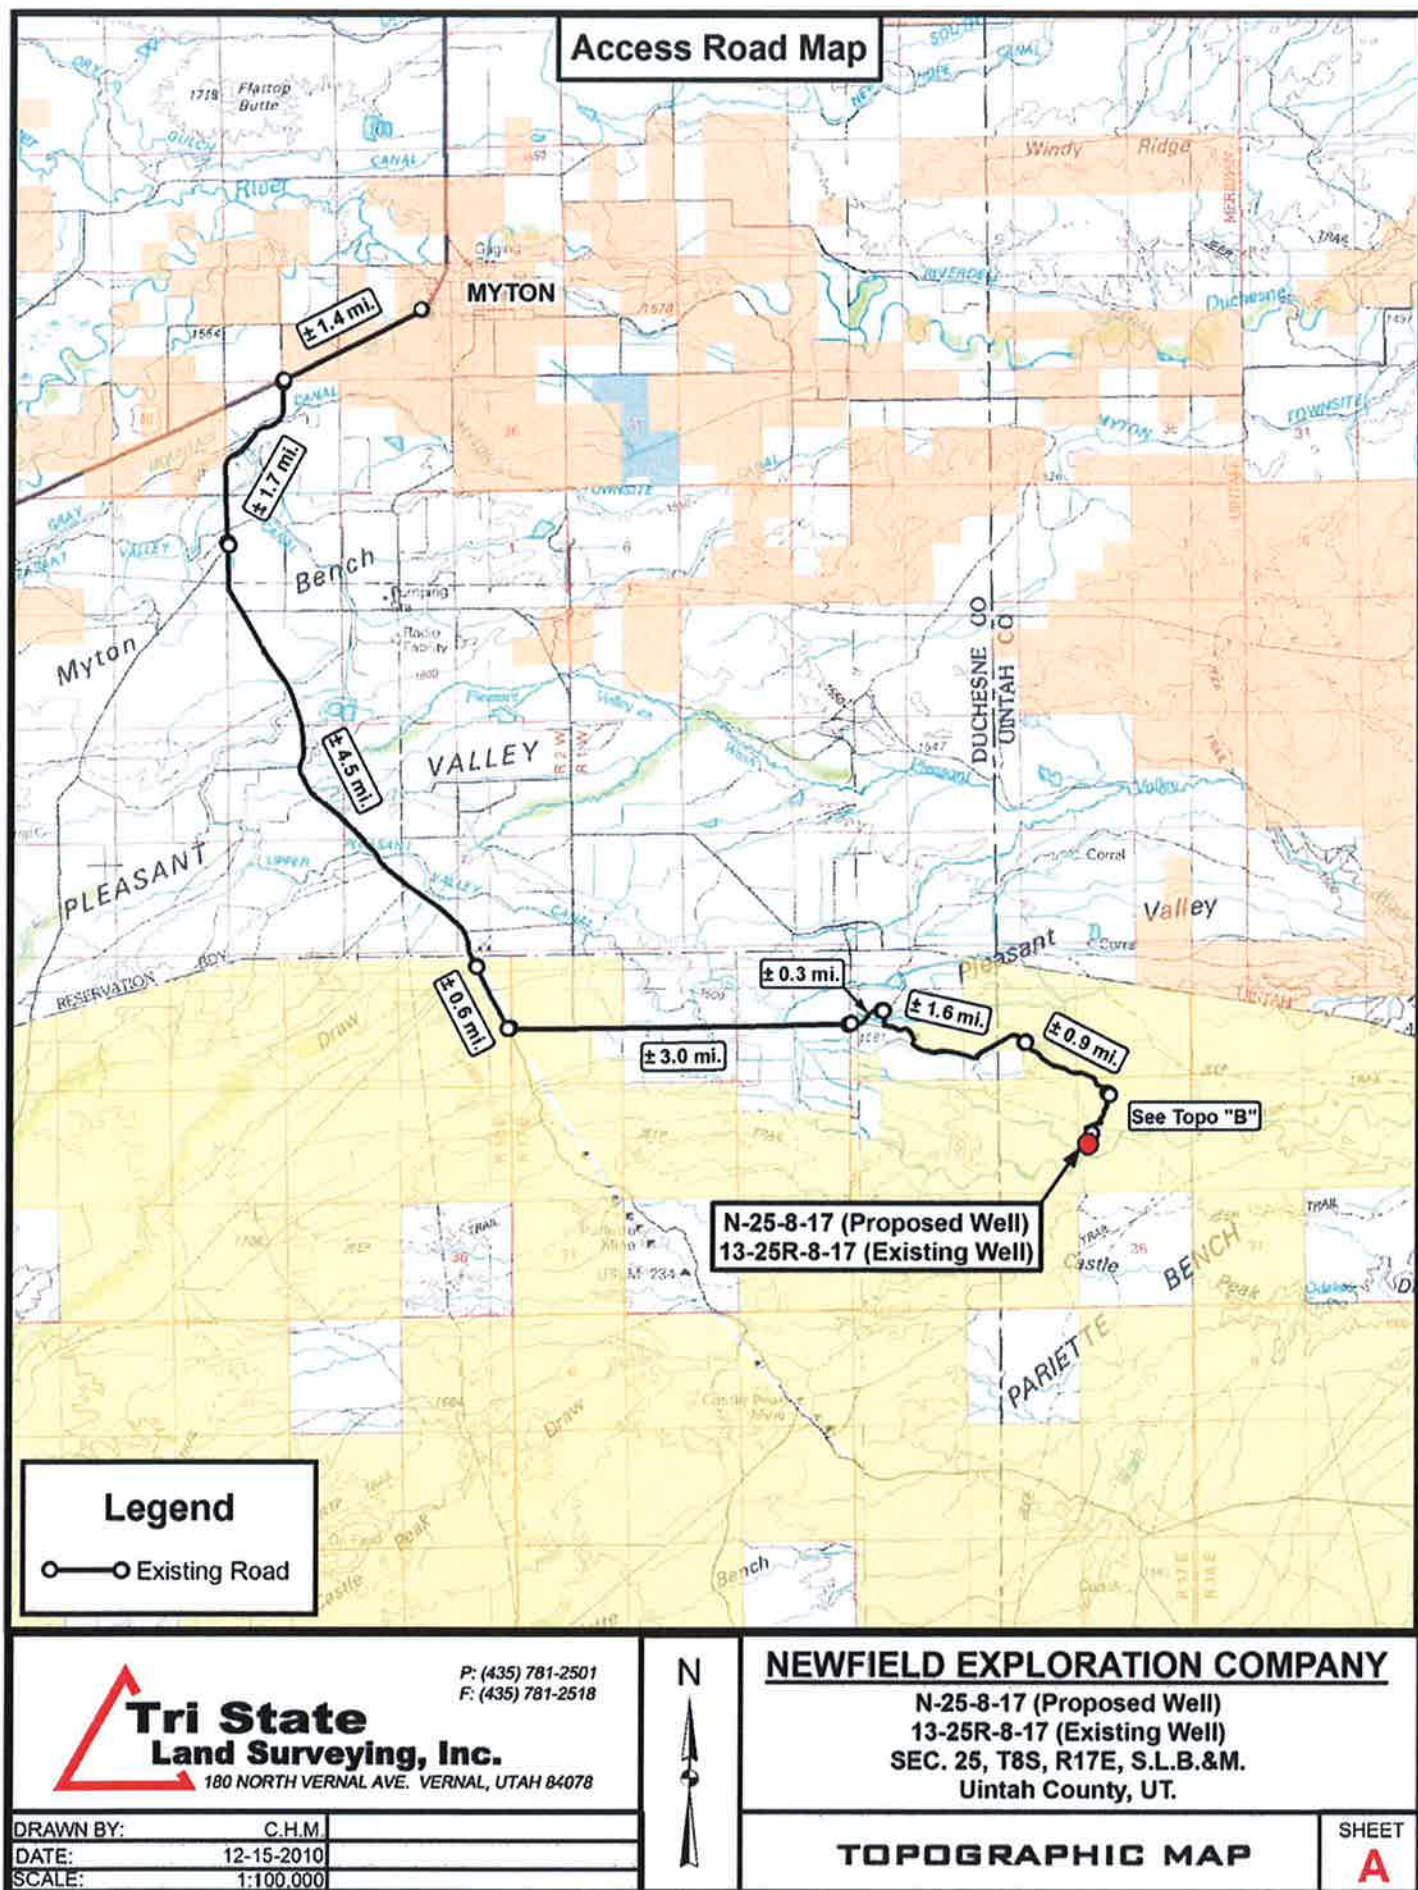

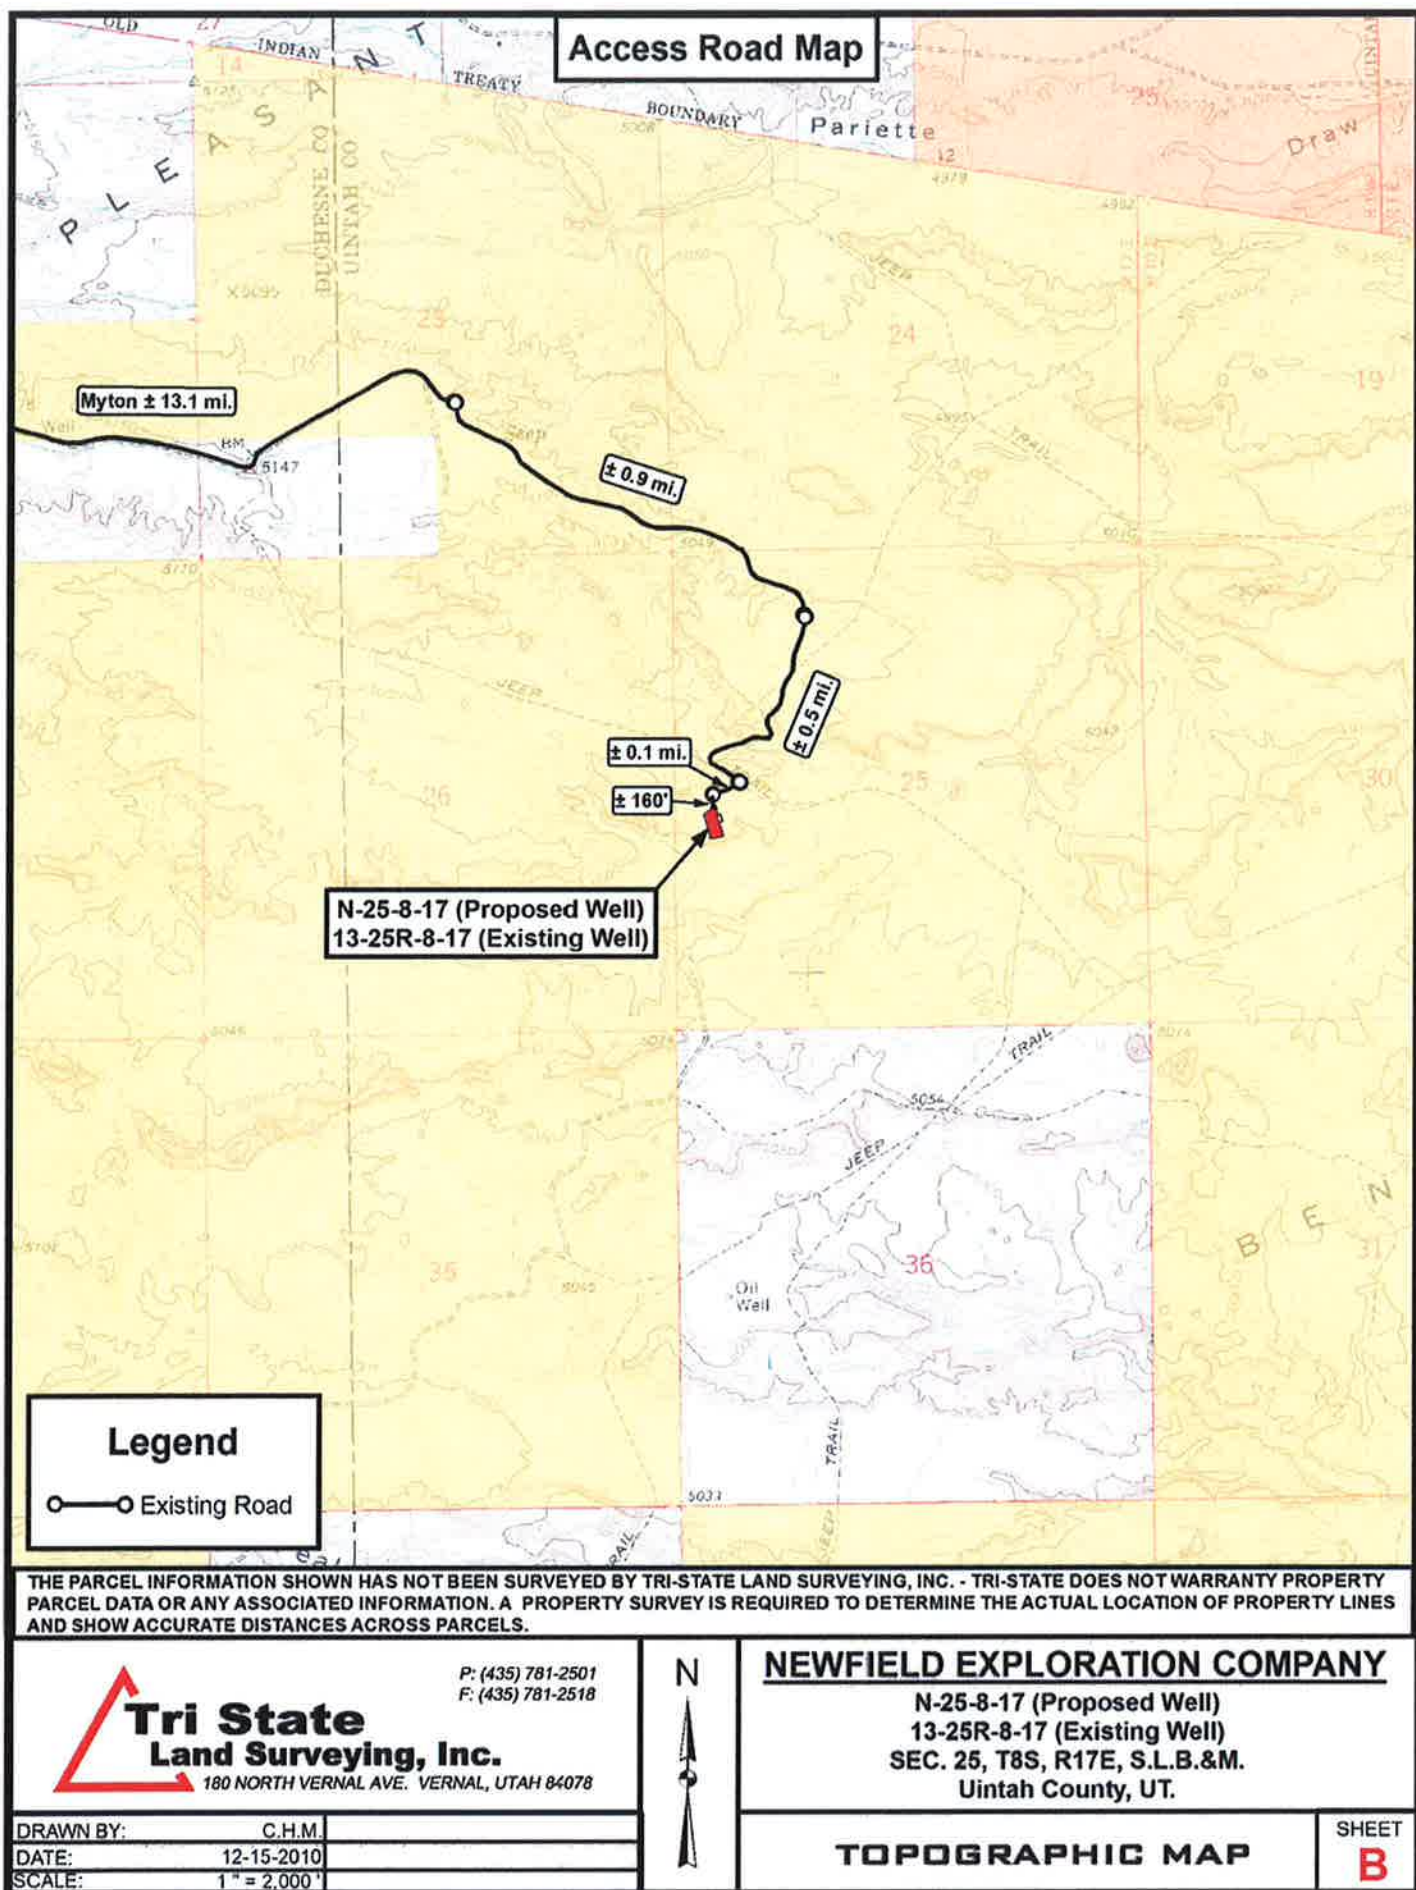

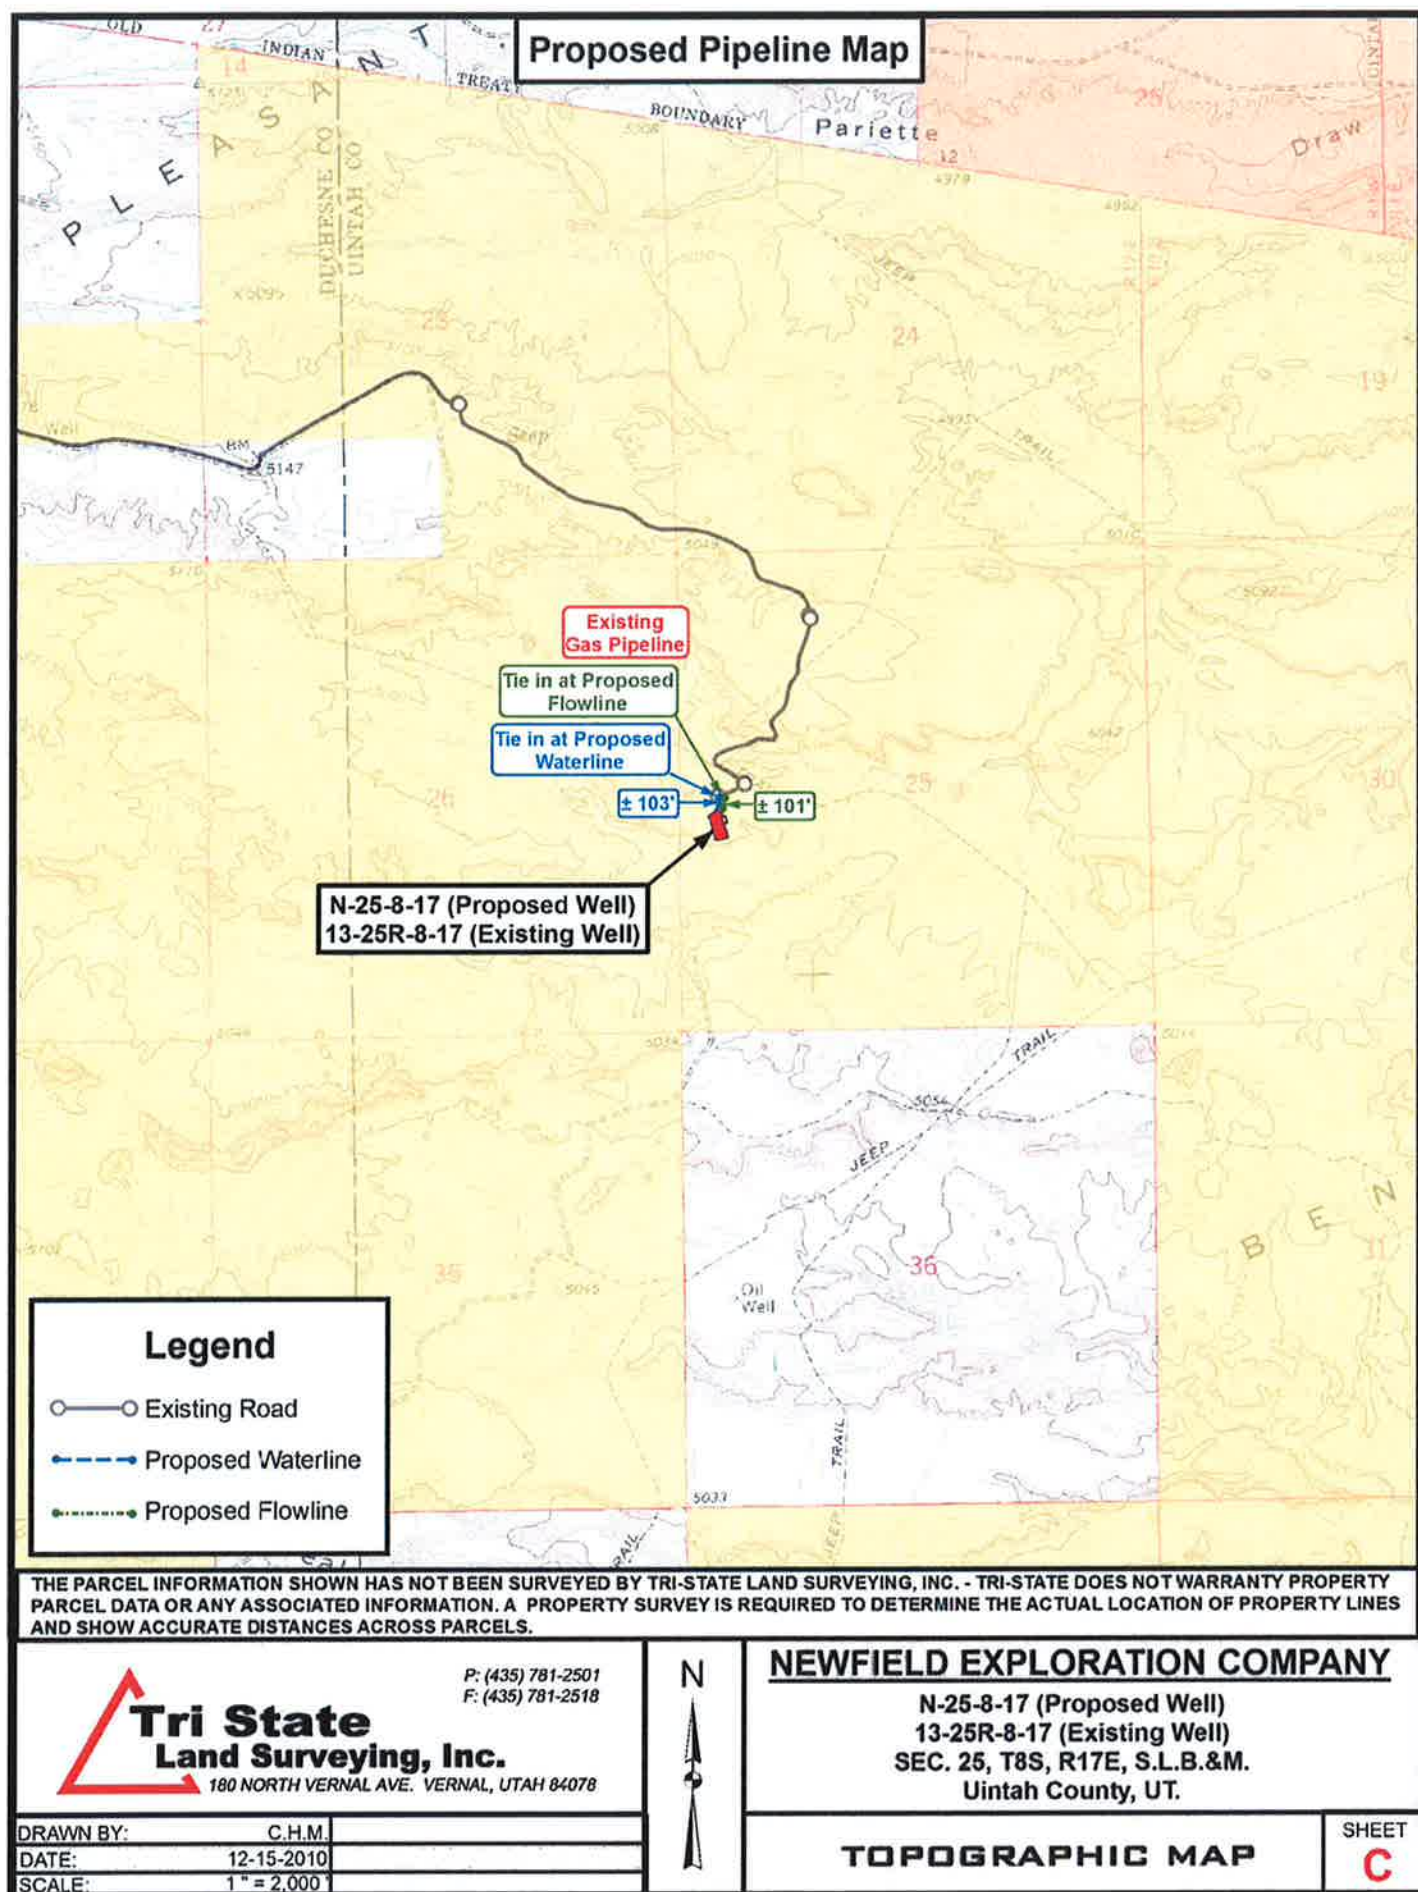

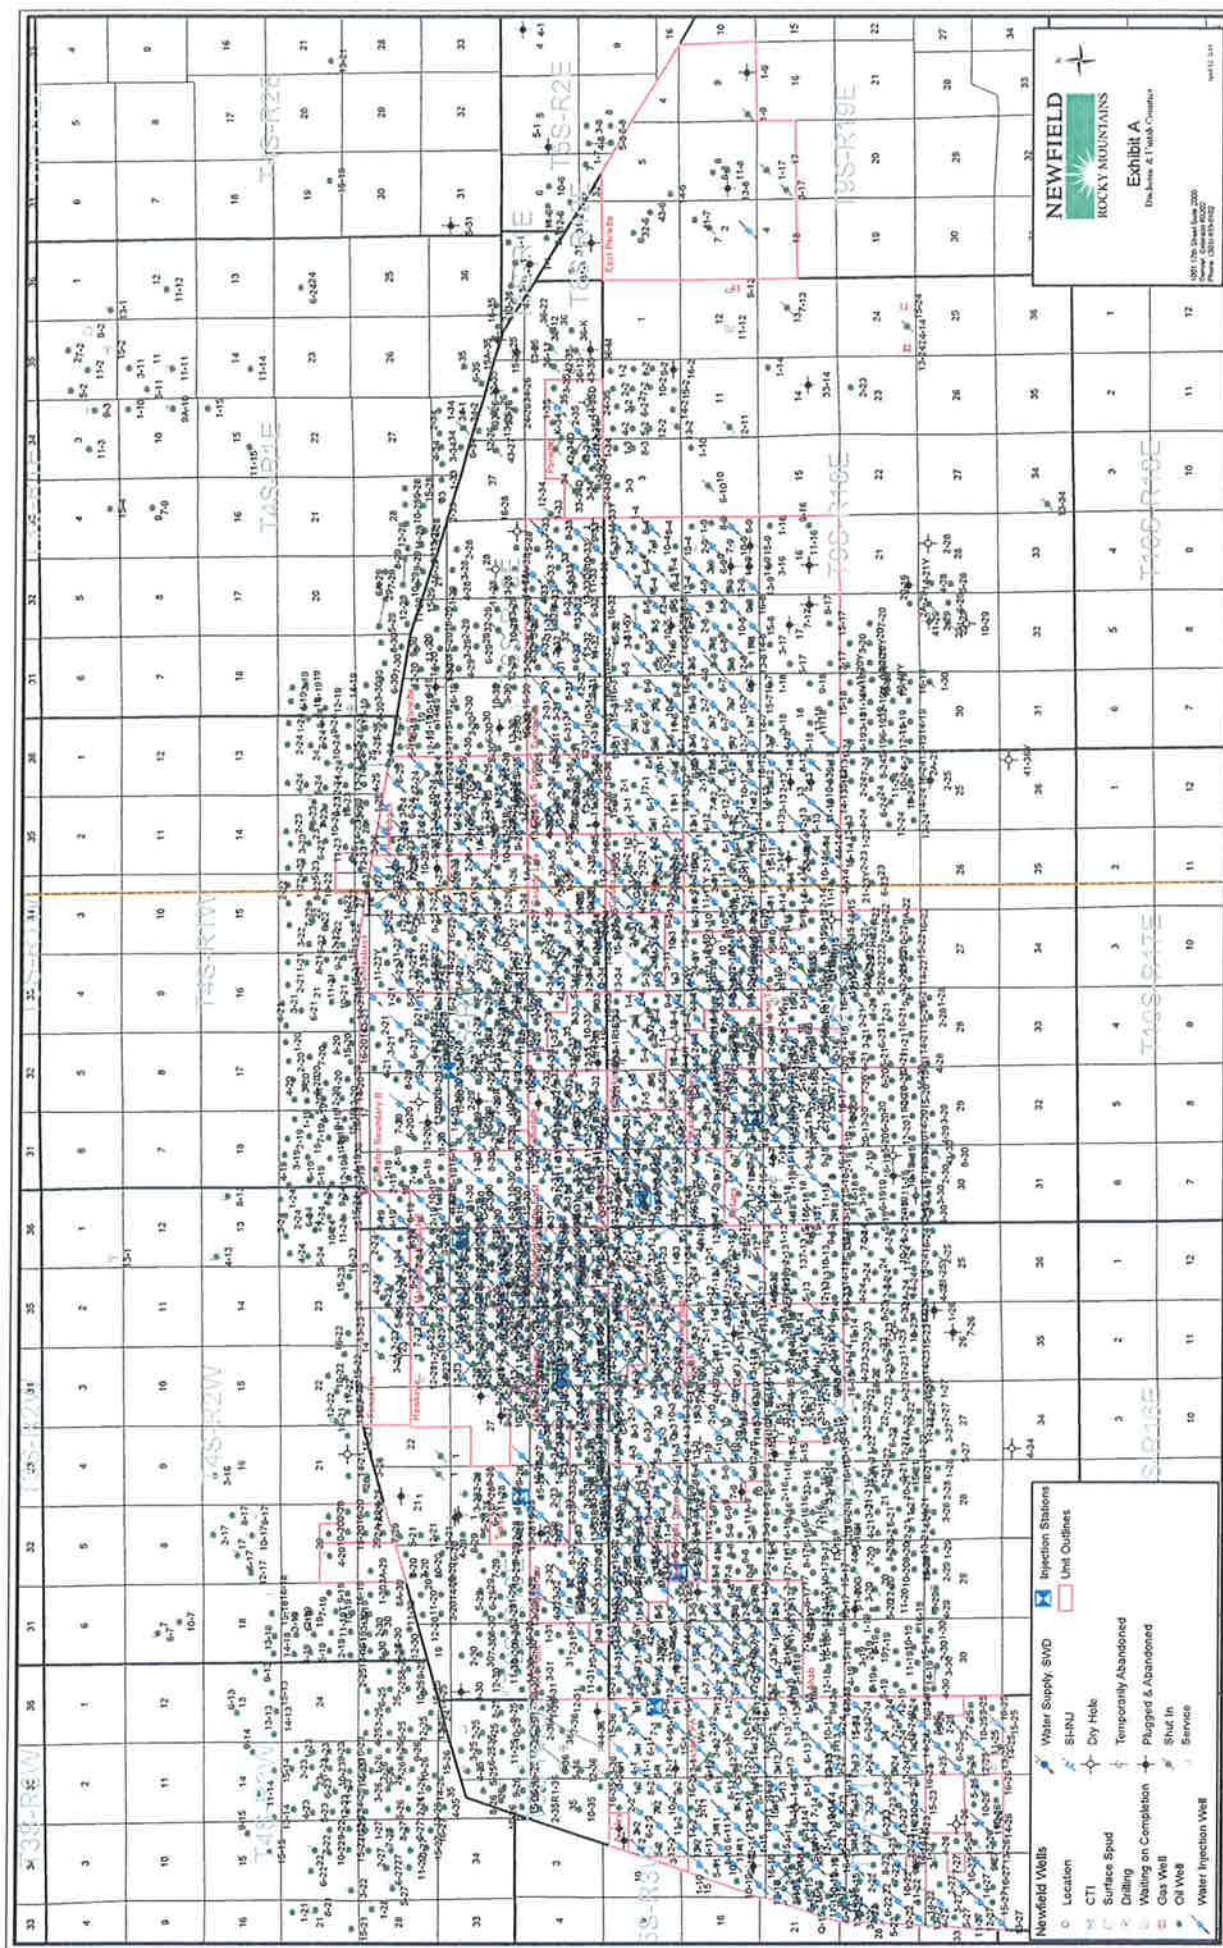

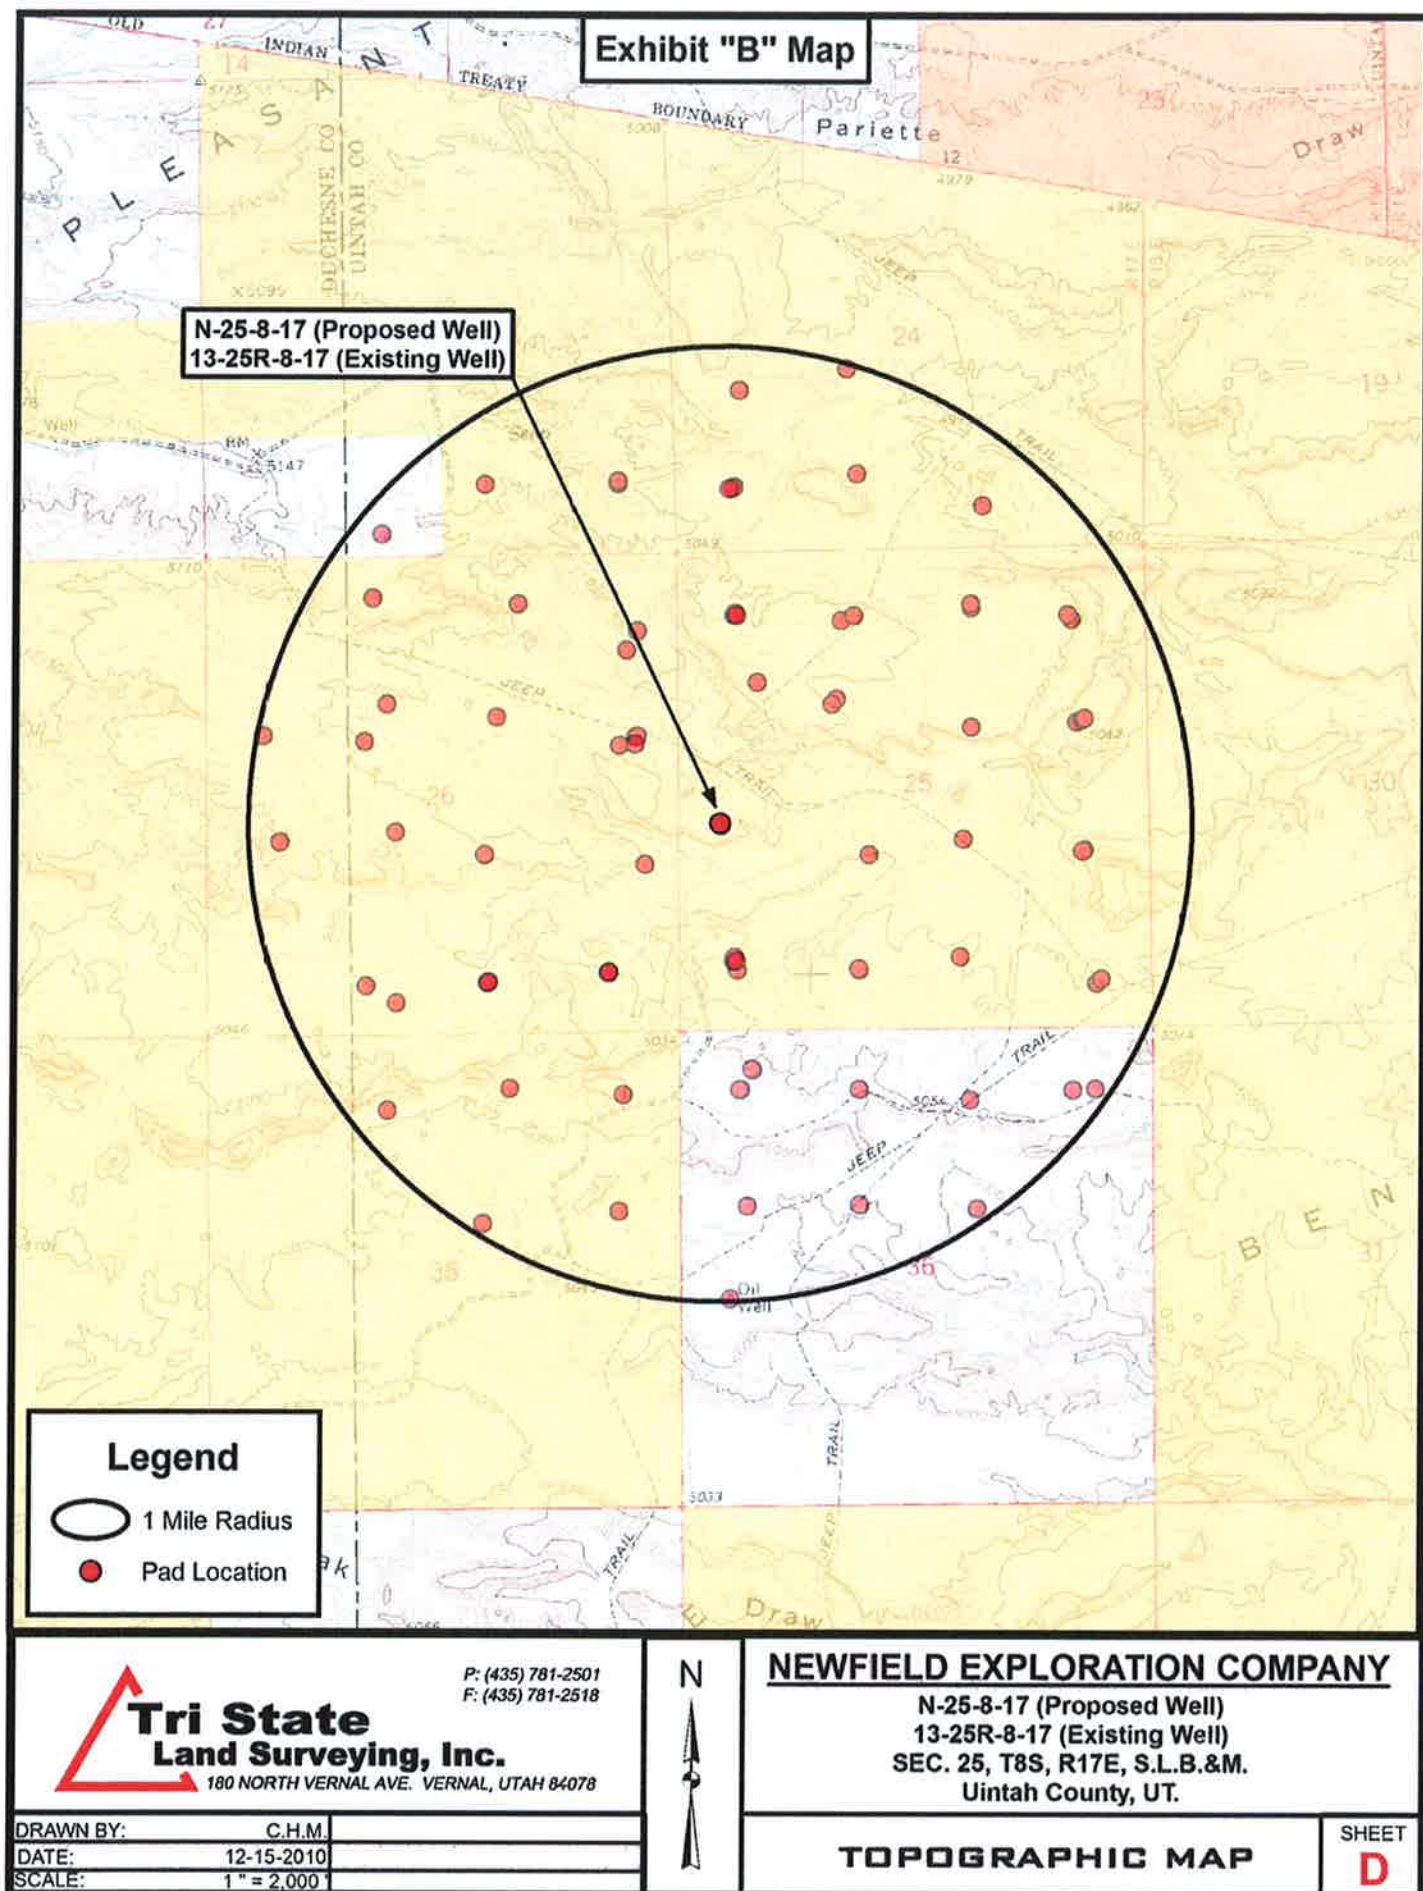



NEWFIELD EXPLORATION

**USGS Myton SW (UT)
SECTION 25 T8S, R17
N-25-8-17**

Wellbore #1

Plan: Design #1

Standard Planning Report

03 December, 2010





| | | | |
|------------------|----------------------------|-------------------------------------|-------------------------------------|
| Database: | EDM 2003.21 Single User Db | Local Co-ordinate Reference: | Well N-25-8-17 |
| Company: | NEWFIELD EXPLORATION | TVD Reference: | N-25-8-17 @ 5027.0ft (NEWFIELD RIG) |
| Project: | USGS Myton SW (UT) | MD Reference: | N-25-8-17 @ 5027.0ft (NEWFIELD RIG) |
| Site: | SECTION 25 T8S, R17 | North Reference: | Grid |
| Well: | N-25-8-17 | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | Design #1 | | |

| | | | |
|--------------------|--|----------------------|----------------|
| Project | USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA | | |
| Map System: | US State Plane 1983 | System Datum: | Mean Sea Level |
| Geo Datum: | North American Datum 1983 | | |
| Map Zone: | Utah Central Zone | | |

| | | | | | |
|-----------------------|----------|---------------------|-----------------|-------------------|-------------------|
| Site | | SECTION 25 T8S, R17 | | | |
| Site Position: | | Northing: | 7,205,389.13 ft | Latitude: | 40° 5' 26.000 N |
| From: | Lat/Long | Easting: | 2,069,565.26 ft | Longitude: | 109° 57' 57.510 W |
| Position Uncertainty: | 0.0 ft | Slot Radius: | " | Grid Convergence: | 0.98 ° |

| | | | | | | |
|----------------------|---|-----------|---------------------|-----------------|---------------|-------------------|
| Well | N-25-8-17, SHL LAT: 40 05 16.50 LONG: -109 57 45.62 | | | | | |
| Well Position | +N/-S | -945.2 ft | Northing: | 7,204,443.89 ft | Latitude: | 40° 5' 16.500 N |
| | +E/-W | 940.4 ft | Easting: | 2,070,505.66 ft | Longitude: | 109° 57' 45.620 W |
| Position Uncertainty | | 0.0 ft | Wellhead Elevation: | 5,027.0 ft | Ground Level: | 5,015.0 ft |

| | | | | | |
|------------------|-------------------|--------------------|------------------------|----------------------|----------------------------|
| Wellbore | Wellbore #1 | | | | |
| Magnetics | Model Name | Sample Date | Declination (°) | Dip Angle (°) | Field Strength (nT) |
| | IGRF2010 | 2010/12/03 | 11.35 | 65.86 | 52,364 |

| | | | | |
|--------------------------|------------------------------|-------------------|----------------------|----------------------|
| Design | Design #1 | | | |
| Audit Notes: | | | | |
| Version: | Phase: | PROTOTYPE | Tie On Depth: | 0.0 |
| Vertical Section: | Depth From (TVD) (ft) | +N/-S (ft) | +E/-W (ft) | Direction (°) |
| | 5,100.0 | 0.0 | 0.0 | 60.89 |

| Plan Sections | | | | | | | | | | |
|----------------------|-----------------|-------------|---------------------|------------|------------|-----------------------|----------------------|---------------------|---------|---------------|
| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) | TFO (°) | Target |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 1,590.6 | 14.86 | 60.89 | 1,579.5 | 62.1 | 111.6 | 1.50 | 1.50 | 0.00 | 60.89 | |
| 5,232.9 | 14.86 | 60.89 | 5,100.0 | 516.5 | 927.6 | 0.00 | 0.00 | 0.00 | 0.00 | N-25-8-17 TGT |
| 6,629.6 | 14.86 | 60.89 | 6,450.0 | 690.7 | 1,240.6 | 0.00 | 0.00 | 0.00 | 0.00 | |



| | | | |
|------------------|----------------------------|-------------------------------------|-------------------------------------|
| Database: | EDM 2003.21 Single User Db | Local Co-ordinate Reference: | Well N-25-8-17 |
| Company: | NEWFIELD EXPLORATION | TVD Reference: | N-25-8-17 @ 5027.0ft (NEWFIELD RIG) |
| Project: | USGS Myton SW (UT) | MD Reference: | N-25-8-17 @ 5027.0ft (NEWFIELD RIG) |
| Site: | SECTION 25 T8S, R17 | North Reference: | Grid |
| Well: | N-25-8-17 | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | Design #1 | | |

| Planned Survey | | | | | | | | | |
|---------------------|-----------------|-------------|---------------------|------------|------------|-----------------------|-----------------------|----------------------|---------------------|
| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Vertical Section (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 100.0 | 0.00 | 0.00 | 100.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 200.0 | 0.00 | 0.00 | 200.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 300.0 | 0.00 | 0.00 | 300.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 400.0 | 0.00 | 0.00 | 400.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 500.0 | 0.00 | 0.00 | 500.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 700.0 | 1.50 | 60.89 | 700.0 | 0.6 | 1.1 | 1.3 | 1.50 | 1.50 | 0.00 |
| 800.0 | 3.00 | 60.89 | 799.9 | 2.5 | 4.6 | 5.2 | 1.50 | 1.50 | 0.00 |
| 900.0 | 4.50 | 60.89 | 899.7 | 5.7 | 10.3 | 11.8 | 1.50 | 1.50 | 0.00 |
| 1,000.0 | 6.00 | 60.89 | 999.3 | 10.2 | 18.3 | 20.9 | 1.50 | 1.50 | 0.00 |
| 1,100.0 | 7.50 | 60.89 | 1,098.6 | 15.9 | 28.6 | 32.7 | 1.50 | 1.50 | 0.00 |
| 1,200.0 | 9.00 | 60.89 | 1,197.5 | 22.9 | 41.1 | 47.0 | 1.50 | 1.50 | 0.00 |
| 1,300.0 | 10.50 | 60.89 | 1,296.1 | 31.1 | 55.9 | 64.0 | 1.50 | 1.50 | 0.00 |
| 1,400.0 | 12.00 | 60.89 | 1,394.2 | 40.6 | 72.9 | 83.5 | 1.50 | 1.50 | 0.00 |
| 1,500.0 | 13.50 | 60.89 | 1,491.7 | 51.3 | 92.2 | 105.5 | 1.50 | 1.50 | 0.00 |
| 1,590.6 | 14.86 | 60.89 | 1,579.5 | 62.1 | 111.6 | 127.7 | 1.50 | 1.50 | 0.00 |
| 1,600.0 | 14.86 | 60.89 | 1,588.6 | 63.3 | 113.7 | 130.1 | 0.00 | 0.00 | 0.00 |
| 1,700.0 | 14.86 | 60.89 | 1,685.3 | 75.8 | 136.1 | 155.8 | 0.00 | 0.00 | 0.00 |
| 1,800.0 | 14.86 | 60.89 | 1,781.9 | 88.3 | 158.5 | 181.4 | 0.00 | 0.00 | 0.00 |
| 1,900.0 | 14.86 | 60.89 | 1,878.6 | 100.7 | 180.9 | 207.1 | 0.00 | 0.00 | 0.00 |
| 2,000.0 | 14.86 | 60.89 | 1,975.2 | 113.2 | 203.3 | 232.7 | 0.00 | 0.00 | 0.00 |
| 2,100.0 | 14.86 | 60.89 | 2,071.9 | 125.7 | 225.7 | 258.4 | 0.00 | 0.00 | 0.00 |
| 2,200.0 | 14.86 | 60.89 | 2,168.6 | 138.2 | 248.1 | 284.0 | 0.00 | 0.00 | 0.00 |
| 2,300.0 | 14.86 | 60.89 | 2,265.2 | 150.6 | 270.5 | 309.6 | 0.00 | 0.00 | 0.00 |
| 2,400.0 | 14.86 | 60.89 | 2,361.9 | 163.1 | 292.9 | 335.3 | 0.00 | 0.00 | 0.00 |
| 2,500.0 | 14.86 | 60.89 | 2,458.5 | 175.6 | 315.3 | 360.9 | 0.00 | 0.00 | 0.00 |
| 2,600.0 | 14.86 | 60.89 | 2,555.2 | 188.0 | 337.8 | 386.6 | 0.00 | 0.00 | 0.00 |
| 2,700.0 | 14.86 | 60.89 | 2,651.8 | 200.5 | 360.2 | 412.2 | 0.00 | 0.00 | 0.00 |
| 2,800.0 | 14.86 | 60.89 | 2,748.5 | 213.0 | 382.6 | 437.9 | 0.00 | 0.00 | 0.00 |
| 2,900.0 | 14.86 | 60.89 | 2,845.2 | 225.5 | 405.0 | 463.5 | 0.00 | 0.00 | 0.00 |
| 3,000.0 | 14.86 | 60.89 | 2,941.8 | 237.9 | 427.4 | 489.1 | 0.00 | 0.00 | 0.00 |
| 3,100.0 | 14.86 | 60.89 | 3,038.5 | 250.4 | 449.8 | 514.8 | 0.00 | 0.00 | 0.00 |
| 3,200.0 | 14.86 | 60.89 | 3,135.1 | 262.9 | 472.2 | 540.4 | 0.00 | 0.00 | 0.00 |
| 3,300.0 | 14.86 | 60.89 | 3,231.8 | 275.4 | 494.6 | 566.1 | 0.00 | 0.00 | 0.00 |
| 3,400.0 | 14.86 | 60.89 | 3,328.4 | 287.8 | 517.0 | 591.7 | 0.00 | 0.00 | 0.00 |
| 3,500.0 | 14.86 | 60.89 | 3,425.1 | 300.3 | 539.4 | 617.4 | 0.00 | 0.00 | 0.00 |
| 3,600.0 | 14.86 | 60.89 | 3,521.7 | 312.8 | 561.8 | 643.0 | 0.00 | 0.00 | 0.00 |
| 3,700.0 | 14.86 | 60.89 | 3,618.4 | 325.3 | 584.2 | 668.6 | 0.00 | 0.00 | 0.00 |
| 3,800.0 | 14.86 | 60.89 | 3,715.1 | 337.7 | 606.6 | 694.3 | 0.00 | 0.00 | 0.00 |
| 3,900.0 | 14.86 | 60.89 | 3,811.7 | 350.2 | 629.0 | 719.9 | 0.00 | 0.00 | 0.00 |
| 4,000.0 | 14.86 | 60.89 | 3,908.4 | 362.7 | 651.4 | 745.6 | 0.00 | 0.00 | 0.00 |
| 4,100.0 | 14.86 | 60.89 | 4,005.0 | 375.2 | 673.8 | 771.2 | 0.00 | 0.00 | 0.00 |
| 4,200.0 | 14.86 | 60.89 | 4,101.7 | 387.6 | 696.2 | 796.9 | 0.00 | 0.00 | 0.00 |
| 4,300.0 | 14.86 | 60.89 | 4,198.3 | 400.1 | 718.6 | 822.5 | 0.00 | 0.00 | 0.00 |
| 4,400.0 | 14.86 | 60.89 | 4,295.0 | 412.6 | 741.0 | 848.1 | 0.00 | 0.00 | 0.00 |
| 4,500.0 | 14.86 | 60.89 | 4,391.7 | 425.1 | 763.4 | 873.8 | 0.00 | 0.00 | 0.00 |
| 4,600.0 | 14.86 | 60.89 | 4,488.3 | 437.5 | 785.8 | 899.4 | 0.00 | 0.00 | 0.00 |
| 4,700.0 | 14.86 | 60.89 | 4,585.0 | 450.0 | 808.3 | 925.1 | 0.00 | 0.00 | 0.00 |
| 4,800.0 | 14.86 | 60.89 | 4,681.6 | 462.5 | 830.7 | 950.7 | 0.00 | 0.00 | 0.00 |
| 4,900.0 | 14.86 | 60.89 | 4,778.3 | 474.9 | 853.1 | 976.4 | 0.00 | 0.00 | 0.00 |
| 5,000.0 | 14.86 | 60.89 | 4,874.9 | 487.4 | 875.5 | 1,002.0 | 0.00 | 0.00 | 0.00 |
| 5,100.0 | 14.86 | 60.89 | 4,971.6 | 499.9 | 897.9 | 1,027.7 | 0.00 | 0.00 | 0.00 |
| 5,200.0 | 14.86 | 60.89 | 5,068.2 | 512.4 | 920.3 | 1,053.3 | 0.00 | 0.00 | 0.00 |



| | | | |
|------------------|----------------------------|-------------------------------------|-------------------------------------|
| Database: | EDM 2003.21 Single User Db | Local Co-ordinate Reference: | Well N-25-8-17 |
| Company: | NEWFIELD EXPLORATION | TVD Reference: | N-25-8-17 @ 5027.0ft (NEWFIELD RIG) |
| Project: | USGS Myton SW (UT) | MD Reference: | N-25-8-17 @ 5027.0ft (NEWFIELD RIG) |
| Site: | SECTION 25 T8S, R17 | North Reference: | Grid |
| Well: | N-25-8-17 | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | Design #1 | | |


| Planned Survey | | | | | | | | | |
|---------------------|-----------------|-------------|---------------------|------------|------------|-----------------------|-----------------------|----------------------|---------------------|
| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Vertical Section (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
| 5,232.9 | 14.86 | 60.89 | 5,100.0 | 516.5 | 927.6 | 1,061.7 | 0.00 | 0.00 | 0.00 |
| N-25-8-17 TGT | | | | | | | | | |
| 5,300.0 | 14.86 | 60.89 | 5,164.9 | 524.8 | 942.7 | 1,078.9 | 0.00 | 0.00 | 0.00 |
| 5,400.0 | 14.86 | 60.89 | 5,261.6 | 537.3 | 965.1 | 1,104.6 | 0.00 | 0.00 | 0.00 |
| 5,500.0 | 14.86 | 60.89 | 5,358.2 | 549.8 | 987.5 | 1,130.2 | 0.00 | 0.00 | 0.00 |
| 5,600.0 | 14.86 | 60.89 | 5,454.9 | 562.3 | 1,009.9 | 1,155.9 | 0.00 | 0.00 | 0.00 |
| 5,700.0 | 14.86 | 60.89 | 5,551.5 | 574.7 | 1,032.3 | 1,181.5 | 0.00 | 0.00 | 0.00 |
| 5,800.0 | 14.86 | 60.89 | 5,648.2 | 587.2 | 1,054.7 | 1,207.2 | 0.00 | 0.00 | 0.00 |
| 5,900.0 | 14.86 | 60.89 | 5,744.8 | 599.7 | 1,077.1 | 1,232.8 | 0.00 | 0.00 | 0.00 |
| 6,000.0 | 14.86 | 60.89 | 5,841.5 | 612.2 | 1,099.5 | 1,258.4 | 0.00 | 0.00 | 0.00 |
| 6,100.0 | 14.86 | 60.89 | 5,938.2 | 624.6 | 1,121.9 | 1,284.1 | 0.00 | 0.00 | 0.00 |
| 6,200.0 | 14.86 | 60.89 | 6,034.8 | 637.1 | 1,144.3 | 1,309.7 | 0.00 | 0.00 | 0.00 |
| 6,300.0 | 14.86 | 60.89 | 6,131.5 | 649.6 | 1,166.7 | 1,335.4 | 0.00 | 0.00 | 0.00 |
| 6,400.0 | 14.86 | 60.89 | 6,228.1 | 662.1 | 1,189.1 | 1,361.0 | 0.00 | 0.00 | 0.00 |
| 6,500.0 | 14.86 | 60.89 | 6,324.8 | 674.5 | 1,211.5 | 1,386.7 | 0.00 | 0.00 | 0.00 |
| 6,600.0 | 14.86 | 60.89 | 6,421.4 | 687.0 | 1,233.9 | 1,412.3 | 0.00 | 0.00 | 0.00 |
| 6,629.6 | 14.86 | 60.89 | 6,450.0 | 690.7 | 1,240.6 | 1,419.9 | 0.00 | 0.00 | 0.00 |

| Targets | | | | | | | | | |
|------------------------|---------------|--------------|----------|------------|------------|---------------|--------------|-----------------|-------------------|
| Target Name | Dip Angle (°) | Dip Dir. (°) | TVD (ft) | +N/-S (ft) | +E/-W (ft) | Northing (ft) | Easting (ft) | Latitude | Longitude |
| - hit/miss target | | | | | | | | | |
| - Shape | | | | | | | | | |
| N-25-8-17 TGT | 0.00 | 0.00 | 5,100.0 | 516.5 | 927.6 | 7,204,960.36 | 2,071,433.29 | 40° 5' 21.446 N | 109° 57' 33.571 W |
| - plan hits target | | | | | | | | | |
| - Circle (radius 75.0) | | | | | | | | | |

API Well Number: 43047516490000





Project: USGS Myton SW (UT)
 Site: SECTION 25 T8S, R17
 Well: N-25-8-17
 Wellbore: Wellbore #1
 Design: Design #1



Azimuths to Grid North
 True North: -0.98°
 Magnetic North: 10.36°

Magnetic Field
 Strength: 52364.4snT
 Dip Angle: 65.86°
 Date: 2010/12/03
 Model: IGRF2010

KOP @ 600'
 DOGLEG RATE 1.5 DEG/100
 TARGET RADIUS IS 75'

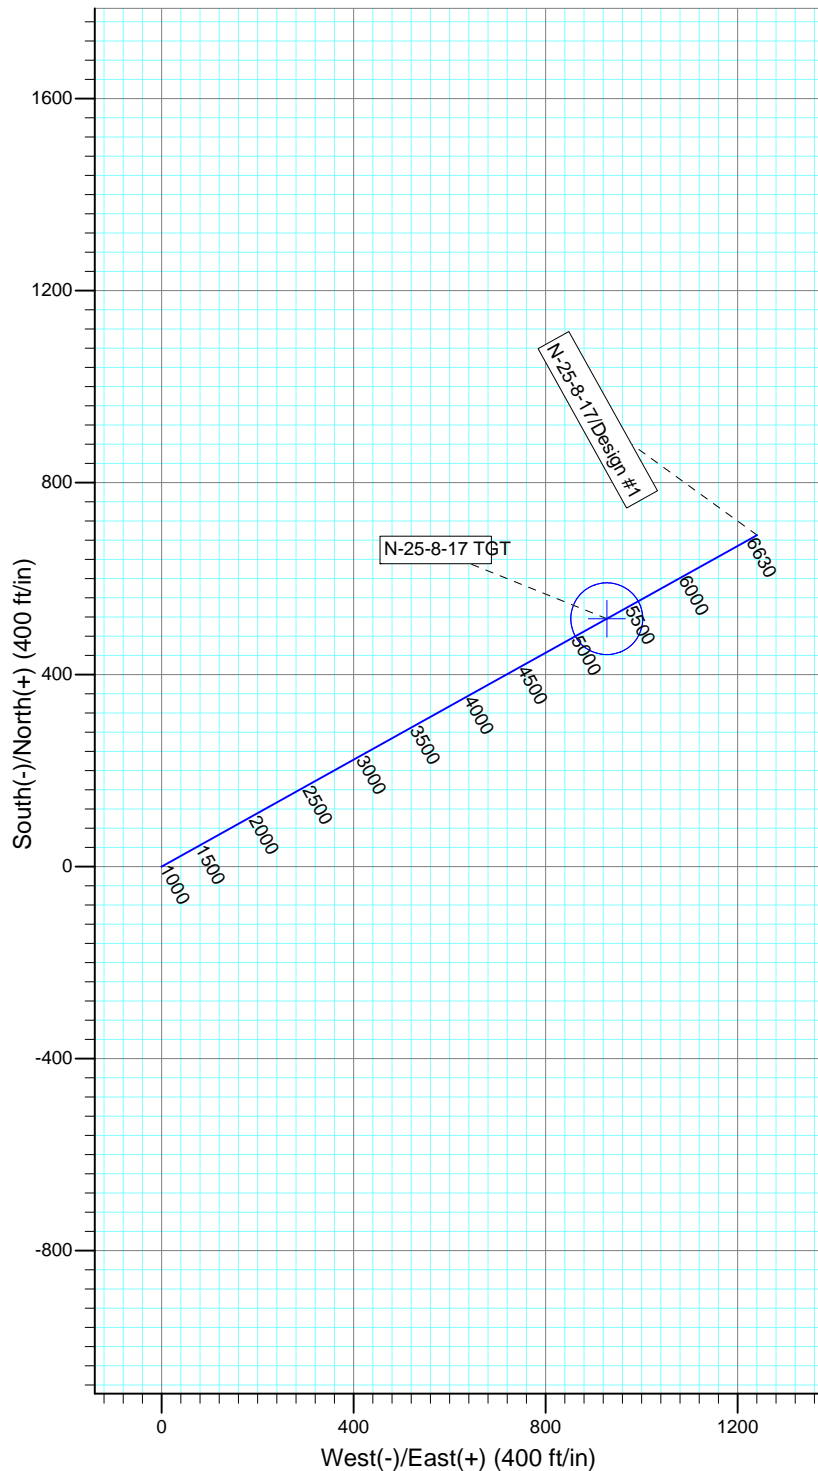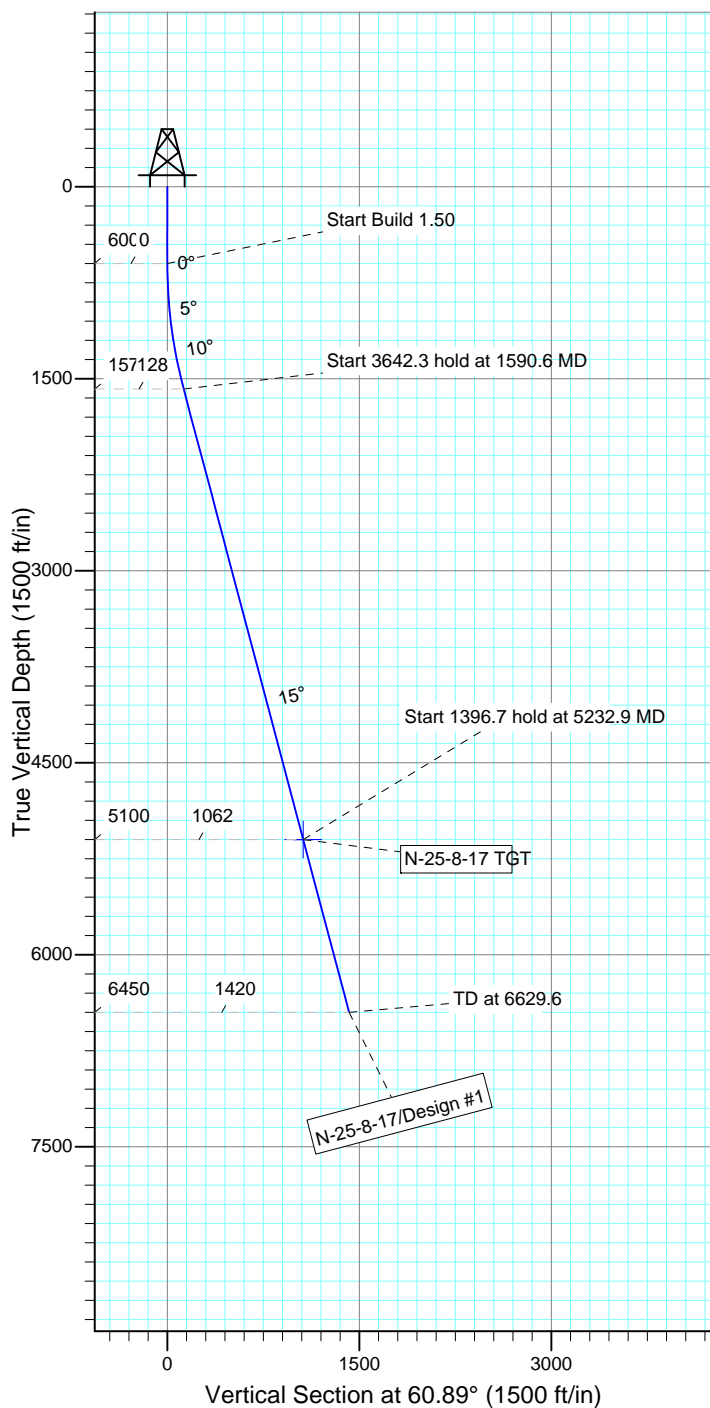

WELLBORE TARGET DETAILS

| Name | TVD | +N/-S | +E/-W | Shape |
|---------------|--------|-------|-------|-----------------------|
| N-25-8-17 TGT | 5100.0 | 516.5 | 927.6 | Circle (Radius: 75.0) |

SECTION DETAILS

| Sec | MD | Inc | Azi | TVD | +N/-S | +E/-W | DLeg | TFace | VSec | Target |
|-----|--------|-------|-------|--------|-------|--------|------|-------|--------|---------------|
| 1 | 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.0 | |
| 2 | 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.0 | |
| 3 | 1590.6 | 14.86 | 60.89 | 1579.5 | 62.1 | 111.6 | 1.50 | 60.89 | 127.7 | |
| 4 | 5232.9 | 14.86 | 60.89 | 5100.0 | 516.5 | 927.6 | 0.00 | 0.00 | 1061.7 | N-25-8-17 TGT |
| 5 | 6629.6 | 14.86 | 60.89 | 6450.0 | 690.7 | 1240.6 | 0.00 | 0.00 | 1419.9 | |



RECEIVED: Jun. 20, 2011

**NEWFIELD PRODUCTION COMPANY
GMBU N-25-8-17
AT SURFACE: NW/SW SECTION 25, T8S, R17E
UINTAH COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site GMBU N-25-8-17 located in the NW 1/4 SW 1/4 Section 25, T8S, R17E, Uintah County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.4 miles \pm to the junction of this highway and UT State Hwy 53; proceed in a southeasterly direction - 6.8 miles to it's junction with an existing dirt road to the east; proceed in a easterly direction - 3.0 miles to it's junction with an existing road to the northeast; proceed in a northeasterly direction - 0.3 miles to it's junction with an existing road to the southeast; proceed in a southeasterly direction approximately 2.5 miles to it's junction with an existing road to the southwest; proceed in a southwesterly direction approximately 0.6 miles to it's junction with the beginning of the access road to the existing 13-25R-8-17 well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

There is no proposed access road for this location. The proposed well will be drilled directionaly off of the existing 13-25R-8-17 well pad. See attached **Topographic Map "B"**.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District
Water Right : 43-10136

Maurice Harvey Pond
Water Right: 47-1358

Neil Moon Pond
Water Right: 43-11787

Newfield Collector Well
Water Right: 47-1817 (A30414DVA, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – Bureau of Land Management.

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. State of Utah Antiquities Project Permit #U-11-MQ-0009b 1/12/11, prepared by Montgomery Archaeological Consultants. Paleontological Resource Survey prepared by, Wade E. Miller, 4/27/11. See attached report cover pages, Exhibit "D".

Newfield Production Company requests 103' of buried water line to be granted for the proposed GMBU N-25-8-17.

It is proposed that the disturbed area will be 30' wide to allow for construction of the proposed buried 10" steel water injection line and a buried 3" poly water return line. The proposed buried water lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** The proposed water pipelines will be buried in a 4-5' deep trench constructed with a trencher or backhoe for the length of the proposal. The equipment will run on the surface and not be flat bladed to minimize surface impacts to precious topsoil in these High Desert environments. If possible, all proposed surface gas pipelines will be installed on the same side of the road as existing gas lines. The construction phase of the proposed water lines will last approximately (5) days.

In the event that the proposed well is converted to a water injection well, a Sundry Notice 3160-5 form will be applied for through the Bureau of Land Management field office.

For a ROW plan of development, please refer to the Greater Monument Butte Green River Development SOP and as well as the Castle Peak and Eight Mile Flat Reclamation and Weed Management Plan.

Surface Flow Line

Newfield requests 101' of surface flow line be granted. The Surface Flow Line will consist of up to a 14" bundled pipe consisting of 2-2" poly glycol lines and 1-3" production line. For all new wells, Newfield. **Refer to Topographic Map "C"** for the proposed location of the proposed flow line. Flow lines will be tan and will be constructed using the following procedures:

Clearing and Grading: No clearing or grading of the ROW will be required. The centerline of the proposed route will be staked prior to installation. Flow lines shall be placed as close to existing roads as possible without interfering with normal road travel or road maintenance activities. Due to the proximity of existing facilities, no temporary use or construction/storage areas are anticipated. If necessary, temporary use or construction/storage areas will be identified on a topographic map included in the approved permit.

Installation: The proposed flow lines will be installed 4-6" above the ground. For portions along existing two-track and primary access roads, lengths of pipe will be strung out in the borrow ditch, welded together, and rolled or dragged into place with heavy equipment. For pipelines that are installed cross-country (not along existing or proposed roads), travel along the lines will be infrequent and for maintenance needs only. No installation activities will be performed during periods when the soil is too wet to adequately support installation equipment. If such equipment creates ruts in excess of three (3) inches deep, the soil will be deemed too wet to adequately support the equipment.

Termination and Final Reclamation: After abandonment of the associated production facilities, the flow lines will be cut and removed, and any incidental surface disturbance reclaimed. Reclamation procedures will follow those outlined in the Castle Peak and Eight Mile Flat Reclamation and Weed Management Plan.

Water Disposal

After first production, if the production water meets quality guidelines, it will be transported to the Ashley, Monument Butte, Jonah, South Wells Draw and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project. Water not meeting quality criteria, will be disposed at Newfield's Pariette #4

disposal well (Sec. 7, T9S R19E), Federally approved surface disposal facilities or at a State of Utah approved surface disposal facilities.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Details of the On-Site Inspection

The proposed GMBU N-25-8-17 was on-sited on 1/26/11. The following were present; Tim Eaton (Newfield Production), Janna Simonsen (Bureau of Land Management), and Suzanne Grayson (Bureau of Land Management).

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the GMBU N-25-8-17, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the GMBU N-25-8-17, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**
Representative

Name: Tim Eaton
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #N-25-8-17, Section 25, Township 8S, Range 17E: Lease UTU-67845 Uintah County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

6/1/11
Date

Mandie Crozier
Regulatory Specialist
Newfield Production Company

2-M SYSTEM

Blowout Prevention Equipment Systems

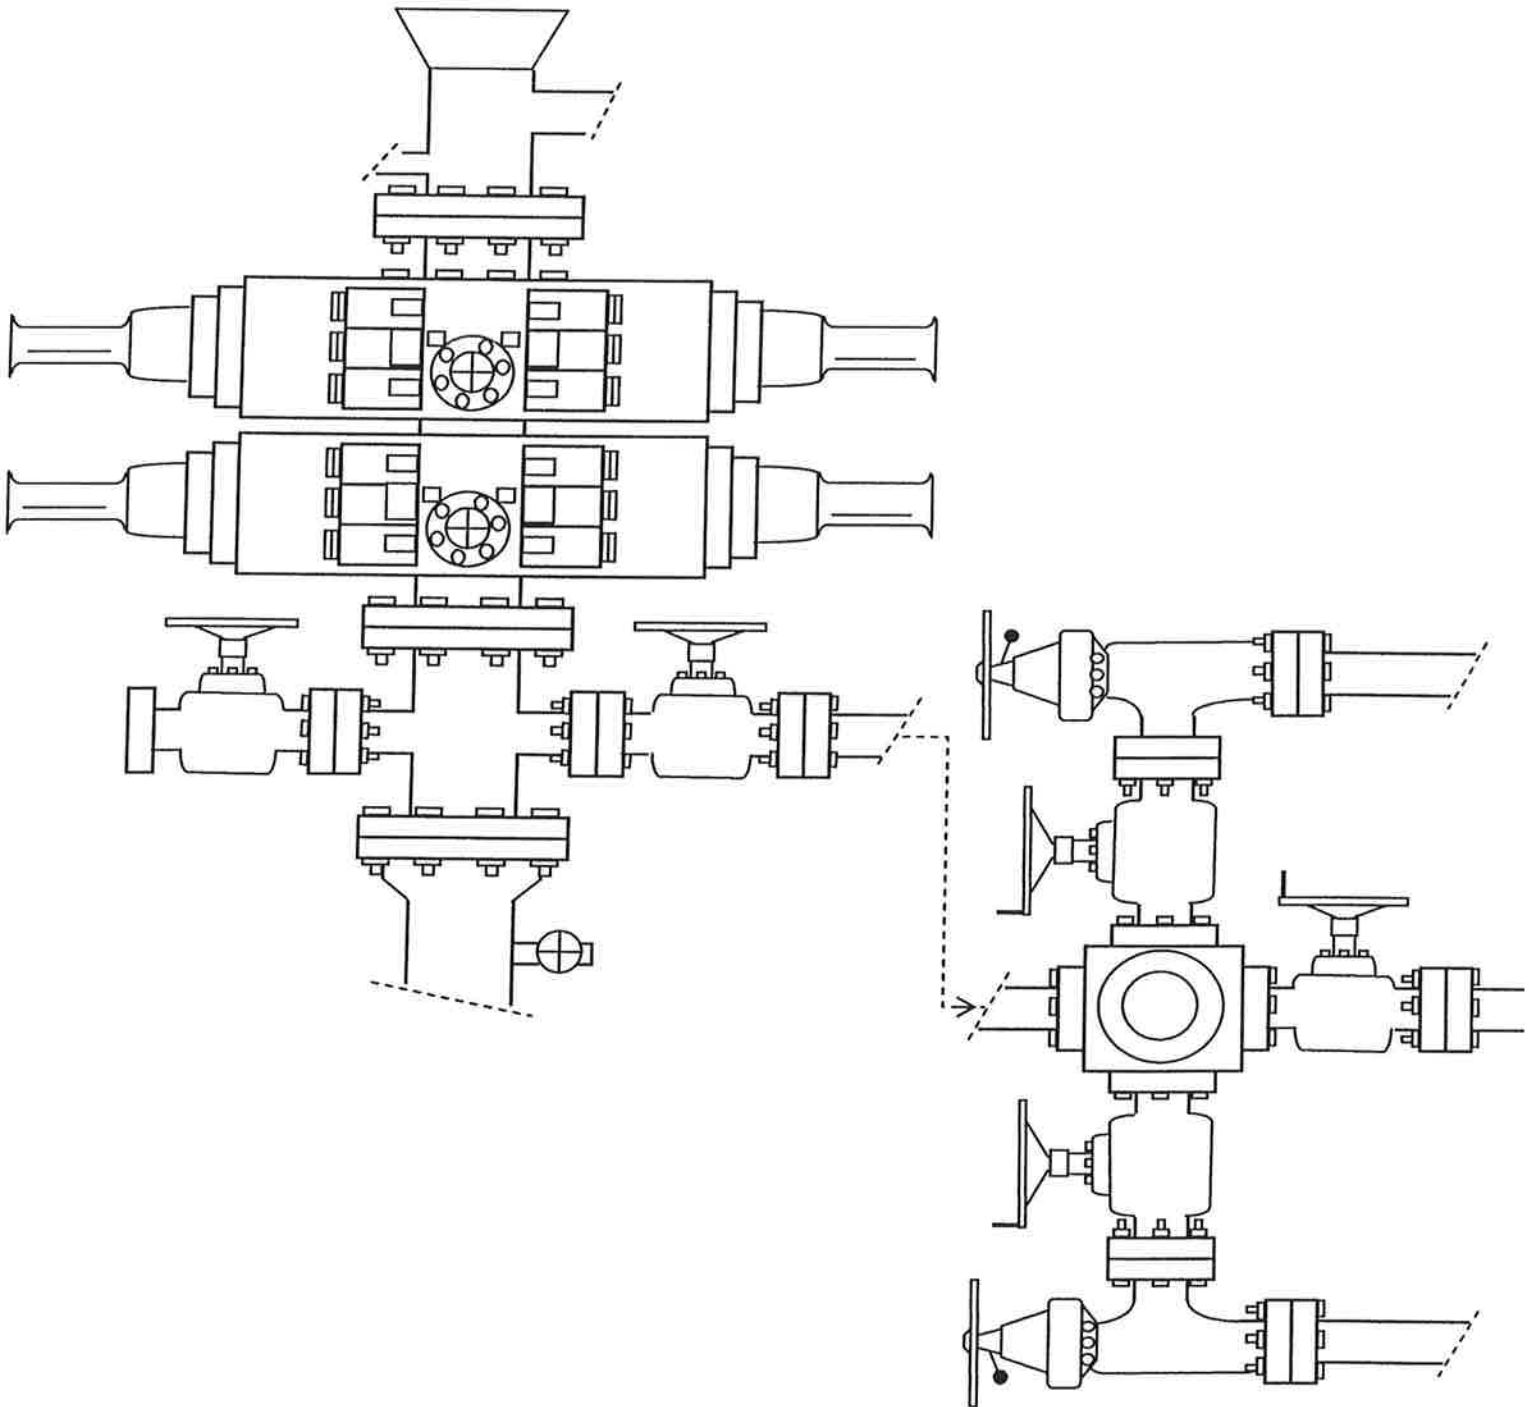


EXHIBIT C

NEWFIELD EXPLORATION COMPANY

WELL PAD INTERFERENCE PLAT

N-25-8-17 (Proposed Well)

13-25R-8-17 (Existing Well)

Pad Location: NWSW Section 25, T8S, R17E, S.L.B.&M.




TOP HOLE FOOTAGES

N-25-8-17 (PROPOSED)
2265' FSL & 464' FWL

CENTER OF PATTERN FOOTAGES

N-25-8-17 (PROPOSED)
2535' FNL & 1400' FWL

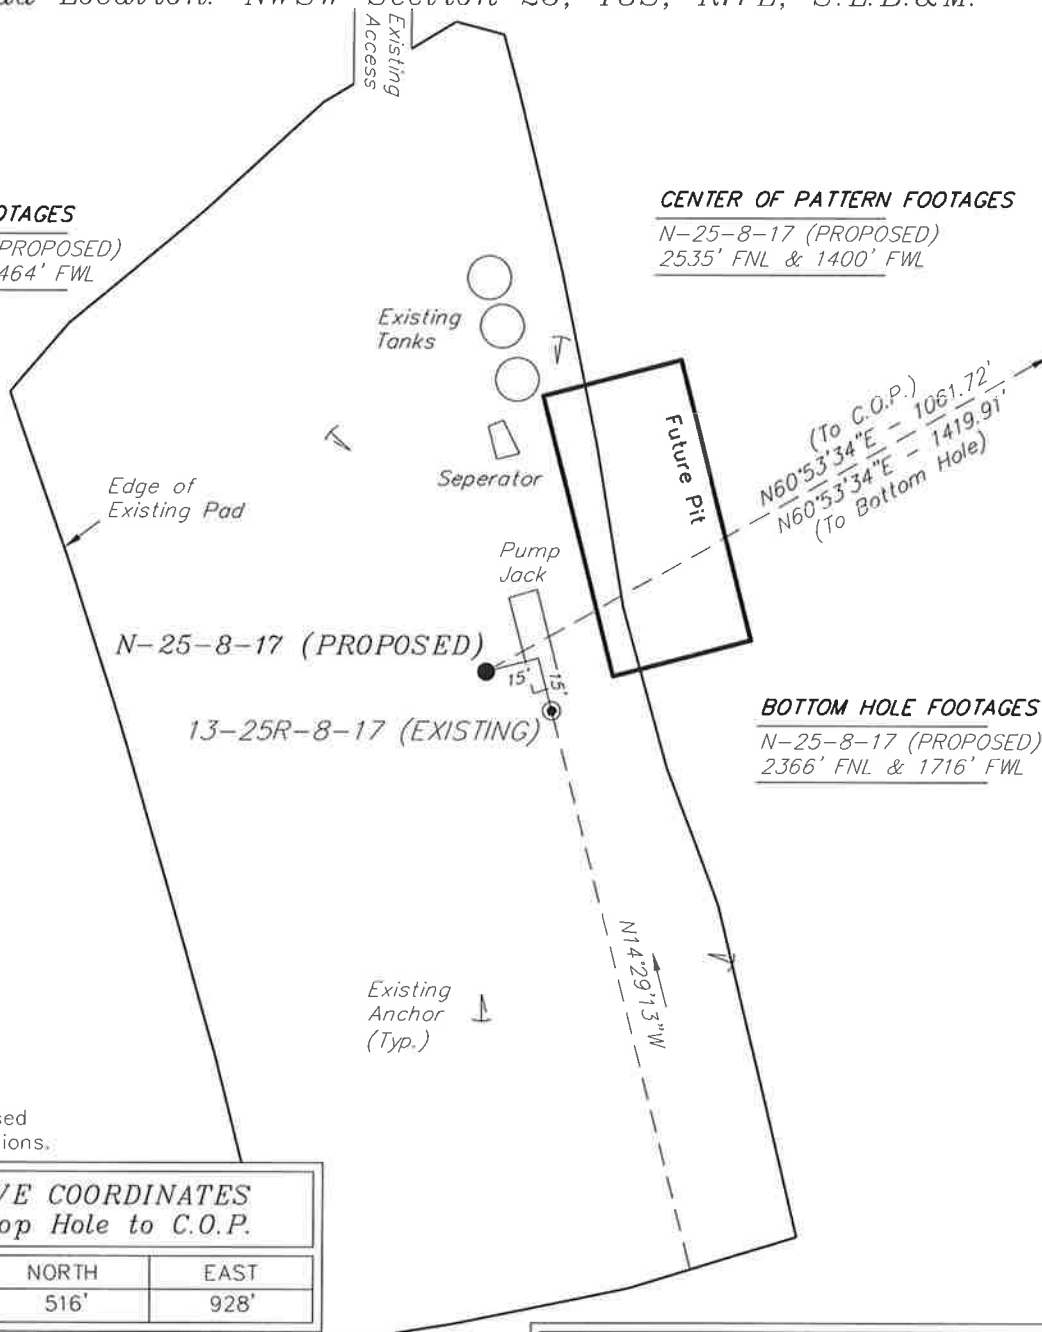

Note:

Bearings are based
on GPS Observations.

RELATIVE COORDINATES From Top Hole to C.O.P.

| WELL | NORTH | EAST |
|-----------|-------|------|
| N-25-8-17 | 516' | 928' |

RELATIVE COORDINATES From Top Hole to Bottom Hole

| WELL | NORTH | EAST |
|-----------|-------|--------|
| N-25-8-17 | 691' | 1,241' |

LATITUDE & LONGITUDE Surface position of Wells (NAD 83)

| WELL | LATITUDE | LONGITUDE |
|-------------|----------------|-----------------|
| N-25-8-17 | 40° 05' 16.50" | 109° 57' 45.62" |
| 13-25R-8-17 | 40° 05' 16.39" | 109° 57' 45.39" |

| | |
|-------------------|-------------------------|
| SURVEYED BY: D.G. | DATE SURVEYED: 10-09-10 |
| DRAWN BY: M.W. | DATE DRAWN: 12-14-10 |
| SCALE: 1" = 50' | REVISED: |

Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078


NEWFIELD EXPLORATION COMPANY

LOCATION LAYOUT

N-25-8-17 (Proposed Well)

13-25R-8-17 (Existing Well)

Pad Location: NWSW Section 25, T8S, R17E, S.L.B.&M.

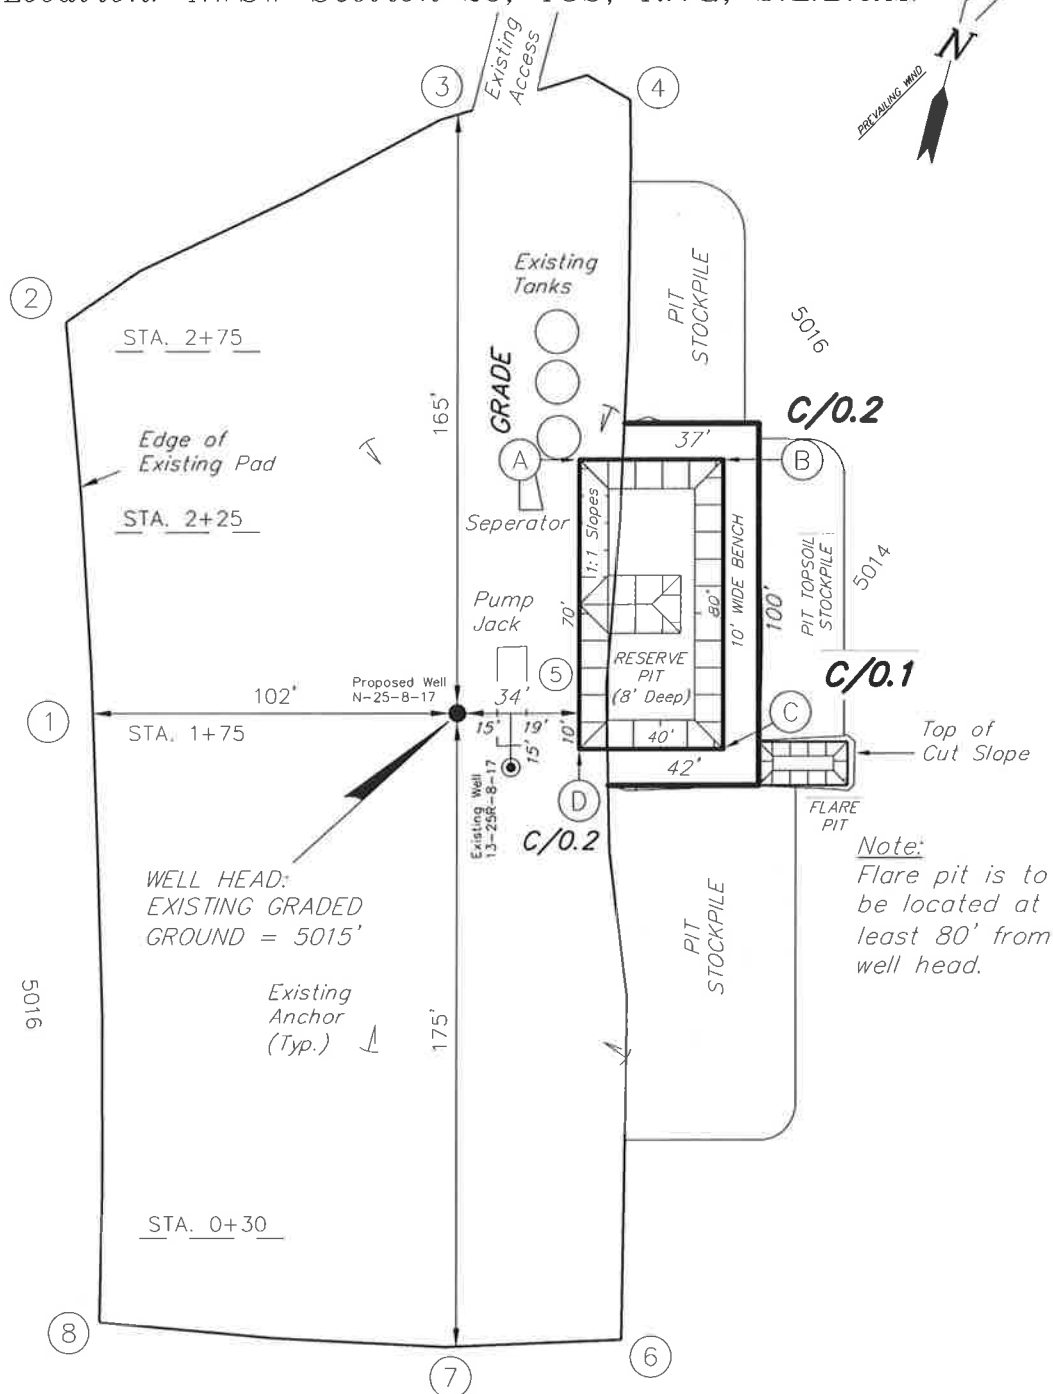

SURVEYED BY: D.G.

DATE SURVEYED: 10-09-10

DRAWN BY: M.W.

DATE DRAWN: 12-14-10

SCALE: 1" = 50'

REVISED:

Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078


NEWFIELD EXPLORATION COMPANY

CROSS SECTIONS

N-25-8-17 (Proposed Well)

13-25R-8-17 (Existing Well)

Pad Location: NWSW Section 25, T8S, R17E, S.L.B.&M.

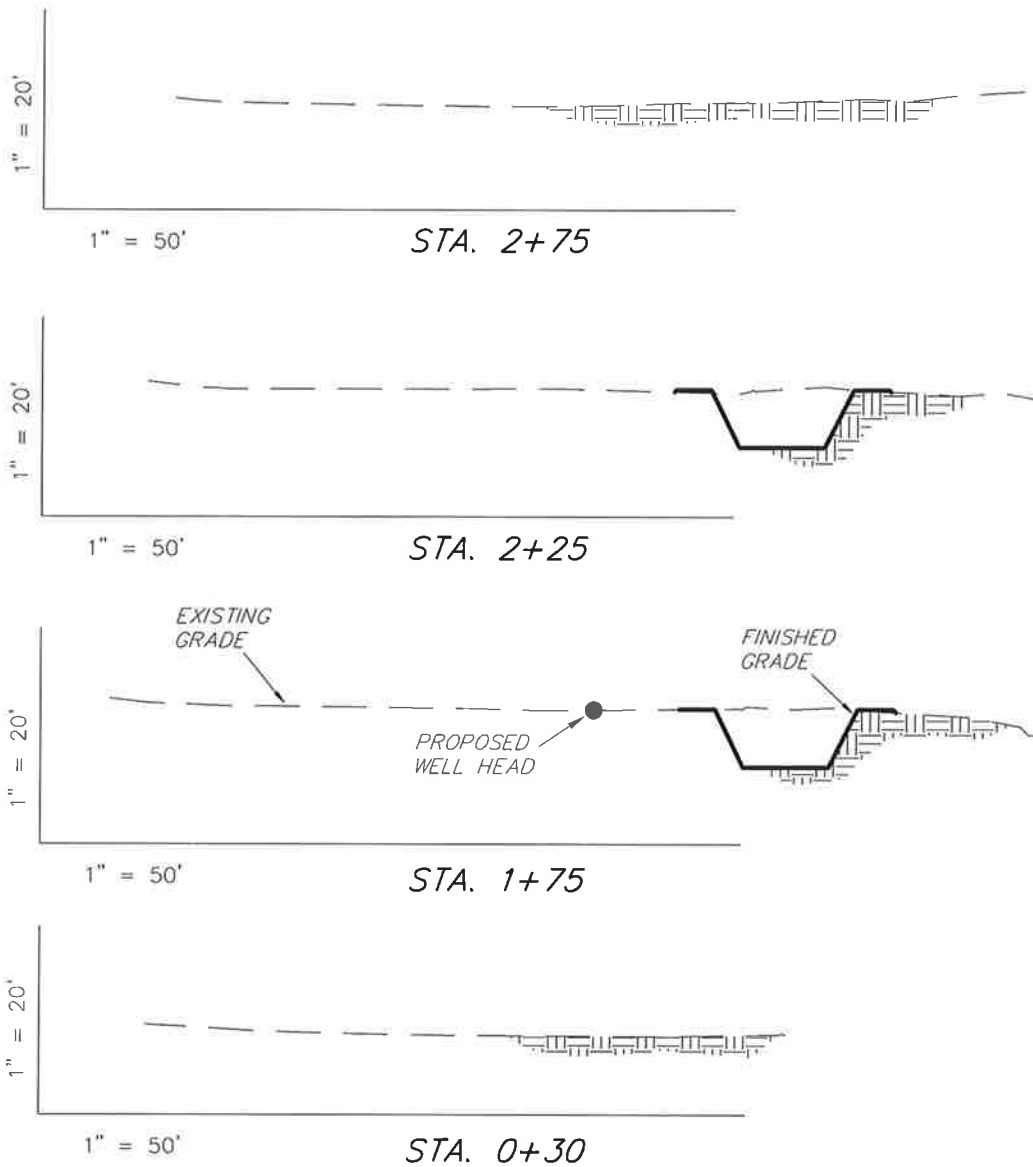

NOTE:
UNLESS OTHERWISE NOTED
CUT SLOPES ARE AT 1:1
FILL SLOPES ARE AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards)

| ITEM | CUT | FILL | 6" TOPSOIL | EXCESS |
|--------|-----|------|--|--------|
| PAD | 0 | 20 | Topsoil is not included in Pad Cut | -20 |
| PIT | 640 | 0 | | 640 |
| TOTALS | 640 | 20 | 120 | 620 |

SURVEYED BY: D.G. DATE SURVEYED: 10-09-10
 DRAWN BY: M.W. DATE DRAWN: 12-14-10
 SCALE: 1" = 50' REVISED:

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078


NEWFIELD EXPLORATION COMPANY

TYPICAL RIG LAYOUT

N-25-8-17 (Proposed Well)

13-25R-8-17 (Existing Well)

Pad Location: NWSW Section 25, T8S, R17E, S.L.B.&M.

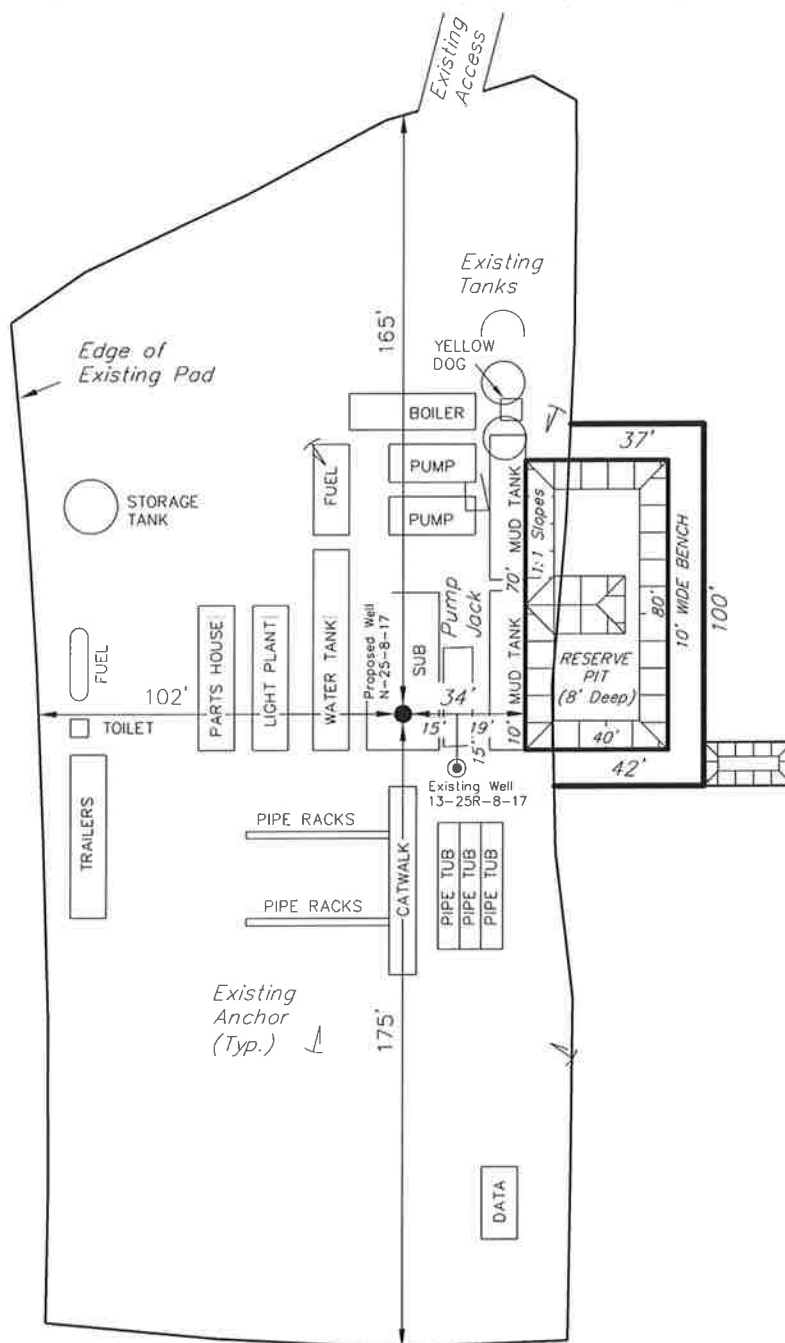

| | |
|-------------------|-------------------------|
| SURVEYED BY: D.G. | DATE SURVEYED: 10-09-10 |
| DRAWN BY: M.W. | DATE DRAWN: 12-14-10 |
| SCALE: 1" = 50' | REVISED: |

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

VIA ELECTRONIC DELIVERY



June 7, 2011

State of Utah, Division of Oil, Gas and Mining
ATTN: Diana Mason
P.O. Box 145801
Salt Lake City, UT 84114-5801

RE: Directional Drilling
GMBU N-25-8-17
Greater Monument Butte (Green River) Unit

Surface Hole: T8S-R17E Section 25: NWSW (UTU-67845)
2265' FSL 464' FWL

At Target: T8S-R17E Section 25: SENW (UTU-67845)
2366' FNL 1716' FWL

Uintah County, Utah

Dear Ms. Mason:

Pursuant to the filing by Newfield Production Company ("NPC") of an Application for Permit to Drill the above referenced well dated 6/1/2011, a copy of which is attached, and in accordance with Oil and Gas Conservation Rule R649-3-11, NPC hereby submits this letter as notice of our intention to directionally drill this well.

The surface hole and target locations of this well are both within the boundaries of the Greater Monument Butte Unit (UTU-87538X), of which Newfield certifies that it is the operator. Further, Newfield certifies that all lands within 460 feet of the entire directional well bore are within the Greater Monument Butte Unit.

NPC is permitting this well as a directional well in order to mitigate surface disturbance by utilizing pre-existing roads and pipelines.

NPC hereby requests our application for permit to drill be granted pursuant to R649-3-11. If you have any questions or require further information, please contact the undersigned at 303-383-4153 or by email at pburns@newfield.com. Your consideration in this matter is greatly appreciated.

Sincerely,
Newfield Production Company

A handwritten signature in blue ink, appearing to read "Peter Burns".

Peter Burns
Land Associate

Form 3160-3
(August 2007)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
APPLICATION FOR PERMIT TO DRILL OR REENTER


FORM APPROVED
OMB No 1004-0137
Expires July 31, 2010

| | | |
|--|--|---|
| 1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER 1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone 2. Name of Operator Newfield Production Company 3a. Address Route #3 Box 3630, Myton UT 84052 3b. Phone No. (include area codes) (435) 646-3721 4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NW/SW 2265' FSL 464' FWL Sec. 25, T8S R17E (UTU-67845) At proposed prod. zone SE/NW 2366' FNL 1716' FWL Sec. 25, T8S R17E (UTU-67845) 14. Distance in miles and direction from nearest town or post office* Approximately 14.7 miles southeast of Myton, UT 15. Distance from proposed* location to nearest property or lease line, ft. Approx. 2,366' f/lse, NA f/unit (Also to nearest drig. unit line, if any) 16. No. of acres in lease 560.00 17. Spacing Unit dedicated to this well 20 Acres 18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 756' 19. Proposed Depth 6,630' 20. BLM/BIA Bond No. on file WYB000493 21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5015' GL 22. Approximate date work will start* 3rd Sept. 2011 23. Estimated duration (7) days from SPUD to rig release | | 5. Lease Serial No. UTU-67845 6. If Indian, Allottee or Tribe Name NA 7. If Unit or CA Agreement, Name and No. Greater Monument Butte 8. Lease Name and Well No. GMBU N-25-8-17 9. API Well No. 10. Field and Pool, or Exploratory Monument Butte 11. Sec., T. R. M. or Blk. and Survey or Area Sec. 25, T8S R17E 12. County or Parish Utah 13. State UT |
|--|--|---|

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- | | |
|---|---|
| 1. Well plat certified by a registered surveyor. 2. A Drilling Plan. 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). 5. Operator certification 6. Such other site specific information and/or plans as may be required by the BLM. |
|---|---|

| | | |
|--|---|------------------------|
| 25. Signature  Title Regulatory Specialist | Name (Printed Typed) Mandie Crozier | Date 6/11/11 |
| Approved by (Signature) Title | Name (Printed Typed) Office | Date |

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
 Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)


T8S, R17E, S.L.B.&M.

N89°58'W - 79.90 (G.L.O.)

NEWFIELD EXPLORATION COMPANY

WELL LOCATION, N-25-8-17, LOCATED AS SHOWN IN THE NW 1/4 SW 1/4 OF SECTION 25, T8S, R17E, S.L.B.&M. UTAH COUNTY, UTAH.


TARGET BOTTOM HOLE, N-25-8-17, LOCATED AS SHOWN IN THE SE 1/4 NW 1/4 OF SECTION 25, T8S, R17E, S.L.B.&M. UTAH COUNTY, UTAH.

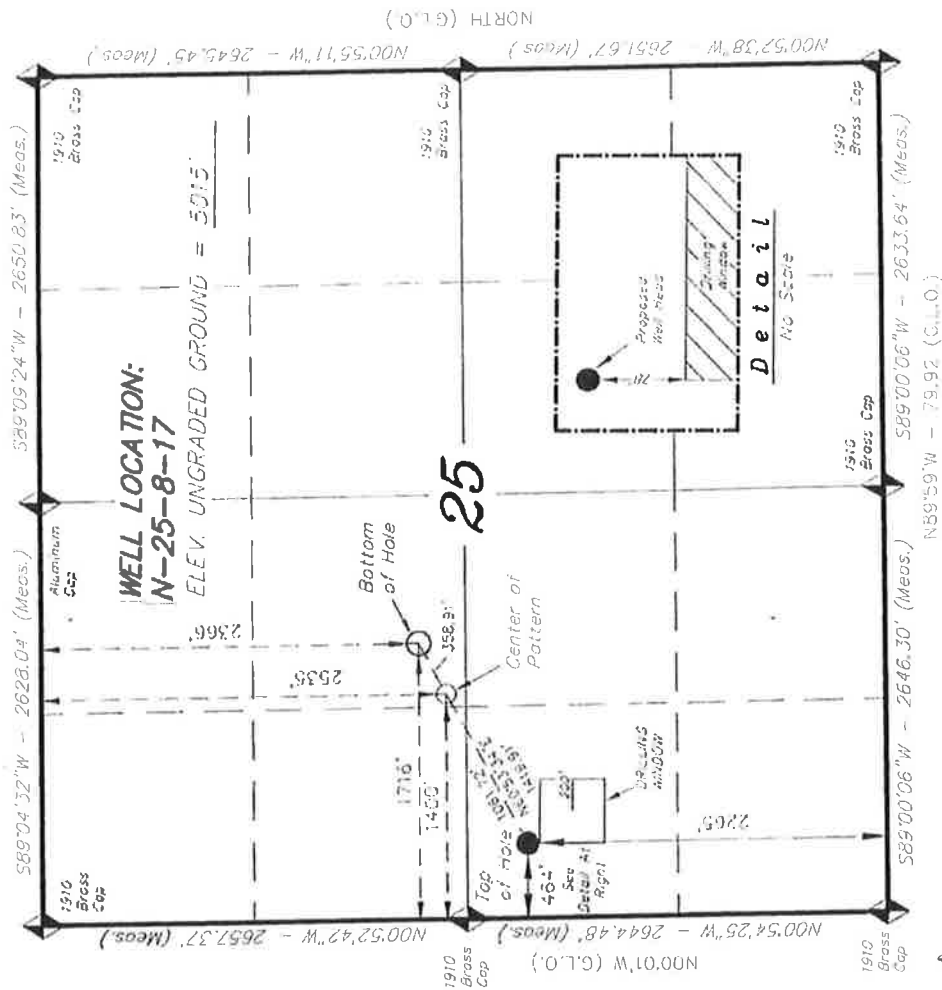

SECTION CORNERS LOCATED

BASIS OF ELEV. Elevations are base on LOCATION: on N.G.S. OPUS Correction, LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'

N-25-8-17
(Surface Location) NAD 83
LATITUDE = 40° 05' 16.50"
LONGITUDE = 109° 57' 45.62"

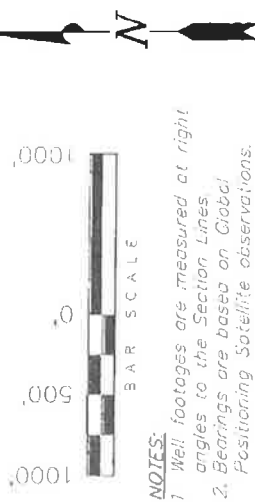


- NOTES:**
1. Well footages are measured at right angles to the Section Lines.
 2. Bearings are based on Global Positioning Satellite observations.


THIS IS TO CERTIFY THAT THE SURVEY WAS PREPARED FROM FIELD NOTES AND SURVEYS MADE BY ME OR UNDER MY SUPERVISION THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

STACY W. STEWART
REGISTERED LAND SURVEYOR
REG. NO. 189377
STATE OF UTAH

TRI STATE LAND SURVEYING & CONSULTING
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 761-2501

| | |
|----------------|-------------------|
| DATE SURVEYED: | SURVEYED BY: J.G. |
| 10-09-10 | |
| DATE DRAWN: | DRAWN BY: M.W. |
| 12-13-10 | |
| REVISED: | SCALE: 1" = 1000' |

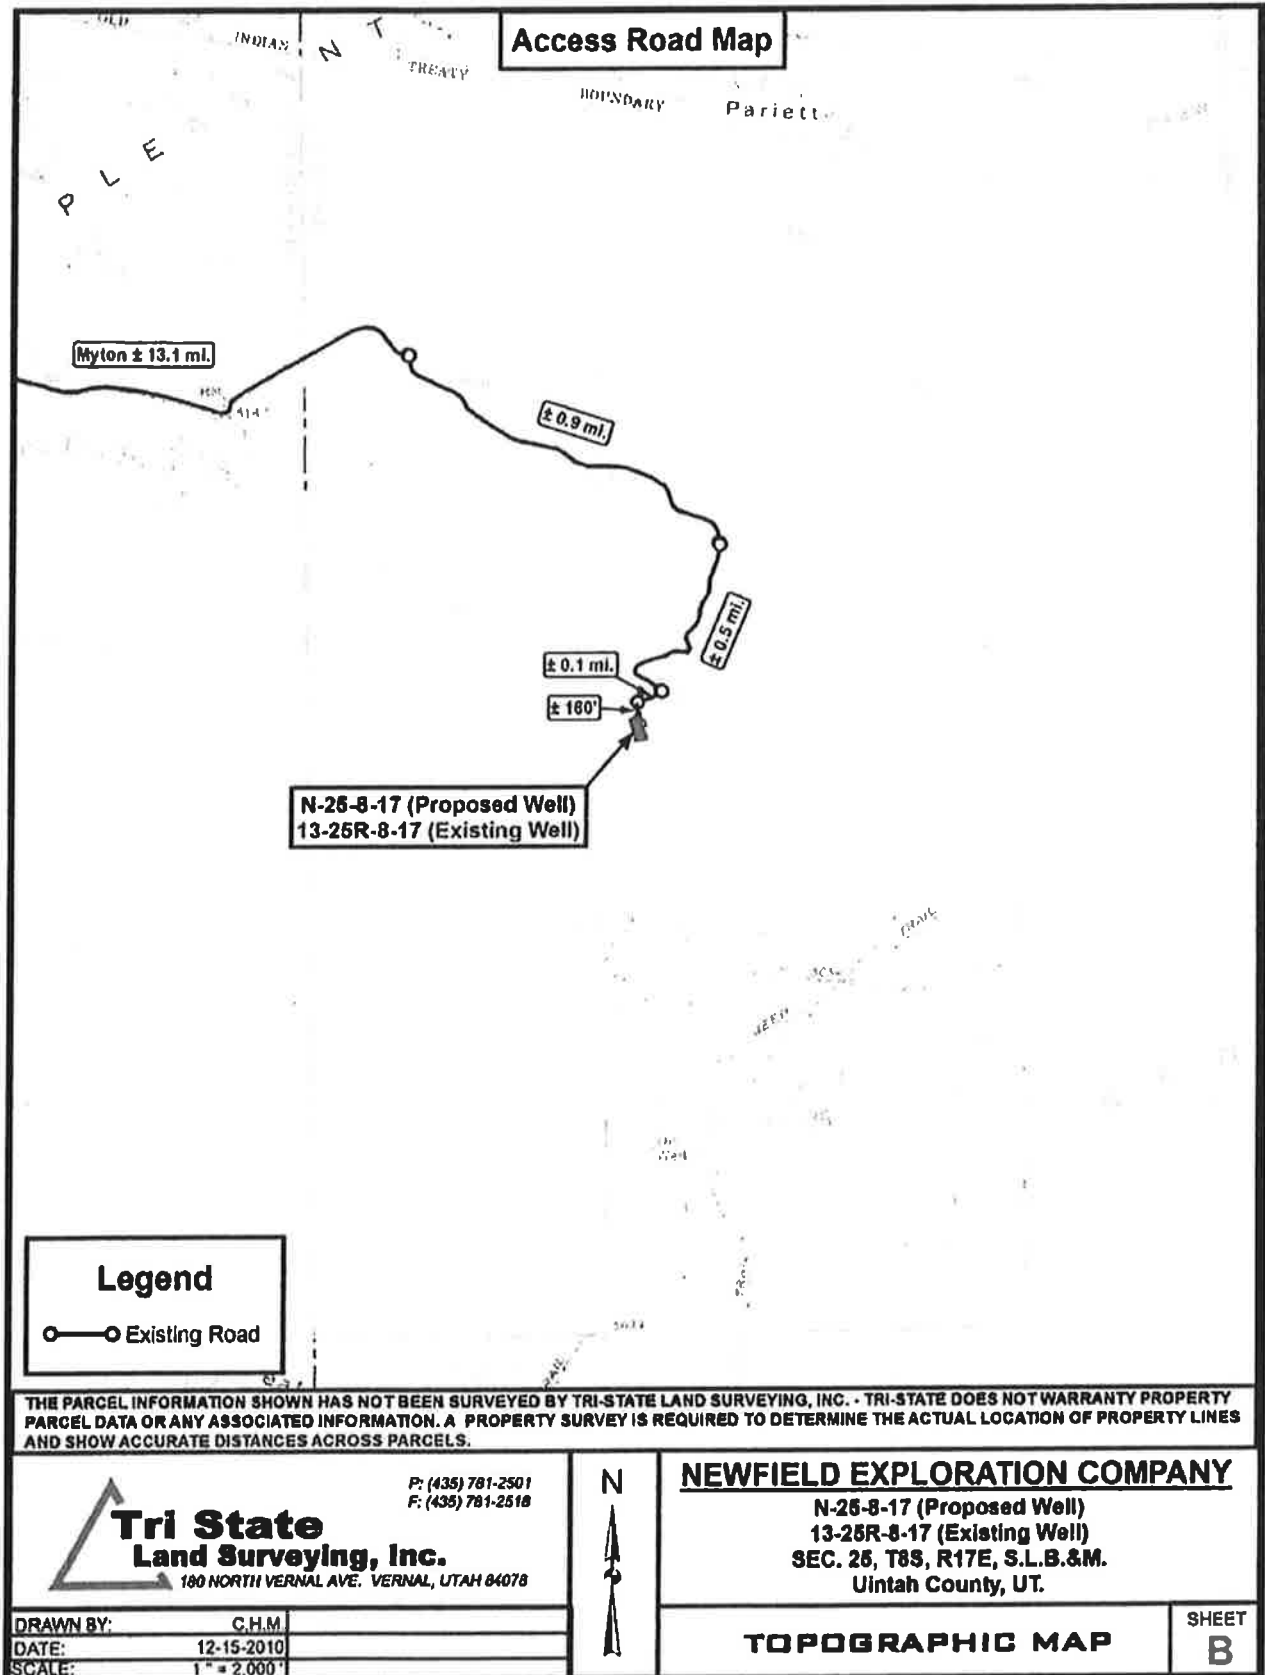


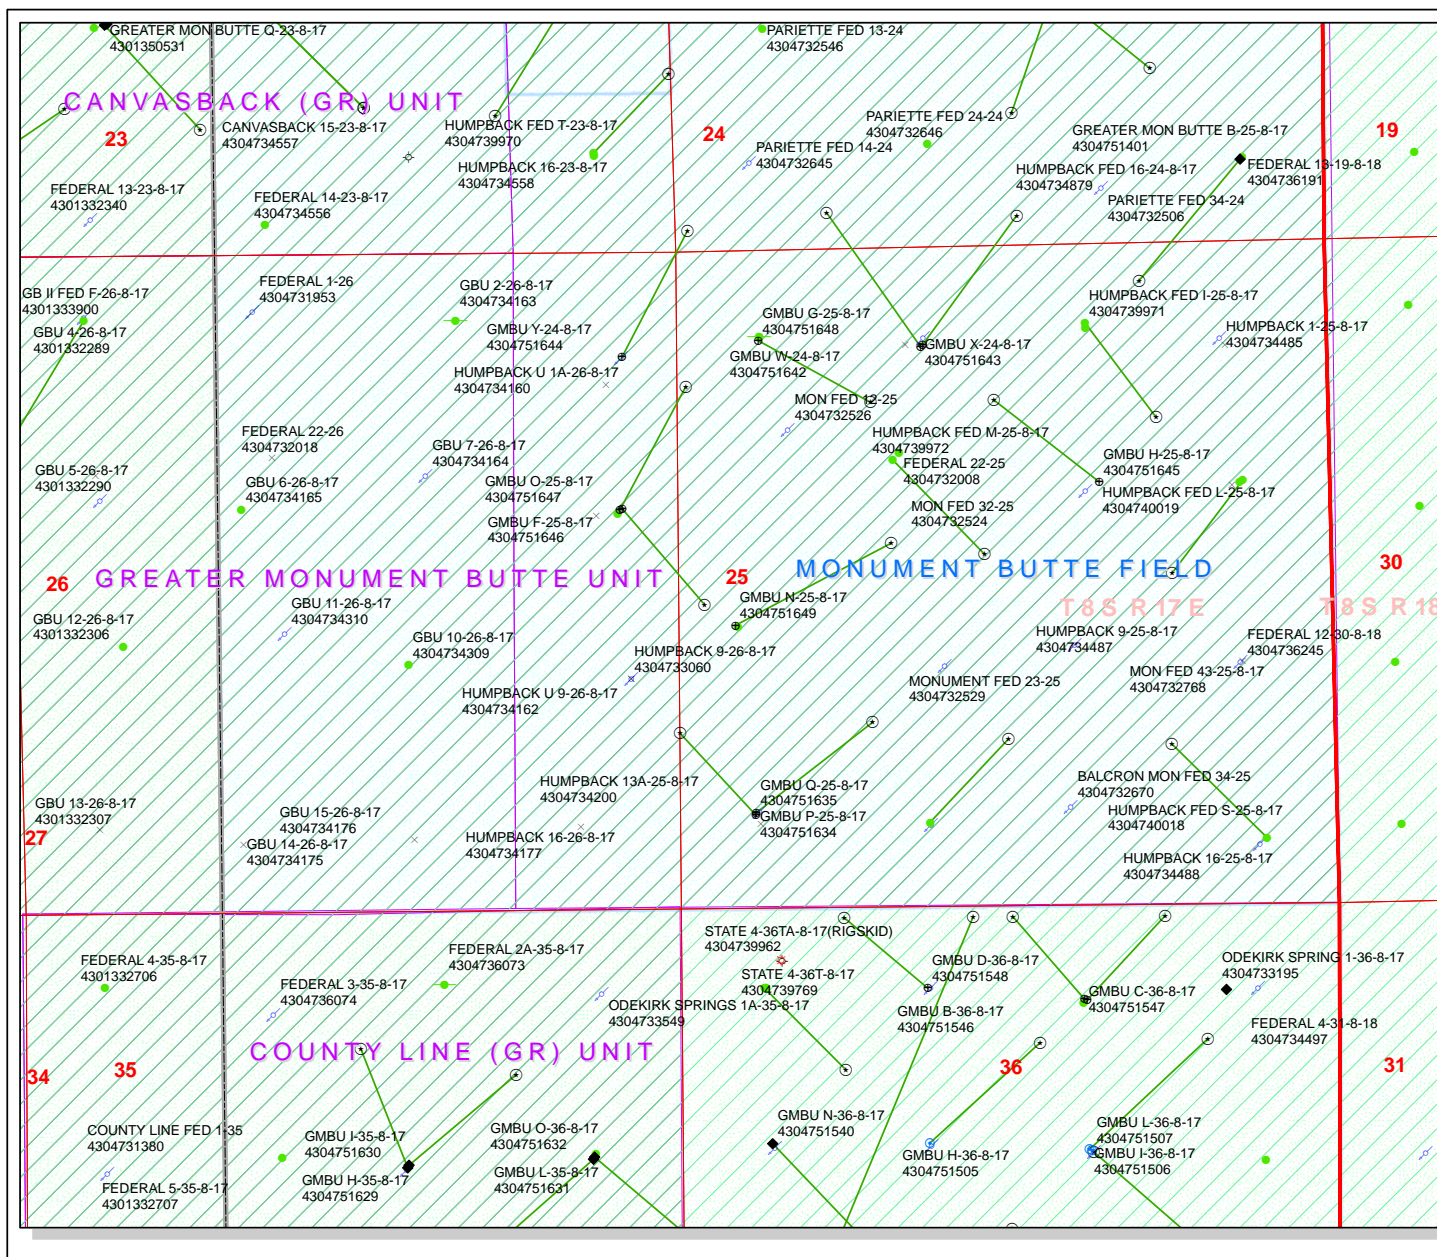

API Number: 4304751649
Well Name: GMBU N-25-8-17
Township T08. Range R17. Section 25
Meridian: SLBM
Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
 Map Produced by Diana Mason

| Units | Wells Query |
|---------------|------------------------------------|
| STATUS | STATUS |
| ACTIVE | APD - Approved Permit |
| EXPLORATORY | DRL - Spudded (Drilling Commenced) |
| GAS STORAGE | GIW - Gas Injection |
| NF PP OIL | GS - Gas Storage |
| NF SECONDARY | LA - Location Abandoned |
| PI OIL | LOC - New Location |
| PP GAS | OPS - Operation Suspended |
| PP GEOTHERMAL | PA - Plugged Abandoned |
| PP OIL | PGW - Producing Gas Well |
| SECONDARY | POW - Producing Oil Well |
| TERMINATED | RET - Returned APD |
| Fields | SGW - Shut-in Gas Well |
| Unknown | SOW - Shut-in Oil Well |
| ABANDONED | TA - Temp. Abandoned |
| ACTIVE | TW - Test Well |
| COMBINED | WDW - Water Disposal |
| INACTIVE | WWI - Water Injection Well |
| STORAGE | WSW - Water Supply Well |
| TERMINATED | |
| Sections | |
| Township | |



United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office

P.O. Box 45155

Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:

3160

(UT-922)

June 10, 2011

Memorandum

To: Assistant District Manager Minerals, Vernal District

From: Michael Coulthard, Petroleum Engineer

Subject: 2011 Plan of Development Greater Monument
Butte Unit, Duchesne and Uintah Counties,
Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2011 within the Greater Monument Butte Unit, Duchesne and Uintah Counties, Utah.

| API# | WELL NAME | LOCATION |
|------|-----------|----------|
|------|-----------|----------|

(Proposed PZ GREEN RIVER)

| | | |
|--------------|---|--|
| 43-047-51638 | GMBU G-24-8-17 Sec 24 T08S R17E 1528 FNL 0508 FWL | |
| | BHL Sec 24 T08S R17E 0682 FNL 1125 FWL | |

| | | |
|--------------|---|--|
| 43-047-51639 | GMBU N-24-8-17 Sec 24 T08S R17E 1543 FNL 0491 FWL | |
| | BHL Sec 24 T08S R17E 2376 FSL 1318 FWL | |

| | | |
|--------------|---|--|
| 43-047-51640 | GMBU S-35-8-17 Sec 35 T08S R17E 1956 FSL 0695 FEL | |
| | BHL Sec 35 T08S R17E 0974 FSL 1549 FEL | |

| | | |
|--------------|---|--|
| 43-047-51641 | GMBU P-36-8-17 Sec 35 T08S R17E 1962 FSL 0675 FEL | |
| | BHL Sec 36 T08S R17E 1157 FSL 0290 FWL | |

| | | |
|--------------|---|--|
| 43-047-51642 | GMBU W-24-8-17 Sec 25 T08S R17E 0771 FNL 1979 FWL | |
| | BHL Sec 24 T08S R17E 0189 FSL 2469 FEL | |

| | | |
|--------------|---|--|
| 43-047-51643 | GMBU X-24-8-17 Sec 25 T08S R17E 0784 FNL 1962 FWL | |
| | BHL Sec 24 T08S R17E 0322 FSL 1215 FWL | |

| | | |
|--------------|---|--|
| 43-047-51644 | GMBU Y-24-8-17 Sec 26 T08S R17E 0846 FNL 0436 FEL | |
| | BHL Sec 24 T08S R17E 0170 FSL 0095 FWL | |

| | | |
|--------------|---|--|
| 43-047-51645 | GMBU H-25-8-17 Sec 25 T08S R17E 1885 FNL 1898 FEL | |
| | BHL Sec 25 T08S R17E 1220 FNL 2553 FWL | |

RECEIVED: Jun. 20, 2011

| API # | WELL NAME | LOCATION |
|---------------------------|----------------|------------------------------------|
| (Proposed PZ GREEN RIVER) | | |
| 43-013-50821 | GMBU Y-35-8-17 | Sec 03 T09S R17E 0769 FNL 0514 FEL |
| | BHL | Sec 35 T08S R17E 0138 FSL 0210 FWL |
| 43-047-51646 | GMBU F-25-8-17 | Sec 26 T08S R17E 2076 FNL 0461 FEL |
| | BHL | Sec 25 T08S R17E 1090 FNL 0075 FWL |
| 43-047-51647 | GMBU O-25-8-17 | Sec 26 T08S R17E 2071 FNL 0441 FEL |
| | BHL | Sec 25 T08S R17E 2433 FSL 0215 FWL |
| 43-047-51648 | GMBU G-25-8-17 | Sec 25 T08S R17E 0723 FNL 0664 FWL |
| | BHL | Sec 25 T08S R17E 1228 FNL 1560 FWL |
| 43-047-51649 | GMBU N-25-8-17 | Sec 25 T08S R17E 2265 FSL 0464 FWL |
| | BHL | Sec 25 T08S R17E 2366 FNL 1716 FWL |
| 43-013-50795 | GMBU X-1-9-16 | Sec 12 T09S R16E 0646 FNL 0645 FWL |
| | BHL | Sec 01 T09S R16E 0079 FSL 1352 FWL |
| 43-013-50796 | GMBU J-11-9-16 | Sec 12 T09S R16E 0641 FNL 0625 FWL |
| | BHL | Sec 11 T09S R16E 1421 FNL 0210 FEL |
| 43-013-50823 | GMBU U-19-8-17 | Sec 29 T08S R17E 0624 FNL 0684 FWL |
| | BHL | Sec 19 T08S R17E 0269 FSL 0276 FEL |
| 43-013-50824 | GMBU S-30-8-17 | Sec 30 T08S R17E 1971 FSL 1996 FEL |
| | BHL | Sec 30 T08S R17E 1023 FSL 1029 FEL |
| 43-013-50825 | GMBU G-33-8-17 | Sec 33 T08S R17E 0537 FNL 1927 FWL |
| | BHL | Sec 33 T08S R17E 1531 FNL 1410 FWL |
| 43-013-50826 | GMBU H-33-8-17 | Sec 33 T08S R17E 0522 FNL 1942 FWL |
| | BHL | Sec 33 T08S R17E 1555 FNL 2440 FEL |
| 43-013-50827 | GMBU E-32-8-17 | Sec 30 T08S R17E 0789 FSL 0478 FEL |
| | BHL | Sec 32 T08S R17E 0128 FNL 0168 FWL |
| 43-013-50828 | GMBU H-31-8-17 | Sec 31 T08S R17E 1936 FNL 1891 FEL |
| | BHL | Sec 31 T08S R17E 1239 FNL 2405 FWL |
| 43-013-50829 | GMBU B-32-8-17 | Sec 29 T08S R17E 0619 FSL 1975 FEL |
| | BHL | Sec 32 T08S R17E 0270 FNL 1223 FEL |
| 43-013-50830 | GMBU C-32-8-17 | Sec 29 T08S R17E 0599 FSL 1982 FEL |
| | BHL | Sec 32 T08S R17E 0181 FNL 2431 FWL |
| 43-013-50831 | GMBU F-32-8-17 | Sec 31 T08S R17E 0682 FNL 0640 FEL |
| | BHL | Sec 32 T08S R17E 1503 FNL 0178 FWL |

| API # | WELL NAME | LOCATION |
|---------------------------|----------------|------------------------------------|
| (Proposed PZ GREEN RIVER) | | |
| 43-013-50832 | GMBU K-32-8-17 | Sec 33 T08S R17E 1831 FNL 0718 FWL |
| | BHL Sec 32 | T08S R17E 2378 FSL 0306 FEL |

This office has no objection to permitting the wells at this time.

Michael L. Coulthard


Digitally signed by Michael L. Coulthard
DN: cn=Michael L. Coulthard, o=Bureau of Land
Management, ou=Branch of Minerals,
email=Michael_Coulthard@blm.gov, c=US
Date: 2011.06.10 13:37:42 -06'00'

bcc: File - Greater Monument Butte Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:6-10-11

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 6/6/2011**API NO. ASSIGNED:** 43047516490000**WELL NAME:** GMBU N-25-8-17**OPERATOR:** NEWFIELD PRODUCTION COMPANY (N2695)**PHONE NUMBER:** 435 646-4825**CONTACT:** Mandie Crozier**PROPOSED LOCATION:** NSW 25 080S 170E**Permit Tech Review:** ☒**SURFACE:** 2265 FSL 0464 FWL**Engineering Review:** ☐**BOTTOM:** 2366 FNL 1716 FWL**Geology Review:** ☒**COUNTY:** UINTAH**LATITUDE:** 40.08788**LONGITUDE:** -109.96195**UTM SURF EASTINGS:** 588497.00**NORTHINGS:** 4437817.00**FIELD NAME:** MONUMENT BUTTE**LEASE TYPE:** 1 - Federal**LEASE NUMBER:** UTU-67845**PROPOSED PRODUCING FORMATION(S):** GREEN RIVER**SURFACE OWNER:** 1 - Federal**COALBED METHANE:** NO**RECEIVED AND/OR REVIEWED:**☒ **PLAT**☒ **Bond:** FEDERAL - WYB000493☐ **Potash**☐ **Oil Shale 190-5**☐ **Oil Shale 190-3**☐ **Oil Shale 190-13**☒ **Water Permit:** 437478☐ **RDCC Review:**☐ **Fee Surface Agreement**☐ **Intent to Commingle****Commingle Approved****LOCATION AND SITING:**☐ **R649-2-3.****Unit:** GMBU (GRRV)☐ **R649-3-2. General**☐ **R649-3-3. Exception**☒ **Drilling Unit****Board Cause No:** Cause 213-11**Effective Date:** 11/30/2009**Siting:** Suspends General Siting☒ **R649-3-11. Directional Drill****Comments:** Presite Completed**Stipulations:**
4 - Federal Approval - dmason
15 - Directional - dmason
27 - Other - bhill**RECEIVED:** Jun. 20, 2011



State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: GMBU N-25-8-17
API Well Number: 43047516490000
Lease Number: UTU-67845
Surface Owner: FEDERAL
Approval Date: 6/20/2011

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 213-11. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

Production casing cement shall be brought up to or above the top of the unitized interval for the Greater Monument Butte Unit (Cause No. 213-11).

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)
OR
submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <http://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "J. Rogers", written over a horizontal line.

For John Rogers
Associate Director, Oil & Gas

RECEIVED

Form 3160-3
(August 2007)



JUN 07 2011

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
BLM VERNAL, UTAH**APPLICATION FOR PERMIT TO DRILL OR REENTER**

| | | |
|--|--|--|
| 1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER | | 5. Lease Serial No. UTU-67845 |
| 1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone | | 6. If Indian, Allottee or Tribe Name NA |
| 2. Name of Operator Newfield Production Company | | 7. If Unit or CA Agreement, Name and No. Greater Monument Butte |
| 3a. Address Route #3 Box 3630, Myton UT 84052 | 3b. Phone No. (include area code) (435) 646-3721 | 8. Lease Name and Well No. GMBU N-25-8-17 |
| 4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NW/SW 2265' FSL 464' FWL Sec. 25, T8S R17E (UTU-67845) At proposed prod. zone SE/NW 2366' FNL 1716' FWL Sec. 25, T8S R17E (UTU-67845) | | 9. API Well No. 43-047-51649 |
| 14. Distance in miles and direction from nearest town or post office* Approximately 14.7 miles southeast of Myton, UT | | 10. Field and Pool, or Exploratory Monument Butte |
| 15. Distance from proposed* location to nearest property or lease line, ft. Approx. 2,366' f/lse, NA f/unit (Also to nearest drig. unit line, if any) | 16. No. of acres in lease 560.00 | 11. Sec., T. R. M. or Blk. and Survey or Area Sec. 25, T8S R17E |
| 18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 756' | 19. Proposed Depth 6,630' | 12. County or Parish Uintah |
| 21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5015' GL | 22. Approximate date work will start* 3rd Qtr. 2011 | 13. State UT |
| 23. Estimated duration (7) days from SPUD to rig release | | |
| 24. Attachments | | |

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

| | | |
|--|--|---------------------|
| 25. Signature  | Name (Printed/Typed) Mandie Crozier | Date 6/1/11 |
| Title Regulatory Specialist | | |
| Approved by (Signature)  | Name (Printed/Typed) Jerry Kenczka | Date JAN 31 2012 |
| Title Assistant Field Manager Lands & Mineral Resources | Office VERNAL FIELD OFFICE | |

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

CONDITIONS OF APPROVAL ATTACHED

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

RECEIVED

FEB 08 2012

UDOGM

DIV. OF OIL, GAS & MINING

NOTICE OF APPROVAL



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company
Well No: GMBU N-25-8-17
API No: 43-047-51649

Location: NWSW, Sec. 25, T8S, R17E
Lease No: UTU-67845
Agreement: Greater Monument Butte (GR)

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

| | |
|---|---|
| Location Construction (Notify Environmental Scientist) | - Forty-Eight (48) hours prior to construction of location and access roads. |
| Location Completion (Notify Environmental Scientist) | - Prior to moving on the drilling rig. |
| Spud Notice (Notify Petroleum Engineer) | - Twenty-Four (24) hours prior to spudding the well. |
| Casing String & Cementing (Notify Supv. Petroleum Tech.) | - Twenty-Four (24) hours prior to running casing and cementing all casing strings to: blm_ut_vn_opreport@blm.gov |
| BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.) | - Twenty-Four (24) hours prior to initiating pressure tests. |
| First Production Notice (Notify Petroleum Engineer) | - Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days. |

**SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.
- Protection of the following watershed resources due to close proximity:
90 meters to Pariette Creek 100 year Floodplain,
140 meters to the Pariette Southwest Draw Wetland/Riparian Area, and
20 meters away from Pariette Area of Critical Environmental Concern (ACEC).
- After cessation of drilling and completion operations, any visible or measurable layer of oil must be removed from the surface of the reserve pit and the pit kept free of oil.
- Pits must be free of oil and other liquid and solid wastes prior to filling. Pit liners must not be breached (cut) or filled (squeezed) while still containing fluids. The pit liner must be removed to the solids level or treated to prevent its reemergence to the surface or its interference with long-term successful revegetation.

Wildlife

If construction and drilling is anticipated during any of the following wildlife seasonal or spatial restrictions, a qualified consulting firm biologist must be contacted in order to conduct applicable surveys using an accepted protocol prior to any ground disturbing activities.

- A BLM biologist or a BLM-approved contractor will conduct a raptor nest survey during the nesting season within 0.5 miles from the respective host location well pad and liquid gathering line corridor. If occupied/active raptor nests are found, construction would not occur during the nesting season for that species within the species-specific buffer described in the BLM Raptor Best Management Practices. If during the surveys known nests/habitat is found to be inactive, an exemption may be requested in writing and approved by the BLM Authorized officer.
- No surface occupancy or use is allowed within 1/4 mile of **prairie falcon** nests from April 1 to August 31. If during the surveys known nests/habitat is found to be inactive, an exemption may be requested in writing and approved by the BLM Authorized officer.
- **Mountain plover** surveys will be conducted to protocol by a professional Environmental Consulting Firm biologist prior to any ground disturbing activities. Reports from survey results must be

reviewed by a BLM minerals biologist prior to proceeding with the proposed project. A seasonal restriction for all ground disturbing activities in mountain plover habitat from May 1-June 15 is required.

- **White-tailed prairie dog burrows** and animals sighted will be recorded/mapped while conducting (to protocol) **burrowing owl** surveys. If burrowing owls/burrows are located, a seasonal restriction from March 1-August 31 within 0.25 mile is required.
- Install hospital mufflers to reduce noise impacts to wildlife.

Reclamation

- Reclamation will be completed in accordance with the Newfield Exploration Company Castle Peak and Eight Mile Flat Reclamation Plan on file with the Vernal Field Office of the BLM.
- The reclamation seed mix will incorporate low growing grasses, instead of crested wheatgrass, which negatively impacts mountain plover habitat.
- Appropriate erosion control and revegetation measures will be employed. In areas with unstable soils where seeding alone may not adequately control erosion, grading will be used to minimize slopes and water bars will be installed on disturbed slopes. Erosion control efforts will be monitored by Newfield and, if necessary, modifications will be made to control erosion.

Monitoring and Reporting

- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) that designates the proposed site-specific monitoring and reference sites chosen for the location. A description of the proposed sites shall be included, as well as a map showing the locations of the proposed sites.
- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) 3 growing seasons after reclamation efforts have occurred evaluating the status of the reclaimed areas in order to determine whether the BLM standards set forth in the Green River District Reclamation Guidelines have been met (30% or greater basal cover).

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Newfield Production Company shall comply with all applicable requirements in the SOP (version: "Greater Monument Butte Green River Development Program," June 24, 2008). The operator shall also comply with applicable laws and regulations; with the lease terms, Onshore Oil and Gas Orders, NTL's; and with other orders and instructions of the Authorized Officer.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB

or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to BLM_UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs,

core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross 26 Submitted By
Branden Arnold Phone Number 435-401-0223
Well Name/Number GMBU N-25-8-17
Qtr/Qtr NW/SW Section 25 Township 8S Range 17E
Lease Serial Number UTU-67845
API Number 43-047-51649

Spud Notice – Spud is the initial spudding of the well, not drilling
out below a casing string.

Date/Time 4/4/12 9:00 AM ☒ PM ☐

Casing – Please report time casing run starts, not cementing
times.

- ☒ Surface Casing
- ☐ Intermediate Casing
- ☐ Production Casing
- ☐ Liner
- ☐ Other

Date/Time 4/4/12 3:00 AM ☐ PM ☒

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time _____ AM ☐ PM ☐

Remarks _____

Carol Daniels - DrillWell: Daily Report Drilling for GMBU N-25-8-17 - Drilling

From: "NDSI SS2" <Den_ss2@nfxrig.com>
To: "Branden Arnold" <barnold@newfield.com>, "Carol Daniels" <caroldaniels@u...
Date: 4/16/2012 5:47 AM
Subject: DrillWell: Daily Report Drilling for GMBU N-25-8-17 - Drilling
Attachments: rptDailyReportDrilling.snp

Well Name: GMBU N-25-8-17 - Drilling *43-047-51649 T08S R17E S-25*
 Report Number: 4
 TD At Midnight: 6,618
 Daily TVD: 6,450
 Footage Drilled Today: 1,247.0
 Hours Drilled: 15.5
 ROP: 80.5
 Daily Cost: \$26,924
 Cumulative Cost: \$203,281

Time Activity:

12:00:00 AM-2:00:00 AM Drill from 5371' to 5504' WOB/21,TGPM/370,RPM/145,ROP/66
 2:00:00 AM-4:30:00 AM Change wash pipe and packing.
 4:30:00 AM-3:00:00 PM Drill from 5504' to 6333' WOB/21,TGPM/370,RPM/145,ROP/78
 3:00:00 PM-3:30:00 PM Rig service and check crownomatic
 3:30:00 PM-6:30:00 PM Drill from 6333' to 6618' WOB/21,TGPM/370,RPM/145,ROP/95
 6:30:00 PM-7:30:00 PM Circulate for logs
 7:30:00 PM-12:00:00 AM LDDP and BHA. Pumped 130bbls of 10.5# mud @ 3000' to kill flow.

Summary of Operations from 00:00 to 0500 hrs:

Log with PSI standard triple combo. Change and test casing rams 2000psi for 10min.

RECEIVED**APR 17 2012****DIV. OF OIL, GAS & MINING**

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# _____ SS#2

Submitted By Jay Burton Phone Number 823-6013

Well Name/Number GMBU N-25-8-17

Qtr/Qtr SE/NW Section 25 Township 8S Range 17E

Lease Serial Number UTU-67845

API Number 43-047-51649

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time _____ AM ☐ PM ☐

Casing – Please report time casing run starts, not cementing times.

- ☐ Surface Casing
- ☐ Intermediate Casing
- ☒ Production Casing
- ☐ Liner
- ☐ Other

RECEIVED

APR 17 2012

DIV. OF OIL, GAS & MINING

Date/Time 4/16/12 1:00 AM ☒ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time _____ AM ☐ PM ☐

Remarks TD notice and production csg run

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM -FORM 6

OPERATOR: **NEWFIELD PRODUCTION COMPANY**
ADDRESS: **RT. 3 BOX 3630**
MYTON, UT 84052

OPERATOR ACCT. NO. **N2695**


| ACTION CODE | CURRENT ENTITY NO. | NEW ENTITY NO. | API NUMBER | WELL NAME | WELL LOCATION | | | | | SPUD DATE | EFFECTIVE DATE |
|---------------------------------|--------------------|----------------|-------------------|------------------------|---------------|-----------|-----------|------------|-----------------|-----------------|----------------|
| | | | | | QQ | SC | TP | RG | COUNTY | | |
| B | 99999 | 17400 | 4304751649 | GMBU N-25-8-17 | NWSW | 25 | 8S | 17E | Uintah | 4/4/2012 | 4/12/12 |
| WELL 1 COMMENTS: GRRV | | | | | | | | | | | |
| B | 16361 | 17400 | 4304734943 | GMBU 3-14-9-18H | NENW | 14 | 9S | 18E | Uintah | 4/4/2012 | 4/12/12 |
| CONFIDENTIAL | | | | | | | | | | | |
| B | 99999 | 17400 | 4301350745 | GMBU F-8-9-17 | NENE | 7 | 9S | 17E | Duchesne | 4/4/2012 | 4/12/12 |
| GRRV | | | | | | | | | | | |
| B | 99999 | 17400 | 4301350581 | GMBU R-6-9-17 | SESW | 6 | 9S | 17E | Duchesne | 4/5/2012 | 4/12/12 |
| GRRV | | | | | | | | | | | |
| B | 99999 | 17400 | 4301350684 | GMBU V-6-9-17 | NENE | 7 | 9S | 17E | Duchesne | 4/4/2012 | 4/12/12 |
| GRRV | | | | | | | | | | | |
| | | | | | | | | | | | |

ACTION CODES (See instructions on back of form)
A - 1 new entity for new well (single well only)
B - 1 well to existing entity (group or unit well)
C - from one existing entity to another existing entity
D - well from one existing entity to a new entity
E - other (explain in comments section)

RECEIVED

APR 18 2012

Div. of Oil, Gas & Mining


Signature
Tabitha Timothy
Production Clerk
04/11/12

NOTE: Use COMMENT section to explain why each Action Code was selected.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630

Myton, UT 84052

3b. Phone (include area code)

435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

2285 FSL 0464 FWL

Section 25 T8S R17E

5. Lease Serial No.

UTU-67845

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

GMBU

8. Well Name and No.

GMBU N-25-8-17

9. API Well No.

4304751649

10. Field and Pool, or Exploratory Area

GREATER MB UNIT

11. County or Parish, State

UINTAH, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

| TYPE OF SUBMISSION | TYPE OF ACTION | | | |
|---|--|---|--|---|
| <input type="checkbox"/> Notice of Intent | <input type="checkbox"/> Acidize | <input type="checkbox"/> Deepen | <input type="checkbox"/> Production (Start/Resume) | <input type="checkbox"/> Water Shut-Off |
| <input checked="" type="checkbox"/> Subsequent Report | <input type="checkbox"/> Alter Casing | <input type="checkbox"/> Fracture Treat | <input type="checkbox"/> Reclamation | <input type="checkbox"/> Well Integrity |
| <input type="checkbox"/> Final Abandonment | <input type="checkbox"/> Casing Repair | <input type="checkbox"/> New Construction | <input type="checkbox"/> Recomplete | <input checked="" type="checkbox"/> Other _____ |
| | <input type="checkbox"/> Change Plans | <input type="checkbox"/> Plug & Abandon | <input type="checkbox"/> Temporarily Abandon | Spud Notice |
| | <input type="checkbox"/> Convert to Injector | <input type="checkbox"/> Plug Back | <input type="checkbox"/> Water Disposal | |

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 4/4/12 MIRU Ross #29. Spud well @9:00 AM. Drill 340' of 12 1/4" hole with air mist. TIH W/ 8 Jt's 8 5/8" J-55 24# csgn. Set @ 331.19'. On 4/5/12 cement with 164 sks of class "G" w/ 2% CaCL2 + 0.25#/sk Cello- Flake Mixed @ 15.8ppg w/ 1.17ft3/sk yield. Returned 6 barrels cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Branden Arnold

Signature



Title

Date

04/11/2012

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

RECEIVED

APR 19 2012

DIV. OF OIL, GAS & MINING

Casing / Liner Detail

Well GMBU N-25-8-17
Prospect Monument Butte
Foreman _____
Run Date: _____
String Type Surface, 8.625", 24#, J-55, STC (Generic)

- Detail From Top To Bottom -

| Depth | Length | JTS | Description | OD | ID |
|--------|--------|-----|---------------|-------|----|
| 342.09 | 1.42 | | Wellhead | | |
| 343.51 | -2.00 | | Cutoff | | |
| 10.00 | 42.16 | 1 | Shoe Joint | 8.625 | |
| 52.16 | 289.03 | 7 | 8 5/8" Casing | 8.625 | |
| 341.19 | 0.90 | 1 | Guide Shoe | 8.625 | |
| 341.51 | | | KB | | |

Cement Detail

| | | | | | |
|-----------------|------------|--------------|-------|--------------|--|
| Cement Company: | | BJ | | | |
| Slurry | # of Sacks | Weight (ppg) | Yield | Volume (ft³) | Description - Slurry Class and Additives |
| Slurry 1 | 164 | 15.8 | 1.17 | 191.88 | Class "G"+2%CaCl |

| | |
|--|-------|
| Stab-In-Job? | No |
| BHT: | 0 |
| Initial Circulation Pressure: | |
| Initial Circulation Rate: | |
| Final Circulation Pressure: | |
| Final Circulation Rate: | |
| Displacement Fluid: | Water |
| Displacement Rate: | |
| Displacement Volume: | 18.8 |
| Mud Returns: | |
| Centralizer Type And Placement: | |
| Middle of first, top of second and third for a total of three. | |

| | |
|-------------------------------|-------|
| Cement To Surface? | Yes |
| Est. Top of Cement: | 0 |
| Plugs Bumped? | Yes |
| Pressure Plugs Bumped: | 662 |
| Floats Holding? | No |
| Casing Stuck On / Off Bottom? | No |
| Casing Reciprocated? | No |
| Casing Rotated? | No |
| CIP: | 10:00 |
| Casing Wt Prior To Cement: | |
| Casing Weight Set On Slips: | |

| | | |
|--|--|---|
| STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING | | FORM 9 |
| SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals. | | 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67845 |
| 1. TYPE OF WELL Oil Well | | 6. IF INDIAN, ALLOTTEE OR TRIBE NAME: |
| 2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY | | 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV) |
| 3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052 | | 8. WELL NAME and NUMBER: GMBU N-25-8-17 |
| 4. LOCATION OF WELL FOOTAGES AT SURFACE: 2265 FSL 0464 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 08.0S Range: 17.0E Meridian: S | | 9. API NUMBER: 43047516490000 |
| PHONE NUMBER: 435 646-4825 Ext | | 9. FIELD and POOL or WILDCAT: MONUMENT BUTTE |
| COUNTY: UINTAH | | STATE: UTAH |
| 11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA | | |
| TYPE OF SUBMISSION | TYPE OF ACTION | |
| <input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input checked="" type="checkbox"/> DRILLING REPORT Report Date: 5/8/2012 | <div style="display: flex; flex-wrap: wrap;"> <div style="width: 33%;"> <input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input checked="" type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION </div> <div style="width: 33%;"> <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER </div> <div style="width: 33%;"> <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100%;" type="text"/> </div> </div> | |
| 12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. <div style="display: flex; justify-content: space-between; align-items: flex-start;"> <div style="width: 60%;"> <p>The above well was placed on production on 05/08/2012 at 16:00 hours.</p> </div> <div style="width: 35%; text-align: center;"> <p>Accepted by the Utah Division of Oil, Gas and Mining</p> <p>FOR RECORD ONLY</p> <p>May 17, 2012</p> </div> </div> | | |
| NAME (PLEASE PRINT) Jennifer Peatross | PHONE NUMBER 435 646-4885 | TITLE Production Technician |
| SIGNATURE N/A | DATE 5/17/2012 | |

| | | |
|--|--|---|
| STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING | | FORM 9 |
| SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals. | | 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67845 |
| 1. TYPE OF WELL Oil Well | | 6. IF INDIAN, ALLOTTEE OR TRIBE NAME: |
| 2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY | | 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV) |
| 3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052 | | 8. WELL NAME and NUMBER: GMBU N-25-8-17 |
| 4. LOCATION OF WELL FOOTAGES AT SURFACE: 2265 FSL 0464 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 08.0S Range: 17.0E Meridian: S | | 9. API NUMBER: 43047516490000 |
| PHONE NUMBER: 435 646-4825 Ext | | 9. FIELD and POOL or WILDCAT: MONUMENT BUTTE |
| COUNTY: UINTAH | | STATE: UTAH |
| 11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA | | |
| TYPE OF SUBMISSION | TYPE OF ACTION | |
| <input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: | <input type="checkbox"/> ACIDIZE | |
| <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: | <input type="checkbox"/> ALTER CASING | |
| <input type="checkbox"/> SPUD REPORT Date of Spud: | <input type="checkbox"/> CASING REPAIR | |
| <input checked="" type="checkbox"/> DRILLING REPORT Report Date: 5/8/2012 | <input type="checkbox"/> CHANGE TO PREVIOUS PLANS | |
| | <input type="checkbox"/> CHANGE TUBING | |
| | <input type="checkbox"/> CHANGE WELL STATUS | |
| | <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS | |
| | <input type="checkbox"/> CONVERT WELL TYPE | |
| | <input type="checkbox"/> DEEPEN | |
| | <input type="checkbox"/> FRACTURE TREAT | |
| | <input type="checkbox"/> NEW CONSTRUCTION | |
| | <input type="checkbox"/> OPERATOR CHANGE | |
| | <input type="checkbox"/> PLUG AND ABANDON | |
| | <input type="checkbox"/> PLUG BACK | |
| | <input checked="" type="checkbox"/> PRODUCTION START OR RESUME | |
| | <input type="checkbox"/> RECLAMATION OF WELL SITE | |
| | <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION | |
| | <input type="checkbox"/> REPERFORATE CURRENT FORMATION | |
| | <input type="checkbox"/> SIDETRACK TO REPAIR WELL | |
| | <input type="checkbox"/> TEMPORARY ABANDON | |
| | <input type="checkbox"/> TUBING REPAIR | |
| | <input type="checkbox"/> VENT OR FLARE | |
| | <input type="checkbox"/> WATER DISPOSAL | |
| | <input type="checkbox"/> WATER SHUTOFF | |
| | <input type="checkbox"/> SI TA STATUS EXTENSION | |
| | <input type="checkbox"/> WILDCAT WELL DETERMINATION | |
| | <input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/> | |
| 12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. The above well was placed on production on 05/08/2012 at 16:00 hours. Production Start Sundry re-sent 10/07/2012. | | |
| Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY October 12, 2012 | | |
| NAME (PLEASE PRINT) Kaci Deveraux | PHONE NUMBER 435 646-4867 | TITLE Production Technician |
| SIGNATURE N/A | DATE 10/7/2012 | |

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTFORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

| | | | | | | | | | |
|---|----------------------------|--|--------------------|--|-------------------------|--|--------------------------|--------------------------|---------------------------------------|
| 1a. Type of Well <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Dry <input type="checkbox"/> Other | | | | | | 5. Lease Serial No. UTU-67845 | | | |
| b. Type of Completion: <input checked="" type="checkbox"/> New Well <input type="checkbox"/> Work Over <input type="checkbox"/> Deepen <input type="checkbox"/> Plug Back <input type="checkbox"/> Diff. Resvr., Other: _____ | | | | | | 6. If Indian, Allottee or Tribe Name NA | | | |
| 2. Name of Operator NEWFIELD EXPLORATION COMPANY | | | | | | 7. Unit or CA Agreement Name and No. GMBU (GRRV) | | | |
| 3. Address 1401 17TH ST. SUITE 1000 DENVER, CO 80202 | | | | 3a. Phone No. (include area code) (435) 646-3721 | | 8. Lease Name and Well No. GMBU N-25-8-17 | | | |
| 4. Location of Well (Report location clearly and in accordance with Federal requirements)* At surface 2265' FSL & 464' FWL (NW/SW) SEC. 25, T8S, R17E (UTU-67845) At top prod. interval reported below 2572' FNL & 1233' FWL (SW/NW) SEC. 25, T8S, R17E (UTU-67845) At total depth 2346' FNL & 1642' FWL (SE/NW) SEC. 25, T8S, R17E (UTU-67845) BHL by HGM | | | | | | 9. AFI Well No. 43-047-51649 | | | |
| 10. Field and Pool or Exploratory MONUMENT BUTTE | | | | | | 11. Sec., T., R., M., on Block and Survey or Area SEC. 25, T8S, R17E | | | |
| 12. County or Parish UINTAH | | | | | | 13. State UT | | | |
| 14. Date Spudded 04/04/2012 | | 15. Date T.D. Reached 04/16/2012 | | 16. Date Completed 05/08/2012 <input type="checkbox"/> D & A <input checked="" type="checkbox"/> Ready to Prod. | | 17. Elevations (DF, RKB, RT, GL)* 5015' GL 5025' KB | | | |
| 18. Total Depth: MD 6618' TVD 6451' | | 19. Plug Back T.D.: MD 6560' TVD 6394 | | 20. Depth Bridge Plug Set: MD TVD | | 22. Was well cored? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Submit analysis) Was DST run? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Submit report) Directional Survey? <input type="checkbox"/> No <input checked="" type="checkbox"/> Yes (Submit copy) | | | |
| 21. Type Electric & Other Mechanical Logs Run (Submit copy of each) DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND | | | | | | | | | |
| 23. Casing and Liner Record (Report all strings set in well) | | | | | | | | | |
| Hole Size | Size/Grade | Wt. (#/ft.) | Top (MD) | Bottom (MD) | Stage Cementer Depth | No. of Sk. & Type of Cement | Slurry Vol. (BBL) | Cement Top* | Amount Pulled |
| 12-1/4" | 8-5/8" J-55 | 24# | 0 | 331' | | 164 CLASS G | | | |
| 7-7/8" | 5-1/2" J-55 | 15.5# | 0 | 6615' | | 275 PRIMLITE | | 24' | |
| | | | | | | 450 50/50 POZ | | | |
| 24. Tubing Record | | | | | | | | | |
| Size | Depth Set (MD) | Packer Depth (MD) | Size | Depth Set (MD) | Packer Depth (MD) | Size | Depth Set (MD) | Packer Depth (MD) | |
| 2-7/8" | EOT@ 6429' | TA @ 6330' | | | | | | | |
| 25. Producing Intervals | | | | 26. Perforation Record | | | | | |
| Formation | | Top | Bottom | Perforated Interval | | Size | No. Holes | Perf. Status | |
| A) Green River | | 4546' | 6350' | 4546-6350' | | 0.34" | 75 | | |
| B) | | | | | | | | | |
| C) | | | | | | | | | |
| D) | | | | | | | | | |
| 27. Acid, Fracture, Treatment, Cement Squeeze, etc. | | | | | | | | | |
| Depth Interval | | | | Amount and Type of Material | | | | | |
| 4546-6350' | | | | Frac w/ 246729#s 20/40 white sand in 2375 bbls of Lightning 17 fluid, in 6 stages. | | | | | |
| 28. Production - Interval A | | | | | | | | | |
| Date First Produced | Test Date | Hours Tested | Test Production | Oil BBL | Gas MCF | Water BBL | Oil Gravity Corr. API | Gas Gravity | Production Method |
| 5/7/12 | 5/17/12 | 24 | → | 46 | 28 | 56 | | | 2-1/2" x 1-1/2" x 21' x 24' RHAC Pump |
| Choke Size | Tbg. Press. Flwg. SI | Csg. Press. | 24 Hr. Rate | Oil BBL | Gas MCF | Water BBL | Gas/Oil Ratio | Well Status PRODUCING | |
| | | | → | | | | | | |
| 28a. Production - Interval B | | | | | | | | | |
| Date First Produced | Test Date | Hours Tested | Test Production | Oil BBL | Gas MCF | Water BBL | Oil Gravity Corr. API | Gas Gravity | Production Method |
| | | | → | | | | | | |
| Choke Size | Tbg. Press. Flwg. SI | Csg. Press. | 24 Hr. Rate | Oil BBL | Gas MCF | Water BBL | Gas/Oil Ratio | Well Status | |
| | | | → | | | | | | |

*(See instructions and spaces for additional data on page 2)

Div. of Oil, Gas & Mining

RECEIVED

OCT 09 2012

28b. Production - Interval C

| Date First Produced | Test Date | Hours Tested | Test Production → | Oil BBL | Gas MCF | Water BBL | Oil Gravity Corr. API | Gas Gravity | Production Method |
|---------------------|----------------------------|--------------|----------------------|---------|---------|-----------|--------------------------|-------------|-------------------|
| Choke Size | Tbg. Press. Flwg. SI | Csg. Press. | 24 Hr. Rate → | Oil BBL | Gas MCF | Water BBL | Gas/Oil Ratio | Well Status | |

28c. Production - Interval D

| Date First Produced | Test Date | Hours Tested | Test Production → | Oil BBL | Gas MCF | Water BBL | Oil Gravity Corr. API | Gas Gravity | Production Method |
|---------------------|----------------------------|--------------|----------------------|---------|---------|-----------|--------------------------|-------------|-------------------|
| Choke Size | Tbg. Press. Flwg. SI | Csg. Press. | 24 Hr. Rate → | Oil BBL | Gas MCF | Water BBL | Gas/Oil Ratio | Well Status | |

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD AND USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

| Formation | Top | Bottom | Descriptions, Contents, etc. | Name | Top |
|-------------|-------|--------|------------------------------|---------------------------------------|----------------|
| | | | | | Meas. Depth |
| GREEN RIVER | 4546' | 6350' | | GARDEN GULCH MRK GARDEN GULCH 1 | 4139' 4328' |
| | | | | GARDEN GULCH 2 POINT 3 | 4446' 4732' |
| | | | | X MRKR Y MRKR | 4960' 5000' |
| | | | | DOUGLAS CREEK MRK BI CARBONATE MRK | 5124' 5396' |
| | | | | B LIMESTON MRK CASTLE PEAK | 5566' 5993' |
| | | | | BASAL CARBONATE WASATCH | 6419' 6545' |

32. Additional remarks (include plugging procedure):

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- ☐ Electrical/Mechanical Logs (1 full set req'd.)
 ☐ Geologic Report
 ☐ DST Report
 ☒ Directional Survey
☐ Sundry Notice for plugging and cement verification
 ☐ Core Analysis
 ☐ Other:

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Jennifer PeatrossTitle Production TechnicianSignature Date 06/12/2012

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Daily Activity Report**Format For Sundry****GMBU N-25-8-17****4/1/2012 To 6/30/2012****5/1/2012 Day: 1****Completion**

Rigless on 5/1/2012 - Run CBL & perf stg. 1 - R/U frac crew hold pre job safety meeting & review JSA's pres. Test frac iron to 5200# (good) - Frac stg. 1 w/ 59,354# of 20/40 white & 17# lightning - P/U perf gun test lub. To 4500# (good) RIH perf stg. 1 all CP zone as follows 6348-50', 6245-46', 6181-82', 6149-50' & 6111-12' all 3 spf @ 120 ph. POOH R/D w/l shut well in what on frac. - P/U perf gun test lub. To 4500# (good) RIH perf stg. 1 all CP zone as follows 6348-50', 6245-46', 6181-82', 6149-50' & 6111-12' all 3 spf @ 120 ph. POOH R/D w/l shut well in what on frac. - R/U test truck test csg. To 4500# hold for 30 min. (good) - R/U test truck test csg. To 4500# hold for 30 min. (good) - RIH preform CBL tag PBTD @ 6560' est. TOC @ 24' L/D w/l tools - RIH preform CBL tag PBTD @ 6560' est. TOC @ 24' L/D w/l tools - R/U perforators w/l test lub. To 4500# (good) - R/U perforators w/l test lub. To 4500# (good) - Hold pre job safety meeting, review JSA's - Hold pre job safety meeting, review JSA's - Turn well over to flowback open on #20 choke @ 3 bpm flow back 600 turned to 10% oil SWIFN - Turn well over to flowback open on #20 choke @ 3 bpm flow back 600 turned to 10% oil SWIFN - Frac stg. 6 w/ 27,806# 20/40 white & 17# lightning - Frac stg. 6 w/ 27,806# 20/40 white & 17# lightning - P/T RIH set 5th CBP @ 4760' & perf stg. 6 f/ 4716-18' (GB-6) & 4546-47' (GB-2) POOH R/D w/l - P/T RIH set 5th CBP @ 4760' & perf stg. 6 f/ 4716-18' (GB-6) & 4546-47' (GB-2) POOH R/D w/l - P/T to 4500# (good) RIH attp. To set CBP @ 4760' (misrun) POOH L/D tools tear dwn. Find loose det. - P/T to 4500# (good) RIH attp. To set CBP @ 4760' (misrun) POOH L/D tools tear dwn. Find loose det. - Frac stg. 5 w/ 29,987# 20/40 white & 17 lightning - Frac stg. 5 w/ 29,987# 20/40 white & 17 lightning - P/T lub. 4500# (good) RIH set 4th CBP @ 5000' & perf stg. 5 f/ 4921-23' (PB-11) 4798-99' (PB-7) POOH L/d tools - P/T lub. 4500# (good) RIH set 4th CBP @ 5000' & perf stg. 5 f/ 4921-23' (PB-11) 4798-99' (PB-7) POOH L/d tools - Frac stg. 4 w/ 29,865# 20/40 white & 17# lightning - Frac stg. 4 w/ 29,865# 20/40 white & 17# lightning - P/T lub. 4500# (good) RIH set 3rd CBP @ 5300' and perf stg. 4 f/ 5226-28' (D-3) 5143-44' 5137-38' (D-1) POOH l/d tools - P/T lub. 4500# (good) RIH set 3rd CBP @ 5300' and perf stg. 4 f/ 5226-28' (D-3) 5143-44' 5137-38' (D-1) POOH l/d tools - Frac stg. 3 W/ 74,706# 20/40 white & 17# lightning - Frac stg. 3 W/ 74,706# 20/40 white & 17# lightning - Pres. Test lub. To 4500# (good) RIH set 2nd CBP @ 5560' and perf stg. 3 f/ 5486-88' (b-2) 5387-88' 5375-76' 5367-68' 5359-60' (C-sand) POOH L/D tools - Pres. Test lub. To 4500# (good) RIH set 2nd CBP @ 5560' and perf stg. 3 f/ 5486-88' (b-2) 5387-88' 5375-76' 5367-68' 5359-60' (C-sand) POOH L/D tools - Pres. Test frac stg. 2 w/ 25,011, 20/40 white & 17# lightning - Pres. Test frac stg. 2 w/ 25,011, 20/40 white & 17# lightning - R/U Extreme w/l pres. Test lub. To 4500# (good) RIH set 1st CBP @ 5830' & perf stg. 2 A-3 zone f/ 5757-59' & 5751-52' POOH L/D perf guns & setting tool - R/U Extreme w/l pres. Test lub. To 4500# (good) RIH set 1st CBP @ 5830' & perf stg. 2 A-3 zone f/ 5757-59' & 5751-52' POOH L/D perf guns & setting tool - Frac stg. 1 w/ 59,354# of 20/40 white & 17# lightning - R/U frac crew hold pre job safety meeting & review JSA's pres. Test frac iron to 5200# (good)

Daily Cost: \$26,946**Cumulative Cost:** \$26,946**5/2/2012 Day: 3****Completion**

Stone #3 on 5/2/2012 - MIRUSU N/U 5k BOP P/U RIH w/ Mill & tbg. EOT @ 3437 - P/U RIH w/ 4 3/4 chomp mill, BRS w/o float, 1 jt. 2 7/8 PSN followed by 109 jts. EOT @ 3437' SWIFN - N/D frac valve N/U 5k BOP w/ double 2 7/8 pipe rams pres. Test all comp. off BOP to 4500# (good) (note: replaced pipe rams prior to N/U) - Preform neg. test on CBP no signs of pres. Or

flowback - R/U perforators W/L test lub. To 4500# (good) RIH set solid CBP @ 4460' POOH L/D setting tool open well bleed to 0# in 10 min. - R/U H/O test line to 4000# (good) pump 20bbls htd. Wtr. Dwn csg. SIP 1250# - Spot "T" seal MIRUSU - Morning tail gate meeting, review JSA's - Crew Travel

Daily Cost: \$12,550

Cumulative Cost: \$179,622

5/3/2012 Day: 4**Completion**

Stone #3 on 5/3/2012 - D/O K/P & 4 Add. CBP's - P/U 32 jts. Tag Kill plug @ 4448'(SLM) - R/U Nabors P/S D/O Plug cont. in hole tag fill @ 4690' C/O to cbp @ 4768' (78') - D/O plug @ 4768' - D/O plug @ 5011" - D/O plug @ 5303' - D/O plug @ 5561' wash dwn to 5571' Circ. Btms. Up L/D 1 jt. EOT @ 5540' SWIFN - Tailgate meeting, review JSA's

Daily Cost: \$6,763

Cumulative Cost: \$186,385

5/4/2012 Day: 5**Completion**

Stone #3 on 5/4/2012 - D/O last CBP C/O to PBTD @ 6573' R/U swab recover 86 bbls - R/D P/S POOH w/ 3 jts. Tbg. - Hold tailgate meeting & review JSA's - SITP 50#, SICP 350#, RIH tag CBP @ 5838' (SLM) R/U P/S D/O plug. Cont. in hole tag fill @ 6371' C/O to PBTD @ 6573' (202') - Circ. Well clean - EOT @ 6480" R/U swab IFL @ sur. Make 8 ttls runs recovered 86 bbls FFI @ 1640' SWIFN

Daily Cost: \$6,618

Cumulative Cost: \$193,003

5/7/2012 Day: 6**Completion**

Stone #3 on 5/7/2012 - Swab recovered 428 bbls trace of oil still pulling sand - SICP 150#, SITP 200#, bleed well dwn. In 3 min. R/U swab IFL @ sur. Make 37 ttl runs recovered 428 bbls seeing a trace of oil & still seeing ~cup of sand pre run SWIFN - Hold pre job safety meeting, review JSA's

Daily Cost: \$7,085

Cumulative Cost: \$200,088

5/8/2012 Day: 7**Completion**

Stone #3 on 5/8/2012 - Cont. to swab Pooh w/ tbg. P/U & RIH w/ prod. Tbg. - P/u 3 jts. Tag PBTD @ 6572' no added fill Pooh w/ tbg. & L/D BHA - SICP#350,SITP#50, bleed well dwn in 2 Min. R/U swab make ttl of 8 runs recovered 92 bbls w/ 10% oil cut & sand cleaning up IFL @ sur. & FFI @ 1400' R/D swab - R/D floor N/D 5k BOP set TAC w/ 18k tension N/U prod. Well head TAC @ 6332', PSN @ 6365' & EOT @ 6428' Change over to rod equip. SWIFN - P/U RIH w/ 2 7/8 NC, 2 jts, 2 7/8 PSN, 1 jt, 5 1/2 TAC & 201 jts. Of tbg. - Hold pre job safety meeting, review JSA's

Daily Cost: \$7,578

Cumulative Cost: \$207,666

5/9/2012 Day: 8**Completion**

Stone #3 on 5/9/2012 - PU & RU w/ 2 1/2" X 1 3/4" X 21' X 24' Central hydraulic rod pump and "RLC "A"grade rod string. Hang head and space out rods. Fill tbg w/ 5 bbls of wtr.

Pressure test to 800 psi. RDMOSU. POP @ 4:00 PM @ 4 SPM w/ 142" SL. FINAL REPORT. 2265 BWTR. - Crew travel. Hold safety meeting on PU rods. - PU & RU w/ 2 1/2" X 1 3/4" X 21' X 24' Central hydraulic rod pump and "RLC "A"grade rod string. Hang head and space out rods. Fill tbg w/ 5 bbls of wtr. Pressure test to 800 psi. RDMOSU. POP @ 4:00 PM @ 4 SPM w/ 142" SL. FINAL REPORT. 2265 BWTR. **Finalized**

Daily Cost: \$79,629

Cumulative Cost: \$287,295

Pertinent Files: Go to File List

NEWFIELD



NEWFIELD EXPLORATION

USGS Myton SW (UT)

SECTION 25 T8S, R17


N-25-8-17

Wellbore #1

Design: Actual

Standard Survey Report

25 April, 2012





Payzone Directional

Survey Report



Company: NEWFIELD EXPLORATION
Project: USGS Myton SW (UT)
Site: SECTION 25 T8S, R17
Well: N-25-8-17
Wellbore: Wellbore #1
Design: Actual

Local Co-ordinate Reference: Well N-25-8-17
TVD Reference: N-25-8-17 @ 5027.0ft (NDSI SS #2)
MD Reference: N-25-8-17 @ 5027.0ft (NDSI SS #2)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM 2003.21 Single User Db

Project USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA

Map System: US State Plane 1983
Geo Datum: North American Datum 1983
Map Zone: Utah Central Zone
System Datum: Mean Sea Level

Site SECTION 25 T8S, R17

Site Position: Northing: 7,205,389.13 ft Latitude: 40° 5' 26.000 N
From: Lat/Long Easting: 2,069,565.26 ft Longitude: 109° 57' 57.510 W
Position Uncertainty: 0.0 ft Slot Radius: " Grid Convergence: 0.98 °

Well N-25-8-17, SHL LAT: 40 05 16.50 LONG: -109 57 45.62

Well Position +N/-S 0.0 ft Northing: 7,204,443.89 ft Latitude: 40° 5' 16.500 N
+E/-W 0.0 ft Easting: 2,070,505.66 ft Longitude: 109° 57' 45.620 W
Position Uncertainty 0.0 ft Wellhead Elevation: 5,027.0 ft Ground Level: 5,015.0 ft

Wellbore Wellbore #1

| Magnetics | Model Name | Sample Date | Declination (°) | Dip Angle (°) | Field Strength (nT) |
|-----------|------------|-------------|-----------------|---------------|---------------------|
| | IGRF2010 | 12/3/2010 | 11.35 | 65.86 | 52,364 |

Design Actual

Audit Notes:

Version: 1.0 **Phase:** ACTUAL **Tie On Depth:** 0.0
Vertical Section: Depth From (TVD) (ft) +N/-S (ft) +E/-W (ft) Direction (°)
0.0 0.0 0.0 60.89

Survey Program Date 4/25/2012

| From (ft) | To (ft) | Survey (Wellbore) | Tool Name | Description |
|-----------|---------|-------------------------|-----------|----------------|
| 347.0 | 6,618.0 | Survey #1 (Wellbore #1) | MWD | MWD - Standard |

Survey

| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Vertical Section (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
|---------------------|-----------------|-------------|---------------------|------------|------------|-----------------------|-----------------------|----------------------|---------------------|
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 347.0 | 0.20 | 103.20 | 347.0 | -0.1 | 0.6 | 0.4 | 0.06 | 0.06 | 0.00 |
| 378.0 | 0.30 | 308.30 | 378.0 | -0.1 | 0.6 | 0.5 | 1.58 | 0.32 | -499.68 |
| 408.0 | 0.20 | 191.70 | 408.0 | -0.1 | 0.5 | 0.4 | 1.43 | -0.33 | -388.67 |
| 439.0 | 0.40 | 32.10 | 439.0 | -0.1 | 0.6 | 0.5 | 1.91 | 0.65 | -514.84 |
| 470.0 | 0.70 | 26.60 | 470.0 | 0.2 | 0.7 | 0.7 | 0.98 | 0.97 | -17.74 |
| 500.0 | 0.60 | 9.80 | 500.0 | 0.5 | 0.8 | 1.0 | 0.71 | -0.33 | -56.00 |
| 531.0 | 1.10 | 41.50 | 531.0 | 0.9 | 1.0 | 1.3 | 2.16 | 1.61 | 102.26 |
| 561.0 | 1.00 | 24.40 | 561.0 | 1.4 | 1.3 | 1.8 | 1.09 | -0.33 | -57.00 |
| 591.0 | 0.90 | 51.50 | 591.0 | 1.7 | 1.6 | 2.3 | 1.52 | -0.33 | 90.33 |
| 622.0 | 1.10 | 33.50 | 622.0 | 2.1 | 2.0 | 2.8 | 1.19 | 0.65 | -58.06 |
| 653.0 | 1.60 | 31.20 | 653.0 | 2.8 | 2.4 | 3.4 | 1.62 | 1.61 | -7.42 |
| 684.0 | 2.10 | 44.70 | 684.0 | 3.5 | 3.0 | 4.3 | 2.13 | 1.61 | 43.55 |



Payzone Directional

Survey Report



Company: NEWFIELD EXPLORATION
Project: USGS Myton SW (UT)
Site: SECTION 25 T8S, R17
Well: N-25-8-17
Wellbore: Wellbore #1
Design: Actual

Local Co-ordinate Reference: Well N-25-8-17
TVD Reference: N-25-8-17 @ 5027.0ft (NDSI SS #2)
MD Reference: N-25-8-17 @ 5027.0ft (NDSI SS #2)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM 2003.21 Single User Db

Survey

| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Vertical Section (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
|---------------------------|--------------------|----------------|---------------------------|---------------|---------------|-----------------------------|-----------------------------|----------------------------|---------------------------|
| 714.0 | 2.30 | 44.00 | 713.9 | 4.4 | 3.8 | 5.4 | 0.67 | 0.67 | -2.33 |
| 745.0 | 2.50 | 43.40 | 744.9 | 5.3 | 4.7 | 6.7 | 0.65 | 0.65 | -1.94 |
| 775.0 | 3.10 | 43.80 | 774.9 | 6.4 | 5.7 | 8.1 | 2.00 | 2.00 | 1.33 |
| 805.0 | 3.50 | 38.10 | 804.8 | 7.7 | 6.8 | 9.7 | 1.72 | 1.33 | -19.00 |
| 835.0 | 4.10 | 42.90 | 834.8 | 9.2 | 8.1 | 11.6 | 2.26 | 2.00 | 16.00 |
| 866.0 | 4.40 | 47.80 | 865.7 | 10.8 | 9.8 | 13.8 | 1.52 | 0.97 | 15.81 |
| 896.0 | 4.50 | 49.00 | 895.6 | 12.3 | 11.5 | 16.0 | 0.46 | 0.33 | 4.00 |
| 926.0 | 5.20 | 48.70 | 925.5 | 14.0 | 13.4 | 18.5 | 2.33 | 2.33 | -1.00 |
| 958.0 | 6.00 | 45.90 | 957.3 | 16.1 | 15.7 | 21.6 | 2.64 | 2.50 | -8.75 |
| 988.0 | 6.60 | 46.00 | 987.1 | 18.4 | 18.1 | 24.7 | 2.00 | 2.00 | 0.33 |
| 1,032.0 | 7.40 | 46.70 | 1,030.8 | 22.1 | 21.9 | 29.9 | 1.83 | 1.82 | 1.59 |
| 1,075.0 | 7.60 | 47.10 | 1,073.4 | 25.9 | 26.0 | 35.4 | 0.48 | 0.47 | 0.93 |
| 1,119.0 | 8.20 | 48.00 | 1,117.0 | 30.0 | 30.5 | 41.3 | 1.39 | 1.36 | 2.05 |
| 1,163.0 | 9.10 | 50.80 | 1,160.5 | 34.3 | 35.5 | 47.7 | 2.26 | 2.05 | 6.36 |
| 1,207.0 | 9.50 | 52.40 | 1,203.9 | 38.7 | 41.1 | 54.8 | 1.08 | 0.91 | 3.64 |
| 1,250.0 | 10.20 | 55.40 | 1,246.3 | 43.1 | 47.1 | 62.1 | 2.02 | 1.63 | 6.98 |
| 1,294.0 | 10.80 | 57.20 | 1,289.6 | 47.5 | 53.7 | 70.0 | 1.55 | 1.36 | 4.09 |
| 1,338.0 | 11.70 | 59.50 | 1,332.7 | 52.0 | 61.0 | 78.6 | 2.29 | 2.05 | 5.23 |
| 1,382.0 | 12.50 | 62.40 | 1,375.7 | 56.5 | 69.1 | 87.8 | 2.28 | 1.82 | 6.59 |
| 1,425.0 | 12.70 | 64.30 | 1,417.7 | 60.7 | 77.5 | 97.2 | 1.07 | 0.47 | 4.42 |
| 1,469.0 | 14.20 | 65.70 | 1,460.5 | 65.0 | 86.8 | 107.4 | 3.49 | 3.41 | 3.18 |
| 1,513.0 | 15.20 | 65.60 | 1,503.1 | 69.6 | 96.9 | 118.5 | 2.27 | 2.27 | -0.23 |
| 1,557.0 | 15.50 | 64.00 | 1,545.5 | 74.6 | 107.5 | 130.2 | 1.18 | 0.68 | -3.64 |
| 1,600.0 | 16.50 | 63.50 | 1,586.8 | 79.8 | 118.1 | 142.0 | 2.35 | 2.33 | -1.16 |
| 1,644.0 | 17.00 | 62.30 | 1,629.0 | 85.6 | 129.4 | 154.7 | 1.38 | 1.14 | -2.73 |
| 1,688.0 | 17.30 | 60.40 | 1,671.0 | 91.8 | 140.8 | 167.6 | 1.44 | 0.68 | -4.32 |
| 1,731.0 | 17.90 | 60.00 | 1,712.0 | 98.3 | 152.1 | 180.6 | 1.42 | 1.40 | -0.93 |
| 1,775.0 | 17.89 | 59.07 | 1,753.9 | 105.1 | 163.7 | 194.2 | 0.65 | -0.02 | -2.11 |
| 1,819.0 | 17.84 | 58.90 | 1,795.7 | 112.1 | 175.3 | 207.7 | 0.16 | -0.11 | -0.39 |
| 1,863.0 | 17.49 | 57.80 | 1,837.7 | 119.1 | 186.6 | 221.0 | 1.10 | -0.80 | -2.50 |
| 1,907.0 | 17.45 | 56.90 | 1,879.6 | 126.2 | 197.8 | 234.2 | 0.62 | -0.09 | -2.05 |
| 1,951.0 | 17.70 | 57.00 | 1,921.6 | 133.4 | 208.9 | 247.4 | 0.57 | 0.57 | 0.23 |
| 1,994.0 | 17.40 | 56.10 | 1,962.6 | 140.6 | 219.7 | 260.4 | 0.94 | -0.70 | -2.09 |
| 2,038.0 | 16.54 | 57.60 | 2,004.7 | 147.6 | 230.5 | 273.2 | 2.19 | -1.95 | 3.41 |
| 2,082.0 | 15.64 | 58.63 | 2,046.9 | 154.1 | 240.8 | 285.3 | 2.15 | -2.05 | 2.34 |
| 2,126.0 | 15.60 | 58.60 | 2,089.3 | 160.2 | 250.9 | 297.2 | 0.09 | -0.09 | -0.07 |
| 2,169.0 | 14.80 | 58.90 | 2,130.8 | 166.1 | 260.6 | 308.5 | 1.87 | -1.86 | 0.70 |
| 2,213.0 | 13.80 | 59.10 | 2,173.4 | 171.7 | 269.9 | 319.3 | 2.28 | -2.27 | 0.45 |
| 2,257.0 | 13.30 | 59.30 | 2,216.2 | 177.0 | 278.7 | 329.6 | 1.14 | -1.14 | 0.45 |
| 2,301.0 | 12.40 | 57.90 | 2,259.1 | 182.1 | 287.1 | 339.4 | 2.16 | -2.05 | -3.18 |
| 2,344.0 | 11.50 | 58.80 | 2,301.2 | 186.7 | 294.7 | 348.3 | 2.14 | -2.09 | 2.09 |
| 2,388.0 | 11.10 | 58.70 | 2,344.3 | 191.2 | 302.0 | 356.9 | 0.91 | -0.91 | -0.23 |
| 2,432.0 | 10.90 | 57.40 | 2,387.5 | 195.6 | 309.2 | 365.3 | 0.72 | -0.45 | -2.95 |
| 2,476.0 | 10.40 | 56.90 | 2,430.8 | 200.1 | 316.0 | 373.4 | 1.16 | -1.14 | -1.14 |
| 2,520.0 | 10.77 | 57.80 | 2,474.0 | 204.4 | 322.8 | 381.5 | 0.92 | 0.84 | 2.05 |
| 2,563.0 | 10.50 | 57.60 | 2,516.3 | 208.7 | 329.5 | 389.4 | 0.63 | -0.63 | -0.47 |
| 2,607.0 | 10.63 | 59.00 | 2,559.5 | 212.9 | 336.4 | 397.5 | 0.65 | 0.30 | 3.18 |
| 2,651.0 | 10.30 | 56.80 | 2,602.8 | 217.1 | 343.1 | 405.4 | 1.18 | -0.75 | -5.00 |
| 2,695.0 | 9.90 | 56.90 | 2,646.1 | 221.4 | 349.6 | 413.1 | 0.91 | -0.91 | 0.23 |
| 2,739.0 | 9.50 | 56.40 | 2,689.5 | 225.4 | 355.8 | 420.5 | 0.93 | -0.91 | -1.14 |
| 2,782.0 | 10.20 | 54.80 | 2,731.9 | 229.6 | 361.9 | 427.8 | 1.75 | 1.63 | -3.72 |
| 2,826.0 | 10.50 | 56.70 | 2,775.1 | 234.0 | 368.4 | 435.7 | 1.03 | 0.68 | 4.32 |
| 2,870.0 | 10.94 | 57.80 | 2,818.4 | 238.5 | 375.3 | 443.9 | 1.10 | 1.00 | 2.50 |
| 2,914.0 | 11.70 | 57.50 | 2,861.5 | 243.1 | 382.6 | 452.5 | 1.73 | 1.73 | -0.68 |



Payzone Directional Survey Report



Company: NEWFIELD EXPLORATION
Project: USGS Myton SW (UT)
Site: SECTION 25 T8S, R17
Well: N-25-8-17
Wellbore: Wellbore #1
Design: Actual

Local Co-ordinate Reference: Well N-25-8-17
TVD Reference: N-25-8-17 @ 5027.0ft (NDSI SS #2)
MD Reference: N-25-8-17 @ 5027.0ft (NDSI SS #2)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM 2003.21 Single User Db

Survey

| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Vertical Section (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
|---------------------------|--------------------|----------------|---------------------------|---------------|---------------|-----------------------------|-----------------------------|----------------------------|---------------------------|
| 2,958.0 | 13.10 | 57.75 | 2,904.5 | 248.1 | 390.6 | 461.9 | 3.18 | 3.18 | 0.57 |
| 3,002.0 | 14.10 | 58.00 | 2,947.3 | 253.6 | 399.3 | 472.3 | 2.28 | 2.27 | 0.57 |
| 3,045.0 | 14.70 | 56.90 | 2,988.9 | 259.4 | 408.3 | 482.9 | 1.53 | 1.40 | -2.56 |
| 3,089.0 | 13.90 | 56.50 | 3,031.5 | 265.4 | 417.4 | 493.8 | 1.83 | -1.82 | -0.91 |
| 3,133.0 | 13.00 | 58.00 | 3,074.3 | 270.9 | 426.0 | 504.0 | 2.19 | -2.05 | 3.41 |
| 3,177.0 | 12.90 | 57.90 | 3,117.2 | 276.1 | 434.4 | 513.8 | 0.23 | -0.23 | -0.23 |
| 3,220.0 | 12.70 | 57.50 | 3,159.1 | 281.2 | 442.4 | 523.4 | 0.51 | -0.47 | -0.93 |
| 3,264.0 | 13.20 | 58.50 | 3,202.0 | 286.4 | 450.8 | 533.2 | 1.25 | 1.14 | 2.27 |
| 3,308.0 | 13.10 | 59.90 | 3,244.9 | 291.6 | 459.4 | 543.2 | 0.76 | -0.23 | 3.18 |
| 3,351.0 | 13.40 | 61.50 | 3,286.7 | 296.4 | 468.0 | 553.1 | 1.10 | 0.70 | 3.72 |
| 3,396.0 | 14.70 | 63.30 | 3,330.4 | 301.4 | 477.7 | 564.0 | 3.05 | 2.89 | 4.00 |
| 3,439.0 | 15.40 | 64.10 | 3,371.9 | 306.4 | 487.7 | 575.1 | 1.70 | 1.63 | 1.86 |
| 3,483.0 | 15.00 | 62.10 | 3,414.4 | 311.6 | 498.0 | 586.7 | 1.50 | -0.91 | -4.55 |
| 3,527.0 | 15.10 | 61.70 | 3,456.9 | 317.0 | 508.0 | 598.1 | 0.33 | 0.23 | -0.91 |
| 3,571.0 | 15.70 | 63.10 | 3,499.3 | 322.4 | 518.4 | 609.8 | 1.60 | 1.36 | 3.18 |
| 3,614.0 | 15.80 | 63.50 | 3,540.7 | 327.6 | 528.8 | 621.4 | 0.34 | 0.23 | 0.93 |
| 3,658.0 | 16.60 | 65.10 | 3,582.9 | 333.0 | 539.9 | 633.7 | 2.08 | 1.82 | 3.64 |
| 3,702.0 | 16.80 | 64.40 | 3,625.1 | 338.4 | 551.3 | 646.3 | 0.64 | 0.45 | -1.59 |
| 3,746.0 | 16.70 | 63.70 | 3,667.2 | 343.9 | 562.7 | 659.0 | 0.51 | -0.23 | -1.59 |
| 3,789.0 | 17.10 | 63.70 | 3,708.3 | 349.4 | 573.9 | 671.4 | 0.93 | 0.93 | 0.00 |
| 3,833.0 | 17.00 | 63.30 | 3,750.4 | 355.2 | 585.5 | 684.3 | 0.35 | -0.23 | -0.91 |
| 3,877.0 | 17.30 | 63.60 | 3,792.4 | 361.0 | 597.1 | 697.3 | 0.71 | 0.68 | 0.68 |
| 3,921.0 | 17.20 | 64.90 | 3,834.5 | 366.7 | 608.8 | 710.3 | 0.91 | -0.23 | 2.95 |
| 3,964.0 | 17.90 | 65.30 | 3,875.5 | 372.1 | 620.6 | 723.2 | 1.65 | 1.63 | 0.93 |
| 4,008.0 | 17.60 | 64.90 | 3,917.4 | 377.8 | 632.8 | 736.6 | 0.74 | -0.68 | -0.91 |
| 4,052.0 | 17.23 | 64.00 | 3,959.4 | 383.5 | 644.6 | 749.8 | 1.04 | -0.84 | -2.05 |
| 4,096.0 | 16.30 | 63.40 | 4,001.5 | 389.1 | 656.0 | 762.4 | 2.15 | -2.11 | -1.36 |
| 4,140.0 | 15.80 | 63.20 | 4,043.8 | 394.5 | 666.9 | 774.6 | 1.14 | -1.14 | -0.45 |
| 4,184.0 | 16.00 | 65.00 | 4,086.1 | 399.8 | 677.7 | 786.6 | 1.21 | 0.45 | 4.09 |
| 4,228.0 | 15.80 | 65.50 | 4,128.4 | 404.9 | 688.7 | 798.6 | 0.55 | -0.45 | 1.14 |
| 4,271.0 | 16.35 | 65.00 | 4,169.7 | 409.8 | 699.5 | 810.5 | 1.32 | 1.28 | -1.16 |
| 4,315.0 | 16.44 | 65.20 | 4,211.9 | 415.1 | 710.8 | 822.9 | 0.24 | 0.20 | 0.45 |
| 4,359.0 | 17.00 | 65.10 | 4,254.1 | 420.4 | 722.2 | 835.5 | 1.27 | 1.27 | -0.23 |
| 4,403.0 | 17.00 | 65.00 | 4,296.2 | 425.8 | 733.9 | 848.4 | 0.07 | 0.00 | -0.23 |
| 4,447.0 | 17.49 | 64.10 | 4,338.2 | 431.4 | 745.7 | 861.4 | 1.27 | 1.11 | -2.05 |
| 4,490.0 | 17.97 | 63.90 | 4,379.1 | 437.2 | 757.5 | 874.5 | 1.13 | 1.12 | -0.47 |
| 4,533.0 | 17.80 | 62.90 | 4,420.1 | 443.1 | 769.3 | 887.6 | 0.82 | -0.40 | -2.33 |
| 4,577.0 | 17.70 | 62.80 | 4,462.0 | 449.2 | 781.2 | 901.1 | 0.24 | -0.23 | -0.23 |
| 4,621.0 | 16.75 | 62.20 | 4,504.0 | 455.2 | 792.8 | 914.1 | 2.20 | -2.16 | -1.36 |
| 4,665.0 | 16.50 | 62.60 | 4,546.1 | 461.0 | 803.9 | 926.7 | 0.62 | -0.57 | 0.91 |
| 4,709.0 | 15.80 | 62.20 | 4,588.4 | 466.7 | 814.8 | 938.9 | 1.61 | -1.59 | -0.91 |
| 4,753.0 | 15.70 | 62.40 | 4,630.8 | 472.3 | 825.3 | 950.8 | 0.26 | -0.23 | 0.45 |
| 4,797.0 | 15.00 | 61.31 | 4,673.2 | 477.8 | 835.6 | 962.5 | 1.72 | -1.59 | -2.48 |
| 4,841.0 | 13.60 | 60.70 | 4,715.8 | 483.0 | 845.1 | 973.3 | 3.20 | -3.18 | -1.39 |
| 4,885.0 | 13.70 | 62.10 | 4,758.6 | 488.0 | 854.2 | 983.7 | 0.78 | 0.23 | 3.18 |
| 4,928.0 | 13.60 | 61.90 | 4,800.4 | 492.8 | 863.2 | 993.9 | 0.26 | -0.23 | -0.47 |
| 4,971.0 | 13.20 | 62.10 | 4,842.2 | 497.4 | 872.0 | 1,003.8 | 0.94 | -0.93 | 0.47 |
| 5,015.0 | 12.70 | 62.10 | 4,885.1 | 502.0 | 880.7 | 1,013.7 | 1.14 | -1.14 | 0.00 |
| 5,058.0 | 12.30 | 61.10 | 4,927.1 | 506.5 | 888.9 | 1,023.0 | 1.06 | -0.93 | -2.33 |
| 5,101.0 | 11.90 | 61.30 | 4,969.1 | 510.8 | 896.8 | 1,032.0 | 0.94 | -0.93 | 0.47 |
| 5,145.0 | 12.00 | 62.10 | 5,012.1 | 515.1 | 904.8 | 1,041.1 | 0.44 | 0.23 | 1.82 |
| 5,189.0 | 12.40 | 63.90 | 5,055.2 | 519.4 | 913.1 | 1,050.4 | 1.25 | 0.91 | 4.09 |
| 5,233.0 | 11.80 | 64.20 | 5,098.2 | 523.4 | 921.4 | 1,059.6 | 1.37 | -1.36 | 0.68 |
| 5,235.3 | 11.83 | 64.17 | 5,100.4 | 523.6 | 921.8 | 1,060.1 | 1.20 | 1.16 | -1.45 |



Payzone Directional Survey Report



Company: NEWFIELD EXPLORATION
Project: USGS Myton SW (UT)
Site: SECTION 25 T8S, R17
Well: N-25-8-17
Wellbore: Wellbore #1
Design: Actual

Local Co-ordinate Reference: Well N-25-8-17
TVD Reference: N-25-8-17 @ 5027.0ft (NDSI SS #2)
MD Reference: N-25-8-17 @ 5027.0ft (NDSI SS #2)
North Reference: Grid
Survey Calculation Method: Minimum Curvature
Database: EDM 2003.21 Single User Db

Survey

| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Vertical Section (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
|---------------------------|--------------------|----------------|---------------------------|---------------|---------------|-----------------------------|-----------------------------|----------------------------|---------------------------|
| N-25-8-17 TGT | | | | | | | | | |
| 5,276.0 | 12.30 | 63.60 | 5,140.2 | 527.3 | 929.4 | 1,068.6 | 1.20 | 1.16 | -1.39 |
| 5,320.0 | 11.90 | 60.80 | 5,183.3 | 531.6 | 937.6 | 1,077.8 | 1.61 | -0.91 | -6.36 |
| 5,364.0 | 11.70 | 60.90 | 5,226.3 | 536.0 | 945.5 | 1,086.8 | 0.46 | -0.45 | 0.23 |
| 5,409.0 | 12.70 | 65.10 | 5,270.3 | 540.3 | 953.9 | 1,096.3 | 2.97 | 2.22 | 9.33 |
| 5,451.0 | 12.50 | 67.90 | 5,311.3 | 544.0 | 962.3 | 1,105.4 | 1.53 | -0.48 | 6.67 |
| 5,495.0 | 12.30 | 68.30 | 5,354.3 | 547.5 | 971.1 | 1,114.8 | 0.49 | -0.45 | 0.91 |
| 5,538.0 | 12.20 | 65.10 | 5,396.3 | 551.1 | 979.5 | 1,123.9 | 1.60 | -0.23 | -7.44 |
| 5,582.0 | 12.50 | 61.20 | 5,439.3 | 555.4 | 987.9 | 1,133.3 | 2.01 | 0.68 | -8.86 |
| 5,627.0 | 12.70 | 57.00 | 5,483.2 | 560.4 | 996.3 | 1,143.1 | 2.08 | 0.44 | -9.33 |
| 5,671.0 | 11.73 | 50.50 | 5,526.2 | 565.9 | 1,003.8 | 1,152.3 | 3.82 | -2.20 | -14.77 |
| 5,714.0 | 11.43 | 46.50 | 5,568.3 | 571.6 | 1,010.3 | 1,160.7 | 1.99 | -0.70 | -9.30 |
| 5,757.0 | 10.70 | 48.30 | 5,610.5 | 577.2 | 1,016.3 | 1,168.7 | 1.88 | -1.70 | 4.19 |
| 5,800.0 | 11.50 | 51.50 | 5,652.7 | 582.5 | 1,022.7 | 1,176.9 | 2.35 | 1.86 | 7.44 |
| 5,845.0 | 12.44 | 52.40 | 5,696.7 | 588.3 | 1,030.0 | 1,186.1 | 2.13 | 2.09 | 2.00 |
| 5,889.0 | 13.30 | 52.10 | 5,739.6 | 594.3 | 1,037.8 | 1,195.8 | 1.96 | 1.95 | -0.68 |
| 5,932.0 | 12.60 | 53.40 | 5,781.5 | 600.1 | 1,045.4 | 1,205.3 | 1.76 | -1.63 | 3.02 |
| 5,974.0 | 12.80 | 55.60 | 5,822.5 | 605.4 | 1,052.9 | 1,214.5 | 1.25 | 0.48 | 5.24 |
| 6,018.0 | 12.60 | 57.20 | 5,865.4 | 610.8 | 1,061.0 | 1,224.1 | 0.92 | -0.45 | 3.64 |
| 6,062.0 | 12.90 | 57.50 | 5,908.3 | 616.0 | 1,069.2 | 1,233.8 | 0.70 | 0.68 | 0.68 |
| 6,106.0 | 13.10 | 58.00 | 5,951.2 | 621.3 | 1,077.5 | 1,243.7 | 0.52 | 0.45 | 1.14 |
| 6,150.0 | 13.40 | 60.60 | 5,994.1 | 626.5 | 1,086.2 | 1,253.8 | 1.52 | 0.68 | 5.91 |
| 6,194.0 | 13.20 | 62.20 | 6,036.9 | 631.3 | 1,095.1 | 1,263.9 | 0.95 | -0.45 | 3.64 |
| 6,238.0 | 13.20 | 61.60 | 6,079.7 | 636.0 | 1,104.0 | 1,274.0 | 0.31 | 0.00 | -1.36 |
| 6,281.0 | 13.30 | 62.60 | 6,121.6 | 640.7 | 1,112.7 | 1,283.8 | 0.58 | 0.23 | 2.33 |
| 6,325.0 | 12.60 | 63.20 | 6,164.4 | 645.1 | 1,121.5 | 1,293.7 | 1.62 | -1.59 | 1.36 |
| 6,369.0 | 12.74 | 64.50 | 6,207.4 | 649.4 | 1,130.1 | 1,303.3 | 0.72 | 0.32 | 2.95 |
| 6,412.0 | 12.74 | 65.90 | 6,249.3 | 653.4 | 1,138.7 | 1,312.8 | 0.72 | 0.00 | 3.26 |
| 6,454.0 | 12.20 | 64.91 | 6,290.3 | 657.2 | 1,147.0 | 1,321.8 | 1.38 | -1.29 | -2.36 |
| 6,498.0 | 12.20 | 67.15 | 6,333.3 | 660.9 | 1,155.5 | 1,331.0 | 1.08 | 0.00 | 5.09 |
| 6,542.0 | 11.60 | 68.80 | 6,376.4 | 664.3 | 1,163.9 | 1,340.1 | 1.57 | -1.36 | 3.75 |
| 6,565.0 | 11.60 | 69.20 | 6,398.9 | 666.0 | 1,168.2 | 1,344.6 | 0.35 | 0.00 | 1.74 |
| 6,618.0 | 11.60 | 69.20 | 6,450.8 | 669.8 | 1,178.2 | 1,355.2 | 0.00 | 0.00 | 0.00 |

Checked By: _____ Approved By: _____ Date: _____






Project: USGS Myton SW (UT)
Site: SECTION 25 T8S, R17
Well: N-25-8-17
Wellbore: Wellbore #1
Design: Actual



Azimuths to Grid North
True North: -0.98°
Magnetic North: 10.36°

Magnetic Field
Strength: 52364.4snT
Dip Angle: 65.86°
Date: 12/3/2010
Model: IGRF2010

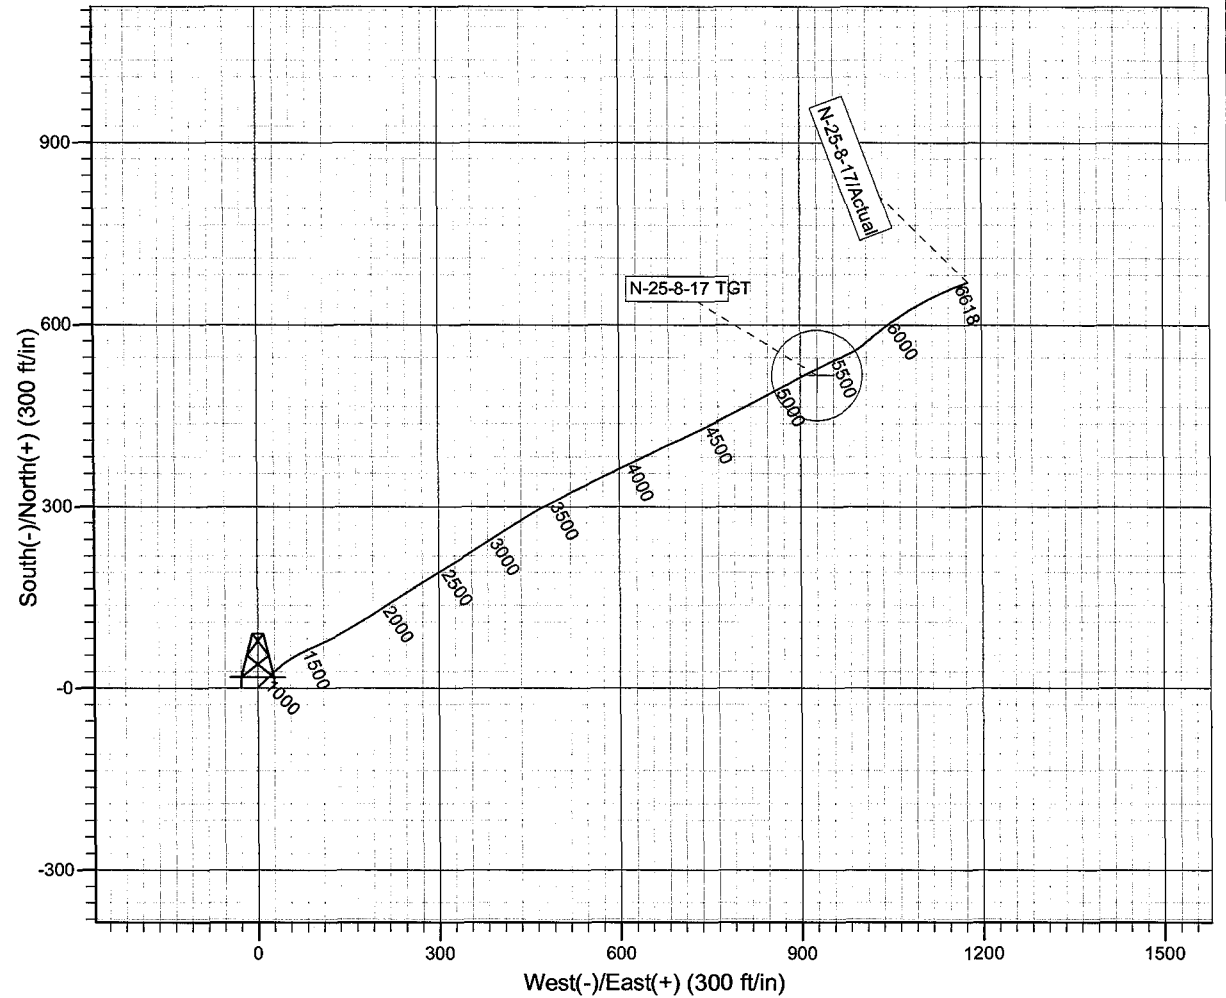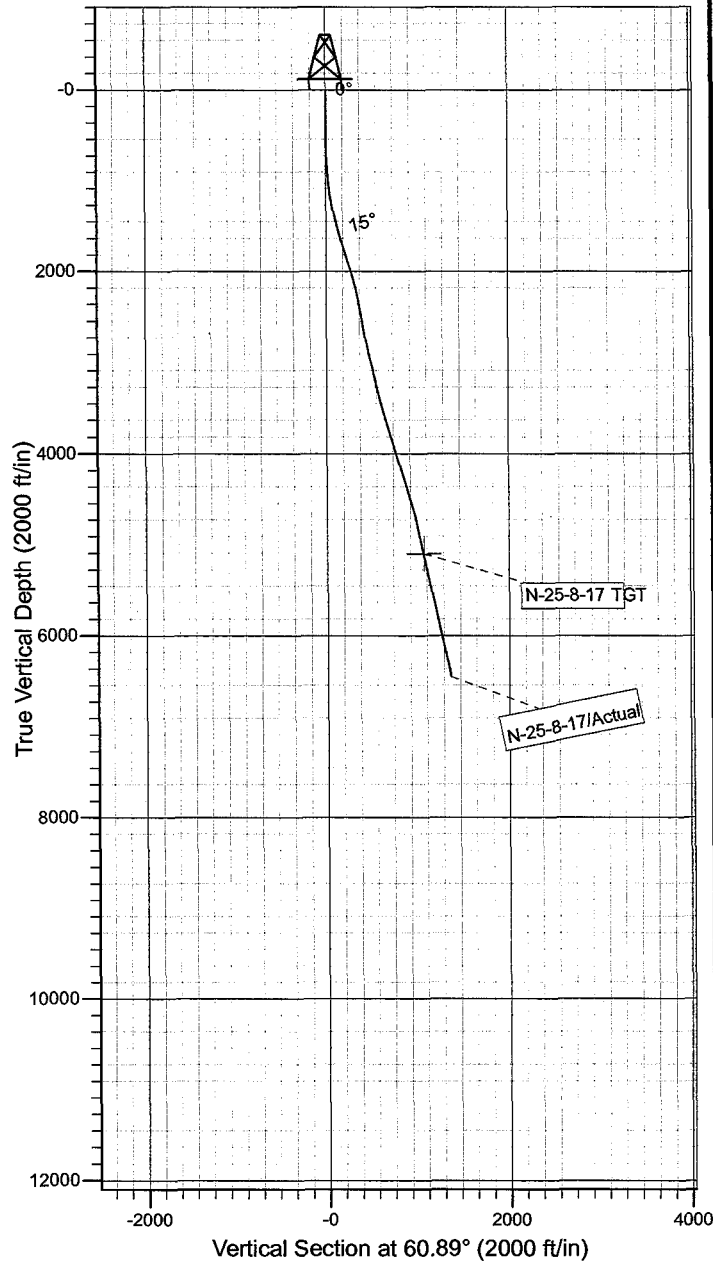

Design: Actual (N-25-8-17/Wellbore #1)

Created By: Sarah Webb

Date: 18:53, April 25 2012

THIS SURVEY IS CORRECT TO THE BEST OF
MY KNOWLEDGE AND IS SUPPORTED
BY ACTUAL FIELD DATA

| | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|--|---|--|----------------------------------|---------------------------------------|--|---|--|---|---|---|--|---------------------------------|---|---|--|---|------------------------------------|---|---|---|--|---|--|--|--|---|--|---|--|---|---|--|
| STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING | | FORM 9 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals. | | 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67845 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 1. TYPE OF WELL Oil Well | | 6. IF INDIAN, ALLOTTEE OR TRIBE NAME: | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY | | 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV) | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052 | | 8. WELL NAME and NUMBER: GMBU N-25-8-17 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 4. LOCATION OF WELL FOOTAGES AT SURFACE: 2265 FSL 0464 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 08.0S Range: 17.0E Meridian: S | | 9. API NUMBER: 43047516490000 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA | | 9. FIELD and POOL or WILDCAT: MONUMENT BUTTE | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| TYPE OF SUBMISSION <input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 8/19/2016 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date: | TYPE OF ACTION <table style="width: 100%;"> <tr> <td><input type="checkbox"/> ACIDIZE</td> <td><input type="checkbox"/> ALTER CASING</td> <td><input type="checkbox"/> CASING REPAIR</td> </tr> <tr> <td><input type="checkbox"/> CHANGE TO PREVIOUS PLANS</td> <td><input type="checkbox"/> CHANGE TUBING</td> <td><input type="checkbox"/> CHANGE WELL NAME</td> </tr> <tr> <td><input type="checkbox"/> CHANGE WELL STATUS</td> <td><input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS</td> <td><input type="checkbox"/> CONVERT WELL TYPE</td> </tr> <tr> <td><input type="checkbox"/> DEEPEN</td> <td><input type="checkbox"/> FRACTURE TREAT</td> <td><input type="checkbox"/> NEW CONSTRUCTION</td> </tr> <tr> <td><input type="checkbox"/> OPERATOR CHANGE</td> <td><input type="checkbox"/> PLUG AND ABANDON</td> <td><input type="checkbox"/> PLUG BACK</td> </tr> <tr> <td><input type="checkbox"/> PRODUCTION START OR RESUME</td> <td><input type="checkbox"/> RECLAMATION OF WELL SITE</td> <td><input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION</td> </tr> <tr> <td><input type="checkbox"/> REPERFORATE CURRENT FORMATION</td> <td><input type="checkbox"/> SIDETRACK TO REPAIR WELL</td> <td><input type="checkbox"/> TEMPORARY ABANDON</td> </tr> <tr> <td><input type="checkbox"/> TUBING REPAIR</td> <td><input type="checkbox"/> VENT OR FLARE</td> <td><input type="checkbox"/> WATER DISPOSAL</td> </tr> <tr> <td><input type="checkbox"/> WATER SHUTOFF</td> <td><input type="checkbox"/> SI TA STATUS EXTENSION</td> <td><input type="checkbox"/> APD EXTENSION</td> </tr> <tr> <td><input type="checkbox"/> WILDCAT WELL DETERMINATION</td> <td><input checked="" type="checkbox"/> OTHER</td> <td>OTHER: <input type="text" value="Well Clean Out"/></td> </tr> </table> | | <input type="checkbox"/> ACIDIZE | <input type="checkbox"/> ALTER CASING | <input type="checkbox"/> CASING REPAIR | <input type="checkbox"/> CHANGE TO PREVIOUS PLANS | <input type="checkbox"/> CHANGE TUBING | <input type="checkbox"/> CHANGE WELL NAME | <input type="checkbox"/> CHANGE WELL STATUS | <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS | <input type="checkbox"/> CONVERT WELL TYPE | <input type="checkbox"/> DEEPEN | <input type="checkbox"/> FRACTURE TREAT | <input type="checkbox"/> NEW CONSTRUCTION | <input type="checkbox"/> OPERATOR CHANGE | <input type="checkbox"/> PLUG AND ABANDON | <input type="checkbox"/> PLUG BACK | <input type="checkbox"/> PRODUCTION START OR RESUME | <input type="checkbox"/> RECLAMATION OF WELL SITE | <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION | <input type="checkbox"/> REPERFORATE CURRENT FORMATION | <input type="checkbox"/> SIDETRACK TO REPAIR WELL | <input type="checkbox"/> TEMPORARY ABANDON | <input type="checkbox"/> TUBING REPAIR | <input type="checkbox"/> VENT OR FLARE | <input type="checkbox"/> WATER DISPOSAL | <input type="checkbox"/> WATER SHUTOFF | <input type="checkbox"/> SI TA STATUS EXTENSION | <input type="checkbox"/> APD EXTENSION | <input type="checkbox"/> WILDCAT WELL DETERMINATION | <input checked="" type="checkbox"/> OTHER | OTHER: <input type="text" value="Well Clean Out"/> |
| <input type="checkbox"/> ACIDIZE | <input type="checkbox"/> ALTER CASING | <input type="checkbox"/> CASING REPAIR | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> CHANGE TO PREVIOUS PLANS | <input type="checkbox"/> CHANGE TUBING | <input type="checkbox"/> CHANGE WELL NAME | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> CHANGE WELL STATUS | <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS | <input type="checkbox"/> CONVERT WELL TYPE | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> DEEPEN | <input type="checkbox"/> FRACTURE TREAT | <input type="checkbox"/> NEW CONSTRUCTION | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> OPERATOR CHANGE | <input type="checkbox"/> PLUG AND ABANDON | <input type="checkbox"/> PLUG BACK | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> PRODUCTION START OR RESUME | <input type="checkbox"/> RECLAMATION OF WELL SITE | <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> REPERFORATE CURRENT FORMATION | <input type="checkbox"/> SIDETRACK TO REPAIR WELL | <input type="checkbox"/> TEMPORARY ABANDON | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> TUBING REPAIR | <input type="checkbox"/> VENT OR FLARE | <input type="checkbox"/> WATER DISPOSAL | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> WATER SHUTOFF | <input type="checkbox"/> SI TA STATUS EXTENSION | <input type="checkbox"/> APD EXTENSION | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| <input type="checkbox"/> WILDCAT WELL DETERMINATION | <input checked="" type="checkbox"/> OTHER | OTHER: <input type="text" value="Well Clean Out"/> | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| 12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. The above mentioned well has had a history of scale. Newfield will be doing a well clean out of the wellbore with the intention to increase hydrocarbon production and bring the well back up to economic production volumes. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| NAME (PLEASE PRINT) Mandie Crozier | | PHONE NUMBER 435 646-4825 | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| SIGNATURE N/A | | TITLE Regulatory Tech | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| DATE 8/19/2016 | | Accepted by the Utah Division of Oil, Gas and Mining Date: August 25, 2016 By: <i>[Signature]</i> | | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
