

CONFIDENTIAL

COPY
FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

7. If Unit or CA Agreement, Name and No.
Peters Point / UTU-63014

8. Lease Name and Well No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
pending **43-007-31406**

10. Field and Pool, or Exploratory
Peter's Point/Wasatch-Mesaverde

11. Sec., T. R. M. or Blk. and Survey or Area
Sec. 26, T12S-R16E

12. County or Parish
Carbon County

13. State
UT

1a. Type of work: DRILL REENTER

1b. Type of Well: Oil Well Gas Well Other Single Zone Multiple Zone

2. Name of Operator Bill Barrett Corporation

3a. Address 1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Report location clearly and in accordance with any State requirements.)*
At surface **SESW, 270' FSL, 1510' FWL**
At proposed prod. zone **NWSE, 1991' FSL, 1950' FEL, Sec. 26**

14. Distance in miles and direction from nearest town or post office*
approximately 51 miles from Myton, Utah

15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)
270' SH / 646' BH

16. No. of acres in lease
1598.62

17. Spacing Unit dedicated to this well
40 acres

18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft.
16' SH / 1317' BH

19. Proposed Depth
8400' MD

20. BLM/BIA Bond No. on file
Nationwide Bond #WYB000040

21. Elevations (Show whether DF, KDB, RT, GL, etc.)
7162' graded ground

22. Approximate date work will start*
09/01/2008

23. Estimated duration
45 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

- 1. Well plat certified by a registered surveyor.
- 2. A Drilling Plan.
- 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- 5. Operator certification
- 6. Such other site specific information and/or plans as may be required by the BLM.

25. Signature *Tracey Fallang* Name (Printed/Typed) Tracey Fallang Date 04/23/2008

Title Environmental Regulatory Analyst

Approved by (Signature) *[Signature]* Name (Printed/Typed) BRADLEY G. HILL Date 05-05-08

Title Office ENVIRONMENTAL MANAGER

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

Surf

577562X
43988924
39.738279
-110.094827

BLL
578104X
43994194
39.742977
-110.088445

RECEIVED

APR 28 2008


DIV. OF OIL, GAS & MINING

Federal Approval of this Action is Necessary

T12S, R16E, S.L.B.&M.

N89°22'W - 2629.44' (G.L.O.)

N89°50'W - 2629.44' (G.L.O.)

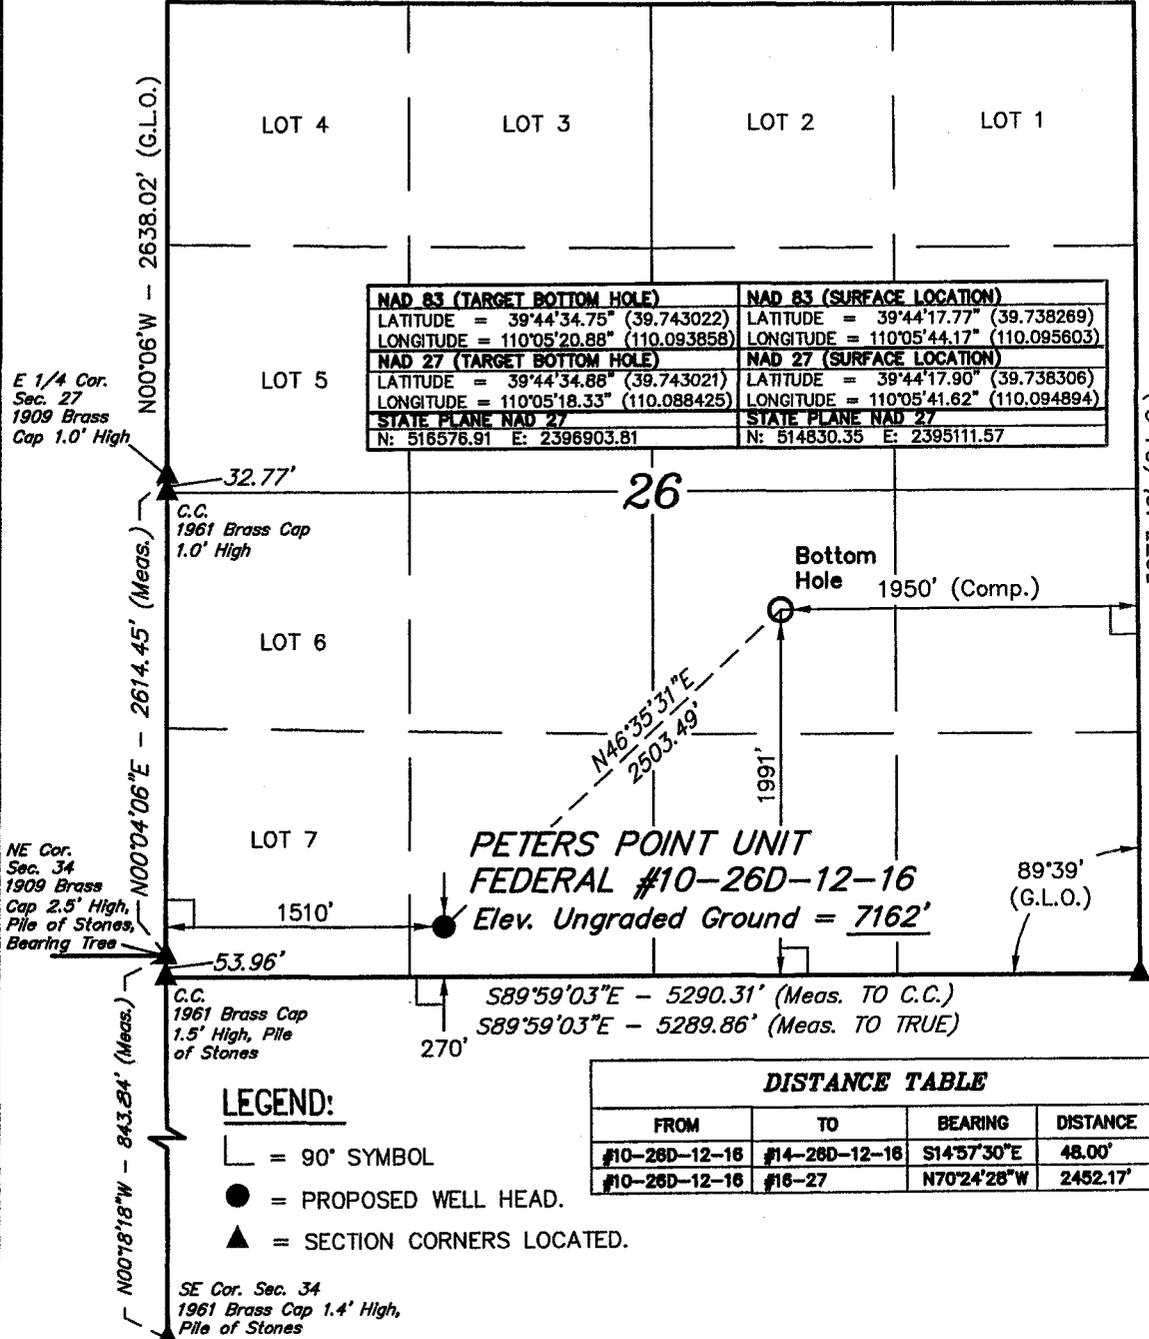

NAD 83 (TARGET BOTTOM HOLE) LATITUDE = 39°44'34.75" (39.743022) LONGITUDE = 110°05'20.88" (110.093858)	NAD 83 (SURFACE LOCATION) LATITUDE = 39°44'17.77" (39.738269) LONGITUDE = 110°05'44.17" (110.095603)
NAD 27 (TARGET BOTTOM HOLE) LATITUDE = 39°44'34.88" (39.743021) LONGITUDE = 110°05'18.33" (110.088425)	NAD 27 (SURFACE LOCATION) LATITUDE = 39°44'17.90" (39.738306) LONGITUDE = 110°05'41.62" (110.094894)
STATE PLANE NAD 27 N: 516576.91 E: 2396903.81	STATE PLANE NAD 27 N: 514830.35 E: 2395111.57

Bottom Hole 1950' (Comp.)

1991'

N46°35'31"E
2503.49'

89°39' (G.L.O.)

1510'

53.96'

270'

S89°59'03"E - 5290.31' (Meas. TO C.C.)
S89°59'03"E - 5289.86' (Meas. TO TRUE)

**PETERS POINT UNIT
FEDERAL #10-26D-12-16**
Elev. Ungraded Ground = 7162'

- LEGEND:**
- └─┘ = 90° SYMBOL
 - = PROPOSED WELL HEAD.
 - ▲ = SECTION CORNERS LOCATED.

DISTANCE TABLE			
FROM	TO	BEARING	DISTANCE
#10-26D-12-16	#14-26D-12-16	S14°57'30"E	48.00'
#10-26D-12-16	#16-27	N70°24'28"W	2452.17'

SE Cor. Sec. 34
1961 Brass Cap 1.4' High,
Pile of Stones

BILL BARRETT CORPORATION


Well location, PETERS POINT UNIT FEDERAL #10-26D-12-16, located as shown in the SE 1/4 SW 1/4 of Section 26, T12S, R16E, S.L.B.&M., Carbon County, Utah.

BASIS OF ELEVATION

COTTON TRIANGULATION STATION LOCATED IN THE NW 1/4 OF SECTION 31, T12S, R16E, S.L.B.&M., TAKEN FROM THE TWIN HOLLOW QUADRANGLE, UTAH, CARBON COUNTY, 7.5 MINUTE SERIES (TOPOGRAPHICAL MAP) PUBLISHED BY THE UNITED STATES DEPARTMENT OF THE INTERIOR, GEOLOGICAL SURVEY. SAID ELEVATION IS MARKED AS BEING 7386 FEET.

BASIS OF BEARINGS

BASIS OF BEARINGS IS A G.P.S. OBSERVATION.



CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

Robert H. Han
REGISTERED LAND SURVEYOR
REGISTRATION NO. 161319
STATE OF UTAH

1961 Brass Cap
0.8' High, Pile
of Stones

UINTAH ENGINEERING & LAND SURVEYING
85 SOUTH 200 EAST - VERNAL, UTAH 84078
(435) 789-1017

SCALE 1" = 1000'	DATE SURVEYED: 03-11-08	DATE DRAWN: 03-28-08
PARTY D.R. A.W. C.C.	REFERENCES G.L.O. PLAT	
WEATHER COOL	FILE BILL BARRETT CORPORATION	



April 24, 2008

Ms. Diana Mason
State of Utah
Division of Oil, Gas and Mining
1594 West North Temple, Suite 1210
P.O. Box 145801
Salt Lake City, Utah 84114-5801

RE: Directional Drilling R649-3-11
Peters Point Unit Federal 10-26D-12-16
SHL: 270' FSL & 1510' FWL SESW 26-T12S-R16E
BHL: 1991' FSL & 1950' FEL NWSE 26-T12S-R16E
Carbon County, Utah

Dear Ms. Mason:

Pursuant to the filing of Bill Barrett Corporation's ("BBC") Application for Permit to Drill ("APD") regarding the above referenced well, we are hereby submitting this letter in accordance with Oil & Gas Conservation Rule R649-3-11 pertaining to the "Exception to Location and Siting of Wells."

- The above-mentioned proposed location is within the Peters Point Unit Area;
- This well is a directional well and is greater than 460 feet from the Peter's Point Unit boundary.
- BBC hereby certifies that it is the sole working interest owner within 460 feet of the entire directional well bore.

Based on the information provided, BBC requests that the permit be granted pursuant to R649-3-11. If you should have any questions or need further information, please contact me at 303-312-8129.

Sincerely,

Doug Gundry-White by TLE
Doug Gundry-White
Senior Landman

RECEIVED
APR 28 2008
DIV. OF OIL, GAS & MINING

1099 18TH STREET
SUITE 2300
DENVER, CO 80202
P 303.293.9100
F 303.291.0420

DRILLING PROGRAM

BILL BARRETT CORPORATION

Peter's Point Unit Federal #10-26D-12-16

SESW, 270' FSL, 1510' FWL, Sec. 26, T12S-R16E (surface hole)

NWSE, 1991' FSL, 1950' FEL, Sec. 26, T12S-R16E (bottom hole)

Carbon County, Utah

1 – 2. Estimated Tops of Geological Markers and Formations Expected to Contain Water, Oil and Gas and Other Minerals

<u>Formation</u>	<u>Depth – MD</u>	<u>Depth – TVD</u>
Green River	Surface	Surface
Wasatch	3604'*	3288'*
North Horn	5739'*	5114'*
Dark Canyon	7300'*	6658'*
Price River	7574'*	6932'*
TD	8400'*	7700'*

PROSPECTIVE PAY

*Members of the Mesaverde formation and Wasatch formation (inclusive of the North Horn) are primary objectives for oil/gas.

3. BOP and Pressure Containment Data

<u>Depth Intervals</u>	<u>BOP Equipment</u>
0 – 1000'	No pressure control required
1000' – TD	11" 3000# Ram Type BOP 11" 3000# Annular BOP
- Drilling spool to accommodate choke and kill lines;	
- Ancillary equipment and choke manifold rated at 3,000#. All BOP and BOPE tests will be in accordance with the requirements of onshore Order No. 2;	
- The BLM and the State of Utah Division of Oil, Gas and Mining will be notified 24 hours in advance of all BOP pressure tests.	
- BOP hand wheels may be underneath the sub-structure of the rig if the drilling rig used is set up to operate most efficiently in this manner.	

4. Casing Program

<u>Hole Size</u>	<u>SETTING DEPTH</u>		<u>Casing Size</u>	<u>Casing Weight</u>	<u>Casing Grade</u>	<u>Thread</u>	<u>Condition</u>
	<u>(FROM)</u>	<u>(TO)</u>					
12 ¼"	surface	1,000'	9 5/8"	36#	J or K 55	ST&C	New
7 7/8" & 8 3/4"	surface	8,400'	5 ½"	17#	N-80	LT&C	New
			4 ½"	11.6#	I-100	LT&C	New
Note: BBC will use one of two options of production casing noted above. 7 7/8" hole size will begin at the point the bit is changed.							

5. **Cementing Program**

9 5/8" Surface Casing	Approximately 240 sx Halliburton Light Premium with additives mixed at 12.7 ppg (yield = 1.85 ft ³ /sx) and 170 sx Premium cement with additives mixed at 15.8 ppg (yield = 1.16 ft ³ /sx) circulated to surface with 100% excess.
5 1/2" Production Casing OR	Approximately 1660 sx 50/50 Poz Premium cement with additives mixed at 13.4 ppg (yield = 1.49 ft ³ /sx). Top of cement to be determined by log and sample evaluation; estimated TOC 900'.
4 1/2" Production Casing	Approximately 2010 sx 50/50 Poz Premium cement with additives mixed at 13.4 ppg (yield = 1.49 ft ³ /sx). Top of cement to be determined by log and sample evaluation; estimated TOC 900'.
Note: Actual volumes to be calculated from caliper log.	

6. **Mud Program**

<u>Interval</u>	<u>Weight</u>	<u>Viscosity</u>	<u>Fluid Loss (API filtrate)</u>	<u>Remarks</u>
0 - 40'	8.3 - 8.6	27 - 40	--	Native Spud Mud
40' - 1000'	8.3 - 8.6	27 - 40	15 cc or less	Native/Gel/Lime
1000' - TD	8.6 - 9.5	38 - 46	15 cc or less	LSND/DAP
Note: Sufficient mud materials to maintain mud properties, control lost circulation and to contain "kicks" will be available at wellsite. BBC may require minor amounts of diesel to be added to its fluid system in order to reduce tork and drag.				
Note: In the event air drilling should occur at this location:				
<ul style="list-style-type: none"> - Fresh water would be used to suppress the dust coming out. The blooie line, approximately 37' long and 6" diameter, would run from the pit to the wellhead. There is no ignition system as burnable gas should not be encountered. - Capacity of compressor: 1250SCFM with an 1170 SCFM on standby, which would be located very near the wellbore. The compressor has switches to shut off should any problems be encountered. - The rig has mud pumps capable of pumping the kill fluid (fresh water), of which there is 500 bbls on location at all times. 				

7. **Testing, Logging and Core Programs**

Cores	None anticipated;
Testing	None anticipated;
Sampling	30' to 50' samples; surface casing to TD. Preserve samples all show intervals;
Surveys	Run every 1000' and on trips, slope only;
Logging	DIL-GR-SP, FDC-CNL-GR-CAL-Pe-Microlog, Sonic-GR, all TD to surface.

8. **Anticipated Abnormal Pressures or Temperatures**

No abnormal pressures or temperatures or other hazards are anticipated.

Maximum anticipated bottom hole pressure equals approximately 3804 psi* and maximum anticipated surface pressure equals approximately 2110 psi** (bottom hole pressure minus the pressure of a partially evacuated hole calculated at 0.22 psi/foot).

*Max Mud Wt x 0.052 x TD = A (bottom hole pressure)

**Maximum surface pressure = A - (0.22 x TD)

9. **Auxiliary Equipment**

- a) Upper kelly cock; lower Kelly cock will be installed while drilling
- b) Inside BOP or stab-in valve (available on rig floor)
- c) Safety valve(s) and subs to fit all string connections in use
- d) Mud monitoring will be visually observed

10. **Drilling Schedule**

Location Construction: September 1, 2008
Spud: September 8, 2008
Duration: 15 days drilling time
30 days completion time

SURFACE USE PLAN

BILL BARRETT CORPORATION

Peter's Point Unit Federal 14-26D-12-16 Pad Wells

<p style="text-align: center;"><u>Peter's Point Unit Federal #3-35D-12-16</u></p> SESW, 208' FSL, 1527' FWL, Sec. 26, T12S-R16E (surface hole) NENW, 632' FNL, 2022' FWL, Sec. 35, T12S-R16E (bottom hole) Carbon County, Utah	<p style="text-align: center;"><u>Peter's Point Unit Federal #15-26D-12-16</u></p> SESW, 239' FSL, 1518' FWL, Sec. 26, T12S-R16E (surface hole) SWSE, 671' FSL, 1953' FEL, Sec. 26, T12S-R16E (bottom hole) Carbon County, Utah
<p style="text-align: center;"><u>Peter's Point Unit Federal #13-26D-12-16</u></p> SESW, 254' FSL, 1514' FWL, Sec. 26, T12S-R16E (surface hole) SWSW, 701' FSL, 679' FWL, Sec. 26, T12S-R16E (bottom hole) Carbon County, Utah	<p style="text-align: center;"><u>Peter's Point Unit Federal #11-26D-12-16</u></p> SESW, 285' FSL, 1506' FWL, Sec. 26, T12S-R16E (surface hole) NESW, 2002' FSL, 1997' FWL, Sec. 26, T12S-R16E (bottom hole) Carbon County, Utah
<p style="text-align: center;"><u>Peter's Point Unit Federal #10-26D-12-16</u></p> SESW, 270' FSL, 1510' FWL, Sec. 26, T12S-R16E (surface hole) NWSE, 1991' FSL, 1950' FEL, Sec. 26, T12S-R16E (bottom hole) Carbon County, Utah	<p style="text-align: center;"><u>Peter's Point Unit Federal #12-26D-12-16</u></p> SESW, 301' FSL, 1502' FWL, Sec. 26, T12S-R16E (surface hole) NWSW, 2015' FSL, 673' FWL, Lot 6, Sec. 26, T12S-R16E (bottom hole) Carbon County, Utah

The onsite for this pad occurred on April 11, 2008. This is an existing pad with one vertical well (the 14-26D-12-15) and six additional directional wells are planned. Minimal additional disturbance is required for expansion to accommodate the additional wells.

The excavation contractor would be provided with an approved copy of the surface use plan of operations before initiating construction.

1. Existing Roads:

- a. The existing well pad is located approximately 51 miles from Myton, Utah. Maps reflecting directions to the proposed well pad are included (see Topographic Maps A and B).
- b. An access road, approximately 1882 feet in length exists to this pad. Total road disturbance requested for this access is 50-feet.
- c. Surface disturbance and vehicular travel would be limited to the approved existing access road. Adequate signs would be posted, as necessary, to warn the public of project related traffic.
- d. BBC would be responsible for all maintenance of the access road including drainage structures.
- e. The use of roads under State and County Road Department maintenance is necessary to access the Peter's Point Unit. However, an encroachment permit is not anticipated since there are no upgrades proposed to the State or County road systems at this time.
- f. All existing roads would be maintained and kept in good repair during all phases of operation.
- g. Vehicle operators would obey posted speed restrictions and observe safe speeds commensurate with road and weather conditions.

2. Planned Access Road:

- a. See 1. b. under Existing Roads.

3. Location of Existing Wells (see Topographic Map C):

a. Following is a list of wells with surface hole locations within a one-mile radius of the proposed well:

i. water wells	none
ii. injection wells	none
iii. disposal wells	none
iv. drilling wells	none
v. temp shut-in wells	none
vi. producing wells	nine
vii. abandoned wells	none

4. Location of Production Facilities (see enclosed "Proposed Facility Layout"):

a. All facilities for this pad would be located adjacent to each other (existing facilities for the Peter's Point 14-26D will be re-located as noted on the facility layout). Each well would have its own meter run and separator and six (6) additional 400-bbl tanks would be installed as necessary.

b. All permanent above-ground structures would be painted a flat, non-reflective Olive Black to match the standard environmental colors. All facilities would be painted the designated color at the time of installation. Facilities required to comply with the Occupational Safety and Health Act (OSHA) may be excluded.

d. Site security guidelines identified in 43 CFR 3162.7-5 and Onshore Oil and Gas Order No. 3 would be adhered to.

e. Gas meter runs would be constructed and located on lease within 500 feet of the wellheads. Meter runs are housed and/or fenced. All gas production and measurement shall comply with the provisions of 43 CFR 3162.7-3, Onshore Oil and Gas Order No. 5, and American Gas Association (AGA) Report No. 3. Use of electronic flow meter (EFMs) for gas measurement purposes is requested with this application as well as use of flow conditioners (versus straightening vanes) for each new well.

f. A tank battery exists on this lease and would be modified as per the proposed facility layout to include additional equipment. All loading lines and valves would be placed inside the berm surrounding the tank battery or would have a secondary containment vessel. All liquid hydrocarbon production and measurement shall conform to the provisions of 43 CFR 3162.7-2 and Onshore Oil and Gas Order No. 4 for the measurement of oil. BBC requests permission to install the necessary production/operation facilities with this application.

g. Any necessary pits would be properly fenced to prevent any wildlife and livestock entry.

h. All access roads would be maintained as necessary to prevent erosion and accommodate year-round traffic as practicable. The roads would be maintained in a safe, useable condition.

- i. The site would require periodic maintenance to ensure that drainages are kept open and free of debris and that surfaces are properly treated to reduce erosion, fugitive dust, and impacts to adjacent areas.
 - j. A 6-inch buried gas pipeline, approximately 2150 feet in length, exists to this location.
5. Location and Type of Water Supply:
 - a. Bill Barrett Corporation would use water consistent with approvals granted by the Utah State Engineer's Office under Application Number 90-1853 (T76109) which expires April 3, 2009 or an existing water well in Sec. 13, T12S-R14E granted by the Utah State Engineer's Office under Application Number 90-1849 (T75896) which expires September 13, 2008.
 - b. Water use for this location will most likely be diverted from Nine Mile Creek, the S $\frac{1}{4}$ of Section 8, T12S-R16E or from a water well located in the N $\frac{1}{4}$ of State Section 32-T12S-R16E. For either of these sources, bobtail trucks would haul the water, traveling Cottonwood Canyon dugway to Peter's Point road.
6. Source of Construction Material:
 - a. The use of materials would conform to 43 CFR 3610.2-3.
 - b. No construction materials would be taken off-lease.
 - c. If any additional gravel is required, it would be obtained from SITLA materials permits or from federal BBC locations within the Peter's Point unit.
7. Methods of Handling Waste Disposal:
 - a. All wastes associated with this application would be contained and disposed of utilizing approved facilities.
 - b. Drill cuttings would be contained and buried on site.
 - c. The fluids in the existing reserve pit for the Peter's Point 14-26D well will be disposed of or evaporated prior to the expansion of the pit, which is necessary to accommodate the additional wells. The reserve pit is located outboard of the location along the west side of the pad.
 - d. The reserve pit would be constructed so as not to leak, break or allow any discharge.
 - e. Due to the expansion necessary, the reserve pit would be re-lined with a 12 mil minimum thickness polyethylene nylon reinforced liner material. The liner would overlay straw, soil and/or bentonite if rock is encountered during excavation. The pit liner would overlap the pit walls and be anchored with soil and/or rocks to hold it in place. No trash, scrap pipe, etc., that could puncture the liner would be disposed of in the pit. Pit walls would be sloped no greater than 2:1 and the depth of the reserve pit would be approximately 8-feet with a minimum of 2 foot freeboard.

- f. The reserve pit has been located in cut material. Three sides of the reserve pit would be fenced before drilling starts. The fourth side would be fenced as soon as drilling is completed and shall remain until the pit is dry. After the reserve pit has dried, all areas not needed for production would be rehabilitated as per the plans for reclamation of surface (10. below).
- g. Chemicals on the EPA's Consolidated List of Chemicals subject to reporting under Title III of the Superfund Amendments and Reauthorization Act of 1986 (SARA) in quantities over 10,000 pounds that may be used, produced, stored, transported or disposed of annually in association with the drilling, testing or completion of each well include diesel fuel, hydrochloric acid and silica sand. This material would be consumed in the drilling and completion process. No extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities would be used, produced, stored, transported or disposed of in association with the drilling, testing or completion of the wells.
- h. Trash would be contained in a trash cage or roll-off container and hauled away to an approved disposal site as necessary but no later than at the completion of drilling operations. The contents of the trash container would be hauled off periodically to the approved Carbon or Uintah County Landfill.
- i. Produced fluids from each well other than water would be produced into a test tank until such time as construction of production facilities is completed. Any spills of oil, gas, salt water or other produced fluids would be cleaned up and removed.
- j. After initial clean-up and based on volumes, BBC would install a tank (maximum size 400 barrel capacity) to contain produced waste water. After first production, produced wastewater would be confined to a lined pit or storage tank for a period not to exceed ninety (90) days. Thereafter, produced water would be used in further drilling and completion activities, evaporated in the pit, or hauled to a State approved disposal facility.
- k. Any salts and/or chemicals, which are an integral part of the drilling system, would be disposed of in the same manner as the drilling fluid.
- l. Sanitary facilities would be on site at all times during operations. Sewage would be placed in a portable chemical toilet and the toilet replaced periodically utilizing a licensed contractor to transport by truck the portable chemical toilet so that its contents can be delivered to the Price or Vernal Wastewater Treatment Facility in accordance with state and county regulations.
- m. Any liquid hydrocarbons produced during completion work would be contained in test tanks on the well location. The tanks would be removed from location at a later date. A flare pit may be constructed a minimum of 110' from the wellheads and may be used during completion work. In the event a flare pit proves to be unworkable in this situation, a flare stack would be installed. BBC would flow back as much fluid and gas as possible into vessels, separating the fluid from the gas. The fluid would then be either returned to the reserve pit or placed into a tank. Gas would be then directed into the flare pit or the flare stack with a constant source of ignition. Natural gas would be directed to the pipeline as soon as pipeline gas quality standards are met.

- n. Hydrocarbons would be removed from the reserve pit as soon as practical. In the event immediate removal is not practical, the reserve pit would be flagged overhead or covered with wire or plastic mesh to protect migrating birds.

8. Ancillary Facilities:

- a. Garbage containers and portable toilets are the only ancillary facilities proposed in this application

9. Well Site Layout:

- a. Each well would be properly identified in accordance with 43 CFR 3162.6.
- b. The rig layout and cross section diagrams are enclosed (see Location Layout and Cross Section Plats).
- c. The pad and road designs are consistent with BLM specifications.
- d. Minimal additional disturbance is necessary to accommodate the additional wells being added. The pad dimensions are 450' x 155' with a reserve pit of 245' x 100'.
- e. All surface disturbing activities would be supervised by a qualified, responsible company representative who is aware of the terms and conditions of the APD and specifications in the approved plans.
- f. All cut and fill slopes would be such that stability can be maintained for the life of the activity.
- g. Diversion ditches would be constructed, if necessary, around the well pad to prevent surface waters from entering the area.
- h. The stockpiled topsoil (first 6 inches or maximum available) would be stored in a windrow on the uphill side of the location to prevent any possible contamination. All topsoil would be stockpiled for reclamation in such a way as to prevent soil loss and contamination.
- i. Pits would remain fenced until site cleanup.
- j. If air drilling occurs, the blooie line would be located at least 100 feet from the individual well head and would run from the each wellhead directly to the pit.
- k. Water application may be implemented if necessary to minimize the amount of fugitive dust.

10. Plan for Restoration of the Surface:

Producing Wells

- a. Rat and mouse holes would be filled and compacted from bottom to top immediately upon release of the drilling rig from location.
- b. The reserve pit would be closed as soon as reasonably practical, but no later than 90 days from completion of the last well on the pad, provided favorable weather conditions and that there are no plans to re-use the pit within one year. An extension may be given at the discretion of the BLM Authorized Officer. The following are requirements for pit closures:
 - Squeezing of pit fluids and cuttings is prohibited;
 - Pits must be dry of fluids or they must be removed via vac-truck or other environmentally acceptable method prior to backfilling, re-contouring and replacement of topsoil;
 - Mud and cuttings left in pit must be buried at least 3-feet below re-contoured grade;
 - If a liner was used, the polyethylene nylon reinforced liner shall be torn and perforated before backfilling;
 - The operator would be responsible for re-contouring any subsidence areas that develop from closing a pit before it is sufficiently dry.
 - The operator shall contact the BLM Authorized Officer at least 48-hours prior to the filling and reclamation of pits and the start of any reclamation such as recontouring and reseeded.
- c. Reclamation requirements would be dependant upon plans for subsequent drilling activity on the pad. The operator shall contact the BLM Authorized Officer within 90 days of completion of the last well on the pad and provide plans for subsequent pad use.
 - In the event that the operator plans to re-occupy the pad within three years, the operator shall seed the unused portions of the pad with a cover crop as approved for this use by the BLM. If necessary, this cover crop would be replanted each year that the pad remains in an un-reclaimed state. Unless otherwise specifically authorized, no pad shall remain in an un-reclaimed state for more than three years.
 - Cover crops would be seeded by broadcasting seed over all unused portions of the pad. Seed would be covered with soil to the appropriate depth by raking or other methods.
 - In the event there are no plans to re-occupy the pad within three years, interim reclamation activities would begin within 90 days. The operator would use the BLM approved seed mix and would seed during the first suitable seeding season.
 - Interim reclamation drill seeding would be conducted on the contour to a depth of 0.5 inch, followed by cultipaction to compact the seedbed, preventing soil and seed losses. To maintain quality and purity, the current years tested, certified seed with a minimum germination rate of 80% and a minimum purity of 90% would be used.

- Topsoil salvaged from the drill site and stored for more than one year would be placed at the location indicated on the well site layout drawing and graded to a depth optimum to maintain topsoil viability, seeded with the BLM prescribed seed mixture and covered with mulch for protection from wind and water erosion and to discourage the invasion of weeds.
- d. The operator would control noxious weeds along access road use authorizations, pipeline route authorizations, well sites or other applicable facilities by spraying or mechanical removal. A list of noxious weeds may be obtained from the BLM or the appropriate county extension office. On BLM administered land it is required that a Pesticide Use Proposal be submitted and approved prior to the application of herbicides, pesticides or possibly hazardous chemicals.

Dry Hole

- a. All disturbed lands associated with this project, including the pipelines, access roads, water management facilities, etc. would be expediently reclaimed and reseeded in accordance with the reclamation plan and any pertinent site-specific COAs.
11. Surface and Mineral Ownership:
- a. Surface ownership – Federal under the management of the Bureau of Land Management – Price Field Office, 125 South 600 West, Price Utah 84078; (435) 636-3600.
- b. Mineral ownership – Federal under the management of the Bureau of Land Management – Price Field Office, 125 South 600 West, Price Utah 84078; (435) 636-3600.
12. Other Information:
- a. Montgomery Archaeological Consultants conducted a Class III archeological survey. A copy of the report was submitted under separate cover to the appropriate agencies by Montgomery as MOAC Report No. 05-480 dated December 12, 2005.
- b. Intermountain Paleo Consulting, Inc. conducted monitoring activities at the time of construction on the Peter's Point 14-26D pad, IPC Report No. 07-159 dated August 24, 2007. No fossils were found.
- c. Areas in the proposed drilling program where fluids escaping the wellbore and exiting onto a hillside might occur will be identified. In those cases, cement and/ or fluid loss compounds (types of lost circulation fluids) would be utilized to heal up vags and cracks. Upon individual evaluation of the proposed well sites, air drilling the hole to surface casing depth may occur.
- d. A combustor may be installed at this location for control of associated condensate tank emissions. A combustor ranges from 24" to 48" wide and is approximately 10' tall. Combustor placement would be on existing disturbance and would not be closer than 100' to any tank or wellhead.

Well name:	Utah: West Tavaputs
Operator:	Bill Barrett
String type:	Surface
Location:	Carbon County, UT

Design parameters:

Collapse

Mud weight: 9.50 ppg

Design is based on evacuated pipe.

Minimum design factors:

Collapse:

Design factor 1.125

Burst:

Design factor 1.00

Environment:

H2S considered? No
 Surface temperature: 75.00 °F
 Bottom hole temperature: 89 °F
 Temperature gradient: 1.40 °F/100ft
 Minimum section length: 1,000 ft

Cement top: Surface

Burst

Max anticipated surface

pressure: 2,735 psi

Internal gradient: 0.22 psi/ft

Calculated BHP 2,955 psi

Annular backup: 9.50 ppg

Tension:

8 Round STC: 1.80 (J)

8 Round LTC: 1.80 (J)

Buttress: 1.80 (J)

Premium: 1.80 (J)

Body yield: 1.80 (B)

Tension is based on buoyed weight.

Neutral point: 859 ft

Non-directional string.

Re subsequent strings:

Next setting depth: 10,000 ft

Next mud weight: 9.500 ppg

Next setting BHP: 4,935 psi

Fracture mud wt: 10.000 ppg

Fracture depth: 10,000 ft

Injection pressure 5,195 psi

Run Seq	Segment Length (ft)	Size (in)	Nominal Weight (lbs/ft)	Grade	End Finish	True Vert Depth (ft)	Measured Depth (ft)	Drift Diameter (in)	Internal Capacity (ft ³)
1	1000	9.625	36.00	J/K-55	ST&C	1000	1000	8.796	71.2
Run Seq	Collapse Load (psi)	Collapse Strength (psi)	Collapse Design Factor	Burst Load (psi)	Burst Strength (psi)	Burst Design Factor	Tension Load (Kips)	Tension Strength (Kips)	Tension Design Factor
1	493	2020	4.094	2735	3520	1.29	31	453	14.64 J

Prepared Dominic Spencer
by: Bill Barrett

Phone: (303) 312-8143
FAX: (303) 312-8195

Date: August 1, 2003
Denver, Colorado

Remarks:

Collapse is based on a vertical depth of 1000 ft, a mud weight of 9.5 ppg. The casing is considered to be evacuated for collapse purposes.
 Collapse strength is based on the Westcott, Dunlop & Kemler method of biaxial correction for tension.

Burst strength is not adjusted for tension.

Engineering responsibility for use of this design will be that of the purchaser.

Well name:
 Operator: **Bill Barrett**
 String type: Production
 Location: Uintah County, UT

Uta: West Tavaputs

Design parameters:

Collapse

Mud weight: 9.50 ppg

Design is based on evacuated pipe.

Minimum design factors:

Collapse:

Design factor 1.125

Burst:

Design factor 1.00

Environment:

H2S considered? No
 Surface temperature: 75.00 °F
 Bottom hole temperature: 215 °F
 Temperature gradient: 1.40 °F/100ft
 Minimum section length: 1,500 ft

Cement top: 900 ft

Burst

Max anticipated surface pressure: 4,705 psi

Internal gradient: 0.02 psi/ft

Calculated BHP 4,935 psi

Annular backup: 9.50 ppg

Tension:

8 Round STC: 1.80 (J)
 8 Round LTC: 1.80 (J)
 Buttress: 1.80 (J)
 Premium: 1.80 (J)
 Body yield: 1.80 (B)

Non-directional string.

Tension is based on buoyed weight.
 Neutral point: 8,559 ft

Run Seq	Segment Length (ft)	Size (in)	Nominal Weight (lbs/ft)	Grade	End Finish	True Vert Depth (ft)	Measured Depth (ft)	Drift Diameter (in)	Internal Capacity (ft³)
1	10000	5.5	17.00	N-80	LT&C	10000	10000	4.767	344.6
Run Seq	Collapse Load (psi)	Collapse Strength (psi)	Collapse Design Factor	Burst Load (psi)	Burst Strength (psi)	Burst Design Factor	Tension Load (Kips)	Tension Strength (Kips)	Tension Design Factor
1	4935	6290	1.275	4705	7740	1.65	146	348	2.39 J

Prepared Dominic Spencer
 by: Bill Barrett

Phone: (303) 312-8143
 FAX: (303) 312-8195

Date: August 1,2003
 Denver, Colorado

Remarks:

Collapse is based on a vertical depth of 10000 ft, a mud weight of 9.5 ppg The casing is considered to be evacuated for collapse purposes.
 Collapse strength is based on the Westcott, Dunlop & Kemler method of biaxial correction for tension.

Burst strength is not adjusted for tension.

Engineering responsibility for use of this design will be that of the purchaser.

Well name:

West Tavaputs General

Operator: **Bill Barrett Corporation**

String type: Production

Design parameters:

Collapse

Mud weight: 9.50 ppg

Design is based on evacuated pipe.

Burst

Max anticipated surface

pressure: 2,735 psi

Internal gradient: 0.22 psi/ft

Calculated BHP 4,935 psi

No backup mud specified.

Minimum design factors:

Collapse:

Design factor 1.125

Burst:

Design factor 1.00

Tension:

8 Round STC: 1.80 (J)

8 Round LTC: 1.80 (J)

Buttress: 1.80 (J)

Premium: 1.80 (J)

Body yield: 1.80 (B)

Tension is based on buoyed weight.

Neutral point: 8,580 ft

Environment:

H2S considered? No

Surface temperature: 60.00 °F

Bottom hole temperature: 200 °F

Temperature gradient: 1.40 °F/100ft

Minimum section length: 1,500 ft

Cement top: 2,500 ft

Non-directional string.

Run Seq	Segment Length (ft)	Size (in)	Nominal Weight (lbs/ft)	Grade	End Finish	True Vert Depth (ft)	Measured Depth (ft)	Drift Diameter (in)	Internal Capacity (ft³)
1	10000	4.5	11.60	I-100	LT&C	10000	10000	3.875	231.8
Run Seq	Collapse Load (psi)	Collapse Strength (psi)	Collapse Design Factor	Burst Load (psi)	Burst Strength (psi)	Burst Design Factor	Tension Load (Kips)	Tension Strength (Kips)	Tension Design Factor
1	4935	7220	1.46	4935	9720	1.97	100	245	2.45

Prepared Dominic Spencer
by: Bill Barrett

Phone: (303) 312-8143
FAX: (303) 312-8195

Date: 7-Apr-08
Denver, Colorado

Remarks:

Collapse is based on a vertical depth of 10000 ft, a mud weight of 9.5 ppg. The casing is considered to be evacuated for collapse purposes. Collapse strength is based on the Westcott, Dunlop & Kemler method of biaxial correction for tension.

Burst strength is not adjusted for tension.



Bill Barrett Corporation

NINE MILE CEMENT VOLUMES

Well Name: Peter's Point Unit Federal 10-26D-12-16

Surface Hole Data:

Total Depth:	1,000'
Top of Cement:	0'
OD of Hole:	12.250"
OD of Casing:	9.625"

Calculated Data:

Lead Volume:	219.2	ft ³
Lead Fill:	700'	
Tail Volume:	94.0	ft ³
Tail Fill:	300'	

Cement Data:

Lead Yield:	1.85	ft ³ /sk
Tail Yield:	1.16	ft ³ /sk
% Excess:	100%	

Calculated # of Sacks:

# SK's Lead:	119
# SK's Tail:	81

Production Hole Data:

Total Depth:	8,400'
Top of Cement:	900'
OD of Hole:	8.750"
OD of Casing:	4.500"

Calculated Data:

Lead Volume:	2303.5	ft ³
Lead Fill:	7,500'	

Cement Data:

Lead Yield:	1.49	ft ³ /sk
% Excess:	30%	

Calculated # of Sacks:

# SK's Lead:	1546
--------------	------

Peter's Point Unit Federal 10-26D-12-16 Proposed Cementing Program

<u>Job Recommendation</u>	<u>Surface Casing</u>
Lead Cement - (700' - 0')	
Halliburton Light Premium	Fluid Weight: 12.7 lbm/gal
2.0% Calcium Chloride	Slurry Yield: 1.85 ft ³ /sk
0.125 lbm/sk Ploy-E-Flake	Total Mixing Fluid: 9.9 Gal/sk
	Top of Fluid: 0'
	Calculated Fill: 700'
	Volume: 78.09 bbl
	Proposed Sacks: 240 sks
Tail Cement - (1000' - 700')	
Premium Cement	Fluid Weight: 15.8 lbm/gal
94 lbm/sk Premium Cement	Slurry Yield: 1.16 ft ³ /sk
2.0% Calcium Chloride	Total Mixing Fluid: 4.97 Gal/sk
0.125 lbm/sk Ploy-E-Flake	Top of Fluid: 700'
	Calculated Fill: 300'
	Volume: 33.47 bbl
	Proposed Sacks: 170 sks

<u>Job Recommendation</u>	<u>Production Casing</u>
Lead Cement - (8400' - 900')	
50/50 Poz Premium	Fluid Weight: 13.4 lbm/gal
3.0 % KCL	Slurry Yield: 1.49 ft ³ /sk
0.75% Halad®-322	Total Mixing Fluid: 7.06 Gal/sk
3.0 lbm/sk Silicalite Compacted	Top of Fluid: 900'
0.2% FWCA	Calculated Fill: 7,500'
0.125 lbm/sk Poly-E-Flake	Volume: 533.31 bbl
1.0 lbm/sk Granulite TR 1/4	Proposed Sacks: 2010 sks



Bill Barrett Corporation

NINE MILE CEMENT VOLUMES

Well Name: Peter's Point Unit Federal 10-26D-12-16

Surface Hole Data:

Total Depth:	1,000'
Top of Cement:	0'
OD of Hole:	12.250"
OD of Casing:	9.625"

Calculated Data:

Lead Volume:	219.2	ft ³
Lead Fill:	700'	
Tail Volume:	94.0	ft ³
Tail Fill:	300'	

Cement Data:

Lead Yield:	1.85	ft ³ /sk
Tail Yield:	1.16	ft ³ /sk
% Excess:	100%	

Calculated # of Sacks:

# SK's Lead:	
# SK's Tail:	

Production Hole Data:

Total Depth:	8,400'
Top of Cement:	900'
OD of Hole:	8.750"
OD of Casing:	5.500"

Calculated Data:

Lead Volume:	1894.4	ft ³
Lead Fill:	7,500'	

Cement Data:

Lead Yield:	1.49	ft ³ /sk
% Excess:	30%	

Calculated # of Sacks:

# SK's Lead:	
--------------	--

Peter's Point Unit Federal 10-26D-12-16 Proposed Cementing Program

<u>Job Recommendation</u>	<u>Surface Casing</u>
Lead Cement - (700' - 0')	
Halliburton Light Premium	Fluid Weight: 12.7 lbm/gal
2.0% Calcium Chloride	Slurry Yield: 1.85 ft ³ /sk
0.125 lbm/sk Ploy-E-Flake	Total Mixing Fluid: 9.9 Gal/sk
	Top of Fluid: 0'
	Calculated Fill: 700'
	Volume: 78.09 bbl
	Proposed Sacks: 240 sks
Tail Cement - (1000' - 700')	
Premium Cement	Fluid Weight: 15.8 lbm/gal
94 lbm/sk Premium Cement	Slurry Yield: 1.16 ft ³ /sk
2.0% Calcium Chloride	Total Mixing Fluid: 4.97 Gal/sk
0.125 lbm/sk Ploy-E-Flake	Top of Fluid: 700'
	Calculated Fill: 300'
	Volume: 33.47 bbl
	Proposed Sacks: 170 sks

<u>Job Recommendation</u>	<u>Production Casing</u>
Lead Cement - (8400' - 900')	
50/50 Poz Premium	Fluid Weight: 13.4 lbm/gal
3.0 % KCL	Slurry Yield: 1.49 ft ³ /sk
0.75% Halad®-322	Total Mixing Fluid: 7.06 Gal/sk
3.0 lbm/sk Silicalite Compacted	Top of Fluid: 900'
0.2% FWCA	Calculated Fill: 7,500'
0.125 lbm/sk Poly-E-Flake	Volume: 438.61 bbl
1.0 lbm/sk Granulite TR 1/4	Proposed Sacks: 1660 sks



Bill Barrett Corporation

BILL BARRETT CORP

CARBON COUNTY, UT (NAD 27)

SECTION 26 T12S R16E

PETERS POINT UF 10-26D-12-16

PT PT 10-26-12-16

Plan: Design #1

Standard Planning Report

04 April, 2008



Database: Compass
 Company: BILL BARRETT CORP
 Project: CARBON COUNTY, UT (NAD 27)
 Site: SECTION 26 T12S R16E
 Well: PETERS POINT UF 10-26D-12-16
 Wellbore: PT PT 10-26-12-16
 Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
 TVD Reference: WELL @ 7177.00ft (Original Well Elev)
 MD Reference: WELL @ 7177.00ft (Original Well Elev)
 North Reference: True
 Survey Calculation Method: Minimum Curvature

Project	CARBON COUNTY, UT (NAD 27)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	Utah Central 4302		Using geodetic scale factor

Site	SECTION 26 T12S R16E, SECTION 26		
Site Position:		Northing:	514,769.114 ft
From:	Lat/Long	Easting:	2,395,129.253 ft
Position Uncertainty:	0.00 ft	Slot Radius:	"
		Latitude:	39° 44' 17.290 N
		Longitude:	110° 5' 41.4100 W
		Grid Convergence:	0.90 °

Well	PETERS POINT UF 10-26D-12-16					
Well Position	+N/-S	61.70 ft	Northing:	514,830.547 ft	Latitude:	39° 44' 17.900 N
	+E/-W	-16.41 ft	Easting:	2,395,111.882 ft	Longitude:	110° 5' 41.6200 W
Position Uncertainty	0.00 ft	Wellhead Elevation:	ft	Ground Level:	7,162.00 ft	

Wellbore	PT PT 10-26-12-16				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	BGGM2007	2/25/2008	11.72	65.62	52,460

Design	Design #1				
Audit Notes:					
Version:	Phase:	PLAN	Tie On Depth:	0.00	
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)	
	0.00	0.00	0.00	46.64	

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
250.00	0.00	0.00	250.00	0.00	0.00	0.00	0.00	0.00	0.00	
650.00	8.00	46.64	648.70	19.14	20.27	2.00	2.00	0.00	46.64	
1,065.34	8.00	46.64	1,060.00	58.83	62.30	0.00	0.00	0.00	0.00	
2,042.12	32.42	46.64	1,969.72	288.77	305.77	2.50	2.50	0.00	0.00	
5,259.09	32.42	46.64	4,685.32	1,472.94	1,559.64	0.00	0.00	0.00	0.00	
6,555.87	0.00	0.00	5,914.00	1,718.19	1,819.33	2.50	-2.50	0.00	180.00	
8,182.87	0.00	0.00	7,541.00	1,718.19	1,819.33	0.00	0.00	0.00	0.00	PBHL_PT PT 10-26-1



BILL BARRETT CORPORATION

Planning Report

Database:	Compass	Local Co-ordinate Reference:	Well PETERS POINT UF 10-26D-12-16
Company:	BILL BARRETT CORP	TVD Reference:	WELL @ 7177.00ft (Original Well Elev)
Project:	CARBON COUNTY, UT (NAD 27)	MD Reference:	WELL @ 7177.00ft (Original Well Elev)
Site:	SECTION 26 T12S R16E	North Reference:	True
Well:	PETERS POINT UF 10-26D-12-16	Survey Calculation Method:	Minimum Curvature
Wellbore:	PT PT 10-26-12-16		
Design:	Design #1		

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
250.00	0.00	0.00	250.00	0.00	0.00	0.00	0.00	0.00	0.00	
Start Build 2.00										
300.00	1.00	46.64	300.00	0.30	0.32	0.44	2.00	2.00	0.00	
400.00	3.00	46.64	399.93	2.70	2.85	3.93	2.00	2.00	0.00	
500.00	5.00	46.64	499.68	7.48	7.93	10.90	2.00	2.00	0.00	
600.00	7.00	46.64	599.13	14.66	15.53	21.35	2.00	2.00	0.00	
650.00	8.00	46.64	648.70	19.14	20.27	27.88	2.00	2.00	0.00	
Start 415.34 hold at 650.00 MD										
700.00	8.00	46.64	698.21	23.92	25.33	34.84	0.00	0.00	0.00	
800.00	8.00	46.64	797.24	33.47	35.45	48.76	0.00	0.00	0.00	
900.00	8.00	46.64	896.27	43.03	45.57	62.67	0.00	0.00	0.00	
1,000.00	8.00	46.64	995.30	52.59	55.69	76.59	0.00	0.00	0.00	
1,004.75	8.00	46.64	1,000.00	53.04	56.17	77.25	0.00	0.00	0.00	
9 5/8"										
1,065.34	8.00	46.64	1,060.00	58.83	62.30	85.68	0.00	0.00	0.00	
Start DLS 2.50 TFO 0.00										
1,100.00	8.87	46.64	1,094.28	62.32	65.99	90.77	2.50	2.50	0.00	
1,200.00	11.37	46.64	1,192.72	74.38	78.76	108.33	2.50	2.50	0.00	
1,300.00	13.87	46.64	1,290.30	89.37	94.64	130.17	2.50	2.50	0.00	
1,400.00	16.37	46.64	1,386.83	107.28	113.60	156.25	2.50	2.50	0.00	
1,500.00	18.87	46.64	1,482.13	128.06	135.60	186.51	2.50	2.50	0.00	
1,600.00	21.37	46.64	1,576.03	151.67	160.60	220.90	2.50	2.50	0.00	
1,700.00	23.87	46.64	1,668.33	178.07	188.56	259.35	2.50	2.50	0.00	
1,800.00	26.37	46.64	1,758.87	207.21	219.42	301.80	2.50	2.50	0.00	
1,900.00	28.87	46.64	1,847.47	239.04	253.12	348.15	2.50	2.50	0.00	
2,000.00	31.37	46.64	1,933.96	273.49	289.59	398.32	2.50	2.50	0.00	
2,042.12	32.42	46.64	1,969.72	288.77	305.77	420.57	2.50	2.50	0.00	
Start 3216.97 hold at 2042.12 MD										
2,100.00	32.42	46.64	2,018.58	310.07	328.33	451.60	0.00	0.00	0.00	
2,200.00	32.42	46.64	2,103.00	346.88	367.31	505.21	0.00	0.00	0.00	
2,300.00	32.42	46.64	2,187.41	383.69	406.28	558.82	0.00	0.00	0.00	
2,400.00	32.42	46.64	2,271.82	420.50	445.26	612.44	0.00	0.00	0.00	
2,500.00	32.42	46.64	2,356.24	457.31	484.24	666.05	0.00	0.00	0.00	
2,600.00	32.42	46.64	2,440.65	494.12	523.21	719.66	0.00	0.00	0.00	
2,700.00	32.42	46.64	2,525.07	530.93	562.19	773.27	0.00	0.00	0.00	
2,800.00	32.42	46.64	2,609.48	567.74	601.17	826.88	0.00	0.00	0.00	
2,900.00	32.42	46.64	2,693.90	604.55	640.14	880.49	0.00	0.00	0.00	
3,000.00	32.42	46.64	2,778.31	641.36	679.12	934.10	0.00	0.00	0.00	
3,100.00	32.42	46.64	2,862.73	678.17	718.10	987.72	0.00	0.00	0.00	
3,200.00	32.42	46.64	2,947.14	714.98	757.07	1,041.33	0.00	0.00	0.00	
3,300.00	32.42	46.64	3,031.56	751.79	796.05	1,094.94	0.00	0.00	0.00	
3,400.00	32.42	46.64	3,115.97	788.60	835.03	1,148.55	0.00	0.00	0.00	
3,500.00	32.42	46.64	3,200.38	825.41	874.00	1,202.16	0.00	0.00	0.00	
3,600.00	32.42	46.64	3,284.80	862.23	912.98	1,255.77	0.00	0.00	0.00	
3,603.79	32.42	46.64	3,288.00	863.62	914.46	1,257.81	0.00	0.00	0.00	
WASATCH										
3,700.00	32.42	46.64	3,369.21	899.04	951.96	1,309.38	0.00	0.00	0.00	
3,800.00	32.42	46.64	3,453.63	935.85	990.93	1,363.00	0.00	0.00	0.00	
3,900.00	32.42	46.64	3,538.04	972.66	1,029.91	1,416.61	0.00	0.00	0.00	
4,000.00	32.42	46.64	3,622.46	1,009.47	1,068.89	1,470.22	0.00	0.00	0.00	
4,100.00	32.42	46.64	3,706.87	1,046.28	1,107.86	1,523.83	0.00	0.00	0.00	
4,200.00	32.42	46.64	3,791.29	1,083.09	1,146.84	1,577.44	0.00	0.00	0.00	
4,300.00	32.42	46.64	3,875.70	1,119.90	1,185.82	1,631.05	0.00	0.00	0.00	



Database: Compass
 Company: BILL BARRETT CORP
 Project: CARBON COUNTY, UT (NAD 27)
 Site: SECTION 26 T12S R16E
 Well: PETERS POINT UF 10-26D-12-16
 Wellbore: PT PT 10-26-12-16
 Design: Design #1

Local Co-ordinate Reference:
 TVD Reference:
 MD Reference:
 North Reference:
 Survey Calculation Method:

Well PETERS POINT UF 10-26D-12-16
 WELL @ 7177.00ft (Original Well Elev)
 WELL @ 7177.00ft (Original Well Elev)
 True
 Minimum Curvature

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
4,400.00	32.42	46.64	3,960.12	1,156.71	1,224.79	1,684.66	0.00	0.00	0.00
4,500.00	32.42	46.64	4,044.53	1,193.52	1,263.77	1,738.27	0.00	0.00	0.00
4,600.00	32.42	46.64	4,128.95	1,230.33	1,302.75	1,791.89	0.00	0.00	0.00
4,700.00	32.42	46.64	4,213.36	1,267.14	1,341.72	1,845.50	0.00	0.00	0.00
4,800.00	32.42	46.64	4,297.77	1,303.95	1,380.70	1,899.11	0.00	0.00	0.00
4,900.00	32.42	46.64	4,382.19	1,340.76	1,419.68	1,952.72	0.00	0.00	0.00
5,000.00	32.42	46.64	4,466.60	1,377.57	1,458.65	2,006.33	0.00	0.00	0.00
5,100.00	32.42	46.64	4,551.02	1,414.38	1,497.63	2,059.94	0.00	0.00	0.00
5,200.00	32.42	46.64	4,635.43	1,451.19	1,536.61	2,113.55	0.00	0.00	0.00
5,259.09	32.42	46.64	4,685.32	1,472.94	1,559.64	2,145.23	0.00	0.00	0.00
Start Drop -2.50									
5,300.00	31.40	46.64	4,720.04	1,487.79	1,575.36	2,166.86	2.50	-2.50	0.00
5,400.00	28.90	46.64	4,806.51	1,522.27	1,611.87	2,217.07	2.50	-2.50	0.00
5,500.00	26.40	46.64	4,895.08	1,554.13	1,645.60	2,263.47	2.50	-2.50	0.00
5,600.00	23.90	46.64	4,985.60	1,583.30	1,676.49	2,305.96	2.50	-2.50	0.00
5,700.00	21.40	46.64	5,077.88	1,609.74	1,704.48	2,344.46	2.50	-2.50	0.00
5,738.67	20.43	46.64	5,114.00	1,619.21	1,714.52	2,358.27	2.50	-2.50	0.00
NORTH HORN									
5,800.00	18.90	46.64	5,171.75	1,633.38	1,729.52	2,378.90	2.50	-2.50	0.00
5,900.00	16.40	46.64	5,267.04	1,654.20	1,751.56	2,409.22	2.50	-2.50	0.00
6,000.00	13.90	46.64	5,363.56	1,672.14	1,770.56	2,435.34	2.50	-2.50	0.00
6,100.00	11.40	46.64	5,461.13	1,687.17	1,786.47	2,457.24	2.50	-2.50	0.00
6,200.00	8.90	46.64	5,559.55	1,699.26	1,799.28	2,474.85	2.50	-2.50	0.00
6,300.00	6.40	46.64	5,658.66	1,708.40	1,808.95	2,488.16	2.50	-2.50	0.00
6,400.00	3.90	46.64	5,758.25	1,714.56	1,815.47	2,497.13	2.50	-2.50	0.00
6,500.00	1.40	46.64	5,858.13	1,717.73	1,818.83	2,501.75	2.50	-2.50	0.00
6,555.87	0.00	0.00	5,914.00	1,718.19	1,819.33	2,502.43	2.50	-2.50	-83.47
Start 1627.00 hold at 6555.87 MD									
6,600.00	0.00	0.00	5,958.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
6,700.00	0.00	0.00	6,058.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
6,800.00	0.00	0.00	6,158.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
6,900.00	0.00	0.00	6,258.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,000.00	0.00	0.00	6,358.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,100.00	0.00	0.00	6,458.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,200.00	0.00	0.00	6,558.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,299.87	0.00	0.00	6,658.00	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
DARK CANYON									
7,300.00	0.00	0.00	6,658.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,400.00	0.00	0.00	6,758.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,500.00	0.00	0.00	6,858.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,573.87	0.00	0.00	6,932.00	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
PRICE RIVER									
7,600.00	0.00	0.00	6,958.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,700.00	0.00	0.00	7,058.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,800.00	0.00	0.00	7,158.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,900.00	0.00	0.00	7,258.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
7,956.87	0.00	0.00	7,315.00	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
PRICE RIVER 6840' SAND									
7,982.87	0.00	0.00	7,341.00	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
PRICE RIVER 6840' BASE									
8,000.00	0.00	0.00	7,358.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
8,100.00	0.00	0.00	7,458.13	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00
8,182.87	0.00	0.00	7,541.00	1,718.19	1,819.33	2,502.43	0.00	0.00	0.00



Database: Compass
 Company: BILL BARRETT CORP
 Project: CARBON COUNTY, UT (NAD 27)
 Site: SECTION 26 T12S R16E
 Well: PETERS POINT UF 10-26D-12-16
 Wellbore: PT PT 10-26-12-16
 Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
 TVD Reference: WELL @ 7177.00ft (Original Well Elev)
 MD Reference: WELL @ 7177.00ft (Original Well Elev)
 North Reference: True
 Survey Calculation Method: Minimum Curvature

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
---------------------	-----------------	-------------	---------------------	------------	------------	-----------------------	-----------------------	----------------------	---------------------

TD at 8182.87

Formations


Measured Depth (ft)	Vertical Depth (ft)	Name	Lithology	Dip (°)	Dip Direction (°)
3,603.79	3,288.00	WASATCH		0.00	
5,738.67	5,114.00	NORTH HORN		0.00	
7,299.87	6,658.00	DARK CANYON		0.00	
7,573.87	6,932.00	PRICE RIVER		0.00	
7,956.87	7,315.00	PRICE RIVER 6840' SAND		0.00	
7,982.87	7,341.00	PRICE RIVER 6840' BASE		0.00	

Plan Annotations

Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates		Comment
		+N/-S (ft)	+E/-W (ft)	
250.00	250.00	0.00	0.00	Start Build 2.00
650.00	648.70	19.14	20.27	Start 415.34 hold at 650.00 MD
1,065.34	1,060.00	58.83	62.30	Start DLS 2.50 TFO 0.00
2,042.12	1,969.72	288.77	305.77	Start 3216.97 hold at 2042.12 MD
5,259.09	4,685.32	1,472.94	1,559.64	Start Drop -2.50
6,555.87	5,914.00	1,718.19	1,819.33	Start 1627.00 hold at 6555.87 MD
8,182.87	7,541.00	1,718.19	1,819.33	TD at 8182.87





PETERS POINT UF 10-26D-12-16
 270' FSL, 1510' FWL
 SECTION 26 T12S R16E
 CARBON COUNTY, UT
 Latitude: 39° 44' 17.900 N
 Longitude: 110° 5' 41.6200 W



Azimuths to True North
 Magnetic North: 11.72°
 Magnetic Field
 Strength: 52460.5enT
 Dip Angle: 65.62°
 Date: 2/25/2008
 Model: BGGM2007

SECTION DETAILS										
Sec	MD	Inc	Azi	TVD	+N-S	+E-W	DLeg	TFace	VSec	Target
1	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
2	250.00	0.00	0.00	250.00	0.00	0.00	0.00	0.00	0.00	
3	650.00	8.00	46.64	648.70	19.14	20.27	2.00	46.64	27.88	
4	1065.34	8.00	46.64	1060.00	58.83	62.30	0.00	0.00	65.69	
5	2042.12	32.42	46.64	1999.72	288.77	305.77	2.50	0.00	420.57	
6	5259.09	32.42	46.64	4885.32	1472.94	1659.64	0.00	0.00	2145.23	
7	6555.87	0.00	0.00	5914.00	1718.19	1819.33	2.50	180.00	2502.43	
8	8182.87	0.00	0.00	7541.00	1718.19	1819.33	0.00	0.00	2502.43	PBHL_PT PT 10-26-12-16

WELLBORE TARGET DETAILS (MAP CO-ORDINATES AND LAT/LONG)									
Name	TVD	+N-S	+E-W	Northing	Easting	Latitude	Longitude	Shape	
PBHL	7541.00	1718.19	1819.33	516576.932	2396903.811	39° 44' 34.880 N	110° 5' 18.3300 W	Circle (Radius: 100.00)	

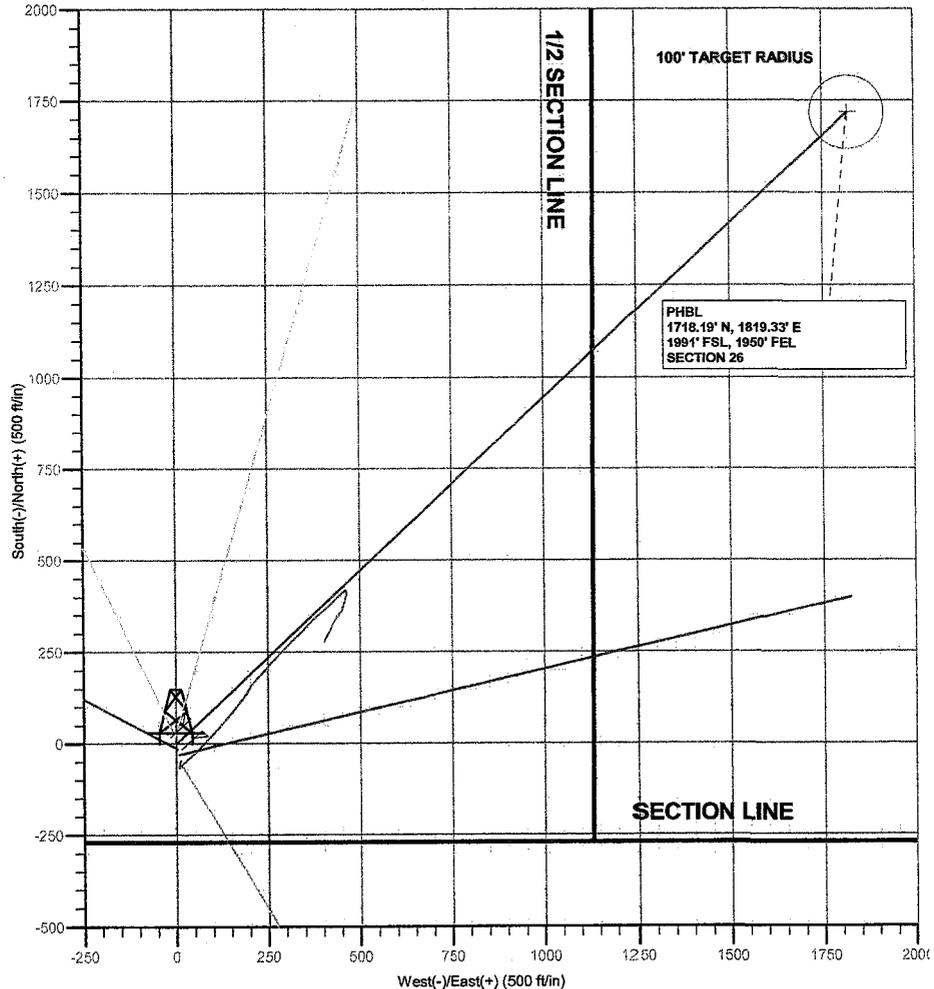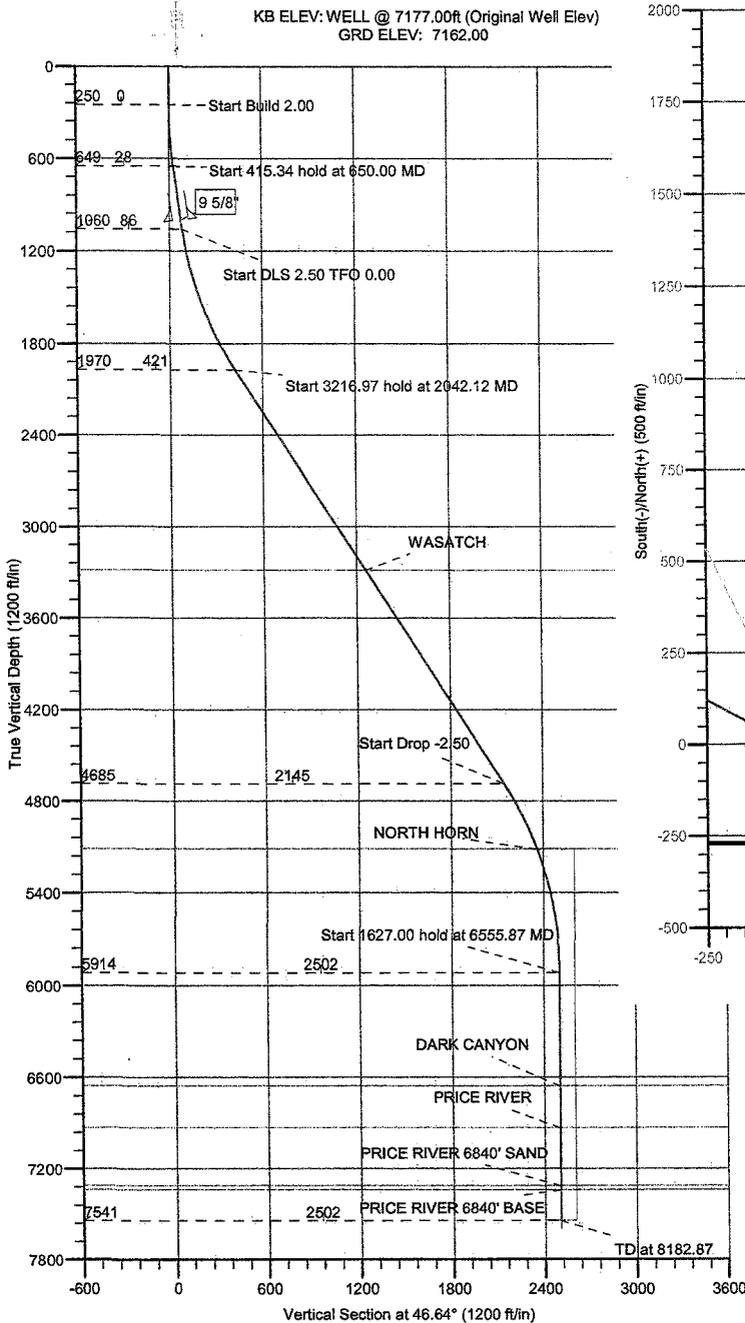

FORMATION TOP DETAILS		
TVDPath	MDPath	Formation
3288.00	3603.79	WASATCH
5114.00	5738.67	NORTH HORN
6658.00	7299.87	DARK CANYON
6932.00	7573.87	PRICE RIVER
7315.00	7956.87	PRICE RIVER 6840' SAND
7341.00	7982.87	PRICE RIVER 6840' BASE



Bill Barrett Corporation

BILL BARRETT CORP

CARBON COUNTY, UT (NAD 27)

SECTION 26 T12S R16E

PETERS POINT UF 10-26D-12-16

PT PT 10-26-12-16

Design #1

Anticollision Report

04 April, 2008



Company: BILL BARRETT CORP
 Project: CARBON COUNTY, UT (NAD 27)
 Reference Site: SECTION 26 T12S R16E
 Site Error: 0.00ft
 Reference Well: PETERS POINT UF 10-26D-12-16
 Well Error: 0.00ft
 Reference Wellbore: PT PT 10-26-12-16
 Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
 TVD Reference: WELL @ 7177.00ft (Original Well Elev)
 MD Reference: WELL @ 7177.00ft (Original Well Elev)
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Output errors are at: 2.00 sigma
 Database: Compass
 Offset TVD Reference: Offset Datum

Reference	Design #1		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	MD + Stations Interval 100.00ft	Error Model:	ISCWSA
Depth Range:	0.00 to 20,000.00ft	Scan Method:	Closest Approach 3D
Results Limited by:	Maximum center-center distance of 10,000.00ft	Error Surface:	Elliptical Conic
Warning Levels Evaluated at:	2.00 Sigma		

Survey Tool Program	Date	4/4/2008		
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description
0.00	8,182.87	Design #1 (PT PT 10-26-12-16)	MWD	MWD - Standard

Site Name	Reference	Offset	Distance		Separation Factor	Warning
	Measured Depth (ft)	Measured Depth (ft)	Between Centres (ft)	Between Ellipses (ft)		
SECTION 26 T12S R16E						
PETERS POINT UF #14-26D-12-16 - PT PT UF 14-26D-	0.00	0.00	47.02			
PETERS POINT UF #14-26D-12-16 - PT PT UF 14-26D-	100.00	99.88	47.15	46.94	223.511	ES
PETERS POINT UF #14-26D-12-16 - PT PT UF 14-26D-	650.00	647.37	71.47	69.36	33.873	SF
PETERS POINT UF #3-35D-12-16 - PT PT UF #3-35D-1	250.00	250.00	63.85	62.99	73.788	CC, ES
PETERS POINT UF #3-35D-12-16 - PT PT UF #3-35D-1	1,100.00	1,083.24	178.66	173.68	35.918	SF
PETERS POINT UF 11-26D-12-16 - PT PT 11-26-12-16	250.00	250.00	15.67	14.81	18.111	CC
PETERS POINT UF 11-26D-12-16 - PT PT 11-26-12-16	300.00	299.76	15.84	14.75	14.559	ES
PETERS POINT UF 11-26D-12-16 - PT PT 11-26-12-16	700.00	698.26	28.23	25.28	9.562	SF
PETERS POINT UF 12-26D-12-16 - PT PT 12-26-12-16	250.00	250.00	32.33	31.46	37.360	CC
PETERS POINT UF 12-26D-12-16 - PT PT 12-26-12-16	300.00	299.45	32.54	31.45	29.943	ES
PETERS POINT UF 12-26D-12-16 - PT PT 12-26-12-16	650.00	645.48	51.04	48.30	18.593	SF
PETERS POINT UF 13-26D-12-16 - PT PT 13-26-12-16	250.00	250.00	15.67	14.81	18.111	CC
PETERS POINT UF 13-26D-12-16 - PT PT 13-26-12-16	300.00	300.00	15.89	14.80	14.594	ES
PETERS POINT UF 13-26D-12-16 - PT PT 13-26-12-16	500.00	499.68	23.02	21.02	11.535	SF
PETERS POINT UF 15-26D-12-16 - PT PT 15-26-12-16	250.00	250.00	31.55	30.69	36.462	CC, ES
PETERS POINT UF 15-26D-12-16 - PT PT 15-26-12-16	1,065.34	1,063.59	75.53	70.83	16.091	SF

Offset Design SECTION 26 T12S R16E - PETERS POINT UF #14-26D-12-16 - PT PT UF 14-26D-12-16 - PT PT UF 1													Offset Site Error:	0.00 ft
Survey Program: 1098-MWD													Offset Well Error:	0.00 ft
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		Minimum Separation (ft)	Separation Factor	Warning	
				Reference (ft)	Offset (ft)		+N-S (ft)	+E-W (ft)	Between Centres (ft)	Between Ellipses (ft)				
0.00	0.00	0.00	0.00	0.00	0.00	165.57	-45.54	11.72	47.02					
100.00	100.00	99.88	99.88	0.10	0.11	165.66	-45.68	11.68	47.15	46.94	0.21	223.511	ES	
200.00	200.00	199.75	199.75	0.32	0.23	165.92	-46.11	11.57	47.54	46.99	0.55	86.265		
250.00	250.00	249.69	249.69	0.43	0.29	166.11	-46.44	11.48	47.84	47.12	0.72	66.331		
300.00	300.00	299.62	299.61	0.54	0.35	120.14	-46.84	11.38	48.42	47.54	0.88	54.980		
400.00	399.93	399.38	399.37	0.77	0.46	124.01	-47.84	11.12	51.21	50.00	1.22	42.111		
500.00	499.68	498.89	498.88	1.01	0.58	130.31	-49.14	10.78	56.70	55.14	1.66	36.270		
600.00	599.13	598.01	597.98	1.26	0.69	137.57	-50.71	10.38	65.58	63.66	1.92	34.077		
650.00	648.70	647.37	647.33	1.41	0.75	141.14	-51.60	10.15	71.47	69.36	2.11	33.873	SF	
700.00	698.21	696.64	696.59	1.56	0.81	144.41	-52.56	9.90	78.03	75.74	2.29	34.020		
800.00	797.24	795.13	795.06	1.87	0.92	149.51	-54.68	9.35	91.96	89.31	2.66	34.585		
900.00	896.27	893.54	893.43	2.19	1.04	153.25	-57.08	8.72	106.72	103.69	3.02	35.312		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



BILL BARRETT CORPORATION

Anticollision Report

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at: 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF #14-26D-12-16 - PT PT UF 14-26D-12-16 - PT PT UF 1													Offset Site Error:	0.00 ft
Survey Program: 1098-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi-Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Tooface (°)	Offset Wellbore Centre +N/-S (ft)	+E/W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
1,000.00	995.30	991.86	991.72	2.51	1.15	156.04	-59.76	8.03	122.09	118.71	3.38	36.084		
1,065.34	1,060.00	1,056.06	1,055.88	2.73	1.22	157.51	-61.67	7.53	132.42	128.80	3.62	36.586		
1,100.00	1,094.28	1,090.05	1,089.96	2.84	1.26	158.18	-62.72	7.26	138.22	134.47	3.75	36.847		
1,200.00	1,192.72	1,190.85	1,190.63	3.22	1.46	160.19	-65.20	6.91	156.99	152.80	4.20	37.400		
1,300.00	1,290.30	1,295.10	1,294.86	3.64	1.64	162.26	-65.12	8.04	177.17	173.27	3.89	45.499		
1,400.00	1,386.83	1,400.70	1,400.33	4.13	1.83	164.16	-61.58	11.70	197.68	193.61	4.07	48.548		
1,500.00	1,482.13	1,508.57	1,507.69	4.69	2.04	165.77	-54.23	18.99	217.89	213.74	4.15	52.496		
1,600.00	1,576.03	1,616.43	1,614.45	5.32	2.27	167.03	-43.59	30.07	237.99	233.93	4.06	58.555		
1,700.00	1,668.33	1,725.94	1,721.95	6.03	2.57	168.00	-29.48	45.32	257.82	254.16	3.66	70.471		
1,800.00	1,758.87	1,837.66	1,830.49	6.81	2.96	168.91	-11.20	64.41	277.24	270.40	6.83	40.572		
1,900.00	1,847.47	1,949.83	1,937.99	7.67	3.44	169.99	12.06	86.38	295.83	288.66	7.17	41.279		
2,000.00	1,933.96	2,054.96	2,037.59	8.62	3.98	171.03	36.89	109.09	315.12	307.70	7.42	42.489		
2,042.12	1,969.72	2,099.47	2,079.53	9.04	4.23	171.50	48.02	118.98	323.89	316.40	7.50	43.202		
2,100.00	2,018.58	2,160.52	2,136.80	9.63	4.58	172.19	63.97	132.67	335.78	328.15	7.63	44.010		
2,200.00	2,103.00	2,258.16	2,228.17	10.66	5.15	173.31	90.41	154.87	355.78	347.97	7.81	45.546		
2,300.00	2,187.41	2,353.09	2,317.16	11.70	5.66	174.37	116.16	175.61	376.32	368.43	7.89	47.669		
2,400.00	2,271.82	2,448.89	2,407.04	12.75	6.20	175.78	143.78	193.89	397.55	389.23	8.32	47.791		
2,500.00	2,356.24	2,545.29	2,497.67	13.80	6.75	176.85	170.34	213.13	419.35	408.11	11.24	37.318		
2,600.00	2,440.65	2,646.94	2,593.16	14.86	7.37	177.41	196.35	236.30	440.73	428.79	11.94	36.914		
2,700.00	2,525.07	2,740.78	2,681.34	15.92	7.94	177.84	220.12	257.90	462.19	449.56	12.63	36.604		
2,800.00	2,609.48	2,834.20	2,769.38	16.98	8.47	178.15	242.84	279.31	484.48	471.16	13.32	36.386		
2,900.00	2,693.90	2,926.00	2,856.21	18.05	9.00	178.38	264.24	300.07	507.75	493.74	14.00	36.264		
3,000.00	2,778.31	3,013.44	2,939.31	19.11	9.49	178.56	283.58	319.18	532.43	517.76	14.67	36.282		
3,100.00	2,862.73	3,097.20	3,019.43	20.18	9.93	178.70	300.89	336.42	559.09	543.75	15.34	36.458		
3,200.00	2,947.14	3,180.96	3,100.07	21.25	10.36	178.83	316.98	352.30	587.91	571.92	15.99	36.766		
3,300.00	3,031.56	3,262.36	3,178.89	22.32	10.75	178.96	331.54	366.49	618.74	602.11	16.63	37.196		
3,400.00	3,115.97	3,340.21	3,254.73	23.40	11.10	179.05	343.94	378.99	651.88	634.62	17.26	37.760		
3,500.00	3,200.38	3,415.32	3,328.33	24.47	11.40	179.05	353.92	390.15	687.60	669.72	17.88	38.453		
3,600.00	3,284.80	3,492.93	3,404.72	25.54	11.69	179.03	362.74	400.59	725.54	707.05	18.50	39.225		
3,700.00	3,369.21	3,574.42	3,485.18	26.62	11.97	179.03	371.20	410.31	765.14	746.03	19.11	40.032		
3,800.00	3,453.63	3,654.35	3,564.27	27.69	12.23	179.06	379.04	418.82	805.97	786.25	19.72	40.869		
3,900.00	3,538.04	3,731.96	3,641.23	28.77	12.47	179.09	385.82	426.27	848.18	827.86	20.32	41.742		
4,000.00	3,622.46	3,808.65	3,717.42	29.84	12.69	179.15	392.04	432.37	891.84	870.93	20.91	42.648		
4,100.00	3,706.87	3,888.00	3,796.36	30.92	12.90	179.22	397.91	437.85	936.64	915.14	21.51	43.553		
4,200.00	3,791.29	3,970.90	3,878.91	31.99	13.10	179.27	403.37	443.24	982.22	960.11	22.10	44.438		
4,300.00	3,875.70	4,048.95	3,956.67	33.07	13.29	179.30	407.83	448.08	1,028.52	1,005.83	22.69	45.331		
4,400.00	3,960.12	4,122.19	4,029.72	34.15	13.45	179.31	411.36	452.04	1,075.88	1,052.62	23.26	46.246		
4,500.00	4,044.53	4,191.75	4,099.17	35.23	13.59	179.33	413.95	455.03	1,124.62	1,100.79	23.83	47.193		
4,600.00	4,128.95	4,259.04	4,166.40	36.30	13.71	179.34	415.65	457.15	1,174.79	1,150.40	24.39	48.170		
4,700.00	4,213.36	4,328.97	4,236.32	37.38	13.82	179.35	416.67	458.58	1,226.28	1,201.33	24.95	49.154		
4,800.00	4,297.77	4,403.91	4,311.25	38.46	13.92	179.36	417.20	459.46	1,278.74	1,253.23	25.51	50.123		
4,900.00	4,382.19	4,485.82	4,393.15	39.54	14.04	179.37	417.58	460.14	1,331.57	1,312.00	19.57	68.050		
5,000.00	4,466.60	4,569.03	4,476.35	40.62	14.15	179.38	417.80	460.82	1,384.53	1,360.37	24.15	57.324		
5,100.00	4,551.02	4,648.31	4,555.63	41.70	14.25	179.38	417.72	461.47	1,437.70	1,414.88	22.82	63.004		
5,200.00	4,635.43	4,729.03	4,636.35	42.77	14.36	179.37	417.33	462.05	1,491.15	1,463.53	27.62	53.978		
5,259.09	4,685.32	4,776.94	4,684.26	43.41	14.42	179.36	417.02	462.34	1,522.84	1,494.70	28.14	54.118		
5,300.00	4,720.04	4,810.45	4,717.76	43.81	14.47	179.37	416.76	462.55	1,544.49	1,516.06	28.44	54.313		
5,400.00	4,806.51	4,891.95	4,799.27	44.63	14.57	179.36	415.92	463.04	1,594.95	1,565.84	29.11	54.799		
5,500.00	4,895.08	4,973.57	4,880.87	45.38	14.67	179.35	414.77	463.40	1,641.93	1,612.22	29.71	55.266		
5,600.00	4,985.60	5,057.17	4,964.46	46.08	14.78	179.33	413.32	463.57	1,685.38	1,655.13	30.25	55.716		
5,700.00	5,077.88	5,142.84	5,050.11	46.71	14.88	179.32	411.57	463.55	1,725.19	1,694.47	30.72	56.152		
5,800.00	5,171.75	5,230.96	5,138.21	47.28	14.98	179.29	409.46	463.43	1,761.28	1,730.15	31.13	56.576		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



BILL BARRETT CORPORATION

Anticollision Report

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF #14-26D-12-16 - PT PT UF 14-26D-12-16 - PT PT UF 1													Offset Site Error:	0.00 ft
Survey Program: 1098-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance				Minimum Separation		Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Tooface (°)	Offset Wellbore Centre +N/S (ft)	+E/W (ft)	Between Centres (ft)	Between Ellipses (ft)	Separation (ft)	Factor		
5,900.00	5,267.04	5,317.17	5,224.38	47.79	15.08	179.26	407.03	463.22	1,793.62	1,762.15	31.46	57.008		
6,000.00	5,363.56	5,403.61	5,310.77	48.22	15.18	179.22	404.11	462.88	1,822.28	1,790.55	31.72	57.447		
6,100.00	5,461.13	5,492.57	5,399.66	48.59	15.27	179.16	400.59	462.42	1,847.20	1,815.29	31.91	57.888		
6,200.00	5,559.55	5,580.09	5,487.10	48.90	15.36	179.11	396.84	461.71	1,868.33	1,836.31	32.02	58.347		
6,300.00	5,658.66	5,673.57	5,580.47	49.14	15.45	179.05	392.45	460.63	1,885.68	1,853.61	32.06	58.810		
6,400.00	5,758.25	5,769.41	5,676.19	49.32	15.54	178.99	387.98	459.39	1,898.82	1,866.78	32.03	59.278		
6,500.00	5,858.13	5,867.36	5,774.03	49.44	15.63	178.92	383.31	457.92	1,907.84	1,875.90	31.93	59.746		
6,555.87	5,914.00	5,922.66	5,829.25	49.48	15.69	-134.48	380.64	457.13	1,910.97	1,879.13	31.85	60.005		
6,600.00	5,958.13	5,963.75	5,870.28	49.50	15.73	-134.51	378.62	456.52	1,912.96	1,880.99	31.98	59.825		
6,700.00	6,058.13	6,054.55	5,960.95	49.55	15.82	-134.58	373.95	455.00	1,917.77	1,885.49	32.28	59.418		
6,800.00	6,158.13	6,161.99	6,068.22	49.61	15.92	-134.65	368.21	452.97	1,922.88	1,890.28	32.61	58.972		
6,900.00	6,258.13	6,278.17	6,184.29	49.67	16.03	-134.71	363.53	450.75	1,927.06	1,894.12	32.94	58.501		
7,000.00	6,358.13	6,374.86	6,280.90	49.72	16.14	-134.74	360.15	448.84	1,930.93	1,897.68	33.25	58.076		
7,100.00	6,458.13	6,461.03	6,366.99	49.78	16.24	-134.76	356.94	446.78	1,935.25	1,901.71	33.55	57.687		
7,200.00	6,558.13	6,546.91	6,452.75	49.84	16.33	-134.79	353.28	444.27	1,940.33	1,906.48	33.85	57.321		
7,300.00	6,658.13	6,637.97	6,543.66	49.90	16.43	-134.81	348.99	441.20	1,946.04	1,911.87	34.16	56.962		
7,400.00	6,758.13	6,724.77	6,630.29	49.96	16.52	-134.84	344.56	438.10	1,952.17	1,917.70	34.47	56.633		
7,500.00	6,858.13	6,808.09	6,713.40	50.03	16.60	-134.87	339.71	434.70	1,959.17	1,924.40	34.77	56.343		
7,600.00	6,958.13	6,895.49	6,800.53	50.09	16.69	-134.91	333.94	430.91	1,966.90	1,931.82	35.08	56.065		
7,700.00	7,058.13	6,987.16	6,891.87	50.15	16.77	-134.97	327.27	426.93	1,975.12	1,939.72	35.40	55.791		
7,800.00	7,158.13	7,083.48	6,987.79	50.22	16.87	-135.05	319.56	422.99	1,983.67	1,947.93	35.73	55.512		
7,900.00	7,258.13	7,183.07	7,086.97	50.29	16.97	-135.13	311.50	418.97	1,992.25	1,956.17	36.08	55.212		
8,000.00	7,358.13	7,282.66	7,186.16	50.35	17.07	-135.21	303.44	414.94	2,000.85	1,964.41	36.43	54.918		
8,100.00	7,458.13	7,382.25	7,285.34	50.42	17.18	-135.29	295.39	410.91	2,009.44	1,972.66	36.78	54.630		
8,182.87	7,541.00	7,464.78	7,367.53	50.48	17.27	-135.36	288.71	407.58	2,016.57	1,979.50	37.07	54.395		

CC - Min centre to center distance or covergent point, SF - min separation factor, ES - min ellipse separation

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF #3-35D-12-16 - PT PT UF #3-35D-12-16 - Design #1													Offset Site Error:	0.00 ft
Survey Program: 0-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
0.00	0.00	0.00	0.00	0.00	0.00	165.11	-61.71	16.41	63.85					
100.00	100.00	100.00	100.00	0.10	0.10	165.11	-61.71	16.41	63.85	63.66	0.19	334.216		
200.00	200.00	200.00	200.00	0.32	0.32	165.11	-61.71	16.41	63.85	63.21	0.64	99.679		
250.00	250.00	250.00	250.00	0.43	0.43	165.11	-61.71	16.41	63.85	62.99	0.87	73.788 CC, ES		
300.00	300.00	298.94	298.94	0.54	0.53	118.69	-62.07	16.62	64.47	63.40	1.08	59.951		
400.00	389.93	396.61	396.55	0.77	0.73	120.32	-64.94	18.32	69.46	67.96	1.50	46.317		
500.00	499.68	493.65	493.36	1.01	0.94	122.94	-70.62	21.68	79.56	77.60	1.96	40.572		
600.00	599.13	592.35	591.68	1.26	1.19	126.22	-78.02	26.06	93.57	91.13	2.45	38.260		
650.00	648.70	641.61	640.75	1.41	1.32	128.07	-81.71	28.24	101.48	98.79	2.69	37.671		
700.00	698.21	690.80	689.76	1.56	1.44	129.94	-85.40	30.43	109.77	106.83	2.94	37.332		
800.00	797.24	789.18	787.77	1.87	1.71	132.94	-92.78	34.80	126.61	123.17	3.44	36.793		
900.00	896.27	887.57	885.77	2.19	1.97	135.23	-100.16	39.16	143.72	139.77	3.95	36.398		
1,000.00	995.30	985.95	983.78	2.51	2.24	137.03	-107.54	43.53	161.00	156.54	4.46	36.101		
1,065.34	1,060.00	1,050.23	1,047.82	2.73	2.42	138.01	-112.36	46.38	172.36	167.56	4.80	35.944		
1,100.00	1,094.28	1,083.24	1,080.70	2.84	2.51	138.40	-114.90	47.89	178.66	173.68	4.97	35.918 SF		
1,200.00	1,192.72	1,175.77	1,172.66	3.22	2.79	139.44	-123.69	53.09	200.73	195.22	5.51	36.429		
1,300.00	1,290.30	1,266.36	1,262.33	3.64	3.09	140.31	-134.78	59.65	228.58	222.50	6.08	37.597		
1,400.00	1,386.83	1,354.64	1,349.27	4.13	3.42	140.97	-147.92	67.43	262.04	255.36	6.68	39.218		
1,500.00	1,482.13	1,440.26	1,433.11	4.69	3.77	141.41	-162.86	76.27	300.92	293.60	7.32	41.129		
1,600.00	1,576.03	1,522.92	1,513.52	5.32	4.14	141.64	-179.32	86.02	345.00	337.01	7.99	43.204		
1,700.00	1,668.33	1,602.38	1,590.27	6.03	4.53	141.69	-197.02	96.49	394.04	385.34	8.69	45.335		
1,800.00	1,758.87	1,685.96	1,670.62	6.81	4.97	141.74	-216.81	108.20	447.15	437.71	9.45	47.319		
1,900.00	1,847.47	1,768.32	1,749.80	7.67	5.41	141.87	-236.31	119.75	503.27	493.05	10.22	49.236		
2,000.00	1,933.96	1,848.43	1,826.82	8.62	5.85	142.00	-255.29	130.98	562.35	551.33	11.02	51.035		
2,042.12	1,969.72	1,881.46	1,858.57	9.04	6.03	142.05	-263.11	135.61	588.11	576.75	11.36	51.763		
2,100.00	2,018.58	1,926.54	1,901.92	9.63	6.27	142.77	-273.79	141.93	623.90	612.04	11.86	52.601		
2,200.00	2,103.00	2,004.44	1,976.81	10.66	6.70	143.85	-292.24	152.85	685.85	673.12	12.73	53.875		
2,300.00	2,187.41	2,082.34	2,051.70	11.70	7.14	144.74	-310.69	163.77	747.93	734.32	13.61	54.964		
2,400.00	2,271.82	2,160.24	2,126.59	12.75	7.57	145.50	-329.14	174.69	810.10	795.61	14.49	55.904		
2,500.00	2,356.24	2,238.14	2,201.48	13.80	8.01	146.15	-347.59	185.61	872.35	856.97	15.38	56.725		
2,600.00	2,440.65	2,316.04	2,276.37	14.86	8.45	146.72	-366.04	196.53	934.66	918.39	16.27	57.445		
2,700.00	2,525.07	2,393.94	2,351.26	15.92	8.89	147.21	-384.49	207.45	997.02	979.86	17.17	58.081		
2,800.00	2,609.48	2,471.84	2,426.15	16.98	9.33	147.65	-402.95	218.37	1,059.42	1,041.36	18.07	58.645		
2,900.00	2,693.90	2,549.74	2,501.04	18.05	9.77	148.04	-421.40	229.29	1,121.86	1,102.89	18.97	59.150		
3,000.00	2,778.31	2,627.64	2,575.94	19.11	10.21	148.39	-439.85	240.21	1,184.32	1,164.45	19.87	59.603		
3,100.00	2,862.73	2,705.54	2,650.83	20.18	10.65	148.70	-458.30	251.13	1,246.81	1,226.03	20.78	60.013		
3,200.00	2,947.14	2,783.44	2,725.72	21.25	11.10	148.99	-476.75	262.05	1,309.31	1,287.63	21.68	60.384		
3,300.00	3,031.56	2,861.34	2,800.61	22.32	11.54	149.24	-495.20	272.97	1,371.84	1,349.25	22.59	60.722		
3,400.00	3,115.97	2,939.24	2,875.50	23.40	11.99	149.48	-513.65	283.89	1,434.38	1,410.88	23.50	61.031		
3,500.00	3,200.38	3,017.14	2,950.39	24.47	12.44	149.70	-532.10	294.81	1,496.93	1,472.52	24.41	61.314		
3,600.00	3,284.80	3,095.04	3,025.28	25.54	12.88	149.89	-550.55	305.73	1,559.50	1,534.17	25.33	61.574		
3,700.00	3,369.21	3,172.94	3,100.17	26.62	13.33	150.08	-569.00	316.65	1,622.08	1,595.83	26.24	61.814		
3,800.00	3,453.63	3,250.84	3,175.06	27.69	13.78	150.25	-587.45	327.57	1,684.66	1,657.51	27.16	62.036		
3,900.00	3,538.04	3,328.74	3,249.96	28.77	14.22	150.41	-605.90	338.49	1,747.26	1,719.18	28.07	62.241		
4,000.00	3,622.46	3,406.64	3,324.85	29.84	14.67	150.55	-624.35	349.41	1,809.86	1,780.87	28.99	62.433		
4,100.00	3,706.87	3,484.54	3,399.74	30.92	15.12	150.69	-642.80	360.33	1,872.47	1,842.56	29.91	62.611		
4,200.00	3,791.29	3,562.44	3,474.63	31.99	15.57	150.82	-661.26	371.25	1,935.08	1,904.26	30.82	62.777		
4,300.00	3,875.70	3,640.34	3,549.52	33.07	16.02	150.94	-679.71	382.17	1,997.70	1,965.96	31.74	62.933		
4,400.00	3,960.12	3,718.24	3,624.41	34.15	16.46	151.05	-698.16	393.09	2,060.33	2,027.66	32.66	63.079		
4,500.00	4,044.53	3,796.14	3,699.30	35.23	16.91	151.16	-716.61	404.01	2,122.96	2,089.37	33.58	63.215		
4,600.00	4,128.95	3,874.03	3,774.19	36.30	17.36	151.26	-735.06	414.93	2,185.59	2,151.09	34.50	63.344		
4,700.00	4,213.36	3,951.93	3,849.08	37.38	17.81	151.35	-753.51	425.85	2,248.23	2,212.80	35.42	63.465		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Company: BILL BARRETT CORP
 Project: CARBON COUNTY, UT (NAD 27)
 Reference Site: SECTION 26 T12S R16E
 Site Error: 0.00ft
 Reference Well: PETERS POINT UF 10-26D-12-16
 Well Error: 0.00ft
 Reference Wellbore: PT PT 10-26-12-16
 Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
 TVD Reference: WELL @ 7177.00ft (Original Well Elev)
 MD Reference: WELL @ 7177.00ft (Original Well Elev)
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Output errors are at: 2.00 sigma
 Database: Compass
 Offset TVD Reference: Offset Datum

SECTION 26 T12S R16E - PETERS POINT UF #3-35D-12-16 - PT PT UF #3-35D-12-16 - Design #1													Offset Site Error:	0.00 ft
Survey Program: 0-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Tooface (°)	Offset Wellbore Centre +N-S (ft)	+E/W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
4,800.00	4,297.77	4,029.83	3,923.98	38.46	18.26	151.44	-771.96	436.77	2,310.87	2,274.52	36.35	63.579		
4,900.00	4,382.19	4,143.62	4,033.71	39.54	18.79	151.59	-797.86	452.10	2,373.04	2,335.73	37.31	63.597		
5,000.00	4,466.60	4,269.19	4,155.77	40.62	19.26	151.84	-823.19	467.09	2,433.75	2,395.52	38.23	63.667		
5,100.00	4,551.02	4,397.93	4,281.86	41.70	19.70	152.18	-845.56	480.33	2,492.92	2,453.83	39.09	63.770		
5,200.00	4,635.43	4,529.67	4,411.71	42.77	20.09	152.60	-864.65	491.63	2,550.52	2,510.62	39.90	63.920		
5,259.09	4,685.32	4,608.85	4,490.09	43.41	20.31	152.88	-874.27	497.32	2,583.80	2,543.45	40.35	64.027		
5,300.00	4,720.04	4,664.53	4,545.34	43.81	20.44	153.39	-880.19	500.83	2,606.24	2,565.52	40.72	64.009		
5,400.00	4,806.51	4,805.07	4,685.20	44.63	20.74	154.55	-892.06	507.85	2,657.54	2,616.02	41.52	64.007		
5,500.00	4,895.08	4,951.41	4,831.26	45.38	20.98	155.61	-899.70	512.38	2,703.62	2,661.37	42.24	64.003		
5,600.00	4,985.60	5,102.80	4,982.60	46.08	21.16	156.60	-902.54	514.05	2,744.20	2,701.33	42.87	64.013		
5,700.00	5,077.88	5,198.08	5,077.88	46.71	21.26	157.30	-902.54	514.05	2,780.05	2,754.73	25.31	109.831		
5,800.00	5,171.75	5,291.95	5,171.75	47.28	21.35	157.89	-902.54	514.05	2,812.16	2,787.12	25.05	112.279		
5,900.00	5,267.04	5,387.24	5,267.04	47.79	21.44	158.39	-902.54	514.05	2,840.48	2,815.79	24.69	115.040		
6,000.00	5,363.56	5,483.76	5,363.56	48.22	21.54	158.81	-902.54	514.05	2,864.92	2,840.68	24.23	118.222		
6,100.00	5,461.13	5,581.32	5,461.13	48.59	21.64	159.15	-902.54	514.05	2,885.42	2,861.76	23.65	121.995		
6,200.00	5,559.55	5,679.75	5,559.55	48.90	21.74	159.42	-902.54	514.05	2,901.93	2,879.01	22.91	126.654		
6,300.00	5,658.66	5,778.85	5,658.66	49.14	21.85	159.63	-902.54	514.05	2,914.40	2,892.46	21.94	132.831		
6,400.00	5,758.25	5,878.44	5,758.25	49.32	21.95	159.76	-902.54	514.05	2,922.82	2,902.32	20.51	142.540		
6,500.00	5,858.13	5,978.33	5,858.13	49.44	22.06	159.83	-902.54	514.05	2,927.16	2,883.60	43.56	67.198		
6,555.87	5,914.00	6,034.20	5,914.00	49.48	22.12	-153.52	-902.54	514.05	2,927.80	2,886.71	41.09	71.257		
6,600.00	5,958.13	6,078.32	5,958.13	49.50	22.17	-153.52	-902.54	514.05	2,927.80	2,886.60	41.20	71.064		
6,700.00	6,058.13	6,178.32	6,058.13	49.55	22.29	-153.52	-902.54	514.05	2,927.80	2,886.33	41.46	70.613		
6,800.00	6,158.13	6,278.32	6,158.13	49.61	22.40	-153.52	-902.54	514.05	2,927.80	2,910.02	17.77	164.723		
6,900.00	6,258.13	6,378.32	6,258.13	49.67	22.52	-153.52	-902.54	514.05	2,927.80	2,908.70	19.10	153.291		
7,000.00	6,358.13	6,478.32	6,358.13	49.72	22.63	-153.52	-902.54	514.05	2,927.80	2,907.70	20.09	145.701		
7,100.00	6,458.13	6,578.32	6,458.13	49.78	22.75	-153.52	-902.54	514.05	2,927.80	2,906.85	20.95	139.755		
7,200.00	6,558.13	6,678.32	6,558.13	49.84	22.87	-153.52	-902.54	514.05	2,927.80	2,906.07	21.72	134.782		
7,300.00	6,658.13	6,778.32	6,658.13	49.90	23.00	-153.52	-902.54	514.05	2,927.80	2,905.35	22.44	130.468		
7,400.00	6,758.13	6,878.32	6,758.13	49.96	23.12	-153.52	-902.54	514.05	2,927.80	2,904.68	23.12	126.639		
7,500.00	6,858.13	6,978.32	6,858.13	50.03	23.24	-153.52	-902.54	514.05	2,927.80	2,904.03	23.77	123.185		
7,600.00	6,958.13	7,078.32	6,958.13	50.09	23.37	-153.52	-902.54	514.05	2,927.80	2,903.40	24.39	120.031		
7,700.00	7,058.13	7,178.32	7,058.13	50.15	23.50	-153.52	-902.54	514.05	2,927.80	2,902.80	25.00	117.125		
7,800.00	7,158.13	7,278.32	7,158.13	50.22	23.63	-153.52	-902.54	514.05	2,927.80	2,902.21	25.59	114.428		
7,900.00	7,258.13	7,378.32	7,258.13	50.29	23.76	-153.52	-902.54	514.05	2,927.80	2,901.63	26.16	111.910		
8,000.00	7,358.13	7,478.32	7,358.13	50.35	23.89	-153.52	-902.54	514.05	2,927.80	2,901.07	26.73	109.548		
8,100.00	7,458.13	7,578.32	7,458.13	50.42	24.03	-153.52	-902.54	514.05	2,927.80	2,900.51	27.28	107.322		
8,136.03	7,494.16	7,614.35	7,494.16	50.45	24.08	-153.52	-902.54	514.05	2,927.80	2,900.32	27.48	106.549		
8,182.87	7,541.00	7,627.20	7,507.00	50.48	24.09	-153.52	-902.54	514.05	2,927.99	2,900.32	27.67	105.811		

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at: 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF 11-26D-12-16 - PT PT 11-26-12-16 - Design #1													Offset Site Error:	0.00 ft
Survey Program: 0-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi-Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N-S (ft)	+E-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
0.00	0.00	0.00	0.00	0.00	0.00	-14.43	15.18	-3.91	15.67					
100.00	100.00	100.00	100.00	0.10	0.10	-14.43	15.18	-3.91	15.67	15.48	0.19	82.031		
200.00	200.00	200.00	200.00	0.32	0.32	-14.43	15.18	-3.91	15.67	15.03	0.64	24.466		
250.00	250.00	250.00	250.00	0.43	0.43	-14.43	15.18	-3.91	15.67	14.81	0.87	18.111 CC		
300.00	300.00	299.76	299.76	0.54	0.54	-61.65	15.59	-3.79	15.84	14.75	1.09	14.559 ES		
400.00	399.93	399.27	399.20	0.77	0.77	-65.87	18.91	-2.83	17.20	15.67	1.53	11.225		
500.00	499.68	498.70	498.39	1.01	1.01	-72.49	25.54	-0.92	20.15	18.17	1.98	10.152		
600.00	599.13	598.54	597.85	1.26	1.25	-82.43	33.91	1.49	23.85	21.40	2.46	9.715		
650.00	648.70	648.42	647.54	1.41	1.38	-89.15	38.08	2.69	25.87	23.17	2.70	9.574		
700.00	698.21	698.26	697.19	1.56	1.51	-95.75	42.26	3.89	28.23	25.28	2.95	9.562 SF		
800.00	797.24	797.96	796.51	1.87	1.77	-105.88	50.61	6.30	33.82	30.37	3.45	9.804		
900.00	896.27	897.65	895.82	2.19	2.04	-112.99	59.96	8.71	40.16	36.22	3.94	10.199		
1,000.00	995.30	997.35	995.14	2.51	2.30	-118.11	67.31	11.11	46.94	42.53	4.42	10.629		
1,065.34	1,060.00	1,062.49	1,060.03	2.73	2.48	-120.71	72.76	12.68	51.53	46.81	4.73	10.905		
1,100.00	1,094.28	1,097.05	1,094.43	2.84	2.57	-121.82	75.91	13.59	54.14	49.25	4.89	11.069		
1,200.00	1,192.72	1,196.73	1,193.34	3.22	2.87	-123.98	87.76	17.00	63.20	57.81	5.39	11.730		
1,300.00	1,290.30	1,296.32	1,291.53	3.64	3.21	-124.91	103.72	21.60	74.45	68.52	5.92	12.573		
1,400.00	1,386.83	1,395.75	1,388.74	4.13	3.60	-125.01	123.73	27.37	87.81	81.31	6.50	13.507		
1,500.00	1,482.13	1,494.93	1,484.73	4.69	4.04	-124.57	147.71	34.28	103.25	96.11	7.14	14.460		
1,600.00	1,576.03	1,593.82	1,579.26	5.32	4.55	-123.80	175.56	42.30	120.73	112.89	7.85	15.381		
1,700.00	1,668.33	1,692.34	1,672.12	6.03	5.11	-122.84	207.19	51.41	140.25	131.62	8.64	16.235		
1,800.00	1,758.87	1,790.44	1,763.08	6.81	5.75	-121.78	242.45	61.57	161.78	152.27	9.52	17.000		
1,900.00	1,847.47	1,887.89	1,851.95	7.67	6.44	-120.77	280.90	72.85	185.31	174.83	10.48	17.689		
2,000.00	1,933.96	1,984.53	1,939.74	8.62	7.15	-120.66	319.69	83.83	210.96	199.53	11.44	18.443		
2,042.12	1,969.72	2,025.02	1,976.54	9.04	7.46	-120.86	335.95	88.51	222.42	210.59	11.84	18.794		
2,100.00	2,018.58	2,080.58	2,027.01	9.63	7.87	-121.53	358.25	94.94	238.46	226.08	12.38	19.257		
2,200.00	2,103.00	2,176.56	2,114.21	10.66	8.60	-122.51	396.78	106.04	266.22	252.88	13.34	19.956		
2,300.00	2,187.41	2,272.54	2,201.41	11.70	9.34	-123.30	435.32	117.15	294.04	279.74	14.31	20.552		
2,400.00	2,271.82	2,368.52	2,288.61	12.75	10.07	-123.95	473.85	128.25	321.91	306.62	15.28	21.064		
2,500.00	2,356.24	2,464.50	2,375.82	13.80	10.82	-124.50	512.38	139.35	349.80	333.54	16.26	21.508		
2,600.00	2,440.65	2,560.48	2,463.02	14.86	11.56	-124.96	550.91	150.45	377.72	360.47	17.25	21.896		
2,700.00	2,525.07	2,656.46	2,550.22	15.92	12.31	-125.37	589.45	161.56	405.66	387.42	18.24	22.239		
2,800.00	2,609.48	2,752.44	2,637.42	16.98	13.06	-125.72	627.98	172.66	433.62	414.38	19.24	22.542		
2,900.00	2,693.90	2,848.42	2,724.63	18.05	13.82	-126.03	666.51	183.76	461.59	441.36	20.23	22.813		
3,000.00	2,778.31	2,944.40	2,811.83	19.11	14.57	-126.30	705.04	194.87	489.57	468.34	21.23	23.056		
3,100.00	2,862.73	3,040.38	2,899.03	20.18	15.33	-126.54	743.58	205.97	517.56	496.33	22.24	23.275		
3,200.00	2,947.14	3,136.37	2,988.23	21.25	16.08	-126.76	782.11	217.07	545.56	522.32	23.24	23.474		
3,300.00	3,031.56	3,232.35	3,073.44	22.32	16.84	-126.96	820.64	228.17	573.56	549.32	24.25	23.655		
3,400.00	3,115.97	3,328.33	3,160.64	23.40	17.60	-127.14	859.18	239.28	601.57	576.32	25.26	23.820		
3,500.00	3,200.38	3,424.31	3,247.84	24.47	18.36	-127.30	897.71	250.38	629.59	603.33	26.26	23.971		
3,600.00	3,284.80	3,520.29	3,335.04	25.54	19.12	-127.45	936.24	261.48	657.61	630.33	27.27	24.111		
3,700.00	3,369.21	3,616.27	3,422.25	26.62	19.88	-127.59	974.77	272.59	685.63	657.35	28.29	24.239		
3,800.00	3,453.63	3,712.25	3,509.45	27.69	20.64	-127.72	1,013.31	283.69	713.66	684.36	29.30	24.358		
3,900.00	3,538.04	3,808.23	3,596.65	28.77	21.40	-127.83	1,051.84	294.79	741.69	711.38	30.31	24.469		
4,000.00	3,622.46	3,904.21	3,683.85	29.84	22.17	-127.94	1,090.37	305.89	769.72	738.40	31.33	24.571		
4,100.00	3,706.87	4,000.19	3,771.06	30.92	22.93	-128.04	1,128.90	317.00	797.76	765.42	32.34	24.667		
4,200.00	3,791.29	4,096.17	3,858.26	31.99	23.69	-128.13	1,167.44	328.10	825.79	792.44	33.36	24.757		
4,300.00	3,875.70	4,192.15	3,945.46	33.07	24.46	-128.22	1,205.97	339.20	853.83	819.46	34.37	24.841		
4,400.00	3,960.12	4,288.13	4,032.66	34.15	25.22	-128.30	1,244.50	350.31	881.87	846.48	35.39	24.920		
4,500.00	4,044.53	4,384.12	4,119.87	35.23	25.98	-128.38	1,283.03	361.41	909.91	873.51	36.41	24.994		
4,600.00	4,128.95	4,480.10	4,207.07	36.30	26.75	-128.45	1,321.57	372.51	937.96	900.53	37.42	25.064		
4,700.00	4,213.36	4,576.08	4,294.27	37.38	27.51	-128.52	1,360.10	383.61	966.00	927.56	38.44	25.129		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



BILL BARRETT CORPORATION

Anticollision Report

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF 11-26D-12-16 - PT PT 11-26-12-16 - Design #1													Offset Site Error:	0.00 ft
Survey Program: O-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
4,800.00	4,297.77	4,672.06	4,381.47	38.46	28.27	-128.59	1,398.63	394.72	994.05	954.59	39.46	25.192		
4,900.00	4,382.19	4,768.04	4,468.68	39.54	29.04	-128.65	1,437.17	405.82	1,022.10	981.62	40.48	25.251		
5,000.00	4,466.60	4,864.02	4,555.88	40.62	29.80	-128.71	1,475.70	416.92	1,050.14	1,008.65	41.50	25.306		
5,100.00	4,551.02	4,960.00	4,643.08	41.70	30.57	-128.76	1,514.23	428.03	1,078.19	1,035.68	42.52	25.359		
5,200.00	4,635.43	5,050.83	4,725.85	42.77	31.19	-128.84	1,550.18	438.39	1,106.37	1,063.01	43.37	25.512		
5,258.09	4,685.32	5,100.00	4,771.18	43.41	31.48	-128.95	1,568.48	443.66	1,123.35	1,079.59	43.76	25.673		
5,300.00	4,720.04	5,137.71	4,806.22	43.81	31.69	-129.29	1,581.88	447.52	1,135.03	1,091.11	43.93	25.839		
5,400.00	4,806.51	5,224.56	4,887.75	44.63	32.15	-130.08	1,610.61	455.80	1,162.28	1,118.09	44.19	26.300		
5,500.00	4,895.08	5,311.50	4,970.45	45.38	32.58	-130.82	1,636.38	463.22	1,187.63	1,143.22	44.41	26.744		
5,600.00	4,985.60	5,400.00	5,055.60	46.08	32.97	-131.52	1,659.50	469.88	1,211.04	1,166.48	44.56	27.179		
5,700.00	5,077.88	5,485.58	5,138.76	46.71	33.30	-132.17	1,678.83	475.45	1,232.47	1,187.83	44.64	27.609		
5,800.00	5,171.75	5,572.60	5,224.06	47.28	33.60	-132.80	1,695.42	480.23	1,251.92	1,207.27	44.65	28.037		
5,900.00	5,267.04	5,659.60	5,309.93	47.79	33.85	-133.38	1,708.89	484.11	1,269.35	1,224.76	44.59	28.467		
6,000.00	5,363.56	5,746.54	5,396.19	48.22	34.06	-133.94	1,719.20	487.09	1,284.75	1,240.29	44.45	28.902		
6,100.00	5,461.13	5,833.36	5,482.69	48.59	34.23	-134.47	1,726.35	489.15	1,298.09	1,253.86	44.24	29.344		
6,200.00	5,559.55	5,920.02	5,569.24	48.90	34.35	-134.98	1,730.35	490.30	1,309.38	1,265.25	44.14	29.666		
6,300.00	5,658.66	6,009.44	5,658.66	49.14	34.43	-135.46	1,731.29	490.57	1,318.58	1,262.86	55.72	23.665		
6,400.00	5,758.25	6,109.03	5,758.25	49.32	34.50	-135.85	1,731.29	490.57	1,325.01	1,269.46	55.55	23.853		
6,500.00	5,858.13	6,208.92	5,858.13	49.44	34.58	-136.04	1,731.29	490.57	1,328.33	1,272.87	55.46	23.951		
6,555.87	5,914.00	6,264.79	5,914.00	49.48	34.62	-89.44	1,731.29	490.57	1,328.82	1,280.24	48.58	27.351		
6,600.00	5,958.13	6,308.91	5,958.13	49.50	34.65	-89.44	1,731.29	490.57	1,328.82	1,280.14	48.68	27.298		
6,700.00	6,058.13	6,408.91	6,058.13	49.55	34.73	-89.44	1,731.29	490.57	1,328.82	1,279.93	48.89	27.178		
6,800.00	6,158.13	6,508.91	6,158.13	49.61	34.81	-89.44	1,731.29	490.57	1,328.82	1,279.71	49.11	27.058		
6,900.00	6,258.13	6,608.91	6,258.13	49.67	34.89	-89.44	1,731.29	490.57	1,328.82	1,279.49	49.33	26.937		
7,000.00	6,358.13	6,708.91	6,358.13	49.72	34.97	-89.44	1,731.29	490.57	1,328.82	1,279.27	49.56	26.815		
7,100.00	6,458.13	6,808.91	6,458.13	49.78	35.05	-89.44	1,731.29	490.57	1,328.82	1,279.04	49.78	26.693		
7,200.00	6,558.13	6,908.91	6,558.13	49.84	35.13	-89.44	1,731.29	490.57	1,328.82	1,278.81	50.01	26.570		
7,300.00	6,658.13	7,008.91	6,658.13	49.90	35.22	-89.44	1,731.29	490.57	1,328.82	1,278.58	50.24	26.447		
7,400.00	6,758.13	7,108.91	6,758.13	49.96	35.30	-89.44	1,731.29	490.57	1,328.82	1,278.34	50.48	26.323		
7,500.00	6,858.13	7,208.91	6,858.13	50.03	35.39	-89.44	1,731.29	490.57	1,328.82	1,278.10	50.72	26.199		
7,600.00	6,958.13	7,308.91	6,958.13	50.09	35.48	-89.44	1,731.29	490.57	1,328.82	1,277.86	50.96	26.075		
7,700.00	7,058.13	7,408.91	7,058.13	50.15	35.57	-89.44	1,731.29	490.57	1,328.82	1,277.62	51.21	25.951		
7,800.00	7,158.13	7,508.91	7,158.13	50.22	35.66	-89.44	1,731.29	490.57	1,328.82	1,277.37	51.45	25.826		
7,900.00	7,258.13	7,608.91	7,258.13	50.29	35.75	-89.44	1,731.29	490.57	1,328.82	1,277.12	51.70	25.701		
8,000.00	7,358.13	7,708.91	7,358.13	50.35	35.85	-89.44	1,731.29	490.57	1,328.82	1,276.87	51.95	25.577		
8,100.00	7,458.13	7,808.91	7,458.13	50.42	35.94	-89.44	1,731.29	490.57	1,328.82	1,276.61	52.21	25.452		
8,136.97	7,495.10	7,845.88	7,495.10	50.45	35.98	-89.44	1,731.29	490.57	1,328.82	1,276.52	52.30	25.405		
8,162.87	7,541.00	7,898.79	7,508.00	50.48	35.99	-89.44	1,731.29	490.57	1,329.23	1,276.86	52.38	25.379		

CC - Min centre to center distance or covergent point, SF - min separation factor, ES - min ellipse separation



BILL BARRETT CORPORATION

Anticollision Report

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at: 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF 12-26D-12-16 - PT PT 12-26-12-16 - Design #1													Offset Site Error:	0.00 ft
Survey Program: O-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
0.00	0.00	0.00	0.00	0.00	0.00	-13.98	31.37	-7.81	32.33					
100.00	100.00	100.00	100.00	0.10	0.10	-13.98	31.37	-7.81	32.33	32.14	0.19	169.220		
200.00	200.00	200.00	200.00	0.32	0.32	-13.98	31.37	-7.81	32.33	31.69	0.64	50.469		
250.00	250.00	250.00	250.00	0.43	0.43	-13.98	31.37	-7.81	32.33	31.46	0.87	37.360 CC		
300.00	300.00	299.45	299.45	0.54	0.54	-61.43	31.76	-8.00	32.54	31.45	1.09	29.943 ES		
400.00	399.93	398.22	398.16	0.77	0.77	-67.52	34.83	-9.48	34.46	32.93	1.53	22.486		
500.00	499.68	496.63	496.32	1.01	1.00	-77.57	40.93	-12.42	39.29	37.29	2.00	19.679		
600.00	599.13	595.92	595.24	1.26	1.25	-89.00	48.72	-16.17	46.69	44.20	2.49	18.769		
650.00	648.70	645.48	644.61	1.41	1.38	-94.81	52.62	-18.05	51.04	48.30	2.75	18.593 SF		
700.00	698.21	694.99	693.93	1.56	1.51	-100.17	56.50	-19.92	55.92	52.92	3.01	18.596		
800.00	797.24	794.01	792.57	1.87	1.77	-108.41	64.28	-23.66	66.82	63.28	3.54	18.889		
900.00	896.27	893.02	891.21	2.19	2.03	-114.27	72.05	-27.41	78.70	74.63	4.07	19.335		
1,000.00	995.30	992.04	989.85	2.51	2.30	-118.56	79.83	-31.15	91.17	86.57	4.60	19.807		
1,065.34	1,060.00	1,056.74	1,054.30	2.73	2.47	-120.78	84.91	-33.60	99.54	94.59	4.95	20.103		
1,100.00	1,094.28	1,090.22	1,087.64	2.84	2.57	-121.74	87.69	-34.94	104.28	99.15	5.14	20.295		
1,200.00	1,192.72	1,185.66	1,182.39	3.22	2.85	-124.04	98.00	-39.91	121.44	115.73	5.71	21.267		
1,300.00	1,290.30	1,279.83	1,275.33	3.64	3.17	-125.67	111.65	-46.48	143.65	137.31	6.34	22.672		
1,400.00	1,386.83	1,372.42	1,368.01	4.13	3.53	-126.70	128.40	-54.55	170.75	163.73	7.02	24.322		
1,500.00	1,482.13	1,463.13	1,454.07	4.69	3.93	-127.26	148.01	-64.00	202.55	194.78	7.77	26.074		
1,600.00	1,576.03	1,551.73	1,539.18	5.32	4.37	-127.45	170.18	-74.68	238.87	230.28	8.58	27.827		
1,700.00	1,668.33	1,638.01	1,621.09	6.03	4.85	-127.36	194.60	-86.44	279.52	270.04	9.47	29.508		
1,800.00	1,758.87	1,721.78	1,699.59	6.81	5.37	-127.06	220.95	-99.13	324.31	313.88	10.43	31.092		
1,900.00	1,847.47	1,800.00	1,771.87	7.67	5.89	-126.56	247.87	-112.10	373.06	361.62	11.45	32.596		
2,000.00	1,933.96	1,881.31	1,845.88	8.62	6.51	-125.96	278.19	-126.71	425.54	412.97	12.57	33.856		
2,042.12	1,969.72	1,913.49	1,874.83	9.04	6.75	-125.65	290.85	-132.80	448.72	435.67	13.06	34.370		
2,100.00	2,018.58	1,960.97	1,917.36	9.63	7.14	-126.00	309.86	-141.96	481.06	467.29	13.77	34.938		
2,200.00	2,103.00	2,043.61	1,991.56	10.66	7.83	-126.50	343.04	-157.95	536.96	521.94	15.02	35.752		
2,300.00	2,187.41	2,126.64	2,065.76	11.70	8.52	-126.91	376.22	-173.93	592.88	576.59	16.29	36.401		
2,400.00	2,271.82	2,209.48	2,139.95	12.75	9.22	-127.25	409.41	-189.91	648.81	631.24	17.57	36.925		
2,500.00	2,356.24	2,292.31	2,214.15	13.80	9.92	-127.54	442.59	-205.90	704.76	685.89	18.87	37.352		
2,600.00	2,440.65	2,375.15	2,288.35	14.86	10.63	-127.78	475.77	-221.88	760.72	740.55	20.18	37.705		
2,700.00	2,525.07	2,457.99	2,362.55	15.92	11.35	-127.99	508.95	-237.87	816.69	795.20	21.49	38.002		
2,800.00	2,609.48	2,540.82	2,436.74	16.98	12.06	-128.18	542.13	-253.85	872.67	849.85	22.81	38.253		
2,900.00	2,693.90	2,623.66	2,510.94	18.05	12.78	-128.34	575.32	-269.83	928.65	904.51	24.14	38.468		
3,000.00	2,778.31	2,706.49	2,585.14	19.11	13.51	-128.48	608.50	-285.82	984.63	959.16	25.47	38.654		
3,100.00	2,862.73	2,789.33	2,659.33	20.18	14.23	-128.61	641.68	-301.80	1,040.62	1,013.81	26.81	38.815		
3,200.00	2,947.14	2,872.16	2,733.53	21.25	14.96	-128.72	674.86	-317.79	1,096.61	1,068.46	28.15	38.956		
3,300.00	3,031.56	2,955.00	2,807.73	22.32	15.68	-128.83	708.05	-333.77	1,152.61	1,123.11	29.49	39.080		
3,400.00	3,115.97	3,037.84	2,881.93	23.40	16.41	-128.92	741.23	-349.75	1,208.60	1,177.76	30.84	39.191		
3,500.00	3,200.38	3,120.67	2,956.12	24.47	17.14	-129.01	774.41	-365.74	1,264.60	1,232.42	32.19	39.289		
3,600.00	3,284.80	3,203.51	3,030.32	25.54	17.87	-129.09	807.59	-381.72	1,320.60	1,287.07	33.54	39.377		
3,700.00	3,369.21	3,286.34	3,104.52	26.62	18.60	-129.16	840.77	-397.70	1,376.61	1,341.72	34.89	39.456		
3,800.00	3,453.63	3,369.18	3,178.72	27.69	19.33	-129.22	873.96	-413.69	1,432.61	1,396.37	36.24	39.527		
3,900.00	3,538.04	3,452.01	3,252.91	28.77	20.06	-129.29	907.14	-429.67	1,488.61	1,451.02	37.60	39.592		
4,000.00	3,622.46	3,534.85	3,327.11	29.84	20.80	-129.34	940.32	-445.66	1,544.62	1,505.67	38.96	39.651		
4,100.00	3,706.87	3,617.69	3,401.31	30.92	21.53	-129.40	973.50	-461.64	1,600.63	1,560.32	40.31	39.705		
4,200.00	3,791.29	3,700.52	3,475.50	31.99	22.26	-129.44	1,006.68	-477.62	1,656.64	1,614.96	41.67	39.755		
4,300.00	3,875.70	3,783.36	3,549.70	33.07	23.00	-129.49	1,039.87	-493.61	1,712.64	1,669.61	43.03	39.800		
4,400.00	3,960.12	3,866.19	3,623.90	34.15	23.73	-129.53	1,073.05	-509.59	1,768.65	1,724.26	44.39	39.842		
4,500.00	4,044.53	3,949.03	3,698.10	35.23	24.47	-129.57	1,106.23	-525.58	1,824.66	1,778.91	45.75	39.880		
4,600.00	4,128.95	4,031.86	3,772.29	36.30	25.20	-129.61	1,139.41	-541.56	1,880.67	1,833.56	47.12	39.916		
4,700.00	4,213.36	4,114.70	3,846.49	37.38	25.94	-129.65	1,172.59	-557.54	1,936.69	1,888.21	48.48	39.949		

CC - Min centre to center distance or covergent point, SF - min separation factor, ES - min ellipse separation



BILL BARRETT CORPORATION

Anticollision Report

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at: 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF 12-26D-12-16 - PT PT 12-26-12-16 - Design #1													Offset Site Error:	0.00 ft
Survey Program: 0-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Tooface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
4,800.00	4,297.77	4,197.54	3,920.69	38.46	26.67	-129.68	1,205.78	-573.53	1,992.70	1,942.86	49.84	39.980		
4,900.00	4,382.19	4,280.37	3,994.88	39.54	27.41	-129.71	1,238.96	-589.51	2,048.71	1,997.50	51.21	40.009		
5,000.00	4,466.60	4,363.21	4,069.08	40.62	28.14	-129.74	1,272.14	-605.50	2,104.72	2,052.15	52.57	40.036		
5,100.00	4,551.02	4,446.04	4,143.28	41.70	28.88	-129.77	1,305.32	-621.48	2,160.73	2,106.80	53.94	40.061		
5,200.00	4,635.43	4,528.88	4,217.48	42.77	29.62	-129.80	1,338.50	-637.46	2,216.75	2,161.45	55.30	40.084		
5,259.09	4,685.32	4,577.83	4,261.32	43.41	30.05	-129.82	1,358.11	-646.91	2,249.85	2,193.74	56.11	40.097		
5,300.00	4,720.04	4,611.85	4,291.79	43.81	30.35	-130.34	1,371.74	-653.47	2,272.57	2,215.86	56.70	40.077		
5,400.00	4,806.51	4,696.06	4,367.23	44.63	31.10	-131.48	1,405.47	-669.72	2,326.43	2,268.35	58.08	40.056		
5,500.00	4,895.08	4,781.66	4,443.89	45.38	31.86	-132.45	1,439.76	-686.24	2,377.84	2,318.40	59.45	40.000		
5,600.00	4,985.60	4,868.46	4,521.64	46.08	32.64	-133.24	1,474.53	-702.99	2,426.73	2,365.94	60.79	39.918		
5,700.00	5,077.88	4,956.30	4,600.33	46.71	33.42	-133.88	1,509.72	-719.94	2,473.03	2,410.92	62.12	39.814		
5,800.00	5,171.75	5,080.24	4,711.85	47.28	34.43	-134.25	1,558.42	-743.40	2,516.44	2,452.82	63.82	39.553		
5,900.00	5,267.04	5,259.45	4,877.56	47.79	35.55	-134.41	1,619.76	-772.95	2,554.61	2,489.42	65.19	39.186		
6,000.00	5,363.56	5,447.95	5,057.06	48.22	36.50	-134.61	1,671.49	-797.87	2,586.65	2,520.11	66.54	38.875		
6,100.00	5,461.13	5,644.12	5,248.19	48.59	37.25	-134.86	1,711.03	-816.91	2,612.19	2,544.56	67.62	38.628		
6,200.00	5,559.55	5,845.74	5,447.80	48.90	37.77	-135.22	1,736.17	-829.02	2,630.94	2,562.53	68.41	38.459		
6,300.00	5,658.66	6,050.19	5,651.92	49.14	38.04	-135.64	1,745.43	-833.48	2,642.70	2,573.67	69.04	38.280		
6,400.00	5,758.25	6,156.51	5,758.25	49.32	38.11	-135.90	1,745.46	-833.50	2,649.15	2,592.22	69.33	46.533		
6,500.00	5,858.13	6,256.39	5,858.13	49.44	38.18	-136.03	1,745.46	-833.50	2,652.48	2,595.43	69.44	46.501		
6,555.87	5,914.00	6,312.26	5,914.00	49.48	38.22	-89.41	1,745.46	-833.50	2,652.97	2,602.26	50.71	52.316		
6,600.00	5,958.13	6,356.39	5,958.13	49.50	38.25	-89.41	1,745.46	-833.50	2,652.97	2,602.17	50.80	52.225		
6,700.00	6,058.13	6,456.39	6,058.13	49.55	38.33	-89.41	1,745.46	-833.50	2,652.97	2,601.96	51.00	52.016		
6,800.00	6,158.13	6,556.39	6,158.13	49.61	38.40	-89.41	1,745.46	-833.50	2,652.97	2,601.76	51.21	51.806		
6,900.00	6,258.13	6,656.39	6,258.13	49.67	38.47	-89.41	1,745.46	-833.50	2,652.97	2,601.55	51.42	51.594		
7,000.00	6,358.13	6,756.39	6,358.13	49.72	38.55	-89.41	1,745.46	-833.50	2,652.97	2,601.33	51.63	51.381		
7,100.00	6,458.13	6,856.39	6,458.13	49.78	38.63	-89.41	1,745.46	-833.50	2,652.97	2,601.12	51.85	51.167		
7,200.00	6,558.13	6,956.39	6,558.13	49.84	38.70	-89.41	1,745.46	-833.50	2,652.97	2,600.90	52.07	50.951		
7,300.00	6,658.13	7,056.39	6,658.13	49.90	38.78	-89.41	1,745.46	-833.50	2,652.97	2,600.67	52.29	50.735		
7,400.00	6,758.13	7,156.39	6,758.13	49.96	38.86	-89.41	1,745.46	-833.50	2,652.97	2,600.45	52.52	50.518		
7,500.00	6,858.13	7,256.39	6,858.13	50.03	38.94	-89.41	1,745.46	-833.50	2,652.97	2,600.22	52.74	50.299		
7,600.00	6,958.13	7,356.39	6,958.13	50.09	39.03	-89.41	1,745.46	-833.50	2,652.97	2,599.99	52.97	50.080		
7,700.00	7,058.13	7,456.39	7,058.13	50.15	39.11	-89.41	1,745.46	-833.50	2,652.97	2,599.76	53.21	49.860		
7,800.00	7,158.13	7,556.39	7,158.13	50.22	39.19	-89.41	1,745.46	-833.50	2,652.97	2,599.52	53.44	49.640		
7,900.00	7,258.13	7,656.39	7,258.13	50.29	39.28	-89.41	1,745.46	-833.50	2,652.97	2,599.28	53.68	49.419		
8,000.00	7,358.13	7,756.39	7,358.13	50.35	39.37	-89.41	1,745.46	-833.50	2,652.97	2,599.04	53.92	49.198		
8,100.00	7,458.13	7,856.39	7,458.13	50.42	39.45	-89.41	1,745.46	-833.50	2,652.97	2,598.80	54.17	48.976		
8,138.74	7,496.87	7,895.13	7,496.87	50.45	39.49	-89.41	1,745.46	-833.50	2,652.97	2,598.70	54.26	48.890		
8,182.87	7,541.00	7,908.26	7,510.00	50.48	39.50	-89.41	1,745.46	-833.50	2,653.15	2,598.81	54.33	48.832		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



BILL BARRETT CORPORATION

Anticollision Report

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at: 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF 13-26D-12-16 - PT PT 13-26-12-16 - Design #1														Offset Site Error:	0.00 ft
Survey Program: 0-MWD														Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance		Minimum Separation		Warning				
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning		
0.00	0.00	0.00	0.00	0.00	0.00	165.57	-15.18	3.91	15.67						
100.00	100.00	100.00	100.00	0.10	0.10	165.57	-15.18	3.91	15.67	15.48	0.19	82.031			
200.00	200.00	200.00	200.00	0.32	0.32	165.57	-15.18	3.91	15.67	15.03	0.64	24.466			
250.00	250.00	250.00	250.00	0.43	0.43	165.57	-15.18	3.91	15.67	14.81	0.87	18.111 CC			
300.00	300.00	300.00	300.00	0.54	0.55	120.30	-15.18	3.91	15.89	14.80	1.09	14.594 ES			
400.00	399.93	399.93	399.93	0.77	0.77	129.95	-15.18	3.91	17.90	16.37	1.54	11.639			
500.00	499.68	499.68	499.68	1.01	0.99	143.31	-15.18	3.91	23.02	21.02	2.00	11.535 SF			
600.00	599.13	599.13	599.13	1.26	1.22	154.47	-15.18	3.91	32.02	29.57	2.45	13.082			
650.00	648.70	648.70	648.70	1.41	1.33	158.66	-15.18	3.91	38.02	35.35	2.67	14.248			
700.00	698.21	698.21	698.21	1.56	1.44	161.92	-15.18	3.91	44.58	41.70	2.88	15.469			
800.00	797.24	797.24	797.24	1.87	1.66	166.19	-15.18	3.91	57.98	54.68	3.31	17.540			
900.00	896.27	896.27	896.27	2.19	1.89	168.85	-15.18	3.91	71.58	67.85	3.73	19.203			
1,000.00	995.30	995.30	995.30	2.51	2.11	170.65	-15.18	3.91	85.28	81.13	4.15	20.556			
1,065.34	1,060.00	1,060.00	1,060.00	2.73	2.25	171.55	-15.18	3.91	94.27	89.84	4.42	21.310			
1,100.00	1,094.28	1,094.07	1,094.07	2.84	2.33	172.08	-15.08	3.73	99.34	94.59	4.75	20.913			
1,200.00	1,192.72	1,191.54	1,191.50	3.22	2.54	174.58	-13.75	1.24	117.38	112.19	5.19	22.615			
1,300.00	1,290.30	1,287.39	1,287.15	3.64	2.75	177.82	-10.92	-4.04	140.74	135.10	5.63	24.991			
1,400.00	1,386.83	1,381.11	1,380.44	4.13	2.96	-178.81	-6.68	-11.94	169.67	163.59	6.08	27.908			
1,500.00	1,482.13	1,472.25	1,470.83	4.69	3.19	-175.85	-1.19	-22.19	204.28	197.74	6.54	31.226			
1,600.00	1,576.03	1,560.41	1,557.87	5.32	3.44	-172.81	5.42	-34.52	244.52	237.50	7.02	34.813			
1,700.00	1,668.33	1,645.25	1,641.19	6.03	3.70	-170.30	12.97	-48.60	290.24	282.71	7.53	38.546			
1,800.00	1,758.87	1,726.47	1,720.47	6.81	3.98	-168.09	21.29	-64.11	341.22	333.16	8.06	42.324			
1,900.00	1,847.47	1,803.85	1,795.52	7.67	4.27	-166.11	30.19	-80.73	397.20	388.58	8.62	46.063			
2,000.00	1,933.96	1,877.21	1,866.17	8.62	4.59	-164.33	39.52	-98.13	457.89	448.67	9.22	49.668			
2,042.12	1,969.72	1,906.87	1,894.59	9.04	4.73	-163.62	43.53	-105.61	484.79	475.31	9.48	51.149			
2,100.00	2,018.58	1,946.82	1,932.73	9.63	4.92	-163.01	49.16	-116.11	522.46	512.66	9.90	52.762			
2,200.00	2,103.00	2,021.49	2,003.81	10.66	5.30	-162.00	59.96	-136.26	588.00	577.32	10.68	55.059			
2,300.00	2,187.41	2,096.66	2,075.36	11.70	5.70	-161.19	70.84	-156.55	653.61	642.15	11.47	56.991			
2,400.00	2,271.82	2,171.82	2,146.91	12.75	6.11	-160.52	81.72	-176.84	719.30	707.02	12.28	58.589			
2,500.00	2,356.24	2,246.98	2,218.46	13.80	6.53	-159.96	92.60	-197.13	785.02	771.93	13.10	59.934			
2,600.00	2,440.65	2,322.14	2,290.01	14.86	6.96	-159.49	103.47	-217.42	850.79	836.86	13.93	61.075			
2,700.00	2,525.07	2,397.31	2,361.56	15.92	7.40	-159.09	114.35	-237.71	916.58	901.81	14.77	62.051			
2,800.00	2,609.48	2,472.47	2,433.11	16.98	7.84	-158.74	125.23	-258.00	982.39	966.77	15.62	62.885			
2,900.00	2,693.90	2,547.63	2,504.66	18.05	8.29	-158.43	136.10	-278.29	1,048.23	1,031.75	16.48	63.611			
3,000.00	2,778.31	2,622.79	2,576.21	19.11	8.74	-158.16	146.98	-298.58	1,114.07	1,096.73	17.34	64.245			
3,100.00	2,862.73	2,697.96	2,647.76	20.18	9.19	-157.92	157.86	-318.87	1,179.93	1,161.73	18.21	64.803			
3,200.00	2,947.14	2,773.12	2,719.31	21.25	9.64	-157.71	168.74	-339.16	1,245.81	1,226.72	19.08	65.292			
3,300.00	3,031.56	2,848.28	2,790.86	22.32	10.10	-157.51	179.61	-359.45	1,311.68	1,291.73	19.96	65.728			
3,400.00	3,115.97	2,923.44	2,862.41	23.40	10.56	-157.34	190.49	-379.75	1,377.57	1,356.74	20.84	66.117			
3,500.00	3,200.38	2,998.61	2,933.96	24.47	11.03	-157.18	201.37	-400.04	1,443.47	1,421.75	21.72	66.465			
3,600.00	3,284.80	3,073.77	3,005.51	25.54	11.49	-157.04	212.25	-420.33	1,509.36	1,486.76	22.60	66.778			
3,700.00	3,369.21	3,148.93	3,077.06	26.62	11.96	-156.90	223.12	-440.62	1,575.27	1,551.78	23.49	67.060			
3,800.00	3,453.63	3,224.09	3,148.61	27.69	12.42	-156.78	234.00	-460.91	1,641.18	1,616.80	24.38	67.317			
3,900.00	3,538.04	3,299.26	3,220.16	28.77	12.89	-156.67	244.88	-481.20	1,707.09	1,681.82	25.27	67.550			
4,000.00	3,622.46	3,374.42	3,291.71	29.84	13.36	-156.56	255.76	-501.49	1,773.01	1,746.84	26.17	67.762			
4,100.00	3,706.87	3,449.58	3,363.26	30.92	13.83	-156.47	266.63	-521.78	1,838.93	1,811.87	27.06	67.957			
4,200.00	3,791.29	3,524.74	3,434.81	31.99	14.30	-156.38	277.51	-542.07	1,904.85	1,876.89	27.96	68.135			
4,300.00	3,875.70	3,599.91	3,506.36	33.07	14.77	-156.29	288.39	-562.36	1,970.77	1,941.82	28.85	68.300			
4,400.00	3,960.12	3,675.07	3,577.91	34.15	15.25	-156.21	299.26	-582.65	2,036.70	2,006.94	29.75	68.451			
4,500.00	4,044.53	3,750.23	3,649.46	35.23	15.72	-156.14	310.14	-602.94	2,102.63	2,071.97	30.65	68.591			
4,600.00	4,128.95	3,825.39	3,721.01	36.30	16.19	-156.07	321.02	-623.23	2,168.56	2,137.00	31.56	68.720			
4,700.00	4,213.36	3,900.55	3,792.56	37.38	16.67	-156.01	331.90	-643.52	2,234.49	2,202.03	32.46	68.841			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



BILL BARRETT CORPORATION

Anticollision Report

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at: 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

SECTION 26 T12S R16E - PETERS POINT UF 13-26D-12-16 - PT PT 13-26-12-16 - Design #1													Offset Site Error:	0.00 ft
Survey Program: O-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance		Minimum Separation		Warning			
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning	
4,800.00	4,297.77	3,975.72	3,864.11	38.46	17.14	-155.94	342.77	-663.81	2,300.42	2,287.06	33.36	68.953		
4,900.00	4,382.19	4,086.28	3,969.69	39.54	17.71	-155.89	358.27	-692.71	2,365.93	2,331.59	34.34	68.901		
5,000.00	4,466.60	4,211.50	4,090.35	40.62	18.27	-155.92	374.08	-722.21	2,429.96	2,394.66	35.30	68.839		
5,100.00	4,551.02	4,340.84	4,216.06	41.70	18.80	-156.05	388.45	-749.01	2,492.41	2,456.20	36.22	68.820		
5,200.00	4,635.43	4,474.19	4,346.67	42.77	19.28	-156.28	401.14	-772.69	2,553.20	2,516.12	37.09	68.845		
5,259.09	4,685.32	4,554.83	4,426.07	43.41	19.54	-156.45	407.77	-785.06	2,588.32	2,550.75	37.57	68.887		
5,300.00	4,720.04	4,611.77	4,482.31	43.81	19.72	-156.88	411.98	-792.90	2,612.00	2,574.02	37.98	68.771		
5,400.00	4,806.51	4,756.42	4,625.72	44.63	20.10	-157.84	420.87	-809.49	2,666.22	2,627.32	38.90	68.538		
5,500.00	4,895.08	4,908.30	4,776.96	45.38	20.43	-158.73	427.44	-821.74	2,714.99	2,675.24	39.75	68.304		
5,600.00	4,985.60	5,066.65	4,935.09	46.08	20.68	-159.56	431.26	-828.87	2,758.00	2,717.51	40.49	68.111		
5,700.00	5,077.88	5,209.46	5,077.88	46.71	20.85	-160.29	432.09	-830.42	2,795.10	2,774.01	21.09	132.536		
5,800.00	5,171.75	5,303.33	5,171.75	47.28	20.96	-160.81	432.09	-830.42	2,827.79	2,807.84	19.95	141.710		
5,900.00	5,267.04	5,398.62	5,267.04	47.79	21.07	-161.25	432.09	-830.42	2,856.60	2,815.09	41.51	68.823		
6,000.00	5,363.56	5,495.14	5,363.56	48.22	21.19	-161.62	432.09	-830.42	2,881.45	2,839.53	41.92	68.736		
6,100.00	5,461.13	5,592.71	5,461.13	48.59	21.30	-161.93	432.09	-830.42	2,902.30	2,860.03	42.26	68.673		
6,200.00	5,559.55	5,691.13	5,559.55	48.90	21.42	-162.16	432.09	-830.42	2,919.08	2,876.55	42.53	68.634		
6,300.00	5,658.66	5,790.24	5,658.66	49.14	21.54	-162.34	432.09	-830.42	2,931.76	2,889.04	42.73	68.619		
6,400.00	5,758.25	5,889.82	5,758.25	49.32	21.67	-162.46	432.09	-830.42	2,940.32	2,897.47	42.85	68.625		
6,500.00	5,858.13	5,989.71	5,858.13	49.44	21.79	-162.52	432.09	-830.42	2,944.72	2,901.83	42.89	68.650		
6,555.87	5,914.00	6,045.58	5,914.00	49.48	21.87	-115.89	432.09	-830.42	2,945.37	2,903.11	42.26	69.700		
6,600.00	5,958.13	6,089.70	5,958.13	49.50	21.92	-115.89	432.09	-830.42	2,945.37	2,903.00	42.37	69.520		
6,700.00	6,058.13	6,189.70	6,058.13	49.55	22.05	-115.89	432.09	-830.42	2,945.37	2,902.75	42.62	69.106		
6,800.00	6,158.13	6,289.70	6,158.13	49.61	22.18	-115.89	432.09	-830.42	2,945.37	2,902.49	42.88	68.692		
6,900.00	6,258.13	6,389.70	6,258.13	49.67	22.32	-115.89	432.09	-830.42	2,945.37	2,902.23	43.14	68.279		
7,000.00	6,358.13	6,489.70	6,358.13	49.72	22.45	-115.89	432.09	-830.42	2,945.37	2,901.97	43.40	67.865		
7,100.00	6,458.13	6,589.70	6,458.13	49.78	22.59	-115.89	432.09	-830.42	2,945.37	2,901.70	43.67	67.452		
7,200.00	6,558.13	6,689.70	6,558.13	49.84	22.72	-115.89	432.09	-830.42	2,945.37	2,901.44	43.93	67.039		
7,300.00	6,658.13	6,789.70	6,658.13	49.90	22.86	-115.89	432.09	-830.42	2,945.37	2,901.16	44.21	66.627		
7,400.00	6,758.13	6,889.70	6,758.13	49.96	23.00	-115.89	432.09	-830.42	2,945.37	2,900.89	44.48	66.216		
7,500.00	6,858.13	6,989.70	6,858.13	50.03	23.14	-115.89	432.09	-830.42	2,945.37	2,900.61	44.76	65.806		
7,600.00	6,958.13	7,089.70	6,958.13	50.09	23.28	-115.89	432.09	-830.42	2,945.37	2,900.33	45.04	65.398		
7,700.00	7,058.13	7,189.70	7,058.13	50.15	23.43	-115.89	432.09	-830.42	2,945.37	2,900.05	45.32	64.990		
7,800.00	7,158.13	7,289.70	7,158.13	50.22	23.57	-115.89	432.09	-830.42	2,945.37	2,899.77	45.61	64.584		
7,900.00	7,258.13	7,389.70	7,258.13	50.29	23.72	-115.89	432.09	-830.42	2,945.37	2,899.48	45.89	64.179		
8,000.00	7,358.13	7,489.70	7,358.13	50.35	23.87	-115.89	432.09	-830.42	2,945.37	2,899.19	46.18	63.776		
8,100.00	7,458.13	7,589.70	7,458.13	50.42	24.01	-115.89	432.09	-830.42	2,945.37	2,922.45	22.92	128.519		
8,137.87	7,496.00	7,627.58	7,496.00	50.45	24.07	-115.89	432.09	-830.42	2,945.37	2,921.89	23.48	125.426		
8,182.87	7,541.00	7,640.58	7,509.00	50.48	24.09	-115.89	432.09	-830.42	2,945.54	2,921.55	24.00	122.734		

CC - Min centre to center distance or covergent point, SF - min separation factor, ES - min ellipse separation



BILL BARRETT CORPORATION

Anticollision Report

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at: 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum

Offset Design SECTION 26 T12S R16E - PETERS POINT UF 15-26D-12-16 - PT PT 15-26-12-16 - Design #1														Offset Site Error:	0.00 ft
Survey Program: 0-MWD														Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis		Highside Toolface (°)	Offset Wellbore Centre		Distance		Minimum Separation (ft)	Separation Factor	Warning		
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)		+N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)					
0.00	0.00	0.00	0.00	0.00	0.00	164.20	-30.36	8.59	31.55						
100.00	100.00	100.00	100.00	0.10	0.10	164.20	-30.36	8.59	31.55	31.36	0.19	165.152			
200.00	200.00	200.00	200.00	0.32	0.32	164.20	-30.36	8.59	31.55	30.91	0.64	49.256			
250.00	250.00	250.00	250.00	0.43	0.43	164.20	-30.36	8.59	31.55	30.69	0.87	36.462 CC, ES			
300.00	300.00	299.98	299.97	0.54	0.54	117.46	-30.26	9.02	31.77	30.69	1.08	29.322			
400.00	399.93	399.90	399.83	0.77	0.76	116.77	-29.46	12.41	33.54	32.02	1.52	22.066			
500.00	499.68	499.75	499.44	1.01	0.99	115.58	-27.86	19.18	37.09	35.11	1.98	18.775			
600.00	599.13	599.61	598.91	1.26	1.24	116.49	-25.85	27.65	42.29	39.84	2.45	17.261			
650.00	648.70	649.49	648.60	1.41	1.37	118.33	-24.85	31.88	45.50	42.81	2.69	16.898			
700.00	698.21	699.34	698.26	1.56	1.50	120.41	-23.85	36.11	48.97	46.04	2.93	16.689			
800.00	797.24	799.04	797.58	1.87	1.77	123.78	-21.85	44.56	56.07	52.65	3.42	16.401			
900.00	896.27	898.73	896.90	2.19	2.04	126.40	-19.85	53.02	63.32	59.42	3.90	16.231			
1,000.00	995.30	998.43	996.22	2.51	2.31	128.47	-17.85	61.48	70.68	66.30	4.38	16.131			
1,065.34	1,060.00	1,063.59	1,061.12	2.73	2.48	129.60	-16.54	67.00	75.53	70.83	4.69	16.091 SF			
1,100.00	1,094.28	1,098.34	1,095.72	2.84	2.58	130.05	-15.78	70.22	78.23	73.37	4.86	16.093			
1,200.00	1,192.72	1,198.58	1,195.17	3.22	2.89	130.68	-12.91	82.36	87.39	82.03	5.36	16.293			
1,300.00	1,290.30	1,298.74	1,293.90	3.64	3.24	130.54	-9.04	98.71	98.56	92.66	5.90	16.696			
1,400.00	1,386.83	1,398.73	1,391.65	4.13	3.64	129.86	-4.19	119.20	111.72	105.22	6.49	17.206			
1,500.00	1,482.13	1,498.50	1,488.16	4.69	4.11	128.83	1.62	143.76	126.85	119.70	7.15	17.752			
1,600.00	1,576.03	1,597.98	1,583.21	5.32	4.64	127.57	8.37	172.29	143.96	136.08	7.88	18.277			
1,700.00	1,668.33	1,697.10	1,676.57	6.03	5.25	126.21	16.03	204.69	163.05	154.35	8.70	18.740			
1,800.00	1,758.87	1,795.81	1,768.02	6.81	5.94	124.79	24.58	240.83	184.11	174.48	9.63	19.120			
1,900.00	1,847.47	1,894.06	1,857.37	7.67	6.71	123.37	33.98	280.57	207.12	196.45	10.67	19.406			
2,000.00	1,933.96	1,991.23	1,944.28	8.62	7.55	122.16	43.98	322.85	232.13	220.32	11.81	19.656			
2,042.12	1,969.72	2,031.83	1,980.54	9.04	7.91	121.91	48.19	340.64	243.33	231.04	12.29	19.797			
2,100.00	2,018.58	2,087.55	2,030.29	9.63	8.40	122.02	53.97	365.05	258.99	246.02	12.97	19.975			
2,200.00	2,103.00	2,183.81	2,116.25	10.66	9.27	122.16	63.94	407.23	286.05	271.90	14.15	20.210			
2,300.00	2,187.41	2,280.08	2,202.21	11.70	10.15	122.29	73.92	449.40	313.11	297.75	15.36	20.382			
2,400.00	2,271.82	2,376.35	2,288.17	12.75	11.03	122.39	83.90	491.58	340.17	323.58	16.59	20.509			
2,500.00	2,356.24	2,472.62	2,374.13	13.80	11.92	122.48	93.87	533.75	367.23	349.41	17.82	20.604			
2,600.00	2,440.65	2,568.88	2,460.09	14.86	12.81	122.56	103.85	575.92	394.30	375.22	19.07	20.675			
2,700.00	2,525.07	2,665.15	2,546.05	15.92	13.71	122.62	113.83	618.10	421.36	401.03	20.33	20.729			
2,800.00	2,609.48	2,761.42	2,632.01	16.98	14.61	122.68	123.80	660.27	448.42	426.83	21.59	20.770			
2,900.00	2,693.90	2,857.68	2,717.97	18.05	15.51	122.74	133.78	702.45	475.49	452.63	22.86	20.802			
3,000.00	2,778.31	2,953.95	2,803.93	19.11	16.42	122.78	143.76	744.62	502.55	478.42	24.13	20.826			
3,100.00	2,862.73	3,050.22	2,889.89	20.18	17.33	122.82	153.73	786.80	529.62	504.21	25.41	20.844			
3,200.00	2,947.14	3,146.49	2,975.85	21.25	18.23	122.86	163.71	828.97	556.68	529.99	26.69	20.858			
3,300.00	3,031.56	3,242.75	3,061.81	22.32	19.14	122.90	173.69	871.15	583.75	555.78	27.97	20.868			
3,400.00	3,115.97	3,339.02	3,147.77	23.40	20.06	122.93	183.66	913.32	610.81	581.55	29.26	20.875			
3,500.00	3,200.38	3,435.29	3,233.73	24.47	20.97	122.95	193.64	955.50	637.88	607.33	30.55	20.880			
3,600.00	3,284.80	3,531.55	3,319.69	25.54	21.88	122.98	203.62	997.67	664.95	633.11	31.84	20.884			
3,700.00	3,369.21	3,627.82	3,405.65	26.62	22.79	123.00	213.59	1,039.85	692.01	658.88	33.13	20.886			
3,800.00	3,453.63	3,724.09	3,491.61	27.69	23.71	123.03	223.57	1,082.02	719.08	684.65	34.43	20.887			
3,900.00	3,538.04	3,820.36	3,577.57	28.77	24.62	123.05	233.55	1,124.20	746.15	710.42	35.72	20.887			
4,000.00	3,622.46	3,916.62	3,663.53	29.84	25.54	123.07	243.52	1,166.37	773.21	736.19	37.02	20.886			
4,100.00	3,706.87	4,012.89	3,749.49	30.92	26.45	123.08	253.50	1,208.54	800.28	761.96	38.32	20.885			
4,200.00	3,791.29	4,109.16	3,835.45	31.99	27.37	123.10	263.48	1,250.72	827.34	787.73	39.62	20.883			
4,300.00	3,875.70	4,205.42	3,921.41	33.07	28.29	123.12	273.46	1,292.89	854.41	813.49	40.92	20.881			
4,400.00	3,960.12	4,301.69	4,007.37	34.15	29.20	123.13	283.43	1,335.07	881.48	839.26	42.22	20.879			
4,500.00	4,044.53	4,397.96	4,093.33	35.23	30.12	123.15	293.41	1,377.24	908.54	865.02	43.52	20.876			
4,600.00	4,128.95	4,494.22	4,179.29	36.30	31.04	123.16	303.39	1,419.42	935.61	890.79	44.82	20.874			
4,700.00	4,213.36	4,590.49	4,265.25	37.38	31.95	123.17	313.36	1,461.59	962.68	916.55	46.13	20.871			

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation

Company: BILL BARRETT CORP
Project: CARBON COUNTY, UT (NAD 27)
Reference Site: SECTION 26 T12S R16E
Site Error: 0.00ft
Reference Well: PETERS POINT UF 10-26D-12-16
Well Error: 0.00ft
Reference Wellbore: PT PT 10-26-12-16
Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
TVD Reference: WELL @ 7177.00ft (Original Well Elev)
MD Reference: WELL @ 7177.00ft (Original Well Elev)
North Reference: True
Survey Calculation Method: Minimum Curvature
Output errors are at: 2.00 sigma
Database: Compass
Offset TVD Reference: Offset Datum


Offset Design SECTION 26 T12S R16E - PETERS POINT UF 15-26D-12-16 - PT PT 15-26-12-16 - Design #1													Offset Site Error:	0.00 ft
Survey Program: 0-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre -N-S (ft)	+E-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
4,800.00	4,297.77	4,686.76	4,351.21	38.46	32.87	123.18	323.34	1,503.77	989.74	942.31	47.43	20.868		
4,900.00	4,382.19	4,783.03	4,437.17	39.54	33.79	123.19	333.32	1,545.94	1,016.81	968.08	48.73	20.865		
5,000.00	4,466.60	4,878.78	4,522.67	40.62	34.69	123.21	343.24	1,587.87	1,043.88	993.86	50.02	20.868		
5,100.00	4,551.02	4,969.84	4,604.94	41.70	35.39	123.34	352.22	1,625.86	1,071.23	1,020.19	51.04	20.990		
5,200.00	4,635.43	5,060.32	4,688.16	42.77	36.00	123.65	360.40	1,660.42	1,099.06	1,047.18	51.88	21.184		
5,259.09	4,685.32	5,113.41	4,737.61	43.41	36.34	123.92	364.84	1,679.20	1,115.76	1,063.44	52.32	21.328		
5,300.00	4,720.04	5,150.05	4,772.00	43.81	36.56	124.37	367.75	1,691.51	1,127.24	1,074.72	52.52	21.463		
5,400.00	4,806.51	5,239.60	4,856.86	44.63	37.05	125.42	374.33	1,719.33	1,154.05	1,101.21	52.84	21.840		
5,500.00	4,895.08	5,329.11	4,942.73	45.38	37.49	126.41	380.14	1,743.89	1,179.05	1,125.98	53.07	22.215		
5,600.00	4,985.60	5,418.55	5,029.45	46.08	37.87	127.34	385.17	1,765.16	1,202.20	1,148.98	53.22	22.590		
5,700.00	5,077.88	5,507.88	5,116.85	46.71	38.19	128.22	389.42	1,783.10	1,223.47	1,170.20	53.27	22.968		
5,800.00	5,171.75	5,600.00	5,207.66	47.28	38.47	129.07	392.97	1,798.11	1,242.83	1,189.60	53.22	23.351		
5,900.00	5,267.04	5,686.08	5,293.02	47.79	38.67	129.84	395.53	1,808.92	1,260.24	1,207.15	53.09	23.737		
6,000.00	5,363.56	5,774.88	5,381.45	48.22	38.83	130.59	397.39	1,816.79	1,275.71	1,222.84	52.87	24.130		
6,100.00	5,461.13	5,863.42	5,469.86	48.59	38.94	131.31	398.46	1,821.32	1,289.21	1,236.65	52.55	24.531		
6,200.00	5,559.55	5,953.13	5,559.55	48.90	39.02	131.99	398.75	1,822.55	1,300.72	1,233.01	67.71	19.209		
6,300.00	5,658.66	6,052.23	5,658.66	49.14	39.08	132.59	398.75	1,822.55	1,309.72	1,242.23	67.49	19.407		
6,400.00	5,758.25	6,151.82	5,758.25	49.32	39.15	132.99	398.75	1,822.55	1,315.83	1,248.50	67.32	19.544		
6,500.00	5,858.13	6,251.71	5,858.13	49.44	39.22	133.19	398.75	1,822.55	1,318.98	1,251.75	67.24	19.617		
6,555.87	5,914.00	6,307.58	5,914.00	49.48	39.26	179.86	398.75	1,822.55	1,319.45	1,252.51	66.93	19.713		
6,600.00	5,958.13	6,351.70	5,958.13	49.50	39.29	179.86	398.75	1,822.55	1,319.45	1,252.44	67.00	19.692		
6,700.00	6,058.13	6,451.70	6,058.13	49.55	39.37	179.86	398.75	1,822.55	1,319.45	1,252.28	67.17	19.642		
6,800.00	6,158.13	6,551.70	6,158.13	49.61	39.44	179.86	398.75	1,822.55	1,319.45	1,252.10	67.35	19.592		
6,900.00	6,258.13	6,651.70	6,258.13	49.67	39.51	179.86	398.75	1,822.55	1,319.45	1,251.93	67.52	19.542		
7,000.00	6,358.13	6,751.70	6,358.13	49.72	39.59	179.86	398.75	1,822.55	1,319.45	1,251.75	67.70	19.491		
7,100.00	6,458.13	6,851.70	6,458.13	49.78	39.67	179.86	398.75	1,822.55	1,319.45	1,251.57	67.88	19.439		
7,200.00	6,558.13	6,951.70	6,558.13	49.84	39.74	179.86	398.75	1,822.55	1,319.45	1,251.39	68.06	19.387		
7,300.00	6,658.13	7,051.70	6,658.13	49.90	39.82	179.86	398.75	1,822.55	1,319.45	1,251.21	68.24	19.335		
7,400.00	6,758.13	7,151.70	6,758.13	49.96	39.90	179.86	398.75	1,822.55	1,319.45	1,251.02	68.43	19.282		
7,500.00	6,858.13	7,251.70	6,858.13	50.03	39.98	179.86	398.75	1,822.55	1,319.45	1,250.83	68.62	19.229		
7,600.00	6,958.13	7,351.70	6,958.13	50.09	40.07	179.86	398.75	1,822.55	1,319.45	1,250.64	68.81	19.175		
7,700.00	7,058.13	7,451.70	7,058.13	50.15	40.15	179.86	398.75	1,822.55	1,319.45	1,250.45	69.00	19.121		
7,800.00	7,158.13	7,551.70	7,158.13	50.22	40.23	179.86	398.75	1,822.55	1,319.45	1,250.25	69.20	19.067		
7,900.00	7,258.13	7,651.70	7,258.13	50.29	40.32	179.86	398.75	1,822.55	1,319.45	1,250.05	69.40	19.013		
8,000.00	7,358.13	7,751.70	7,358.13	50.35	40.41	179.86	398.75	1,822.55	1,319.45	1,249.85	69.60	18.958		
8,100.00	7,458.13	7,851.70	7,458.13	50.42	40.49	179.86	398.75	1,822.55	1,319.45	1,249.65	69.80	18.902		
8,136.97	7,495.10	7,888.67	7,495.10	50.45	40.53	179.86	398.75	1,822.55	1,319.45	1,249.57	69.88	18.882		
8,182.87	7,541.00	7,901.58	7,508.00	50.48	40.54	179.86	398.75	1,822.55	1,319.86	1,249.92	69.94	18.870		

Company: BILL BARRETT CORP
 Project: CARBON COUNTY, UT (NAD 27)
 Reference Site: SECTION 26 T12S R16E
 Site Error: 0.00ft
 Reference Well: PETERS POINT UF 10-26D-12-16
 Well Error: 0.00ft
 Reference Wellbore: PT PT 10-26-12-16
 Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
 TVD Reference: WELL @ 7177.00ft (Original Well Elev)
 MD Reference: WELL @ 7177.00ft (Original Well Elev)
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Output errors are at: 2.00 sigma
 Database: Compass
 Offset TVD Reference: Offset Datum

Reference Depths are relative to WELL @ 7177.00ft (Original Well Elev)
 Offset Depths are relative to Offset Datum
 Central Meridian is 111° 30' 0.0000 W°

Coordinates are relative to: PETERS POINT UF 10-26D-12-16
 Coordinate System is US State Plane 1927 (Exact solution), Utah Central 4302
 Grid Convergence at Surface is: 0.90°

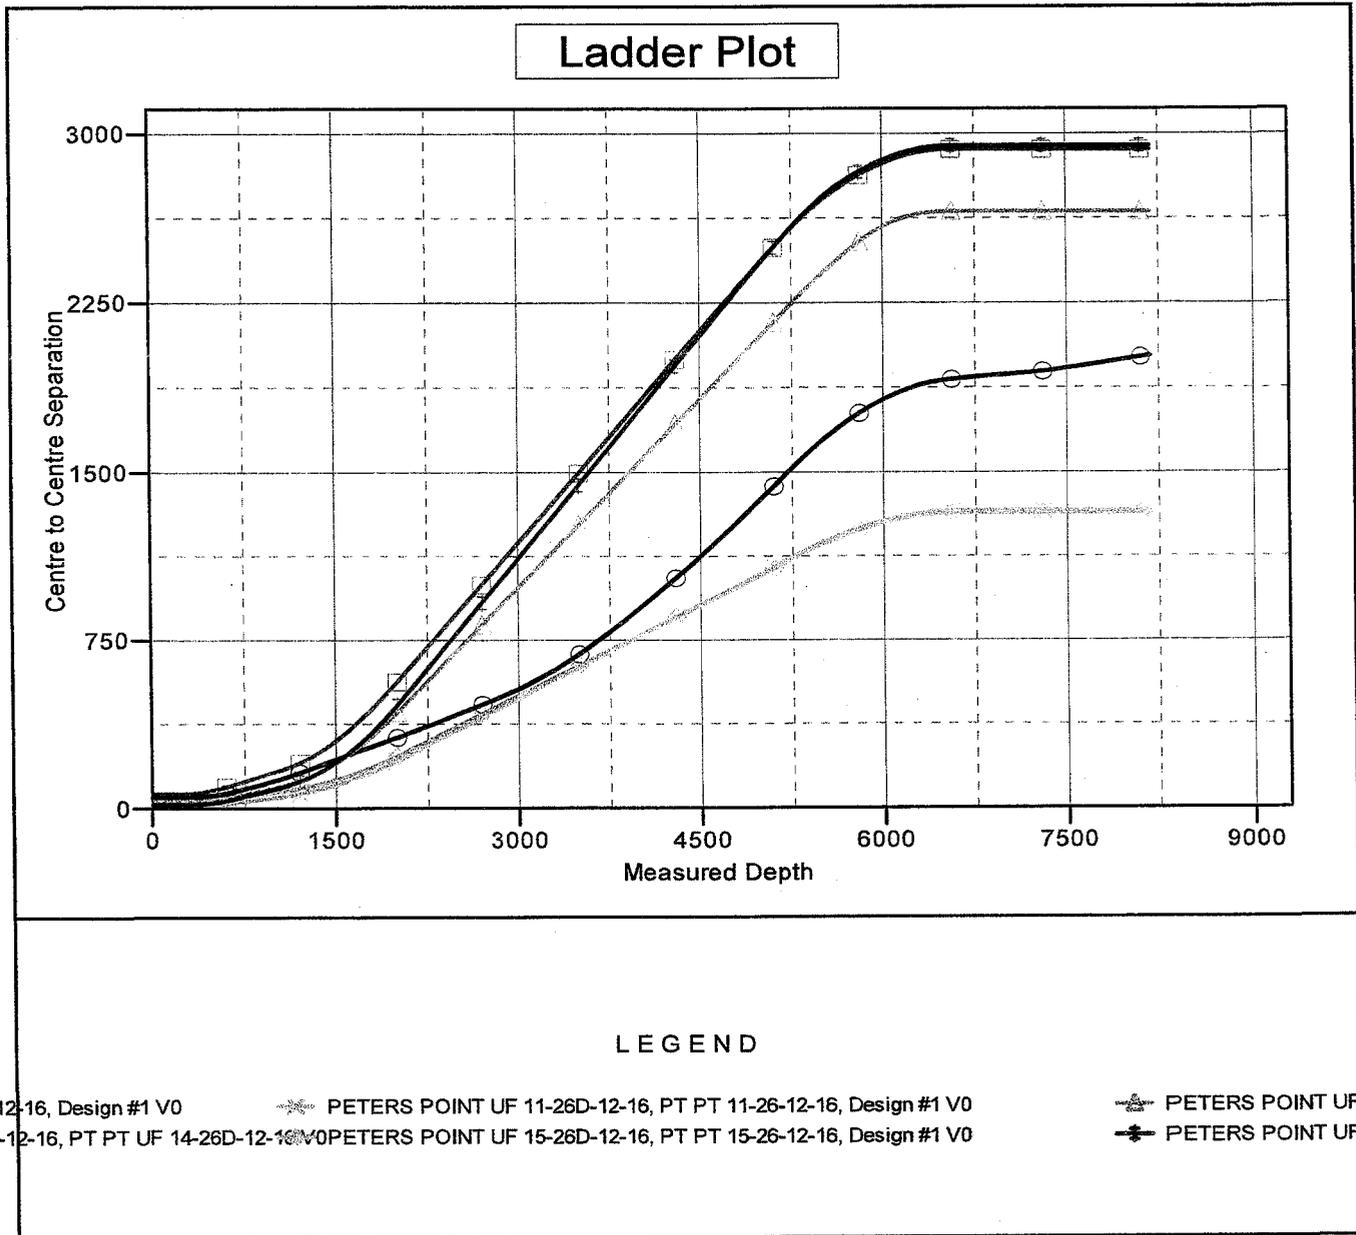


Company: BILL BARRETT CORP
 Project: CARBON COUNTY, UT (NAD 27)
 Reference Site: SECTION 26 T12S R16E
 Site Error: 0.00ft
 Reference Well: PETERS POINT UF 10-26D-12-16
 Well Error: 0.00ft
 Reference Wellbore: PT PT 10-26-12-16
 Reference Design: Design #1

Local Co-ordinate Reference: Well PETERS POINT UF 10-26D-12-16
 TVD Reference: WELL @ 7177.00ft (Original Well Elev)
 MD Reference: WELL @ 7177.00ft (Original Well Elev)
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Output errors are at: 2.00 sigma
 Database: Compass
 Offset TVD Reference: Offset Datum

Reference Depths are relative to WELL @ 7177.00ft (Original Well Elev)
 Offset Depths are relative to Offset Datum
 Central Meridian is 111° 30' 0.0000 W°

Coordinates are relative to: PETERS POINT UF 10-26D-12-16
 Coordinate System is US State Plane 1927 (Exact solution), Utah Central 4302
 Grid Convergence at Surface is: 0.90°

Separation Factor Plot

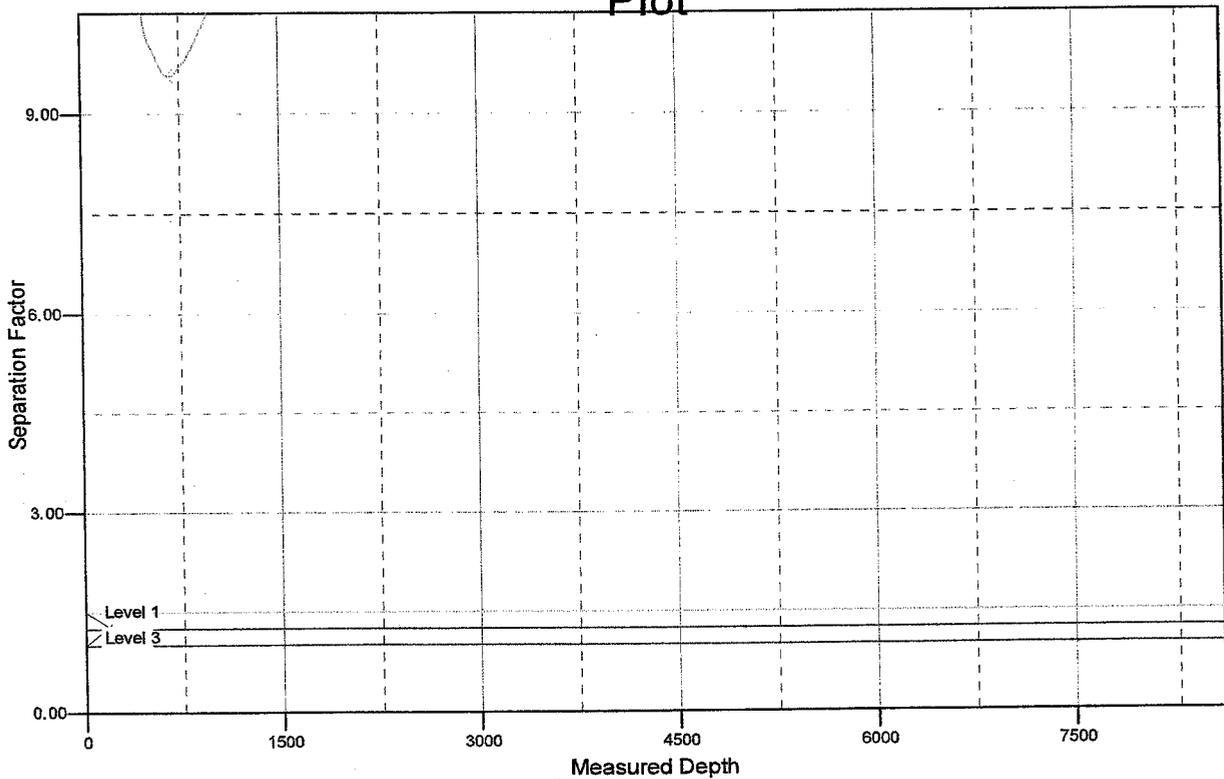

LEGEND

12-16, Design #1 V0 PETERS POINT UF 11-26D-12-16, PT PT 11-26-12-16, Design #1 V0 PETERS POINT UF 1:
 -12-16, PT PT UF 14-26D-12-16 V0 PETERS POINT UF 15-26D-12-16, PT PT 15-26-12-16, Design #1 V0 PETERS POINT UF 1:

PRESSURE CONTROL EQUIPMENT – Schematic Attached

A. Type: Eleven (11) Inch Double Gate Hydraulic BOP with Eleven (11) Inch Annular Preventer. The blow out preventer will be equipped as follows:

1. One (1) blind ram (above).
2. One (1) pipe ram (below).
3. Drilling spool with two (2) side outlets (choke side 3-inch minimum, kill side 2-inch minimum).
4. 3-inch diameter choke line.
5. Two (2) choke line valves (3-inch minimum).
6. Kill line (2-inch minimum).
7. Two (2) chokes.
8. Two (2) kill line valves, one of which shall be a check valve (2-inch minimum).
9. Upper kelly cock valve with handles available.
10. Safety valve(s) & subs to fit all drill string connections in use.
11. Pressure gauge on choke manifold.
12. Fill-up line above the uppermost preventer.

B. Pressure Rating: 3,000 psi

C. Testing Procedure:

Annular Preventer

At a minimum, the Annular Preventer will be pressure tested to 50% of the rated working pressure for a period of ten (10) minutes or until provisions of the test are met, whichever is longer.

At a minimum the above pressure test will be performed:

1. When the annular preventer is initially installed;
2. Whenever any seal subject to test pressure is broken;
3. Following related repairs; and
4. At thirty (30) day intervals.

In addition, the Annular Preventer will be functionally operated at least weekly.

Blow-Out Preventer

At a minimum, the BOP, choke manifold, and related equipment will be pressure tested to the approved working pressure of the BOP stack (if isolated from the surface casing by a test plug) or to 70% of the internal yield strength of the surface casing (if the BOP is not isolated from the casing by a test plug). Pressure will be

maintained for a period of at least ten (10) minutes or until the requirements of the test are met, whichever is longer.

At a minimum, the above pressure test will be performed:

1. When the BOP is initially installed;
2. Whenever any seal subject to test pressure is broken;
3. Following related repairs; and
4. At thirty (30) day intervals.

In addition the pipe and blind rams will be activated each trip, but not more than once each day. All BOP drills and tests will be recorded in the IADC driller's log.

D. Choke Manifold Equipment:

All choke lines will be straight lines unless turns use tee blocks or are targeted with running tees, and will be anchored to prevent whip and vibration.

E. Accumulator:

The accumulator will have sufficient capacity to open the hydraulically-controlled choke line valve (if so equipped), close all rams plus the annular preventer, and retain a minimum of 200 psi above precharge on the closing manifold without the use of closing unit pumps. The fluid reservoir capacity will be double the usable fluid volume of the accumulator system capacity and the fluid level of the reservoir will be maintained at the manufacturer's recommendations.

The BOP system will have two (2) independent power sources to close the preventers. Nitrogen bottles (3 minimum) will be one (1) of these independent power sources and will maintain a charge equal to the manufacturer's specifications.

The accumulator precharge pressure test will be conducted prior to connecting the closing unit to the BOP stack and at least once every six (6) months thereafter. The accumulator pressure will be corrected if the measured precharge pressure is found to be above or below the maximum or minimum limits specified in the *Onshore Oil & Gas Order Number 2*.

A manual locking device (i.e. hand wheels) or automatic locking device will be installed on all systems of 2M or greater. A valve will be installed in the closing line as close as possible to the annular preventer to act as a locking device. This valve will be maintained in the open position and will be closed only when the power source for the accumulator is inoperative.

BILL BARRETT CORPORATION
PRICKLY PEAR UNIT FEDERAL #3-35D-12-16,
#15-26D-12-16, #13-26D-12-16, #11-26D-12-16,
#12-26D-12-16 & #10-26D-12-16
SECTION 26, T12S, R16E, S.L.B.&M.

PROCEED IN A SOUTHWESTERLY DIRECTION FROM MYTON, UTAH ALONG U.S. HIGHWAY 40 APPROXIMATELY 1.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTH; TURN LEFT AND PROCEED IN A SOUTHERLY, THEN SOUTHWESTERLY, THEN SOUTHERLY DIRECTION APPROXIMATELY 1.5 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTHWEST; TURN RIGHT AND PROCEED IN A SOUTHWESTERLY DIRECTION APPROXIMATELY 31.8 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTHEAST; TURN LEFT AND PROCEED IN A SOUTHEASTERLY DIRECTION APPROXIMATELY 6.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTH; TURN RIGHT AND PROCEED IN A SOUTHWESTERLY, THEN SOUTHEASTERLY, THEN SOUTHWESTERLY DIRECTION APPROXIMATELY 7.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE EAST; TURN LEFT AND PROCEED IN A EASTERLY, THEN SOUTHEASTERLY DIRECTION APPROXIMATELY 1.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE NORTHEAST; TURN LEFT AND PROCEED IN A NORTHEASTERLY DIRECTION APPROXIMATELY 3.1 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE EAST; TURN RIGHT AND PROCEED IN AN EASTERLY DIRECTION APPROXIMATELY 100' TO THE EXISTING ACCESS TO THE SOUTHEAST; TURN RIGHT AND PROCEED IN A SOUTHEASTERLY, THEN EASTERLY, THEN NORTHEASTERLY, THEN SOUTHEASTERLY DIRECTION APPROXIMATELY 0.4 MILES TO THE LOCATION.

TOTAL DISTANCE FROM MYTON, UTAH TO THE PROPOSED WELL LOCATION IS APPROXIMATELY 50.5 MILES.

BILL BARRETT CORPORATION

PETERS POINT UNIT FEDERAL #3-35D-12-16,
 #15-26D-12-16, #13-26D-12-16, #11-26D-12-16,
 #12-26D-12-16 & #10-26D-12-16

LOCATED IN CARBON COUNTY, UTAH
 SECTION 26, T12S, R16E, S.L.B.&M.

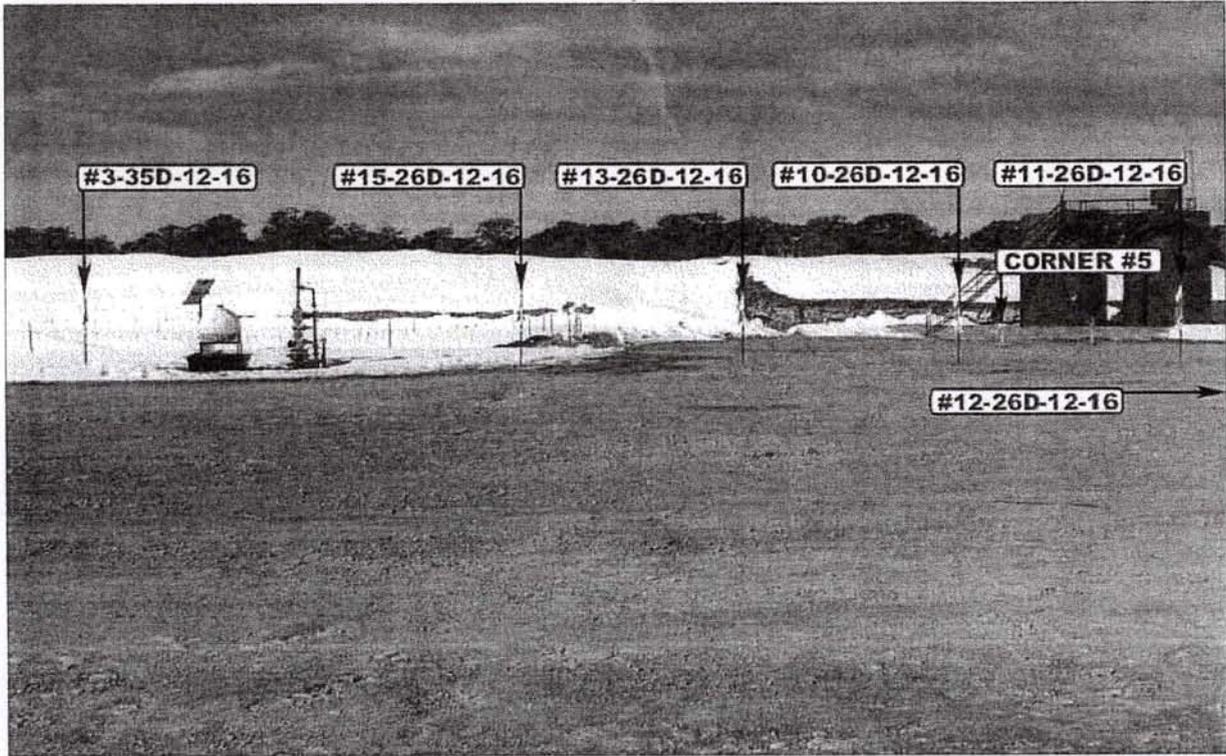


PHOTO: VIEW FROM LOCATION STAKES TO CORNER #5

CAMERA ANGLE: SOUTHWESTERLY



PHOTO: VIEW OF EXISTING ACCESS

CAMERA ANGLE: SOUTHERLY



- Since 1964 -

UELS Uintah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 435-789-1017 uels@uelsinc.com


LOCATION PHOTOS	3	25	08	PHOTO
	MONTH	DAY	YEAR	
TAKEN BY: D.R.	DRAWN BY: GL.	REVISED: 3-25-08		

BILL BARRETT CORPORATION

LOCATION LAYOUT FOR

PETER'S POINT UNIT FEDERAL #3-35D-12-16, #15-26D-12-16,
 #13-26D-12-16, #10-26D-12-16, #11-26D-12-16 & #12-26D-12-16
 SECTION 26, T12S, R16E, S.L.B.&M.
 SE 1/4 SW 1/4

FIGURE #1

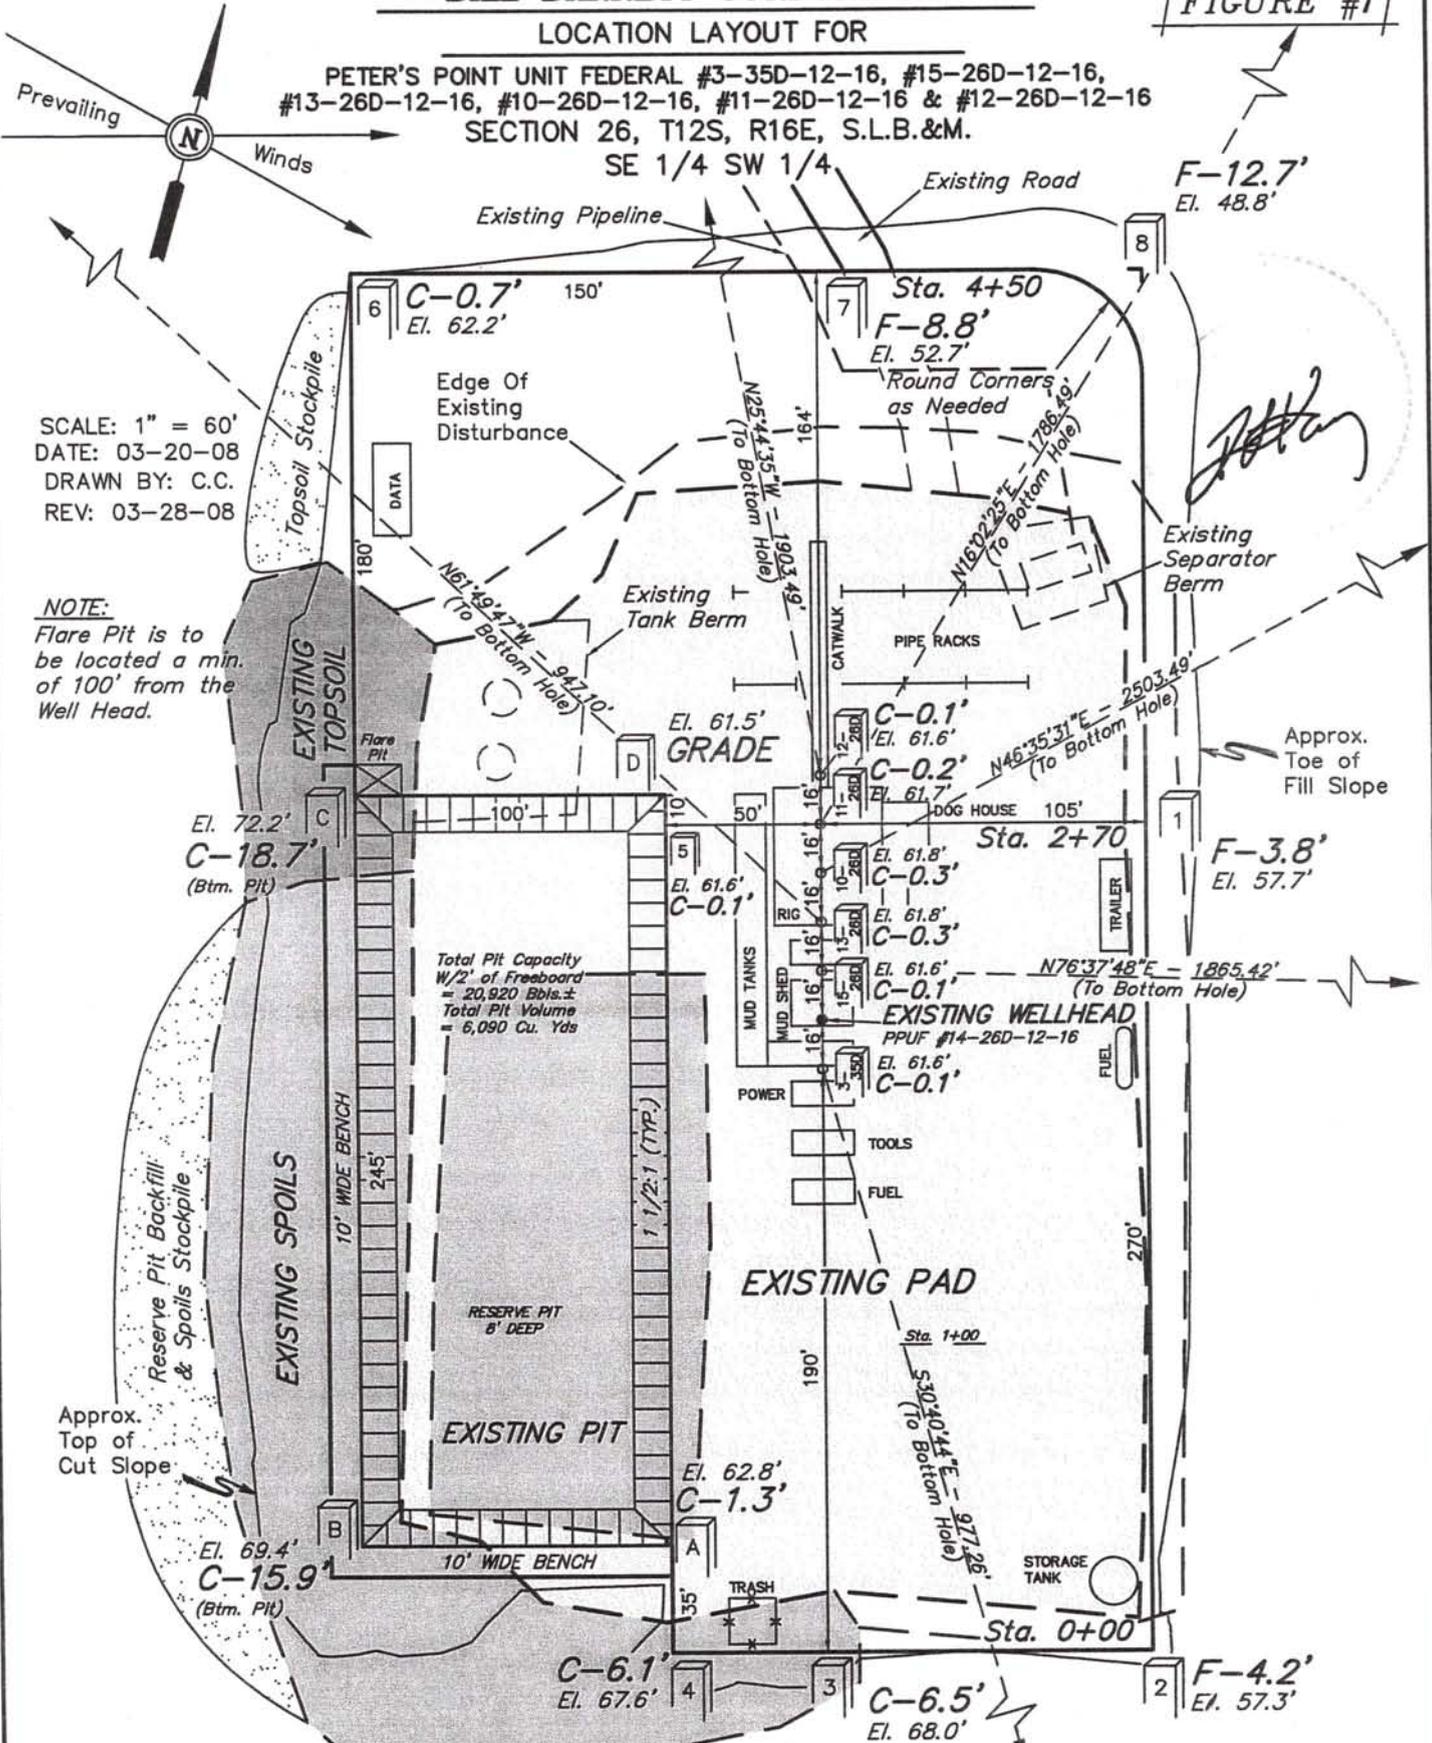

SCALE: 1" = 60'
 DATE: 03-20-08
 DRAWN BY: C.C.
 REV: 03-28-08

NOTE:
 Flare Pit is to be located a min. of 100' from the Well Head.

Total Pit Capacity
 W/2' of Freeboard
 = 20,920 Bbls.±
 Total Pit Volume
 = 6,090 Cu. Yds

Elev. Ungraded Ground at #12-26D Location Stake = 7161.7'
 Elev. Graded Ground at #12-26D Location Stake = 7161.5'

UINTAH ENGINEERING & LAND SURVEYING
 85 So. 200 East * Vernal, Utah 84078 * (435) 789-1017

BILL BARRETT CORPORATION


FIGURE #2

TYPICAL CROSS SECTIONS FOR

**PETER'S POINT UNIT FEDERAL #3-35D-12-16, #15-26D-12-16,
#13-26D-12-16, #10-26D-12-16, #11-26D-12-16 & #12-26D-12-16
SECTION 26, T12S, R16E, S.L.B.&M.
SE 1/4 SW 1/4**

1" = 40'
X-Section
Scale
1" = 100'

DATE: 03-20-08
DRAWN BY: C.C.
REV: 03-28-08

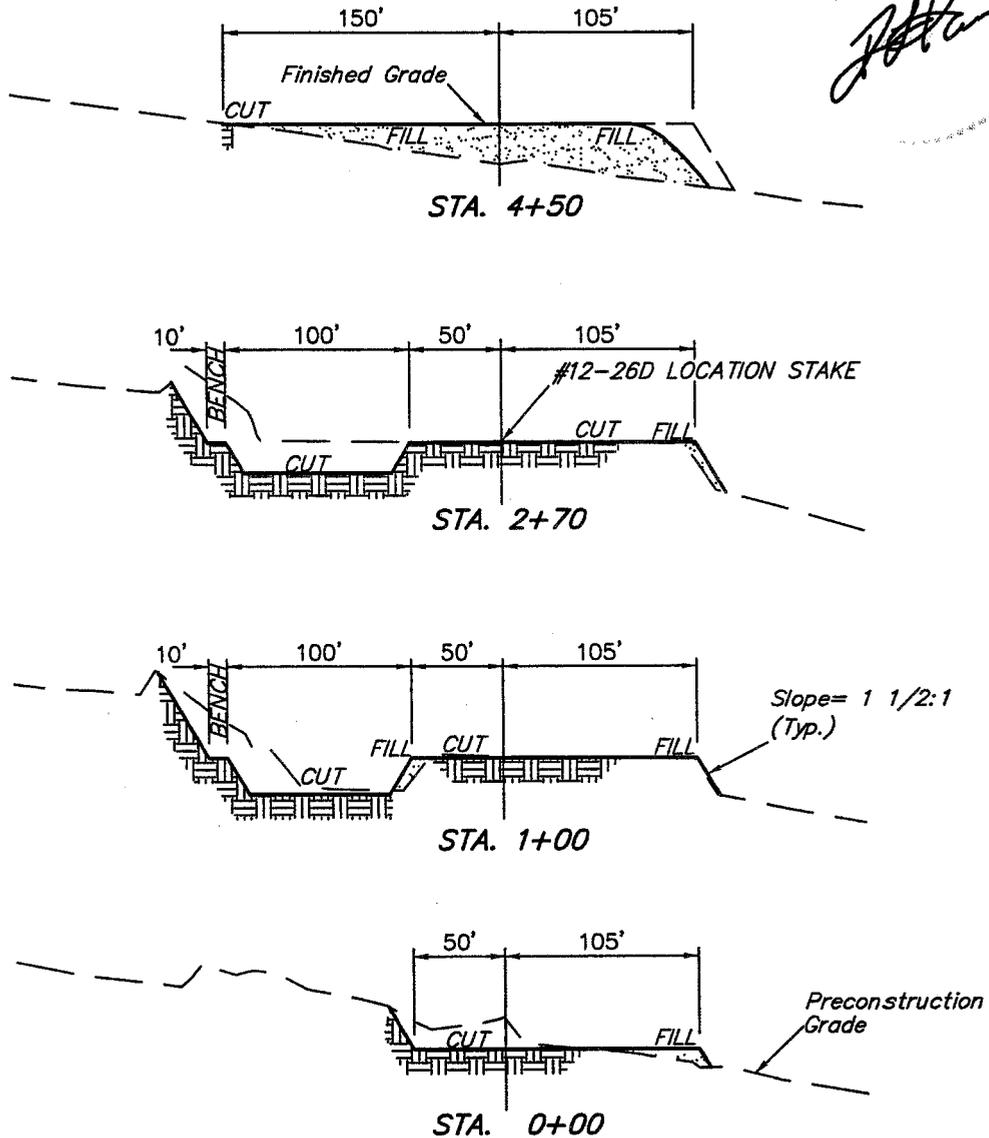

APPROXIMATE ACREAGES

EXISTING DISTURBANCE = ±2.817 ACRES
NEW DISTURBANCE = ±0.753 ACRES
TOTAL = ±3.570 ACRES


* NOTE:
FILL QUANTITY INCLUDES
5% FOR COMPACTION

APPROXIMATE YARDAGES

(6") Topsoil Stripping = 640 Cu. Yds.
(New Construction Only)
Remaining Location = 9,300 Cu. Yds.
TOTAL CUT = 9,940 CU.YDS.
FILL = 4,940 CU.YDS.

EXCESS MATERIAL = 5,000 Cu. Yds.
Topsoil & Pit Backfill = 3,690 Cu. Yds.
(1/2 Pit Vol.)
EXCESS UNBALANCE = 1,310 Cu. Yds.
(After Interim Rehabilitation)

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East * Vernal, Utah 84078 * (435) 789-1017

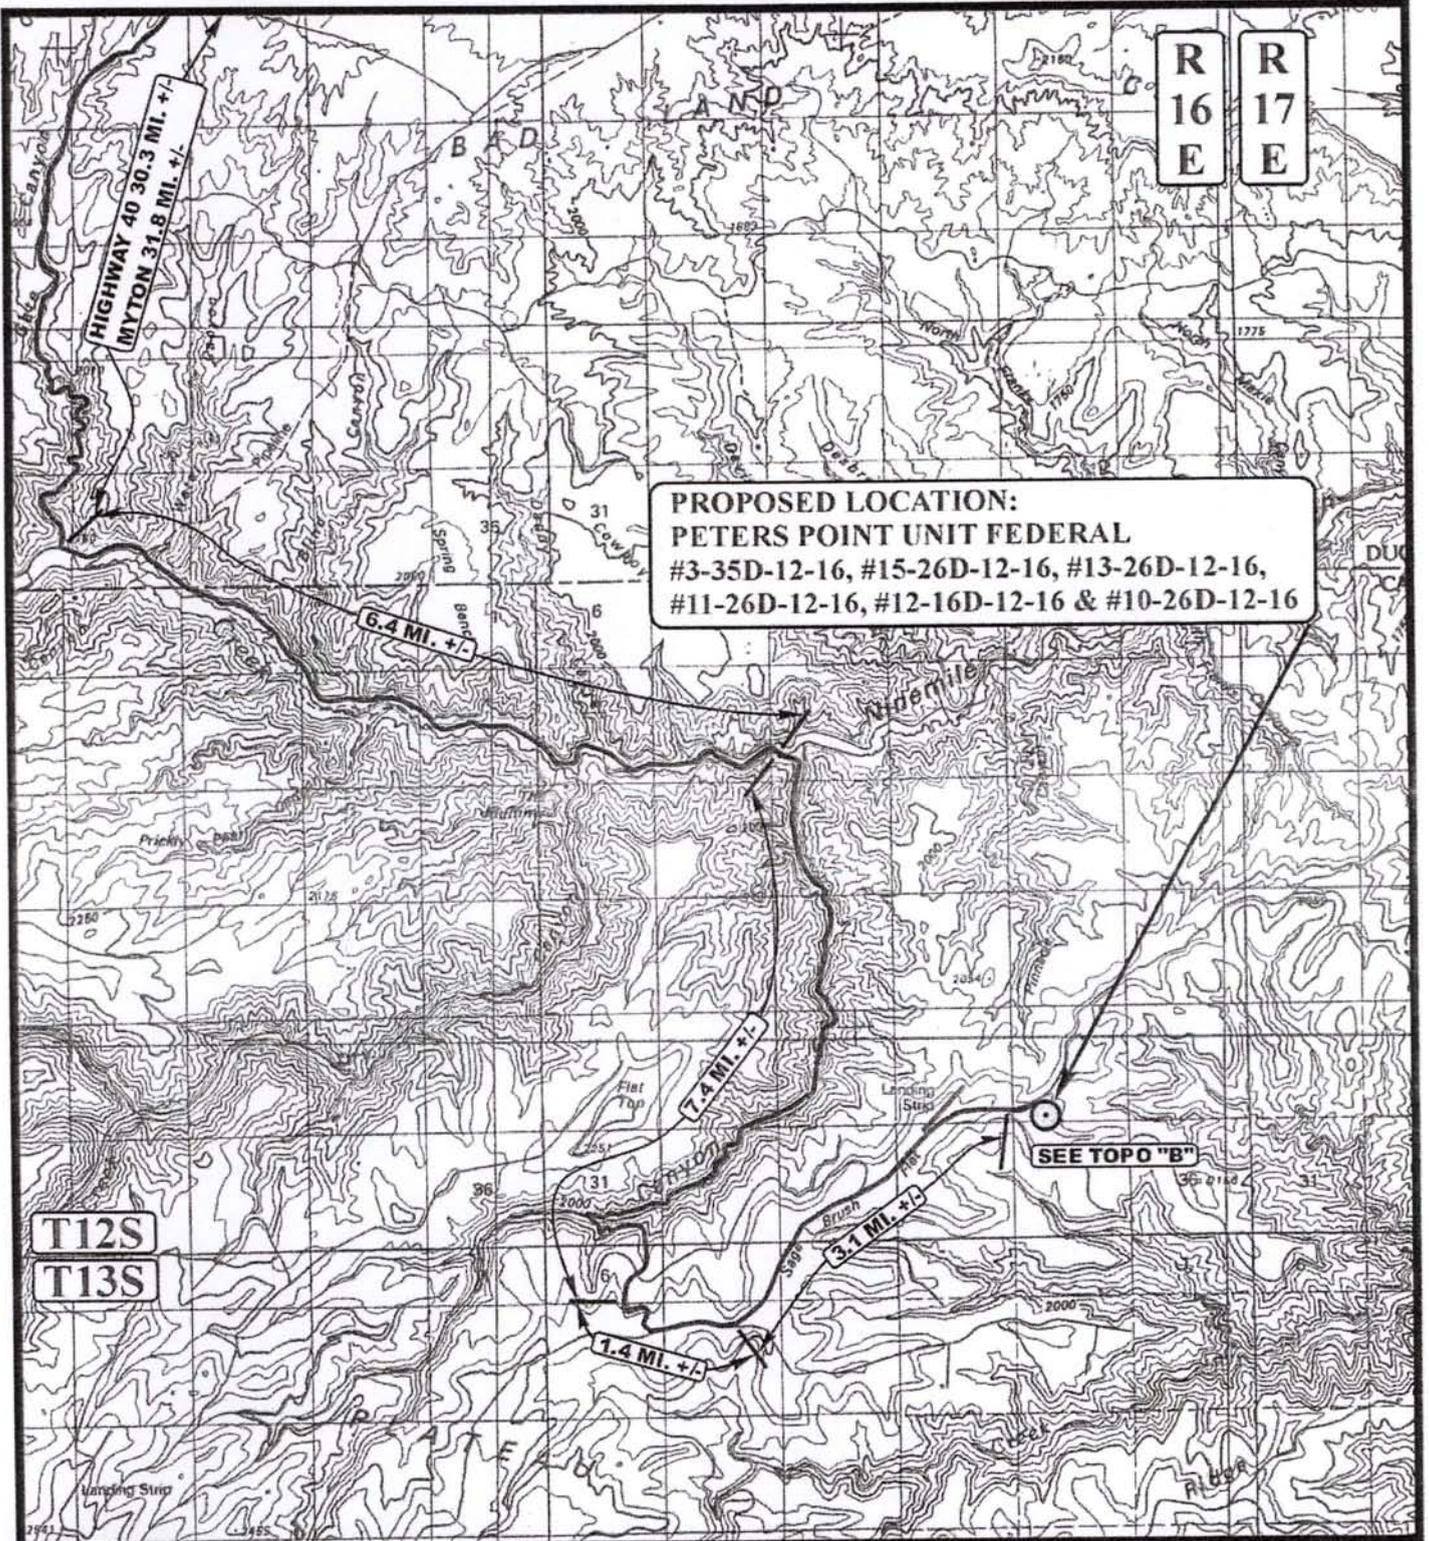

PROPOSED LOCATION:
PETERS POINT UNIT FEDERAL
 #3-35D-12-16, #15-26D-12-16, #13-26D-12-16,
 #11-26D-12-16, #12-16D-12-16 & #10-26D-12-16

T12S
 T13S

LEGEND:

○ PROPOSED LOCATION

BILL BARRETT CORPORATION

PETERS POINT UNIT FEDERAL #3-35D-12-16, #15-26D-12-16,
 #13-26D-12-16, #11-26D-12-16, #12-26D-12-16 & #10-26D-12-16
 SECTION 26, T12S, R16E, S.L.B.&M.
 SE 1/4 SW 1/4


U&Ls Uintah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 (435) 789-1017 * FAX (435) 789-1813



TOPOGRAPHIC MAP
 SCALE: 1:100,000 DRAWN BY: GL REVISED: 3-25-08
 3 25 08
 MONTH DAY YEAR



R
16
E

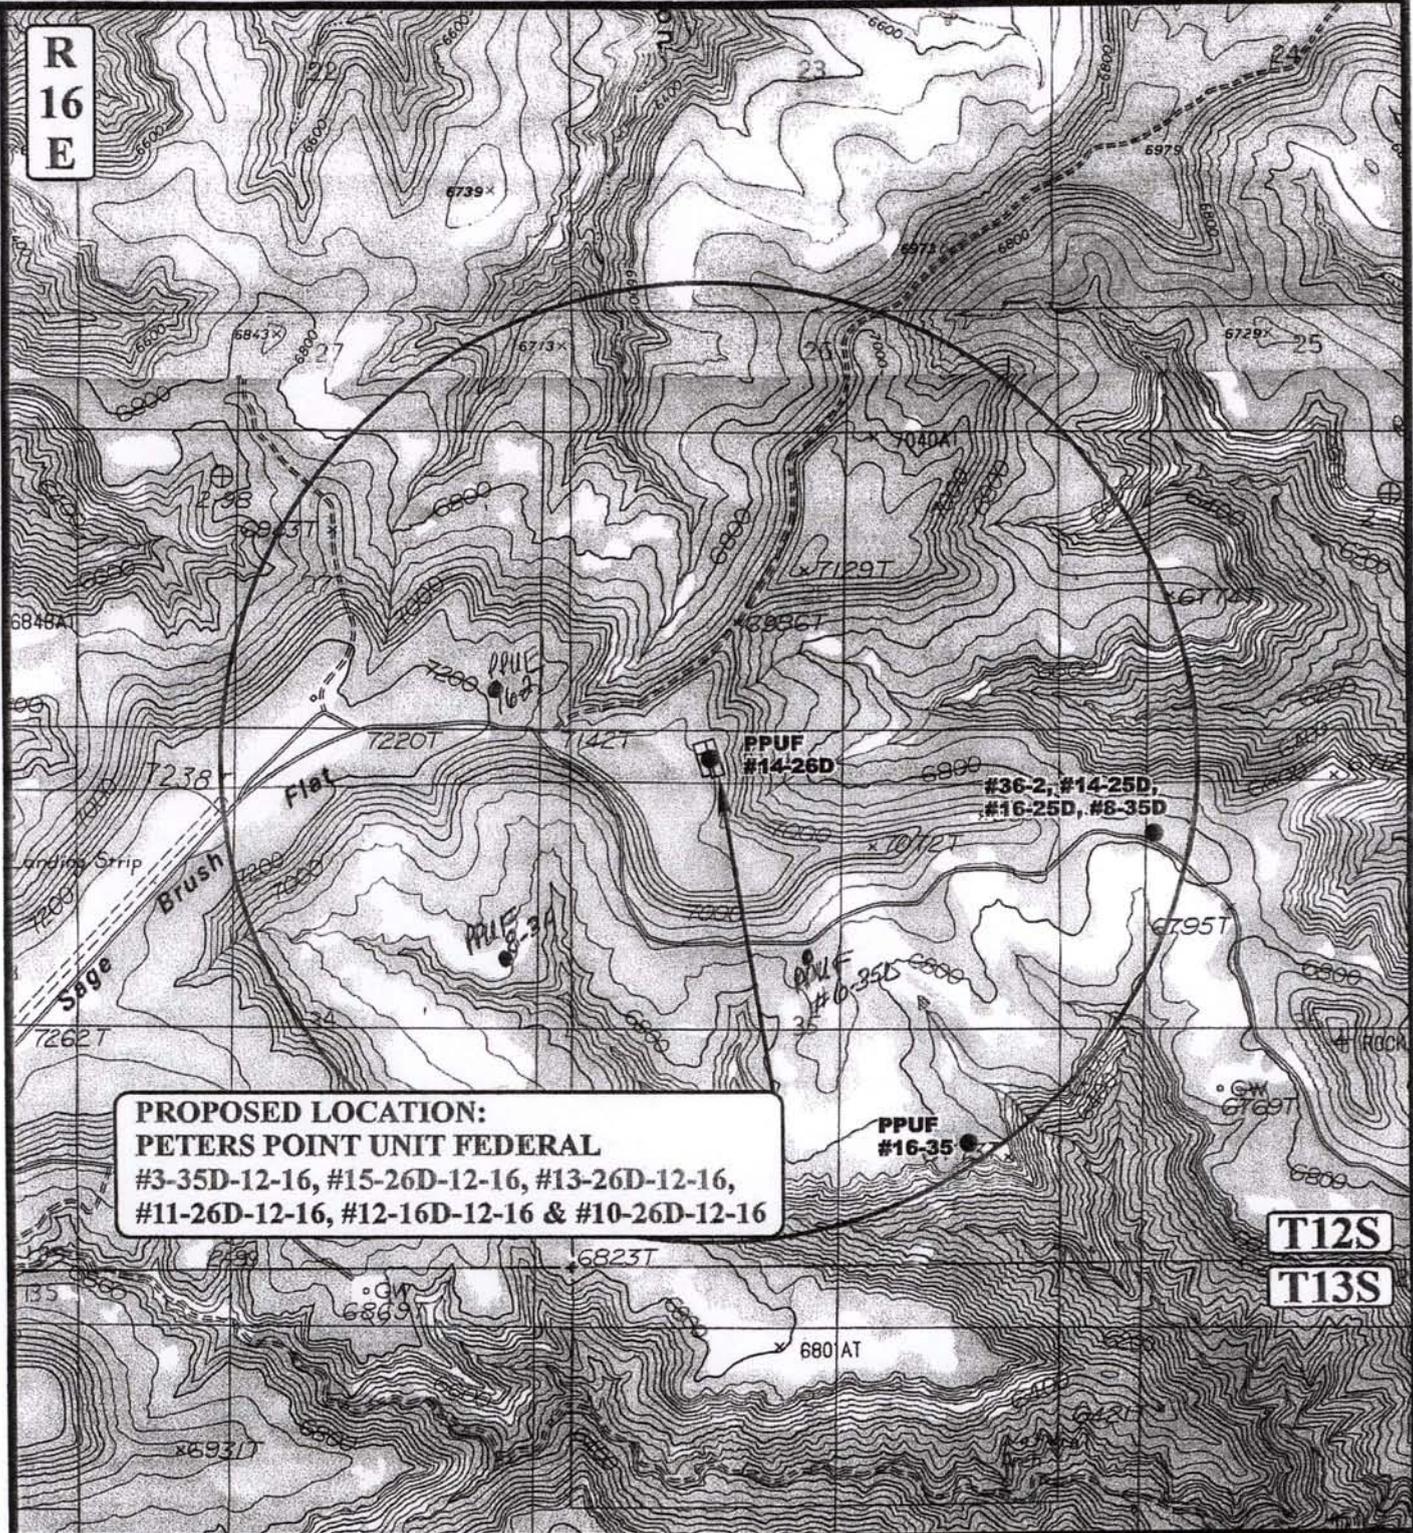

PROPOSED LOCATION:
PETERS POINT UNIT FEDERAL
 #3-35D-12-16, #15-26D-12-16, #13-26D-12-16,
 #11-26D-12-16, #12-16D-12-16 & #10-26D-12-16

T12S
T13S

LEGEND:

- DISPOSAL WELLS
- PRODUCING WELLS
- SHUT IN WELLS
- WATER WELLS
- ABANDONED WELLS
- TEMPORARILY ABANDONED

BILL BARRETT CORPORATION

PETERS POINT UNIT FEDERAL #3-35D-12-16, #15-26D-12-16,
 #13-26D-12-16, #11-26D-12-16, #12-26D-12-16 & #10-26D-12-16
 SECTION 26, T12S, R16E, S.L.R.&M.
 SE 1/4 SW 1/4



Utah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 (435) 789-1017 * FAX (435) 789-1813



TOPOGRAPHIC MAP
 3 25 08
 MONTH DAY YEAR
 SCALE: 1" = 2000' DRAWN BY: GL. REVISED: 3-25-08



OPERATOR CERTIFICATION

Certification:

I hereby certify that I, or someone under my direction supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein would be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filings of false statements.

Executed this 23rd day of April 2008
Name: Tracey Fallang
Position Title: Regulatory Analyst
Address: 1099 18th Street, Suite 2300, Denver, CO 80202
Telephone: 303-312-8134
Field Representative Fred Goodrich
Address: 1820 W. Hwy 40, Roosevelt, UT 84066
Telephone: 435-725-3515
E-mail: _____

Tracey Fallang
Tracey Fallang, Environmental/Regulatory Analyst

**WORKSHEET
APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 04/28/2008

API NO. ASSIGNED: 43-007-31406

WELL NAME: PPU FED 10-26D-12-16
 OPERATOR: BILL BARRETT CORP (N2165)
 CONTACT: TRACEY FALLANG

PHONE NUMBER: 303-312-8134

PROPOSED LOCATION:

INSPECT LOCATN BY: / /		
Tech Review	Initials	Date
Engineering		
Geology		
Surface		

NWSE

SESW 26 120S 160E
 SURFACE: 0270 FSL 15#0 FWL
 BOTTOM: 1991 FSL 1950 FEL
 COUNTY: CARBON
 LATITUDE: 39.73828 LONGITUDE: -110.0948
 UTM SURF EASTINGS: 577562 NORTHINGS: 4398892
 FIELD NAME: PETER'S POINT (40)

LEASE TYPE: 1 - Federal
 LEASE NUMBER: UTU-0681
 SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: WSMVD
 COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:

- Plat
- Bond: Fed[1] Ind[] Sta[] Fee[]
(No. WYB000040)
- Potash (Y/N)
- Oil Shale 190-5 (B) or 190-3 or 190-13
- Water Permit
(No. 90-1853)
- RDCC Review (Y/N)
(Date: _____)
- Fee Surf Agreement (Y/N)
- Intent to Commingle (Y/N)

LOCATION AND SITING:

- ___ R649-2-3.
- Unit: PETERS POINT
- ___ R649-3-2. General
Siting: 460 From Qtr/Qtr & 920' Between Wells
- ___ R649-3-3. Exception
- Drilling Unit
Board Cause No: 157-03
Eff Date: 5-29-2001
Siting: Well must be at least 400' from ext bdr
- R649-3-11. Directional Drill


COMMENTS: _____

STIPULATIONS: 1. Federal Approval

T12S R16E

22

23

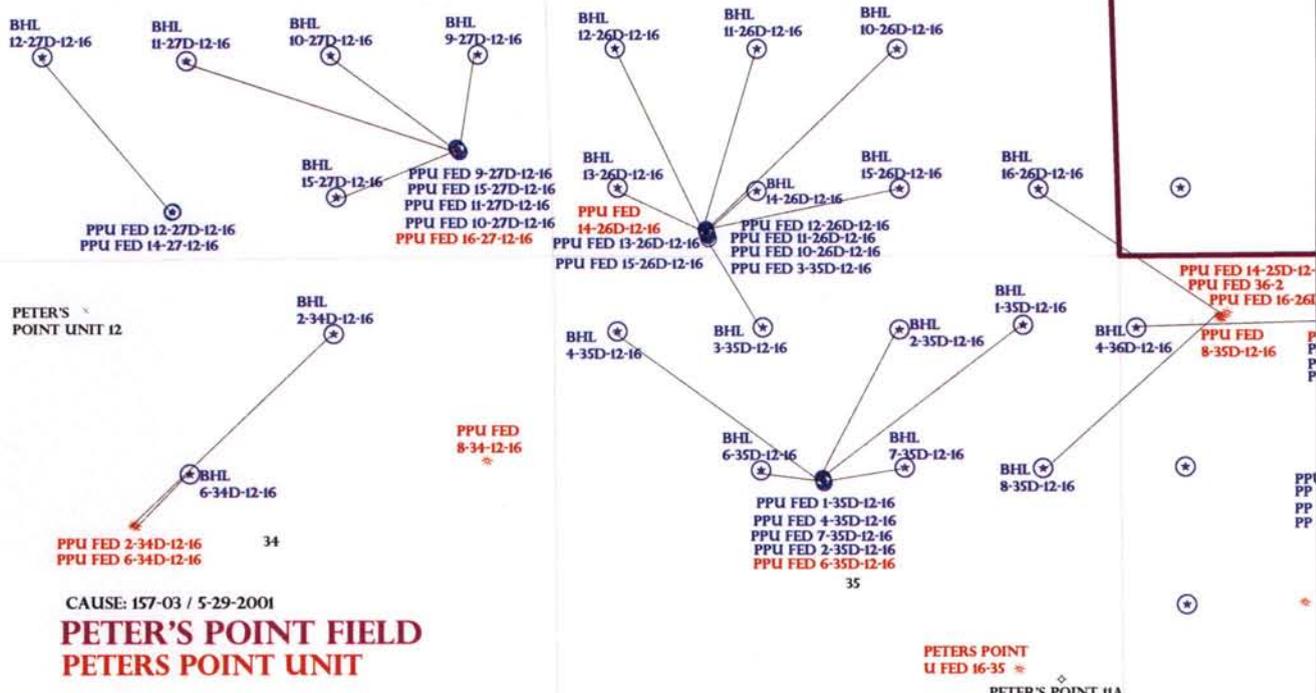

OPERATOR: BILL BARRETT CORP (N2165)

SEC: 26,27 T.12S R. 16E

FIELD: PETERS POINT (40)

COUNTY: CARBON

CAUSE: 157-03 / 5-29-2001

- Wells Status**
- ⊗ GAS INJECTION
 - ⊗ GAS STORAGE
 - ⊗ LOCATION ABANDONED
 - ⊗ NEW LOCATION
 - ⊗ PLUGGED & ABANDONED
 - ⊗ PRODUCING GAS
 - ⊗ PRODUCING OIL
 - ⊗ SHUT-IN GAS
 - ⊗ SHUT-IN OIL
 - ⊗ TEMP. ABANDONED
 - ⊗ TEST WELL
 - ⊗ WATER INJECTION
 - ⊗ WATER SUPPLY
 - ⊗ WATER DISPOSAL
 - ⊗ DRILLING

- Field Status**
- ⬜ ABANDONED
 - ⬜ ACTIVE
 - ⬜ COMBINED
 - ⬜ INACTIVE
 - ⬜ PROPOSED
 - ⬜ STORAGE
 - ⬜ TERMINATED

- Unit Status**
- ⬜ EXPLORATORY
 - ⬜ GAS STORAGE
 - ⬜ NF PP OIL
 - ⬜ NF SECONDARY
 - ⬜ PENDING
 - ⬜ PI OIL
 - ⬜ PP GAS
 - ⬜ PP GEOTHERML
 - ⬜ PP OIL
 - ⬜ SECONDARY
 - ⬜ TERMINATED



OIL, GAS & MINING



PREPARED BY: DIANA MASON
DATE: 01-MAY-2008

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office

P.O. Box 45155

Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:

3160

(UT-922)

May 1, 2008

Memorandum

To: Assistant Field Office Manager Resources,
Moab Field Office

From: Michael Coulthard, Petroleum Engineer

Subject: 2008 Plan of Development Peter's Point Unit
Carbon County, Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2008 within the Peter's Point Unit, Carbon County, Utah.

API#	WELL NAME	LOCATION
------	-----------	----------

(Proposed PZ Wasatch/MesaVerde)

43-007-31406	PPU Fed 10-26D-12-16	Sec 26 T12S R16E 0270 FSL 1540 FWL
		BHL Sec 26 T12S R16E 1991 FSL 1950 FEL

43-007-31409	PPU Fed 11-27D-12-16	Sec 27 T12S R16E 1088 FSL 0819 FEL
		BHL 1929 FSL 1993 FWL

This office has no objection to permitting the wells at this time.

/s/ Michael L. Coulthard

bcc: File - Peter's Point Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:5-1-08



JON M. HUNTSMAN, JR.
Governor

GARY R. HERBERT
Lieutenant Governor

State of Utah
DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

May 5, 2008

Bill Barrett Corporation
1099 18th St., Ste. 2300
Denver, CO 80202

Re: Peter's Point Unit Federal 10-26D-12-16 Well, Surface Location 270' FSL, 1510' FWL, SE SW, Sec. 26, T. 12 South, R. 16 East, Bottom Location 1991' FSL, 1950' FEL, NW SE, Sec. 26, T. 12 South, R. 16 East, Carbon County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-007-31406.

Sincerely,

Gil Hunt
Associate Director

pab
Enclosures

cc: Carbon County Assessor
Bureau of Land Management, Moab Office

Operator: Bill Barrett Corporation

Well Name & Number Peter's Point Unit Federal 10-26D-12-16

API Number: 43-007-31406

Lease: UTU-0681

Surface Location: SE SW Sec. 26 T. 12 South R. 16 East

Bottom Location: NW SE Sec. 26 T. 12 South R. 16 East

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

2. Notification Requirements

Notify the Division within 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dustin Doucet at (801) 538-5281 (801) 733-0983 home

3. Reporting Requirements

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.
5. In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

CONFIDENTIAL

COPY

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No. UTU-0681	
6. If Indian, Allottee or Tribe Name N/A	
7. If Unit or CA Agreement, Name and No. Peters Point / UTU-63014	
8. Lease Name and Well No. Peter's Point Unit Federal 10-26D-12-16	
9. API Well No. pending 43007-31406	
10. Field and Pool, or Exploratory Peter's Point/Wasatch-Mesaverde	11. Sec., T. R. M. or Blk. and Survey or Area Sec. 26, T12S-R16E
12. County or Parish Carbon County	13. State UT
14. Distance in miles and direction from nearest town or post office* approximately 51 miles from Myton, Utah	15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 270' SH / 646' BH
16. No. of acres in lease 1598.62	17. Spacing Unit dedicated to this well 40 acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. 16' SH / 1317' BH	19. Proposed Depth 8400' MD
20. BLM/BIA Bond No. on file Nationwide Bond #WYB000040	21. Elevations (Show whether DF, KDB, RT, GL, etc.) 7162' graded ground
22. Approximate date work will start* 09/01/2008	23. Estimated duration 45 days

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

25. Signature <i>Tracey Fallang</i>	Name (Printed/Typed) Tracey Fallang	Date 04/23/2008
--	--	--------------------

Title
Environmental/Regulatory Analyst

Approved by (Signature) <i>/s/ Michael Stiewig</i>	Name (Printed/Typed)	Date JUN 20 2008
---	----------------------	----------------------------

Title <i>Acting Field Manager</i>	Office PRICE FIELD OFFICE
--------------------------------------	------------------------------

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

CONDITIONS OF APPROVAL ENFORCED

JUN 26 2008


DIV. OF OIL, GAS & MINING UBOGM

2008 APR 28 PM 12:02
PRICE FIELD OFFICE
RECEIVED

T12S, R16E, S.L.B.&M.

N89°22'W - 2629.44' (G.L.O.)

N89°50'W - 2629.44' (G.L.O.)

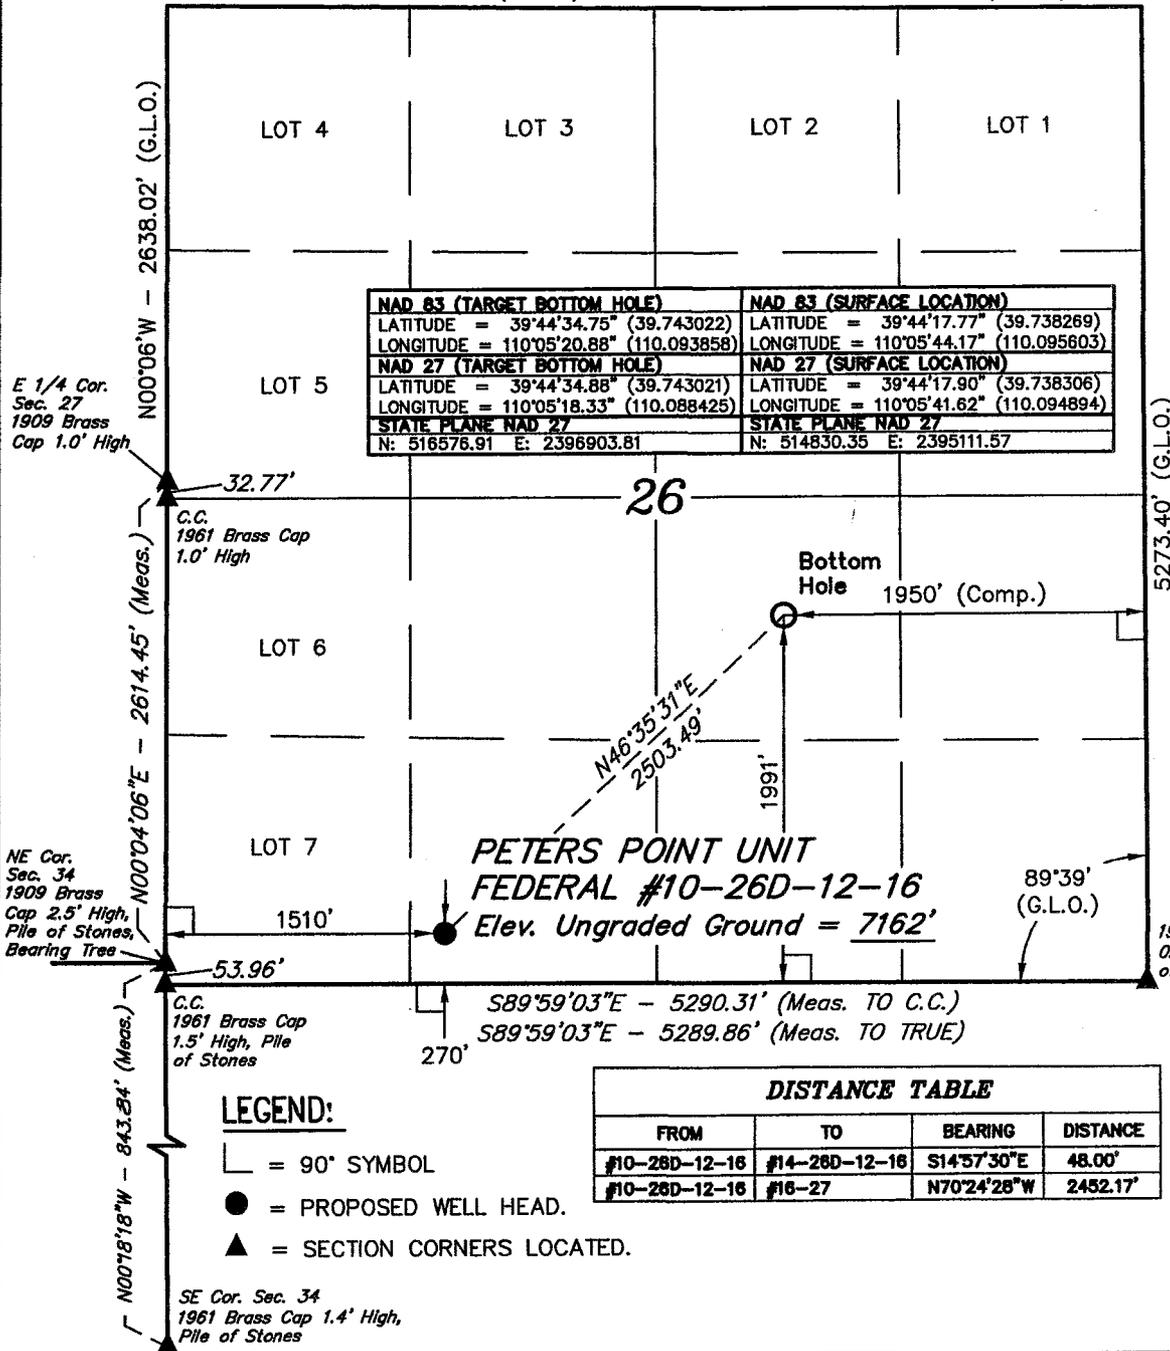

NAD 83 (TARGET BOTTOM HOLE)		NAD 83 (SURFACE LOCATION)	
LATITUDE = 39°44'34.75" (39.743022)		LATITUDE = 39°44'17.77" (39.738269)	
LONGITUDE = 110°05'20.88" (110.093858)		LONGITUDE = 110°05'44.17" (110.095603)	
NAD 27 (TARGET BOTTOM HOLE)		NAD 27 (SURFACE LOCATION)	
LATITUDE = 39°44'34.88" (39.743021)		LATITUDE = 39°44'17.90" (39.738306)	
LONGITUDE = 110°05'18.33" (110.088425)		LONGITUDE = 110°05'41.62" (110.094894)	
STATE PLANE NAD 27		STATE PLANE NAD 27	
N: 516576.91 E: 2396903.81		N: 514830.35 E: 2395111.57	

BILL BARRETT CORPORATION


Well location, PETERS POINT UNIT FEDERAL #10-26D-12-16, located as shown in the SE 1/4 SW 1/4 of Section 26, T12S, R16E, S.L.B.&M., Carbon County, Utah.

BASIS OF ELEVATION

COTTON TRIANGULATION STATION LOCATED IN THE NW 1/4 OF SECTION 31, T12S, R16E, S.L.B.&M., TAKEN FROM THE TWIN HOLLOW QUADRANGLE, UTAH, CARBON COUNTY, 7.5 MINUTE SERIES (TOPOGRAPHICAL MAP) PUBLISHED BY THE UNITED STATES DEPARTMENT OF THE INTERIOR, GEOLOGICAL SURVEY. SAID ELEVATION IS MARKED AS BEING 7386 FEET.

BASIS OF BEARINGS

BASIS OF BEARINGS IS A G.P.S. OBSERVATION.

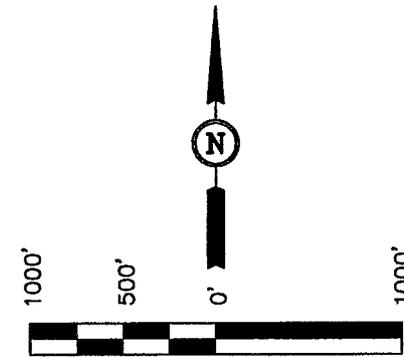

CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

Robert H. Hays
REGISTERED LAND SURVEYOR
REGISTRATION NO. 161319
STATE OF UTAH

LEGEND:

- └─┘ = 90° SYMBOL
- = PROPOSED WELL HEAD.
- ▲ = SECTION CORNERS LOCATED.

DISTANCE TABLE

FROM	TO	BEARING	DISTANCE
#10-28D-12-16	#14-28D-12-16	S14°57'30"E	48.00'
#10-28D-12-16	#16-27	N70°24'28"W	2452.17'

UINTAH ENGINEERING & LAND SURVEYING
85 SOUTH 200 EAST - VERNAL, UTAH 84078
(435) 789-1017

SCALE 1" = 1000'	DATE SURVEYED: 03-11-08	DATE DRAWN: 03-28-08
PARTY D.R. A.W. C.C.	REFERENCES G.L.O. PLAT	
WEATHER COOL	FILE BILL BARRETT CORPORATION	

BILL BARRETT CORPORATION
PRICKLY PEAR UNIT FEDERAL #3-35D-12-16,
#15-26D-12-16, #13-26D-12-16, #11-26D-12-16,
#12-26D-12-16 & #10-26D-12-16
SECTION 26, T12S, R16E, S.L.B.&M.

PROCEED IN A SOUTHWESTERLY DIRECTION FROM MYTON, UTAH ALONG U.S. HIGHWAY 40 APPROXIMATELY 1.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTH; TURN LEFT AND PROCEED IN A SOUTHERLY, THEN SOUTHWESTERLY, THEN SOUTHERLY DIRECTION APPROXIMATELY 1.5 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTHWEST; TURN RIGHT AND PROCEED IN A SOUTHWESTERLY DIRECTION APPROXIMATELY 31.8 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTHEAST; TURN LEFT AND PROCEED IN A SOUTHEASTERLY DIRECTION APPROXIMATELY 6.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTH; TURN RIGHT AND PROCEED IN A SOUTHWESTERLY, THEN SOUTHEASTERLY, THEN SOUTHWESTERLY DIRECTION APPROXIMATELY 7.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE EAST; TURN LEFT AND PROCEED IN A EASTERLY, THEN SOUTHEASTERLY DIRECTION APPROXIMATELY 1.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE NORTHEAST; TURN LEFT AND PROCEED IN A NORTHEASTERLY DIRECTION APPROXIMATELY 3.1 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE EAST; TURN RIGHT AND PROCEED IN AN EASTERLY DIRECTION APPROXIMATELY 100' TO THE EXISTING ACCESS TO THE SOUTHEAST; TURN RIGHT AND PROCEED IN A SOUTHEASTERLY, THEN EASTERLY, THEN NORTHEASTERLY, THEN SOUTHEASTERLY DIRECTION APPROXIMATELY 0.4 MILES TO THE LOCATION.

TOTAL DISTANCE FROM MYTON, UTAH TO THE PROPOSED WELL LOCATION IS APPROXIMATELY 50.5 MILES.



**UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
PRICE FIELD OFFICE**



125 SOUTH 600 WEST PRICE, UT 84501 (435) 636-3600

CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company:	Bill Barrett Corporation	Location:	SESW Section 26-T12S-R16E
Well No:	Peters Point Unit Federal 10-26D-12-16	Lease No:	UTU-0681
API No:	43-013-	Agreement:	Peters Point (UTU-63014)

Title	Name	Office Phone Number	Cell Phone Number
Acting Field Manager & Authorized Officer:	Michael Stiewig	(435) 636-3633	(435) 650-9135
Senior Petroleum Engineer:	Matthew Baker (Primary)	(435) 781-4490	(435) 828-4470
Petroleum Engineer:	James Ashley (Alt.)	(435) 781-4470	(435) 828-7874
Petroleum Engineering Technician	Randy Knight (Primary)	(435) 636-3615	(435) 650-9143
Petroleum Engineering Technician	Walton Willis (Alt.)	(435) 636-3662	(435) 650-9140
NRS/Enviro Scientist:	Nathan Sill (Alt.)	(435) 636-3668	
NRS/Enviro Scientist:	Don Stephens (Primary)	(435) 636-3608	

Fax: (435) 636-3657

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify NRS)	- Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify NRS)	- Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings.
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

Bill Barrett Corporation
Peters Point Unit Federal 10-26D-12-16
Peters Point Unit
Lease, Surface: UTU-0681
Bottom-hole: UTU-0681
Location, Surface: SE/SW Sec. 26, T12S, R16E
Bottom-hole: NW/SE Sec. 26, T12S, R16E
Carbon County, Utah

A COMPLETE COPY OF THIS APPROVED PERMIT and Conditions of Approval shall be maintained on location during all construction and drilling operations, and shall be available to contractors to ensure compliance.

CONDITIONS OF APPROVAL

Approval of this application does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Be advised that Bill Barrett Corporation is considered to be the operator of the above well and is responsible under the terms and conditions of the lease for the operations conducted on the leased lands.

Bond coverage for this well is provided by **WYB000040** (Principal – Bill Barrett Corporation) via surety consent as provided for in 43 CFR 3104.2.

This office will hold the aforementioned operator and bond liable until the provisions of 43 CFR 3106.7-2 continuing responsibility are met.

This permit will be valid for a period of two years from the date of approval. After permit termination, a new application must be filed for approval.

All lease operations will be conducted in full compliance with applicable regulations (43 CFR 3100), Onshore Oil and Gas Orders, lease terms, notices to lessees, and the approved plan of operations. The operator is fully responsible for the actions of his subcontractors. Failure to comply with the provisions of this permit, including applicable regulations, stipulations, and/or approval conditions, will be considered a violation subject to the enforcement provisions of 43 CFR Subpart 3163.

A. DRILLING PROGRAM

1. The proposed 3M BOP system is adequate for anticipated conditions. Installation, testing and operation of the system shall be in conformance with Onshore Oil and Gas Order No. 2.
2. If air drilling operations are utilized, the requirements of Onshore Oil and Gas Order No. 2 (Order 2), Part III.E *Special Drilling Operations*, shall be implemented.
3. Concurrent approval from the State of Utah, Division of Oil, Gas & Mining (DOG M) is required before conducting any surface disturbing activities.
4. The proposal included a provision for using minor amounts of diesel in the drilling fluid system. Diesel may be added to the system only after cementing the surface casing into place.
5. Either of the two production casing options proposed may be used.
6. A cement bond log (CBL) or other appropriate tool for determining top-of-cement, shall be run on the production casing string, unless cement is circulated to surface.
7. If logging reveals that the cementing objectives were not met, remedial cementing will be required.
8. Locally, the Green River Formation is known to contain oil, gas, oil shale and tar sand deposits. However, the lateral occurrence, distribution and grade of the oil shale and tar sand deposits are not well defined. The operator shall pay particular attention to this section, and shall attempt to identify and describe any of these resources that may be penetrated. Any information obtained on these resources shall be included as part of the Well Completion Report.
9. The use of a flow conditioner in lieu of straightening vanes in the gas meter run cannot be approved with the information provided. This proposal is not consistent with the provisions of Onshore Oil & Gas Order No. 5, and as such, can only be considered for approval as a "variance" from Order No. 5. A written request for variance would identify the Order No. 5 requirement(s) from which the variance is being requested, and it would include supporting justification as to how the alternate method of measurement would meet or exceed the minimum standards established in Order No. 5. A variance request for the use of a flow conditioner would also include the make, model, dimensions, and description of use for the specific flow conditioner being proposed.

10. Approval to use an Electronic Flow Computer is granted with the following conditions:

The EFC shall meet or exceed all standards and requirements of Utah NTL 2007-1 regarding the Use of Electronic Flow Computers.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Price Field Office Petroleum Engineer within 24 hours of spudding.
- Notify Price Field Office Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Price Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Price Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.
- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Price BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Price Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.

- **Please submit a copy of all other logs run on this well to the BLM Price Field Office.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Price Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Price Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Price Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Price Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or

data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Price Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Price Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Price Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Price Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Price Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Price Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Price Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Price Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
Price Field Office
Price, Utah

SURFACE USE
CONDITIONS OF APPROVAL

Project Name: Peters Point Unit Drilling

Operator: Bill Barrett Corporation

Well:

<u>Name</u>	<u>Number</u>	<u>Section SH</u>	<u>TWP/RNG</u>	<u>Lease Number</u>
Peters Point Unit Federal	10-26D-12-16	26	12S/16E	UTU-0681

I Site Specific Conditions of Approval

1. A pre-construction field meeting may be conducted prior to beginning any dirt work approved under this APD. The operator shall contact the BLM Authorized Officer Don Stephens ^{rep} @ 435-636-3608 at least 48-hours prior to beginning operations so that the meeting can be scheduled. The operator is responsible for having all contractors present (dirt contractors, drilling contractor, pipeline contractor, project oversight personnel, etc.) including the overall field operations superintendent, and for providing all contractors copies of the approved APD(s), project map and BLM Conditions of Approval pertinent to the work that each will be doing.
2. The following appendices are attached for your reference. They are to be followed as conditions of approval:
 - a. SM-A, Seed Mixture for Berms, Topsoil Piles, Pad Margins
 - b. SM-B, Seed Mixture for Final Reclamation (buried pipelines, abandoned pads, roads, etc.)
 - c. TMC1, Browse Hand Planting Tubeling Mixtures
 - d. Lease Stipulations, see attached Table 2.3 from EA for West Tavaputs Plateau Drilling Program.
 - e. Applicant-committed environmental protection measures, see attached Appendix B
3. The company shall furnish and apply water or other means satisfactory to the authorized officer for dust control. Dust is controlled when the following standards are met: (1) no dust is generated above the cab of the vehicle, or (2) no hanging dust plumes. These standards are applicable to Nine Mile Canyon between Harmon and Cottonwood Canyons, and in Harmon and Cottonwood Canyons. If dust exceeds these standards, operations shall be shut down until the standards are met.

4. The company shall supply a third party monitor to report directly to the BLM which shall monitor for dust on a daily basis, as necessary. A written monitoring report shall be submitted to the BLM on a weekly basis, and a phone report shall be made to the authorized officer on a daily basis, as necessary. If dust control standards are not met, operations shall be shut down until the standards are met.
5. The company shall submit interim reclamation plans and location layout with proposed interim reclaimed areas to the authorized office within 90 days of the spudding of the well.
6. There is an eligible cultural site (42Cb2085) along the access road. If new construction is required along the access road, the site shall be flagged for avoidance and the pipeline shall be "boomed" into place to further avoid the eligible site.
7. The area that encompasses the well location and road is environmentally sensitive including fragile soils and vegetation. The operator may be required to perform special measures such as mulching, erosion fencing, use of erosion fabric, etc. per the direction of the BLM Authorized Officer to stabilize any disturbed areas and ensure the reestablishment of long-term perennial vegetation.
8. The operator will be responsible for performing any remediation and/or necessary road upgrading (e.g. elevating, surfacing, culverts, low-water crossings, water-wings, surfacing, etc.) as directed by the BLM Authorized Officer, resulting from untimely access.
9. All equipment and personnel used during drilling and construction activities will be restricted to only approved access roads.
10. If the well is productive and after completion operations, the road will be upgraded to a **Resource Road** status in accordance with the *Surface Operating Standards for Oil & Gas Exploration and Development*, Fourth Edition and/or BLM Manual Section 9113 concerning road construction standards on projects subject to federal jurisdiction.
11. All permanent above-ground structures (e.g., production equipment, tanks, etc.) not subject to safety requirements will be painted to blend with the natural color of the landscape. The paint used will be a color which simulates "Standard Environmental Colors." The color selected for the Peters Point Unit Federal 10-26D-12-16 well is Olive Black, 5WA20-6. All facilities will be painted the designated color at the time of installation.
12. All trees salvaged from the construction of the well pad will be clearly segregated from the spoil material, to prevent burying of trees in the spoil material.
13. No salvaged trees will be pushed up against live trees or buried in the spoil material.
14. All areas not needed for production of the well will be reclaimed within 90 days of completion of the last well if weather conditions are favorable, unless the BLM Authorized Officer gives an extension.
15. Reserve pits will be closed as soon as possible, but no later than 90 days from time of drilling/well completion, unless the BLM Authorized Officer gives an extension. Squeezing of pit fluids and cuttings is prohibited. Pits must be dry of fluids or they must be removed via vac-truck or other environmentally acceptable method prior to backfilling, re-contouring and replacement of topsoil. Mud and cuttings left in pit must be buried at least 3-feet below re-contoured grade. The operator will be responsible for re-contouring any subsidence areas that develop from closing a pit before it is sufficiently dry.

16. The operator will drill seed on the contour to a depth of 0.5 inch, followed by cultipaction to compact the seedbed, preventing soil and seed losses. To maintain quality and purity, the current years tested, certified seed with a minimum germination rate of 80% and a minimum purity of 90% will be used.
17. Please contact Don Stephens, Natural Resource Specialist, (435) 636-3608, Bureau of Land Management, Price Field Office, if there are any questions concerning these surface use COAs.
18. A Paleontologist acceptable to the BLM will monitor during surface disturbing activities. If paleontologic resources are uncovered during surface disturbing activities, the paleontologist shall immediately notify the Authorized Officer (AO). The AO will arrange for a determination of significance and, if necessary, recommend a recovery or avoidance plan.
19. The pipeline(s) shall be buried.
20. During the activities of road maintenance, new road construction or the construction of well pads, if any standing live or dead trees are damaged, cut down or knocked over by grading or construction equipment, actions would be taken to remove excessive vegetation from the road or pad edge.
21. An impermeable liner shall be used in the containment area of all permanent condensate and water tanks.
22. Gas shall be measured on the well pad unless the BLM Authorized Officer authorizes another location.
23. If the well has not been spudded by APD Approval date + 2 years the APD will expire and the operator is to cease all operations related to preparing to drill the well.
24. The Mexican Spotted Owl Conservation Measures to avoid impacts:
 - a. Employ best available technology on production wells and compression equipment within .5 miles of canyon habitat model.
 - b. Upon discovery of individuals or sightings of this species, halt construction/drilling activities and notify authorized official.
25. No construction/drilling activities shall occur during the time of the year November 1 through April 15 for sage-grouse winter habitat.
26. Mule deer on critical winter ranges shall be protected by seasonal restrictions on construction from November 1 through May 15 where federal permits are required.
27. Elk on high priority and critical winter ranges would be protected by seasonal restrictions on construction from November 1 through May 15.
28. Centralize tanks and facilities with old wells. Utilize low profile tanks.
29. Leave trees on the edge of the well site.
30. The operator shall contact the BLM Authorized Officer Don Stephens @ 435-636-3608 at least 48-hours prior to the filling and reclamation of pits.

II Standard Conditions of Approval

A. General

1. If any cultural values [sites, artifacts, human remains] are observed during operation of this lease/permit/right-of-way, they will be left intact and the Price Field Manager notified. The authorized officer will conduct an evaluation of the cultural values to establish appropriate mitigation, salvage or treatment. The operator is responsible for

informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, the operator is to immediately stop work that might further disturb such materials, and contact the authorized BLM officer (AO). Within five working days the AO will inform the operator as to:

- whether the materials appear eligible for the National Register of Historic Places;
 - the mitigation measures the operator will likely have to undertake before the site can be used (assuming in situ preservation is not necessary); and,
 - a time-frame for the AO to complete an expedited review under 36 CFR 800.11 to confirm, through the State Historic Preservation Officer, that the findings of the AO are correct and that mitigation is appropriate. The AO will provide technical and procedural guidelines for the conduct of mitigation. Upon verification from the AO that the required mitigation has been completed, the operator will then be allowed to resume construction measures.
2. The operator shall restrict travel on unimproved roads during periods of inclement weather or spring thaw when the possibility exists for excessive surface resource damage (e.g., rutting in excess of 4-inches, travel outside roadway, etc.).
 3. The Companies will provide georeferenced spatial data depicting as-built locations of all facilities, wells, roads, pipelines, power lines, and other related facilities to the BLM by November 1 of each year until completion of project construction activities has occurred.
 4. If any dead or injured threatened, endangered, proposed, or candidate species is located during construction or operation, the BLM Price Field Office (435-636-3600) shall be notified within 24 hours.
 5. The Company will conduct clearance surveys for threatened, endangered or other special-concern species at the optimum time. This will require coordination with the BLM before November 1 annually to review the potential for disturbance and to agree on inventory parameters.

B. Construction

1. The operator will limit vegetation removal and the degree of surface disturbance wherever possible. Where surface disturbance cannot be avoided, all practicable measures will be utilized to minimize erosion and stabilize disturbed soils.
2. Construction and drilling activity will not be conducted using frozen or saturated soil material during periods when watershed damage or excessive rutting is likely to occur.
3. Remove all available topsoil from constructed well locations including areas of cut and fill, and stockpile at the site. Topsoil will also be salvaged for use in reclamation on all other areas of surface disturbance (roads, pipelines, etc.). Clearly segregate topsoil from excess spoil material. Any topsoil stockpiled for one year or longer will be signed and stabilized with annual ryegrass or other suitable cover crop.
4. The operator will not push soil material and overburden over side slopes or into drainages. All soil material disturbed will be placed in an area where it can be retrieved without creating additional undue surface disturbance and where it does not impede watershed and drainage flows.

5. Construct the backslope no steeper than 1½:1, and construct the foreslope no steeper than 2:1, unless otherwise directed by the BLM Authorized Officer.
6. Maintain a minimum 20-foot undisturbed vegetative border between toe-of-fill of pad and/or pit areas and the edge of adjacent drainages, unless otherwise directed by the BLM Authorized Officer.
7. With the overall objective of minimizing surface disturbance and retaining land stability and productivity, the operator shall utilize equipment that is appropriate to the scope and scale of work being done for roads and well pads (utilize equipment no larger than needed for the job).
8. Reserve pits will be adequately fenced during and after drilling operations until pit is reclaimed so as to effectively keep out wildlife and livestock. Adequate fencing, in lieu of more stringent requirements by the surface owner, is defined as follows:
 - Construction materials will consist of steel or wood posts. Three or four strand wire (smooth or barbed) fence or hog panel (16-foot length by 50-inch height) or plastic snow fence must be used with connectors such as fence staples, quick-connect clips, hog rings, hose clamps, twisted wire, etc. Electric fences will not be allowed.
 - Construction standards: Posts shall be firmly set in ground. If wire is used, it must be taut and evenly spaced, from ground level to top wire, to effectively keep out animals. Hog panels must be tied securely into posts and one another using fence staples, clamps, etc. Plastic snow fencing must be taut and sturdy. Fence must be at least 2-feet from edge of pit. 3 sides fenced before beginning drilling, the fourth side fenced immediately upon completion of drilling and prior to rig release. Fence must be left up and maintained in adequate condition until pit is closed.
9. The reserve pit will be oriented to prevent collection of surface runoff. After the drilling rig is removed, the operator may need to construct a trench on the uphill side of the reserve pit to divert surface drainage around it. If constructed, the trench will be left intact until the pit is closed.
10. The reserve pit will be lined with an impermeable liner if permeable subsurface material is encountered. An impermeable liner is any liner having a permeability of less than 10^{-7} cm/sec. The liner will be installed so that it will not leak and will be chemically compatible with all substances that may be put in the pit. Liners made of any man-made synthetic material will be of sufficient strength and thickness to withstand normal installation and pit use. In gravelly or rocky soils, a suitable bedding material such as sand will be used prior to installing the liner.
11. The reserve pit will be constructed so that at least half of its total volume is in solid cut material (below natural ground level).
12. The reserve pit shall have 2 foot of freeboard maintained at all times to prevent overflow of fluids.
13. Culverts will be placed on channel bottoms on firm, uniform beds, which have been shaped to accept them, and aligned parallel to the channel to minimize erosion. Backfill will be thoroughly compacted.
14. The minimum diameter for culverts will be 18 inches. However, all culverts will be appropriately sized in accordance with standards in BLM Manual 9113.
15. Construction and other project-related traffic will be restricted to approved routes. Cross-country vehicle travel will not be allowed.

16. Maximum design speed on all operator-constructed and maintained roads will not exceed 25 miles per hour.
17. Pipeline construction shall not block nor change the natural course of any drainage. Pipelines shall cross perpendicular to drainages. Pipelines shall not be run parallel in drainage bottoms. Suspended pipelines shall provide adequate clearance for maximum runoff.
18. Pipeline trenches shall be compacted during backfilling. Pipeline trenches shall be routinely inspected and maintained to ensure proper settling, stabilization and reclamation.
19. The pipeline right-of-way will be brush-hogged to prevent unnecessary disturbance. Only those areas where safety, absolute need for construction or other regulations may warrant the use of topsoil removal by blading or scalping.
20. During construction, emissions of particulate matter from well pad and road construction would be minimized by application of water or other non-saline dust suppressants with at least 50 percent control efficiency. Dust inhibitors (surfacing materials, non-saline dust suppressants, and water) will be used as necessary on unpaved roads that present a fugitive dust problem. The use of chemical dust suppressants on public surface will require prior approval from the BLM Authorized Officer.
21. The operator shall submit a Sundry Notice (Form 3160-5) to BLM for approval prior to construction of any new surface disturbing activities that are not specifically addressed in the approved APD.

C. Operations/Maintenance

1. If in the process of air drilling the wells there is a need to utilize mud, all circulating fluids will be contained either in an approved pit or in an aboveground containment tank. The pit or containment tank will be large enough to safely contain the capacity of all expected fluids without danger of overflow. Fluid and cuttings will not be squeezed out of the pit, and the pit will be reclaimed in an expedient manner.
2. Confine all equipment and vehicles to the access road(s), pad(s), and area(s) specified in the approved APD.
3. All waste, other than human waste and drilling fluids, will be contained in a portable trash cage. This waste will be transported to a State approved waste disposal site immediately upon completion of drilling operations. No trash or empty barrels will be placed in the reserve pit or buried on location. All state and local laws and regulations pertaining to disposal of human and solid waste will be complied with.
4. Rat and mouse holes shall be filled and compacted from the bottom to the top immediately upon release of the drilling rig from the location.
5. The operator will be responsible for prevention and control of noxious weeds and weeds of concern on all areas of surface disturbance associated with this project (well locations, roads, water management facilities, etc.) Use of pesticides shall comply with the applicable Federal and State laws. Pesticides shall be used only in accordance with their registered uses and within limitations imposed by the Secretary of Interior. Prior to the use of pesticides on public land, the holder shall obtain from the BLM authorized officer written approval of a plan showing the type and quantity of material to be used, pest(s) to be controlled, method of application, location of storage and disposal of containers, and any other information deemed necessary by the authorized officer to such use.

6. Sewage shall be placed in a self-contained, chemically treated porta-potty on location.
7. The operator and their contractors shall ensure that all use, production, storage, transport and disposal of hazardous and extremely hazardous materials associated with the drilling, completion and production of these wells will be in accordance with all applicable existing or hereafter promulgated federal, state and local government rules, regulations and guidelines. All project-related activities involving hazardous materials will be conducted in a manner to minimize potential environmental impacts. In accordance with OSHA requirements, a file will be maintained onsite containing current Material Safety Data Sheets (MSDS) for all chemicals, compounds and/or substances which are used in the course of construction, drilling, completion and production operations.
8. Produced fluids shall be put in test tanks on location during completion work. Produced water will be put in the reserve pit during completion work per Onshore Order #7.
9. The only fluids/waste materials which are authorized to go into the reserve pit are RCRA exempt exploration and production wastes. These include:
 - drilling muds & cuttings
 - rigwash
 - excess cement and certain completion & stimulation fluids defined by EPA as exempt
 It does not include drilling rig waste, such as:
 - spent hydraulic fluids
 - used engine oil
 - used oil filter
 - empty cement, drilling mud, or other product sacks
 - empty paint, pipe dope, chemical or other product containers
 - excess chemicals or chemical rinsate
 Any evidence of non-exempt wastes being put into the reserve pit may result in the BLM Authorized Officer requiring specific testing and closure requirements.
10. If this well is drilled during the fire season (June-October), the operator shall institute all necessary precautions to ensure that fire hazard is minimized, including but not limited to mowing vegetation on the access route(s) and well location(s), keeping fire fighting equipment readily available when drilling, etc.

D. Dry Hole/Reclamation

1. All disturbed lands associated with this project, including the pipelines, access roads, water management facilities, etc will be expediently reclaimed and reseeded in accordance with the surface use plan and any pertinent site-specific COAs.
2. Disturbed lands will be re-contoured back to conform with existing undisturbed topography. No depressions will be left that trap water or form ponds.
3. Before the location has been reshaped and prior to redistributing the topsoil, the operator will rip or scarify the drilling platform and access road on the contour, to a depth of at least 12 inches. The rippers are to be no farther than 24 inches apart.
4. Distribute the topsoil evenly over the entire location and other disturbed areas. Prepare the seedbed by disking to a depth of 4-to-6 inches following the contour.
5. Phased reclamation plans will be submitted to BLM for approval prior to individual POD facility abandonment via a Notice of Intent (NOI) Sundry Notice. Individual facilities, such as well locations, pipelines, discharge points, impoundments, etc. need to be

addressed in these plans as they are no longer needed. Individual items that will need to be addressed in reclamation plans include:

- Pit closure (Close ASAP after suitably dry, but no later than 90 days from time of drilling unless an extension is given by BLM Authorized Officer.) BLM may require closure prior to 90 days in some cases due to land use or environmental concerns.
 - Configuration of reshaped topography, drainage systems, and other surface manipulations
 - Waste disposal
 - Revegetation methods, including specific seed mix (pounds pure live seed/acre) and soil treatments (seedbed preparation, fertilization, mulching, etc.). On private surface, the landowner should be consulted for the specific seed mix.
 - Other practices that will be used to reclaim and stabilize all disturbed areas, such as water bars, erosion fabric, hydro-mulching, etc.
 - An estimate of the timetables for beginning and completing various reclamation operations relative to weather and local land uses.
 - Methods and measures that will be used to control noxious weeds, addressing both ingress and egress to the individual well or POD.
 - Decommissioning/removal of all surface facilities
6. BLM will not release the performance bond until all disturbed areas associated with the APD/POD have been successfully revegetated (evaluation will be made after the second complete growing season) and has met all other reclamation goals of the surface owner and surface management agency.
 7. A Notice of Intent to Abandon and a Subsequent Report of Abandonment must be submitted for abandonment approval.
 8. For performance bond release approval, a Final Abandonment Notice (with a surface owner release letter on split-estate) must be submitted prior to a final abandonment evaluation by BLM.
 9. Soil fertility testing and the addition of soil amendments may be required to stabilize some disturbed lands.
 10. Any mulch utilized for reclamation needs to be certified weed free.
 11. Waterbars are to be constructed at least one (1) foot deep, on the contour with approximately two (2) feet of drop per 100 feet of waterbar to ensure drainage, and extended into established vegetation. All waterbars are to be constructed with the berm on the downhill side to prevent the soft material from silting in the trench. The initial waterbar should be constructed at the top of the backslope. Subsequent waterbars should follow the following general spacing guidelines:

Slope (percent)	Spacing Interval (feet)
≤ 2	200
2 – 4	100
4 – 5	75
≥ 5	50

E. Producing Well

1. Reclaim those areas not required for production as soon as possible. The fluids and mud must be dry in the reserve pit before re-contouring pit area. The operator will be responsible for re-contouring and reseeding of any subsidence areas that develop from closing a pit before it is completely dry.
2. Reduce the backslope to 2:1 and the foreslope to 3:1, unless otherwise directed by the BLM Authorized Officer. Reduce slopes by pulling fill material up from foreslope into the toe of cut slopes.
3. Production facilities (including dikes) must be placed on the cut portion of the location and a minimum of 15 feet from the toe of the back cut unless otherwise approved by the BLM Authorized Officer.
4. Any spilled or leaked oil, produced water or treatment chemicals must be reported in accordance with NTL-3A and immediately cleaned up in accordance with BLM requirements. This includes clean-up and proper disposition of soils contaminated as a result of such spills/leaks.
5. Distribute stockpiled topsoil evenly over those areas not required for production and reseed as recommended.
6. Upgrade and maintain access roads and drainage control (e.g., culverts, drainage dips, ditching, crowning, surfacing, etc.) as necessary and as directed by the BLM Authorized Officer to prevent soil erosion and accommodate safe, environmentally-sound access.
7. Prior to construction of production facilities not specifically addressed in the APD, the operator shall submit a Sundry Notice to the BLM Authorized Officer for approval.
8. If not already required prior to constructing and drilling the well location, the operator shall immediately upgrade the entire access road to BLM standards (including topsoiling, crowning, ditching, drainage culverts, surfacing, etc.) to ensure safe, environmentally-sound, year-round access. Waterbars shall be installed on all reclaimed pipeline corridors per the guidelines in D #11.

Seed Mix A¹
Temporary Disturbance
(for berms, topsoil piles, pad margins)

Forbes Lbs

Yellow Sweetclover	2.0 lbs/acre
Ladak Alfalfa	2.0 lbs/acre
Cicer Milkvetch	1.0 lbs/acre
Palmer Penstemon	0.5 lbs/acre

Grasses Lbs

Crested Wheatgrass	2.0 lbs/acre
Great Basin Wildrye	2.0 lbs/acre
Intermediate Wheatgrass	2.0 lbs/acre

Total 11.5 lbs/acre

¹ Seed mix A is designed for rapid establishment, soil holding ability, and nitrogen fixing capability.
C-4 EA, West Tavaputs Plateau Drilling Program

Seed Mix B
Final Reclamation
(for buried pipe lines, abandoned pads, road, etc.)

Forbes Lbs

Palmer Penstemon	0.5 lbs/acre
Golden Cryptantha	0.25 lbs/acre
Utah Sweetvetch	0.5 lbs/acre
Yellow Sweetclover ¹	2.0 lbs/acre
Lewis Flax	1.0 lbs/acre

Grasses Lbs

Indian Ricegrass	1.0 lbs/acre
Needle & Thread Grass	1.0 lbs/acre
Intermediate Wheatgrass	2.0 lbs/acre
Blue Grama	0.5 lbs/acre
Galletta	0.5 lbs/acre
Great Basin Wildrye	2.0 lbs/acre

Woody Plants Lbs

Fourwing Saltbush	2.0 lbs/acre
Winterfat	0.5 lbs/acre

Wyoming Big Sage brush 0.25 lbs/acre
 Utah Serviceberry 1.0 lbs/acre
 Blue Elderberry (Raw Seeds) 1.0 lbs/acre

Total 16.0 lbs/acre

1 Yellow Sweetclover is planted as a nurse crop to provide solar protection, soil binding and nitrogen fixing. It will normally be crowded out in 2 to 3 years.

**TMC 1: Browse Hand Planting
 Tubeling Mixtures**

One of the two browse species lists (checked below) are to be hand planted at the prescribed application rate and according to the following prescribed methods on areas that are undergoing long term reclamation. The would include all pipeline corridors, berm around edge of drill pads, miscellaneous disturbed areas associated with construction such as staging areas for equipment, sidecast on road cuts, along side upgraded or new roads up to and including borrow ditch and in the termination of redundant access roads being closed. This planting shall be completed in the first planting window following completion of construction and on all other disturbed areas upon final reclamation.

Planting Methods:

Planting shall be accomplished using a labor force with specific experience in landscape restoration, hand planting methods and handling and care of browse tubling and or bareroot stock plants.

Browse plants to be utilized can be bareroot stock or tubling stock plants of 1 year old age class or greater.

Browse seedling protectors will be used to provide protection from browsing ungulates for two years. Seedling protectors will be of an open mesh rigid design that will break down when exposed to sunlight and that measures a minimum of 12 inches in length and 4 inches in diameter.

Planting shall be completed in the spring (March 1-April 1) and or fall (November 1-December 1) planting windows.

Browse plants shall be stored and handled in such a manner as to maintain viability, according to the type of browse stock being used.

Planting Species and Application Rate: Sagebrush-Grass Pinyon-Juniper

Species	Plants Per Acre	
	Sagebrush-Grass	Pinyon-Juniper
Wyoming Sagebrush (Gordon Creek)	100	50
Fourwing Saltbush (Utah seed source collected at or above 5,000 feet elevation)	100	50
True Mountain Mahogany (Utah seed source)	0	50
Antelope Bitterbrush (Utah seed source)	0	50
TOTAL	200	200
Suitable Substitutions:		
Utah Serviceberry	No	50

Table 2.3 Lease Numbers, Oil and Gas Units, Federal ROW Requirements, and Lease Stipulations for State and Federal Wells Proposed by BBC.

Location/Well Number	Federal Lease Number and Stipulations	Unit Name	Federal ROW Needs
Federal Wells			
7-25	UTU-59970	Prickly Pear Unit	Lower Flat Iron Road
16-34	UTU-73671	Prickly Pear Unit	Lower Flat Iron Road
27-3	UTU-73670 ^{1,2,3}	Prickly Pear Unit	None
21-2	UTU-73670 ^{1,2,3}	Prickly Pear Unit	None
13-4	UTU-74385	Prickly Pear Unit	None
5-13	UTU-73665	Prickly Pear Unit	None
24-12	UTU-77513 ^{1,2,3}	Prickly Pear Unit	None
10-4	UTU-74386 ^{1,2,3,4}	Prickly Pear Unit	None
15-19	UTU-66801 ^{1,2,3}	Jack Canyon Unit	None
Existing Pads			
UT-10	UTU-66801 ^{1,2,3}	Jack Canyon Unit	None
PPH-8	UTU-66801 ^{1,2,3}	Jack Canyon Unit	None
PP-11	UTU-66801 ^{1,2,3}	Jack Canyon Unit	None
State Wells			
Section 2, T13S, R15E	NA	Prickly Pear Unit	Lower Flat Iron Road
Section 36, T12S, R15E	NA	Prickly Pear Unit	Lower Flat Iron Road
Section 32, T12S, R16E	NA	Jack Canyon Unit	Cottonwood Canyon Road
Section 2, T13S, R16E	NA	None	Peters Point Road Extension

- ¹ No occupancy or other surface disturbance will be allowed within 330 feet of the centerline or within the 100-year recurrence interval floodplain, whichever is greater, of the perennial streams or within 660 feet of springs, whether flowing or not. This distance may be modified when specifically approved in writing by the authorized officer of the BLM.
- ² In order to minimize watershed damage, exploration drilling and other development activity will be allowed only during the period from May 1 to October 31. This limitation does not apply to maintenance and operation of producing wells. Exceptions to this limitation in any year may be specifically approved in writing by the authorized officer of the BLM.
- ³ Construction of access roads and drill pads on slopes in excess of 30 percent will require special design standards to minimize watershed damage. Drilling operations and any associated construction activities on slopes in excess of 50 percent may require directional drilling to prevent damage to the watershed. Exceptions to the limitations may be specifically approved in writing by the authorized officer of the BLM.
- ⁴ Raptor surveys will be required whenever surface disturbance and/or occupancy proposed in association with oil/gas exploration occur within a known nesting complex for raptors located in the NWNW, Sec. 10, T12S, R14E. Field surveys will be conducted by the lessee/operator as determined by the AO of the BLM. When surveys are required of the lessee/operator, the consultant hired must be found acceptable to the AO prior to the field survey being conducted. Based on the result of the field survey, the AO will determine appropriate buffer zones.

APPENDIX B:
APPLICANT-COMMITTED ENVIRONMENTAL PROTECTION MEASURES

1.0 INTRODUCTION

Appendix B is part of BBC's Proposed Action for the WTPDP as described in Chapter 2.0, and BBC will comply with the standards, procedures, and requirements contained in Appendix B when implementing the Alternatives unless otherwise provided for by the BLM Authorized Officer (AO). Appendix B describes standard practices utilized to mitigate adverse effects caused by surface-disturbing activities.

2.0 STANDARD PRACTICES

The following BMPs/Applicant-Committed Protection Measures (ACEPM) will be applied to all federal lands within the WTPPA by BBC to minimize impacts to the environment. Exception, modification, or waiver of a mitigation requirement may be granted if a thorough analysis by BLM determines that the resource(s) for which the measure was developed will not be impacted by the project activity. Further site-specific mitigation measures may be identified during the application for permit to drill (APD) and/or right-of-way (ROW) application review processes.

2.1 PRECONSTRUCTION PLANNING AND DESIGN MEASURES

1. BBC and/or their contractors and subcontractors will conduct all phases of project implementation, including well location, road and pipeline construction, drilling and completion operations, maintenance, reclamation, and abandonment in full compliance with all applicable federal, state, and local laws and regulations and within the guidelines specified in approved APDs and ROW permits. BBC will be held fully accountable for their contractor's and subcontractor's compliance with the requirements of the approved permit and/or plan.
2. Implementation of site-specific activities/actions will be contingent on BLM determining that the activity/action complies with the following plans:
 - Surface Use Plan and/or Plan of Development; and
 - Site-specific APD plans/reports (e.g., road and wellpad design plans, cultural clearance, special status plant species clearance, etc.).

The above plans may be prepared by the Companies for the project area or submitted incrementally with each APD, ROW application, or Sundry Notice (SN).

2.2 ROADS

1. BBC will construct roads on private surface in a safe and prudent manner to the specifications of landowners.
 2. Roads on federal surface will be constructed as described in BLM Manual 9113. Where necessary, running surfaces of the roads will be graveled if the base does not already contain sufficient aggregate.
 3. Existing roads will be used when the alignment is acceptable for the proposed use. Generally, roads will be required to follow natural contours; provide visual screening by constructing curves, etc.; and be reclaimed to BLM standards.
 4. To control or reduce sediment from roads, guidance involving proper road placement and buffer strips to stream channels, graveling, proper drainage, seasonal closure, and in some cases, redesign or closure of old roads will be developed when necessary. Construction may also be prohibited during periods when soil material is saturated, frozen, or when watershed damage is likely to occur.
 5. Available topsoil will be stripped from all road corridors prior to commencement of construction activities and will be redistributed and reseeded on backslope areas of the borrow ditch after completion of road construction activities. Borrow ditches will be reseeded in the first appropriate season after initial disturbance.
-

-
6. On newly constructed roads and permanent roads, the placement of topsoil, seeding, and stabilization will be required on all cut and fill slopes unless conditions prohibit this (e.g., rock). No unnecessary side-casting of material (e.g., maintenance) on steep slopes will be allowed.
 7. Reclamation of abandoned roads will include requirements for reshaping, recontouring, resurfacing with topsoil, installation of water bars, and seeding on the contour. Road beds, wellpads, and other compacted areas will be ripped to a depth of 1.0 foot on 1.5 feet centers to reduce compaction prior to spreading the topsoil across the disturbed area. Stripped vegetation will be spread over the disturbance for nutrient recycling, where practical. Fertilization or fencing of these disturbances will not normally be required. Additional erosion control measures (e.g., fiber matting) and road barriers to discourage travel may be required. Graveled roads, wellpads, and other sites will be stripped of usable gravel and hauled to new construction sites prior to ripping as deemed necessary by the AO. The removal of structures such as bridges, culverts, cattleguards, and signs will usually be required.
 8. Main artery roads, regardless of the primary user, will be crowned, ditched, drained, and, if deemed appropriate by the AO, surfaced with gravel.
 9. Unnecessary topographic alterations will be mitigated by avoiding, where possible, steep slopes, rugged topography, and perennial and ephemeral/intermittent drainages, and by minimizing the area disturbed.
 10. Upon completion of construction and/or production activities, the Companies will restore, to the extent practicable, the topography to near pre-existing contours at well sites, access roads, pipelines, and other facility sites.
 11. Existing roads will be used to the maximum extent possible and upgraded as necessary.
 12. BBC will comply with existing federal, state, and county requirements and restrictions to protect road networks and the traveling public.
 13. Special arrangements will be made with the Utah Department of Transportation to transport oversize loads to the project area. Otherwise, load limits will be observed at all times to prevent damage to existing road surfaces.
 14. All development activities along approved ROWs will be restricted to areas authorized in the approved ROW.
 15. Roads and pipelines will be located adjacent to existing linear facilities wherever practical.
 16. BBC and/or their contractors will post appropriate warning signs and require project vehicles to adhere to appropriate speed limits on project-required roads, as deemed necessary by the AO.
 16. BBC will be responsible for necessary preventative and corrective road maintenance for the duration of the project. Maintenance responsibilities may include, but are not limited to, blading, gravel surfacing, cleaning ditches and drainage facilities, dust abatement, noxious weed control, or other requirements as directed by the AO.
-

2.3 WELLPADS AND FACILITIES

1. In conformance with Onshore Oil and Gas Order No. 1, BBC will prepare and submit individual comprehensive drill site design plans for BLM approval. These plans will show the drill location layout over the existing topography; dimensions of the location; volumes and cross sections of cut and fill; location and dimensions of reserve pits; existing drainage patterns; and access road egress and ingress. Plans will be submitted and approved prior to initiation of construction.
2. No surface disturbance is recommended on slopes in excess of 25% unless erosion controls can be ensured and adequate revegetation is expected. Engineering proposals and revegetation and restoration plans will be required in these areas.
3. Reserve pits will be constructed to ensure protection of surface and ground water. The review to determine the need for installation of lining material will be done on a case-by-case basis and consider soil permeability, water quality, and depth to ground water.
4. Reserve pit liners will have a mullen burst strength that is equal to or exceeds 300 pounds, a puncture strength that is equal to or exceeds 160 pounds, and grab tensile strengths that are equal to or exceed 150 pounds. There will be verified test results conducted according to ASTM test standards. The liner will be totally resistant to deterioration by hydrocarbons.
5. Produced water from oil and gas operations will be disposed of in accordance with the requirements of Onshore Oil and Gas Order #7.
6. Pits will be fenced as specified in individual authorizations. Any pit containing harmful fluids will be maintained in a manner that will prevent migratory bird mortality.
7. Disturbances will be managed/reclaimed for zero runoff from the wellpad or other facility until the area is stabilized. All excavations and pits will be closed by backfilling and contouring to conform to surrounding terrain. On wellpads and other facilities, the surface use plan will include objectives for successful reclamation including soil stabilization, plant community composition, and desired vegetation density and diversity.
8. On producing wells, BBC will reduce slopes to original contours (not to exceed 3:1 slopes). Areas not used for production purposes will be backfilled and blended into the surrounding terrain, reseeded, and erosion control measures installed. Erosion control measures will be required after slope reduction. Mulching, erosion control measures, and fertilization may be required to achieve acceptable stabilization.
9. Abandoned sites will be satisfactorily rehabilitated in accordance with the approved APD.

2.4 PIPELINES

1. Pipeline construction methods and practices will be completed in such a manner so as to obtain good reclamation and the re-establishment of the native plant community.
 2. On ditches exceeding 24 inches in width, 6 to 12 inches of surface soil will be salvaged on the entire right-of-way, where practicable. When pipelines are buried, there will be at least 30 inches of backfill on top of the pipe. Backfill will not extend above the original ground level after the fill has settled. Guides for construction and water bar placement found in "Surface Operating Standards for Oil and
-

Gas Exploration and Development" (BLM and USFS 1989) will be followed. Bladed surface materials will be re-spread upon the cleared route once construction is completed. Disturbed areas that have been reclaimed will be fenced when the route is near livestock watering areas at the discretion of the AO.

3. Pipeline ROWs will be located to minimize soil disturbance to the greatest extent practicable. Mitigation will include locating pipeline ROWs adjacent to access roads to minimize ROW disturbance widths, or routing pipeline ROWs directly to minimize disturbance lengths.
4. Existing crowned and ditched roads will be used for access where possible to minimize surface disturbances. Clearing of pipeline ROWs will be accomplished with the least degree of disturbance to topsoil. Where topsoil removal is necessary, it will be stockpiled (windrowed) and re-spread over the disturbed area after construction and backfilling are completed. Vegetation removed from the ROW will also be re-spread to provide protection, nutrient recycling, and a seed source.
5. Temporary disturbances which do not require major excavation (e.g., small pipelines) may be stripped of vegetation to ground level using mechanical treatment, leaving topsoil intact and root masses relatively undisturbed.
6. To promote soil stability, backfill over the trench will be compacted so as not to extend above the original ground level after the fill has settled. Wheel or other methods of compacting the pipeline trench backfill will occur at two levels to reduce trench settling and water channeling--once after 3 feet of fill has been replaced and once within 6-12 inches of the surface. Water bars, mulching, and terracing will be installed, as needed, to minimize erosion. Instream protection structures (e.g., drop structures) in drainages crossed by a pipeline will be installed at the discretion of the AO to prevent erosion.
7. BBC will adhere to the following procedures regarding the installation of pipelines during periods when the earth is frozen.
 - The BLM Price Field Office will be contacted at least 10 days prior to anticipated start of project. The project will not proceed until such time as authorization from BLM has been received by the Companies.
 - A BLM representative will be on the ground at the beginning of construction.
 - Snow, if present, will be removed utilizing a motor grader.
 - Vegetation will be scalped and windrowed to one side of the right-of-way.
 - A wheel trencher will be used to remove approximately 6-8 inches of topsoil from the top of the pipeline ditch and windrow it to one side.
 - A trench approximately 4 feet deep will be dug using a wheel trencher and the soil will be stockpiled to one side, making sure the top soil or spoil do not get mixed together.
 - The pipeline will be installed, the trench backfilled, and the spoil compacted in the trench.
 - Stockpiled topsoil will be placed in the trench and compacted.
 - Scalped vegetation back will be placed back on right-of-way using a motor grader.
 - The entire right-of-way will be reseeded as normal in the spring after the thaw.

These procedures will be incorporated in every Plan of Development where construction in frozen earth is anticipated.

2.5 AIR QUALITY

1. BBC will comply with all applicable local, state, and federal air quality laws, statutes, regulations, standards, and implementation plans.
2. BBC will obtain all necessary air quality permits from UDAQ to construct, test, and operate facilities.
3. All internal combustion equipment will be kept in good working order.
4. The Companies will use water at construction sites, as necessary, to abate fugitive dust.
5. The Companies will not allow any open burning of garbage or refuse at well sites or other facilities.

2.6 VEGETATION

1. Removal and disturbance of vegetation will be kept to a minimum through construction site management (e.g., using previously disturbed areas and existing easements, limiting equipment/materials storage yard and staging area size, etc.).
2. Wellpads and associated roads and pipelines will be located to avoid or minimize impacts in areas of high value (e.g., sensitive species habitats, wetland/riparian areas).

2.7 SOILS

1. Surface-disturbing activities will be examined on a site-specific basis, evaluating the potential for soil loss and the compatibility of soil properties with project design. Stipulations and mitigating measures will be developed on a case-by-case basis to ensure soil conservation and practical management.
 2. BBC will restrict construction activities during periods when soils are saturated and excessive rutting (>4 inches with multiple passes) would occur.
 3. Salvage and subsequent replacement of topsoil will occur for surface-disturbing activities wherever specified by the AO.
 4. Before a surface-disturbing activity is undertaken, topsoil depth will be determined and the amount of topsoil to be removed, along with topsoil placement areas, will be specified in the authorization. The uniform distribution of topsoil over the area to be reclaimed will occur unless conditions warrant a varying depth. On large surface-disturbing projects topsoil will be stockpiled and seeded to reduce erosion. Where feasible, topsoil stockpiles will be designed to maximize surface area to reduce impacts to soil microorganisms. Areas used for spoil storage will be stripped of topsoil before spoil placement, and the replacement of topsoil after spoil removal will be required.
 5. BBC will avoid adverse impacts to soils by:
 - minimizing the area of disturbance;
 - avoiding construction with frozen soil materials to the extent practicable;
 - avoiding areas with high erosion potential (e.g., unstable soil, dunal areas, slopes greater than 25%, floodplains), where practicable;
 - salvaging and selectively handling topsoil from disturbed areas;
 - adequately protecting stockpiled topsoil and replacing it on the surface during reclamation;
 - leaving the soil intact (scalping only) during pipeline construction, where practicable;
-

-
- using appropriate erosion and sedimentation control techniques including, but not limited to, diversion terraces, riprap, and matting;
 - promptly revegetating disturbed areas using adapted species;
 - applying temporary erosion control measures such as temporary vegetation cover, application of mulch, netting, or soil stabilizers; and/or
 - constructing barriers, as appropriate, to minimize wind and water erosion and sedimentation prior to vegetation establishment.
6. Appropriate erosion control and revegetation measures will be employed. Grading and landscaping will be used to minimize slopes, and water bars will be installed on disturbed slopes in areas with unstable soils where seeding alone may not adequately control erosion. Erosion control efforts will be monitored by the Companies and necessary modifications made to control erosion.
 7. Sufficient topsoil or other suitable material to facilitate revegetation will be segregated from subsoils during all construction operations requiring excavation and will be returned to the surface upon completion of operations. Soils compacted during construction will be ripped and tilled as necessary prior to reseeding. Cut and fill sections on all roads and along pipelines will be revegetated with native species.
 8. Any accidental soil contamination by spills of petroleum products or other hazardous materials will be cleaned up by the Companies and the soil disposed of or rehabilitated according to applicable rules.
 9. BBC will restrict off-road vehicle (ORV) activity by employees and contract workers to the immediate area of authorized activity or existing roads and trails.

2.8 RECLAMATION

1. BBC's reclamation goals will emphasize: 1) protection of existing native vegetation; 2) minimal disturbance of the existing environment; 3) soil stabilization through establishment of ground cover; and 4) establishment of native vegetation consistent with land use planning.
 2. All reclamation will be accomplished as soon as possible after the disturbance occurs with efforts continuing until a satisfactory revegetation cover is established.
 3. Seed mixtures for reclaimed areas will be site-specific, composed of native species, and will include species promoting soil stability. A pre-disturbance species composition list will be developed if the site includes several different plant communities. Livestock palatability and wildlife habitat needs will be given consideration during seed mix formulation. BLM Manual 1745, *Introduction, Transplant, Augmentation, and Reestablishment of Fish, Wildlife, and Plants*, and Executive Order No. 11987, *Exotic Organisms*, will be used as guidance.
 4. Interseeding, secondary seeding, or staggered seeding may be used to accomplish revegetation objectives. During rehabilitation of areas in important wildlife habitat, provision will be made for the establishment of native browse and forb species. Follow-up seeding or corrective erosion control measures will occur on areas where initial reclamation efforts are unsuccessful.
 5. Any mulch used by BBC will be weed free and free from mold, fungi, or noxious weed seeds. Mulch may include native hay, small grain straw, wood fiber, live mulch, cotton, jute, synthetic netting, and
-

rock. Straw mulch will contain fibers long enough to facilitate crimping and provide the greatest cover.

6. BBC will be responsible for the control of all noxious weed infestations on disturbed surfaces. Aerial application of chemicals will be prohibited within 0.25 mile of special status plant locations, and hand application will be prohibited within 500 feet. Herbicide application will be monitored by the AO.
7. Recontouring and seedbed preparation will occur immediately prior to reseeding on the unused portion of wellpads, road ROWs, and entire pipeline ROWs outside of road ROWs. In the event of uneconomical wells, BBC will initiate reclamation of the entire wellpads, access road, and adjacent disturbed habitat as soon as possible. BBC assumes the responsibility to see that their exploration, development, production, and construction operations are conducted in a manner which results in the proper reclamation of disturbed lands. BBC will monitor reclamation to determine and ensure successful establishment of vegetation. No consent to termination of any bond will be given by the AO until all the terms and conditions of the approved permit(s) have been met.
8. Proper erosion and sediment control structures and techniques will be incorporated by the Companies into the design of wellpads, roads, pipelines, and other facilities. Revegetation using a BLM-approved, locally adapted seed mixture containing native grasses, forbs, and shrubs will begin in the first appropriate season following disturbance. Vegetation removed will be replaced with plants of equal forage value and growth form using procedures that include:
 - fall reseeding (September 15 to freeze-up), where feasible;
 - spring reseeding (April 30 - May 31) if fall seeding is not feasible;
 - deep ripping of compacted soils prior to reseeding;
 - surface pitting/roughening prior to reseeding;
 - utilization of native cool season grasses, forbs, and shrubs in the seed mix;
 - interseeding shrubs into an established stand of grasses and forbs at least one year after seeding;
 - appropriate, approved weed control techniques;
 - broadcast or drill seeding, depending on site conditions; and
 - fencing of certain sensitive reclamation sites (e.g., riparian areas, steep slopes, and areas within 0.5 mile of livestock watering facilities) as determined necessary through monitoring.
9. BBC will monitor noxious weed occurrence on the project area and implement a noxious weed control program in cooperation with BLM. Weed-free certification by county extension agents will be required for grain or straw used for mulching revegetated areas.

2.9 CANDIDATE PLANTS/SPECIAL STATUS PLANTS

1. Herbicide applications will be kept at least 500 feet from known special status plant species populations or other distances deemed safe by the AO.
2. Wellpads and associated roads and pipelines will be located to avoid or minimize impacts to areas of high value (e.g., special status plant species habitats, wetland/riparian areas).

2.10 WATERSHEDS

1. Crossings of ephemeral, intermittent, and perennial streams associated with road and utility line construction will generally be restricted until normal flows are established after spring runoff.
-

2.11 GEOLOGICAL/PALEONTOLOGICAL RESOURCES

1. Wells, pipelines, and ancillary facilities will be designed and constructed such that they will not be damaged by moderate earthquakes. Any facilities defined as critical according to the Uniform Building Code will be constructed in accordance with applicable Uniform Building Code Standards for Seismic Risk Zone 2B.
2. If paleontological resources are uncovered during surface-disturbing activities, BBC will suspend operations at the site that will further disturb such materials and immediately contact the AO, who will arrange for a determination of significance, and, if necessary, recommend a recovery or avoidance plan.

2.12 CULTURAL/HISTORICAL RESOURCES

1. BBC will follow the cultural resources and recovery plan for the project.
2. If cultural resources are located within frozen soils or sediments that preclude the possibility of adequately recording or evaluating the find, construction work will cease and the site will be protected for the duration of frozen soil conditions. Recordation, evaluation and recommendations concerning further management will be made to the AO following natural thaw. The AO will consult with the affected parties and construction work will resume once management of the threatened site has been finalized and the Notice to Proceed has been issued.
3. BBC will inform their employees, contractors and subcontractors about relevant federal regulations intended to protect archaeological and cultural resources. All personnel will be informed that collecting artifacts, including arrowheads, is a violation of federal law and that employees engaged in this activity may be subject to disciplinary action.

2.13 WATER RESOURCES

1. BBC will maintain a complete copy of the SPCC Plan at each facility if the facility is normally attended at least 8 hours per day, or at the nearest field office if the facility is not so attended (40 CFR 112.3(e)).
 2. BBC will implement and adhere to SPCC Plans in a manner such that any spill or accidental discharge of oil will be remediated. An orientation will be conducted by the Companies to ensure that project personnel are aware of the potential impacts that can result from accidental spills, as well as the appropriate recourse if a spill does occur. Where applicable and/or required by law, streams at pipeline crossings will be protected from contamination by pipeline shutoff valves or other systems capable of minimizing accidental discharge.
 3. If reserve pit leakage is detected, operations at the site will be curtailed, as directed by the BLM, until the leakage is corrected.
 4. BBC will case and cement all gas wells to protect subsurface mineral and freshwater zones. Unproductive wells and wells that have completed their intended purpose will be properly abandoned and plugged using procedures identified by BLM (federal mineral estate) and/or WOGCC (state and fee mineral estate).
-

5. All water used in association with this project will be obtained from sources previously approved by the Utah State Engineer's Office.
 6. Erosion-prone or high salinity areas will be avoided where practicable. Necessary construction in these areas will be timed to avoid periods of greatest runoff.
 7. BBC will incorporate proper containment of condensate and produced water in tanks and drilling fluids in reserve pits, and will locate staging areas for storage of equipment away from drainages to prevent contaminants from entering surface waters.
 8. Prudent use of erosion control measures, including diversion terraces, riprap, matting, temporary sediment traps, and water bars will be employed by the Companies as necessary. These erosion control measures will be used as appropriate to control surface runoff generated at wellpads. The type and location of sediment control structures, including construction methods, will be described in APD and ROW plans. If necessary, BBC may treat diverted water in detention ponds prior to release to meet applicable state or federal standards.
 9. BBC will construct channel crossings by pipelines so that the pipe is buried at least 3 feet below the channel bottom.
 10. Streams/channels crossed by roads will have culverts installed at all appropriate locations as specified in the BLM Manual 9112-*Bridges and Major Culverts* and Manual 9113-*Roads*. Streams will be crossed perpendicular to flow, where possible, and all stream crossing structures will be designed to carry the 25-year discharge event or other capacities as directed by the AO.
 11. BBC will reshape disturbed channel beds to their approximate original configuration.
 12. The disposal of all hydrostatic test water will be done in conformance with BLM Onshore Oil and Gas Order No. 7. BBC will comply with state and federal regulations for water discharged into an established drainage channel. The rate of discharge will not exceed the capacity of the channel to convey the increased flow. Waters that do not meet applicable state or federal standards will be evaporated, treated, or disposed of at an approved disposal facility.
 13. BBC will prepare Storm Water Pollution Prevention Plans (SWPPPs) as required by WDEQ National Pollution Discharge Elimination System (NPDES) permit requirements on individual disturbances that exceed 5 acres in size or as required by future changes in regulations.
 14. Any disturbances to wetlands and/or waters of the U.S. will be coordinated with the COE, and 404 permits will be secured as necessary prior to disturbance.
 15. Where disturbance of wetlands, riparian areas, streams, or ephemeral/intermittent stream channels cannot be avoided, COE Section 404 permits will be obtained by BBC as required, and, in addition to applicable above-listed measures, the following measures will be applied where appropriate:
 - wetland areas will be crossed during dry conditions (i.e., late summer, fall, or dry winters);
 - streams, wetlands, and riparian areas disturbed during project construction will be restored to as near re-project conditions as practical and, if impermeable soils contributed to wetland formation, soils will be compacted to reestablish impermeability;
 - wetland topsoil will be selectively handled;
 - disturbed areas will be recontoured and BLM-approved species will be used for reclamation; and
-

-
- reclamation activities will begin on disturbed wetlands immediately after completion of project activities.

2.14 NOISE

1. All engines required for project activities will be properly muffled and maintained in accordance with state and federal laws.

2.15 WILDLIFE, FISHERIES, AND THREATENED AND ENDANGERED (T&E) SPECIES

1. To minimize wildlife mortality due to vehicle collisions, BBC will advise project personnel regarding appropriate speed limits in the project area. Roads no longer required for operations will be reclaimed as soon as possible. Potential increases in poaching will be minimized through employee and contractor education regarding wildlife laws. If wildlife law violations are discovered, the offending employee will be subject to disciplinary action by BBC.
2. BBC will protect (e.g., fence or net) reserve, workover, and production pits potentially hazardous to prohibit wildlife access as directed by BLM.
3. BBC will utilize wildlife-proof fencing on reclaimed areas in accordance with standards specified in BLM Handbook 1741-1, *Fencing*, if it is determined that wildlife are interfering with successful reestablishment of vegetation.
4. Consultation and coordination with USFWS and UDWR will be conducted for all mitigation activities relating to raptors and T&E species and their habitats, and all permits required for movement, removal, and/or establishment of raptor nests will be obtained.
5. BBC will adhere to all survey, mitigation, and monitoring requirements identified in the Biological Assessment prepared for this project.

2.16 LIVESTOCK/GRAZING MANAGEMENT

1. BBC will reclaim nonessential areas disturbed during construction activities in the first appropriate season after well completion.
 2. Nonessential areas include portions of the wellpads not needed for production operations, the borrow ditch and outslope portions of new road ROWs, entire pipeline ROWs outside of road ROWs, and all roads and associated disturbed areas at nonproductive wells.
 3. BBC will repair or replace fences, cattleguards, gates, drift fences, and natural barriers to current BLM standards. Cattleguards will be used instead of gates for livestock control on most road ROWs. Livestock will be protected from pipeline trenches, and livestock access to existing water sources will be maintained.
 4. BBC will review livestock impacts from roads or disturbance from construction and drilling activities at least annually with livestock permittees and BLM. Appropriate measures will be taken to correct any adverse impacts, should they occur.
-

2.17 RECREATION

1. BBC will instruct employees, contractors, and subcontractors that camp sites on federal lands or at federal recreation sites must not be occupied for more than 14 consecutive days.
2. BBC will require that employees, contractors, and subcontractors abide by all state and federal laws and regulations regarding hunting.

2.18 VISUAL RESOURCES

1. Pipeline ROWs will be located within existing ROWs whenever possible, and aboveground facilities not requiring safety coloration will be painted with appropriate nonreflective standard environmental colors (Carlsbad Canyon or Desert Brown, or other specified standard environmental colors) as determined by the AO. Topographic screening, vegetation manipulation, project scheduling, and traffic control procedures may all be employed, as practicable, to further reduce visual impacts.
2. Within VRM Class II areas, BBC will utilize existing topography to screen roads, pipeline corridors, drill rigs, wells, and production facilities from view where practicable. The Companies will paint all aboveground production facilities with appropriate colors (e.g., Carlsbad Canyon or Desert Brown) to blend with adjacent terrain, except for structures that require safety coloration in accordance with OSHA requirements.

2.19 HEALTH AND SAFETY/HAZARDOUS MATERIALS

1. BBC will utilize BLM-approved portable sanitation facilities at drill sites; place warning signs near hazardous areas and along roadways; place dumpsters at each construction site to collect and store garbage and refuse; ensure that all refuse and garbage is transported to a State-approved sanitary landfill for disposal; and institute a Hazard Communication Program for its employees and require subcontractor programs in accordance with OSHA (29 CFR 1910.1200).
 2. In accordance with 29 CFR 1910.1200, a Material Safety Data Sheet for every chemical or hazardous material brought on-site will be kept on file BBC's field offices.
 3. Chemicals and hazardous materials will be inventoried and reported by BBC in accordance with the SARA Title III (40 CFR 335). If quantities exceeding 10,000 pounds or the threshold planning quantity are to be produced or stored, BBC will submit appropriate Section 311 and 312 forms at the required times to the State and County Emergency Management Coordinators and the local fire departments.
 4. BBC will transport and/or dispose of any hazardous wastes, as defined by the Resource Conservation and Recovery Act of 1976 (RCRA), as amended, in accordance with all applicable federal, state, and local regulations.
 5. BBC commits to the following practices regarding hazardous material containment.
 - All storage tank batteries that contain any oil, glycol, produced water, or other fluid which may constitute a hazard to public health or safety will be surrounded by a secondary means of containment for the entire contents of the largest single tank in use plus freeboard for precipitation, or to contain 110% of the capacity of the largest vessel. The appropriate containment and/or diversionary structures or equipment, including walls and floor, will contain
-

any oil, glycol or produced water and shall be constructed so that any discharge from a primary containment system, such as a tank or pipe, will not drain, infiltrate, or otherwise escape to ground or surface waters before cleanup is completed.

- Treaters, dehydrators and other production facilities that have the potential to leak or spill oil, glycol, produced water, or other fluid which may constitute a hazard to public health or safety, shall be placed on or within appropriate containment and/or diversionary structure to prevent spilled or leaking fluid from reaching ground or surface waters. The appropriate containment and/or diversionary structure will be sufficiently impervious to oil, glycol, produced water, or other fluid and will be installed so that any spill or leakage will not drain, infiltrate, or otherwise escape to ground or surface waters prior to completion of cleanup.
 - Notice of any spill or leakage, as defined in BLM NTL 3A, will be immediately reported to the AO by the Companies as well as to such other federal and state officials as required by law. Oral notice will be given as soon as possible, but within no more than 24 hours, and those oral notices will be confirmed in writing within 72 hours of any such occurrence.
-

DIVISION OF OIL, GAS AND MINING

SPUDDING INFORMATION

Name of Company: BILL BARRETT CORPORATION

Well Name: PPU FED 10-26D-12-16

Api No: 43-007-31406 Lease Type: FEDERAL

Section 26 Township 12S Range 16E County CARBON

Drilling Contractor CRAIG'S ROUSTABOUT SERV RIG # 3

SPUDDED:

Date 08/21/08

Time 5:00 AM

How DRY

Drilling will Commence: _____

Reported by JOHN FINDLAY VIA E-MAIL

Telephone # _____

Date 08/21/08 Signed CHD

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 6

ENTITY ACTION FORM

Operator: Bill Barrett Corporation Operator Account Number: N 2165
Address: 1099 18th Street, Suite 2300
city Denver
state CO zip 80202 Phone Number: (303) 312-8134

Well 1

API Number	Well Name		QQ	Sec	Twp	Rng	County
4300731406	Peter's Point Unit Federal 10-26D-12-16		SESW	26	12S	16E	Carbon
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
<i>AB</i>	<i>99999</i>	<i>2470</i>	8/21/2008		8/25/08		
Comments: To be spud by Craig's Roustabout setting conductor pipe only. This well will not begin continuous drilling operations until September 2008. <i>WSTMVD BHL = NWSE</i>							

CONFIDENTIAL

Well 2

API Number	Well Name		QQ	Sec	Twp	Rng	County
4300731407	Peter's Point Unit Federal 11-26D-12-16		SESW	26	12S	16E	Carbon
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
<i>AB</i>	<i>99999</i>	<i>2470</i>	8/21/2008		8/25/08		
Comments: To be spud by Craig's Roustabout setting conductor pipe only. This well will not begin continuous drilling operations until September 2008. <i>WSTMVD BHL = NESW</i>							

CONFIDENTIAL

Well 3

API Number	Well Name		QQ	Sec	Twp	Rng	County
4300731408	Peter's Point Unit Federal 12-26D-12-16		SESW	26	12S	16E	Carbon
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
<i>AB</i>	<i>99999</i>	<i>2470</i>	8/21/2008		8/25/08		
Comments: To be spud by Craig's Roustabout setting conductor pipe only. This well will not begin continuous drilling operations until September 2008. <i>WSTMVD BHL = NWSW</i>							

CONFIDENTIAL

ACTION CODES:

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (Explain in 'comments' section)

Tracey Fallang

Name (Please Print)

Tracey Fallang

Signature

Environmental Analyst

Title

8/21/2008

Date

RECEIVED

AUG 25 2008

DIV. OF OIL, GAS & MINING

tfallang
CONFIDENTIAL

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

COPY

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-068

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other		7. If Unit of CA/Agreement, Name and/or No. Peter's Point/UTU-63014
2. Name of Operator Bill Barrett Corporation		8. Well Name and No. Peter's Point Unit Federal 10-26D-12-16
3a. Address 1099 18th Street, Suite 2300 Denver, CO 80202	3b. Phone No. (include area code) 303-312-8134	9. API Well No. 43-007-31406
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) SESW, 270' FSL, 1510' FWL Sec. 26, T12S-R16E		10. Field and Pool or Exploratory Area Peter's Point/Wasatch-Mesaverde
		11. Country or Parish, State Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	<u>Report</u>
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Weekly drilling activity report from 10/10/08-10/17/08 (report #'s 2-9).

RECEIVED
OCT 27 2008
DIV OF OIL, GAS & MINING

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)
Tracey Fallang

Title Regulatory Analyst

Signature *Tracey Fallang*

Date 10/17/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

REGULATORY DRILLING SUMMARY

WELLCORE

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/11/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 3

Depth At 06:00 : 1145.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 52

Morning Operations : DRILLING 8 3/4" HOLE W/ BIT #1, SPUD @3:30 AM, 10/11/08

Remarks :

DAYS SINCE LTA: 131 DAYS
 NOTE: BLM REP, Randy Knight Notified of Start-UP & BOP Test on Cell Phone @ 8:30 AM, 10/10/08
 SAFETY MEETING TOPIC: RIG MOVE, TRUCKS-BLIND SPOTS, NU & Press TESTING, PU BHA.

DRILL WATER: USED DAILEY= 1360 Bbl- TOTAL USED= 1360 Bbls

DIESEL: on Loc:= 5210 Gal - Dailey Use= 202 Gal.- Total Used= 369 Gal

Time To	Description
1:30 PM	RD, SKID W/ TRUCKS, RU
5:30 PM	NU BOP'S, PU KELLEY, On Daywork @13:30, ON 10/10/08
10:00 PM	PR.Test W/ Single Jack, Mark, Test PIPE Blind Rams, Choke Line, Kill Line, Upper Kelley, Lower Kelley, Safety Valves, Choke Manifold, 250# Low Pr for 5 Min & 3000# High Press for 10 Min ea Test, P.T. Annular 250# Lo & 1500# Hi, PT Csg 1500# For 30 Min, Done Accumulator Test, Nitrogen, AIR Pump, Electric Pump. Time to Regain Press= 1 MIN 45 SEC, Pre Chg Press Drop Nitrogen Bottles= 900#, 1600# Remaining Press on Test, Install Wear Bushing
11:30 PM	PU BIT #1, MOTOR, MWD Tools, LOAD & SCRIBE TOOLS, PU MONEL DC
2:00 AM	TIH PU 4.5", SWDP, TAG CMT @920 FT, INSTAL ROT HEAD RUBBER
3:30 AM	DRILL PLUG, Float, CMT, Guide Shoe @1033'
6:00 AM	DRILL 8 3/4" HOLE W/ BIT #1 F/1033'-1145'

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/10/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 2

Depth At 06:00 : 1033.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 51

Morning Operations : RD PREP RIG FOR SKID TO THIS WELL

Remarks :

DAYS SINCE LTA: 130 DAYS

SAFETY MEETING TOPIC: CUT DRILL LINE, RDRT, CONFINED SPACES. RIG MOVE, TRUCKS-BLIND SPOTS

DRILL WATER: USED DAILEY= 0000 Bbl- TOTAL USED= 0000 Bbls

DIESEL: on Loc:= 1587 Gal - Dailey Use= 167 Gal.- Total Used= 167 Gal

Time To	Description
7:00 AM	CUT DRILL LINE
6:00 PM	PREPARE RIG FOR SKID & RIG REPAIR'S: IE: CHANGE OUT VALVES & CHICKANS ON GUN LINE, REPAIR LEAKS IN SUCTION LINES FOR HOPPER & GUN LINES, WELDER USED FOR SOME OF THESE REPAIRS ON DAY TOUR
6:00 AM	RD & PREPARE RIG TO SKID TO THIS WELL, NOTE: DAWN TRUCKING TO BE ON LOC AT DAYLIGHT TO SKID RIG, 10/10/08

REGULATORY DRILLING SUMMARY

WELLCORE

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/13/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 5

Depth At 06:00 : 3985.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 54

Morning Operations : DRILLING W/ 8 3/4" BIT #1 @3985 Ft

Remarks :

DAYS SINCE LTA: 133 DAYS
 SAFETY MEETING TOPIC: Cold Weather, BOP DRILL
 Day Tour= 1 Min-40 Sec,- MIXING CHEMICALS, BOP
 DRILL NITE= 1 MIN 20 SEC
 DRILL WATER: USED DAILEY= 800 Bbl- TOTAL USED=
 2160 Bbls
 DIESEL: on Loc:= 3347 Gal - Dailey Use= 1097 Gal.- Total
 Used= 2272 Gal Bit #1 Mud Motor, .16/3.3/Adj-SN:2003
 ; dailey hrs= 24.0 - Total hrs= 50.5
 NOTE: Started Boiler 10/12/08
 ACC PRESS=2800#-ANN PRESS=1200#- Manifold Press=
 1300#

Time To	Description
6:00 AM	DRILL From 2692 Ft to 3985 Ft With MWD SURVEYS, ROTATING w/ SLIDES AS NEEDED

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/12/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 4

Depth At 06:00 : 2692.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 53

Morning Operations : DRILLING W/ BIT #1 @ 2692 FT

Remarks :

DAYS SINCE LTA: 132 DAYS
 SAFETY MEETING TOPIC: FORKLIFT, BOP DRILL Day
 Tour= 1 Min-35 Sec, COLD WEATHER, BOP DRILL NITE=
 1 MIN 20 SEC
 DRILL WATER: USED DAILEY= 0 Bbl- TOTAL USED=
 1360 Bbls
 DIESEL: on Loc:= 4404 Gal - Dailey Use= 806 Gal.- Total
 Used= 1175 Gal Bit #1 Mud Motor, .16/3.3/Adj-SN:2003
 ; dailey hrs= 24.0 - Total hrs= 26.5

Time To	Description
6:00 AM	DRILL From 1145 Ft to 2692 Ft With MWD SURVEYS, ROTATING w/ SLIDES AS NEEDED

REGULATORY DRILLING SUMMARY

WELLCORE

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/15/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 7

Depth At 06:00 : 5964.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 56

Morning Operations : DRILLING W/ 8 3/4" BIT #1 @5964 Ft

Remarks :

DAYS SINCE LTA: 135 DAYS
 SAFETY MEETING TOPIC:S. Mtg on BOP DRILL, Bop. drill
 Day Tour= 1 Min-55 Sec,- FCT PIPE RAMS & Annular
 Preventer, Mix Mud, BOP DRILL NITE= 2 MIN 13 SEC
 DRILL WATER: USED DAILEY= 560 Bbl- TOTAL USED=
 2720 Bbls
 DIESEL:on Loc.= 4806 Gal - Dailey Use= 1342 Gal.- Total
 Used= 4813 Gal - -Bit #1 Mud Motor,.16/3.3/Adj-SN:2003
 ; dailey hrs= 23.5 -Total hrs= 97.5 hr
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2700#-ANN PRESS=1100#- Manifold Press=
 1400#
 Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28'
 Mkr Jt for Total of 199 Jts 4.5", 11.6#, I-80, LTC PROD
 CSG on Loc= 8350 FT Total 4 1/2"

Time To	Description
5:30 PM	DRILL From 5125 Ft to 5618 Ft With MWD SURVEYS, ROTATING w/ SLIDES AS NEEDED
6:00 PM	RIG SERVICE + FUC Test Pipe Rams & Annular
6:00 AM	DRILL F/ 5618 Ft to 5964 Ft, SURV,ROT,Slide

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/14/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 6

Depth At 06:00 : 5125.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 55

Morning Operations : DRILLING W/ 8 3/4" BIT #1 @5125 Ft

Remarks :

DAYS SINCE LTA: 134 DAYS
 SAFETY MEETING TOPIC:Cold Weather Boiler, BOP
 DRILL Day Tour= 1 Min-48 Sec,- FCT PIPE RAMS,
 MIXING CHEMICALS, BOP DRILL NITE= 2 MIN 13 SEC
 DRILL WATER: USED DAILEY= 0 Bbl- TOTAL USED=
 2160 Bbls
 DIESEL:on Loc.= 6148 Gal - Dailey Use= 1199 Gal.- Total
 Used= 3471 Gal Bit #1 Mud Motor, .16/3.3/Adj-SN:2003
 ; dailey hrs= 23.5 - Total hrs= 74.0
 NOTE: Started Boiler 10/12/08
 ACC PRESS=2650#-ANN PRESS=1300#- Manifold Press=
 1450#

Time To	Description
3:00 PM	DRILL From 3985 Ft to 4486 Ft With MWD SURVEYS, ROTATING w/ SLIDES AS NEEDED
3:30 PM	RIG SERVICE + Function Test Pipe Rams
6:00 AM	DRILL F/ 4486 Ft to 5125 Ft, SURV,ROT,Slide

REGULATORY DRILLING SUMMARY

WELLCORE

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/17/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 9

Depth At 06:00 : 6941.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 58

Morning Operations : DRILLING W/ BIT #1 @6941 FT

Remarks :

Time To	Description
5:30 PM	DRILL FROM 6385 Ft to 6689 Ft, MWD SURVEYS, SLIDES & ROTATING
6:00 PM	RIG SERVICE, Function Test Pipe Rams & Annular Preventer
6:00 AM	DRILL F/ 6689 Ft to 6941 Ft W/ MWD Surveys, Rotating & Slide to Drop Angle

DAYS SINCE LTA: 137 DAYS
 SAFETY MEETING TOPIC:S: Working on Pumps, Bop drill Day Tour= 1 Min-48 Sec,- FCT PIPE RAMS & Annular, MSDS Sheets, Bop Drill Nite= 1 Min 55 Sec
 DRILL WATER: USED DAILEY= 850 Bbl- TOTAL USED= 3890 Bbls
 DIESEL: on Loc:= 4270 Gal - Dailey Use= 1262 Gal.- Total Used= 8171 Gal - Bit #1 Mud Motor., 16/3.3/Adj-SN:2003 ; dailey hrs= 23.5 -Total hrs= 144.5 hr
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2800#-ANN PRESS=1400#- Manifold Press= 1700#
 Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD
 CSG on Racks= 8350 FT Total 4 1/2"
 (Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/16/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 8

Depth At 06:00 : 6385.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 57

Morning Operations : DRILLING W/ BIT#1 @6385 Ft

Remarks :

Time To	Description
5:30 PM	DRILL F/5964 Ft to 6185 Ft
6:00 PM	RIG SERVICE
6:00 AM	DRILL F/ 6185 Ft to 6385' + SURVEY W/ MWD, ROTATING & SLIDING AS NEEDED

DAYS SINCE LTA: 136 DAYS
 SAFETY MEETING TOPIC:S.CONNECTIONS, Bop drill Day Tour= 1 Min-50 Sec,- FCT PIPE RAMS ,PPE, Boiler, BOP DRILL NITE= 2 MIN 13 SEC
 DRILL WATER: USED DAILEY= 320 Bbl- TOTAL USED= 3040 Bbls
 DIESEL: on Loc:= 2710 Gal - Dailey Use= 2096 Gal.- Total Used= 6909 Gal - Bit #1 Mud Motor., 16/3.3/Adj-SN:2003 ; dailey hrs= 23.5 -Total hrs= 121.0 hr
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2800#-ANN PRESS=1300#- Manifold Press= 1400#
 Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD
 CSG on Racks= 8350 FT Total 4 1/2"
 (Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

COPY

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input checked="" type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

This sundry is being submitted as subsequent notification of a surface casing repair that was completed on this well. Verbal notification of the damage was provided to Randy Knight and verbal approval received from Matt Baker.

Attached please find information as per the condition of approval explaining why there have been a large number of surface casing repairs.

14. I hereby certify that the foregoing is true and correct.
Name (Printed/Typed)
Tracey Fallang

Title Regulatory Analyst

Signature *Tracey Fallang*

Date 10/24/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

RECEIVED

OCT 27 2008

DIV. OF OIL, GAS & MINING

REGULATORY DRILLING SUMMARY

WELLCORE

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/20/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 12

Depth At 06:00 : 7667.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008

Days From Spud : 61

Morning Operations : Tooh to unplug bit

Remarks :

DAYS SINCE LTA: 141 DAYS

Safety Meeting Topic's: , Spinning chain

DRILL WATER: USED DAILEY= 240 Bbl- TOTAL USED= 4130 Bbls

DIESEL: on Loc:= 2261 Gal - Dailey Use= 674 Gal.- Total Used= 12268 Gal - Bit #1 drlg motor, .13-Adj-sn:2003

;dailey hrs= 11 -total=155.5 hr-out @7144' 7 7/8" bit #2, Motor, 6.5"- .16-adj-sn 6292: dailey= 0 hr- Ttl= 18.5 hrs failed

Motor #3 6.25 .16 Ser # 6321 Hrs= 2.5

NOTE: Started Boiler 10/12/08 Run 24 hr ea Day

ACC PRESS=2800#-ANN PRESS=1400#- Manifold Press= 1700#

(Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD CSG on Racks= 8350 FT Total 4 1/2")

(Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

Time To	Description
7:00 AM	XO bit & motor, Function blind rams
10:00 AM	Tih to 7545 wash 45' to btm 3' fill
12:30 PM	Drill f/ 7590 to 7666, 34 vis 9.3 wt
4:30 PM	Circ & work pipe while waiting on tools to repair hole in surface Csg, The hole is in the csg starting @ the wellhead weld and runs straight down 4" f/ weld, We cleaned out the cellar 6' f/ ground level and did not find any other damaged areas in csg.
7:30 PM	Tooh into surface csg timed to tool arival.
1:30 AM	Repair hole w/ csg patch starting @ wellhead weld 8" wide & 24" long.
3:30 AM	Tih to 4000' fill pipe, plugged string.
6:00 AM	Tooh to unplug string

Surface Casing Repair Details

BBC believes the reason there has been a significant number of surface casing repairs is due to the bucket rig drilling the conductor hole without having the boom level. The conductor was subsequently cemented in the hole at an angle and the surface casing was then cemented in the hole while hanging in the elevators of the air rig. The angle in the conductor pipe pushed the surface casing over to one side of the conductor while the surface cement was setting up. Even though the cuts on the surface pipe and conductor were level, the surface casing was set at an angle severe enough that the Kelly and Saber-Sub wore on the wall of the surface casing for the entirety of the drilling operation, thus wearing a hole in the surface casing.

Steps implemented to avoid Surface CSG damage.

- 1) Install Magnet in possum belly and check for shavings after every connection, or every half hour and record findings in drilling notes on Pason.
- 2) If metal shavings appear on magnet install Non-Rotating Protectors to keep the Kelly, Saber-Sub, and tool joint connections off of the Surface Casing.
- 3) Install new Kelly and Saber-Sub on all rigs to ensure the equipment is in optimum operating condition.


It is significant enough to note that the Service Company contracted to drill the conductor holes on the Prickly Pear 3-22 pad, Prickly Pear 21-2 pad, and Peter's Point 14-26 pad went through three bucket rig operators on the Prickly Pear 3-22 pad. That same operator then went on to assist drilling the conductors on the Prickly Pear 21-2 and Peter's Point 14-26 pads. It is our opinion that the

Attachments:

- Pictures showing Conductor pipe set at an angle
- Pictures showing Surface Casing Pulled to one side of conductor
- Spreadsheet containing Well and Rig data

Well Name	PAD	Bucket RIG	Air RIG	Drilling RIG	SPUD DATE	RR Date (From Pad)	Comments
Prickly Pear UF 14-15D-12-15	PrPr 3-22	Craigs Roustabout #1	Craig's Roustabout #3	Patterson #12	8/17/2008	8/28/2008	Wore hole in 9 5/8" CSG
Prickly Pear UF 6-22D-12-15		Craigs Roustabout #1	Craig's Roustabout #3	Patterson #12	8/29/2008	9/8/2008	Wore hole in 9 5/8" CSG
Prickly Pear UF 13-15D-12-15		Craigs Roustabout #1	Craig's Roustabout #3	Patterson #12	9/10/2008	9/22/2008	Wore hole in 9 5/8" CSG
Prickly Pear UF 4-22D-12-15		Craigs Roustabout #1	Craig's Roustabout #3	Patterson #12	9/23/2008	10/3/2008	Installed Non-Rotating Protectors
Prickly Pear UF 12-21D-12-15	PrPr 21-2	Craigs Roustabout #1	Craig's Roustabout #5	Patterson #51	9/16/2008	9/26/2008	Well was drilled w/out hole in surface CSG
Prickly Pear UF 11-21D-12-15		Craigs Roustabout #1	Craig's Roustabout #5	Patterson #51	9/27/2008	10/6/2008	Well was drilled w/out hole in surface CSG
Prickly Pear UF 4-21D-12-15		Craigs Roustabout #1	Craig's Roustabout #5	Patterson #51	10/7/2008	10/17/2008	Well was drilled w/out hole in surface CSG
Prickly Pear UF 6-21D-12-15		Craigs Roustabout #1	Craig's Roustabout #5	Patterson #51	10/18/2008	10/28/2008	Wore hole in 9 5/8" CSG
Prickly Pear UF 3-21D-12-15		Craigs Roustabout #1	Craig's Roustabout #5	Patterson #51	10/30/2008	11/9/2008	
Prickly Pear UF 5-21D-12-15		AAA #4	Craig's Roustabout #5	Patterson #51	11/11/2008	11/21/2008	
Peter's Point UF 3-35D-12-16	PtPt 14-26	Craigs Roustabout #1	Pro Petro #4	SST #2	9/9/2008	9/19/2008	Well was drilled w/out hole in surface CSG
Peter's Point UF 15-26D-12-16		Craigs Roustabout #1	Pro Petro #4	SST #2	9/20/2008	9/30/2008	Well was drilled w/out hole in surface CSG
Peter's Point UF 13-26D-12-16		Craigs Roustabout #2	Pro Petro #4	SST #2	9/30/2008	10/9/2008	Well was drilled w/out hole in surface CSG
Peter's Point UF 10-26D-12-16		Craigs Roustabout #1	Pro Petro #4	SST #2	10/11/2008	10/23/2008	Wore hole in 9 5/8" CSG
Peter's Point UF 11-26D-12-16		Craigs Roustabout #2	Pro Petro #4	SST #2	10/24/2008	11/6/2008	
Peter's Point UF 12-26D-12-16		Craigs Roustabout #1	Pro Petro #4	SST #2	11/8/2008	11/21/2008	

	Drilling Operations Complete
	Currently Being Drilled
	Conductor and Surface Casing is Set

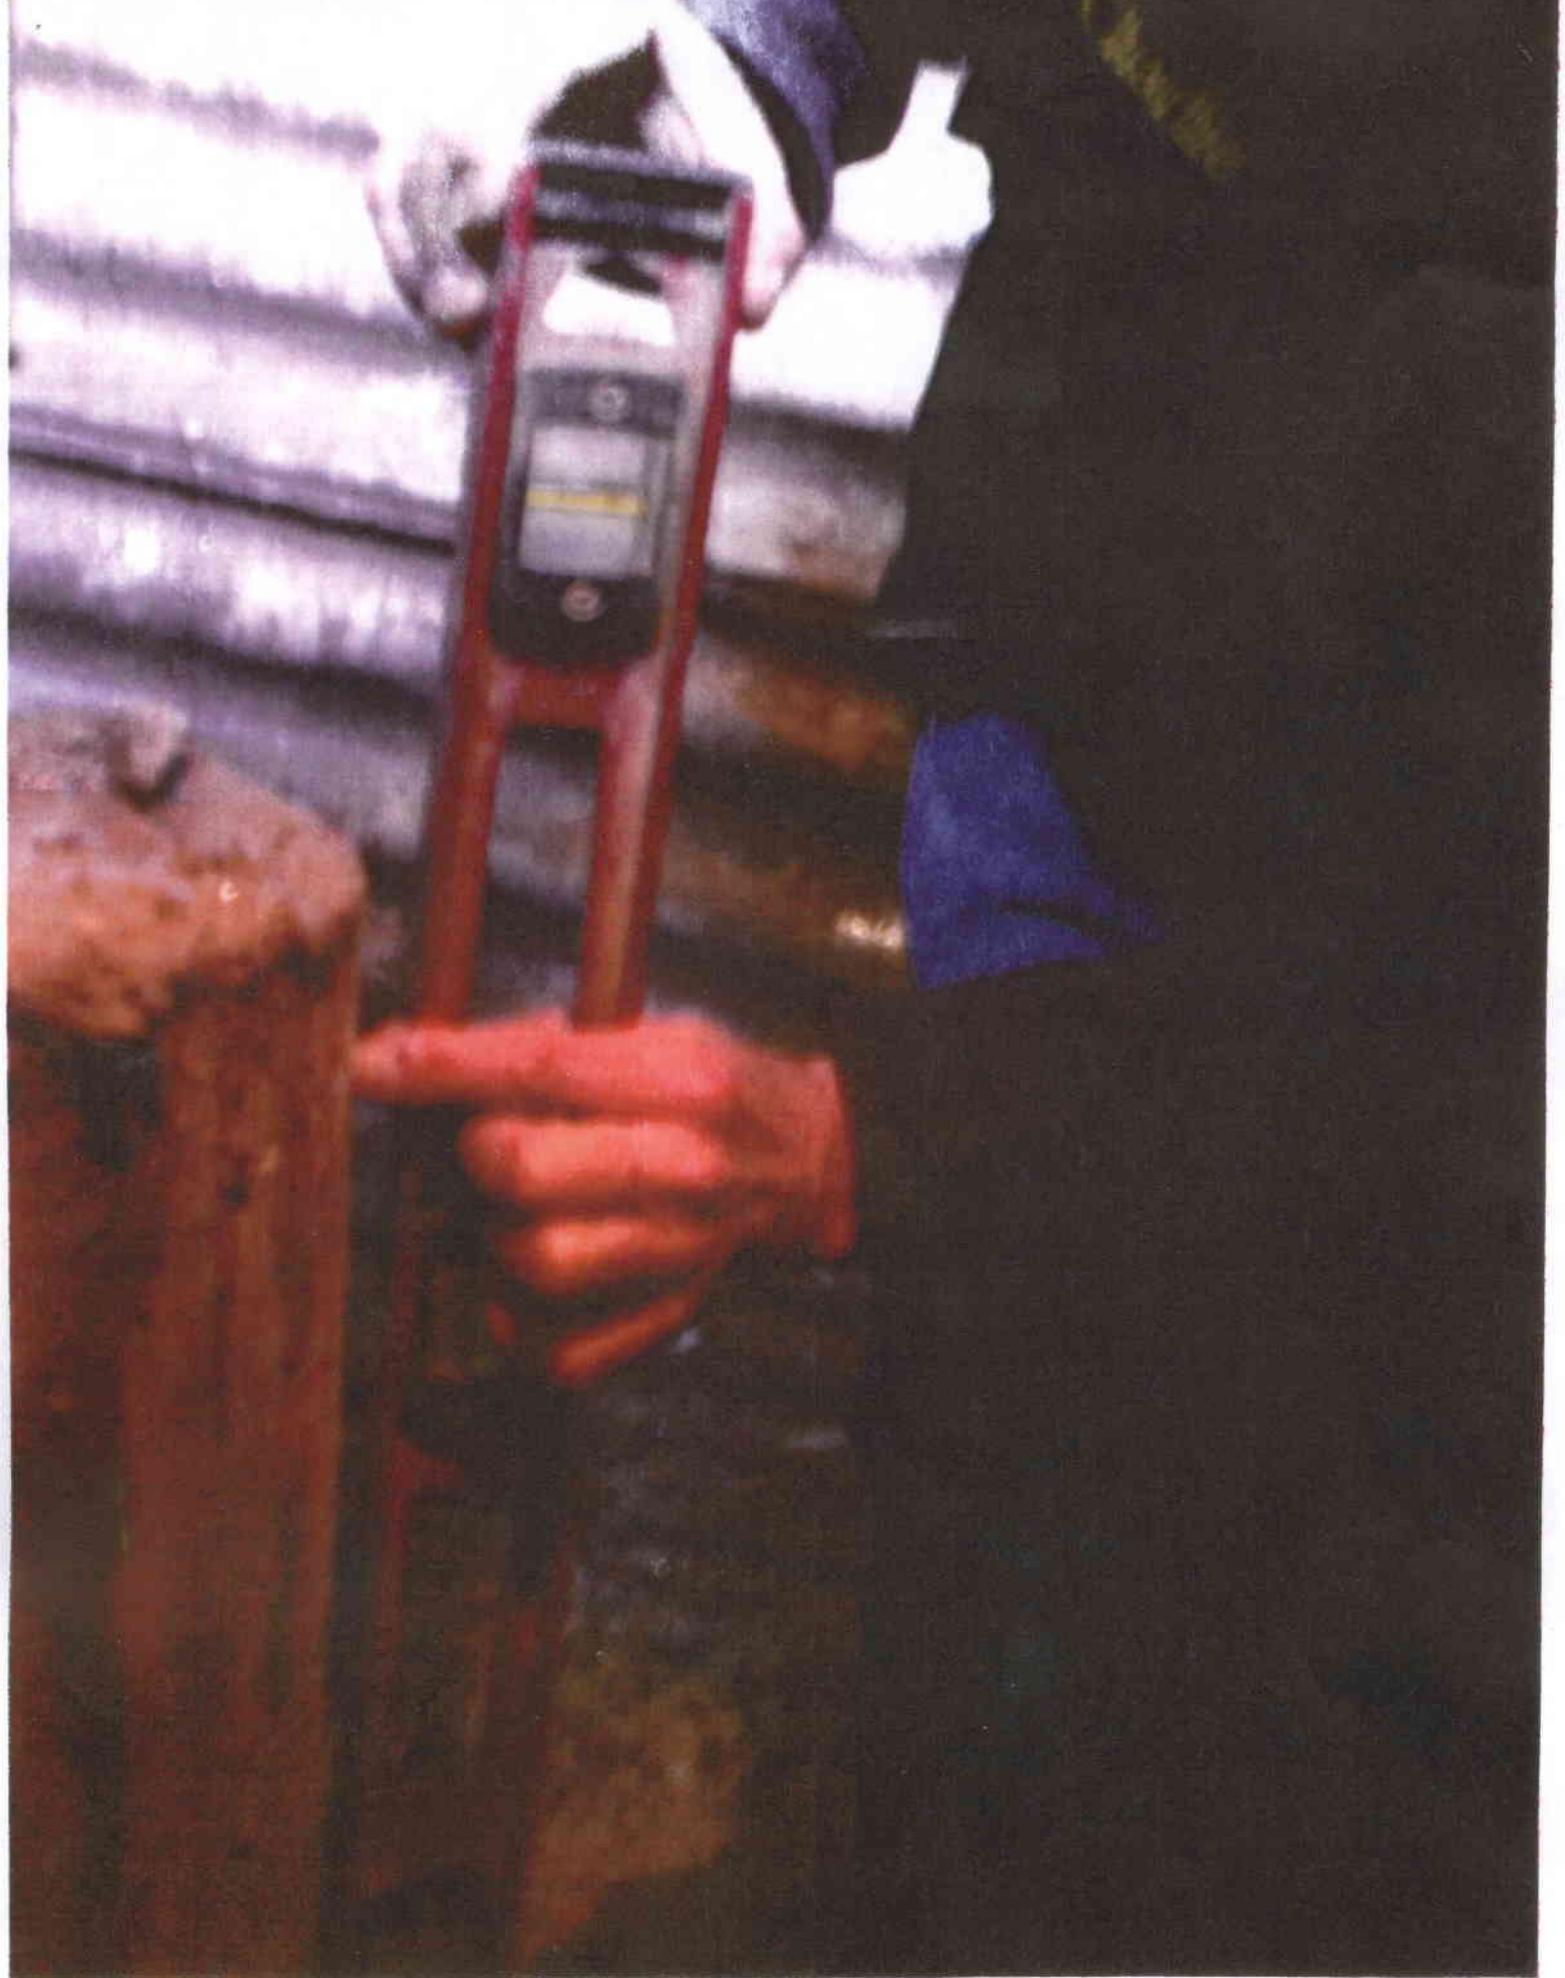



UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL

COPY

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE - Other instructions on page 2.

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Report _____
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Weekly drilling activity report from 10/18/08-10/23/08 (report #'s 10-15). Final drilling report, waiting on completion (2009). No further reports until operations resume.

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)
Tracey Fallang

Title Regulatory Analyst

Signature

Tracey Fallang

Date 10/24/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

RECEIVED

(Instructions on page 2)

OCT 27 2008

DIV. OF OIL, GAS & MINING

REGULATORY DRILLING SUMMARY

WELLCORE

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/19/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 11

Depth At 06:00 : 7590.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 60

Morning Operations : Change out bit & motor.

Remarks :

DAYS SINCE LTA: 140 DAYS
 Safety Meeting Topic's : Tripping pipe
 DRILL WATER: USED DAILEY= 240 Bbl- TOTAL USED= 4130 Bbls
 DIESEL: on Loc= 2835 Gal - Dailey Use= 1703 Gal.- Total Used= 11634 Gal - Bit #1 drlg motor, 13-Adj-sn:2003 ;dailey hrs= 11 -total=155.5 hr-out @7144'
 7 7/8" bit #2, Motor, 6.5"-16-adj-sn 6292: dailey= 0 hr- Ttl= 18.5 hrs failed
 Motor #3 6.25 .16 Ser # 6321 Hrs=
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2800#-ANN PRESS=1400#- Manifold Press= 1700#
 (Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD CSG on Racks= 8350 FT Total 4 1/2")
 (Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

Time To	Description
7:00 AM	FIN TIH BIT #2, BREAK CIRC
5:30 PM	Drlg f/ 7144 to 7478.
6:00 PM	Rig service, Function pipe rams.
2:00 AM	Drill f/ 7478 to 7590, Mud motor started spiking & bit slowed to 11' per hr
6:00 AM	Tooh f/ bit & Mtr.

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/18/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 10

Depth At 06:00 : 7144.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 59

Morning Operations : TRIPPING IN HOLE W/ 7 7/8" PDC BIT #2

Remarks :

DAYS SINCE LTA: 138 DAYS
 Safety Meeting Topic's: Fall Protection, Bop drill Day Tour= 1 Min-48 Sec,- FCT Blind Rams, TRIPPING, WORK TIGHT HOLE, Bop Drill Nite= 1 Min 55 Sec
 DRILL WATER: USED DAILEY= 0 Bbl- TOTAL USED= 3890 Bbls
 DIESEL: on Loc= 4538 Gal - Dailey Use= 1760 Gal.- Total Used= 9931 Gal - Bit #1 drlg motor, 13-Adj-sn:2003 ;dailey hrs= 11 -total=155.5 hr-out @7144'
 7 7/8" bit #2, Motor, 6.5"-16-adj-sn 6292: dailey= 0 hr- Ttl= 0 hrs
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2800#-ANN PRESS=1400#- Manifold Press= 1700#
 Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD CSG on Racks= 8350 FT Total 4 1/2"
 (Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

Time To	Description
5:00 PM	DRILL F/6041'-7144', ROT & SLIDE
1:00 AM	PUMP PILL, TOH, Work Tight Hole 4408'-4304'
2:00 AM	LD Bit #1, DIR TOOLS & MUD MOTOR, FCT BLIND RAMS
6:00 AM	PU 7 7/8" BIT #2 & 6 1/2" DRLG MOTOR & TIH

REGULATORY DRILLING SUMMARY

WELLCORE

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/21/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 13

Depth At 06:00 : 8161.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 62

Morning Operations : Circ to short trip

Remarks :

DAYS SINCE LTA: 142 DAYS
 Safety Meeting Topic's: , Working with steam
 DRILL WATER: USED DAILEY= 240 Bbl- TOTAL USED= 4130 Bbls
 DIESEL: on Loc:= 2261 Gal - Dailey Use= 674 Gal.- Total Used= 12268 Gal - Bit #1 drlg motor, .13-Adj-sn:2003 ;dailey hrs= 11 -total=155.5 hr-out @7144'
 7 7/8" bit #2, Motor, 6.5"-.16-adj-sn 6292: dailey= 0 hr- Ttl= 18.5 hrs failed
 Motor #3 6.25 .16 Ser # 6321 Hrs= 2.5
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2800#-ANN PRESS=1400#- Manifold Press= 1700#
 (Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD CSG on Racks= 8350 FT Total 4 1/2")
 (Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

Time To	Description
8:00 AM	Tooh to unplug Motor, Function blind rams.
1:00 PM	Motor locked up, Wait on new motor.
5:00 PM	Pu new Mtr, Tih to 7626 wash 45' to Btm 2' fill
5:30 AM	Drill f/ 7666 to 8161, TD
6:00 AM	Circ & cond f/ short trip, 42 vis 9.4 wt 6.8 fi

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/20/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 12

Depth At 06:00 : 7667.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 61

Morning Operations : Tooh to unplug bit

Remarks :

DAYS SINCE LTA: 141 DAYS
 Safety Meeting Topic's: , Spinning chain
 DRILL WATER: USED DAILEY= 240 Bbl- TOTAL USED= 4130 Bbls
 DIESEL: on Loc:= 2261 Gal - Dailey Use= 674 Gal.- Total Used= 12268 Gal - Bit #1 drlg motor, .13-Adj-sn:2003 ;dailey hrs= 11 -total=155.5 hr-out @7144'
 7 7/8" bit #2, Motor, 6.5"-.16-adj-sn 6292: dailey= 0 hr- Ttl= 18.5 hrs failed
 Motor #3 6.25 .16 Ser # 6321 Hrs= 2.5
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2800#-ANN PRESS=1400#- Manifold Press= 1700#
 (Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD CSG on Racks= 8350 FT Total 4 1/2")
 (Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

Time To	Description
7:00 AM	XO bit & motor, Function blind rams
10:00 AM	Tih to 7545 wash 45' to btm 3' fill
12:30 PM	Drill f/ 7590 to 7666, 34 vis 9.3 wt
4:30 PM	Circ & work pipe while waiting on tools to repair hole in surface Csg, The hole is in the csg starting @ the wellhead weld and runs straight down 4" f/ weld, We cleaned out the cellar 6' f/ ground level and did not find any other damaged areas in csg.
7:30 PM	Tooh into surface csg timed to tool arival.
1:30 AM	Repair hole w/ csg patch starting @ wellhead weld 8" wide & 24" long.
3:30 AM	Tih to 4000' fill pipe, plugged string.
6:00 AM	Tooh to unplug string

REGULATORY DRILLING SUMMARY

WELLCORE

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/23/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 15

Depth At 06:00 : 8161.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 64

Morning Operations : Rig down to skid onto the 11-26D-12-16

Remarks :

DAYS SINCE LTA: 144 DAYS
 Safety Meeting Topic's: , PPE
 DRILL WATER: USED DAILEY= 290 Bbl- TOTAL USED= 4940 Bbls
 DIESEL: on Loc:= 4003 Gal - Dailey Use= 803 Gal.- Total Used= 13771 Gal - Bit #1 drlg motor, 13-Adj-sn:2003 ;dailey hrs= 11 -total=155.5 hr-out @7144'
 7 7/8" bit #2, Motor, 6.5"-16-adj-sn 6292: dailey= 0 hr- Ttl= 18.5 hrs failed
 Motor #3 6.25 .16 Ser # 6321 Hrs= 15, TD
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2800#-ANN PRESS=1400#- Manifold Press= 1700#
 (Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD CSG on Racks= 8350 FT Total 4 1/2")
 (Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

Time To	Description
9:00 AM	Lay down Dp & Bha, Pull wear ring.
3:00 PM	Hold safety meeting, Rig up Franks & run 194 joints of 4.5" 11.6# I-80 casing, Tagged bottom @ 8161'.
4:00 PM	Circ 4.5 csg, 50 vis, 9.5 wt, 6.0 fl
6:00 PM	Circ & rig up Halliburton, Very slow.
10:30 PM	Hold safety meeting, Pump 1670 sx 50/50 poz Cmt, Their computer was down so i have no cmt details, Bumped plug floats held, Had constant returns no cmt to surface.
12:00 AM	Nipple down & set slips, string wt 90k picked up & set slips @ 105k.
6:00 AM	Clean pits, Released rig @ 6:00 am 10/23/2008

Well : Peter's Point #10-26D-12-16

Phase/Area : West Tavaputs

Operations Date : 10/22/2008

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Report # : 14

Depth At 06:00 : 8161.00

Estimated Total Depth :

Surface Location : SESW-26-12S-16E-W26M

Spud Date : 8/20/2008 Days From Spud : 63

Morning Operations : Lay down drill pipe & BHA

Remarks :

DAYS SINCE LTA: 143 DAYS
 Safety Meeting Topic's: , PPE
 DRILL WATER: USED DAILEY= 520 Bbl- TOTAL USED= 4650 Bbls
 DIESEL: on Loc:= 5061 Gal - Dailey Use= 700 Gal.- Total Used= 12968 Gal - Bit #1 drlg motor, 13-Adj-sn:2003 ;dailey hrs= 11 -total=155.5 hr-out @7144'
 7 7/8" bit #2, Motor, 6.5"-16-adj-sn 6292: dailey= 0 hr- Ttl= 18.5 hrs failed
 Motor #3 6.25 .16 Ser # 6321 Hrs= 15, TD
 NOTE: Started Boiler 10/12/08 Run 24 hr ea Day
 ACC PRESS=2800#-ANN PRESS=1400#- Manifold Press= 1700#
 (Recv'd 195 Jts 4.5"-11.6#-I-80-LTC Rng III Prod Csg+ 1 28' Mkr Jt for Total of 198 Jts 4.5", 11.6#, I-80, LTC PROD CSG on Racks= 8350 FT Total 4 1/2")
 (Total of 9 Jts 4.5"-11.6#-I-80-LTC, Rng 3 off Racks)= 207 jts on Loc

Time To	Description
7:00 AM	Circ & cond f/ loggs, vis 40 9.3 wt 6.0 fl
11:30 AM	Tooh f/ loggs SLM= 8159.52
12:00 PM	Rig service, function pipe & blind rams
5:00 PM	Log open hole w/ Halliburton Depth= 8156, RWCH, DSN/SDL, HRI.
9:00 PM	Tih to Lay down Dp & BHA, Wash 30' to btm no fill.
10:30 PM	Circ & cond f/ 4.5 csg, wt 9.3, vis 41, fl 6.0
6:00 AM	Hold safety meeting, Rig up Franks Westates & lay down Dp & BHA.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

COPY

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE - Other instructions on page 2.

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input checked="" type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Casing repairs to be performed as follows (verbal notification provided to Randy Knight on 10/20):

- 1) TOOH and LD DIR tools, Bit, MM
- 2) TIH w/ 9 5/8" Bridge Plug
- 3) Set Bridge Plug @ 950'
- 4) TOOH with Bridge Plug Retrieving Head
- 5) Nipple down BOP
- 6) Jack Hammer 9' out of bottom of cellar to find casing w/ good integrity
- 7) Cut CSG
- 8) Weld on new CSG
- 9) Weld on Slip Collar
- 10) Rough Cut 9 5/8" CSG @ grade level
- 11) Set new CSG Head and weld on
- 12) Nipple up BOP
- 13) Test BOP
- 14) TIH w/ Retrieving head
- 15) TOOH w/ Bridge plug
- 16) Pick up Bit, MM, DIR tools
- 17) TIH w/ Bit, MM, DIR tools

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)
Tracey Fallang

Title Regulatory Analyst

Signature

Tracey Fallang

Date 10/20/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

D. K. [Signature]

Title

Reg. Eng.

Date

11/20/08

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

DOGAN

Federal Approval Of This
Action Is Necessary

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

trialang
CONFIDENTIAL

Form 3160-5
(August 2007)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681
6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well
 Oil Well Gas Well Other
2. Name of Operator
Bill Barrett Corporation
3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202
3b. Phone No. (include area code)
303-312-8134
4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014
8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16
9. API Well No.
43-007-31406
10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde
11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Report
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

No activity.

**** STATE ONLY ****

14. I hereby certify that the foregoing is true and correct.
Name (Printed/Typed)
Tracey Fallang
Title Regulatory Analyst
Signature *Tracey Fallang*
Date 11/21/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by
Title
Date
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction?

RECEIVED

NOV 25 2008

DIV. OF OIL, GAS & MINING

(Instructions on page 2)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

tfallang
CONFIDENTIAL

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

COPY

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE - Other instructions on page 2.

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	<u>Report</u>
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Weekly completion activity from 11/22/08-12/04/08 (report #1). Ran CBL, no further reports until completion operations resume (2009).

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)
Tracey Fallang

Title Regulatory Analyst

Signature *Tracey Fallang*

Date 12/04/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

RECEIVED

DEC 08 2008

REGULATORY COMPLETION SUMMARY



Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 11/26/2008

Report # : 1

AFE # : 15186D

Summary : Rig up Schlumberger EL Truck. Pick up CBL tool. RIH to 8062'. Log up to 850'. With 1000 PSI on CSG.CMT @ 1073'. POOH. Rig down.

End Time

Description

8:00 AM

SI

2:00 PM

Rig up Schlumberger EL Truck. Pick up CBL tool with 3.60" gauge ring. TIH to 8062'. Log up to 850'. With 1000 PSI on CSG. CMT @ 1072'. POOH. Lay tools down. Rig down.

11:59 PM

SI

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

tfallang
CONFIDENTIAL

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other		7. If Unit of CA/Agreement, Name and/or No. Peter's Point/UTU-63014
2. Name of Operator Bill Barrett Corporation		8. Well Name and No. Peter's Point Unit Federal 10-26D-12-16
3a. Address 1099 18th Street, Suite 2300 Denver, CO 80202	3b. Phone No. (include area code) 303-312-8134	9. API Well No. 43-007-31406
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) SESW, 270' FSL, 1510' FWL Sec. 26, T12S-R16E		10. Field and Pool or Exploratory Area Peter's Point/Wasatch-Mesaverde
		11. Country or Parish, State Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Report
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

No activity, waiting on completions.

STATE ONLY

RECEIVED
JAN 08 2009
DIV. OF OIL, GAS & MINING

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed) Tracey Fallang	Title: Regulatory Analyst
Signature: <i>Tracey Fallang</i>	Date: 01/05/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by	Title	Date
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

tfallang
CONFIDENTIAL

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well
 Oil Well Gas Well Other

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

2. Name of Operator
Bill Barrett Corporation

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Report
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

No activity, waiting on completions.

STATE ONLY

RECEIVED
FEB 05 2009
DIV. OF OIL, GAS & MINING

14. I hereby certify that the foregoing is true and correct.
Name (Printed/Typed)
Tracey Fallang

Title Regulatory Analyst

Signature *Tracey Fallang*

Date 02/02/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

COPY

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	<u>Report</u>
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Weekly completion activity report from 2/3/09 though 2/10/09 (report #'s 2-7).

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)

Tracey Fallang

Title Regulatory Analyst

Signature

Tracey Fallang

Date 02/10/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

RECEIVED

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

FEB 12 2009

(Instructions on page 2)

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/6/2009

Report # : 3

AFE # : 15186D

Summary	End Time	Description
SI. BWWC EL stage 1 P.R. Schlumberger frac stage 1 Clearfrac.	6:00 AM	SI.
BWWC EL stage 2 Stuck EL tools setting frac plug. Lowered Crane Worked EL line could not pull tools free. Pulled out of cable head with EL POOH. Rehead EL.	7:15 AM	BWWC EL stage 1 price River. PU 10 ft. perf guns. RIH correlate to short jt. run to perf depth Perforate @ 7950-7960 3 JSPF, 120 phasing, 19 gram charges, .390 holes. POOH turn well over to frac.
PU 3.265" gauge ring junkbasket, weight bars. RIH tag fill 4 ft. above EL tools. POOH. Ready equipment for Pomrenke to fish EL tools. SI.	8:15 AM	Schlumberger frac stage 1 Price River 70Q Clearfrac. Load & Break @ 5,290 PSI @ 5.1 BPM. Avg. Rate:20 BPM. Avg. Pressure:4141 PSI. Max. Rate:28.7 BPM. Max. Pressure : 4,942PSI. Total Fluid Pumped: 10,173 Gal. Total Sand in Formation:27,200 lb.(20/40 Jordan) Praxair CO2 Downhole:52 tons. ISIP:3550 PSI. Frac Gradient:.88 psi/ft. Successfully flushed wellbore with 30Q 10 bbl over flush with 500 gal. fluid cap.
	12:15 PM	BWWC EL stage 2 Price River PU HES CFP with Bio plug. and 9 ft. Perf guns. RIH correlate to short jt. run to setting depth set CFP @ 7880 ft. setting tool did not shear off frac plug. Worked EI couldnot free tools. Lowered Crane Warrior pulled out of cable head. POOH lay down Lub. Pulled off 2200 ft. EL line off truck that was bad. Rehead EL .
	2:15 PM	BWWC PU 3.625" gauge rin with junk basket and two weight bars. RIH correlate to short jt. run to 7835 tag fill on EL tools. 4 foot covering EL tools. POOH 100 ft. RIH tag same place. POOH lay down gauge ring junkbasket. Ready EL for fishen with Pomrenke EL.
	2:15 PM	Shut in wait on Pomrenke EL.

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/5/2009

Report # : 2

AFE # : 15186D

Summary	End Time	Description
SI. Rig BWWC & Schlumberger on fracq tree. Pressure test tree and casing to 6300 psi 10 mins. OK bleed off. SDFN	1:00 PM	SI
	2:00 PM	Rig up Schlumberger. and Black Warrior EL
	2:20 PM	Pressure test frac tree and casing to 6300 psi. held for 10 mins. OK. Bleed off.
	2:20 PM	SDFN

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/7/2009

Report # : 4

AFE # : 15186D

Summary	End Time	Description
SI. MIRU Pomrenke EL and Black Warrior. PU over shot Jars, weight bars. RIH flow casing. catch BWWC EL tools. Frac plug had set and guns were stuck in sand. Setting sleeve had sand in it. Lay down over shot and perf guns. Rig down Pomrenke EL and release. Rig Black Warrior to perf stage 2. Pressure test frac plug. to 5850 psi. held. BWWC RIH perf stage 2. Safety Meeting. Schlumberger frac stage 2 P.R. BWWC EL stage 3. Stuck perf guns and CFP @ 7750 ft. Shut in well. wait on bio plug to desolve before opening casing to flow.	3:00 AM 4:30 AM 5:30 AM 6:30 AM 7:30 AM 9:30 AM	SI. Move in Pomrenke EL and Black Warrior crane and lub. to fish wire line tools. Pomrenke PU 1-7/16" over shot, jars, weight bars. RIH with tools start flowing casing through Opsco flow back equip. tag EL tools @ 7854. latched on tool picked up tools free, set down on tools. Picked up start out of hole. POOH lay down perfguns and fishen tools. lay down lub rig down Pomrenke EL and release Rig Black Warrior EL and equipment. BWWC EL stage 3 P.R. PU HES CFP with 13 ft perf guns. RIH correlate to casing collars. seen obstuction in casing at 5700 ft. Ran in to 6800 ft. POOH showed EL tools dragging on casing pulling up hole. POOH with EL 1500 ft. Ran back in hole to 7200 ft no problems running in hole. . POOH 1000 ft. perf guns and showed drag on casing wall. Ran in hole to 7780 ft. PU did not seen drag on EL tools. set on plug depth. set CFP stuck on plug or sanded in tools. could not free tools. SWEFN to let Bio plug desolve before flowing casing.
	8:30 AM	Schlumberger frac stage 2 Price River 70 Q Clearfrac. Load & Break @ 3420 psi. @ 5.1 BPM. Avg. Sultry Rate: BPM. Avg. Pressure: PSI. Max. rate: BPM. Max. Pressure: PSI. Total Fluid Pumped; Gal. Total Sand in Formation. lb.(20/40 Jordan) Praxair CO2 Downhole: tons. ISIP:PSI. Frac Gradient:: psi/ft. Successfully flushed wellbore with 20 bbl over flush cut CO2 pumped wellbore vol.with 2% KCL water.
	2:30 PM	Stuck in well with EL tools.
	11:59 PM	Shut in for night. wait on Bio ball to desolve. to try to flow casing by perf guns.

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/8/2009

Report # : 5

AFE # : 15186D

Summary : SICP: 3200. Wire line stuck in well. Work EL. no movment, Open casing through Opsco flow back. perf guns free. POOH drag in sand up to 6300 ft. came free. POOH. lay down perf guns. Shut in. RDMO Black Warrior EL. Schlumberger frac equipment to make room for Coil tubing unit. to drill out.

End Time

Description

7:00 AM

SICP: 3200

7:05 AM

Black Warrior EL stuck in well over night.

8:00 AM

BWWC. work EI perf guns stuck. Open casing to flow tanks through Opsco. perf guns came free. POOH had drag up to 6300 fct. came free. POOH lay down tools.

8:05 AM

Shut in

10:00 AM

Rigged down BWWC EL and crane, rigged down Schlumberger frac equipment to make room for Coil tubing unit to drill out wellbore.

11:59 PM

Wait on Coil tubing Services.

REGULATORY COMPLETION SUMMARY



Well Name : Peter's Point #10-26D-12-16 Phase/Area West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/10/2009 Report # : 7

AFE # : 15186D

Summary : Shut in wait on EL & Fracs. End Time Description

Well Name : Peter's Point #10-26D-12-16 Phase/Area West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/9/2009 Report # : 6

AFE # : 15186D

Summary : SI. Rig Coil tubing. PU Weatherford 3-7/8" Concave mill , motor. Pressure test . TIH with coil. Tag & drill CFP@ 7763 hand 4 ft. sand on plug. RIH tag CFP #2 @ 7892 drill out. RIH tag & clean out to PBTD @ 1817 ft circ hloe clean. drop ball cut fluid jet N2 @ 1000 SCFM N2. POOH flow to flow tanks. Shut in. Pull off well. lay down Weatherford BHA and mill.

End Time	Description
12:30 PM	SHUT IN
1:00 PM	Rig Coil Tubing Services PU Weatherford BHA. Concave mill 3-7/8" Pressure test .
2:30 PM	Coil RIH with BHA. .50 BPM. with 300 SCFM N2. weight check @ 7500 15K
2:45 PM	TIH tag @ CFP #1 7763, CTP 3700
3:30 PM	Drill CFP @ 7763 drilled 4 ft. b efore drilling CFP. no pressure change on surface.
4:00 PM	TIH tag CFP #2 @ 7892 ft. Drill out no fill on plug pumping 2 BPM and 500 SCFM N2.
4:15 PM	TIH tag sand @ 8059 wash sand to 8117 ft. PBTD. pump 20 bbl sweep.
5:00 PM	Circ well clean POOH slow to 6800 ft. dropped ball to open downhole valve pumped 10 bbl sweep..
7:00 PM	Cut fluid RIH pumping 700 SCFM N2. ran in to 8000 ft. POOH jetting N2 @ 1000 SCFM. no fluid pumped. flowing to flow tanks.
9:30 PM	shut down N2. POOH shut in . Lay down Weatherford Downhole motor, mill. move Coil to 11-26D. dran and lock down equipment for night.
11:59 PM	si

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL

FORM APPROVED
OMB No. 1004-0157
Expires July 31, 2009

COPY

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION				
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off	
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity	
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>	
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Report	
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal		

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Weekly completion activity report from 2/11/09 though 2/18/09 (report #'s 8-11).

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)
Tracey Fallang

Title
Regulatory Analyst

Signature
Tracey Fallang

Date
02/18/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

RECEIVED
FEB 23 2009
DIV. OF OIL, GAS & MINING

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/11/2009

Report # : 8

AFE # : 15186D

Summary	End Time	Description
SICP: 1100. MIRU Black Warrior EL and crane. MIRU Schlumberger frac equipment. BWWC EL gauge ring 3.375" with junk basket. POOH PU perf guns with HES CFP. RIH plug & Perf stage 3. Frac stage3 . EL stage 4. Frac #4. EL stage 5. Stuck perf guns after perforating. Flow casing worked EL try to perf guns. Lower cane boom. Pulled EL to 3000 lbs. free perf guns. POOH flowing well during pull out of perf guns. Shut in . Schlumberger started frac pumped 15 bbl pressured up to max PSI. Shut down. Bleed off psi to 3500 psi. SI. Turn well over to flow back for night. Flow stages 1-4 through Opsco flow equip.	7:00 AM	Shut in CSG. 1100 psi
	10:00 AM	MIRU Black Warrior EL Schlumberger frac equipment. . PU 3.375" gauge ring and junkbasket. RIH to 7890 ft.
	12:00 PM	BWWC EL stage 3 Price River. RIH correlate to short jt. run to setting depth set @7876 ft. PU perforate Price River @7691-7696, 7622-7626, & 7596-7600, 3 JSPF, 120 phasing, 19 gram charges, .390 holes. POOH turn well over to frac.
	1:00 PM	Schlumberger frac stage 3 Price River 70Q Clearfrac. Load & Break @ 4200 PSI @ 20 BPM. Avg. Rate:25.7 BPM. Avg. Pressure:4285 PSI. Max. Rate 31.7 :BPM. Max. Pressure:5647 PSI. Total Fluid Pumped: 12,215 Gal. Total Sand in Formation: 46,200 lb.(20/40 Jordan) Linde CO2: Downhole: 64 Tons. ISIP:3500 PSI. Frac Gradient: .89 psi/ft. 10 BBL over flush cut CO2. Water flush wellbore.
	2:00 PM	BWWC EL stage 4 LDC. PU HES CFP no Bio plugwith 13 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 7555 ft. PU perforate at 7496-7500, 7478-7483 & 7455-7459, 3 JSPF, 120 phasing, 21 gram charges, .370 hole 43 inch. pen Owen Hero charges.. Pumping 2 BPM during perforation up pump rate to 3 BPM. POOH 700 ft. before shut down. POOH turn well over to frac.
	2:40 PM	Schlumberger frac stage 4 Lower Dark Canyon 70Q Clearfrac. Load & Break @ 3,416 PSI @ 5.3 BPM. Avg. Rate:29.2 BPM. Avg. Pressure:5436 PSI. Max. Rate:32.6 BPM. Max. Pressure:6166 PSI. Total Fluid Pumped: 16,567 gal. Total Sand in Formation: 93,256 lb. (20/40 Jordan) Linde CO2 Downhole:117 tons. ISIP3980 :PSI. Frac Gradient:.96 psi/ft. Flushed with 10 bbl over flush with 30Q with 500 gal fluid cap.
	5:15 PM	BWWC EL stage 5 Upper Dark Canyon. PU HES CFP no Bio plug with 11 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 7400 ft. PU start pumping fluid @ 2 BPM perforate stage @ 7342-7348 & 7308-7313, 3 JSPF, 120 phasing, 21 gram charges, .370 Holes. Owen Hero charges. upped pump rate to 3 BPM. Stuck perf guns 75 ft. above perfs. Worked EI try to free perf guns.. Lowered Crane worked EI up to 3000 lbs. pulled guns free. POOH turn well over to frac.
	5:30 PM	Schlumberger frac stage 5 70Q Clearfrac. started pumping @ 15 BBL well pressure up to 6000 psi , no bleed off in formation. Bleed off to 3500 psi.
	6:30 PM	shut in
	11:59 PM	Flow stages 1-4 through Opsco equipment.

REGULATORY COMPLETION SUMMARY

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/12/2009

Report # : 9

AFE # : 15186D

Summary : Flow stages 1-4. SI. Rig Schlumberger to frac stage 5. Start pumping frac. pressured up kicked out pumps. Shut down . Flow casing to flow tanks. recovered light trace of sand. fluid. Start Schlumberger frac. pressured up casing. kicked out pumps. Started pump at 1/2 BPM. @ 6200 psi. pumping into formation could not increase rate. Shut down after pumping 4 bbl. . BWWC RIH with perf guns. tag fill @ 7100 ft. 230 ft. sand from bottom perf to tag stuck perf guns. open casing free perf guns. POOH . Flow back stages 1-4 to open top tanks. LELs put flow through test unit. light trace of sand fluid 10 to 20 bbl per hour. Shut in well. Rig off Black Warrior and Schlumberger frac. Move to 3-35D. rig to start fracing. AM.

End Time	Description
1:00 AM	flow stages 1-4. FCP: 300 psi on 42 ck. recovered 238 bbl in 8.5 hours
1:05 AM	Shut in casing dry flow back.
7:00 AM	shut in CSG: 1035 PSI.
7:30 AM	Schlumberger start frac pumped 45 BBL before pressured up to max.psi.
9:30 AM	Flow stages 1-4 through flow equipment. recovered fluid light trace of sand.
9:45 AM	Shut in. Schlumberger started frac stage 5. pumped 43 BBL before pressured up to max. had light bleed off. pumped 1.2 bpm. at 6200 psi. pumped 4 BBL no rate change. pressure climbed to 6350 psi. shut down. bleed off casing to 2500 psi. turned well over to Wire line.
10:30 AM	BWWC PU perf guns for stage 5 UDC. RIH correlate to short jt. run to 7100 ft. tag sand fill. stuck perf guns. Open casing to flow tanks. free guns. Shut in casing. POOH with perf guns.
1:30 PM	Flow stages 1-4 to open top flow tanks. LELs. turn to test unit. .60 sand 10 to 20 BBL fluid hour.
2:00 PM	Shut in Rig Schlumberger and Black Warrior off well.
11:59 PM	SI.

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/15/2009

Report # : 11

AFE # : 15186D

Summary	End Time	Description
Flow back stages 1-5 . Wait on CTS 4 hours late to bottom of cottonwood dugway. MI CTS coil unit. spot equipment. Hyd. leak on coil unit. made repairs 3.5 hours. rig on to frac tree. Pressure test. RIH with jetting nozzle clean out sand. over stage 5. Pumping 1000 SCFM with 1 BPM fluid. returns trace of sand at flow tanks. Rig Coil tub unit off well. Nipple up Goat head move to 3-35D. Shut in.	6:00 AM	flow stages 1-5 stage 5 is not fraced. FCP: 230 psi on 48 ck. recovered 222 bbl in 22 hours. CO2 21% gas rate: 1.103 MMCFD.
	11:00 AM	flow stages 1-5
	11:30 AM	CTS 4 hours late at bottom of cottonwood dugway. Move in Coil Tubing Services.
	1:30 PM	On loc had Hyd leak in coil unit made repairs.
	3:20 PM	Nipple down goat head. Rig up coil unit on frac tree . Safety meeting. clean out sand , flow back, moving to the next well.
	3:30 PM	pressure test to 3000 psi.
	5:25 PM	RIH with jetting nozzle pumping 1/4 BPM. with 500 SCFM N2. wash down to 7400 ft.
	7:00 PM	Circ and pump 4 sweeps running coil up and down through perfs and tagging CFP , pumping 1000 SCFM. N2 with 1 BPM fluid.
	9:00 PM	Cut N2. pump 55 bbl fluid on bottom pulling up hole to 3000 ft. started Nw at 400 SCFM. to jet out of hole. trace of sand on surface.
	9:01 PM	Shut in
	9:45 PM	Rig Coil off well. Nipple up Goat head.
	11:59 PM	shut in wait on frac's.

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/14/2009

Report # : 10

AFE # : 15186D

Summary	End Time	Description
SI. SICP: Flow through Opsco equipment. to flare stack and flow tank.	6:00 AM	SICP:
	9:00 AM	SI.
	11:59 PM	Open up casing. flow through Opsco equipment.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL

FORM APPROVED
OMB No. 1004-0137
Expires 03/31/2010

COPY

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	Report _____
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Weekly completion activity report from 2/18/09 though 2/25/09 (report #'s 12-14).

14. I hereby certify that the foregoing is true and correct.
Name (Printed/Typed)

Tracey Fallang

Title Regulatory Analyst

Signature

Tracey Fallang

Date 02/25/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

RECEIVED

MAR 03 2009

DIV. OF OIL, GAS & MINING

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/18/2009

Report # : 12

AFE # : 15186D

Summary : SI. Rig BWWC and Schlumberger on well.

End Time

Description

5:00 PM

SI

7:00 PM

Rig Black Warrior EI and Schlumberger on well.

11:59 PM

Shut in

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/19/2009

Report # : 13

AFE # : 15186D

Summary : SI. Schlumberger Pressure test. Safety Meeting. Frac, Smoking area. well on Production. flare. Frac stage 5 UDC. El stage 6. Frac #6. El stage 7. Frac #7. EL stage 8. Frac #8. EL stage 9. Frac #9. El stage 10. Frac #10. EL stage 11. Frac #11. Shut in. Flow stages 1-11

End Time

11:59 PM

Description

flow stages 1-11 through Opsco equipment.

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/19/2009

Report # : 13

AFE # : 15186D

Summary : Sl. Schlumberger Pressure test. Safety Meeting. Frac, Smoking area. well on Production. flare. Frac stage 5 UDC. El stage 6. Frac #6. El stage 7. Frac #7. EL stage 8. Frac #8. EL stage 9. Frac #9. El stage 10. Frac #10. EL stage 11. Frac #11. Shut in. Flow stages 1-11

End Time	Description
12:30 PM	Schlumberger frac stage 8 North Horn 60Q Clearfrac. Load & Break @ 3779 PSI @ 5.3 BPM. Avg. Rate: 17.6 BPM. Avg. Pressure: 4116 PSI. Max. Rate: 21.5 BPM. Max. Pressure: 4919 PSI. Total Fluid Pumped: 325 BBLs. Total Sand in Formation: 37329 lb. (20/40 Jordan) Linde CO2 Downhole: 49 tons. ISIP: 3307 PSI Frac Gradient: .99 psi/ft. Successfully flushed wellbore with 30Q Clearfrac 30 BBL over flush with 500 gal. fluid cap.
1:45 PM	BWWC EL stage 9 North Horn. PU HES CFP with 8 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 5955 ft. PU start pumping fluid @ 2 BPM. Perforate @ 5882-5886 & 5862-5866, 3 JSPF, 120 phasing, 19 gram charges. .390 holes. POOH turn well over to frac.
2:30 PM	Schlumberger frac stage 9 North Horn 60Q Clearfrac. Load & Break @ 3570 PSI @ 5.3 BPM. Avg. Rate: 20.7 BPM. Avg. Pressure: 4406 PSI. Max. Rate: 24.9 BPM. Max. Pressure: 5614 PSI. Total Fluid Pumped: 300 BBLs. Total Sand in Formation: 33,631 lb. (20/40 Jordan) Linde Co2: Downhole: 43 tons. ISIP: 2900 PSI. Frac Gradient: .98 psi/ft. Successfully flushed wellbore with 30Q clearfrac 30 bbl over flush with 500 gal. fluid cap.
3:30 PM	BWWC EL stage 10 North Horn. PU HES CFP with 10 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 5830 ft. PU start pumping fluid at 2 bpm. Perforate @ 5758-5768, 3 JSPF, 120 phasing, 19 gram charges. .390 holes. POOH turn well over to frac.
4:15 PM	Schlumberger frac stage 10 North Horn 60Q Clearfrac. Load & break @ 2644 PSI @ 5.3 BPM. Avg. Rate: 19.5 BPM. Avg. Pressure: 3588 PSI. Max. Rate: 23.2 BPM. Max. Pressure: 3869 PSI. Total Fluid Pumped: 350 BBLs. Total Sand in Formation: 45087 lb. (20/40 Jordan) Linde CO2 Downhole: 56 tons. ISIP: 2050 PSI. Frac Gradient: 1.02 psi/ft. Successfully flushed wellbore with 30Q Clearfrac 30 bbl over flush with 500 gal. fluid cap.
5:00 PM	BWWC El stage 11 Middle Wasatch. PU HES CFP with 11 ft. perf guns. RIH correlate to casing collars. run to setting depth set CFP @ 5700 ft. PU start pumping fluid at 2 BPM. Perforate @ 5668-5672, 5618-5620, 5571-5573 & 5493-5496, 3 jspf 120 Phasing, 19 gram charges. .390 holes. POOH turn well over to frac.
5:30 PM	Schlumberger frac stage 11 Wasatch 60Q Clearfrac. Load & Break @ 2848 PSI @ 5.3 BPM. Avg. Rate: 27.1 BPM. Avg. Pressure: 4031 PSI. Max. Rate: 33.5 BPM. Max. pressure: 5567 PSI. Total Fluid Pumped: 425 BBLs. Total Sand in Formation: 60409 lb. (20/40 White Sand) Praxair CO2 Downhole: 52 tons. ISIP: 2900 PSI. Frac Gradient: .99 psi/ft. Successfully flushed wellbore with 30Q clearfrac. 30 bbl over flush with 500 gal fluid cap.
5:35 PM	shut in for four hour before flowing back stages.

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/19/2009

Report # : 13

AFE # : 15186D

Summary : SI. Schlumberger Pressure test. Safety Meeting. Frac. Smoking area. well on Production. flare. Frac stage 5 UDC. EI stage 6. Frac #6. EI stage 7. Frac #7. EL stage 8. Frac #8. EL stage 9. Frac #9. EI stage 10. Frac #10. EL stage 11. Frac #11. Shut in. Flow stages 1-11

End Time	Description
6:00 AM	SI
6:40 AM	Schlumberger prime up. Saety Meeting. Frac. wells on Production. surface lines pressure up. Flare stack. flow back on 3-35D
7:20 AM	Schlumberger frac stage 5 Upper Dark Canyon. Load & Break @ 5400 PSI @ 27 BPM. Avg. Rate: 28.5 BPM. Avg. Pressure: 4717 PSI. Max. Rate: 35.5 BPM. Max. Pressure: 5823 PSI. Total Fluid Pumped: 431 bbl. Total Sand in Formation: 58,985 lb. Cut sand due to pressure increasing. 265 sacks short of design vol. (20/40 Jordan) Praxair CO2 Downhole: 90 tons. ISIP:3880 PSI. Frac Gradient:.96 psi/ft. Successfully flushed wellbore with 30Q clearfrac. 30 bbl over flush with 500 gal. fluid cap.
8:20 AM	BWWC EL stage 6 North Horn PU HES CFP with 9 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 7275 ft. PU start pumping @ 2 BPM. Perforate @ 7253-7258 & 7178-7182, 3 JSPF 120 phasing, 19 gram charges, .390 holes. POOH turn well over to frac.
9:00 AM	Schlumberger Frac stage 6 North Horn 60Q Clearfrac. Load & Break @ 4606 PSI @ 5.3 BPM. Avg. Rate: 27.4 BPM. Avg. Pressure:5229 PSI. Max. Rate: 34.2 BPM. Max. Pressure: 6101 PSI. Total Fluid Pumped:378 bbl. Total Sand in Formation:46,388 lb.(20/40 Jordan) Praxair CO2 Downhole: tons. ISIP: 3800 PSI. Frac Gradient: .96 psi/ft. Successfully flushed wellbore with 30Q clearfrac. 30 BBL over flush with 500 gal. fluid cap.
10:00 AM	BWWC EL stage 7 North Horn. PU HES CFP with 8 ft. perf gun. RIH correlate to short jt. run to setting depth set CFP @ 6760. PU start pumping at 2 BPM. Perforate @ 6678-6686, 3 JSPF, 120 phasing. 19 gram charges. .390 holes. POOH turn well over to frac.
10:40 AM	Schlumberger frac stage 7 North Horn 60Q clearfrac. Load & Break @ 2816 PSI @ 5.3 BPM. Avg. Rate: 17.4 BPM. Avg. Pressure: 3598 PSI. Max. Rate: 40.8 BPM. Max. Pressure: 3865 PSI. Total Fluid Pumped: 292 BBLs. Total Sand in Formation: 29,478 lb. (20/40 Jordan) Linde CO2 Downhole: 40 tons. ISIP: 3400 PSI. frac Gradient: .94 psi/ft. Successfully flushed wellbore with 30Q clearfrac 30 bbl over flush with 500 gal. fluid cap.
11:40 AM	BWWC EI stage 8 North Horn. PU HES CFP with 10 ft. Perf guns. RIH correlate to short jt. run to setting depth set CFP @ 6590 ft. PU start pumping fluid @ 2 BPM. Perforate @ 6500-6510, 3 JSPF, 120 phasiing, 19 gram charges. .390 holes. POOH turn well over to frac.

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : Peter's Point #10-26D-12-16

Phase/Area West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 2/20/2009

Report # : 14

AFE # : 15186D

Summary : Flow stages 1-11

End Time	Description
6:00 AM	flow back stages 1-11; FCP: 800 psi on 38 ck. recovered 256 bbl in 24 hours Gas rate: 4,536 MMCFD. CO2:8%
12:00 PM	Flow stages 1-11
12:00 PM	Rig casing for Production sales. 3.5 MMCFD

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL
COPY

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input checked="" type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

This sundy is being submitted as notification that this well had first sales on 2/20/09.

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)
Tracey Fallang

Title Regulatory Analyst

Signature *Tracey Fallang*

Date 02/24/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____

Office _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

RECEIVED

MAR 03 2009

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0681

6. If Indian, Allottee or Tribe Name
N/A

SUBMIT IN TRIPLICATE – Other instructions on page 2.

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	<u>Report</u>
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Weekly completion activity report from 02/26/09 though 3/19/09 (report #'s 15-17).

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)

Tracey Fallang

Title Regulatory Analyst

Signature

Tracey Fallang

Date 03/19/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

RECEIVED

MAR 25 2009

BUREAU OF LAND MANAGEMENT
DEPT. OF THE INTERIOR

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : **Peter's Point #10-26D-12-16**

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 3/12/2009

Report # : 15

AFE # : 15186D

Summary : well flowing to production facility, MI/RU
rig and equipment, SDFN

End Time

Description

3:30 PM

well flowing to production facility.

5:00 PM

MI/RU rig and equipment,

6:00 AM

well flowing to production facility. SDFN

REGULATORY COMPLETION SUMMARY



Well Name : **Peter's Point #10-26D-12-16**

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 3/14/2009

Report # : 17

AFE # : 15186D

Summary :	End Time	Description
TIH to plug # 1, drill out 7 plugs and 1 is questionable, no sand on plugs except plug # 7 had +/- 3', returns choked back to 36-40 choke to control sand, cleaned out to PBSD @ 8062' and pumped a 20 BBLs sweep followed by 15 MINS of N2, TOH w/ TBG and LD string float, continue TOH and leave in a 2000' kill string, SDFN leave well to sell line on a 44 choke to control sand.	8:00 AM	bleed off TBG pressure, TIH w/ TBG to plug # 1 @ 5700'
	2:00 PM	RU sower swivel and N2 unit, drill plug and let clean up 15 MINS, PU TBG and tag plug # 2 @ 5830', drillout plug and continue to plug # 3 @ 5953', drill out no change in pressures, TIH to plug # 4 @ 6590' and drill out, TIH to plug # 5 @ 6760' and drill out, TIH to plug # 6 @ 7275' and drill out, TIH to plug # 7 and tag +/- 3' of sand on plug @ 7397' clean out to plug 7400' and drillout, no change in pressures, TIH and tag plug or object @ 7767', drillout and continue to PBSD @ 8062'.
	3:00 PM	pump a 20 BBL sweep and fallow w/ 15 MIN N2.
	5:00 PM	RD power swivel and N2 unit, TOH and LD string float, continue TOH and leave a 2000' kill string.
	6:00 AM	SDFN and let well clean up, send to sell line on a 44 choke to hold sand.

Well Name : **Peter's Point #10-26D-12-16**

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 3/13/2009

Report # : 16

AFE # : 15186D

Summary :	End Time	Description
well flowing to sell line, RU PSI WL and set comp. bridge plug @ 5290', POOH RD WL, bleed off CSG to blow down tank, ND frac tree, NU BOP, PU/MU bit and pump off bit sub, 8' sub, xn-nipple, PU TBG and TIH to kill plug @ 5290', RU power swivel and N2 unit, pump a 20 BBL cushion drill out kill plug, TIH to plug # 1 @ 5700' no sand, pump 20 MINS N2, TOH above top perf, let clean up and send to sell line, SDFN	9:00 AM	well flowing to production facility, PSI WL MI/RU.
	10:00 AM	unload TBG trailer to TBG racks.
	12:30 PM	bleed off CSG, ND frac tree, NU BOP.
	11:30 AM	PU/MU 4 1/2" composite bridge plug, RIH and set @ 5290', POOH and LD setting tool, RD WL.
	4:00 PM	PU/MU bit and pump off bit sub, 8' sub, xn-nipple, TBG and TIH to plug @ 5290'.
	4:20 PM	RU power swivel and N2 unit.
	4:45 PM	pump a 20 BBL cushion and drill out plug, 20 BBLs flowed bac and plug, pressure up to 550 PSI.
	6:00 PM	PU TBG and tag plug @ 5700' no sand, pump 20 MINS w/ N2.
	7:00 PM	TOH above top perf.
6:00 AM	flow to sell line.	

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

trallang
~~CONFIDENTIAL~~
CONFIDENTIAL

COPY
FORM APPROVED
OMB No. 1004-0114
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU-0007

6. If Indian, Allottee or Tribe Name
N/A

7. If Unit of CA/Agreement, Name and/or No.
Peter's Point/UTU-63014

8. Well Name and No.
Peter's Point Unit Federal 10-26D-12-16

9. API Well No.
43-007-31406

10. Field and Pool or Exploratory Area
Peter's Point/Wasatch-Mesaverde

11. Country or Parish, State
Carbon County, UT

SUBMIT IN TRIPLICATE - Other instructions on page 2.

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300
Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SESW, 270' FSL, 1510' FWL
Sec. 26, T12S-R16E

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Weekly Activity</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	<u>Report</u>
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Weekly completion activity report from 03/19/09 though 3/29/09 (report #'s 18-22).

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)
Tracey Fallang

Title
Regulatory Analyst

Signature *Tracey Fallang*

Date
03/30/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

RECEIVED

APR 02 2009

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : **Peter's Point #10-26D-12-16**

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 3/18/2009

Report # : 18

AFE # : 15186D

Summary : unload TBG to pipe racks, rig maintenance.

End Time

Description

10:00 AM

well flowing to sell line wait on TBG truck.

2:00 PM

unload TBG off truck to pipe racks, rig maintenance.

6:00 AM

SDFN

REGULATORY COMPLETION SUMMARY

WELLCORE

Well Name : **Peter's Point #10-26D-12-16**

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 3/21/2009

Report # : 20

AFE # : 15186D

Summary : NU pump "T" and kill CSG w/ 40 BBLS and TBG w/ 20 BBLS, RU cap string feeder and trickle 1 BBL per min. down TBG while RIH w/ 1/4" cap string, 2415' run inside of 2 7/8" UFJ, pump 20 BBLS down TBG and cut cap, sting in x-over mandere/, TIH w/ TBG and band 1/4" cap string to outside of TBG to surface, land TBG ND BOP, NU production tree and cap string to off production side of well head, TBG string is, 78 JTS 2 7/8" UFJ w/ 1/4" capillary string inside - x-over 2 7/8" UFJ to 2 3/8" eue 8 rd - 8' 2 3/8" sub - 2 3/8" disconnect - 2 3/8" x-over injection manderel (cap string to out side of TBG) - xn-nipple w/ retrievable plug - 1 JT - CVR perf sub w/ x-nipple built in - 174 JTS 2 3/8", well flowing through CSG to sell line. SDFN

End Time
8:00 AM
9:00 AM
11:00 AM
3:00 PM
4:00 PM
5:00 PM
6:00 AM

Description

RU pump and kill CSG w/ 40 BBLS, and TBG w/ 20 BBLS,
RU pump "T" w/ cap string pack off on top, RU cap string feeder.
trickle water down TBG @ 1 BBL per minute while RIH w/ 2415' of cap string, pack off and pump 20 BBLS down TBG to kill, break "T" and pack off and cut cap string, sting into x-over manderel.
start to band cap string on out side of TBG, TIH w/ x-over 2 3/8" to 2 7/8" UFJ, 8' sub, shear sub, x-over manderel, xn-nipple w/ plug, 1 JT, CVR sleeve w/ x-nipple built in, 174 JTS TBG, TBG flow 2 times, we shut hydril and let unload before pumping a kill, land TBG and ND BOP, pull TBG hanger and try to rig up cap string well start to flow, let unload and kill w/ 40 BBLS,
NU cap string and land TBG, NU production tree.
stay RU and let CSG unload and clean up, turn over to sell line.
SDFN

EOT @ 7967' (1/4" CAP @ 7965', CVR intake sub @ 5509', perforation range 5493' - 7960', PBDT @ 8062'

Well Name : **Peter's Point #10-26D-12-16**

Phase/Area

West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 3/20/2009

Report # : 19

AFE # : 15186D

Summary : TIH w/ TBG and LD some 2 3/8", finish TOH w/ TBG LD bit and xn-nipple, PU and TIH w/ 2 7/8" UFJ, and x-over to 2 3/8" TBG, RU cap string equipment and RIH w/ 1/4" cap string to 2408', TBG start to flow and have no way to shut in TBG, pressure blow out cap string out of TBG, no one injured, have a meeting and RU a pack off w/ a pump "T" SDFN leave well flowing to sell line.

End Time
10:00 AM
12:00 PM
1:00 PM
3:00 PM
5:00 PM
7:00 PM
6:00 AM

Description

TIH w/ TBG and LD some 2 3/8" TBG, finish TOH w/ TBG LD bit and xn-nipple.
PU and TIH w/ 2408' of 2 7/8" UFJ TBG x-over to 2 3/8" 8 rd and 8' sub.
RU nalco source one cap string equipment, while pumping a 20 BBL TBG kill, (well was dead when started to pump)
had trouble w/ cap string crane, RIH and cut cap string to sting in x-over, TBG start to flow and had no way to shut in TBG, blew out 2400' of 1/4" cap string onto the ground, (no one injured), start to pump down CSG and slow the flow of TBG, stab a TI valve.
well shut in, and clean well head up, have a meeting on well control and figure out how to run cap string and be able to shut in.
gather materials and build a pack off w/ circulating "T"
SDFN, leave well flowing to sell line.

REGULATORY COMPLETION SUMMARY

WELL CORE

Well Name : **Peter's Point #10-26D-12-16**

Phase/Area West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 3/26/2009 Report # : 22

AFE # : 15186D

Summary :	End Time	Description
well flowing to production facility, PLS SL MI/RU RIH retrieve xn-nipple plug, RIH w/ CVR sleeve, RU N2 unit and roll the hole for 1hr 15 mins, flow CSG PLS SL RIH and retrieve CVR sleeve, RIH set plug in xn-nipple, RD/MO, let CSG flow through OPSCO and clean up, flow through TBG and let clean up, turn over to sells.	8:00 AM	well flowing to sell line, wait on PLS SL.
	8:15 AM	RU PLS WL RIH and retrieve xn-plug, POOH
	8:30 AM	PU/MU CVR blanking sleeve RIH and set in CVR sub, POOH
	10:15 AM	RU N2 unit and roll the hole 1hr, pumping down TBG return up CSG
	11:00 AM	RIH w/ retrieving tool and latch on CVR blanking sleeve, POOH, RIH w/ xn-plug and set in xn-nipple, POOH.
	12:00 PM	flow back CSG through OPSCO, @ 380 PSI csg on open 2" let clean up, x-over to TBG SITP @ 650 PSI and level off @ 280 PSI on open 2", CSG 400 PSI.
	6:00 AM	turn TBG to sells CSG 3.4 MMCF CSG pressure 610 PSI.

Well Name : **Peter's Point #10-26D-12-16**

Phase/Area West Tavaputs

Bottom Hole Display	API #/License
NWSE-26-12S-16E-W26M	43-007-31406

Ops Date : 3/22/2009 Report # : 21

AFE # : 15186D

Summary :	End Time	Description
well flowing to production facility, equalize TBG and CSG, flow back CSG to sell line, RU PLS SL, RIH w/ retrieving tool, and sting in blanking plug and let equalize, pull plug free and POOH, LD blanking sleeve, PLS RD/MO, open TBG to sell line and shut in CSG.	8:00 AM	well flowing to sell line, wait on slick line. equalize TBG and CSG pressure and let CSG flow.
	10:00 AM	RU PLS SL, RIH and sting into blanking plug on CVR tool, let equalize and pull sleeve, POOH w/ sleeve.
	11:00 AM	PLS SL RD/MO.
	6:00 AM	open TBG and flow to production facility, CSG shut in.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL

FORM APPROVED
BLM NO. 1004-0137
Expires July 31, 2010
COPY

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
UTU-0681

1a. Type of Well: Oil Well Gas Well Dry Other
 b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Resvr.,
 Other: _____

6. If Indian, Allottee or Tribe Name
N/A

2. Name of Operator
Bill Barrett Corporation

7. Unit or CA Agreement Name and No.
Peters Point / UTU-63014

3. Address 1099 18th Street, Suite 2300
Denver CO 80202

3a. Phone No. (include area code)
(303) 312-8134

8. Lease Name and Well No.
Peters Point Unit Federal 10-26D-12-16

4. Location of Well (Report location clearly and in accordance with Federal requirements)*
At surface
SESW, 270' FSL, 1,510' FWL

9. AFI Well No.
43-007-31406

At top prod. interval reported below
NWSE, 1,612' FSL, 2,307' FEL, Sec. 26

10. Field and Pool or Exploratory
Peters Point/Wasatch-Mesaverde

At total depth NWSE, 2,002' FSL, 1,949' FEL, Sec. 26 *per HSM review*

11. Sec., T., R., M., on Block and Survey or Area Sec. 26, T12S-R16E

12. County or Parish
Carbon County

13. State
UT

14. Date Spudded
08/21/2008

15. Date T.D. Reached
10/21/2008

16. Date Completed 02/19/2009
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
7,177.5' RKB

18. Total Depth: MD 8,161'
TVD 7,545'

19. Plug Back T.D.: MD 8,117'
TVD 7,501'

20. Depth Bridge Plug Set: MD
TVD N/A PBSD is Float Collar

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
Halliburton Triple Combo, Schlumberger CBL *mud, SD, DSN, HRI*

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sks. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
20"	16" H-40	65#	0	40'	grout			Surface	0 lbs
12 1/4"	9 5/8" J-55	36.0#	0	1,033'	N/A	450 sx Prem.	92 bbls	Surface	0 lbs
8 3/4" & 7 7/8"	4 1/2" I-80	11.6#	0	7,999'	N/A	1,670 sx 50/50 Poz Premium	437 bbls	1,050' (CBL)	15,000 lbs

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2 3/8"	5,559'	N/A	2 7/8"	7,968'				

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Mesaverde	7,328'	7,960'	7,950' - 7,960'	0.390"	30	Open
B) Wasatch	5493'	7,327'	7,768' - 7,798'	0.390"	30	Open
C)			7,596' - 7,696'	0.390"	39	Open
D)			7,455' - 7,500'	0.390"	39	Open

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
7,950' - 7,960'	Stage 1: 70Q CO2 Foam Frac: 47 Tons CO2, 242 bbl fluid, 27,200# 20/40 Jordan Sand
7,768' - 7,798'	Stage 2: 70Q CO2 Foam Frac: 89 Tons CO2, 385 bbl fluid, 74,100# 20/40 Jordan Sand
7,596' - 7,696'	Stage 3: 70Q CO2 Foam Frac: 60 Tons CO2, 291 bbl fluid, 46,200# 20/40 Jordan Sand
7,455' - 7,500'	Stage 4: 70Q CO2 Foam Frac: 116 Tons CO2, 396 bbl fluid, 93,256# 20/40 Jordan Sand

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
02/17/09	02/19/09	12	→	0	2,162	53	N/A		Flowing through test equipment
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
38	N/A	800	→	0	4,324	106	N/A	Producing	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

*(See instructions and spaces for additional data on page 2)

RECEIVED

APR 20 2009

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)
Sold

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
				Wasatch North Horn	3,451' 5,675'
				Dark Canyon Price River	7,328' 7,521'

32. Additional remarks (include plugging procedure):

Copies of logs previously submitted under separate cover. In the event logs were not received please contact Jim Kinser at 303-312-8163.
7-7/8" Hole Started @ 7,144'

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other:

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Tracey Fallang Title Regulatory Analyst
 Signature *Tracey Fallang* Date 04/14/2009

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Peter's Point Unit Federal #10-26D-12-16 Report Continued

26. PERFORATION RECORD (cont.)				27. ACID, FRACTURE, TREATMENT, CEMENT SQUEEZE, ETC. (cont.)									
INTERVAL (Top/Bot-MD)		SIZE	NO. HOLES	PERFORATION STATUS	AMOUNT AND TYPE OF MATERIAL								
7,308'	7,348'	0.390"	39	Open	Stg 5	60% CO2 foam frac:	84	tons CO2	431	bbls total fluid	58,985#	20/40 Jordan Sand	
7,178'	7,253'	0.390"	27	Open	Stg 6	60% CO2 foam frac:	56	tons CO2	328	bbls total fluid	46,388#	20/40 Jordan Sand	
6,678'	6,685'	0.390"	21	Open	Stg 7	60% CO2 foam frac:	38	tons CO2	292	bbls total fluid	29,478#	20/40 Jordan Sand	
6,500'	6,510'	0.390"	30	Open	Stg 8	60% CO2 foam frac:	41	tons CO2	325	bbls total fluid	37,329#	20/40 Jordan Sand	
5,862'	5,886'	0.390"	24	Open	Stg 9	60% CO2 foam frac:	36	tons CO2	300	bbls total fluid	33,631#	20/40 Jordan Sand	
5,758'	5,768'	0.390"	30	Open	Stg 10	60% CO2 foam frac:	47	tons CO2	301	bbls total fluid	45,087#	20/40 Jordan Sand	
5,493'	5,672'	0.390"	33	Open	Stg 11	60% CO2 foam frac:	58	tons CO2	359	bbls total fluid	60,409#	20/40 Jordan Sand	

*Depth intervals for frac information same as perforation record intervals.

Directional Surveys

WFL CORE

Location Information		
Business Unit	Phase/Area	Surface Location
Operations	West Tavaputs	SESW-26-12S-16E-W26M
Project	Well Name	Main Hole
Uinta	Peter's Point #10-26D-12-16	

Bottom Hole Information		Survey Section Details					
UWI	API / License #	Section	KOP (ft)	KOP Date	TMD (ft)	TVD (ft)	TD Date
NWSE-26-12S-16E-W26M	43-007-31406	Surface	1060.00				
		Main	1094.00	10/11/2008			

Survey Information		
Survey Company	Direction of Vertical Section (°)	Magnetic Dec. Correction (°)
WEATHERFORD-PENLEE	46.64	11.64

Details											
Corrected											
Extrap.	Depth MD (ft)	Inclination (°)	Azimuth (°)	TVD (ft)	Sub Sea (ft)	Northings (ft)	N/S	Eastings (ft)	E/W	Vertical Section (ft)	Dog Leg
	877.00	1.10	166.38	876.81		11.23	S	12.67	E	1.51	0.53
	1094.00	0.87	173.31	1093.94		8.25	S	0.97	E	-4.96	0.08
	1188.00	2.50	55.54	1187.89		7.80	S	2.74	E	-3.36	3.20
	1283.00	5.31	48.54	1282.64		3.71	S	7.74	E	3.08	2.99
	1378.00	8.63	52.04	1376.90		3.58	N	16.66	E	14.57	3.52
	1473.00	10.56	45.91	1470.55		14.02	N	28.53	E	30.37	2.30
	1568.00	12.44	49.29	1563.63		26.75	N	42.54	E	49.29	2.10
	1663.00	15.06	49.04	1655.89		41.52	N	59.61	E	71.85	2.76
	1758.00	17.00	45.41	1747.18		59.36	N	78.83	E	98.06	2.30
	1853.00	20.06	47.91	1837.22		80.03	N	100.81	E	128.24	3.33
	1948.00	23.50	47.41	1925.40		103.77	N	126.84	E	163.46	3.63
	2043.00	25.38	48.79	2011.88		130.00	N	156.10	E	202.75	2.07
	2137.00	27.69	49.29	2095.96		157.51	N	187.81	E	244.70	2.47
	2232.00	30.56	49.66	2178.92		187.54	N	222.95	E	290.86	3.03
	2327.00	31.31	49.04	2260.41		219.36	N	260.00	E	339.64	0.86
	2421.00	32.56	48.91	2340.17		251.99	N	297.51	E	389.32	1.33
	2516.00	33.06	48.91	2420.02		285.83	N	336.31	E	440.75	0.53
	2610.00	33.94	49.16	2498.40		319.84	N	375.48	E	492.59	0.95
	2705.00	34.50	49.29	2576.95		354.73	N	415.94	E	545.96	0.59
	2800.00	33.69	47.66	2655.62		390.02	N	455.81	E	599.18	1.29
	2894.00	32.38	45.79	2734.42		425.13	N	493.12	E	650.41	1.77
	2988.00	31.13	45.79	2814.35		459.63	N	528.58	E	699.88	1.33
	3083.00	32.06	46.16	2895.26		494.21	N	564.37	E	749.64	1.00
	3178.00	30.00	46.41	2976.65		528.05	N	599.76	E	798.61	2.17
	3272.00	29.06	45.79	3058.44		560.17	N	633.14	E	844.93	1.05
	3366.00	28.88	45.79	3140.68		591.92	N	665.77	E	890.46	0.19
	3459.00	29.75	44.29	3221.77		624.10	N	697.98	E	935.97	1.22
	3554.00	31.44	43.91	3303.53		658.82	N	731.63	E	984.26	1.79
	3650.00	32.63	44.29	3384.91		695.38	N	767.06	E	1035.13	1.26
	3745.00	31.69	44.04	3465.33		731.66	N	802.30	E	1085.65	1.00
	3840.00	32.31	43.79	3545.89		767.92	N	837.21	E	1135.94	0.67
	3936.00	31.56	44.66	3627.36		804.31	N	872.62	E	1186.67	0.92
	4030.00	32.63	44.91	3706.99		839.76	N	907.81	E	1236.58	1.15
	4124.00	32.56	44.79	3786.19		875.66	N	943.52	E	1287.20	0.10
	4218.00	32.69	44.16	3865.36		911.82	N	979.02	E	1337.84	0.39
	4313.00	32.81	44.16	3945.25		948.69	N	1014.83	E	1389.18	0.13
	4408.00	32.25	44.54	4025.35		985.22	N	1050.54	E	1440.23	0.63
	4500.00	33.00	44.79	4102.83		1020.49	N	1085.40	E	1489.80	0.83
	4594.00	31.31	43.66	4182.40		1056.33	N	1120.30	E	1539.77	1.91
	4689.00	30.94	44.29	4263.73		1091.67	N	1154.39	E	1588.83	0.52
	4782.00	31.13	45.29	4343.41		1125.69	N	1188.17	E	1636.75	0.59
	4875.00	31.25	47.16	4422.97		1159.01	N	1222.95	E	1684.90	1.05
	4969.00	31.38	47.16	4503.28		1192.23	N	1258.77	E	1733.75	0.14
	5063.00	30.25	47.29	4583.84		1218.29	N	1306.50	E	1786.35	1.20
	5158.00	31.31	48.41	4665.46		1250.90	N	1342.54	E	1834.95	1.27

Directional Surveys

WFL: CORE

Location Information

Business Unit	Phase/Area	Surface Location
Operations	West Tavaputs	SESW-26-12S-16E-W26M
Project	Well Name	Main Hole
Uinta	Peter's Point #10-26D-12-16	

Extrap.	Depth MD (ft)	Inclination (°)	Azimuth (°)	TVD (ft)	Sub Sea (ft)	Northings (ft)	N/S	Eastings (ft)	E/W	Vertical Section (ft)	Dog Leg
	5253.00	29.38	47.66	4747.43		1282.99	N	1378.23	E	1882.92	2.07
	5346.00	27.50	46.91	4829.20		1313.02	N	1410.77	E	1927.20	2.06
	5442.00	26.44	47.06	4914.75		1342.72	N	1442.60	E	1970.74	1.11
	5537.00	25.63	46.29	5000.11		1371.33	N	1472.94	E	2012.43	0.92
	5631.00	25.69	45.79	5084.84		1399.58	N	1502.24	E	2053.13	0.24
	5725.00	25.13	44.66	5169.75		1427.98	N	1530.87	E	2093.45	0.79
	5820.00	24.81	44.41	5255.87		1456.57	N	1559.00	E	2133.53	0.35
	5914.00	25.19	44.91	5341.06		1484.83	N	1586.92	E	2173.23	0.46
	6009.00	22.13	46.79	5428.04		1511.40	N	1614.24	E	2211.33	3.32
	6103.00	20.94	48.29	5515.48		1534.69	N	1639.68	E	2245.83	1.39
	6197.00	19.25	47.41	5603.74		1556.36	N	1663.63	E	2278.11	1.83
	6292.00	17.56	45.16	5693.87		1577.06	N	1685.32	E	2308.10	1.93
	6387.00	15.50	46.16	5784.93		1595.96	N	1704.64	E	2335.12	2.19
	6483.00	12.63	46.54	5878.03		1612.06	N	1721.51	E	2358.44	2.99
	6576.00	12.56	46.54	5968.79		1626.01	N	1736.23	E	2378.72	0.08
	6671.00	11.31	40.91	6061.73		1640.16	N	1749.83	E	2398.32	1.80
	6764.00	9.44	44.91	6153.20		1652.45	N	1761.18	E	2415.02	2.15
	6859.00	7.31	41.16	6247.17		1662.52	N	1770.66	E	2428.82	2.31
	6955.00	7.13	41.66	6342.41		1671.57	N	1778.64	E	2440.83	0.20
	7049.00	6.19	41.54	6435.77		1679.72	N	1785.88	E	2451.69	1.00
	7081.00	5.81	42.54	6467.59		1682.20	N	1788.12	E	2455.03	1.23
	7094.00	5.50	41.29	6480.53		1683.16	N	1788.97	E	2456.30	2.56
	7144.00	5.50	41.29	6530.30		1686.76	N	1792.14	E	2461.07	0.00
	8161.00	1.20	41.29	7544.85		1731.38	N	1831.32	E	2520.20	0.42

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.

6. If Indian, Allottee or Tribe Name

SUBMIT IN TRIPLICATE - Other instructions on page 2.

7. If Unit of CA/Agreement, Name and/or No

Prickly Pear Unit/UTU-79487
Peter's Point Unit/UTU-63014

8. Well Name and No.
See Attached

9. API Well No.

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator
Bill Barrett Corporation

3a. Address
1099 18th Street, Suite 2300, Denver, CO 80202

3b. Phone No. (include area code)
303-312-8134

10. Field and Pool or Exploratory Area

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

11. Country or Parish, State
Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Off-lease Water Treatment</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Bill Barrett Corporation (BBC) is submitting this as an update to the previously submitted sundry dated 09/16/09. BBC will be also be treating produced water from Peter's Point unit, in addition to Prickly Pear unit, for re-use for the state water needs. All operations to meet additional water needs. A list and map of Peter's Point unit wells is attached.

If you have further questions, please contact me at 303-312-8134.

Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
RECEIVED
FEB 16 2010

DIV. OF OIL, GAS & MINING

COA: Approval is granted to take the water produced by Peter's Point Federal wells to be treated by the temporary water treatment facility located on SI TLA lands in Sec. 16, T12S R15E through July 2010.

14. I hereby certify that the foregoing is true and correct.

Name (Printed/Typed)
Tracey Fallang

Title Regulatory Analyst

Signature

Tracey Fallang

Date 02/04/2010

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Mary Henderson

Petroleum Engineer

Date FEB 08 2010

Title

Office

PRICE FIELD OFFICE

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

UDOGM

COPY

UWI/API	LABEL	Status
430073007000	5-14-PETERS POINT	GAS
430073002300	9-PTRS PT UNIT	GAS
430071539300	4-PTRS PT UNIT	GAS
430071539100	2-PTRS PT UNIT	GAS
430073076100	36-2-PtrsPtFed	GAS
430073076200	36-3-PtrPtFed	GAS
430073076300	36-4-PtrsPtFed	GAS
430071021600	1-PETERS POINT UNIT	GAS
430071021600	1-PETERS POINT UNIT	GAS
430073098200	11-6-13-17	GAS
430073096500	16-35-12-16	GAS
430073131800	16-27-12-16	GAS
430073127900	8-34-12-16	GAS
430073127500	6-35D-12-16	GAS
430073129300	7-1D-13-16 Ultra Dee	GAS
430073100500	16-31D-12-17	GAS
430073100400	16-6D-13-17	GAS
430073101000	2-36D-12-16	GAS
430073100900	12-31D-12-17	GAS
430073101100	9-36-12-16	GAS
430073081000	4-31D-12-17	GAS
430073085900	6-7D-13-17 Deep	GAS
430073102400	8-35D-12-16	GAS
430073081200	16-26D-12-16	GAS
430073076400	14-25D-12-16	GAS
430073115800	2-12D-13-16 Deep	GAS
430073127700	14-26D-12-16	GAS
430073128100	6-34D-12-16	GAS
430073127200	6-36-12-16	GAS
430073127100	3-36-12-16	GAS
430073117500	12-36D-12-16	GAS
430073117400	10-36D-12-16	GAS
430073126100	15-6D-13-17 Deep	GAS
430073104900	4-12D-13-16 Deep ST	GAS
430073141100	9-27D-12-16	GAS
430073140900	11-27D-12-16	GAS
430073141000	15-27D-12-16	GAS
430073140600	10-26D-12-16	GAS
430073140400	15-26D-12-16	GAS
430073140700	11-26D-12-16	GAS
430073135200	13-25D-12-16	GAS
430073140300	13-26D-12-16	GAS
430073140800	12-26D-12-16	GAS
430073142700	1-34D-12-16	GAS
430073142800	7-34D-12-16	GAS
430073140500	3-35D-12-16	GAS
430073134500	2-35D-12-16	GAS
430073136500	1-35D-12-16	GAS
430073147400	10-35D-12-16	WOC
430073147600	9-35D-12-16	WOC
430073142900	5-35D-12-16	GAS


UWI/API	LABEL	Status
430073134700	4-35D-12-16	GAS
430073134600	7-35D-12-16	GAS
430073134800	7-36D-12-16	GAS
430073135000	5-36D-12-16	GAS
430073135100	15-25D-12-16	GAS
430073131900	10-27D-12-16	GAS
430073132600	2-7D-13-17 Deep	GAS
430073132000	2-34D-12-16	GAS
430073134900	11-36D-12-16	GAS
430073135300	4-36D-12-16	GAS

PETER'S POINT UNIT

Status Legend

GAS Currently Producing
WOC Waiting on Completion

Water could come from any of these GAS wells to be used in treatment process and reused for state completions.

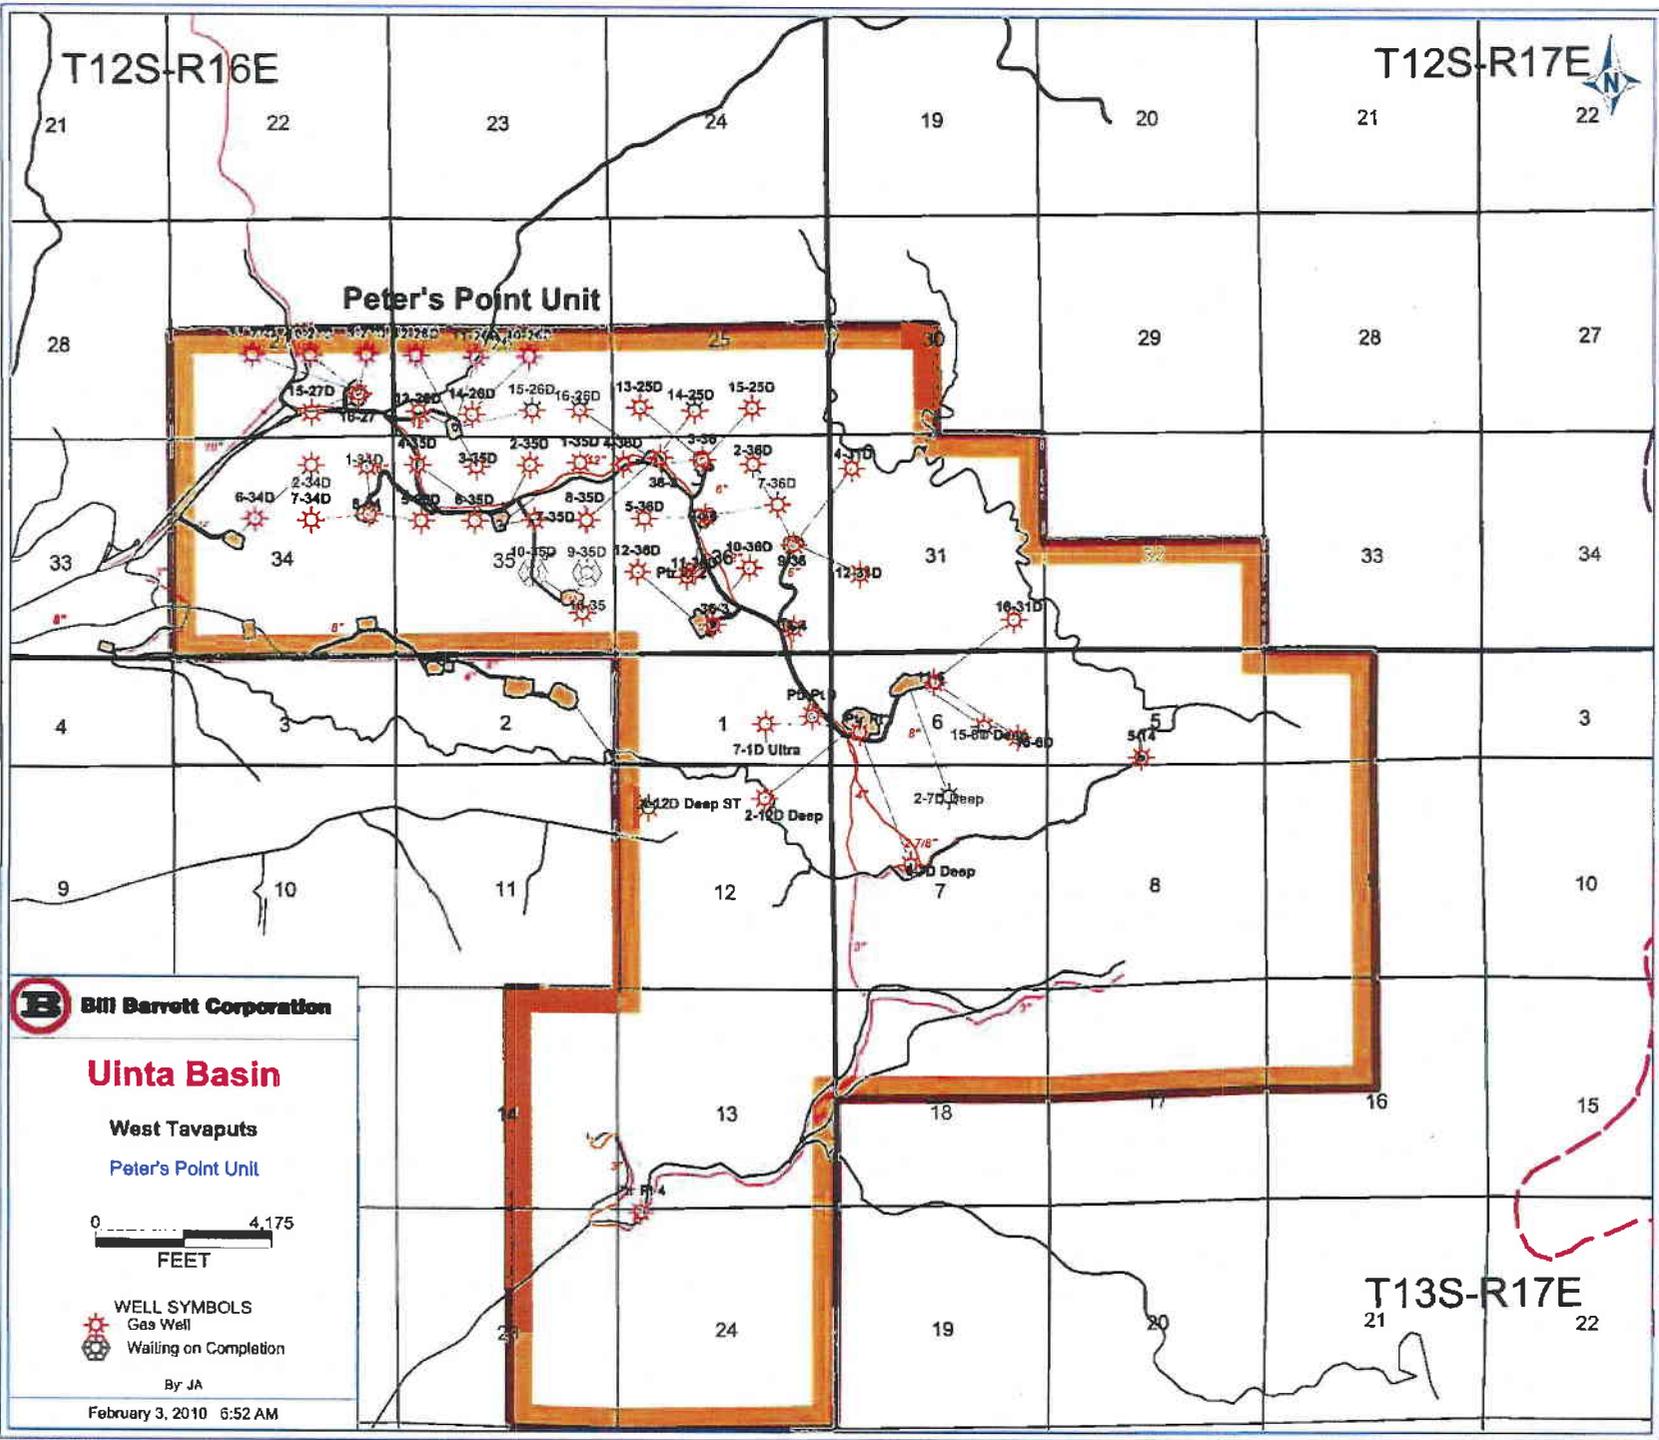

WEST TAVAPUTS PILOT WATER TREATMENT FACILITY NESW, SECTION 16, T12S-R15E

This is being submitted as notification that Bill Barrett Corporation (BBC) will be setting a temporary "pilot" water treatment facility within existing disturbance (no surface-laid lines are proposed) at the Prickly Pear Unit State 11-16 location. This facility will test the ability for BBC to reuse and recycle Prickly Pear unit water for approximately 16 state wells in Section 16 which are to be completed in 2010. It would also reduce truck traffic through Harmon Canyon associated with water hauling by approximately 16 trucks per day. Wells on Prickly Pear mesa generate approximately 1000 barrels of water per day (BWPD) and each well completion will take approximately 1300 BWPD. Any additional water needed for completion will come from currently approved water sources. This pilot facility will be in operation from January through July of 2010 and if successful, BBC will discuss the potential of making the facility permanent.

The process description is listed below and attachments to this proposal include proposed facility diagrams and maps and spreadsheets which indicate Prickly Pear wells involved with the water treatment process.

PROCESS DESCRIPTION

BBC will use an electro-coagulation (EC) process which transmits an electrical current through the water between iron plates. Iron hydroxyl-oxide (IHO) is formed by the electrical current in the form of a floc which then adsorbs compounds in the water. Compounds bound to the IHO create larger floc/solids known as hematite. The hematite is then skimmed off and placed into a tank to be hauled off of to a state approved disposal facility and a pH buffer is added to the water to lower the pH for re-use.

The EC system will treat approximately 1000-1200 BWPD (including flow-back water) and will be stored in clean tanks adjacent to the system. There will be ten 450-bbl holding tanks (two inlet water and eight treated water), three 450-bbl weir (skim) tanks and the actual EC system. There will also be a small generator to power a pump on location to assist in keeping the water flowing through the system. The tank battery will be bermed and the berms will be constructed to contain at a minimum 120 percent of the storage capacity of the largest tank within the berm. Any load lines and valves will be placed inside the berm.

After completion operations have ceased within Section 16, water will once again be diverted back to BBC's permitted saltwater disposal well in Sec. 24, T12S-R14E or a request for a permanent facility may be filed.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other instructions on page 2.

1. Type of Well <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input checked="" type="checkbox"/> Other		5. Lease Serial No.
2. Name of Operator Bill Barrett Corporation		6. If Indian, Allottee or Tribe Name
3a. Address 1099 18th Street, Suite 2300, Denver, CO 80202	3b. Phone No. (include area code) 303-312-8134	7. If Unit of CA/Agreement, Name and/or No. Prickly Pear Unit/UTU-79487
4. Location of Well (Footage, Secs, T., R., M., or Survey Description)		8. Well Name and No. See Attached
		9. API Well No.
		10. Field and Pool or Exploratory Area
		11. Country or Parish, State Carbon County, UT

12. CHECK THE APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, REPORT OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other <u>Off-lease Water</u>
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug and Abandon	<input type="checkbox"/> Temporarily Abandon	<u>Treatment of Prickly</u>
	<input type="checkbox"/> Convert to Injection	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	<u>Pear Unit Water</u>

13. Describe Proposed or Completed Operation: Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports must be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 must be filed once testing has been completed. Final Abandonment Notices must be filed only after all requirements, including reclamation, have been completed and the operator has determined that the site is ready for final inspection.)

Bill Barrett Corporation (BBC) is submitting this sundry in accordance with Onshore Order No. 7, III.B.2.b, Disposal of Produced Water on State or Privately Owned Lands. BBC will be taking produced water and flowback water from federal and state leases (a map and list of these wells is attached) within the Prickly Pear unit, hauling it to a temporary, "pilot" water treatment facility on SITLA lands in Sec. 16, T12S-R15E where it will be treated and reused for completion operations for approximately 16 state wells. This water treatment and recycling process will be in operation from January through July of 2010 and if successful, there is the potential of this being a permanent facility.

BBC has attached the SITLA submittal information for your records.

If you have further questions, please contact me at 303-312-8134.

COPY

COA: Once received, please provide a copy of SITLA's approval letter.

14. I hereby certify that the foregoing is true and correct. Name (Printed/Typed) Tracey Fallang		Title Regulatory Analyst
Signature <i>Tracey Fallang</i>		Date 01/14/2010

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by <i>Manny Heubrich</i>	Petroleum Engineer	Date JAN 14 2010
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.		Office PRICE FIELD OFFICE

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

WEST TAVAPUTS PILOT WATER TREATMENT FACILITY NESW, SECTION 16, T12S-R15E

This is being submitted as notification that Bill Barrett Corporation (BBC) will be setting a temporary "pilot" water treatment facility within existing disturbance (no surface-laid lines are proposed) at the Prickly Pear Unit State 11-16 location. This facility will test the ability for BBC to reuse and recycle Prickly Pear unit water for approximately 16 state wells in Section 16 which are to be completed in 2010. It would also reduce truck traffic through Harmon Canyon associated with water hauling by approximately 16 trucks per day. Wells on Prickly Pear mesa generate approximately 1000 barrels of water per day (BWPD) and each well completion will take approximately 1300 BWPD. Any additional water needed for completion will come from currently approved water sources. This pilot facility will be in operation from January through July of 2010 and if successful, BBC will discuss the potential of making the facility permanent.


The process description is listed below and attachments to this proposal include proposed facility diagrams and maps and spreadsheets which indicate Prickly Pear wells involved with the water treatment process.

PROCESS DESCRIPTION

BBC will use an electro-coagulation (EC) process which transmits an electrical current through the water between iron plates. Iron hydroxyl-oxide (IHO) is formed by the electrical current in the form of a floc which then adsorbs compounds in the water. Compounds bound to the IHO create larger floc/solids known as hematite. The hematite is then skimmed off and placed into a tank to be hauled off of to a state approved disposal facility and a pH buffer is added to the water to lower the pH for re-use.


The EC system will treat approximately 1000-1200 BWPD (including flow-back water) and will be stored in clean tanks adjacent to the system. There will be ten 450-bbl holding tanks (two inlet water and eight treated water), three 450-bbl weir (skim) tanks and the actual EC system. There will also be a small generator to power a pump on location to assist in keeping the water flowing through the system. The tank battery will be bermed and the berms will be constructed to contain at a minimum 120 percent of the storage capacity of the largest tank within the berm. Any load lines and valves will be placed inside the berm.

After completion operations have ceased within Section 16, water will once again be diverted back to BBC's permitted saltwater disposal well in Sec. 24, T12S-R14E or a request for a permanent facility may be filed.

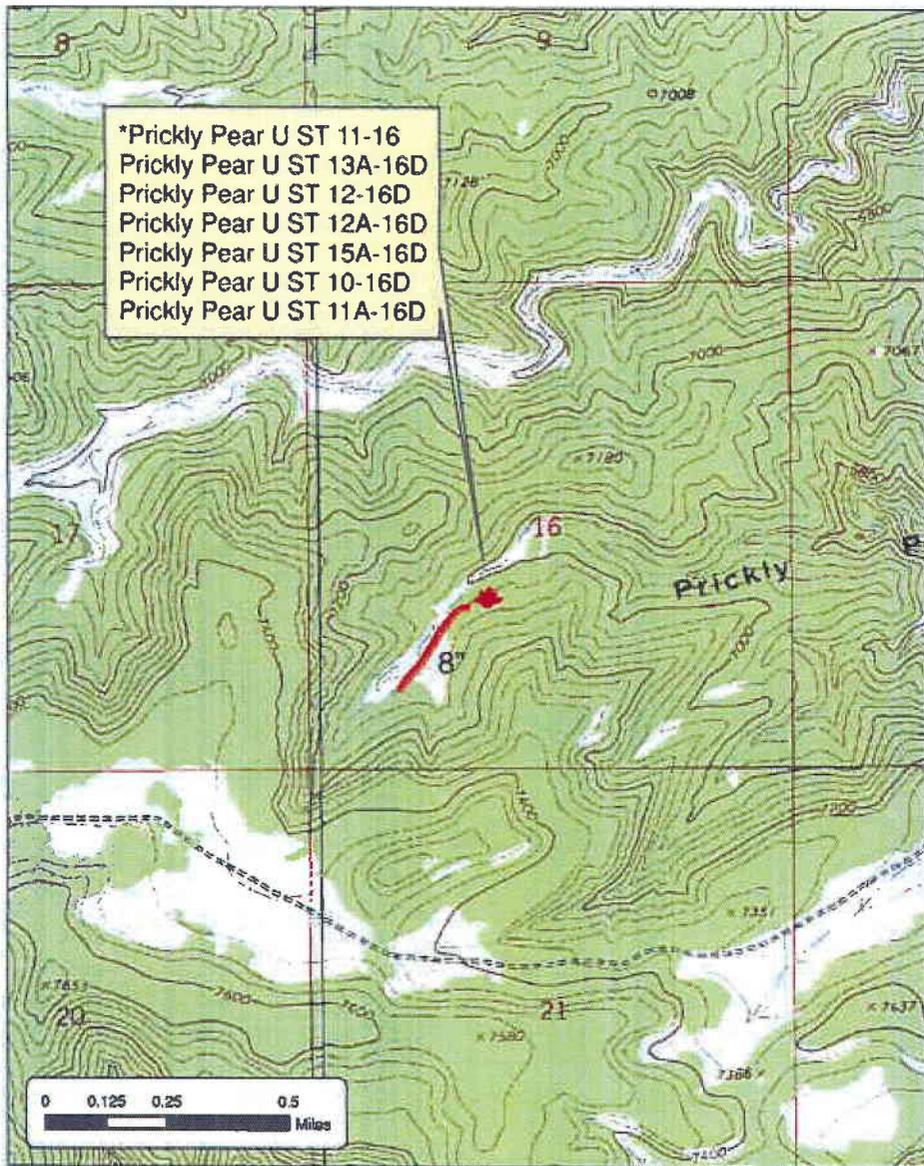

*Prickly Pear U ST 11-16
 Prickly Pear U ST 13A-16D
 Prickly Pear U ST 12-16D
 Prickly Pear U ST 12A-16D
 Prickly Pear U ST 15A-16D
 Prickly Pear U ST 10-16D
 Prickly Pear U ST 11A-16D

STATE
 Prickly Pear U ST 11-16 (1841' FSL & 1985' FWL)
 Prickly Pear U ST 13A-16D (1859' FSL & 2016' FWL)
 Prickly Pear U ST 12-16D (1864' FSL & 2023' FWL)
 Prickly Pear U ST 12A-16D (1868' FSL & 2030' FWL)
 Prickly Pear U ST 15A-16D (1872' FSL & 2037' FWL)
 Prickly Pear U ST 10-16D (1877' FSL & 2043' FWL)
 Prickly Pear U ST 11A-16D (1881' FSL & 2050' FWL)

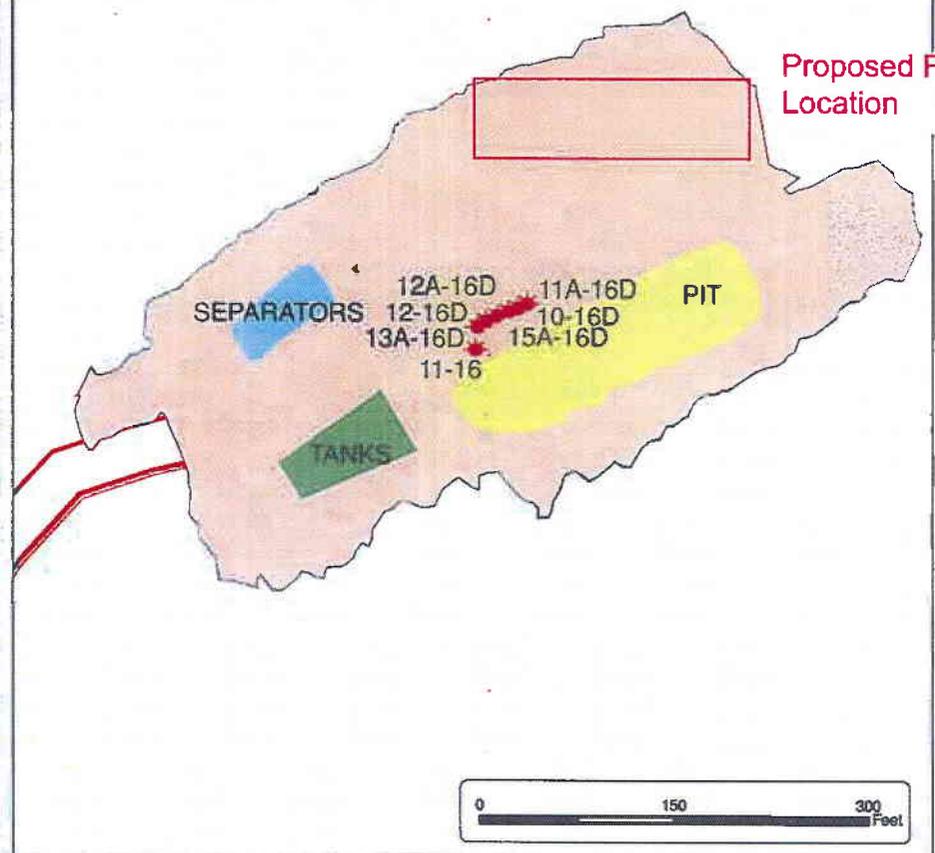

Proposed Facility Location

*Only those access and utility corridors constructed and/or applied for in this APD, are shown.

LEGEND — ROAD — PIPE SURFACE — PIPE BURIED * WELL LOCATION * SHUT IN WELL LOCATION ■ WELL DISTURBANCE ■ SEPARATORS ■ TANKS ■ PIT

Environmental Industrial Services
 Environmental & Engineering Consulting
 31 North Main Street
 Helper, Utah 84526
 (435) 472-3814
 fax (435) 472-8780
 eisec@preciscom.net

Total Road Length - 1176 ft
 Ave. Road Disturbance Total Width - 38 ft
 Ave. Road Disturbance Running Width - 30 ft
 Total Road Disturbance - 1.0 Acres
 Total Pipeline Length - 1153 ft
 Total Pipeline Disturbance - 0 Acres
 Total Pad Disturbance - 3.5 Acres



As-Built
 Bill Barrett Corporation
 NESW, Sec. 16, T12S, R15E, SLB&M
 Carbon County, Utah

UWI/API	Well	Status	UWI/API	Well	Status
430071604500	1-GOVT PCKRL	GAS	430073123900	3-27D-12-15	GAS
430071654200	SC 1-STONE CABIN	GAS	430073123700	4-27D-12-15	GAS
430073001400	1-11-ST CAB-FED	GAS	430073124300	1-28-12-15	GAS
430071501600	33-1A-CLAYBANK SPRIN	GAS	430073124200	5-27D-12-15	GAS
430073052200	16-15 (12S-15E)	GAS	430073124400	8-28D-12-15	GAS
430073001800	2-B-27-ST CAB FED	GAS	430073124100	9-28D-12-15	GAS
430071654200	SC 1-ST CAB UNIT	GAS	430073128700	9-17-12-15	GAS
430073101800	36-06-12-15	GAS	430073129500	7-18D-12-15	GAS
430073082500	13-4 (12S-14E)	GAS	430073129400	1-18D-12-15	GAS
430073082800	21-2-12-15	GAS	430073124000	9-16-12-15	GAS
430073082300	10-4-12-14	GAS	430073124500	1-16-12-15	GAS
430073095400	7-25-12-15	GAS	430073136200	2-28D-12-15	GAS
430073093300	13-16-12-15	GAS	430073139900	11-22D-12-15	GAS
430073100800	5-13-12-14	GAS	430073136000	4-22D-12-15	GAS
430073094300	5-16-12-15	GAS	430073140000	14-22D-12-15	GAS
430073094500	7-16-12-15	GAS	430073139800	12-22D-12-15	GAS
430073094400	11-16-12-15	GAS	430073136100	6-22D-12-15	GAS
430073119300	15-18-12-15	GAS	430073141300	6-21D-12-15	GAS
430073098500	7-33D-12-15	GAS	430073141200	11-21D-12-15	GAS
430073128900	7-17D-12-15	GAS	430073141400	12-21D-12-15	GAS
430073086000	5-19-12-15	GAS	430073142100	2-20D-12-15	GAS
430073107300	13-23-12-15	GAS	430073141900	8-20D-12-15	GAS
430073119600	10-27-12-15	GAS	430073135900	14-15D-12-15	GAS
430073120600	1-20-12-15	GAS	430073145600	12-16D-12-15	GAS
430073118300	15-17-12-15	GAS	430073139400	10-18D-12-15	GAS
430073119800	7-20-12-15	GAS	430073128200	14-26D-12-15	GAS
430073116400	15-21-12-15	GAS	430073128800	1-17D-12-15	GAS
430073116600	13-21D-12-15	GAS	430073129600	5-17D-12-15	GAS
430073116500	7-28D-12-15	GAS	430073131400	3-18D-12-15	GAS
430073112100	3-28D-12-15	GAS	430073131600	5-18D-12-15	GAS
430073107500	3-26D-12-15	GAS	430073131000	13-17D-12-15	GAS
430073107400	1-27D-12-15	GAS	430073130900	12-17D-12-15	GAS
430073107600	15-22D-12-15	GAS	430073131100	14-17D-12-15	GAS
430073118700	3-22-12-15	GAS	430073131200	16-18D-12-15	GAS
430073118600	7-22D-12-15	GAS	430073132800	3-21D-12-15	GAS
430073118800	5-22D-12-15	GAS	430073131500	4-18-12-15	GAS
430073135800	13-15D-12-15	GAS	430073130800	8-17D-12-15	GAS
430073119200	9-18D-12-15	GAS	430073130700	10-17D-12-15	GAS
430073118400	11-17D-12-15	GAS	430073131300	8-18D-12-15	GAS
430073119700	9-20D-12-15	GAS	430073131700	6-18D-12-15	GAS
430073119400	16-27D-12-15	GAS	430073145900	10-16D-12-15	GAS
430073119500	12-27D-12-15	GAS	430073132100	16-17D-12-15	GAS
430073118900	11-15D-12-15	GAS	430073132400	14-16D-12-15	GAS
430073125900	4-25D-12-15	GAS	430073132900	4-21D-12-15	GAS
430073126000	12-25D-12-15	GAS	430073136400	5A-27D-12-15	GAS
430073128300	2-35-12-15	GAS	430073136800	1A-28D-12-15	GAS
430073128500	4-35D-12-15	GAS	430073136300	16X-21D-12-15	GAS
430073128400	10-26D-12-15	GAS	430073140100	4A-27D-12-15	GAS
430073125700	11-18D-12-15	GAS	430073139300	14A-18D-12-15	GAS
430073125800	11-20D-12-15	GAS	430073139500	15A-18D-12-15	GAS
430073122600	2-36-12-15	GAS	430073139600	16A-18D-12-15	GAS
430073122700	4-36-12-15	GAS	430073145800	15A-16D-12-15	GAS
430073123800	13-22-12-15	GAS	430073146100	13A-16D-12-15	GAS
			430073146000	11A-16D-12-15	GAS

UWI/API	Well	Status
430073148000	5A-16D-12-15	LOC
430073148500	9A-16D-12-15	LOC
430073147900	4A-16D-12-15	LOC
430073148100	3A-16D-12-15	LOC
430073147700	6A-16D-12-15	LOC
430073148400	16A-16D-12-15	LOC
430073151600	13B-16D-12-15	LOC
430073095300	12-24-12-14	SWD
430073142200	7A-16D-12-15	WOC
430073142500	3-16D-12-15	WOC
430073145500	8-16D-12-15	WOC
430073142300	6-16D-12-15	WOC
430073132300	16-16D-12-15	WOC
430073142400	10A-16D-12-15	WOC
430073151500	14B-16D-12-15	WOC
430073132200	15-16D-12-15	WOC
430073147800	4-16D-12-15	WOC
430073151400	16B-16D-12-15	DRL

Status Legend


DRL	Currently Drilling
GAS	Currently Producing
LOC	2010 Location
SWD	Salt Water Disposal
WOC	Waiting on Completion

Yellow indicates state wells that will be completed in 2010 using treated Prickly Pear Unit water. Water could come from any of these wells to be used in treatment process and reused for state well completions.

Inlet

Weir Tanks/Treatment

Treated Water

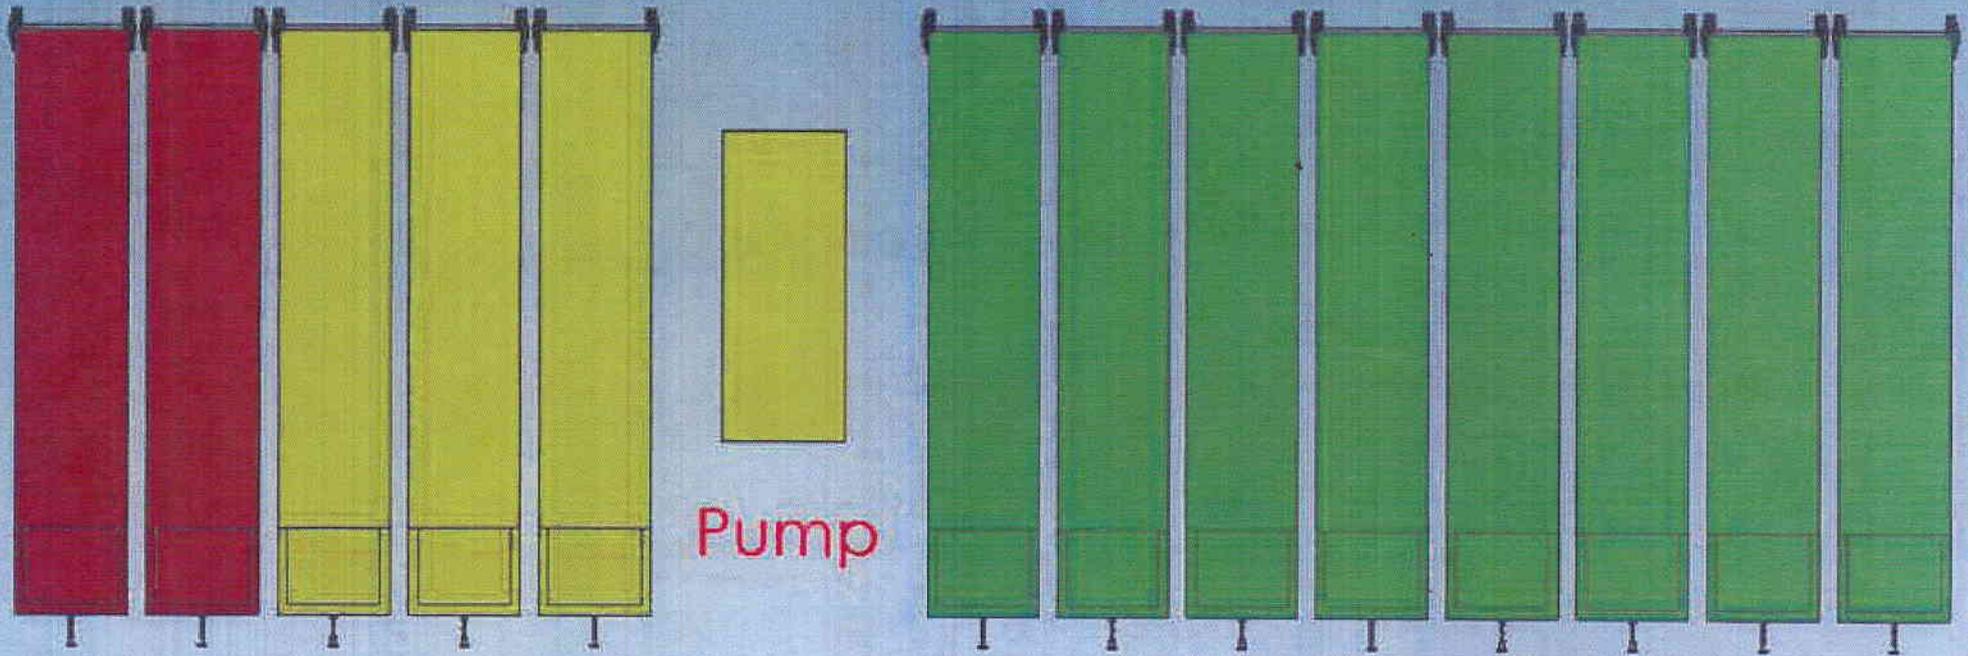

2010 STATE WELL COMPLETIONS

Uinta Basin


West Tavaputs
Prickly Pear Section 16



- WELL SYMBOLS
▲ Active Drilling Well
□ Location
⊗ Waiting on Completion

By JA

January 11, 2010 12:18 PM

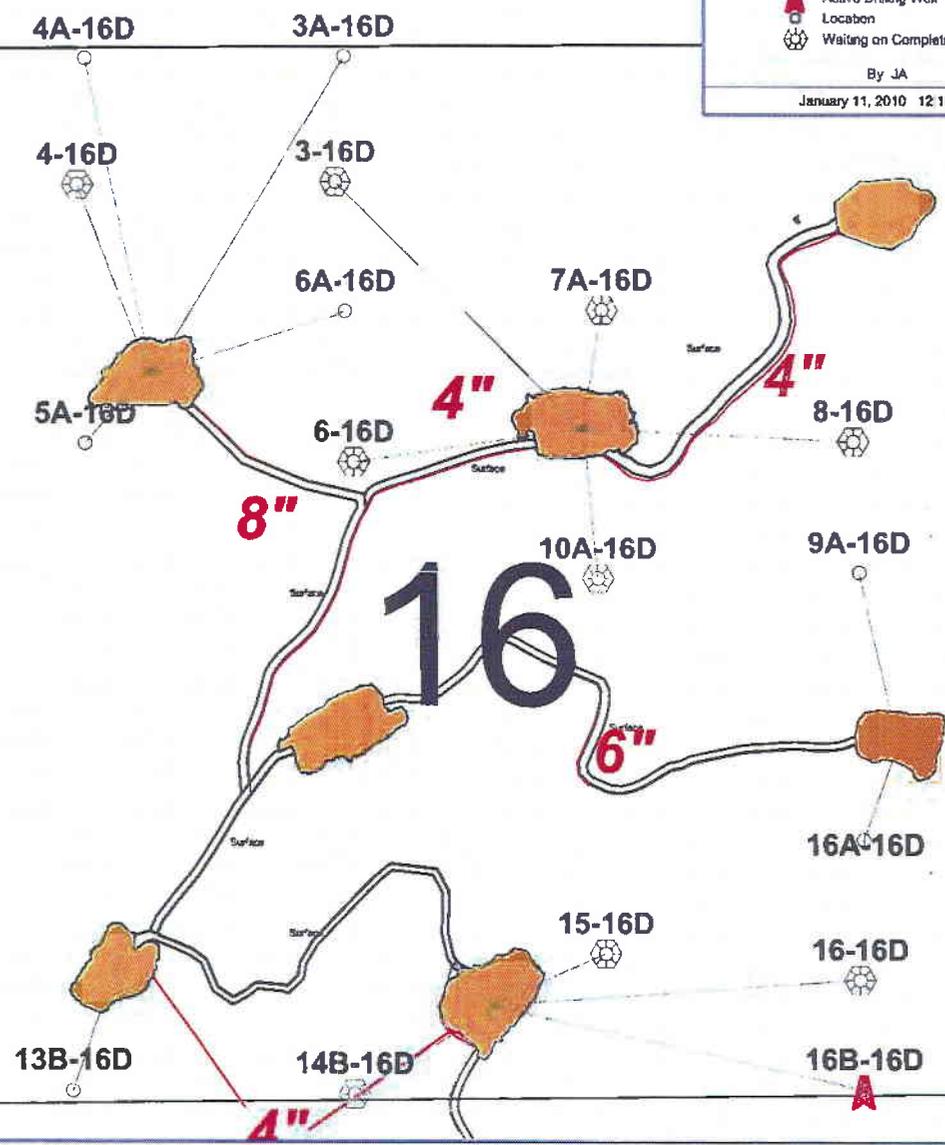

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-0681
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: PETERS POINT
1. TYPE OF WELL Gas Well	8. WELL NAME and NUMBER: PPU FED 10-26D-12-16
2. NAME OF OPERATOR: BILL BARRETT CORP	9. API NUMBER: 43007314060000
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202	PHONE NUMBER: 303 312-8164 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0270 FSL 1510 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SESW Section: 26 Township: 12.0S Range: 16.0E Meridian: S	9. FIELD and POOL or WILDCAT: PETERS POINT COUNTY: CARBON STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 2/27/2012	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> OTHER	OTHER: <input type="text" value="lower tubing"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

BBC is proposing to lower the tubing on this well to enhance production. Tubing is currently set at 5508'. Please contact Brian Hilgers with questions at 303.312.8183.

**Accepted by the
Utah Division of
Oil, Gas and Mining**

Date: February 16, 2012

By: David K. Quist

NAME (PLEASE PRINT) Brady Riley	PHONE NUMBER 303 312-8115	TITLE Permit Analyst
SIGNATURE N/A	DATE 2/13/2012	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-0681
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Gas Well		7. UNIT or CA AGREEMENT NAME: PETERS POINT
2. NAME OF OPERATOR: BILL BARRETT CORP		8. WELL NAME and NUMBER: PPU FED 10-26D-12-16
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202		9. API NUMBER: 43007314060000
PHONE NUMBER: 303 312-8164 Ext		9. FIELD and POOL or WILDCAT: PETERS POINT
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0270 FSL 1510 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SESW Section: 26 Township: 12.0S Range: 16.0E Meridian: S		COUNTY: CARBON
		STATE: UTAH

11.

CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 3/28/2012	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input checked="" type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Attached to this sundry are the procedures that took place to lower tubing on this well from 3/25/2012 - 3/28/2012. Please contact Brady Riley at 303-312-8115 with questions.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
May 02, 2012**

NAME (PLEASE PRINT) Brady Riley	PHONE NUMBER 303 312-8115	TITLE Permit Analyst
SIGNATURE N/A	DATE 4/5/2012	

**Peter's Point #10-26D-12-16 3/25/2012 06:00 - 3/26/2012 06:00**

API/UWI 43-007-31406	State/Province UT	County CARBON	Field Name West Tavaputs	Well Status Released for Work	Total Depth (ftKB) 8,161.0	Primary Job Type Workover
-------------------------	----------------------	------------------	-----------------------------	----------------------------------	-------------------------------	------------------------------

Time Log

Start Time	Dur (hr)	End Time	Code	Category	Com
06:00	2.50	08:30	SRIG	Rig Up/Down	MIRU WSU. Blow down tubing. pump 5 bbl ND tree. NU BOPs. Rig work floor.
08:30		08:30	FBCK	Flowback Well	CSG flowing to sales.
08:30	2.50	11:00	CTRL	Crew Travel	Crew travel

Peter's Point #10-26D-12-16 3/26/2012 06:00 - 3/27/2012 06:00

API/UWI 43-007-31406	State/Province UT	County CARBON	Field Name West Tavaputs	Well Status Released for Work	Total Depth (ftKB) 8,161.0	Primary Job Type Workover
-------------------------	----------------------	------------------	-----------------------------	----------------------------------	-------------------------------	------------------------------

Time Log

Start Time	Dur (hr)	End Time	Code	Category	Com
06:00	7.00	13:00	CTRL	Crew Travel	Crew Travel / safety Meet. pulling cap string. Wind & snow. PPE. pumping on well.
13:00	1.00	14:00	PULT	Pull Tubing	MI RU Weatherford to spool cap string.
14:00	3.50	17:30	FBCK	Flowback Well	Shut down wait on storm front to move through. high winds & snow
17:30	2.50	20:00	PULT	Pull Tubing	POOH with 2 3/8 and 1/4" High wind. Lay down CVR /subs. nipple. pull 1/4" out of UFJ change over to 2 7/8 UF.
20:00	2.00	22:00	PULT	Pull Tubing	POOH lay down 2 7/8 UFJ. 78 joints. well kept flowing. had to pump throughout lay down of 2 7/8.
22:00	0.50	22:30	GOP	General Operations	Change over to run production string.
22:30	2.50	01:00	CTRL	Crew Travel	Crew travel
01:00	5.00	06:00	FBCK	Flowback Well	Flow casing to production

Peter's Point #10-26D-12-16 3/27/2012 06:00 - 3/28/2012 06:00

API/UWI 43-007-31406	State/Province UT	County CARBON	Field Name West Tavaputs	Well Status Released for Work	Total Depth (ftKB) 8,161.0	Primary Job Type Workover
-------------------------	----------------------	------------------	-----------------------------	----------------------------------	-------------------------------	------------------------------

Time Log

Start Time	Dur (hr)	End Time	Code	Category	Com
06:00	5.50	11:30	FBCK	Flowback Well	CSG flow to sales.
11:30	1.50	13:00	CTRL	Crew Travel	Crew Travel. Safety Meet. Running tub. PU pipe. PPE. clear of suspended loads. ND? NU
13:00	2.25	15:15	RUTB	Run Tubing	Open well Tally. Run tubing from derrick. total of jts.
15:15	0.50	15:45	RUTB	Run Tubing	Tally new pipe PU rabbit RIH 36 jts.1137.23 ft. Old string total= 174 joints= 5494.02 ft. Hanger. Total of 210 jts. (IN WELL Mule shoe= .40", one jt 2 3/8 EUE= 31.51 ft. XN nipple 1.875 ID. 1.45L. .209 jts 2 3/8EUE= 6631.15 tub ft. land on hanger @ 6649 KB. (210 JOINTS IN WELL)
15:45	0.50	16:15	BOPR	Remove BOP's	ND/ NU tree
16:15	0.75	17:00	SRIG	Rig Up/Down	RD WSU
17:00	13.00	06:00	FBCK	Flowback Well	Turn to production

Division of Oil, Gas and Mining
OPERATOR CHANGE WORKSHEET (for state use only)

ROUTING
 CDW

X - Change of Operator (Well Sold)

Operator Name Change/Merger

The operator of the well(s) listed below has changed, effective: 1/1/2014

FROM: (Old Operator): N2165-Bill Barrett Corporation 1099 18th Street, Suite 230 Denver, CO 80202 Phone: 1 (303) 312-8134	TO: (New Operator): N4040-EnerVest Operating, LLC 1001 Fannin Street, Suite 800 Houston, TX 77002 Phone: 1 (713) 659-3500
--	---

CA No.		Unit:		Peter Point				
WELL NAME	SEC	TWN	RNG	API NO	ENTITY NO	LEASE TYPE	WELL TYPE	WELL STATUS
See Attached List								

OPERATOR CHANGES DOCUMENTATION

Enter date after each listed item is completed

- (R649-8-10) Sundry or legal documentation was received from the **FORMER** operator on: 1/7/2014
- (R649-8-10) Sundry or legal documentation was received from the **NEW** operator on: 1/7/2014
- The new company was checked on the **Department of Commerce, Division of Corporations Database** on: 1/28/2014
- a. Is the new operator registered in the State of Utah: _____ Business Number: 8850806-0161
- 5a. (R649-9-2)Waste Management Plan has been received on: Not Yet
- 5b. Inspections of LA PA state/fee well sites complete on: Yes
- 5c. Reports current for Production/Disposition & Sundries on: 1/24/2014
- Federal and Indian Lease Wells:** The BLM and or the BIA has approved the merger, name change, or operator change for all wells listed on Federal or Indian leases on: BLM Not Yet BIA N/A
- Federal and Indian Units:**
 The BLM or BIA has approved the successor of unit operator for wells listed on: Not Yet
- Federal and Indian Communization Agreements ("CA"):**
 The BLM or BIA has approved the operator for all wells listed within a CA on: N/A
- Underground Injection Control ("UIC")** Division has approved UIC Form 5 Transfer of Authority to **Inject**, for the enhanced/secondary recovery unit/project for the water disposal well(s) listed on: Yes

DATA ENTRY:

- Changes entered in the **Oil and Gas Database** on: 1/28/2014
- Changes have been entered on the **Monthly Operator Change Spread Sheet** on: 1/28/2014
- Bond information entered in RBDMS on: 1/28/2014
- Fee/State wells attached to bond in RBDMS on: 1/28/2014
- Injection Projects to new operator in RBDMS on: 1/28/2014
- Receipt of Acceptance of Drilling Procedures for APD/New on: 1/7/2014
- Surface Agreement Sundry from **NEW** operator on Fee Surface wells received on: 1/7/2014

BOND VERIFICATION:

- Federal well(s) covered by Bond Number: RLB7886
- Indian well(s) covered by Bond Number: RLB7886
- a. (R649-3-1) The **NEW** operator of any state/fee well(s) listed covered by Bond Number B008371
- b. The **FORMER** operator has requested a release of liability from their bond on: N/A

LEASE INTEREST OWNER NOTIFICATION:

- (R649-2-10) The **NEW** operator of the fee wells has been contacted and informed by a letter from the Division of their responsibility to notify all interest owners of this change on: 1/28/2014

COMMENTS:

Bill Barrett Corporation (N2165) to EnerVest Operating, LLC (N4040)

Effective 1/1/2014

Peter Point Unit

Well Name	Sec	TWN	RNG	API Number	Entity	Mineral Lease	Surface Lease	Well Type	Well Status
PPU FED 11-34D-12-16	34	120S	160E	4300731465		Federal	Federal	GW	APD
PPU FED 10-34D-12-16	34	120S	160E	4300731469		Federal	Federal	GW	APD
PETERS POINT UF 15X-36D-12-16	36	120S	160E	4300750178		Federal	Federal	GW	APD
PETERS POINT UF 10-1D-13-16	36	120S	160E	4300750182		Federal	Federal	GW	APD
PETERS POINT UF 9-1D-13-16	36	120S	160E	4300750183		Federal	Federal	GW	APD
PPU FED 9-34D-12-16	34	120S	160E	4300731430	17225	Federal	Federal	GW	OPS
PPU FED 15-35D-12-16	35	120S	160E	4300731475	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 12A-6D-13-17	31	120S	170E	4300750034	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 11A-31D-12-17	31	120S	170E	4300750036	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 9-6D-13-17	6	130S	170E	4300750120	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 14-6D-13-17	6	130S	170E	4300750121	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 15-6D-13-17	6	130S	170E	4300750122	2470	Federal	Federal	GW	OPS
PETERS POINT UF 2-7D-13-17	6	130S	170E	4300750149	2470	Federal	Federal	GW	OPS
PETERS POINT UF 1-7D-13-17	6	130S	170E	4300750150	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 36-2	36	120S	160E	4300730761	2470	Federal	Federal	GW	P
PETERS POINT U FED 36-3	36	120S	160E	4300730762	2470	Federal	Federal	GW	P
PETERS POINT U FED 36-4	36	120S	160E	4300730763	2470	Federal	Federal	GW	P
PETERS POINT U FED 14-25D-12-16	36	120S	160E	4300730764	2470	Federal	Federal	GW	P
PETERS POINT U FED 4-31D-12-17	36	120S	160E	4300730810	2470	Federal	Federal	GW	P
PETERS POINT U FED 16-26D-12-16	36	120S	160E	4300730812	2470	Federal	Federal	GW	P
PETERS POINT U FED 6-7D-13-17	6	130S	170E	4300730859	14692	Federal	Federal	GW	P
PETERS POINT U FED 16-35	35	120S	160E	4300730965	2470	Federal	Federal	GW	P
PETERS POINT U FED 11-6-13-17	6	130S	170E	4300730982	2470	Federal	Federal	GW	P
PETERS POINT U FED 16-6D-13-17	6	130S	170E	4300731004	2470	Federal	Federal	GW	P
PETERS POINT U FED 16-31D-12-17	6	130S	170E	4300731005	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-31D-12-17	36	120S	160E	4300731009	2470	Federal	Federal	GW	P
PETERS POINT U FED 2-36D-12-16	36	120S	160E	4300731010	2470	Federal	Federal	GW	P
PETERS POINT U FED 9-36-12-16	36	120S	160E	4300731011	2470	Federal	Federal	GW	P
PETERS POINT U FED 8-35D-12-16	36	120S	160E	4300731024	2470	Federal	Federal	GW	P
PETERS POINT U FED 4-12D-13-16	2	130S	160E	4300731049	14692	Federal	State	GW	P
PETERS POINT U FED 2-12D-13-16	6	130S	170E	4300731158	14692	Federal	Federal	GW	P
PETERS POINT U FED 10-36D-12-16	36	120S	160E	4300731174	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-36D-12-16	36	120S	160E	4300731175	2470	Federal	Federal	GW	P
PPU FED 15-6D-13-17	6	130S	170E	4300731261	16103	Federal	Federal	GW	P
PP UF 3-36-12-16	36	120S	160E	4300731271	2470	Federal	Federal	GW	P
PP UF 6-36-12-16	36	120S	160E	4300731272	2470	Federal	Federal	GW	P
PPU FED 6-35D-12-16	35	120S	160E	4300731275	2470	Federal	Federal	GW	P
PPU FED 8-34-12-16	34	120S	160E	4300731279	2470	Federal	Federal	GW	P
PPU FED 6-34D-12-16	34	120S	160E	4300731281	2470	Federal	Federal	GW	P
PPU FED 7-1D-13-16 ULTRA DEEP	6	130S	170E	4300731293	14692	Federal	Federal	GW	P
PPU FED 16-27-12-16	27	120S	160E	4300731318	2470	Federal	Federal	GW	P
PPU FED 10-27D-12-16	27	120S	160E	4300731319	2470	Federal	Federal	GW	P
PPU FED 2-34D-12-16	34	120S	160E	4300731320	2470	Federal	Federal	GW	P
PPU FED 2-7D-13-17 DEEP	6	130S	170E	4300731326	14692	Federal	Federal	GW	P
PPU FED 2-35D-12-16	35	120S	160E	4300731345	2470	Federal	Federal	GW	P
PPU FED 7-35D-12-16	35	120S	160E	4300731346	2470	Federal	Federal	GW	P
PPU FED 4-35D-12-16	35	120S	160E	4300731347	2470	Federal	Federal	GW	P
PPU FED 7-36D-12-16	36	120S	160E	4300731348	2470	Federal	Federal	GW	P
PPU FED 11-36D-12-16	36	120S	160E	4300731349	2470	Federal	Federal	GW	P
PPU FED 15-25D-12-16	36	120S	160E	4300731351	2470	Federal	Federal	GW	P
PPU FED 13-25D-12-16	36	120S	160E	4300731352	2470	Federal	Federal	GW	P
PPU FED 4-36D-12-16	36	120S	160E	4300731353	2470	Federal	Federal	GW	P
PPU FED 1-35D-12-16	35	120S	160E	4300731365	2470	Federal	Federal	GW	P
PPU FED 13-26D-12-16	26	120S	160E	4300731403	2470	Federal	Federal	GW	P
PPU FED 15-26D-12-16	26	120S	160E	4300731404	2470	Federal	Federal	GW	P
PPU FED 3-35D-12-16	26	120S	160E	4300731405	2470	Federal	Federal	GW	P

Bill Barrett Corporation (N2165) to EnerVest Operating, LLC (N4040)

Effective 1/1/2014

Peter Point Unit

Well Name	Sec	TWN	RNG	API Number	Entity	Mineral Lease	Surface Lease	Well Type	Well Status
PPU FED 10-26D-12-16	26	120S	160E	4300731406	2470	Federal	Federal	GW	P
PPU FED 11-26D-12-16	26	120S	160E	4300731407	2470	Federal	Federal	GW	P
PPU FED 12-26D-12-16	26	120S	160E	4300731408	2470	Federal	Federal	GW	P
PPU FED 11-27D-12-16	27	120S	160E	4300731409	2470	Federal	Federal	GW	P
PPU FED 15-27D-12-16	27	120S	160E	4300731410	2470	Federal	Federal	GW	P
PPU FED 9-27D-12-16	27	120S	160E	4300731411	2470	Federal	Federal	GW	P
PPU FED 1-34D-12-16	34	120S	160E	4300731427	2470	Federal	Federal	GW	P
PPU FED 7-34D-12-16	34	120S	160E	4300731428	2470	Federal	Federal	GW	P
PPU FED 5-35D-12-16	34	120S	160E	4300731429	2470	Federal	Federal	GW	P
PPU FED 3-34D-12-16	34	120S	160E	4300731466	2470	Federal	Federal	GW	P
PPU FED 5-34D-12-16	34	120S	160E	4300731467	2470	Federal	Federal	GW	P
PPU FED 4-34D-12-16	34	120S	160E	4300731468	2470	Federal	Federal	GW	P
PPU FED 10-35D-12-16	35	120S	160E	4300731474	2470	Federal	Federal	GW	P
PPU FED 9-35D-12-16	35	120S	160E	4300731476	2470	Federal	Federal	GW	P
PETERS POINT U FED 9-26D-12-16	25	120S	160E	4300750021	2470	Federal	Federal	GW	P
PETERS POINT U FED 11-25D-12-16	25	120S	160E	4300750022	2470	Federal	Federal	GW	P
PETERS POINT U FED 10-31D-12-17	31	120S	170E	4300750023	2470	Federal	Federal	GW	P
PETERS POINT U FED 11-31D-12-17	31	120S	170E	4300750024	2470	Federal	Federal	GW	P
PETERS POINT U FED 13A-31D-12-17	31	120S	170E	4300750025	2470	Federal	Federal	GW	P
PETERS POINT U FED 13-31D-12-17	31	120S	170E	4300750026	2470	Federal	Federal	GW	P
PETERS POINT U FED 14-31D-12-17	31	120S	170E	4300750027	2470	Federal	Federal	GW	P
PETERS POINT U FED 14A-31D-12-17	31	120S	170E	4300750028	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-25D-12-16	25	120S	160E	4300750029	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-6D-13-17	31	120S	170E	4300750033	2470	Federal	Federal	GW	P
PETERS POINT U FED 10-25D-12-16	25	120S	160E	4300750035	2470	Federal	Federal	GW	P
PETERS POINT U FED 13-36D-12-16	36	120S	160E	4300750037	2470	Federal	Federal	GW	P
PETERS POINT U FED 15-36D-12-16	36	120S	160E	4300750038	2470	Federal	Federal	GW	P
PETERS POINT U FED 11-1D-13-16	36	120S	160E	4300750039	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-1D-13-16	36	120S	160E	4300750040	2470	Federal	Federal	GW	P
PETERS POINT U FED 3A-34D-12-16	27	120S	160E	4300750063	2470	Federal	Federal	GW	P
PETERS POINT U FED 4A-34D-12-16	27	120S	160E	4300750064	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-27D-12-16	27	120S	160E	4300750065	2470	Federal	Federal	GW	P
PETERS POINT U FED 13-27D-12-16	27	120S	160E	4300750066	2470	Federal	Federal	GW	P
PETERS POINT U FED 13A-27D-12-16	27	120S	160E	4300750067	2470	Federal	Federal	GW	P
PETERS POINT U FED 14A-27D-12-16	27	120S	160E	4300750069	2470	Federal	Federal	GW	P
PETERS POINT U FED 5-31D-12-17	36	120S	160E	4300750109	2470	Federal	Federal	GW	P
PETERS POINT U FED 6-31D-12-17	36	120S	160E	4300750116	2470	Federal	Federal	GW	P
PETERS POINT U FED 9X-36D-12-16	36	120S	160E	4300750117	2470	Federal	Federal	GW	P
PETERS POINT U FED 1-36D-12-16	36	120S	160E	4300750118	2470	Federal	Federal	GW	P
PETERS POINT U FED 10-6D-13-17	6	130S	170E	4300750119	2470	Federal	Federal	GW	P
PETERS POINT U FED 15-31D-12-17	6	130S	170E	4300750123	2470	Federal	Federal	GW	P
PETERS POINT UF 12-5D-13-17	6	130S	170E	4300750151	2470	Federal	Federal	GW	P
PETERS POINT UF 13-5D-13-17	6	130S	170E	4300750152	2470	Federal	Federal	GW	P
PETERS POINT UF 13-30D-12-17	30	120S	170E	4300750153	18347	Federal	Federal	GW	P
PETERS POINT UF 14-30D-12-17	30	120S	170E	4300750154	18350	Federal	Federal	GW	P
PETERS POINT UF 12-30D-12-17	30	120S	170E	4300750155	18346	Federal	Federal	GW	P
PETERS POINT UF 11-30D-12-17	30	120S	170E	4300750156	18348	Federal	Federal	GW	P
PETERS POINT UF 3-31D-12-17	30	120S	170E	4300750157	2470	Federal	Federal	GW	P
PETERS POINT UF 2-31D-12-17	30	120S	170E	4300750158	18349	Federal	Federal	GW	P
PETERS POINT UF 16-25D-12-16	30	120S	170E	4300750159	2470	Federal	Federal	GW	P
PETERS POINT UF 9-25D-12-16	30	120S	170E	4300750160	2470	Federal	Federal	GW	P
PETERS POINT UF 7X-36D-12-16	36	120S	160E	4300750231	2470	Federal	Federal	GW	P
PETERS POINT UF 8-36D-12-16	36	120S	160E	4300750232	2470	Federal	Federal	GW	P
PPU FED 14-26D-12-16	26	120S	160E	4300731277	2470	Federal	Federal	GW	S
PPU FED 5-36D-12-16	36	120S	160E	4300731350	2470	Federal	Federal	GW	S

COPY

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 9

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

5. LEASE DESIGNATION AND SERIAL NUMBER:
(see attached well list)

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
N/A

7. UNIT or CA AGREEMENT NAME:

8. WELL NAME and NUMBER:
(see attached well list)

9. API NUMBER:

10. FIELD AND POOL, OR WILDCAT:

1. TYPE OF WELL
OIL WELL GAS WELL OTHER _____

2. NAME OF OPERATOR:
ENERVEST OPERATING, LLC

3. ADDRESS OF OPERATOR:
1001 FANNIN, ST. STE 800 CITY HOUSTON STATE TX ZIP 77002 PHONE NUMBER:
(713) 659-3500

4. LOCATION OF WELL
FOOTAGES AT SURFACE: (see attached well list) COUNTY:
QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will start: 1/1/2014	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
<input type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of work completion:	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input checked="" type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLARE
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/RESUME)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: _____
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
ENERVEST OPERATING, LLC IS SUBMITTING THIS SUNDRY AS NOTIFICATION THAT THE WELLS LISTED ON THE ATTACHED LIST HAVE BEEN SOLD TO ENERVEST OPERATING, LLC BY BILL BARRETT CORPORATION EFFECTIVE 1/1/2014. PLEASE REFER ALL FUTURE CORRESPONDENCE TO THE ADDRESS BELOW.

EnerVest Operating, L.L.C.
1001 Fannin, Suite 800
Houston, Texas 77002
713-659-3500
(BLM BOND # RLB 7886, STATE/FEE BOND # B008321)

BILL BARRETT CORPORATION
Duane Zavadil NAME (PLEASE PRINT)
[Signature] SIGNATURE
Senior Vice President -
EH&S, Government and Regulatory Affairs N2115

ENERVEST OPERATING, LLC
RONNIE L YOUNG NAME (PLEASE PRINT)
[Signature] SIGNATURE
DIRECTOR - REGULATORY N4040

NAME (PLEASE PRINT) RONNIE YOUNG TITLE DIRECTOR - REGULATORY
SIGNATURE [Signature] DATE 12/10/2013

(This space for State use on) **APPROVED** RECEIVED
JAN 28 2014 4-PM JAN 07 2014
DIV. OF OIL, GAS & MINING (See Instructions on Reverse Side) DIV. OF OIL, GAS & MINING
Rachael Medina

UDOGM CHANGE OF OPERATOR WELL LIST

Well Name	Sec	TWN	RNG	API Number	Entity	Lease	Well Type	Well Status	Unit
JACK CANYON UNIT 8-32	32	120S	160E	4300730460	15167	State	WI	A	
JACK CYN U ST 14-32	32	120S	160E	4300730913	15166	State	WD	A	
PRICKLY PEAR U FED 12-24	24	120S	140E	4300730953	14467	Federal	WD	A	
PPU FED 11-23D-12-15	23	120S	150E	4300731440		Federal	GW	APD	PRICKLY PEAR
PPU FED 4-26D-12-15	23	120S	150E	4300731441		Federal	GW	APD	PRICKLY PEAR
PPU FED 14-23D-12-15	23	120S	150E	4300731442		Federal	GW	APD	PRICKLY PEAR
PPU FED 12-23D-12-15	23	120S	150E	4300731443		Federal	GW	APD	PRICKLY PEAR
PPU FED 11-34D-12-16	34	120S	160E	4300731465		Federal	GW	APD	PETERS POINT
PPU FED 10-34D-12-16	34	120S	160E	4300731469		Federal	GW	APD	PETERS POINT
HORSE BENCH FED 4-27D-12-16	27	120S	160E	4300750092		Federal	GW	APD	
HORSE BENCH FED 5-27D-12-16	27	120S	160E	4300750093		Federal	GW	APD	
PRICKLY PEAR U FED 12-7D-12-15	07	120S	150E	4300750094		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR U FED 11-7D-12-15	07	120S	150E	4300750095		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR U FED 13-7D-12-15	07	120S	150E	4300750096		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR U FED 14-7D-12-15	07	120S	150E	4300750097		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11-8D-12-15	08	120S	150E	4300750124		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12-8D-12-15	08	120S	150E	4300750125		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13-8D-12-15	08	120S	150E	4300750126		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14-8D-12-15	08	120S	150E	4300750127		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9-21D-12-15	21	120S	150E	4300750128		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-21D-12-15	21	120S	150E	4300750129		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10-21D-12-15	21	120S	150E	4300750130		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-21D-12-15	21	120S	150E	4300750131		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-21D-12-15	21	120S	150E	4300750132		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15X-21D-12-15	21	120S	150E	4300750133		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16-21D-12-15	21	120S	150E	4300750134		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-21D-12-15	21	120S	150E	4300750135		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-22D-12-15	21	120S	150E	4300750148		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1A-27D-12-15	22	120S	150E	4300750161		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2A-27D-12-15	22	120S	150E	4300750162		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3A-27D-12-15	22	120S	150E	4300750163		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-22D-12-15	22	120S	150E	4300750164		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-22D-12-15	22	120S	150E	4300750165		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-22D-12-15	22	120S	150E	4300750166		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12A-22D-12-15	22	120S	150E	4300750167		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-22D-12-15	22	120S	150E	4300750168		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-22D-12-15	22	120S	150E	4300750169		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-22D-12-15	22	120S	150E	4300750170		Federal	GW	APD	PRICKLY PEAR
PETERS POINT UF 15X-36D-12-16	36	120S	160E	4300750178		Federal	GW	APD	PETERS POINT
PRICKLY PEAR UF 15A-15D-12-15	15	120S	150E	4300750180		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11B-15D-12-15	15	120S	150E	4300750181		Federal	GW	APD	PRICKLY PEAR
PETERS POINT UF 10-1D-13-16	36	120S	160E	4300750182		Federal	GW	APD	PETERS POINT
PETERS POINT UF 9-1D-13-16	36	120S	160E	4300750183		Federal	GW	APD	PETERS POINT
PRICKLY PEAR UF 16A-15D-12-15	15	120S	150E	4300750184		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3A-18D-12-15	07	120S	150E	4300750185		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4A-18D-12-15	07	120S	150E	4300750186		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-7D-12-15	07	120S	150E	4300750187		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-18D-12-15	07	120S	150E	4300750188		Federal	GW	APD	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR UF 12A-7D-12-15	07	120S	150E	4300750189	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-7D-12-15	07	120S	150E	4300750190	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-7D-12-15	07	120S	150E	4300750191	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR FEDERAL 1-12D-12-14	12	120S	140E	4300750205	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-12D-12-14	12	120S	140E	4300750206	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-12D-12-14	12	120S	140E	4300750207	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-12D-12-14	12	120S	140E	4300750208	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8-12D-12-14	12	120S	140E	4300750209	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-7D-12-15	12	120S	140E	4300750210	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5-7D-12-15	12	120S	140E	4300750211	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-12D-12-14	12	120S	140E	4300750212	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-7D-12-15	12	120S	140E	4300750213	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-14D-12-15	14	120S	150E	4300750214	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-14D-12-15	14	120S	150E	4300750215	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9-14D-12-15	14	120S	150E	4300750217	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-14D-12-15	14	120S	150E	4300750218	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10-14D-12-15	14	120S	150E	4300750219	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-14D-12-15	14	120S	150E	4300750220	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-14D-12-15	14	120S	150E	4300750222	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16-14D-12-15	14	120S	150E	4300750223	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-14D-12-15	14	120S	150E	4300750224	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1A-18D-12-15	07	120S	150E	4300750225	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2A-18D-12-15	07	120S	150E	4300750226	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-7D-12-15	07	120S	150E	4300750227	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-7D-12-15	07	120S	150E	4300750228	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-7D-12-15	07	120S	150E	4300750229	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-7D-12-15	07	120S	150E	4300750230	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-12D-12-14	12	120S	140E	4300750233	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-12D-12-14	12	120S	140E	4300750234	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-12D-12-14	12	120S	140E	4300750235	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12A-8D-12-15	08	120S	150E	4300750236	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-12D-12-14	12	120S	140E	4300750237	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-8D-12-15	08	120S	150E	4300750238	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-8D-12-15	08	120S	150E	4300750239	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-8D-12-15	08	120S	150E	4300750240	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-8D-12-15	08	120S	150E	4300750260	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-8D-12-15	08	120S	150E	4300750261	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-8D-12-15	08	120S	150E	4300750262	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-8D-12-15	08	120S	150E	4300750263	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-8D-12-15	08	120S	150E	4300750264	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-8D-12-15	08	120S	150E	4300750265	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-8D-12-15	08	120S	150E	4300750266	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5-8D-12-15	08	120S	150E	4300750267	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6-8D-12-15	08	120S	150E	4300750268	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-8D-12-15	08	120S	150E	4300750269	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-8D-12-15	08	120S	150E	4300750270	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8-8D-12-15	08	120S	150E	4300750271	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1-8D-12-15	08	120S	150E	4300750272	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-8D-12-15	08	120S	150E	4300750273	Federal	GW	APD	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR UF 5-9D-12-15	09	120S	150E	4300750274	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-9D-12-15	09	120S	150E	4300750275	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-9D-12-15	09	120S	150E	4300750276	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-9D-12-15	09	120S	150E	4300750277	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-9D-12-15	09	120S	150E	4300750278	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11-9D-12-15	09	120S	150E	4300750279	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12A-9D-12-15	09	120S	150E	4300750280	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6-9D-12-15	09	120S	150E	4300750281	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-9D-12-15	09	120S	150E	4300750282	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR US 1X-16D-12-15	10	120S	150E	4300750283	State	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-15D-12-15	10	120S	150E	4300750284	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-15D-12-15	10	120S	150E	4300750285	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-15D-13-15	10	120S	150E	4300750286	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-10D-12-15	15	120S	150E	4300750287	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13-10D-12-15	10	120S	150E	4300750288	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15-10D-12-15	15	120S	150E	4300750289	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-10D-12-15	15	120S	150E	4300750290	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9-10D-12-15	15	120S	150E	4300750291	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-10D-12-15	10	120S	150E	4300750292	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10-10D-12-15	15	120S	150E	4300750293	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16-10D-12-15	15	120S	150E	4300750294	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13-11D-12-15	15	120S	150E	4300750295	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-11D-12-15	15	120S	150E	4300750296	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12-11D-12-15	15	120S	150E	4300750297	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-10D-12-15	10	120S	150E	4300750298	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12-10D-12-15	10	120S	150E	4300750299	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11-10D-12-15	10	120S	150E	4300750300	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3A-15D-12-15	10	120S	150E	4300750301	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12-14D-12-15	14	120S	150E	4300750302	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-15D-12-15	10	120S	150E	4300750303	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4A-15D-12-15	10	120S	150E	4300750304	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14-10D-12-15	10	120S	150E	4300750305	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-17D-12-15	17	120S	150E	4300750306	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-17D-12-15	17	120S	150E	4300750307	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-17D-12-15	17	120S	150E	4300750308	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-7D-12-15	07	120S	150E	4300750309	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-17D-12-15	17	120S	150E	4300750310	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6-7D-12-15	07	120S	150E	4300750311	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-17D-12-15	17	120S	150E	4300750312	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-7D-12-15	07	120S	150E	4300750313	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-7D-12-15	07	120S	150E	4300750314	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-7D-12-15	07	120S	150E	4300750315	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6X-17D-12-15	17	120S	150E	4300750316	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-17D-12-15	17	120S	150E	4300750317	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15B-17D-12-15	17	120S	150E	4300750318	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-20D-12-15	20	120S	150E	4300750319	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1-7D-12-15	07	120S	150E	4300750320	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-20D-12-15	20	120S	150E	4300750321	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-20D-12-15	20	120S	150E	4300750322	Federal	GW	APD	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR UF 10A-20D-12-15	20	120S	150E	4300750323		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10-20D-12-15	20	120S	150E	4300750324		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-7D-12-15	07	120S	150E	4300750325		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-20D-12-15	20	120S	150E	4300750326		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-20D-12-15	20	120S	150E	4300750327		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-20D-12-15	20	120S	150E	4300750328		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8-7D-12-15	07	120S	150E	4300750329		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15-20D-12-15	20	120S	150E	4300750330		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-7D-12-15	07	120S	150E	4300750331		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6-10D-12-15	09	120S	150E	4300750332		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-10D-12-15	09	120S	150E	4300750333		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-10D-12-15	09	120S	150E	4300750334		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-10D-12-15	09	120S	150E	4300750335		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5-10D-12-15	09	120S	150E	4300750336		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12A-10D-12-15	09	120S	150E	4300750338		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-10D-12-15	09	120S	150E	4300750339		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-10D-12-15	09	120S	150E	4300750340		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8-9D-12-15	09	120S	150E	4300750341		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-9D-12-15	09	120S	150E	4300750342		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-9D-12-15	09	120S	150E	4300750343		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-9D-12-15	09	120S	150E	4300750344		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1-9D-12-15	09	120S	150E	4300750345		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-9D-12-15	09	120S	150E	4300750346		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1-24D-12-1	24	120S	150E	4300750348		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9-13D-12-15	13	120S	150E	4300750349		Federal	GW	APD	PRICKLY PEAR
HORSE BENCH FED 4-20D-12-17	19	120S	170E	4300750350		Federal	GW	APD	
Horse Bench Federal 16-18D-12-17	19	120S	170E	4300750351		Federal	GW	APD	
PPU FED 9-34D-12-16	34	120S	160E	4300731430	17225	Federal	GW	OPS	PETERS POINT
PPU FED 15-35D-12-16	35	120S	160E	4300731475	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT U FED 12A-6D-13-17	31	120S	170E	4300750034	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT U FED 11A-31D-12-17	31	120S	170E	4300750036	2470	Federal	GW	OPS	PETERS POINT
PRICKLY PEAR U FED 7-21D-12-15	21	120S	150E	4300750055	14794	Federal	GW	OPS	PRICKLY PEAR
PETERS POINT U FED 9-6D-13-17	06	130S	170E	4300750120	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT U FED 14-6D-13-17	06	130S	170E	4300750121	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT U FED 15-6D-13-17	06	130S	170E	4300750122	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT UF 2-7D-13-17	06	130S	170E	4300750149	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT UF 1-7D-13-17	06	130S	170E	4300750150	2470	Federal	GW	OPS	PETERS POINT
PRICKLY PEAR US 1A-16D-12-15	09	120S	150E	4300750192	14794	State	GW	OPS	PRICKLY PEAR
PRICKLY PEAR US 2A-16D-12-15	09	120S	150E	4300750193	14794	State	GW	OPS	PRICKLY PEAR
PRICKLY PEAR US 2-16D-12-15	09	120S	150E	4300750194	14794	State	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 9A-9D-12-15	09	120S	150E	4300750196	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 10-9D-12-15	09	120S	150E	4300750197	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 10A-9D-12-15	09	120S	150E	4300750198	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 14-9D-12-15	09	120S	150E	4300750199	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 14A-9D-12-15	09	120S	150E	4300750200	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 15-9D-12-15	09	120S	150E	4300750201	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 15A-9D-12-15	09	120S	150E	4300750203	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 16A-9D-12-15	09	120S	150E	4300750204	14794	Federal	GW	OPS	PRICKLY PEAR
SHARPLES 1 GOVT PICKRELL	11	120S	150E	4300716045	7030	Federal	GW	P	

UDOGM CHANGE OF OPERATOR WELL LIST

STONE CABIN UNIT 1	13	120S	140E	4300716542	12052 Federal	GW	P	
STONE CABIN FED 1-11	11	120S	140E	4300730014	6046 Federal	GW	P	
STONE CABIN FED 2-B-27	27	120S	150E	4300730018	14794 Federal	GW	P	PRICKLY PEAR
JACK CANYON 101-A	33	120S	160E	4300730049	2455 Federal	GW	P	
PETERS POINT ST 2-2-13-16	02	130S	160E	4300730521	14387 State	GW	P	
PRICKLY PEAR ST 16-15	16	120S	150E	4300730522	14794 State	GW	P	PRICKLY PEAR
PETERS POINT U FED 36-2	36	120S	160E	4300730761	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 36-3	36	120S	160E	4300730762	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 36-4	36	120S	160E	4300730763	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 14-25D-12-16	36	120S	160E	4300730764	2470 Federal	GW	P	PETERS POINT
HUNT RANCH 3-4	03	120S	150E	4300730775	13158 State	GW	P	
PETERS POINT U FED 4-31D-12-17	36	120S	160E	4300730810	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 16-26D-12-16	36	120S	160E	4300730812	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR UNIT 13-4	13	120S	140E	4300730825	14353 Federal	GW	P	
PRICKLY PEAR UNIT 21-2	21	120S	150E	4300730828	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 6-7D-13-17	06	130S	170E	4300730859	14692 Federal	GW	P	PETERS POINT
PETERS POINT ST 4-2-13-16	02	130S	160E	4300730866	14386 State	GW	P	
PRICKLY PEAR U ST 13-16	16	120S	150E	4300730933	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 11-16	16	120S	150E	4300730944	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 7-16	16	120S	150E	4300730945	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7-25	25	120S	150E	4300730954	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 16-35	35	120S	160E	4300730965	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 11-6-13-17	06	130S	170E	4300730982	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 16-6D-13-17	06	130S	170E	4300731004	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 16-31D-12-17	06	130S	170E	4300731005	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 5-13-12-14	13	120S	140E	4300731008	14897 Federal	GW	P	
PETERS POINT U FED 12-31D-12-17	36	120S	160E	4300731009	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 2-36D-12-16	36	120S	160E	4300731010	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 9-36-12-16	36	120S	160E	4300731011	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U ST 36-06	36	120S	150E	4300731018	14794 State	GW	P	PRICKLY PEAR
PETERS POINT U FED 8-35D-12-16	36	120S	160E	4300731024	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 4-12D-13-16	02	130S	160E	4300731049	14692 Federal	GW	P	PETERS POINT
PETERS POINT ST 5-2D-13-16 DEEP	02	130S	160E	4300731056	15909 State	GW	P	
PRICKLY PEAR U FED 13-23-12-15	23	120S	150E	4300731073	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1-27D-12-15	23	120S	150E	4300731074	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-26D-12-15	23	120S	150E	4300731075	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-22D-12-15	23	120S	150E	4300731076	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-28D-12-15	21	120S	150E	4300731121	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 2-12D-13-16	06	130S	170E	4300731158	14692 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 15-21-12-15	21	120S	150E	4300731164	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7-28D-12-15	21	120S	150E	4300731165	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 13-21D-12-15	21	120S	150E	4300731166	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 10-36D-12-16	36	120S	160E	4300731174	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-36D-12-16	36	120S	160E	4300731175	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 15-17-12-15	17	120S	150E	4300731183	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 11-17D-12-15	17	120S	150E	4300731184	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7-22D-12-15	22	120S	150E	4300731186	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-22-12-15	22	120S	150E	4300731187	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5-22D-12-15	22	120S	150E	4300731188	14794 Federal	GW	P	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR 11-15D-12-15	22	120S	150E	4300731189	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-18D-12-15	18	120S	150E	4300731192	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-18-12-15	18	120S	150E	4300731193	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-27D-12-15	27	120S	150E	4300731194	15569 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 12-27D-12-15	27	120S	150E	4300731195	15568 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 10-27-12-15	27	120S	150E	4300731196	15570 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-20D-12-15	20	120S	150E	4300731197	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7-20-12-15	20	120S	150E	4300731198	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1-20-12-15	20	120S	150E	4300731206	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 2-36-12-15	36	120S	150E	4300731226	15719 State	GW	P	
PRICKLY PEAR U ST 4-36-12-15	36	120S	150E	4300731227	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4-27D-12-15	22	120S	150E	4300731237	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 13-22-12-15	22	120S	150E	4300731238	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-27D-12-15	22	120S	150E	4300731239	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 9-16-12-15	16	120S	150E	4300731240	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-28D-12-15	28	120S	150E	4300731241	16028 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5-27D-12-15	28	120S	150E	4300731242	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1-28-12-15	28	120S	150E	4300731243	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 8-28D-12-15	28	120S	150E	4300731244	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 1-16-12-15	16	120S	150E	4300731245	14794 State	GW	P	PRICKLY PEAR
PPU FED 11-18D-12-15	18	120S	150E	4300731257	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 11-20D-12-15	20	120S	150E	4300731258	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4-25D-12-15	25	120S	150E	4300731259	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 12-25D-12-15	25	120S	150E	4300731260	16068 Federal	GW	P	PRICKLY PEAR
PPU FED 15-6D-13-17	06	130S	170E	4300731261	16103 Federal	GW	P	PETERS POINT
PP UF 3-36-12-16	36	120S	160E	4300731271	2470 Federal	GW	P	PETERS POINT
PP UF 6-36-12-16	36	120S	160E	4300731272	2470 Federal	GW	P	PETERS POINT
PPU FED 6-35D-12-16	35	120S	160E	4300731275	2470 Federal	GW	P	PETERS POINT
PPU FED 14-26D-12-16	26	120S	160E	4300731277	2470 Federal	GW	P	PETERS POINT
PPU FED 8-34-12-16	34	120S	160E	4300731279	2470 Federal	GW	P	PETERS POINT
PP ST 8-2D-13-16 (DEEP)	02	130S	160E	4300731280	16069 State	GW	P	
PPU FED 6-34D-12-16	34	120S	160E	4300731281	2470 Federal	GW	P	PETERS POINT
PPU FED 14-26D-12-15	35	120S	150E	4300731282	16224 Federal	GW	P	PRICKLY PEAR
PPU FED 2-35-12-15	35	120S	150E	4300731283	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 10-26D-12-15	35	120S	150E	4300731284	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 9-17-12-15	17	120S	150E	4300731287	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 1-17D-12-15	17	120S	150E	4300731288	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 7-17D-12-15	17	120S	150E	4300731289	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 7-1D-13-16 ULTRA DEEP	06	130S	170E	4300731293	14692 Federal	GW	P	PETERS POINT
PPU FED 1-18D-12-15	18	120S	150E	4300731294	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 7-18D-12-15	18	120S	150E	4300731295	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 5-17D-12-15	18	120S	150E	4300731296	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 10-17D-12-15	17	120S	150E	4300731307	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 8-17D-12-15	17	120S	150E	4300731308	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 12-17D-12-15	17	120S	150E	4300731309	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 13-17D-12-15	17	120S	150E	4300731310	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 14-17D-12-15	17	120S	150E	4300731311	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16-18D-12-15	17	120S	150E	4300731312	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 8-18D-12-15	18	120S	150E	4300731313	14794 Federal	GW	P	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PPU FED 3-18D-12-15	18	120S	150E	4300731314	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4-18-12-15	18	120S	150E	4300731315	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 5-18D-12-15	18	120S	150E	4300731316	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 6-18D-12-15	18	120S	150E	4300731317	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16-27-12-16	27	120S	160E	4300731318	2470 Federal	GW	P	PETERS POINT
PPU FED 10-27D-12-16	27	120S	160E	4300731319	2470 Federal	GW	P	PETERS POINT
PPU FED 2-34D-12-16	34	120S	160E	4300731320	2470 Federal	GW	P	PETERS POINT
PPU FED 16-17D-12-15	17	120S	150E	4300731321	14794 Federal	GW	P	PRICKLY PEAR
PPU ST 15-16D-12-15	16	120S	150E	4300731322	14794 State	GW	P	PRICKLY PEAR
PPU ST 16-16D-12-15	16	120S	150E	4300731323	14794 State	GW	P	PRICKLY PEAR
PPU ST 14-16D-12-15	16	120S	150E	4300731324	14794 State	GW	P	PRICKLY PEAR
PPU FED 2-7D-13-17 DEEP	06	130S	170E	4300731326	14692 Federal	GW	P	PETERS POINT
PPU FED 3-21D-12-15	21	120S	150E	4300731328	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4-21D-12-15	21	120S	150E	4300731329	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 2-35D-12-16	35	120S	160E	4300731345	2470 Federal	GW	P	PETERS POINT
PPU FED 7-35D-12-16	35	120S	160E	4300731346	2470 Federal	GW	P	PETERS POINT
PPU FED 4-35D-12-16	35	120S	160E	4300731347	2470 Federal	GW	P	PETERS POINT
PPU FED 7-36D-12-16	36	120S	160E	4300731348	2470 Federal	GW	P	PETERS POINT
PPU FED 11-36D-12-16	36	120S	160E	4300731349	2470 Federal	GW	P	PETERS POINT
PPU FED 15-25D-12-16	36	120S	160E	4300731351	2470 Federal	GW	P	PETERS POINT
PPU FED 13-25D-12-16	36	120S	160E	4300731352	2470 Federal	GW	P	PETERS POINT
PPU FED 4-36D-12-16	36	120S	160E	4300731353	2470 Federal	GW	P	PETERS POINT
PPU FED 13-15D-12-15	22	120S	150E	4300731358	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 14-15D-12-15	22	120S	150E	4300731359	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4-22D-12-15	22	120S	150E	4300731360	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 6-22D-12-15	22	120S	150E	4300731361	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 2-28D-12-15	28	120S	150E	4300731362	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16X-21D-12-15	28	120S	150E	4300731363	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 5A-27D-12-15	28	120S	150E	4300731364	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 1-35D-12-16	35	120S	160E	4300731365	2470 Federal	GW	P	PETERS POINT
PPU FED 1A-28D-12-15	28	120S	150E	4300731368	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 14A-18D-12-15	18	120S	150E	4300731393	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 10-18D-12-15	18	120S	150E	4300731394	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 15A-18D-12-15	18	120S	150E	4300731395	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16A-18D-12-15	18	120S	150E	4300731396	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 12-22D-12-15	22	120S	150E	4300731398	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 11-22D-12-15	22	120S	150E	4300731399	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 14-22D-12-15	22	120S	150E	4300731400	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4A-27D-12-15	22	120S	150E	4300731401	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 13-26D-12-16	26	120S	160E	4300731403	2470 Federal	GW	P	PETERS POINT
PPU FED 15-26D-12-16	26	120S	160E	4300731404	2470 Federal	GW	P	PETERS POINT
PPU FED 3-35D-12-16	26	120S	160E	4300731405	2470 Federal	GW	P	PETERS POINT
PPU FED 10-26D-12-16	26	120S	160E	4300731406	2470 Federal	GW	P	PETERS POINT
PPU FED 11-26D-12-16	26	120S	160E	4300731407	2470 Federal	GW	P	PETERS POINT
PPU FED 12-26D-12-16	26	120S	160E	4300731408	2470 Federal	GW	P	PETERS POINT
PPU FED 11-27D-12-16	27	120S	160E	4300731409	2470 Federal	GW	P	PETERS POINT
PPU FED 15-27D-12-16	27	120S	160E	4300731410	2470 Federal	GW	P	PETERS POINT
PPU FED 9-27D-12-16	27	120S	160E	4300731411	2470 Federal	GW	P	PETERS POINT
PPU FED 11-21D-12-15	21	120S	150E	4300731412	14794 Federal	GW	P	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PPU FED 6-21D-12-15	21	120S	150E	4300731413	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 12-21D-12-15	21	120S	150E	4300731414	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 8-20D-12-15	20	120S	150E	4300731419	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 1A-20D-12-15	20	120S	150E	4300731420	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 2-20D-12-15	20	120S	150E	4300731421	14794 Federal	GW	P	PRICKLY PEAR
PPU ST 7A-16D-12-15	16	120S	150E	4300731422	14794 State	GW	P	PRICKLY PEAR
PPU ST 6-16D-12-15	16	120S	150E	4300731423	14794 State	GW	P	PRICKLY PEAR
PPU ST 10A-16D-12-15	16	120S	150E	4300731424	14794 State	GW	P	PRICKLY PEAR
PPU ST 3-16D-12-15	16	120S	150E	4300731425	14794 State	GW	P	PRICKLY PEAR
PPU FED 1-34D-12-16	34	120S	160E	4300731427	2470 Federal	GW	P	PETERS POINT
PPU FED 7-34D-12-16	34	120S	160E	4300731428	2470 Federal	GW	P	PETERS POINT
PPU FED 5-35D-12-16	34	120S	160E	4300731429	2470 Federal	GW	P	PETERS POINT
PPU FED 5-21D-12-15	21	120S	150E	4300731451	14794 Federal	GW	P	PRICKLY PEAR
PPU ST 8-16D-12-15	16	120S	150E	4300731455	14794 State	GW	P	PRICKLY PEAR
PPU ST 12-16D-12-15	16	120S	150E	4300731456	14794 State	GW	P	PRICKLY PEAR
PPU ST 12A-16D-12-15	16	120S	150E	4300731457	14794 State	GW	P	PRICKLY PEAR
PPU ST 15A-16D-12-15	16	120S	150E	4300731458	14794 State	GW	P	PRICKLY PEAR
PPU ST 10-16D-12-15	16	120S	150E	4300731459	14794 State	GW	P	PRICKLY PEAR
PPU ST 11A-16D-12-15	16	120S	150E	4300731460	14794 State	GW	P	PRICKLY PEAR
PPU ST 13A-16D-12-15	16	120S	150E	4300731461	14794 State	GW	P	PRICKLY PEAR
PPU FED 3-34D-12-16	34	120S	160E	4300731466	2470 Federal	GW	P	PETERS POINT
PPU FED 5-34D-12-16	34	120S	160E	4300731467	2470 Federal	GW	P	PETERS POINT
PPU FED 4-34D-12-16	34	120S	160E	4300731468	2470 Federal	GW	P	PETERS POINT
PPU FED 10-7D-12-15	07	120S	150E	4300731470	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 15-7D-12-15	07	120S	150E	4300731471	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 9-7D-12-15	07	120S	150E	4300731472	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16-7D-12-15	07	120S	150E	4300731473	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 10-35D-12-16	35	120S	160E	4300731474	2470 Federal	GW	P	PETERS POINT
PPU FED 9-35D-12-16	35	120S	160E	4300731476	2470 Federal	GW	P	PETERS POINT
PPU ST 6A-16D-12-15	16	120S	150E	4300731477	14794 State	GW	P	PRICKLY PEAR
PPU ST 4-16D-12-15	16	120S	150E	4300731478	14794 State	GW	P	PRICKLY PEAR
PPU ST 4A-16D-12-15	16	120S	150E	4300731479	14794 State	GW	P	PRICKLY PEAR
PPU ST 5A-16D-12-15	16	120S	150E	4300731480	14794 State	GW	P	PRICKLY PEAR
PPU ST 3A-16D-12-15	16	120S	150E	4300731481	14794 State	GW	P	PRICKLY PEAR
PPU ST 16A-16D-12-15	16	120S	150E	4300731484	14794 State	GW	P	PRICKLY PEAR
PPU ST 9A-16D-12-15	16	120S	150E	4300731485	14794 State	GW	P	PRICKLY PEAR
PPU ST 16B-16D-12-15	16	120S	150E	4300731514	14794 State	GW	P	PRICKLY PEAR
PPU ST 14B-16D-12-15	16	120S	150E	4300731515	14794 State	GW	P	PRICKLY PEAR
PPU ST 13B-16D-12-15	16	120S	150E	4300731516	14794 State	GW	P	PRICKLY PEAR
PETERS POINT U FED 9-26D-12-16	25	120S	160E	4300750021	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 11-25D-12-16	25	120S	160E	4300750022	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 10-31D-12-17	31	120S	170E	4300750023	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 11-31D-12-17	31	120S	170E	4300750024	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13A-31D-12-17	31	120S	170E	4300750025	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13-31D-12-17	31	120S	170E	4300750026	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 14-31D-12-17	31	120S	170E	4300750027	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 14A-31D-12-17	31	120S	170E	4300750028	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-25D-12-16	25	120S	160E	4300750029	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-6D-13-17	31	120S	170E	4300750033	2470 Federal	GW	P	PETERS POINT

UDOGM CHANGE OF OPERATOR WELL LIST

PETERS POINT U FED 10-25D-12-16	25	120S	160E	4300750035	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13-36D-12-16	36	120S	160E	4300750037	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 15-36D-12-16	36	120S	160E	4300750038	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 11-1D-13-16	36	120S	160E	4300750039	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-1D-13-16	36	120S	160E	4300750040	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 9-22D-12-15	22	120S	150E	4300750041	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 10-22D-12-15	22	120S	150E	4300750042	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-22D-12-15	22	120S	150E	4300750043	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2-27D-12-15	22	120S	150E	4300750044	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-15D-12-15	15	120S	150E	4300750045	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-15D-12-15	15	120S	150E	4300750046	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 10-15D-12-15	15	120S	150E	4300750047	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-15D-12-15	15	120S	150E	4300750048	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 11A-15D-12-15	15	120S	150E	4300750049	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1-21D-12-15	21	120S	150E	4300750050	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2-21D-12-15	21	120S	150E	4300750051	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2A-21D-12-15	21	120S	150E	4300750052	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4A-22D-12-15	21	120S	150E	4300750053	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5A-22D-12-15	21	120S	150E	4300750054	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7A-21D-12-15	21	120S	150E	4300750056	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 8-21D-12-15	21	120S	150E	4300750057	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 8A-21D-12-15	21	120S	150E	4300750058	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-8D-12-15	08	120S	150E	4300750059	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-8D-12-15	08	120S	150E	4300750060	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2-17D-12-15	08	120S	150E	4300750061	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1A-17D-12-15	08	120S	150E	4300750062	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 3A-34D-12-16	27	120S	160E	4300750063	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 4A-34D-12-16	27	120S	160E	4300750064	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-27D-12-16	27	120S	160E	4300750065	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13-27D-12-16	27	120S	160E	4300750066	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13A-27D-12-16	27	120S	160E	4300750067	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 14-27D-12-16	27	120S	160E	4300750068	18204 Federal	GW	P	
PETERS POINT U FED 14A-27D-12-16	27	120S	160E	4300750069	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 1-22D-12-15	22	120S	150E	4300750076	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2-22D-12-15	22	120S	150E	4300750077	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 8-22D-12-15	22	120S	150E	4300750078	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-17D-12-15	17	120S	150E	4300750079	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3A-17D-12-15	17	120S	150E	4300750080	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4-17D-12-15	17	120S	150E	4300750081	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4A-17D-12-15	17	120S	150E	4300750082	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5A-17D-12-15	17	120S	150E	4300750083	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 6-17D-12-15	17	120S	150E	4300750084	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 6A-17D-12-15	17	120S	150E	4300750085	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7A-17D-12-15	17	120S	150E	4300750086	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 12A-17D-12-15	17	120S	150E	4300750087	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-12D-12-14	12	120S	140E	4300750088	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 10-12D-12-14	12	120S	140E	4300750089	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-12D-12-14	12	120S	140E	4300750090	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-12D-12-14	12	120S	140E	4300750091	14794 Federal	GW	P	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR U FED 3-20D-12-15	20	120S	150E	4300750098	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3A-20D-12-15	20	120S	150E	4300750099	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4-20D-12-15	20	120S	150E	4300750100	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4A-20D-12-15	20	120S	150E	4300750101	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5-20D-12-15	20	120S	150E	4300750102	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 6-20D-12-15	20	120S	150E	4300750104	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 6A-20D-12-15	20	120S	150E	4300750105	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 11A-20D-12-15	20	120S	150E	4300750106	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 12A-20D-12-15	20	120S	150E	4300750107	14794	Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 5-31D-12-17	36	120S	160E	4300750109	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 6-31D-12-17	36	120S	160E	4300750116	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 9X-36D-12-16	36	120S	160E	4300750117	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 1-36D-12-16	36	120S	160E	4300750118	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 10-6D-13-17	06	130S	170E	4300750119	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 15-31D-12-17	06	130S	170E	4300750123	2470	Federal	GW	P	PETERS POINT
PRICKLY PEAR UF 7A-18D-12-15	17	120S	150E	4300750136	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 8A-18D-12-15	17	120S	150E	4300750137	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 9A-18D-12-15	17	120S	150E	4300750138	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 12-20D-12-15	20	120S	150E	4300750139	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 16A-8D-12-15	08	120S	150E	4300750140	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 15A-8D-12-15	08	120S	150E	4300750141	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 13A-9D-12-15	08	120S	150E	4300750142	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 13-9D-12-15	08	120S	150E	4300750143	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 12-9D-12-15	08	120S	150E	4300750144	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 10-8D-12-15	08	120S	150E	4300750145	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 9-8D-12-15	08	120S	150E	4300750146	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 2A-17D-12-15	08	120S	150E	4300750147	14794	Federal	GW	P	PRICKLY PEAR
PETERS POINT UF 12-5D-13-17	06	130S	170E	4300750151	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 13-5D-13-17	06	130S	170E	4300750152	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 13-30D-12-17	30	120S	170E	4300750153	18347	Federal	GW	P	PETERS POINT
PETERS POINT UF 14-30D-12-17	30	120S	170E	4300750154	18350	Federal	GW	P	PETERS POINT
PETERS POINT UF 12-30D-12-17	30	120S	170E	4300750155	18346	Federal	GW	P	PETERS POINT
PETERS POINT UF 11-30D-12-17	30	120S	170E	4300750156	18348	Federal	GW	P	PETERS POINT
PETERS POINT UF 3-31D-12-17	30	120S	170E	4300750157	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 2-31D-12-17	30	120S	170E	4300750158	18349	Federal	GW	P	PETERS POINT
PETERS POINT UF 16-25D-12-16	30	120S	170E	4300750159	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 9-25D-12-16	30	120S	170E	4300750160	2470	Federal	GW	P	PETERS POINT
PRICKLY PEAR UF 1A-22D-12-15	22	120S	150E	4300750171	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 6A-22D-12-15	22	120S	150E	4300750173	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 7A-22D-12-15	22	120S	150E	4300750174	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 8A-22D-12-15	22	120S	150E	4300750175	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 14B-15D-12-15	22	120S	150E	4300750176	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 9-9D-12-15	09	120S	150E	4300750195	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 16-9D-12-15	09	120S	150E	4300750202	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 8-14D-12-15	14	120S	150E	4300750216	18289	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 15-14D-12-15	14	120S	150E	4300750221	18290	Federal	GW	P	PRICKLY PEAR
PETERS POINT UF 7X-36D-12-16	36	120S	160E	4300750231	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 8-36D-12-16	36	120S	160E	4300750232	2470	Federal	GW	P	PETERS POINT
PETERS POINT ST 6-2D-13-16	02	130S	160E	4300731017	14472	State	D	PA	

UDOGM CHANGE OF OPERATOR WELL LIST

PTS 33-36 STATE	36	110S	140E	4301330486	6190 State	GW	PA	ARGYLE
PRICKLY PEAR U FED 10-4	10	120S	140E	4300730823	14462 Federal	GW	S	
PRICKLY PEAR U FASSELIN 5-19-12-15	19	120S	150E	4300730860	14853 Fee	GW	S	
PRICKLY PEAR U ST 5-16	16	120S	150E	4300730943	14794 State	GW	S	PRICKLY PEAR
PRICKLY PEAR U FED 7-33D-12-15	33	120S	150E	4300730985	14771 Federal	GW	S	
PETERS POINT ST 8-2D-13-16	02	130S	160E	4300731016	14471 State	GW	S	
PPU FED 4-35D-12-15	35	120S	150E	4300731285	16223 Federal	GW	S	PRICKLY PEAR
PPU FED 5-36D-12-16	36	120S	160E	4300731350	2470 Federal	GW	S	PETERS POINT
PRICKLY PEAR U FED 5A-20D-12-15	20	120S	150E	4300750103	14794 Federal	GW	S	PRICKLY PEAR
PRICKLY PEAR U FED 13A-17D-12-15	20	120S	150E	4300750108	14794 Federal	GW	S	PRICKLY PEAR
PRICKLY PEAR UF 2A-22D-12-15	22	120S	150E	4300750172	14794 Federal	GW	S	PRICKLY PEAR
