

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL					1. WELL NAME and NUMBER Peter's Point Unit Federal 12-25D-12-16		
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>					3. FIELD OR WILDCAT UNDESIGNATED		
4. TYPE OF WELL Gas Well Coalbed Methane Well: NO					5. UNIT or COMMUNITIZATION AGREEMENT NAME PETERS POINT		
6. NAME OF OPERATOR BILL BARRETT CORP					7. OPERATOR PHONE 303 312-8164		
8. ADDRESS OF OPERATOR 1099 18th Street Ste 2300, Denver, CO, 80202					9. OPERATOR E-MAIL dspencer@billbarrettcorp.com		
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU0681			11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>		12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>		
13. NAME OF SURFACE OWNER (if box 12 = 'fee')					14. SURFACE OWNER PHONE (if box 12 = 'fee')		
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')					16. SURFACE OWNER E-MAIL (if box 12 = 'fee')		
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>		19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/>		
20. LOCATION OF WELL	FOOTAGES	QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN	
LOCATION AT SURFACE	2414 FSL 1290 FWL	NWSW	25	12.0 S	16.0 E	S	
Top of Uppermost Producing Zone	2202 FSL 1007 FWL	NWSW	25	12.0 S	16.0 E	S	
At Total Depth	1971 FSL 696 FWL	NWSW	25	12.0 S	16.0 E	S	
21. COUNTY CARBON			22. DISTANCE TO NEAREST LEASE LINE (Feet) 667		23. NUMBER OF ACRES IN DRILLING UNIT 40		
			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 1256		26. PROPOSED DEPTH MD: 7400 TVD: 7300		
27. ELEVATION - GROUND LEVEL 6708			28. BOND NUMBER WYB000040		29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE Nine Mile Creek		

ATTACHMENTS

VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES

<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER	<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)	<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER
<input checked="" type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)	<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP

NAME Elaine Winick	TITLE Sr. Permit Analyst	PHONE 303 293-9100
SIGNATURE	DATE 06/30/2010	EMAIL ewinick@billbarrettcorp.com
API NUMBER ASSIGNED 43007500290000	APPROVAL  Permit Manager	

Proposed Hole, Casing, and Cement

String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Cond	26	16	0	40		
Pipe	Grade	Length	Weight			
	Unknown	40	65.0			

Proposed Hole, Casing, and Cement

String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Surf	12.25	9.625	0	1000		
Pipe	Grade	Length	Weight			
	Grade J-55 ST&C	1000	36.0			

Proposed Hole, Casing, and Cement

String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Prod	8.75	4.5	0	7400		
Pipe	Grade	Length	Weight			
	Grade N-80 LT&C	7400	11.6			

DRILLING PROGRAM

BILL BARRETT CORPORATION

Peter's Point Unit Federal 12-25D-12-16

NWSW, 2414' FSL, 1290' FWL, Sec. 25, T12S-R16E (surface hole)

NWSW, 1971' FSL, 696' FWL, Sec. 25, T12S-R16E (bottom hole)

Carbon County, Utah

1 – 2. Estimated Tops of Geological Markers and Formations Expected to Contain Water, Oil and Gas and Other Minerals

<u>Formation</u>	<u>Depth – MD</u>	<u>Depth – TVD</u>
Green River	Surface	Surface
Wasatch	2840'*	2796'*
North Horn	4728'*	4636'*
Dark Canyon	6304'*	6211'*
Price River	6509'*	6416'*
TD	7400'*	7300'*

PROSPECTIVE PAY: *Members of the Mesaverde formation and Wasatch formation (inclusive of the North Horn) are primary objectives for oil/gas. Any shallow water zones encountered will be adequately protected and reported. All potentially productive hydrocarbon zones will be cemented off.

3. BOP and Pressure Containment Data

<u>Depth Intervals</u>	<u>BOP Equipment</u>
0 – 1000'	No pressure control required
1000' – TD	11" 3000# Ram Type BOP 11" 3000# Annular BOP
- Drilling spool to accommodate choke and kill lines;	
- Ancillary equipment and choke manifold rated at 3,000#. All BOP and BOPE tests will be in accordance with the requirements of onshore Order No. 2;	
- The BLM and the State of Utah Division of Oil, Gas and Mining will be notified 24 hours in advance of all BOP pressure tests.	
- BOP hand wheels may be underneath the sub-structure of the rig if the drilling rig used is set up to operate most efficiently in this manner.	

'APIWellNo:43007500290000'

4. Casing Program

Hole Size	Setting Depth		Casing Size	Casing Weight	Casing Grade	Thread	Condition
	From	To					
26"	Surface	40'	16"	65#			
12 1/4"	Surface	1000'	9 5/8"	36#	Jor K 55	ST&C	New
8 3/4" and 7 7/8"	Surface	7400'	5 1/2" 4 1/2"	17.0# 11.6#	I-100 N -80	LT&C LT&C	New New

Note: BBC will use one of the options of production casing size noted above. Casing grade for each option could be I-100, P-110 or I-80. In addition, the 7 7/8" hole size will begin at the point the bit is changed.

5. Cementing Program

16" Conductor Casing	Grout cement
9 5/8" Surface Casing	<p><i>Lead</i> with approximately 170 sx Varicem cement + additives mixed at 12.0 ppg (yield = 2.53 ft³/sx).</p> <p><i>Tail</i> with approximately and 190 sx Halcem cement with additives mixed at 15.8 ppg (yield = 1.16 ft³/sx) circulated to surface with 100% excess.</p>
5 1/2" Production Casing OR 4 1/2" Production Casing	<p><i>Lead</i> with approximately 320 sx (4 1/2" csg) or 260 sx (5 1/2" csg) of Halliburton Light Premium cement with additives mixed at 12.5 ppg (yield = 1.96 ft³/sx).</p> <p><i>Tail</i> with approximately 1200 sx (4 1/2" csg) or 990 sx (5 1/2" csg) of 50/50 Poz cement + additives mixed at 13.4 ppg (yield = 1.45 ft³/sk), circulated to ~800' with 15% excess.</p>

Note: Actual volumes to be calculated from caliper log.

6. Mud Program

Interval	Weight	Viscosity	Fluid Loss (API filtrate)	Remarks
0 - 40'	8.3 - 8.6	27 - 40	--	Native Spud Mud
40' - 1000'	8.3 - 8.6	27 - 40	15 cc or less	Native/Gel/Lime
1000' - TD	8.6 - 9.5	38 - 46	15 cc or less	LSND/DAP

Note: Sufficient mud materials to maintain mud properties, control lost circulation and to contain "kicks" will be available at wellsite. BBC may require minor amounts of diesel to be added to its fluid system in order to reduce tork and drag.

7. Testing, Logging and Core Programs

Cores	None anticipated;
Testing	None anticipated;
Sampling	30' to 50' samples; surface casing to TD. Preserve samples all show intervals;
Surveys	Run every 1000' and on trips, slope only;
Logging	DIL-GR-SP, FDC-CNL-GR-CAL-Pe-Microlog, Sonic-GR, all TD to surface.

8. Anticipated Abnormal Pressures or Temperatures

No abnormal pressures or temperatures or other hazards are anticipated.

Maximum anticipated bottom hole pressure equals approximately 3606 psi* and maximum anticipated surface pressure equals approximately 2000 psi** (bottom hole pressure minus the pressure of a partially evacuated hole calculated at 0.22 psi/foot).

*Max Mud Wt x 0.052 x TD = A (bottom hole pressure)

**Maximum surface pressure = A - (0.22 x TD)

9. Auxiliary Equipment

- a) Upper kelly cock; lower Kelly cock will be installed while drilling
- b) Inside BOP or stab-in valve (available on rig floor)
- c) Safety valve(s) and subs to fit all string connections in use
- d) Mud monitoring will be visually observed

10. Drilling Schedule

Location Construction: August 15, 2010
Spud: August 22, 2010
Duration: 10 days drilling time
30 days completion time

T12S, R16E, S.L.B.&M.

NE Cor. Sec 26
1909 Brass Cap,
2.2' High, Pile of
Stones.

C.C.
1961 Brass Cap,
3.0' High, Pile of
Stones.

17.36'

41.54'

N89°57'32"W - 2653.66' (Meas.)

S89°47'42"W - 2651.85' (Meas.)

S 1/4 Cor.
Sec 24
1909 Brass Cap,
1.4' High.

C.C.
1961 Brass Cap,
1.9' High, Pile of
Stones.

Brass Cap,
1.4' High

Lot 4

Lot 3

Lot 2

Lot 1

DISTANCE TABLE

FROM	TO	BEARING	DISTANCE
#12-250-12-18	#36-2	S05°31'53"W	2986.87'
#12-250-12-18	#8-350-12-16	S05°14'37"W	2989.72'
#12-250-12-18	#16-260-12-18	S04°57'54"W	2892.39'
#12-250-12-18	#14-250-12-18	S04°40'32"W	2895.04'

N00°20'20"W - 2633.66' (Meas. to C.C.)

N00°22'17"W - 2633.25' (Meas.)

1961 Brass Cap,
2.0' High, Pile of
Stones.

1961 Brass Cap,
2.0' High, Pile of
Stones.

25

**PETERS POINT UNIT
FEDERAL #12-25D-12-16**
Elev. Ungraded Ground = 6708'

Bottom Hole

N00°20'25"W - 2637.84' (Meas.)

N00°22'48"W - 2640.51' (Meas.)

1290'

696'

1971'

2414'

S89°56'50"W - 2633.41' (Meas.)

S89°56'11"W - 2633.88' (Meas.)

1961 Brass Cap,
0.3' High, Pile of
Stones.

1961 Brass Cap,
2.0' High, Pile of
Stones.

1961 Brass Cap,
1.0' High, Pile of
Stones.

LEGEND:

- └─┘ = 90° SYMBOL
- = PROPOSED WELL HEAD.
- ▲ = SECTION CORNERS LOCATED.

NAD 83 (TARGET BOTTOM HOLE)	NAD 83 (SURFACE LOCATION)
LATITUDE = 39°44'34.53" (39.742925)	LATITUDE = 39°44'38.91" (39.744142)
LONGITUDE = 110°04'47.01" (110.079725)	LONGITUDE = 110°04'39.44" (110.077822)
NAD 27 (TARGET BOTTOM HOLE)	NAD 27 (SURFACE LOCATION)
LATITUDE = 39°44'34.86" (39.742981)	LATITUDE = 39°44'39.04" (39.744178)
LONGITUDE = 110°04'44.47" (110.078019)	LONGITUDE = 110°04'38.90" (110.076917)
STATE PLANE NAD 27 N: 518586.53 E: 2388548.58	STATE PLANE NAD 27 N: 517049.24 E: 2400132.80

BILL BARRETT CORPORATION


Well location, PETERS POINT UNIT FEDERAL #12-25D-12-16, located as shown in the NW 1/4 SW 1/4 of Section 25, T12S, R16E, S.L.B.&M., Duchesne County, Utah.

BASIS OF ELEVATION

COTTON TRIANGULATION STATION LOCATED IN THE NW 1/4 OF SECTION 31, T12S, R16E, S.L.B.&M. TAKEN FROM THE TWIN HOLLOW QUADRANGLE, UTAH, CARBON COUNTY, 7.5 MINUTE SERIES (TOPOGRAPHICAL MAP) PUBLISHED BY THE UNITED STATES DEPARTMENT OF THE INTERIOR, GEOLOGICAL SURVEY. SAID ELEVATION IS MARKED AS BEING 7386 FEET.

BASIS OF BEARINGS

BASIS OF BEARINGS IS A G.P.S. OBSERVATION.

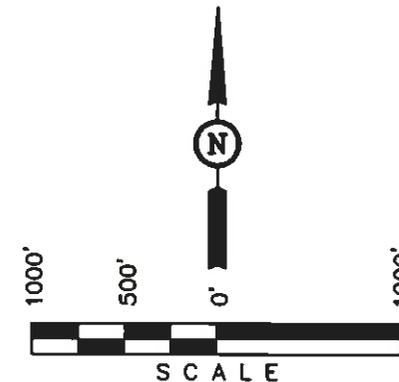


CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAN WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

ROBERT L. KAY
REGISTERED LAND SURVEYOR
REGISTRATION NO. 161319
STATE OF UTAH

UNTAH ENGINEERING & LAND SURVEYING
85 SOUTH 200 EAST - VERNAL, UTAH 84078
(435) 789-1017

SCALE 1" = 1000'	DATE SURVEYED: 02-01-10	DATE DRAWN: 02-25-10
PARTY D.R. T.A. C.C.	REFERENCES G.L.O. PLAT	
WEATHER COLD	FILE BILL BARRETT CORPORATION	

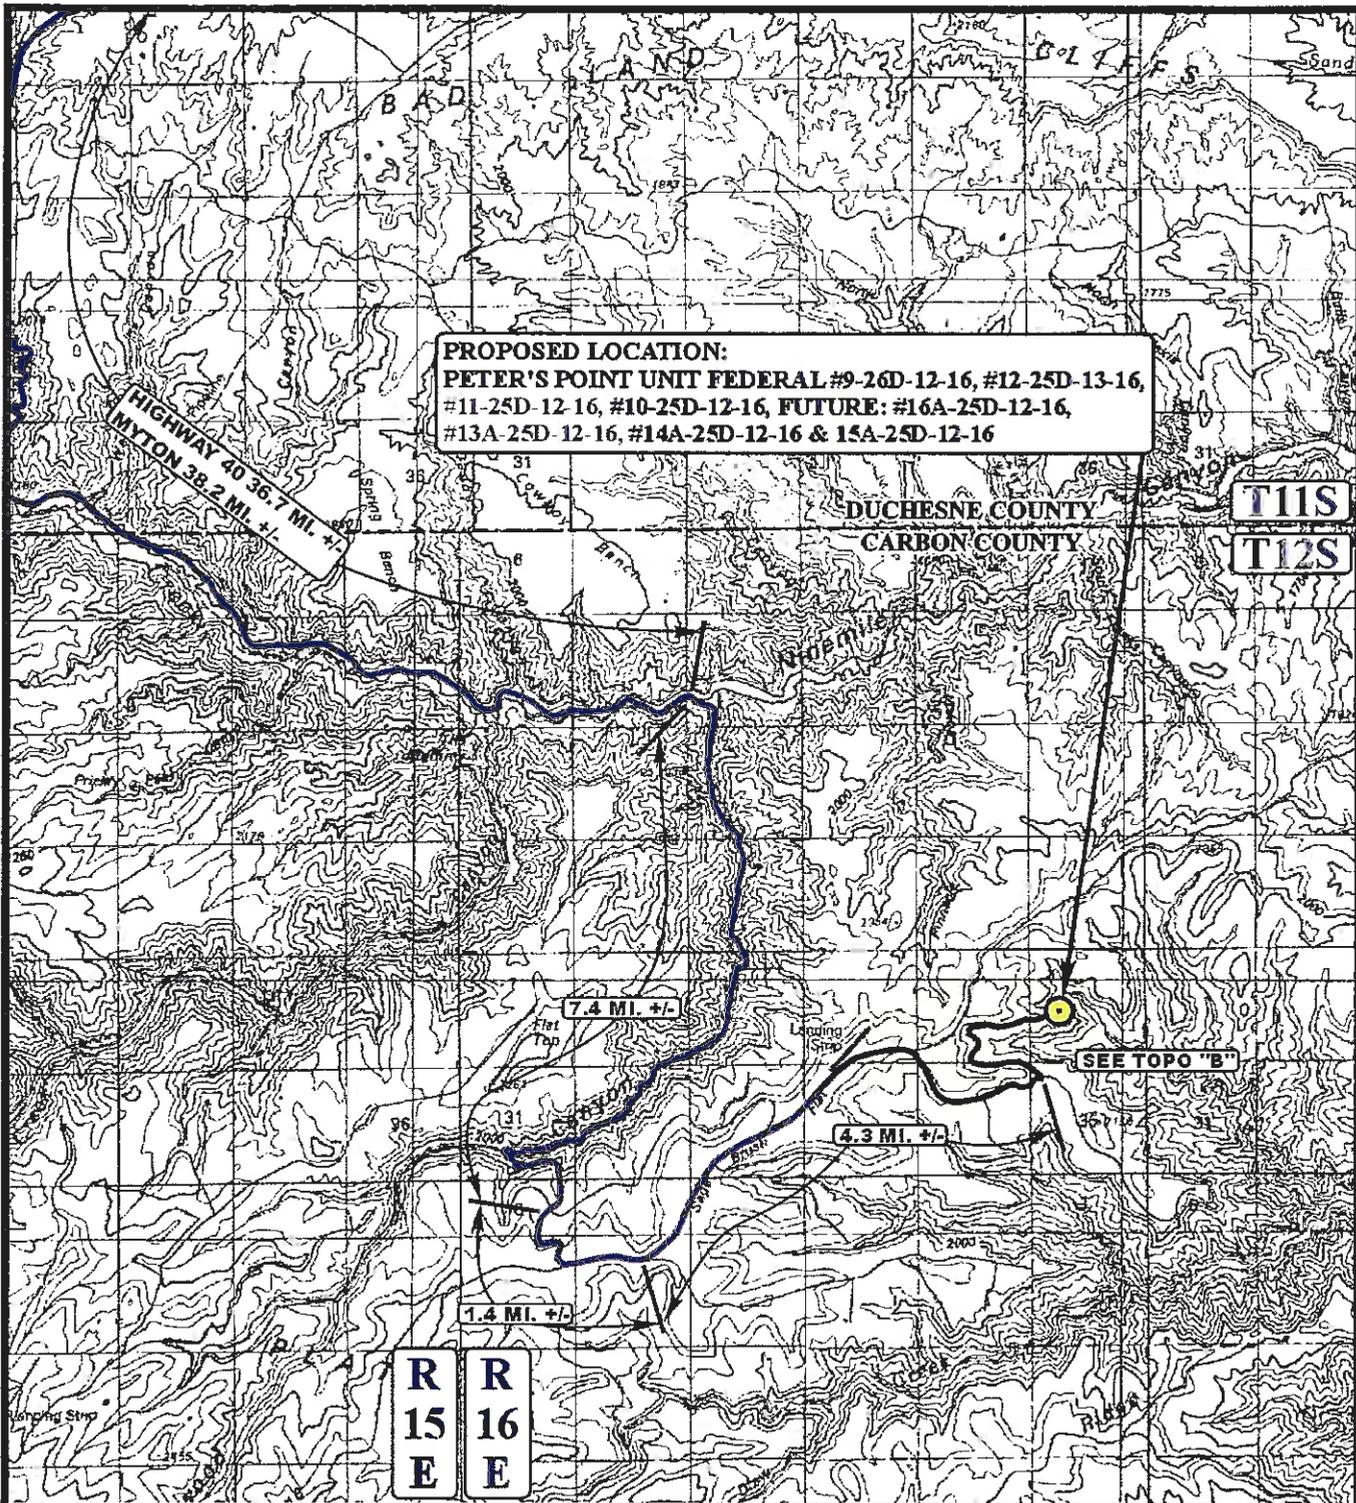

PROPOSED LOCATION:
PETER'S POINT UNIT FEDERAL #9-26D-12-16, #12-25D-13-16,
#11-25D-12-16, #10-25D-12-16, FUTURE: #16A-25D-12-16,
#13A-25D-12-16, #14A-25D-12-16 & #15A-25D-12-16

DUCHESE COUNTY
 CARBON COUNTY

T11S
 T12S

R
15
E

R
16
E

LEGEND:

PROPOSED LOCATION

BILL BARRETT CORPORATION

PETER'S POINT UNIT FEDERAL #9-26D-12-16,
 #12-25D-13-16, #11-25D-12-16, #10-25D-12-16,
 FUTURE: #16A-25D-12-16, #13A-25D-12-16, #14A-25D-12-16
 & #15A-25D-12-16
 SECTION 25, T12S, R16E, S.L.B.&M. SW 1/4

U&L S
 Uintah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 (435) 789-1017 * FAX (435) 789-1813



TOPOGRAPHIC MAP 02 24 10
 MONTH DAY YEAR
 SCALE: 1:100,000 DRAWN BY: J.H. REVISED: 05-06-10



'APIWellNo:43007500290000'




Project: CARBON COUNTY, UT (NAD 27)
 Site: PETERS POINT UF 9-26D
 Well: PETERS POINT UF 12-25D-12-16
 Wellbore: PETERS POINT UF 12-25D-12-16
 Design: Design #1
 Lat: 39° 44' 39.040 N
 Long: 110° 4' 38.900 W
 KB: WELL @ 6721.50ft (Original Well Elev)
 GR: 6705.50



WELLBORE TARGET DETAILS (MAP CO-ORDINATES AND LAT/LONG)

Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude	Shape
PBHL PETERS POINT UF 12-25D-12-16	7221.00	-443.17	-591.34	516596.55	2399548.58	39° 44' 34.680 N	110° 4' 44.470 W	Circle (Radius: 100.00)





SECTION DETAILS

MD	Inc	Azi	TVD	+N/-S	+E/-W	DLeg	TFace	VSec	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
1060.00	0.00	0.00	1060.00	0.00	0.00	0.00	0.00	0.00	Start Build 1.50
2179.76	18.80	233.15	2163.79	-97.73	-130.40	1.50	233.15	162.96	Start 1429.39 hold at 2179.76 MD
3609.16	18.80	233.15	3532.21	-345.44	-480.94	0.00	0.00	578.01	Start Drop -1.50
4728.92	0.00	0.00	4636.00	-443.17	-591.34	1.50	180.00	736.97	Start 2565.00 hold at 4728.92 MD
7313.92	0.00	0.00	7221.00	-443.17	-591.34	0.00	0.00	736.97	TD at 7313.92

WELL DETAILS: PETERS POINT UF 12-25D-12-16

+N/-S	+E/-W	Northing	Easting	Ground Level:	6705.50	Latitude	Longitude	Slot
0.00	0.00	517049.03	2400132.73			39° 44' 39.040 N	110° 4' 38.900 W	

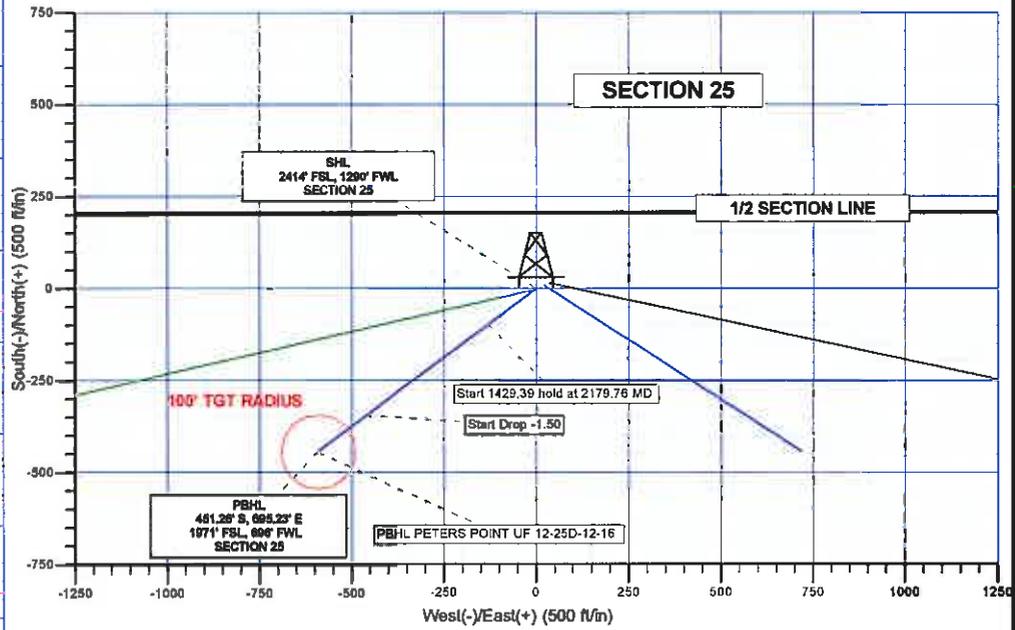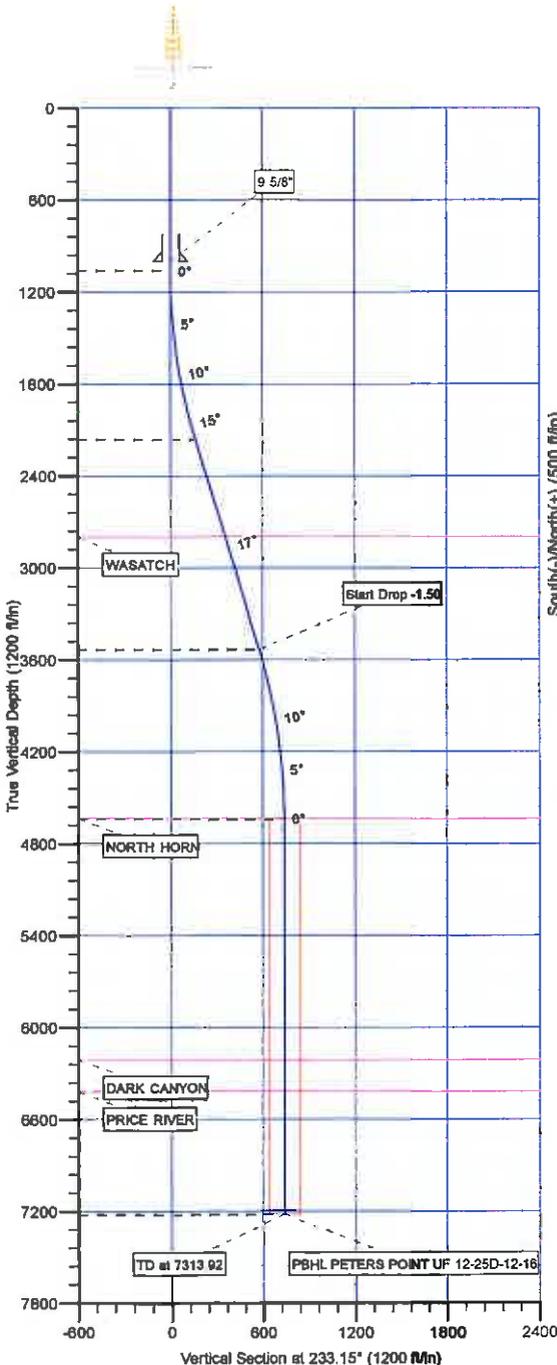

CASING DETAILS

TVD	MD	Name	Size
1000.00	1000.00	9 5/8"	9-5/8"

FORMATION TOP DETAILS

TVDPath	MDPath	Formation
2796.00	2840.14	WASATCH
4636.00	4728.92	NORTH HORN
6211.00	6303.92	DARK CANYON
6416.00	6506.92	PRICE RIVER

LEGEND

- ⊕ PETERS POINT UF 11-25D-12-16, PETERS POINT UF 11-25D-12-16, Design #1 V0
- △ PETERS POINT UF 10-25D-12-16, PETERS POINT UF 10-25D-12-16, Design #1 V0
- PETERS POINT UF 9-26D-12-16, PETERS POINT UF 9-26D-12-16, Design #1 V0
- ⊞ Design #1

Plan: Design #1 (PETERS POINT UF 12-25D-12-16/PETERS POINT UF 12-25D-12-16)

Created By: TRACY WILLIAMS Date: 13:34, June 03 2010

A PLW井No:43007500290000

Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well PETERS POINT UF 12-25D-12-16
Company:	BILL BARRETT CORP	TVD Reference:	WELL @ 6721.50ft (Original Well Elev)
Project:	CARBON COUNTY, UT (NAD 27)	MD Reference:	WELL @ 6721.50ft (Original Well Elev)
Site:	PETERS POINT UF 9-26D	North Reference:	True
Well:	PETERS POINT UF 12-25D-12-16	Survey Calculation Method:	Minimum Curvature
Wellbore:	PETERS POINT UF 12-25D-12-16		
Design:	Design #1		

Project	CARBON COUNTY, UT (NAD 27)		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	Utah Central 4302		Using geodetic scale factor

Site	PETERS POINT UF 9-26D				
Site Position:		Northing:	517,063.80 ft	Latitude:	39° 44' 39.180 N
From:	Lat/Long	Easting:	2,400,169.99 ft	Longitude:	110° 4' 36.420 W
Position Uncertainty:	0.00 ft	Slot Radius:	"	Grid Convergence:	0.91 °

Well	PETERS POINT UF 12-25D-12-16					
Well Position	+N/-S	-14.18 ft	Northing:	517,049.03 ft	Latitude:	39° 44' 39.040 N
	+E/-W	-37.50 ft	Easting:	2,400,132.73 ft	Longitude:	110° 4' 36.900 W
Position Uncertainty		0.00 ft	Wellhead Elevation:	ft	Ground Level:	6,705.50 ft

Wellbore	PETERS POINT UF 12-25D-12-16				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	BGGM2010	6/3/2010	11.44	65.59	52,178

Design	Design #1			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)
	0.00	0.00	0.00	233.15

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
1,060.00	0.00	0.00	1,060.00	0.00	0.00	0.00	0.00	0.00	0.00	
2,179.76	16.80	233.15	2,163.79	-97.73	-130.40	1.50	1.50	0.00	233.15	
3,609.16	16.80	233.15	3,532.21	-345.44	-460.94	0.00	0.00	0.00	0.00	
4,728.92	0.00	0.00	4,636.00	-443.17	-591.34	1.50	-1.50	0.00	180.00	
7,313.92	0.00	0.00	7,221.00	-443.17	-591.34	0.00	0.00	0.00	0.00	PBHL PETERS PO

Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well PETERS POINT UF 12-25D-12-16
Company:	BILL BARRETT CORP	TVD Reference:	WELL @ 6721.50ft (Original Well Elev)
Project:	CARBON COUNTY, UT (NAD 27)	MD Reference:	WELL @ 6721.50ft (Original Well Elev)
Site:	PETERS POINT UF 9-26D	North Reference:	True
Well:	PETERS POINT UF 12-25D-12-16	Survey Calculation Method:	Minimum Curvature
Wellbore:	PETERS POINT UF 12-25D-12-16		
Design:	Design #1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00	0.00	0.00
200.00	0.00	0.00	200.00	0.00	0.00	0.00	0.00	0.00	0.00
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	0.00	0.00	400.00	0.00	0.00	0.00	0.00	0.00	0.00
500.00	0.00	0.00	500.00	0.00	0.00	0.00	0.00	0.00	0.00
600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00	0.00	0.00
700.00	0.00	0.00	700.00	0.00	0.00	0.00	0.00	0.00	0.00
800.00	0.00	0.00	800.00	0.00	0.00	0.00	0.00	0.00	0.00
900.00	0.00	0.00	900.00	0.00	0.00	0.00	0.00	0.00	0.00
9 5/8"									
1,000.00	0.00	0.00	1,000.00	0.00	0.00	0.00	0.00	0.00	0.00
Start Build 1.50									
1,060.00	0.00	0.00	1,060.00	0.00	0.00	0.00	0.00	0.00	0.00
1,100.00	0.60	233.15	1,100.00	-0.13	-0.17	0.21	1.50	1.50	0.00
1,200.00	2.10	233.15	1,199.97	-1.54	-2.05	2.57	1.50	1.50	0.00
1,300.00	3.60	233.15	1,299.84	-4.52	-6.03	7.54	1.50	1.50	0.00
1,400.00	5.10	233.15	1,399.55	-9.07	-12.10	15.12	1.50	1.50	0.00
1,500.00	6.60	233.15	1,499.03	-15.18	-20.26	25.31	1.50	1.50	0.00
1,600.00	8.10	233.15	1,598.20	-22.85	-30.49	38.11	1.50	1.50	0.00
1,700.00	9.60	233.15	1,697.01	-32.08	-42.80	53.49	1.50	1.50	0.00
1,800.00	11.10	233.15	1,795.38	-42.85	-57.18	71.46	1.50	1.50	0.00
1,900.00	12.60	233.15	1,893.25	-55.17	-73.61	91.99	1.50	1.50	0.00
2,000.00	14.10	233.15	1,990.54	-69.01	-92.09	115.08	1.50	1.50	0.00
2,100.00	15.60	233.15	2,087.20	-84.38	-112.60	140.71	1.50	1.50	0.00
Start 1429.39 hold at 2179.76 MD									
2,179.76	16.80	233.15	2,163.79	-97.73	-130.40	162.96	1.50	1.50	0.00
2,200.00	16.80	233.15	2,183.17	-101.23	-135.08	168.81	0.00	0.00	0.00
2,300.00	16.80	233.15	2,278.90	-118.56	-158.21	197.70	0.00	0.00	0.00
2,400.00	16.80	233.15	2,374.63	-135.89	-181.33	226.60	0.00	0.00	0.00
2,500.00	16.80	233.15	2,470.37	-153.22	-204.45	255.50	0.00	0.00	0.00
2,600.00	16.80	233.15	2,566.10	-170.55	-227.58	284.40	0.00	0.00	0.00
2,700.00	16.80	233.15	2,661.84	-187.88	-250.70	313.29	0.00	0.00	0.00
2,800.00	16.80	233.15	2,757.57	-205.21	-273.83	342.19	0.00	0.00	0.00
WASATCH									
2,840.14	16.80	233.15	2,796.00	-212.17	-283.11	353.79	0.00	0.00	0.00
2,900.00	16.80	233.15	2,853.30	-222.54	-296.95	371.09	0.00	0.00	0.00
3,000.00	16.80	233.15	2,949.04	-239.87	-320.08	399.98	0.00	0.00	0.00
3,100.00	16.80	233.15	3,044.77	-257.20	-343.20	428.88	0.00	0.00	0.00
3,200.00	16.80	233.15	3,140.50	-274.53	-366.32	457.78	0.00	0.00	0.00
3,300.00	16.80	233.15	3,236.24	-291.86	-389.45	486.68	0.00	0.00	0.00
3,400.00	16.80	233.15	3,331.97	-309.19	-412.57	515.57	0.00	0.00	0.00
3,500.00	16.80	233.15	3,427.71	-326.52	-435.70	544.47	0.00	0.00	0.00
Start Drop -1.50									
3,609.16	16.80	233.15	3,532.21	-345.44	-460.94	576.01	0.00	0.00	0.00
3,700.00	15.43	233.15	3,619.48	-360.56	-481.11	601.23	1.50	-1.50	0.00
3,800.00	13.93	233.15	3,716.21	-375.76	-501.40	626.58	1.50	-1.50	0.00
3,900.00	12.43	233.15	3,813.57	-389.44	-519.65	649.38	1.50	-1.50	0.00
4,000.00	10.93	233.15	3,911.50	-401.58	-535.85	669.63	1.50	-1.50	0.00
4,100.00	9.43	233.15	4,009.92	-412.19	-550.00	687.31	1.50	-1.50	0.00
4,200.00	7.93	233.15	4,108.77	-421.24	-562.08	702.41	1.50	-1.50	0.00
4,300.00	6.43	233.15	4,207.98	-428.74	-572.09	714.92	1.50	-1.50	0.00
4,400.00	4.93	233.15	4,307.49	-434.68	-580.01	724.82	1.50	-1.50	0.00
4,500.00	3.43	233.15	4,407.22	-439.05	-585.85	732.11	1.50	-1.50	0.00

'APIWellNo:43007500290000'

Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well PETERS POINT UF 12-25D-12-16
Company:	BILL BARRETT CORP	TVD Reference:	WELL @ 6721.50ft (Original Well Elev)
Project:	CARBON COUNTY, UT (NAD 27)	MD Reference:	WELL @ 6721.50ft (Original Well Elev)
Site:	PETERS POINT UF 9-26D	North Reference:	True
Well:	PETERS POINT UF 12-25D-12-16	Survey Calculation Method:	Minimum Curvature
Wellbore:	PETERS POINT UF 12-25D-12-16		
Design:	Design #1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
4,600.00	1.93	233.15	4,507.10	-441.86	-589.60	736.80	1.50	-1.50	0.00
4,700.00	0.43	233.15	4,607.08	-443.10	-591.25	738.86	1.50	-1.50	0.00
Start 2585.00 hold at 4728.92 MD - NORTH HORN									
4,728.92	0.00	0.00	4,636.00	-443.17	-591.34	738.97	1.50	-1.50	0.00
4,800.00	0.00	0.00	4,707.08	-443.17	-591.34	738.97	0.00	0.00	0.00
4,900.00	0.00	0.00	4,807.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,000.00	0.00	0.00	4,907.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,100.00	0.00	0.00	5,007.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,200.00	0.00	0.00	5,107.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,300.00	0.00	0.00	5,207.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,400.00	0.00	0.00	5,307.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,500.00	0.00	0.00	5,407.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,600.00	0.00	0.00	5,507.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,700.00	0.00	0.00	5,607.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,800.00	0.00	0.00	5,707.08	-443.17	-591.34	738.97	0.00	0.00	0.00
5,900.00	0.00	0.00	5,807.08	-443.17	-591.34	738.97	0.00	0.00	0.00
6,000.00	0.00	0.00	5,907.08	-443.17	-591.34	738.97	0.00	0.00	0.00
6,100.00	0.00	0.00	6,007.08	-443.17	-591.34	738.97	0.00	0.00	0.00
6,200.00	0.00	0.00	6,107.08	-443.17	-591.34	738.97	0.00	0.00	0.00
6,300.00	0.00	0.00	6,207.08	-443.17	-591.34	738.97	0.00	0.00	0.00
DARK CANYON									
6,303.92	0.00	0.00	6,211.00	-443.17	-591.34	738.97	0.00	0.00	0.00
6,400.00	0.00	0.00	6,307.08	-443.17	-591.34	738.97	0.00	0.00	0.00
6,500.00	0.00	0.00	6,407.08	-443.17	-591.34	738.97	0.00	0.00	0.00
PRICE RIVER									
6,508.92	0.00	0.00	6,416.00	-443.17	-591.34	738.97	0.00	0.00	0.00
6,600.00	0.00	0.00	6,507.08	-443.17	-591.34	738.97	0.00	0.00	0.00
6,700.00	0.00	0.00	6,607.08	-443.17	-591.34	738.97	0.00	0.00	0.00
6,800.00	0.00	0.00	6,707.08	-443.17	-591.34	738.97	0.00	0.00	0.00
6,900.00	0.00	0.00	6,807.08	-443.17	-591.34	738.97	0.00	0.00	0.00
7,000.00	0.00	0.00	6,907.08	-443.17	-591.34	738.97	0.00	0.00	0.00
7,100.00	0.00	0.00	7,007.08	-443.17	-591.34	738.97	0.00	0.00	0.00
7,200.00	0.00	0.00	7,107.08	-443.17	-591.34	738.97	0.00	0.00	0.00
7,300.00	0.00	0.00	7,207.08	-443.17	-591.34	738.97	0.00	0.00	0.00
PBHL PETERS POINT UF 12-25D-12-16									
7,313.92	0.00	0.00	7,221.00	-443.17	-591.34	738.97	0.00	0.00	0.00

Design Targets									
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (ft)	Easting (ft)	Latitude	Longitude
PBHL PETERS POIN	0.00	0.00	7,221.00	-443.17	-591.34	516,596.55	2,399,548.58	39° 44' 34.660 N	110° 4' 44.470 W
- hit/miss target									
- Shape									
- plan hits target center									
- Circle (radius 100.00)									

'APIWellNo:43007500290000'

Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well PETERS POINT UF 12-25D-12-16
Company:	BILL BARRETT CORP	TVD Reference:	WELL @ 6721.50ft (Original Well Elev)
Project:	CARBON COUNTY, UT (NAD 27)	MD Reference:	WELL @ 6721.50ft (Original Well Elev)
Site:	PETERS POINT UF 9-26D	North Reference:	True
Well:	PETERS POINT UF 12-25D-12-16	Survey Calculation Method:	Minimum Curvature
Wellbore:	PETERS POINT UF 12-25D-12-16		
Design:	Design #1		

Casing Points				
Measured Depth (ft)	Vertical Depth (ft)	Name	Casing Diameter (")	Hole Diameter (")
1,000.00	1,000.00	9 5/8"	9-5/8	12-1/4

Formations					
Measured Depth (ft)	Vertical Depth (ft)	Name	Lithology	Dip (")	Dip Direction (")
2,840.14	2,796.00	WASATCH		0.00	
4,728.92	4,636.00	NORTH HORN		0.00	
6,303.92	6,211.00	DARK CANYON		0.00	
6,508.92	6,416.00	PRICE RIVER		0.00	

Plan Annotations					
Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates		Comment	
		+N/-S (ft)	+E/-W (ft)		
1,060.00	1,060.00	0.00	0.00	Start Build 1.50	
2,179.76	2,163.79	-97.73	-130.40	Start 1429.39 hold at 2179.76 MD	
3,609.16	3,532.21	-345.44	-460.94	Start Drop -1.50	
4,728.92	4,636.00	-443.17	-591.34	Start 2585.00 hold at 4728.92 MD	
7,313.92	7,221.00	-443.17	-591.34	TD at 7313.92	

SURFACE USE PLAN

**BILL BARRETT CORPORATION
Peter's Point Unit Federal N/2 SW 25 Pad
Carbon County, UT**

<p><u>Peter's Point Unit Federal 10-25D-12-16</u> NESW, 2428' FSL, 1328' FWL, Sec. 25, T12S-R16E (surface hole) NWSE, 1999' FSL, 1950' FEL, Sec. 25, T12S-R16E (bottom hole)</p>	<p><u>Peter's Point Unit Federal 11-25D-12-16</u> NWSW, 2423' FSL, 1313' FWL, Sec. 25, T12S-R16E (surface hole) NESW, 1971' FSL, 2006' FWL, Sec. 25, T12S-R16E (bottom hole)</p>
<p><u>Peter's Point Unit Federal 12-25D-12-16</u> NWSW, 2414' FSL, 1290' FWL, Sec. 25, T12S-R16E (surface hole) NWSW, 1971' FSL, 696' FWL, Sec. 25, T12S-R16E (bottom hole)</p>	<p><u>Peter's Point Unit Federal 9-26D-12-16</u> NWSW, 2409' FSL, 1275' FWL, Sec. 25, T12S-R16E (surface hole) NESE, 1970' FSL, 627' FEL, Sec. 26, T12S-R16E (bottom hole)</p>

The onsite for this pad occurred June 29, 2010. This is a new pad with a total of eight directional wells (four to be drilled in Phase 1, four future wells to be drilled in Phase 2 if down spacing proves to be viable).

The excavation contractor would be provided with an approved copy of the surface use plan of operations before initiating construction.

1. **Existing Roads:**

- a. The proposed pad is located approximately 53 miles from Myton, Utah. Maps reflecting directions to the proposed pad are included (see Topographic maps A and B).
- b. The use of roads under State and County Road Department maintenance is necessary to access the Peter's Point Unit. However, an encroachment permit is not anticipated as there are no upgrades to the State or County road systems proposed at this time.
- c. No topsoil stripping would occur as there are no improvements proposed to existing State, County or main BLM access roads.
- d. Project roads would require routine year-round maintenance to provide year-round access. Maintenance would include inspections, reduction of ruts and holes, maintenance to keep water off the road, replacement of surfacing materials, and clearing of sediment blocking ditches and culverts. Should snow removal become necessary, roads would be cleared with a scraper and snow would be stored along the down gradient side to prohibit runoff onto the road. Aggregate would be used as necessary to maintain a solid running surface and minimize dust generation.
- e. Vehicle operators would obey posted speed restrictions and observe safe speeds commensurate with road and weather conditions. Travel would be limited to the existing access roads and proposed access road.
- f. To address safety-related traffic concerns, drivers and rig crews would be advised of the hazards to recreational traffic along the existing and proposed access roads, as well as hazards present due to blind corners, cars parked on the road, pedestrian traffic, and mountain bikers. In addition, appropriate signs would be erected to warn non-project personnel about traffic hazards associated with project-related activities and during times of rig moves, when there is heavy equipment, traffic may be controlled on sections of roads. Traffic would be controlled using roadside signs, flagmen, and barricades as appropriate.
- g. Dust suppression and monitoring would be implemented where necessary and as prescribed by the BLM.
- h. An off-lease federal right-of-way for the access road and utility corridor is not anticipated at this time since existing roads are being utilized into the Peter's Point Unit area. All new construction would be within the Unit.

2. Planned Access Road:

- a. From the existing Peter's Point road, approximately 1.8 miles of new access road is proposed (see Topographic Map B) within the Peter's Point Unit. A road design plan is not anticipated at this time.
- b. The new proposed access road would be co-located by pipeline(s) and the requested corridor disturbance would be 100 ft with a short-term corridor disturbance of 80 ft (18.4 acres) reclaimed to a long-term corridor of 30 ft (6.9 acres).
- c. The proposed road would be constructed to facilitate drainage, control erosion and minimize visual impacts by following natural contours where practical. No unnecessary side-casting of material would occur on steep slopes.
- d. Intervisible turnouts would be constructed, where necessary and as topographic conditions allow, to improve traffic safety. A maximum grade of 10 percent would be maintained with minimum cuts and fills, as necessary, to access the well pad.
- e. New road construction and improvements of existing roads would typically require the use of motorgraders, crawler tractors, 10-yard end dump trucks, and water trucks. The standard methodology for building new roads involves the use of a crawler tractor or track hoe to windrow the vegetation to one side of the road corridor, remove topsoil to the opposing side of the corridor, and rough-in the roadway. This is followed by a grader or bulldozer to establish barrow ditches and crown the road surface. Where culverts are required, a track hoe or backhoe would trench the road and install the culverts. Some hand labor would be required when installing and armoring culverts. Road base or gravel in some instances would be necessary and would be hauled in and a grader used to smooth the running surface.
- f. Excess rock from construction of the pad may be used for surfacing of the access road if necessary. Any additional aggregate necessary would be obtained from private, State of Utah, or federal lands in conformance with applicable regulations. Aggregate would be of sufficient size, type, and amount to allow all weather access and alleviate dust.
- g. Where topsoil removal is necessary, it would be windrowed (i.e. stockpiled/accumulated along the edge of the ROW and in a low row/pile parallel with the ROW) and re-spread over the disturbed area after construction and backfilling are completed. Vegetation removed from the disturbed area would also be re-spread to provide protection, nutrient recycling, and a seed source for reclamation.
- h. Adequate drainage structures would be incorporated and culverts, with a minimum diameter of 18 inches, would be installed as necessary. Turnouts would also be incorporated where necessary.
- i. No gates or cattle guards are anticipated at this time.
- j. Surface disturbance and vehicular travel would be limited to the approved location access road. Adequate signs would be posted, as necessary, to warn the public of project related traffic.
- k. All access roads and surface disturbing activities would conform to the appropriate standard, no higher than necessary, to accommodate their intended function adequately as outlined in the Bureau of Land Management and Forest Service publication: Surface Operating Standards for Oil and Gas Exploration and Development, Fourth Edition – Revised 2007. BBC would be responsible for all maintenance of the access road.

3. Location of Existing Wells (see One-Mile Radius Map):

a. Following is a list of wells with surface hole locations within a one-mile radius of the proposed pad:

i. water wells	none
ii. injection wells	none
iii. disposal wells	none
iv. drilling wells	none
v. temp shut-in wells	none
vi. producing wells	twelve
vii. abandoned wells	none

4. Location of Production Facilities:

- a. Each proposed well would have its own meter run and separator. Proposed wellheads and christmas trees would be contained below location grade in pre-cast concrete trenches. All wellheads associated with the drilling operations for this pad would be contained in the same trench measuring approximately 12 ft wide, 10 ft deep, and 64 ft long (# wells x 8 ft + 16 ft for two end pieces). Drawings of below ground cellars can be provided by BBC upon request.
- b. Up to eight tanks (up to 500-bbl in capacity) would be installed for this pad. Tank facilities for this pad would be located at a centralized tank battery facility (CTB) located at the existing Peter's Point 36-2 well pad in the NWNW, Sec. 36, T12S-R16E located within the Peter's Point unit. As all the new proposed wells for this pad and the existing wells on the 36-2 pad are within the Peter's Point unit and within the participating area, tanks would be shared among the wells. Figure 4 and the Site Plan reflect facility plans and are attached.
- c. The CTB would be surrounded by a secondary containment berm of sufficient capacity to contain the 1.1 times the entire capacity of the largest single tank and sufficient freeboard to contain precipitation. All loading lines and valves would be placed inside the berm surrounding the CTB or would utilize catchment basins to contain spills. All liquid hydrocarbon production and measurement shall conform to the provisions of 43 CFR 3162.7-2 and Onshore Oil and Gas Order No. 4 for the measurement of oil. BBC requests permission to install the necessary production/operation facilities with this application.
- d. Most wells would be fitted with plunger lift systems to assist liquid production. However, pump jacks may be used if liquid volumes and/or low formation pressures require it. Plunger lift systems do not require any outside source of energy. The prime mover for pump jacks would be small (50 horsepower or less), natural gas-fired internal combustion engines.
- e. Gas meter run(s) would be constructed and located on lease within 500 feet of the wellheads. Meter runs would be housed and/or fenced. As practicably feasible, meters would be equipped with remote telemetry monitoring systems. All gas production and measurement shall comply with the provisions of 43 CFR 3162.7-3, Onshore Oil and Gas Order No. 5, and American Gas Association (AGA) Report No. 3
- f. A combustor may be installed at this location for control of associated condensate tank emissions. A combustor ranges from 24 inches to 48 inches wide and is approximately 10 ft tall. Combustor placement would be on existing disturbance and would not be closer than 100 ft to any tank or wellhead(s).
- g. A gas gathering pipeline (up to 8 inch diameter) and a liquids line (up to 4 inch diameter), approximately 10,056 feet in length, is associated with this application and is being applied for at this time (see Topographic Map D). Both lines would leave the west end of the pad, traverse west, south and then east where the gas pipeline would tie into the existing 12 inch line and the liquids line would transport the liquids to the Peter's Point 36-2 CTB.

- h. The proposed new gas pipeline would be constructed of steel while the liquids line would be constructed of steel, polyethylene, or fiberglass. The gas pipeline and liquids line would be buried, where soil conditions permit, within the proposed co-located access road and pipeline corridor noted above in Section 2(b) (Planned Access Roads).
 - i. Burial of pipelines would depend upon the site-specific topographic and soil conditions and operational requirements. The determination to bury or surface lay the pipeline would be made by the Authorized Officer at the time of construction.
 - j. BBC intends on stringing the pipeline on the surface, welding many joints into long lengths, dragging the long lengths into position and then completing a final welding pass to join the long lengths together. The welded joints would either remain on the surface or would be placed within the trench, depending on the scenario. BBC intends on connecting the pipeline together utilizing conventional welding technology.
 - k. Pipeline construction methods and practices would be planned and conducted by BBC with the objective of enhancing reclamation and fostering the re-establishment of the native plant community.
 - l. To limit erosion potential, backfill over pipeline trenches would be compacted so as not to extend above the original ground level after the fill has settled. Wheel or other methods of compacting backfill would be utilized as practicably feasible to reduce trench settling and water channeling.
 - m. All **permanent** above-ground structures would be painted a flat, non-reflective Olive Black to match the standard environmental colors. These structures would be painted the designated color at the time of installation or within 6 months of being located on site. Facilities that are required to comply with the Occupational Safety and Health Act (OSHA) may be excluded.
 - n. Site security guidelines identified in 43 CFR 3162.7-5 and Onshore Oil and Gas Order No. 3 would be adhered to.
 - o. The site would require periodic maintenance to ensure that drainages are kept open and free of debris, and that surfaces are properly treated to reduce erosion, fugitive dust, and impacts to adjacent areas.
5. Location and Type of Water Supply:
- a. Bill Barrett Corporation would use water consistent with approvals granted by the Utah State Engineer's Office under:
 - Application Number 90-1863, expires June 6, 2011
 - Application Number 98-860, expires September 30, 2010
 - Application Number 90-4, expires December 31, 2014
 - Application Number 90-1861, expires May 11, 2011
 - b. Water use for this location would most likely be diverted from Nine Mile Creek, the S¼ of Section 8, T12S-R16E or from a water well located in the N¼ of State Section 32-T12S-R16E. For either of these sources, bobtail trucks would haul the water, traveling Cottonwood Canyon dugway to Peter's Point road.
 - c. Water use would vary in accordance with the formations to be drilled but would average approximately 1 acre-foot (7,758 barrels) during drilling operations and 1 acre-foot (7,758 barrels) during completion operations.
6. Source of Construction Material:
- a. The use of materials would conform to 43 CFR 3610.2-3.
 - b. No construction materials would be taken out of the Peter's Point Unit.

- c. If any additional gravel is required, it would be obtained from SITLA materials permits, federal BBC locations within the Peter's Point unit or from private sources.

7. Methods of Handling Waste Disposal:

- a. All wastes associated with this application would be contained and disposed of utilizing approved facilities.

Closed Loop Drilling System

- b. BBC intends to employ a closed loop drilling system in which drilling fluids and cuttings would be thoroughly processed such that the separated cuttings are relatively dry. The cuttings would be stored on location in either secured piles or in a 250 ft x 50 ft cuttings trench (indicated as reserve pit on Figure 1 located outboard of the location along the southeast side of the pad).
- c. The cuttings trench would not be lined. Three sides of the trench would be fenced before drilling starts and the fourth side would be fenced at the time drilling is completed on the last well on the pad and shall remain until cuttings trench has been reclaimed.
- d. Upon completion of drilling, the cuttings would be tested and further processed as necessary to meet standards for burial on site or other BLM approved uses such as a media for road surfacing or growing media for reclamation.

Conventional or Semi-Closed Loop Drilling System

- e. In the event closed loop drilling is not employed, a conventional or semi-closed loop system would be used where a small amount of fluid is retained in the cuttings and the cuttings are placed in the reserve pit. The reserve pit would also store water to make up losses and store any excess drilling fluids. Reserve pits would be constructed with an impermeable liner so as to prevent releases. The pit liner would overlap the pit walls and be anchored with soil and/or rocks to hold it in place. No trash, scrap pipe, etc. that could puncture the liner would be disposed of in the pit and a minimum of 2 ft of freeboard would be maintained in the pit at all times. Reserve pits would be constructed and maintained according to BLM or UDOGM requirements as appropriate.
- f. Three sides of the reserve pit would be fenced before drilling starts and the fourth side would be fenced at the time drilling is completed on the last well on the pad and shall remain until the pit is dry.
- g. Any hydrocarbons floating on the surface of the reserve pit would be removed as soon as possible after drilling and completion operations are finished. In some cases, the reserve pit may be flagged overhead or covered with wire or plastic mesh to protect migrating birds.

Completion Pit

- h. Where closed loop drilling is employed, the cuttings trench disturbed area would typically also be used to store water for completion activities. The completion pit would be constructed with an impermeable liner to prevent releases and would be fenced and constructed and maintained according to BLM or UDOGM requirements.

Other

- i. Produced fluids from the wells other than water would be decanted into steel test tanks until such time as construction of production facilities is completed. Produced water may be used in further drilling and completion activities, evaporated in the pit or would be hauled to a state approved disposal facility.

- j. After initial clean-up and based on volumes, BBC would install a tank (maximum size 400 barrel capacity) to contain produced waste water. After first production, produced wastewater would be confined to tanks within the CTB for a period not to exceed ninety (90) days. Thereafter, produced water would be used in further drilling and completion activities or hauled to a State approved disposal facility.
- k. Any salts and/or chemicals, which are an integral part of the drilling system, would be disposed of in the same manner as the drilling fluid.
- l. Any spills of oil, condensate, produced or frac water, drilling fluids, or other potentially deleterious substances would be recovered and either returned to its origin or disposed of at an approved disposal site, most likely in Duchesne, Utah.
- m. Chemicals on the EPA's Consolidated List of Chemicals subject to reporting under Title III of the Superfund Amendments and Reauthorization Act of 1986 (SARA) may be used or stored in quantities over reportable quantities. In the course of drilling, BBC could potentially store and use diesel fuel, sand (silica), hydrochloric acid, and CO₂ gas, all described as hazardous substances in 40 CFR Part 302, Section 302.4, in quantities exceeding 10,000 pounds. In addition, natural gas condensate and crude oil and methanol may be stored or used in reportable quantities. Small quantities of retail products (paint/spray paints, solvents {e.g., WD-40}, and lubrication oil) containing non-reportable volumes of hazardous substances may be stored and used on site at any time. No extremely hazardous substances, as defined in 40 CFR 355, would be used, produced, stored, transported or disposed of in association with the drilling, testing or completion of the wells.
- n. Portable toilets and trash containers would be located onsite during drilling and completion operations. A commercial supplier would install and maintain portable toilets and equipment and would be responsible for removing sanitary waste. Sanitary waste facilities (i.e. toilet holding tanks) would be regularly pumped and their contents disposed of at approved sewage disposal facilities in Carbon, Duchesne, and/or Uintah Counties, in accordance with applicable rules and regulations regarding sewage treatment and disposal. Accumulated trash and nonflammable waste materials would be hauled to an approved landfill once a week or as often as necessary. All debris and waste materials not contained in the trash containers would be cleaned up, removed from the construction ROW, well pad, or worker housing location, and disposed of at an approved landfill. Trash would be cleaned up everyday.
- o. Sanitary waste equipment and trash bins would be removed from the WTP Project Area upon completion of access road or pipeline construction; following drilling and completion operations at an individual well pad; when worker housing is no longer needed; or as required.
- p. A flare pit may be constructed a minimum of 110' from the wellhead(s) and may be used during completion work. In the event a flare pit proves to be unworkable, a temporary flare stack or open top tank would be installed. BBC would flow back as much fluid and gas as possible into pressurized vessels, separating the fluids from the gas. In some instances, due to the completion fluids utilized within the West Tavaputs Project area, it is not feasible to direct the flow stream from the wellbore through pressurized vessels. In such instances BBC proposes to direct the flow to the open top tanks until flow through the pressurized vessels is possible. At which point the fluid would either be returned to the reserve pit or placed into a tank(s). The gas would be directed to the flare pit, flare stack (each with a constant source of ignition), or may be directed into the sales pipeline.
- q. Flare lines would be directed so as to avoid damage to surrounding vegetation, adjacent rock faces, or other resources, and as required by regulations. Flare lines would be in place on all well locations. In the event it becomes necessary to flare a well, a deflector and/or directional orifice would also be used to safeguard both personnel and adjacent natural rock faces.

8. Ancillary Facilities:

- a. Garbage containers and portable toilets are the only ancillary facilities proposed in this application.
- b. BLM approved and permitted storage yards for tubulars and other equipment and temporary housing areas would be utilized.
- c. On well pads where active drilling and completion is occurring, temporary housing would be provided on location for the well pad supervisor, geologist, tool pusher, and others that are required to be on location at all times. Active drilling locations could include up to five single wide mobile homes or fifth wheel campers/trailers.

9. Well Site Layout:

- a. Each well would be properly identified in accordance with 43 CFR 3162.6
- b. The pad has been staked at its maximum size of 436 ft x 255 ft with a 250 ft x 50 ft (5.0 acres) cuttings trench/reserve pit/completion pit outboard of the pad. The location layout and cross section diagrams are enclosed.
- c. Within the approved well pad location, a crawler tractor would strip whatever topsoil is present and stockpile it along the edge of the well pad for use during reclamation. Vegetation would be distributed along the sides of the well pad.
- d. Proposed wellheads and christmas trees would be contained below location grade in pre-cast concrete trenches.
- e. The cuttings trench or reserve pit would be fenced on three sides during drilling and on the fourth side immediately after the removal of the drilling rig. In the event closed loop drilling is employed, the cuttings trench would be removed or stockpiled on one edge of the trench and the area would be used for a completion pit during completion operations.
- f. Fill from pit excavation would be stockpiled along the edge of the pit and the adjacent edge of the well pad.
- g. Use of erosion control measures, including proper grading to minimize slopes, diversion terraces and ditches, mulching, terracing, riprap, fiber matting, temporary sediment traps, and broad-based drainage dips or low water crossings would be employed by BBC as necessary and appropriate to minimize erosion and surface runoff during well pad construction and operation. Cut and fill slopes would be constructed such that stability would be maintained for the life of the activity.
- h. Construction of the well pad would take from 1 to 3 weeks depending on the features at the particular site.
- i. Dust suppression may be implemented if necessary to minimize the amount of fugitive dust.

10. Plan for Restoration of the Surface:

Interim Reclamation (see Figure 4)

- a. Portions of the disturbed area within a construction ROW or portions of well pads not needed for production would be reclaimed according to specifications of the BLM as appropriate.
- b. Prior to interim reclamation activities, all solid wastes and refuse would be removed and placed at approved landfills. The portions of the well pad or access and pipeline corridor not needed for production would be re-contoured to promote proper drainage, salvaged topsoil would be replaced, and side slopes would be ripped and disked on the contour. Following site preparation, reseeding

would be completed during either the spring or fall planting season, when weather conditions are most favorable. Seed mixtures for reclaimed areas would be site-specific and would require approval by the BLM. BBC would apply and meet BLM's Green River District Reclamation Standards.

- c. The operator would control noxious weeds along access road use authorizations, pipeline route authorizations, well sites or other applicable facilities by spraying or mechanical removal. A list of noxious weeds may be obtained from the BLM or the appropriate county extension office. On BLM administered land it is required that a Pesticide Use Proposal be submitted and approved prior to the application of herbicides, pesticides or possibly hazardous chemicals.
- d. Following interim reclamation, access roads (including roads co-located with pipeline) would be reduced to approximately 30 feet of disturbance. Roads leading to well sites that would not have surface production equipment would be designed and reclaimed in a way that minimizes impacts to the visual character of the host lands.
- e. Weather permitting, earthwork for interim reclamation would be completed within 6 months of completion of the final well on the pad or plugging and would continue until satisfactory revegetation cover is established. Inter-seeding (i.e. seeding into existing vegetation), secondary seeding, or staggered seeding may be used to accomplish revegetation objectives. During rehabilitation of areas in important wildlife habitat, provisions would be made for the establishment of native browse and forb species. Follow-up seeding or corrective erosion control measures would occur on areas where initial reclamation efforts are unsuccessful, as determined by the BLM or the appropriate surface management agency.

Dry Hole/Final Reclamation

- f. All disturbed lands associated with this project, including the pipelines, access roads, water management facilities, etc. would be expediently reclaimed and reseeded in accordance with the reclamation plan and any pertinent site-specific COAs.
- g. When a well is to be plugged and abandoned, BBC would submit a Notice of Intent to Abandon (NOA) to the BLM or UDOGM as appropriate. The BLM or UDOGM would then attach the appropriate surface rehabilitation COAs for the well pad, and as appropriate, for the associated access road, pipeline, and ancillary facilities. During plugging and abandonment, all structures and equipment would be removed from the well pad. Backfilling, leveling, and re-contouring would then be performed according to the BLM or UDOGM order.
- h. Any mulch used by BBC would be weed-free and free from mold, fungi, or noxious weeds. Mulch may include native hay, small grain straw, wood fiber, live mulch, cotton, jute, synthetic netting or rock.
- i. BBC would reshape disturbed channel beds to their approximate original configuration.
- j. Reclamation of abandoned roads may include re-shaping, re-contouring, re-surfacing with topsoil, installation of water bars, and seeding on the contours. Road beds, well pads, and other compacted areas would be ripped to a depth of approximately 1 foot on 1.5 foot centers to reduce compaction prior to spreading the topsoil across the disturbed area. Stripped vegetation would be spread over the disturbance area for nutrient recycling, where practical. Additional erosion control measures (e.g. fiber matting) and road barriers to discourage travel may be constructed if appropriate. Graveled roads, well pads, and other sites would be stripped of usable gravel prior to ripping as deemed necessary. Culverts, cattleguards, and signs would be removed as roads are abandoned.

11. Surface and Mineral Ownership:
 - a. Surface ownership – Federal under the management of the Bureau of Land Management – Price Field Office, 125 South 600 West, Price Utah 84078; (435) 636-3600.
 - b. Mineral ownership – Federal under the management of the Bureau of Land Management – Price Field Office, 125 South 600 West, Price Utah 84078; (435) 636-3600.

12. Other Information:
 - a. Montgomery Archaeological Consultants conducted cultural resource inventories under MOAC 09-053, dated July 9, 2009 and MOAC 10-049, dated May 11, 2010.
 - b. BBC would require that their personnel, contractors, and subcontractors to comply with Federal regulations intended to protect archeological and cultural resources.
 - c. Project personnel and contractors would be educated on and subject to the following requirements:
 - No dogs within the WTP Project Area;
 - No firearms within the WTP Project Area;
 - No littering within the WTP Project Area;
 - Smoking within the WTP Project Area would only be allowed in off-operator active locations or in specifically designated smoking areas. All cigarette butts would be placed in appropriate containers and not thrown on the ground or out windows of vehicles; personnel and contractors would abide by all fire restriction orders;
 - Campfires or uncontained fires of any kind would be prohibited within the WTP Project Area;
 - Portable generators used in the WTP Project Area would have spark arrestors.
 - d. All proposed disturbances are within the Peter's Point unit: well pad, access and pipeline would occur on lease UTU-0681 while facilities and a portion of the liquids line would occur on lease UTU-04049.

OPERATOR CERTIFICATION

Certification:

I hereby certify that I, or someone under my direction supervision, have inspected the drill site and access route proposed herein; that I am familiar with the conditions which currently exist; that I have full knowledge of state and Federal laws applicable to this operation; that the statements made in this APD package are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein would be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for the operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filings of false statements.

Executed this 23rd day of June 2010
Name: Tracey Fallang
Position Title: Regulatory Analyst
Address: 1099 18th Street, Suite 2300, Denver, CO 80202
Telephone: 303-312-8134
Field Representative Brandon Murdoch
Address: 1820 W. Hwy 40, Roosevelt, UT 84066
Telephone: 435-724-5252
E-mail: bmurdoch@billbarrettcorp.com

Tracey Fallang
Tracey Fallang, Regulatory Analyst

PRESSURE CONTROL EQUIPMENT – Schematic Attached

A. Type: Eleven (11) Inch Double Gate Hydraulic BOP with Eleven (11) Inch Annular Preventer. The blow out preventer will be equipped as follows:

1. One (1) blind ram (above).
2. One (1) pipe ram (below).
3. Drilling spool with two (2) side outlets (choke side 3-inch minimum, kill side 2-inch minimum).
4. 3-inch diameter choke line.
5. Two (2) choke line valves (3-inch minimum).
6. Kill line (2-inch minimum).
7. Two (2) chokes.
8. Two (2) kill line valves, one of which shall be a check valve (2-inch minimum).
9. Upper kelly cock valve with handles available.
10. Safety valve(s) & subs to fit all drill string connections in use.
11. Pressure gauge on choke manifold.
12. Fill-up line above the uppermost preventer.

B. Pressure Rating: 3,000 psi

C. Testing Procedure:

Annular Preventer

At a minimum, the Annular Preventer will be pressure tested to 50% of the rated working pressure for a period of ten (10) minutes or until provisions of the test are met, whichever is longer.

At a minimum the above pressure test will be performed:

1. When the annular preventer is initially installed;
2. Whenever any seal subject to test pressure is broken;
3. Following related repairs; and
4. At thirty (30) day intervals.

In addition, the Annular Preventer will be functionally operated at least weekly.

Blow-Out Preventer

At a minimum, the BOP, choke manifold, and related equipment will be pressure tested to the approved working pressure of the BOP stack (if isolated from the surface casing by a test plug) or to 70% of the internal yield strength of the surface casing (if the BOP is not isolated from the casing by a test plug). Pressure will be

maintained for a period of at least ten (10) minutes or until the requirements of the test are met, whichever is longer.

At a minimum, the above pressure test will be performed:

1. When the BOP is initially installed;
2. Whenever any seal subject to test pressure is broken;
3. Following related repairs; and
4. At thirty (30) day intervals.

In addition the pipe and blind rams will be activated each trip, but not more than once each day. All BOP drills and tests will be recorded in the IADC driller's log.

D. Choke Manifold Equipment:

All choke lines will be straight lines unless turns use tee blocks or are targeted with running tees, and will be anchored to prevent whip and vibration.

E. Accumulator:

The accumulator will have sufficient capacity to open the hydraulically-controlled choke line valve (if so equipped), close all rams plus the annular preventer, and retain a minimum of 200 psi above precharge on the closing manifold without the use of closing unit pumps. The fluid reservoir capacity will be double the usable fluid volume of the accumulator system capacity and the fluid level of the reservoir will be maintained at the manufacturer's recommendations.

The BOP system will have two (2) independent power sources to close the preventers. Nitrogen bottles (3 minimum) will be one (1) of these independent power sources and will maintain a charge equal to the manufacturer's specifications.

The accumulator precharge pressure test will be conducted prior to connecting the closing unit to the BOP stack and at least once every six (6) months thereafter. The accumulator pressure will be corrected if the measured precharge pressure is found to be above or below the maximum or minimum limits specified in the *Onshore Oil & Gas Order Number 2*.

A manual locking device (i.e. hand wheels) or automatic locking device will be installed on all systems of 2M or greater. A valve will be installed in the closing line as close as possible to the annular preventer to act as a locking device. This valve will be maintained in the open position and will be closed only when the power source for the accumulator is inoperative.

Remote controls shall be readily accessible to the driller. Remote controls for all 3M or greater systems will be capable of closing all preventers. Remote controls for 5M or greater systems will be capable of both opening and closing all preventers. Master controls will be at the accumulator and will be capable of opening and closing all preventers and the choke line valve (if so equipped).


F. Miscellaneous Information:

The Blow-Out Preventer and related pressure control equipment will be installed, tested and maintained in compliance with the specifications in and requirements of *Onshore Oil & Gas Order Number 2*. The choke manifold will be located outside the rig sub-structure. The hydraulic BOP closing unit will be located at least twenty-five (25) feet from the well head but readily accessible to the driller. Exact locations and configurations of the hydraulic BOP closing unit will depend upon the particular rig contracted to drill this hole.


A flare line will be installed after the choke manifold, extending 125 feet (minimum) from the center of the drill hole to a separate flare pit.

BILL BARRETT CORPORATION

TYPICAL 3,000 p.s.i. CHOKE MANIFOLD

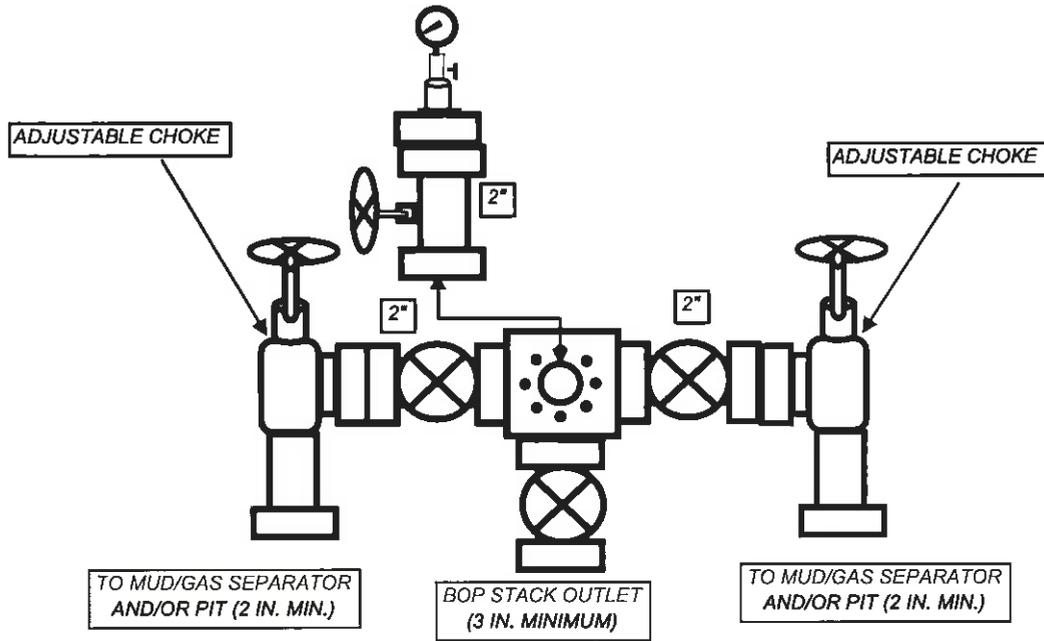

BILL BARRETT CORPORATION
TYPICAL 3,000 p.s.i. BLOWOUT PREVENTER

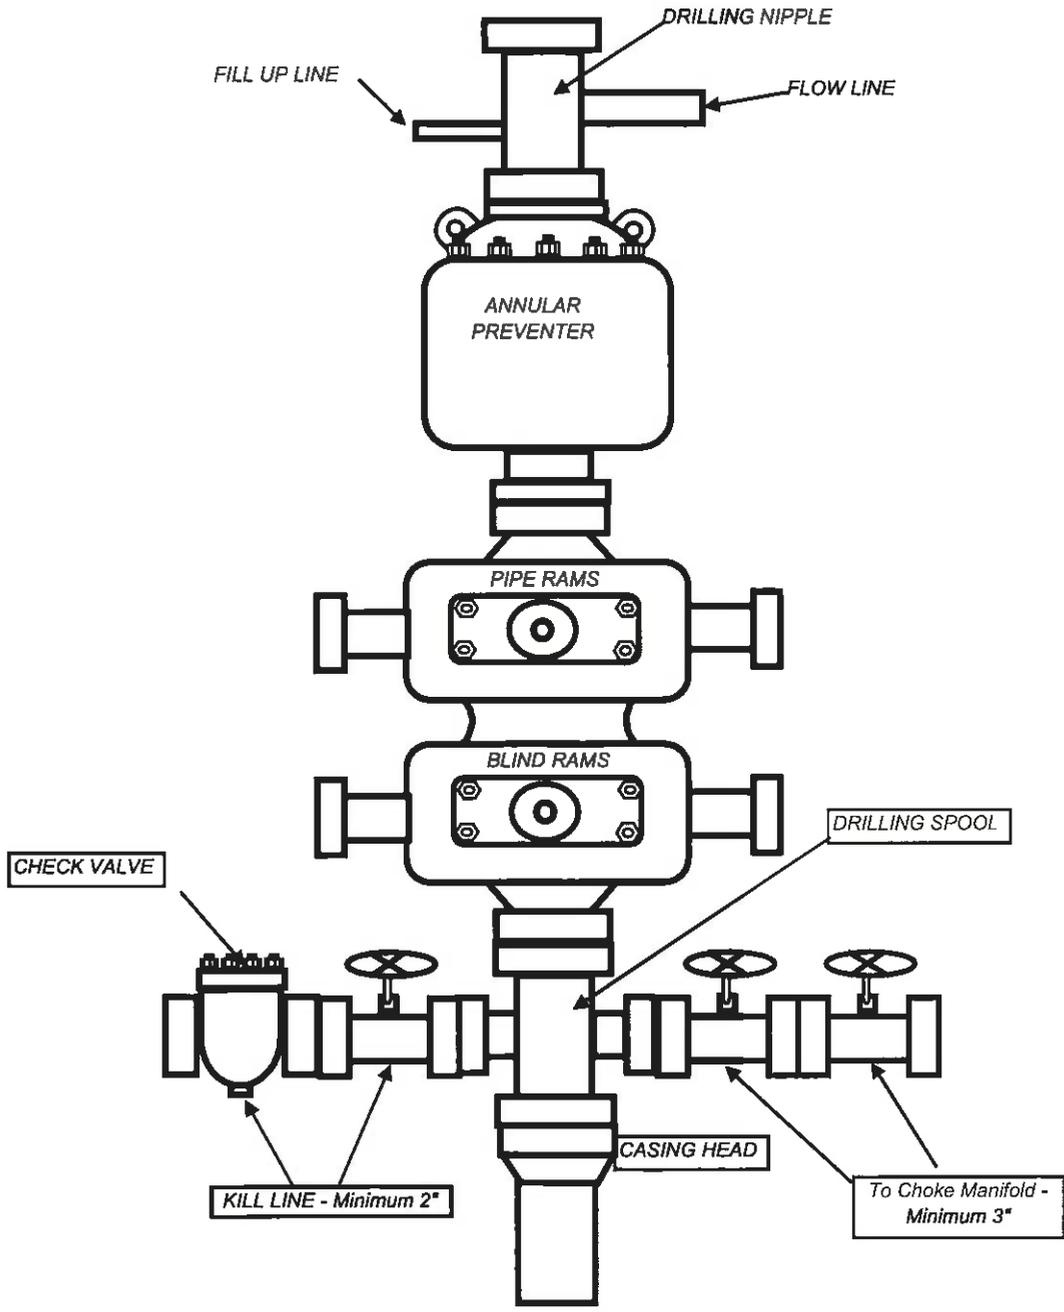



June 23, 2010

Ms. Diana Mason
State of Utah
Division of Oil, Gas and Mining
1594 West North Temple, Suite 1210
P.O. Box 145801
Salt Lake City, Utah 84114-5801

RE: Directional Drilling R649-3-11
Peters Point Unit Federal 12-25D-12-16
SHL: 2414' FSL & 1290' FWL NWSW 25-T12S-R16E
BHL: 1971' FSL & 696' FWL NWSW 25-T12S-R16E
Carbon County, Utah

Dear Ms. Mason:

Pursuant to the filing of Bill Barrett Corporation's ("BBC") Application for Permit to Drill ("APD") regarding the above referenced well, we are hereby submitting this letter in accordance with Oil & Gas Conservation Rule R649-3-11 pertaining to the "Exception to Location and Siting of Wells."

- The above-mentioned proposed location is within the Peters Point Unit Area and a Participating Area;
- This well is a directional well and is greater than 460 feet from the Peter's Point Unit boundary.
- BBC hereby certifies that it is the sole working interest owner within 460 feet of the entire directional well bore.

Based on the information provided, BBC requests that the permit be granted pursuant to R649-3-11. If you should have any questions or need further information, please contact me at 303-312-8513.

Sincerely,


A handwritten signature in blue ink that reads 'Vicki Wambolt'.

Vicki Wambolt
Landman


1099 18TH STREET
SUITE 2300
DENVER, CO 80202
O 303.293.9100
F 303.291.0420

API Number: 4300750029
Well Name: Peter's Point Unit Federal 12-25D-1
Township 12.0 S Range 16.0 E Section 25
Meridian: SLBM
 Operator: BILL BARRETT CORP

Map Prepared:
 Map Produced by Diana Mason

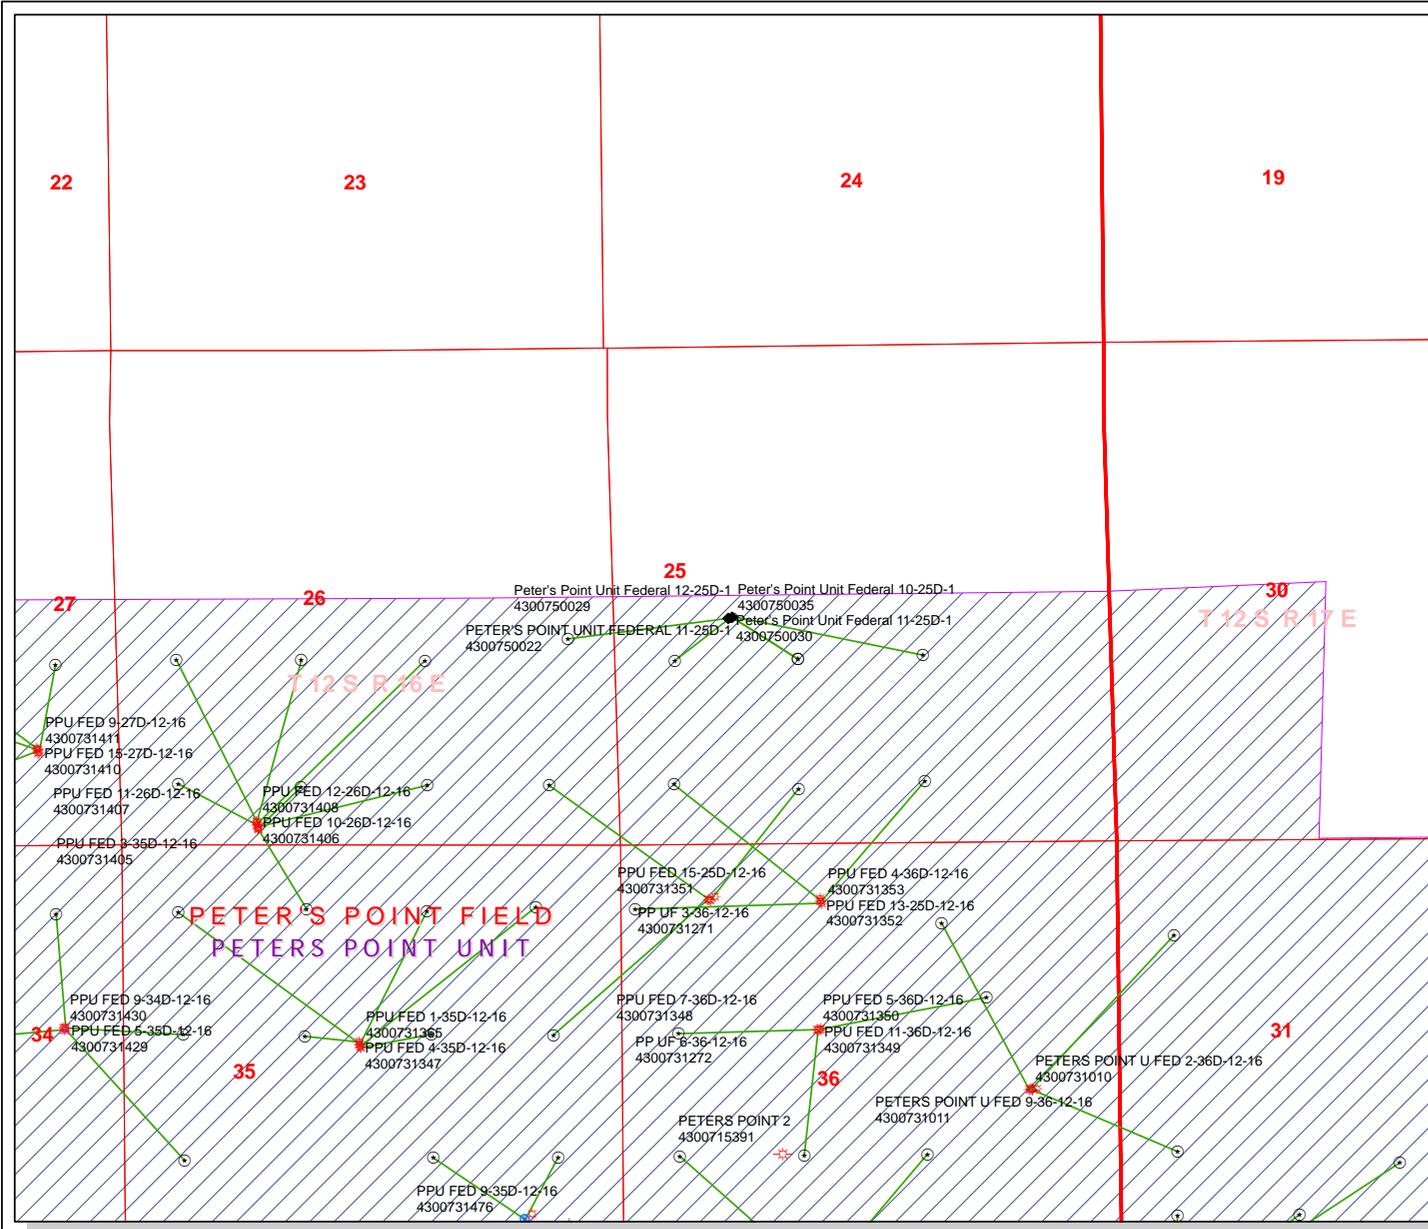

- | | |
|---------------|------------------------------------|
| Units | Wells Query |
| STATUS | Status |
| ACTIVE | APD - Approved Permit |
| EXPLORATORY | DRL - Spudded (Drilling Commenced) |
| GAS STORAGE | GIW - Gas Injection |
| NF PP OIL | GS - Gas Storage |
| NF SECONDARY | LA - Location Abandoned |
| PI OIL | LOC - New Location |
| PP GAS | OPS - Operation Suspended |
| PP GEOTHERM | PA - Plugged Abandoned |
| PP OIL | PGW - Producing Gas Well |
| SECONDARY | POW - Producing Oil Well |
| TERMINATED | RET - Returned APD |
| Fields | SGW - Shut-in Gas Well |
| Sections | SOW - Shut-in Oil Well |
| Township | TA - Temp. Abandoned |
| | TW - Test Well |
| | WDW - Water Disposal |
| | WWI - Water Injection Well |
| | WSW - Water Supply Well |



WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 6/30/2010

API NO. ASSIGNED: 43007500290000

WELL NAME: Peter's Point Unit Federal 12-25D-12-16

OPERATOR: BILL BARRETT CORP (N2165)

PHONE NUMBER: 303 293-9100

CONTACT: Elaine Winick

PROPOSED LOCATION: NWSW 25 120S 160E

Permit Tech Review:

SURFACE: 2414 FSL 1290 FWL

Engineering Review:

BOTTOM: 2202 FSL 1007 FWL

Geology Review:

COUNTY: CARBON

LATITUDE: 39.74412

LONGITUDE: -110.07694

UTM SURF EASTINGS: 579088.00

NORTHINGS: 4399556.00

FIELD NAME: UNDESIGNATED

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU0681

PROPOSED PRODUCING FORMATION(S): MESA VERDE

SURFACE OWNER: 1 - Federal

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

PLAT

Bond: FEDERAL - WYB000040

Potash

LOCATION AND SITING:

R649-2-3.

Unit: PETERS POINT

R649-3-2. General

Oil Shale 190-3

Oil Shale 190-13

Water Permit: Nine Mile Creek

RDCC Review:

Fee Surface Agreement

Intent to Commingle

Commingling Approved

R649-3-3. Exception

Drilling Unit

Board Cause No: Cause 157-03


Effective Date: 5/29/2001

Siting: 460' Fr Exterior Unit Boundary

R649-3-11. Directional Drill

Comments: Presite Completed
APD IS IN UPOD:

Stipulations: 4 - Federal Approval - dmason
15 - Directional - dmason



State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Peter's Point Unit Federal 12-25D-12-16
API Well Number: 43007500290000
Lease Number: UTU0681
Surface Owner: FEDERAL
Approval Date: 7/6/2010

Issued to:

BILL BARRETT CORP, 1099 18th Street Ste 2300, Denver, CO 80202

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 157-03. The expected producing formation or pool is the MESA VERDE Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)

OR

submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <https://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "B. S. [unclear]", written in a cursive style.

Acting Associate Director, Oil & Gas

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0681
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: PETERS POINT
1. TYPE OF WELL Gas Well	8. WELL NAME and NUMBER: PETERS POINT UNIT FED 12-25D-12-16
2. NAME OF OPERATOR: BILL BARRETT CORP	9. API NUMBER: 43007500290000
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202	PHONE NUMBER: 303 312-8164 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2414 FSL 1290 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 12.0S Range: 16.0E Meridian: S	9. FIELD and POOL or WILDCAT: UNDESIGNATED COUNTY: CARBON STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 3/31/2011	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input checked="" type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

In accordance with Utah Division of Oil, Gas, and Mining's Rule 649-3-22, Completion Into Two or More Pools, BBC is submitting this sundry to request commingling approval for the Wasatch and Mesaverde formations. Gas composition is similar across all formations. The pressure profile across the formations is similar and BBC does not anticipate any cross flow. Production is considered to be from one pool. In the event that allocation by zone or interval is required, BBC would use representative sampling obtained from production logs and allocate on a percentage basis by zone or interval. A letter and affidavit of notice is attached. As per Marvin Hendrickson with the Price BLM, federal authority of this action is not necessary.

**Accepted by the
Utah Division of
Oil, Gas and Mining**

Date: September 21, 2010
 By: *Derek Quist*

NAME (PLEASE PRINT) Tracey Fallang	PHONE NUMBER 303 312-8134	TITLE Regulatory Analyst
SIGNATURE N/A	DATE 8/26/2010	



August 5, 2010

Utah Division of Oil, Gas & Mining
1594 W. North Temple, Suite 1210
Salt Lake City, UT 84116

Attention: Dustin Doucet

RE: Sundry Notices
Peters Point Unit
Sections 25 & 26 T12S R16E
Carbon Co., UT

Bill Barrett Corporation has submitted Sundry Notices to commingle production from the Wasatch and Mesaverde Formations in the Peters Point Unit Federal 9-26D-12-16, 12-25D-12-16, 11-25D-12-16 & 10-25D-12-16 wells. As required by the Utah OGM regulations R649-3-22, BBC has enclosed copies of the completed Sundry Notices.

Should you require additional information in this regard, please feel free to contact me at 303-312-8513.

BILL BARRETT CORPORATION

A handwritten signature in blue ink that reads 'Vicki L. Wambolt'.

Vicki L. Wambolt
Landman

Enclosures

1099 18TH STREET
SUITE 2300
DENVER, CO 80202
P 303.293.9100
F 303.291.0420

RECEIVED August 26, 2010



AFFIDAVIT OF NOTICE

My name is Vicki L. Wambolt and I am a Landman with Bill Barrett Corporation (BBC). BBC has submitted Sundry Notices to commingle production from the Wasatch and Mesaverde Formations in the Peters Point Unit Federal 9-26D-12-16, 12-25D-12-16, 11-25D-12-16 & 10-25D-12-16 wells drilled from the pad located in the N2SW of Section 25, Township 12 South, Range 16 East. In compliance with the Utah OGM regulation R649-3-22, I have provided a copy of the Sundry Notices, by certified mail, to the owners as listed below of all contiguous oil and gas leases or drilling units overlying the pool.

State of Utah
School and Institutional Trust Lands Administration
675 East 500 South, Suite 500
Salt Lake City, UT 84102

Bureau of Land Management
Price Field Office
125 South 600 West
Price, UT 84501

Date: August 5, 2010

Affiant

A handwritten signature in blue ink that reads 'Vicki L. Wambolt'. The signature is written in a cursive style and is positioned above a horizontal line.

Vicki L. Wambolt

1099 18TH STREET
SUITE 2300
DENVER, CO 80202
P 303.293.9100
F 303.291.0420

RECEIVED August 26, 2010

Uinta Basin

West Tavaputs Plateau



- WELL SYMBOLS**
- Abandoned GAS Well
 - Abandoned Oil Well
 - Dry hole
 - Gas Well
 - Junked
 - Location
 - Shut In Gas Well
 - Water Well

By: JA


August 16, 2010 4:33 PM

T12S-R16E

Peter's Point Unit

N/2 SW 25 Pad

RECEIVED August 26, 2010

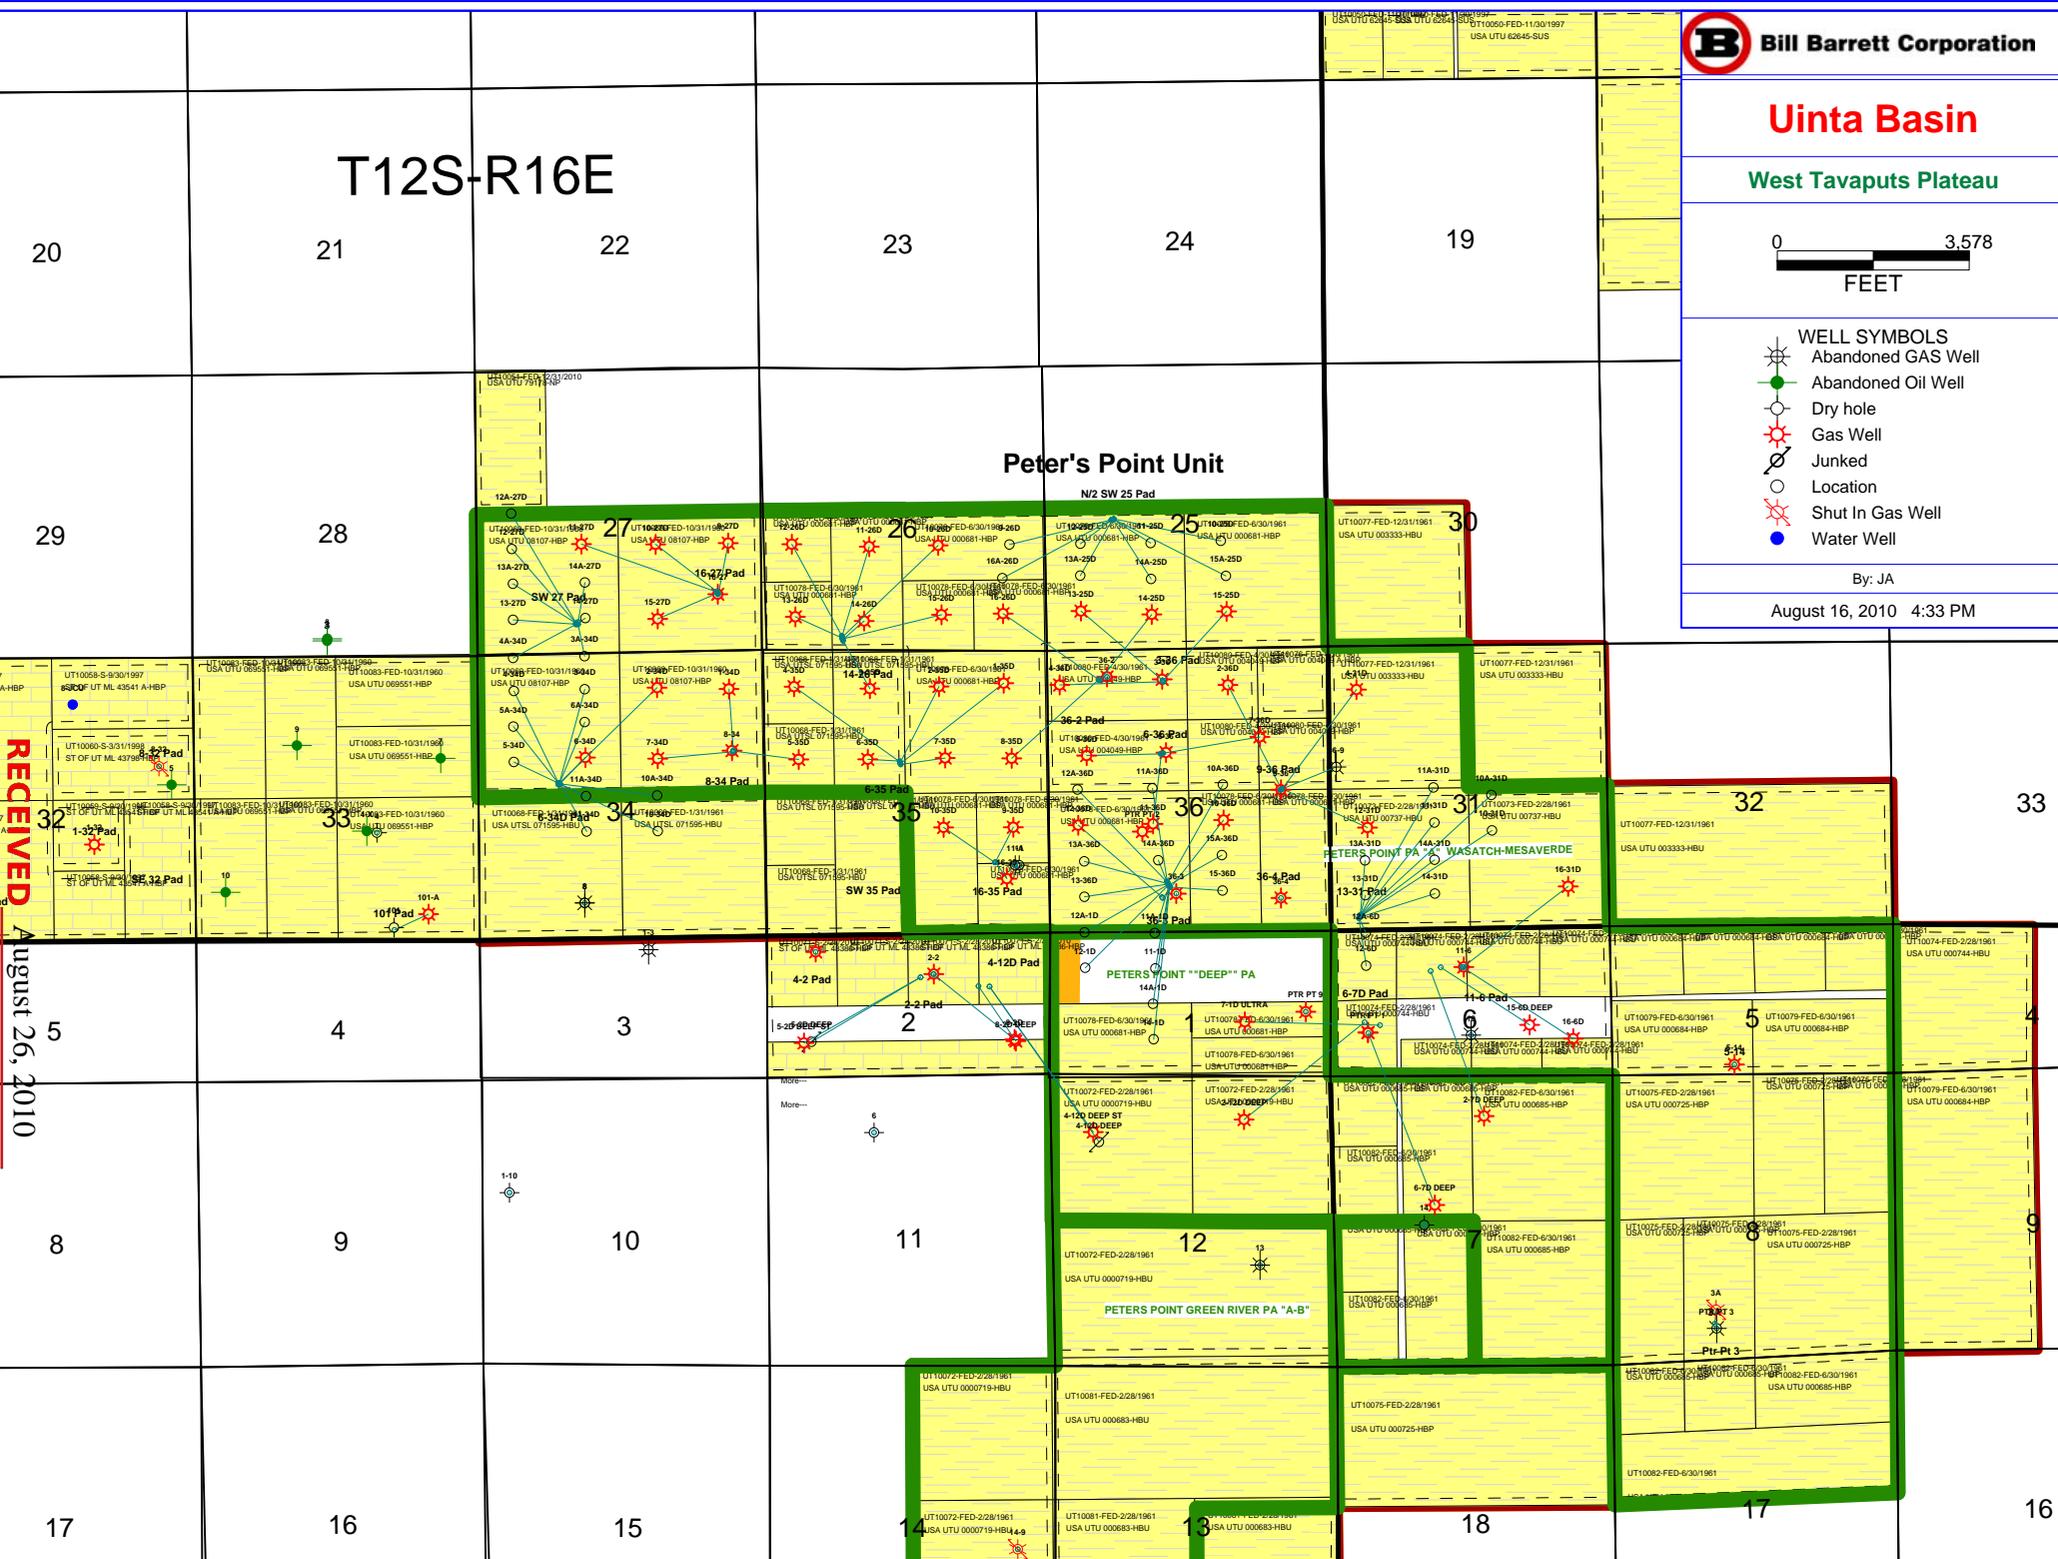



August 5, 2010

Bureau of Land Management
Price Field Office
125 South 600 West
Price, UT 84501

Certified Mail 7008 2810 0002 3823 8828

Attention: Marvin Hendricks

RE: Sundry Notices
Peters Point Unit
Sections 25 & 26 T12S R16E
Carbon Co., UT

Bill Barrett Corporation has submitted Sundry Notices to commingle production from the Wasatch and Mesaverde Formations in the Peters Point Unit Federal 9-26D-12-16, 12-25D-12-16, 11-25D-12-16 & 10-25D-12-16 wells. As required by the Utah OGM regulations R649-3-22, BBC has enclosed copies of the completed Sundry Notices.

Should you require additional information in this regard, please feel free to contact me at 303-312-8513.

BILL BARRETT CORPORATION


Vicki L. Wambolt
Landman

Enclosures

1099 18TH STREET
SUITE 2300
DENVER, CO 80202
P 303.293.9100
F 303.291.0420

RECEIVED August 26, 2010



August 5, 2010

State of Utah
School and Institutional Trust Lands Administration
675 East 500 South, Suite 500
Salt Lake City, UT 84102

Certified Mail 7008 2810 0002 3823 8835

Attention: LaVonne Garrison

RE: Sundry Notices
Peters Point Unit
Sections 25 & 26 T12S R16E
Carbon Co., UT

Bill Barrett Corporation has submitted Sundry Notices to commingle production from the Wasatch and Mesaverde Formations in the Peters Point Unit Federal 9-26D-12-16, 12-25D-12-16, 11-25D-12-16 & 10-25D-12-16 wells. As required by the Utah OGM regulations R649-3-22, BBC has enclosed copies of the completed Sundry Notices.

Should you require additional information in this regard, please feel free to contact me at 303-312-8513.

BILL BARRETT CORPORATION

A handwritten signature in black ink that reads 'Vicki L. Wambolt'.

Vicki L. Wambolt
Landman

Enclosures

1099 18TH STREET
SUITE 2300
DENVER, CO 80202
P 303.293.9100
F 303.291.0420

RECEIVED August 26, 2010

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 6

ENTITY ACTION FORM

Operator: Bill Barrett Corporation Operator Account Number: N 2165
 Address: 1099 18th Street, Suite 2300
city Denver
state CO zip 80202 Phone Number: (303) 312-8115

Well 1

API Number	Well Name		QQ	Sec	Twp	Rng	County
4300750021	Peter's Point Unit Fed 9-26D-12-16		NWSW	25	12S	16E	Carbon
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
<i>AB</i>	<i>99999</i>	<i>2470</i>	<i>11/4/2010</i>		<i>11/29/10</i>		
Comments: Spud by Triple A Drilling @ 12:00 pm, setting conductor pipe only. <i>WSMVD BHL = Sec 26 NESE</i>							

Well 2

API Number	Well Name		QQ	Sec	Twp	Rng	County
4300750022	Peter's Point Unit Fed 11-25D-12-16		NWSW	25	12S	16E	Carbon
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
<i>AB</i>	<i>99999</i>	<i>2470</i>	<i>11/6/2010</i>		<i>11/29/10</i>		
Comments: Spud by Triple A Drilling @ 12:00 pm, setting conductor pipe only. <i>WSMVD BHL = NESW</i>							

Well 3

API Number	Well Name		QQ	Sec	Twp	Rng	County
4300750029	Peter's Point Unit Fed 12-25D-12-16		NWSW	25	12S	16E	Carbon
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
<i>AB</i>	<i>99999</i>	<i>2470</i>	<i>11/5/2010</i>		<i>11/29/10</i>		
Comments: Spud by Triple A Drilling @ 12:00 pm, setting conductor pipe only. <i>WSMVD BHL = NWSW</i>							

ACTION CODES:

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (Explain in 'comments' section)

RECEIVED

NOV 24 2010

Brady Riley

Name (Please Print)
Brady Riley

Signature
Permit Analyst

Title

11/24/2010

Date



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
PRICE FIELD OFFICE



125 SOUTH 600 WEST PRICE, UT 84501 (435) 636-3600

CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Bill Barrett Corporation Surface Location: NWSW-Sec 25-T12S-R16E
Well No: Peters Point Unit Federal 12-25D-12-16 Lease No: UTU-0681
API No: 43-007-50029 Agreement: UTU-63014D

OFFICE NUMBER: (435) 636-3600

OFFICE FAX NUMBER: (435) 636-3657

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify NRS)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify NRS)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Petroleum Eng. Technician)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings.
BOP & Related Equipment Tests (Notify Petroleum Eng. Technician)	-	Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins, or production resumes after well has been off production for more than ninety (90) days.

UDOGM

**DRILLING PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DRILLING & PRODUCTION COAs

- While drilling the surface hole with air, a float valve shall be run above the bit, per Onshore Order #2 Part III.E Special Drilling Operations.
- Bill Barrett Corporation (BBC) proposed the possibility of using several different grades of production casing (including N-80, I-80, I-100 and P-110). Per subsequent conversations with BBC, BBC stated only P-110 grade production casing will be used for this well. Therefore, use of N-80, I-80 and I-100 casing is not approved for use in this well, however the use of any of these grades may be requested in the future by sundry notice.
- A cement bond log (CBL) shall be run to determine the top of cement behind the production casing, and a field copy sent to the Price Field Office.
- A complete set of angular deviation and directional surveys for this directional well will be submitted to the Price Field Office petroleum engineer within 30 days of completing the well.
- A copy of the approved Application for Permit to Drill (APD) for this well shall be on location at all times once drilling operations have commenced.

VARIANCES GRANTED

- BBC's request for variance to not use de-duster equipment (Onshore Order #2 Part III.E Special Drilling Operations) is granted, unless the air/mist system is not used.
- BBC's request for variance to use an electronic flow meter for gas measurement (Onshore Order #5 Measurement of Gas) is granted as long as it meets or exceeds the requirements of Utah NTL 2007-1 regarding the use of Electronic Flow Computers.
- BBC's request for variance from Onshore Order #5 Part III.C.3 Gas Measurement by Orifice Meter to use a flow conditioner on this well instead of straightening vanes is approved with the following conditions:
 1. Flow conditioners must be installed in accordance with the manufacturer's specifications.
 2. The make, model, and location of flow conditioner must be clearly identified and available to BLM on-site at all times.
 3. This is a provisional approval that is subject to change pending final review and analysis by BLM. If BLM determines that this flow conditioner cannot meet or exceed the minimum standards required by Onshore Order #5, you will be required to retrofit the installation to comply with BLM requirements, or replace the installation with one that complies with AGA Report Number 3, 1985. The time frame for compliance will be specified by the Price Field Office.

STANDARD OPERATING REQUIREMENTS

- The requirements included in Onshore Order #2 Drilling Operations shall be followed.
- The Price Field Office petroleum engineer will be notified 24 hours verbally prior to spudding the well.
- Notify the Price Field Office petroleum engineering technician at least 24 hours in advance of casing cementing operations, BOPE tests and casing pressure or mud weight equivalency tests.
- Should H₂S be encountered in concentrations greater than 100 ppm, the requirements of Onshore Order #6 Hydrogen Sulfide Operations shall be followed.
- Any deviation from the permitted APD's proposed drilling program shall have prior approval from the petroleum engineer. Changes may be requested verbally (to be followed by a written sundry sent to this office), or submitted by written sundry if time warrants.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed. The closing unit controls shall remain unobstructed and readily accessible at all times, and choke manifolds shall be located outside of the rig substructure.
- BOP testing shall be conducted within 24 hours of drilling out from under the surface casing, and weekly thereafter as specified in Onshore Order #2.
- All BOPE components shall be inspected daily, and the inspections recorded in the daily drilling report. Components shall be operated and tested, as required by Onshore Order #2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder, and not by the rig pumps. Test results shall be reported in the driller's log.
- All casing strings below the conductor pipe shall be pressure tested to .22 psi/foot or 1500 psi (whichever is greater), but not to exceed 70% of the internal yield pressure.
- No aggressive/fresh hard-banded drill pipe shall be used in the casing design. The proposed use of non-API standard casing must be approved in advance by the petroleum engineer.
- During drilling operations, daily drilling reports shall be submitted by sundry on a weekly basis to the Price Field Office. Within 30 days of finishing drilling and completion operations, a chronological daily operations history shall be submitted by sundry to this office.
- A copy of all logs run on this well shall be submitted digitally (in PDF or TIFF format) to the Price Field Office.
- The venting or flaring of gas while initially testing the well shall be done in accordance with the requirements specified in Notice to Lessees #4A, and shall not exceed a period of 30 days or the production of 50 MMCF of gas, whichever occurs first. Additional time needed to vent or flare gas during production operations requires prior approval from the Price Field Office.
- Should this well be successfully completed as a producing well, the Price Field Office must be notified within 5 business days following the date the well has first sales.

STANDARD OPERATING REQUIREMENTS (cont.)

- Proposed production operations that involve: 1) the commingling of production from wells located on-lease or off-lease, 2) off-lease measurement, or 3) off-lease storage shall have prior written approval from the Price Field Office.
- Operators shall meet the requirements listed in Onshore Order #4 Measurement of Oil and Onshore Order #5 Measurement of Gas. New oil and gas meters shall be calibrated prior to initial product sales. The operator (or its contractors) is responsible for providing the date and time of the initial meter calibration (and all future meter proving schedules) to the petroleum engineering technician. Copies of all meter calibration reports that are performed shall be submitted to the Price Field Office.
- In accordance with 43 CFR 3162.4-3, this well's production data shall be reported on the "Monthly Report of Operations" starting with the month in which operations commence and continue each month until the well is plugged and abandoned.
- The operator is responsible for submitting the information required in 43 CFR 3162.4-1 Well Records and Reports, including BLM Form 3160-4, Well Completion and Recompletion Report and Log which must be submitted to the Price Field Office within 30 days of completing the well.
- Onshore Order #7 authorizes the disposal of water produced from this well in the reserve pit for a period of 90 days after the date of initial production. A permanent disposal method must be submitted and approved by this office, and in operation prior to the end of this 90-day period.
- The requirements of Onshore Order #3 Site Security shall be implemented, and include (as applicable): 1) all lines entering and leaving hydrocarbon storage tanks shall be effectively sealed and seal records maintained, 2) no by-passes are allowed to be constructed around gas meters, 3) a site facility diagram shall be submitted to the Price Field Office within 60 days following construction of the facilities.
- Additional construction that is proposed, or the proposed alteration of existing facilities (including roads, gathering lines, batteries, etc.), which will result in the disturbance of new ground, requires prior approval of the Price Field Office natural resource specialist.
- This well and its associated facilities shall have identifying signs on location in accordance with 43 CFR 3162.6 requirements.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the Price Field Office natural resource specialist.
- The Price Field Office petroleum engineer shall be notified 24 hours in advance of the plugging of the well (unless the plugging is to take place immediately upon receipt of oral approval), so that a technician may have sufficient time to schedule and witness the plugging operations.
- If operations are to be suspended on a well for more than 30 days, prior approval of the Price Field Office shall be obtained, and notification also given before operations resume.

**SURFACE USE
CONDITIONS OF APPROVAL**

Project Name: BBC Peter's Point Drilling Program One Multiple Well Location

Operator: Bill Barrett Corporation

List of Wells:

Name	Number	Section	TWP/RNG
Peter's Point Unit Federal	9-26D-12-16	25	12S/16E
Peter's Point Unit Federal	12-25D-12-16		
Peter's Point Unit Federal	11-25D-12-16		
Peter's Point Unit Federal	10-25D-12-16		

I To be followed as Conditions of Approval:

The following attachments from the Record of Decision West Tavaputs Plateau Natural Gas Full Field Development Plan:

Attachment 2	Conditions of Approval and Stipulations
Attachment 3	Green River District Reclamation Guidelines
Attachment 4	Programmatic Agreement
Attachment 5	Special Protection Measures for Wildlife
Attachment 6	Agency Wildlife Mitigation Plan
Attachment 7	Long-Term Monitoring Plan for Water Resources
Attachment 8	Mitigation Compliance and Monitoring Plan

II Site Specific Conditions of Approval

1. A pre-construction field meeting may be conducted prior to beginning any dirt work approved under this APD. The operator shall contact the BLM Authorized Officer Don Stephens @ 435-636-3608 at least 48-hours prior to beginning operations so that the meeting can be scheduled. The operator is responsible for having all contractors present (dirt contractors, drilling contractor, pipeline contractor, project oversight personnel, etc.) including the overall field operations superintendent, and for providing all contractors copies of the approved APD(s), project map and BLM Conditions of Approval pertinent to the work that each will be doing.
2. A Paleontologist permitted by BLM will monitor construction activity during surface disturbing activities described in the APD. If paleontologic resources are uncovered during construction activities, the operator shall immediately suspend all operations that will further disturb such resources, and immediately notify the Authorized Officer (AO). The AO will arrange for a determination of significance and, if necessary, recommend a recovery or avoidance plan. Contact the Price Field Office paleontological lead (Michael Leschin @ 435-636-3619) prior to start of surface disturbing activities.

3. The cuttings trench shall be lined.
4. The cuttings shall not be removed from the location without prior approval of the Authorized Officer.
5. The operator shall retain a strip of Pinyon-Juniper trees on the North East side of pad.
6. The operator shall follow the attached Upper Colorado River Recovery Program guidance.
7. The operator shall on an annual basis report to the BLM the acre feet of water used for the project with a total for each type of source. This report shall contain the information found under monitoring on page 53 of attachment 9 (Biological Opinion) of the WTP ROD and shall be reported to BLM by September 15 of each year.
8. When water is pumped directly from Nine Mile Creek or perennial drainages, the following measures shall be applied to reduce or eliminate direct impacts to habitat for the Colorado River fish species. Where directed by the BLM, the operator will construct erosion control devices (e.g., riprap, bales, and heavy vegetation) at culvert outlets. All construction activities shall be performed to retain natural water flows.
9. Contact Don Stephens, Natural Resource Specialist, (435) 636-3608, Bureau of Land Management, Price Field Office, if there are any questions concerning these surface use COAs.

III Standard Conditions of Approval

A. General

1. If any cultural values [sites, artifacts, human remains] are observed during operation of this lease/permit/right-of-way, they will be left intact and the Price Field Manager notified. The authorized officer will conduct an evaluation of the cultural values to establish appropriate mitigation, salvage or treatment. The operator is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, the operator is to immediately stop work that might further disturb such materials, and contact the authorized BLM officer (AO).

B. Construction

1. Remove all available topsoil from constructed well locations including areas of cut and fill, and stockpile at the site. Topsoil will also be salvaged for use in reclamation on all other areas of surface disturbance (roads, pipelines, etc.). Clearly segregate topsoil from excess spoil material.
2. During construction, emissions of particulate matter from well pad and road construction would be minimized by application of water or other non-saline dust suppressants with at least 50 percent control efficiency. Dust inhibitors (surfacing materials, non-saline dust suppressants, and water) will be used as necessary on unpaved roads that present a fugitive dust problem. The use of chemical dust suppressants on public surface will require prior approval from the BLM Authorized Officer.
3. The operator shall submit a Sundry Notice (Form 3160-5) to BLM for approval prior to construction of any new surface disturbing activities that are not specifically addressed in the approved APD.

C. Operations/Maintenance

1. In accordance with OSHA requirements, a file will be maintained onsite containing current Material Safety Data Sheets (MSDS) for all chemicals, compounds and/or substances which are used in the course of construction, drilling, completion and production operations.

D. Dry Hole/Reclamation

1. Phased reclamation plans will be submitted to BLM for approval prior to individual POD facility abandonment via a Notice of Intent (NOI) Sundry Notice.
2. BLM will not release the performance bond until all disturbed areas associated with the APD/POD have been successfully revegetated (evaluation will be made after the second complete growing season) and has met all other reclamation goals of the surface owner and surface management agency.
3. A Notice of Intent to Abandon and a Subsequent Report of Abandonment must be submitted for abandonment approval.
4. For performance bond release approval, a Final Abandonment Notice (with a surface owner release letter on split-estate) must be submitted prior to a final abandonment evaluation by BLM.

E. Producing Well

1. An interim reclamation plan shall be submitted to BLM within 90 days of APD approval.
2. Upgrade and maintain access roads and drainage control (e.g., culverts, drainage dips, ditching, crowning, surfacing, etc.) as necessary and as directed by the BLM Authorized Officer to prevent soil erosion and accommodate safe, environmentally-sound access.
3. Prior to construction of production facilities not specifically addressed in the APD, the operator shall submit a Sundry Notice to the BLM Authorized Officer for approval.

F. Roads and Pipelines

1. Roads constructed on BLM lands shall be constructed to allow for drainage and erosion control. The operator is responsible for maintenance of all roads authorized through the lease or right-of-way. Construction and maintenance shall comply with Class III Road Standards with a 16-ft wide graveled travel surface as described in BLM Manual Section 9113, and the BLM Gold Book standards, except as modified by BLM. Maintenance may include but is not limited to grading, applying gravel, snow removal, ditch cleaning, and headcut restoration/prevention.
2. The operator may be required to provide an inspector under the direction of a registered professional engineer (PE) at all times during road construction. A PE shall certify (statement with PE stamp) that the road was constructed to the required Bureau of Land Management (BLM) road standards.
3. Erosion-control structures such as water bars, diversion channels, and terraces will be constructed to divert water and reduce soil erosion on the disturbed area. Road ditch turnouts shall be equipped with energy dissipaters as needed to avoid erosion. Where roads interrupt overland sheet-flow and convert this runoff to channel flow, ditch turnouts shall be designed to reconvert channel flow to sheet flow. As necessary cut banks, road drainages, and road crossings shall be armored or otherwise engineered to prevent headcutting.

Upper Colorado River Recovery Program

In addition, the applicant has agreed to have the Upper Colorado River Recovery Program (Recovery Program) serve as a conservation measure within the proposed action. The following paragraphs further clarify the Recovery Program's role.

In determining if sufficient progress has been achieved under the Recovery Program, we consider--a) actions which result in a measurable population response, a measurable improvement in habitat for the fishes, legal protection of flows needed for recovery, or a reduction in the threat of immediate extinction; b) status of fish populations; c) adequacy of flows; and, d) magnitude of the Project impact. In addition, we consider support activities (funding, research, information, and education, etc.) of the Recovery Program if they help achieve a measurable population response, a measurable improvement in habitat for the fishes, legal protection of flows needed for recovery, or a reduction in the threat of immediate extinction. We evaluate progress separately for the Colorado River and Green River Subbasins; however, it gives due consideration to progress throughout the Upper Basin in evaluating progress toward recovery.

Depletion impacts can be offset by--a) the water Project proponent's one-time contribution to the Recovery Program in the amount of \$18.99 per acre-foot of the Project's average annual depletion; b) appropriate legal protection of instream flows pursuant to State law; and, c) accomplishment of activities necessary to recover the endangered fishes as specified under the RIPRAP. We believe it is essential that protection of instream flows proceed expeditiously, before significant additional water depletions occur. As the project's peak annual new depletion of 289.78 acre-feet is below the current sufficient progress threshold of 4,500 acre-feet, Recovery Program activities will serve as the conservation measures to minimize adverse affects to the Colorado pikeminnow, razorback sucker, humpback chub, and bonytail and destruction or adverse modification of critical habitat caused by the project's new depletion.

With respect to (a) above (i.e., depletion charge), the applicant will make a one-time payment which has been calculated by multiplying the Project's peak annual depletion (289.78 acre-feet) by the depletion charge in effect at the time payment is made. For Fiscal Year 2010 (October 1, 2009, to September 30, 2010), the depletion charge is \$18.99 per acre-foot for the average annual depletion which equals a total payment of **\$5,502** for this Project. A minimum of 10% of the total payment will be provided to the Service's designated agent, the National Fish and Wildlife Foundation (Foundation), at the time of issuance of the Federal approvals from the BLM, with the rest to be paid when construction commences. Fifty percent of the funds will be used for acquisition of water rights to meet the instream flow needs of the endangered fishes (unless otherwise recommended by the Implementation Committee); the balance will be used to support other recovery activities for the Colorado River endangered fishes. All payments should be made to the National Fish and Wildlife Foundation.

National Fish and Wildlife Foundation
1133 15th Street, NW
Suite 1100
Washington, DC 20005

Each payment is to be accompanied by a cover letter that identifies the Project and biological opinion that requires the payment, the amount of payment enclosed, check number, and any special conditions identified in the biological opinion relative to disbursement or use of the funds (there are none in this instance). A copy of the cover letter and of the check is to be sent directly to the Service field office that issued the biological opinion. The cover letter shall identify the name and address of the payor, the name and address of the Federal Agency responsible for authorizing the Project, and the address of the Service office issuing the biological opinion. This information will be used by the Foundation to notify the payor, the lead Federal Agency, and the Service that payment has been received. The Foundation is to send notices of receipt to these entities within 5 working days of its receipt of payment.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0681
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: PETERS POINT
1. TYPE OF WELL Gas Well	8. WELL NAME and NUMBER: PETERS POINT U FED 12-25D-12-16
2. NAME OF OPERATOR: BILL BARRETT CORP	9. API NUMBER: 43007500290000
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202	PHONE NUMBER: 303 312-8164 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2414 FSL 1290 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 12.0S Range: 16.0E Meridian: S	9. FIELD and POOL or WILDCAT: UNDESIGNATED COUNTY: CARBON STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 12/15/2010 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input checked="" type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input type="text" value="general well test proced"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

This sundry is being submitted to further clarify testing procedures discussed and verbally approved by the BLM as well as final equipment installations. Please see attached document for details specific to the Peter's Point N/2 SW 25 Pad and contact Brady Riley at 303-312-8115 with any questions.

Accepted by the Utah Division of Oil, Gas and Mining

Date: 12/14/2010

By: *Dark K. Quist*

NAME (PLEASE PRINT) Brady Riley	PHONE NUMBER 303 312-8115	TITLE Permit Analyst
SIGNATURE N/A		DATE 12/10/2010

General Well Testing

Initial testing of wells would occur within 15 days of first sales and would be a 1-3 day test to get a baseline for allocation. After the initial test is performed, testing would occur within 90 days thereafter, testing each well for approximately 3 days and rotating through the wells without any downtime between tests.


As both Prickly Pear and Peter's Point have participating areas (PA) and wells drilled from each pad could include both PA and non-PA wells, specific procedures are implemented for these situations. PA and non-PA will always be measured separately and production would not be combined together within the same tanks. All wells drilled are within units. These procedures are as follows:

- 1) Isolate the PA test tank(s);
- 2) Transfer any remaining liquids from the test tank(s) to the PA production tank(s);
- 3) Strap the starting fluid levels in the test tank(s);
- 4) Note date and time of beginning test, document and record in eVIN;
- 5) Flow test well into test tank(s) for pre-determined period, not to be less than a 24 hour period;
- 6) Isolate the test tank(s), divert the test well's production to the in PA production tank(s);
- 7) Strap the ending fluid levels in the test tank(s);
- 8) Record and document the length of test time, amount of oil produced, amount of water produced and amount of gas produced (through wellhead meter) for the test period into eVIN;
- 9) Procedures for non-PA would be same steps as 1-8.

Details specific to the Peter's Point N/2 SW 25 Pad are as follows:

Well Name Peter's Point Unit Fed	API	Drill Phase ¹	Lease UTU-	PA Boundary	Facilities
9-26D-12-16	4300750021	1	0681	In	1) All phase 1 wells proposed are within the PA; Phase 2 wells are outside the PA. 2) Liquids to be piped to the existing 36-2 well pad/CTB. Up to 4 liquids lines up to 4 inch, one PA test, one PA and one non-PA, one non-PA test. 3) One 8 inch buried gas line to the main tie-in was laid. 4) One 300-bbl low profile test tank to be installed on the N/2 SW 25 pad. The 36-2 CTB will have up to 9-400 bbl tanks. 5) Four existing (in PA wells) are located on the 36-2 pad and production would be combined between these existing PA wells and the newly proposed in PA wells
12-25D-12-16	4300750029	1	0681	In	
13A-25D-12-16	not yet permitted	2	0681	In	
14A-25D-12-16	not yet permitted	2	0681	In	
15A-25D-12-16	not yet permitted	2	0681	In	
16A-26D-12-16	not yet permitted	2	0681	In	
11-25D-12-16	4300750022	1	0681	In	
10-25D-12-16	4300750035	1	0681	In	

¹Drill Phase 2 indicates that well(s) not initially planned to be drilled during the first phase of drilling on the pad.

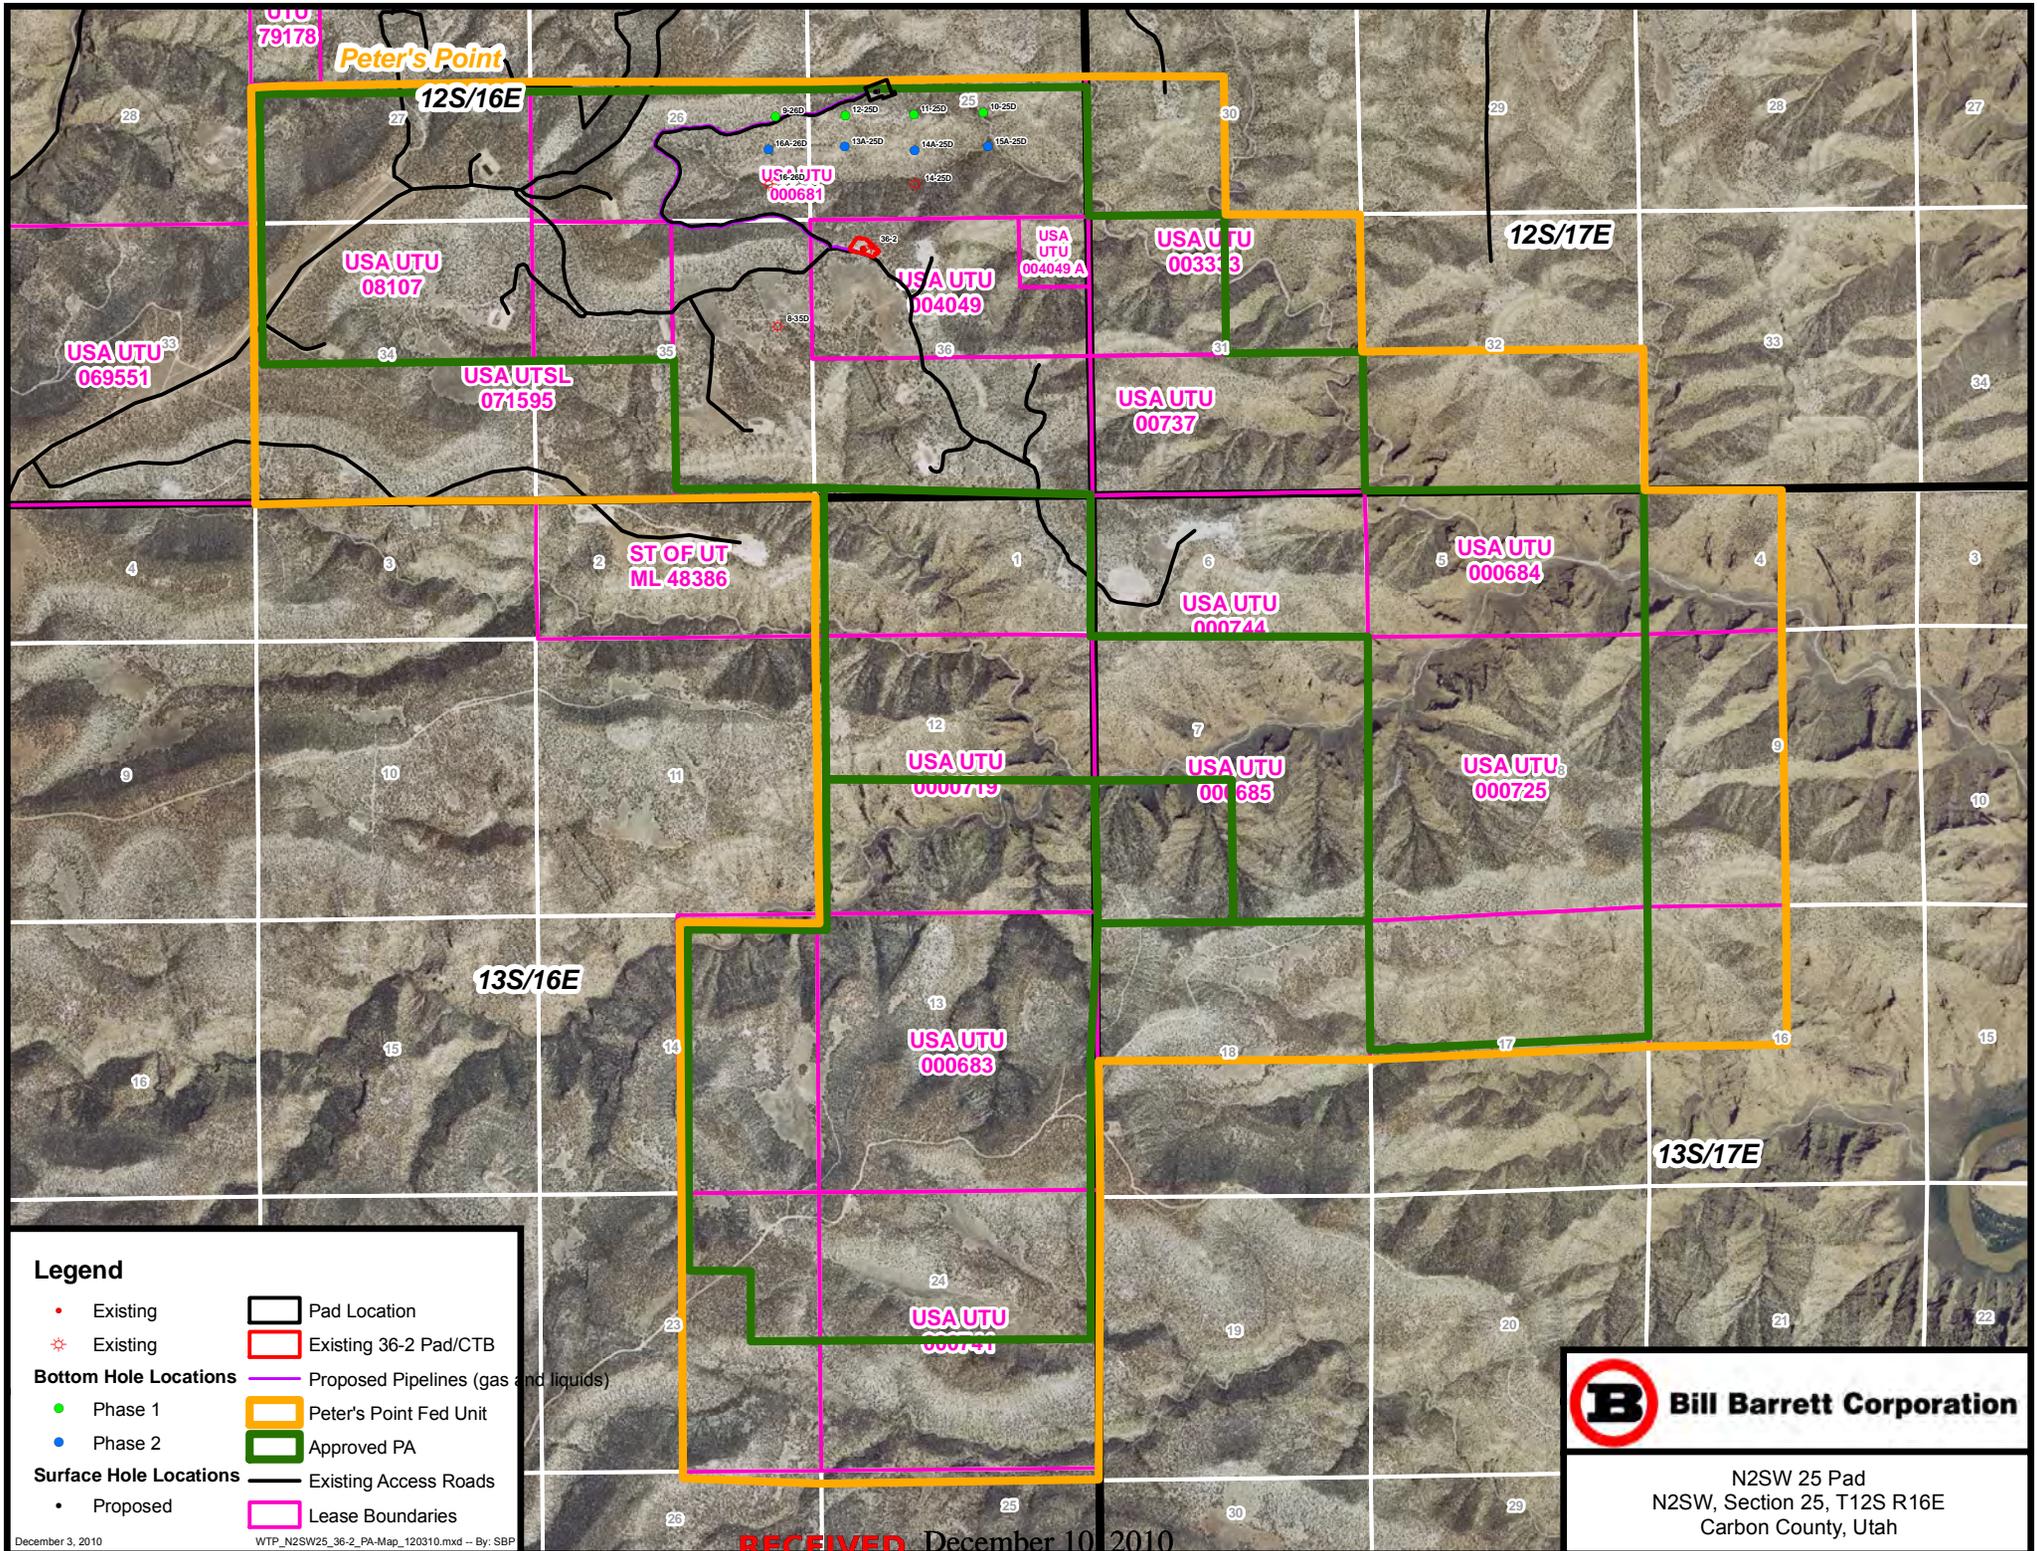

Legend

- Existing
- ★ Existing
- Bottom Hole Locations**
- Phase 1
- Phase 2
- Surface Hole Locations**
- Proposed
- ▭ Pad Location
- ▭ Existing 36-2 Pad/CTB
- Proposed Pipelines (gas and liquids)
- ▭ Peter's Point Fed Unit
- ▭ Approved PA
- Existing Access Roads
- ▭ Lease Boundaries



N2SW 25 Pad
 N2SW, Section 25, T12S R16E
 Carbon County, Utah

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0681
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: PETERS POINT
1. TYPE OF WELL Gas Well	8. WELL NAME and NUMBER: PETERS POINT U FED 12-25D-12-16
2. NAME OF OPERATOR: BILL BARRETT CORP	9. API NUMBER: 43007500290000
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202	PHONE NUMBER: 303 312-8164 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2414 FSL 1290 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 12.0S Range: 16.0E Meridian: S	9. FIELD and POOL or WILDCAT: UNDESIGNATED COUNTY: CARBON STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 12/1/2010	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

December 2010 Monthly Activity Report. No activity reported since spud of well on 11/5/10.

**Accepted by the
 Utah Division of
 Oil, Gas and Mining
 FOR RECORD ONLY**

NAME (PLEASE PRINT) Brady Riley	PHONE NUMBER 303 312-8115	TITLE Permit Analyst
SIGNATURE N/A		DATE 1/3/2011

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0681
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: PETERS POINT
1. TYPE OF WELL Gas Well	8. WELL NAME and NUMBER: PETERS POINT U FED 12-25D-12-16
2. NAME OF OPERATOR: BILL BARRETT CORP	9. API NUMBER: 43007500290000
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202	PHONE NUMBER: 303 312-8164 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2414 FSL 1290 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 12.0S Range: 16.0E Meridian: S	9. FIELD and POOL or WILDCAT: UNDESIGNATED COUNTY: CARBON STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 2/28/2011	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Febuary Monthly Activity Report attached.

Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY

NAME (PLEASE PRINT) Brady Riley	PHONE NUMBER 303 312-8115	TITLE Permit Analyst
SIGNATURE N/A		DATE 3/2/2011

Peter's Point #12-25D-12-16 2/17/2011 22:00 - 2/18/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion

Time Log Summary

WALK RIG TO PETERS POINT 12-25D-12-16 - 3, NIPPLE UP BOPs - 2, TEST BOP WITH REBEL TESTING PIPE & BLIND RAMS, CHOKE LINE & VALVES
 FLOOR VALVES & IBOP, KILL LINE VALVES
 CHOKE MANIFOLD TO 3000 PSI FOR 10 MIN
 TEST HYDRILL TO 1500 PSI FOR 10 MIN
 TEST SURFACE CSG TO 1500 PSI FOR 30 MIN - 3

Peter's Point #12-25D-12-16 2/18/2011 06:00 - 2/19/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion

Time Log Summary

FINNISH BOP TEST - 2.5, INSTALL WEAR BUSHING - 0.5, INSTALL MWD TOOL - 0.5, TRIP IN TO 965' - 0.5, DRLG PLUG, FLOAT COLLAR, CMT & SHOE
 985' - 1030' - 0.5, DRLG 1030' - 2054' (170 FPH) BOTH PUMPS @ 70 SPM
 576 GPM BIT 97 RPM PIPE 45 RPM 25 K ON BIT - 6, RIG SERVICE - 0.5, DRLG 2054' - 3766' (122 FPH) BOTH PUMPS @ 70 SPM
 576 GPM BIT 97 RPM PIPE 45 RPM 25 K ON BIT - 14

Peter's Point #12-25D-12-16 2/19/2011 06:00 - 2/20/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion

Time Log Summary

DRLG 3766' - 3798' (64 FPH) BOTH PUMPS @ 70 SPM
 576 GPM BIT 97 RPM PIPE 45 RPM 25 K ON BIT - 0.5, MUD MOTOR FAILED, CIRC FOR TRIP - 0.5, TOH TO CHANGE MUD MOTOR (HOLE GOOD) - 2,
 CHANGE MUD MOTOR & SCRIBE - 1.5, TIH TO DRLG (HOLE GOOD) - 2, DRLG 3798' - 4432' (140 FPH) BOTH PUMPS @ 70 SPM
 576 GPM BIT 97 RPM PIPE 45 RPM 25 K ON BIT - 4.5, RIG SERVICE - 0.5, DRLG 4432' - 5280' (94 FPH) BOTH PUMPS @ 70 SPM
 576 GPM BIT 97 RPM PIPE 45 RPM 25 K ON BIT - 9, RIG REPAIR - EDS NOT WORKING TROUBLE SHOOT - 3.5

Peter's Point #12-25D-12-16 2/20/2011 06:00 - 2/21/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion

Time Log Summary

EDS NOT WORKING - WAIT ON TECH TO COME OUT OF TEXAS TO REPROGRAM PCL - 19.5, DRLG 5280' - 5668' (86 FPH) BOTH PUMPS @ 70 SPM
 576 GPM BIT 97 RPM PIPE 45 RPM 30 K ON BIT - 4.5

Peter's Point #12-25D-12-16 2/21/2011 06:00 - 2/22/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion

Time Log Summary

DRLG 8 3/4" HOLE FROM 5668' TO 6333' - 7, TRIP OUT OF HOLE FOR BIT - TIGHT SPOTS FROM 6333' THROUGH TO 1825' - 3.5, CHANGE BITS &
 SURFACE TEST MOTOR - OK - WELL STATIC - FUNCTION BLIND & PIPE RAMS - 0.5, TRIP INTO HOLE - LOST 45 BBLs. OF MD ON TRIP - 2, DRLG 7 7/8"
 HOLE FROM 6333' TO 7079' - 11

Peter's Point #12-25D-12-16 2/22/2011 06:00 - 2/23/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion

Time Log Summary

DRLG 7 7/8" HOLE FROM 7079' TO 7257' - 2.5, CIRC & COND. HOLE - 1.5, SHORT TRIP 20 STANDS - CLEAN TRIP - 1.5, CIRC & COND. HOLE - 1.5, TRIP
 OUT OF HOLE - WELL STATIC - 3, LAY DOWN BATTERIES & MOTOR - FUNCTION BLIND & PIPE RAMS - 1, PULL WEAR RING - 0.5, RIG UP & HELD
 SAFETY MEETING - RUN TRIPLE COMBO LOGS TO 7250' - 6, RIG UP WEATHERFORD & START TO RUN CASING - 6

Peter's Point #12-25D-12-16 2/23/2011 06:00 - 2/24/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion

Time Log Summary

RAN 168 JTS. OF 4.5" - 11.60# - P 110 - LT&C - CASING TO 7257' - TAGGED UP @ 7250' & WASHED TO BOTTOM - FILLED PIPE @ 1020' , 3758' , 5514' &
 7250' - MARKERS @ 6619' & 4478' - RAN CENTRALIZER'S EVERY 130' FROM 7232' THROUGH TO 3538' - 1.5, CIRC @ 100 SPM @ 430 GPM - WAITING
 ON HALCO TO ARRIVE , WAS DUE ON LOCATION @ 8:00 AM - FIRST BULK TRUCK & PUMP TRUCK ON LOCATION BY 3:31 PM - SECOND BULK TRUCK
 ON LOCATION BY 4:30 PM - 10, HELD SAFETY MEETING - PSI TEST TO 5000 PSI - PUMP 5 BBLs. H 2/0 - 40 BBL. SUPERFLUSH - 10 BBLs. H 2/0 - PUMP
 136 BBLs. OF LEAD HALCHEM @ 12.5 PPG - 1.91 YIELD - 10.31 GAL/SK @ 400 SK CEMENT - PUMP 273 BBLs OF TAIL POZ PREMIUM 50/50 @ 13.4 PPG
 - 1.46 YIELD - 6.92 GAL/SK @ 1050 SK CEMENT - SHUT DOWN & DROP PLUG - WASH LINES - DISPLACE @ 112 BBLs CLAYFIX @ 112 BBLs. @ 1000 PSI
 - BUMP PLUG @ 2773 PSI - FLOATS HELD - RELEASE PSI & RIG DOWN - GOOD RETURNS THROUGHOUT JOB & NO CEMENT BACK TO SURFACE - 3,
 NIPPLE DOWN & SET SLIPS @ 171K - HUNG CASING @ 7254' - RELEASED RIG @ 9:00 PM - 2/23/11 - 0.5

T12S R16E S-25 43-007-50029

From: Pat313 <pat313@billbarrettcorp.com>
To: "waltonwillis@yahoo.com" <waltonwillis@yahoo.com>, "walton_willis@blm.go...
Date: 2/16/2011 5:58 PM
Subject: BOP TEST

ON PATTERSON #313 FOR BILL BARRETT CO.
PETERS POINT SW 25 PAD
WE WILL BE TESTING BOPs ON PETERS POINT UNIT FEDERAL 12-25D-12-16
API# 43-007-50029-0000 EARLY MORNING 2/18/11
IF ANY QUESTIONS OR CONCERNS PLEASE CALL
THANK YOU

BILL BARRETT CO.
PATTERSON #313
303-353-5394

RECEIVED
FEB 16 2011
DIV. OF OIL, GAS & MINING

T125R16E S-25 API # 43-007-50029

From: Pat313 <pat313@billbarrettcorp.com>
To: "waltonwillis@yahoo.com" <waltonwillis@yahoo.com>, "walton_willis@blm.go...
Date: 2/22/2011 9:54 AM
Subject: PATTERSON RIG # 313

BILL BARRETT CO.
PATTERSON #313
303-353-5394

LADIES & GENTLEMEN
WE'RE APPROX. 24 HRS. FROM RUNNING CASING & 30 HRS. FROM CEMENTING THE PETER'S
POINT # 12-25D-12-16 WELL WITH PATTERSON RIG # 313.
API # 43-~~00~~7-50029-00-X1
TOTAL DEPTH OF 7257' WITH 9.6 PPG MUD WT & 45 BBLs MUD LOSS TOTAL.
ANY QUESTIONS OR CONCERNS E-MAIL OR CALL ME AT ABOVE PHONE #.
THANKS : ROBERT

RECEIVED

FEB 22 2011

DIV. OF OIL, GAS & MINING


Peter's Point #12-25D-12-16 3/15/2011 06:00 - 3/16/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
Set in prod. equip - 4, MI Cameron well head cut off casing set tubing head and tree. - 2						

Peter's Point #12-25D-12-16 3/21/2011 06:00 - 3/22/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
WAITING ON FRAC TREE - 3, INSTALL FRAC MANDREL, TEST TO 5K, INSTALL FRAC TREE - 2, WAITING ON W/L - 19						

Peter's Point #12-25D-12-16 3/22/2011 06:00 - 3/23/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
WAITING ON W/L - 3.25, RIH W/ 3.63" GAUGE RING / JUNK BASKET TO 6987'. FLOAT COLLAR @ 7208'. 221' HIGH. - 1, WAITING ON W/L - 7.5, RIH W/ CBL TOOLS TO 7050'. 158' ABOVE FLOAT COLLAR. LOG TO SURFACE. VERY GOOD BOND 7050' TO 4010'. FAIR BOND 4010' TO 2300'. POOR BOND TO 820'. - 2.75, SHUT IN - 9.5						

Peter's Point #12-25D-12-16 3/26/2011 06:00 - 3/27/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
SHUT IN - 10.25, LOAD CSG, TEST TO 8500 PSI. TEST GOOD - 0.75, RIG UP FLOW BACK - 13						

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9	
SUNDRY NOTICES AND REPORTS ON WELLS		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0681	
Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:	
1. TYPE OF WELL Gas Well		7. UNIT or CA AGREEMENT NAME: PETERS POINT	
2. NAME OF OPERATOR: BILL BARRETT CORP		8. WELL NAME and NUMBER: PETERS POINT U FED 12-25D-12-16	
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202		9. API NUMBER: 43007500290000	
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2414 FSL 1290 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 12.0S Range: 16.0E Meridian: S		9. FIELD and POOL or WILDCAT: UNDESIGNATED	
		COUNTY: CARBON	
		STATE: UTAH	
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA			
TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input checked="" type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 50px;" type="text"/>
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.			
This sundry is to report that this well had first gas sales on 4/5/2011 at 1:30pm.			
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY			
NAME (PLEASE PRINT) Brady Riley		PHONE NUMBER 303 312-8115	
SIGNATURE N/A		TITLE Permit Analyst	
		DATE 4/6/2011	


Peter's Point #12-25D-12-16 4/1/2011 06:00 - 4/2/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
<p>SICP: 250 Cathedral flow iron leaking back to well. Flow back crew did not try to isolate pressure problem. - 5.5, Cutters EL stage 2. Rebuild perf gun with 2 ft. gun to pickup upper interval of stage 1 @ 7032-7034. PU 12 ft.perf guns RIH correlate to short jt. run to perf depth check depth to casing collar. Perforate @ 7032-7034, 6968-6970, 6960-6964, 6949-6951 & 6915-6917. 3 SPF, 120 phasing, 23 gram charge. .350 holes. POOH turn well over to frac. - 1, Safety Meeting. Frac, Wire line. Flow back. CO2., Pressure lines. - 0.25, HES frac stage 2 Price River 70Q foam frac. designed frac for top interval of stage 1 added 10% to frac. Load & Break @4,022 PSI @ 5 BPM. Avg. Wellhead Rate: 28.8 BPM. Avg. Slurry Rate: 11.7 BPM.Avg. Pressure:5789 PSI. Max. Wellhead Rate: 29.3 BPM. Max. Slurry Rate:13 BPM. Max CO2 Rate: 18.5 BPM. Max. Pressure: 6137 PSI. Total Fluid Pumped; 14,428 Gal. Total Sand in Formation: 55,500 lb.(20/40 White) Linde CO2 Downhole;78 tons. CO2 Cooldown: 4 tons. ISIP:3,800 PSI. Frac Gradient: 0.99 psi/ft. No problems with frac. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal. fluid cap. (((Cathedral flow back employs walked by flow tanks with fluid running over take top made no attempt to fix problem overflowing. found day supervisor sleeping in office shack))). - 1.25, Cutters EL stage 3 Pricr River. PU HES CFP with 10 ft. perf guns. RIH correlate to sghort jt. run to setting depth set CFP @ ft. PU. Perforate @ 6699-6703, 6664-6666, 6632-6634 & 6577-6579, 3 SPF, 120 phasing, 23 gram charge, .350 holes. POOH turn well over to frac. - 1, HES frac stage 3 Price Ricer 70Q foam frac. Load & Break @ 4111 PSI @ 15 BPM. Avg. Wellhead Rate: 33.5 BPM. Avg. Slurry Rate:13.5 BPM. Avg. CO2 Rate: 18.5 BPM. Avg. Pressure:6,190 PSI. Max. Wellhead Rate: 34.8 BPM. Max. Slurry Rate:15.9 BPM. Max. CO2 Rate:22.8 BPM. Max. Pressure: 6515 PSI. Total Fluid Pumped: 19,857 gal. Total Sand in Formation: 88,000 lb.(20/40 White) Praxair: CO2 Downhole; 121 tons. CO2 Cooldown: 6 tons. ISIP: 3,662 PSI. Frac Gradient: 0.99 psi/ft. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal. fluid cap. - 1, Cutters EL stage 4 Dark Canyon. PU HES CFP with 10 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ ft. PU. Perforate @ 6524-6526, 6512-6514, 6502,6504, 6486-6488 & 6466-6468, 3 SPF, 120 phasing, 23 gram charge, .350 holes. POOH turn well ove to frac. - 1, HES frac stage 4 Dark Canyon 70Q foam frac. Load & Break @4234 PSI @ 15.2 BPM. Avg. Wellhead Rate:38.3 BPM. Avg. Slurry Rate:15.5 BPM. Avg. CO2 Rate: 21.1 BPM. Avg. Pressure: 6936 PSI. Max. Wellhead Rate: 39.6 BPM. Max. Slurry Rate: 18.3 BPM.Max. CO2 Rate: 25.1 BPM. Max. Pressure: 7256 PSI. Total Fluid Pumped: 21,318 gal. Total Sand in Formation: 98,100 lb.(20/40 White) Linde CO2 Downhole: 129 tons. CO2 Cooldown: 6 tons. ISIP: 3,851 PSI. Frac Gradient: 1.00 psi/ft. No problems with frac. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal. fluid cap. - 1, Cutters EL stage 5 Dark Canyon. PU HES CFP with 12 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ ft. PU. Pressure up casing. Perforate @ 6390-6392, 6377-6379, 6360-6362, 6346-6348, 6335-6337 & 6327-6329, 3 SPF, 120 phasing, 23 gram charge, .350 holes. Stuck perf guns baker seting tool setting sleeve. CCL & cable head at 6224.5 ft. to 6254 ft. 3 1/8" tools. Pumped 4 BPM around tools trying to work free. Flowed well back through HES bleed off iron working tools. had no success. Worked tools 2 hours before pulling out of cable head. POOH with EL. - 3, Rig down move crane , Rig up crane to pickup Cutters fishen tools with Cutters braided wire line truck. - 1.5, SIFN - 7.5</p>						

Peter's Point #12-25D-12-16 4/2/2011 06:00 - 4/3/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
<p>SICP: 1500. Monitor cellar for Ox. H2S. - 7, MIRU Cutters Breided line truck. PU 70 ft. lub. over shot jars weight bars. RIH tag fish @ 6324.5 fish fail to 6427 ft. RIH tag picked up had tools POOH SI. bleed off lub. lay down setting tool. perf guns CCL & fishen tools. (Sand on perf guns) lay down lub. PU Lub / BOP with EL. - 4.25, Safety meet , frac, flow back. CO2. Wire line work. Pressure lines. flowing of wells. - 0.25, HES frac stage 5 Dark Canyon 70Q foam frac. Load & Break @3375 PSI @ 15 BPM. Avg. Wellhead Rate: 38.3 BPM.Avg. Slurry Rate: 15.4 BPM. Avg. CO2 Rate: 21.2 BPM. Avg. Pressure; 6537 PSI. Max. Wellhead Rate: 40 BPM. Max. Slurry Rate:18.2 BPM. Max. CO2 Rate:25.2 BPM. Max. Pressure: 7,061 PSI. Total Fluid Pumped: 28,277 Gal. Total Sand in Formation:140,100 lb.(20/40 White) Praxair CO2 Downhole; 182 tons. CO2 Cooldown: 6 tons.ISIP:4,017 PSI. Frac Gradient: 1.07 psi/ft. No frac problems. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal. fluid cap., - 1, Cutters EL stage 6 North Horn. PU HES CFP with 10 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 6250 ft. PU. Pressure up casing. Perforate @ 6199-6207 & 6145-6147, 3 SPF, 120 phasing, 23 gram charge. .350 holes. POOH turn well over to frac. - 1, HES frac stage 6 North Horn 60Q foam frac. Load & Break @ 4834 PSI @ 14.9 BPM. Avg. Wellhead Rate: 29 BPM. Avg. Slurry Rate 13.9 BPM. Avg. CO2 Rate:13.8 BPM. Avg Pressure: 6051 PSI. Max Wellhead Rate: 30.2 BPM. Max. Slurry Rate: 16.7 BPM. Max. CO2 Rate:18 BPM. Max. Pressure: 6,450 PSI. Total Fluid Pumped: 19,418 gal. Total Sand in Formation: 67,900 lb.(20/40 White) Praxair CO2 Downhole: 85 tons. CO2 Cooldown: 6 tons. ISIP:3,587 PSI. Frac Gradient: 1.02 psi/ft. No frac problems. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal. fluid cap. - 1, Cutters EL stage 7 North Horn. PU HES CFP with 10 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 6120 ft. PU. Pressure up casing. Perforate @ 6086-6090 &6049-6055, 3 SPF, 120 phasing, 23 gram charge. .350 holes. POOH turn well over to frac. - 1, HES frac stage 7 North Horn 60Q foam frac. Load & Break @ 3630 PSI @ 15.2 BPM. Avg. Wellhead Rate: 29 BPM. Avg. Slurry Rate: 13.8 BPM. Avg. CO2 Rate:13.8 BPM. Avg. Pressure: 5592 PSI. Max. Wellhead Rate: 30.5 BPM. Max. Slurry Rate: 16.6 BPM. Max. CO2 Rate: 18.2 BPM. Max. Pressure: 6011 PSI. Total Fluid Pumped: 18,229 gal. Total sand in Formation: 60,000 lb.(20/40 White) Linde CO2 Downhole; 76 tons. CO2 Cooldown:4 tons. ISIP:3,837 PSI. Frac Gradient: 1.07 psi/ft. No problems with frac. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal. fluid cap. - 0.8, Cutters EI stage 8 North Horn PU HES CFP with 10 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 5600 ft. PU Perforate @ 5552-5557 & 5501-5506, 3 SPF, 120 phasing, 23 gram charge. .350 holes. POOH turn well over to frac. - 0.8, HES frac stage 8 North Horn 60Q foam frac. Load & Break @ 3162 PSI @ 15 BPM. Avg Wellhead Rate: 33.8 BPM. Avg. Slurry Rate: 16.3 BPM. Avg. CO2 Rate:15.9 BPM. Avg. Pressure:5333 PSI. Max. Wellhead Rate: 19.4 BPM. Max. Slurry Rate: 21 BPM. Max. CO2 Rate: 21 BPM. Max. Pressure: 5573 PSI. Total Fluid Pumped:21,332 gal. Total Sand in Formation: 76,200 lb.(20/40 White) Linde CO2 Downhole; 92 tons. CO2 Cooldown: 5 tons. ISIP:3,540 PSI. Frac Gradient: 1.08 psi/ft. No frac problems. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal. fluid cap. - 0.9, SIFN monitor psi over night. - 6</p>						



Peter's Point #12-25D-12-16 4/3/2011 06:00 - 4/4/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
SICP: 1900 - 5.5, Cutters EL stage 9 North Horn. PU HES CFP with 10 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 5380 ft. PU. Pressure up casing. Perforate @ 5301-5303, 5181-5186 & 5096-5100, 3 SPF, 120 phasing, 23 gram charge. .350 holes. POOH turn well over to frac. - 1, Safety Meet. Frac's, CO2, Flow back. Cellar. Shut down. Rig down & moving equip. Pressure lines. Monitor for LELs. - 0.25, HES frac stage 9 North Horn 60Q foam frac. Load & Break @ 3,719 PSI @ 15 BPM. Avg. Wellhead Rate: 28.9 BPM. Avg Slurry Rate: 14 BPM. Avg. CO2 Rate: 13.4 BPM. Avg. Pressure: 5033 PSI. Max. Wellhead Rate:30 BPM. Max. Slurry Rate: 16.6 BPM. Max. CO2 Rate: 17.9 BPM. Max. Pressure: 5308 PSI. Total Fluid Pumped: 14,478 gal. Total Sand in Formation: 45,000 lb. (20/40 White) Linde CO2 Downhole:57 tons. CO2 Cooldown: 4 tons. ISIP:3,547 PSI. Frac Gradient: 1.12 psi/ft. No frac problems. Slow start in frac van computers. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal.fluid cap. - 1.5, Cutters EL stage 10 North Horn. PU HES CFP with 10 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 5040 ft. PU.Pressure up casing. Perforate @ 4981-4985, 4973-4977& 4949-4951. 3 SPF, 120 phasing, 23 gram charge. .350 holes. POOH turn well over to frac. - 0.8, HES frac stage 10 North Horn 60Q foam frac. Load & Break @3,366 PSI @ 14.9 BPM. Avg. Wellhead Rate: 24.1 BPM. Avg. Slurry Rate:11.6 BPM. Avg. CO2 Rate:11.2 BPM. Avg. Pressure: 4153 PSI. Max. Wellhead Rate:25.3 BPM. Max. Slurry Rate:13.9 BPM. Max CO2 Rate:14.9 BPM. Max. Pressure: 4,413 PSI. Total Fluid Pumped: 14,279 gal. Total Sand in Formation: 43,900 lb.(20/40 White) Praxair CO2 Downhole: 57 tons. CO2 Cooldown: 4 tons. ISIP: 3,193 PSI. Frac Gradient: 1.08 psi/ft. No frac problems. Successfully flushed wellbore with 50Q foam 50 bbl over flush with 500 gal. fluid cap. - 0.8, Cutters EL stage 11 North Horn. PU HES CFP with 10 ft. perf guns. RIH correlate to short jt. run to setting depth set CFP @ 4550 ft. PU. Pressure up. Perforate @ 4476-4481 & 4464-4469. 3 SPF, 120 phasing, 23 gram charge. .350 holes. POOH turn well over to frac. - 0.75, HES frac stage 11 North horn 60Q foam frac. Load & Break @ 3036 PSI @ 15 BPM. Avg. Wellhead Rate: 21.1 BPM. Avg. Slurry Rate: 10.2 BPM. Avg. CO2 Rate: 9.7 BPM. Avg. Pressure: 3,550 PSI. Max Wellhead Rate: 22.1 BPM. Max. Slurry Rate: 12.3 BPM. Max. CO2 Rate: 13.6 BPM. Max. Pressure: 3,755 PSI. Total Fluid Pumped; 11,582 gal. Total Sand in Formation: 38,000 lb.(20/40 White) Linde CO2 Downhole; 45 tons. CO2 Cooldown: 4 tons. ISIP:2,837 PSI. Frac Gradient: 1.07 npsi/ft. No frac problems. Successfully flushed wellbore with 50Q foam 10 bbl over flush with 500 gal. fl;uid cap - 0.8, SI. Rig HES & Cutters off well. move to 11-25D - 2, Start flow back through Cathedral flow equipment. Total Fluid to recover 4363 bbls. - 0						

Peter's Point #12-25D-12-16 4/4/2011 06:00 - 4/5/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
Flow stages 1-11 FCP: 1080 on 48 ck. recovered 615 bbl in 17 hours avg of 36.17 BPH CO2: 38%. H2S: 6 ppm. 3748 bbl left to recover. - 6, Flow back stages 1-11 CO2: 17% at 6:30PM - 18						

Peter's Point #12-25D-12-16 4/5/2011 06:00 - 4/6/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
Flow back stages 1-11 through Cathedral flow equipment. FCP: 1050 psi on 48 ck. recovered 141 bbl in 24 hours. avg. of 5.87 BPH. CO2: 16%. H2S: 3 ppm. Gas rate of 5.321MMCFD. Total Fluid left to recover 3607 bbl. - 6, Flow back stages - 6, Turn well over to production . 24 ck. 1120 psi 6.200 MMCFD - 12						

Peter's Point #12-25D-12-16 4/11/2011 06:00 - 4/12/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion
Time Log Summary						
FLOWING TO SALES - 9.25, RIG CTS 2" COIL TBG OVER F/ 9-26D - 0.5, TEST LUB TO 5000 PSI. RIH W/ FOLLOWING 5 BLADE MILL 3.75" X 1.25" X .95' MUD MOTOR 2.875" X 12.75' CIRCULATING SUB 2.875 X 1.33' DISCONNECT 2.875" X .50" X 3.12' BI-DIRECTIONAL JAR 2.875" X 1" X 4.52' COIL TBG CONNECTOR 2.87" X 2" X .69' PUMP 1.0 BPM & 500 SCF - 0.5, INCREASE FLUID TO 2.00 BPM & 1000 SCFM. TAG PLUG #1 @ 4550', DRILL PLUG IN 14 MIN, PUMP 10 BBL SWIPE. 300# CP TAG PLUG #2 @ 5040', DRILL PLUG IN 14 MIN, PUMP 10 BBL SWEEP. 350# CP TAG PLUG #3 @ 5380', DRILL PLUG IN 15 MIN, PUMP 10 BBL SWEEP. 325# CP TAG PLUG #4 @ 5600', DRILL PLUG IN 18 MIN, PUMP 10 BBL SWEEP. 275# CP TAG PLUG #5 @ 6120', DRILL PLUG IN 24 MIN, PUMP 10 BBL SWEEP. 225# CP TAG PLUG #6 @ 6250', DRILL PLUG IN 16 MIN, PUMP 10 BBL SWEEP. 500# CP TAG PLUG #7 @ 6450', DRILL PLUG IN 25 MIN, PUMP 10 BBL SWEEP. 450# CP TAG PLUG #8 @ 6550', DRILL PLUG IN 33 MIN, PUMP 10 BBL SWEEP. 450# CP TAG PLUG #9 @ 6750', DRILL PLUG IN 10 MIN, PUMP 10 BBL SWEEP. 500# CP TAG PBTD @ 7200', BOTTOM PERF @ 7034'. FC @ 7208'. CIR ON BOTTOM F/ 1 HR. VERY STICKY 7030' TO 7200' POOH JETTING @ 1BBL & 1000 SCF / MIN - 8.5, LAY DOWN TOOLS. BLOW COIL DRY. RIG DOWN TO MOVE - 1.5, FLOW TO FLARE F/ 1 HR. TURN TO SALES - 3.75						


Peter's Point #12-25D-12-16 4/17/2011 06:00 - 4/18/2011 06:00

API/UWI	State/Province	County	Field Name	Well Status	Total Depth (ftKB)	Primary Job Type
43-007-50029			West Tavaputs		7,257.0	Drilling & Completion

Time Log Summary

FLOW TO SALES - 4.25, RIG UP PIONEER W/L & PROTECHNICS - 0.75, HOLD SAFETY MEETING - 0.25, RIH W/ 2" GAUGE RING / JUNK BASKET TO 7215' WLM. FC @ 7208', CLEANED OUT TO 7200' W/ COIL. POOH. PICK UP PROTECHNICS LOGGING TOOLS. LOG WELL. - 5, RIG DOWN W/L. DOWN LOAD LOGGING TOOLS. GOOD LOG. - 0.5, FLOW TO SALES - 13.25

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
UTU0681

1a. Type of Well Oil Well Gas Well Dry Other
b. Type of Completion New Well Work Over Deepen Plug Back Diff. Resvr.
Other _____

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.
UTU63014

2. Name of Operator **BILL BARRETT CORPORATION** Contact: BRADY RILEY
E-Mail: briley@billbarrettcorp.com

8. Lease Name and Well No.
PETERS POINT UNIT FEDERAL 12-25D-12-38 **16**

3. Address 1099 18TH STREET SUITE 2300
DENVER, CO 80202

3a. Phone No. (include area code)
Ph: 303-312-8115

9. API Well No.
43-007-50029

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

At surface NWSW 2414FSL 1290FWL

At top prod interval reported below NWSW 1988FSL 726FWL

At total depth NWSW 1923FSL 679FWL

10. Field and Pool, or Exploratory
PETERS POINT

11. Sec., T., R., M., or Block and Survey
or Area Sec 25 T12S R16E Mer SLB

12. County or Parish
CARBON

13. State
UT

14. Date Spudded
11/05/2010

15. Date T.D. Reached
02/22/2011

16. Date Completed
 D & A Ready to Prod.
04/04/2011

17. Elevations (DF, KB, RT, GL)*
6708 GL

18. Total Depth. MD 7258
TVD 7171

19. Plug Back T.D.: MD 7209
TVD 7122

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
 TRIPLE COMBO, CBL

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit analysis)
Directional Survey? No Yes (Submit analysis)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
24.000	14.000 COND		0	80	80			0	
12.250	9.625 J55	36.0	0	1007	1007	170	60	0	
7.875	4.500 P110	11.6	0	7258	7254	400	136	815	15000

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)

25. Producing Intervals

26. Perforation Record

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) WASATCH	4464	6329	4464 TO 6329	0.350	186	OPEN
B) MESAVERDE	6335	7034	6335 TO 7034	0.350	126	OPEN
C)						
D)						

27. Acid, Fracture, Treatment, Cement Squeeze, Etc.

Depth Interval	Amount and Type of Material
4464 TO 6329	WASATCH - SEE STAGES 6-10
6335 TO 7034	MESAVERDE - SEE STAGES 1-5

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr API	Gas Gravity	Production Method
04/05/2011	04/06/2011	24	→	0.0	4343.0	85.0	0.0	0.00	FLOWS FROM WELL
Choke Size	Top Press Flwg SI	Csg Press	24 Hr Rate	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	
25/64	SI	1133.0	→	0	4343	85	0	PGW	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr API	Gas Gravity	Production Method
			→						
Choke Size	Top Press Flwg SI	Csg Press	24 Hr Rate	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	
	SI		→						

RECEIVED
MAY 03 2011

(See Instructions and spaces for additional data on reverse side)

ELECTRONIC SUBMISSION #107392 VERIFIED BY THE BLM WELL INFORMATION SYSTEM

DIV. OF OIL, GAS & MINING

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **

Peter's Point Unit Federal #12-25D-12-16 Report Continued*

44. ACID, FRACTURE, TREATMENT, CEMENT SQUEEZE, ETC. (cont.)		
AMOUNT AND TYPE OF MATERIAL		
<u>Stage</u>	<u>Bbls Slurry</u>	<u>20/40 lbs White Sand</u>
1	403	55,500
2	568	88,000
3	613	98,100
4	824	140,100
5	536	67,900
6	499	60,000
7	590	76,200
8	393	45,000
9	387	43,900
10	317	38,000

*Depth intervals for frac information same as perforation record intervals.

RECEIVED
MAY 03 2011
DIV. OF OIL, GAS & MINING



Bill Barrett Corporation

Bill Barrett Corp.

Carbon County, UT [NAD27]
Peter's Point N2 SW 25 Pad
Peter's Point UF 12-25D-12-16

Wellbore #1

Survey: Surveys

Standard Survey Report

22 February, 2011

RECEIVED

MAY 03 2011

DIV. OF OIL, GAS & MINING






WELL DETAILS: Peter's Point UF 12-25D-12-16

US State Plane 1927 (Exact solution) , Utah Central 4302 , NAD 1927 (NADCON CONUS)

Ground Level: 6708.00

+N/-S	+E/-W	Northing	Easting	Latitude	Longitude
0.00	0.00	517049.11	2400132.64	39° 44' 39.04 N	110° 4' 36.90 W

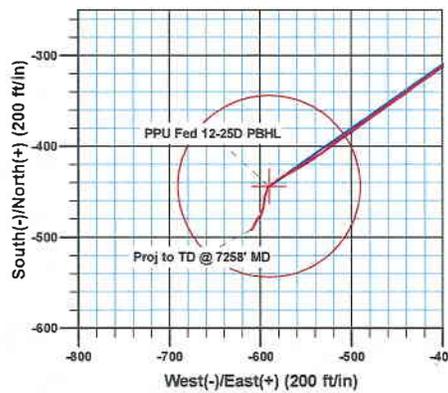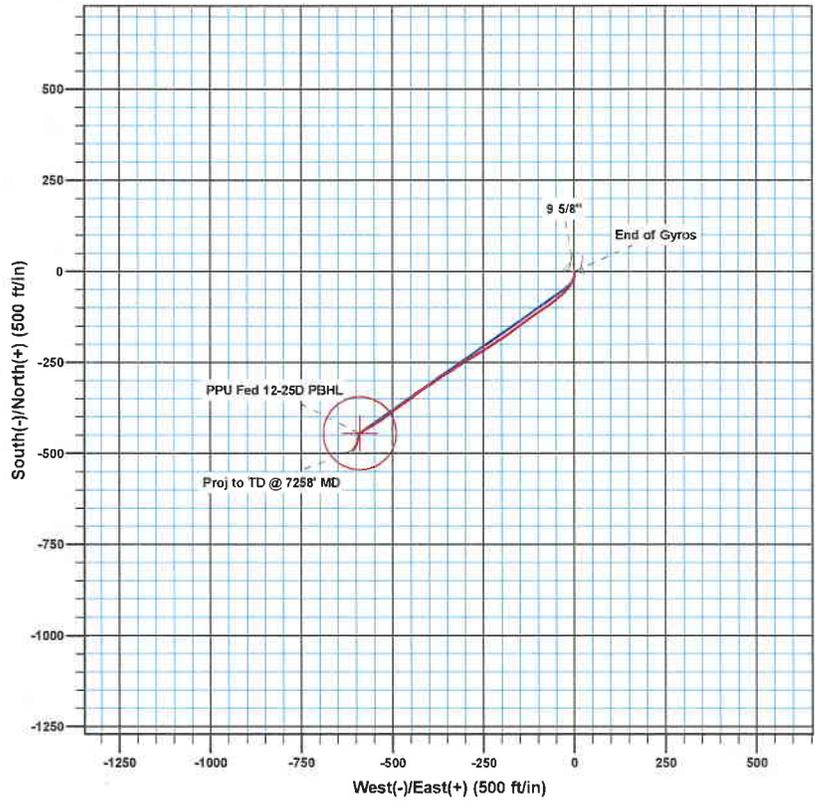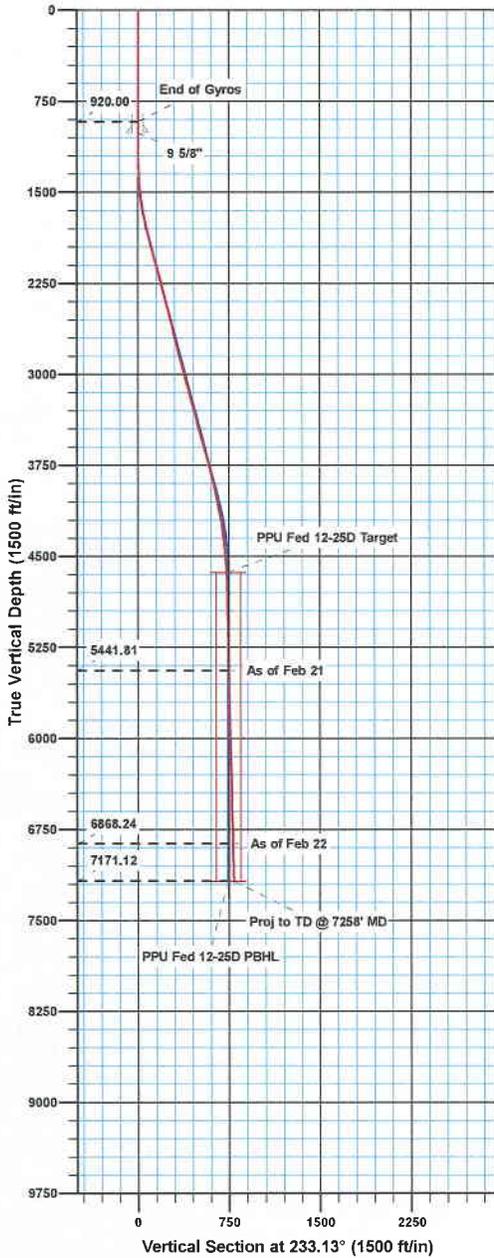

Azimuths to True North
Magnetic North: 11.30°

Magnetic Field
Strength: 52166.7snT
Dip Angle: 65.56°
Date: 02/03/2011
Model: IGRF200510

ANNOTATIONS

TVD	MD	Inc	Azi	+N/-S	+E/-W	VSect	Departure	Annotation
5441.81	5528.00	1.700	201.10	-447.76	-593.65	743.58	754.53	As of Feb 21
6868.24	6955.00	1.600	210.30	-483.86	-606.23	775.30	793.78	As of Feb 22
7171.12	7258.00	1.400	210.20	-491.38	-610.51	783.24	802.44	Proj to TD @ 7258' MD





Company: Bill Barrett Corp.
 Project: Carbon County, UT [NAD27]
 Site: Peter's Point N2 SW 25 Pad
 Well: Peter's Point UF 12-25D-12-16
 Wellbore: Wellbore #1
 Design: Wellbore #1

Local Co-ordinate Reference: Well Peter's Point UF 12-25D-12-16
 TVD Reference: GL @ 6708.00ft
 MD Reference: GL @ 6708.00ft
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Database: Compass VM

Project	Carbon County, UT [NAD27]		
Map System:	US State Plane 1927 (Exact solution)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	Utah Central 4302		Using geodetic scale factor

Site	Peter's Point N2 SW 25 Pad		
Site Position:		Northing:	517,043.78 usft
From:	Lat/Long	Easting:	2,400,117.26 usft
Position Uncertainty:	0.00 ft	Slot Radius:	1.10 ft
		Latitude:	39° 44' 38.99 N
		Longitude:	110° 4' 37.10 W
		Grid Convergence:	0.91 °

Well	Peter's Point UF 12-25D-12-16		
Well Position	+N/-S	0.00 ft	Northing:
	+E/-W	0.00 ft	Easting:
Position Uncertainty	0.00 ft	Wellhead Elevation:	ft
		Latitude:	39° 44' 39.04 N
		Longitude:	110° 4' 36.90 W
		Ground Level:	6,708.00 ft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination	Dip Angle	Field Strength
	IGRF200510	02/03/11	(°)	(°)	(nT)
			11.30	65.56	52,167

Design	Wellbore #1				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W	Direction	
	(ft)	(ft)	(ft)	(°)	
	0.00	0.00	0.00	233.13	

Survey Program	Date	02/22/11			
From	To	Survey (Wellbore)	Tool Name	Description	
(ft)	(ft)				
100.00	920.00	Gyro Surveys (Wellbore #1)	MWD	MWD - Standard	
1,153.00	7,258.00	Surveys (Wellbore #1)	MWD	MWD - Standard	

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
920.00	0.200	274.55	920.00	0.46	0.21	-0.44	0.00	0.00	0.00
1,007.40	0.103	192.98	1,007.40	0.40	0.04	-0.27	0.24	-0.11	-93.33
9 5/8"									
1,153.00	0.400	137.50	1,153.00	-0.11	0.35	-0.22	0.24	0.20	-38.11
1,249.00	1.700	186.70	1,248.98	-1.77	0.41	0.73	1.53	1.35	51.25
1,344.00	3.500	192.90	1,343.88	-6.00	-0.40	3.92	1.91	1.89	6.53
1,439.00	5.600	198.90	1,438.57	-13.21	-2.55	9.96	2.26	2.21	6.32
1,534.00	8.400	203.00	1,532.86	-23.98	-6.76	19.80	2.99	2.95	4.32
1,629.00	10.200	212.80	1,626.61	-37.44	-14.03	33.69	2.52	1.89	10.32
1,724.00	12.200	221.60	1,719.80	-52.02	-25.25	51.42	2.76	2.11	9.26



Sharewell
Survey Report



Company: Bill Barrett Corp.
 Project: Carbon County, UT [NAD27]
 Site: Peter's Point N2 SW 25 Pad
 Well: Peter's Point UF 12-25D-12-16
 Wellbore: Wellbore #1
 Design: Wellbore #1

Local Co-ordinate Reference: Well Peter's Point UF 12-25D-12-16
 TVD Reference: GL @ 6708.00ft
 MD Reference: GL @ 6708.00ft
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Database: Compass VM

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N-S (ft)	+E-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
1,819.00	14.200	231.60	1,812.30	-66.77	-41.05	72.90	3.19	2.11	10.53
1,914.00	14.200	230.70	1,904.40	-81.39	-59.20	96.19	0.23	0.00	-0.95
2,009.00	15.200	236.80	1,996.29	-95.59	-78.64	120.27	1.94	1.05	6.42
2,104.00	14.900	235.50	2,088.03	-109.33	-99.13	144.90	0.48	-0.32	-1.37
2,200.00	14.700	235.10	2,180.85	-123.29	-119.29	169.40	0.23	-0.21	-0.42
2,295.00	14.500	234.20	2,272.78	-137.14	-138.82	193.34	0.32	-0.21	-0.95
2,390.00	14.800	232.90	2,364.69	-151.41	-158.15	217.37	0.47	0.32	-1.37
2,485.00	14.500	234.50	2,456.61	-165.64	-177.51	241.39	0.53	-0.32	1.68
2,580.00	14.400	236.00	2,548.60	-179.15	-196.98	265.08	0.41	-0.11	1.58
2,675.00	13.400	235.40	2,640.82	-192.01	-215.84	287.87	1.06	-1.05	-0.63
2,770.00	13.400	237.50	2,733.23	-204.17	-234.18	309.85	0.51	0.00	2.21
2,865.00	14.500	237.40	2,825.43	-216.50	-253.49	332.69	1.16	1.16	-0.11
2,960.00	15.700	238.60	2,917.15	-229.60	-274.48	357.34	1.31	1.26	1.26
3,056.00	15.300	237.80	3,009.65	-243.12	-296.28	382.90	0.47	-0.42	-0.83
3,151.00	14.100	238.10	3,101.54	-255.91	-316.71	406.92	1.27	-1.26	0.32
3,246.00	15.600	236.30	3,193.37	-269.12	-337.16	431.20	1.65	1.58	-1.89
3,341.00	15.300	236.50	3,284.94	-283.12	-358.24	456.47	0.32	-0.32	0.21
3,436.00	14.200	236.40	3,376.80	-296.49	-378.40	480.61	1.16	-1.16	-0.11
3,531.00	15.600	235.30	3,468.61	-310.21	-398.61	505.01	1.50	1.47	-1.16
3,626.00	15.600	235.00	3,560.11	-324.81	-419.58	530.54	0.08	0.00	-0.32
3,721.00	14.700	232.90	3,651.81	-339.41	-439.65	555.37	1.11	-0.95	-2.21
3,816.00	15.300	235.50	3,743.57	-353.78	-459.60	579.94	0.95	0.63	2.74
3,911.00	13.600	234.50	3,835.56	-367.36	-479.02	603.63	1.81	-1.79	-1.05
4,007.00	12.700	234.40	3,929.04	-380.06	-496.79	625.47	0.94	-0.94	-0.10
4,102.00	11.900	233.40	4,021.86	-391.98	-513.15	645.70	0.87	-0.84	-1.05
4,197.00	11.000	232.60	4,114.97	-403.32	-528.21	664.56	0.96	-0.95	-0.84
4,292.00	8.900	239.50	4,208.54	-412.56	-541.74	680.93	2.54	-2.21	7.26
4,387.00	8.300	236.60	4,302.47	-420.06	-553.80	695.08	0.78	-0.63	-3.05
4,482.00	6.000	242.20	4,396.73	-426.16	-563.92	706.83	2.53	-2.42	5.89
4,577.00	3.700	241.00	4,491.38	-429.96	-570.99	714.77	2.42	-2.42	-1.26
4,673.00	3.300	239.10	4,587.20	-432.88	-576.07	720.58	0.43	-0.42	-1.98
4,768.00	3.100	239.60	4,682.05	-435.58	-580.63	725.86	0.21	-0.21	0.53
4,863.00	1.100	221.70	4,776.98	-437.56	-583.46	729.30	2.19	-2.11	-18.84
4,958.00	1.200	208.30	4,871.97	-439.12	-584.53	731.10	0.30	0.11	-14.11
5,053.00	1.100	248.10	4,966.95	-440.34	-585.85	732.88	0.83	-0.11	41.89
5,148.00	1.400	242.50	5,061.93	-441.21	-587.73	734.91	0.34	0.32	-5.89
5,243.00	1.200	242.00	5,156.90	-442.21	-589.63	737.04	0.21	-0.21	-0.53
5,338.00	1.100	225.10	5,251.88	-443.33	-591.16	738.92	0.37	-0.11	-17.79
5,433.00	1.700	208.40	5,346.85	-445.21	-592.48	741.11	0.76	0.63	-17.58
5,528.00	1.700	201.10	5,441.81	-447.76	-593.65	743.58	0.23	0.00	-7.68
5,623.00	1.500	198.50	5,536.78	-450.26	-594.55	745.80	0.22	-0.21	-2.74
5,718.00	1.200	202.30	5,631.75	-452.36	-595.33	747.68	0.33	-0.32	4.00
5,814.00	1.700	190.00	5,727.72	-454.69	-595.96	749.58	0.61	0.52	-12.81



Company: Bill Barrett Corp.
 Project: Carbon County, UT [NAD27]
 Site: Peter's Point N2 SW 25 Pad
 Well: Peter's Point UF 12-25D-12-16
 Wellbore: Wellbore #1
 Design: Wellbore #1

Local Co-ordinate Reference: Well Peter's Point UF 12-25D-12-16
 TVD Reference: GL @ 6708.00ft
 MD Reference: GL @ 6708.00ft
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Database: Compass VM

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
5,909.00	1.900	184.40	5,822.67	-457.65	-596.32	751.64	0.28	0.21	-5.89
6,004.00	1.800	191.10	5,917.62	-460.68	-596.73	753.79	0.25	-0.11	7.05
6,099.00	1.700	183.30	6,012.58	-463.55	-597.10	755.81	0.27	-0.11	-8.21
6,194.00	2.100	192.90	6,107.53	-466.66	-597.57	758.05	0.54	0.42	10.11
6,289.00	2.200	201.50	6,202.46	-470.05	-598.62	760.93	0.36	0.11	9.05
6,384.00	2.300	191.60	6,297.39	-473.61	-599.68	763.91	0.42	0.11	-10.42
6,479.00	1.000	229.80	6,392.35	-476.02	-600.69	766.16	1.72	-1.37	40.21
6,574.00	1.100	224.80	6,487.33	-477.20	-601.97	767.89	0.14	0.11	-5.26
6,670.00	1.100	228.70	6,583.31	-478.46	-603.31	769.72	0.08	0.00	4.06
6,765.00	1.100	203.20	6,678.30	-479.90	-604.35	771.42	0.51	0.00	-26.84
6,860.00	1.300	203.20	6,773.28	-481.73	-605.14	773.15	0.21	0.21	0.00
6,955.00	1.600	210.30	6,868.24	-483.86	-606.23	775.30	0.37	0.32	7.47
7,050.00	1.800	211.60	6,963.20	-486.28	-607.68	777.91	0.21	0.21	1.37
7,145.00	1.700	206.40	7,058.16	-488.81	-609.09	780.56	0.20	-0.11	-5.47
7,213.00	1.400	210.20	7,126.13	-490.43	-609.96	782.23	0.47	-0.44	5.59
7,258.00	1.400	210.20	7,171.12	-491.38	-610.51	783.24	0.00	0.00	0.00

Casing Points

Measured Depth (ft)	Vertical Depth (ft)	Name	Casing Diameter (ft)	Hole Diameter (ft)
1,007.40	1,007.40	9 5/8"	0.80	1.02

Survey Annotations

Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates		Comment
		+N/-S (ft)	+E/-W (ft)	
5,528.00	5,441.81	-447.76	-593.65	As of Feb 21
6,955.00	6,868.24	-483.86	-606.23	As of Feb 22
7,258.00	7,171.12	-491.38	-610.51	Proj to TD @ 7258' MD

Checked By: _____ Approved By: _____ Date: _____

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0681
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: PETERS POINT
1. TYPE OF WELL Gas Well	8. WELL NAME and NUMBER: PETERS POINT U FED 12-25D-12-16
2. NAME OF OPERATOR: BILL BARRETT CORP	9. API NUMBER: 43007500290000
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202	PHONE NUMBER: 303 312-8164 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2414 FSL 1290 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 12.0S Range: 16.0E Meridian: S	9. FIELD and POOL or WILDCAT: UNDESIGNATED COUNTY: CARBON STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 4/15/2012	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input checked="" type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 50px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

BBC is submitting this sundry to request an exception to BLM Onshore Order #7 and UDOGM R649-3-16-3, allowing the cuttings pit/trench on the Peters Point N2SW 25 pad to remain open past the allocated time. The pit will be closed after 4/15/2012, when the WTPs special protective measures for wildlife and high county watershed stipulations are lifted. The pit will be fenced on all four sides until closed. Please contact Brady Riley at 303-312-8115.

Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY

NAME (PLEASE PRINT) Brady Riley	PHONE NUMBER 303 312-8115	TITLE Permit Analyst
SIGNATURE N/A	DATE 12/2/2011	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0681
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: PETERS POINT
1. TYPE OF WELL Gas Well	8. WELL NAME and NUMBER: PETERS POINT U FED 12-25D-12-16
2. NAME OF OPERATOR: BILL BARRETT CORP	9. API NUMBER: 43007500290000
3. ADDRESS OF OPERATOR: 1099 18th Street Ste 2300 , Denver, CO, 80202	PHONE NUMBER: 303 312-8164 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2414 FSL 1290 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 12.0S Range: 16.0E Meridian: S	9. FIELD and POOL or WILDCAT: PETERS POINT COUNTY: CARBON STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: <input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 7/31/2012 <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input checked="" type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input checked="" type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text" value="pit closure"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The pit was closed on the above referenced well location on the Peters Point N/2SW 25 Pad, on 7/31/2012.

**Accepted by the
 Utah Division of
 Oil, Gas and Mining
 FOR RECORD ONLY
 August 07, 2012**

NAME (PLEASE PRINT) Brady Riley	PHONE NUMBER 303 312-8115	TITLE Permit Analyst
SIGNATURE N/A	DATE 8/3/2012	

Division of Oil, Gas and Mining
OPERATOR CHANGE WORKSHEET (for state use only)

ROUTING
 CDW

X - Change of Operator (Well Sold)

Operator Name Change/Merger

The operator of the well(s) listed below has changed, effective: 1/1/2014

FROM: (Old Operator): N2165-Bill Barrett Corporation 1099 18th Street, Suite 230 Denver, CO 80202 Phone: 1 (303) 312-8134	TO: (New Operator): N4040-EnerVest Operating, LLC 1001 Fannin Street, Suite 800 Houston, TX 77002 Phone: 1 (713) 659-3500
--------------------------------------------------------------------------------------------------------------------------------------------------	---------------------------------------------------------------------------------------------------------------------------------------------------

WELL NAME	SEC	TWN	RNG	API NO	ENTITY NO	LEASE TYPE	WELL TYPE	WELL STATUS
See Attached List								

OPERATOR CHANGES DOCUMENTATION

Enter date after each listed item is completed

- (R649-8-10) Sundry or legal documentation was received from the **FORMER** operator on: 1/7/2014
- (R649-8-10) Sundry or legal documentation was received from the **NEW** operator on: 1/7/2014
- The new company was checked on the **Department of Commerce, Division of Corporations Database** on: 1/28/2014
- a. Is the new operator registered in the State of Utah: Business Number: 8850806-0161
- 5a. (R649-9-2)Waste Management Plan has been received on: Not Yet
- 5b. Inspections of LA PA state/fee well sites complete on: Yes
- 5c. Reports current for Production/Disposition & Sundries on: 1/24/2014
- Federal and Indian Lease Wells:** The BLM and or the BIA has approved the merger, name change, or operator change for all wells listed on Federal or Indian leases on: BLM Not Yet BIA N/A
- Federal and Indian Units:**
 The BLM or BIA has approved the successor of unit operator for wells listed on: Not Yet
- Federal and Indian Communization Agreements ("CA"):**
 The BLM or BIA has approved the operator for all wells listed within a CA on: N/A
- Underground Injection Control ("UIC")** Division has approved UIC Form 5 Transfer of Authority to **Inject**, for the enhanced/secondary recovery unit/project for the water disposal well(s) listed on: Yes

DATA ENTRY:

- Changes entered in the **Oil and Gas Database** on: 1/28/2014
- Changes have been entered on the **Monthly Operator Change Spread Sheet** on: 1/28/2014
- Bond information entered in RBDMS on: 1/28/2014
- Fee/State wells attached to bond in RBDMS on: 1/28/2014
- Injection Projects to new operator in RBDMS on: 1/28/2014
- Receipt of Acceptance of Drilling Procedures for APD/New on: 1/7/2014
- Surface Agreement Sundry from **NEW** operator on Fee Surface wells received on: 1/7/2014

BOND VERIFICATION:

- Federal well(s) covered by Bond Number: RLB7886
- Indian well(s) covered by Bond Number: RLB7886
- a. (R649-3-1) The **NEW** operator of any state/fee well(s) listed covered by Bond Number B008371
- b. The **FORMER** operator has requested a release of liability from their bond on: N/A

LEASE INTEREST OWNER NOTIFICATION:

- (R649-2-10) The **NEW** operator of the fee wells has been contacted and informed by a letter from the Division of their responsibility to notify all interest owners of this change on: 1/28/2014

COMMENTS:

Bill Barrett Corporation (N2165) to EnerVest Operating, LLC (N4040)

Effective 1/1/2014

Peter Point Unit

Well Name	Sec	TWN	RNG	API Number	Entity	Mineral Lease	Surface Lease	Well Type	Well Status
PPU FED 11-34D-12-16	34	120S	160E	4300731465		Federal	Federal	GW	APD
PPU FED 10-34D-12-16	34	120S	160E	4300731469		Federal	Federal	GW	APD
PETERS POINT UF 15X-36D-12-16	36	120S	160E	4300750178		Federal	Federal	GW	APD
PETERS POINT UF 10-1D-13-16	36	120S	160E	4300750182		Federal	Federal	GW	APD
PETERS POINT UF 9-1D-13-16	36	120S	160E	4300750183		Federal	Federal	GW	APD
PPU FED 9-34D-12-16	34	120S	160E	4300731430	17225	Federal	Federal	GW	OPS
PPU FED 15-35D-12-16	35	120S	160E	4300731475	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 12A-6D-13-17	31	120S	170E	4300750034	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 11A-31D-12-17	31	120S	170E	4300750036	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 9-6D-13-17	6	130S	170E	4300750120	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 14-6D-13-17	6	130S	170E	4300750121	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 15-6D-13-17	6	130S	170E	4300750122	2470	Federal	Federal	GW	OPS
PETERS POINT UF 2-7D-13-17	6	130S	170E	4300750149	2470	Federal	Federal	GW	OPS
PETERS POINT UF 1-7D-13-17	6	130S	170E	4300750150	2470	Federal	Federal	GW	OPS
PETERS POINT U FED 36-2	36	120S	160E	4300730761	2470	Federal	Federal	GW	P
PETERS POINT U FED 36-3	36	120S	160E	4300730762	2470	Federal	Federal	GW	P
PETERS POINT U FED 36-4	36	120S	160E	4300730763	2470	Federal	Federal	GW	P
PETERS POINT U FED 14-25D-12-16	36	120S	160E	4300730764	2470	Federal	Federal	GW	P
PETERS POINT U FED 4-31D-12-17	36	120S	160E	4300730810	2470	Federal	Federal	GW	P
PETERS POINT U FED 16-26D-12-16	36	120S	160E	4300730812	2470	Federal	Federal	GW	P
PETERS POINT U FED 6-7D-13-17	6	130S	170E	4300730859	14692	Federal	Federal	GW	P
PETERS POINT U FED 16-35	35	120S	160E	4300730965	2470	Federal	Federal	GW	P
PETERS POINT U FED 11-6-13-17	6	130S	170E	4300730982	2470	Federal	Federal	GW	P
PETERS POINT U FED 16-6D-13-17	6	130S	170E	4300731004	2470	Federal	Federal	GW	P
PETERS POINT U FED 16-31D-12-17	6	130S	170E	4300731005	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-31D-12-17	36	120S	160E	4300731009	2470	Federal	Federal	GW	P
PETERS POINT U FED 2-36D-12-16	36	120S	160E	4300731010	2470	Federal	Federal	GW	P
PETERS POINT U FED 9-36-12-16	36	120S	160E	4300731011	2470	Federal	Federal	GW	P
PETERS POINT U FED 8-35D-12-16	36	120S	160E	4300731024	2470	Federal	Federal	GW	P
PETERS POINT U FED 4-12D-13-16	2	130S	160E	4300731049	14692	Federal	State	GW	P
PETERS POINT U FED 2-12D-13-16	6	130S	170E	4300731158	14692	Federal	Federal	GW	P
PETERS POINT U FED 10-36D-12-16	36	120S	160E	4300731174	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-36D-12-16	36	120S	160E	4300731175	2470	Federal	Federal	GW	P
PPU FED 15-6D-13-17	6	130S	170E	4300731261	16103	Federal	Federal	GW	P
PP UF 3-36-12-16	36	120S	160E	4300731271	2470	Federal	Federal	GW	P
PP UF 6-36-12-16	36	120S	160E	4300731272	2470	Federal	Federal	GW	P
PPU FED 6-35D-12-16	35	120S	160E	4300731275	2470	Federal	Federal	GW	P
PPU FED 8-34-12-16	34	120S	160E	4300731279	2470	Federal	Federal	GW	P
PPU FED 6-34D-12-16	34	120S	160E	4300731281	2470	Federal	Federal	GW	P
PPU FED 7-1D-13-16 ULTRA DEEP	6	130S	170E	4300731293	14692	Federal	Federal	GW	P
PPU FED 16-27-12-16	27	120S	160E	4300731318	2470	Federal	Federal	GW	P
PPU FED 10-27D-12-16	27	120S	160E	4300731319	2470	Federal	Federal	GW	P
PPU FED 2-34D-12-16	34	120S	160E	4300731320	2470	Federal	Federal	GW	P
PPU FED 2-7D-13-17 DEEP	6	130S	170E	4300731326	14692	Federal	Federal	GW	P
PPU FED 2-35D-12-16	35	120S	160E	4300731345	2470	Federal	Federal	GW	P
PPU FED 7-35D-12-16	35	120S	160E	4300731346	2470	Federal	Federal	GW	P
PPU FED 4-35D-12-16	35	120S	160E	4300731347	2470	Federal	Federal	GW	P
PPU FED 7-36D-12-16	36	120S	160E	4300731348	2470	Federal	Federal	GW	P
PPU FED 11-36D-12-16	36	120S	160E	4300731349	2470	Federal	Federal	GW	P
PPU FED 15-25D-12-16	36	120S	160E	4300731351	2470	Federal	Federal	GW	P
PPU FED 13-25D-12-16	36	120S	160E	4300731352	2470	Federal	Federal	GW	P
PPU FED 4-36D-12-16	36	120S	160E	4300731353	2470	Federal	Federal	GW	P
PPU FED 1-35D-12-16	35	120S	160E	4300731365	2470	Federal	Federal	GW	P
PPU FED 13-26D-12-16	26	120S	160E	4300731403	2470	Federal	Federal	GW	P
PPU FED 15-26D-12-16	26	120S	160E	4300731404	2470	Federal	Federal	GW	P
PPU FED 3-35D-12-16	26	120S	160E	4300731405	2470	Federal	Federal	GW	P

Bill Barrett Corporation (N2165) to EnerVest Operating, LLC (N4040)

Effective 1/1/2014

Peter Point Unit

Well Name	Sec	TWN	RNG	API Number	Entity	Mineral Lease	Surface Lease	Well Type	Well Status
PPU FED 10-26D-12-16	26	120S	160E	4300731406	2470	Federal	Federal	GW	P
PPU FED 11-26D-12-16	26	120S	160E	4300731407	2470	Federal	Federal	GW	P
PPU FED 12-26D-12-16	26	120S	160E	4300731408	2470	Federal	Federal	GW	P
PPU FED 11-27D-12-16	27	120S	160E	4300731409	2470	Federal	Federal	GW	P
PPU FED 15-27D-12-16	27	120S	160E	4300731410	2470	Federal	Federal	GW	P
PPU FED 9-27D-12-16	27	120S	160E	4300731411	2470	Federal	Federal	GW	P
PPU FED 1-34D-12-16	34	120S	160E	4300731427	2470	Federal	Federal	GW	P
PPU FED 7-34D-12-16	34	120S	160E	4300731428	2470	Federal	Federal	GW	P
PPU FED 5-35D-12-16	34	120S	160E	4300731429	2470	Federal	Federal	GW	P
PPU FED 3-34D-12-16	34	120S	160E	4300731466	2470	Federal	Federal	GW	P
PPU FED 5-34D-12-16	34	120S	160E	4300731467	2470	Federal	Federal	GW	P
PPU FED 4-34D-12-16	34	120S	160E	4300731468	2470	Federal	Federal	GW	P
PPU FED 10-35D-12-16	35	120S	160E	4300731474	2470	Federal	Federal	GW	P
PPU FED 9-35D-12-16	35	120S	160E	4300731476	2470	Federal	Federal	GW	P
PETERS POINT U FED 9-26D-12-16	25	120S	160E	4300750021	2470	Federal	Federal	GW	P
PETERS POINT U FED 11-25D-12-16	25	120S	160E	4300750022	2470	Federal	Federal	GW	P
PETERS POINT U FED 10-31D-12-17	31	120S	170E	4300750023	2470	Federal	Federal	GW	P
PETERS POINT U FED 11-31D-12-17	31	120S	170E	4300750024	2470	Federal	Federal	GW	P
PETERS POINT U FED 13A-31D-12-17	31	120S	170E	4300750025	2470	Federal	Federal	GW	P
PETERS POINT U FED 13-31D-12-17	31	120S	170E	4300750026	2470	Federal	Federal	GW	P
PETERS POINT U FED 14-31D-12-17	31	120S	170E	4300750027	2470	Federal	Federal	GW	P
PETERS POINT U FED 14A-31D-12-17	31	120S	170E	4300750028	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-25D-12-16	25	120S	160E	4300750029	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-6D-13-17	31	120S	170E	4300750033	2470	Federal	Federal	GW	P
PETERS POINT U FED 10-25D-12-16	25	120S	160E	4300750035	2470	Federal	Federal	GW	P
PETERS POINT U FED 13-36D-12-16	36	120S	160E	4300750037	2470	Federal	Federal	GW	P
PETERS POINT U FED 15-36D-12-16	36	120S	160E	4300750038	2470	Federal	Federal	GW	P
PETERS POINT U FED 11-1D-13-16	36	120S	160E	4300750039	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-1D-13-16	36	120S	160E	4300750040	2470	Federal	Federal	GW	P
PETERS POINT U FED 3A-34D-12-16	27	120S	160E	4300750063	2470	Federal	Federal	GW	P
PETERS POINT U FED 4A-34D-12-16	27	120S	160E	4300750064	2470	Federal	Federal	GW	P
PETERS POINT U FED 12-27D-12-16	27	120S	160E	4300750065	2470	Federal	Federal	GW	P
PETERS POINT U FED 13-27D-12-16	27	120S	160E	4300750066	2470	Federal	Federal	GW	P
PETERS POINT U FED 13A-27D-12-16	27	120S	160E	4300750067	2470	Federal	Federal	GW	P
PETERS POINT U FED 14A-27D-12-16	27	120S	160E	4300750069	2470	Federal	Federal	GW	P
PETERS POINT U FED 5-31D-12-17	36	120S	160E	4300750109	2470	Federal	Federal	GW	P
PETERS POINT U FED 6-31D-12-17	36	120S	160E	4300750116	2470	Federal	Federal	GW	P
PETERS POINT U FED 9X-36D-12-16	36	120S	160E	4300750117	2470	Federal	Federal	GW	P
PETERS POINT U FED 1-36D-12-16	36	120S	160E	4300750118	2470	Federal	Federal	GW	P
PETERS POINT U FED 10-6D-13-17	6	130S	170E	4300750119	2470	Federal	Federal	GW	P
PETERS POINT U FED 15-31D-12-17	6	130S	170E	4300750123	2470	Federal	Federal	GW	P
PETERS POINT UF 12-5D-13-17	6	130S	170E	4300750151	2470	Federal	Federal	GW	P
PETERS POINT UF 13-5D-13-17	6	130S	170E	4300750152	2470	Federal	Federal	GW	P
PETERS POINT UF 13-30D-12-17	30	120S	170E	4300750153	18347	Federal	Federal	GW	P
PETERS POINT UF 14-30D-12-17	30	120S	170E	4300750154	18350	Federal	Federal	GW	P
PETERS POINT UF 12-30D-12-17	30	120S	170E	4300750155	18346	Federal	Federal	GW	P
PETERS POINT UF 11-30D-12-17	30	120S	170E	4300750156	18348	Federal	Federal	GW	P
PETERS POINT UF 3-31D-12-17	30	120S	170E	4300750157	2470	Federal	Federal	GW	P
PETERS POINT UF 2-31D-12-17	30	120S	170E	4300750158	18349	Federal	Federal	GW	P
PETERS POINT UF 16-25D-12-16	30	120S	170E	4300750159	2470	Federal	Federal	GW	P
PETERS POINT UF 9-25D-12-16	30	120S	170E	4300750160	2470	Federal	Federal	GW	P
PETERS POINT UF 7X-36D-12-16	36	120S	160E	4300750231	2470	Federal	Federal	GW	P
PETERS POINT UF 8-36D-12-16	36	120S	160E	4300750232	2470	Federal	Federal	GW	P
PPU FED 14-26D-12-16	26	120S	160E	4300731277	2470	Federal	Federal	GW	S
PPU FED 5-36D-12-16	36	120S	160E	4300731350	2470	Federal	Federal	GW	S

COPY

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 9

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL OIL WELL <input type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER _____		5. LEASE DESIGNATION AND SERIAL NUMBER: (see attached well list)
2. NAME OF OPERATOR: ENERVEST OPERATING, LLC		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: N/A
3. ADDRESS OF OPERATOR: 1001 FANNIN, ST. STE 800 CITY HOUSTON STATE TX ZIP 77002		7. UNIT or CA AGREEMENT NAME:
4. LOCATION OF WELL FOOTAGES AT SURFACE: (see attached well list) QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN:		8. WELL NAME and NUMBER: (see attached well list)
PHONE NUMBER: (713) 659-3500		9. API NUMBER:
		10. FIELD AND POOL, OR WILDCAT:
		COUNTY:
		STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will start: 1/1/2014	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
<input type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of work completion:	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input checked="" type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLARE
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/RESUME)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: _____
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

ENERVEST OPERATING, LLC IS SUBMITTING THIS SUNDRY AS NOTIFICATION THAT THE WELLS LISTED ON THE ATTACHED LIST HAVE BEEN SOLD TO ENERVEST OPERATING, LLC BY BILL BARRETT CORPORATION EFFECTIVE 1/1/2014. PLEASE REFER ALL FUTURE CORRESPONDENCE TO THE ADDRESS BELOW.

EnerVest Operating, L.L.C.
1001 Fannin, Suite 800
Houston, Texas 77002
713-659-3500
(BLM BOND # RLB 7886, STATE/FEE BOND # B008371)

BILL BARRETT CORPORATION
Duane Zavadil NAME (PLEASE PRINT)
Duane Zavadil SIGNATURE
Senior Vice President -
EH&S, Government and Regulatory Affairs N2115

ENERVEST OPERATING, LLC
RONNIE L YOUNG NAME (PLEASE PRINT)
Ronnée L Young SIGNATURE
DIRECTOR - REGULATORY N4040

NAME (PLEASE PRINT) RONNIE YOUNG TITLE DIRECTOR - REGULATORY
SIGNATURE Ronnée L Young DATE 12/10/2013

(This space for State use only)

APPROVED

JAN 28 2014 4:00 PM

RECEIVED

JAN 07 2014

DIV. OIL, GAS & MINING
Rachael Medina

UDOGM CHANGE OF OPERATOR WELL LIST

Well Name	Sec	TWN	RNG	API Number	Entity	Lease	Well Type	Well Status	Unit
JACK CANYON UNIT 8-32	32	120S	160E	4300730460	15167	State	WI	A	
JACK CYN U ST 14-32	32	120S	160E	4300730913	15166	State	WD	A	
PRICKLY PEAR U FED 12-24	24	120S	140E	4300730953	14467	Federal	WD	A	
PPU FED 11-23D-12-15	23	120S	150E	4300731440		Federal	GW	APD	PRICKLY PEAR
PPU FED 4-26D-12-15	23	120S	150E	4300731441		Federal	GW	APD	PRICKLY PEAR
PPU FED 14-23D-12-15	23	120S	150E	4300731442		Federal	GW	APD	PRICKLY PEAR
PPU FED 12-23D-12-15	23	120S	150E	4300731443		Federal	GW	APD	PRICKLY PEAR
PPU FED 11-34D-12-16	34	120S	160E	4300731465		Federal	GW	APD	PETERS POINT
PPU FED 10-34D-12-16	34	120S	160E	4300731469		Federal	GW	APD	PETERS POINT
HORSE BENCH FED 4-27D-12-16	27	120S	160E	4300750092		Federal	GW	APD	
HORSE BENCH FED 5-27D-12-16	27	120S	160E	4300750093		Federal	GW	APD	
PRICKLY PEAR U FED 12-7D-12-15	07	120S	150E	4300750094		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR U FED 11-7D-12-15	07	120S	150E	4300750095		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR U FED 13-7D-12-15	07	120S	150E	4300750096		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR U FED 14-7D-12-15	07	120S	150E	4300750097		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11-8D-12-15	08	120S	150E	4300750124		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12-8D-12-15	08	120S	150E	4300750125		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13-8D-12-15	08	120S	150E	4300750126		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14-8D-12-15	08	120S	150E	4300750127		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9-21D-12-15	21	120S	150E	4300750128		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-21D-12-15	21	120S	150E	4300750129		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10-21D-12-15	21	120S	150E	4300750130		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-21D-12-15	21	120S	150E	4300750131		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-21D-12-15	21	120S	150E	4300750132		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15X-21D-12-15	21	120S	150E	4300750133		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16-21D-12-15	21	120S	150E	4300750134		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-21D-12-15	21	120S	150E	4300750135		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-22D-12-15	21	120S	150E	4300750148		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1A-27D-12-15	22	120S	150E	4300750161		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2A-27D-12-15	22	120S	150E	4300750162		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3A-27D-12-15	22	120S	150E	4300750163		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-22D-12-15	22	120S	150E	4300750164		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-22D-12-15	22	120S	150E	4300750165		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-22D-12-15	22	120S	150E	4300750166		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12A-22D-12-15	22	120S	150E	4300750167		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-22D-12-15	22	120S	150E	4300750168		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-22D-12-15	22	120S	150E	4300750169		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-22D-12-15	22	120S	150E	4300750170		Federal	GW	APD	PRICKLY PEAR
PETERS POINT UF 15X-36D-12-16	36	120S	160E	4300750178		Federal	GW	APD	PETERS POINT
PRICKLY PEAR UF 15A-15D-12-15	15	120S	150E	4300750180		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11B-15D-12-15	15	120S	150E	4300750181		Federal	GW	APD	PRICKLY PEAR
PETERS POINT UF 10-1D-13-16	36	120S	160E	4300750182		Federal	GW	APD	PETERS POINT
PETERS POINT UF 9-1D-13-16	36	120S	160E	4300750183		Federal	GW	APD	PETERS POINT
PRICKLY PEAR UF 16A-15D-12-15	15	120S	150E	4300750184		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3A-18D-12-15	07	120S	150E	4300750185		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4A-18D-12-15	07	120S	150E	4300750186		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-7D-12-15	07	120S	150E	4300750187		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-18D-12-15	07	120S	150E	4300750188		Federal	GW	APD	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR UF 12A-7D-12-15	07	120S	150E	4300750189	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-7D-12-15	07	120S	150E	4300750190	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-7D-12-15	07	120S	150E	4300750191	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR FEDERAL 1-12D-12-14	12	120S	140E	4300750205	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-12D-12-14	12	120S	140E	4300750206	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-12D-12-14	12	120S	140E	4300750207	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-12D-12-14	12	120S	140E	4300750208	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8-12D-12-14	12	120S	140E	4300750209	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-7D-12-15	12	120S	140E	4300750210	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5-7D-12-15	12	120S	140E	4300750211	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-12D-12-14	12	120S	140E	4300750212	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-7D-12-15	12	120S	140E	4300750213	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-14D-12-15	14	120S	150E	4300750214	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-14D-12-15	14	120S	150E	4300750215	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9-14D-12-15	14	120S	150E	4300750217	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-14D-12-15	14	120S	150E	4300750218	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10-14D-12-15	14	120S	150E	4300750219	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-14D-12-15	14	120S	150E	4300750220	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-14D-12-15	14	120S	150E	4300750222	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16-14D-12-15	14	120S	150E	4300750223	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-14D-12-15	14	120S	150E	4300750224	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1A-18D-12-15	07	120S	150E	4300750225	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2A-18D-12-15	07	120S	150E	4300750226	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-7D-12-15	07	120S	150E	4300750227	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-7D-12-15	07	120S	150E	4300750228	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-7D-12-15	07	120S	150E	4300750229	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-7D-12-15	07	120S	150E	4300750230	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-12D-12-14	12	120S	140E	4300750233	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-12D-12-14	12	120S	140E	4300750234	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-12D-12-14	12	120S	140E	4300750235	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12A-8D-12-15	08	120S	150E	4300750236	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-12D-12-14	12	120S	140E	4300750237	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-8D-12-15	08	120S	150E	4300750238	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-8D-12-15	08	120S	150E	4300750239	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-8D-12-15	08	120S	150E	4300750240	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-8D-12-15	08	120S	150E	4300750260	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-8D-12-15	08	120S	150E	4300750261	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-8D-12-15	08	120S	150E	4300750262	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-8D-12-15	08	120S	150E	4300750263	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-8D-12-15	08	120S	150E	4300750264	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-8D-12-15	08	120S	150E	4300750265	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-8D-12-15	08	120S	150E	4300750266	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5-8D-12-15	08	120S	150E	4300750267	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6-8D-12-15	08	120S	150E	4300750268	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-8D-12-15	08	120S	150E	4300750269	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-8D-12-15	08	120S	150E	4300750270	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8-8D-12-15	08	120S	150E	4300750271	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1-8D-12-15	08	120S	150E	4300750272	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-8D-12-15	08	120S	150E	4300750273	Federal	GW	APD	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR UF 5-9D-12-15	09	120S	150E	4300750274	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-9D-12-15	09	120S	150E	4300750275	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-9D-12-15	09	120S	150E	4300750276	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-9D-12-15	09	120S	150E	4300750277	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-9D-12-15	09	120S	150E	4300750278	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11-9D-12-15	09	120S	150E	4300750279	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12A-9D-12-15	09	120S	150E	4300750280	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6-9D-12-15	09	120S	150E	4300750281	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-9D-12-15	09	120S	150E	4300750282	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR US 1X-16D-12-15	10	120S	150E	4300750283	State	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-15D-12-15	10	120S	150E	4300750284	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-15D-12-15	10	120S	150E	4300750285	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-15D-13-15	10	120S	150E	4300750286	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-10D-12-15	15	120S	150E	4300750287	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13-10D-12-15	10	120S	150E	4300750288	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15-10D-12-15	15	120S	150E	4300750289	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-10D-12-15	15	120S	150E	4300750290	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9-10D-12-15	15	120S	150E	4300750291	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-10D-12-15	10	120S	150E	4300750292	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10-10D-12-15	15	120S	150E	4300750293	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16-10D-12-15	15	120S	150E	4300750294	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13-11D-12-15	15	120S	150E	4300750295	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-11D-12-15	15	120S	150E	4300750296	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12-11D-12-15	15	120S	150E	4300750297	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 13A-10D-12-15	10	120S	150E	4300750298	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12-10D-12-15	10	120S	150E	4300750299	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11-10D-12-15	10	120S	150E	4300750300	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3A-15D-12-15	10	120S	150E	4300750301	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12-14D-12-15	14	120S	150E	4300750302	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-15D-12-15	10	120S	150E	4300750303	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4A-15D-12-15	10	120S	150E	4300750304	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14-10D-12-15	10	120S	150E	4300750305	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-17D-12-15	17	120S	150E	4300750306	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-17D-12-15	17	120S	150E	4300750307	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10A-17D-12-15	17	120S	150E	4300750308	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-7D-12-15	07	120S	150E	4300750309	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-17D-12-15	17	120S	150E	4300750310	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6-7D-12-15	07	120S	150E	4300750311	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-17D-12-15	17	120S	150E	4300750312	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-7D-12-15	07	120S	150E	4300750313	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-7D-12-15	07	120S	150E	4300750314	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-7D-12-15	07	120S	150E	4300750315	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6X-17D-12-15	17	120S	150E	4300750316	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-17D-12-15	17	120S	150E	4300750317	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15B-17D-12-15	17	120S	150E	4300750318	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-20D-12-15	20	120S	150E	4300750319	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1-7D-12-15	07	120S	150E	4300750320	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-20D-12-15	20	120S	150E	4300750321	Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9A-20D-12-15	20	120S	150E	4300750322	Federal	GW	APD	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR UF 10A-20D-12-15	20	120S	150E	4300750323		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 10-20D-12-15	20	120S	150E	4300750324		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-7D-12-15	07	120S	150E	4300750325		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 14A-20D-12-15	20	120S	150E	4300750326		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 16A-20D-12-15	20	120S	150E	4300750327		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15A-20D-12-15	20	120S	150E	4300750328		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8-7D-12-15	07	120S	150E	4300750329		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 15-20D-12-15	20	120S	150E	4300750330		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-7D-12-15	07	120S	150E	4300750331		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6-10D-12-15	09	120S	150E	4300750332		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5A-10D-12-15	09	120S	150E	4300750333		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 11A-10D-12-15	09	120S	150E	4300750334		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 6A-10D-12-15	09	120S	150E	4300750335		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 5-10D-12-15	09	120S	150E	4300750336		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 12A-10D-12-15	09	120S	150E	4300750338		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 3-10D-12-15	09	120S	150E	4300750339		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 4-10D-12-15	09	120S	150E	4300750340		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8-9D-12-15	09	120S	150E	4300750341		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 8A-9D-12-15	09	120S	150E	4300750342		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7A-9D-12-15	09	120S	150E	4300750343		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 7-9D-12-15	09	120S	150E	4300750344		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1-9D-12-15	09	120S	150E	4300750345		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 2-9D-12-15	09	120S	150E	4300750346		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 1-24D-12-1	24	120S	150E	4300750348		Federal	GW	APD	PRICKLY PEAR
PRICKLY PEAR UF 9-13D-12-15	13	120S	150E	4300750349		Federal	GW	APD	PRICKLY PEAR
HORSE BENCH FED 4-20D-12-17	19	120S	170E	4300750350		Federal	GW	APD	
Horse Bench Federal 16-18D-12-17	19	120S	170E	4300750351		Federal	GW	APD	
PPU FED 9-34D-12-16	34	120S	160E	4300731430	17225	Federal	GW	OPS	PETERS POINT
PPU FED 15-35D-12-16	35	120S	160E	4300731475	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT U FED 12A-6D-13-17	31	120S	170E	4300750034	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT U FED 11A-31D-12-17	31	120S	170E	4300750036	2470	Federal	GW	OPS	PETERS POINT
PRICKLY PEAR U FED 7-21D-12-15	21	120S	150E	4300750055	14794	Federal	GW	OPS	PRICKLY PEAR
PETERS POINT U FED 9-6D-13-17	06	130S	170E	4300750120	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT U FED 14-6D-13-17	06	130S	170E	4300750121	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT U FED 15-6D-13-17	06	130S	170E	4300750122	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT UF 2-7D-13-17	06	130S	170E	4300750149	2470	Federal	GW	OPS	PETERS POINT
PETERS POINT UF 1-7D-13-17	06	130S	170E	4300750150	2470	Federal	GW	OPS	PETERS POINT
PRICKLY PEAR US 1A-16D-12-15	09	120S	150E	4300750192	14794	State	GW	OPS	PRICKLY PEAR
PRICKLY PEAR US 2A-16D-12-15	09	120S	150E	4300750193	14794	State	GW	OPS	PRICKLY PEAR
PRICKLY PEAR US 2-16D-12-15	09	120S	150E	4300750194	14794	State	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 9A-9D-12-15	09	120S	150E	4300750196	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 10-9D-12-15	09	120S	150E	4300750197	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 10A-9D-12-15	09	120S	150E	4300750198	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 14-9D-12-15	09	120S	150E	4300750199	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 14A-9D-12-15	09	120S	150E	4300750200	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 15-9D-12-15	09	120S	150E	4300750201	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 15A-9D-12-15	09	120S	150E	4300750203	14794	Federal	GW	OPS	PRICKLY PEAR
PRICKLY PEAR UF 16A-9D-12-15	09	120S	150E	4300750204	14794	Federal	GW	OPS	PRICKLY PEAR
SHARPLES 1 GOVT PICKRELL	11	120S	150E	4300716045	7030	Federal	GW	P	

UDOGM CHANGE OF OPERATOR WELL LIST

STONE CABIN UNIT 1	13	120S	140E	4300716542	12052 Federal	GW	P	
STONE CABIN FED 1-11	11	120S	140E	4300730014	6046 Federal	GW	P	
STONE CABIN FED 2-B-27	27	120S	150E	4300730018	14794 Federal	GW	P	PRICKLY PEAR
JACK CANYON 101-A	33	120S	160E	4300730049	2455 Federal	GW	P	
PETERS POINT ST 2-2-13-16	02	130S	160E	4300730521	14387 State	GW	P	
PRICKLY PEAR ST 16-15	16	120S	150E	4300730522	14794 State	GW	P	PRICKLY PEAR
PETERS POINT U FED 36-2	36	120S	160E	4300730761	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 36-3	36	120S	160E	4300730762	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 36-4	36	120S	160E	4300730763	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 14-25D-12-16	36	120S	160E	4300730764	2470 Federal	GW	P	PETERS POINT
HUNT RANCH 3-4	03	120S	150E	4300730775	13158 State	GW	P	
PETERS POINT U FED 4-31D-12-17	36	120S	160E	4300730810	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 16-26D-12-16	36	120S	160E	4300730812	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR UNIT 13-4	13	120S	140E	4300730825	14353 Federal	GW	P	
PRICKLY PEAR UNIT 21-2	21	120S	150E	4300730828	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 6-7D-13-17	06	130S	170E	4300730859	14692 Federal	GW	P	PETERS POINT
PETERS POINT ST 4-2-13-16	02	130S	160E	4300730866	14386 State	GW	P	
PRICKLY PEAR U ST 13-16	16	120S	150E	4300730933	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 11-16	16	120S	150E	4300730944	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 7-16	16	120S	150E	4300730945	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7-25	25	120S	150E	4300730954	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 16-35	35	120S	160E	4300730965	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 11-6-13-17	06	130S	170E	4300730982	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 16-6D-13-17	06	130S	170E	4300731004	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 16-31D-12-17	06	130S	170E	4300731005	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 5-13-12-14	13	120S	140E	4300731008	14897 Federal	GW	P	
PETERS POINT U FED 12-31D-12-17	36	120S	160E	4300731009	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 2-36D-12-16	36	120S	160E	4300731010	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 9-36-12-16	36	120S	160E	4300731011	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U ST 36-06	36	120S	150E	4300731018	14794 State	GW	P	PRICKLY PEAR
PETERS POINT U FED 8-35D-12-16	36	120S	160E	4300731024	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 4-12D-13-16	02	130S	160E	4300731049	14692 Federal	GW	P	PETERS POINT
PETERS POINT ST 5-2D-13-16 DEEP	02	130S	160E	4300731056	15909 State	GW	P	
PRICKLY PEAR U FED 13-23-12-15	23	120S	150E	4300731073	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1-27D-12-15	23	120S	150E	4300731074	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-26D-12-15	23	120S	150E	4300731075	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-22D-12-15	23	120S	150E	4300731076	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-28D-12-15	21	120S	150E	4300731121	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 2-12D-13-16	06	130S	170E	4300731158	14692 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 15-21-12-15	21	120S	150E	4300731164	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7-28D-12-15	21	120S	150E	4300731165	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 13-21D-12-15	21	120S	150E	4300731166	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 10-36D-12-16	36	120S	160E	4300731174	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-36D-12-16	36	120S	160E	4300731175	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 15-17-12-15	17	120S	150E	4300731183	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 11-17D-12-15	17	120S	150E	4300731184	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7-22D-12-15	22	120S	150E	4300731186	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-22-12-15	22	120S	150E	4300731187	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5-22D-12-15	22	120S	150E	4300731188	14794 Federal	GW	P	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR 11-15D-12-15	22	120S	150E	4300731189	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-18D-12-15	18	120S	150E	4300731192	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-18-12-15	18	120S	150E	4300731193	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-27D-12-15	27	120S	150E	4300731194	15569 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 12-27D-12-15	27	120S	150E	4300731195	15568 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 10-27-12-15	27	120S	150E	4300731196	15570 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-20D-12-15	20	120S	150E	4300731197	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7-20-12-15	20	120S	150E	4300731198	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1-20-12-15	20	120S	150E	4300731206	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 2-36-12-15	36	120S	150E	4300731226	15719 State	GW	P	
PRICKLY PEAR U ST 4-36-12-15	36	120S	150E	4300731227	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4-27D-12-15	22	120S	150E	4300731237	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 13-22-12-15	22	120S	150E	4300731238	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-27D-12-15	22	120S	150E	4300731239	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 9-16-12-15	16	120S	150E	4300731240	14794 State	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-28D-12-15	28	120S	150E	4300731241	16028 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5-27D-12-15	28	120S	150E	4300731242	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1-28-12-15	28	120S	150E	4300731243	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 8-28D-12-15	28	120S	150E	4300731244	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U ST 1-16-12-15	16	120S	150E	4300731245	14794 State	GW	P	PRICKLY PEAR
PPU FED 11-18D-12-15	18	120S	150E	4300731257	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 11-20D-12-15	20	120S	150E	4300731258	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4-25D-12-15	25	120S	150E	4300731259	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 12-25D-12-15	25	120S	150E	4300731260	16068 Federal	GW	P	PRICKLY PEAR
PPU FED 15-6D-13-17	06	130S	170E	4300731261	16103 Federal	GW	P	PETERS POINT
PP UF 3-36-12-16	36	120S	160E	4300731271	2470 Federal	GW	P	PETERS POINT
PP UF 6-36-12-16	36	120S	160E	4300731272	2470 Federal	GW	P	PETERS POINT
PPU FED 6-35D-12-16	35	120S	160E	4300731275	2470 Federal	GW	P	PETERS POINT
PPU FED 14-26D-12-16	26	120S	160E	4300731277	2470 Federal	GW	P	PETERS POINT
PPU FED 8-34-12-16	34	120S	160E	4300731279	2470 Federal	GW	P	PETERS POINT
PP ST 8-2D-13-16 (DEEP)	02	130S	160E	4300731280	16069 State	GW	P	
PPU FED 6-34D-12-16	34	120S	160E	4300731281	2470 Federal	GW	P	PETERS POINT
PPU FED 14-26D-12-15	35	120S	150E	4300731282	16224 Federal	GW	P	PRICKLY PEAR
PPU FED 2-35-12-15	35	120S	150E	4300731283	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 10-26D-12-15	35	120S	150E	4300731284	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 9-17-12-15	17	120S	150E	4300731287	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 1-17D-12-15	17	120S	150E	4300731288	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 7-17D-12-15	17	120S	150E	4300731289	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 7-1D-13-16 ULTRA DEEP	06	130S	170E	4300731293	14692 Federal	GW	P	PETERS POINT
PPU FED 1-18D-12-15	18	120S	150E	4300731294	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 7-18D-12-15	18	120S	150E	4300731295	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 5-17D-12-15	18	120S	150E	4300731296	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 10-17D-12-15	17	120S	150E	4300731307	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 8-17D-12-15	17	120S	150E	4300731308	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 12-17D-12-15	17	120S	150E	4300731309	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 13-17D-12-15	17	120S	150E	4300731310	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 14-17D-12-15	17	120S	150E	4300731311	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16-18D-12-15	17	120S	150E	4300731312	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 8-18D-12-15	18	120S	150E	4300731313	14794 Federal	GW	P	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PPU FED 3-18D-12-15	18	120S	150E	4300731314	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4-18-12-15	18	120S	150E	4300731315	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 5-18D-12-15	18	120S	150E	4300731316	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 6-18D-12-15	18	120S	150E	4300731317	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16-27-12-16	27	120S	160E	4300731318	2470 Federal	GW	P	PETERS POINT
PPU FED 10-27D-12-16	27	120S	160E	4300731319	2470 Federal	GW	P	PETERS POINT
PPU FED 2-34D-12-16	34	120S	160E	4300731320	2470 Federal	GW	P	PETERS POINT
PPU FED 16-17D-12-15	17	120S	150E	4300731321	14794 Federal	GW	P	PRICKLY PEAR
PPU ST 15-16D-12-15	16	120S	150E	4300731322	14794 State	GW	P	PRICKLY PEAR
PPU ST 16-16D-12-15	16	120S	150E	4300731323	14794 State	GW	P	PRICKLY PEAR
PPU ST 14-16D-12-15	16	120S	150E	4300731324	14794 State	GW	P	PRICKLY PEAR
PPU FED 2-7D-13-17 DEEP	06	130S	170E	4300731326	14692 Federal	GW	P	PETERS POINT
PPU FED 3-21D-12-15	21	120S	150E	4300731328	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4-21D-12-15	21	120S	150E	4300731329	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 2-35D-12-16	35	120S	160E	4300731345	2470 Federal	GW	P	PETERS POINT
PPU FED 7-35D-12-16	35	120S	160E	4300731346	2470 Federal	GW	P	PETERS POINT
PPU FED 4-35D-12-16	35	120S	160E	4300731347	2470 Federal	GW	P	PETERS POINT
PPU FED 7-36D-12-16	36	120S	160E	4300731348	2470 Federal	GW	P	PETERS POINT
PPU FED 11-36D-12-16	36	120S	160E	4300731349	2470 Federal	GW	P	PETERS POINT
PPU FED 15-25D-12-16	36	120S	160E	4300731351	2470 Federal	GW	P	PETERS POINT
PPU FED 13-25D-12-16	36	120S	160E	4300731352	2470 Federal	GW	P	PETERS POINT
PPU FED 4-36D-12-16	36	120S	160E	4300731353	2470 Federal	GW	P	PETERS POINT
PPU FED 13-15D-12-15	22	120S	150E	4300731358	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 14-15D-12-15	22	120S	150E	4300731359	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4-22D-12-15	22	120S	150E	4300731360	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 6-22D-12-15	22	120S	150E	4300731361	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 2-28D-12-15	28	120S	150E	4300731362	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16X-21D-12-15	28	120S	150E	4300731363	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 5A-27D-12-15	28	120S	150E	4300731364	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 1-35D-12-16	35	120S	160E	4300731365	2470 Federal	GW	P	PETERS POINT
PPU FED 1A-28D-12-15	28	120S	150E	4300731368	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 14A-18D-12-15	18	120S	150E	4300731393	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 10-18D-12-15	18	120S	150E	4300731394	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 15A-18D-12-15	18	120S	150E	4300731395	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16A-18D-12-15	18	120S	150E	4300731396	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 12-22D-12-15	22	120S	150E	4300731398	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 11-22D-12-15	22	120S	150E	4300731399	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 14-22D-12-15	22	120S	150E	4300731400	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 4A-27D-12-15	22	120S	150E	4300731401	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 13-26D-12-16	26	120S	160E	4300731403	2470 Federal	GW	P	PETERS POINT
PPU FED 15-26D-12-16	26	120S	160E	4300731404	2470 Federal	GW	P	PETERS POINT
PPU FED 3-35D-12-16	26	120S	160E	4300731405	2470 Federal	GW	P	PETERS POINT
PPU FED 10-26D-12-16	26	120S	160E	4300731406	2470 Federal	GW	P	PETERS POINT
PPU FED 11-26D-12-16	26	120S	160E	4300731407	2470 Federal	GW	P	PETERS POINT
PPU FED 12-26D-12-16	26	120S	160E	4300731408	2470 Federal	GW	P	PETERS POINT
PPU FED 11-27D-12-16	27	120S	160E	4300731409	2470 Federal	GW	P	PETERS POINT
PPU FED 15-27D-12-16	27	120S	160E	4300731410	2470 Federal	GW	P	PETERS POINT
PPU FED 9-27D-12-16	27	120S	160E	4300731411	2470 Federal	GW	P	PETERS POINT
PPU FED 11-21D-12-15	21	120S	150E	4300731412	14794 Federal	GW	P	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PPU FED 6-21D-12-15	21	120S	150E	4300731413	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 12-21D-12-15	21	120S	150E	4300731414	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 8-20D-12-15	20	120S	150E	4300731419	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 1A-20D-12-15	20	120S	150E	4300731420	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 2-20D-12-15	20	120S	150E	4300731421	14794 Federal	GW	P	PRICKLY PEAR
PPU ST 7A-16D-12-15	16	120S	150E	4300731422	14794 State	GW	P	PRICKLY PEAR
PPU ST 6-16D-12-15	16	120S	150E	4300731423	14794 State	GW	P	PRICKLY PEAR
PPU ST 10A-16D-12-15	16	120S	150E	4300731424	14794 State	GW	P	PRICKLY PEAR
PPU ST 3-16D-12-15	16	120S	150E	4300731425	14794 State	GW	P	PRICKLY PEAR
PPU FED 1-34D-12-16	34	120S	160E	4300731427	2470 Federal	GW	P	PETERS POINT
PPU FED 7-34D-12-16	34	120S	160E	4300731428	2470 Federal	GW	P	PETERS POINT
PPU FED 5-35D-12-16	34	120S	160E	4300731429	2470 Federal	GW	P	PETERS POINT
PPU FED 5-21D-12-15	21	120S	150E	4300731451	14794 Federal	GW	P	PRICKLY PEAR
PPU ST 8-16D-12-15	16	120S	150E	4300731455	14794 State	GW	P	PRICKLY PEAR
PPU ST 12-16D-12-15	16	120S	150E	4300731456	14794 State	GW	P	PRICKLY PEAR
PPU ST 12A-16D-12-15	16	120S	150E	4300731457	14794 State	GW	P	PRICKLY PEAR
PPU ST 15A-16D-12-15	16	120S	150E	4300731458	14794 State	GW	P	PRICKLY PEAR
PPU ST 10-16D-12-15	16	120S	150E	4300731459	14794 State	GW	P	PRICKLY PEAR
PPU ST 11A-16D-12-15	16	120S	150E	4300731460	14794 State	GW	P	PRICKLY PEAR
PPU ST 13A-16D-12-15	16	120S	150E	4300731461	14794 State	GW	P	PRICKLY PEAR
PPU FED 3-34D-12-16	34	120S	160E	4300731466	2470 Federal	GW	P	PETERS POINT
PPU FED 5-34D-12-16	34	120S	160E	4300731467	2470 Federal	GW	P	PETERS POINT
PPU FED 4-34D-12-16	34	120S	160E	4300731468	2470 Federal	GW	P	PETERS POINT
PPU FED 10-7D-12-15	07	120S	150E	4300731470	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 15-7D-12-15	07	120S	150E	4300731471	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 9-7D-12-15	07	120S	150E	4300731472	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 16-7D-12-15	07	120S	150E	4300731473	14794 Federal	GW	P	PRICKLY PEAR
PPU FED 10-35D-12-16	35	120S	160E	4300731474	2470 Federal	GW	P	PETERS POINT
PPU FED 9-35D-12-16	35	120S	160E	4300731476	2470 Federal	GW	P	PETERS POINT
PPU ST 6A-16D-12-15	16	120S	150E	4300731477	14794 State	GW	P	PRICKLY PEAR
PPU ST 4-16D-12-15	16	120S	150E	4300731478	14794 State	GW	P	PRICKLY PEAR
PPU ST 4A-16D-12-15	16	120S	150E	4300731479	14794 State	GW	P	PRICKLY PEAR
PPU ST 5A-16D-12-15	16	120S	150E	4300731480	14794 State	GW	P	PRICKLY PEAR
PPU ST 3A-16D-12-15	16	120S	150E	4300731481	14794 State	GW	P	PRICKLY PEAR
PPU ST 16A-16D-12-15	16	120S	150E	4300731484	14794 State	GW	P	PRICKLY PEAR
PPU ST 9A-16D-12-15	16	120S	150E	4300731485	14794 State	GW	P	PRICKLY PEAR
PPU ST 16B-16D-12-15	16	120S	150E	4300731514	14794 State	GW	P	PRICKLY PEAR
PPU ST 14B-16D-12-15	16	120S	150E	4300731515	14794 State	GW	P	PRICKLY PEAR
PPU ST 13B-16D-12-15	16	120S	150E	4300731516	14794 State	GW	P	PRICKLY PEAR
PETERS POINT U FED 9-26D-12-16	25	120S	160E	4300750021	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 11-25D-12-16	25	120S	160E	4300750022	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 10-31D-12-17	31	120S	170E	4300750023	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 11-31D-12-17	31	120S	170E	4300750024	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13A-31D-12-17	31	120S	170E	4300750025	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13-31D-12-17	31	120S	170E	4300750026	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 14-31D-12-17	31	120S	170E	4300750027	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 14A-31D-12-17	31	120S	170E	4300750028	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-25D-12-16	25	120S	160E	4300750029	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-6D-13-17	31	120S	170E	4300750033	2470 Federal	GW	P	PETERS POINT

UDOGM CHANGE OF OPERATOR WELL LIST

PETERS POINT U FED 10-25D-12-16	25	120S	160E	4300750035	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13-36D-12-16	36	120S	160E	4300750037	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 15-36D-12-16	36	120S	160E	4300750038	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 11-1D-13-16	36	120S	160E	4300750039	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-1D-13-16	36	120S	160E	4300750040	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 9-22D-12-15	22	120S	150E	4300750041	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 10-22D-12-15	22	120S	150E	4300750042	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-22D-12-15	22	120S	150E	4300750043	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2-27D-12-15	22	120S	150E	4300750044	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-15D-12-15	15	120S	150E	4300750045	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-15D-12-15	15	120S	150E	4300750046	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 10-15D-12-15	15	120S	150E	4300750047	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-15D-12-15	15	120S	150E	4300750048	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 11A-15D-12-15	15	120S	150E	4300750049	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1-21D-12-15	21	120S	150E	4300750050	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2-21D-12-15	21	120S	150E	4300750051	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2A-21D-12-15	21	120S	150E	4300750052	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4A-22D-12-15	21	120S	150E	4300750053	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5A-22D-12-15	21	120S	150E	4300750054	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7A-21D-12-15	21	120S	150E	4300750056	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 8-21D-12-15	21	120S	150E	4300750057	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 8A-21D-12-15	21	120S	150E	4300750058	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-8D-12-15	08	120S	150E	4300750059	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-8D-12-15	08	120S	150E	4300750060	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2-17D-12-15	08	120S	150E	4300750061	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 1A-17D-12-15	08	120S	150E	4300750062	14794 Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 3A-34D-12-16	27	120S	160E	4300750063	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 4A-34D-12-16	27	120S	160E	4300750064	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 12-27D-12-16	27	120S	160E	4300750065	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13-27D-12-16	27	120S	160E	4300750066	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 13A-27D-12-16	27	120S	160E	4300750067	2470 Federal	GW	P	PETERS POINT
PETERS POINT U FED 14-27D-12-16	27	120S	160E	4300750068	18204 Federal	GW	P	
PETERS POINT U FED 14A-27D-12-16	27	120S	160E	4300750069	2470 Federal	GW	P	PETERS POINT
PRICKLY PEAR U FED 1-22D-12-15	22	120S	150E	4300750076	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 2-22D-12-15	22	120S	150E	4300750077	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 8-22D-12-15	22	120S	150E	4300750078	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3-17D-12-15	17	120S	150E	4300750079	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3A-17D-12-15	17	120S	150E	4300750080	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4-17D-12-15	17	120S	150E	4300750081	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4A-17D-12-15	17	120S	150E	4300750082	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5A-17D-12-15	17	120S	150E	4300750083	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 6-17D-12-15	17	120S	150E	4300750084	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 6A-17D-12-15	17	120S	150E	4300750085	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 7A-17D-12-15	17	120S	150E	4300750086	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 12A-17D-12-15	17	120S	150E	4300750087	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 9-12D-12-14	12	120S	140E	4300750088	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 10-12D-12-14	12	120S	140E	4300750089	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 15-12D-12-14	12	120S	140E	4300750090	14794 Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 16-12D-12-14	12	120S	140E	4300750091	14794 Federal	GW	P	PRICKLY PEAR

UDOGM CHANGE OF OPERATOR WELL LIST

PRICKLY PEAR U FED 3-20D-12-15	20	120S	150E	4300750098	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 3A-20D-12-15	20	120S	150E	4300750099	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4-20D-12-15	20	120S	150E	4300750100	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 4A-20D-12-15	20	120S	150E	4300750101	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 5-20D-12-15	20	120S	150E	4300750102	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 6-20D-12-15	20	120S	150E	4300750104	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 6A-20D-12-15	20	120S	150E	4300750105	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 11A-20D-12-15	20	120S	150E	4300750106	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR U FED 12A-20D-12-15	20	120S	150E	4300750107	14794	Federal	GW	P	PRICKLY PEAR
PETERS POINT U FED 5-31D-12-17	36	120S	160E	4300750109	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 6-31D-12-17	36	120S	160E	4300750116	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 9X-36D-12-16	36	120S	160E	4300750117	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 1-36D-12-16	36	120S	160E	4300750118	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 10-6D-13-17	06	130S	170E	4300750119	2470	Federal	GW	P	PETERS POINT
PETERS POINT U FED 15-31D-12-17	06	130S	170E	4300750123	2470	Federal	GW	P	PETERS POINT
PRICKLY PEAR UF 7A-18D-12-15	17	120S	150E	4300750136	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 8A-18D-12-15	17	120S	150E	4300750137	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 9A-18D-12-15	17	120S	150E	4300750138	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 12-20D-12-15	20	120S	150E	4300750139	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 16A-8D-12-15	08	120S	150E	4300750140	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 15A-8D-12-15	08	120S	150E	4300750141	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 13A-9D-12-15	08	120S	150E	4300750142	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 13-9D-12-15	08	120S	150E	4300750143	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 12-9D-12-15	08	120S	150E	4300750144	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 10-8D-12-15	08	120S	150E	4300750145	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 9-8D-12-15	08	120S	150E	4300750146	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 2A-17D-12-15	08	120S	150E	4300750147	14794	Federal	GW	P	PRICKLY PEAR
PETERS POINT UF 12-5D-13-17	06	130S	170E	4300750151	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 13-5D-13-17	06	130S	170E	4300750152	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 13-30D-12-17	30	120S	170E	4300750153	18347	Federal	GW	P	PETERS POINT
PETERS POINT UF 14-30D-12-17	30	120S	170E	4300750154	18350	Federal	GW	P	PETERS POINT
PETERS POINT UF 12-30D-12-17	30	120S	170E	4300750155	18346	Federal	GW	P	PETERS POINT
PETERS POINT UF 11-30D-12-17	30	120S	170E	4300750156	18348	Federal	GW	P	PETERS POINT
PETERS POINT UF 3-31D-12-17	30	120S	170E	4300750157	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 2-31D-12-17	30	120S	170E	4300750158	18349	Federal	GW	P	PETERS POINT
PETERS POINT UF 16-25D-12-16	30	120S	170E	4300750159	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 9-25D-12-16	30	120S	170E	4300750160	2470	Federal	GW	P	PETERS POINT
PRICKLY PEAR UF 1A-22D-12-15	22	120S	150E	4300750171	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 6A-22D-12-15	22	120S	150E	4300750173	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 7A-22D-12-15	22	120S	150E	4300750174	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 8A-22D-12-15	22	120S	150E	4300750175	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 14B-15D-12-15	22	120S	150E	4300750176	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 9-9D-12-15	09	120S	150E	4300750195	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 16-9D-12-15	09	120S	150E	4300750202	14794	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 8-14D-12-15	14	120S	150E	4300750216	18289	Federal	GW	P	PRICKLY PEAR
PRICKLY PEAR UF 15-14D-12-15	14	120S	150E	4300750221	18290	Federal	GW	P	PRICKLY PEAR
PETERS POINT UF 7X-36D-12-16	36	120S	160E	4300750231	2470	Federal	GW	P	PETERS POINT
PETERS POINT UF 8-36D-12-16	36	120S	160E	4300750232	2470	Federal	GW	P	PETERS POINT
PETERS POINT ST 6-2D-13-16	02	130S	160E	4300731017	14472	State	D	PA	

UDOGM CHANGE OF OPERATOR WELL LIST

PTS 33-36 STATE	36	110S	140E	4301330486	6190 State	GW	PA	ARGYLE
PRICKLY PEAR U FED 10-4	10	120S	140E	4300730823	14462 Federal	GW	S	
PRICKLY PEAR U FASSELIN 5-19-12-15	19	120S	150E	4300730860	14853 Fee	GW	S	
PRICKLY PEAR U ST 5-16	16	120S	150E	4300730943	14794 State	GW	S	PRICKLY PEAR
PRICKLY PEAR U FED 7-33D-12-15	33	120S	150E	4300730985	14771 Federal	GW	S	
PETERS POINT ST 8-2D-13-16	02	130S	160E	4300731016	14471 State	GW	S	
PPU FED 4-35D-12-15	35	120S	150E	4300731285	16223 Federal	GW	S	PRICKLY PEAR
PPU FED 5-36D-12-16	36	120S	160E	4300731350	2470 Federal	GW	S	PETERS POINT
PRICKLY PEAR U FED 5A-20D-12-15	20	120S	150E	4300750103	14794 Federal	GW	S	PRICKLY PEAR
PRICKLY PEAR U FED 13A-17D-12-15	20	120S	150E	4300750108	14794 Federal	GW	S	PRICKLY PEAR
PRICKLY PEAR UF 2A-22D-12-15	22	120S	150E	4300750172	14794 Federal	GW	S	PRICKLY PEAR

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU0681
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Gas Well		7. UNIT or CA AGREEMENT NAME: PETERS POINT
2. NAME OF OPERATOR: ENERVEST OPERATING, LLC		8. WELL NAME and NUMBER: PETERS POINT U FED 12-25D-12-16
3. ADDRESS OF OPERATOR: 1001 Fannin Street, Suite 800 , Houston, TX, 77002		9. API NUMBER: 43007500290000
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2414 FSL 1290 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 25 Township: 12.0S Range: 16.0E Meridian: S		9. FIELD and POOL or WILDCAT: PETERS POINT
		COUNTY: CARBON
		STATE: UTAH

11.

CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 8/20/2015	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> OTHER	OTHER: <input type="text" value="Ran Tubing"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On 08/20/2015 EnerVest Operating L.L.C. ran 2 3/8 tubing set depth @
5484.75MD

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
September 04, 2015**

NAME (PLEASE PRINT) Rebecca Tidwell	PHONE NUMBER 713 970-1847	TITLE Regulatory Analyst
SIGNATURE N/A	DATE 9/3/2015	
