

UTAH OIL AND GAS CONSERVATION COMMISSION

REMARKS: WELL LOG ELECTRIC LOGS WATER SANDS LOCATION INSPECTED SUB. REPORT/abd

990611 Comp Exp!

DATE FILED: OCTOBER 14, 1997

LAND: FEE & PATENTED STATE LEASE NO. PUBLIC LEASE NO.

INDIAN #

DRILLING APPROVED: OCTOBER 27, 1997

14-20-H62-3514

SPUDED IN: 4-17-98

COMPLETED: 5-11-98 POW PUT TO PRODUCING: 5/22/98

INITIAL PRODUCTION: Oil-0 Gas-0 Water-45-bbl

GRAVITY API

GOR

PRODUCING ZONES: 4431-4841'

TOTAL DEPTH: 5258'

WELL ELEVATION: 6088' N/B

DATE ABANDONED:

FIELD: ANTELOPE CREEK

UNIT:

COUNTY: DUCHESNE

WELL NO: UTE TRIBAL 19-11

API NO. 43-013-31967

LOCATION 2226 FSL FT. FROM (N) (S) LINE. 1484 FWL

FT. FROM (E) (W) LINE. NE SW

1/4 - 1/4 SEC.

19

TWP.	RGE.	SEC.	OPERATOR	TWP.	RGE.	SEC.	OPERATOR
5S	3W	19	PETROGLYPH OPERATING				


GEOLOGIC TOPS:

QUATERNARY	Star Point	Chinie	Molas
Alluvium	Wahweap	Shinarump	Manning Canyon
Lake beds	Masuk	Moenkopi	Mississippian
Pleistocene	Colorado	Sinbad	Humbug
Lake beds	Sego	PERMIAN	Brazer
TERTIARY	Buck Tongue	Kaibab	Pilot Shale
Pliocene	Castlegate	Coconino	Madison
Salt Lake	Mancos	Cutler	Leadville
Oligocene	Upper	Hoskinnini	Redwall
Nonwood	Middle	DeChelly	DEVONIAN
Eocene	Lower	White Rim	Upper
Duchesne River	Emery	Organ Rock	Middle
Uinta	Blue Gate	Cedar Mesa	Lower
Bridger	Ferron	Halgaite Tongue	Ouray
Green River	Frontier	Phosphoria	Elbert
<i>B. MKP</i>	<i>3610</i>	Dakota	McCracken
<i>X MKP</i>	<i>4090</i>	Burro Canyon	Aneth
<i>Dough Creek</i>	<i>4336</i>	Cedar Mountain	Simonson Dolomite
<i>E. Timonians</i>	<i>4114</i>	Buckhorn	Sevy Dolomite
<i>Carlie R. M.</i>	<i>5159</i>	JURASSIC	CARBONIFEROUS
<i>Wasatch Blvd. Camp</i>	<i>5574</i>	Morrison	Pennsylvanian
Stone Cabin	Salt Wash	Oquirrh	Laketown Dolomite
Colton	San Rafael Gr.	Weber	ORDOVICIAN
Flagstaff	Summerville	Morgan	Eureka Quartzite
North Horn	Bluff Sandstone	Hermosa	Pogonip Limestone
Aimy	Curtis		CAMBRIAN
Paleocene	Entrada	Pardox	Lynch
Current Creek	Moab Tongue	Ismay	Bowman
North Horn	Carmel	Desert Creek	Tapeats
CRETACEOUS	Glen Canyon Gr.	Akah	Ophir
Montana	Navajo	Barker Creek	Tintic
Mesaverde	Kayenta		PRE - CAMBRIAN
Price River	Wingate	Cane Creek	
Blackhawk	TRIASSIC		

Petroglyph Operating Co., Inc.
P.O. Box 1839
Hutchinson, KS 67504-1839

October 3, 1997

Utah Division of Oil, Gas, & Mining
1594 West North Temple
Box 145801
Salt Lake City, UT 84114-5801



RE: APPLICATION FOR PERMIT TO DRILL
UTE TRIBAL #19-11
NE/SW, SEC. 19, T5S, R3W
DUCHESNE COUNTY, UTAH
LEASE NO. BIA 14-20-H62-3514
UTE TRIBAL LANDS

Enclosed please find a copy of the Application for Permit to Drill and associated attachments for the referenced well.

Please address further communication regarding this matter (including approval) to:

Ed Trotter
P.O. Box 1910
Vernal, UT 84078
Phone # (801) 789-4120
Fax # (801) 789-1420

Sincerely,

A handwritten signature in cursive script, appearing to read "Ed Trotter".

Ed Trotter
Agent

Petroglyph Operating Co., Inc.

Attachments

/EHT/dmt

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR DEEPEN

1a. TYPE OF WORK
 DRILL DEEPEN

b. TYPE OF WELL
 OIL WELL GAS WELL OTHER SINGLE ZONE MULTIPLE ZONE

2. NAME OF OPERATOR
 PETROGLYPH OPERATING COMPANY, INC.

3. ADDRESS AND TELEPHONE NO.
 P.O. BOX 607, ROOSEVELT, UTAH 84066

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.)
 At surface ⁶⁷⁸ 2226' FSL & 1484' FWL NE/SW
 At proposed prod. zone ⁴⁵²

14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*
 19.4 MILES SOUTHWEST OF MYTON, UTAH

15. DISTANCE FROM PROPOSED* LOCATION TO NEAREST PROPERTY OR LEASE LINE, FT. (Also to nearest drlg. unit line, if any) 1484' ±

16. NO. OF ACRES IN LEASE 640

17. NO. OF ACRES ASSIGNED TO THIS WELL 80

18. DISTANCE FROM PROPOSED LOCATION* TO NEAREST WELL, DRILLING, COMPLETED, OR APPLIED FOR, ON THIS LEASE, FT. 5714.6'

19. PROPOSED DEPTH 5714.6'

20. ROTARY OR CABLE TOOLS ROTARY

21. ELEVATIONS (Show whether DF, RT, GR, etc.) 6077.6' GRADED GROUND

22. APPROX. DATE WORK WILL START* OCTOBER 1997

5. LEASE DESIGNATION AND SERIAL NO.
14-20-H62-3514

6. IF INDIAN, ALLOTTEE OR TRIBE NAME
UTE INDIAN TRIBE

7. UNIT AGREEMENT NAME

8. FARM OR LEASE NAME, WELL NO.
UTE TRIBAL

9. AP WELL NO.
#19-11

10. FIELD AND POOL, OR WILDCAT
ANTELOPE CREEK

11. SEC., T., R., M., OR BLK. AND SURVEY OR AREA
SEC. 19, T5S, R3W

12. COUNTY OR PARISH
DUCHESNE

13. STATE
UTAH

CONFIDENTIAL


PROPOSED CASING AND CEMENTING PROGRAM

SIZE OF HOLE	GRADE SIZE OF CASING	WEIGHT PER FOOT	SETTING DEPTH	QUANTITY OF CEMENT
12 1/4	8 5/8	24.0#	250'	135 sx class "G" + 2% CaCl ₂ + 1/4 #/sx celloflake. 50/50 POZMIX + 2% GEL + 10% SALT TO 400' ABOVE ALL ZONES OF INTEREST (+ 10% EXCESS). LIGHT CEMENT (11 PPG+) + LCM TO 200' ABOVE OIL SHALE OR FRESH WATER INTERVALS (+ 5% EXCESS).
7 7/8	5 1/2	15.5#	5714.6'	

CONFIDENTIAL

PETROGLYPH OPERATING COMPANY, INC. WILL BE THE DESIGNATED OPERATOR OF THE SUBJECT WELL UNDER BOND #4556.

pc: Utah Division of Oil, Gas, and Mining
Bureau of Indian Affairs, Fort Duchesne, Utah
Ute Tribe, Fort Duchesne, Utah



IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24. SIGNED [Signature] TITLE AGENT FOR PETROGLYPH DATE 10-8-97

(This space for Federal or State office use)

PERMIT NO. 43-013-31967 APPROVAL DATE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. CONDITIONS OF APPROVAL, IF ANY:

APPROVED BY [Signature] TITLE Associate Director DATE 10/27/97

*See Instructions On Reverse Side

T5S, R3W, U.S.B.&M.

PETROGLYPH OPERATING CO., INC.

Well Location, UTE TRIBAL #19-11, located as shown in the NE 1/4 SW 1/4 of Section 19, T5S, R3W, U.S.B.&M. Duchesne County, Utah.

S89°57'E - 80.02 (G.L.O.)

Set Stone,
Pile of Stones

NORTH (G.L.O.)

NOTE:
BASIS OF BEARINGS IS THE WEST
LINE OF SECTION 30, T5S, R3W,
U.S.B.&M. WHICH IS ASSUMED FROM
G.L.O. INFORMATION TO BEAR NORTH.

5267.91' (Meas.)

Set Marked
Stone

19

UTE TRIBAL #19-11
Elev. Ungraded Ground - 6079'

1484'

N00°00'08"W

2226'

Set Marked
Stone

Set Marked
Stone,
Pile of Stones


N00°07'21"W 2638.45' (Meas.)

1 1/2" Galv. Cap, N89°55'36"E 2622.17' (Meas.)
Set Marked Stone,
Steel Post & Pile
of Stones

N89°59'02"E 2643.66' (Meas.)

BASIS OF ELEVATION

SPOT ELEVATION AT THE NORTHWEST CORNER OF SECTION 30, T5S, R3W, U.S.B.&M. TAKEN FROM THE DUCHESNE SE QUADRANGLE, UTAH, DUCHESNE COUNTY, 7.5 MINUTE SERIES (TOPOGRAPHICAL MAP) PUBLISHED BY THE UNITED STATES DEPARTMENT OF THE INTERIOR, GEOLOGICAL SURVEY. SAID ELEVATION IS MARKED AS BEING 6116 FEET.

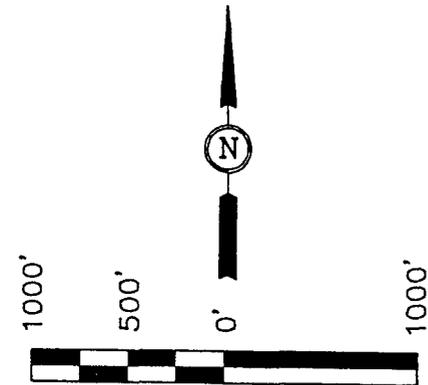

SCALE

CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

REGISTERED LAND SURVEYOR,
REGISTRATION NO. 161319
STATE OF UTAH

UINTAH ENGINEERING & LAND SURVEYING

85 SOUTH 200 EAST - VERNAL, UTAH 84078

(801) 789-1017

LEGEND:


└─┘ = 90° SYMBOL

● = PROPOSED WELL HEAD.

▲ = SECTION CORNERS LOCATED.

SCALE 1" = 1000'	DATE SURVEYED: 4-28-97	DATE DRAWN: 6-25-97
PARTY B.B. D.R. J.L.G.	REFERENCES G.L.O. PLAT	
WEATHER WARM	FILE PETROGLYPH OPERATING CO., INC.	

State of Utah
Division of Oil, Gas & Mining
1594 West North Temple
Box 145801
Salt Lake City, UT 84114-5801



October 8, 1997

RE: Application for Exception Well Location
Proposed Ute Tribal #19-11
Township 5 South, Range 3 West
Section 19: NE/4 SW/4
Duchesne County, Utah

Gentlemen;

Petroglyph Operating Company, Inc. (Petroglyph) respectfully requests administrative approval per R-649-3-3 to drill the Ute Tribal #19-11 a 5715' Green River test, at a location 2226' FSL & 1484' FWL, NE/4 SW/4, Section 19, Township 5 South Range 3 West, Duchesne County, Utah.

The aforementioned footage is not a location at which a well could be drilled in compliance with the spacing order of this lease, which established 40 acre drilling units.

Enclosed is a topographic map which depicts the surface contour in the area of the subject location. Petroglyph believes the proposed exceptionally spaced location to be the preferred location from a construction standpoint. Also this location is preferred by the Bureau of Indian Affairs Resource Department and the Ute Indian Tribe, Energy and Minerals Department who regulate activities on this land.

Petroglyph Operating Company Inc. holds 100% of the operating rights underlying the subject drilling unit as well as drilling units to the north, south, east and west.

Petroglyph respectfully requests the Division of Oil, Gas and Mining Administratively grant this application for the exceptional well location at its earliest opportunity.

Please direct further correspondence and approval to myself at P.O. Box 1910, Vernal, Utah 84078, or phone me at 801-789-4120.

Sincerely,

A handwritten signature in cursive script, appearing to read "Ed Trotter".

Petroglyph Operating Company Inc.
Ed Trotter, Agent


R
4
W

R
3
W

BRIDGELAND 7.6 MI. +/-
MYTON 19.3 MI. +/-

PROPOSED LOCATION:
UTE TRIBAL #19-11

PROPOSED ACCESS 0.1 MI. +/-

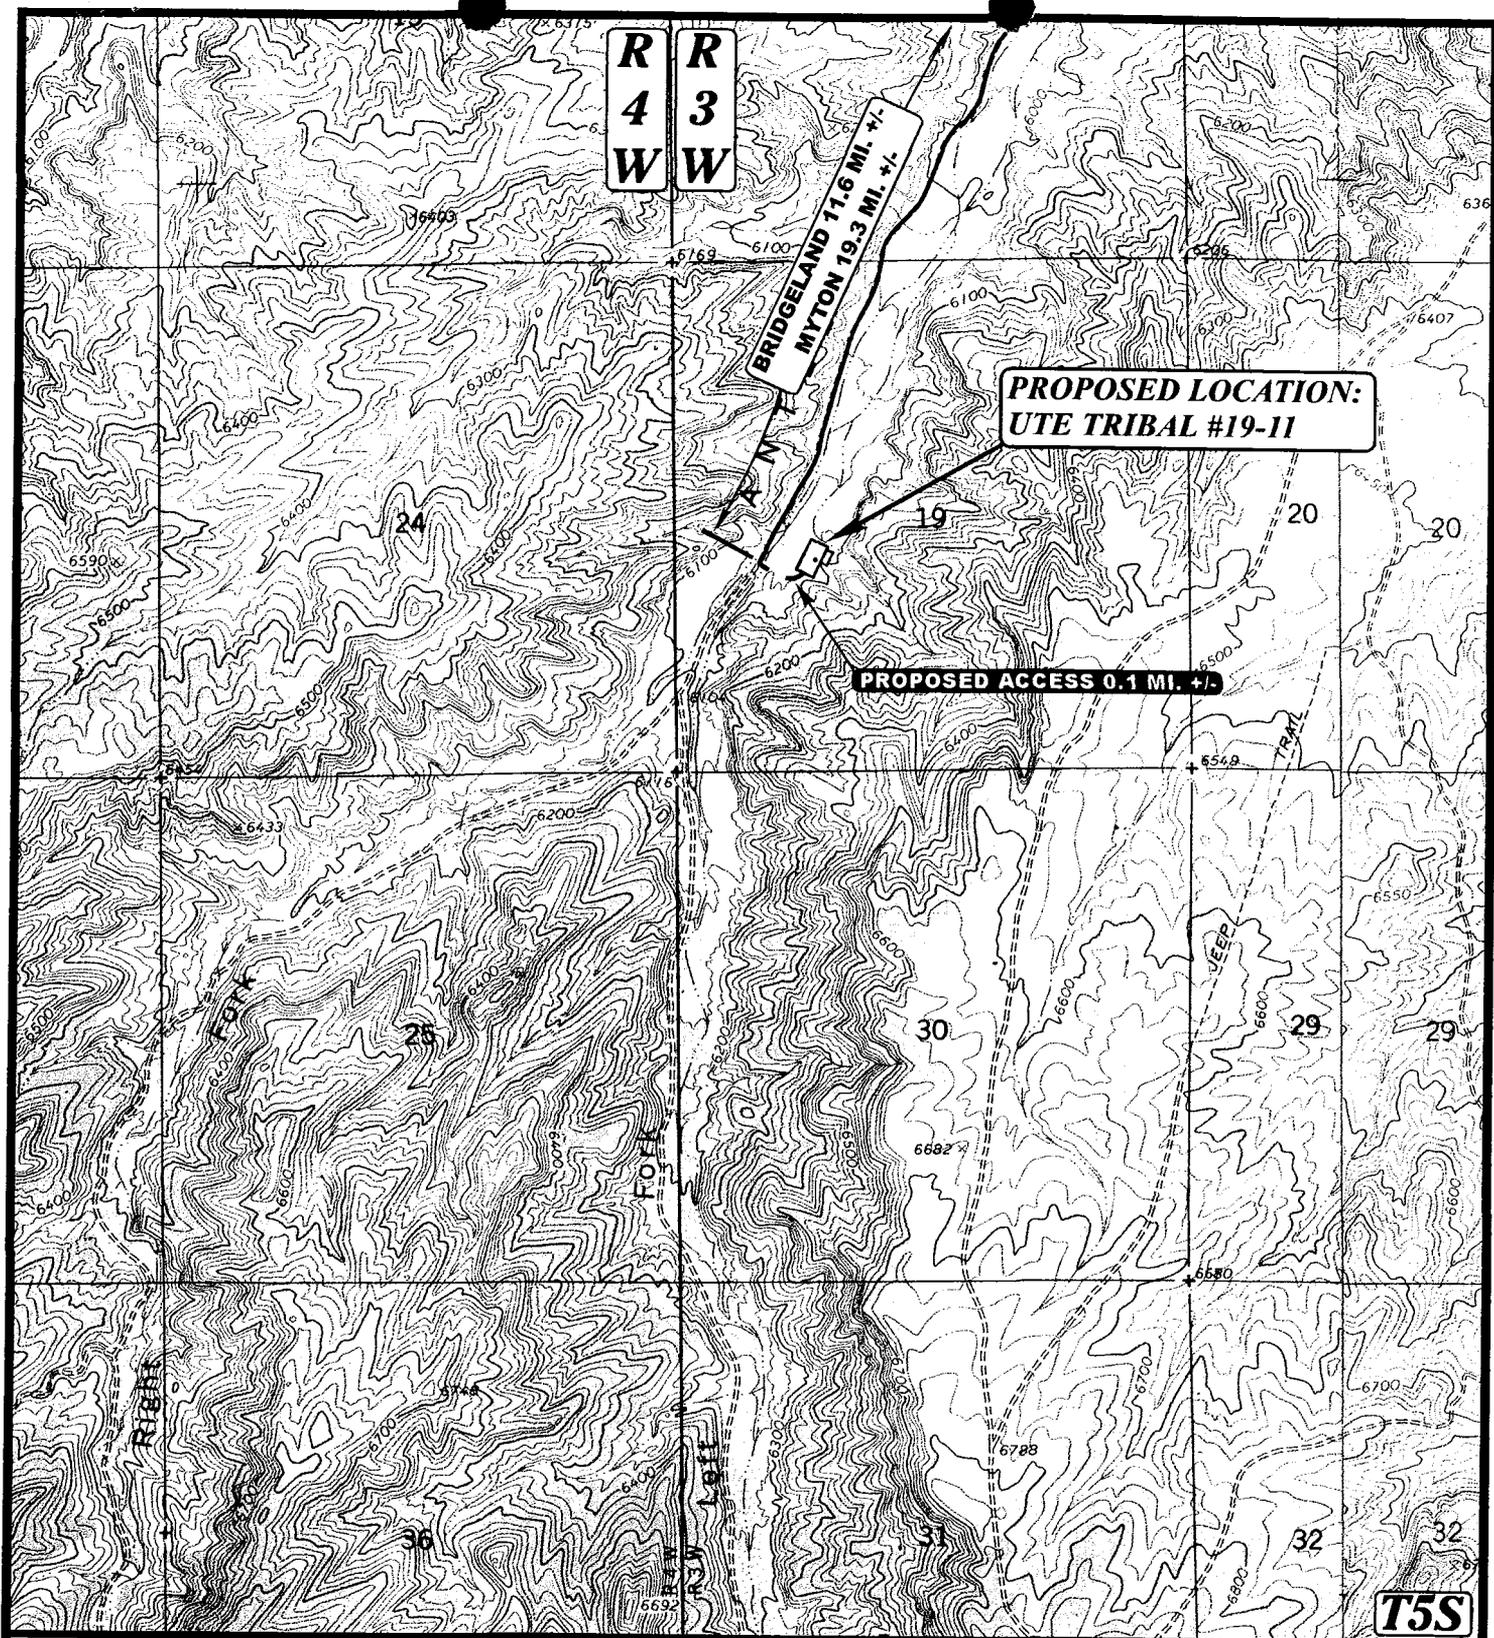

T5S

LEGEND:

- PROPOSED ACCESS ROAD
- EXISTING ROAD

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #19-11
SECTION 19, T5S, R3W, U.S.B.&M.
2226' FSL 1484' FWL



U E I S
Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(801) 789-1017 * FAX (801) 789-1813
Email: uels@easilink.com

TOPOGRAPHIC 6 21 97
MAP MONTH DAY YEAR
SCALE: 1" = 2000' DRAWN BY: D.COX REVISED: 00-00-00

B
TOPO

EIGHT POINT PLAN

UTE TRIBAL #19-11
NE/SW, SEC. 19, T5S R3W
DUCHESNE COUNTY, UTAH

1. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

FORMATIONS	DEPTH	SUBSEA
Mahogany Shale	2521.6	3566
"X" Marker	4099.6	1988
Douglas Creek	4231.6	1856
"B" Limestone	4624.6	1463
B/Castle Peak Limestone	5188.6	899
Basal Carbonate Limestone	5804.6	483
Total Depth	5714.6	373

Anticipated BHP 2000 psi

2. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS FORMATIONS:

<u>Substance</u>	<u>Formation</u>	<u>Depth</u>	<u>Subsea</u>
Oil/Gas	Douglas Creek	4231.6	1856
Oil/Gas	B/Castle Peak	5186.6	899
Other mineral zones	N/A		

3. PRESSURE CONTROL EQUIPMENT : BOP Schematic Diagram attached.

4. CASING PROGRAM :

<u>HOLE SIZE</u>	<u>INTERVAL</u>	<u>LENGTH</u>	<u>SIZE</u>	<u>WEIGHT</u>	<u>GRADE</u>	<u>MINIMUM SAFETY FACTOR</u>		
						<u>COLLAPSE</u>	<u>BURST</u>	<u>TENSILE</u>
12 1/4	0' - 250'	250'	8 5/8	24.0 #	J-55	1370 PSI	2950 PSI	263,000#
7 7/8	0' - 5714.6'	5714.6'	5 1/2	15.5 #	M-50	3650 PSI	4550 PSI	186,000#

All casing will be new or inspected.

EIGHT POINT PLAN

UTE TRIBAL #19-11
NE/SW, SEC. 19, T5S R3W
DUCHESNE COUNTY, UTAH

5. MUD PROGRAM

<u>INTERVAL</u>	<u>MUD TYPE</u>
0' - 250'	Air
250' - 4000'	Air/Mist & Aerated Water
4000' - TD	Air/3% KCL water or KCL substitute
TD	Gel/polyacrylamide polymer w/5-10% LCM

Sufficient mud inventory will be maintained on location during drilling to handle any adverse conditions that may arise.

6. VARIANCE REQUESTS:

- A. Petroglyph Operating Co., Inc. requests a variance to regulations requiring a straight run blooie line.
- B. Petroglyph Operating Co., Inc. requests a variance to regulations requiring an automatic ignitor or continuous pilot light on the blooie line.

7. EVALUATION PROGRAM:

Logs: Mud Logging	T.D. to base of surface csg.
Compensated Density-Compensated Neutron Log	T.D. to base of surface csg.
Dual Laterolog - Micro-SFL	T.D. to base of surface csg.
Numar (Magnetic Resonance Imaging Log)	@ Geologists discretion

Cores: None Programmed

DST: None Programmed

Completion: To be submitted at a later date.

8. ABNORMAL CONDITIONS:

None anticipated.

EIGHT POINT PLAN

UTE TRIBAL #19-11
NE/SW, SEC. 19, T5S R3W
DUCHESNE COUNTY, UTAH

9. STANDARD REQUIRED EQUIPMENT:

- A. Choke Manifold
- B. Kelly Cock
- C. Stabbing Valve
- D. Visual Mud Monitoring

10. HAZARDOUS CHEMICALS:

No chemicals subject to reporting under SARA title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling of this well.


(Attachment: BOP Schematic Diagram)


2000 PSIG DIAGRAM

BOTH RAMS ARE 2000 PSIG RATED.
 CASING FLANGE IS 9" 2000 PSIG RATED.
 BOPE 9" 2000 PSIG

TESTING PROCEDURE:

1. BOPE 's will be tested with a professional tester to conform to Onshore Order #2 with retest every 14 days.
2. Blind & Pipe rams will be tested to rated working pressure, 2000 psig
3. Casing will be tested to 0.22 psi/ft. or 1500 psig. Not to exceed 70% of burst strength, whichever is greater.
4. All lines subject to well pressure will be pressure tested to the same pressure as blind & pipe rams.
5. All BOPE specifications and configurations will meet Onshore Order #2 requirements for 2000 psig BOPE specifications.

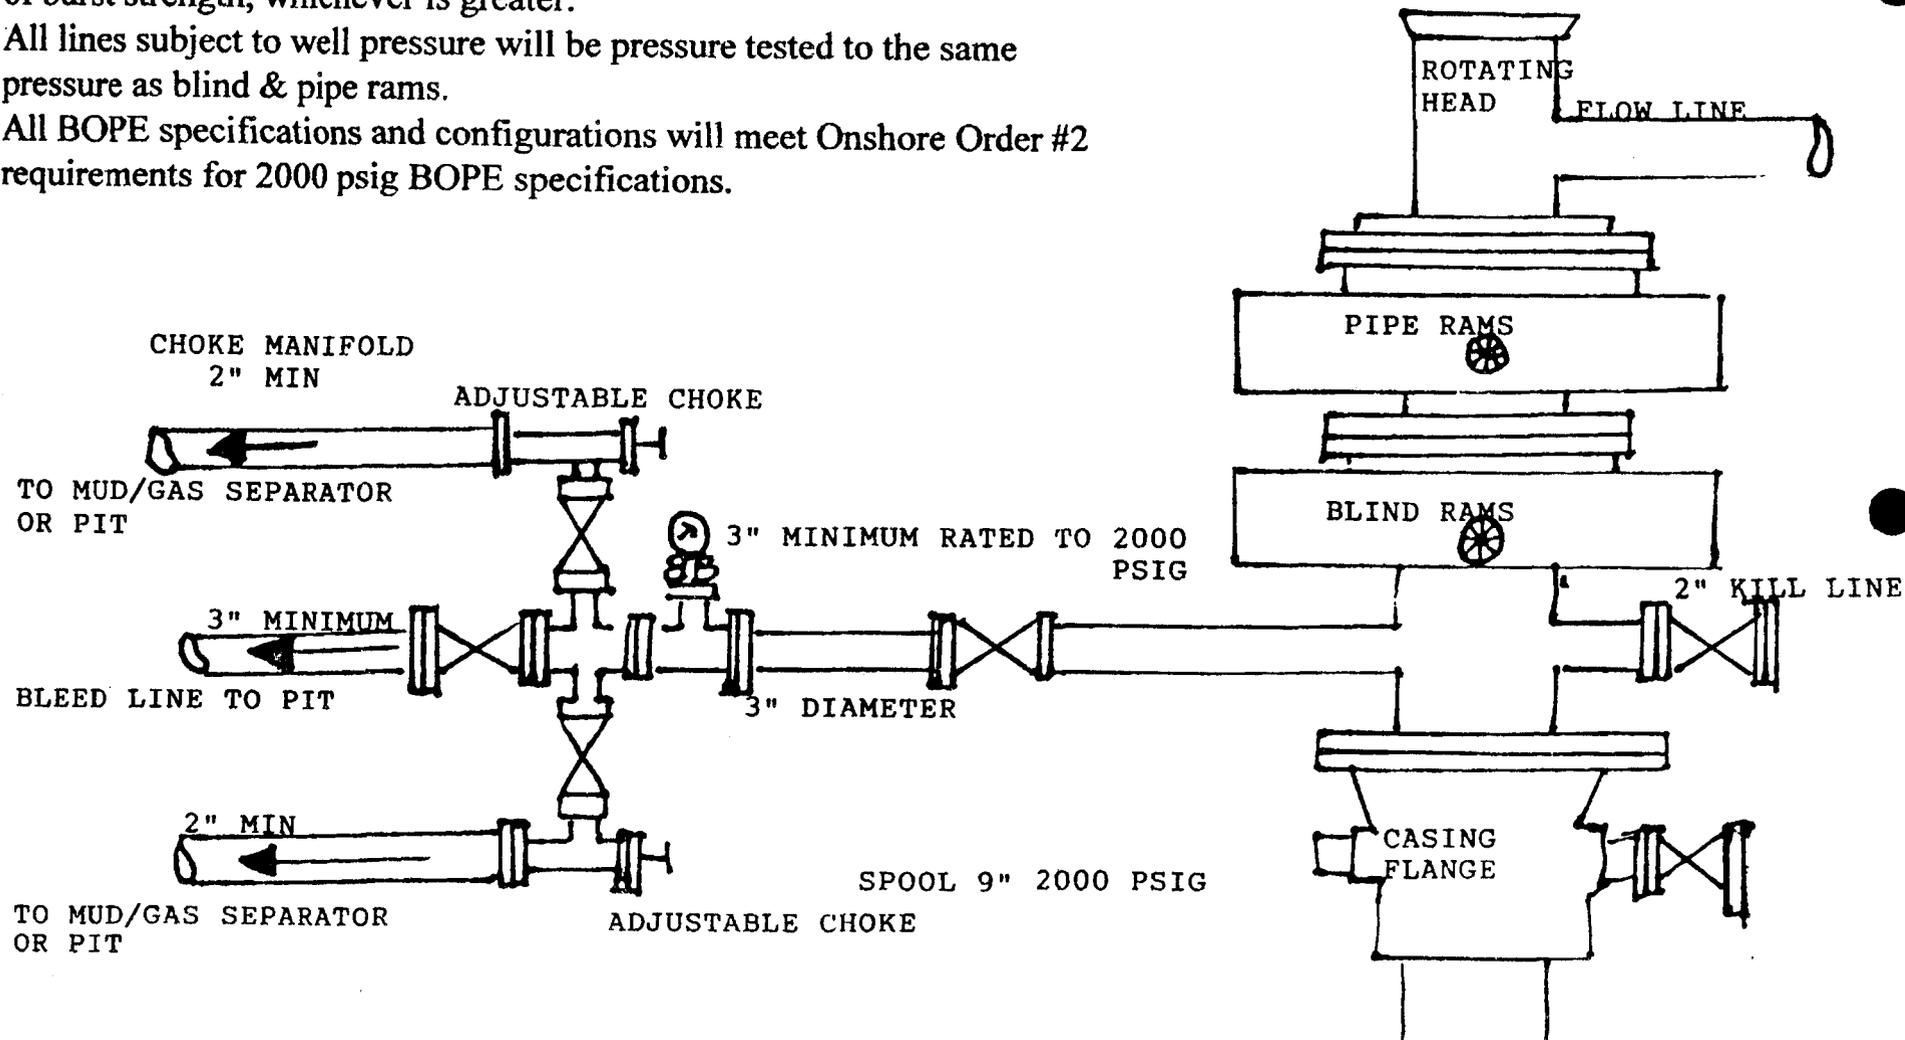



CONDITIONS OF APPROVAL
FOR THE SURFACE USE PROGRAM OF THE
APPLICATION FOR PERMIT TO DRILL

Company/Operator: Petroglyph Operating Co., Inc.
Well Name & Number: Ute Tribal #19-11
Lease Number: BIA 14-20-H62-3514
Location: 2226' FSL & 1484' FWL NE/SW, Sec. 19, T5S R3W
U.S.B.&M., Duchesne County, Utah
Surface Ownership: Ute Indian Tribe

NOTIFICATION REQUIREMENTS

- Location Construction - forty-eight (48) hours prior to construction of location and access roads.
- Location Completion - prior to moving on the drilling rig.
- Spud Notice - at least twenty-four (24) hours prior to spudding the well.
- Casing String and Cementing - twenty-four (24) hours prior to running casing and cementing all casing strings.
- BOP and related Equipment Tests - twenty-four (24) hours prior to running casing and tests.
- First Production Notice - within five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

For more specific details on notification requirements, please check the Conditions of Approval for Notice To Drill and Surface Use Program.

THIRTEEN POINT SURFACE USE PROGRAM

1. EXISTING ROADS

- A. See attached Wellsite Plats showing directional reference stakes on location, and attached TOPO Map "B" showing access to location from existing road.
- B. The proposed well site is located approximately 19.4 miles southwest of Myton, Utah - See attached TOPO Map "A".
- C. Refer to attached Topographic Map "A" showing labeled access route to location.
- D. Existing roads will be maintained and repaired as necessary. No off lease Right-of-Way will be required.

2. PLANNED ACCESS ROAD

- A. The access road will be approximately 0.1 miles in length. See attached TOPO Map "B".
- B. The access road has a 30 foot ROW w/18 foot running surface.
- C. Maximum grade on access road will be 8%
- D. No turnouts will be required.
- E. Road drainage crossings shall be of the typical dry creek drainage crossing type.
- F. No culverts, bridges or major cuts & fills will be required.
- G. The access road will be dirt surface.
- H. No gates, cattleguards or fences will be required or encountered.

New or reconstructed roads will be centerlined - flagged at time of location staking.

All travel will be confined to existing access road Right-of-Way. Access roads and surface disturbing activities will conform to standards outlined in the Bureau of Land Management and Forest Service Publication: Surface Operating Standards For Oil & Gas Exploration and Development, (1989).

The road shall be upgraded to meet the standards of the anticipated traffic flow and all-weather road requirements. Upgrading shall include ditching, drainage, graveling, crowning, and capping the

roadbed as necessary to provide a well-constructed safe road.

Prior to upgrading, the road shall be cleared of any snow cover and allowed to dry completely. Traveling off the 30 foot Right-of- Way will not be allowed.

Road drainage crossings shall be of the typical dry creek drainage crossing type. Crossings shall be designed so they will not cause siltation or accumulation of debris in the drainage crossings nor shall the drainages be blocked by the roadbed. Erosion of drainage ditches by run off water shall be prevented by diverting water off at frequent intervals by means of cutouts. Upgrading shall not be allowed during muddy conditions. Should mud holes develop, they shall be filled in and detours around them avoided.

As operator, Petroglyph Operating Co., Inc. shall be responsible for all maintenance on cattleguards, or gates associated with this oil and/or gas operation.

3. LOCATION OF EXISTING WELLS WITHIN A ONE MILE RADIUS OF PROPOSED WELL LOCATION

- A. Water wells - None
- B. Abandoned wells - None
- C. Temporarily abandoned wells - None.
- D. Disposal wells - None.
- E. Drilling wells - None.
- F. Producing wells - 6*
- G. Shut in wells - 1*
- H. Injection wells - 1*

(*See attached TOPO map "C" for location)

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

A. ON WELL PAD

- 1. Tank batteries - None
- 2. Production facilities-To be submitted later
- 3. Oil gathering lines - None

4. Gas gathering lines-None
5. Injection lines - None
6. Disposal lines - None
7. Surface pits - None

B. OFF WELL PAD

1. Proposed location of attendant off pad flowlines shall be flagged prior to archaeological clearance.
2. A 4 1/2" OD steel above ground production pipeline will be laid approximately 500' from proposed location to a point in the NW/SW of Section 19, T5S, R3W, where it will tie into Petroglyph Operating Co., Inc.'s existing pipeline. Proposed pipeline crosses Ute Tribe lands, thus a Right-of-Way grant will be required. See attached TOPO Map D showing pipeline route.
3. Proposed pipeline will be a 4 1/2" OD steel, welded line laid on the surface.
4. Protective measures and devices for livestock and wildlife will be taken and/or installed where required.

If storage facilities/tank batteries are constructed on this lease, the facility/battery or the well pad shall be surrounded by a containment dike of sufficient capacity to contain, at a minimum, the entire contents of the largest tank within the facility/battery, unless more stringent protective requirements are deemed necessary by the authorized officer.

The production facilities will be placed on the Northwest side of the location.

All permanent (on site for six months or longer) structures constructed or installed (including pumping units) will be painted a flat, non-reflective, earthtone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities required will be painted within 6 months of installation. Facilities required to comply with O.S.H.A.

(Occupational Safety and Health Act) will be excluded.
The required paint color is Desert Brown.

5. LOCATION & TYPE OF WATER SUPPLY

- A. Water supply will be from Target Trucking's Roosevelt Brine Storage and/or Target's water source in SE 1/4, Sec. 1, T 4S, R 5W Duchesne County, Utah (State water right #43-10152). All water will come from a non-depletable source.
- B. Water will be hauled by Target Trucking.
- C. No water well will be drilled on lease.

6. SOURCE OF CONSTRUCTION MATERIAL

- A. All construction material for this location and access road will be of native borrow and soil accumulated during the construction of location.
- B. All construction material will come from Ute Tribal Land.
- C. No mineral materials will be required.

7. METHODS OF HANDLING WASTE DISPOSAL

A. METHODS AND LOCATION

- 1. Cuttings will be confined in the reserve pit.
- 2. A portable toilet will be provided for human waste during the drilling and completion of the well. Disposal will be at the Vernal sewage disposal plant.
- 3. Burning will not be allowed. Trash and other waste material will be contained in a wire mesh cage and disposed of at an approved waste disposal facility.
- 4. Produced waste water will be confined to a lined pit or storage tank for a period not to exceed 90 days after initial production. During the 90 day period, an application for approval of a permanent disposal method and location, together with the required water analysis, will be submitted for the AO's approval.

5. All chemicals will be disposed of at an authorized disposal site. Drip pans and absorbent pads will be used on drilling rig to avoid leakage of oil to pit.

B. Water from drilling fluids and recovered during testing operations will be disposed of by either evaporating in reserve pit or be removed and disposed of at an authorized disposal site. Introduction of well bore hydrocarbons to reserve pit will be avoided by flaring them off in flare pit at time of recovery.

Burning of trash will not be allowed. All trash must be contained in a trash cage and hauled away to an approved disposal site at the completion of the drilling activities.

On BIA administered land:

All reserve pits will be lined with either native clay, commercial bentonite or plastic sufficient to prevent seepage. (If a plastic nylon reinforced liner is used, it shall be torn and perforated after the pit dries and before backfilling of the reserve pit).

A 12 mill liner shall be installed in the reserve pit.

To protect the environment:

If the reserve pit is lined the operator will provide the BIA with a chemical analysis of the fluids in that pit no later than 90 days after the well completion to determine the method for final reclamation of the reserve pit. If the elemental concentrations shown by the chemical analysis exceeds the requirements described by part II, Standards of Quality for Waters of the State, Wastewater Disposal Regulations, State of Utah Division of Health, the contents and liner will be removed and disposed of at an authorized disposal site.

To protect the environment (without a chemical analysis)
reserve pits will be constructed so as not to leak, break, or allow discharge of liquids.

Storage tanks will be used if drill sites are located on tribal

irrigable land, flood plains, or on lands under crop production. After first production, produced waste water will be confined to a lined pit or storage tank for a period not to exceed ninety (90) days. During the 90 day period, in accordance with NTL-2B, an application for approval of a permanent disposal method and location, along with required water analysis, shall be submitted for the AO's approval. Failure to file an application within the time allowed will be considered an incident of noncompliance.

8. ANCILLARY FACILITIES

- A. No airstrips or camps are planned for this well.

9. WELL SITE LAYOUT

- A. Refer to attached well site plat for related topography cuts and fills & cross sections.
- B. Refer to attached well site plat for rig layout and soil material stockpile location as approved on On-site.
- C. Refer to attached well site plat for rig orientation parking areas, and access road.

The reserve pit will be located on the Southeast side of the location. The flare pit will be located downwind of the prevailing wind direction on the Southeast side of the location, a minimum of 100 feet from the well head and 30 feet from the reserve pit fence. The stockpiled topsoil will be stored on the West side.

Access to the well pad will be from the West.

N/A Diversion ditch(es) shall be constructed on the _____ side of the location (above/below) the cut slope, draining to the _____

N/A Soil compacted earthen berm(s) shall be placed on the _____ side(s) of the location between the _____

N/A The drainage(s) shall be diverted around the sides of the well pad location.

N/A The reserve pit and/or pad locations shall be constructed long and narrow for topographic reasons _____

N/A Corner No. will be rounded off to minimize excavation.

FENCING REQUIREMENTS

All pits will be fenced according to the following minimum standards:

- A. 39 inch net wire shall be used with at least one strand of barbed wire on top of the net wire. (barbed wire is not necessary if pipe or some type of reinforcement rod is attached to the top of the entire fence).
- B. The net wire shall be no more than 2 inches above the ground. The barbed wire strand shall be 3 inches above the net wire. Total height of the fence shall be at least 42 inches.
- C. Corner posts shall be cemented and/or braced in such a manner to keep the fence tight at all times.
- D. Standard steel, wood, or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than 16'.
- E. All wire shall be stretched by using a stretching device before it is attached to the corner posts.

The reserve pit fencing will be on the three sides during drilling operations and on the fourth side when the rig moves off the location. Pits will be fenced and maintained until clean-up.

Each existing fence to be crossed by the access road shall be braced and tied off before cutting so as to prevent slacking of the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BIA or SMA specifications. A cattleguard with an adjacent 16 foot gate shall be installed in any fence where a road is to be regularly travelled. If the well is a producer, the cattleguards (shall/ shall not) be permanently mounted on concrete bases. Prior to a new road, crossing any fence located on federal land, or any fence between federal land and private land, the operator will contact the BIA, who will in turn contact the grazing permittee or owner of said fence and offer him/her the opportunity to be present when the fence is cut in order to

satisfy himself/herself that the fence is adequately braced and tied off.

10. PLANS FOR RESTORATION OF SURFACE

A. PRODUCING LOCATION

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, materials, trash, and junk not required for production.

Immediately upon well completion, any hydrocarbons on the pit shall be removed in accordance with CFR 3162.7-1.

If a plastic nylon reinforced liner is used, it shall be torn and perforated before backfilling of the reserve pit.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximate natural contours. The reserve pit will be reclaimed within 120 days from the date of well completion (weather permitting). Before any dirt work takes place, the reserve pit will be completely dry and all cans, barrels, pipe, fluid, and hydrocarbons, will be removed.

Contact appropriate surface management agency for required seed mixture.

B. DRY HOLE/ABANDONED LOCATION

At such time as the well is plugged and abandoned, the operator will submit a subsequent report of abandonment and BIA will attach the appropriate surface rehabilitation conditions of approval.

ON BIA Administered lands:

Abandoned well sites, roads, or other disturbed areas will be restored to near their original condition. This procedure will include: (a) reestablishing irrigation systems where applicable, (b) reestablishing soil conditions in irrigated fields in such a way as to ensure cultivation and harvesting of crops and, (c) ensuring revegetation of the disturbed areas to the specifications of the Ute Indian Tribe or the BIA at the time of abandonment.

11. SURFACE OWNERSHIP

Access road: Ute Indian Tribe

Location: Ute Indian Tribe

12. OTHER INFORMATION

- A. Petroglyph Operating Co., Inc. will inform all persons in the area who are associated with this project that they are subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, the operator will immediately stop work that might further disturb such materials, and contact the AO. Within five working days the AO will inform the operator as to:
- whether the materials appear eligible for the National Register of historic Places;

the mitigation measures the operator will likely have to undertake before the site can be used.

-a time frame for the AO to complete an expedited review under 36 CFR 800.11 to confirm, through the State Historic Preservation Officer, that the findings of the AO are correct and that mitigation is appropriate.

If the operator wished, at any time, to relocate activities to avoid the expense of mitigation and/or the delays associated with this process, the AO will assume responsibility for whatever recordation and stabilization of the exposed materials that may be required. Otherwise, the operator will be responsible for mitigation costs. The AO will provide technical and procedural guidelines for the conduct of mitigation. Upon verification from the AO that required mitigation has been completed, the operator will then be allowed to resume construction.

- B. As operator, Petroglyph Operating Co., Inc. will control noxious weeds along Right-of-Ways for roads, pipelines, well sites, or other applicable facilities. A list of noxious weeds will be obtained from the BIA,

or the appropriate County Extension Office. On BIA administered land, a Pesticide Use proposal shall be submitted, and given approval, prior to the application of herbicides or other pesticides or possible hazardous chemicals.

- C. Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on Tribal Lands after the conclusion of drilling operations or at any other time without BIA authorization. However, if BIA authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

On BIA administered land:

Operator's employees, including subcontractors, will not gather firewood along roads constructed by operators. If wood cutting is required, a permit will be obtained from the Forestry Department of the BIA pursuant to 25 CFR 169.13 "Assessed Damages Incident to Right-of-Way authorization". All operators, subcontractors, vendors, and their employees or agents may not disturb saleable timber (including firewood) without a duly granted wood permit from the BIA Forester.

If the surface rights are owned by the Ute Indian Tribe and mineral rights are owned by another entity, an approved right-of-way will be obtained from the BIA before the operator begins any construction activities. If the surface is owned by another entity and the mineral rights are owned by the Ute Indian Tribe, rights-of-way will be obtained from the other entity.

All roads constructed by operators on the Uintah and Ouray Indian Reservation will have appropriate signs. Signs will be neat and of sound construction. They will state: (a) that the land is owned by the Ute Indian Tribe, (b) the name of the operator, (c) that firearms are prohibited to all non-Ute Tribal members (d) that permits must be obtained from the BIA before cutting firewood or other timber products, and (e) only authorized personnel permitted. All well site locations on the Uintah and Ouray Indian Reservation will have an appropriate sign indicating the name of the operator,

the lease serial number, the well name and number, the survey description of the well (either footage or the quarter-quarter section, the section, township, and range).

Additional Surface Stipulations

N/A No construction or drilling activities shall be conducted between

_____ and _____ because of _____

N/A No surface occupancy will be allowed within 1,000 feet of any sage grouse strutting ground.

N/A No construction or exploration activities are permitted within 1.5 mile radius of sage grouse strutting grounds from April 1 to June 30.

N/A There shall be no surface disturbance within 600 feet of live water (includes stock tanks, springs, and guzzlers).

N/A No cottonwood trees will be removed or damaged.

N/A Pond will be constructed according to BLM specifications approximately _____ ft. _____ of the location, as flagged on onsite.

LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION

PERMITTING

Ed Trotter
1620 West 750 North
Vernal UT 84078
Telephone # (801)789-4120
Fax # (801) 789-1420

OPERATIONS

Vince Guinn
P.O. Box 607
Roosevelt, UT 84066
(801) 722-2531
Fax # (801) 722-9145

All lease/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws, regulations, Onshore Oil and Gas Orders, the approval plan of operations, and any applicable Notice to Lessees. Petroglyph Operating Co., Inc. is fully responsible for the actions of their subcontractors. A copy of these conditions will be furnished to the field representative to insure compliance.

A copy of the approved APD and ROW grant, if applicable, shall be on location during construction of the location and drilling activities.

The BIA Office shall be notified upon site completion prior to moving on the drilling rig.

Certification:



I hereby certify that I, or persons under my direct supervision, have inspected the proposed drillsite and access route; that I am familiar with the conditions which presently exist; that the statements made in the Plan are to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed by Petroglyph Operating Co., Inc. and its contractors and sub-contractors in conformity with this Plan and the terms and conditions under which it is approved.

Date

PETROGLYPH OPERATING CO., INC.

LOCATION LAYOUT FOR


UTE TRIBAL #19-11
SECTION 19, T5S, R3W, U.S.B.&M.
2226' FSL 1484' FWL

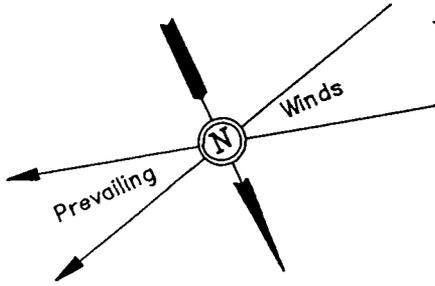

Sta. 2+90

SCALE: 1" = 50'
DATE: 6-25-97
Drawn By: J.L.G.

NOTE:
Flare Pit is to be located a min. of 100' from the Well Head.

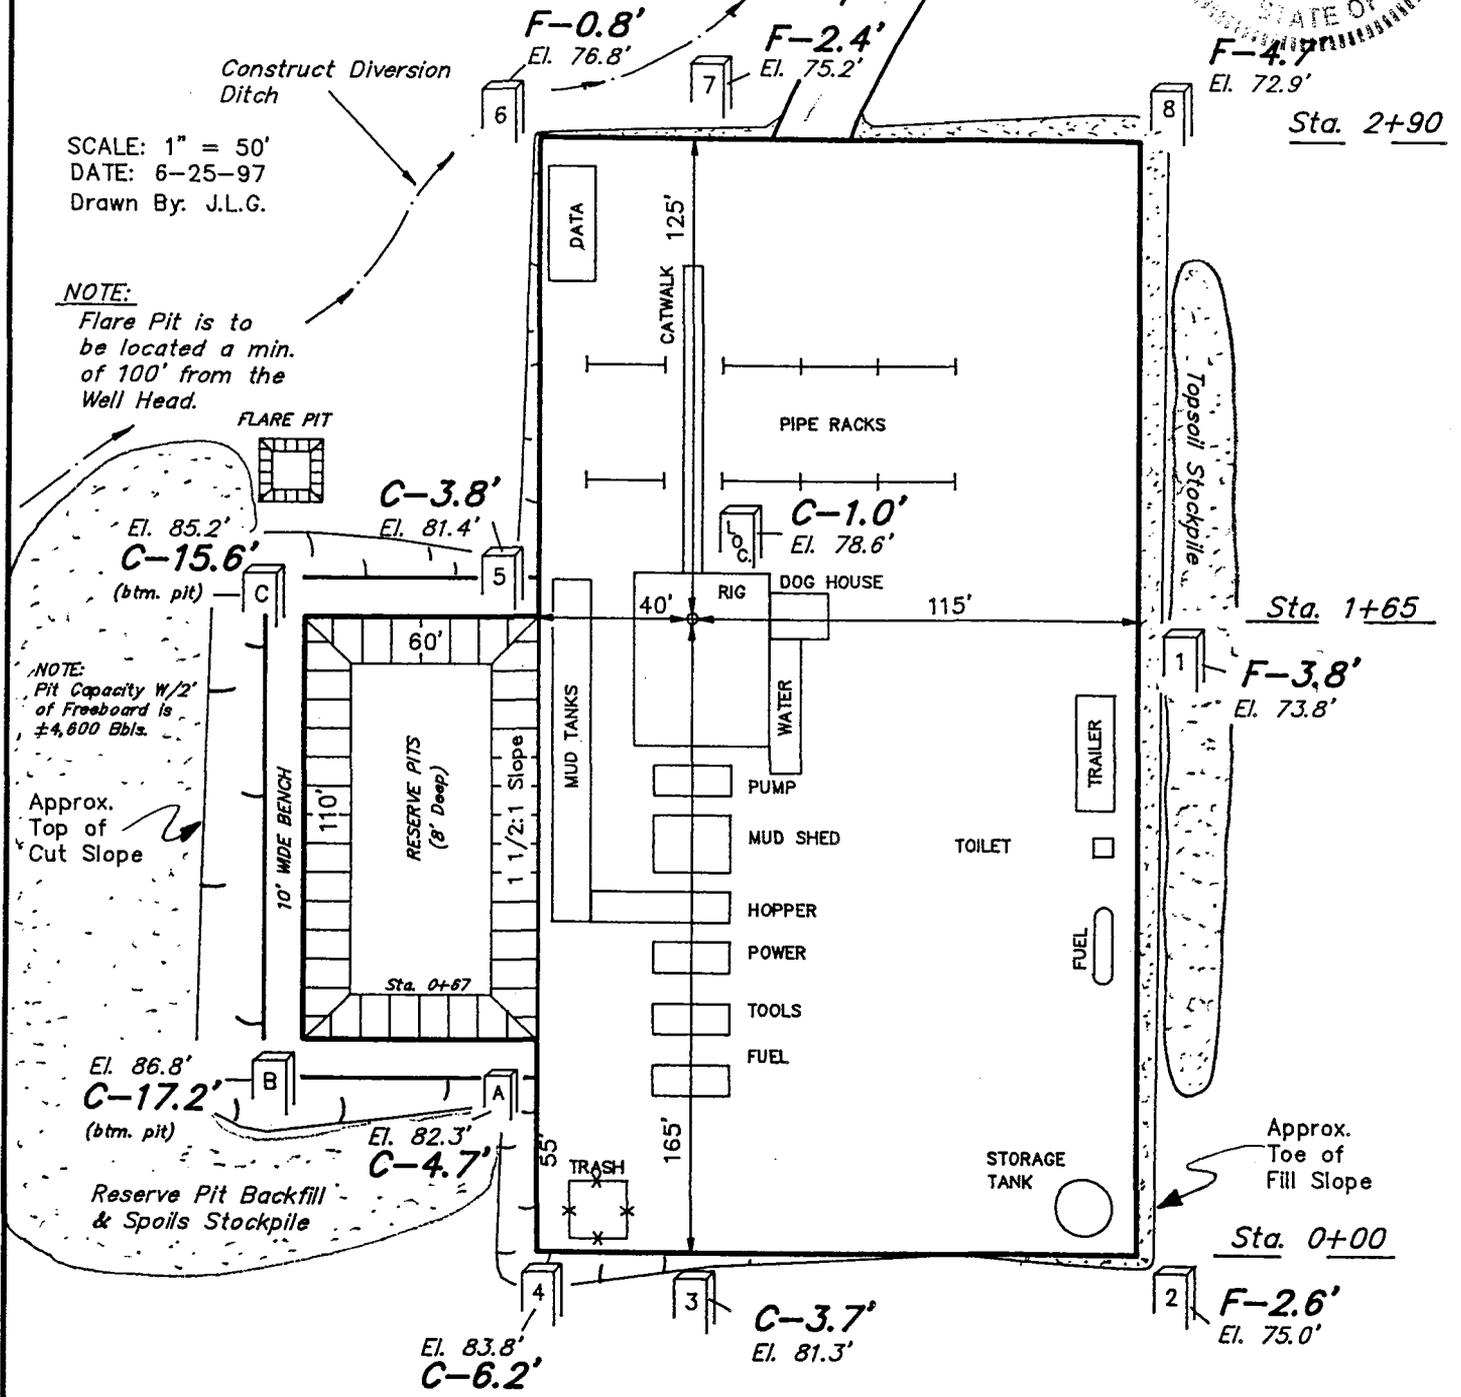



Elev. Ungraded Ground at Location Stake = 6078.6'

Elev. Graded Ground at Location Stake = 6077.6'





PETROGLYPH OPERATING CO., INC.

TYPICAL CROSS SECTIONS FOR

UTE TRIBAL #19-11
SECTION 19, T5S, R3W, U.S.B.&M.
2226' FSL 1484' FWL



DATE: 6-25-97
Drawn By: J.L.G.

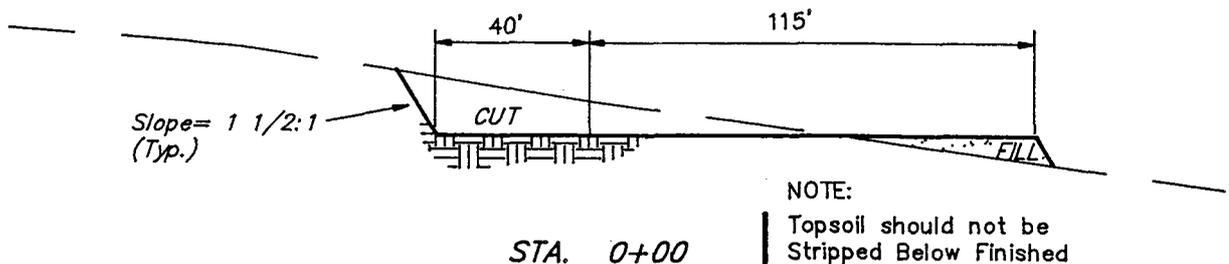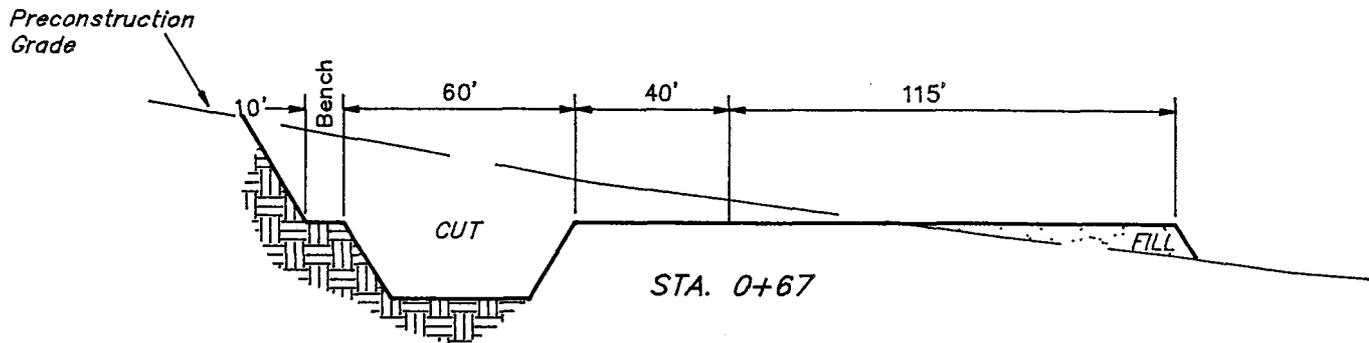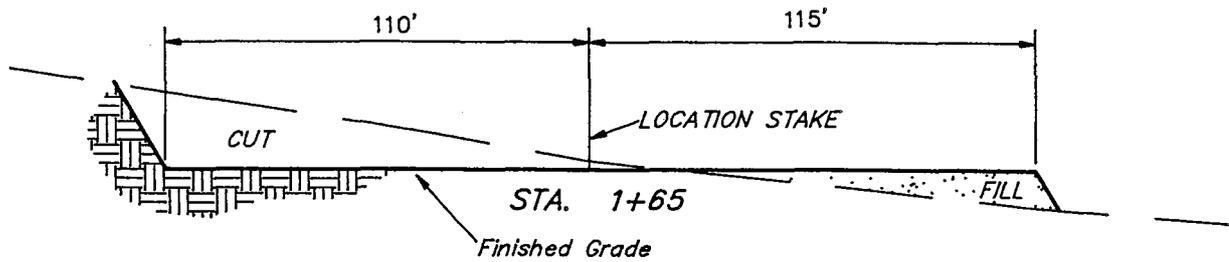

NOTE:
Topsoil should not be Stripped Below Finished Grade on Substructure Area.

APPROXIMATE YARDAGES

(12") Topsoil Stripping	=	1,910 Cu. Yds.
Remaining Location	=	4,490 Cu. Yds.
TOTAL CUT	=	6,400 CU.YDS.
FILL	=	3,590 CU.YDS.

EXCESS MATERIAL AFTER 5% COMPACTION	=	2,620 Cu. Yds.
Topsoil & Pit Backfill (1/2 Pit Vol.)	=	2,610 Cu. Yds.
EXCESS UNBALANCE (After Rehabilitation)	=	10 Cu. Yds.

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East • Vernal, Utah 84078 • (801) 789-1017


R
4
W

R
3
W

BRIDGELAND 7.6 MI. +/-
MYTON 19.3 MI. +/-

PROPOSED LOCATION:
UTE TRIBAL #19-11

PROPOSED ACCESS 0.1 MI. +/-

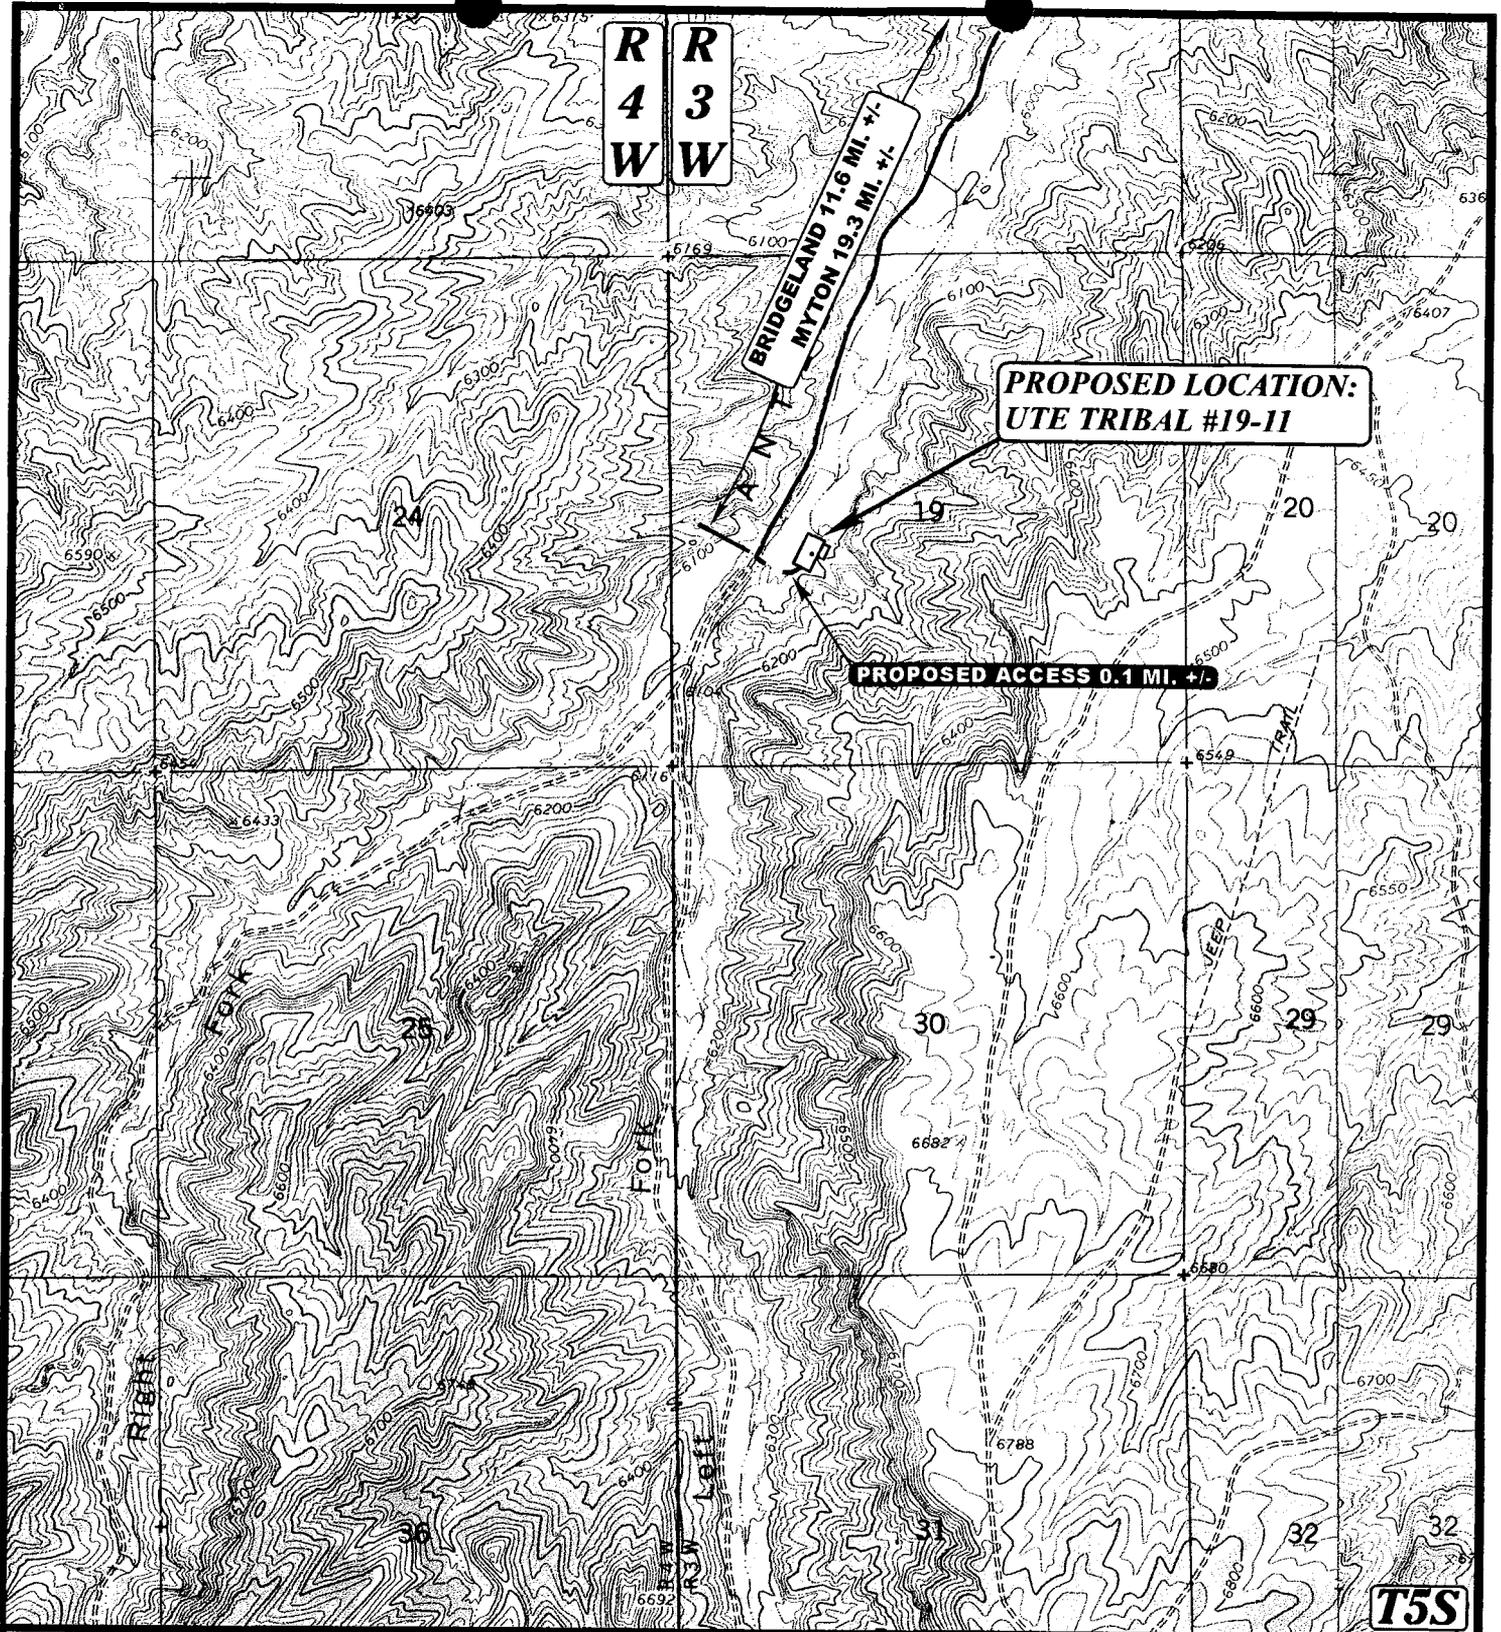

T5S

LEGEND:

- PROPOSED ACCESS ROAD
- EXISTING ROAD

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #19-11
SECTION 19, T5S, R3W, U.S.B.&M.
2226' FSL 1484' FWL



Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(801) 789-1017 * FAX (801) 789-1813
Email: uels@easlink.com



TOPOGRAPHIC
MAP


6 21 97
MONTH DAY YEAR

SCALE: 1" = 2000' | DRAWN BY: D.COX | REVISED: 00-00-00

B
TOPO

R
4
W

R
3
W

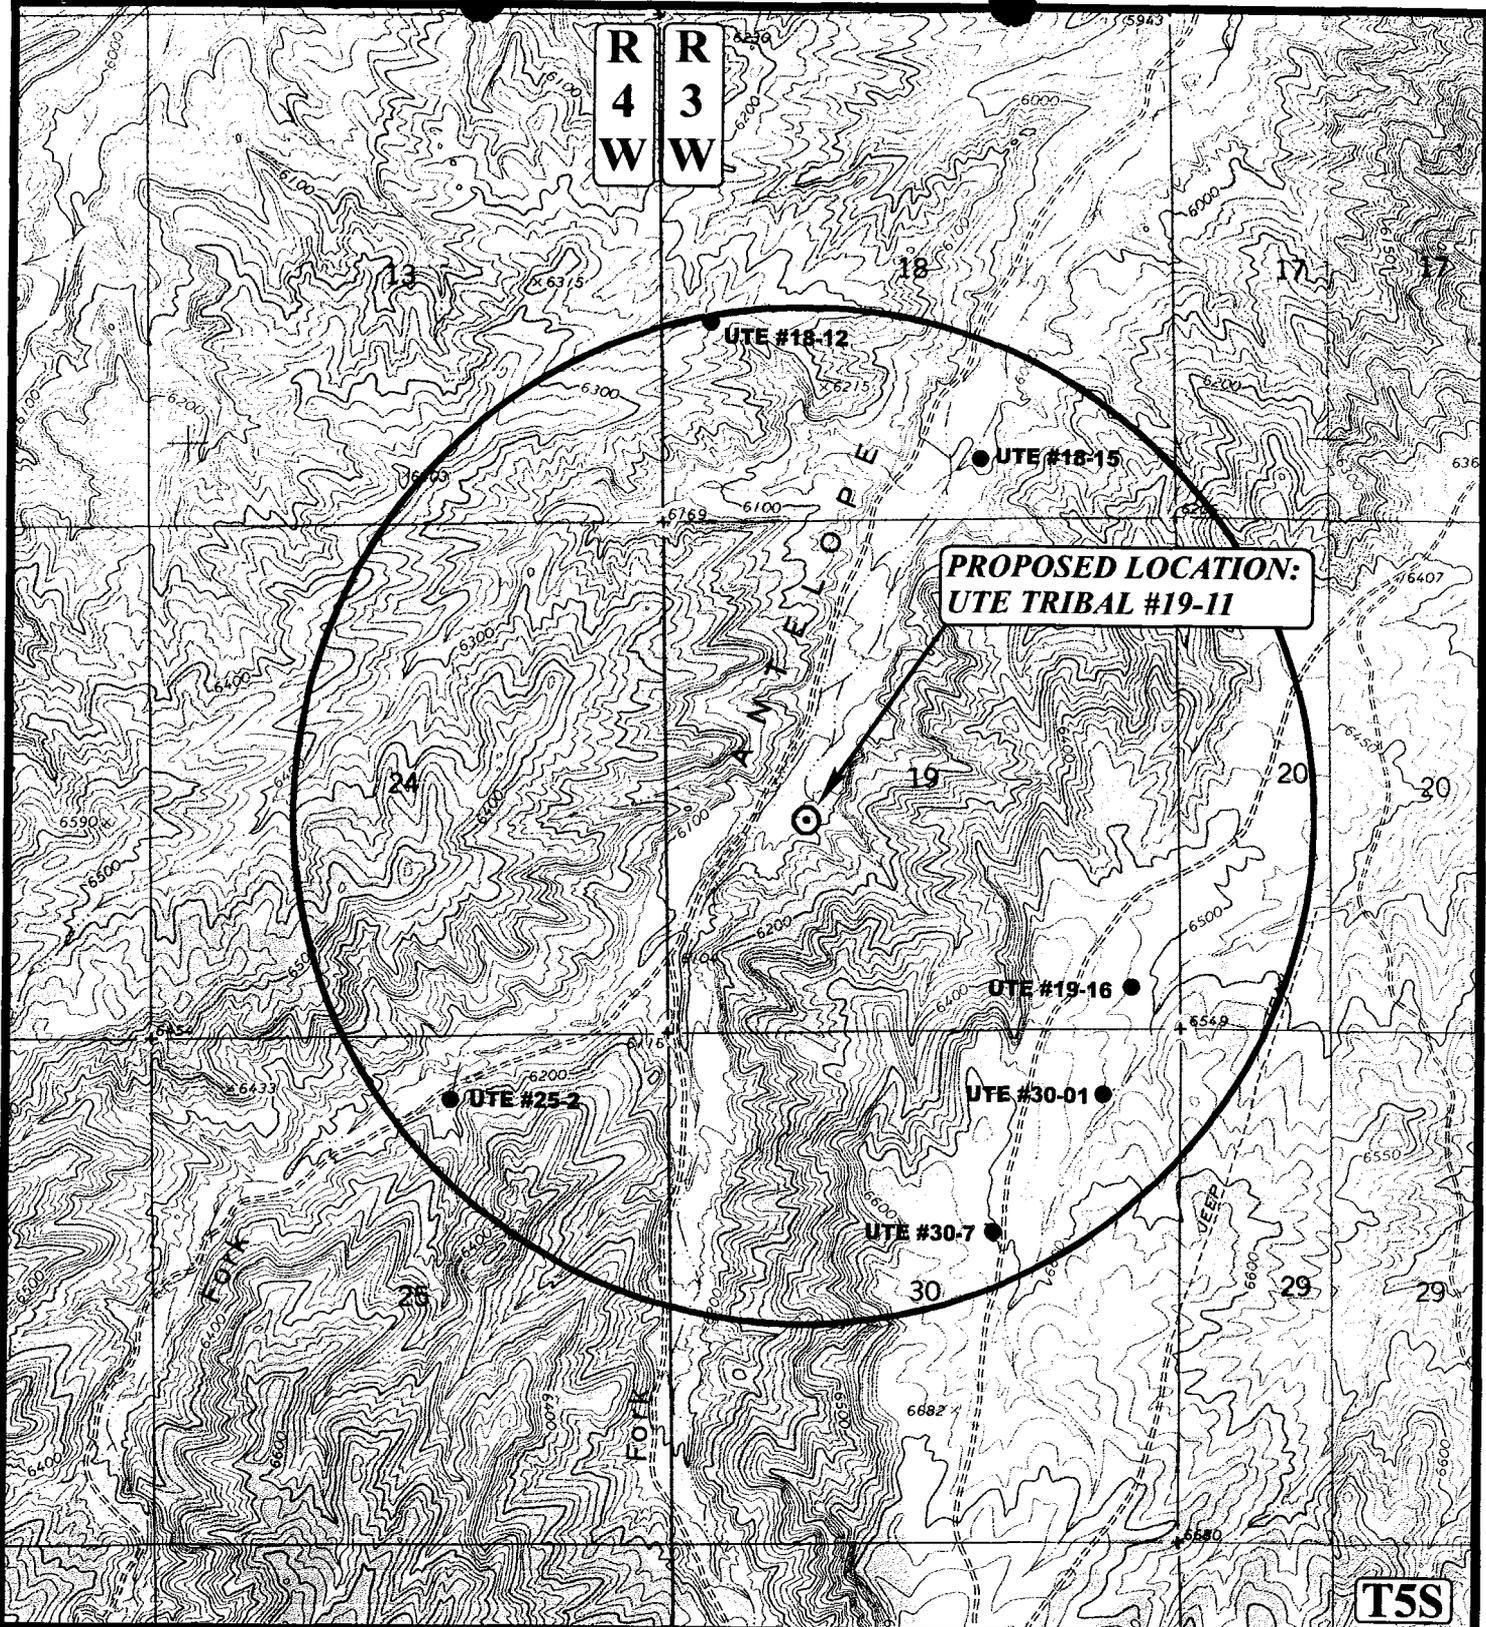

**PROPOSED LOCATION:
UTE TRIBAL #19-11**

T5S

LEGEND:

- | | |
|-------------------|-------------------------|
| ∅ DISPOSAL WELLS | ⊕ WATER WELLS |
| ● PRODUCING WELLS | ⊖ ABANDONED WELLS |
| ⊙ SHUT IN WELLS | ⊙ TEMPORARILY ABANDONED |

PETROGLYPH OPERATING CO., INC.

**UTE TRIBAL #19-11
SECTION 19, T5S, R3W, U.S.B.&M.
2226' FSL 1484' FWL**



Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(801) 789-1017 * FAX (801) 789-1813
Email: uels@easilink.com




**TOPOGRAPHIC
MAP**

6 21 97
MONTH DAY YEAR

SCALE: 1" = 2000' DRAWN BY: D.COX REVISED: 00-00-00



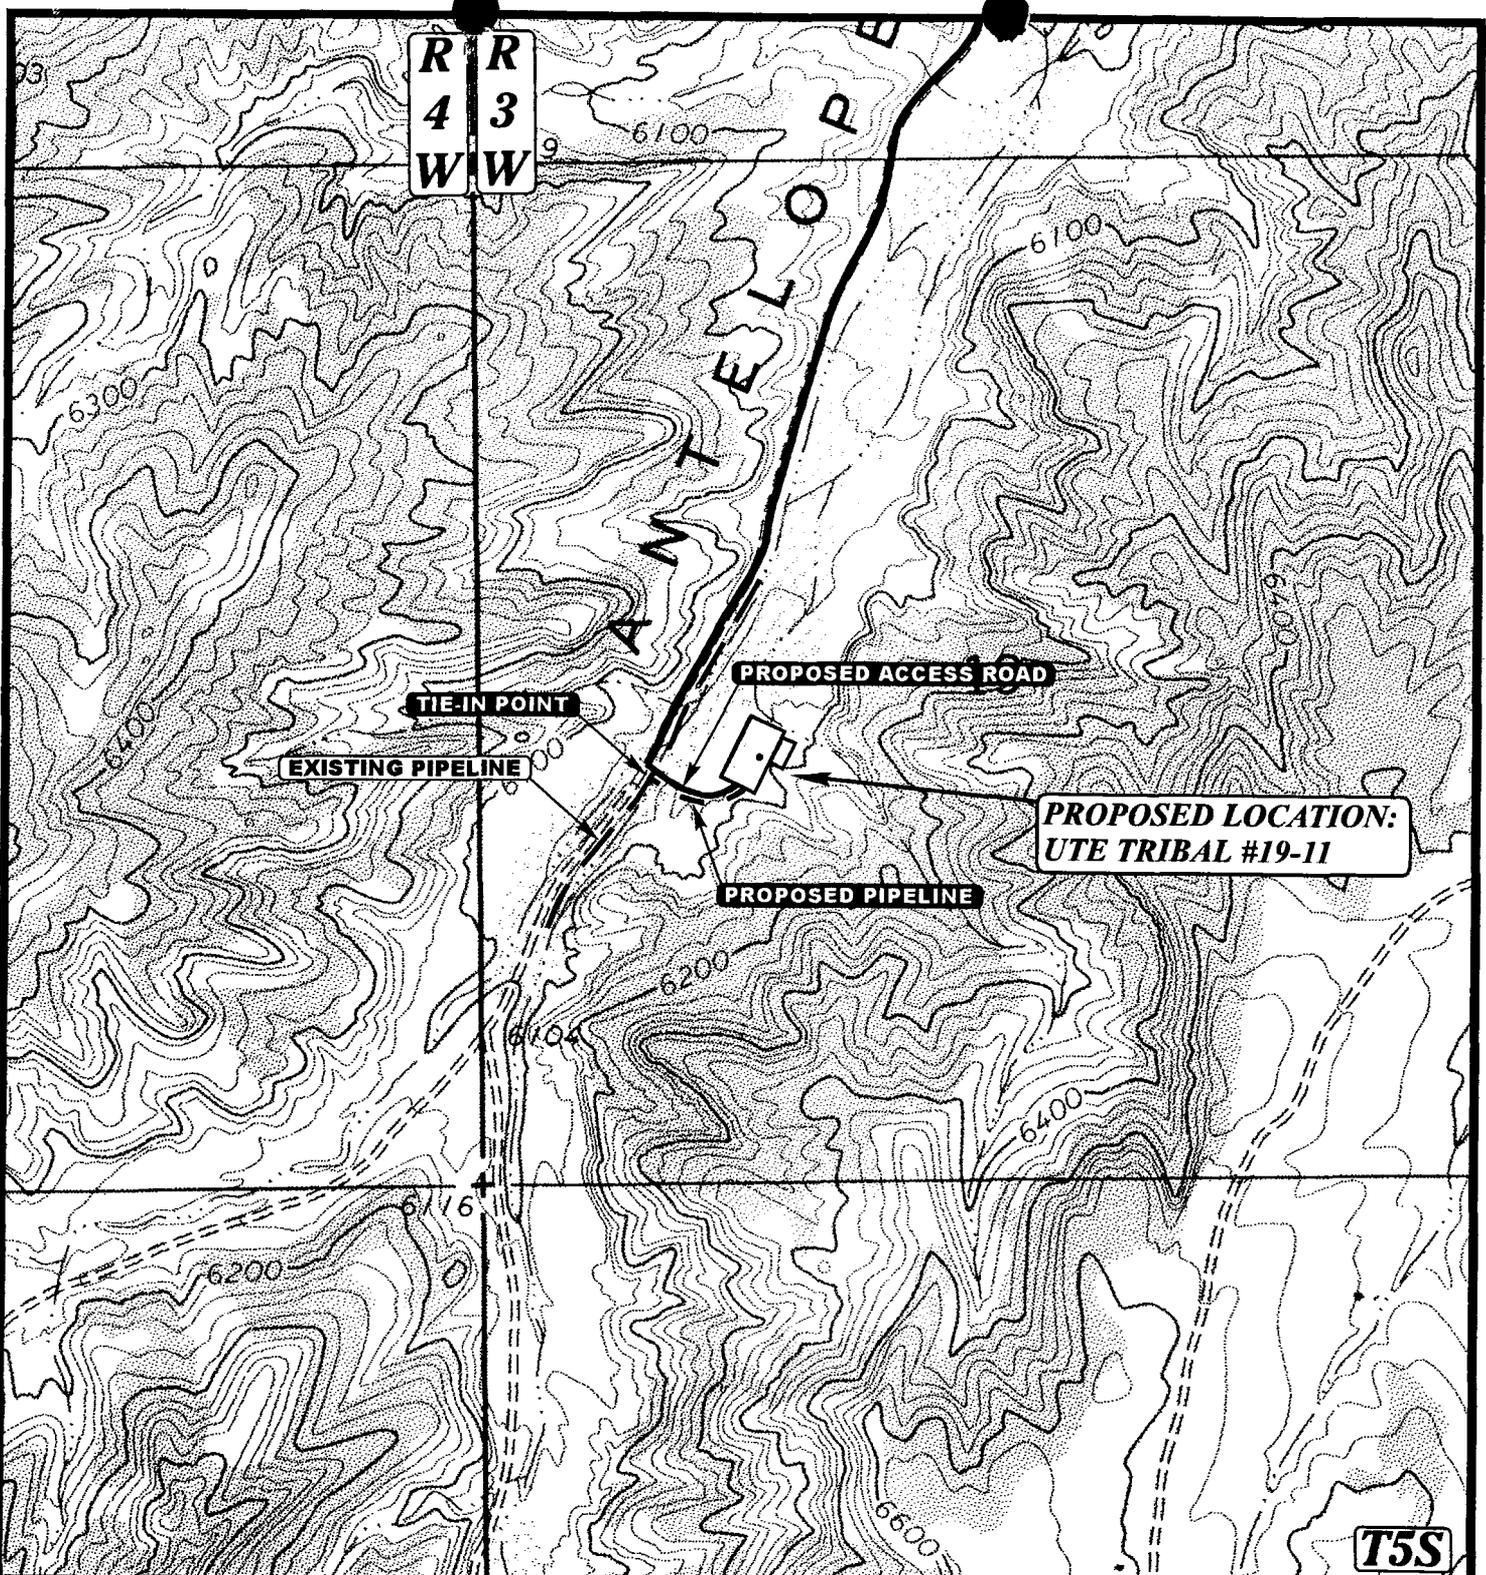

APPROXIMATE TOTAL PIPELINE DISTANCE = 500' +/-

LEGEND:

- EXISTING PIPELINE
- PROPOSED PIPELINE
- PROPOSED ACCESS

PETROGLYPH OPERATING CO., INC.

**UTE TRIBAL #19-11
SECTION 19, T5S, R3W, U.S.B.&M.
2226' FSL 1484' FWL**



Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(801) 789-1017 * FAX (801) 789-1813
Email: uels@easilink.com



**TOPOGRAPHIC
MAP**

6 21 97
MONTH DAY YEAR

SCALE: 1" = 1000' DRAWN BY: D.COX REVISED: 00-00-00

D
TOPO

WORKSHEET
APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 10/14/97

API NO. ASSIGNED: 43-013-31967

WELL NAME: UTE TRIBAL 19-11
OPERATOR: PETROGLYPH OPERATING (N3800)

PROPOSED LOCATION:
NESW 19 - T05S - R03W
SURFACE: 2226-FSL-1484-FWL
BOTTOM: 2226-FSL-1484-FWL
DUCHESNE COUNTY
ANTELOPE CREEK FIELD (060)

LEASE TYPE: IND
LEASE NUMBER: 14-20-H62-3514

PROPOSED PRODUCING FORMATION: GRRV

INSPECT LOCATION BY: / /		
TECH REVIEW	Initials	Date
Engineering		
Geology		
Surface		

RECEIVED AND/OR REVIEWED:


Plat
 Bond: Federal State Fee
(Number 4556)
 Potash (Y/N)
 Oil shale (Y/N)
 Water permit
(Number 43-10152)
 RDCC Review (Y/N)
(Date: _____)

LOCATION AND SITING:

R649-2-3. Unit: _____
 R649-3-2. General.
 R649-3-3. Exception.
 Drilling Unit.
Board Cause no: _____
Date: _____

COMMENTS: Exc. loc. OK

STIPULATIONS:




DIVISION OF OIL, GAS & MINING

OPERATOR: PETROGLYPH OPERATING (N3800)

FIELD: ANTELOPE CREEK (060)

SEC. TWP, RNG: 19 & 30, T5S, R3W

COUNTY: DUCHESNE UAC: R649-2-3 & R649-3-3

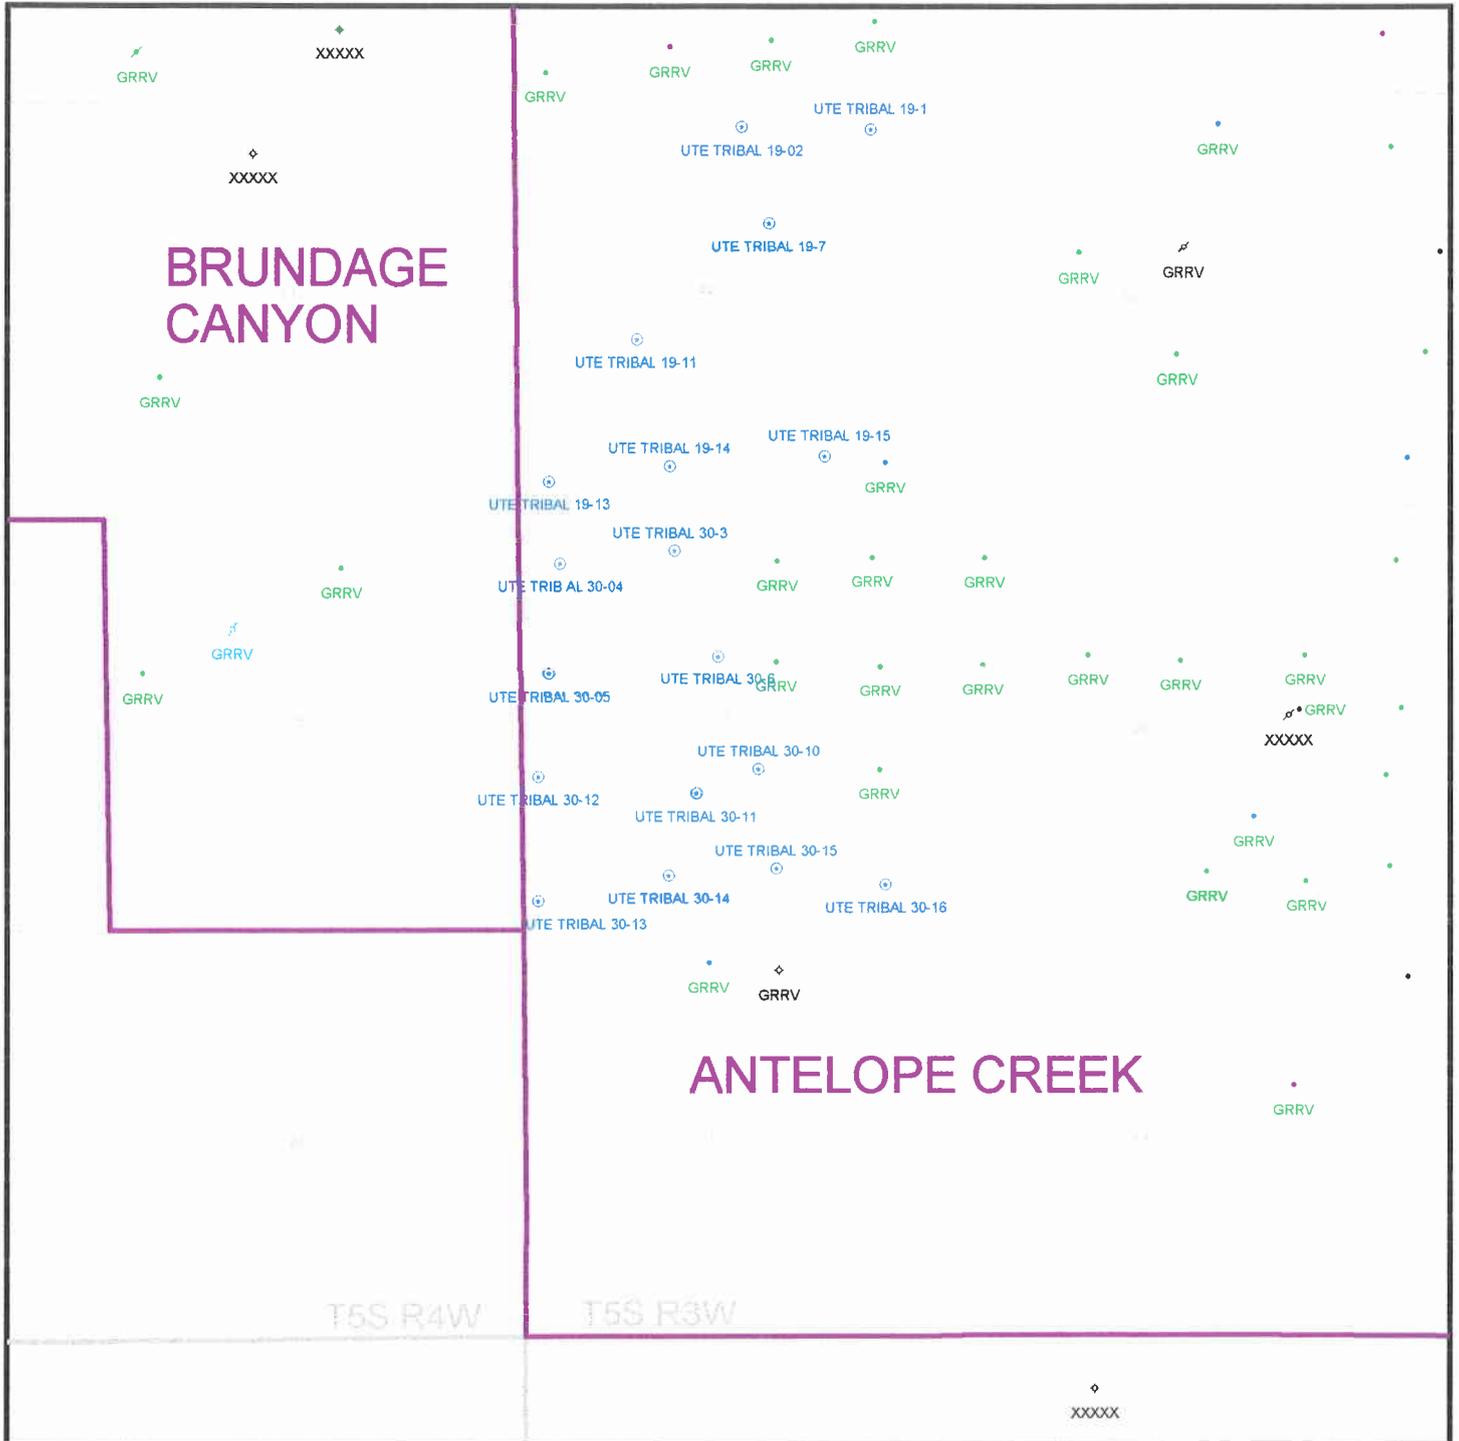

DATE PREPARED:
17-OCT-1997



State of Utah
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

Michael O. Leavitt
Governor
Ted Stewart
Executive Director
James W. Carter
Division Director

1594 West North Temple, Suite 1210
Box 145801
Salt Lake City, Utah 84114-5801
801-538-5340
801-359-3940 (Fax)
801-538-7223 (TDD)

October 27, 1997

Petroglyph Operating Company, Inc.
P.O. Box 607
Roosevelt, Utah 84066


Re: Ute Tribal 19-11 Well, 2226' FSL, 1484' FWL, NE SW, Sec. 19,
T. 5 S., R. 3 W., Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. 40-6-1 et seq., Utah Administrative Code R649-3-1 et seq., and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-31967.

Sincerely,


John R. Baza
Associate Director

lwp

Enclosures

cc: Duchesne County Assessor
Bureau of Land Management, Vernal District Office

Operator: Petroglyph Operating Company, Inc.
Well Name & Number: Ute Tribal 19-11
API Number: 43-013-31967
Lease: 14-20-H62-3514
Location: NE SW Sec. 19 T. 5 S. R. 3 W.

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for Permit to Drill.

2. Notification Requirements

Notify the Division within 24 hours following spudding the well or commencing drilling operations. Contact Jim Thompson at (801)538-5336.

Notify the Division prior to commencing operations to plug and abandon the well. Contact John R. Baza (801)538-5334.

3. Reporting Requirements

All required reports, forms and submittals shall be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR DEEPEN

1a. TYPE OF WORK

DRILL DEEPEN

b. TYPE OF WELL

OIL WELL GAS WELL OTHER SINGLE ZONE MULTIPLE ZONE

2. NAME OF OPERATOR

PETROGLYPH OPERATING COMPANY, INC.

3. ADDRESS AND TELEPHONE NO.

P. O. BOX 607, ROOSEVELT, UTAH 84066

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.*)
At surface

2226' FSL & 1484' FWL NE/SW

At proposed prod. zone

14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*

19.4 MILES SOUTHWEST OF MYTON, UTAH

15. DISTANCE FROM PROPOSED*

LOCATION TO NEAREST PROPERTY OR LEASE LINE, FT. 1484' ±
(Also to nearest drlg. unit line, if any)

16. NO. OF ACRES IN LEASE

640

17. NO. OF ACRES ASSIGNED TO THIS WELL

80

18. DISTANCE FROM PROPOSED LOCATION* TO NEAREST WELL, DRILLING, COMPLETED, OR APPLIED FOR, ON THIS LEASE, FT.

19. PROPOSED DEPTH

5714.6'

20. ROTARY OR CABLE TOOLS

ROTARY

21. ELEVATIONS (Show whether DF, RT, GR, etc.)

6077.6' GRADED GROUND


22. APPROX. DATE WORK WILL START*

OCTOBER 1997

23. PROPOSED CASING AND CEMENTING PROGRAM

SIZE OF HOLE	GRADE SIZE OF CASING	WEIGHT PER FOOT	SETTING DEPTH	QUANTITY OF CEMENT
12 1/4	8 5/8	24.0#	250'	135 sx class "G" + 2% CaCl ₂ + 1/4 #/sx celloflake.
7 7/8	5 1/2	15.5#	5714.6'	

50/50 POZMIX + 2% GEL + 10% SALT TO 400' ABOVE ALL ZONE OF INTEREST (+ 10% EXCESS). LIGHT CEMENT (11 PPG+) + LCM TO 200' ABOVE OIL SHALE OR FRESH WATER INTERVALS (+ 5% EXCESS).



PETROGLYPH OPERATING COMPANY, INC. WILL BE THE DESIGNATED OPERATOR OF THE SUBJECT WELL UNDER BOND #4556.

pc: Utah Division of Oil, Gas, and Mining
Bureau of Indian Affairs, Fort Duchesne, Utah
Ute Tribe, Fort Duchesne, Utah

RECEIVED
OCT 29 1997

IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directions, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24. SIGNED [Signature] TITLE AGENT FOR PETROGLYPH DATE 10-8-97

(This space for Federal or State office use)

PERMIT NO. _____ APPROVAL DATE _____

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
CONDITIONS OF APPROVAL, IF ANY:

APPROVED BY [Signature] ASSISTANT FIELD MANAGER
Mineral Resources DATE OCT 23 1997

*See Instructions On Reverse Side

UNITED STATES GOVERNMENT
memorandum

September 26, 1997

DATE:

REPLY TO: Superintendent, Uintah & Ouray Agency
ATTN OF:

RECEIVED

OCT 02 1997

SUBJECT: Concurrence letter for Petroglyph Oper. Co. all in T5S.R3W
UteTribal 30-03 NENW, Sec 30 UteTribal 30-06 SENW, Sec. 30 UteTribal 19-11, NESW, Sec 19
UteTribal 19-02, NWNE, Sec. 19 Ute Tribal 19-13, SWSE, Sec.19 UteTribal 19-14, SESW, Sec. 19
UteTribal 19-01, NENE, Sec. 19 Ute Tribal 19-07, SWNE, Sec.19 UteTribal 19-15, SWSE, Sec. 19
TO: Bureau of Land Management, Vernal District Office
ATTENTION: Minerals and Mining Division

We recommend approval of the Application for Permit to Drill on the subject well

Based on available information received on September 26, 1997, we cleared the proposed location in the following area of environmental impact.

- YES NO Listed threatened or endangered species
- YES NO Critical wildlife habitat
- YES NO Archeological or cultural resources
- YES NO Air quality aspects (to be used only if project is in or adjacent to a Class I area.

REMARKS: The Ute Tribe Energy & Minerals Department is recommending the following criteria to be adhered during all phases of construction activities.

1. The Ute Tribe Energy & Minerals Department is to be notified 48 hours prior to construction as a Tribal Technician is to monitor construction.
2. 75 foot corridor rights of way shall be granted with the following:
 - A. Buried pipelines shall be buried minimum of 3 feet below soil surface
 - B. Access roads shall be limited to 22 feet wide.
 - C. Surface pipelines shall be limited to 13 feet wide.
 - D. Buried pipelines shall be limited to 15 feet wide, and construction will be monitored by Tribal Technician.
3. Pipelines adjacent to access roads shall be buried within 1.5 feet from the outside edge of the barrow ditch. Additional pipelines shall be parallel to each other, as safety requirements will allow.
4. Petroglyph Operating Company will assure the UteTribe that any/all contractors and any sub-contractors has acquired a Tribal Business License and have an access permit prior to construction.
5. All vehicular traffic, personnel movement, construction and restoration operations should be confined to the area examined, as referenced in report and to the existing roadways and/or evaluated access routes.
6. All personnel should refrain from collecting artifacts and from disturbing any significant cultral resources in the area.
7. The personnel from the Ute Tribe Energy and Minerals Department should be consulted should cultural remains from sub-surface deposits be exposed or identified during construction.
8. All mitigative stipulations contained in the Bureau of Indian Affairs site specific Enviromental Analysis (EA) will be strictly adhered.
9. Upon completion of Application for Right-of-way the Ute Tribe Energy and Minerals Department will be notified by Petroglyph Operating Company, so that a Tribal Technician can verify Affidavit of Completions.

CONDITIONS OF APPROVAL
APPLICATION FOR PERMIT TO DRILL

Company/Operator: Petroglyph Operating Company

Well Name & Number: Ute Tribal 19-11

API Number: 43-013-31967

Lease Number: 14-20-H62-3514

Location: NESW Sec. 19 T. 5S R. 3W

NOTIFICATION REQUIREMENTS

- Location Construction - at least forty-eight (48) hours prior to construction of location and access roads.
- Location Completion - prior to moving on the drilling rig.
- Spud Notice - at least twenty-four (24) hours prior to spudding the well.
- Casing String and Cementing - at least twenty-four (24) hours prior to running casing and cementing all casing strings.
- BOP and Related Equipment Tests - at least twenty-four (24) hours prior to initiating pressure tests.
- First Production Notice - within five (5) business days after new well begins, or production resumes after well has been off production for more than ninety (90) days.

For more specific details on notification requirements, please check the Conditions of Approval for Notice to Drill and Surface Use Program.

CONDITIONS OF APPROVAL FOR NOTICE TO DRILL

Approval of this application does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

All lease and/or unit operations will be conducted in such a manner that full compliance is made with applicable laws, regulations (43 CFR 3100), Onshore Oil and Gas Orders, and the approved plan of operations. The operator is fully responsible for the actions of his subcontractors. A copy of these conditions will be furnished to the field representative by the operator to insure compliance.

Be aware fire restrictions may be in effect when location is being constructed and/or when well is being drilled. Contact the appropriate Surface Management Agency for information.

A. DRILLING PROGRAM

1. Estimated Depth at Which Oil, Gas, Water, or Other Mineral Bearing Zones are Expected to be Encountered

Report **ALL** water shows and water-bearing sands to Tim Ingwell of this office **prior to setting the next casing string or requesting plugging orders**. Faxed copies of State of Utah form OGC-8-X are acceptable. If noticeable water flows are detected, submit samples to this office along with any water analyses conducted.

All usable water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling, will be recorded by depth and adequately protected. All oil and gas shows will be tested to determine commercial potential.

2. Pressure Control Equipment

The BOP and related equipment shall meet the minimum requirements of Onshore Oil and Gas Order No. 2 for equipment and testing requirements, procedures, etc., for a **2M** system and individual components shall be operable as designed. Chart recorders shall be used for all pressure tests.

Test charts, with individual test results identified, shall be maintained on location while drilling and shall be made available to a BLM representative upon request.

If an air compressor is on location and is being utilized to provide air for the drilling medium while drilling, the special drilling requirements in Onshore Oil and Gas Order No. 2, regarding air or gas drilling shall be adhered to. If a mist system is being utilized then the requirement for a deduster shall be waived.

3. Casing Program and Auxiliary Equipment

Surface casing shall have centralizers on the bottom three joints, with a minimum of one centralizer per joint.

If conductor pipe is set it will be cemented to surface. If drive pipe is used it will be pulled prior to cementing surface casing.

As a minimum, the usable water and oil shale resources shall be isolated and/or protected via the cementing program. If gilsonite is encountered while drilling, it shall be isolated and/or protected via the cementing program.

4. Mud Program and Circulating Medium

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

No chromate additives will be used in the mud system on Federal and Indian lands without prior BLM approval to ensure adequate protection of fresh water aquifers.

5. Coring, Logging and Testing Program

Daily drilling and completion progress reports shall be submitted to this office on a weekly basis.

All Drill Stem tests (DST) shall be accomplished during daylight hours, unless specific approval to start during other hours is obtained from the AO. However, DSTs may be allowed to continue at night if the test was initiated during daylight hours and the rate of flow is stabilized and if adequate lighting is available (i.e., lighting which is adequate for visibility and vaporproof for safe operations). Packers can be released, but tripping should not begin before daylight unless prior approval is obtained from the AO.

The Gamma Ray and Induction Logs need to be pulled from TD to the Surface Shoe.

A cement bond log (CBL) will be run from the production casing shoe to **Top Of Cement** and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.

Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (Form 3160-4) will be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3164. One copy of all logs, core descriptions, core analyses, well-test data, geologic summaries, sample description, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, will be filed with Form 3160-4. Samples (cuttings, fluids, and/or gases) will be submitted when requested by the AO.

6. Notifications of Operations

No location will be constructed or moved, no well will be plugged, and no drilling or workover equipment will be removed from a well to be placed in a suspended status without prior approval of the AO. If operations are to be suspended, prior approval of the AO will be obtained and notification given before resumption of operations.

The Vernal District Office shall be notified, during regular work hours (7:45 a.m.-4:30 p.m., Monday through Friday except holidays), at least 24 hours **prior** to spudding the well.

Operator shall report production data to MMS pursuant to 30 CFR 216.5 using form MMS/3160.

Immediate Report: Spills, blowouts, fires, leaks, accidents, or any other unusual occurrences shall be promptly reported in accordance with the requirements of NTL-3A or its revision.

If a replacement rig is contemplated for completion operations, a "Sundry Notice" (Form 3160-5) to that effect will be filed, for prior approval of the AO, and all conditions of this approved plan are applicable during all operations conducted with the replacement rig.

The date on which production is commenced or resumed will be construed for oil wells as the date on which liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated or, the date on which liquid hydrocarbons are first produced into a permanent storage facility, whichever first occurs; and, for gas wells as the date on which associated liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated or, the date on which gas is first measured through permanent metering facilities, whichever first occurs.

Should the well be successfully completed for production, the AO will be notified when the well is placed in a producing status. Such notification will be sent by telegram or other written communication, not later than five (5) days following the date on which the well is placed on production.

Gas produced from this well may not be vented or flared beyond an initial authorized test period of 30 days or 50 MMCF following its completion, whichever occurs first, without the prior written approval of the Authorized Officer. Should gas be vented or flared without approval beyond the authorized test period, the operator may be directed to shut-in the well until the gas can be captured or approval to continue venting or flaring as uneconomic is granted and the operator shall be required to compensate the lessor for that portion of the gas vented or flared without approval which is determined to have been avoidably lost.

A schematic facilities diagram as required by 43 CFR 3162.7-5 (b.9. d.), and shall be submitted to the appropriate District Office within sixty (60) days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with 43 CFR 3162.7-5 (b. 4).

No well abandonment operations will be commenced without the prior approval of the AO. In the case of newly drilled dry holes or failures, and in emergency situations, oral approval will be obtained from the AO. A "Subsequent Report of Abandonment" Form 3160-5, will be filed with the AO within thirty (30) days following completion of the well for abandonment. This report will indicate where plugs were placed and the current status of surface restoration. Final abandonment will not be approved until the surface reclamation work required by the approved APD or approved abandonment notice has been completed to the satisfaction of the AO or his representative, or the appropriate Surface Managing Agency.

7. Other Information

All loading lines will be placed inside the berm surrounding the tank battery.

All off-lease storage, off-lease measurement, or commingling on-lease or off-lease will have prior written approval from the AO.

The oil and gas measurement facilities will be installed on the well location. The oil and gas meters will be calibrated in place prior to any deliveries. Tests for meter accuracy will be conducted following initial installation and at least quarterly thereafter. The AO will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports will be submitted to the Vernal District Office. All meter measurement facilities will conform with Onshore Oil & Gas Order No. 4 for liquid hydrocarbons and Onshore Oil & Gas Order No. 5 for natural gas measurement.

The use of materials under BLM jurisdiction will conform to 43 CFR 3610.2-3.

There will be no deviation from the proposed drilling and/or workover program without prior approval from the AO. Safe drilling and operating practices must be observed. All wells, whether drilling, producing, suspended, or abandoned will be identified in accordance with 43 CFR 3162.

"Sundry Notice and Report on Wells" (Form 3160-5) will be filed for approval for all changes of plans and other operations in accordance with 43 CFR 3162.3-2.

Section 102(b)(3) of the Federal Oil and Gas Royalty Management Act of 1982, as implemented by the applicable provisions of the operating regulations at Title 43 CFR 3162.4-1(c), requires that "not later than the 5th business day after any well begins production on which royalty is due anywhere on a lease site or allocated to a lease site, or resumes production in the case of a well which has been off production for more than 90 days, the operator shall notify the authorized officer by letter or sundry notice, Form 3160-5, or orally to be followed by a letter or sundry notice, of the date on which such production has begun or resumed."

If you fail to comply with this requirement in the manner and time allowed, you shall be liable for a civil penalty of up to \$10,000 per violation for each day such violation continues, not to exceed a maximum of 20 days. See Section 109(c)(3) of the Federal Oil and Gas Royalty Management Act of 1982 and the implementing regulations at Title 43 CFR 3162.4-1(b)(5)(ii).

APD approval is valid for a period of one (1) year from the signature date. An extension period may be granted, if requested, prior to the expiration of the original approval period.

In the event after-hours approval or notification is necessary, please contact one of the following individuals:

Wayne Bankert (801) 789-4170
Petroleum Engineer

Ed Forsman (801) 789-7077
Petroleum Engineer

Jerry Kenczka (801) 789-1190
Petroleum Engineer

BLM FAX Machine (801) 781-4410

EPA'S LIST OF NONEXEMPT EXPLORATION AND PRODUCTION WASTES

While the following wastes are nonexempt, they are not necessarily hazardous.

- Unused fracturing fluids or acids
- Gas plant cooling tower cleaning wastes
- Painting wastes
- Oil and gas service company wastes, such as empty drums, drum rinsate, vacuum truck rinsate, sandblast media, painting wastes, spend solvents, spilled chemicals, and waste acids
- Vacuum truck and drum rinsate from trucks and drums, transporting or containing nonexempt waste
- Refinery wastes
- Liquid and solid wastes generated by crude oil and tank bottom reclaimers
- Used equipment lubrication oils
- Waste compressor oil, filters, and blowdown
- Used hydraulic fluids
- Waste solvents
- Waste in transportation pipeline-related pits
- Caustic or acid cleaners
- Boiler cleaning wastes
- Boiler refractory bricks
- Incinerator ash
- Laboratory wastes
- Sanitary wastes
- Pesticide wastes
- Radioactive tracer wastes
- Drums, insulation and miscellaneous solids.

SURFACE USE PROGRAM

The Surface Use Conditions of Approval all come from the Bureau of Indian Affairs Concurrence Memorandum and Site Specific Environmental Analysis.

The Ute Tribe Energy and Mineral Department is to be notified 48 hours prior to construction. A Tribal Technician is to monitor construction.

Seventy-five (75) foot wide Rights-Of-Way (ROWs) corridor shall be granted for the following:

Access roads which shall have constructed travel width limited to 22 feet within a 30 foot allocation of the ROW, except as granted for sharp curves or intersections.

Surface pipelines shall be limited to 13 feet of the ROW. The pipeline will be constructed to lay on the soil surface, and the ROW for the pipeline will not be bladed or cleared of vegetation.

Where pipelines are constructed parallel to roads they may be welded on the road and then lifted from the road onto the ROW. Where pipelines cross country between stations, they shall be welded in place at wellsites or on roads and then pulled into place with suitable equipment. Traffic will be restricted along these areas so that the pipeline ROW will not be used as an access road.

Buried pipelines shall be buried a minimum of 3 feet below the soil surface within an area of disturbance limited to 15 feet wide, and construction will be monitored by a Tribal Technician.

Buried pipelines adjacent to access roads shall be buried within 1.5 feet from the outside edge of the barrow ditch. Any additional buried pipelines shall be parallel to the outer side of the first buried pipeline and shall be constructed as close to the first pipeline as safety requirements allow.

After construction of the buried pipeline is completed the disturbed area of the right-of-way shall be contoured to blend into the natural landscape and it shall be reseeded with desirable vegetation as recommended by the BIA. Between September 15 and November 1 of the year following pipeline construction all disturbed areas shall be reseeded with perennial vegetation according to BIA, or Ute Tribe specifications.

Petroglyph will assure the Ute Tribe that any/all contractors and subcontractors have acquired a Tribal Business License and have access permits prior to construction.

All vehicular traffic, personnel movement, construction, and restoration activities shall be confined to the areas examined, as referenced in report, and to the existing roadways and/or evaluated access routes.

All personnel shall refrain from collecting artifacts and from disturbing any significant cultural resources in the area.

The Ute Tribe Energy & Mineral Department shall be consulted if cultural remains from subsurface deposits are exposed or identified during construction.

Before the site is abandoned, the company shall be required to restore the well site and ROWs to near their original state. The disturbed areas will be reseeded with desirable perennial vegetation.

Noxious weeds shall be controlled on the well site and rights-of-way. If noxious weeds spread from the project area onto adjoining land, the company shall also be responsible for their control.

Reserve pits will be lined with impervious synthetic liners. Prior to backfilling the reserve pit all fluids will be pumped from the pit into trucks and hauled to approved disposal sites. When the reserve pits are backfilled the cuttings and mud, etc. left in them to be buried will be buried a minimum of three feet below the surface of the soil.

A closed production system shall be used. Production fluids will be contained in leak proof tanks. All production fluids will be disposed of at approved disposal sites. The indiscriminate dumping of production fluids on roads, wellsites or other areas will not be allowed.

Firewood shall be stockpiled at convenient locations near the wellsite and along the access road.

Upon completion of the project approved under this Application for Permit to Drill and Right-of-way, the Ute Tribe Energy & Minerals Resources Department will be notified by Petroglyph Operating Company so that a Tribal Technician can verify Affidavit of Completion's.

ENTITY ACTION FORM - FORM 6

OPERATOR Petroglyph Operating Company, Inc.
ADDRESS P. O. Box 607
Roosevelt, UT 84066


OPERATOR ACCT. NO. N3800

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	12353	→	43-013-31795	Ute Tribal 19-12	NWSW	19	5S	3W	Duchesne	4/10/98	
WELL 1 COMMENTS: CONFIDENTIAL Entity previously added 4-17-98. <i>fcc</i>											
B	12353	→	43-013-31967	Ute Tribal 19-11	NESW	19	5S	3W	Duchesne	4/17/98	
WELL 2 COMMENTS: CONFIDENTIAL Entity added 4-28-98. <i>fcc</i> Ute Tribal 19-11 is the tank battery that will include the Ute Tribal 19-12											
WELL 3 COMMENTS:											
WELL 4 COMMENTS:											
APR 27 1998 BY _____											
WELL 5 COMMENTS:											

ACTION CODES (See instructions on back of form)

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group of unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.



Deanna Bell
Signature Deanna Bell

Operations Coordinator 4/27/98
Title Date

Phone No. (435) 722-2531

REPORT OF WATER ENCOUNTERED DURING DRILLING

1. Well name and number: UteTribal 19-11
API number: 43-013-31967

2. Well Location: QQ NESW Section 19 Township 5S Range 3W County Duchesne

3. Well Operator: Petroglyph Operating Company, Inc.
Address: P.O. Box 607
Roosevelt, UT 84066. Phone: (435) 722-2531

4. Drilling Contractor: Union Drilling
Address: P.O. Drawer 40
Buckhannon, WV 26201 Phone: (304) 472-4610

5. Water encountered (attach additional pages as needed):

DEPTH		VOLUME (FLOW RATE OR HEAD)	QUALITY (FRESH OR SALTY)
FROM	TO		
<u>245</u>		<u>1" x 7"</u>	<u>FRESH</u>
		<u>Hole Damp under 8 3/8</u>	
		<u>Did't DUST</u>	
	<u>905</u>	<u>blow test 5gal per min</u>	
	<u>1629</u>	<u>WATER INCREASE 2' X 7 STREAM</u>	

6. Formation tops: APR 27 1998 DOGm APR 27 1998 KS
do db

If an analysis has been made of the water encountered, please attach a copy of the report to this form.

I hereby certify that this report is true and complete to the best of my knowledge. Date: 4-27-98
Name & Signature Deanna Bell Deanna Bell Title: Operations Coordinator

SUBMIT IN DUPLICATE
(See other instructions on
reverse side)

Form approved.
Budget Bureau No. 1004-0137
(Expires August 31, 1985)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

5. LEASE DESIGNATION AND SERIAL NO.
14-20-H62-3514

6. IF INDIAN, ALLOTTEE OR TRIBE NAME
Ute Indian Tribe

WELL COMPLETION OR RECOMPLETION REPORT AND LOG*

1.a. TYPE OF WELL: Oil Well Gas Well Dry Other

7. UNIT AGREEMENT NAME
14-20-H62-4650

b. TYPE OF COMPLETION:
New Well Workover Deepen Plug Back Diff. Reserv. Other

8. FARM OR LEASE NAME

2. NAME OF OPERATOR
PETROGLYPH OPERATING COMPANY, INC.

9. WELL NO.
Ute Tribal 19-11

3. ADDRESS OF OPERATOR
P.O. BOX 607, ROOSEVELT, UT 84066 (435) 722-2531

10. FIELD AND POOL, OR WILDCAT
Antelope Creek

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements)*
At surface 2226' FSL 1484' FWL

11. SEC., T., R., M., OR BLOCK AND
SURVEY OR AREA
NESW SEC. 19-T5S-R3W

CONFIDENTIAL

At top prod. interval reported below

14. PERMIT NO.
43-013-31967

DATE ISSUED
10/27/97

12. County or Parish
Duchesne

13. State
Utah

At total depth 5758' RTD

15. DATE SPUDDED 4/17/98

16. DATE T.D. REACHED
4/24/98

17. DATE COMPLETED (Ready to prod.)
5/11/98

18. ELEVATIONS (DF, RKB, RT, GR, ETC.)*
6088' KB

19. ELEV. CASINGHEAD
6078' GGL

20. TOTAL DEPTH, MD & TVD
5758' TD

21. PLUG BACK T.D., MD & TVD
5694' PBTD

22. IF MULTIPLE COMPL., HOW MANY*
2

23. INTERVALS
DRILLED BY

ROTARY TOOLS

CABLE TOOLS

24. PRODUCING INTERVAL(S) OF THIS COMPLETION -- TOP, BOTTOM, NAME (MD AND TVD)*
GREEN RIVER C6.1, D5

25. WAS DIRECTIONAL SURVEY MADE
No

26. TYPE ELECTRIC AND OTHER LOGS RUN
Gamma Ray to surface, Density-Compensated Neutron Porosity, AIT (normal suite)

27. WAS WELL CORDED
No

28. CASING RECORD (Report all strings set in well)					
CASING SIZE	WEIGHT, LB./FT.	DEPTH SET (MD)	HOLE SIZE	CEMENTING RECORD	AMOUNT PULLED
8-5/8"	24.0#	350'	12-1/4"	220 sxs Class H w/ 2% CaCl ₂ , all cement had .25#/sk cellophane flake	
5-1/2"	15.5#	5738'	7-7/8"	240 sxs Highfill & 340 sxs Thixotropic	

29. LINER RECORD				30. TUBING RECORD		
SIZE	TOP	BOTTOM (MD)	SACKS CEMENT*	SCREEN (MD)	SIZE	DEPTH SET (MD)
					2-7/8"	4948'

31. PERFORATION RECORD (Interval, size and number)		32. ACID, SHOT, FRACTURE, CEMENT SQUEEZE, ETC.	
CONFIDENTIAL		DEPTH INTERVAL (MD)	AMOUNT AND KIND OF MATERIAL USED
D5 4835-41' (24 holes)		4835-41'	3000 gal Boragel 30, 12500# 20/40 prop, 19000# 16/30 prop
C6.1 4435-38' (12 holes)		4435-4438' & 4421-24'	8477 gal Boragel 30, 12500# 20/40 prop & 19000# 16/30 prop
C6.1 4421-24' (12 holes)			

CONFIDENTIAL

33. PRODUCTION							
DATE FIRST PRODUCTION		PRODUCTION METHOD (Flowing, gas lift, pumping - size and type of pump)				WELL STATUS (Producing or shut-in)	
5/22/98		2 1/2" x 1-3/4" x 16' 40 ring PA pump				producing	
DATE OF TEST	HOURS TESTED	CHOKE SIZE	PROD'N FOR TEST PERIOD	OIL - BBL. #	GAS - MCF.	WATER - BBL.	GAS-OIL RATIO
5/27/98	24				0	45	
FLOW. TUBING PRESS.	CASING PRESSURE	CALCULATED 24 HR. RATE	OIL - BBL.	GAS - MCF.	WATER - BBL.	OIL GRAVITY - API (CORR.)	
	450						

34. DISPOSITION OF GAS (Sold, used for fuel, vented, etc.)
Sold, used for fuel

TEST WITNESSED BY
Dave Schreiner

35. LIST OF ATTACHMENTS

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records

Signed

Jenna Bell

Title


Operations Coordinator

Date

6/8/98

*(See Instructions and Spaces for Additional Data on Reverse Side)

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly or willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.



37. SUMMARY OF POROUS ZONES: (Show all important zones of porosity and contents thereof, cored intervals; and all drill-stem, tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures, and recoveries):

FORMATION	TOP	BOTTOM	DESCRIPTION, CONTENTS, ETC.	NAME	TOP	
					MEAS. DEPTH	TRUE VERT. DEPTH
Ute Tribal 19-11						
B Marker	3610					
X Marker	4090					
Douglas Creek	4236					
B Limestone	4614					
Castle Peak	5157					
Basal Carbonate	5597					

CONFIDENTIAL

CONFIDENTIAL

38.

GEOLOGIC MARKERS

Form 7

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING

REPORT OF WATER ENCOUNTERED DURING DRILLING

- 1. Well name and number: UteTribal 19-11
API number: 43-013-31967
- 2. Well Location: QQ NESW Section 19 Township 5S Range 3W County Duchesne
- 3. Well Operator: Petroglyph Operating Company, Inc.
Address: P.O. Box 607
Roosevelt, UT 84066 Phone: (435) 722-2531
- 4. Drilling Contractor: Union Drilling
Address: P.O. Drawer 40
Buckhannon, WV 26201 Phone: (304) 472-4610
- 5. Water encountered (attach additional pages as needed):

DEPTH		VOLUME (FLOW RATE OR HEAD)	QUALITY (FRESH OR SALTY)
FROM	TO		
<u>245</u>		<u>1" X 7"</u>	<u>FRESH</u>
		<u>Hole Damp under 8 3/8</u>	
		<u>Didn't Dust</u>	
	<u>905</u>	<u>blow test 5gal per min</u>	
	<u>1629</u>	<u>Water increase 2" X 7 stream</u>	

6. Formation tops: _____

If an analysis has been made of the water encountered, please attach a copy of the report to this form.

I hereby certify that this report is true and complete to the best of my knowledge. Date: 4-27-98
Name & Signature Deanna Bell Deanna Bell Title: Operations Coordinator

DATE: 11-18-1999

UTE TRIBAL # 19-11
Wellbore Diagram

GL 6077
KB 6087

AFTER CONVERSION

WELL HISTORY:

SPUD WELL: 04-17-98

FIRST PROD: 05-22-98

05-06-98 C-6.1 ZONES

PERFS: 4421 TO 4424'
4 SPK

4435 TO 4438'
4 SPK

FRAC'ED, ISIP 2398 PSI.

05-06-98 D-5 ZONE

PERFS: 4835 TO 4841'
4 SPK

FRAC'ED, ISIP 2425 PSI.

CONDUCTOR HOLE SIZE 17 1/2"
13 3/8" 49# CONDUCTOR @ 67'
CEMENTED W/ 126 SXS

← Surface Hole Size 12 1/4"


8 5/8" 24# Surface Csg @
350' KB Cmt'd w/ 220 SXS

← Hole Size: 7 7/8" Bit.

Cement Tops:
1st Stage: CIRCULATED CEMENT

5 1/2" 15.5# CSG @ 5738'
CMT'd w/ 580 Sxs. 1st. Stage

← 136 JTS OF 2 3/8"
4.7# TUBING SET ON
PACKER @ 4352'

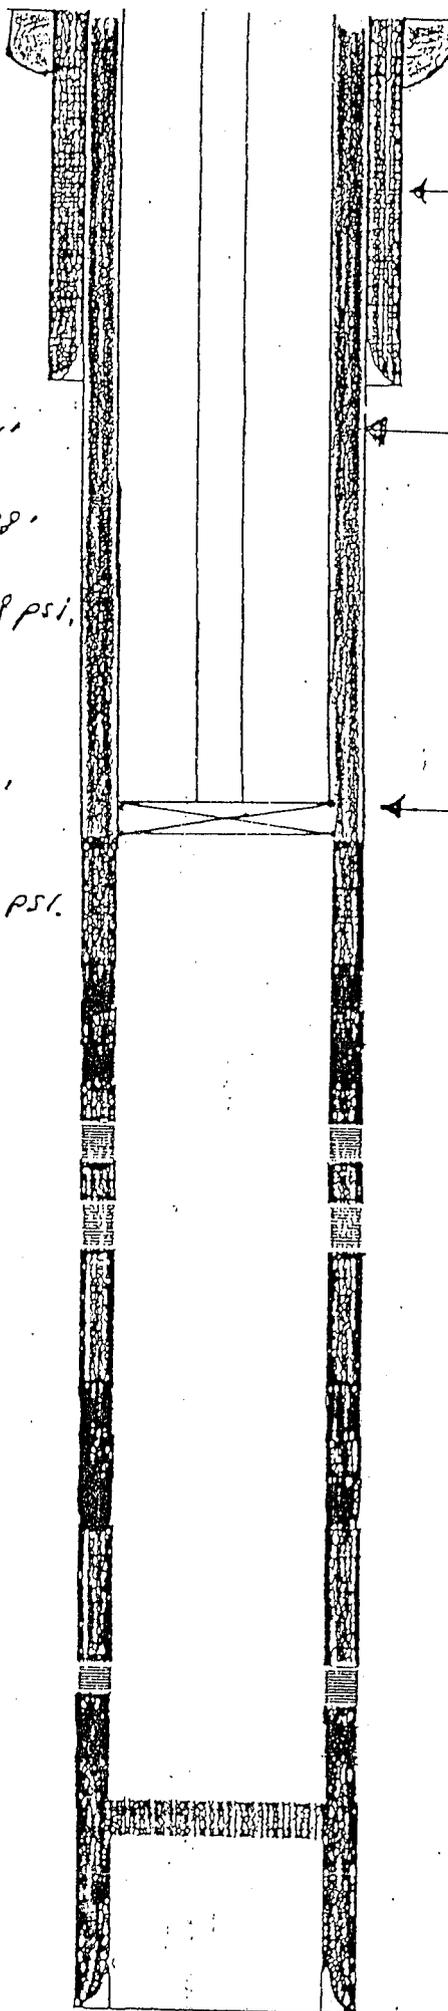

PBTD @ 5677
TD @ 5758 KB

(Not to Scale)

Petroglyph Operating Co., Inc.

Ute Tribal # 19-11

226 F5H 1484 FWH

NE SW SEC. 19-55-3W

Antelope Creek Field

Duchesne Co. Utah

358 # 14-20-1167-3514

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry to a different reservoir.
Use "APPLICATION FOR PERMIT" for such proposals

SUBMIT IN TRIPLICATE

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
Petroglyph Operating Company, Inc.

3. Address and Telephone No.
P.O. Box 607, Roosevelt, UT 84066 (435) 722-2531

4. Location of Well (Footage, Sec., T., R., or Survey Description)
**2226' FSL 1484' FWL
NESW Sec. 19-T5S-R3W**

5. Lease Designation and Serial No.
14-20-H6-3514

6. If Indian, Allottee or Tribe Name
Ute Indian Tribe

7. If Unit or CA, Agreement Designation
14-20-H62-4650

8. Well Name and No.
Ute Tribal 19-11

9. API Well No.
43-013-31967

10. Field and Pool, or Exploratory Area
Antelope Creek

11. County or Parish, State
Duchesne County, UT

12. CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Abandonment
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Recompletion
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Plugging Back
	<input type="checkbox"/> Casing Repair
	<input type="checkbox"/> Altering Casing
	<input checked="" type="checkbox"/> CONVERT TO INJECTOR
	<input type="checkbox"/> Change of Plans
	<input type="checkbox"/> New Construction
	<input type="checkbox"/> Non-Routine Fracturing
	<input type="checkbox"/> Water Shut-Off
	<input type="checkbox"/> Conversion to Injection
	<input type="checkbox"/> Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

Petroglyph Operating Company, Inc. has submitted an application for a UIC permit to convert the Ute Tribal 19-11 from a producing well to an injection well under the EPA Area Permit #UT2736-00000 within the Antelope Creek Waterflood Project Area located in Duchesne County, Utah.

14. I hereby certify that the foregoing is true and correct

Signed Waldo Smith Title Operations Coordinator Date 2-21-00

(This space for Federal or State official use)

Approved by _____ Title _____ Date _____

Conditions of Approval, if any:

UNITED STATES ENVIRONMENTAL PROTECTION AGENCY

WASHINGTON, DC 20460

RECEIVED

EPA

WELL REWORK RECORD

AUG 21 2000

NAME AND ADDRESS OF PERMITTEE
 Petroglyph Operating Company, Inc.
 P.O. Box 1839
 Hutchinson, KS 67504-1839


NAME AND ADDRESS OF CONTRACTOR
 Ute Indian Tribe
 DIVISION OF OIL, GAS AND MINING

LOCATE WELL AND OUTLINE UNIT ON SECTION PLAT -- 640 ACRES

STATE COUNTY PERMIT NUMBER
 UT Duchesne UT2736-04521

SURFACE LOCATION DESCRIPTION
 NE 1/4 OF SW 1/4 SECTION 19 TOWNSHIP 5S RANGE 3W

LOCATE WELL IN TWO DIRECTIONS FROM NEAREST LINES OF QUARTER SECTION AND DRILLING UNIT
 Surface Location 2226 ft. from South Line of quarter section
 and 1484 ft. from West Line of quarter section

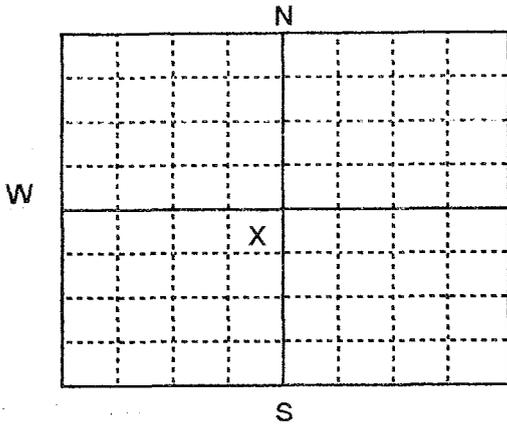

WELL ACTIVITY	Total Depth Before Rework	TYPE OF PERMIT
<input type="checkbox"/> Brine Disposal	5758	<input type="checkbox"/> Individual
<input checked="" type="checkbox"/> Enhanced Recovery	Total Depth After Rework	<input checked="" type="checkbox"/> Area
<input type="checkbox"/> Hydrocarbon Storage	5758	Number of Wells 1
Lease Name	Date Rework Commenced	Well Number
Ute Tribal	7/19/00	Ute Tribal 19-11
	Date Rework Completed	
	7/24/00	

WELL CASING RECORD - BEFORE REWORK

Casing		Cement		Perforations		Acid or Fracture Treatment Record
Size	Depth	Sacks	Type	From	To	
8-5/8" 24#	350'	220	Class H	4835	4841	3000 gal Boragel 30, 12500# 20/40 prop, 19000 16/30 prop
5-1/2" 15.5#	5738'	240/340	Highfill/Thixotrop	4435	4438	8477 gal Boragel 30, 12500# 20/40 prop & 19000# 16/30 prop
				4421	4424	8477 gal Boragel 30, 12500# 20/40 prop & 19000# 16/30 prop

WELL CASING RECORD - AFTER REWORK (Indicate Additions and Changes Only)

Casing		Cement		Perforations		Acid or Fracture Treatment Record
Size	Depth	Sacks	Type	From	To	
Same as above						See attached page

DESCRIBE REWORK OPERATIONS IN DETAIL
 USE ADDITIONAL SHEETS IF NECESSARY

WIRE LINE LOGS, LIST EACH TYPE
 Log Types Logged Intervals

Complete as injection w/ 2-3/8" @ 4354'. Set pkr, test annulus. Performed M.I.T. test. CNL, AIT, CBL

CERTIFICATION

I certify under the penalty of law that I have personally examined and am familiar with the information submitted in this document and all attachments and that, based on my inquiry of those individuals immediately responsible for obtaining the information, I believe that the information is true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment. (Ref. 40 CFR 144.32).

NAME AND OFFICIAL TITLE (Please type or print)

SIGNATURE

DATE SIGNED

Micheal Safford
 Operations Coordinator

7-31-00

Ute Tribal 19-11

Page 2 Treatment record

Perforations		Acid or Fracture
From	To	Treatment Record
4421	4438	Acidzed zone with 800 gals 7.5 HCL w/ additives & perf 4 spf
4551	4563	Frac w/ 32,000# sand 2,900# psi & perf 4 spf
4680	4690	Frac w/ 30,500# sand 3,000# psi & perf 4 spf
4832	4844	Acidzed zone with 1200 gals 7.5 HCL w/ additives, & perf 4 spf

RECEIVED

AUG 7 1 2000

DIVISION OF
OIL, GAS AND MINING

Ute Tribal 19-11
Wellbore Diagram
After Conversion

Well History:

4/17/98 Spud Well


5/22/98 First Production

5/6/98 C6.1 Zones
perfs 4421' to 4424' 4 spf
perfs 4435' to 4438' 4 spf
frac'ed ISIP 2398 psi

5/6/98 D5 zone
perfs 4835' to 4841' 4 spf
frac'ed ISIP 2423 psi

7/21/00 D9.2 zone
Perfs 4551' to 4553 4 spf
perfs 4555' to 4563 4 spf
frac'ed ISIP 3300 psi

7/21/00 D3 zone
perfs 4680' to 4684' 4 spf
perfs 4687' to 4690' 4 spf
frac'ed ISIP 3456

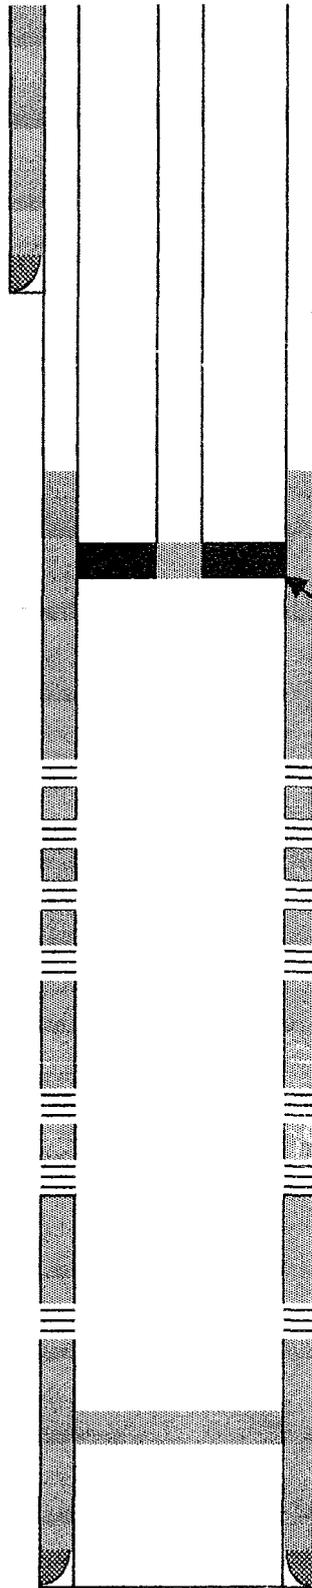

GL: 6077
KB: 6087
Conductor hole size 17 1/2"
13 3/8" 48# conductor @67'
cemented w/ 126 sxs
Surface Hole Size: 12 1/4"
8-5/8" 24# Surface Csg @
350' KB cm't'd w/ 220 sxs
Hole Size 7-7/8" bit
Cement Tops:
5 1/2" 15.5# csg @ 5738'
Cemented w/ 580 sxs.
Tubing 134 jts of 2-3/8" 4.7#
J55 @ 4340'
Packer @ 4349'

PBTD @ 5677'
TD @ 5758' KB

<p>Petroglyph Operating Co., Inc.</p> <p>Ute Tribal 19-11 2226' FSL & 1484' FWL NE SW Sec. 19-T5S-R3W</p> <p>Antelope Creek Field Duchesne Co, Utah Lease #14-20-H62-3514 API #43-013-31967</p>

(Not to Scale)

REC'D
AUG 21 2000
DIVISION OF
OIL, GAS AND MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry to a different reservoir.
Use "APPLICATION FOR PERMIT" for such proposals

SUBMIT IN TRIPLICATE

5. Lease Designation and Serial No.
14-20-H6-3514

6. If Indian, Allottee or Tribe Name
Ute Indian Tribe

7. If Unit or CA, Agreement Designation
14-20-H62-4650

8. Well Name and No.
Ute Tribal 19-11

9. API Well No.
43-013-31967

10. Field and Pool, or Exploratory Area
Antelope Creek

11. County or Parish, State
Duchesne County, UT

1. Type of Well
 Oil Well Gas Well Other
2. Name of Operator
Petroglyph Operating Company, Inc.
3. Address and Telephone No.
P.O. Box 607, Roosevelt, UT 84066 (435) 722-2531
4. Location of Well (Footage, Sec., T., R., or Survey Description)
**2226' FSL 1484' FWL
NESW Sec. 19-T5S-R3W**

12. CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION	
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Abandonment	<input type="checkbox"/> Change of Plans
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Recompletion	<input type="checkbox"/> New Construction
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Plugging Back	<input type="checkbox"/> Non-Routine Fracturing
	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> Water Shut-Off
	<input type="checkbox"/> Altering Casing	<input type="checkbox"/> Conversion to Injection
	<input checked="" type="checkbox"/> Commence injection	<input type="checkbox"/> Dispose Water

(Note. Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

Further to BLM & EPA approval (Permit #UT2736-04521), Enclosed are copies of the MIT and job summary. Injection commenced on 8/10/2000.

RECEIVED

AUG 21 2000

**DIVISION OF
OIL, GAS AND MINING**

14. I hereby certify that the foregoing is true and correct.

Signed *[Signature]* Title Operations Coordinator Date 8/16/2000

(This space for Federal or State official use)

Approved by _____ Title _____ Date _____

Conditions of Approval, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter in its jurisdiction.



UNITED STATES ENVIRONMENTAL PROTECTION AGENCY

REGION 8
999 18TH STREET - SUITE 500
DENVER, CO 80202-2466

AUG 9 2000

Ref: 8P-W-GW

CERTIFIED MAIL
RETURN RECEIPT REQUESTED

Mr. Micheal Safford
Operations Coordinator
Petroglyph Operating Company, Inc.
P.O. Box 607
Roosevelt, UT 84066

Re: AUTHORIZATION TO COMMENCE INJECTION
Ute Tribal #19-11 (UT04521)
Antelope Creek Field
EPA AREA PERMIT UT2736-00000
Duchesne County, Utah

Dear Mr. Safford:

Thank you for submitting information pertaining to Ute Tribal #19-11 to the Environmental Protection Agency (EPA) Region VIII Groundwater Program. Requirements of UIC Area Permit UT2736-00000 Part II Sections (C)(2) "Prior To Commencing Injection" required submittal of the following information:

1. Well Rework Record (EPA Form 7520-12) with after conversion well schematic,
2. Successfully run Mechanical Integrity Test (MIT) with pressure chart,
3. Injection zone fluid pore pressure survey.

All required information has been submitted, and has been reviewed and approved by the EPA. Petroglyph has complied with all pertinent conditions of UIC Area Permit UT2736-00000 Part II Section (C)(2). Therefore, effective upon your receipt of this letter, Administrative approval hereby is granted for injection into the Ute Tribal #19-11 under the conditions of UIC Permit UT2736-00000. The Director has determined that the maximum surface injection pressure for the Ute Tribal #19-11 shall not exceed 1900 psig.

RECEIVED

AUG 21 2000

DIVISION OF
OIL, GAS AND MINING

RECEIVED AUG 15 2000

KS/WF/SF *[Signature]*
8/15/00



Printed on Recycled Paper


Please be reminded that it is the responsibility of the permittee to be aware of, and to comply with, all conditions of the Permit. Effective upon receipt of this letter, EPA administration of this well is transferred to Mr. Al Craver Compliance Officer in the Office of Enforcement, Compliance, and Environmental Justice Technical Enforcement Program, who is your point of contact for routine compliance matters and reports.

Please send all reporting forms and other required correspondence to Mr. Craver at the address listed below, referencing EPA WELL ID: UT04521 on all reports and correspondence or contact Mr. Craver at 303.312.7821.

Mr. Al Craver,
 Technical Enforcement Program, Mail Code 8ENF-T
 U.S. Environmental Protection Agency
 999 18th Street, Suite 500
 Denver, Colorado, USA, 80202-2466

If you have any questions concerning this authorization or the Permit, please contact Mr. Dan Jackson of my staff at 303.312.6155.

Sincerely,



D. Edwin Hogle
 Director
 Ground Water Program

cc: Mr. Ronald Wopsock, Chairman
 Uintah & Ouray Business Committee
 Ute Indian Tribe

Ms. Elaine Willie, Environmental Director
 Ute Indian Tribe

Mr. Norman Cambridge
 BIA - Uintah & Ouray Agency

Mr. Gil Hunt
 State of Utah Natural Resources
 Division of Oil, Gas, and Mining

Mr. Jerry Kenczka
 BLM - Vernal District Office

RECEIVED

AUG 21 2000

DIVISION OF
 OIL, GAS AND MINING

RECEIVED AUG 15 2000

AUG 21 2000

Casing or Annulus Pressure Mechanical Integrity Test

DIVISION OF OIL, GAS AND MINING

U.S. Environmental Protection Agency
Underground Injection Control Program, UIC Direct Implementation Program 8P-W-GW
999 18th Street, Suite 500 Denver, CO 80202-2466

EPA Witness: _____ Date: 7 128 100
Test conducted by: CHAD STEVENSON
Others present: CLIFF ATWOOD

Well Name: UTE TRIBAL 19-11 Type: ER SWD Status: AC TA UC
Field: ANTELOPE CREEK
Location: 19-11 Sec: 19 T 5 N 18 R 3 E 1 W County: DUCHESNE State: UT
Operator: PETROGLYPH OPERATIONS COMPANY
Last MIT: / / Maximum Allowable Pressure: PSIG

- Is this a regularly scheduled test? [] Yes [] No
Initial test for permit? [X] Yes [] No
Test after well rework? [] Yes [] No
Well injecting during test? [] Yes [X] No If Yes, rate: _____ bpd

Pre-test casing/tubing annulus pressure: 1325 / VAC. psig

MIT DATA TABLE with columns for Test #1, Test #2, Test #3 and rows for Tubing Pressure and Casing/Tubing Annulus Pressure over time.

Does the annulus pressure build back up after the test? [] Yes [X] No

WORKOVER REPORT

7/26/00

Petroglyph Operating Co., Inc.

Operator: Petroglyph Operating Company, Inc.	Elevation: 0
Lease: Ute Tribal 19-11	0
API #: 43-013-31967	Property: 13410
Location: 19-S-3-W	AFE/EPE Number:
County, St.: Duchesne UT	Event Type: convert to injector

Activity Date Daily Cost Activity Description

7/24/00

7 AM set 5.5 pkr @ 4373'. RU HES. Treat perms 4421-38' w/ 800 gal 16% HCl w/ 128 gal xylene & 28 gal paraffin removal. Avg. rate 0.6 BPM, max rate 1 BPM, avg. press 1950#, max press 2001#. ISIP 1807, 5 min 1376, 10 min 916, 15 min 623. Total load 37 bbbls. RD HES & RU swab equipment. IFL @ surface. Made 6 runs & recovered 48 bbbls wtr. FFL @ 3100' PH @ 5. RD swab. Release 5.5 pkr @ 4373' & 5.5 RBP @ 4490'. POOH w/ tbg & tools. RU hydro-tester. RIH w/ notched collar, F nipple, 4' tbg sub, 5.5 hydro l pkr, & 134 jts 2 3/8" tbg. Testing to 3500#, no leaks. RD same. NO BOP & NU B1 adapter. Circ well w/ 100 bbbls pkr fluid. Drop setting tool. Press to 1800# & set pkr @ 4349' w/ 10,000# camp. F nipple & EOT @ 4354'. NU well head & surface valves. Retrieve setting tool w/ sand line. Rack out pump & lines. 450 bbbls wtr lost. 1500 psi left on annulus.

TUBING DETAIL	LENGTH	DEPTH
KB	10.00	10.00
134 jts 2 3/8" 8 rd tbg	4330.65	4340.65
x-over 2 3/8" box x 2 7/8" pin	.75	4341.40
Weatherford Hydro l pkr	7.70	4349.10
2 3/8" tbg sub	4.10	4353.20
2 3/8" x 1.81 F nipple	.90	4354.10
2 3/8" notched collar	.43	4354.53
		4354.53

7/22/00

7 AM circ well w/ 90 bbbls KCl wtr. POOH & LD 143 jts 3.5 P-110 tbg, 5.5 pkr, & ret head. RU 2 3/8" tbg & OBP equipment. PU & RIH w/ ret head, 5.5 pkr, & 142 jts 2 5/8" tbg. Tag sand @ 4579'. Circ sand out to 5.5 RBP @ 4622'. Release, move & reset RBP @ 4430'. Test tools to 2000#. Pull 5.5 pkr above perms. EOT @ 4373'. SWIFN @ 5:30 PM

7/21/00

7 AM perms 4832-44'. RU swab IFL @ 2200'. Made 4 runs & recovered 38 bbbls wtr. Tbg was dry. PH @ 1. Load tbg w/ KCl wtr. Release 5.5 pkr @ 4756'. RIH & tag 5.5 RBP @ 4492'. Circ well w/ KCl wtr until clean. Move tools to test to 3000 psi, held. RBP @ 4735'. Pkr @ 4632'. RU HES & frac perms 4680-90' w/ 30,500# sand. Avg. rate 18 BPM, max 15 BPM, avg. press 3000#, max press 3456#. Total load 179 bbbls. Flow frac back to float tank recovered 35 bbbls. Release 5.5 pkr & circ sand off 5.5 RBP. Move & test tools to 3000 psi, held. RBP @ 4622'. Pkr @ 4505'. Frac perms 4551-63' w/ 32,000# sand. Avg. rate 19.7 BPM, max rate 19.9 BPM, avg. press 2900#, max press 3300#. Total load was 224 bbbls. Possible communication during flush. Bleed off tbg, release pkr & circ w/ 110 bbbls wtr w/ sand in returns. POOH w/ 20 jts 3.5 tbg. EOT @ 3874'. SWIFN @ 8 PM.

RECEIVED

AUG 21 2000

DIVISION OF
OIL, GAS AND MINING

WORKOVER REPORT

Petroglyph Operating Co., Inc.

7/26/00

Operator:	Petroglyph Operating Company, Inc.	Elevation:	0
Well:	Ute Tribal 19-11		0
County, St.:	Duchesne UT		

Activity Date	Daily Cost	Activity Description
---------------	------------	----------------------

7/20/00

PERFORATIONS:

4832-4844	Green River D (05)	4 SPF	48 shots
4687-4690	Green River D (03)	4 SPF	12 shots
4680-4884	Green River C (03)	4 SPF	18 shots
4556-4563	Green River C (09.2)	4 SPF	32 shots
4551-4553	Green River C (09.2)	4 SPF	8 shots
4435-4438	Green River C (06.1)	4 SPF	12 shots
4421-4424	Green River C (06.1)	4 SPF	12 shots

7 AM RU Weatherford wireline. Perf green river fm from 4832-44', 4680-84', 4687-90', 4551-53', 4555-63' w/ 4 csg guns spf. 120 deg phasing & 116 FFL holes. Had 3 miss fires while pack. RD same. RU 3.5 tbg & BOP equipment. PU & RIH w/ 5.5 RBP, 5.5 pkr. & 156 jts 3.5 P-110 tbg. Set 5.5 RBP @ 4922'. LD jt & set pkr @ 4895'. Test tool to 2500#, held. Move & reset pkr @ 4756'. RU HES. Treat D5 perms w/ 1200 gal 15% HCl, 180 gal Xylene & 72 gal paraffin removal. Breakdwn psi 1880#. Injection rate of 1 BPM @ 1700#. ISIP 1797, 5 min 987, 10 min 652, 15 min 426. Total load = 104 bbis. Over displaced w/ 10 bbis wtr. SWIFN @ 8 PM.

7/19/00

7 AM RD Lead to haul off pumping unit. RU PU & equipment. Unseat pump. Flush ends w/ 30 bbis wtr. P00H & LD 66 slick 7/8" rods, 122 slick 3/4" rods, 5 guided 3/4" rods, & 1 3/4" pump #5112. RU tbg equipment. ND well head. Release 5.5 TAC @ 4396'. NU BOP. P00H w/ 156 jts 2 7/8" tbg. LD BHA. RIH w/ 4 3/4 bit, 5 1/2" x 15.5 csg, scraper, & 179 jts 2 7/8" tbg. Tag fill @ 5544'. PBTD @ 5694'. P00H & LD 179 jts 2 7/8" csg, scraper, & bit. SWIFN @ 8 PM.

Cumulative Cost: /

Days Since Start: 6

RECEIVED

AUG 21 2000

DIVISION OF Page 2
OIL, GAS AND MINING

Mechanical Integrity Test

Casing or Annulus Pressure Mechanical Integrity Test

U.S. Environmental Protection Agency
Underground Injection Control Program, UIC Direct Implementation Program 8P-W-GW
999 18th Street, Suite 500 Denver, CO 80202-2466

EPA Witness: _____ Date: 11.22.05

Test conducted by: CHAD STEVENSON

Others present: 431013131967 55 300 19

Well Name: <u>19-11</u>	Type: ER SWD	Status: AC TA UC
Field: <u>ANTELOPE CREEK</u>		
Location: <u>19-11</u> Sec: _____ T _____ N/S R _____ E/W County: <u>Duchesne</u> State: <u>UT</u>		
Operator: <u>PETROGLYPH OPERATION</u>		
Last MIT: <u>1</u> / <u>1</u>		Maximum Allowable Pressure: _____ PSIG

- Is this a regularly scheduled test? Yes [] No
- Initial test for permit? [] Yes [] No
- Test after well rework? [] Yes [] No
- Well injecting during test? Yes [] No

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY**

If Yes, rate: _____ 50 bpd

Pre-test casing/tubing annulus pressure: _____ psig

MIT DATA TABLE	Test #1	Test #2	Test #3
TUBING PRESSURE			
Initial Pressure	<u>1900</u> psig	psig	psig
End of test pressure	<u>1900</u> psig	psig	psig
CASING/TUBING ANNULUS PRESSURE			
0 minutes	<u>1320</u> psig	psig	psig
5 minutes	<u>1320</u> psig	psig	psig
10 minutes	<u>1320</u> psig	psig	psig
15 minutes	<u>1320</u> psig	psig	psig
20 minutes	<u>1320</u> psig	psig	psig
25 minutes	<u>1320</u> psig	psig	psig
30 minutes	<u>1320</u> psig	psig	psig
<u>1 Hour</u> minutes	<u>1320</u> psig	psig	psig
minutes	psig	psig	psig
RESULT	[] Pass [] Fail	[] Pass [] Fail	[] Pass [] Fail

Does the annulus pressure build back up after the test? [] Yes [] No



UNITED STATES ENVIRONMENTAL PROTECTION AGENCY
REGION 8

1595 Wynkoop Street
DENVER, CO 80202-1129
Phone 800-227-8917
<http://www.epa.gov/region08>

Ref: 8ENF-UFO

MAR 19 2010

CERTIFIED MAIL 7005-0390-0000-4848-7058
RETURN RECEIPT REQUESTED

Jason Bywater, District Supervisor
Petroglyph Operating Company, Inc.
P.O. Box 607
Roosevelt, Utah 84066

43 013 31967
5S 3W 19

Re: Underground Injection Control (UIC)
Permission To Resume Injection
Ute Tribal #19-11 Well
EPA Permit# UT20736-04521
Antelope Creek Oil Field
Duchesne County, Utah

Dear Mr. Bywater:

On March 17, 2010, EPA received information from Petroglyph Operating Company, Inc. on the above referenced well concerning the workover to address leaks in the well's tubing and packer and the followup mechanical integrity test (MIT) conducted on March 9, 2010. The data submitted shows that the well passed the required MIT. Therefore, pursuant to Title 40 of the Code of Federal Regulations Section 144.51(q)(2) (40 C.F.R. §144.51(q)(2)), permission to resume injection is granted. Under continuous service, the next MIT will be due on or before March 9, 2015.

Pursuant to 40 C.F.R. §144.52(a)(6), if the well is not used for a period of at least two (2) years ("temporary abandonment"), it shall be plugged and abandoned unless EPA is notified and procedures are described to EPA ensuring the well will not endanger underground sources of drinking water ("non-endangerment demonstration") during its continued temporary abandonment. A successful MIT is an acceptable non-endangerment demonstration and would be necessary every two (2) years the well continues in temporary abandonment.

Failure to comply with a UIC Permit, or the UIC regulations found at 40 C.F.R. Parts 144 through 148 constitute one or more violations of the Safe Drinking Water Act, 42 U.S.C. §300h. Such non-compliance may subject you to formal enforcement by EPA, as codified at 40 C.F.R. Part 22.

RECEIVED

MAR 29 2010

DIV. OF OIL, GAS & MINING

If you have any questions concerning this letter, you may contact Nathan Wiser at (303) 312-6211. Please direct all correspondence to the attention of Nathan Wiser at Mail Code 8ENF-UFO.

Sincerely,



Mark A.R. Chalfant
Director
Technical Enforcement Program

cc: Curtis Cesspooch, Chairman
Uintah & Ouray Business Committee
P.O. Box 190
Fort Duchesne, Utah 84026

Ferron Secakuku, Natural Resources Director
Ute Indian Tribe
P.O. Box 190
Fort Duchesne, Utah 84026

Gil Hunt
Utah Division of Oil, Gas and Mining
P.O. Box 145801
Salt Lake City, Utah 84114

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: 14-20-H62-3514
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
1. TYPE OF WELL Water Injection Well	8. WELL NAME and NUMBER: UTE TRIBAL 19-11
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO	9. API NUMBER: 43013319670000
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703	PHONE NUMBER: 208 685-7685 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2226 FSL 1484 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESW Section: 19 Township: 05.0S Range: 03.0W Meridian: U	9. FIELD and POOL or WILDCAT: ANTELOPE CREEK COUNTY: DUCHESNE STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 8/1/2013 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input checked="" type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On or around 8/1/2013, depending on equipment availability, we plan to acidize the existing perforations of the well referenced above with 15% Hcl with additives using a Coiled Tubing Unit through the injection tubing. We do not anticipate having to release the injection packer or pull the injection tubing. We plan to rig up the Coiled Tubing Unit and related equipment, run in hole through the injection tubing, circulate and clean the well as needed, establish and injection rate and pump approx 1,750 gal 15% Hcl with additives and approx 1,750 gal 0.3% Chlorine Dioxide solution followed by the appropriate fresh water over flush. The well will then be flowed back to a neutral PH before being returned to injection. Exact volumes and additives will be reported at a later date. This work is being performed to improved the injection rates of the referenced well.

Accepted by the Utah Division of Oil, Gas and Mining

Date: July 29, 2013

By: *Derek Quist*

NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 7/25/2013	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS		5. LEASE DESIGNATION AND SERIAL NUMBER: INDIAN
Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Water Injection Well		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO		8. WELL NAME and NUMBER: UTE TRIBAL 19-11
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703		9. API NUMBER: 43013319670000
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2226 FSL 1484 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESW Section: 19 Township: 05.0S Range: 03.0W Meridian: U		9. FIELD and POOL or WILDCAT: ANTELOPE CREEK
		COUNTY: DUCHESNE
		STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input checked="" type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 8/2/2013	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On 8/2/2013 Petroglyph Operating rigged up a coiled tubing unit, ran in through the injection tubing and circulated and cleaned the well. Heavy scale and hard oil encountered. We then pumped the prescribed Acid and Chlorine Dioxide treatment followed by a 50 Bbls fresh water over flush. Prescribed treatment was the following: 1764 gal 15% Hcl, 1764 gal Chlorine Dioxide @ 3000 PPM, 8 gal ASA-300 Anti-Sludge Additive, 10 gal 4097-FE-5 Iron Control, 3 gal 7508-I-24 Acid Corrosion Inhibitor, 4 gal 9408-NE-20 Non Emulsifer, 10 gal 7688-EMS_44 Micullar Surfactant & 5 gal EC 1317A. This treatment was performed to improve the injection rates of this well.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
September 18, 2013**

NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 8/21/2013	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: INDIAN
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
1. TYPE OF WELL Water Injection Well	8. WELL NAME and NUMBER: UTE TRIBAL 19-11
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO	9. API NUMBER: 43013319670000
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703	PHONE NUMBER: 208 685-7685 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2226 FSL 1484 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESW Section: 19 Township: 05.0S Range: 03.0W Meridian: U	9. FIELD and POOL or WILDCAT: ANTELOPE CREEK COUNTY: DUCHESNE STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 7/13/2015 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input checked="" type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

This well is currently down due to loss of mechanical integrity. We intend to re-perforate the well before restoring mechanical integrity. Our plan is as follows: release the packer and pull the tubing, inspecting the tubing as it comes out of the hole, make a bit and scraper run past the perforations, and circulate and clean the well. We will re-perforate existing perforations and add new perforations. Existing perforations are the following: 4421-24, 4435-38, 4551-53, 4555-63, 4680-84, 4687-90 & 4835-41. We plan to shoot the following: 4420-26, 4432-42, 4550-64, 4680-84, 4686-92, 4780-83, 4830-44, 5154-58, 5193-97, 5202-10 & 5240-44. All perforations lie within the permitted injection interval of 3,610'-5,597'. We will break down perfs, test their injection rates, then run in an Arrowset 1 Packer and perform an MIT on the casing to 1900psi. We will resume injection after approved.

Accepted by the Utah Division of Oil, Gas and Mining

Date: July 15, 2015

By: *Dark Oust*

NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 7/9/2015	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: INDIAN
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Water Injection Well		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO		8. WELL NAME and NUMBER: UTE TRIBAL 19-11
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703		9. API NUMBER: 43013319670000
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2226 FSL 1484 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESW Section: 19 Township: 05.0S Range: 03.0W Meridian: U		9. FIELD and POOL or WILDCAT: ANTELOPE CREEK
		COUNTY: DUCHESNE
		STATE: UTAH

11.

CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 7/27/2015	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input checked="" type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Please see attached.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
August 03, 2015**

NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 7/30/2015	

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 9

SUNDRY NOTICES AND REPORTS ON WELLS		5. LEASE DESIGNATION AND SERIAL NUMBER: 14-20-H62-3514
Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: Ute Indian Tribe
1. TYPE OF WELL OIL WELL <input type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER _____		7. UNIT or CA AGREEMENT NAME: 14-20-H62-4650
2. NAME OF OPERATOR: Petroglyph Operating Company Inc.		8. WELL NAME and NUMBER: Ute Tribal 19-11
3. ADDRESS OF OPERATOR: P.O. Box 607 CITY Roosevelt STATE UT ZIP 84066		9. API NUMBER: 4301331967
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2226' FSL, 1484' FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: NESW 19 5S 3W U		10. FIELD AND POOL, OR WILDCAT: Antelope Creek COUNTY: Duchesne STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will start: _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input checked="" type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLARE
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of work completion: 7/27/2015	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/RESUME)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: _____
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On 7/13/2015 we rigged up, released the packer, pulled the tubing and scan logged it on the way out. We laid down the whole string. We picked up new tubing, made a bit and scraper run to PBD, 5355' then circulated and cleaned the well. We then ran in hole and perforated the following: 4420'-26', 4432'-42', 4550'-64', 4680'-84', 4686'-92', 4780'-83', 4830'-44', 5154'-58', 5193'-97', 5202'-10', 5240'-44'. Existing perforations were: 4421'-24', 4435'-38', 4451'-53', 4455'-63', 4680'-84', 4687'-90', 4832'-41'. We isolated various intervals, broke down perms then pulled all tools. We then ran in with a new Arrowset 1 Packer and new tubing, doping all joints on the way in and pressure tested the tubing and successfully performed an MIT on the casing to 1900 psi with no loss. Perforations were made using were Titan 3-1/8" perf guns containing 19 grams charges, 0.40" EHD, 26" TTP, 4 SPF @ 120° Phased. MIT has been submitted to EPA for approval to resume injection. Injection will resume once appropriate approval is granted. Contact our staff if you need any additional information.

NAME (PLEASE PRINT) <u>Rodrigo Jurado</u>	TITLE <u>Regulatory Compliance Specialist</u>
SIGNATURE	DATE <u>7/30/2015</u>

(This space for State use only)



UNITED STATES ENVIRONMENTAL PROTECTION AGENCY
REGION 8

1595 Wynkoop Street
DENVER, CO 80202-1129
Phone 800-227-8917
<http://www.epa.gov/region08>

AUG 07 2015

RECEIVED
AUG 13 2015
DIV. OF OIL, GAS & MINING

Ref: 8ENF-UFO

CERTIFIED MAIL 7009-3410-0000-2600-8435
RETURN RECEIPT REQUESTED

Mr. Les Farnsworth, District Supervisor
Petroglyph Operating Company, Inc.
4116 W 3000 S Ioka Lane
P.O. Box 607
Roosevelt, Utah 84066

19 55 3W

Re: Underground Injection Control (UIC)
Permission to Resume Injection
Tribal 19-11 Well
EPA Permit ID# UT20736-04521
API # 43-013-31967
Antelope Creek Oil Field
Duchesne County, Utah

Accepted by the
Utah Division of
Oil, Gas and Mining

FOR RECORD ONLY

Dear Mr. Farnsworth:


On August 4, 2015, the Environmental Protection Agency (EPA) received information from Petroglyph Operating Company, Inc. on the above referenced well concerning the workover to address a loss of mechanical integrity and the followup mechanical integrity test (MIT) conducted on July 27, 2015. The data submitted shows that the well passed the required MIT. Therefore, pursuant to Title 40 of the Code of Federal Regulations Section 144.51(q)(2) (40 C.F.R. § 144.51(q)(2)), permission to resume injection is granted. Under continuous service, the next MIT will be due on or before July 27, 2020.

Pursuant to 40 C.F.R. § 144.52(a)(6), if the well is not used for a period of at least two (2) years ("temporary abandonment"), it shall be plugged and abandoned unless the EPA is notified and procedures are described to the EPA ensuring the well will not endanger underground sources of drinking water ("non-endangerment demonstration") during its continued temporary abandonment. A successful MIT is an acceptable non-endangerment demonstration and would be necessary every two (2) years the well continues in temporary abandonment.

Failure to comply with a UIC Permit, or the UIC regulations found at 40 C.F.R. Parts 144 through 148 constitute one or more violations of the Safe Drinking Water Act, 42 U.S.C. § 300h. Such non-compliance may subject you to formal enforcement by the EPA, as codified at 40 C.F.R. Part 22.

If you have any questions concerning this letter, you may contact Gary Wang at (303) 312-6469. Please direct all correspondence to the attention of Gary Wang at Mail Code 8ENF-UFO.

Sincerely,



Arturo Palomares, Director
Water Technical Enforcement Program
Office of Enforcement, Compliance
and Environmental Justice

cc: Shaun Chapoose, Chairman, Uintah & Ouray Business Committee
Edred Secakuku, Vice-Chairman, Uintah & Ouray Business Committee
Reannin Tapoof, Executive Assistant, Uintah & Ouray Business Committee

Arturo Palomares
Director
Water Technical Enforcement Program
Office of Enforcement, Compliance
and Environmental Justice

FOR RECORD ONLY
