

NEWFIELD



September 1, 2005

State of Utah
Division of Oil, Gas & Mining
Attn: Diana Whitney
1594 West North Temple - Suite 1210
P.O. Box 145801
Salt Lake City, Utah 84114-5801

RE: Applications for Permit to Drill: Ashley Federal 1-25-9-15, 2-25-9-15, 4-25-9-15, 5-25-9-15, and 12-25-9-15.

Dear Diana:

Enclosed find APD's on the above referenced wells. The proposed 1-25-9-15, 2-25-9-15, and 4-25-9-15 are Exception Locations. Our Land Department will send you the required Exception Location Letter. If you have any questions, feel free to give either Shon Mckinnon or myself a call.

Sincerely,

Mandie Crozier
Regulatory Specialist

mc
enclosures

RECEIVED

SEP 02 2005

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0136
Expires January 31, 2004

5. Lease Serial No.
UTU-66185

6. If Indian, Allottee or Tribe Name
N/A

7. If Unit or CA Agreement, Name and No.
Ashley

8. Lease Name and Well No.
Ashley Federal 5-25-9-15

9. API Well No.
43-013-32885

10. Field and Pool, or Exploratory
~~Mendocino State~~ Undesignated

11. Sec., T., R., M., or Blk. and Survey or Area
SW/NW Sec. 25, T9S R15E

12. County or Parish
Duchesne

13. State
UT

1a. Type of Work: ☒ DRILL ☐ REENTER

1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other ☒ Single Zone ☐ Multiple Zone

2. Name of Operator
Newfield Production Company

3a. Address
Route #3 Box 3630, Myton UT 84052

3b. Phone No. (include area code)
(435) 646-3721

4. Location of Well (Report location clearly and in accordance with any State requirements. *)
At surface SW/NW 2091' FNL 505' FWL 569357X 40.003469
At proposed prod. zone 4428248Y -110.187455

14. Distance in miles and direction from nearest town or post office*
Approximatley 17.7 miles southwest of Myton, Utah

15. Distance from proposed*
location to nearest
property or lease line, ft.
(Also to nearest drig. unit line, if any) Approx. 2091' f/line, 3189' f/unit

16. No. of Acres in lease
2,286.43

17. Spacing Unit dedicated to this well
40 Acres

18. Distance from proposed location*
to nearest well, drilling, completed,
applied for, on this lease, ft. Approx. 1375'

19. Proposed Depth
5830'

20. BLM/BIA Bond No. on file
UT0056

21. Elevations (Show whether DF, KDB, RT, GL, etc.)
6301' GL


22. Approximate date work will start*
1st Quarter 2006

23. Estimated duration
Approximately seven (7) days from spud to rig release.

24. Attachments


The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature

Title
Regulatory Specialist

Name (Printed/Typed)
Mandie Crozier

Date
8/31/05

Approved by (Signature)

Title
ENVIRONMENTAL SCIENTIST III

Name (Printed/Typed)
BRADLEY G. HILL
ENVIRONMENTAL SCIENTIST III

Date
09-06-05

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on reverse)

Federal Approval or this
Action is Necessary


RECEIVED

SEP 02 2005

DIV. OF OIL, GAS & MINING

T9S, R15E, S.L.B.&M.


NEWFIELD PRODUCTION COMPANY

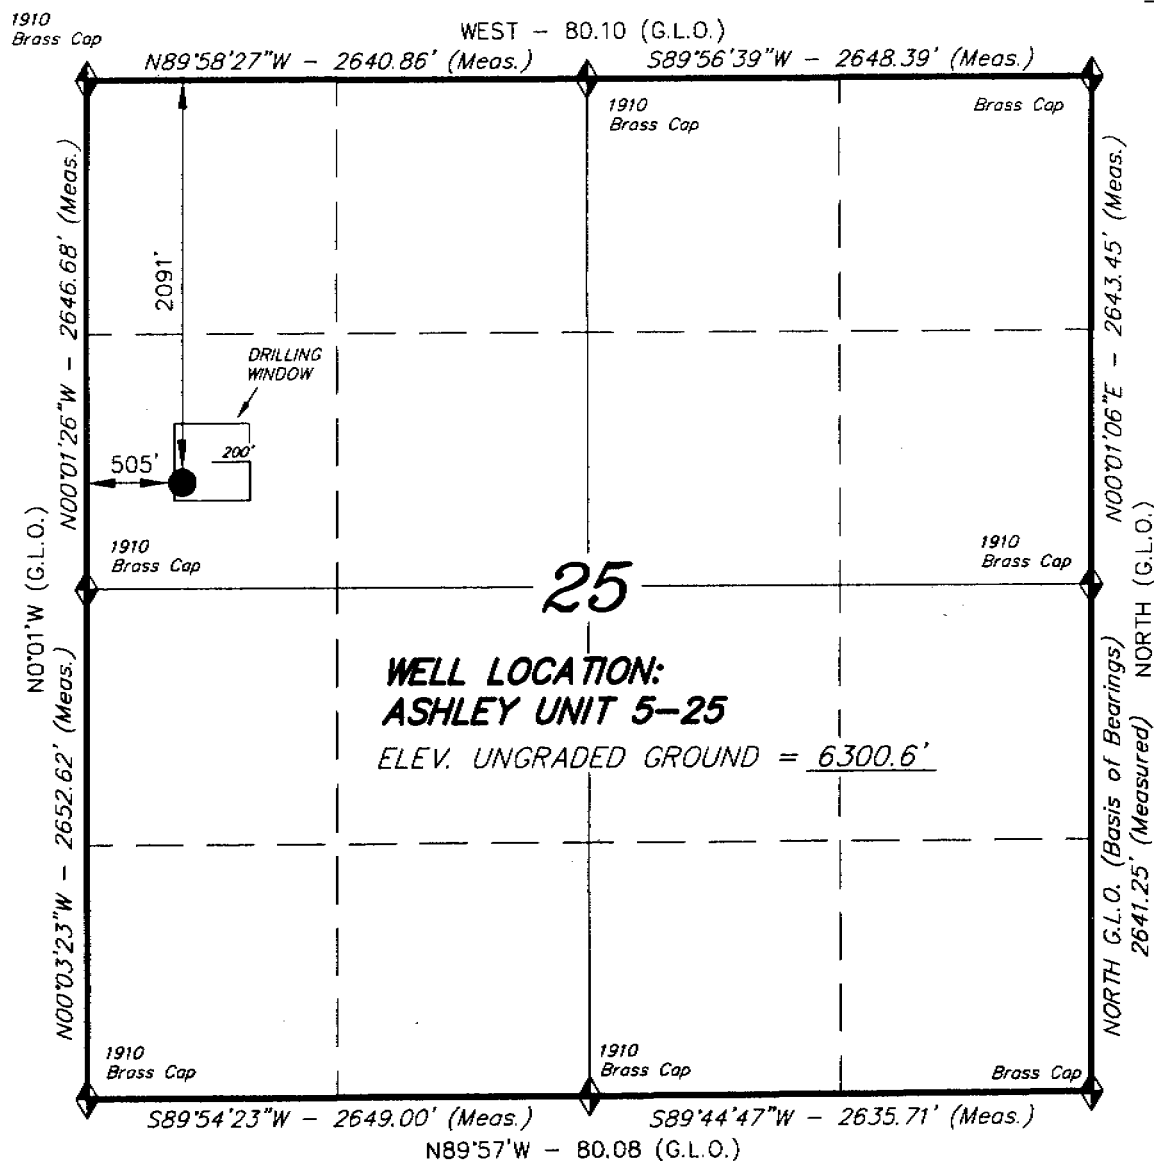

WELL LOCATION, ASHLEY UNIT 5-25,
LOCATED AS SHOWN IN THE SW 1/4 NW
1/4 OF SECTION 25, T9S, R15E,
S.L.B.&M. DUCHESNE COUNTY, UTAH.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
MADE BY ME OR UNDER MY SUPERVISION AND THAT
THE SAME ARE TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF No.189377



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; U.S.G.S. 7-1/2 min QUAD (MYTON SW)

TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

SCALE: 1" = 1000'

SURVEYED BY: D.P.

DATE: 7-7-05

DRAWN BY: F.T.M.

NOTES:

FILE #

**NEWFIELD PRODUCTION COMPANY
ASHLEY FEDERAL #5-25-9-15
SW/NW SECTION 25, T9S, R15E
DUCHESNE COUNTY, UTAH**

ONSHORE ORDER NO. 1

DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta	0' - 2390'
Green River	2390'
Wasatch	5830'

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation 2390' - 5830' - Oil

4. PROPOSED CASING PROGRAM

Please refer to the Monument Butte Field Standard Operation Procedure (SOP).

5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:

Please refer to the Monument Butte Field SOP. See Exhibit "C".

6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:

Please refer to the Monument Butte Field SOP.

7. AUXILIARY SAFETY EQUIPMENT TO BE USED:

Please refer to the Monument Butte Field SOP.

8. TESTING, LOGGING AND CORING PROGRAMS:

Please refer to the Monument Butte Field SOP.

9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:

The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered.

10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:

Please refer to the Monument Butte Field SOP.

NEWFIELD PRODUCTION COMPANY
ASHLEY FEDERAL #5-25-9-15
SW/NW SECTION 25, T9S, R15E
DUCHESNE COUNTY, UTAH

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Ashley Federal #5-25-9-15 located in the SW 1/4 NW 1/4 Section 25, T9S, R15E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.6 miles \pm to the junction of this highway and UT State Hwy 53; proceed southwesterly along Hwy 53 - 1.8 miles \pm to it's junction with an existing road to the southwest; proceed southwesterly - 12.5 miles \pm to it's junction with the beginning of the proposed access road; proceed along the proposed access road 9,720' \pm to the proposed well location.

2. PLANNED ACCESS ROAD

See Topographic Map "B" for the location of the proposed access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

All permanent surfaces equipment will be painted Olive Black.
Please refer to the Monument Butte Field Standard Operating Procedure (SOP).

5. LOCATION AND TYPE OF WATER SUPPLY

Please refer to the Monument Butte Field SOP. See Exhibit "A".

6. SOURCE OF CONSTRUCTION MATERIALS

Please refer to the Monument Butte Field SOP.

7. METHODS FOR HANDLING WASTE DISPOSAL

Please refer to the Monument Butte Field SOP.

8. ANCILLARY FACILITIES

Please refer to the Monument Butte Field SOP.

9. **WELL SITE LAYOUT**

See attached Location Layout Diagram.

10. **PLANS FOR RESTORATION OF SURFACE**

Please refer to the Monument Butte Field SOP.

11. **SURFACE OWNERSHIP** - Bureau Of Land Management

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. MOAC Report #04-205, 6/28/05. Paleontological Resource Survey prepared by, Wade E. Miller, 8/29/05. See attached report cover pages, Exhibit "D".

For the Ashley Federal #5-25-9-15 Newfield Production Company requests 250' of disturbed area be granted in Lease UTU-74391 and 9470' of disturbed area be granted in Lease UTU-66185 to allow for construction of the proposed access road. **Refer to Topographic Map "B".** The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be a culvert as deemed necessary along the secondary road from the proposed 9-26-9-15 well location. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 250' of disturbed area be granted in Lease UTU-74391 and 9470' of disturbed area be granted in Lease UTU-66185 to allow for construction of the proposed gas lines. It is proposed that the ROW and disturbed area will be 50' wide to allow for construction of a 6" gas gathering line, and a 3" poly fuel gas line. Both lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Newfield Production Company requests 250' of disturbed area be granted in Lease UTU-74391 and 9470' of disturbed area be granted in Lease UTU-66185 to allow for construction of the proposed water lines. It is proposed that the ROW and disturbed area will be 50' wide to allow for construction of a buried 3" steel water injection line and a 3" poly water return line. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Water Disposal

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

Threatened, Endangered, And Other Sensitive Species

Golden Eagle: Due to this proposed well access roads proximity (less than 0.5 mile) to an existing inactive golden eagle nest site, no new construction or surface disturbing activities will

be allowed between February 1 and July 15. If the nest remains inactive on July 15th (based on a pre-construction survey by a qualified biologist), the operator may construct and drill the location between July 15 and February 1 of the following year. If the nest site becomes active prior to July 15, no new construction or surface disturbing activities will be allowed within 0.5 mile of the nest until the nest becomes inactive for two full breeding seasons. In the event that this well becomes a producing well, it must be equipped with a multi-cylinder engine or hospital muffler to reduce noise levels.

Reserve Pit Liner

A 12 mil liner with felt is required. Please refer to the Monument Butte Field SOP.

Location and Reserve Pit Reclamation

Please refer to the Monument Butte Field SOP.

The following seed mixture will be used on the topsoil stockpile, to the recontoured surface of the reserve pit, and for final reclamation: (All poundages are in pure live seed)

Needle and Threadgrass	<i>Stipa Comata</i>	4 lbs/acre
Indian Ricegrass	<i>Oryzopsis Hymenoides</i>	4 lbs/acre
Black Sage	<i>Artemisia Nova</i>	1 lbs/acre
Scarlet Globemallow	<i>Sphaeralcea Conccinea</i>	3 lbs/acre

If the proposed location is converted to an injection well, pit backfill, spreading of topsoil, and seeding can all be done at the time of conversion.

Details of the On-Site Inspection

The proposed Ashley Federal #5-25-9-15 was on-sited on 6/9/05. The following were present; Shon Mckinnon (Newfeild Production), Byron Tolman (Bureau of Land Management), and Amy Torres (Bureau of Landmanagement). Weather conditions were clear and ground cover was 100% open.

13. LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION

Representative

Name: Shon Mckinnon
Address: Route #3 Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #5-25-9-15 SW/NW Section 25, Township 9S, Range 15E: Lease UTU-66185 Duchesne County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by Hartford Accident #4488944.

I hereby certify that the proposed drillsite and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and

subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

8/31/05

Date

Mandie Crozier

Mandie Crozier



Regulatory Specialist

Newfield Production Company

NEWFIELD PRODUCTION COMPANY

ASHLEY UNIT 5-25

Section 25, T9S, R15E, S.L.B.&M.

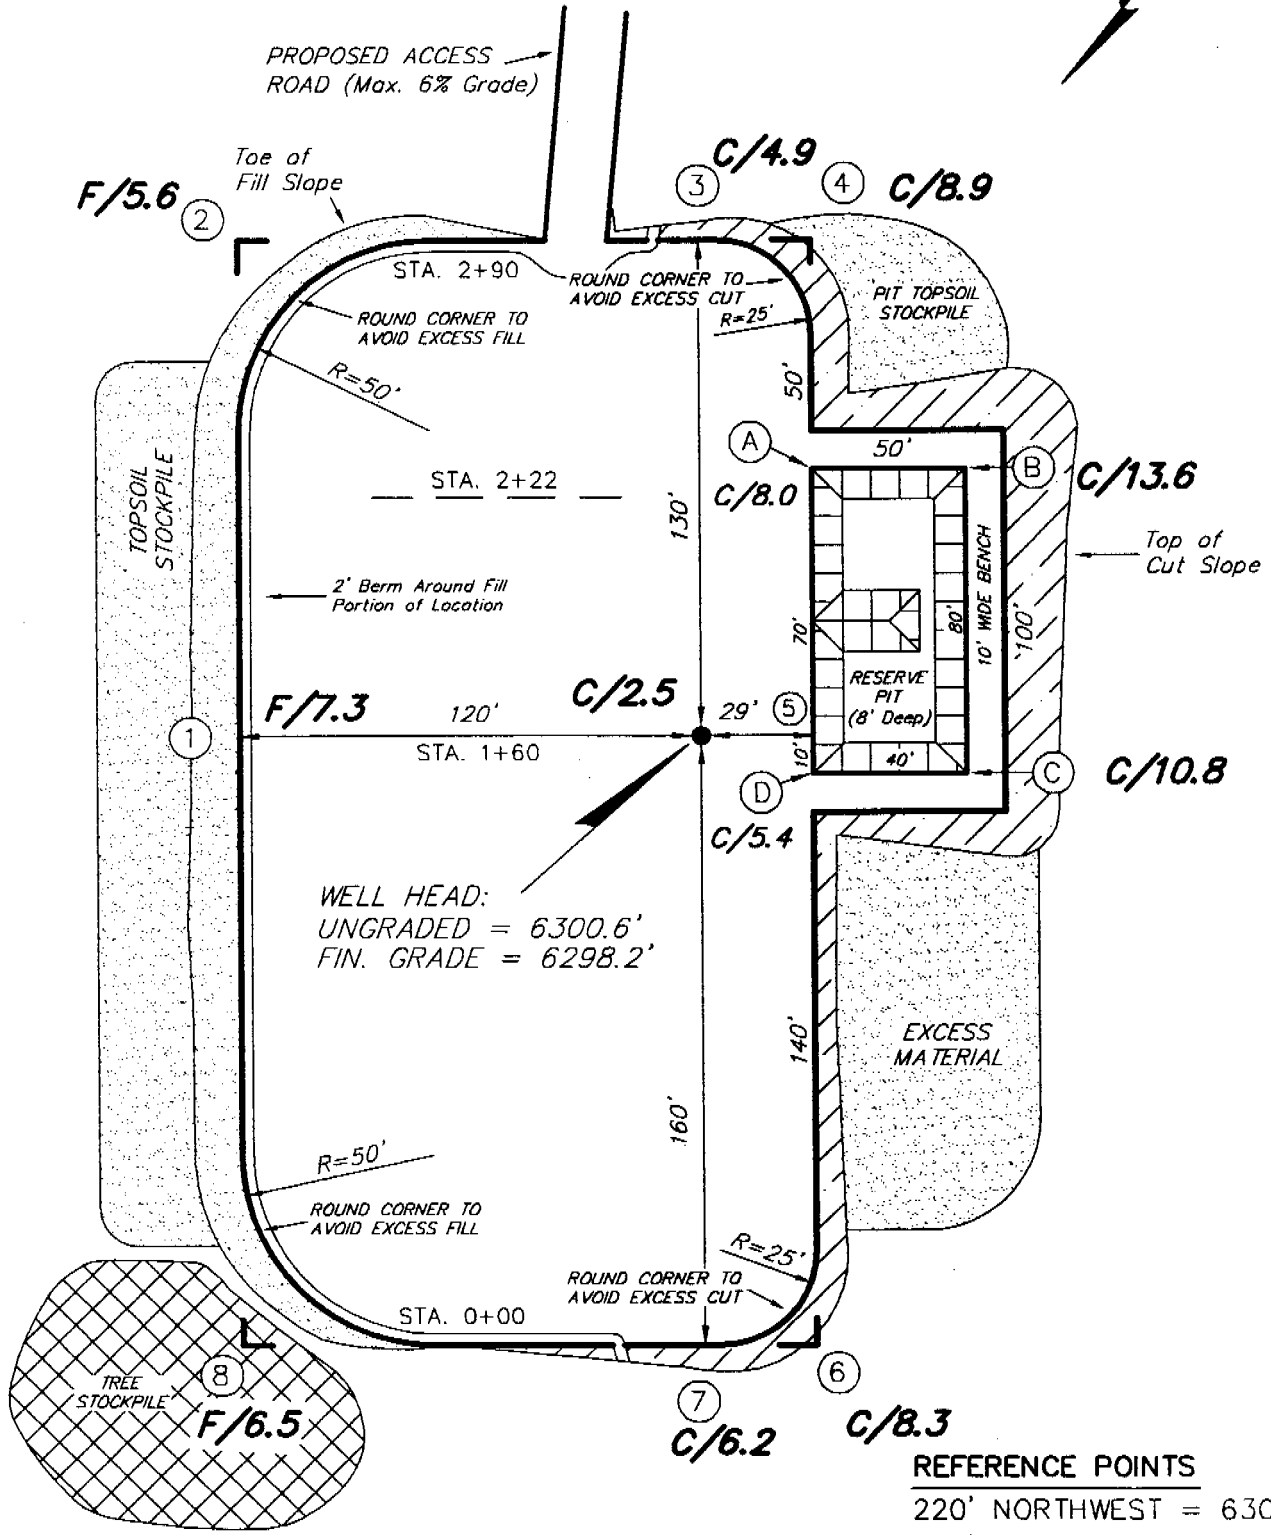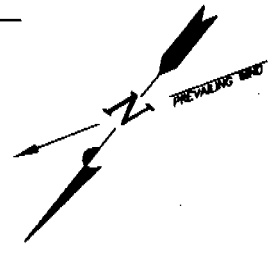

WELL HEAD:
UNGRADED = 6300.6'
FIN. GRADE = 6298.2'

REFERENCE POINTS

220' NORTHWEST = 6309.2'
260' NORTHWEST = 6309.4'
170' NORTHEAST = 6283.6'
220' NORTHEAST = 6277.7'

SURVEYED BY: D.P.

SCALE: 1" = 50'

DRAWN BY: F.T.M.

DATE: 7-8-05





Tri State
Land Surveying, Inc.

(435) 781-2501

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

CROSS SECTIONS ASHLEY UNIT 5-25

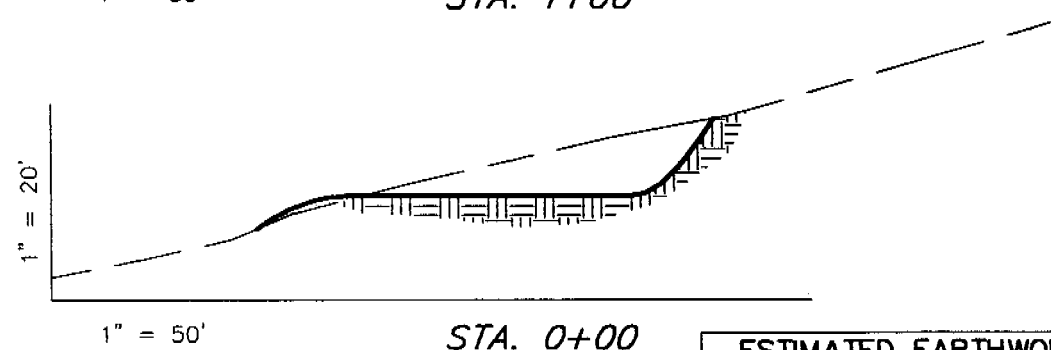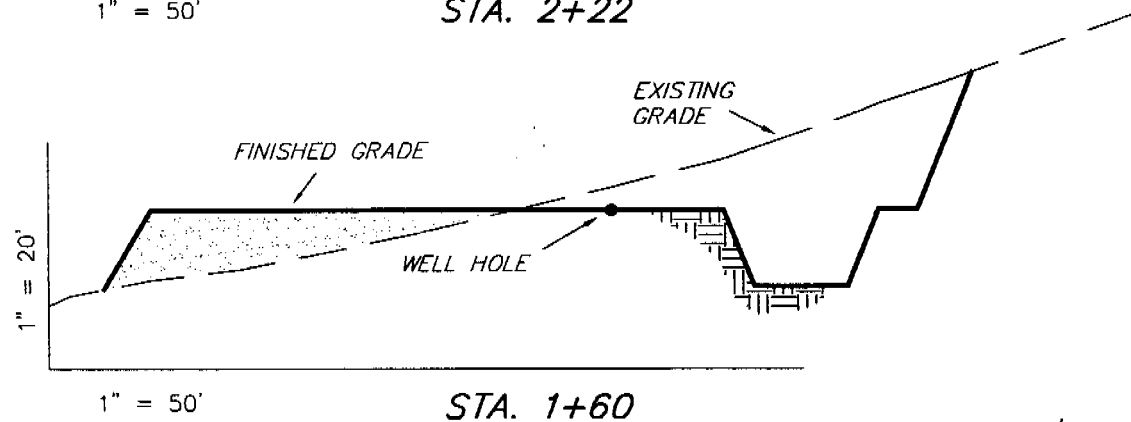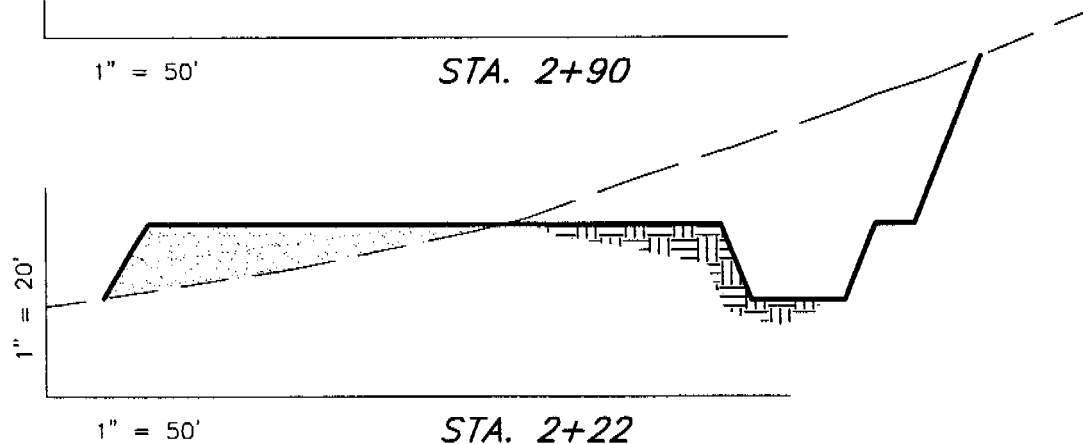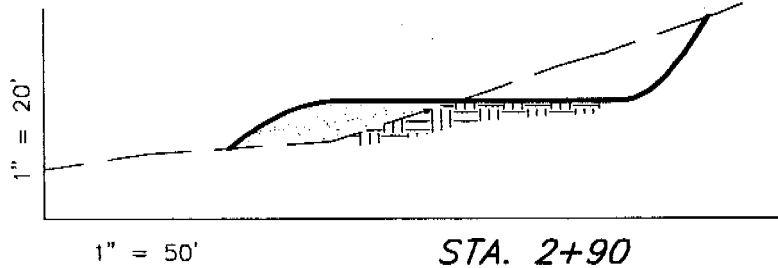

NOTE:
UNLESS OTHERWISE NOTED
ALL CUT/FILL SLOPES ARE
AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	4,320	4,310	Topsoil is not included in Pad Cut	10
PIT	640	0		640
TOTALS	4,960	4,310	1,030	650

SURVEYED BY: D.P.

SCALE: 1" = 50'

DRAWN BY: F.T.M.

DATE: 7-8-05

Tri State
Land Surveying, Inc.


(435) 781-2501

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

TYPICAL RIG LAYOUT

ASHLEY UNIT 5-25

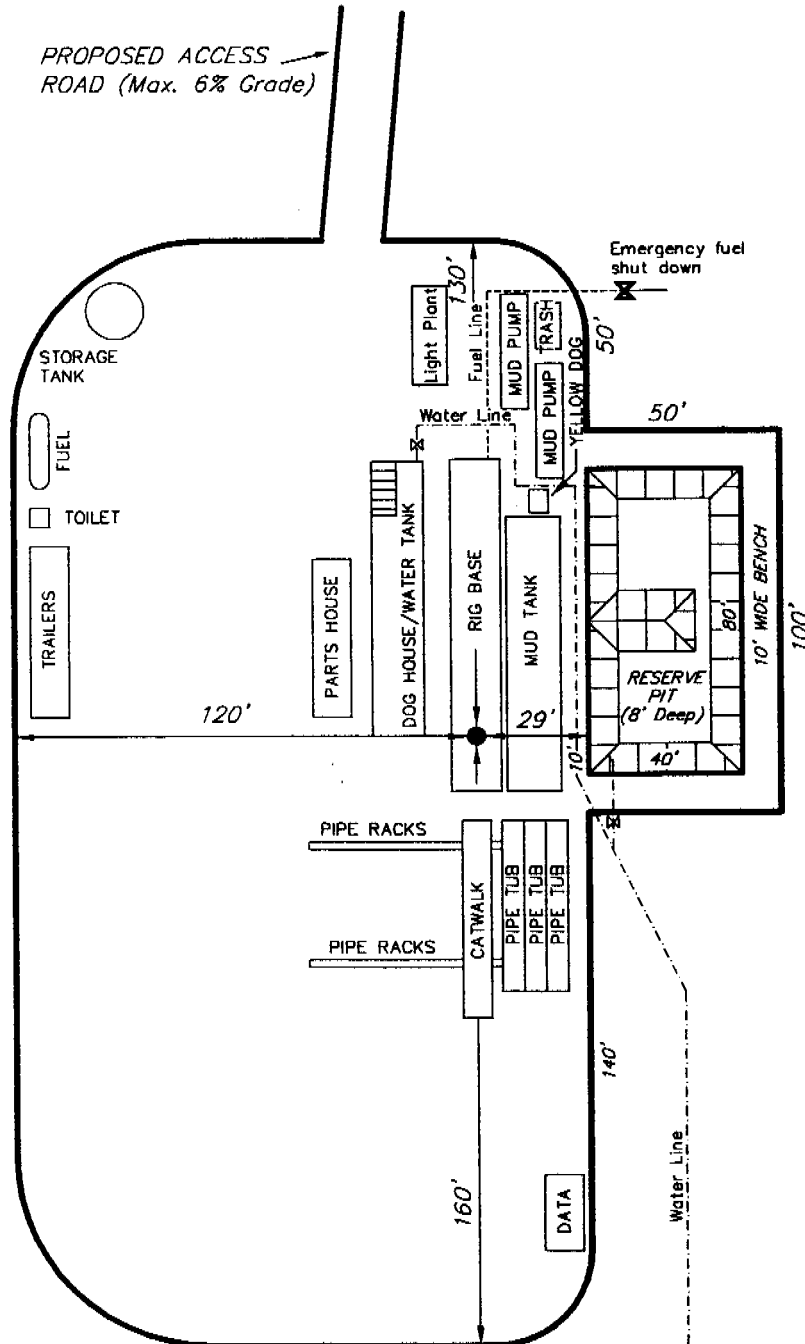

SURVEYED BY: D.P.

SCALE: 1" = 50'


DRAWN BY: F.T.M.

DATE: 7-8-05

Tri State
Land Surveying, Inc.

(435) 781-2501

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

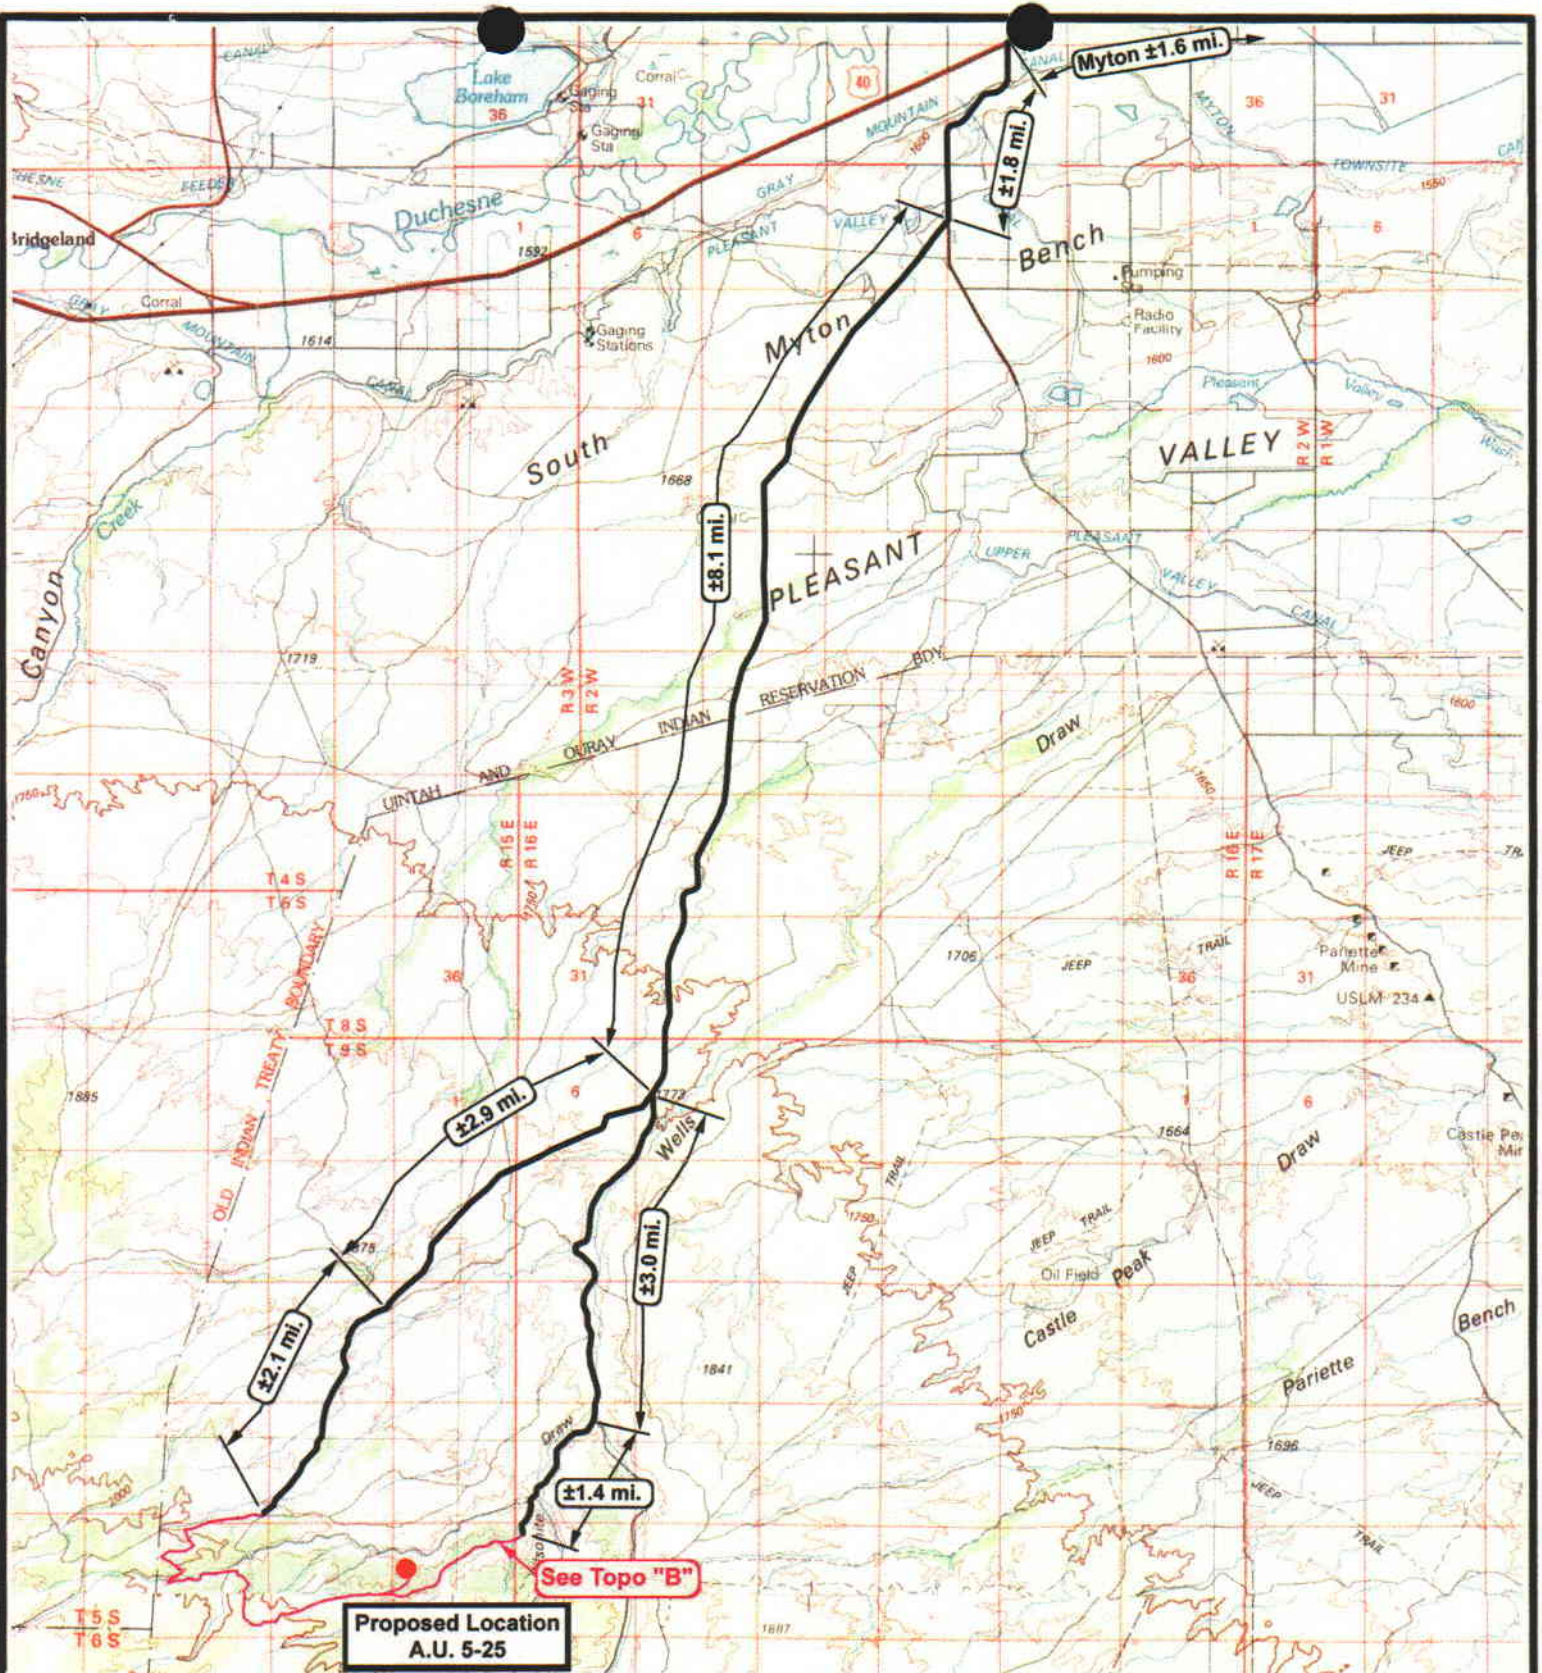

Ashley Unit 5-25-9-15
SEC. 25, T9S, R15E, S.L.B.&M.




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1 = 100,000
DRAWN BY: mw
DATE: 07-19-2005

Legend
Existing Road
Proposed Access

TOPOGRAPHIC MAP

"A"

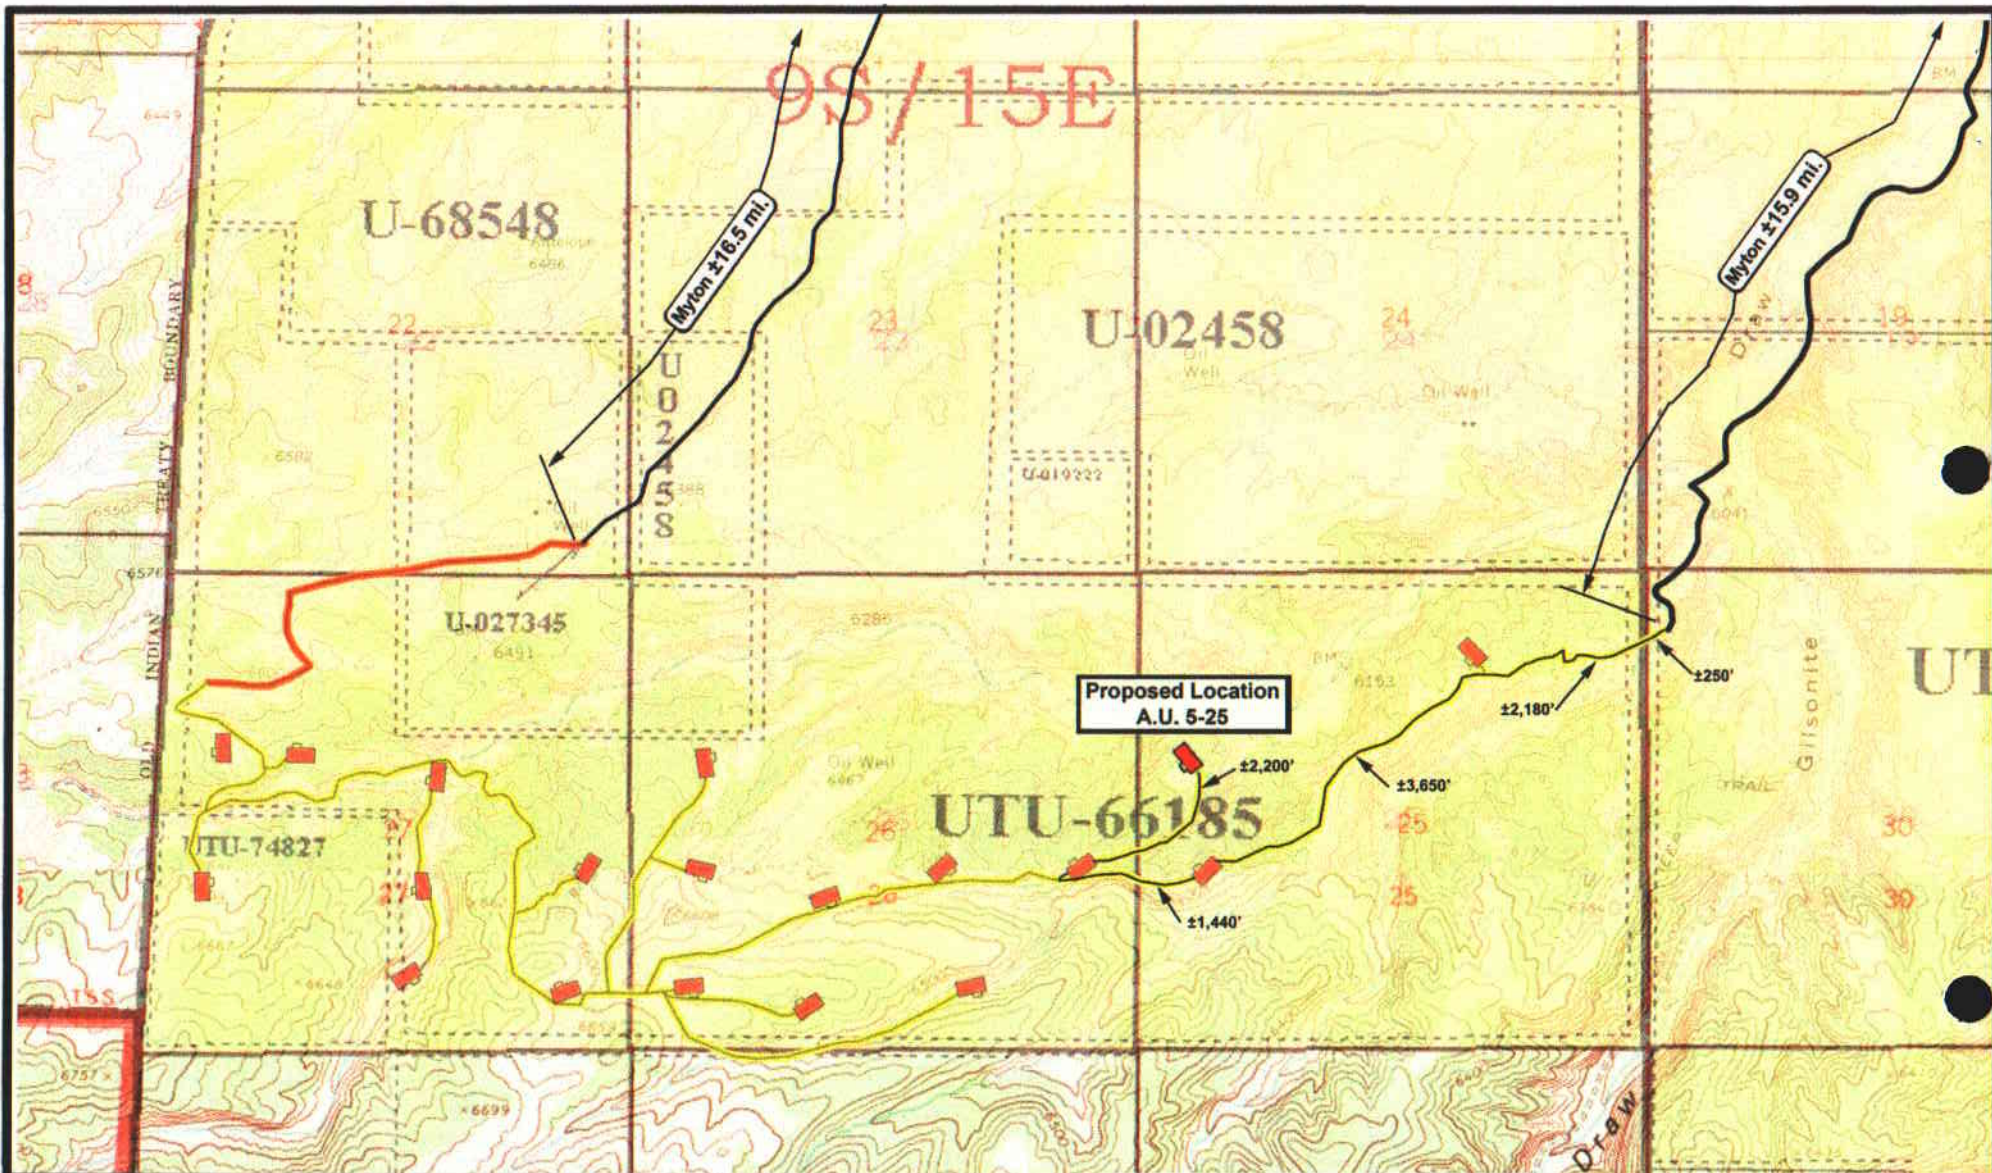

NEWFIELD
Exploration Company

Ashley Unit 5-25-9-15
SEC. 25, T9S, R15E, S.L.B.&M.


Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 07-19-2005

Legend

- Existing Road
- Proposed Access
- Upgraded Access

"B"

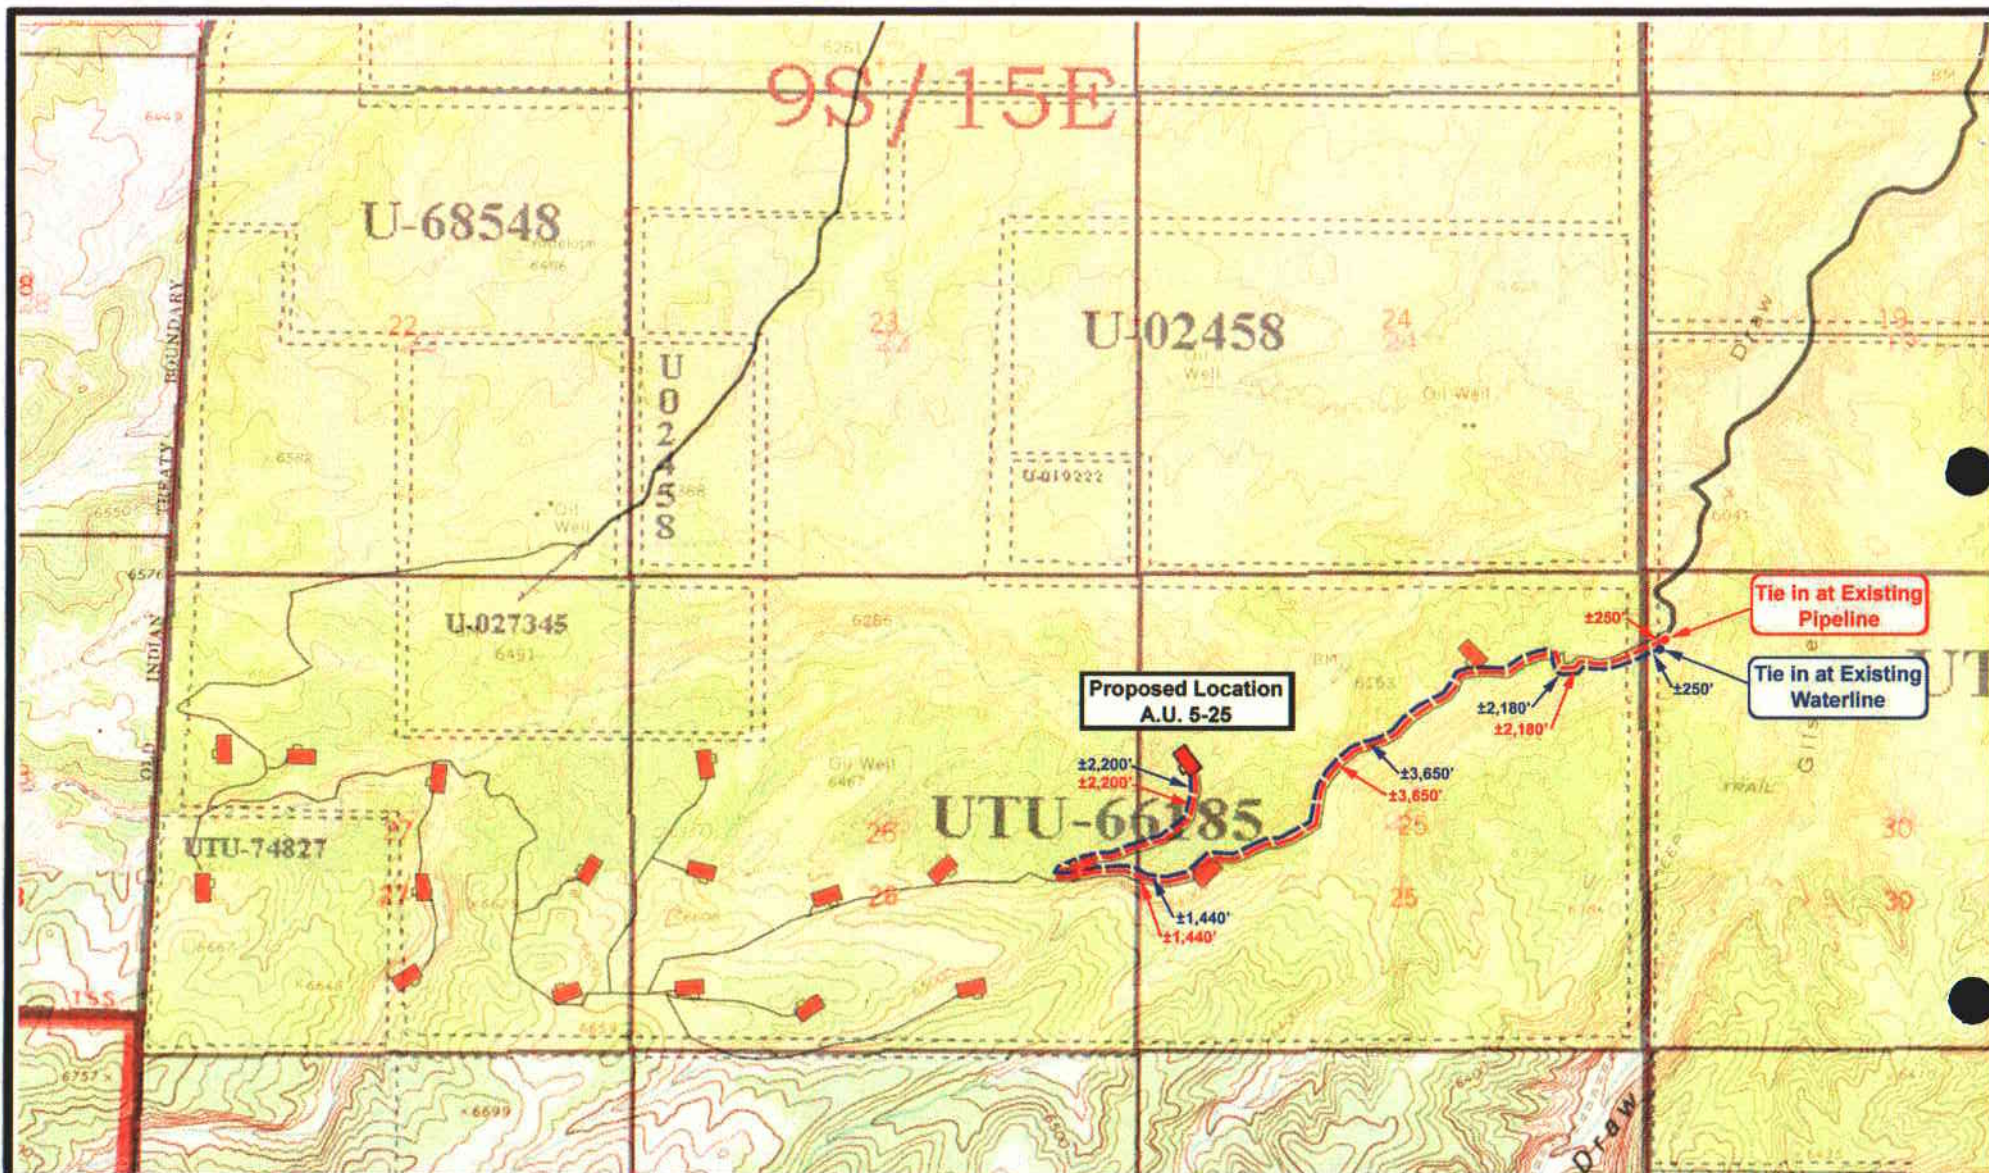

NEWFIELD
Exploration Company

Ashley Unit 5-25-9-15
SEC. 25, T9S, R15E, S.L.B.&M.


Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 07-19-2005



Legend

- Roads
- Proposed Gas Line
- Proposed Water Line

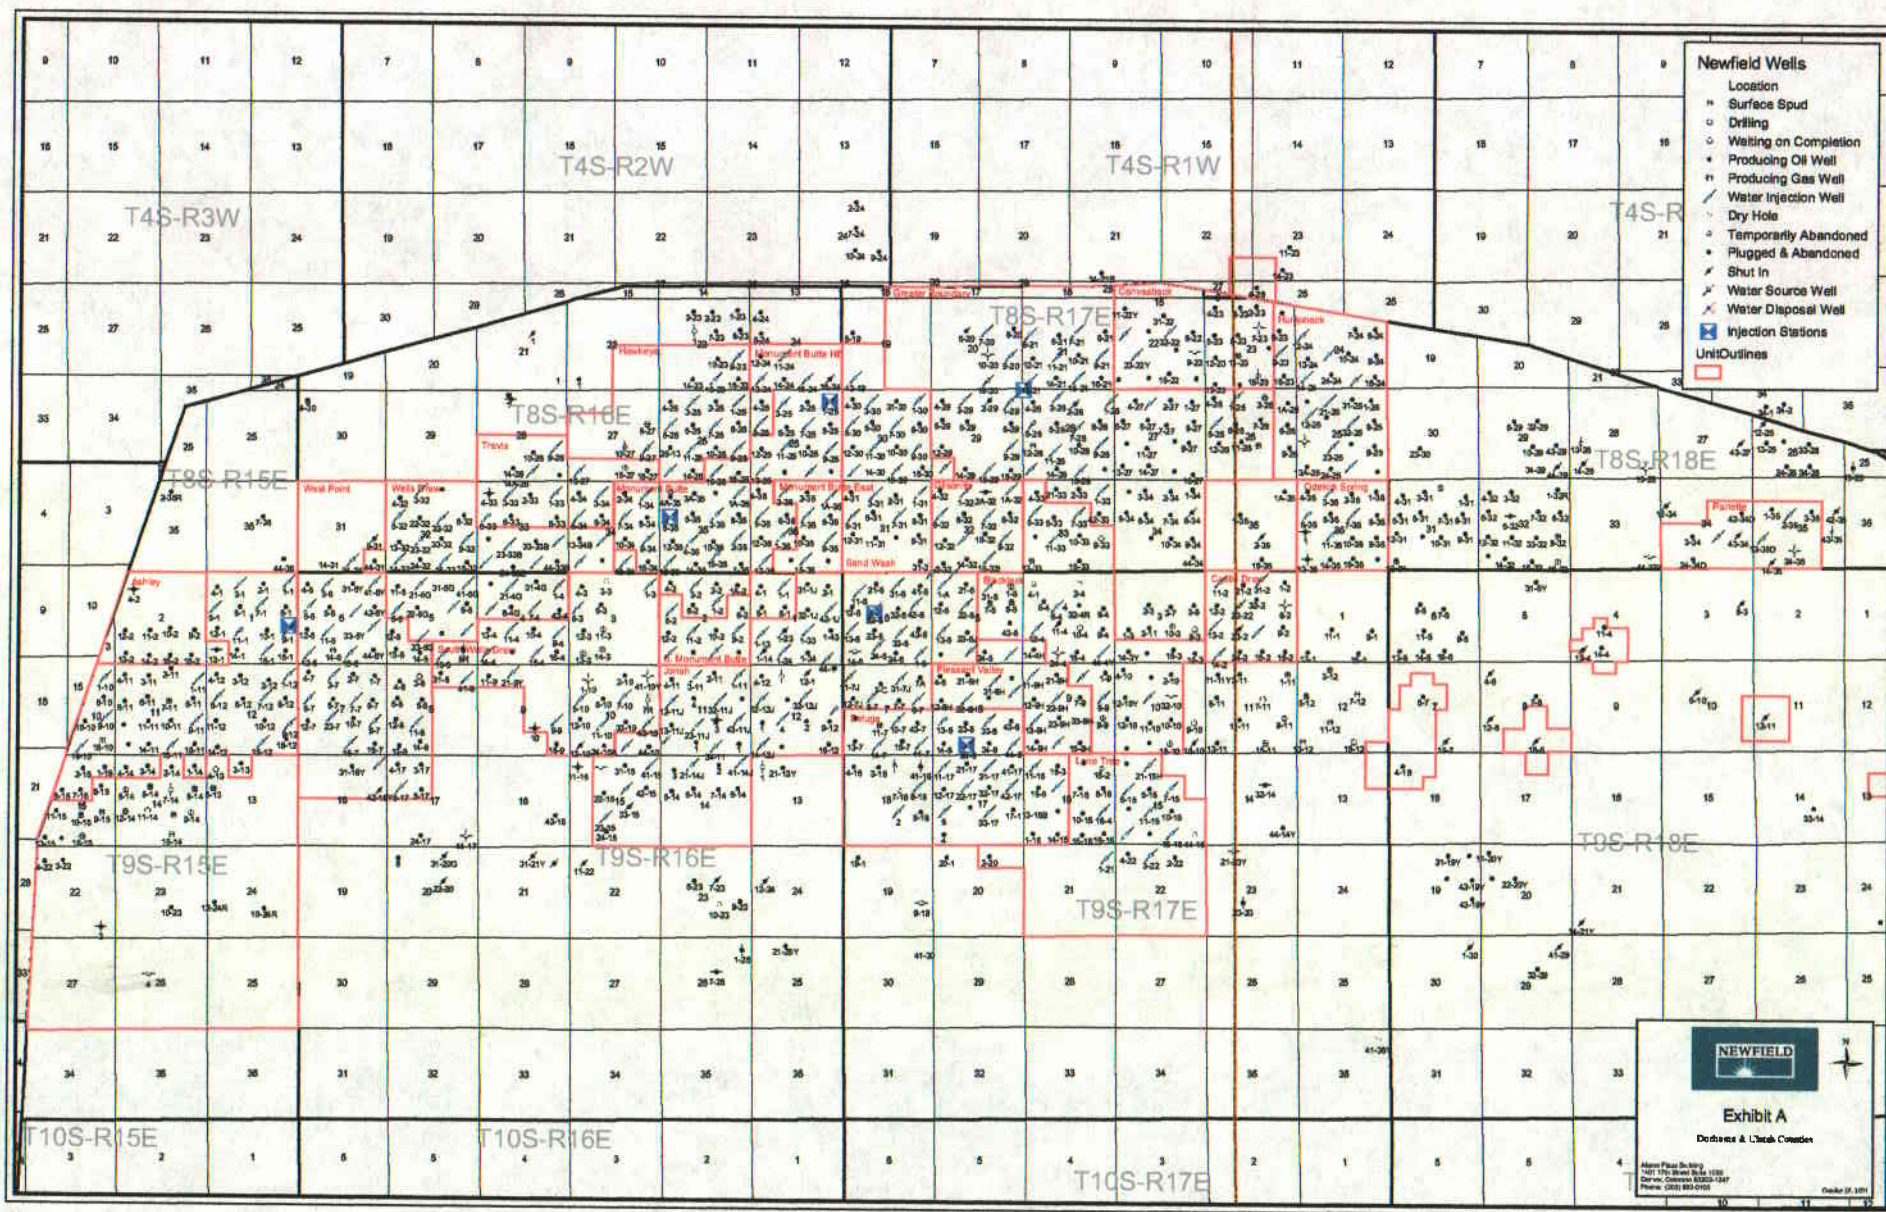"C"

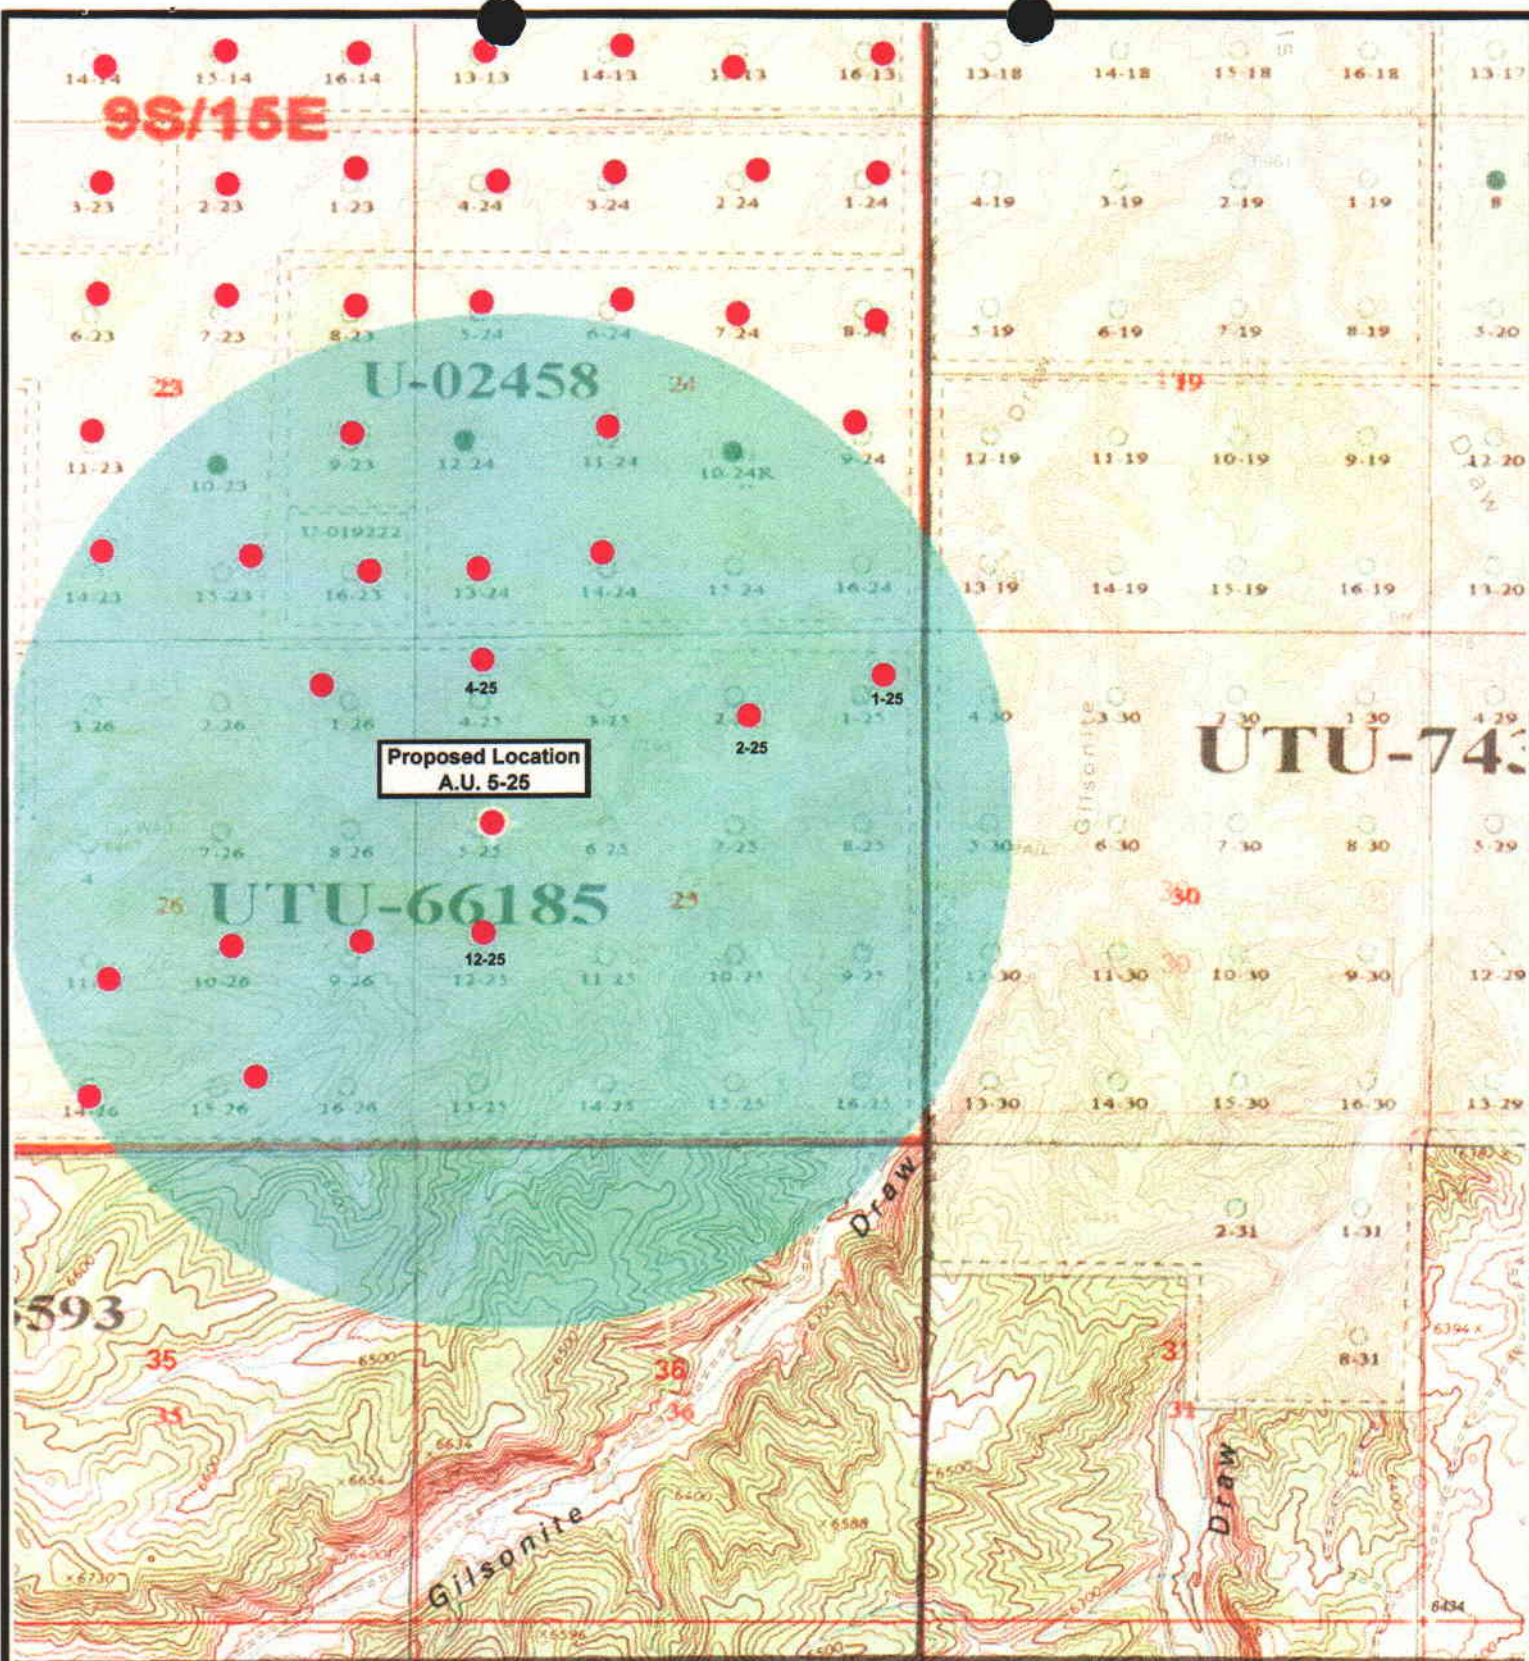



 <p>NEWFIELD Exploration Company</p> <p>Ashley Unit 5-25-9-15 SEC. 25, T9S, R15E, S.L.B.&M.</p>		 <p>Tri-State Land Surveying Inc. (435) 781-2501 180 North Vernal Ave. Vernal, Utah 84078</p> <p>SCALE: 1" = 2,000' DRAWN BY: mw DATE: 07-19-2005</p>	<p>Legend</p> <ul style="list-style-type: none"> ● Proposed Location ○ One-Mile Radius <p>Exhibit "B"</p>
---	---	--	---

2-M SYSTEM

Blowout Prevention Equipment Systems

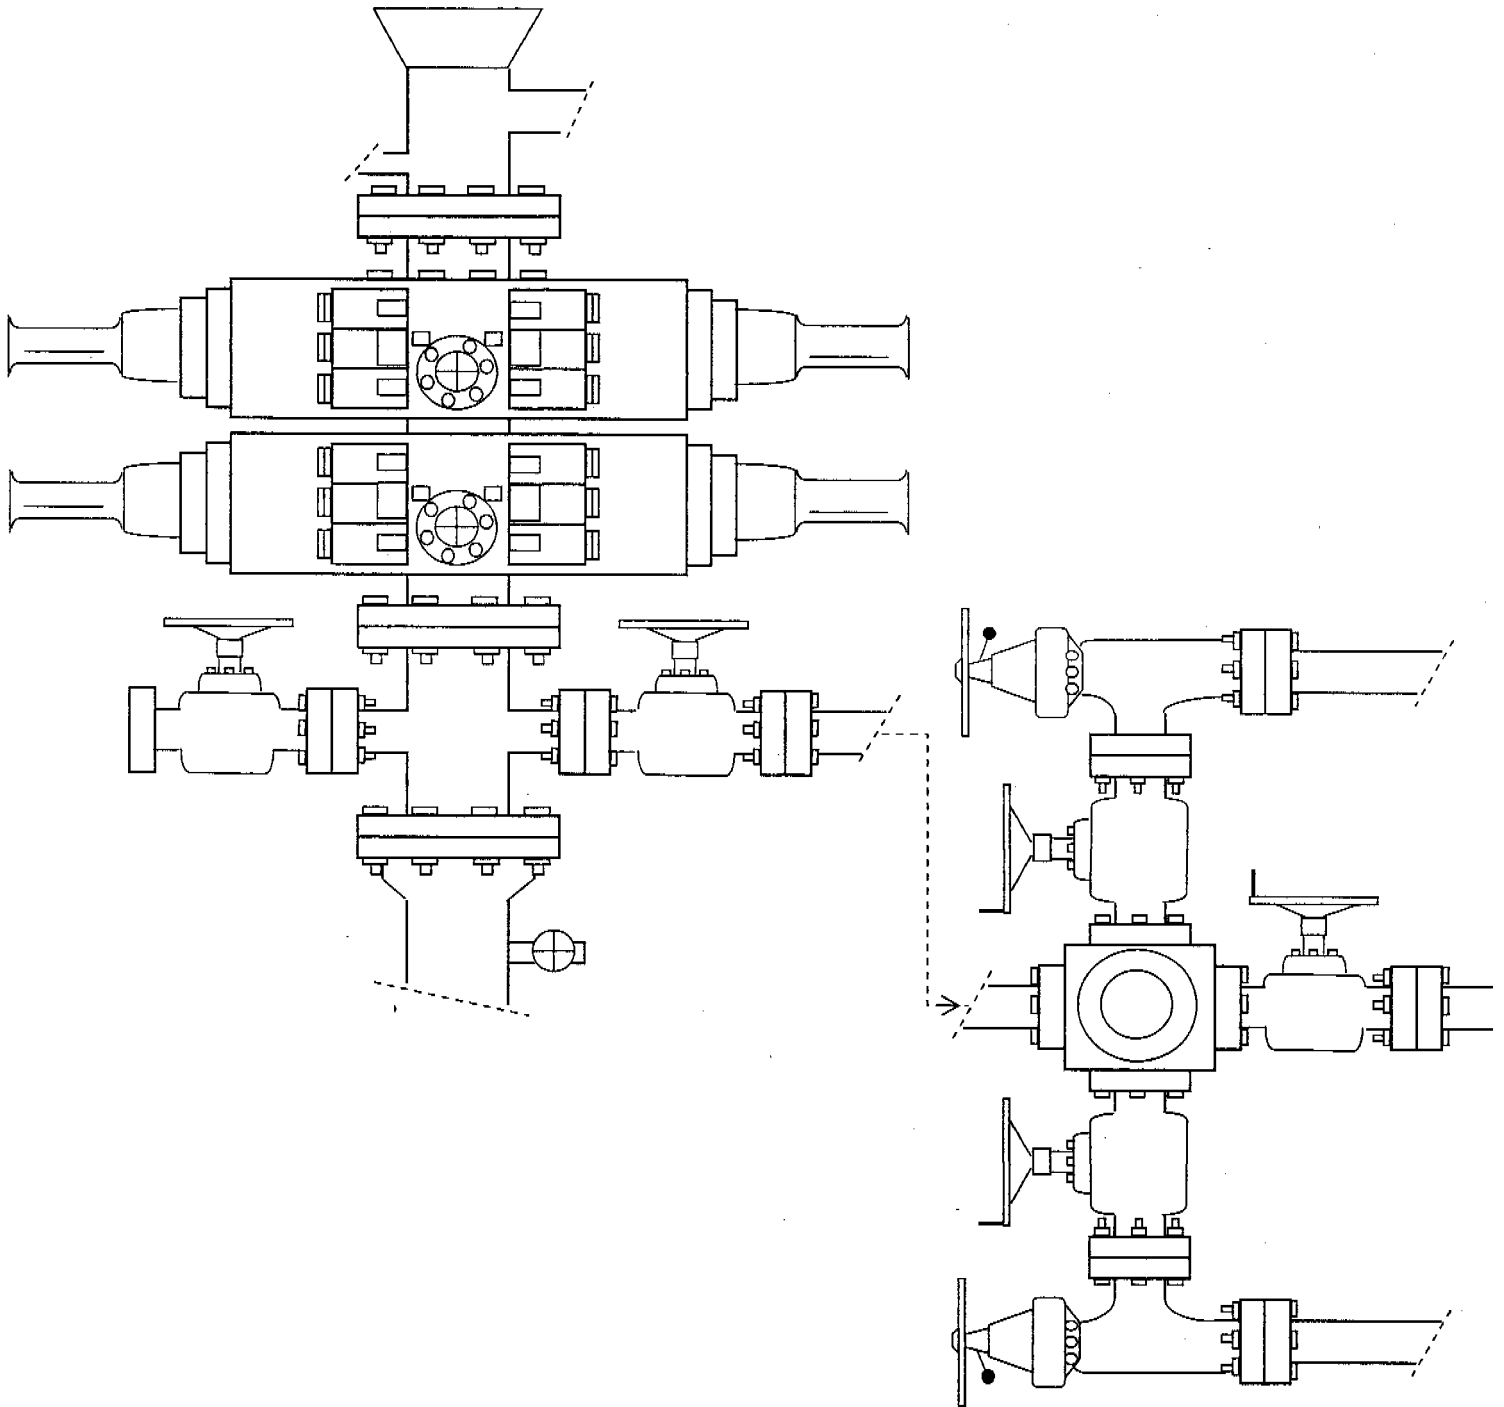


EXHIBIT C

CULTURAL RESOURCE INVENTORY OF
NEWFIELD EXPLORATIONS 1800 ACRE BLOCK PARCELS
IN TOWNSHIP 9 SOUTH, RANGE 15 EAST
SECTIONS 25, 26 AND 27, DUCHESNE COUNTY, UTAH

By:

Kylie Lower-Eskelson
and
Keith Montgomery

Prepared For:

Bureau of Land Management
Vernal Field Office

Prepared Under Contract With:

Newfield Exploration Company
Route 3 Box 3630
Myton, Utah 84052

Prepared By:

Montgomery Archaeological Consultants
P.O. Box 147
Moab, Utah 84532

MOAC Report No. 04-205

June 28, 2005

United States Department of Interior (FLPMA)
Permit No. 04-UT-60122

State of Utah Antiquities Project (Survey)
Permit No. U-04-MQ-1417b

NEWFIELD PRODUCTION COMPANY

**PALEONTOLOGICAL SURVEY OF PROPOSED
PRODUCTION DEVELOPMENT AREAS,
DUCHESNE COUNTY, UTAH**

NE1/4, NW 1/4 Section 34, T 9 S, R 15 E [3-34-9-15]; Entire Section 25,
T 9 S, R 15 E [1 through 16-25-9-15]; Entire Section 26, T 9 S, R 15 E
[1 through 16-26-9-15]

REPORT OF SURVEY

Prepared for:

Newfield Production Company

Prepared by:

Wade E. Miller
Consulting Paleontologist
August 29, 2005

WORKSHEET
APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 09/02/2005

API NO. ASSIGNED: 43-013-32885

WELL NAME: ASHLEY FED 5-25-9-15

OPERATOR: NEWFIELD PRODUCTION (N2695)

CONTACT: MANDIE CROZIER

PHONE NUMBER: 435-646-3721

PROPOSED LOCATION:

SWNW 25 090S 150E

SURFACE: 2091 FNL 0505 FWL

BOTTOM: 2091 FNL 0505 FWL

DUCHESNE

UNDESIGNATED (2)

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-66185

SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: GRRV

COALBED METHANE WELL? NO

INSPECT LOCATN BY: / /

Tech Review	Initials	Date
Engineering		
Geology		
Surface		

LATITUDE: 40.00347

LONGITUDE: -110.1875

RECEIVED AND/OR REVIEWED:


☒ Plat
☒ Bond: Fed[] Ind[] Sta[] Fee[]
(No. UT0056)
☒ Potash (Y/N)
☒ Oil Shale 190-5 (B) or 190-3 or 190-13
☒ Water Permit
(No. MUNICIPAL)
☒ RDCC Review (Y/N)
(Date: _____)
☒ Fee Surf Agreement (Y/N)
☒ Intent to Commingle (Y/N)

LOCATION AND SITING:

_____ R649-2-3.
Unit ASHLEY
_____ R649-3-2. General
Siting: 460 From Qtr/Qtr & 920' Between Wells
_____ R649-3-3. Exception
☒ Drilling Unit
Board Cause No: 242-1
Eff Date: 8-25-1998
Siting: Suspends General Siting
_____ R649-3-11. Directional Drill

COMMENTS: _____

STIPULATIONS: _____

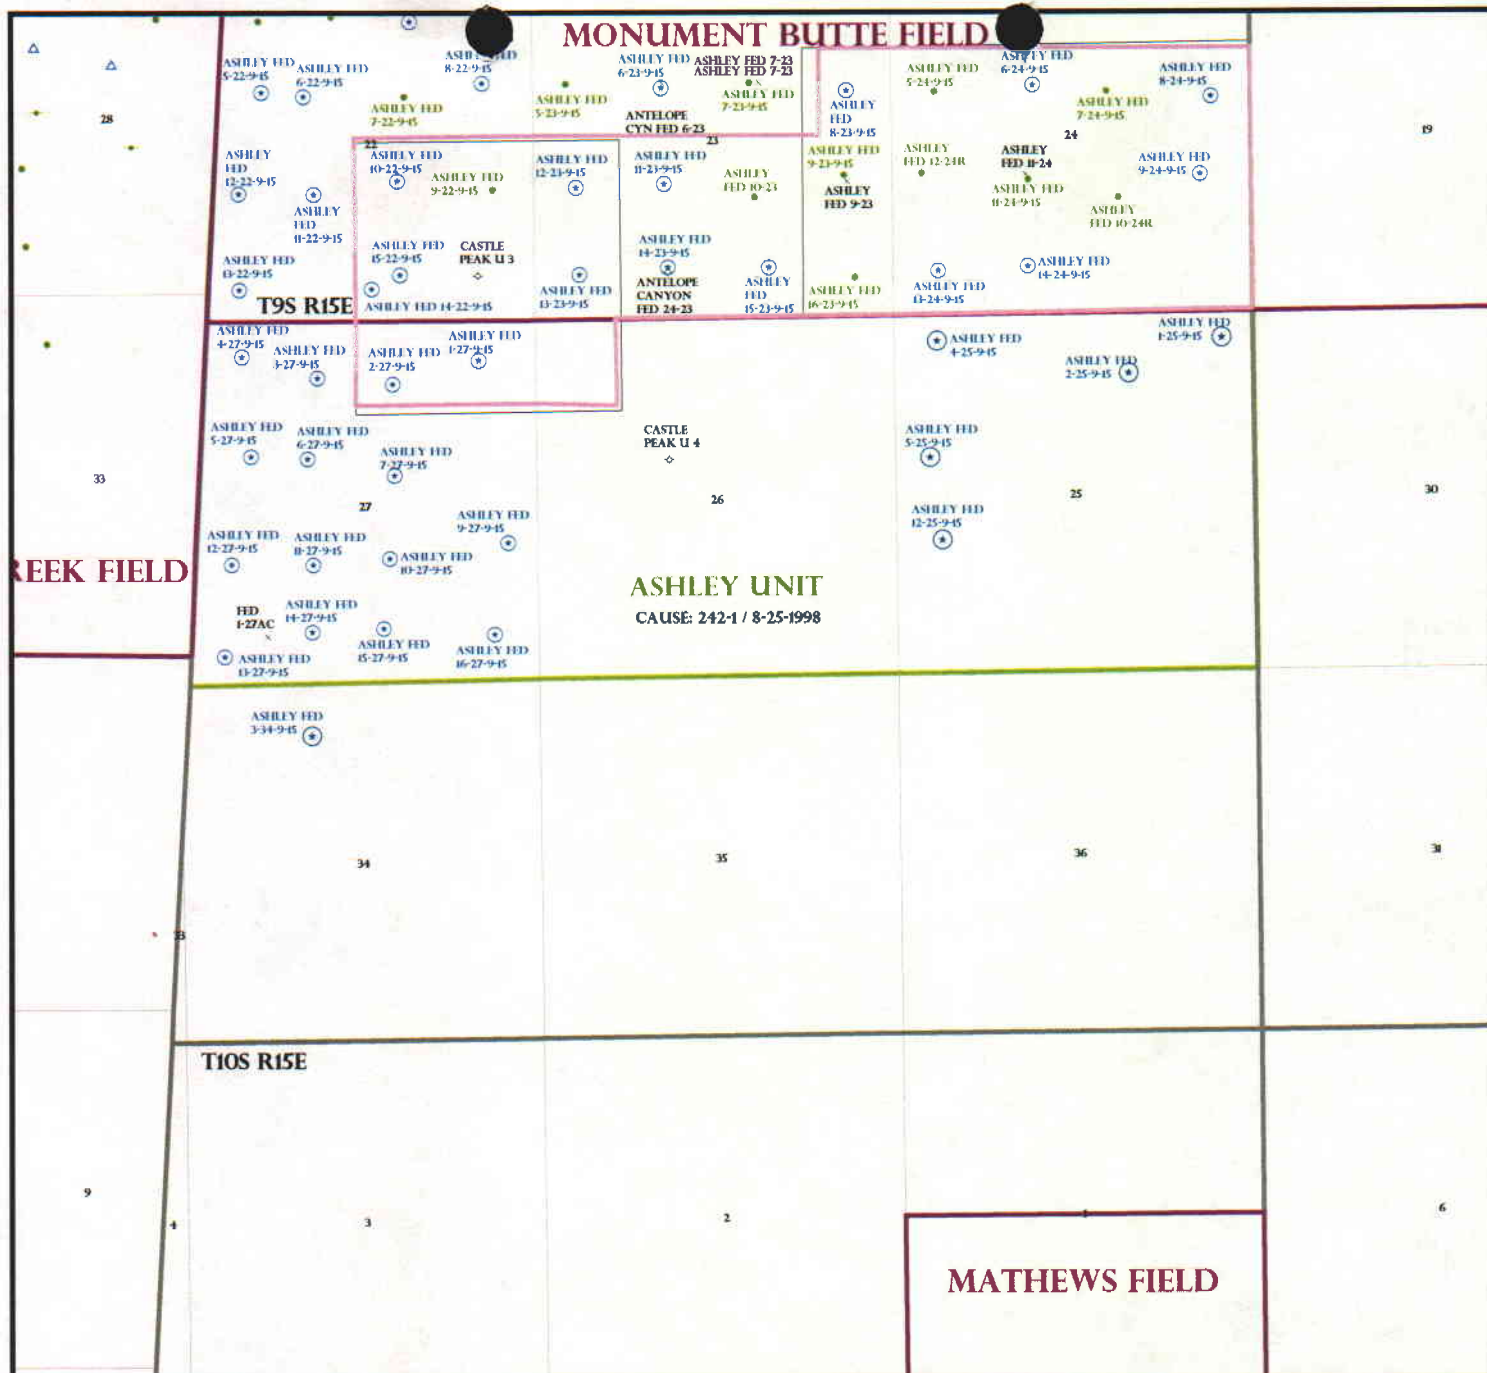

OPERATOR: NEWFIELD PROD CO (N2695)

SEC: 25 T. 9 R. 15E

FIELD: UNDESIGNATED (001)

COUNTY: DUCHESNE

CAUSE: 242-1 / 8-25-1998

Field Status


- ABANDONED
- ACTIVE
- COMBINED
- INACTIVE
- PROPOSED
- STORAGE
- TERMINATED

Unit Status

- EXPLORATORY
- GAS STORAGE
- NF PP OIL
- NF SECONDARY
- PENDING
- PI OIL
- PP GAS
- PP GEOTHERML
- PP OIL
- SECONDARY
- TERMINATED

Wells Status

- ✖ GAS INJECTION
- ✖ GAS STORAGE
- ✖ LOCATION ABANDONED
- ⊙ NEW LOCATION
- ✖ PLUGGED & ABANDONED
- ✖ PRODUCING GAS
- ✖ PRODUCING OIL
- ✖ SHUT-IN GAS
- ✖ SHUT-IN OIL
- ✖ TEMP. ABANDONED
- TEST WELL
- △ WATER INJECTION
- ⊙ WATER SUPPLY
- ⊙ WATER DISPOSAL
- ⊙ DRILLING



Utah Oil Gas and Mining



PREPARED BY: DIANA WHITNEY
DATE: 02-SEPTEMBER-2005

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office
P.O. Box 45155
Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:

3160
(UT-922)

September 6, 2005

Memorandum

To: Assistant District Manager Minerals, Vernal District

From: Michael Coulthard, Petroleum Engineer

Subject: 2005 Plan of Development Ashley Unit, Duchesne County,
Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2005 within the Ashley Unit, Duchesne County, Utah.

API #	WELL NAME	LOCATION
(Proposed PZ Green River)		
43-013-32882	Ashley Fed	1-25-9-15 Sec 25 T09S R15E 0406 FNL 0461 FEL
43-013-32883	Ashley Fed	2-25-9-15 Sec 25 T09S R15E 0903 FNL 1835 FEL
43-013-32884	Ashley Fed	4-25-9-15 Sec 25 T09S R15E 0394 FNL 0624 FWL
43-013-32885	Ashley Fed	5-25-9-15 Sec 25 T09S R15E 2091 FNL 0505 FWL
43-013-32886	Ashley Fed	12-25-9-15 Sec 25 T09S R15E 1985 FSL 0676 FWL

This office has no objection to permitting the wells at this time.

/s/ Michael L. Coulthard

bcc: File – Ashley Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:9-6-05



State of Utah

**Department of
Natural Resources**

MICHAEL R. STYLER
Executive Director

**Division of
Oil, Gas & Mining**

JOHN R. BAZA
Division Director

JON M. HUNTSMAN, JR.
Governor

GARY R. HERBERT
Lieutenant Governor

September 6, 2005

Newfield Production Company
Rt. #3, Box 3630
Myton, UT 84052

Re: Ashley Federal 5-25-9-15 Well, 2091' FNL, 505' FWL, SW NW, Sec. 25,
T. 9 South, R. 15 East, Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-32885.

Sincerely,

Gil Hunt
Associate Director

pab
Enclosures

cc: Duchesne County Assessor
Bureau of Land Management, Vernal District Office

Operator: Newfield Production Company
Well Name & Number Ashley Federal 5-25-9-15
API Number: 43-013-32885
Lease: UTU-66185

Location: SW NW Sec. 25 T. 9 South R. 15 East

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

2. Notification Requirements

Notify the Division within 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dan Jarvis at (801) 538-5338

3. Reporting Requirements

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.

RECEIVED

AUG 04 2006

RECEIVED

SEP 02 2005

DIV. OF OIL, GAS & MINING

BLM VERNAL, UTAH

Form 3160-3
(September 2001)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0136
Expires January 31, 20045. Lease Serial No.
UTU-661856. If Indian, Allottee or Tribe Name
N/A7. If Unit or CA Agreement, Name and No.
Ashley8. Lease Name and Well No.
Ashley Federal 5-25-9-159. API Well No.
43-013-3288510. Field and Pool, or Exploratory
Monument Butte11. Sec., T., R., M., or Blk. and Survey or Area
SW/NW Sec. 25, T9S R15E12. County or Parish
Duchesne13. State
UT1a. Type of Work: ☒ DRILL ☐ REENTER1b. Type of Well: ☒ Oil Well ☐ Gas Well ☐ Other ☒ Single Zone ☐ Multiple Zone2. Name of Operator
Newfield Production Company3a. Address
Route #3 Box 3630, Myton UT 840523b. Phone No. (include area code)
(435) 646-37214. Location of Well (Report location clearly and in accordance with any State requirements. *)
At surface SW/NW 2091' FNL 505' FWL
At proposed prod. zone14. Distance in miles and direction from nearest town or post office*
Approximately 17.7 miles southwest of Myton, Utah15. Distance from proposed*
location to nearest
property or lease line, ft.
(Also to nearest drig. unit line, if any) Approx. 2091' f/sea, 3189' f/unit16. No. of Acres in lease
2,286.4317. Spacing Unit dedicated to this well
40 Acres18. Distance from proposed location*
to nearest well, drilling, completed,
applied for, on this lease, ft. Approx. 1375'19. Proposed Depth
5830'20. BLM/BIA Bond No. on file
UT005621. Elevations (Show whether DF, KDB, RT, GL, etc.)
6301' GL22. Approximate date work will start*
1st Quarter 200623. Estimated duration
Approximately seven (7) days from spud to rig release.

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).

4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature
Mandie Crozier
Title
Regulatory SpecialistName (Printed/Typed)
Mandie CrozierDate
8/31/05Approved by (Signature)
Jerry Kervza
Title
Assistant Field Manager
Mineral ResourcesName (Printed/Typed)
JERRY KERVZA
Office
VERNAL FIELD OFFICEDate
7-28-2006

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

* (Instructions on reverse)

NOTICE OF APPROVAL

CONDITIONS OF APPROVAL ATTACHED

Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East VERNAL, UT 84078 (435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company:	Newfield Production Company	Location:	SWNW, Sec. 25, T9S, R15E
Well No:	Ashley Federal 5-25-9-15	Lease No:	UTU-66185
API No:	43-013-32885	Agreement:	Ashley Unit

Petroleum Engineer:	Matt Baker	Office: 435-781-4490	Cell: 435-828-4470
Petroleum Engineer:	Michael Lee	Office: 435-781-4432	Cell: 435-828-7875
Supervisory Petroleum Technician:	Jamie Sparger	Office: 435-781-4502	Cell: 435-828-3913
Environmental Scientist:	Paul Buhler	Office: 435-781-4475	Cell: 435-828-4029
Environmental Scientist:	Karl Wright	Office: 435-781-4484	
Natural Resource Specialist:	Chris Carusona	Office: 435-781-4441	
Natural Resource Specialist:	Holly Villa	Office: 435-781-4404	
Natural Resource Specialist:	Melissa Hawk	Office: 435-781-4476	
Natural Resource Specialist:	Scott Ackerman	Office: 435-781-4437	
Natural Resource Specialist:	Nathaniel West	Office: 435-781-4447	
After hours contact number: (435) 781-4513		FAX: (435) 781-4410	

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a one-year period. An additional year extension may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

- | | |
|---|--|
| Location Construction
(Notify Chris Carusona) | - Forty-Eight (48) hours prior to construction of location and access roads. |
| Location Completion
(Notify Chris Carusona) | - Prior to moving on the drilling rig. |
| Spud Notice
(Notify Petroleum Engineer) | - Twenty-Four (24) hours prior to spudding the well. |
| Casing String & Cementing
(Notify Jamie Sparger SPT) | - Twenty-Four (24) hours prior to running casing and cementing all casing strings. |
| BOP & Related Equipment Tests
(Notify Jamie Sparger SPT) | - Twenty-Four (24) hours prior to initiating pressure tests. |
| First Production Notice
(Notify Petroleum Engineer) | - Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days. |

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

DRILLING AND CONSTRUCTION

All applicable local, state, and/or federal laws, regulations, and/or statutes must be complied with.

In accordance with the Migratory Bird Treaty Act if a nest is found the operator shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the authorized officer.

Prior to construction the operator must consult with the U.S. Army Corps of Engineers regarding compliance with Section 404 of the Clean Water Act.

Construction related traffic shall be restricted to approved routes. Cross-country vehicle travel shall not be allowed.

If additional erosion occurs during the life of this project, more culverts, low water crossings, berms, wing ditches or etc. may be needed to control the erosion. The operator shall submit a proposal to control erosion to the BLM.

The reserve pit shall be double lined with felt and a 12 ml or greater liner.

No vehicle travel, construction or routine maintenance activities shall be performed during periods when the soil is too wet to adequately support vehicles and/or construction equipment. If such equipment creates ruts in excess of four inches deep, the soil shall be deemed too wet to adequately support construction equipment.

The liner is to be cut at the level of the cuttings or treated to prevent the reemergence of the pit liner and pit material to the surface or its interference with long-term successful re-vegetation. Any excess liner material removed from the pit is to be disposed of at an authorized disposal site.

When the reserve pit contains fluids or toxic substances, the operator must ensure that animals do not ingest or become entrapped in pit fluids.

Drill cuttings and mud shall remain in the reserve pit until **DRY**. The reserve pit must be free of oil and other liquid and solid wastes, allowed to dry, be pumped dry, or solidified in-situ prior to filling. The reserve pit shall not be "squeezed," (filled with soil while still containing fluids) or "cut" (puncturing the pit liner while still containing fluids to allow pit fluids to drain from the pit). Prevent fill and stock piles from entering drainages.

CULTURAL AND PALEONTOLOGICAL RESOURCES STIPULATION

Any cultural and/or paleontological resource (historic or prehistoric site or object or fossil) discovered by the holder, or any person working on his behalf, on public or Federal land shall be immediately reported to the authorized officer. Holder shall suspend all operations in the immediate area of such discovery until written authorization to proceed is issued by the authorized officer. An evaluation of the discovery shall be made by the authorized officer to determine appropriate actions to prevent the loss of significant cultural or scientific values. The holder shall be responsible for the cost of evaluation and a decision as to proper mitigation

measures shall be made by the authorized officer after consulting with the holder.
The access road shall be crowned and ditched. Flat-bladed roads are **NOT** allowed.

Notify the Authorized Officer 48 hours prior to surface disturbing activities.

All well facilities not regulated by OSHA shall be painted Olive Black.

Following well plugging and abandonment, the location, access roads, pipelines, and other facilities shall be reclaimed. All disturbed surfaces shall be reshaped to approximate the original contour; the top soil respread over the surface; and, the surface revegetated. The surface of approved staging areas where construction activities did not occur may require disking or ripping and reseeding.

Noxious weeds and any undesirable plants, as determined by the BLM, shall be controlled by the operator. The operator shall submit a pesticide use proposal to control weeds if they develop on the location or access road.

Trees must be removed from the location must be piled separately off location and saved for final reclamation purposes.

INTERIM RECLAMATION

Where possible, strip six inches of topsoil from the location as shown on the cut sheet. After the well is completed, the topsoil shall be spread and re-contoured on the location and immediately seeded with the seed mix below. Topsoil shall not be piled deeper than 2 feet.

Interim Reclamation Seed Mix for location:

Crested wheat grass <i>Agropyron cristatum</i>	4 lbs/acre
Per Live Seed Total	4 lbs/acre

Certified weed free seed and straw shall be used for final and interim reclamation. The operator shall submit a receipt with certification for the seed and any straw used on location.

The topsoil from the reserve pit shall be stripped and piled separately near the reserve pit. When the reserve pit is closed it shall be re-contoured, then the area shall be seeded in the same manner as the topsoil.

There shall be no primary or secondary noxious weeds in the seed mixture.

The above listed seed mix shall be used to seed all unused portions of the pad including the topsoil and stock piles, and the reserve pits. Re-seeding may be required if the first seeding is not successful.

The seed shall be drilled or disked into the ground or hand broadcast onto the ground. Planting depth shall not exceed one-half inch using a seed drill. If the seed is hand broadcast then the seed mixture shall be doubled and the area raked or chained to cover the seed. Seeding shall be conducted in fall.

COMPLETION AND PRODUCTION

All Blow back fluids from completion operations shall be contained in such a manner that no oil reaches the reserve pit.

During all road building, pad construction, drilling, well completion, producing and abandonment activities, all gasoline, diesel powered equipment used must be equipped with approved spark arresters or mufflers.

Production facilities (including dikes) shall be placed on cut and a minimum of 20' from the toe of the backcut.

Pesticides may not be used to control undesirable woody and herbaceous vegetation, aquatic plants, insects, rodents, trash fish, etc., **without the prior written approval** of the BLM. A request for approval of planned uses of pesticides shall be submitted 4 months prior to the proposed starting date.

No production pits shall be allowed on the location.

Load outs shall be inside the dike. A drip barrel shall be installed under the end of the loadout line.

All production facilities, i.e. pump, pump house, storage tanks, oil-water separator, galvanized dikes, propane tanks, etc. shall be painted with a lusterless color (Olive Black). All facilities shall be painted within twelve (12) months of installation.

The well location shall be maintained in a clean environmentally friendly manner, using good house keeping practices.

Equipment not being used for production shall not be stored on the well location.

All oil and chemical barrels shall be labeled and have a spill containment device to protect soils from possible contamination.

ABANDONED WELL – FINAL RECLAMATION

A sundry notice shall be submitted to the BLM prior to abandonment, a final reclamation seed mix shall be designated at the time the sundry is approved.

The cut and fill slopes shall be recontoured to original contours. The entire disturbed area shall then be back-filled with topsoil, landscaped, seeded and fenced to exclude livestock. The fence shall remain in place. It shall be removed prior to approval of final abandonment.

The seed shall be drilled or hand broadcast and harrowed into the ground during September of the year following earthwork for initial or final reclamation. Planting depth shall not exceed one-half inch using a seed drill. Weed seed free mulch shall also be applied to the planting area sufficiently to uniformly cover 80% of the seeded area. Hydroseeding and mulching can also be used, but seeding rates will need to be doubled.

When seeding *Artemisia spp* or shrubs, broadcast seed and chain.

Final reclamation shall be a stage process:

If invasive or undesirable species are present in the area the location to be reclaimed will be sprayed with a pesticide in fall preferably October. (pesticide determined by the Vernal Field Office).

30 days after treatment drill seed the location with 4 lbs/acre Crested wheatgrass.

Once the desired pioneer species has established (2 yrs +) the seeded area shall be sprayed in a mosaic pattern with the above determined pesticide.

Reseed within 30 days with an approved native final reclamation seed mix.

Final reclamation will be considered complete once desired plants are > 5 plants per square meter and invasive or un-desirable species are < 100 plants per square meter.

LEASE STIPULATIONS:

UTU-66185

No occupancy or other surface disturbance in Sec. 25; NE, NENW, S2NW, S2 Sec. 26... T. 9 S., R. 15 E., SLM, Utah, will be allowed on slopes in excess of 40 percent, without written permission from the authorized office of the Bureau of Land Management.

In order to minimize watershed damage during the period from November 1 to April 30, exploration, drilling, and other development activity in Sec. 25; NE, NENW, S2NW, S2 Sec. 26; T. 9 S., R. 15 E., SLM, Utah, will be allowed only during dry soil periods, over a snow cover or frozen ground.

In order to protect big game seasonal wildlife habitat, exploration, drilling, and other development activity will be allowed only during the period from April 30 to November 1.

No drilling or construction from February 1 through July 15 to protect nesting golden eagles. Crucial Deer and Elk Winter Range - No surface use December 1 through April 30. Install culverts as needed along access road.

DOWNHOLE CONDITIONS OF APPROVAL

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

SITE SPECIFIC DOWNHOLE CONDITIONS OF APPROVAL

- None

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well. Any changes in operation must have prior approval from the BLM, Vernal Field Office Petroleum Engineers.
- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- **Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.**
- Blowout prevention equipment (BOPE) will remain in use until the well is completed or abandoned. Closing unit controls must remain unobstructed and readily accessible at all times. Choke manifolds must be located outside of the rig substructure.
- All BOPE components will be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests must be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test must be reported in the driller's log.
- BOP drills must be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- All shows of fresh water and minerals will be reported and protected. A sample will be taken of any water flows and a water analysis furnished the BLM, Vernal Field Office. All oil and gas shows will be adequately tested for commercial possibilities, reported, and protected.
- No location will be constructed or moved, no well will be plugged, and no drilling or workover equipment will be removed from a well to be placed in a suspended status without prior approval of the BLM, Vernal Field Office. If operations are to be suspended

for more than 30 days, prior approval of the BLM, Vernal Field Office must be obtained and notification given before resumption of operations.

- Chronologic drilling progress reports must be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- Any change in the program must be approved by the BLM, Vernal Field Office. "Sundry Notices and Reports on Wells" (Form BLM 3160-5) must be filed for all changes of plans and other operations in accordance with 43 CFR 3162.3-2.
- Emergency approval may be obtained orally, but such approval does not waive the written report requirement. Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, will require the filing of a suitable plan pursuant to Onshore Oil & Gas Order No. 1 of 43 CFR 3164.1 and prior approval by the BLM, Vernal Field Office.
- In accordance with 43 CFR 3162.4-3, this well must be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) will be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, will be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) will be submitted only when requested by the BLM, Vernal Field Office.
- **Please submit an electronic copy of all logs run on this well in LAS format to UT_VN_Wellogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM. The cement bond log must be submitted in raster format (TIF, PDF other).**
- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease will have prior written approval from the BLM, Vernal Field Office.
- All measurement points shall be identified as point of sales or allocation for royalty determination prior to the installation of facilities.
- Oil and gas meters will be calibrated in place prior to any deliveries. The Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports will be

submitted to the BLM, Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement.

- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM, Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- This APD is approved subject to the requirement that, shall the well be successfully completed for production, the BLM, Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and / or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas will be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from Field Office Petroleum Engineers.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events as defined in NTL3A, will be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.

- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires: March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry a different reservoir.
Use "APPLICATION FOR PERMIT -" for such proposals

5. Lease Designation and Serial No.

UTU-66185

6. If Indian, Allottee or Tribe Name

NA

7. If Unit or CA, Agreement Designation

ASHLEY (GR RVR)

8. Well Name and No.

ASHLEY FEDERAL 5-25-9-15

9. API Well No.

43-013-32885

10. Field and Pool, or Exploratory Area

MONUMENT BUTTE

11. County or Parish, State

DUCHESNE COUNTY, UT.

SUBMIT IN TRIPLICATE

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3. Address and Telephone No.

Rt. 3 Box 3630, Myton Utah, 84052 435-646-3721

4. Location of Well (Footage, Sec., T., R., m., or Survey Description)

2091 FNL 505 FWL SW/NW Section 25, T9S R15E

12. **CHECK APPROPRIATE BOX(s) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA**

TYPE OF SUBMISSION

☒ Notice of Intent
☐ Subsequent Report
☐ Final Abandonment Notice

TYPE OF ACTION

☐ Abandonment
☐ Recompletion
☐ Plugging Back
☐ Casing Repair
☐ Altering Casing
☒ Other **Permit Extension**

☐ Change of Plans
☐ New Construction
☐ Non-Routine Fracturing
☐ Water Shut-Off
☐ Conversion to Injection
☐ Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)

Newfield Production Company requests to extend the Permit to Drill this well for one year. The original approval date was 9/6/05 (expiration 9/6/06).

This APD was approved yet by the BLM on 7/28/06.

**Approved by the
Utah Division of
Oil, Gas and Mining**

Date:

By:

14. I hereby certify that the foregoing is true and correct

Signed

Mandie Crozier
Mandie Crozier

Title

Regulatory Specialist

Date

9/1/2006

CC: UTAH DOGM

(This space for Federal or State office use)

Approved by

Title

Conditions of Approval, Plans:

9/28/06
RM

RECEIVED

Date

SEP 05 2006

DIV. OF OIL, GAS & MINING



**Application for Permit to Drill
Request for Permit Extension
Validation**

(this form should accompany the Sundry Notice requesting permit extension)

API: 43-013-32885
Well Name: Ashley Federal 5-25-9-15
Location: SW/NW Section 25, T9S R15E
Company Permit Issued to: Newfield Production Company
Date Original Permit Issued: 9/6/2005

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision.

Following is a checklist of some items related to the application, which should be verified.

If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes ☐ No ☐ NA

Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes ☐ No ☒


Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes ☐ No ☒

Have there been any changes to the access route including ownership, or right-of-way, which could affect the proposed location? Yes ☐ No ☒

Has the approved source of water for drilling changed? Yes ☐ No ☒

Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes ☐ No ☒

Is bonding still in place, which covers this proposed well? Yes ☒ No ☐


Signature

9/1/2006

Date

Title: Regulatory Specialist

Representing: Newfield Production Company

**RECEIVED
SEP 05 2006**

DIV. OF OIL, GAS & MINING

DIVISION OF OIL, GAS AND MINING

SPUDDING INFORMATION

Name of Company: NEWFIELD PRODUCTION COMPANY

Well Name: ASHLEY FED 5-25-9-15

Api No: 43-013-32885 Lease Type: FEDERAL

Section 25 Township 09S Range 15E County DUCHESNE

Drilling Contractor NDSI RIG # NS#1

SPUDDED:

Date 09/25/06

Time 11:00 AM

How DRY

Drilling will Commence: _____

Reported by JOHNNY DAVIS

Telephone # (435) 823-3610

Date 09/27/06 Signed CHD

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM - FORM 6

RECEIVED
SEP 27 2006

OPERATOR: NEWFIELD PRODUCTION COMPANY
ADDRESS: RT. 3 BOX 3830
MYTON, UT 84062

OPERATOR ACCT. NO. N2695

DIV. OF OIL, GAS & MINING

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	15675	43-013-32945	Ashley Federal 3-25-9-15	NE/NW	25	9S	15E	DUCHESNE	09/21/06	9/28/06

WELL 1 COMMENTS: GRU

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	15676	43-013-32946	Ashley Federal 6-25-9-15	SE/NW	25	9S	15E	DUCHESNE	09/22/06	9/28/06

WELL 2 COMMENTS: GRU

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	15677	43-013-32885	Ashley Federal 5-25-9-15	SW/NW	25	9S	15E	DUCHESNE	09/25/06	9/28/06

WELL 3 COMMENTS: GRU

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	15678	43-013-32902	Ashley Federal 9-26-9-15	NE/SE	26	9S	15E	DUCHESNE	09/26/06	9/28/06

WELL 4 COMMENTS: GRU

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		

WELL 5 COMMENTS:


ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		

WELL 6 COMMENTS:

ACTION CODES (See instructions on back of form)

- A- Establish new entity for new well (single well only)
- B- Add new well to existing entity (group or unit well)
- C- Re-assign well from one existing entity to another existing entity
- D- Re-assign well from one existing entity to a new entity
- E- Other (explain in comments section)

NOTE: Use COMMENTS section to explain why each Action Code was selected.


Signature LANA NEBEKER

Production Analyst
Title

September 27, 2006
Date

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

5. Lease Serial No.

uku-66185

6. If Indian, Allottee or Tribe Name.

NA

7. If Unit or CA/Agreement, Name and/or

ASHLEY PA A

8. Well Name and No.

ASHLEY 5-25-9-15

9. API Well No.

4301332885

10. Field and Pool, or Exploratory Area

MONUMENT BUTTE

11. County or Parish, State

, UT

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630

Myton, UT 84052

3b. Phone (include area code)

435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Section T R S-25 T09S R15E

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 9/25/06 MIRU NDSI NS # 1. Spud well @ 11:00 AM. Drill 320' of 12 1/4" hole with air mist. TIH W/ 7 Jt's 8 5/8" J-55 24 # csgn. Set @ 322.69 KB On 9/30/06 cement with 160 sks of class "G" w/ 2% CaCL2 + 1/4# sk Cello- Flake Mixed @ 15.8 ppg > 1.17 cf/ sk yeild. Returned 4.5 bbls cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Alvin Nielsen

Signature

Title

Drilling Foreman

Date

10/01/2006

Approved by

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED

OCT 03 2006

DIV. OF OIL, GAS & MINING

NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

8 5/8 CASING SET AT 322.69

LAST CASING 8 5/8" set @ 322.69
 DATUM 12' KB
 DATUM TO CUT OFF CASING _____
 DATUM TO BRADENHEAD FLANGE _____
 TD DRILLER 320' LOGGER _____
 HOLE SIZE 12 1/4

OPERATOR Newfield Production Company
 WELL Ashley Federal 5-25-9-15
 FIELD/PROSPECT Monument Butte
 CONTRACTOR & RIG # NDSI NS # 1

LOG OF CASING STRING:

PIECES	OD	ITEM - MAKE - DESCRIPTION	WT / FT	GRD	THREAD	CONDT	LENGTH	
		Shoe 43.9						
		WHI - 92 csg head			8rd	A	0.95	
7	8 5/8"	Maverick ST&C csg	24#	J-55	8rd	A	310.84	
		GUIDE shoe			8rd	A	0.9	
CASING INVENTORY BAL.		FEET	JTS	TOTAL LENGTH OF STRING LESS CUT OFF PIECE PLUS DATUM TO T/CUT OFF CSG CASING SET DEPTH } COMPARE				312.69
TOTAL LENGTH OF STRING		312.69	7					2
LESS NON CSG. ITEMS		1.85						12
PLUS FULL JTS. LEFT OUT		0						322.69
TOTAL		310.84	7					
TOTAL CSG. DEL. (W/O THRDS)		310.84	7					
TIMING		1ST STAGE						
BEGIN RUN CSG.		Spud	9/25/2006	11:00 AM	GOOD CIRC THRU JOB			Yes
CSG. IN HOLE			9/25/2006	5:00 PM	Bbls CMT CIRC TO SURFACE			4.5
BEGIN CIRC			9/30/2006	12:06 PM	RECIPROCATED PIPE FOR			N/A
BEGIN PUMP CMT			9/30/2006	12:19 PM				
BEGIN DSPL. CMT			9/30/2006	12:34 PM	BUMPED PLUG TO			Did not 117 psi
PLUG DOWN			9/30/2006	12:42 PM				
CEMENT USED		CEMENT COMPANY- B. J.						
STAGE	# SX	CEMENT TYPE & ADDITIVES						
1	160	Class "G" w/ 2% CaCL2 + 1/4#/sk Cello-Flake mixed @ 15.8 ppg 1.17 cf/sk yield						
CENTRALIZER & SCRATCHER PLACEMENT				SHOW MAKE & SPACING				
Centralizers - Middle first, top second & third for 3								

COMPANY REPRESENTATIVE Johnny Davis DATE 10/1/2006

RECEIVED

OCT 03 2006

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
USA UTU-66185

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or
ASHLEY PA A

8. Well Name and No.
ASHLEY FEDERAL 5-25-9-15

9. API Well No.
4301332885

10. Field and Pool, or Exploratory Area
MONUMENT BUTTE

11. County or Parish, State
DUCHESNE, UT

1. Type of Well
☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include area code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

SWNW Section 25 T9S R15E

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to	<input type="checkbox"/> Plug Back	<input checked="" type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

Formation water is produced to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY

I hereby certify that the foregoing is true and
correct (Printed/ Typed)

Mandie Crozier

Signature

Title

Regulatory Specialist

Date

12/04/2006

Approved by

Conditions of approval, if any, are attached. Approval of this notice does not warrant or
certify that the applicant holds legal or equitable title to those rights in the subject lease
which would entitle the applicant to conduct operations thereon.

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United
States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED

DEC 05 2006

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.

USA UTU-66185

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

ASHLEY PA A

8. Well Name and No.

ASHLEY FEDERAL 5-25-9-15

9. API Well No.

4301332885

10. Field and Pool, or Exploratory Area

MONUMENT BUTTE

11. County or Parish, State

DUCHESNE, UT

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630

Myton, UT 84052

3b. Phone (include area code)

435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

SWNW Section 25 T9S R15E

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Weekly Status Report
	<input type="checkbox"/> Convert to	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 10/15/06 MIRU NDSI Rig # 1. Set all equipment. Pressure test Kelly, TIW, Choke manifold, & Bop's to 2,000 psi. Test 8.625 csgn to 1,500 psi. Vernal BLM field, & Roosevelt DOGM office was notified of test. PU BHA and tag cement @ 320'. Drill out cement & shoe. Drill a 7.875 hole with fresh water to a depth of 5830'. Lay down drill string & BHA. Open hole log w/ Dig/SP/GR log's TD to surface. PU & TIH with Guide shoe, shoe jt, float collar, 131 jt's of 5.5 J-55, 15.5# csgn. Set @ 5800' / KB. Cement with 300 sks cement mixed @ 11.0 ppg & 3.43 yld. The 450 sks cement mixed @ 14.4 ppg & 1.24 yld. Returned 0 bbls of cement to reserve pit. Nipple down Bop's. Drop slips @ 80,000 #'s tension. Release rig @ 1:00 PM on 10/24/06.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Justin Crum

Signature

Title

Drilling Foreman

Date

12/09/2006

Approved by

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED

DEC 12 2006

DIV. OF OIL, GAS & MINING

NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

5 1/2" CASING SET AT 5800.95

LAST CASING 8 5/8" SET AT 322
 DATUM 12' KB
 DATUM TO CUT OFF CASING 12'
 DATUM TO BRADENHEAD FLANGE _____
 TD DRILLER _____ LOGGER _____
 HOLE SIZE 7 7/8"

Flt cllr @ _____
 OPERATOR Newfield Production Company
 WELL Ashley Federal 5-25-9-15
 FIELD/PROSPECT Monument Butte
 CONTRACTOR & RIG # NDSI rig # 1

LOG OF CASING STRING:

PIECES	OD	ITEM - MAKE - DESCRIPTION	WT / FT	GRD	THREAD	CONDT	LENGTH
		Landing Jt					14
		Short jt 6.05' (4007'					
130	5 1/2"	ETC LT & C casing	15.5#	J-55	8rd	A	5757.33
							0.6
1	5 1/2"	ETC LT&C csg	15.5#	J-55	8rd	A	44.37
		GUIDE shoe			8rd	A	0.65

CASING INVENTORY BAL.	FEET	JTS	TOTAL LENGTH OF STRING	5802.95
TOTAL LENGTH OF STRING	5802.95	131	LESS CUT OFF PIECE	14
LESS NON CSG. ITEMS	15.25		PLUS DATUM TO T/CUT OFF CSG	12
PLUS FULL JTS. LEFT OUT	311.14	7	CASING SET DEPTH	5800.95
TOTAL	6098.84	138		

TOTAL CSG. DEL. (W/O THRDS)	6098.84	138	} COMPARE	
TIMING	1ST STAGE	2nd STAGE		
BEGIN RUN CSG.	10/24/2006	2:30 AM	GOOD CIRC THRU JOB	Partial
CSG. IN HOLE	10/24/2006	6:00 AM	Bbls CMT CIRC TO SURFACE	0
BEGIN CIRC	10/24/2006	7:12 AM	RECIPROCATED PIPE FOR	THRUSTROKE
BEGIN PUMP CMT	10/24/2006	7:21 AM	DID BACK PRES. VALVE HOLD ?	Yes
BEGIN DSPL. CMT	10/24/2006	8:15 AM	BUMPED PLUG TO	1257 PSI
PLUG DOWN	10/24/2006	8:44 AM		

CEMENT USED		CEMENT COMPANY- B. J.
STAGE	# SX	CEMENT TYPE & ADDITIVES
1	300	Prem-lite II w/ 10% gel + 3 % KCL, 3#’s /sk CSE + 2# sk/kolseal + 1/4#’s/sk Cello Flake
		mixed @ 11.0 ppg W / 3.43 cf/sk yield
2	450	50/50 poz W/ 2% Gel + 3% KCL, .5%EC1, 1/4# sk C.F. 2% gel. 3% SM mixed @ 14.4 ppg W/ 1.24 YLD
CENTRALIZER & SCRATCHER PLACEMENT		SHOW MAKE & SPACING
Centralizers - Middle first, top second & third. Then every third collar for a total of 20.		

COMPANY REPRESENTATIVE Johnny Davis DATE 10/25/2006

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL: OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER <input type="checkbox"/>		5. LEASE DESIGNATION AND SERIAL NUMBER: USA UTU-66185
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052		7. UNIT or CA AGREEMENT NAME: ASHLEY PA A
4. LOCATION OF WELL: FOOTAGES AT SURFACE: _____		8. WELL NAME and NUMBER: ASHLEY FEDERAL 5-25-9-15
OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: SWNW, 25, T9S, R15E		9. API NUMBER: 4301332885
		10. FIELD AND POOL, OR WILDCAT: MONUMENT BUTTE
		COUNTY: DUCHESNE
		STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: <u>12/14/2006</u>	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Status report for time period 10/31/06 - 11/27/06

Subject well had completion procedures initiated in the Green River formation on 10-31-06 without the use of a service rig over the well. A cement bond log was run and a total of ONE Green River intervals were perforated and hydraulically fracture treated with 20/40 mesh sand. Perforated intervals are as follows: Stage #1 (5228'-5244'). All perforations, were 4 JSPF. Composite flow-through frac plugs were used between stages. Fracs were flowed back through chokes. A service rig was moved over the well on 11-14-2006. Bridge plugs were drilled out and well was cleaned to 5733'. Zones were swab tested for sand cleanup. A new 1 1/2" bore rod pump was run in well on sucker rods. Well was placed on production via rod pump on 11-27-2006.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY**

NAME (PLEASE PRINT) <u>Jentri Park</u>	TITLE <u>Production Clerk</u>
SIGNATURE 	DATE <u>12/14/2006</u>

(This space for State use only)

**RECEIVED
DEC 15 2006
DIV. OF OIL, GAS & MINING**

**UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT**

WELL COMPLETION OR RECOMPLETION REPORT AND LOG*

1a. TYPE OF WORK

OIL WELL ☒ GAS WELL ☐ DRY ☐ Other _____

1b. TYPE OF WELL

NEW WELL ☒ WORK OVER ☐ DEEPEN ☐ PLUG BACK ☐ DIFF RESVR. ☐ Other _____

2. NAME OF OPERATOR

Newfield Exploration Company

3. ADDRESS AND TELEPHONE NO.

1401 17th St. Suite 1000 Denver, CO 80202

4. LOCATION OF WELL (Report locations clearly and in accordance with any State requirements.)*

At Surface 2091' FNL & 505' FWL (SW/NW) Sec. 25, T9S, R15E

At top prod. Interval reported below

At total depth

14. API NO. 43-013-32885 DATE ISSUED 9/06/06

12. COUNTY OR PARISH Duchesne 13. STATE UT

15. DATE SPUDDED 9/25/06 16. DATE T.D. REACHED 10/21/06 17. DATE COMPL. (Ready to prod.) 11/27/06 18. ELEVATIONS (DF, RKB, RT, GR, ETC.)* 6301' GL 6313' KB 19. ELEV. CASINGHEAD

20. TOTAL DEPTH, MD & TVD 5830' 21. PLUG BACK T.D., MD & TVD 5733' 22. IF MULTIPLE COMPL., HOW MANY* 23. INTERVALS DRILLED BY -----> ROTARY TOOLS X CABLE TOOLS

24. PRODUCING INTERVAL(S), OF THIS COMPLETION--TOP, BOTTOM, NAME (MD AND TVD)* Green River 5228'-5244' 25. WAS DIRECTIONAL SURVEY MADE No

26. TYPE ELECTRIC AND OTHER LOGS RUN

Dual Induction Guard, SP, Compensated Density, Compensated Neutron, GR, Caliper, Cement Bond Log

27. WAS WELL CORED No

23. CASING RECORD (Report all strings set in well)

CASING SIZE/GRADE	WEIGHT, LB./FT.	DEPTH SET (MD)	HOLE SIZE	TOP OF CEMENT, CEMENTING RECORD	AMOUNT PULLED
8-5/8" - J-55	24#	323'	12-1/4"	To surface with 160 sx Class "G" cmt	
5-1/2" - J-55	15.5#	5801'	7-7/8"	300 sx Premlite II and 450 sx 50/50 Poz	

29. LINER RECORD

SIZE	TOP (MD)	BOTTOM (MD)	SACKS CEMENT*	SCREEN (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)
					2-7/8"	EOT @ 5295	TA @ 5199'

31. PERFORATION RECORD (Interval, size and number)

INTERVAL	SIZE	SPF/NUMBER	DEPTH INTERVAL (MD)	AMOUNT AND KIND OF MATERIAL USED
(LODC) 5228'-5244'	.46"	4/64	5228'-5244'	Frac w/ 85,862# of 20/40 sand in 662 bbls fluid

33.* PRODUCTION

DATE FIRST PRODUCTION 11/27/06		PRODUCTION METHOD (Flowing, gas lift, pumping--size and type of pump) 2-1/2" x 1-1/2" x 14' RHAC SM Plunger Pump					WELL STATUS (Producing or shut-in) PRODUCING	
DATE OF TEST 10 day ave	HOURS TESTED	CHOKE SIZE	PROD'N. FOR TEST PERIOD ---->	OIL--BBLs. 50	GAS--MCF. 0	WATER--BBL. 8		GAS-OIL RATIO 0
FLOW. TUBING PRESS.	CASING PRESSURE	CALCULATED 24-HOUR RATE ----->	OIL--BBL.	GAS--MCF.	WATER--BBL.		OIL GRAVITY-API (CORR.)	

34. DISPOSITION OF GAS (Sold, used for fuel, vented, etc.)

Sold & Used for Fuel

35. LIST OF ATTACHMENTS

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records

SIGNED Jennifer Park TITLE Production Clerk

DIV. OF OIL, GAS & MINING 12/14/2006

*(See Instructions and Spaces for Additional Data on Reverse Side)

RECEIVED
DEC 15 2006

37. SUMMARY OF POROUS ZONES: (Show all important zones of porosity and contents thereof; cored intervals, and all drill-stem, tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures, and recoveries);				38. GEOLOGIC MARKERS		
FORMATION	TOP	BOTTOM	DESCRIPTION, CONTENTS, ETC.	NAME	TOP	
			Well Name Ashley Federal 5-25-9-15		MEAS. DEPTH	TRUE VERT. DEPTH
				Garden Gulch Mkr	3404'	
				Garden Gulch 1	3612'	
				Garden Gulch 2	3724'	
				Point 3 Mkr	3971'	
				X Mkr	4229'	
				Y-Mkr	4264'	
				Douglas Creek Mkr	4371'	
				BiCarbonate Mkr	4516'	
				B Limestone Mkr	4694'	
				Castle Peak	5270'	
				Basal Carbonate	5716'	
				Total Depth (LOGGERS)	5765'	

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM - FORM 6

OPERATOR: NEWFIELD PRODUCTION COMPANY
ADDRESS: RT. 3 BOX 3630
MYTON, UT 84052

OPERATOR ACCT. NO. N2095

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RS	COUNTY		
C	15675	12419	4301332945	ASHLEY FEDERAL 3-25-9-15	NENW	25	9S	15E	DUCHESNE		2/13/07
WELL 5 COMMENT: <u>GRPV</u> ASHLEY PA 'AB' 1ST REVISION EFFECTIVE 10-1-2006											
ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RS	COUNTY		
C	15663	12419	4301332903	ASHLEY FEDERAL 10-26-9-15	NW/SE	26	9S	15E	DUCHESNE		2/13/07
WELL 5 COMMENT: <u>GRPV</u> ASHLEY PA 'AB' 1ST REVISION EFFECTIVE 10-1-2006											
ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RS	COUNTY		
C	15676	12419	4301332946	ASHLEY FEDERAL 6-25-9-15	SE/NW	25	9S	15E	DUCHESNE		2/13/07
WELL 5 COMMENT: <u>GRPV</u> ASHLEY PA 'AB' 1ST REVISION EFFECTIVE 10-1-2006											
ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RS	COUNTY		
C	15678	12419	4301332902	ASHLEY FEDERAL 9-26-9-15	NE/SE	26	9S	15E	DUCHESNE		2/13/07
WELL 5 COMMENT: <u>GRPV</u> ASHLEY PA 'AB' 1ST REVISION EFFECTIVE 10-1-2006											
ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RS	COUNTY		
C	15677	12419	4301332885	ASHLEY FEDERAL 5-25-9-15	SW/NW	25	9S	15E	DUCHESNE		2/13/07
WELL 5 COMMENT: <u>GRPV</u> ASHLEY PA 'AB' 1ST REVISION EFFECTIVE 10-1-2006											
ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RS	COUNTY		
C	15686	12419	4301332883	ASHLEY FEDERAL 2-25-9-15	NW/NE	26	9S	15E	DUCHESNE		2/13/07
WELL 5 COMMENT: <u>GRPV</u> ASHLEY PA 'AB' 1ST REVISION EFFECTIVE 10-1-2006											

ACTION CODES (See instructions on back of form)

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or well only)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected

RECEIVED

FEB 14 2007

RECEIVED

JAN 14 2007

DIV. OF OIL, GAS & MINING

DIV. OF OIL, GAS & MINING

Lana Nebeker

LANA NEBEKER

Production Analyst

Title

February 12, 2006

Date



United States Department of the Interior

BUREAU OF LAND MANAGEMENT
Utah State Office
P.O. Box 45155
Salt Lake City, UT 84145-0155
<http://www.blm.gov>



IN REPLY REFER TO:
3180
UT-922

FEB 02 2007

RECEIVED

FEB 07 2007

Newfield Exploration Company
Attn: Laurie Deseau
1401 Seventeenth Street, Suite 1000
Denver, CO 80202

DIV. OF OIL, GAS & MINING

Re: 1st Revision Consolidated
Green River Formation PA "A, B"
Ashley Unit
Duchesne County, Utah

The 1st Revision of the Consolidated Green River Formation "A,B" Ashley Unit, CRS UTU73520C, is hereby approved effective as of October 1, 2006, pursuant to Section 11 of the Ashley Unit Agreement, Duchesne County, Utah.

The 1st Revision of the Consolidated Green River Formation PA "A, B" results in a Participating Area of 7,350.49 acres, and is based upon the completion of the following wells as being capable of producing unitized substances in paying quantities:

WELL NO.	API NO.	LOCATION	LEASE NO.
15-24	43-013-32943	SWSE, 24-9S-15E	UTU02458
16-24	43-013-32944	SESE, 24-9S-15E	UTU02458
16-27	43-013-32881	SESE, 27-9S-15E	UTU66185
14-26	43-013-32907	SESW, 26-9S-15E	UTU66185
13-26	43-013-32906	SWSW, 26-9S-15E	UTU66185
15-26	43-013-32908	SWSE, 26-9S-15E	UTU66185
11-26	43-013-32904	NESW, 26-9S-15E	UTU66185
3-25	43-013-32945	NENW, 25-9S-15E	UTU66185
10-26	43-013-32903	NWSE, 26-9S-15E	UTU66185
6-25	43-013-32946	SENW, 25-9S-15E	UTU66185
9-26	43-013-32902	NESE, 26-9S-15E	UTU66185
5-25	43-013-32885	SWNW, 25-9S-15E	UTU66185
2-25	43-013-32883	NWNE, 25, 9S-15E	UTU66185
11-25	43-013-32905 32910	NWSW, 26, 9S-15E	UTU66185
9-25	43-013-32948	NESE, 25, 9S-15E	UTU66185
15-25	43-013-32950	SWSE, 25, 9S-15E	UTU66185

Copies of the approved request are being distributed to the appropriate agencies and one copy is returned herewith. Please advise all interested parties of the approval of the 1st Revision of the Consolidated Green River PA "A, B", Ashley Unit.

Sincerely,

/s/ Douglas F. Cook

Douglas F. Cook
Chief, Branch of Fluid Minerals

bcc: Division of Oil, Gas & Mining
SITLA
Ashley Unit w/enclosure
MMS - Data Management Division (Attn: James Sykes)
Field Manager - Vernal w/enclosure
Agr. Sec. Chron.
Central Files
CSeare:cs (01/31/06)Ashley Consolidated PA "A, B"1st.Rev.

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.


1. TYPE OF WELL: OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER <input type="checkbox"/>		5. LEASE DESIGNATION AND SERIAL NUMBER: USA UTU-66185
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052		7. UNIT or CA AGREEMENT NAME: ASHLEY PA AB
4. LOCATION OF WELL: FOOTAGES AT SURFACE: 2091 FNL 505 FWL		8. WELL NAME and NUMBER: ASHLEY FEDERAL 5-25-9-15
OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: SWNW, 25, T9S, R15E		9. API NUMBER: 4301332885
		10. FIELD AND POOL, OR WILDCAT: MONUMENT BUTTE
		COUNTY: DUCHESNE
		STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> DEEPEN <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> PLUG BACK <input type="checkbox"/> PRODUCTION (START/STOP) <input type="checkbox"/> RECLAMATION OF WELL SITE <input checked="" type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	<input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> TEMPORARILY ABANDON <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> VENT OR FLAIR <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> WATER SHUT-OFF <input type="checkbox"/> OTHER: -
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 08/07/2007			

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was recompleted on 07/15/07, attached is a daily recompletion status report.

NAME (PLEASE PRINT) Jenni Park TITLE Production Clerk
SIGNATURE  DATE 08/07/2007

(This space for State use only)

RECEIVED
AUG 15 2007
DIV. OF OIL, GAS & MINING

Daily Activity Report

Format For Sundry

ASHLEY 5-25-9-15**5/1/2007 To 9/30/2007****7/9/2007 Day: 1****Recompletion**

NC #2 on 7/8/2007 - MIRU NC #2. Hot oiler had 70 BW pumped down csg @ 250°. RD pumping unit. Soft seat rod pump. Fill tbg w/ 15 BW & pressure test tbg to 3000#. Unseat rod pump & flush rods & tbg w/ 40 BW. TOO H w/ rods as detailed below. Flushed tbg & rods w/ additional 30 BW while TOO H. SWIFN.

7/10/2007 Day: 2**Recompletion**

NC #2 on 7/9/2007 - X-over for tbg. ND wellhead. Release TA. NU BOPs. RU rig floor. TOO H w/ tbg as detailed below. RD rig floor. ND 3000# BOPs & production wellhead. NU 5000# frac head & 5000# cameron BOPs. RU Lone Wolf wireline, inc. RIH w/ BP on wireline & set BP @ 5130'. Perforate the LODC sands from 5088'-5094'. RD Lone Wolf. SWIFN.

7/11/2007 Day: 3**Recompletion**

NC #2 on 7/10/2007 - RU BJ Services "Ram Head" frac flange. RU BJ & frac stage #1, LODC sds down casing w/ 21,374#'s of 20/40 sand in 391 bbls of Lightning 17 frac fluid. Open well w/ 0 psi on casing. Took 70 bbls to load hole. Perfs broke down @ 2575 psi. Treated @ ave pressure of 2901 @ ave rate of 24.8 w/ 6.5 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 2775. 476 bbls EWTR. Leave pressure on well. RU WLT. RIH w/ flow through frac plug & 10' perf gun. Set plug @ 4660'. Perforate B.5 sds @ 4554-64' w/ 4 spf for total of 40 shots. RU BJ & perfs won't break down. RIH & spot 8 gals of 15% HCL acid on perfs. RU BJ & frac stage #2 w/ 29,766#'s of 20/40 sand in 356 bbls of Lightning 17 frac fluid. Open well w/ 1912 psi on casing. Perfs broke down @ 2256 psi. Treated @ ave pressure of 2082 @ ave rate of 24.8 w/ 8 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 1965. 832 bbls EWTR. Leave pressure on well. RU WLT. RIH w/ solid frac plug & 4', 4', 5' perf guns. Set plug @ 4490'. Perforate D2 sds @ 4423-27', D1 sds @ 4408-12', 4392-97' w/ 4 spf for total of 52 shots. RU BJ & frac stage #3 w/ 50,286#'s of 20/40 sand in 461 bbls of Lightning 17 frac fluid. Open well w/ 153 psi on casing. Perfs broke down @ 3582 psi. Treated @ ave pressure of 1414 @ ave rate of 24.8 w/ 8 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 1628. 1293 bbls EWTR. Leave pressure on well. RU WLT. RIH w/ flow through frac plug & 5', 8' perf guns. Set plug @ 4070'. Perforate GB6 sds @ 3962-67', GB4 sds @ 3904-12' w/ 4 spf for total of 52 shots. RU BJ & frac stage #4 w/ 44,217#'s of 20/40 sand in 393 bbls of Lightning 17 frac fluid. Open well w/ 1285 psi on casing. Perfs broke down @ 1895 psi. Treated @ ave pressure of 1273 @ ave rate of 17.8 w/ 8 ppg of sand. ISIP was 1345. 1686 bbls EWTR. RD BJ & WLT. Flow well back. Well flowed for 3 hours & died w/ 220 bbls rec'd. SIFN.

7/12/2007 Day: 4**Recompletion**

NC #2 on 7/11/2007 - Bleed off well. ND 5000# cameron BOPs & frac head. NU 3000# production head & BOPs. TIH w/ 2 7/8 tbg & tag fill @ 3960'. Clean out to plug @ 4070'. Drill up plug in 38 minutes. Circulate well clean. TIH & tag fill @ 4400'. Clean out to plug @ 4490'. Drill up plug in 44 minutes. Circulate well clean. TIH & tag fill @ 4540'. Clean out to plug @ 4660'. Drill up plug in 42 minutes. Circulate well clean. TIH & tag fill @ 5040'. Clean out to plug @ 5130'. Drill up plug in 40 minutes.

Circulate well clean. TIH @ tag fill @ 5722'. Clean out to PBTD @ 5733'. Circulate well clean.

7/13/2007 Day: 5

Recompletion

NC #2 on 7/12/2007 - TOOH w/ 14 jts 2 7/8 tbg. RU swab. Made 17 swab runs w/ SFL @ surface & EFL @ 2300'. Recovered 155 Bbls fluid. Ending w/ trace of oil, good show of gas, no show of sand. TIH w/ 14 jts tbg & tag @ 5733 (PBTD) no additional fill. TOOH w/ tbg, LD 14 jts on trailer. TIH w/ production tbg as detailed below. Flush tbg w/ 60 BW. SWIFN.

7/16/2007 Day: 6

Recompletion

NC #2 on 7/15/2007 - X-over for rods. TIH w/ rods as detailed below. LD 10- 3/4" plain rods. PU 10- 3/4" guided rods. Fill tbg w/ 2 BW and test to 200 psi. Stroke test pump w/ rig to 800 psi. RU pumping unit. Hang off rods. Adjust tag. RD rig pump & pump lines. RDMO NC #2. PWOP @ 10:00 AM w/ 1463 BWTR. Final Report.

Pertinent Files: Go to File List



December 3, 2007

Mr. Dan Jarvis
State of Utah
Division of Oil, Gas and Mining
Post Office Box 145801
Salt Lake City, Utah 84114-5801


RE: Permit Application for Water Injection Well
Ashley Federal #5-25-9-15
Monument Butte Field, Ashley PA AB, Lease #UTU-66185
Section 25-Township 9S-Range 15E
Duchesne County, Utah

Dear Mr. Jarvis:

Newfield Production Company herein requests approval to convert the Ashley Federal #5-25-9-15 from a producing oil well to a water injection well in the Monument Butte (Green River) Field, Ashley PA AB.

I hope you find this application complete; however, if you have any questions or require additional information, please contact me at (303) 893-0102.

Sincerely,


David Gerbig
Operations Engineer

RECEIVED

JAN 22 2008

DIV. OF OIL, GAS & MINING

NEWFIELD PRODUCTION COMPANY
APPLICATION FOR APPROVAL OF CLASS II INJECTION WELL
ASHLEY FEDERAL #5-25-9-15
MONUMENT BUTTE FIELD (GREEN RIVER)
ASHLEY PA AB
LEASE #UTU-66185
DECEMBER 3, 2007

RECEIVED
JAN 22 2008
DIV. OF OIL, GAS & MINING

TABLE OF CONTENTS

LETTER OF INTENT	
COVER PAGE	
TABLE OF CONTENTS	
UIC FORM 1 – APPLICATION FOR INJECTION WELL	
WELLBORE DIAGRAM OF PROPOSED INJECTION	
WORK PROCEDURE FOR INJECTION CONVERSION	
COMPLETED RULE R615-5-1 QUESTIONNAIRE	
COMPLETED RULE R615-5-2 QUESTIONNAIRE	
ATTACHMENT A	ONE-HALF MILE RADIUS MAP
ATTACHMENT A-1	WELL LOCATION PLAT
ATTACHMENT B	LIST OF SURFACE OWNERS WITHIN ONE-HALF MILE RADIUS
ATTACHMENT C	CERTIFICATION FOR SURFACE OWNER NOTIFICATION
ATTACHMENT E	WELLBORE DIAGRAM – ASHLEY FEDERAL #5-25-9-15
ATTACHMENT E-1	WELLBORE DIAGRAM – ASHLEY FEDERAL #13-24-9-15
ATTACHMENT E-2	WELLBORE DIAGRAM – ASHLEY FEDERAL #4-25-9-15
ATTACHMENT E-3	WELLBORE DIAGRAM – ASHLEY FEDERAL #3-25-9-15
ATTACHMENT E-4	WELLBORE DIAGRAM – ASHLEY FEDERAL #6-25-9-15
ATTACHMENT E-5	WELLBORE DIAGRAM – ASHLEY FEDERAL #9-26-9-15
ATTACHMENT E-6	WELLBORE DIAGRAM – ASHLEY FEDERAL #12-25-9-16
ATTACHMENT E-7	WELLBORE DIAGRAM – ASHLEY FEDERAL #11-25-9-15
ATTACHMENT E-8	WELLBORE DIAGRAM – ASHLEY FEDERAL #13-25-9-15
ATTACHMENT F	WATER ANALYSIS
ATTACHMENT G	FRACTURE GRADIENT CALCULATIONS
ATTACHMENT G-1	FRACTURE REPORTS DATED 11/1/06 – 11/11/06
ATTACHMENT H	WORK PROCEDURE FOR PROPOSED PLUG AND ABANDON
ATTACHMENT H-1	WELLBORE DIAGRAM OF PROPOSED PLUGGED WELL

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING

APPLICATION FOR INJECTION WELL - UIC FORM 1

OPERATOR Newfield Production Company
ADDRESS 1401 17th Street, Suite 1000
Denver, Colorado 80202

Well Name and number: Ashley Federal #5-25-9-15
Field or Unit name: Monument Butte (Green River), Ashley PA AB Lease No. UTU-66185
Well Location: QQ SW/NW section 25 township 9S range 15E county Duchesne


Is this application for expansion of an existing project? Yes [X] No []
Will the proposed well be used for: Enhanced Recovery? Yes [X] No []
Disposal? Yes [] No [X]
Storage? Yes [] No [X]
Is this application for a new well to be drilled? Yes [] No [X]
If this application is for an existing well,
has a casing test been performed on the well? Yes [] No [X]
Date of test: _____
API number: 43-013-32885

Proposed injection interval: from 3724 to 5716
Proposed maximum injection: rate 500 bpd pressure 2646 psig
Proposed injection zone contains [x] oil, [] gas, and/or [] fresh water within 1/2
mile of the well.

IMPORTANT: Additional information as required by R615-5-2 should
accompany this form.

List of Attachments: Attachments "A" through "H-1"

I certify that this report is true and complete to the best of my knowledge.

Name: David Gerbig Signature 
Title Operations Engineer Date 1-15-08
Phone No. (303) 893-0102

(State use only)
Application approved by _____ Title _____
Approval Date _____

Comments:

Ashley Federal 5-25-9-15

Spud Date 09/25/2006
Put on Production: 11/27/2006
GL: 6301' KB: 6313'

Proposed Injection Wellbore Diagram

Initial Production: BOPD,
MCFD, BWPD

SURFACE CASING

CSG SIZE: 8-5/8"
GRADE: J-55
WEIGHT: 24#
LENGTH: 7 jts. (310.84')
DEPTH LANDED: 322.69' KB
HOLE SIZE: 12-1/4"
CEMENT DATA: 160 sxs Class "G" cmt, est 4.5 bbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
GRADE: J-55
WEIGHT: 15.5#
LENGTH: 131 jts. (5801.70')
DEPTH LANDED: 5800.95' KB
HOLE SIZE: 7-7/8"
CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ.

TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55
NO. OF JOINTS: 168 jts (5186.57')
TUBING ANCHOR: 5198.57'
NO. OF JOINTS: 1 jts (29.45')
SEATING NIPPLE: 2-7/8" (1.10')
SN LANDED AT: 5230.82'
NO. OF JOINTS: 2 jts (63.00')
TOTAL STRING LENGTH: EOT @ 5295.37'

FRAC JOB

11/10/2006 5228-5244' **Frac LODC sands as follows:**
85862# 20/40 sand in 662 bbls Lightning 17
frac fluid. Treated @ avg press of 230 psi
w/avg rate of 25.5 BPM. ISIP 2680 psi. Calc
flush: 5226 gal. Actual flush: 4809 gal.

9-6-07 Pump change. Updated rod & tubing details.

Cement Top @ 1320'

Packer @ 5193'

5228-5244'

PBTD @ 5733'

TD @ 5830'

PERFORATION RECORD

10-31-06 5686-5706' 4 JSPP 64 holes

NEWFIELD

Ashley Federal 5-25-9-15

2091' FNL & 505' FWL

SW/NW Section 25-T9S-R15E

Duchesne Co, Utah

API #43-013-32885; Lease #UTU-66185

WORK PROCEDURE FOR INJECTION CONVERSION

1. Rig up hot oil truck to casing. Pump water. Unseat pump. Flush rods. Trip out of hole with rods and pump.
2. Trip out of hole with tubing, breaking and doping every connection. Trip in hole with packer and tubing. Rig up water truck to casing. Pump packer fluid. Set packer.
3. Test casing and packer.
4. Rig down and move out.

**REQUIREMENTS FOR INJECTION OF FLUIDS INTO RESERVOIRS
RULE R615-5-1**

1. **Operations to increase ultimate recovery, such as cycling of gas, the maintenance of pressure, the introduction of gas, water or other substances into a reservoir for the purpose of secondary or other enhanced recovery or for storage and the injection of water into any formation for the purpose of water disposal shall be permitted only by order of the Board after notice and hearing.**
2. **A request for agency action for authority for the injection of gas, liquified petroleum gas, air, water or any other medium into any formation for any reason, including but not necessarily limited to the establishment of or the expansion of waterflood projects, enhanced recovery projects, and pressure maintenance projects shall contain:**

2.1 The name and address of the operator of the project.

Newfield Production Company
1401 17th Street, Suite 1000
Denver, Colorado 80202

2.2 A plat showing the area involved and identifying all wells, including all proposed injection wells, in the project area and within one-half mile of the project area.

See Attachment A.

2.3 A full description of the particular operation for approval is requested.

Approval is requested to convert the Ashley Federal #5-25-9-15 from a producing oil well to a water injection well in Monument Butte (Green River) Field, Ashley PA AB.

2.4 A description of the pools from which the identified wells are producing or have produced.

The proposed injection well will inject into the Green River Formation.

2.5 The names, description and depth of the pool or pools to be affected.

The injection zone is in the Green River Formation. For the Ashley Federal #5-25-9-15 well, the proposed injection zone is from Garden Gulch to Basal Limestone (3724' - 4694'). The confining strata directly above and below the injection zones are the Garden Gulch and Castle Peak Members of the Green River Formation, with the Garden Gulch Marker top at 3404' and the Castle Peak top at 5270'.

2.6 A copy of a log of a representative well completed in the pool.

The referenced log for the Ashley Federal #5-25-9-15 is on file with the Utah Division of Oil, Gas and Mining.

- 2.7 A statement as to the type of fluid to be used for injection, its source and the estimated amounts to be injected daily.**

The primary type and source of fluid to be used for injection will be culinary water commingled with produced water. The average estimated injection of fluids will be at a rate of 300 BPD, and the estimated maximum injection will be at a rate of 500 BPD.

- 2.8 A list of all operators and surface owners within one-half mile radius of the proposed project.**

See Attachment B.

- 2.9 An affidavit certifying that said operators or owners and surface owners within a one-half mile radius have been provided a copy of the petition for injection.**

See Attachment C.

- 2.10 Any additional information the Board may determine is necessary to adequately review the petition.**

Newfield Production Company will supply any additional information requested by the Utah Division of Oil, Gas and Mining.

- 4.0 Establish recovery projects may be expanded and additional wells placed on injection only upon authority from the Board after notice and hearing or by administrative approval.**

This proposed injection well is on a State lease (Lease #UTU-66185) in the Monument Butte (Green River) Field, Ashley PA AB, and this request is for administrative approval.

**REQUIREMENTS FOR CLASS II INJECTION WELLS INCLUDING WATER DISPOSAL,
STORAGE AND ENHANCED RECOVERY WELLS
SECTION V – RULE R615-5-2**

- 1. Injection well shall be completed, equipped, operated, and maintained in a manner that will prevent pollution and damage to any USDW, or other resources and will confine injected fluids to the interval approved.**
- 2. The application for an injection well shall include a properly completed Form DOGM-UIC-1 and the following:**

- 2.1 A plat showing the location of the injection well, all abandoned or active wells within a one-half mile radius of the proposed wells, and the surface owner and the operator of any lands or producing leases, respectively, within a one-half mile radius of the proposed injection well.**

See Attachments A and B.

- 2.2 Copies of electrical or radioactive logs, including gamma ray logs, for the proposed well run prior to the installation of casing and indicating resistivity, spontaneous potential, caliper and porosity.**

All logs are on file with the Utah Division of Oil, Gas and Mining.

- 2.3 A copy of a cement bond or comparable log run for the proposed injection well after casing was set and cemented.**

A copy of the cement bond log is on file with the Utah Division of Oil, Gas and Mining.

- 2.4 Copies of logs already on file with the Division should be referenced, but need not be refiled.**

All copies of logs are on file with the Utah Division of Oil, Gas and Mining.

- 2.5 A description of the casing or proposed casing program of the injection well and of the proposed method for testing the casing before use of the well.**

The casing program is 8-5/8", 24#, J-55 surface casing run to 323' GL, and 5-1/2" 15.5# J-55 casing run from surface to 5801' KB. A casing integrity test will be conducted at the time of conversion. See Attachment E.

- 2.6 A statement as to the type of fluid to be used for injection, its source and estimated amounts to be injected daily.**

The primary type and source of fluid to be used for injection will be culinary water commingled with produced water. The estimated average rate of injection will be 300 BPD, and the estimated maximum rate of injection will be 500 BPD.

- 2.7 Standard laboratory analysis of the fluid to be injected, the fluid in the formation into which the fluid is being injected, and the compatibility of the fluids.**

See Attachment F.

The proposed average and maximum injection pressures.

The proposed average injection pressure will be approximately 1100 psig and the maximum injection pressure will not exceed 2646 psig.

- 2.8 Evidence and data to support a finding that the proposed injection well will not initiate fractures through the overlying strata or a confining interval that could enable the injected fluid or formation fluid to enter the fresh water strata.**

The minimum fracture gradient for the Ashley Federal #5-25-9-15, for existing perforations (5228' - 5244') calculates at 0.95 psig/ft. The maximum injection pressures will be limited so as not to exceed this gradient. A step rate test will be performed periodically to ensure we are below parting pressure. The proposed maximum injection pressure is 2646 psig. We may add additional perforations between 3404' and 5765'. See Attachments G and G-1.

- 2.9 Appropriate geological data on the injection interval and confining beds, including the geologic name, lithologic description, thickness, depth, and lateral extent.**

In the Ashley Federal #5-25-9-15, the proposed injection zone (3724' - 5716') is in the Garden Gulch to Basal limestone members of the Green River Formation. The reservoir is a very fine-grained sandstone with minor imbedded shale streaks. The estimated porosity is 13%. The members are composed of porous and permeable lenticular calcareous sandstone and low porosity carbonates and calcareous shale. The porous and lenticular sandstone varies in thickness from 0-31' and is confined to the Monument Butte Field. Outside the Monument Butte Field, the sandstone is composed of tight, very fine, silty, calcareous sandstone, less than 3' thick. The stratum confining the injection zone is composed of tight, moderately calcareous, sandy lacustrine shale. All of the confining strata are impermeable, and will effectively seal off the oil, gas, and water of the injection zone from any strata directly above or below it.

- 2.10 A review of the mechanical condition of each well within a one-half mile radius of the proposed injection well to assure that no conduit exists that could enable fluids to migrate up or down the wellbore and enter the improper intervals.**

See Attachments E through E-8.


Additionally, the injection system will be equipped with high and low pressure shut down devices that will automatically shut in injection waters if a system blockage or leakage occurs. One way check valves will also ensure proper flow management. Relief valves will also be utilized for high-pressure relief.

- 2.11 An affidavit certifying that a copy of the application has been provided to all operators or owners, and surface owners within a one-half mile radius of the proposed injection well.**

See Attachment C.

- 2.12 Any other information that the Board or Division may determine is necessary to adequately review the application.**

Newfield Production Company will supply any requested information to the Board or Division.

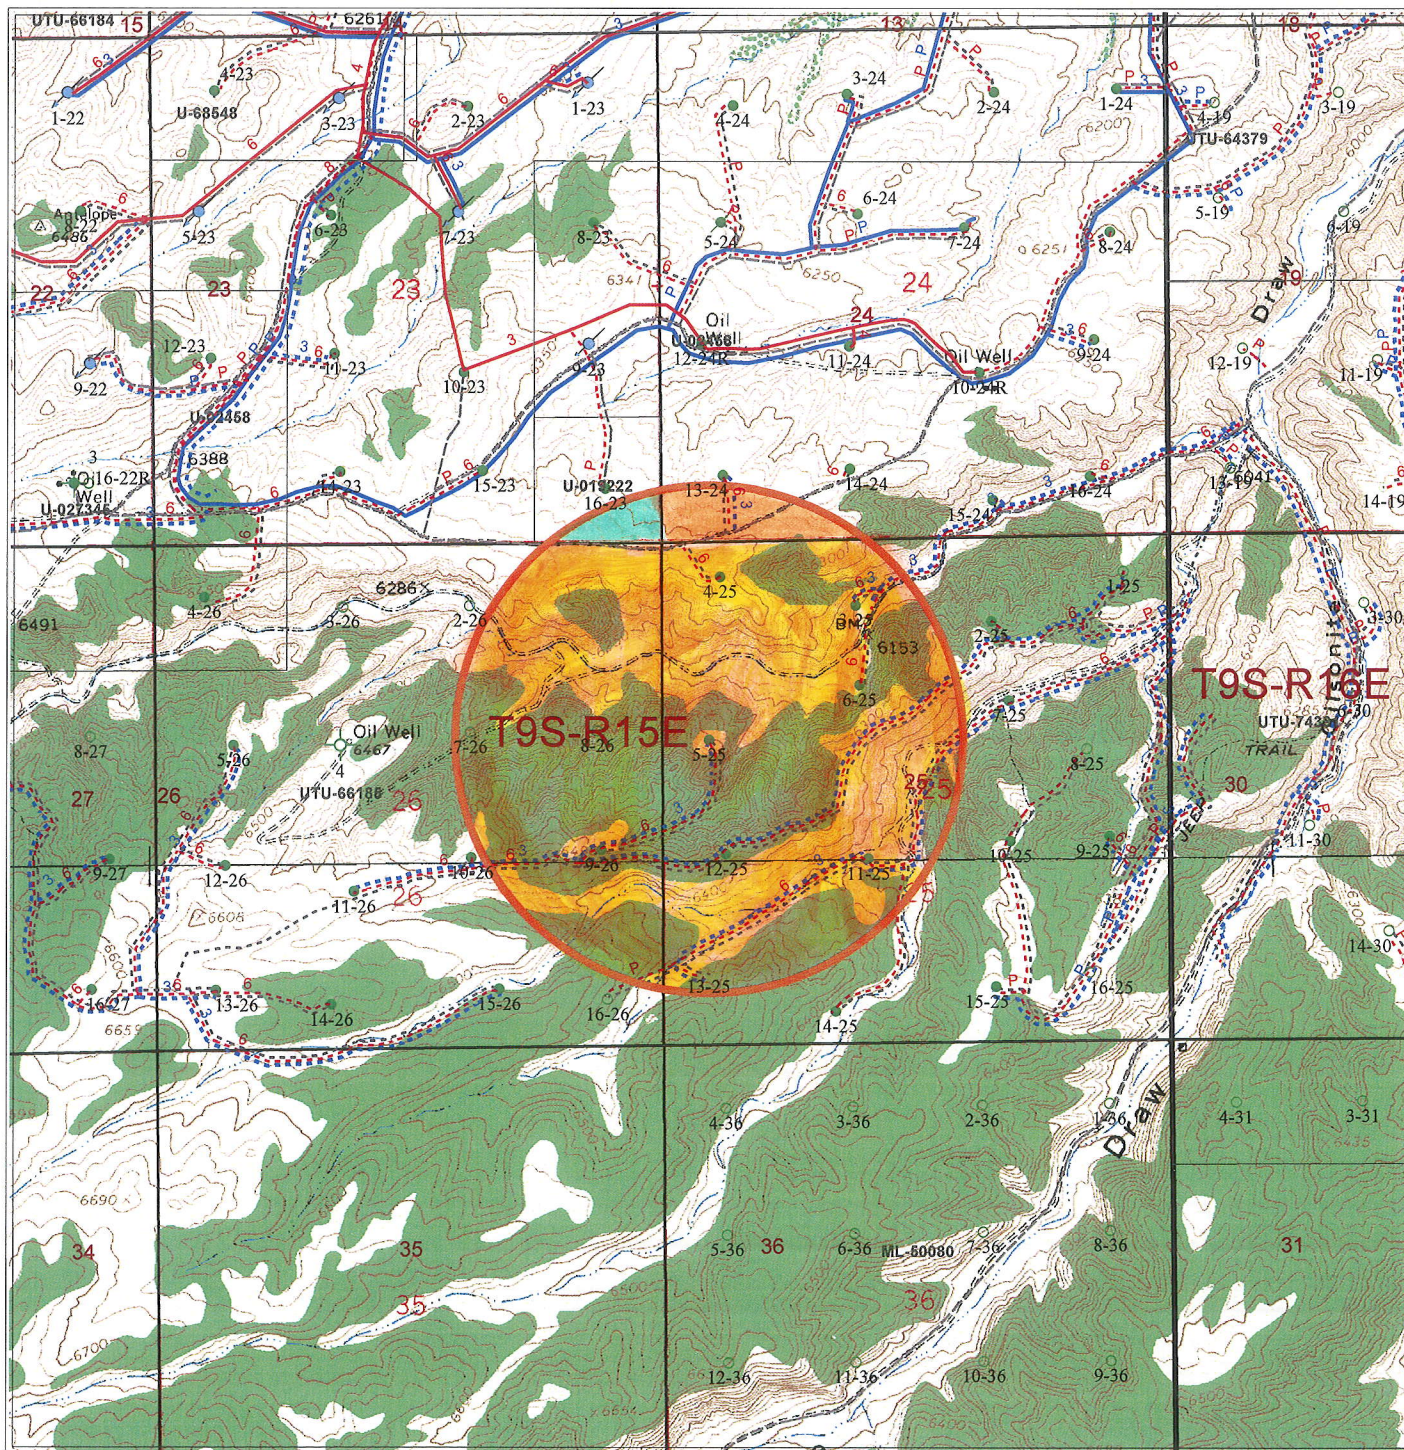

- Well Status**
- Location
 - ⊕ CTI
 - ⊙ Surface Spud
 - ⊙ Drilling
 - ⊙ Waiting on Completion
 - Producing Oil Well
 - ⊙ Producing Gas Well
 - ⊙ Water Injection Well
 - ⊙ Dry Hole
 - ⊙ Temporarily Abandoned
 - ⊙ Plugged & Abandoned
 - ⊙ Shut In
 - Countyline
- Injection system**
- high pressure
 - low pressure
 - proposed
 - return
 - return proposed
- Gas Pipelines**
- Gathering lines
 - Proposed lines
 - Leases
 - 5-25-9-15 1/2mile radius

Attachment A

Ashley 5-25-9-15
Section 25, T9S-R15E

NEWFIELD
ROCKY MOUNTAINS




1/2 Mile Radius Map
Duchesne County

Alamo Plaza Building
1401 17th Street Suite 1000
Denver, Colorado 80202-1247
Phone: (303) 893-0102

February 20, 2007

T9S, R15E, S.L.B.&M.

NEWFIELD PRODUCTION COMPANY

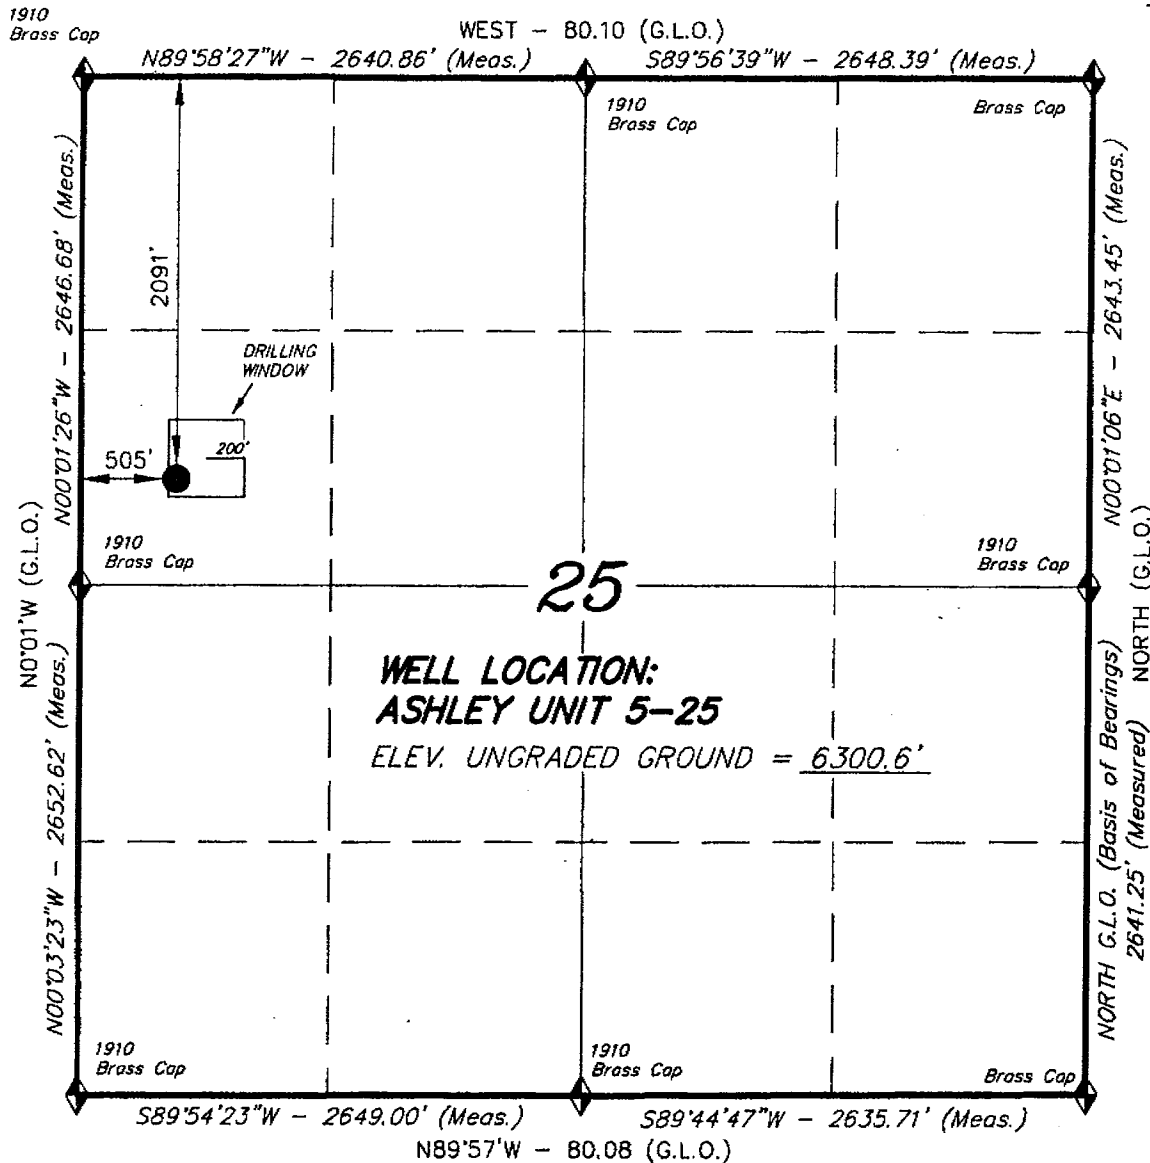


WELL LOCATION, ASHLEY UNIT 5-25,
LOCATED AS SHOWN IN THE SW 1/4 NW
1/4 OF SECTION 25, T9S, R15E,
S.L.B.&M. DUCHESNE COUNTY, UTAH.

Attachment A-1



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
MADE BY ME OR UNDER MY SUPERVISION AND THAT
THE SAME ARE TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF. No. 189377



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; U.S.G.S. 7-1/2 min QUAD (MYTON SW)

TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

SCALE: 1" = 1000'	SURVEYED BY: D.P.
DATE: 7-7-05	DRAWN BY: F.T.M.
NOTES:	FILE #

EXHIBIT B

Page 1

#	Land Description	Minerals Ownership & Expires	Minerals Leased By	Surface Rights
1	<u>Township 9 South, Range 15 East, SLM</u> Section 22: Lots 2, 3, 4, E/2W/2 Section 23: NE/4NE/4, W/2E/2, S/2NW/4, E/2SW/4 Section 24: N/2N/2 Section 25: All Section 26: NE/4, NE/4NW/4, S/2NW/4, S/2 Section 27: Lots 1, 2, S/2NE/4, E/2NW/4, SE/4	UTU-66185 HBP	Newfield Production Company	USA
2	<u>Township 9 South, Range 15 East, SLM</u> Section 23: SE/4SE/4	UTU-019222 HBP	Newfield Production Company	USA


ATTACHMENT C

CERTIFICATION FOR SURFACE OWNER NOTIFICATION

RE: Application for Approval of Class II Injection Well
Ashley Federal #5-25-9-15

I hereby certify that a copy of the injection application has been provided to all surface owners within a one-half mile radius of the proposed injection well.

Signed: _____


Newfield Production Company
David Gerbig
Operations Engineer

Sworn to and subscribed before me this 15 day of January, 2008

Notary Public in and for the State of Colorado: _____



My Commission Expires: _____

05/05/2009

Ashley Federal 5-25-9-15

Spud Date 09/25/2006
Put on Production: 11/27/2006
GL: 6301' KB: 6313'

Wellbore Diagram

Initial Production: BOPD,
MCFD, BWPD

SURFACE CASING

CSG SIZE: 8-5/8"
GRADE: J-55
WEIGHT: 24#
LENGTH: 7 jts. (310.84')
DEPTH LANDED: 322.69' KB
HOLE SIZE: 12-1/4"
CEMENT DATA: 160 sxs Class "G" cmt, est 4.5 bbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
GRADE: J-55
WEIGHT: 15.5#
LENGTH: 131 jts. (5801.70')
DEPTH LANDED: 5800.95' KB
HOLE SIZE: 7-7/8"
CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ.

TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55
NO. OF JOINTS: 168 jts (5186.57')
TUBING ANCHOR: 5198.57'
NO. OF JOINTS: 1 jts (29.45')
SEATING NIPPLE: 2-7/8" (1.10')
SN LANDED AT: 5230.82'
NO. OF JOINTS: 2 jts (63.00')
TOTAL STRING LENGTH: EOT @ 5295.37'

SUCKER RODS

POLISHED ROD: 1-1/2" x 26'
SUCKER RODS: 1-2' x 3/4" pony rod, 98-3/4" scraped rods, 83-3/4" plain rods, 25-3/4" scraped rods, 6-1 1/2" weight rods, 1-2' x 7/8" pony rod.
PUMP SIZE: CDI 2-1/2" x 1-1/2" x 17" x 21' RHBC MG-3 W/ RD kit
STROKE LENGTH: 86"
PUMP SPEED, 5 SPM:

FRAC JOB

11/10/2006 5228-5244' **Frac LODC sands as follows:**
85862# 20/40 sand in 662 bbls Lightning 17
frac fluid. Treated @ avg press of 230 psi
w/avg rate of 25.5 BPM. ISIP 2680 psi. Calc
flush: 5226 gal. Actual flush: 4809 gal.

9-6-07 Pump change. Updated rod & tubing details.

Cement Top @ 1320'

Anchor @ 5199'

5228-5244'

SN @ 5231'

EOT @ 5295'

PBTD @ 5733'

SHOE @ 5801'

TD @ 5830'

PERFORATION RECORD

10-31-06 5686-5706' 4 JSPP 64 holes

NEWFIELD**Ashley Federal 5-25-9-15**

2091' FNL & 505' FWL

SW/NW Section 25-T9S-R15E

Duchesne Co, Utah

API #43-013-32885; Lease #UTU-66185

Ashley Federal 13-24-9-15

Spud Date: 07/09/06
Put on Production: 08/14/06

K.B.: 6343, G.L.: 6331

SURFACE CASING

CSG SIZE: 8-5/8"
GRADE: J-55
WEIGHT: 24#
LENGTH: 7 jts. (310.53')
DEPTH LANDED: 322.38' KB
HOLE SIZE: 12-1/4"
CEMENT DATA: 160 sxs Class "G" cmt, est 4 bbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
GRADE: J-55
WEIGHT: 15.5#
LENGTH: 136 jts. (5936.81')
DEPTH LANDED: 5950.06' KB
HOLE SIZE: 7-7/8"
CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ.
CEMENT TOP: 350'


TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55 / 6.5#
NO. OF JOINTS: 181 jts (5731.12')
TUBING ANCHOR: 5743.12' KB
NO. OF JOINTS: 1 jts (31.58')
SEATING NIPPLE: 2-7/8" (1.10')
SN LANDED AT: 5777.60' KB
NO. OF JOINTS: 2 jts (63.14')
TOTAL STRING LENGTH: EOT @ 5842.29' KB

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM
SUCKER RODS: 1-2, 1-6' x 3/4" pony rod, 100-3/4" guided rods, 114-3/4" plain rods, 10-3/4" scraped rods, 6-1 1/2" weight rods.
PUMP SIZE: 2-1/2" x 1-1/2" 12 x 14' RHAC w/SM plunger
STROKE LENGTH: 86"
PUMP SPEED, 5.5 SPM:

Wellbore Diagram

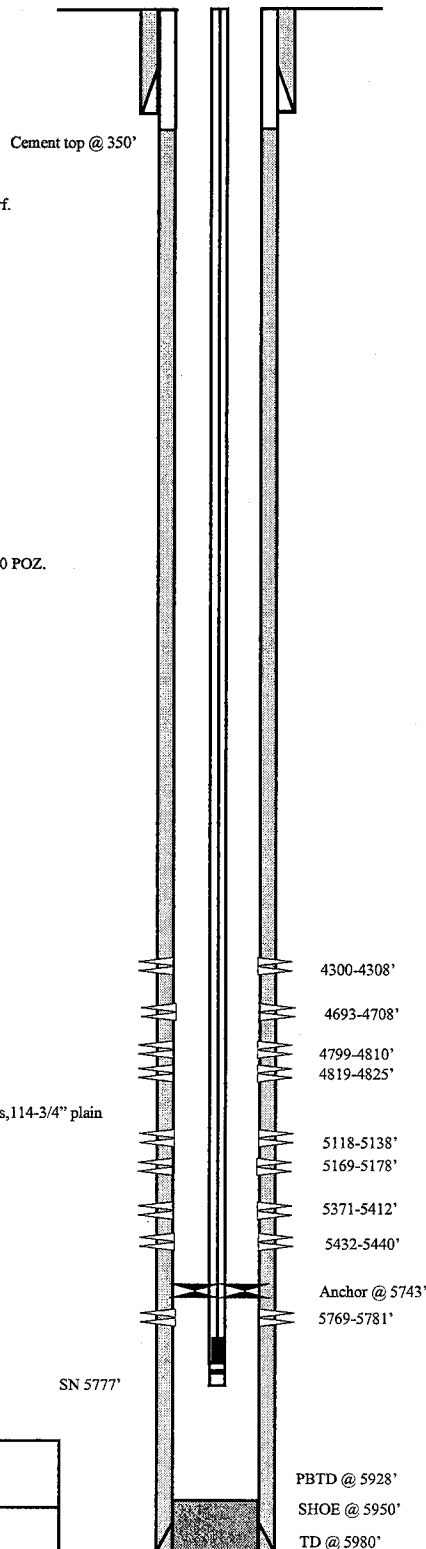

Initial Production: BOPD,
MCFD, BWPD

FRAC JOB

08/08/06 5769-5781' **Frac CP5, sands as follows:**
35142# 20/40 sand in 399 bbls Lightning 17 frac fluid. Treated @ avg press of 2320 psi w/avg rate of 25.1 BPM. ISIP 2425 psi. Calc flush: 5779 gal. Actual flush: 5254 gal.

08/08/06 5371-5440' **Frac CP1, LODC sands as follows:**
147433# 20/40 sand in 998 bbls Lightning 17 frac fluid. Treated @ avg press of 1835 psi w/avg rate of 225 BPM. ISIP 2075 psi. Calc flush: 5438 gal. Actual flush: 4880 gal.

08/08/06 5118-5178' **Frac LODC sands as follows:**
80602# 20/40 sand in 644 bbls Lightning 17 frac fluid. Treated @ avg press of 2500 psi w/avg rate of 24.9 BPM. ISIP 2875 psi. Calc flush: 5176 gal. Actual flush: 4591 gal.


08/09/06 4799-4825' **Frac B2 sands as follows:**
45410# 20/40 sand in 519 bbls Lightning 17 frac fluid. Treated @ avg press of 1710 psi w/avg rate of 25.1 BPM. ISIP 1750 psi. Calc flush: 4823 gal. Actual flush: 4322 gal.

08/09/06 4693-4708' **Frac C sands as follows:**
45123# 20/40 sand in 520 bbls Lightning 17 frac fluid. Treated @ avg press of 2040 psi w/avg rate of 25.2 BPM. ISIP 1975 psi. Calc flush: 4706 gal. Actual flush: 4183 gal.

08/09/06 4300-4308' **Frac PB10 sands as follows:**
30040# 20/40 sand in 334 bbls Lightning 17 frac fluid. Treated @ avg press of 2200 psi w/avg rate of 25 BPM. ISIP 1950 psi. Calc flush: 4306 gal. Actual flush: 4217 gal.

PERFORATION RECORD

Date	Interval	Tool	Holes
07/31/06	5769-5781'	4 JSPF	48 holes
08/08/06	5432-5440'	4 JSPF	32 holes
08/08/06	5371-5412'	2 JSPF	82 holes
08/08/06	5169-5178'	4 JSPF	36 holes
08/08/06	5118-5138'	4 JSPF	80 holes
08/08/06	4819-4825'	4 JSPF	24 holes
08/08/06	4799-4810'	4 JSPF	44 holes
08/09/06	4693-4708'	4 JSPF	60 holes
08/09/06	4300-4308'	4 JSPF	32 holes


Ashley Federal 13-24-9-15 600' FSL & 660' FWL SW/SW Section 24-T9S-R15E Duchesne Co, Utah API #43-013-32820; Lease #UTU-02458

Ashley Federal 4-25-9-15

Spud Date: 06/22/06
 Put on Production: 07/28/06
 K.B.: 6379, G.L.: 6367

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 7 jts. (310.94')
 DEPTH LANDED: 322.79' KB
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 160 sxs Class "G" cmt, est 5 bbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 134 jts. (5869.18')
 DEPTH LANDED: 5882.43' KB
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ.


TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55 / 6.5#
 NO. OF JOINTS: 168 jts (5294.69')
 Prk (3.08 @ 5306.65)
 NO. OF JOINTS: 1 jts(31.49)
 TUBING ANCHOR: 5341.24' KB
 NO. OF JOINTS: 2 jts (63.12')
 SEATING NIPPLE: 2-7/8" (1.10')
 SN LANDED AT: 5407.16' KB
 NO. OF JOINTS: 2 jts (63.10')
 TOTAL STRING LENGTH: EOT @ 5471.81' KB

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM
 SUCKER RODS: 1-4', 6' x 3/4" pony rods, 99-3/4" scraped rods, 59-3/4" plain rods, 50-3/4" scraped rods, 6-1 1/2" weight rods.
 PUMP SIZE: 2-1/2" x 1-1/2" x 17' RTBC w/ballknocker
 STROKE LENGTH: 82"
 PUMP SPEED, 5 SPM:

Wellbore Diagram

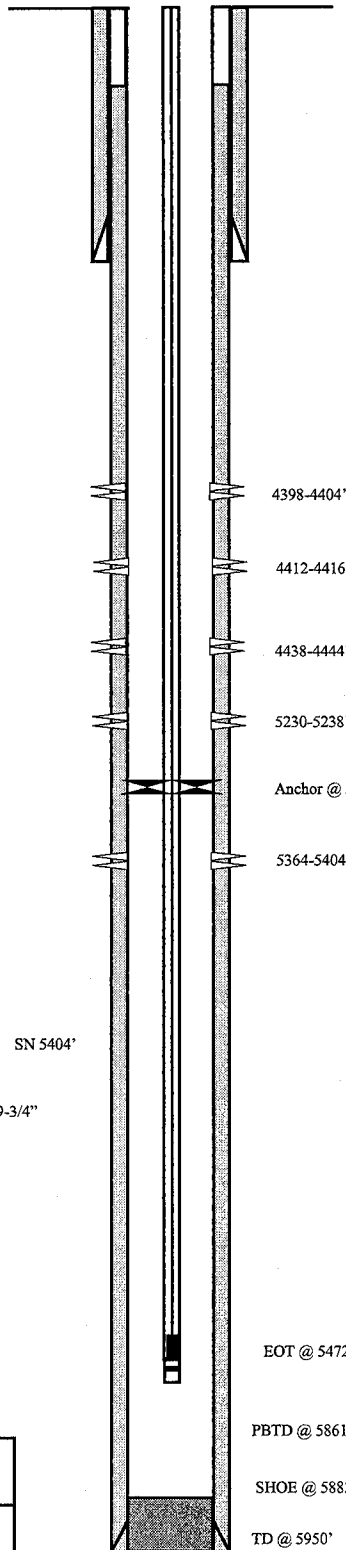FRAC JOB

07/24/06	5364-5404'	Frac LODC sands as follows: 168996# 20/40 sand in 1145 bbls Lightning 17 frac fluid. Treated @ avg press of 2069 psi w/avg rate of 24.8 BPM. ISIP 2260 psi. Calc flush: 5402 gal. Actual flush: 4876 gal.
07/24/06	4398-4444'	Frac DS1, DS2 sands as follows: 39568# 20/40 sand in 421 bbls Lightning 17 frac fluid. Treated @ avg press of 1718 psi w/avg rate of 24.8 BPM. ISIP 1640 psi. Calc flush: 4442 gal. Actual flush: 4284 gal.
06/22/07	Workover	Rod & Tubing detail updated.

PERFORATION RECORD

07/18/06	5364-5404'	2 JSPF	80 holes
07/24/06	5230-5238'	4 JSPF	32 holes
07/24/06	4438-4444'	4 JSPF	24 holes
07/24/06	4412-4416'	4 JSPF	16 holes
07/24/06	4398-4404'	4 JSPF	24 holes

NEWFIELD**Ashley Federal 4-25-9-15**

394' FNL & 624' FWL

NW/NW Section 25-T9S-R15E

Duchesne Co, Utah

API #43-013-32884; Lease #UTU-

Ashley Federal 3-25-9-15

Spud Date: 9-21-06
 Put on Production: 11-01-06
 GL: 6146' KB: 6158'

Initial Production: BOPD,
 MCFD, BWPD

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 7 jts (311-28')
 DEPTH LANDED: 323.13' KB
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 160 sxs Class "G" cmt, est 4 bbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 135 jts. (5749.95')
 DEPTH LANDED: 5763.2' KB
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 330 sxs Prem. Lite II mixed & 400 sxs 50/50 POZ.
 CEMENT TOP AT: 9'

TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55 / 6.5#
 NO. OF JOINTS: 157 jts (4958.81')
 TUBING ANCHOR: 4970.81' KB
 NO. OF JOINTS: 1 jts (31.60')
 SEATING NIPPLE: 2-7/8" (1.10')
 SN LANDED AT: 5005.21' KB
 NO. OF JOINTS: 2 jts (63.12')
 TOTAL STRING LENGTH: EOT @ 5069.88' KB

SUCKER RODS


POLISHED ROD: 1-1/2" x 22' SM
 SUCKER RODS: 1-8', & 1-2' X 3/4" pony rods, 99- 3/4" scraped rods, 84- 3/4" plain rods, 10- 3/4" scraped rods, 6- 1 1/2" weight rods.
 PUMP SIZE: 2-1/2" x 1-1/2" x 16' RHAC w/SM plunger
 STROKE LENGTH: 86"
 PUMP SPEED, SPM: 5 SPM

FRAC JOB

10-25-06	4982-4993'	Frac lodc sands as follows: 59272# 20/40 sand in 475 bbls Lightning 17 frac fluid. Treated @ avg press of 2510 psi w/avg rate of 26.9 BPM. ISIP 2680 psi. Calc flush: 4494 gal. Actual flush: 4980 gal.
10-25-06	4701-4708'	Frac A1 sands as follows: 29486# 20/40 sand in 346 bbls Lightning 17 frac fluid. Treated @ avg press of 2635 psi w/avg rate of 24.9 BPM. ISIP 2700 psi. Calc flush: 4200 gal. Actual flush: 4699 gal.
10-25-06	4584-4591'	Frac B2 sands as follows: 34746# 20/40 sand in 377 bbls Lightning 17 frac fluid. Treated @ avg press of 2050 psi w/avg rate of 25 BPM. ISIP 2025 psi. Calc flush: 4116 gal. Actual flush: 4582 gal.
10-25-06	4472-4488'	Frac C sands as follows: 37000# 20/40 sand in 402 bbls Lightning 17 frac fluid. Treated @ avg press of 2325 w/ avg rate of 24.9 BPM. ISIP 2370 psi. Calc flush: 4368 gal. Actual flush: 4470 gal.

PERFORATION RECORD

10-18-06	4982-4993'	4 JSPF	44 holes
10-25-06	4701-4708'	4 JSPF	28 holes
10-25-06	4584-4591'	4 JSPF	28 holes
10-25-06	4472-4488'	4 JSPF	64 holes

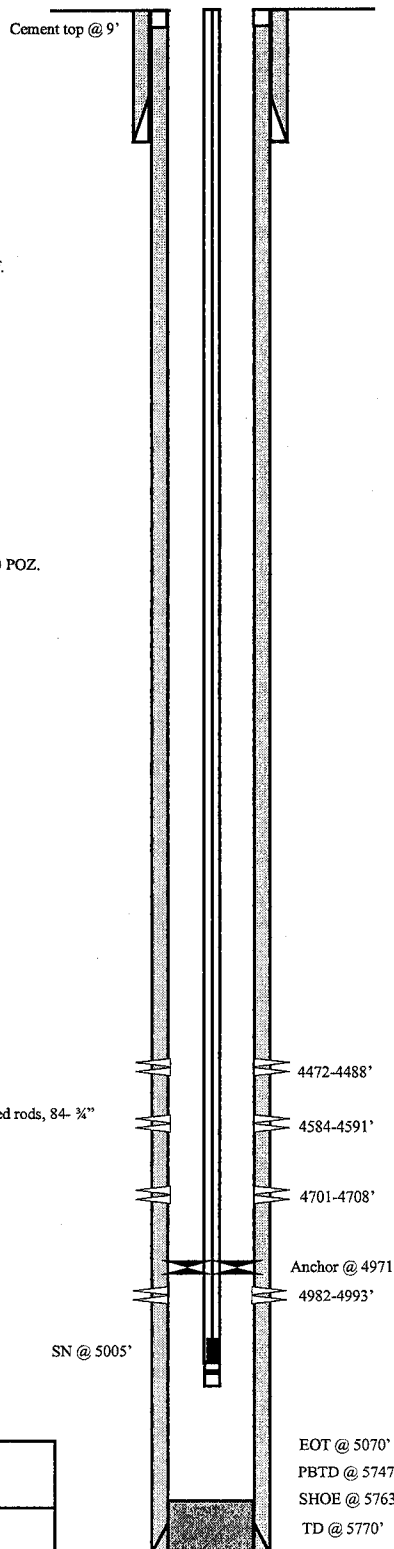

Ashley Federal 3-25-9-15

716' FNL & 2029' FWL

NE/NW Section 25-T9S-R15E

Duchesne Co, Utah

API # 43-013-32945; Lease # UTU-66185

Ashley Federal 6-25-9-15

Spud Date: 09/22/06
Put on Production: 11/07/06
K.B.: 6188, G.L.: 6176

SURFACE CASING

CSG SIZE: 8-5/8"
GRADE: J-55
WEIGHT: 24#
LENGTH: 7 jts. (310.92')
DEPTH LANDED: 322.77' KB
HOLE SIZE: 12-1/4"
CEMENT DATA: 160 sxs Class "G" cmt, est 5 bbls cmt to surf.

PRODUCTION CASING


CSG SIZE: 5-1/2"
GRADE: J-55
WEIGHT: 15.5#
LENGTH: 129 jts. (5671.28')
DEPTH LANDED: 5684.53' KB
HOLE SIZE: 7-7/8"
CEMENT DATA: 330 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ.

TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55 / 6.5#
NO. OF JOINTS: 164 jts (5173.46')
TUBING ANCHOR: 5185.46' KB
NO. OF JOINTS: 1 jts (31.60')
SEATING NIPPLE: 2-7/8" (1.10')
SN LANDED AT: 5219.86' KB
NO. OF JOINTS: 2 jts (62.97')
TOTAL STRING LENGTH: EOT @ 5284.38' KB

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM
SUCKER RODS: 1-8", 1-6", 1-2" x 3/4" pony rod, 100-3/4" guided rods, 92-3/4" plain rods, 10-3/4" scraped rods, 6-1 1/2" weight rods.
PUMP SIZE: 2-1/2" x 1-1/2" x 15' RHAC w/SM plunger
STROKE LENGTH: 86"
PUMP SPEED, 5 SPM:

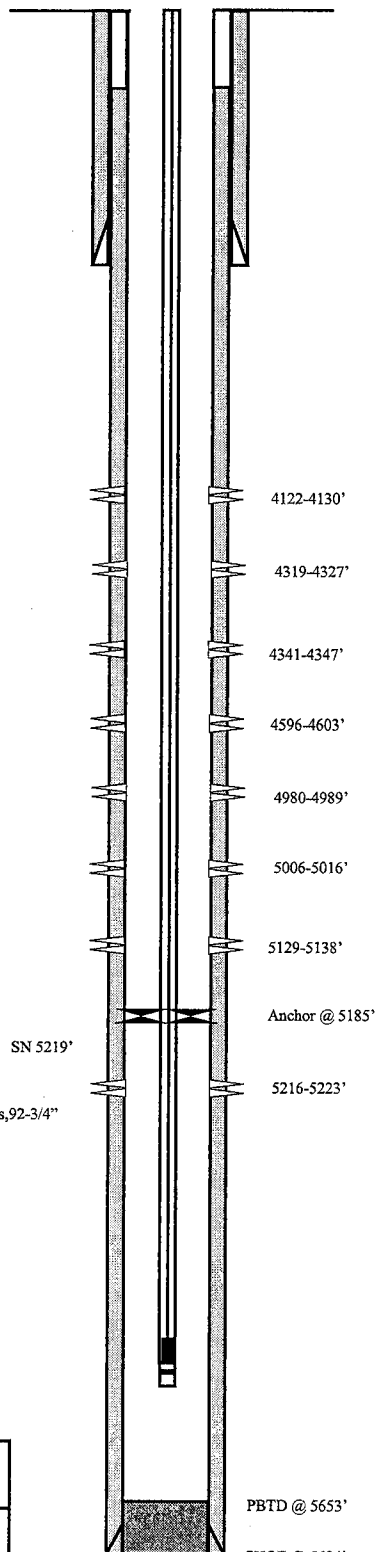Wellbore Diagram

Initial Production: BOPD,
MCFD, BWPD

FRAC JOB

10/30/06 5216-5223' **Frac CP.5 sands as follows:**
24055# 20/40 sand in 329 bbls Lightning 17 frac fluid. Treated @ avg press of 2255 psi w/avg rate 24.8 BPM. ISIP 2010 psi. Calc flush: 5221 gal. Actual flush: 5082 gal.

10/30/06 4980-5138' **Frac LODC sands as follows:**
75092# 20/40 sand in 567 bbls Lightning 17 frac fluid. Treated @ avg press of 2545 psi w/avg rate of 26.7 BPM. ISIP 2010 psi. Calc flush: 5136 gal. Actual flush: 4452 gal.

10/30/06 4596-4603' **Frac B2 sands as follows:**
24277# 20/40 sand in 324 bbls Lightning 17 frac fluid. Treated @ avg press of 2345 psi w/avg rate of 24.9 BPM. ISIP 2080 psi. Calc flush: 4601 gal. Actual flush: 4116 gal.

10/30/06 4319-4347' **Frac D2 sands as follows:**
27462# 20/40 sand in 335 bbls Lightning 17 frac fluid. Treated @ avg press of 2065 psi w/avg rate of 24.9 BPM. ISIP 2050 psi. Calc flush: 4345 gal. Actual flush: 3822 gal.

10/30/06 4122-4130' **Frac PB11 sands as follows:**
30307# 20/40 sand in 331 bbls Lightning 17 frac fluid. Treated @ avg press of 2950 psi w/avg rate 8.25 BPM. ISIP psi. Calc flush: 4128 gal. Actual flush: 4032 gal.

PERFORATION RECORD

Date	Interval	Tool	Holes
10/24/06	5216-5223'	7 JSPF	28 holes
10/24/06	5129-5138'	9 JSPF	36 holes
10/30/06	5006-5016'	4 JSPF	40 holes
10/30/06	4980-4989'	4 JSPF	36 holes
10/30/06	4596-4603'	4 JSPF	28 holes
10/30/06	4341-4347'	4 JSPF	24 holes
10/30/06	4319-4327'	4 JSPF	32 holes
10/30/06	4122-4130'	4 JSPF	32 holes

NEWFIELD**Ashley Federal 6-25-9-15**

1546' FNL & 2069' FWL
SE/NW Section 25-T9S-R15E
Duchesne Co, Utah
API #43-013-32946; Lease #UTU-66185

Ashley Federal 9-26-9-15

Spud Date: 9/26/06
Put on Production: 11/15/06
K.B.: 6483, G.L.: 6471

SURFACE CASING

CSG SIZE: 8-5/8"
GRADE: J-55
WEIGHT: 24#
LENGTH: 7 jts. (310.84')
DEPTH LANDED: 322.69' KB
HOLE SIZE: 12-1/4"
CEMENT DATA: 160 sxs Class "G" cmt, est 2 bbls cmt to surf.

PRODUCTION CASING


CSG SIZE: 5-1/2"
GRADE: J-55
WEIGHT: 15.5#
LENGTH: 135 jts. (5913.65')
DEPTH LANDED: 5926.90' KB
HOLE SIZE: 7-7/8"
CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ.

TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55 / 6.5#
NO. OF JOINTS: 175 jts (5385.93')
TUBING ANCHOR: 5397.93' KB
NO. OF JOINTS: 3 jts (92.75')
SEATING NIPPLE: 2-7/8" (1.10')
SN LANDED AT: 5493.48' KB
NO. OF JOINTS: 2 jts (63.26')
TOTAL STRING LENGTH: EOT @ 5558.07' KB

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM
SUCKER RODS: 2' x 3/4" pony rod, 99-3/4" guided rods, 104-3/4" plain rods,
10-3/4" scraped rods, 6-1 1/2" weight rods.
PUMP SIZE: 2-1/2" x 1-1/2" x 14" RHAC w/SM plunger
STROKE LENGTH: 86"
PUMP SPEED, 6 SPM:

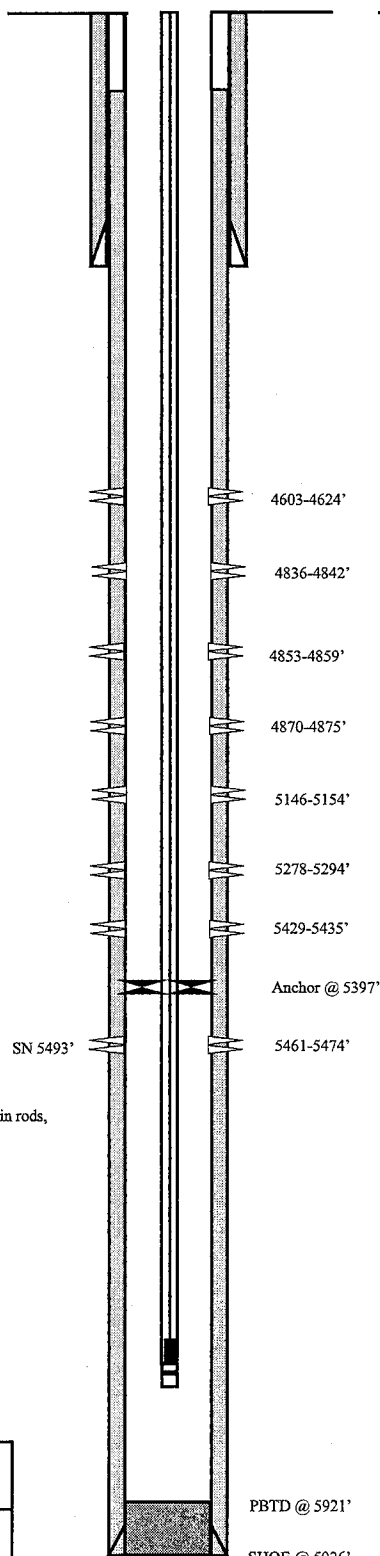Wellbore Diagram**FRAC JOB**

11/01/06	5429-5474'	Frac CP2, CP3 sands as follows: 29378# 20/40 sand in 365 bbls Lightning 17 frac fluid. Treated @ avg press of 2035 psi w/avg rate of 24.9 BPM. ISIP 2200 psi. Calc flush: 5472 gal. Actual flush: 4922 gal.
11/01/06	5278-5294'	Frac LODC sands as follows: 50541# 20/40 sand in 427 bbls Lightning 17 frac fluid. Treated @ avg press of 2425 psi w/avg rate of 24.7 BPM. 3060 psi. Calc flush: 5292 gal. Actual flush: 4771 gal.
11/01/06	5146-5154'	Frac LODC sands as follows: 19886# 20/40 sand in 380 bbls Lightning 17 frac fluid. Treated @ avg press of 2342 psi w/avg rate of 20.2 BPM. ISIP 2700 psi. Calc flush: 5152 gal. Actual flush: 4637 gal.
11/02/06	4836-4875'	Frac A1 sands as follows: 60108# 20/40 sand in 474 bbls Lightning 17 frac fluid. Treated @ avg press of 2160 psi w/avg rate of 25.3 BPM. ISIP 2270 psi. Calc flush: 4873 gal. Actual flush: 4330 gal.
11/01/06	4603-4624'	Frac B.5 sands as follows: 103709# 20/40 sand in 774 bbls Lightning 17 frac fluid. Treated @ avg press of 1940 psi w/avg rate of 25.4 BPM. ISIP 1900 psi. Calc flush: 4622 gal. Actual flush: 4494 gal.

PERFORATION RECORD

10/26/06	5461-5474'	13 JSPF	52 holes
10/26/06	5429-5435'	4 JSPF	24 holes
11/01/06	5278-5294'	4 JSPF	64 holes
11/01/06	5146-5154'	4 JSPF	32 holes
11/01/06	4870-4875'	4 JSPF	20 holes
11/01/06	4853-4859'	4 JSPF	24 holes
11/01/06	4836-4842'	4 JSPF	24 holes
11/02/06	4603-4624'	4 JSPF	84 holes

NEWFIELD**Ashley Federal 9-26-9-15**

2042' FSL & 618' FEL

NE/SE Section 26-T9S-R15E

Duchesne Co, Utah

API #43-013-32902; Lease #UTU-66185

Ashley Federal 12-25-9-15

Spud Date: 09/28/06
 Put on Production: 01/03/07
 K.B.: 6429, G.L.: 6417

Wellbore Diagram

Initial Production: BOPD,
 MCFD, BWPD

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 7 jts. (310.60')
 DEPTH LANDED: 322.45' KB
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 160 sxs Class "G" cmt, est 6 bbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 134 jts. (5888.20')
 DEPTH LANDED: 5887.45' KB
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ.

TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55
 NO. OF JOINTS: 161 jts (5049.48')
 TUBING ANCHOR: 2.80' 5061.48'
 NO. OF JOINTS: 3 jts (94.77')
 SEATING NIPPLE: 1.10
 SN LANDED AT: (5159.05')
 NO. OF JOINTS: 2 jts (63.35')
 TOTAL STRING LENGTH: EOT @ 5223.95'

SUCKER RODS

POLISHED ROD: 1-1/2" x 22'
 SUCKER RODS: 1- 2', 1-6' x 3/4" pony rod, 100-3/4" scraped rods, 89-3/4" plain rods, 10-3/4" scraped rods, 6-1 1/2" weight rods.
 PUMP SIZE: 2-1/2" x 1-1/2" x 15 1/2" RHAC pump rod pump
 STROKE LENGTH: 86"
 PUMP SPEED: 5 SPM


FRAC JOB

12/21/06 5290-5308' **Frac LODC sands as follows:**
 97293# 20/40 sand in 739 bbls Lightning 17 frac fluid. Treated @ avg press of 2215 psi w/avg rate of 25 BPM. ISIP 2480 psi. Calc flush: 5306 gal. Actual flush: 5166 gal.

02/19/07
 02/20/07 5124-5132' **Recompletion**
Frac LODC sands as follows:
 35230# 20/40 sand in 381 bbls Lightning 17 frac fluid. Treated @ avg press of 2771 psi w/avg rate of 21.0 BPM. ISIP 2640 psi. Calc flush: 5122 gal. Actual flush: 4536 gal.

02/21/07 4526-4484' **Frac D1 & D2 sands as follows:**
 45412# 20/40 sand in 405 bbls Lightning 17 frac fluid. Treated @ avg press of 1817 psi w/avg rate of 24.3 BPM. ISIP 1805 psi. Calc flush: 4524 gal. Actual flush: 4368 gal.

7/13/07 Pump change. Updated Tubing & Rod detail.

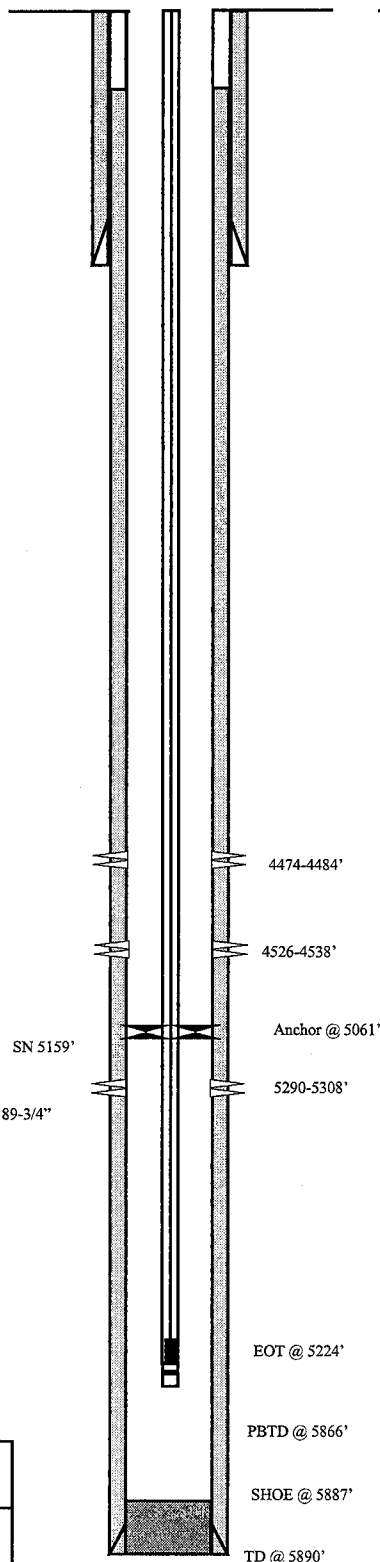PERFORATION RECORD

Date	Interval	Tool	Holes
12/15/06	5290-5308'	4 JSPF	72 holes
02/20/07	5124-5132'	4 JSPF	32 holes
02/20/07	4526-4538'	4 JSPF	48 holes
02/20/07	4474-4484'	4 JSPF	40 holes

NEWFIELD

Ashley Federal 12-25-9-15

1985' FSL & 676' FWL

NW/SW Section 25-T9S-R15E

Duchesne Co, Utah

API #43-013-32886; Lease #UTU-66185

Ashley Federal 11-25-9-15

Spud Date: 10/25/2006

Put on Production:

GL: 6269' KB: 6281'

Wellbore Diagram

Initial Production: BOPD,
MCFD, BWPDSURFACE CASING

CSG SIZE: 8-5/8"

GRADE: J-55

WEIGHT: 24#

LENGTH: 7 jts. (311.00')

DEPTH LANDED: 322.85' KB

HOLE SIZE: 12-1/4"

CEMENT DATA: 160 sxs Class "G" cmt, est 5 bbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"

GRADE: J-55

WEIGHT: 15.5#

LENGTH: 129 jts. (5687.01')

DEPTH LANDED: 5700.26' KB

HOLE SIZE: 7-7/8"

CEMENT DATA: 300 sxs Prem. Lite II mixed & 475 sxs 50/50 POZ.

TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55 / 6.5#

NO. OF JOINTS: 171 jts (5373.82')

TUBING ANCHOR: 5385.82' KB

NO. OF JOINTS: 2 jts (63.21')

SEATING NIPPLE: 2-7/8" (1.10')

SN LANDED AT: 5451.83' KB

NO. OF JOINTS: 2 jts (60.46')

TOTAL STRING LENGTH: EOT @ 5513.84' KB

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM

SUCKER RODS: 4'-6" & -8' x 3/4" pony rod, 99-3/4" scraped rods, 101-3/4" slick rods, 10-3/4" scraped rods, 6-1 1/2" weight rods.

PUMP SIZE: CDI 2-1/2" x 1-1/2" x 12x15' RHAC

STROKE LENGTH: 84"


PUMP SPEED, 6 SPM:

FRAC JOB

11/27/06	5399-5436'	Frac CP2 sands as follows: 34,663# 20/40 sand in 403 bbls Lightning 17 frac fluid. Treated @ avg press of 2420 psi w/avg rate of 24.8 BPM. ISIP 2350 psi. Calc flush: 5397 gal. Actual flush: 4872 gal.
11/27/06	5152-5159'	Frac LODC sands as follows: 24,486# 20/40 sand in 333 bbls Lightning 17 frac fluid. Treated @ avg press of 2635 psi w/avg rate of 25 BPM. ISIP 2450 psi. Calc flush: 5150 gal. Actual flush: 4662 gal.
11/27/06	5034-5044'	Frac LODC sands as follows: 24,788# 20/40 sand in 332 bbls Lightning 17 frac fluid. Treated @ avg press of 2420 psi w/avg rate of 25 BPM. ISIP 2380 psi. Calc flush: 5032 gal. Actual flush: 4536 gal.
11/27/06	4910-4936'	Frac LODC sands as follows: 40,879# 20/40 sand in 387 bbls Lightning 17 frac fluid. Treated @ avg press of 2585 psi w/avg rate of 27 BPM. ISIP 2500 psi. Calc flush: 4908 gal. Actual flush: 4410 gal.
11/27/06	4694-4701'	Frac A5 sands as follows: 19,469# 20/40 sand in 282 bbls Lightning 17 frac fluid. Treated @ avg press of 2315 psi w/avg rate of 25.1 BPM. ISIP 2130 psi. Calc flush: 4692 gal. Actual flush: 4200 gal.
11/27/06	4491-4498'	Frac B.5 sands as follows: 20,982# 20/40 sand in 287 bbls Lightning 17 frac fluid. Treated @ avg press of 2525 psi w/avg rate of 24.9 BPM. ISIP psi. Calc flush: 4489 gal. Actual flush: 33 bbl short gal.

PERFORATION RECORD

11/27/06	5428-5436'	4 JSPF	32 holes
11/27/06	5399-5407'	4 JSPF	32 holes
11/27/06	5152-5159'	4 JSPF	28 holes
11/27/06	5034-5044'	4 JSPF	40 holes
11/27/06	4910-4936'	4 JSPF	104 holes
11/27/06	4694-4701'	4 JSPF	28 holes
11/27/06	4491-4498'	4 JSPF	28 holes

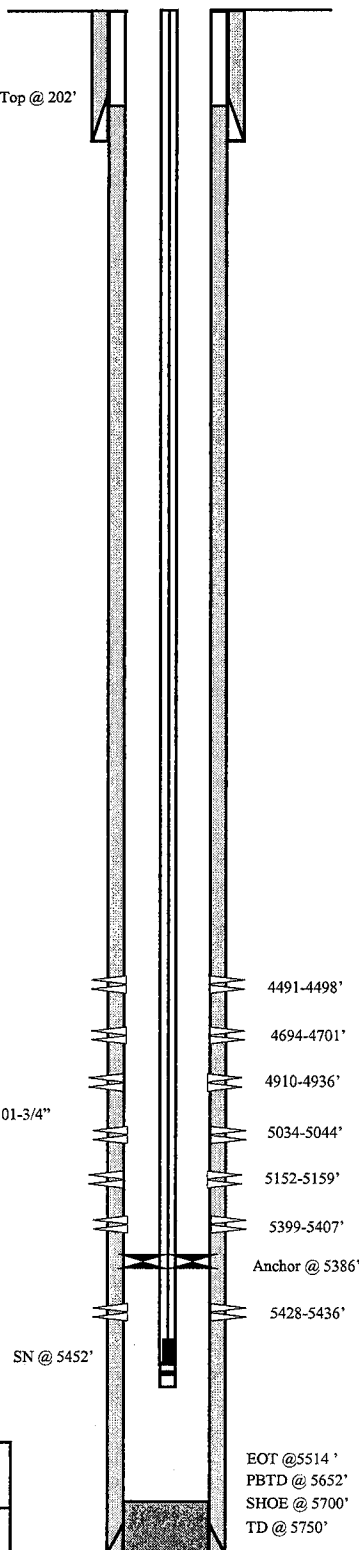**NEWFIELD****Ashley Federal 11-25-9-15**

1916' FSL & 2154' FWL

NE/SW Section 25-T9S-R15E

Duchesne Co, Utah

API #43-013-32910; Lease #UTU-66185

Ashley Federal 13-25-9-15

Spud Date: 10/27/2006

Put on Production:

GL: 6379' KB: 6391'

Wellbore Diagram

Initial Production: BOPD,
MCFD, BWPD

FRAC JOB

Waiting on approval to be completed as injector.

SURFACE CASING

CSG SIZE: 8-5/8"

GRADE: J-55

WEIGHT: 24#

LENGTH: 7 jts. (312.73')

DEPTH LANDED: 323.63' KB

HOLE SIZE: 12-1/4"

CEMENT DATA: 160 sxs Class "G" cmt, est 6 bbbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"

GRADE: J-55

WEIGHT: 15.5#

LENGTH: 131 jts. (5769.86')

DEPTH LANDED: 5783.11' KB

HOLE SIZE: 7-7/8"

CEMENT DATA: 350 sxs Prem. Lite II mixed & 475 sxs 50/50 POZ.

TUBING

SIZE/GRADE/WT.: 2-7/8" / J-55 / 6.5#

NO. OF JOINTS: jts

TUBING ANCHOR: KB

NO. OF JOINTS: jts)

SEATING NIPPLE: 2-7/8" (1.10')

SN LANDED AT: KB

NO. OF JOINTS: jts

TOTAL STRING LENGTH: EOT @

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM

SUCKER RODS:

PUMP SIZE:

STROKE LENGTH:

PUMP SPEED,

SN @ 5566'

Anchor @

PERFORATION RECORDEOT @
PBTD @ 5684'
SHOE @ 5783'
TD @ 5800'**NEWFIELD****Ashley Federal 13-25-9-15**

761' FSL & 488' FWL

SW/SW Section 25-T9S-R15E

Duchesne Co, Utah

API #43-013-32911; Lease #UTU-66185

Water Analysis Report from Baker Petrolite

<i>Summary of Mixing Waters</i>		
Sample Number	389461	384235
Company	NEWFIELD EXPLORATION	NEWFIELD EXPLORATION
Lease	JOHNSON WATER	ASHLEY FACILITY
Well	PUMP STATION 2	5-25-9-25
Sample Location	PUMP DISCHARGE	WELLHEAD
Anions (mg/L)		
Chloride	17.0	5,528
Bicarbonate	319	1,891
Carbonate	0.00	250
Sulfate	89.0	771
Phosphate	0.00	0.00
Borate	0.00	0.00
Silicate	0.00	0.00
Cations (mg/L)		
Sodium	85.9	4,517
Magnesium	22.0	17.0
Calcium	40.0	137
Strontium	0.20	6.00
Barium	0.20	0.30
Iron	0.10	136
Potassium	0.20	55.0
Aluminum	0.00	0.00
Chromium	0.00	0.00
Copper	0.00	0.00
Lead	0.00	0.00
Manganese	0.03	3.00
Nickel	0.00	0.00
Anion/Cation Ratio	1.00	1.00
TDS (mg/L)	574	13,312
Density (g/cm)	1.00	1.01
Sampling Date	1/10/07	2/13/07
Account Manager	RANDY HUBER	RANDY HUBER
Analyst	LISA HAMILTON	LISA HAMILTON
Analysis Date	1/17/07	1/26/07
pH at time of sampling		
pH at time of analysis	8.16	8.78
pH used in Calculations	8.16	8.78

Water Analysis Report from Baker Petrolite

Mixes at 140°F and 0 psi

Predictions of Carbon Dioxide Pressure, Saturation Index and Amount of Scale in lb/1000bbl												
Mix Waters		CO ₂	Calcite CaCO ₃		Gypsum CaSO ₄ •2H ₂ O		Anhydrite CaSO ₄		Celestite SrSO ₄		Barite BaSO ₄	
389461	384235	psi	Index	Amount	Index	Amount	Index	Amount	Index	Amount	Index	Amount
100%	0%	0.09	1.01	16	-1.87		-1.70		-2.39		0.28	0.06
90%	10%	0.06	1.42	31	-1.77		-1.60		-1.77		0.33	0.07
80%	20%	0.07	1.57	44	-1.68		-1.52		-1.50		0.38	0.08
70%	30%	0.09	1.66	54	-1.61		-1.44		-1.33		0.42	0.08
60%	40%	0.11	1.73	64	-1.55		-1.38		-1.21		0.45	0.09
50%	50%	0.13	1.78	73	-1.49		-1.32		-1.11		0.48	0.10
40%	60%	0.15	1.82	82	-1.44		-1.27		-1.03		0.51	0.11
30%	70%	0.18	1.85	90	-1.40		-1.23		-0.96		0.53	0.11
20%	80%	0.20	1.89	99	-1.36		-1.19		-0.90		0.55	0.12
10%	90%	0.23	1.91	107	-1.33		-1.15		-0.84		0.57	0.13
0%	100%	0.25	1.94	116	-1.29		-1.12		-0.79		0.59	0.13

Note 1: The amount of scale indicates the severity of the problem. The saturation index (SI) indicates how difficult it is to control the problem.

Note 2: Precipitation of each scale is considered separately. Total scale will be less than the sum of the amounts of the five scales.

Note 3: The reported CO₂ pressure is the calculated CO₂ fugacity. It is usually nearly the same as the CO₂ partial pressure.

Water Analysis Report by Baker Petrolite

NEWFIELD EXPLORATION

ASHLEY FACILITY
5-25-9-25
WELLHEAD

Account Manager
RANDY HUBER

Summary		Analysis of Sample 384235 @ 75°F					
Sampling Date	2/13/07	Anions	mg/l	meq/l	Cations	mg/l	meq/l
Analysis Date	1/26/07	Chloride	5528	156	Sodium	4517	196
Analyst	LISA HAMILTON	Bicarbonate	1891	31.0	Magnesium	17.0	1.40
		Carbonate	250	8.33	Calcium	137	6.84
TDS (mg/l or g/m ³)	13311.7	Sulfate	771	16.1	Strontium	6.00	0.14
Density (g/cm ³ or tonne/m ³)	1.009	Phosphate	N/A	N/A	Barium	0.30	0.00
Anion/Cation Ratio	1.00	Borate	N/A	N/A	Iron	136	4.87
		Silicate	N/A	N/A	Potassium	55.0	1.41
					Aluminum	N/A	N/A
					Chromium	N/A	N/A
					Copper	N/A	N/A
					Lead	N/A	N/A
		pH at time of sampling			Manganese	3.00	0.11
		pH at time of analysis		8.78	Nickel	N/A	N/A
		pH used in Calculations		8.78			

Specific ion interactions calculated only for ions in bold faced type.

Conditions		Values Calculated at the Given Conditions - Amounts of Scale in lb/1000bbl										
Temp.	Gauge Press.	Calcite CaCO ₃		Gypsum CaSO ₄ •2H ₂ O		Anhydrite CaSO ₄		Celestite SrSO ₄		Barite BaSO ₄		Calc. CO ₂
°F	psi	Index	Amount	Index	Amount	Index	Amount	Index	Amount	Index	Amount	psi
80	0.	2.05	116	-1.28		-1.35		-0.87		0.96	0.16	0.04
100	0.	2.01	116	-1.30		-1.30		-0.85		0.82	0.15	0.07
120	0.	1.97	116	-1.30		-1.22		-0.83		0.69	0.14	0.14
140	0.	1.94	116	-1.29		-1.12		-0.79		0.59	0.13	0.25

Note 1: The amount of scale indicates the severity of the problem. The saturation index (SI) indicates how difficult it is to control the problem.

Note 2: Precipitation of each scale is considered separately. Total scale will be less than the sum of the amounts of the five scales.

Note 3: The reported CO₂ pressure is the calculated CO₂ fugacity. It is usually nearly the same as the CO₂ partial pressure.

Rocky Mountain Region
1675 Broadway, Suite 1500
Denver, CO 80202
(303) 573-2772

Lab Team Leader - Sheila Hernandez
(432) 495-7240

Water Analysis Report by Baker Petrolite

Company:	NEWFIELD EXPLORATION	Sales RDT:	44206
Region:	ROCKY MOUNTAINS	Account Manager:	RANDY HUBER (435) 823-0023
Area:	MYTON, UT	Sample #:	389460
Lease/Platform:	ASHLEY FACILITY	Analysis ID #:	67486
Entity (or well #):	INJECTION SYSTEM	Analysis Cost:	\$80.00
Formation:	UNKNOWN		
Sample Point:	TRIPLEX SUCTION		

Summary		Analysis of Sample 389460 @ 75 °F					
Sampling Date:	1/10/07	Anions	mg/l	meq/l	Cations	mg/l	meq/l
Analysis Date:	1/17/07	Chloride:	797.0	22.48	Sodium:	845.1	36.76
Analyst:	LISA HAMILTON	Bicarbonate:	858.0	14.06	Magnesium:	21.0	1.73
TDS (mg/l or g/m ³):	2790.1	Carbonate:	0.0	0.	Calcium:	45.0	2.25
Density (g/cm ³ , tonne/m ³):	1.001	Sulfate:	214.0	4.46	Strontium:	1.0	0.02
Anion/Cation Ratio:	0.9999998	Phosphate:			Barium:	1.0	0.01
		Borate:			Iron:	2.0	0.07
		Silicate:			Potassium:	6.0	0.15
Carbon Dioxide:		Hydrogen Sulfide:			Aluminum:		
Oxygen:		pH at time of sampling:			Chromium:		
Comments:		pH at time of analysis:		8.06	Copper:		
		pH used in Calculation:		8.06	Lead:		
					Manganese:	0.040	0.
					Nickel:		

Conditions		Values Calculated at the Given Conditions - Amounts of Scale in lb/1000 bbl										
Temp	Gauge Press.	Calcite CaCO ₃		Gypsum CaSO ₄ ·2H ₂ O		Anhydrite CaSO ₄		Celestite SrSO ₄		Barite BaSO ₄		CO ₂ Press
°F	psi	Index	Amount	Index	Amount	Index	Amount	Index	Amount	Index	Amount	psi
80	0	0.90	22.37	-1.77	0.00	-1.84	0.00	-1.69	0.00	1.41	0.70	0.1
100	0	0.97	25.17	-1.78	0.00	-1.78	0.00	-1.68	0.00	1.27	0.70	0.15
120	0	1.04	27.61	-1.77	0.00	-1.70	0.00	-1.65	0.00	1.16	0.70	0.22
140	0	1.12	30.06	-1.76	0.00	-1.60	0.00	-1.61	0.00	1.07	0.70	0.31

Note 1: When assessing the severity of the scale problem, both the saturation index (SI) and amount of scale must be considered.

Note 2: Precipitation of each scale is considered separately. Total scale will be less than the sum of the amounts of the five scales.

Note 3: The reported CO₂ pressure is actually the calculated CO₂ fugacity. It is usually nearly the same as the CO₂ partial pressure.

Attachment "G"

Ashley Federal #5-25-9-15
Proposed Maximum Injection Pressure

Frac Interval (feet)		Avg. Depth (feet)	ISIP (psi)	Calculated Frac Gradient (psi/ft) Minimum	Pmax <u>2646</u> <u>2646</u> ←
Top	Bottom				
5228	5244	5236	2680	0.95	

Calculation of Maximum Surface Injection Pressure

$P_{max} = (\text{Frac Grad} - (0.433 \times 1.015)) \times \text{Depth of Top Perf}$
where pressure gradient for the fresh water is .433 psi/ft and
specific gravity of the injected water is 1.015.

$\text{Frac Gradient} = (\text{ISIP} + (0.433 \times \text{Top Perf.})) / \text{Top Perf.}$

Please note: These are existing perforations; additional perforations may be added during the actual conversion procedure.

NEWFIELD



Attachment G-1
1 of 2

DAILY COMPLETION REPORT

WELL NAME: Ashley Federal 5-25-9-15 Report Date: 11-1-06 Day: 01
Operation: Completion Rig: Rigless

WELL STATUS

Surf Csg: 8-5/8' @ 322' Prod Csg: 5-1/2" @ 5800' Csg PBTD: 5713'WL
Tbg: Size: Wt: Grd: Pkr/EOT @: BP/Sand PBTD:

PERFORATION RECORD

Zone	Perfs	SPF/#shots	Zone	Perfs	SPF/#shots
LODC sds	5228-5244'	4/64			

CHRONOLOGICAL OPERATIONS

Date Work Performed: 31-Oct-06 SITP: SICP: 0

Instal 5M frac head. NU 6" 5M Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head, csg & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 5713' & cement top @ 1320'. Perforate stage #1, LODC sds @ 5228-44' w/ 4" Port guns (19 gram, .46"HE. 120°) w/ 4 spf for total of 64 shots. 136 bbls EWTR. SIFN.

FLUID RECOVERY (BBLs)

Starting fluid load to be recovered: 136 Starting oil rec to date:
Fluid lost/recovered today: 0 Oil lost/recovered today:
Ending fluid to be recovered: 136 Cum oil recovered:
IFL: FFL: FTP: Choke: Final Fluid Rate: Final oil cut:

STIMULATION DETAIL

Base Fluid used: Job Type:
Company:
Procedure or Equipment detail:

COSTS

Weatherford BOP	\$450
NPC NU crew	\$300
NDSI trucking	\$800
Perforators LLC	\$6,312
Drilling cost	\$364,116
NDSI Hot Oil	\$420
Location preparation	\$300
NPC wellhead	\$1,500
Benco - anchors	\$1,200
Admin. Overhead	\$3,000
NPC Supervisor	\$300

Max TP: Max Rate: Total fluid pmpd:
Avg TP: Avg Rate: Total Prop pmpd:
ISIP: 5 min: 10 min: FG:

Completion Supervisor: Ron Shuck

DAILY COST: \$378,698
TOTAL WELL COST: \$378,698

NEWFIELD



Attachment G-1
2 of 2

DAILY COMPLETION REPORT

WELL NAME: Ashley Federal 5-25-9-15

Report Date: 11-11-06

Day: 2

Operation: Completion

Rig: Rigless

WELL STATUS

Surf Csg: 8-5/8' @ 322'

Prod Csg: 5-1/2" @ 5800'

Csg PBTD: 5713'WL

Tbg: Size: Wt:

Grd: Pkr/EOT @:

BP/Sand PBTD:

PERFORATION RECORD

Zone	Perfs	SPF/#shots	Zone	Perfs	SPF/#shots
LODC sds	5228-5244'	4/64			

CHRONOLOGICAL OPERATIONS

Date Work Performed: 11/10/2006

SITP: SICP: 30

RU BJ Services. 30 psi on well. Frac LODC sds w/ 85,862#'s of 20/40 sand in 662 bbls of Lightning 17 fluid. Broke @ 2303 psi Treated w/ ave pressure of 230 psi @ ave rate of 25.5 BPM. ISIP 2680 psi. Open well to pit for immediate flowback @ 1 bpm. Well flowed for 2.5 hrs. & died. Recovered 150 bbls. SWIFN.

FLUID RECOVERY (BBLs)

Starting fluid load to be recovered: 136

Starting oil rec to date:

Fluid lost/recovered today: 512

Oil lost/recovered today:

Ending fluid to be recovered: 648

Cum oil recovered:

IFL: FFL: FTP:

Choke: Final Fluid Rate: Final oil cut:

STIMULATION DETAIL

Base Fluid used: Job Type:

Company:

Procedure or Equipment detail: LODC sds

6800 gals of pad

4625 gals W/ 1-5 ppg of 20/40 sand

9250 gals W/ 5-8 ppg of 20/40 sand

1967 gals W/ 8 ppg of 20/40 sand

Flush W/ 4809 gals of slick water

Max TP: 2760 Max Rate: 25.8 bpm Total fluid pmpd: 662 bbls

Avg TP: 2530 Avg Rate: 25.5 bpm Total Prop pmpd: 85,862#

ISIP: 2680 5 min: 10 min: FG: .95

Completion Supervisor: Don Dulen

COSTS

BJ Services-CP1	\$34,858
NPC frac wtr	\$1,520
NPC fuel gas	\$220
UniChem chemicals	\$350
NPC surface equip.	\$130,000
R/T welding/labor	\$19,500
Mtn. West Sanitation	\$600
NPC location cleanup	\$300
Monk's pit reclaim	\$1,800
NPC trucking	\$300

NPC supervision \$300

DAILY COST: \$189,748

TOTAL WELL COST: \$568,446

ATTACHMENT H

WORK PROCEDURE FOR PLUGGING AND ABANDONMENT

1. Set CIBP @ 5178'.
2. Plug #1 Set 100' plug on top of CIBP using 12 sx Class G cement.
3. Plug #2 Set 200' plug from 2000'-2200' with 25 sx Class "G" cement.
4. Perforate 4 JSPF @373'.
5. Plug #3 Circulate 117 sx Class G cement down 5-1/2" casing and up the 5-1/2" x 8-5/8" annulus

The approximate cost to plug and abandon this well is \$35,401.

Ashley Federal 5-25-9-15

Spud Date 09/25/2006
 Put on Production: 11/27/2006
 GL: 6301' KB: 6313'

Proposed P & A
Wellbore Diagram


Initial Production: BOPD,
 MCFD, BHPD

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 7 jts. (310.84')
 DEPTH LANDED: 322.69' KB
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 160 sxs Class "G" cmt, est 4.5 bbls cmt to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 131 jts. (5801.70')
 DEPTH LANDED: 5800.95' KB
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ.

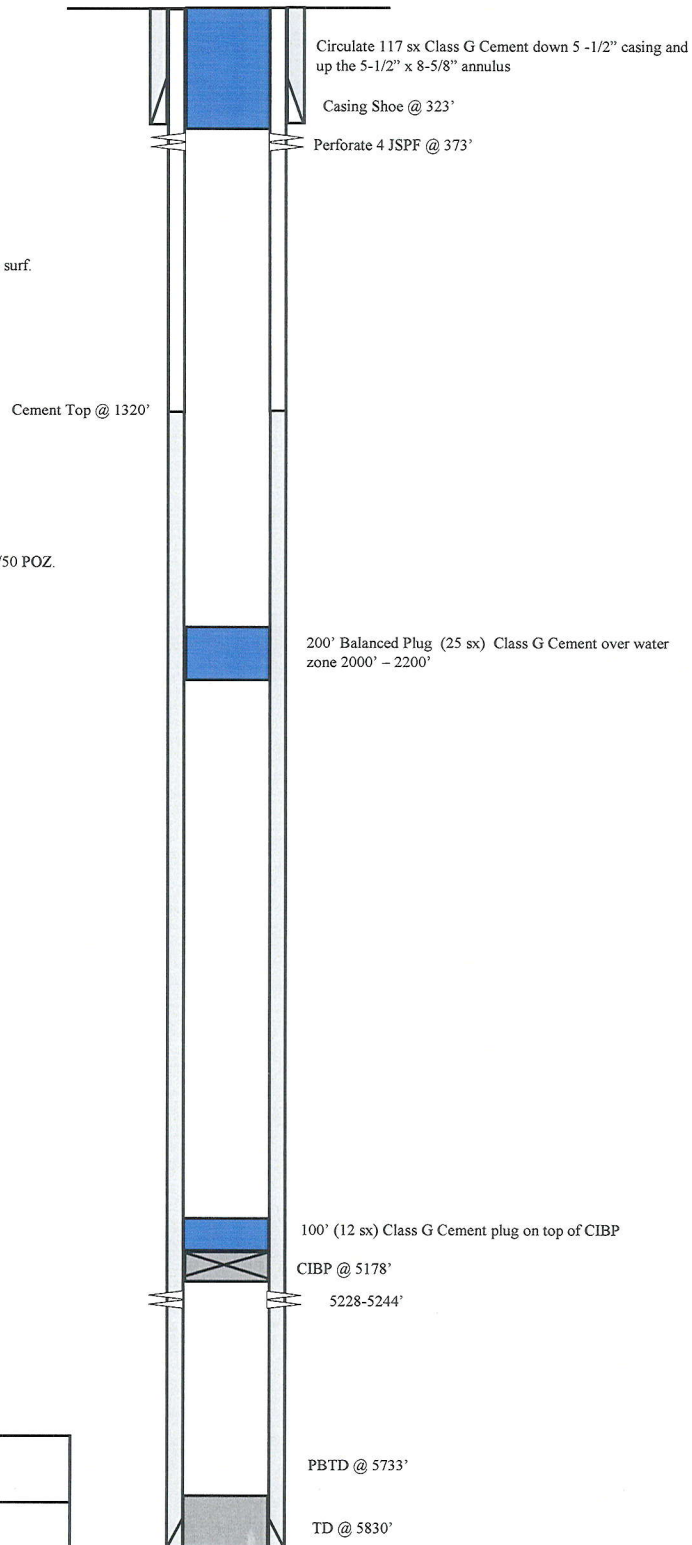

NEWFIELD

Ashley Federal 5-25-9-15

2091' FNL & 505' FWL

SW/NW Section 25-T9S-R15E

Duchesne Co, Utah

API #43-013-32885; Lease #UTU-66185

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on reverse side

1. Type of Well
☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include area code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
2091 FNL 505 FWL
SWNW Section 25 T9S R15E

5. Lease Serial No.

USA UTU-66185

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

ASHLEY PA AB

8. Well Name and No.

ASHLEY FEDERAL 5-25-9-15

9. API Well No.

4301332885

10. Field and Pool, or Exploratory Area

MONUMENT BUTTE

11. County or Parish, State

DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input checked="" type="checkbox"/> Convert to	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

Newfield Production proposes to convert the above mentioned well from a producing oil well to an injection well.

I hereby certify that the foregoing is true and
correct (Printed/ Typed)

Title

Operations Engineer

David Gerbig

Signature

Date

1-25-04

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or
certify that the applicant holds legal or equitable title to those rights in the subject lease
which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United
States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on reverse side

1. Type of Well
☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include area code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
2091 FNL 505 FWL
SWNW Section 25 T9S R15E

5. Lease Serial No.

USA UTU-66185

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

ASHLEY PA AB

8. Well Name and No.

ASHLEY FEDERAL 5-25-9-15

9. API Well No.

4301332885

10. Field and Pool, or Exploratory Area

MONUMENT BUTTE

11. County or Parish, State


DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	_____
	<input checked="" type="checkbox"/> Convert to	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

Newfield Production proposes to convert the above mentioned well from a producing oil well to an injection well.

I hereby certify that the foregoing is true and correct (Printed/ Typed) David Gerbig	Title Operations Engineer
Signature 	Date 1-15-08
THIS SPACE FOR FEDERAL OR STATE OFFICE USE	

Approved by _____	Title _____	Date _____
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office _____	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

IN THE MATTER OF THE APPLICATION OF NEWFIELD
EXPLORATION COMPANY FOR ADMINISTRATIVE
APPROVAL OF THE ASHLEY FEDERAL 13-24-9-15,
ASHLEY FEDERAL 15-24-9-15, ASHLEY FEDERAL 3-25-9-
15, ASHLEY FEDERAL 5-25-9-15, ASHLEY FEDERAL 7-25-
9-15, ASHLEY FEDERAL 9-25-9-15, ASHLEY FEDERAL 11-
25-9-15, ASHLEY FEDERAL 15-25-9-15, ASHLEY FEDERAL
5-26-9-15, ASHLEY FEDERAL 9-26-9-15, ASHLEY FEDERAL
11-26-9-15 WELLS LOCATED IN SECTIONS 24, 25, 26
TOWNSHIP 9 SOUTH, RANGE 15 EAST, DUCHESNE
COUNTY, UTAH, AS CLASS II INJECTION WELLS

CAUSE NO. UIC 342

Gil Hunt
Associate Director

Newfield Exploration Company

**Ashley Federal 13-24-9-15, Ashley Federal 15-24-9-15, Ashley Federal 3-25-9-15, Ashley Federal 5-25-9-15,
Ashley Federal 7-25-9-15, Ashley Federal 9-25-9-15, Ashley Federal 11-25-9-15, Ashley Federal 15-25-9-15,
Ashley Federal 5-26-9-15, Ashley Federal 9-26-9-15, Ashley Federal 11-26-9-15
Cause No. UIC 342**

Publication Notices were sent to the following:

Newfield Exploration Company
1401 17th Street, Suite 1000
Denver, CO 80202

Newfield Production Company
Rt 3 Box 3630
Myton, UT 84052


Via E-mail and Facsimile (435) 722-4140
Uintah Basin Standard
268 South 200 East
Roosevelt, UT 84066

Via E-Mail and Facsimile (801) 237-2776
The Salt Lake Tribune
PO Box 45838
Salt Lake City, UT 84145

Vernal Office
Bureau of Land Management
170 South 500 East
Vernal, UT 84078

Duchesne County Planning
PO Box 910
Duchesne, UT 84021

Dan Jackson
US EPA Region VIII, MS 8P-W-GW
1595 Wynkoop St
Denver, CO 80202-1129



Jean Sweet
Executive Secretary
February 4, 2008

4770 S. 5600 W.
P.O. BOX 704005
WEST VALLEY CITY, UTAH 84170
FED.TAX I.D.# 87-0217663

The Salt Lake Tribune

MEDIAOne
A NEWSPAPER AGENCY COMPANY

Morning News

CUSTOMER'S
COPY

PROOF OF PUBLICATION

CUSTOMER NAME AND ADDRESS	ACCOUNT NUMBER	DATE
DIV OF OIL-GAS & MINING, 1594 W NORTH TEMP #1210 P.O. BOX 145801 SALT LAKE CITY, UT 84114	1001402352	02/11/2008

ACCOUNT NAME	
DIV OF OIL-GAS & MINING,	
TELEPHONE	ADORDER# / INVOICE NUMBER
8015385340	0000231941 /
SCHEDULE	
Start 02/08/2008	End 02/08/2008
CUST. REF. NO.	
CAPTION	
BEFORE THE DIVISION OF OIL, GAS AND MINI	
SIZE	
74 Lines	2.00 COLUMN
TIMES	RATE
2	
MISC. CHARGES	AD CHARGES
TOTAL COST	
190.00	

COPY

AFFIDAVIT OF PUBLICATION

AS NEWSPAPER AGENCY CORPORATION LEGAL BOOKER, I CERTIFY THAT THE ATTACHED ADVERTISEMENT OF
BEFORE THE DIVISION OF OIL, GAS AND MINI FOR DIV OF OIL-GAS & MINING.
WAS PUBLISHED BY THE NEWSPAPER AGENCY CORPORATION, AGENT FOR THE SALT LAKE TRIBUNE AND DESERET
NEWS, DAILY NEWSPAPERS PRINTED IN THE ENGLISH LANGUAGE WITH GENERAL CIRCULATION IN UTAH, AND
PUBLISHED IN SALT LAKE CITY, SALT LAKE COUNTY IN THE STATE OF UTAH.

PUBLISHED ON Start 02/08/2008 End 02/08/2008

SIGNATURE

DATE 02/11/2008

THIS IS NOT A STATEMENT BUT A "PROOF OF PUBLICATION"
PLEASE PAY FROM BILLING STATEMENT

BEFORE THE DIVISION OF OIL, GAS AND MINING
DEPARTMENT OF NATURAL RESOURCES
STATE OF UTAH
NOTICE OF AGENCY ACTION
CAUSE NO. UIC 342

IN THE MATTER OF THE APPLICATION OF NEWFIELD EXPLORATION COMPANY FOR ADMINISTRATIVE APPROVAL OF THE ASHLEY FEDERAL 13-24-9-15, ASHLEY FEDERAL 15-24-9-15, ASHLEY FEDERAL 3-25-9-15, ASHLEY FEDERAL 5-25-9-15, ASHLEY FEDERAL 7-25-9-15, ASHLEY FEDERAL 9-25-9-15, ASHLEY FEDERAL 11-25-9-15, ASHLEY FEDERAL 15-25-9-15, ASHLEY FEDERAL 5-26-9-15, ASHLEY FEDERAL 9-26-9-15, ASHLEY FEDERAL 11-26-9-15 WELLS LOCATED IN SECTIONS 24, 25, 26 TOWNSHIP 9 SOUTH, RANGE 15 EAST, DUCHESNE COUNTY, UTAH, AS CLASS II INJECTION WELLS

THE STATE OF UTAH TO ALL PERSONS INTERESTED IN THE ABOVE ENTITLED MATTER.

Notice is hereby given that the Division of Oil, Gas and Mining (the "Division") is commencing an informal adjudicative proceeding to consider the application of Newfield Exploration Company for administrative approval of the Ashley Federal 13-24-9-15 well, located in SW/4 SW/4 Section 24, Ashley Federal 15-24-9-15 well, located in SW/4 SE/4 Section 24, Ashley Federal 3-25-9-15 well, located in NE/4 NW/4 Section 25, Ashley Federal 5-25-9-15, located in SW/4 NW/4 Section 25, Ashley Federal 7-25-9-15, located in SW/4 NE/4 Section 25, Ashley Federal 9-25-9-15, located in NE/4 SE/4 Section 25, Ashley Federal 11-25-9-15, located in NE/4 SW/4 Section 25, Ashley Federal 15-25-9-15, located in SW/4 SE/4 Section 25, Ashley Federal 5-26-9-15, located in SW/4 NW/4 Section 26, Ashley Federal 9-26-9-15, located in NE/4 SE/4 Section 26, Ashley Federal 11-26-9-15 wells, located in NE/4 SW/4 Section 26, Township 9 South, Range 15 East, Duchesne County, Utah, for conversion to a Class II injection well. This well is located in the Ashley Unit. The adjudicative proceeding will be conducted informally according to Utah Admin. Rule R649-10, Administrative Procedures.

Selective zones in the Green River Formation will be used for water injection. The maximum requested injection pressure and rate will be determined based on fracture gradient information submitted by Newfield Exploration Company.

Any person desiring to object to the proposed application or otherwise intervene in the proceeding, must file a written protest or notice of intervention with the Division within fifteen days following publication of this notice. The Division's Presiding Officer for this proceeding is Gil Hunt, Associate Director at PO Box 145801, Salt Lake City, Utah 84114-5801, phone number (801) 538-5340. If such a protest or notice of intervention is received, a hearing will be scheduled in accordance with the aforementioned administrative procedure rule. Protestants and/or interveners should be prepared to demonstrate at the hearing how this matter affects their interests.

Dated this 4th day of February, 2008

STATE OF UTAH
DIVISION OF OIL, GAS & MINING
/s/ Gil Hunt
Associate Director

231941

UPAXLP



JON M. HUNTSMAN, JR.
Governor

GARY R. HERBERT
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

March 4, 2008

Newfield Production Company
1401 17th Street, Suite 1000
Denver, Colorado 80202


Re: Ashley Unit Well: Ashley Federal 5-25-9-15, Section 25, Township 9 South, Range 15 East, Duchesne County, Utah

Mr. Dave Gerbig,

Pursuant to Utah Admin. Code R649-5-3-3, the Division of Oil, Gas and Mining (the "Division") issues its administrative approval for conversion of the referenced well to a Class II injection well. Accordingly, the following stipulations shall apply for full compliance with this approval:


1. Compliance with all applicable requirements for the operation, maintenance and reporting for Underground Injection Control ("UIC") Class II injection wells pursuant to Utah Admin. Code R649-1 et seq.
2. Conformance with all conditions and requirements of the complete application submitted by Newfield Production Company. The approved maximum injection pressure will be 2,000 psig.
3. A casing/tubing pressure test shall be conducted prior to commencing injection.

The Division will issue an Underground Injection Control Permit after the above stipulations have been met. If you have any questions regarding this approval or the necessary requirements, please contact Brad Hill or Dan Jarvis at this office.

Sincerely,

for Gil Hunt
Associate Director

cc: Dan Jackson, Environmental Protection Agency
Bureau of Land Management, Vernal
Newfield Production Company, Myton
Duchesne County
Well File

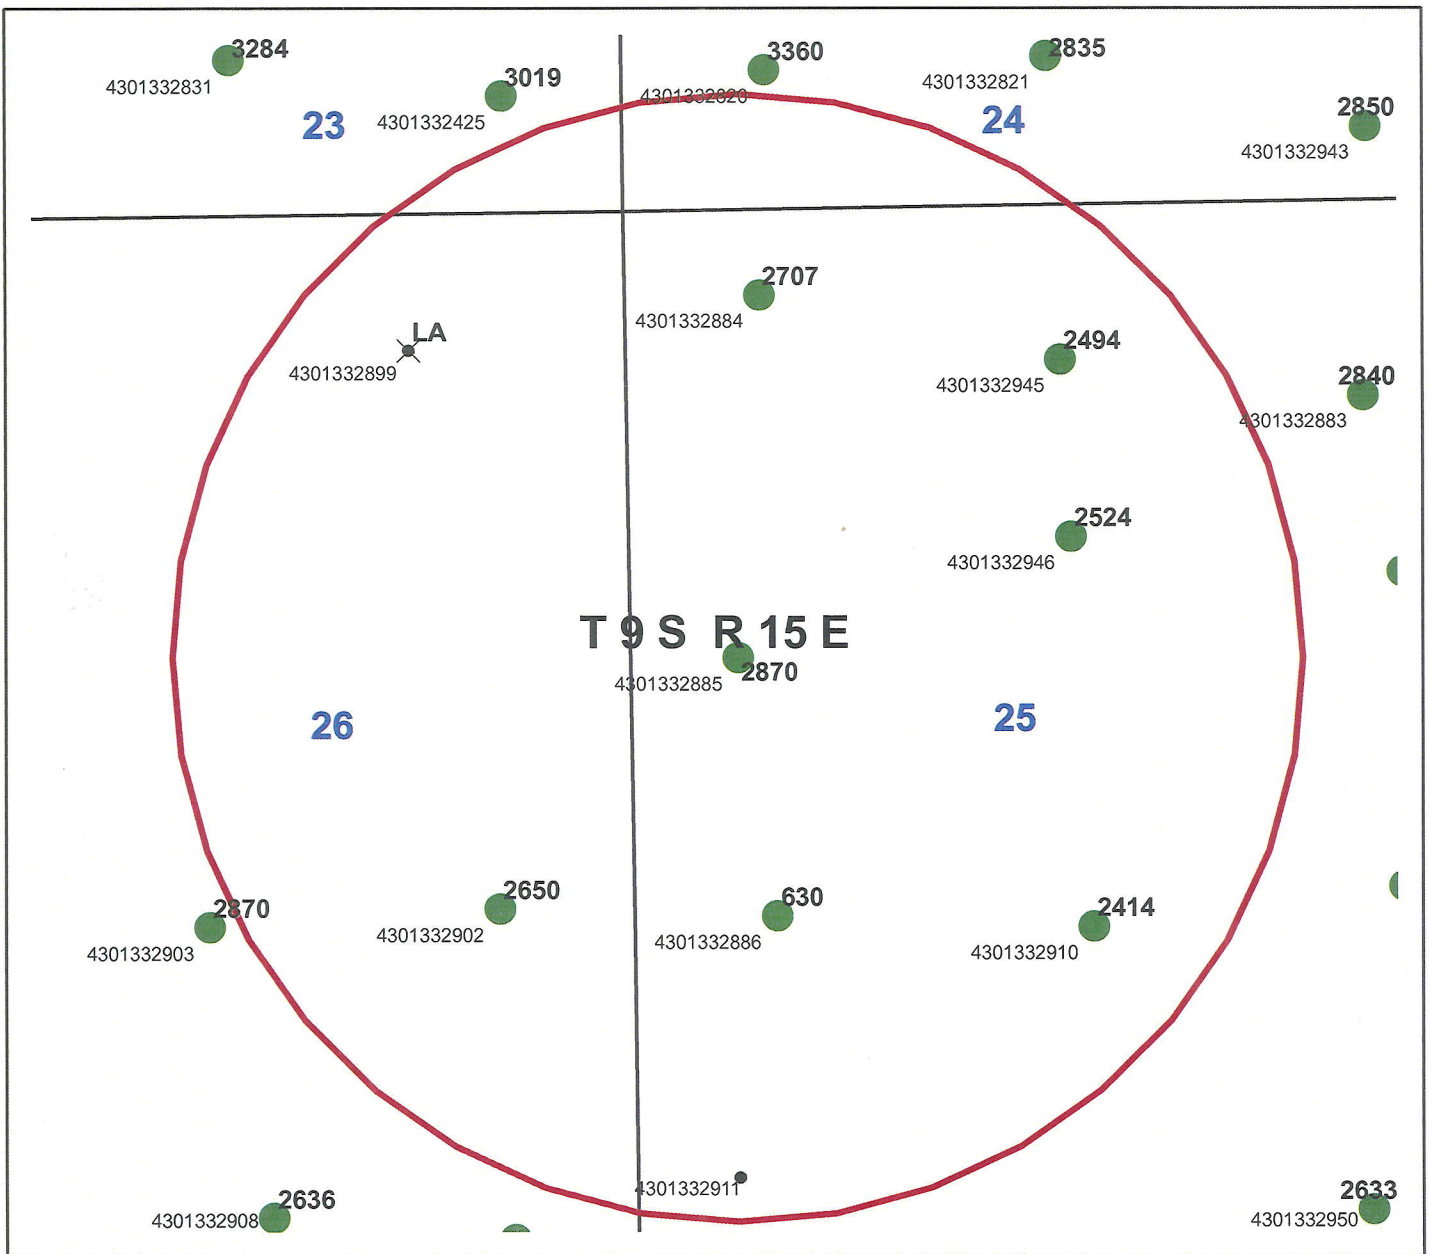



Ashley Federal 5-25-9-15

Legend

wells point	●	POW
WELLTYPE	☀	SGW
☞	☞	SOW
☼	☼	TA
×	○	TW
⊕	☞	WDW
☼	☞	WIW
☀	●	WSW
☼		



0 0.4 Miles

**DIVISION OF OIL, GAS AND MINING
UNDERGROUND INJECTION CONTROL PROGRAM
PERMIT
STATEMENT OF BASIS**

Applicant: Newfield Production Company **Well:** Ashley Federal 5-25-9-15

Location: 25/9S/15E **API:** 43-013-32885

Ownership Issues: The proposed well is located on Federal land. The well is located in the Ashley Unit. Lands in the one-half mile radius of the well are administered by the BLM. The Federal Government is the mineral owner within the area of review. Newfield and other various individuals hold the leases in the unit. Newfield has provided a list of all surface, mineral and lease holders in the half-mile radius. Newfield is the operator of the Ashley Unit. Newfield has submitted an affidavit stating that all owners and interest owners have been notified of their intent.

Well Integrity: The proposed well has surface casing set at 323 feet and has a cement top at the surface. A 5½ inch production casing is set at 5,801 feet. A cement bond log demonstrates adequate bond in this well up to 2,870 feet. A 2 7/8 inch tubing with a packer will be set at 5,193 feet. Higher perforations will be opened at a later date. A mechanical integrity test will be run on the well prior to injection. There are 6 producing wells in the area of review. All of the wells have evidence of adequate casing and cement. No other corrective action will be required.

Ground Water Protection: According to Technical Publication No. 92 the base of moderately saline water is approximately 2,600 feet. Injection shall be the interval between 3,724 feet and 5,716 feet in the Green River Formation. Information submitted by Newfield indicates that the fracture gradient for the 5-25-9-15 well is .95 psi/ft which was the lowest reported fracture gradient for the injection zone. The resulting minimum fracture pressure for the proposed injection interval is 2,646 psig. The approved maximum pressure is 2,000 psig. The anticipated average injection pressure is 1100 psig. Injection at this pressure should not initiate any new fractures or propagate existing fractures in the adjacent confining intervals. Any ground water present should be adequately protected.

Oil/Gas& Other Mineral Resources Protection: The Board of Oil, Gas & Mining approved the Ashley Unit August 25, 1998. Correlative rights issues were addressed at that time. Previous reviews in this area indicate that other mineral resources in the area have been protected or are not at issue.

Bonding: Bonded with the BLM.

Actions Taken and Further Approvals Needed: A notice of agency action has been sent to the Salt Lake Tribune and the Uinta Basin Standard. A casing/tubing pressure test will be required prior to injection. It is recommended that approval of this application be granted.

Note: Applicable technical publications concerning water resources in the general vicinity of this project have been reviewed and taken into consideration during the permit review process.

Reviewer(s): Clinton Dworshak Date 01/31/2008

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL: OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER <input type="checkbox"/>		5. LEASE DESIGNATION AND SERIAL NUMBER: USA UTU-66185
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052		7. UNIT or CA AGREEMENT NAME: GMBU
4. LOCATION OF WELL: FOOTAGES AT SURFACE: 2091 FNL 505 FWL		8. WELL NAME and NUMBER: ASHLEY FEDERAL 5-25-9-15
OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: SWNW, 25, T9S, R15E		9. API NUMBER: 4301332885
		10. FIELD AND POOL, OR WILDCAT: GREATER MB UNIT
		COUNTY: DUCHESNE
		STATE: UT

CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion:	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
09/14/2010	<input checked="" type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: -
	<input checked="" type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.


The subject well has been converted from a producing oil well to an injection well on 08/26/2010.

On 09/10/2010 Dennis Ingram with the State of Utah DOGM was contacted concerning the initial MIT on the above listed well.

Permission was given at that time to perform the test on 09/10/2010. On 09/14/2010 the casing was pressured up to 1260 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tubing pressure was 450 psig during the test. There was not a State representative available to witness the test.

API# 43-013-32885

NAME (PLEASE PRINT) Lucy Chavez-Naupoto TITLE Administrative Assistant

SIGNATURE  DATE 09/15/2010

(This space for State use only)

RECEIVED

SEP 20 2010

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630

Myton, UT 84052

3b. Phone (include area code)

435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

2091 FNL 505 FWL

SWNW Section 25 T9S R15E

5. Lease Serial No.

USA UTU-66185

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

GMBU

8. Well Name and No.

ASHLEY FEDERAL 5-25-9-15

9. API Well No.

4301332885

10. Field and Pool, or Exploratory Area

GREATER MB UNIT

11. County or Parish, State

DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION

- ☐ Notice of Intent
☒ Subsequent Report
☐ Final Abandonment

TYPE OF ACTION

- | | | | |
|---|---|--|---|
| <input type="checkbox"/> Acidize | <input type="checkbox"/> Deepen | <input type="checkbox"/> Production (Start/Resume) | <input type="checkbox"/> Water Shut-Off |
| <input type="checkbox"/> Alter Casing | <input type="checkbox"/> Fracture Treat | <input type="checkbox"/> Reclamation | <input type="checkbox"/> Well Integrity |
| <input type="checkbox"/> Casing Repair | <input type="checkbox"/> New Construction | <input type="checkbox"/> Recomplete | <input checked="" type="checkbox"/> Other _____ |
| <input type="checkbox"/> Change Plans | <input type="checkbox"/> Plug & Abandon | <input type="checkbox"/> Temporarily Abandon | Change Status _____ |
| <input checked="" type="checkbox"/> Convert to Injector | <input type="checkbox"/> Plug Back | <input type="checkbox"/> Water Disposal | _____ |

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

The subject well has been converted from a producing oil well to an injection well on 08/26/2010.

On 09/10/2010 Dennis Ingram with the State of Utah DOGM was contacted concerning the initial MIT on the above listed well. Permission was given at that time to perform the test on 09/10/2010. On 09/14/2010 the casing was pressured up to 1260 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tubing pressure was 450 psig during the test. There was not a State representative available to witness the test.

API# 43-013-32885

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Lucy Chavez-Naupoto

Signature

Title

Administrative Assistant

Date

09/15/2010

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

RECEIVED

SEP 20 2010

DIV. OF OIL, GAS & MINING

Mechanical Integrity Test Casing or Annulus Pressure Test

Newfield Production Company

Rt. 3 Box 3630

Myton, UT 84052

435-646-3721

Witness: _____ Date 9 / 14 / 2010 Time 11:30 am pm

Test Conducted by: Newfield Exploration

Others Present: _____

Well: ASHLEY Federal 5-25-9-15

Field: MONUMENT BUTTE

Well Location: SW/NW, Sec. 25, T9S, R15E

API No: 43-013-32885


<u>Time</u>	<u>Casing Pressure</u>	
0 min	<u>1260</u>	psig
5	<u>1260</u>	psig
10	<u>1260</u>	psig
15	<u>1260</u>	psig
20	<u>1260</u>	psig
25	<u>1260</u>	psig
30 min	<u>1260</u>	psig
35		psig
40		psig
45		psig
50		psig
55		psig
60 min		psig

Tubing pressure: 450 psig

Result: Pass Fail

Signature of Witness: _____

Signature of Person Conducting Test: Ed L. H. H. H.

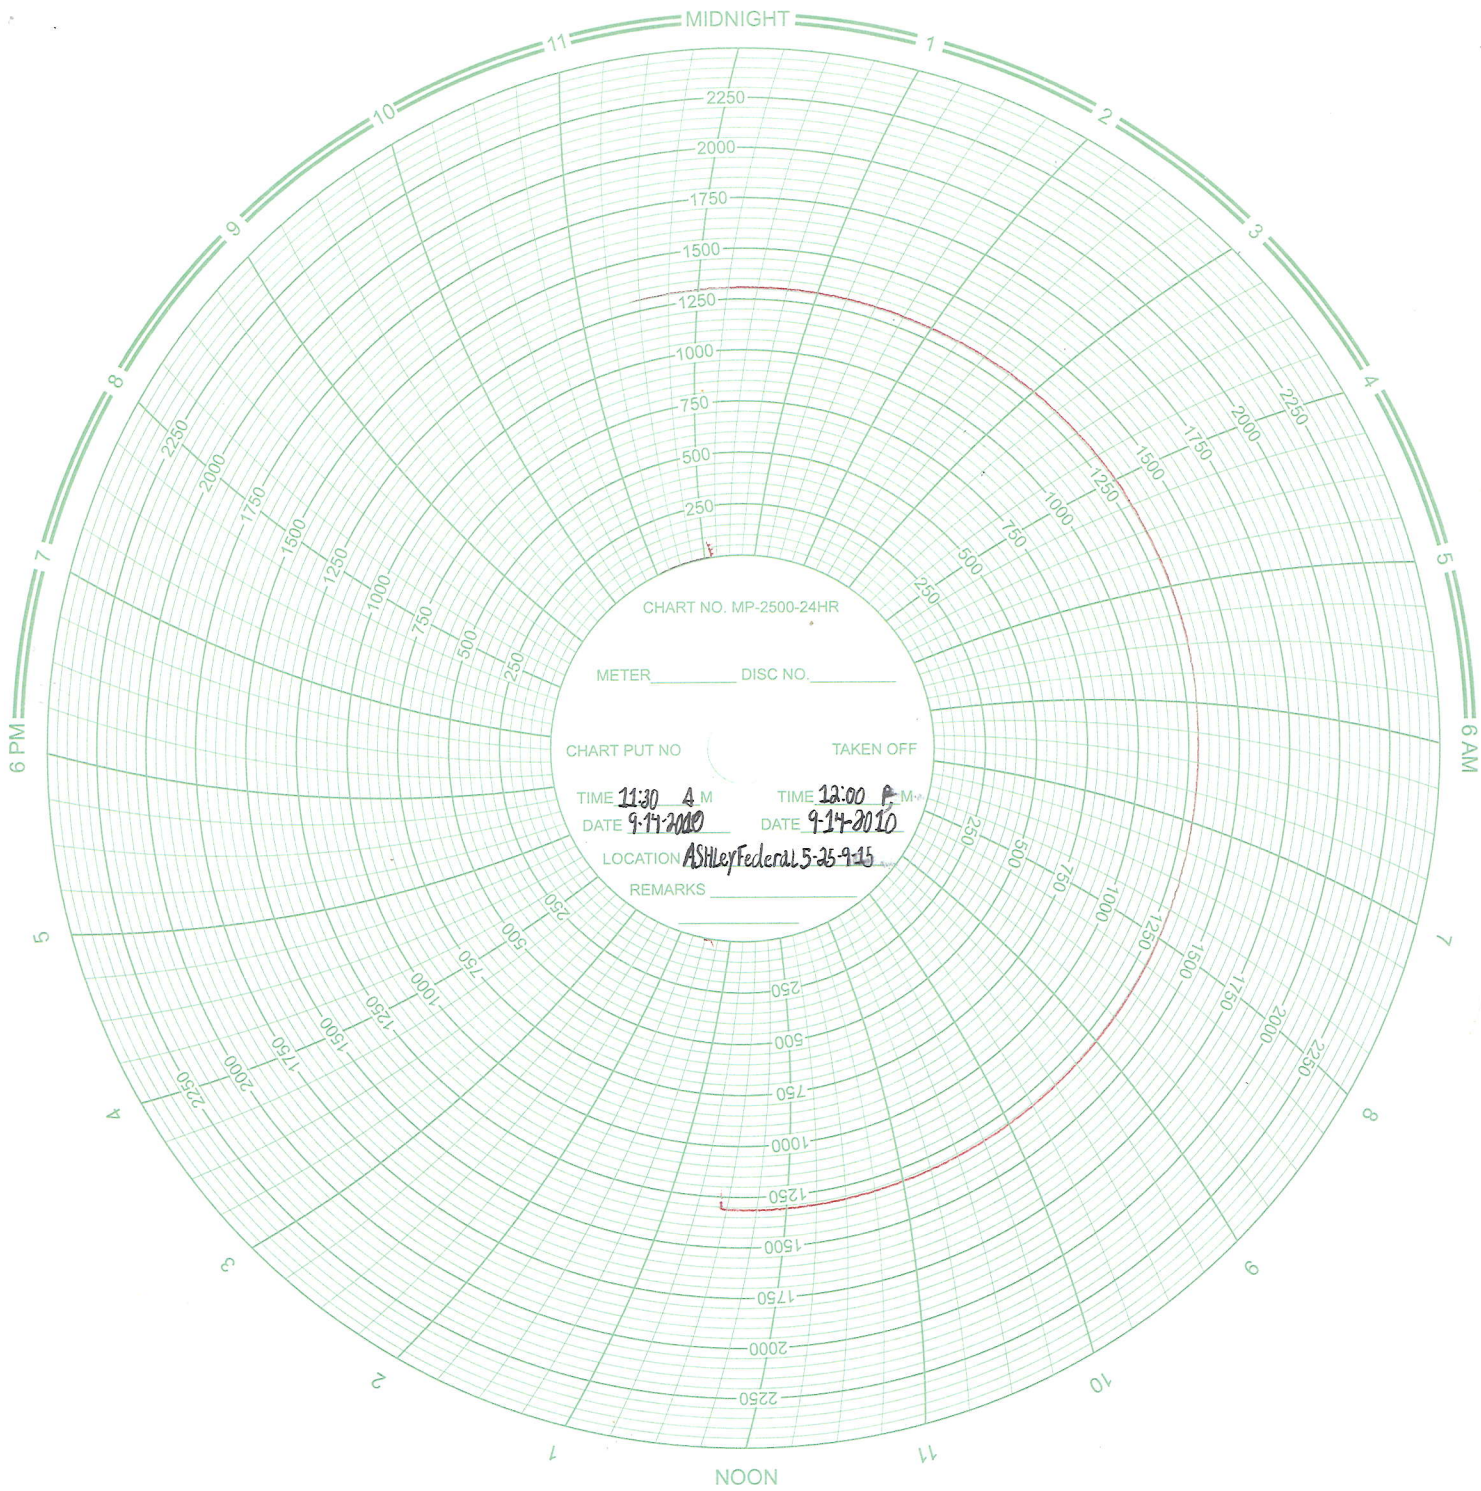

Daily Activity Report**Format For Sundry****ASHLEY 5-25-9-15****6/1/2010 To 10/30/2010****8/26/2010 Day: 1****Conversion**

WWS #7 on 8/26/2010 - LD rod string & pump. Start TOH W/ production tbg. - MIRU Western rig #7. RU HO trk to annulus & pump 60 BW @ 250°F. RU pumping unit & unseat rod pump. Flush tbg & rods W/ 30 BW @ 250°F. Re-seat pump, soft joint rod string & strip off flow-T. Fill tbg W/ 15 BW. Pressure up on tbg to 2200 psi & ruptured. Retrieve rod string & unseat pump. TOH & LD rod string and pump. Re-flushed rods twice more on TOH W/ 40 bbls. ND wellhead & release TA @ 5182'. NU BOP. TOH & talley production tbg. Break each connection, clean & inspect pins and apply Liquid O-ring to pins. Out W/ 124 jts. SIFN.

Daily Cost: \$0**Cumulative Cost:** (\$64,863)

8/27/2010 Day: 2**Conversion**

WWS #7 on 8/27/2010 - Finish TOH W/ production tbg. TIH W/ packer & test injection string. Set & test packer. RDMOSU. - RU HO trk to tbg & flush W/ 30 BW @ 250°F. Con't TOH & talley production tbg. Break each connection, clean & inspect pins and apply Liquid O-ring to pins. LD btm 44 jts & BHA. MU & TIH W/ new Weatherford 5 1/2" Arrowset 1-X packer (W/ wicker slips & W.L. re-entry guide), new 2 7/8 SN and 124 jts 2 7/8 8rd 6.5# J-55 tbg. Re-torque each connection on TIH. RU HO trk & pump 10 bbls pad. Drop standing valve & pump to SN. Pressure test tbg to 3000 psi. Bled air & re-bumped pressure several times. Final test held solid for 30 minutes. Retrieve standing valve W/ overshot on sandline. ND BOP & land tbg on flange. Mix 15 gals Multi-Chem C-6031 & 5 gals B-8850 in 70 bbls fresh water. Pump dn annulus @ 90°F. PU on tbg & set pkr W/ SN @ 3846', CE @ 3850' & EOT @ 3854'. Land tbg W/ 15,000# tension. NU wellhead. Pressure test annulus & pkr to 1500 psi. Holds solid for 1 hour. RDMOSU. - Perform MIT. Run Vaughn Energy Services gyro survey.

Daily Cost: \$0**Cumulative Cost:** (\$57,392)

9/15/2010 Day: 3**Conversion**

Rigless on 9/15/2010 - Conversion MIT. - On 9/10/2010 Dennis Ingram with the State of Utah DOGM was contacted concerning the Conversion MIT on the above listed well (Ashley 5-25-9-15). Permission was given at that time to perform the test on 9/10/2010. On 9/14/2010 the csg was pressured up to 1260 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tbg pressure was 450 psig during the test. There was not a State representative available to witness the test. API # 43-013-32885 **Finalized**

Daily Cost: \$0**Cumulative Cost:** (\$25,572)

Pertinent Files: Go to File List



GARY R. HERBERT
Governor

GREG BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

UNDERGROUND INJECTION CONTROL PERMIT


Cause No. UIC-342

Operator: Newfield Production Company
Well: Ashley Federal 5-25-9-15
Location: Section 25, Township 9 South, Range 15 East
County: Duchesne
API No.: 43-013-32885
Well Type: Enhanced Recovery (waterflood)

Stipulations of Permit Approval

1. Approval for conversion to Injection Well issued on March 4, 2008.
2. Maximum Allowable Injection Pressure: 2,000 psig
3. Maximum Allowable Injection Rate: (restricted by pressure limitation)
4. Injection Interval: Green River Formation (3,724' – 5,716')
5. Any subsequent wells drilled within a ½ mile radius of this well shall have production casing cement brought up to or above the top of the unitized interval for the Greater Monument Butte Unit.

Approved by:


Dan Jarvis
Acting Associate Director

Date

9/27/10

DJJ/MLR/js

cc: Bruce Suchomel, Environmental Protection Agency
Bureau of Land Management, Vernal
Eric Sundberg, Newfield Production Company, Denver
Newfield Production Company, Myton
Duchesne County
Well File

N:\O&G Reviewed Docs\ChronFile\UIC\Newfield



STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
USA UTU-66185

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:
GMBU

1. TYPE OF WELL: OIL WELL ☒ GAS WELL ☐ OTHER

8. WELL NAME and NUMBER:
ASHLEY FEDERAL 5-25-9-15

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:
4301332885

3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

10. FIELD AND POOL, OR WILDCAT:
GREATER MB UNIT

4. LOCATION OF WELL:
FOOTAGES AT SURFACE: 2091 FNL 505 FWL

COUNTY: DUCHESNE

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: SWNW, 25, T9S, R15E

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will 10/20/2010	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON	
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR	
<input type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion:	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Put on Injection	
	<input checked="" type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION		

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above reference well was put on injection at 2:00 PM on 10-20-2010.

RECEIVED

NOV 01 2010

DIV. OF OIL, GAS & MINING

NAME (PLEASE PRINT) Lucy Chavez-Naupoto

TITLE Administrative Assistant

SIGNATURE

DATE 10/25/2010

Ashley Federal 5-25-9-15

Spud Date 09/25/2006
Put on Production: 11/27/2006
GL: 6301' KB: 6313'

Injection Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
GRADE: J-55
WEIGHT: 24#
LENGTH: 7 jts (310.84')
DEPTH LANDED: 322.69' KB
HOLE SIZE: 12-1/4"
CEMENT DATA: 160 sxs Class "G" cement, est 4.5 bbls cement to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
GRADE: J-55
WEIGHT: 15.5#
LENGTH: 131 jts (5801.70')
DEPTH LANDED: 5800.95' KB
HOLE SIZE: 7-7/8"
CEMENT DATA: 300 sxs Prem Lite II mixed & 450 sxs 50-50 POZ.

TUBING

SIZE/GRADE/WT: 2-7/8" J-55 / 6.5#
NO. OF JOINTS: 124 jts (3833.8')
SEATING NIPPLE: 2-7/8" (1.10')
SN LANDED AT: 3845.8'
CE @ 3850.17'
TOTAL STRING LENGTH: EOT @ 3854'

FRAC JOB

11/10/2006	5228-5244'	Frac LODC sands as follows: 85862# 20/40 sand in 662 bbls Lightning 17 frac fluid. Treated @ avg press of 230 psi w/avg rate of 25.5 BPM ISIP 2680 psi Calc flush: 5226 gal. Actual flush: 4809 gal
9-6-07		Pump change. Updated rod & tubing details.
12-28-07		Tubing Leak. Updated rod & tubing details
8-11-08		Tubing Leak Updated rod & tubing details
		Re-Completion
7-10-07	5088-5094'	RU BJ & frac LODC sds as follows: 21,374# 20/40 sand in 391 bbls of Lightning 17 frac fluid. Treated @ avg pressure of 2901 @ avg rate of 24.8 w/ 6.5 ppg of sand. ISIP was 2775. Actual flush: 4620 gals
7-10-07	4554-4564'	RU BJ & frac B.S sds as follows: 29,766# 20/40 sand in 356 bbls of Lightning 17 frac fluid. Treated @ avg pressure of 2082 @ avg rate of 24.8 w/ 8 ppg of sand. ISIP was 1965. Actual flush: 4116 gals
7-10-07	4392-4427'	RU BJ & frac D1 & D2 sds as follows: 50,286# 20/40 sand in 461 bbls of Lightning 17 frac fluid. Treated @ avg pressure of 1414 @ avg rate of 17.8 w/ 8 ppg of sand. ISIP was 1628. Actual flush: 3906 gals
7-10-07	3904-3967'	RU BJ & frac GB4 & GB6 sds as follows: 44,217# 20/40 sand in 393 bbls of Lightning 17 frac fluid. Treated @ avg pressure of 1273 @ avg rate of 17.8 w/ 8 ppg of sand. ISIP was 1345. Actual flush: 3864 gals
8-26-10		Convert to Injection well
9-14-10		MIT Completed - tbg detail updated

Cement Top @ 1320'

Packet @ 3850'
EOT @ 3854'

3904-3912'
3962-3967'
4392-4397'
4408-4412'
4423-4427'
4554-4564'

5088-5094'
5228-5244'

PBTD @ 5733'
TD @ 5830'

PERFORATION RECORD

11/10/06	5228-5244'	4 JSPF	64 holes
7/10/07	3904-3912'	4 JSPF	32 holes
7/10/07	3962-3967'	4 JSPF	20 holes
7/10/07	4392-4397'	4 JSPF	20 holes
7/10/07	4408-4412'	4 JSPF	16 holes
7/10/07	4423-4427'	4 JSPF	16 holes
7/10/07	4554-4564'	4 JSPF	40 holes
7/10/07	5088-5094'	4 JSPF	24 holes

NEWFIELD


Ashley Federal 5-25-9-15

2091' FNL & 505' FWL

SW/NW Section 25-19S-R15E

Duchesne Co, Utah

API #43-013-32885; Lease #UTU-66185

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-66185
1. TYPE OF WELL Water Injection Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
3. ADDRESS OF OPERATOR: Rt 3 Box 3630, Myton, UT, 84052		8. WELL NAME and NUMBER: ASHLEY FED 5-25-9-15
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2091 FNL 0505 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SWNW Section: 25 Township: 09.0S Range: 15.0E Meridian: S		9. API NUMBER: 43013328850000
PHONE NUMBER: 435 646-4825 Ext		9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
COUNTY: DUCHESNE		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 8/13/2015	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input checked="" type="checkbox"/> OTHER	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION	
<input type="checkbox"/> DRILLING REPORT Report Date:	OTHER: 5 YR MIT	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. <div style="display: flex; justify-content: space-between;"> <div style="width: 70%;"> <p>On 08/10/2015 Richard Powell with the State of Utah DOGM was contacted concerning the 5 Year MIT on the above listed well. On 08/13/2015 the casing was pressured up to 1202 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tubing pressure was 1708 psig during the test. There was a not State representative available to witness the test.</p> </div> <div style="width: 25%; text-align: right;"> <p>Accepted by the Utah Division of Oil, Gas and Mining</p> <p>Date: August 20, 2015</p> <p>By: </p> </div> </div>		
NAME (PLEASE PRINT) Lucy Chavez-Naupoto	PHONE NUMBER 435 646-4874	TITLE Water Services Technician
SIGNATURE N/A		DATE 8/14/2015

Mechanical Integrity Test Casing or Annulus Pressure Test

Newfield Production Company
Rt. 3 Box 3630
Myton, UT 84052
435-646-3721

Witness: _____ Date 8/13/15 Time 11:07 am pm
Test Conducted by: Michael Jensen
Others Present: Galen Ross

Well: Ashley Federal 5-25-9-15

Field: Monument Butte

Well Location: SW/4NW Sec. 25, T9S, R1E API No: 43-013-32885

<u>Time</u>	<u>Casing Pressure</u>	
0 min	<u>1208.8</u>	psig
5	<u>1207.4</u>	psig
10	<u>1206.0</u>	psig
15	<u>1204.8</u>	psig
20	<u>1203.8</u>	psig
25	<u>1203.0</u>	psig
30 min	<u>1202.0</u>	psig
35	_____	psig
40	_____	psig
45	_____	psig
50	_____	psig
55	_____	psig
60 min	_____	psig

Tubing pressure: 1708 psig

Result:

Pass

Fail


Signature of Witness: _____

Signature of Person Conducting Test: _____

Michael Jensen

Ashley Federal 5-25-9-15 5 Year MIT (8-13-15)

8/13/2015 11:04:40 AM

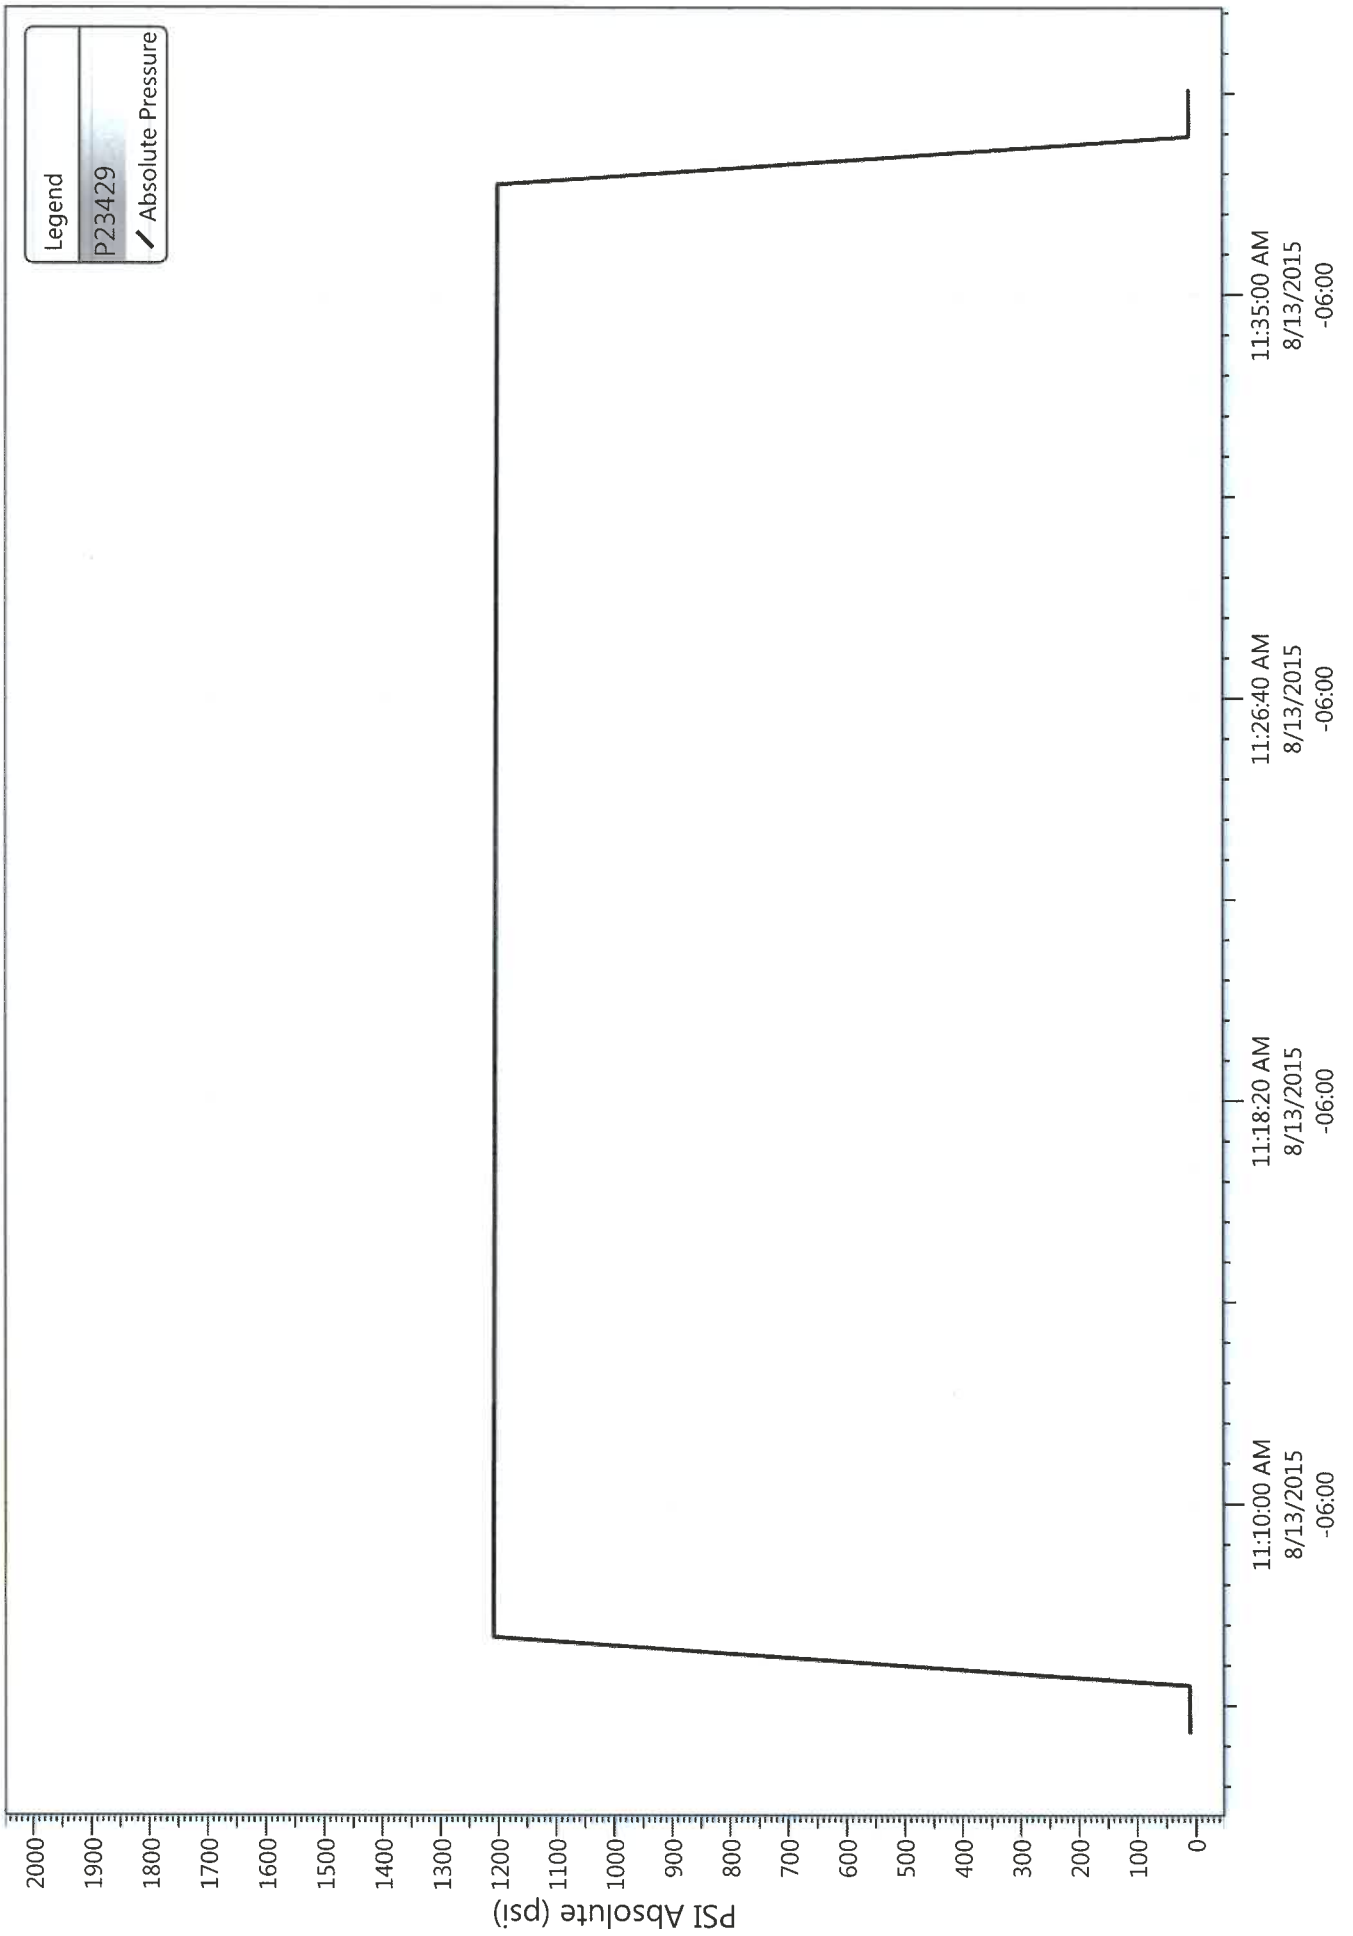

NEWFIELD

Schematic

43-013-32885

Well Name: Ashley 5-25-9-15

Surface Legal Location 25-9S-15E	API/UWI 43013328850000	Well RC 500159067	Lease	State/Province Utah	Field Name GMBU CTB3	County Duchesne
Spud Date	Rig Release Date 11/16/2006	On Production Date 6,313	Original KB Elevation (ft)	Ground Elevation (ft) 6,301	Total Depth All (TVD) (ftKB)	PBTD (All) (ftKB) Original Hole - 5,733.0

Most Recent Job

Job Category Testing	Primary Job Type	Secondary Job Type N/A	Job Start Date 8/13/2015	Job End Date 8/13/2015
-------------------------	------------------	---------------------------	-----------------------------	---------------------------

TD: 5,830.0

Vertical - Original Hole, 12/7/2015 8:18:06 AM

MD (ftKB)	TVD (ftKB)	Incl (°)	DLS	DLS (°...)	Vertical schematic (actual)
12.1					
319.2					
319.9					1; Surface; 8 5/8 in; 8.097 in; 12-320 ftKB; 307.88 ft
1,319.9					6-1; Tubing; 2 7/8; 2.441; 12-3,845; 3,833.45
3,845.5					6-2; Pump Seating Nipple; 2 7/8; 2.441; 3,845-3,847; 1.10
3,846.5					6-3; Packer; 5 1/2; 4.950; 3,847-3,854; 7.40
3,854.0					
3,903.9					Perforated; 3,904-3,967; 7/10/2007
3,966.9					
4,392.1					Perforated; 4,392-4,427; 7/10/2007
4,426.8					
4,554.1					Perforated; 4,554-4,564; 7/10/2007
4,564.0					
5,087.9					Perforated; 5,088-5,244; 7/10/2007
5,228.0					Perforated; 5,228-5,244; 11/10/2006
5,244.1					
5,732.9					
5,754.3					
5,754.9					
5,799.2					
5,799.9					2; Production; 5 1/2 in; 4.950 in; 12-5,800 ftKB; 5,787.88 ft
5,830.1					

NEWFIELD



Newfield Wellbore Diagram Data Ashley 5-25-9-15

Surface Legal Location 25-9S-15E		API/UWI 43013328850000		Lease	
County Duchesne		State/Province Utah		Field Name GMBU CTB3	
Well Start Date 9/25/2006		Spud Date		Final Rig Release Date 11/16/2006	
Original KB Elevation (ft) 6,313	Ground Elevation (ft) 6,301	Total Depth (ftKB) 5,830.0		Total Depth All (TVD) (ftKB)	PBTD (All) (ftKB) Original Hole - 5,733.0

Casing Strings

Csg Des	Run Date	OD (in)	ID (in)	Wt/Len (lb/ft)	Grade	Set Depth (ftKB)
Surface	9/25/2006	8 5/8	8.097	24.00	J-55	320
Production	10/24/2006	5 1/2	4.950	15.50	J-55	5,800

Cement

String: Surface, 320ftKB 9/30/2006

Cementing Company BJ Services Company		Top Depth (ftKB) 12.0	Bottom Depth (ftKB) 320.0	Full Return?	Vol Cement Ret (bbl)
Fluid Description 2% CaCL2 + 1/4#/sk Cello-Flake mixed		Fluid Type Lead	Amount (sacks) 160	Class G	Estimated Top (ftKB) 12.0

String: Production, 5,800ftKB 10/24/2006

Cementing Company BJ Services Company		Top Depth (ftKB) 1,320.0	Bottom Depth (ftKB) 5,830.0	Full Return?	Vol Cement Ret (bbl)
Fluid Description 10% gel + 3 #s /sk KCL, 3#s /sk CSE + 2# sk/kolseal + 1/4#s/sk Cello Flake		Fluid Type Lead	Amount (sacks) 300	Class PREMLITE II	Estimated Top (ftKB) 1,320.0
Fluid Description 2% Gel + 3% KCL, .5%EC1, 1/4# sk C.F. 2% gel. 3% SM mixed		Fluid Type Tail	Amount (sacks) 450	Class 50/50 POZ	Estimated Top (ftKB) 3,000.0

Tubing Strings

Tubing Description					Run Date		Set Depth (ftKB)	
Tubing					8/25/2010		3,854.0	
Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)	Top (ftKB)	Btm (ftKB)
Tubing	124	2 7/8	2.441	6.50	J-55	3,833.45	12.1	3,845.5
Pump Seating Nipple	1	2 7/8	2.441			1.10	3,845.5	3,846.6
Packer	1	5 1/2	4.950			7.40	3,846.6	3,854.0

Rod Strings

Rod Description		Run Date			Set Depth (ftKB)		
Item Des	Jts	OD (in)	Wt (lb/ft)	Grade	Len (ft)	Top (ftKB)	Btm (ftKB)

Perforation Intervals

Stage#	Zone	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Phasing (°)	Nom Hole Dia (in)	Date
5	GB4,6 , Original Hole	3,904	3,967	4			7/10/2007
4	D1, 2, Original Hole	4,392	4,427	4			7/10/2007
3	B.5, Original Hole	4,554	4,564	4			7/10/2007
2	LODC sds, Original Hole	5,088	5,244	4			7/10/2007
1	LODC, Original Hole	5,228	5,244	4			11/10/2006

Stimulations & Treatments

Stage#	ISIP (psi)	Frac Gradient (psi/ft)	Max Rate (bbl/min)	Max PSI (psi)	Total Clean Vol (bbl)	Total Slurry Vol (bbl)	Vol Recov (bbl)
3	1,965	0.86	24.8	2,250			
3	1,965	0.86	24.8	2,250			
3	1,965	0.86	24.8	2,250			
3	1,965	0.86	24.8	2,250			
3	1,965	0.86	24.8	2,250			

Proppant

Stage#	Total Prop Vol Pumped (lb)	Total Add Amount
3		Proppant White Sand 208662 lb
3		Proppant White Sand 208662 lb
3		Proppant White Sand 208662 lb
3		Proppant White Sand 208662 lb
3		Proppant White Sand 208662 lb
