

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0136
Expires January 31, 2004

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU-77339
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name N/A
2. Name of Operator Newfield Production Company		7. If Unit or CA Agreement, Name and No. N/A
3a. Address Route #3 Box 3630, Myton UT 84052	3b. Phone No. (include area code) (435) 646-3721	8. Lease Name and Well No. Federal 7-20-8-16
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NW/SE (Lot #2) 530' FNL 2028' FEL 573270X 40.10332 At proposed prod. zone 44393694 -110.14034		9. API Well No. 43013-33947
14. Distance in miles and direction from nearest town or post office* Approximatley 8.0 miles southwest of Myton, Utah		10. Field and Pool, or Exploratory Monument Undesignated
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 530' f/lse, NA' f/unit	16. No. of Acres in lease 557.08	11. Sec., T., R., M., or Blk. and Survey or Area NW/SE Sec. 20, T8S R16E
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1007'	19. Proposed Depth 6540'	12. County or Parish Duchesne
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5496' GL	22. Approximate date work will start* 4th Quarter 2008	13. State UT
20. BLM/BIA Bond No. on file WYB000493		
23. Estimated duration Approximately seven (7) days from spud to rig release.		

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature 	Name (Printed/Typed) Mandie Crozier	Date 5/28/08
Title Regulatory Specialist		
Approved by (Signature) 	Name (Printed/Typed) BRADLEY G. HILL	Date 07-31-08
Title Office ENVIRONMENTAL MANAGER		

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on reverse)

Federal Approval of this
Action is Necessary

RECEIVED

JUN 04 2008

DIV. OF OIL, GAS & MINING


T8S, R16E, S.L.B.&M.

NEWFIELD PRODUCTION COMPANY


WELL LOCATION: FENCELINE 7-20-8-16

ELEV. UNGRADED GROUND = 5496.2'

WELL LOCATION, FENCELINE 7-20-8-16,
LOCATED AS SHOWN IN THE NW 1/4 SE
1/4 (LOT 2) OF SECTION 20, T8S, R16E,
S.L.B.&M. DUCHESNE COUNTY, UTAH.

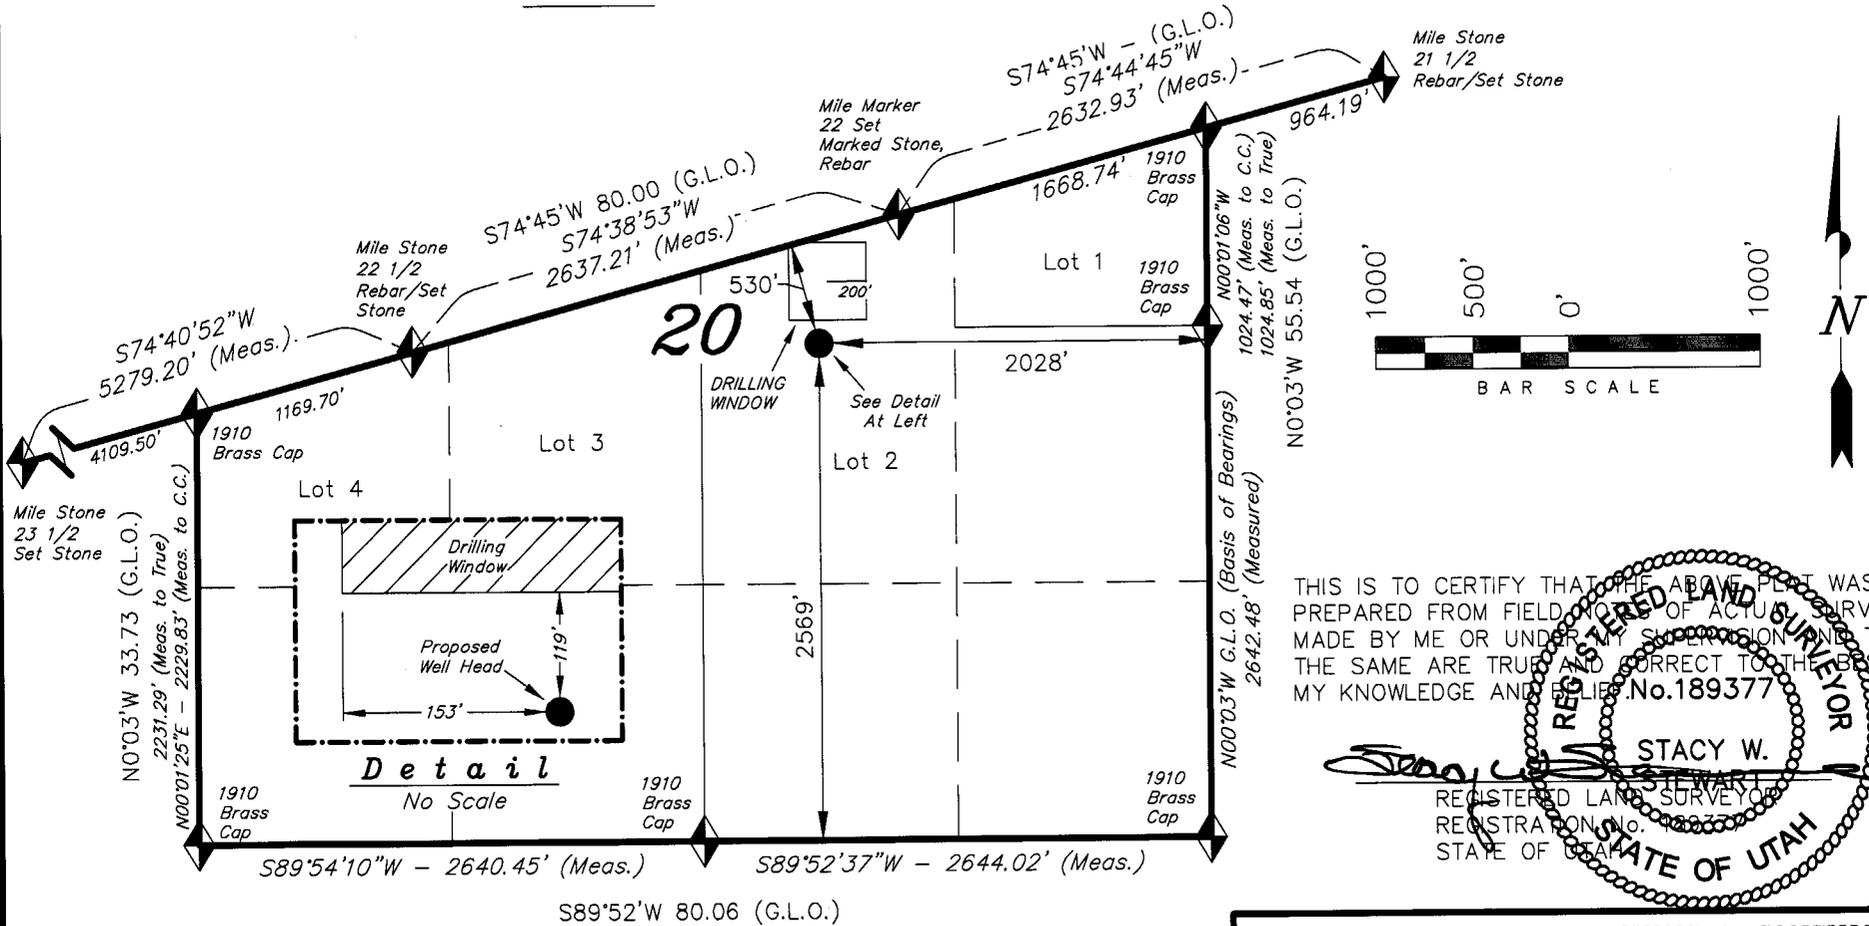

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF. No. 189377



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV;
U.S.G.S. 7-1/2 min QUAD (MYTON SW)

FENCELINE 7-20-8-16
(Surface Location) NAD 83
LATITUDE = 40° 06' 11.62"
LONGITUDE = 110° 08' 27.91"

TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

DATE SURVEYED: 11-26-07
SURVEYED BY: C.M.

DATE DRAWN: 12-17-07
DRAWN BY: F.T.M.

REVISED:
SCALE: 1" = 1000'

NEWFIELD PRODUCTION COMPANY
FEDERAL 7-20-8-16
NW/SE (LOT #2) SECTION 20, T8S, R16E
DUCHESNE COUNTY, UTAH

ONSHORE ORDER NO. 1

DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:
Uinta formation of Upper Eocene Age
2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta	0' – 2905'
Green River	2905'
Wasatch	6540'
3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:
Green River Formation 2905' – 6540' - Oil
4. PROPOSED CASING PROGRAM
Please refer to the Monument Butte Field Standard Operation Procedure (SOP).
5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:
Please refer to the Monument Butte Field SOP. See Exhibit "C".
6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:
Please refer to the Monument Butte Field SOP.
7. AUXILIARY SAFETY EQUIPMENT TO BE USED:
Please refer to the Monument Butte Field SOP.
8. TESTING, LOGGING AND CORING PROGRAMS:
Please refer to the Monument Butte Field SOP.
9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:
The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered.
10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:
Please refer to the Monument Butte Field SOP.

**NEWFIELD PRODUCTION COMPANY
FEDERAL 7-20-8-16
NW/SE (LOT #2) SECTION 20, T8S, R16E
DUCHESNE COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Federal 7-20-8-16 located in the (Lot #2) Section 20, T8S, R16E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.4 miles \pm to the junction of this highway and UT State Hwy 53; proceed southwesterly - 6.4 miles \pm to it's junction with an existing road to the southwest; proceed southwesterly - 0.1 miles \pm to it's junction with the beginning of the proposed access road to the south; proceed along the proposed access road - 520' \pm to the proposed well location.

2. PLANNED ACCESS ROAD

See Topographic Map "B" for the location of the proposed access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

All permanent surface equipment will be painted Carlsbad Canyon.
Please refer to the Monument Butte Field Standard Operating Procedure (SOP).

5. LOCATION AND TYPE OF WATER SUPPLY

Newfield Production will transport water by truck for drilling purposes from the following water sources:

Johnson Water District
Water Right: 43-10136

Neil Moon Pond
Water Right: 43-11787

Maurice Harvey Pond
Water Right: 47-1358

Newfield Collector Well
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

Please refer to the Monument Butte Field SOP. See Exhibit "A".

6. SOURCE OF CONSTRUCTION MATERIALS

Please refer to the Monument Butte Field SOP.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

Please refer to the Monument Butte Field SOP.

8. **ANCILLARY FACILITIES**

Please refer to the Monument Butte Field SOP.

9. **WELL SITE LAYOUT**

See attached Location Layout Diagram.

10. **PLANS FOR RESTORATION OF SURFACE**

Please refer to the Monument Butte Field SOP.

11. **SURFACE OWNERSHIP** - Bureau Of Land Management (Proposed location and access roads leading to).

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. MOAC Report #08-102, 5/9/08. Paleontological Resource Survey prepared by, Wade E. Miller, 4/30/08. See attached report cover pages, Exhibit "D".

Newfield Production Company requests 520' of disturbed area be granted in Lease UTU-77339 to allow for construction of the planned access road. Refer to Topographic Map "B". A permanent width of 30' and a running surface of 18' is proposed for the planned access road. The construction phase of the planned access road will last approximately (5) days. The planned access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 520' of disturbed area be granted in Lease UTU-77339 to allow for construction of the proposed surface gas lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a 6" gas gathering line, and a 3" poly fuel gas line and 30' wide upon completion of the proposed gas lines. Both lines will tie in to the existing pipeline infrastructure. Refer to Topographic Map "C." For a ROW plan of development, please refer to the Monument Butte Field SOP.

Newfield Production Company requests 520' of disturbed area be granted in Lease UTU-77339 to allow for construction of the proposed water lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line and 30' wide upon completion of the proposed water lines. Refer to Topographic Map "C." For a ROW plan of development, please refer to the Monument Butte Field SOP. In the event that the proposed well is converted to a water injection well, a separate injection permit will be applied for through the proper agencies.

Water Disposal

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte,

Jonah, and Beluḡā water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

Threatened, Endangered, And Other Sensitive Species

Mountain Plover: If new construction or surface disturbing activities are scheduled to occur between May 15 and June 15, detailed surveys of the area within 0.5 mile of the proposed location and within 300 feet of proposed access routes must be conducted to detect the presence of mountain plovers. All surveys must be conducted in accordance with the survey protocols outlined in the most recent USFWS Survey Protocol. Surveys must be completed prior to initiating new construction or surface disturbing activities. No new construction or surface disturbing activities will be allowed between May 15 and June 15 within a 0.5 mile radius of any documented mountain plover nest site.

Burrowing Owl: Due to the proximity of the location to active prairie dog towns, there is the potential to encounter nesting burrowing owls between April 1 and August 15. If new construction or surface disturbing activities are scheduled between April 1 and August 15, pre-construction surveys will be conducted to detect the presence of nesting burrowing owls within 0.5 mile of any new construction or surface disturbing activity (see Vernal BLM Field Office Protocol). No new construction or surface disturbing activities will be allowed between April 1 and August 15 within a 0.5 mile radius of any active burrowing owl nest.

Reserve Pit Liner

A 16 mil liner with felt is required. Please refer to the Monument Butte Field SOP.

Location and Reserve Pit Reclamation

Please refer to the Monument Butte Field SOP.

The following seed mixture will be used on the topsoil stockpile, to the recontoured surface of the reserve pit, and for final reclamation: (All poundages are in pure live seed)

Squirrell Tail	<i>Elymus Elymoides</i>	6 lbs/acre
Siberian Wheatgrass	<i>Agropyron Fragile</i>	2 lbs/acre
Gardner Saltbush	<i>Atriplex Gardneri</i>	1 lbs/acre
Shadscale	<i>Atriplex Confertifolia</i>	1 lbs/acre
Fourwing Saltbush	<i>Atriplex Canescens</i>	1 lbs/acre
Scarlet Globemallow	<i>Sphaeralcea Conccinea</i>	0.20 lbs/acre
Forage Kochia	<i>Kochia Prostrata</i>	0.20 lbs/acre

Details of the On-Site Inspection

The proposed Federal #7-20-8-16 was on-sited on 4/16/08. The following were present; Dave Allred (Newfield Production), Kevan Stevens (Newfield Production), Michael Cutler (Bureau of Land Management), Brandon McDonald (Bureau of Land Management)and James Herford (Bureau of Land Management). Weather conditions were clear and ground cover was 100% open.

LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION

Representative

Name: Dave Allred
Address: Route #3 Box 3630
Myton, UT 84052
Telephone: (435) 646-3721


Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #7-20-8-16 (Lot #2) Section 20, Township 8S, Range 16E: Lease UTU-77339 Duchesne County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

5/28/08

Date





Mandie Crozier
Regulatory Specialist
Newfield Production Company

NEWFIELD PRODUCTION COMPANY

FENCELINE 7-20-8-16

Section 20, T8S, R16E, S.L.B.&M.

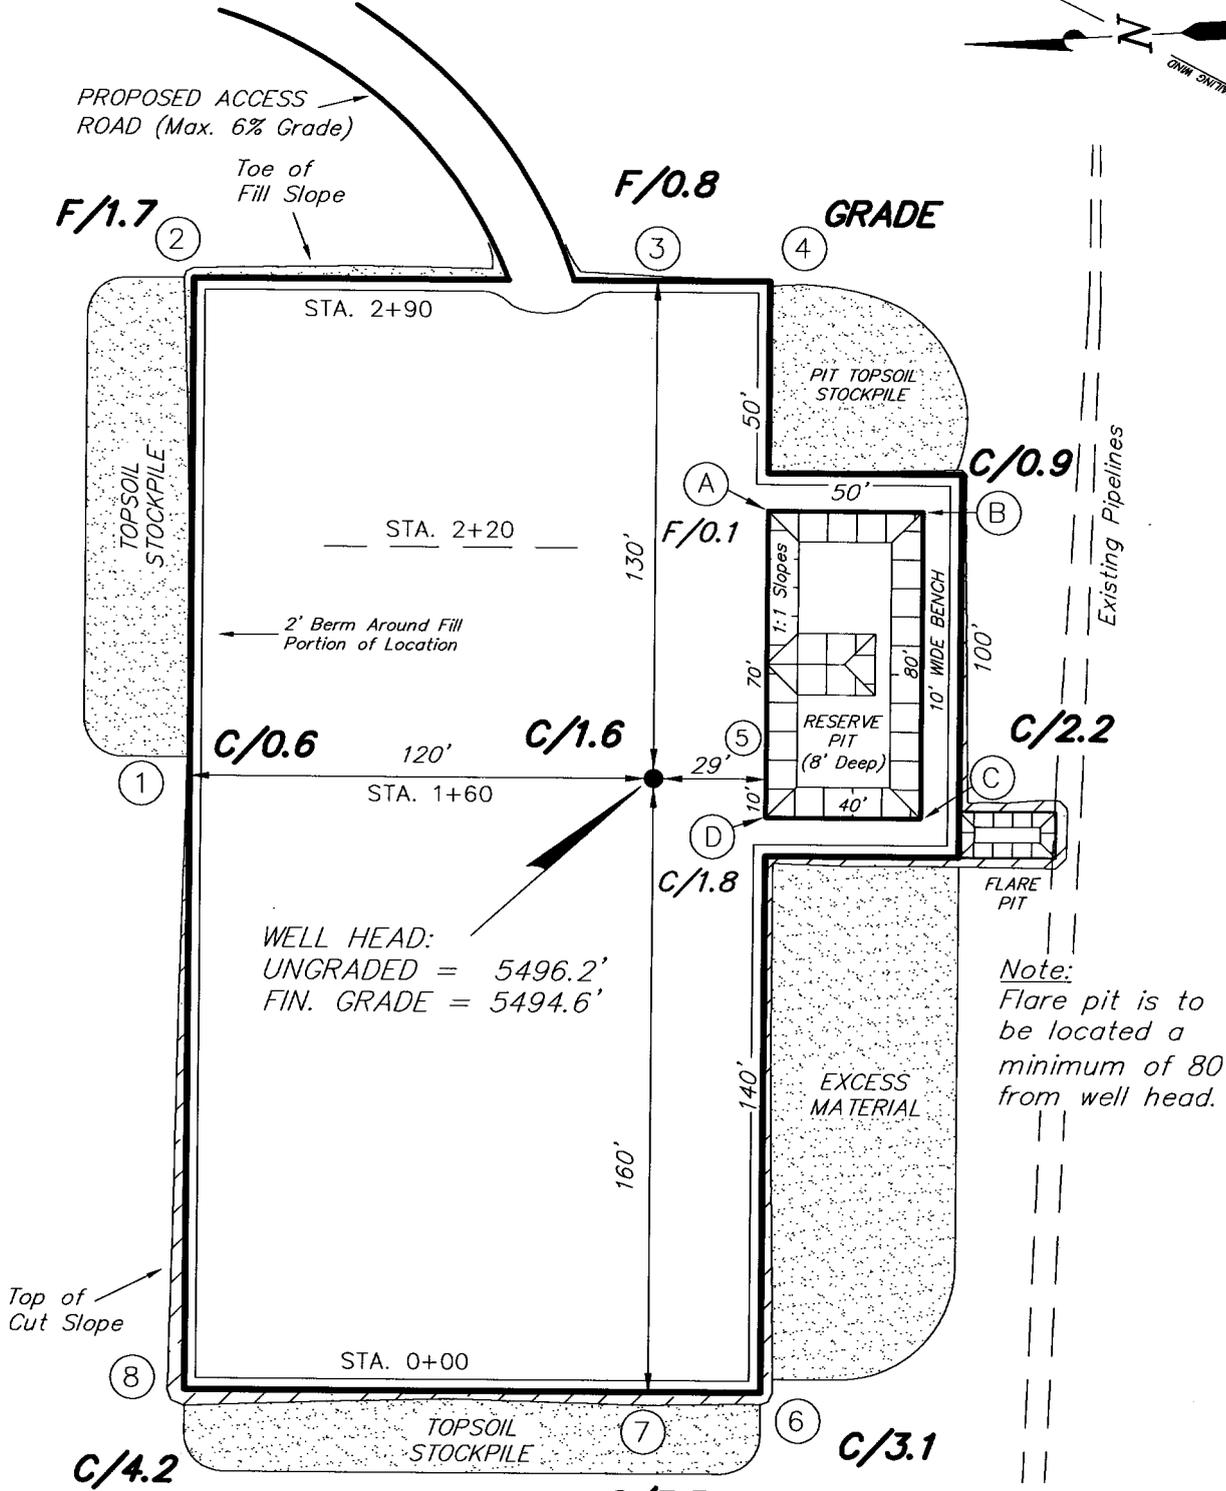

WELL HEAD:
 UNGRADED = 5496.2'
 FIN. GRADE = 5494.6'

Note:
 Flare pit is to be located a minimum of 80' from well head.

REFERENCE POINTS

- 170' NORTHERLY = 5496.3'
- 220' NORTHERLY = 5497.6'
- 210' WESTERLY = 5497.8'
- 260' WESTERLY = 5498.5'





SURVEYED BY: C.M.	DATE SURVEYED: 11-26-07
DRAWN BY: F.T.M.	DATE DRAWN: 12-17-07
SCALE: 1" = 50'	REVISED:

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

CROSS SECTIONS

FENCELINE 7-20-8-16

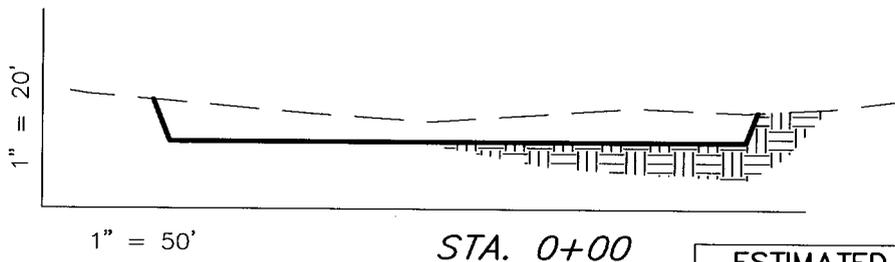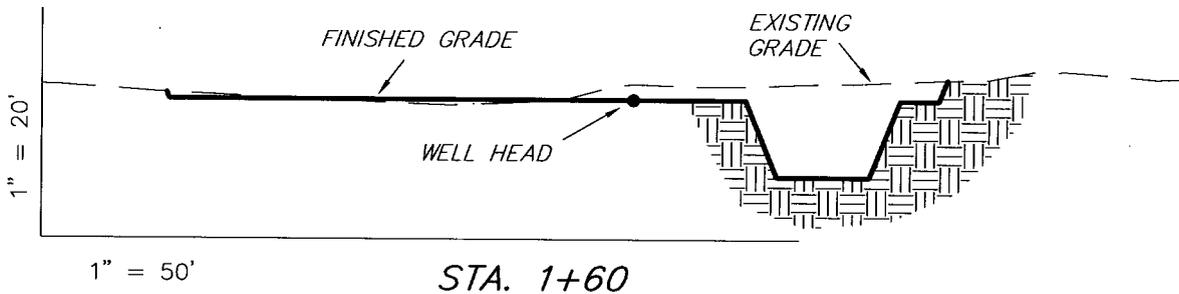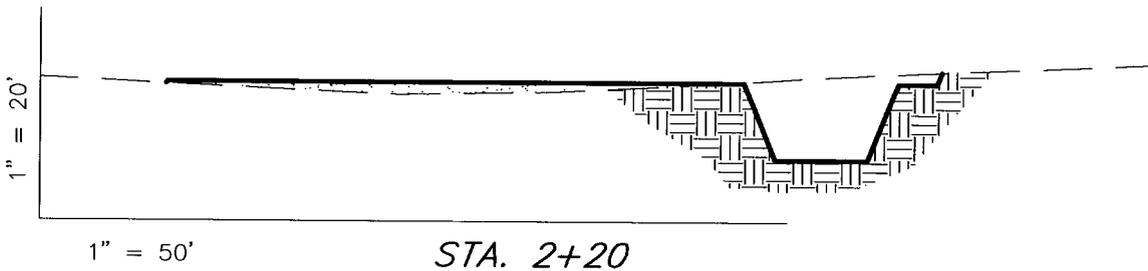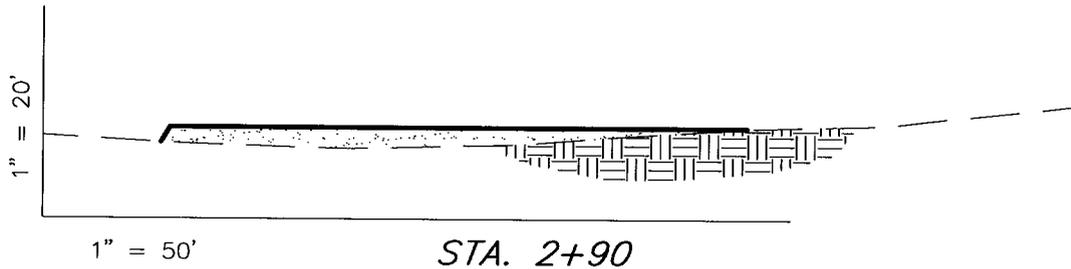

ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	1,100	1,020	Topsoil is not included in Pad Cut	80
PIT	640	0		640
TOTALS	1,740	1,020	940	720

NOTE:
UNLESS OTHERWISE NOTED
CUT SLOPES ARE AT 1:1
FILL SLOPES ARE AT 1.5:1

SURVEYED BY: C.M.	DATE SURVEYED: 11-26-07
DRAWN BY: F.T.M.	DATE DRAWN: 12-17-07
SCALE: 1" = 50'	REVISED:

Tri State
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078
(435) 781-2501


Lowfield Production Company Proposed Site Facility Diagram

Federal 7-20-8-16

NW/SE (Lot #2) Sec. 20, T8S, R16E

Duchesne County, Utah

UTU-77339

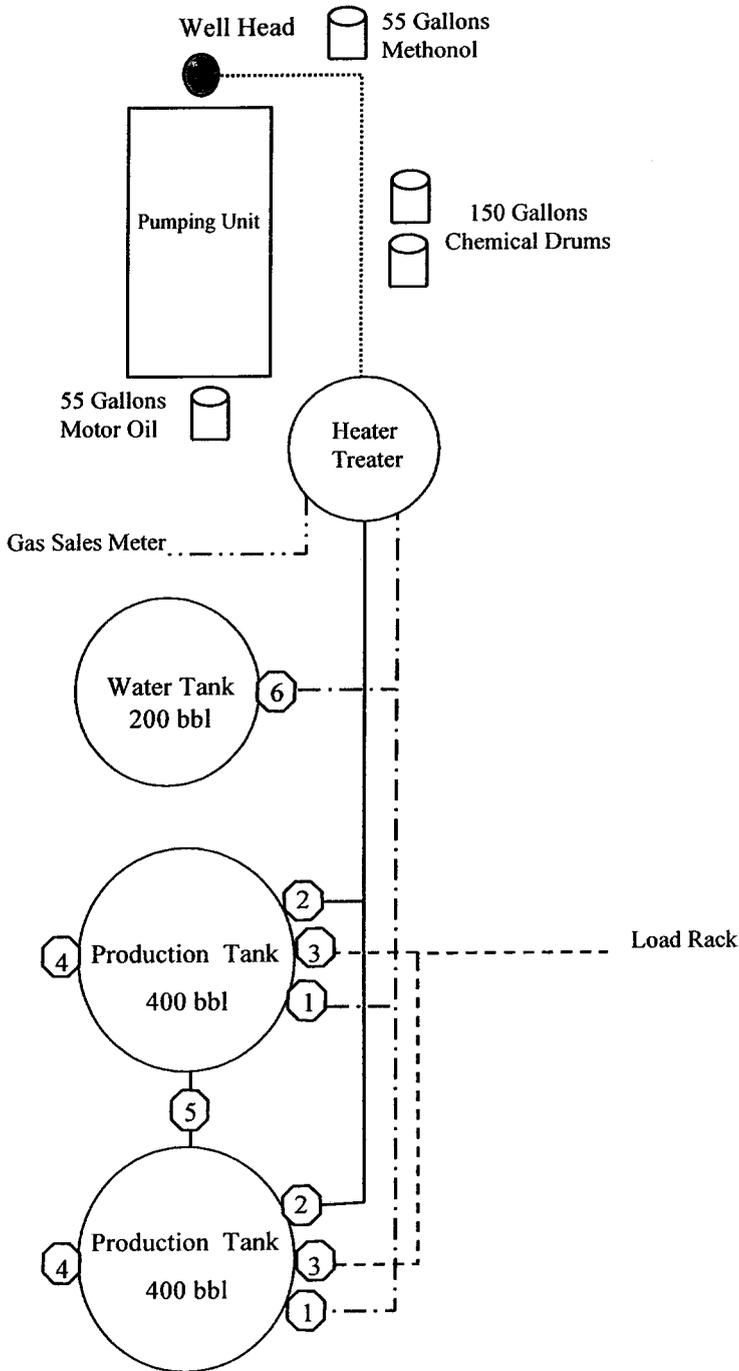

Legend

Emulsion Line
Load Rack	-----
Water Line	- . - . - .
Gas Sales	- . - . - .
Oil Line	—————

Production Phase:

- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open

Sales Phase:


- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

Draining Phase:

- 1) Valves 1 and 6 open

Diked Section



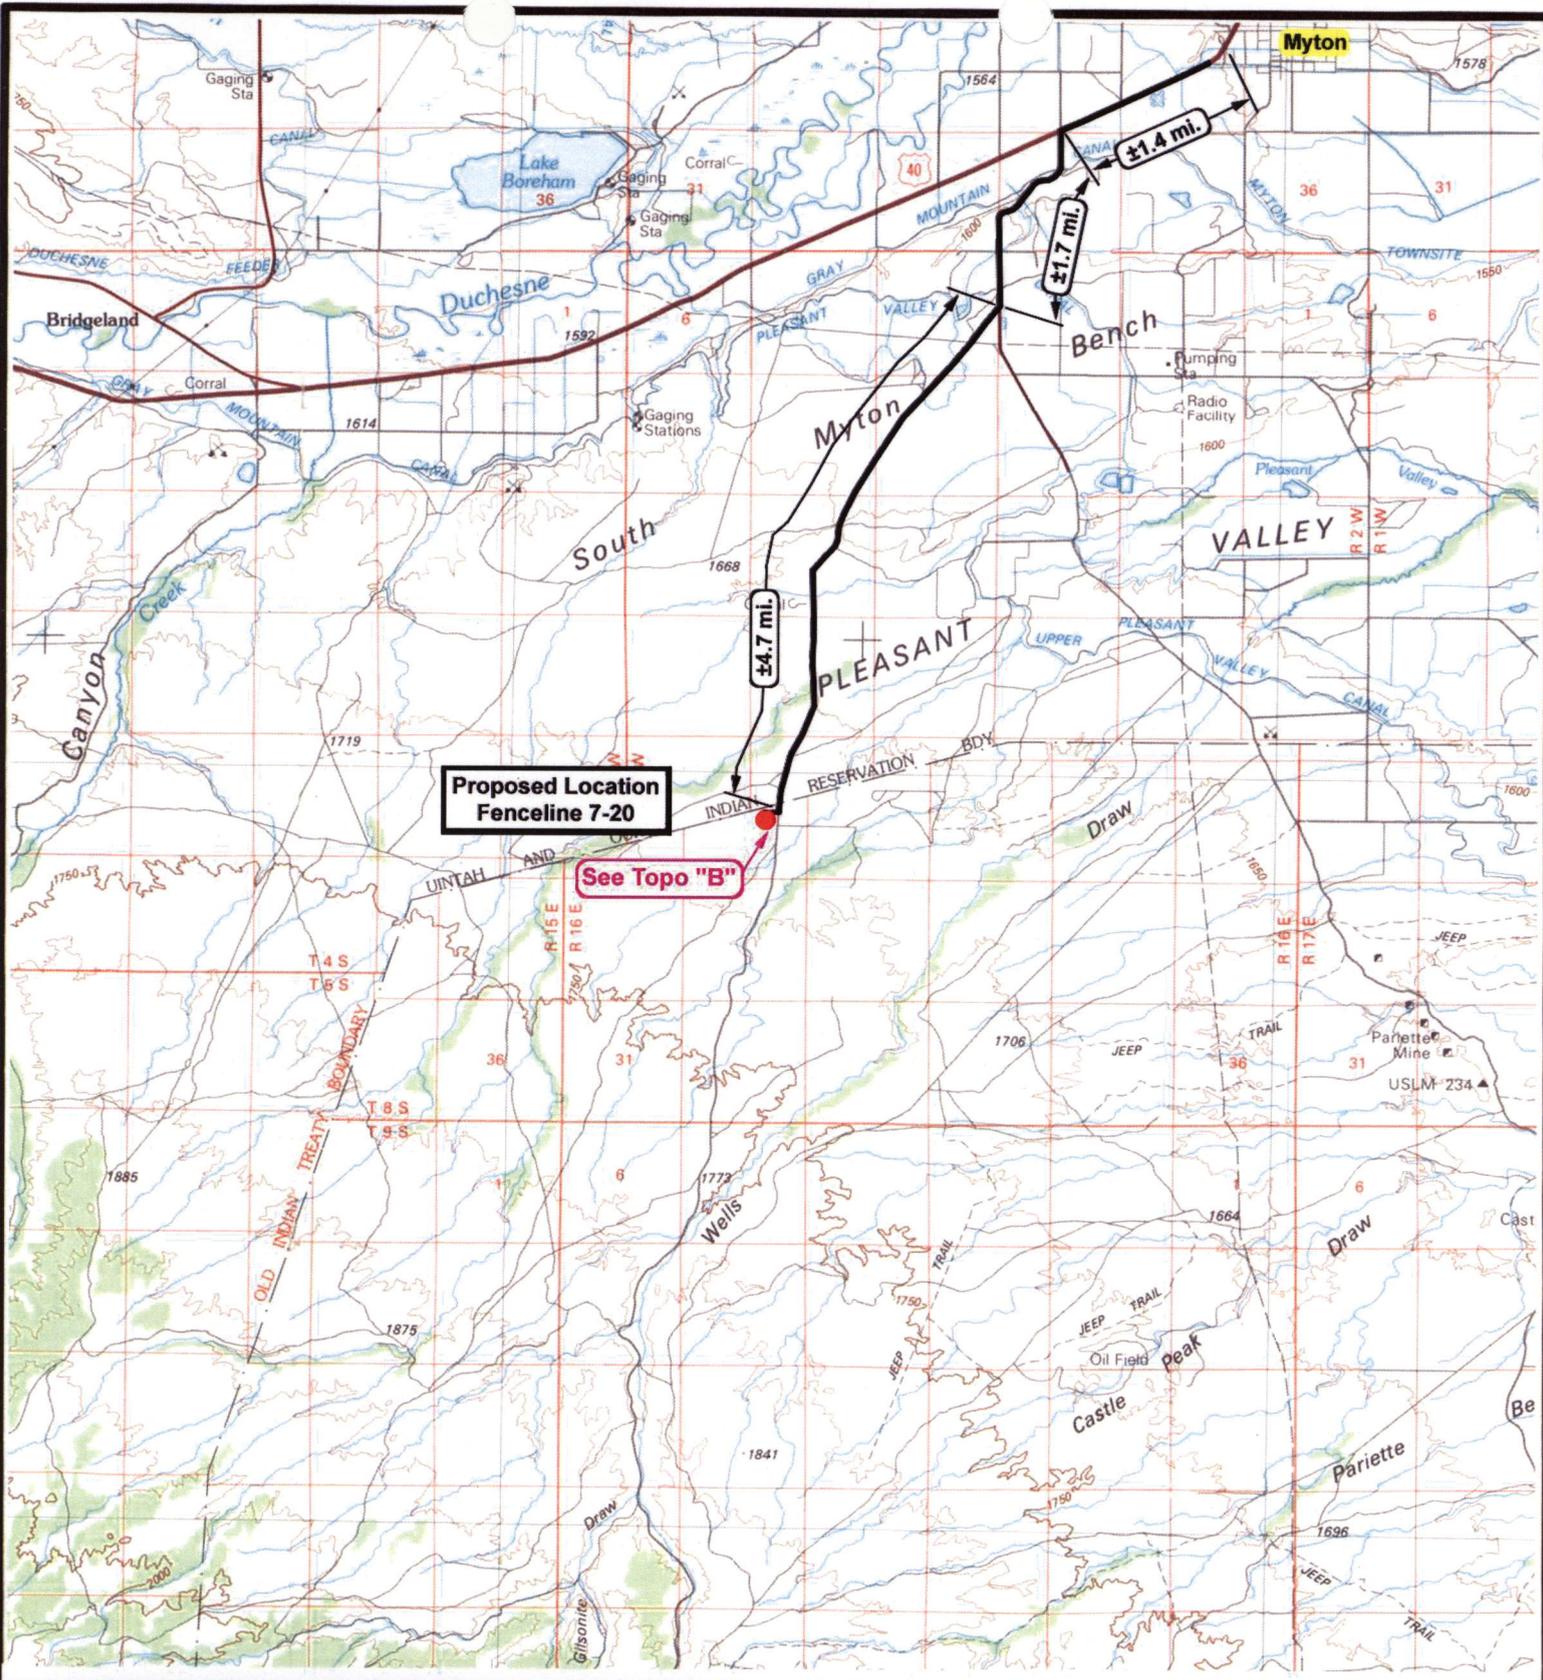

**Proposed Location
Fenceline 7-20**

See Topo "B"

NEWFIELD
Exploration Company

**Fenceline 7-20-8-16
SEC. 20, T8S, R16E, S.L.B.&M.**




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1 = 100,000
DRAWN BY: mw
DATE: 01-03-2008

Legend

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP
"A"

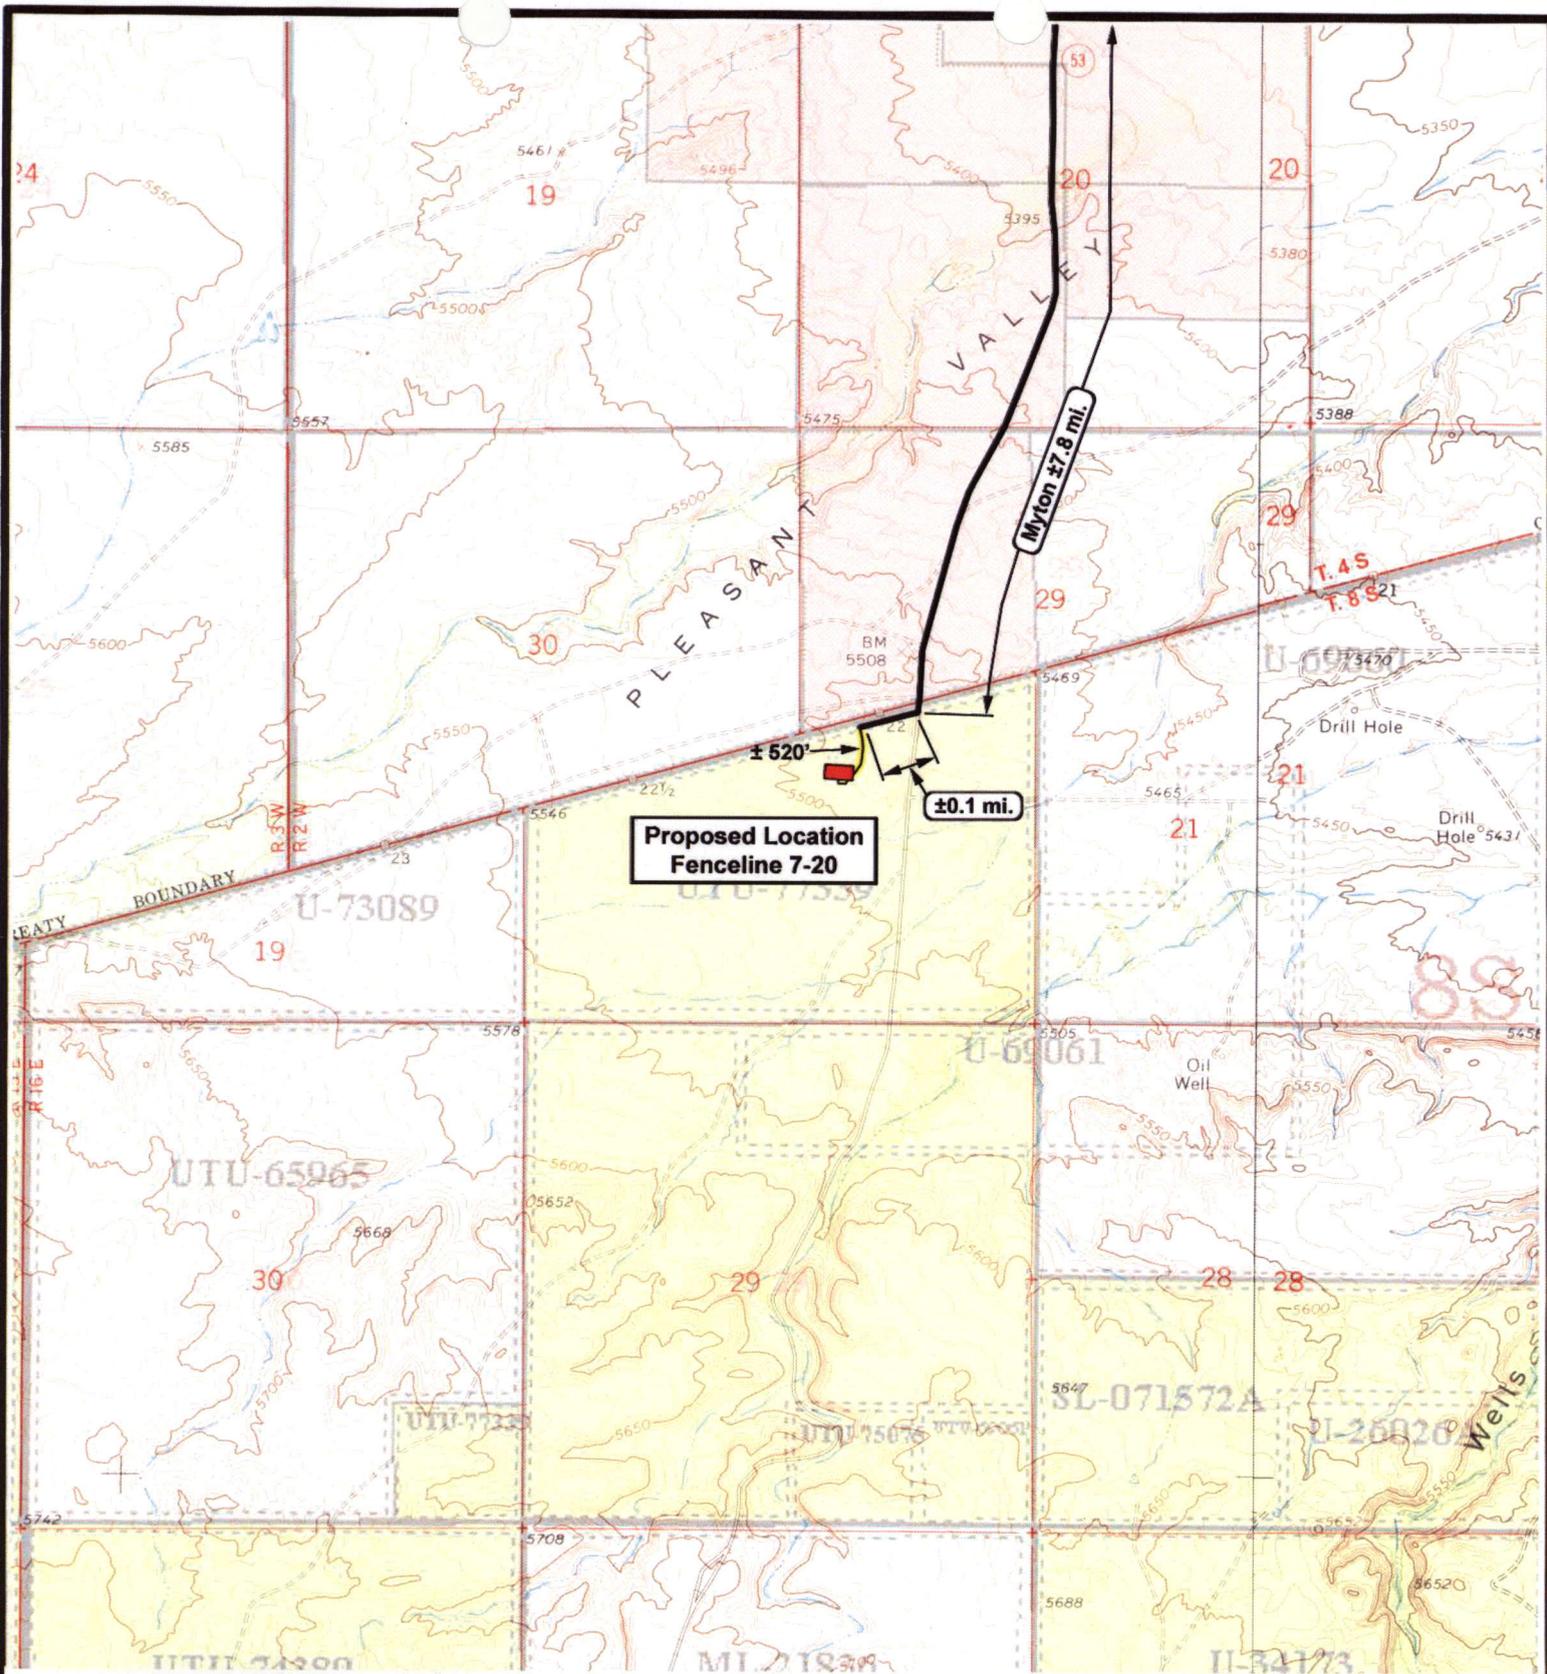


NEWFIELD
Exploration Company

Fenceline 7-20-8-16
SEC. 20, T8S, R16E, S.L.B.&M.



Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 01-03-2008

Legend

-  Existing Road
-  Proposed Access

TOPOGRAPHIC MAP

"B"

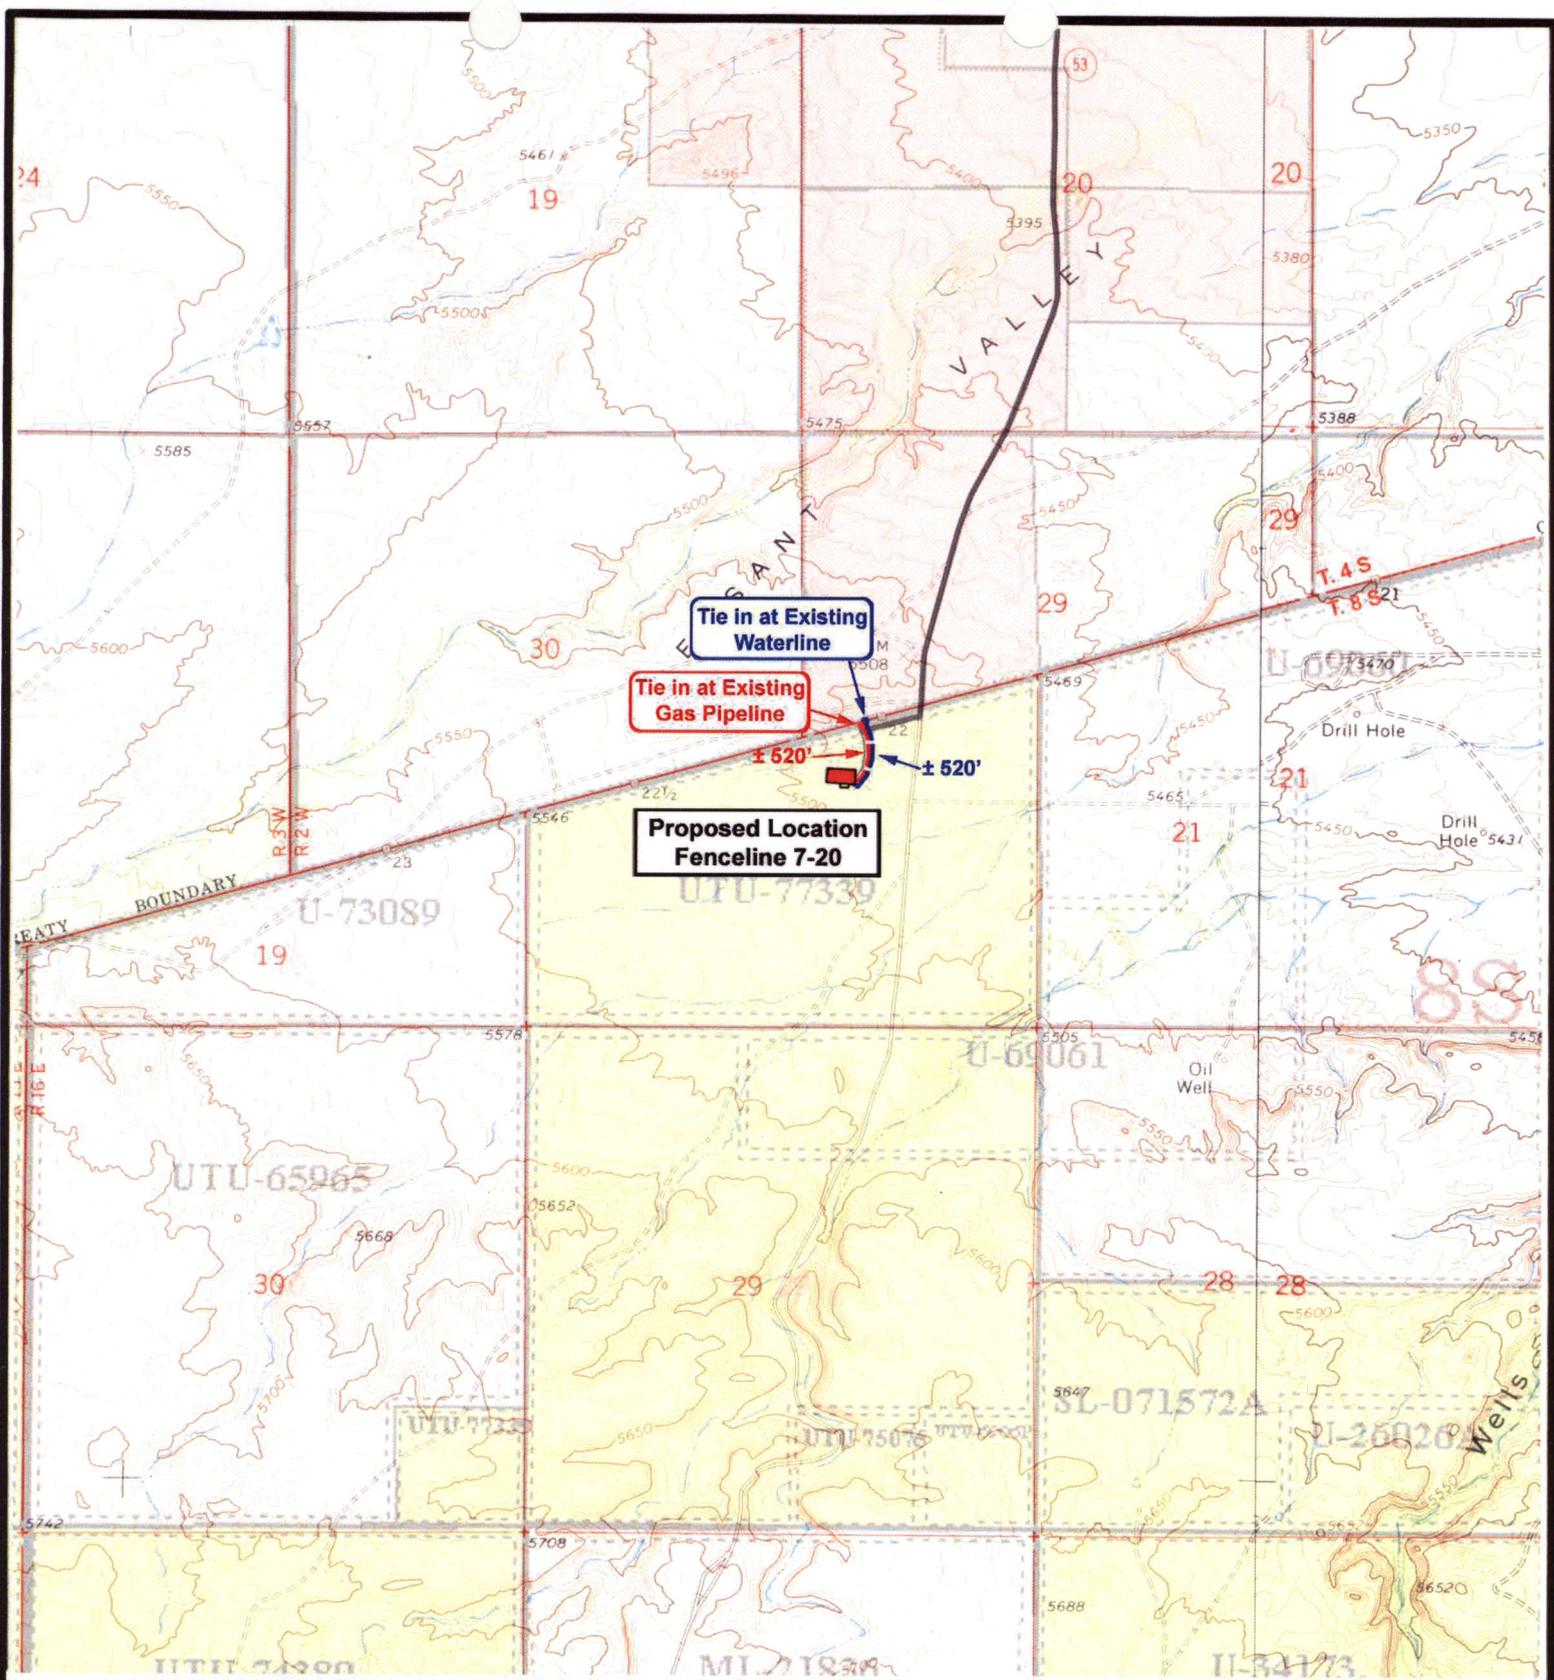


NEWFIELD
Exploration Company

Fenceline 7-20-8-16
SEC. 20, T8S, R16E, S.L.B.&M.




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 01-03-2008


Legend

-  Roads
-  Proposed Gas Line
-  Proposed Water Line

TOPOGRAPHIC MAP

"C"

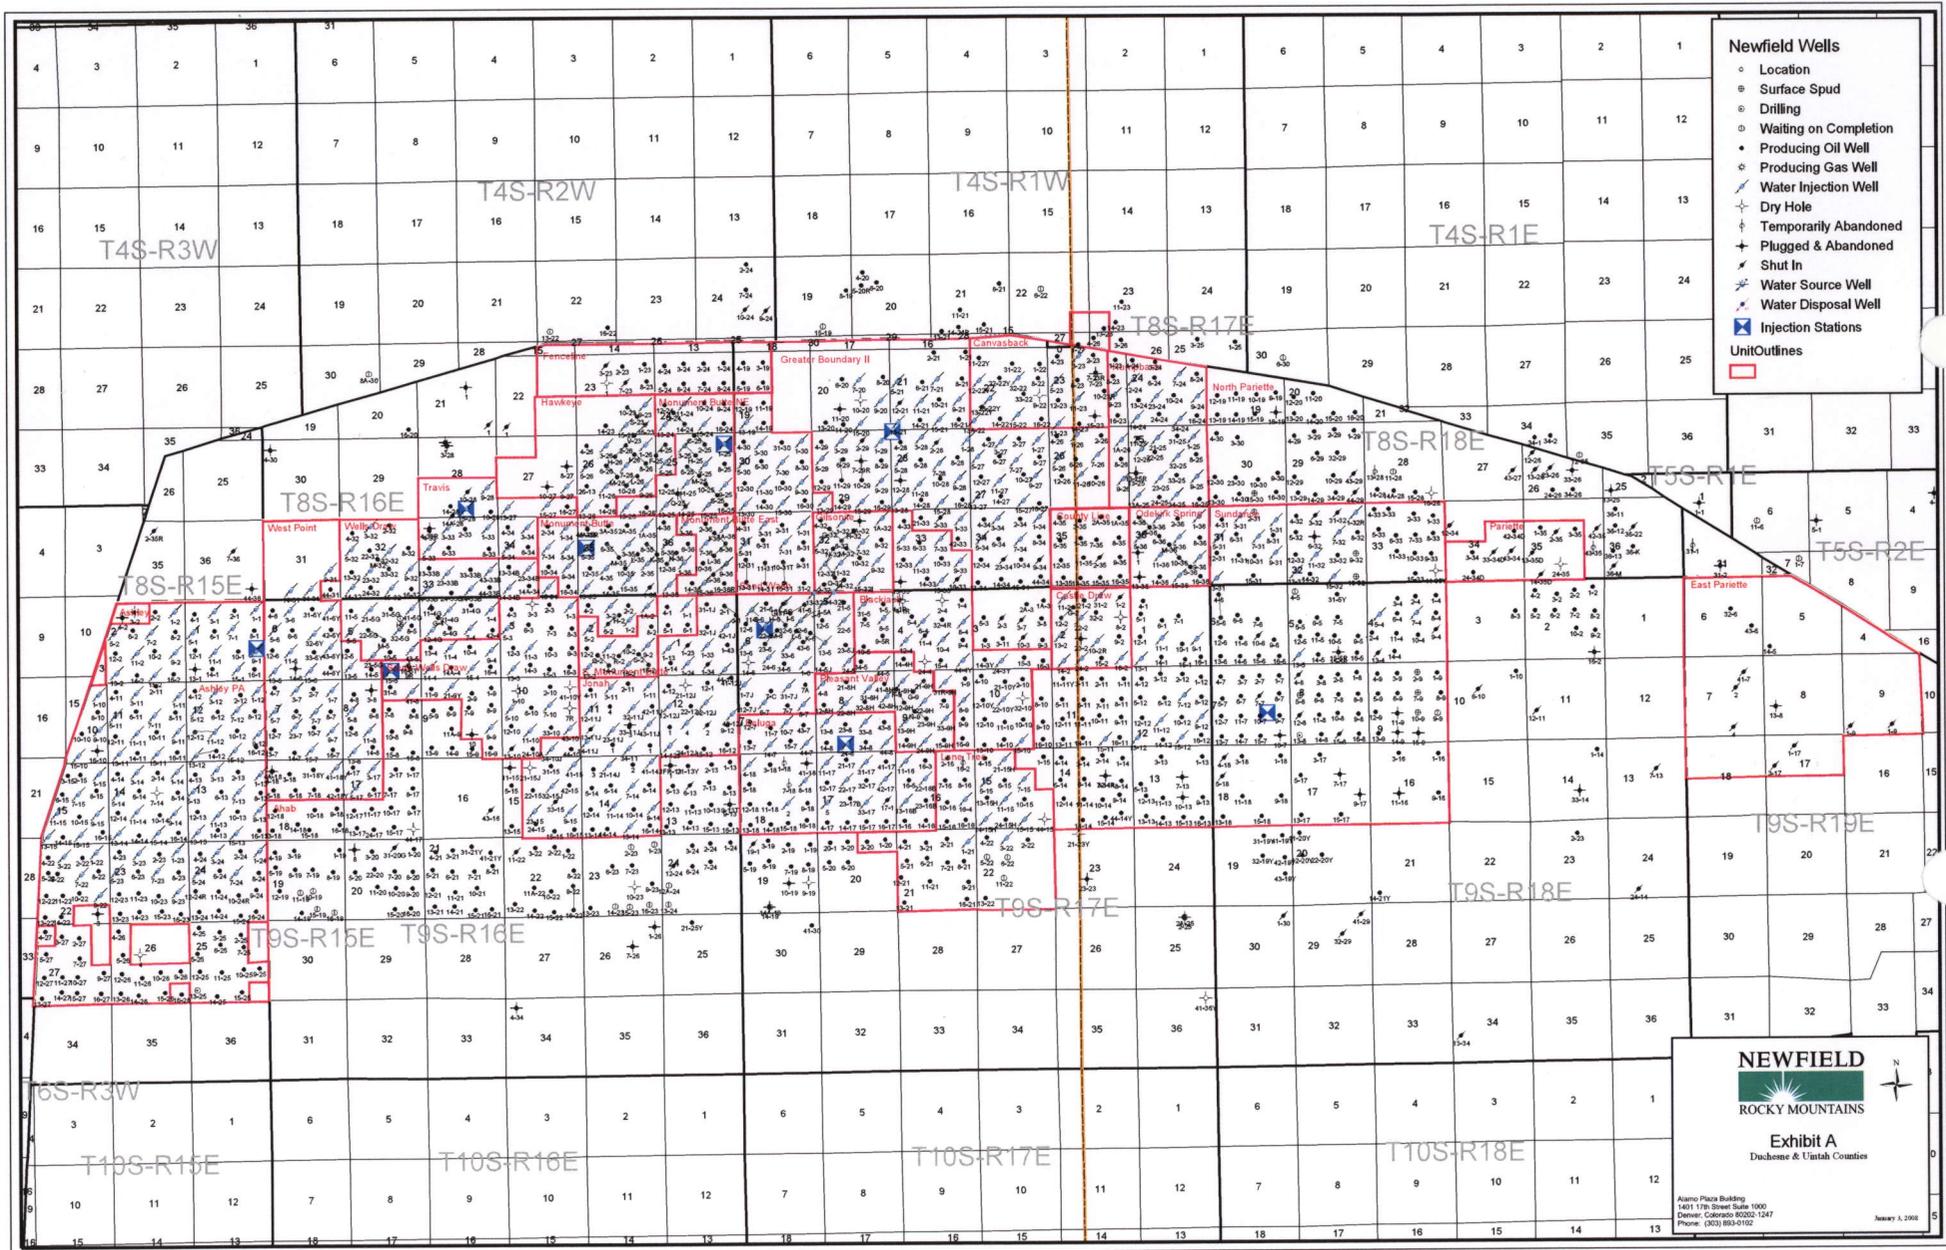

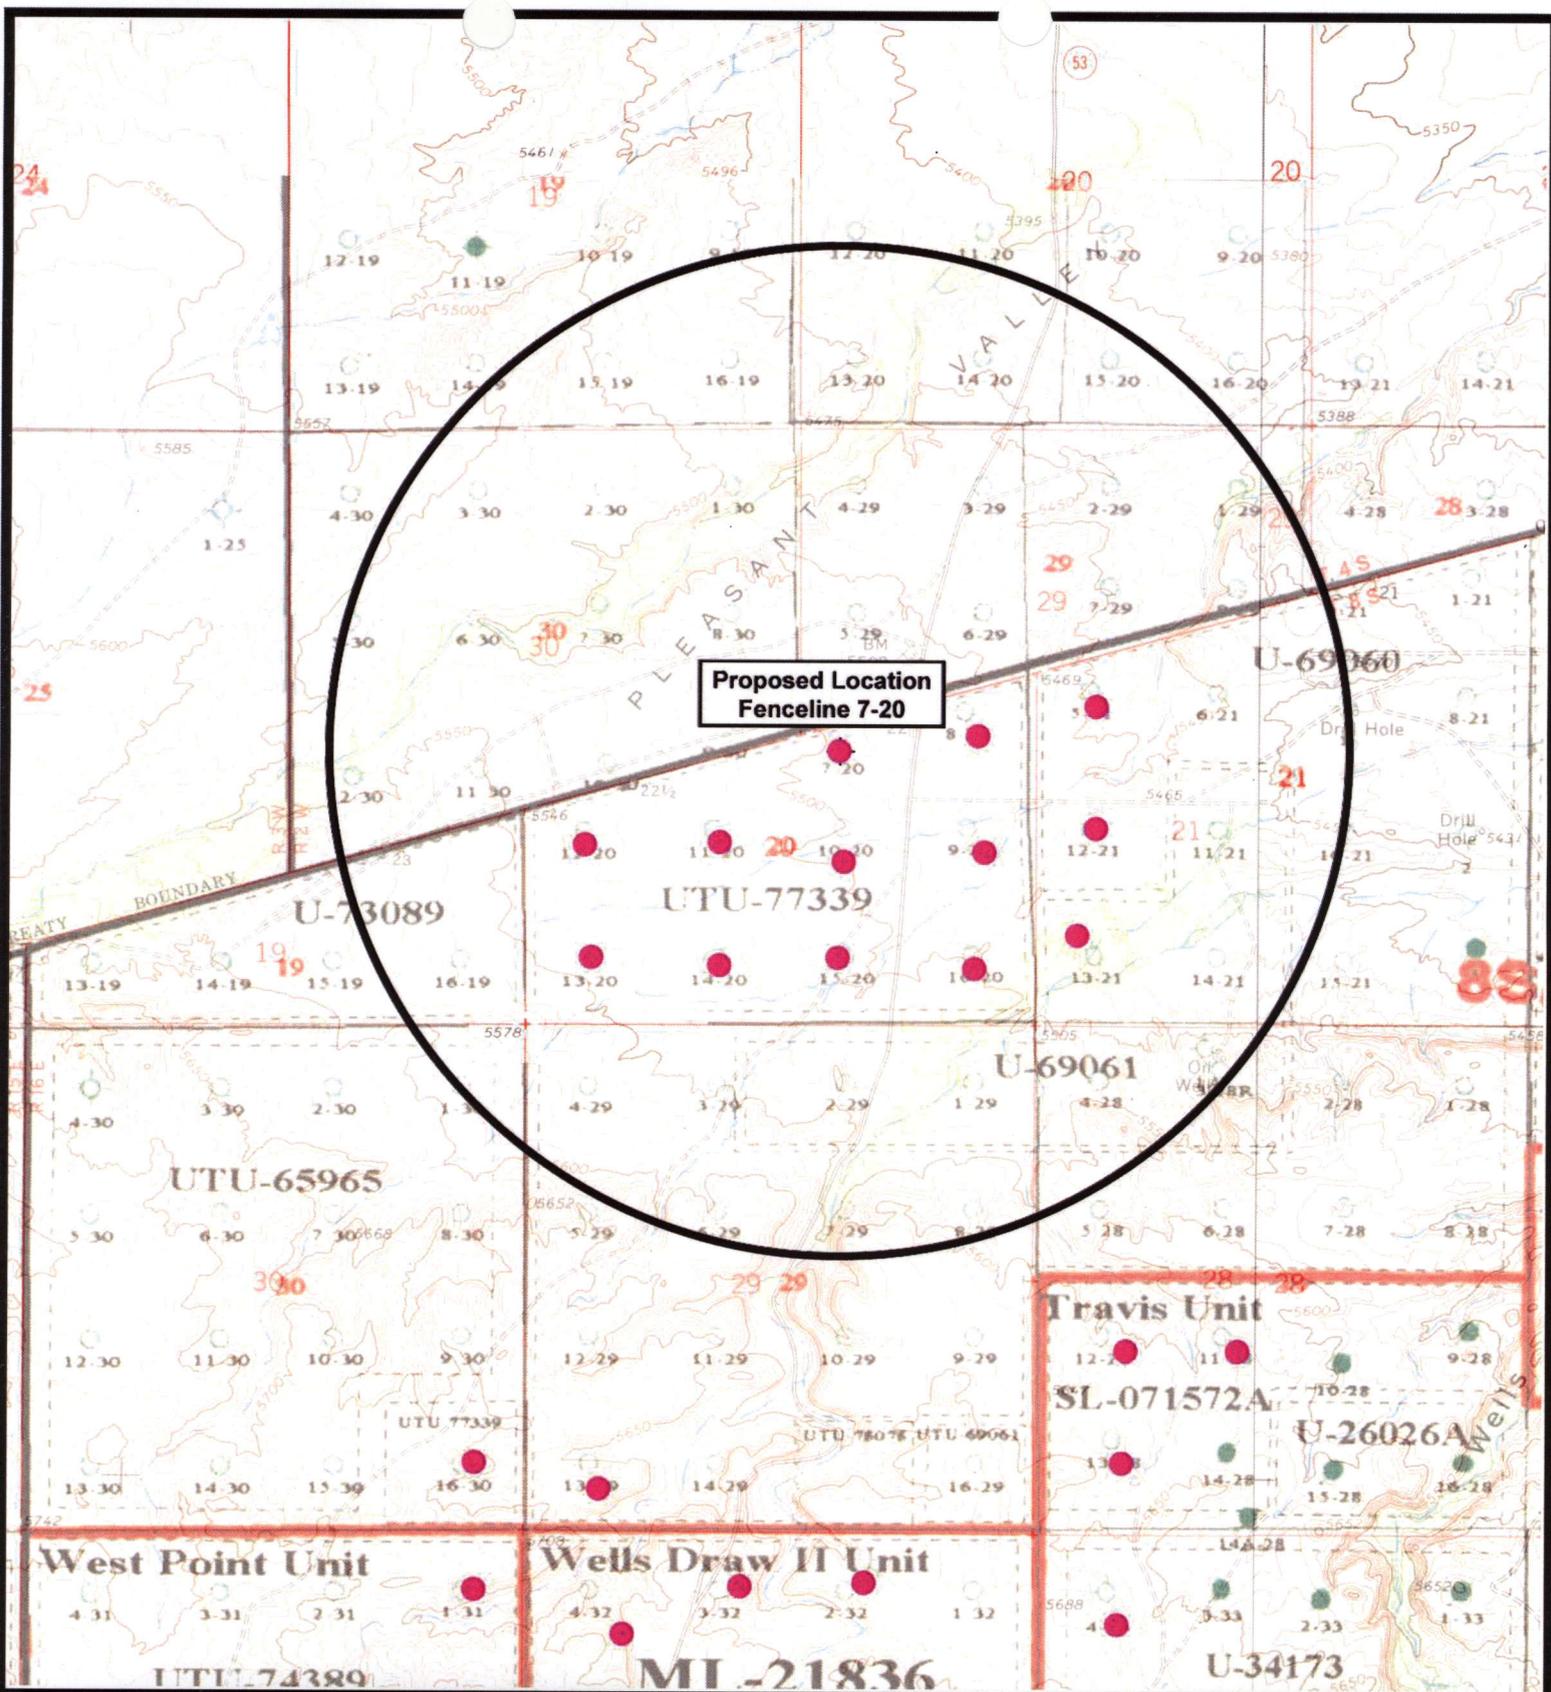

**Proposed Location
Fenceline 7-20**



NEWFIELD
Exploration Company

**Fenceline 7-20-8-16
SEC. 20, T8S, R16E, S.L.B.&M.**



Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 01-03-2008

Legend

- Location
- One-Mile Radius

Exhibit "B"

2-M SYSTEM

Blowout Prevention Equipment Systems

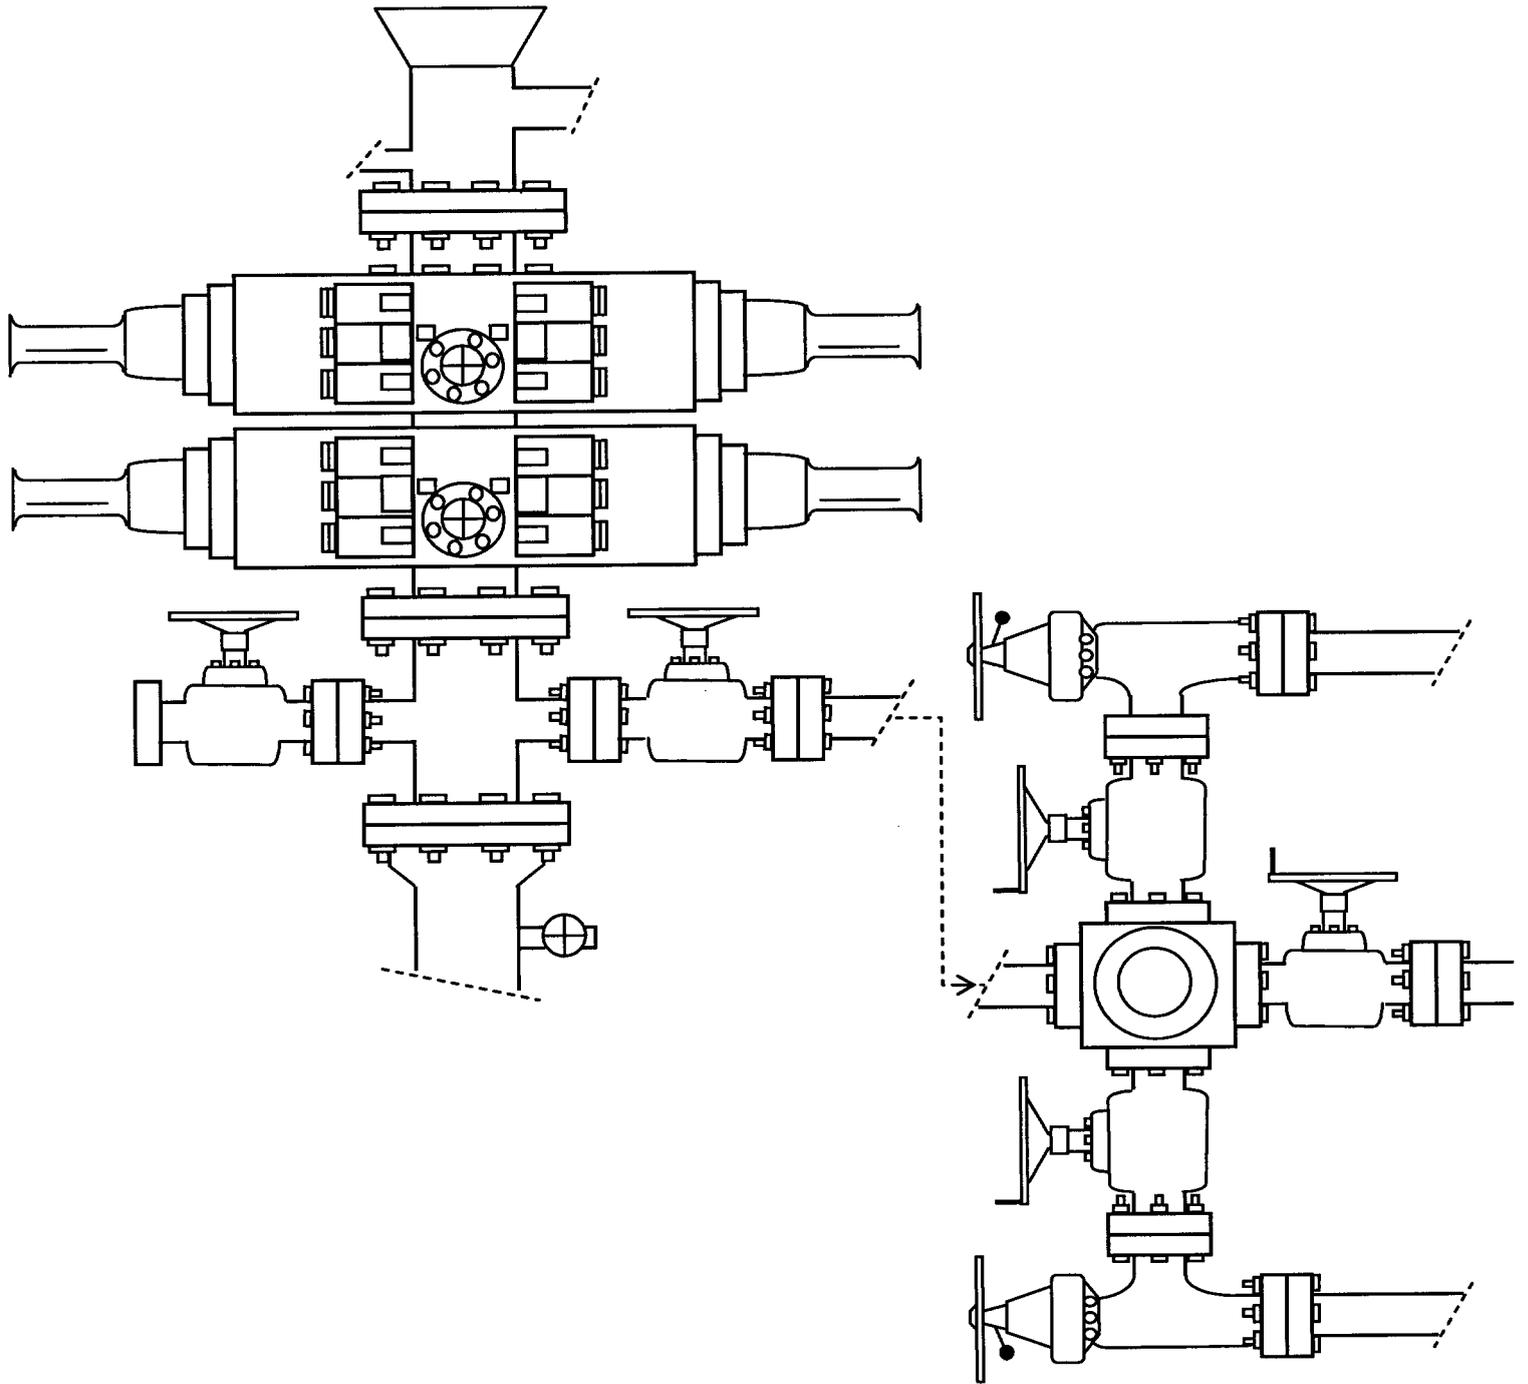


EXHIBIT C

Exhibit "D"

1 of 2

CULTURAL RESOURCE INVENTORY OF
NEWFIELD EXPLORATION'S NINE 40 ACRE PARCELS:
7-20, 8-20, 9-20, 10-20, 11-20, 12-20, 13-20, 14-20,
AND 15-20 (T 8S, R 16E, SECTION 20)
DUCHESNE COUNTY, UTAH

By:

Patricia Stavish

Prepared For:

Bureau of Land Management
Vernal Field Office

Prepared Under Contract With:

Newfield Exploration Company
Rt. 3 Box 3630
Myton, UT 84052

Prepared By:

Montgomery Archaeological Consultants, Inc.
P.O. Box 219
Moab, Utah 84532

MOAC Report No. 08-102

May 9, 2008

United States Department of Interior (FLMPA)
Utah Permit No. 08-UT-60122

State of Utah Antiquities Project (Survey)
Permit No. U-08-MQ-0337b

NEWFIELD EXPLORATION COMPANY

**PALEONTOLOGICAL SURVEY OF PROPOSED
PRODUCTION DEVELOPMENT AREAS,
DUCHESNE & UINTAH COUNTIES, UTAH**

Section 21, T 8 S, R 16 E [Entire section excluding NE/NW (3-21) & NW/NW(4-21)];
Section 20, T 8 S, R 16 E [SW/NE (7-20), SE/NE (8-20), NE/SE (9-20), NW/SE (10-20),
NE/SW (11-20), NW/SW (12-20), SW/SW (13-20), SE/SW (14-20), & SW/SE (15-20);
SE/SE, Section 32, T 8 S, R 18 E (16-32-8-18), NE/NE, Section 36, T 8 S, R 17 E (1-36-8-17),
NE/NW & SW/NW, Section 18, T 9 S, R 19 E (3 & 5-18-9-19), and Proposed Water Injection
Line at SE/SW, Section 1, T 9 S, R 15 E (14-1-9-15).

REPORT OF SURVEY

Prepared for:

Newfield Exploration Company

Prepared by:

Wade E. Miller
Consulting Paleontologist
April 30 & May 1, 2008

**WORKSHEET
APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 06/04/2008

API NO. ASSIGNED: 43-013-33997

WELL NAME: FEDERAL 7-20-8-16

OPERATOR: NEWFIELD PRODUCTION (N2695)

PHONE NUMBER: 435-646-3721

CONTACT: MANDIE CROZIER

PROPOSED LOCATION:

NWSE 20 080S 160E

SURFACE: 0530 FNL 2028 FEL

BOTTOM: 0530 FNL 2028 FEL

COUNTY: DUCHESNE

LATITUDE: 40.10332 LONGITUDE: -110.1404

UTM SURF EASTINGS: 573270 NORTHINGS: 4439369

FIELD NAME: UNDESIGNATED (2)

INSPECT LOCATN BY: / /		
Tech Review	Initials	Date
Engineering		
Geology		
Surface		

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-77339

PROPOSED FORMATION: GRRV

SURFACE OWNER: 1 - Federal

COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:

- Plat
- Bond: Fed[1] Ind[] Sta[] Fee[]
(No. WYB000493)
- Potash (Y/N)
- Oil Shale 190-5 (B) or 190-3 or 190-13
- Water Permit
(No. 43-10136)
- RDCC Review (Y/N)
(Date: _____)
- Fee Surf Agreement (Y/N)
- Intent to Commingle (Y/N)

LOCATION AND SITING:


- R649-2-3.
- Unit: _____
- R649-3-2. General
- Siting: 460 From Qtr/Qtr & 920' Between Wells
- R649-3-3. Exception
- Drilling Unit
- Board Cause No: _____
- Eff Date: _____
- Siting: _____
- R649-3-11. Directional Drill

COMMENTS:

See Separate file

STIPULATIONS:

- 1- Educt Approval*
- 2- Spacing Strip*

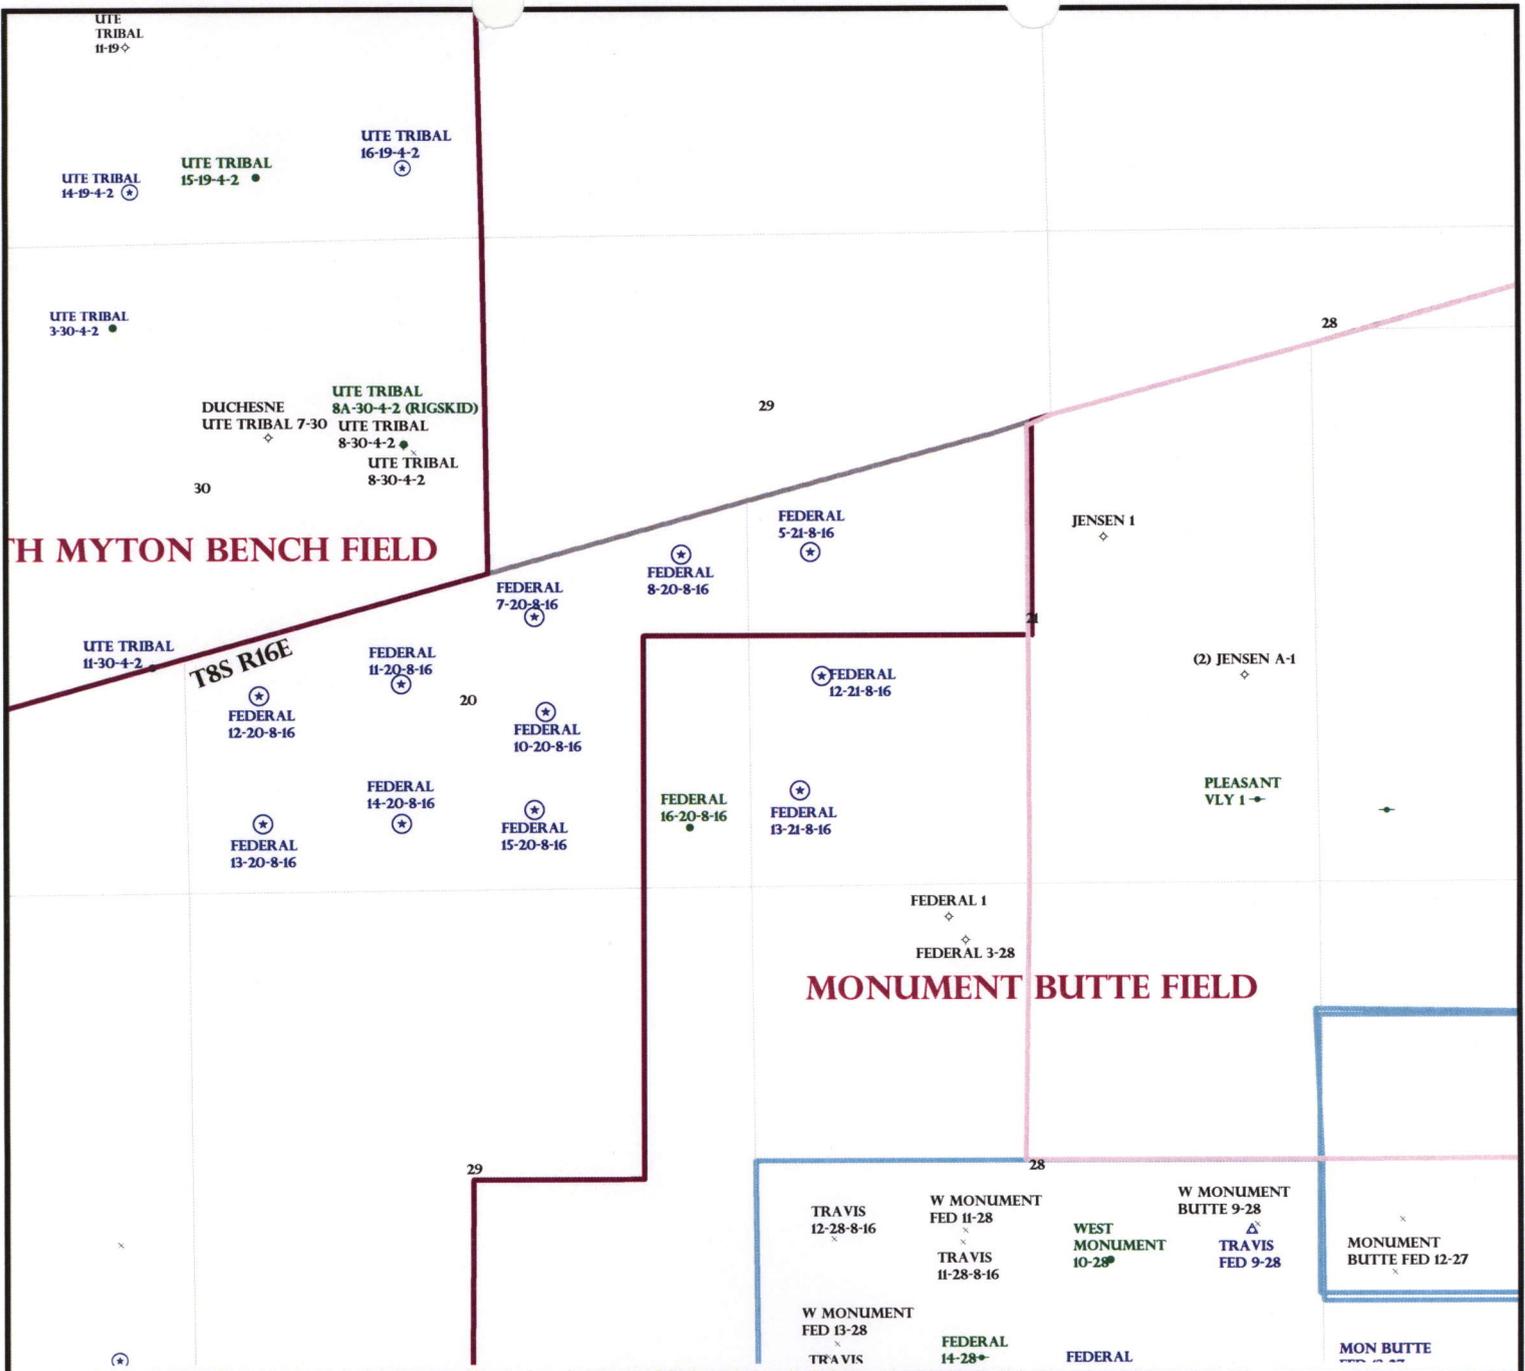

OPERATOR: NEWFIELD PROD CO (N2695)

SEC: 20 T.8S R. 16E

FIELD: UNDESIGNATED(002)

COUNTY: DUCHESNE

SPACING: R649-3-3 / EXCEPTION LOCATION

- Field Status**
- ABANDONED
 - ACTIVE
 - COMBINED
 - INACTIVE
 - PROPOSED
 - STORAGE
 - TERMINATED

- Unit Status**
- EXPLORATORY
 - GAS STORAGE
 - NF PP OIL
 - NF SECONDARY
 - PENDING
 - PI OIL
 - PP GAS
 - PP GEOTHERML
 - PP OIL
 - SECONDARY
 - TERMINATED

- Wells Status**
- ✂ GAS INJECTION
 - ✂ GAS STORAGE
 - ✂ LOCATION ABANDONED
 - ✂ NEW LOCATION
 - ✂ PLUGGED & ABANDONED
 - ✂ PRODUCING GAS
 - ✂ PRODUCING OIL
 - ✂ SHUT-IN GAS
 - ✂ SHUT-IN OIL
 - ✂ TEMP. ABANDONED
 - ✂ TEST WELL
 - ✂ WATER INJECTION
 - ✂ WATER SUPPLY
 - ✂ WATER DISPOSAL
 - ✂ DRILLING



OIL, GAS & MINING



PREPARED BY: DIANA MASON
DATE: 04-JUNE-2008



June 10, 2008

Abo Petroleum Corporation
PO Box 900
Artesia, NM 88211

RE: Exception Location
Federal 7-20-8-16
Duchesne County, Utah

Ladies and/or Gentlemen;

Please be advised Newfield Production Company has submitted an application for permit to drill for the following well:

Federal 7-20-8-16
UTU-77339
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

This well is located outside of the drilling window as required by State of Utah R649-3-2 due to issues with the terrain. It is necessary to obtain your written concurrence with this exception location as a 10% working interest owner in UTU-77339, the lease the well will be drilled on.

Enclosed you will find a plat showing the location of the above referenced well. If you are in agreement to this location, please verify your consent by signing and dating where indicated on page 2 of this letter and returning to my attention as soon as possible by fax to 303-893-0103 or email at reveland@newfield.com.

If you have any questions or need further information, please do not hesitate to contact me at 303-382-4444. I appreciate your prompt attention to this matter.

Sincerely,

A handwritten signature in cursive script that reads "Roxann Eveland".

Roxann Eveland
Land Associate


Enclosure

TO: Newfield Production Company
Attn: Roxann Eveland
reveland@newfield.com
303-893-0103 fax

RE: Exception Location
Federal 7-20-8-16
UTU-77339
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

Please be advised Abo Petroleum Corporation does not have an objection to the proposed location of the
aforementioned well.

ABO PETROLEUM CORPORATION

By: 
Cody J. Moore
Associate Landman
Print Name and Title

Date: July 7, 2008



June 10, 2008

Myco Industries Inc.
PO Box 840
Artesia, NM 88211

RE: Exception Location
Federal 7-20-8-16
Duchesne County, Utah

Ladies and/or Gentlemen;

Please be advised Newfield Production Company has submitted an application for permit to drill for the following well:

Federal 7-20-8-16
UTU-77339
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

This well is located outside of the drilling window as required by State of Utah R649-3-2 due to issues with the terrain. It is necessary to obtain your written concurrence with this exception location as a 10% working interest owner in UTU-77339, the lease the well will be drilled on.

Enclosed you will find a plat showing the location of the above referenced well. If you are in agreement to this location, please verify your consent by signing and dating where indicated on page 2 of this letter and returning to my attention **as soon as possible** by fax to 303-893-0103 or email at reveland@newfield.com.

If you have any questions or need further information, please do not hesitate to contact me at 303-382-4444. I appreciate your prompt attention to this matter.

Sincerely,

A handwritten signature in cursive script that reads "Roxann Eveland".

Roxann Eveland
Land Associate


Enclosure

TO: Newfield Production Company
Attn: Roxann Eveland
reveland@newfield.com
303-893-0103 fax

RE: Exception Location
Federal 7-20-8-16
UTU-77339
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

Please be advised Myco Industries Inc. does not have an objection to the proposed location of the aforementioned well.

MYCO INDUSTRIES INC.

By: 
Cody Moore
Associate Landman
Print Name and Title

Date: July 7, 2008



June 10, 2008

Yates Drilling Company
ATTN: Cody Moore
105 S. 4th Street
Artesia, NM 88210

RE: Exception Location
Federal 7-20-8-16
Duchesne County, Utah

Dear Mr. Moore;

Please be advised Newfield Production Company has submitted an application for permit to drill for the following well:

Federal 7-20-8-16
UTU-77339
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

This well is located outside of the drilling window as required by State of Utah R649-3-2 due to issues with the terrain. It is necessary to obtain your written concurrence with this exception location as a 10% working interest owner in UTU-77339, the lease the well will be drilled on.

Enclosed you will find a plat showing the location of the above referenced well. If you are in agreement to this location, please verify your consent by signing and dating where indicated on page 2 of this letter and returning to my attention **as soon as possible** by fax to 303-893-0103 or email at reveland@newfield.com.

If you have any questions or need further information, please do not hesitate to contact me at 303-382-4444. I appreciate your prompt attention to this matter.

Sincerely,

A handwritten signature in cursive script that reads "Roxann Eveland".

Roxann Eveland
Land Associate


Enclosure

TO: Newfield Production Company
Attn: Roxann Eveland
reveland@newfield.com
303-893-0103 fax

RE: Exception Location
Federal 7-20-8-16
UTU-77339
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

Please be advised Yates Drilling Company does not have an objection to the proposed location of the
aforementioned well.

YATES DRILLING COMPANY

By:  Date: July 7, 2008
Cody J. Moore
Associate Landman
Print Name and Title



June 10, 2008

Yates Petroleum Corporation
ATTN: Cody Moore
105 S. 4th Street
Artesia, NM 88210

RE: Exception Location
Federal 7-20-8-16
Duchesne County, Utah

Dear Mr. Moore;

Please be advised Newfield Production Company has submitted an application for permit to drill for the following well:

Federal 7-20-8-16
UTU-77339
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

This well is located outside of the drilling window as required by State of Utah R649-3-2 due to issues with the terrain. It is necessary to obtain your written concurrence with this exception location as a 20% working interest owner in UTU-77339, the lease the well will be drilled on.

Enclosed you will find a plat showing the location of the above referenced well. If you are in agreement to this location, please verify your consent by signing and dating where indicated on page 2 of this letter and returning to my attention as soon as possible by fax to 303-893-0103 or email at reveland@newfield.com.

If you have any questions or need further information, please do not hesitate to contact me at 303-382-4444. I appreciate your prompt attention to this matter.

Sincerely,

A handwritten signature in cursive script that reads "Roxann Eveland".

Roxann Eveland
Land Associate

Enclosure

TO: Newfield Production Company
Attn: Roxann Eveland
reveland@newfield.com
303-893-0103 fax

RE: Exception Location
Federal 7-20-8-16
UTU-77339
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

Please be advised Yates Petroleum Corporation does not have an objection to the proposed location of the
aforementioned well.

YATES PETROLEUM CORPORATION

By:



Cody J. Moore
Associate Landman
Print Name and Title

Date: July 7, 2008



July 21, 2008

State of Utah, Division of Oil, Gas & Mining
ATTN: Diana Mason
PO Box 145801
Salt Lake City, UT 84114-5801

RE: Exception Location
Federal 7-20-8-16
T8S R16E, Section 20: Lot 2
530' FNL 2028' FEL
Duchesne County, Utah

Dear Ms. Mason;

Pursuant to Rule 649-3-3 of the Oil & Gas Rules and Regulations of the State of Utah, Newfield Production Company ("NPC") hereby requests an exception location for the drilling of the captioned well. The proposed drillsite for this well is located 119' south of the drilling window required by Rule R649-3-2, which requires a well to be located in the center of a forty (40) acre quarter-quarter section, or a substantially equivalent lot or tract, with a tolerance of two hundred (200) feet in any direction from the center.

The attached plat depicts the proposed location and illustrates the deviation from the drilling window. The requested location is outside of the required drilling window due to the irregular size of the lot it is located on.

Please note the drillsite and all acreage within 460' is on U-77339, which is owned by NPC 50%, Yates Petroleum Corporation 20%, Yates Drilling Company 10%, Abo Petroleum Corporation 10% and Myco Industries Inc. 10%. You will find copies of consent letters from the aforementioned owners attached to this letter.

If you have any questions or require further information, please do not hesitate to contact the undersigned at 303-382-4444 or by email at reveland@newfield.com. Your consideration of this matter is greatly appreciated.

Sincerely,

A handwritten signature in cursive script that reads "Roxann Eveland".

Roxann Eveland
Land Associate

Attachment

RECEIVED

JUL 25 2008

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER


FORM APPROVED
OMB No. 1004-0136
Expires January 31, 2004

5a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU-77339
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name N/A
2. Name of Operator Newfield Production Company		7. If Unit or CA Agreement, Name and No. N/A
3a. Address Route #3 Box 3630, Myton UT 84052		8. Lease Name and Well No. Federal 7-20-8-16
3b. Phone No. (include area code) (435) 646-3721		9. API Well No.
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NW/SE (Lot #2) 530' FNL 2028' FEL At proposed prod. zone		10. Field and Pool, or Exploratory Monument Butte
14. Distance in miles and direction from nearest town or post office* Approximately 8.0 miles southwest of Myton, Utah		11. Sec., T., R., M., or Blk. and Survey or Area NW/SE Sec. 20, T8S R16E
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 530' f/lse, NA' f/unit	16. No. of Acres in lease 557.08	12. County or Parish Duchesne
17. Spacing Unit dedicated to this well 40 Acres	13. State UT	
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1007'	19. Proposed Depth 6540'	20. BLM/BIA Bond No. on file WYB000493
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5496' GL	22. Approximate date work will start* 4th Quarter 2008	23. Estimated duration Approximately seven (7) days from spud to rig release.

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- | | |
|---|--|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature 	Name (Printed/Typed) Mandie Crozier	Date 5/28/08
Title Regulatory Specialist		
Approved by (Signature)	Name (Printed/Typed)	Date
Title	Office	

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on reverse)

RECEIVED
JUL 25 2008
DIV. OF OIL, GAS & MINING


T8S, R16E, S.L.B.&M.

NEWFIELD PRODUCTION COMPANY

WELL LOCATION:
FENCELINE 7-20-8-16

ELEV. UNGRADED GROUND = 5496.2'

WELL LOCATION, FENCELINE 7-20-8-16,
LOCATED AS SHOWN IN THE NW 1/4 SE
1/4 (LOT 2) OF SECTION 20, T8S, R16E,
S.L.B.&M. DUCHESNE COUNTY, UTAH.

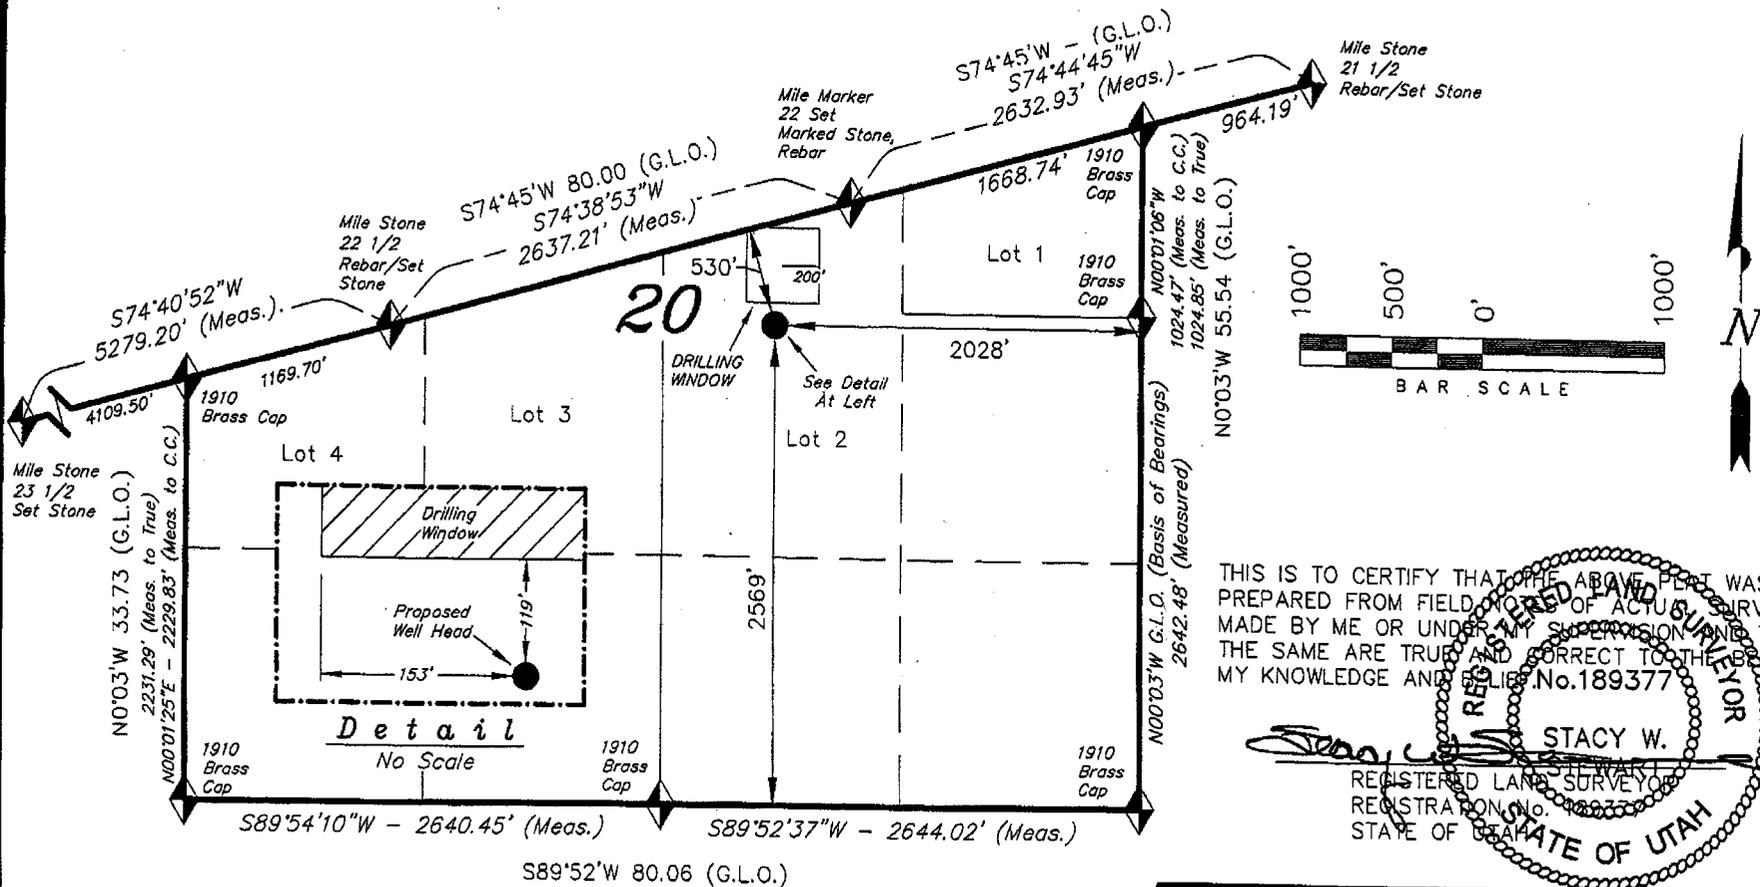

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
MADE BY ME OR UNDER MY SUPERVISION AND THAT
THE SAME ARE TRUE AND CORRECT TO THE BEST OF
MY KNOWLEDGE AND BELIEF. No. 189377

REGISTERED LAND SURVEYOR
STACY W.
REGISTRATION No. 189377
STATE OF UTAH

◆ = SECTION CORNERS LOCATED

BASIS OF ELEV;
U.S.G.S. 7-1/2 min QUAD (MYTON SW)

FENCELINE 7-20-8-16
(Surface Location) NAD 83
LATITUDE = 40° 06' 11.62"
LONGITUDE = 110° 08' 27.91"

TRI STATE LAND SURVEYING & CONSULTING
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

DATE SURVEYED: 11-26-07	SURVEYED BY: C.M.
DATE DRAWN: 12-17-07	DRAWN BY: F.T.M.
REVISED:	SCALE: 1" = 1000'



JON M. HUNTSMAN, JR.
Governor

GARY R. HERBERT
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

July 31, 2008

Newfield Production Company
Rt. #3, Box 3630
Myton, UT 84052

Re: Federal 7-20-8-16 Well, 530' FNL, 2028' FEL, NW SE, Sec. 20, T. 8 South, R. 16 East,
Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

Appropriate information has been submitted to DOGM and administrative approval of the requested exception location is hereby granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-33997.

Sincerely,

Gil Hunt
Associate Director

pab
Enclosures

cc: Duchesne County Assessor
Bureau of Land Management, Vernal Office



Operator: Newfield Production Company

Well Name & Number Federal 7-20-8-16

API Number: 43-013-33997

Lease: UTU-77339

Location: NW SE **Sec.** 20 **T.** 8 South **R.** 16 East

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

2. Notification Requirements

Notify the division within 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dustin Doucet at (801) 538-5281 (801) 733-0983 home

3. Reporting Requirements

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.

5. This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.

RECEIVED
VERNAL FIELD OFFICE

Form 3160-3
(September 2001)

2008 JUN 4 PM 1 10

FORM APPROVED
OMB No. 1004-0136
Expires January 31, 2004

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No. UTU-77339
6. If Indian, Allottee or Tribe Name N/A
7. If Unit or CA Agreement, Name and No. N/A
8. Lease Name and Well No. Federal 7-20-8-16
9. API Well No. 43 013 33997
10. Field and Pool, or Exploratory Monument Butte
11. Sec., T., R., M., or Blk. and Survey or Area NW/SE Sec. 20, T8S R16E
12. County or Parish Duchesne
13. State UT

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone
2. Name of Operator Newfield Production Company
3a. Address Route #3 Box 3630, Myton UT 84052
3b. Phone No. (include area code) (435) 646-3721
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NW/SE (Lot #2) 530' FNL 2028' FEL At proposed prod. zone
14. Distance in miles and direction from nearest town or post office* Approximatley 8.0 miles southwest of Myton, Utah
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 530' fl/se, NA' fl/unit
16. No. of Acres in lease 557.08
17. Spacing Unit dedicated to this well 40 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1007'
19. Proposed Depth 6540'
20. BLM/BIA Bond No. on file WYB000493
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5496' GL
22. Approximate date work will start* 4th Quarter 2008
23. Estimated duration Approximately seven (7) days from spud to rig release.
24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- | | |
|---|--|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification. |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 5/28/08
Title Regulatory Specialist		
Approved by (Signature) <i>Jerry Kenczka</i>	Name (Printed/Typed) JERRY KENCZKA	Date SEP 17 2008
Title Assistant Field Manager Lands & Mineral Resources	Office VERNAL FIELD OFFICE	

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on reverse)

NOTICE OF APPROVAL

CONDITIONS OF APPROVAL ATTACHED

RECEIVED

SEP 23 2008

DIV. OF OIL, GAS & MINING

NOS 3/17/08

08PP0569A



**UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE**

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company
Well No: Federal 7-20-8-16
API No: 43-013-33997

Location: Lot 2, Sec 20, T8S, R16E
Lease No: UTU-77339
Agreement: N/A

Title	Name	Office Phone Number	Cell Phone Number
Petroleum Engineer:	Matt Baker	(435) 781-4490	(435) 828-4470
Petroleum Engineer:	Michael Lee	(435) 781-4432	(435) 828-7875
Petroleum Engineer:	James Ashley	(435) 781-4470	(435) 828-7874
Petroleum Engineer:	Ryan Angus	(435) 781-4430	(435) 828-7368
Supervisory Petroleum Technician:	Jamie Sparger	(435) 781-4502	(435) 828-3913
Supervisory NRS:	Karl Wright	(435) 781-4484	
NRS/Enviro Scientist:	Holly Villa	(435) 781-4404	(435) 828-3544
NRS/Enviro Scientist:	James Hereford	(435) 781-3412	(435) 828-3546
NRS/Enviro Scientist:	Chuck Macdonald	(435) 781-4441	(435) 828-7481
NRS/Enviro Scientist:	Dan Emmett	(435) 781-3414	(435) 828-4029
NRS/Enviro Scientist:	Paul Percival	(435) 781-4493	(435) 828-7381
NRS/Enviro Scientist:	Anna Figueroa	(435) 781-3407	(435) 828-3548
NRS/Enviro Scientist:	Verlyn Pindell	(435) 781-3402	(435) 828-3547
NRS/Enviro Scientist:	Nathan Packer	(435) 781-3405	(435) 828-3545

Fax: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify NRS/Enviro Scientist)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify NRS/Enviro Scientist)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supervisory Petroleum Technician)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings
BOP & Related Equipment Tests (Notify Supervisory Petroleum Technician)	-	Twenty-Four (24) hours prior to initiating pressure tests
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days

SURFACE USE PROGRAM CONDITIONS OF APPROVAL (COAs)

General Surface COAs

- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

Specific Surface COAs

STIPULATIONS:

- An active colony of prairie dogs and their burrows (burrowing owl habitat) were observed on and around the proposed site. With this occurrence there will be a timing restriction during project activity (construction and drilling) to minimize disturbance during Burrowing Owl nesting from April 1 – July 15.
- The proposed area contains Mountain plover habitat. With this occurrence there will be a timing restriction during project activity (construction and drilling) to minimize disturbance during Mountain plover nesting from May 1 – June 15.

Lease Notices from RMP:

- The lessee/operator is given notice the area has been identified as containing Golden eagle habitat. Modifications may be required in the Surface Use Plan to protect the Golden eagle and/or its habitat from surface disturbance activities in accordance with Section 6 of the lease terms, Endangered Species Act, and 43 CFR 3101.1-2.

Comments:

If it is anticipated that construction or drilling will occur during the given timing restrictions for any wildlife, a BLM or qualified biologist shall be notified so surveys can be conducted. Depending upon the results of the surveys, permission to proceed may or may not be recommended or granted (depending on the species being surveyed and the condition of the habitat).

Follow-up Actions and/or Recommendations:

Please be aware that this Special Status Species wildlife clearance is effective for 1 year from the date of the onsite date. Any proposals submitted after the date of this report (onsite) shall require additional surveys and clearances.

CONDITIONS OF APPROVAL:

- All traffic related to this action will be restricted to approved routes. Cross-country vehicle travel will not be allowed.
- All pipelines (surface and buried) will be laid within one 50' wide construction ROW, on one side of the road, and will reduce down to a 30' wide permanent ROW on lease.

- A temporary road ROW will not be granted. The road ROW will be 30 foot for construction and will reduce to an 18 foot running surface.
- The access road will be crowned and ditched. Flat-bladed roads are not allowed. All roads will have an 18', crowned (2 to 3% minimum), running surface. All roads will have drainage ditches along both sides of road.
- No vehicle travel, construction or routine maintenance activities shall be performed during periods when the soil is too wet to adequately support vehicles and/or construction equipment. If such equipment creates ruts in excess of three inches deep, the soil shall be deemed too wet to adequately support construction equipment.
- If additional erosion occurs during the life of this project, more culverts, low water crossings, berms, wing ditches or etc. will be needed to control the erosion.
- Low-water crossings will be appropriately constructed to avoid sedimentation of drainage ways and other water resources.
- Pipelines will be buried at all major drainage crossings.
- Prevent fill and stock piles from entering drainages.
- To insure impermeability, the reserve pit will be lined with a 16 ml or greater liner and felt prior to spudding.
- The liner is to be cut 5 feet below ground surface or at the level of the cuttings, whichever is deeper, and the excess liner material is to be disposed of at an authorized disposal site.
- When the reserve pit contains fluids or toxic substances, the operator must ensure animals do not ingest or become entrapped in pit fluids.
- Any hydrocarbons in the reserve pit will be removed immediately upon well completion; in accordance with 43 CFR 3162.7-1. Pits must be free of oil and other liquid and solid wastes prior to filling.
- Monument Butte SOP, Section 9.2 - Pit Fencing Minimum Standards - will be strictly adhered to. To include 9.2.2.3 - Corner posts will be cemented and/or braced in such a manner as to keep fence tight at all times.
- If Uinta Basin hookless cactus or other special status plants are found, construction will cease and the AO will be notified to determine the appropriate mitigation.
- Within 90 calendar days of the approval date for this Application for Permit to Drill (APD), the operator/lessee shall submit to the Authorized Officer (AO), on Sundry Notice Form 3160-5, an Interim/Final Surface Reclamation Plan for surface disturbance on well pads, access roads, and pipelines. At a minimum, this will include the reshaping of the pad to the original contour to the extent possible; the respreading of the top soil up to the rig anchor points; and, the area reseeded using appropriate reclamation methods. The AO will provide written approval or concurrence within 30 calendar days of receipt.

Interim Reclamation:

- The topsoil from the reserve pit shall be stripped and piled separately near the reserve pit. When the reserve pit is closed, it shall be recontoured and the topsoil respread, and the area shall be seeded using a rangeland drill. Seeding depth as per AO, or seed distributor. If portions of the site are too steep (>40%), or rocky, that portion may be broadcast seeded. If broadcasting seed, the seed shall be walked into the soil with a dozer immediately after the seeding is completed, or covered by soil using a drag chain. Seeding shall occur in the fall (August 1st until snow or ground is frozen) with the following seed mix:

Seed mix:

Common name	Latin name	lbs/acre	Recommended seed planting depth
Squirreltail grass	<i>Elymus elymoides</i>	5.0	¼ - ½"
Siberian wheatgrass	<i>Agropyron fragile</i>	3.0	½"
Shadscale saltbush	<i>Atriplex confertifolia</i>	0.50	½"
Four-wing saltbush	<i>Atriplex canescens</i>	0.50	½"
Gardner's saltbush	<i>Atriplex gardneri</i>	0.50	½"
Scarlet globemallow	<i>Sphaeralcea coccinea</i>	0.20	⅛ - ¼"

- All pounds are pure live seed.
- All seed and mulch will be certified weed free.
- Rates are set for drill seeding; double rate if broadcasting.
- Reseeding may be required if initial seeding is not successful.

Final reclamation:

- Once the location is plugged and abandoned, the well location, access, and any disturbed areas shall be recontoured to natural topography, topsoil shall be respread, and the entire location shall be seeded following guidelines in the seed mix bullet statement above. Final seed mix: same as interim.
- Noxious and/or invasive weeds will be controlled along access roads, pipelines, well sites, and all other applicable facilities. Any noxious and/or invasive weeds outbreak, directly attributed to the activities of the Operator, will be the responsibility of the Operator to control. On BLM administered land, a Pesticide Use Proposal (PUP) must be submitted and approved prior to the application of herbicides, pesticides, or other possibly hazardous chemicals.
- The topsoil from the reserve pit shall be stripped and piled separately near the reserve pit. When the reserve pit is closed, it shall be recontoured and the topsoil respread, and the area shall be seeded in the same manner as the location topsoil.
- Once the location is plugged and abandoned, it shall be recontoured to natural topology, topsoil shall be respread, and the entire location shall be seeded with a seed mix recommended by the AO (see above). Seed application will follow all guidelines in the interim seed mix bullet statement above. If reclamation seeding shall take place using the broadcast method, the seed at a minimum will be walked into the soil with a dozer immediately after the seeding is completed.
- The authorized officer may prohibit surface disturbing activities during severe winter conditions to minimize watershed damage. This limitation does not apply to operation and maintenance of producing wells.

- The authorized officer may prohibit surface disturbing activities during wet or muddy conditions to minimize watershed damage. This limitation does not apply to operation and maintenance of producing wells.
- All well facilities not regulated by OSHA will be painted Carlsbad Canyon.
- All boulders with a length or diameter greater than 3 feet, that are found showing at the surface, will be stockpiled for use during final reclamation.
- Notify the Authorized Officer 48 hours prior to surface disturbing activities.

DOWNHOLE CONDITIONS OF APPROVAL

SITE SPECIFIC DOWNHOLE CONDITIONS OF APPROVAL

- None

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be

filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

^{Spud}
BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# NDSI NS
1 Submitted By Jim Smith Phone Number 823-2072
Well Name/Number Federal 7-20-8-176
Qtr/Qtr NW/SE Section 20 Township 8S Range 16E
Lease Serial Number UTU-77339
API Number 43-013-33997

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 10/16/08 1:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 10/16/08 5:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks Actural spud time

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM - FORM 6

OPERATOR: NEWFIELD PRODUCTION COMPANY
ADDRESS: RT. 3 BOX 3630
MYTON, UT 84052

OPERATOR ACCT. NO. N2695

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION				COUNTY	SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG			
A B	99999	17156	4301333997	FEDERAL 7-20-8-16	NWSE	20	8S	16E	DUCHESNE	10/16/2008	10/28/08
WELL 1 COMMENTS: <i>GERU</i>											
A	99999		4304730000	GUSHER FEDERAL 8-23-6-20	SENE	30	6S	20E	UINTAH	10/18/2008	
WELL 2 COMMENTS:											
B	99999	12308	4301333818	SANDWASH FEDERAL 1-31-8-17	NWNE	31	8S	17E	DUCHESNE	10/20/2008	10/28/08
WELL 3 COMMENTS: <i>GERU</i> <i>BAL = NWNE</i>											
A	99999	17157	4304739449	FEDERAL 1-23-9-17	NENE	23	9S	17E	UINTAH	10/22/2008	10/28/08
WELL 4 COMMENTS: <i>GERU</i>											
WELL 5 COMMENTS:											
WELL 6 COMMENTS:											


RECEIVED

OCT 23 2008

DIV. OF OIL, GAS & MINING

- ACTION CODES (See instructions on back of form)
- A - new entity for new well (single well only)
 - B - well to existing entity (group or unit well)
 - C - from one existing entity to another existing entity
 - D - well from one existing entity to a new entity
 - E - other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.


 Signature _____ JENTRI PARK
 Production Clerk _____ 10/23/08
 Date _____

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
 NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
 Myton, UT 84052

3b. Phone (include are code)
 435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
 530' FNL 2028'FEL
 NWSE Section 20 T8S R16E

5. Lease Serial No.
 USA UTU-77339

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or
 WELLS DRAW UNIT

8. Well Name and No.
 FEDERAL 7-20-8-16

9. API Well No.
 4301333997

10. Field and Pool, or Exploratory Area
 MONUMENT BUTTE

11. County or Parish, State
 DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INIDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 10/16/08 NDSI NS #1. Spud well @ 1:00PM. Drill 305'of 121/4" hole with air mist. TIH w/7 jt's 85/8" j-55 24# csqn. set @ 308.68KB. On 4/15/08 cement with 160 sks of class "G" w/ 3% CaCL2 + 1/4# sk Cello-Flake mixed @15.8 ppg>1.17 cf/sk yeild. Returned 4 bbls cement to pit. Woc.

I hereby certify that the foregoing is true and correct (Printed/ Typed) Jav Burton	Title Drilling Foreman
Signature 	Date 10/23/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by	Title	Date
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

RECEIVED

OCT 27 2008

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include area code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
530' FNL 2028' FEL
NWSE Section 20 T8S R16E

5. Lease Serial No.

USA UTU-77339

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.

FEDERAL 7-20-8-16

9. API Well No.

4301333997

10. Field and Pool, or Exploratory Area

MONUMENT BUTTE

11. County or Parish, State

DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Weekly Status Report _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recomplate in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 11/7/08 MIRU Patterson Rig # 155. Set all equipment. Pressure test Kelly, TIW, Choke manifold, & Bop's to 2,000 psi. Test 8.625 csgn to 1,500 psi. Vernal BLM field, & Roosevelt DOGM office was notified of test. PU BHA and tag cement @ 280'. Drill out cement & shoe. Drill a 7.875 hole with fresh water to a depth of 6500'. Lay down drill string & BHA. Open hole log w/ Dig/SP/GR log's TD to surface. PU & TIH with Guide shoe, shoe jt, float collar, 169 jt's of 5.5 J-55, 15.5# csgn. Set @ 6500.38' / KB. Cement with 350 sks cement mixed @ 11.0 ppg & 3.49 yld. Then 450 sks cement mixed @ 14.4 ppg & 1.24 yld. With 91 bbls cement returned to pit. Nipple down Bop's. Drop slips @ 116,000 #'s tension. Release rig 11:00 AM 11-13-08

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Ryan Crum

Signature

Title

Drilling Foreman

Date

11/14/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

RECEIVED

NOV 19 2008

DIV. OF OIL, GAS & MINING

NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

5 1/2" CASING SET @ 6500.38

LAST CASING: 8-5/8" SET @ 308.68
 DATUM (KB) 12
 DATUM TO CUT OFF CASING 12
 DATUM TO BRADENHEAD FLANGE 12
 DRILLER TD 6500 LOGGER TD 6520
 HOLE SIZE 7-7/8" TOP FLOAT COLLAR @ 6462.51
 TOP SHORT JT @ 4392.92

OPERATOR: Newfield Production Company
 WELL: Federal 7-20-8-17
 FIELD/PROSPECT: Monument Butte
 CONTRACTOR & RIG #: Patterson # 155

LOG OF CASING STRING:							
PIECES	OD	ITEM - MAKE - DESCRIPTION	WT / FT	GRD	THREAD	CONDT	LENGTH
1		Landing Jt	15.5#	J-55	8rd	A	14
168	5 1/2"	LT&C CASING	15.5#	J-55	8rd	A	6450.51
1	5 1/2"	FLOAT COLLAR	-	-	-	A	0.6
1	5 1/2"	LT&C CASING	15.5#	J-55	8rd	A	36.62
1	5 1/2"	GUIDE SHOE					0.65

CASING INVENTORY BAL.	FEET	JTS
TOTAL LENGTH OF STRING	6502.38	169
LESS NON CSG. ITEMS	15.25	-
PLUS FULL JTS. LEFT OUT	348.16	9
TOTAL	6835.29	178
TOTAL CSG. DEL. (W/O THRDS)	6835.29	178

TOTAL LENGTH OF STRING	6502.38
(-) LANDING JT	14
(-) AMOUNT CUTOFF	0
(+) KB ELEVATION	12
CASING SET DEPTH	6500.38

COMPARE (SHOULD BE EQUAL)

CEMENT DATA		TIME	DATE
BEGIN RUN CSG.		8:30 PM	11/12/2008
CSG. IN HOLE		5:00 AM	11/13/2008
BEGIN CIRC		5:10 AM	11/13/2008
BEGIN PUMP CMT		7:01 AM	11/13/2008
BEGIN DSPL. CMT		7:54 AM	11/13/2008
PLUG DOWN		8:16 AM	11/13/2008

GOOD CIRC THRU JOB: Yes
 Bbls CMT CIRC TO SURFACE: 91
 RECIPROCATED PIPE: No
 DID BACK PRES. VALVE HOLD ? Yes
 BUMPED PLUG TO: 1600 PSI

CEMENT USED		
CEMENT COMPANY:	BJ	
STAGE	# SX	CEMENT TYPE & ADDITIVES
1 (lead)	350	Premium Lite II cement + 0.05 lbs/sack Static Free + 3% bwow Potassium Chloride + 0.5 lbs/sack Cello Flake + 2 lbs/sack Kol Seal + 0.002 gps FP-6L + 10% bwoc Bentonite + 0.5% bwoc Sodium Metasilicate + 5 lbs/sack CSE-2 + 204.7% Fresh Water
2 (tail)	450	(50:50) Poz (Fly Ash): Class G Cement + 0.05 lbs/sack Static Free + 3% bwow Potassium Chloride + 0.5% bwoc EC-1 + 0.25 lbs/sack Cello Flake + 0.002 gps FP-6L + 2% bwoc Bentonite + 0.3% bwoc Sodium Metasilicate + 54.7% Fresh Water
CENTRALIZER & SCRATCHER PLACEMENT (SHOW MAKE & SPACING)		
Centralizers - Middle first, top second & third. Then every third collar for a total of 20.		

COMPANY REPRESENTATIVE Ryan Crum

DATE 11/13/2008

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
UTU-77339

1a. Type of Well Oil Well Gas Well Dry Other
 b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Resrv.,
 Other: _____

6. If Indian, Allottee or Tribe Name
NA

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

7. Unit or CA Agreement Name and No.
FEDERAL

3. Address
1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
(435)646-3721

8. Lease Name and Well No.
FEDERAL 7-20-8-16

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

At surface 530' FNL & 2028' FEL (NW/SE) SEC. 20, T8S, R16E

At top prod. interval reported below

At total depth 6500'

10. Field and Pool or Exploratory
MONUMENT BUTTE

11. Sec., T., R., M., on Block and
Survey or Area
SEC. 20, T8S, R16E

12. County or Parish
DUCHESNE

13. State
UT

14. Date Spudded
10/16/2008

15. Date T.D. Reached
11/12/2008

16. Date Completed 12/12/2008
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5496' GL 5508' KB

18. Total Depth: MD 6500'
TVD 6500'

19. Plug Back T.D.: MD 6445'
TVD

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#		309'		160 CLASS G			
7-7/8"	5-1/2" J-55	15.5#		6502'		350 PRIMLITE		248'	
						450 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 6201'	TA @6043'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) GREEN RIVER			(CP2) 6112-22', 6080-90'	.49"	4	80
B) GREEN RIVER			(LODC) see below	.49"	4	168 (2 runs)
C) GREEN RIVER			(A3)5602-18(A1)5552-61'	.49"	4	100
D) GREEN RIVER			(B.5) 5334-5340'	.49"	4	24

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
6080-6112'	Frac w/ 70369# of 20/40 snd 608 bbls fluid
5686-5758'	Frac w/ 100435# 20/40 snd 787 bbls fluid
5552-5618'	Frac w/ 70239# 20/40 snd 590 bbls fluid
5334-5340'	Frac w/ 25330# 20/40 snd 370 bbls fluid

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
12/12/08	01/02/09	24	→	136	399	78			2-1/2" x 1-1/2" x 10 x 14' RHAC Rod Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

RECEIVED
JAN 13 2009

*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
				GARDEN GULCH MRK GARDEN GULCH 1	4020' 4244'
				GARDEN GULCH 2 POINT 3	4360' 4656'
				X MRKR Y MRKR	4910' 4944'
				DOUGALS CREEK MRK BI CARBONATE MRK	5062' 5310'
				B LIMESTON MRK CASTLE PEAK	5446' 5944'
				BASAL CARBONATE TOTAL DEPTH (LOGGERS)	6400' 6520'

32. Additional remarks (include plugging procedure):

(LODC) 5748-5758', 5712-5728', 5686-5702'
 (D1) 5110-5106' .49" 4/24 5110-5106' Frac w/ 25191#'s of 20/40 sand in 364 bbls of fluid
 (PB10) 4820-4828' .49" 4/32 4820-4828' Frac w/ 31379#'s of 20/40 sand in 360 bbls of fluid

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other:

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Tammi Lee Title Production Clerk
 Signature *Tammi Lee* Date 01/07/2009

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:

USA UTU-77339

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:

1. TYPE OF WELL:

OIL WELL GAS WELL OTHER

8. WELL NAME and NUMBER:

FEDERAL 7-20-8-16

2. NAME OF OPERATOR:

NEWFIELD PRODUCTION COMPANY

9. API NUMBER:

4301333997

3. ADDRESS OF OPERATOR:

Route 3 Box 3630 CITY Myton STATE UT ZIP 84052

PHONE NUMBER

435.646.3721

10. FIELD AND POOL, OR WILDCAT:

MONUMENT BUTTE

4. LOCATION OF WELL:

FOOTAGES AT SURFACE: 530' FNL 2028'FEL

COUNTY: DUCHESNE

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NWSE, 20, T8S, R16E

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA


TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will <hr/>	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 12/12/2008	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was completed on 12/12/08, attached is a daily completion status report.

NAME (PLEASE PRINT) Jentri Park

TITLE Production Clerk

SIGNATURE 

DATE 01/09/2009

(This space for State use only)

RECEIVED

JAN 14 2009

DIV. OF OIL, GAS & MINING

Daily Activity Report

Format For Sundry

FEDERAL 7-20-8-16

9/1/2008 To 1/30/2009

11/26/2008 Day: 1

Completion

Rigless on 11/25/2008 - Install 5M frac head. NU 6" 5M Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 6408' cement top @ 248'. Perforate stage #1. CP2 sds @ 6112-22', 6080-90' w/ 3 1/8" slick guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 80 shots. 155 BWTR. SIFN.

12/5/2008 Day: 2

Completion

Rigless on 12/4/2008 - Stage #1, CP2 sands. RU BJ Services. 550 psi on well. Frac CP2 w/ 70,369#'s of 20/40 sand in 608 bbls of Lightning 17 fluid. Broke @ 3167 psi. Pumped 780 gals of fresh wtr mixed with 30 gals of Techni-Hib 767W. Treated w/ ave pressure of 2366 psi @ ave rate of 23.1 BPM. Pumped 504 gals of 15% HCL in flush for Stage #2. ISIP 2308 psi. Leave pressure on well. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 5K composite flow through frac plug, 10', 16' & 16' perf gun. Set plug @ 5840'. Perforate LODC sds @ 5748-58', 5712-28', 5686-5702' w/ 3 1/8" slick guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 168 shots (2 runs). SIWFN w/ 763 BWTR

12/8/2008 Day: 3

Completion

Rigless on 12/7/2008 - tage #2, LODC sands. BOP froze up. RU hot oiler steam & thaw out BOP. RU BJ Services. 1360 psi on well. Frac LODC w/ 100,435#'s of 20/40 sand in 787 bbls of Lightning 17 fluid. Broke @ 3503 psi. Pumped 780 gals of fresh wtr mixed with 30 gals of Techni-Hib 767W. Treated w/ ave pressure of 1920 psi @ ave rate of 23.1 BPM. Pumped 504 gals of 15% HCL in flush for Stage #3. ISIP 2006 psi. Leave pressure on well. 1550 BWTR Stage #3, A1 & A3 sands. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 5K composite flow through frac plug, 16' & 9' perf gun. Set plug @ 5640'. Perforate A3 sds @ 5602-18', A1 sds @ 5552-61' w/ 3 1/8" slick guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 100 shots. RU BJ Services. 1734 psi on well. Frac A1 & A3 w/ 70,239#'s of 20/40 sand in 590 bbls of Lightning 17 fluid. Broke @ 1897 psi. Pumped 780 gals of fresh wtr mixed with 30 gals of Techni-Hib 767W. Treated w/ ave pressure of 2032 psi @ ave rate of 23.1 BPM. Pumped 504 gals of 15% HCL in flush for Stage #4. ISIP 2029 psi. Leave pressure on well. 2140 BWTR. Stage #4, B.5 sands. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 5K composite flow through frac plug & 6' perf gun. Set plug @ 5400'. Perforate B.5 sds @ 5334-40' w/ 3 1/8" slick guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 24 shots. RU BJ Services. 1754 psi on well. Frac B.5 w/ 25,330#'s of 20/40 sand in 371 bbls of Lightning 17 fluid. Broke @ 3183 psi. Pumped 780 gals of fresh wtr mixed with 30 gals of Techni-Hib 767W. Treated w/ ave pressure of 1994 psi @ ave rate of 23.2 BPM. Pumped 504 gals of 15% HCL in flush for Stage #4. ISIP 1703 psi. Leave pressure on well. 2522 BWTR. Stage #5, D1 sands. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 5K composite flow through frac plug & 6' perf gun. Set plug @ 5180'. Perforate D1 sds @ 5100-5106' w/ 3 1/8" slick guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 24 shots. RU BJ Services. 1456 psi on well. Frac D1 w/ 25,191#'s of 20/40 sand in 364 bbls of Lightning 17 fluid. Broke @ 3921 psi.

Pumped 780 gals of fresh wtr mixed with 30 gals of Techni-Hib 767W. Treated w/ ave pressure of 2178 psi @ ave rate of 23.1 BPM. Pumped 504 gals of 15% HCL in flush for Stage #5. ISIP 1853 psi. Leave pressure on well. 2875 BWTR. Stage #6, PB10 sands. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 5K composite flow through frac plug & 8' perf gun. Set plug @ 4900'. Perforate PB10 sds @ 4820-28' w/ 3 1/8" slick guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 32 shots. RU BJ Services. 1638 psi on well. Frac PB10 w/ 31,379#'s of 20/40 sand in 360 bbbls of Lightning 17 fluid. Broke @ 3801 psi. Pumped 780 gals of fresh wtr mixed with 30 gals of Techni-Hib 767W. Treated w/ ave pressure of 2407 psi @ ave rate of 23.1 BPM. ISIP 2430 psi. Begin immediate flowback on 20/64 choke @ 1 BPM. Flowed for 2 1/2 hrs & died. Rec 418 BTF. Turned to oil & gas. SIWFN w/ 300 psi on well. 2817 BWTR.

12/9/2008 Day: 4

Completion

Western #3 on 12/8/2008 - MIRU Western #3. 500 psi on well. RU Zubiate hot oil. Pumped 20 bbbls of wtr down csg @ 150°. RU Perforators WLT & lubricator. RIH w/ Weatherford 5-1/2" 5K composite solid kill frac. Set plug @ 4790'. RD WL. ND Cameron BOP & 5M WH. NU 3M WH & Schaffer BOP. Talley, PU & RIH w/ 4 3/4" chomp bit, Bit sub & 2 7/8" J-55 tbg. EOT @ 1523', Circulate oil out of well. Total of 105 jts, EOT @ 3255'. SIWFN w/ 2852 BWTR.

12/10/2008 Day: 5

Completion

Western #3 on 12/9/2008 - RU hot-oiler & steam & thaw out WH & BOP. 0 psi on well. Continue to PU & RIH w/ tbg. Tagged kill plug @ 4790'. RU Nabors power swivel. Circulate sand & drill out plugs as follows: Plug @ 4790' (Drilled up in 19 mins), Sand @ 4825', Plug @ 4900' (Drilled up in 21 mins), No sand, Plug @ 5180' (Drilled up in 21mins), No sand, Plug @ 5400' (Drilled up in 23 mins), Circulate well for 1 hr to clean up. TIH. Tagged sand @ 5605', Plug @ 5640' (Drilled up in 28 mins). Circulate well clean. LD 1 jt of tbg. EOT @ 5608'. Drain pump & lines. SIWFN w/ 2787 BWTR.

12/11/2008 Day: 6

Completion

Western #3 on 12/10/2008 - RU hot oiler & steam & thaw out WH & BOP. 450 psi on tbg, 500 psi on well. Bleed down well. Circulate oil & gas out of well. Continue to PU & RIH w/ tbg. Tagged plug @ 5840'. RU Nabors power swivel. Drill out plug @ 5840' (29 mins). Continue TIH w/ tbg. Tagged fill @ 6245'. C/O to PBDT @ 6445'. LD 2 jts of tbg. EOT @ 6373'. RU swab equipment. Made 3 swab runs. Well started flowing. Swabbed back 40 BTF, Flowed back 105 BTF in 1 hr 45 mins, No sand & 20% oil. Drain pump & lines. SIWFN w/ 2787 BWTR.

12/12/2008 Day: 7

Completion

Western #3 on 12/11/2008 - Thaw well w/ hotoiler. Bleed off well. Circulate well clean. RIH w/ tbg. Tag PBDT @ 6445'. No new fill. Circulate well w/ 200 bbbls 10# brine water. POOH w/ tbg. LD BHA. RIH w/ 2 7/8" notched collar, 2 jts 2 7/8" tbg., PSN, 3 jts 2 7/8" tbg., 5 1/2" TAC, 195 jts 2 7/8" tbg. ND BOP. Set TAC @ 6042' w/ 16,000# tension. NU wellhead. X-over for rods. Flush tbg. w/ 60 bbbls water. RIH w/ CDI 2 1/2" x 1 1/2" x 10' x 14' RHAC rod pump, 6- 1 1/2" weight bars, 20- 3/4" guided rods, 55- 3/4" slick rods. SWIFN w/ polished rod.

12/13/2008 Day: 8

Completion

Western #3 on 12/12/2008 - Cont. RIH w/ rods. Seat pump. RU pumping unit. Hang

off rods. Fill tbg. w/ 3 bbls water. Stroke test to 800 psi. Good pump action. RD. Put well on production @ 12:00 p.m. 6.5 spm, 74" stroke length. Final Report.

Pertinent Files: Go to File List
