

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No. UTU-81000	
6. If Indian, Allottee or Tribe Name NA	
7. If Unit or CA Agreement, Name and No. NA	
8. Lease Name and Well No. Federal 10-30-8-16	
9. API Well No. 43013-34184	
10. Field and Pool, or Exploratory Monument Butte <i>Undesignated</i>	11. Sec., T. R. M. or Blk. and Survey or Area Sec. 30, T8S R16E
12. County or Parish Duchesne	13. State UT
14. Distance in miles and direction from nearest town or post office* Approximately 10.2 miles southwest of Myton, UT	15. Distance from proposed* location to nearest property or lease line, ft. Approx. 1959' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)
16. No. of acres in lease 580.24	17. Spacing Unit dedicated to this well 40 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1335'	19. Proposed Depth 6,570'
20. BLM/BIA Bond No. on file WYB000493	21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5713' GL
22. Approximate date work will start* 2 nd Qtr. 2009	23. Estimated duration (7) days from SPUD to rig release

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 12/29/08
Title Regulatory Specialist		
Approved by (Signature) <i>Bradley G. Hill</i>	Name (Printed/Typed) BRADLEY G. HILL	Date 01-22-09
Title Office ENVIRONMENTAL MANAGER		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

RECEIVED

JAN 14 2009



DIV. OF OIL, GAS & MINING

Federal Approval of this
Action is Necessary

T8S, R16E, S.L.B.&M.

NEWFIELD PRODUCTION COMPANY

WELL LOCATION, NORTH TRAVIS 10-30-8-16,
 LOCATED AS SHOWN IN THE NW 1/4 SE 1/4
 OF SECTION 30, T8S, R16E, S.L.B.&M.
 DUCHESNE COUNTY, UTAH.

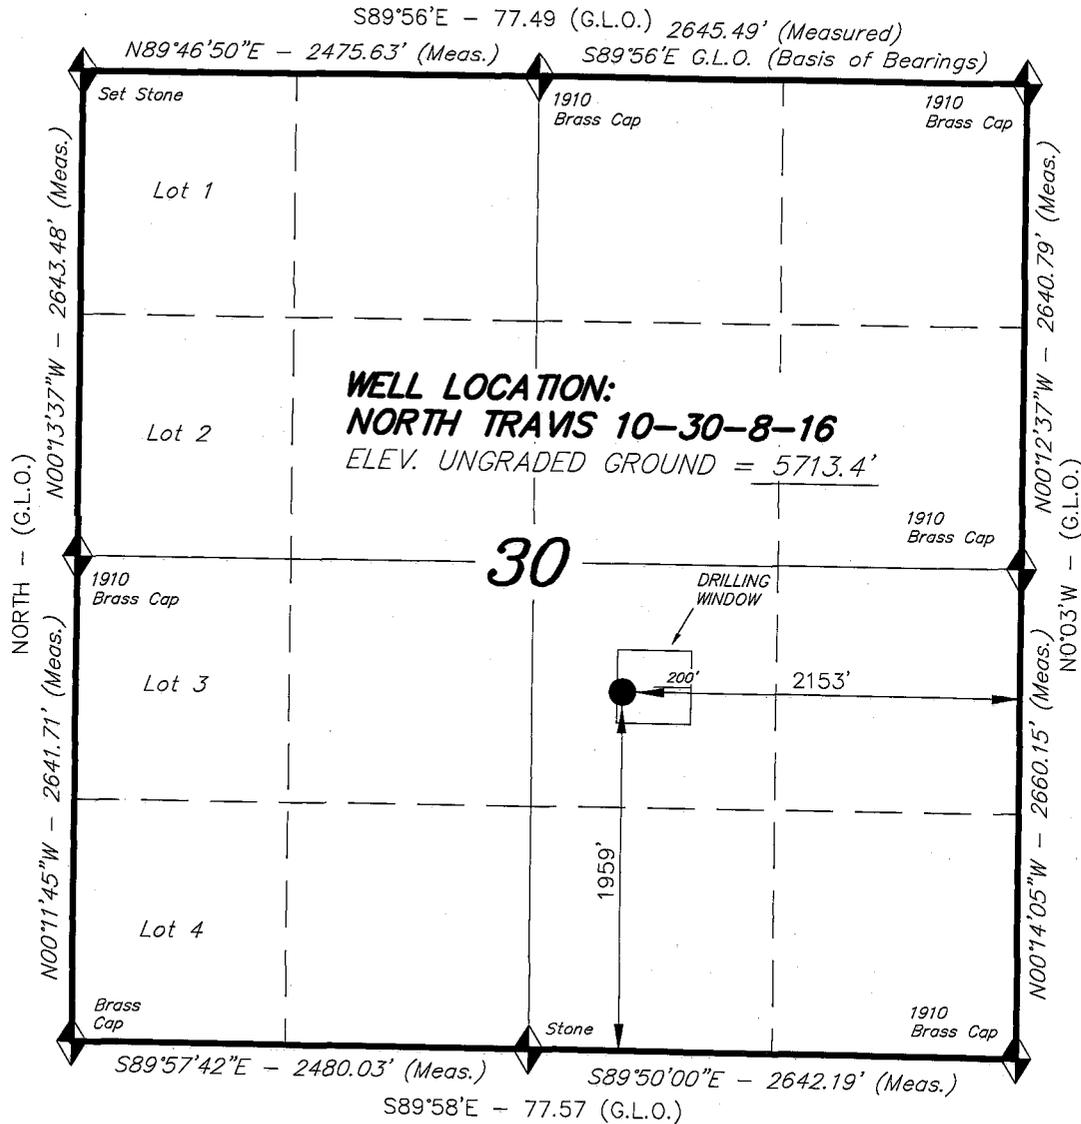

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
 PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
 MADE BY ME OR UNDER MY SUPERVISION AND THAT
 THE SAME ARE TRUE AND CORRECT TO THE BEST OF
 MY KNOWLEDGE AND BELIEF. No. 189377

REGISTERED LAND SURVEYOR
 STACY W.
 REGISTERED LAND SURVEYOR
 REGISTRATION No. 40033
 STATE OF UTAH

◆ = SECTION CORNERS LOCATED
 BASIS OF ELEV;
 U.S.G.S. 7-1/2 min QUAD (MYTON SW)

NORTH TRAVIS 10-30-8-16
 (Surface Location) NAD 83
 LATITUDE = 40° 05' 13.45"
 LONGITUDE = 110° 09' 37.60"

TRI STATE LAND SURVEYING & CONSULTING	
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078 (435) 781-2501	
DATE SURVEYED: 10-23-08	SURVEYED BY: T.H.
DATE DRAWN: 10-28-08	DRAWN BY: F.T.M.
REVISED:	SCALE: 1" = 1000'

NEWFIELD PRODUCTION COMPANY
FEDERAL 10-30-8-16
NW/SE SECTION 30, T8S, R16E
DUCHESNE COUNTY, UTAH

ONSHORE ORDER NO. 1

DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta 0' – 1735'
Green River 1735'
Wasatch 6570'
Base of Moderately Saline Ground Water @ 5250'

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation 1735' – 6570' - Oil

4. PROPOSED CASING PROGRAM

Please refer to the Monument Butte Field Standard Operation Procedure (SOP).

5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:

Please refer to the Monument Butte Field SOP. See Exhibit "C".

6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:

Please refer to the Monument Butte Field SOP.

7. AUXILIARY SAFETY EQUIPMENT TO BE USED:

Please refer to the Monument Butte Field SOP.

8. TESTING, LOGGING AND CORING PROGRAMS:

Please refer to the Monument Butte Field SOP.

9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:

The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered.

10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:

Please refer to the Monument Butte Field SOP.

**NEWFIELD PRODUCTION COMPANY
FEDERAL 10-30-8-16
NW/SE SECTION 30, T8S, R16E
DUCHESNE COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Federal 10-30-8-16 located in the NW 1/4 SE 1/4 Section 30, T8S, R16E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.4 miles \pm to the junction of this highway and UT State Hwy 53; proceed southwesterly - 7.0 miles \pm to its junction with the beginning of the proposed access road to the southwest; proceed southwesterly along the proposed access road - 7760' \pm ; turn and proceed in a northwesterly direction along the proposed access road - 510' \pm ; turn and proceed in a northerly direction along the proposed road - 1340' \pm to the proposed well location.

2. PLANNED ACCESS ROAD

See Topographic Map "B" for the location of the proposed access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

All permanent surface equipment will be painted Carlsbad Canyon.
Please refer to the Monument Butte Field Standard Operating Procedure (SOP).

5. LOCATION AND TYPE OF WATER SUPPLY

Newfield Production will transport water by truck for drilling purposes from the following water sources:

Johnson Water District
Water Right : 43-7478

Neil Moon Pond
Water Right: 43-11787

Maurice Harvey Pond
Water Right: 47-1358

Newfield Collector Well
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

Please refer to the Monument Butte Field SOP. See Exhibit "A".

6. **SOURCE OF CONSTRUCTION MATERIALS**

Please refer to the Monument Butte Field SOP.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

Please refer to the Monument Butte Field SOP.

8. **ANCILLARY FACILITIES**

Please refer to the Monument Butte Field SOP.

9. **WELL SITE LAYOUT**

See attached Location Layout Diagram.

10. **PLANS FOR RESTORATION OF SURFACE**

Please refer to the Monument Butte Field SOP.

11. **SURFACE OWNERSHIP** - Bureau Of Land Management (Proposed location and access roads leading to).

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Surveys have been completed the reports will be forthcoming.

Newfield Production Company requests a 1490' ROW in Lease UTU-69061, a 3480' ROW in Lease UTU-69060, a 1090' ROW in Lease UTU-77339, and 3550' of disturbed area be granted in Lease UTU-81000 to allow for construction of the planned access road. **Refer to Topographic Map "B"**. A permanent width of 30' and a running surface of 18' is proposed for the planned access road. The construction phase of the planned access road will last approximately (5) days. The planned access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 1340' of disturbed area be granted in Lease UTU-81000 to allow for construction of the proposed surface gas lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a 10" or smaller gas gathering line, and a 3" poly fuel gas line, with a permanent width of 30' upon completion of the proposed gas lines. The construction phase of the proposed gas lines will last approximately (5) days. Both lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Newfield Production Company requests 1340' of disturbed area be granted in Lease UTU-81000 to allow for construction of the proposed water lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line, with a permanent width of 30' upon completion of the proposed water return line. The construction phase of the proposed water lines will last approximately (5) days. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP. In the event that the proposed well is converted to a water injection well, a separate injection permit will be applied for through the proper agencies.

Water Disposal

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), State of Utah approved surface disposal facilities, or Federally approved surface disposal facilities.

Threatened, Endangered, And Other Sensitive Species

Mountain Plover: If new construction or surface disturbing activities are scheduled to occur between May 15 and June 15, detailed surveys of the area within 0.5 mile of the proposed location and within 300 feet of proposed access routes must be conducted to detect the presence of mountain plovers. All surveys must be conducted in accordance with the survey protocols outlined in the most recent USFWS Survey Protocol. Surveys must be completed prior to initiating new construction or surface disturbing activities. No new construction or surface disturbing activities will be allowed between May 15 and June 15 within a 0.5 mile radius of any documented mountain plover nest site.

Reserve Pit Liner

A 16 mil liner with felt is required. Please refer to the Monument Butte Field SOP.

Location and Reserve Pit Reclamation

Please refer to the Monument Butte Field SOP.

The following seed mixture will be used on the topsoil stockpile, to the recontoured surface of the reserve pit, and for final reclamation: (All poundages are in pure live seed)

Squirrel Tail	<i>Elymus Elymoides</i>	6 lbs/acre
Siberian Wheatgrass	<i>Agropyron Fragile</i>	2 lbs/acre
Gardner Saltbush	<i>Atriplex Gardneri</i>	1 lbs/acre
Shadscale	<i>Atriplex Confertifolia</i>	1 lbs/acre
Fourwing Saltbush	<i>Atriplex Canescens</i>	1 lbs/acre
Scarlet Globemallow	<i>Sphaeralcea Conccinea</i>	0.20 lbs/acre
Forage Kochia	<i>Kochia Prostrata</i>	0.20 lbs/acre

Details of the On-Site Inspection

The proposed Federal 10-30-8-16 was on-sited on 11/13/08. The following were present; Dave Allred (Newfield Production), Tim Eaton (Newfield Production), James Herford (Bureau of Land Management), Brandon McDonald (Bureau of Land Management), and Dave Gordon (Bureau of Land Management). Weather conditions were clear and ground cover was 100% open.

LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION

Representative

Name: Dave Allred
Address: Route #3 Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification


Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #10-30-8-16 NW/SE Section 30, Township 8S, Range 16E: Lease UTU-81000 Duchesne County, Utah: and is responsible under the terms and conditions of the lease for the

operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

12/29/08

Date




Mandie Crozier
Regulatory Specialist
Newfield Production Company


NEWFIELD PRODUCTION COMPANY

NORTH TRAVIS 10-30-8-16

Section 30, T8S, R16E, S.L.B.&M.



PROPOSED ACCESS ROAD (Max. 6% Grade)

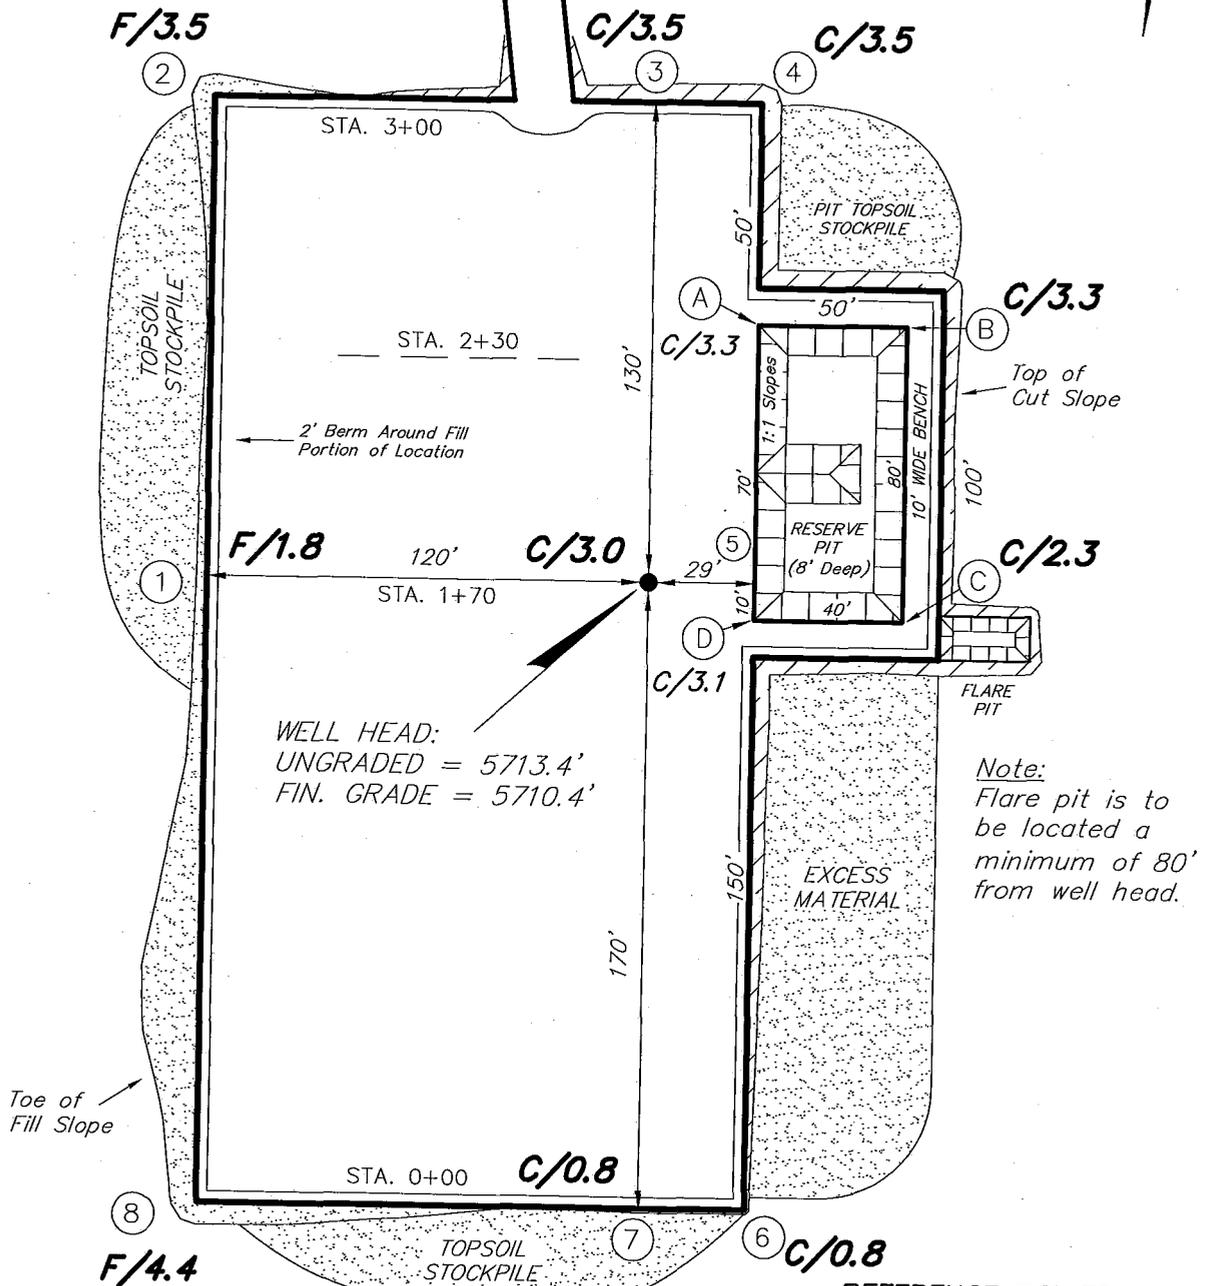

WELL HEAD:
UNGRADED = 5713.4'
FIN. GRADE = 5710.4'

Note:
Flare pit is to be located a minimum of 80' from well head.

REFERENCE POINTS





- 220' NORTHWEST = 5710.0'
- 270' NORTHWEST = 5709.9'
- 170' NORTHEAST = 5707.5'
- 220' NORTHEAST = 5705.1'

SURVEYED BY: T.H.	DATE SURVEYED: 10-23-08
DRAWN BY: F.T.M.	DATE DRAWN: 10-28-08
SCALE: 1" = 50'	REVISED:

Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

CROSS SECTIONS NORTH TRAVIS 10-30-8-16

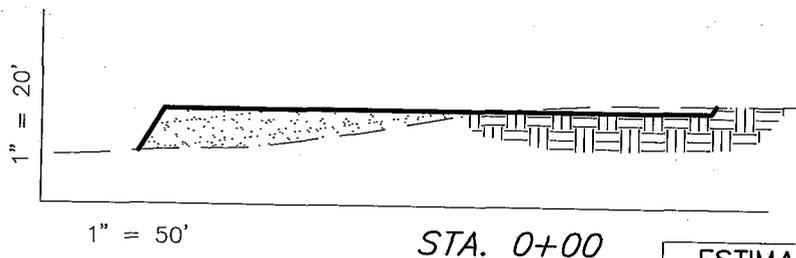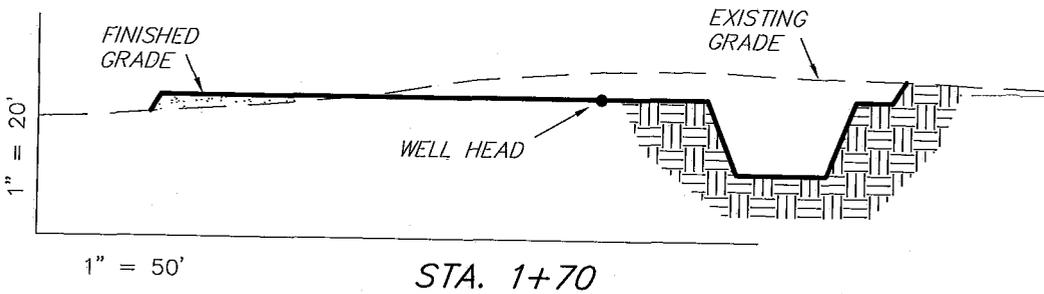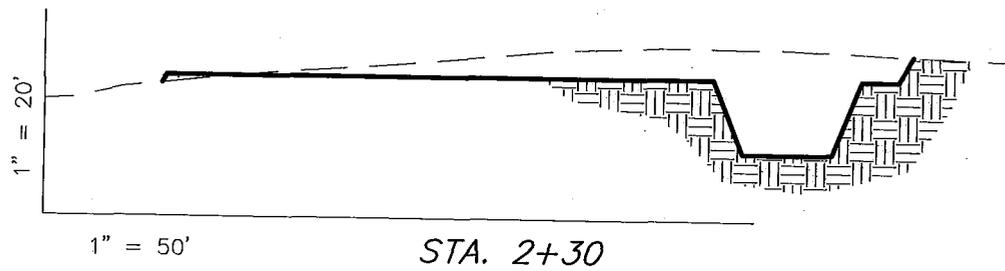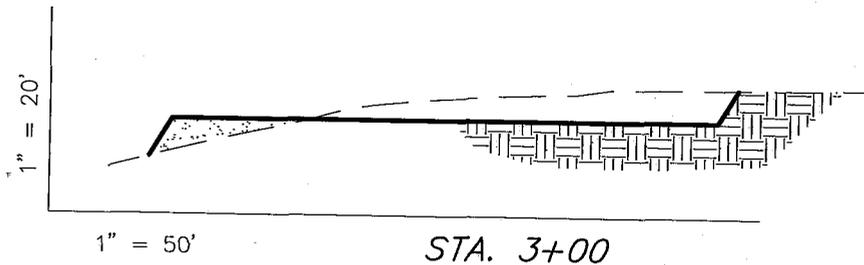

NOTE:
UNLESS OTHERWISE
NOTED ALL CUT/FILL
SLOPES ARE AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	2,030	2,030	Topsoil is not included in Pad Cut	0
PIT	640	0		640
TOTALS	2,670	2,030	1,010	640

SURVEYED BY: T.H.	DATE SURVEYED: 10-23-08
DRAWN BY: F.T.M.	DATE DRAWN: 10-28-08
SCALE: 1" = 50'	REVISED:


Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

TYPICAL RIG LAYOUT

NORTH TRAVIS 10-30-8-16

PROPOSED ACCESS ROAD (Max. 6% Grade)

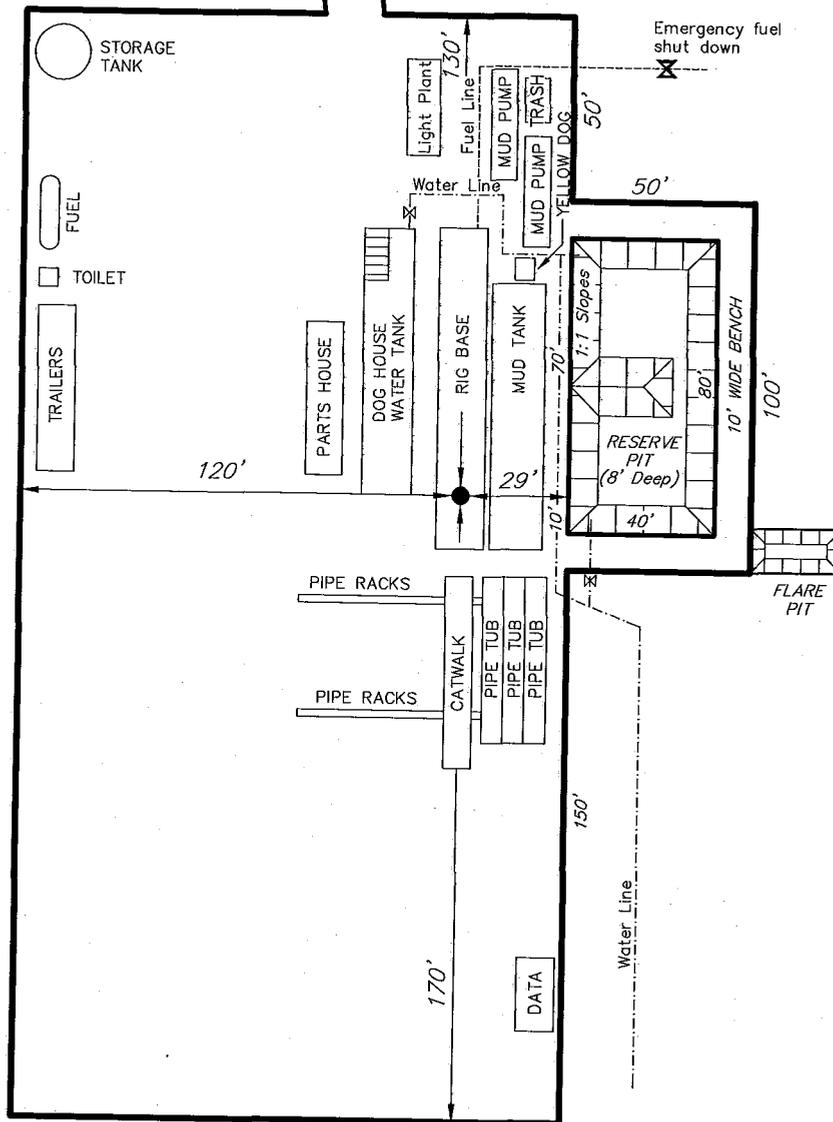

SURVEYED BY: T.H.	DATE SURVEYED: 10-23-08
DRAWN BY: F.T.M.	DATE DRAWN: 10-28-08
SCALE: 1" = 50'	REVISED:

Tri State
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078
 (435) 781-2501


Lowfield Production Company Proposed Site Facility Diagram

Federal 10-30-8-16

NW/SE Sec. 30, T8S, R16E

Duchesne County, Utah

UTU-81000

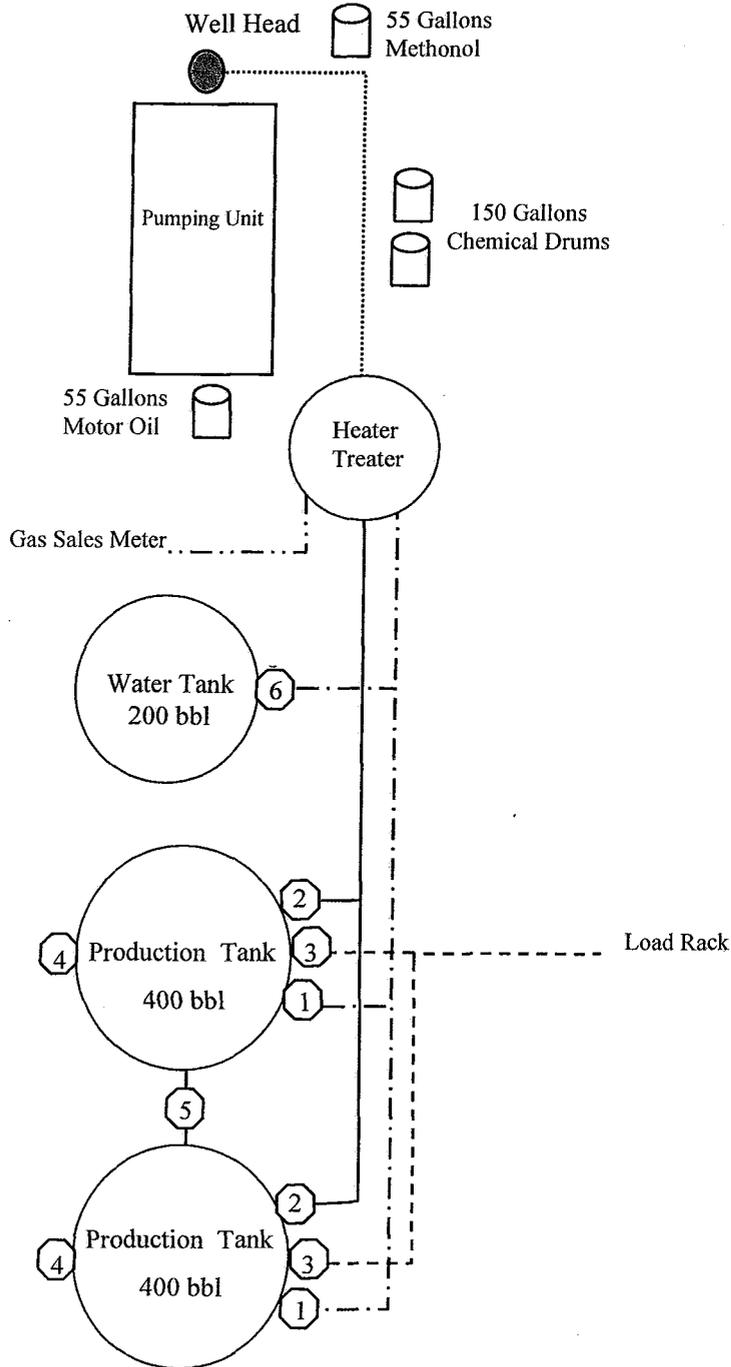

Legend

Emulsion Line
Load Rack	- - - - -
Water Line	- . - . -
Gas Sales	-
Oil Line	—————

Production Phase:

- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open

Sales Phase:


- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

Draining Phase:

- 1) Valves 1 and 6 open

Diked Section



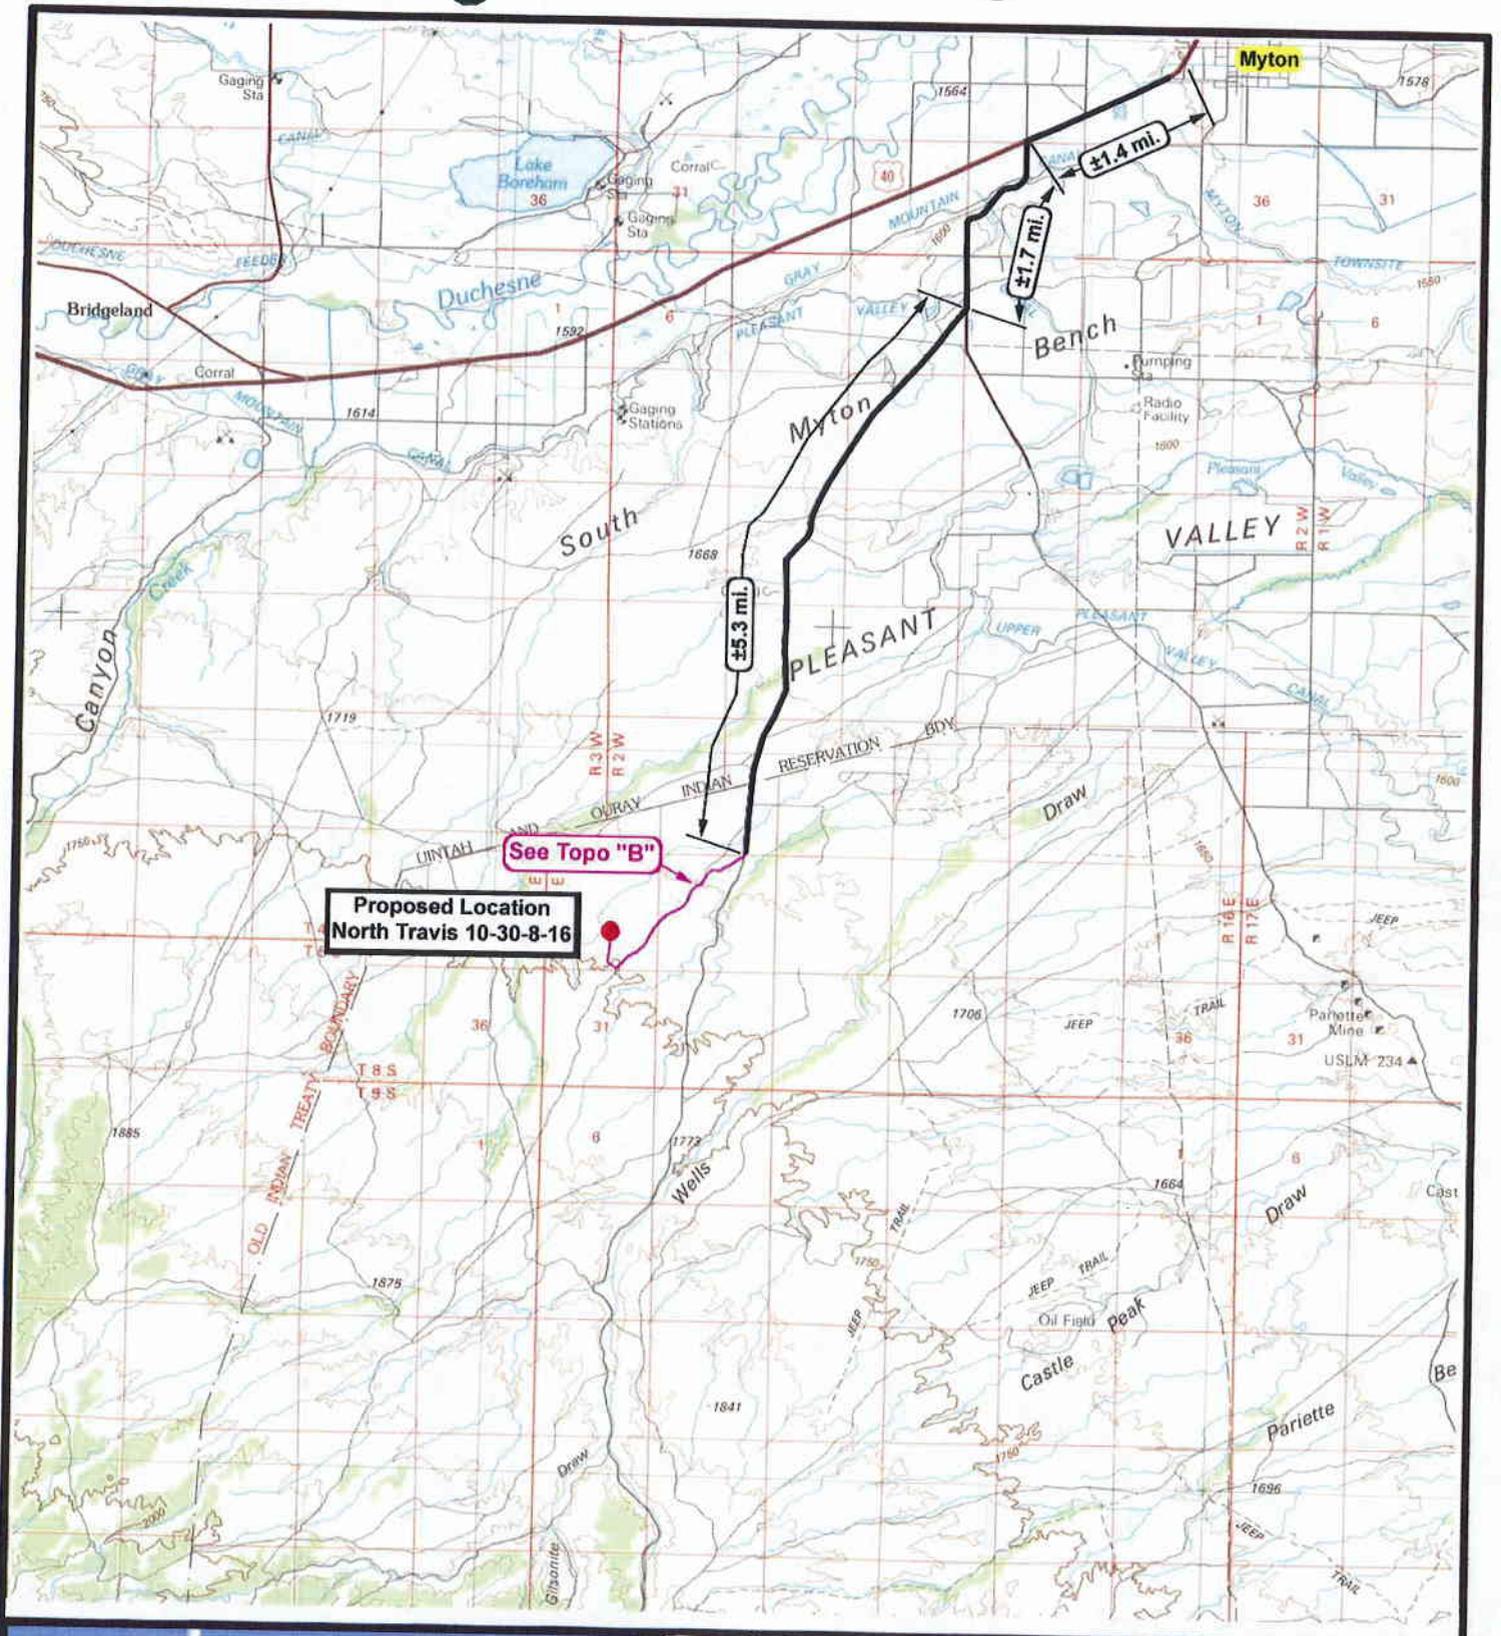

**Proposed Location
North Travis 10-30-8-16**

See Topo "B"

NEWFIELD
Exploration Company

**North Travis 10-30-8-16
SEC. 30, T8S, R16E, S.L.B.&M.**




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1 = 100,000
DRAWN BY: mw
DATE: 10-29-2008

Legend

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP
"A"

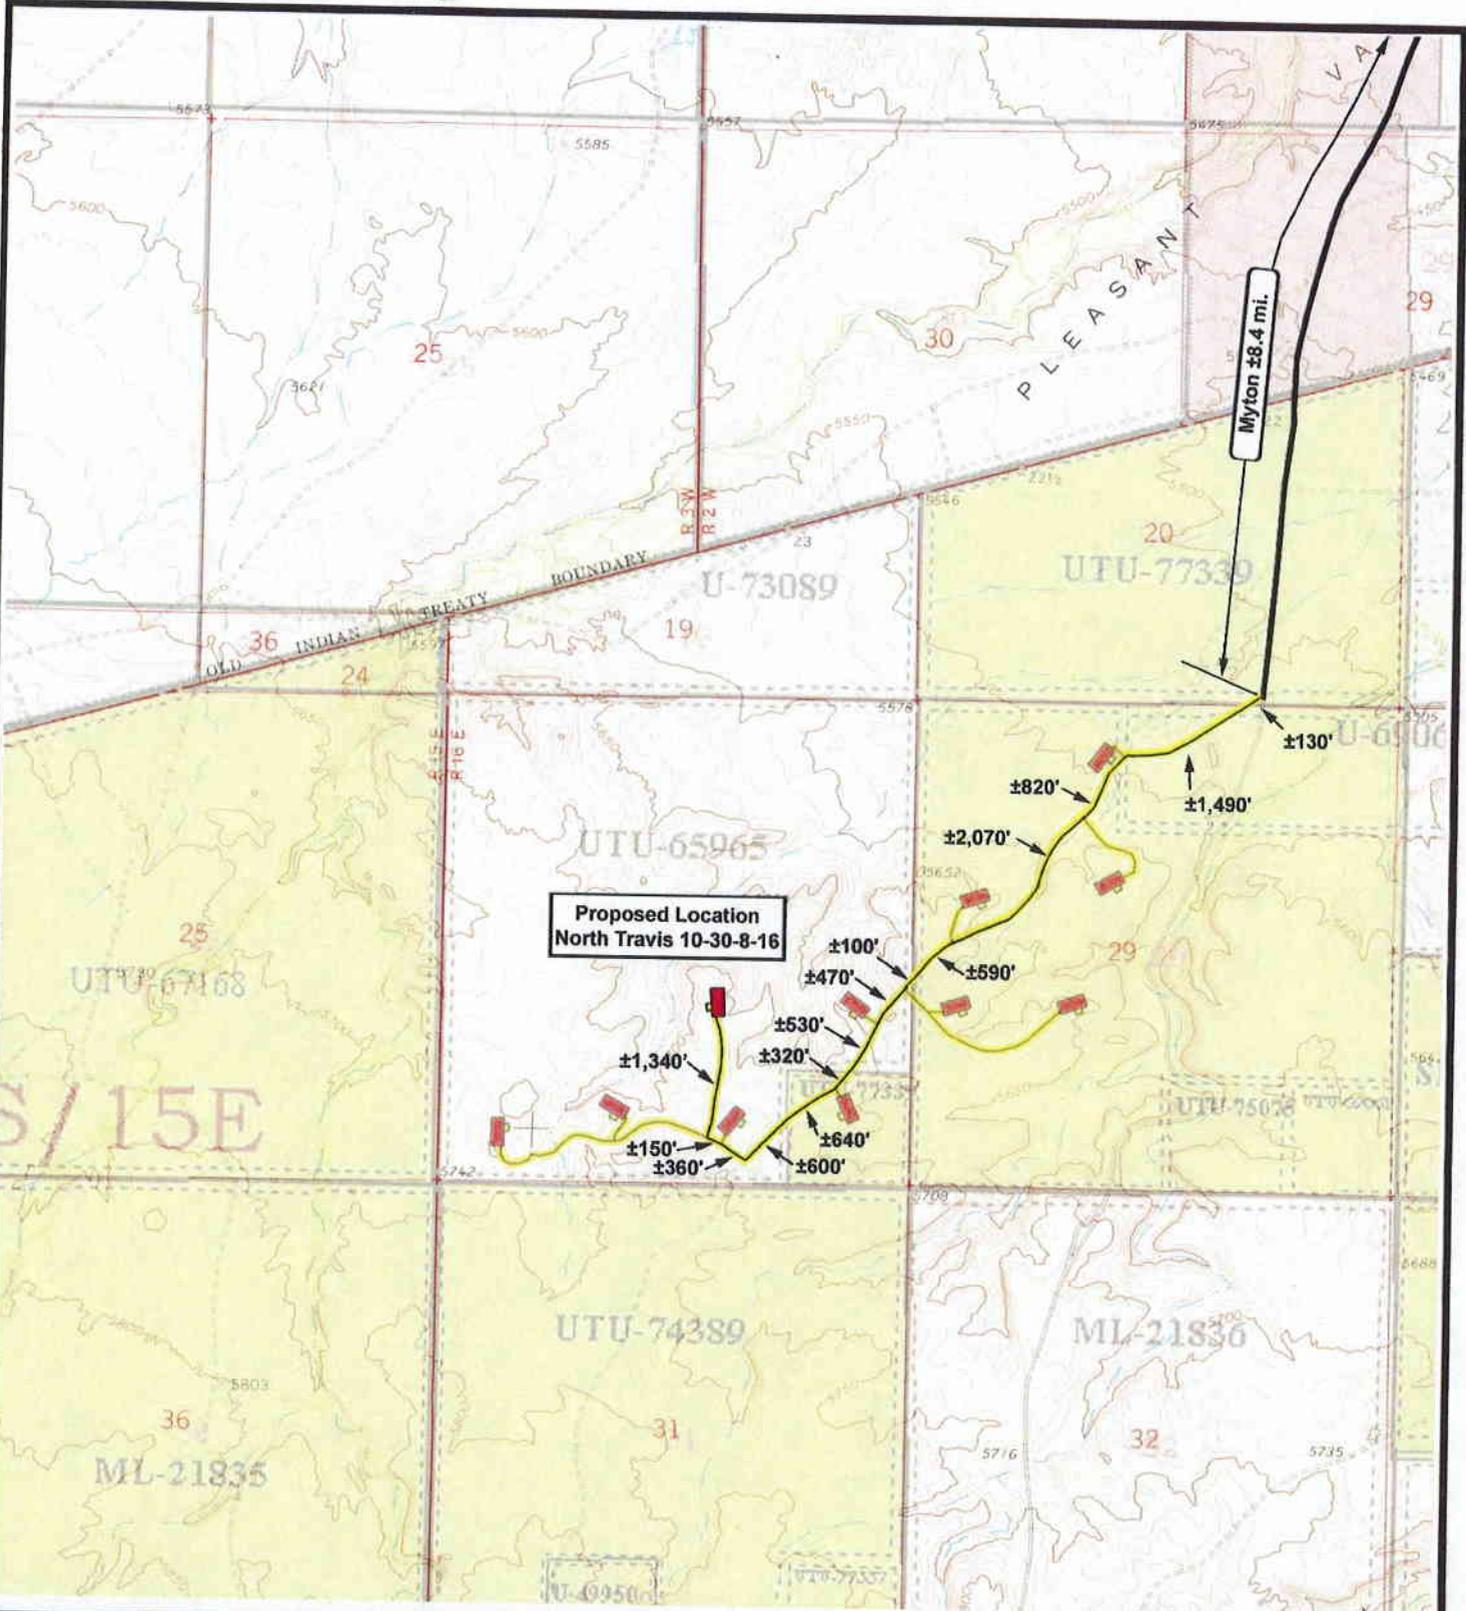

Proposed Location
North Travis 10-30-8-16

Myton ±8.4 mi.



NEWFIELD
Exploration Company

North Travis 10-30-8-16
SEC. 30, T8S, R16E, S.L.B.&M.




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 10-29-2008

Legend

-  Existing Road
-  Proposed Access

TOPOGRAPHIC MAP

"B"

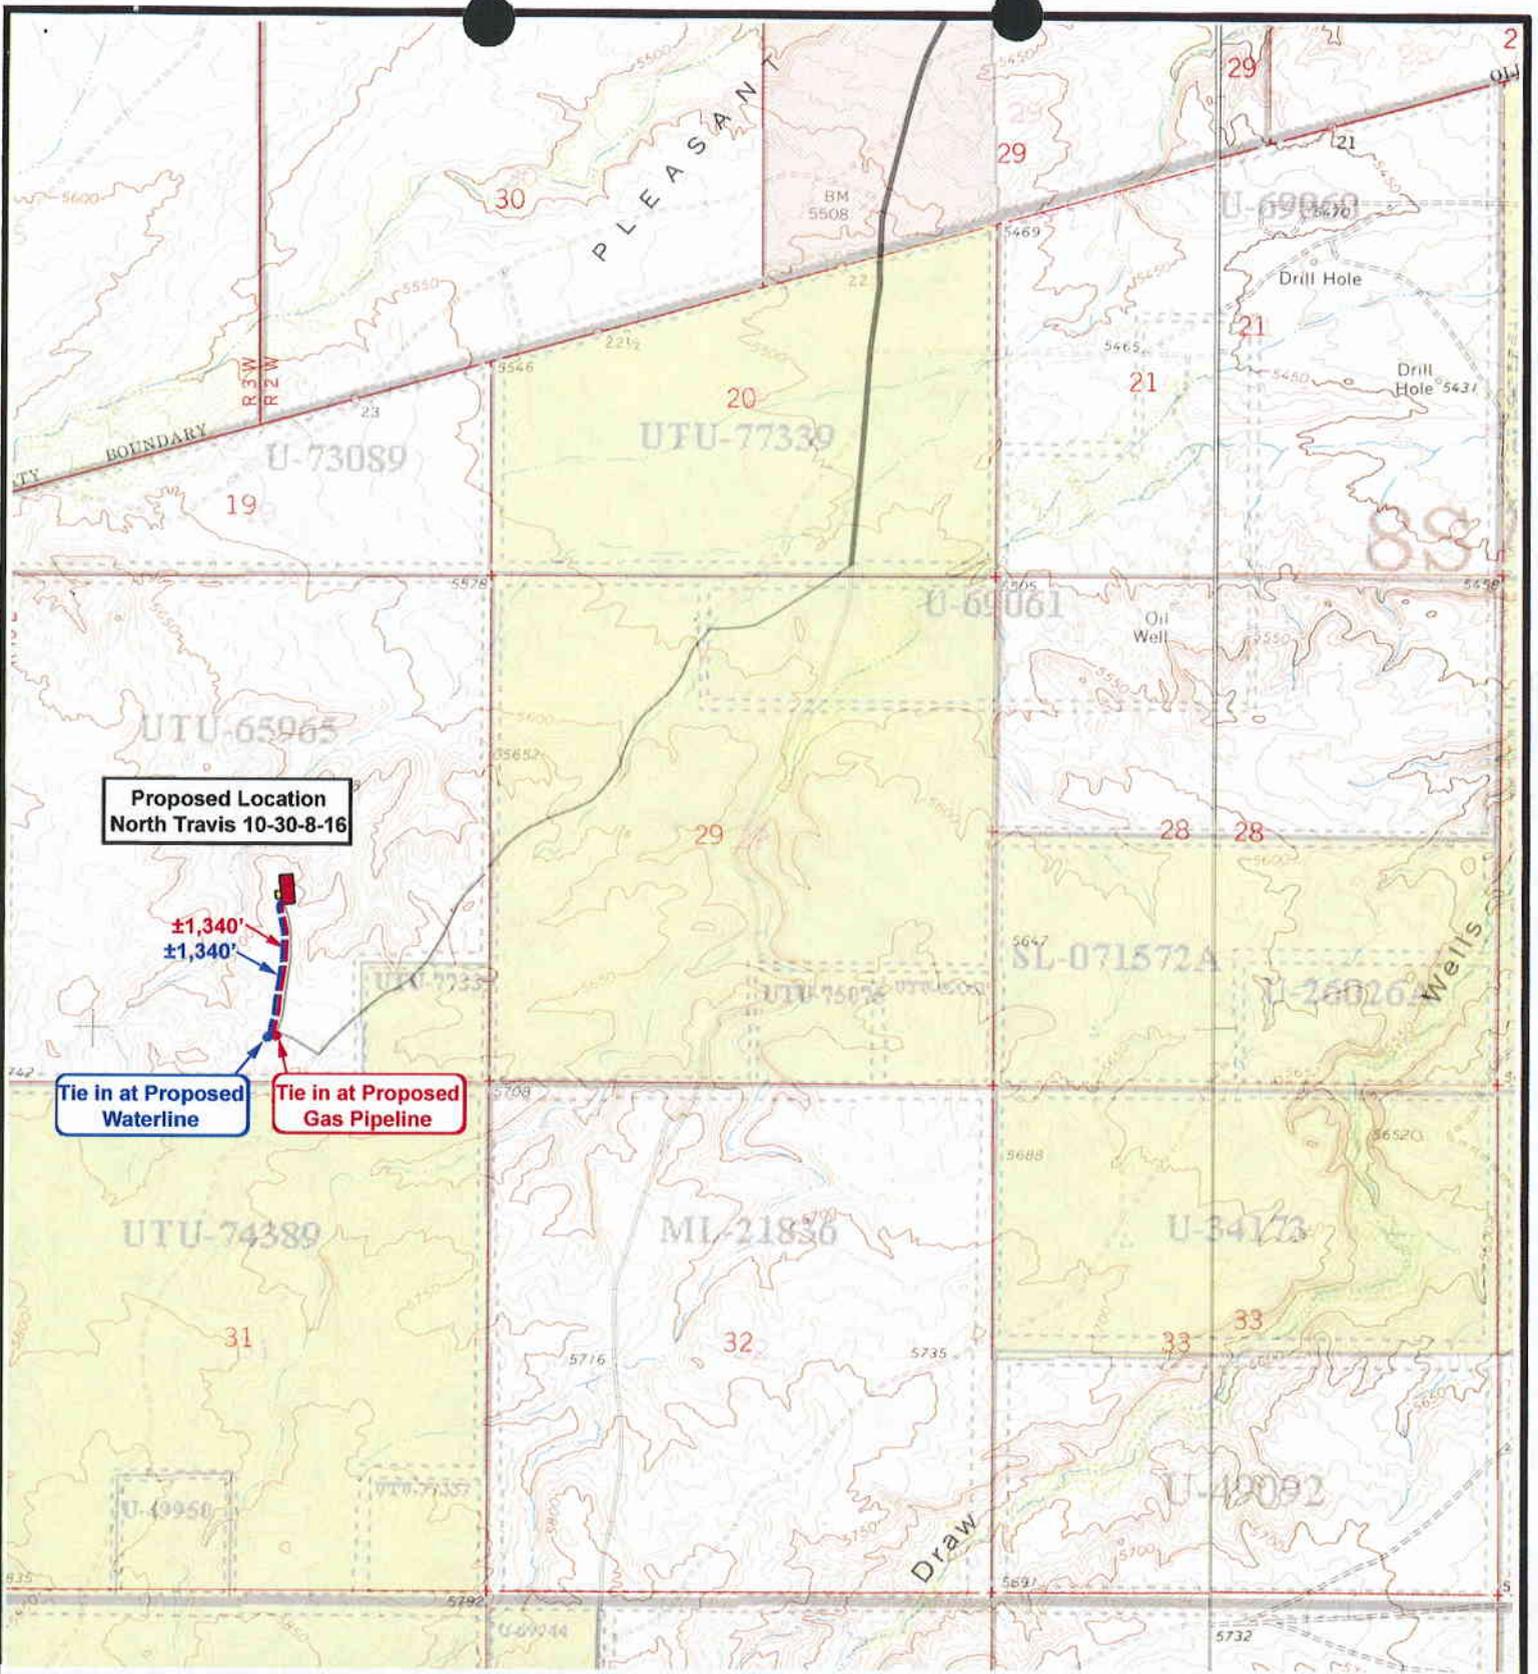

NEWFIELD
Exploration Company

North Travis 10-30-8-16
SEC. 30, T8S, R16E, S.L.B.&M.




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 11-19-2008

- Legend**
- Roads
 - Proposed Gas Line
 - Proposed Water Line

TOPOGRAPHIC MAP

"C"

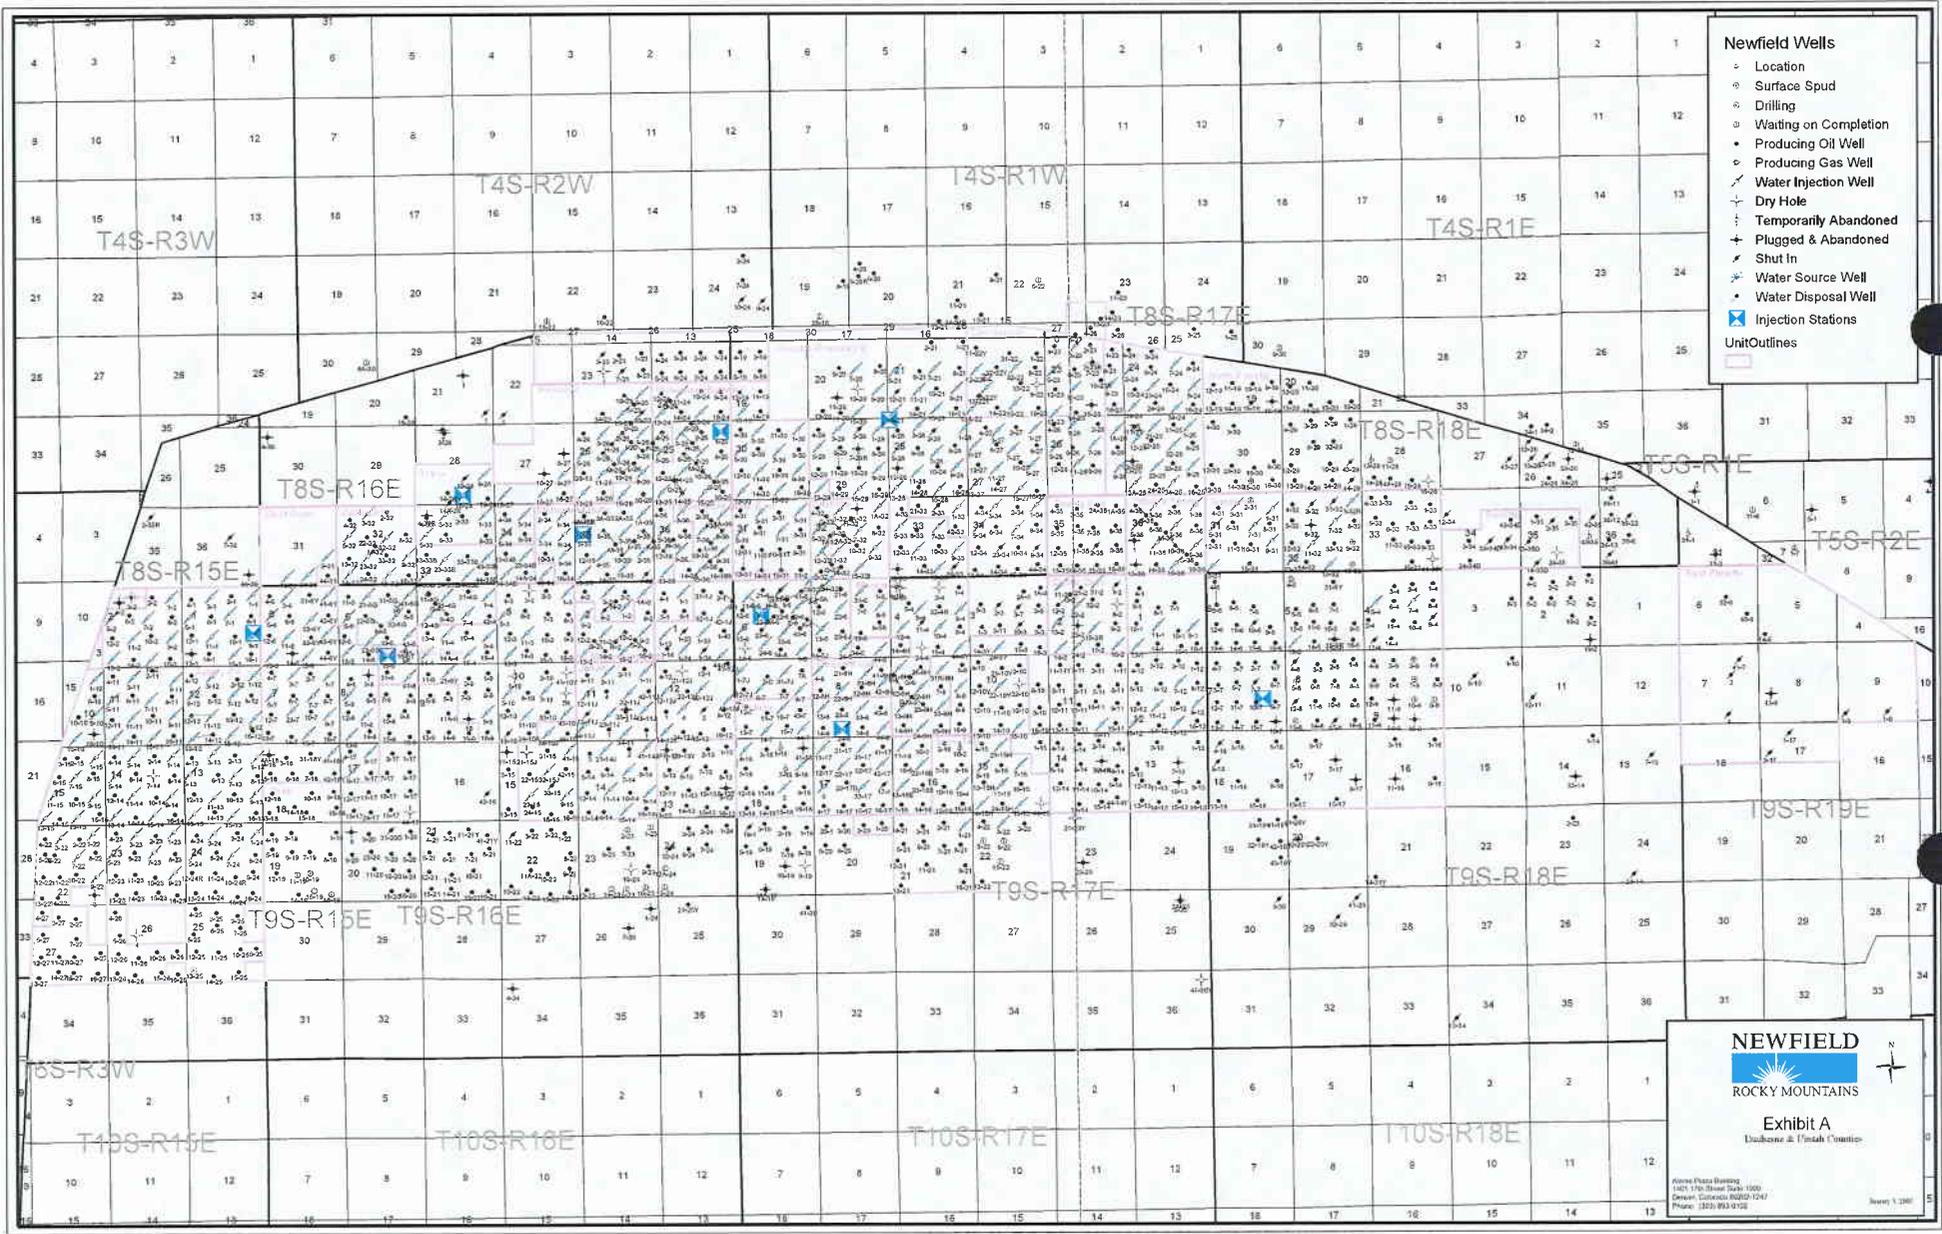

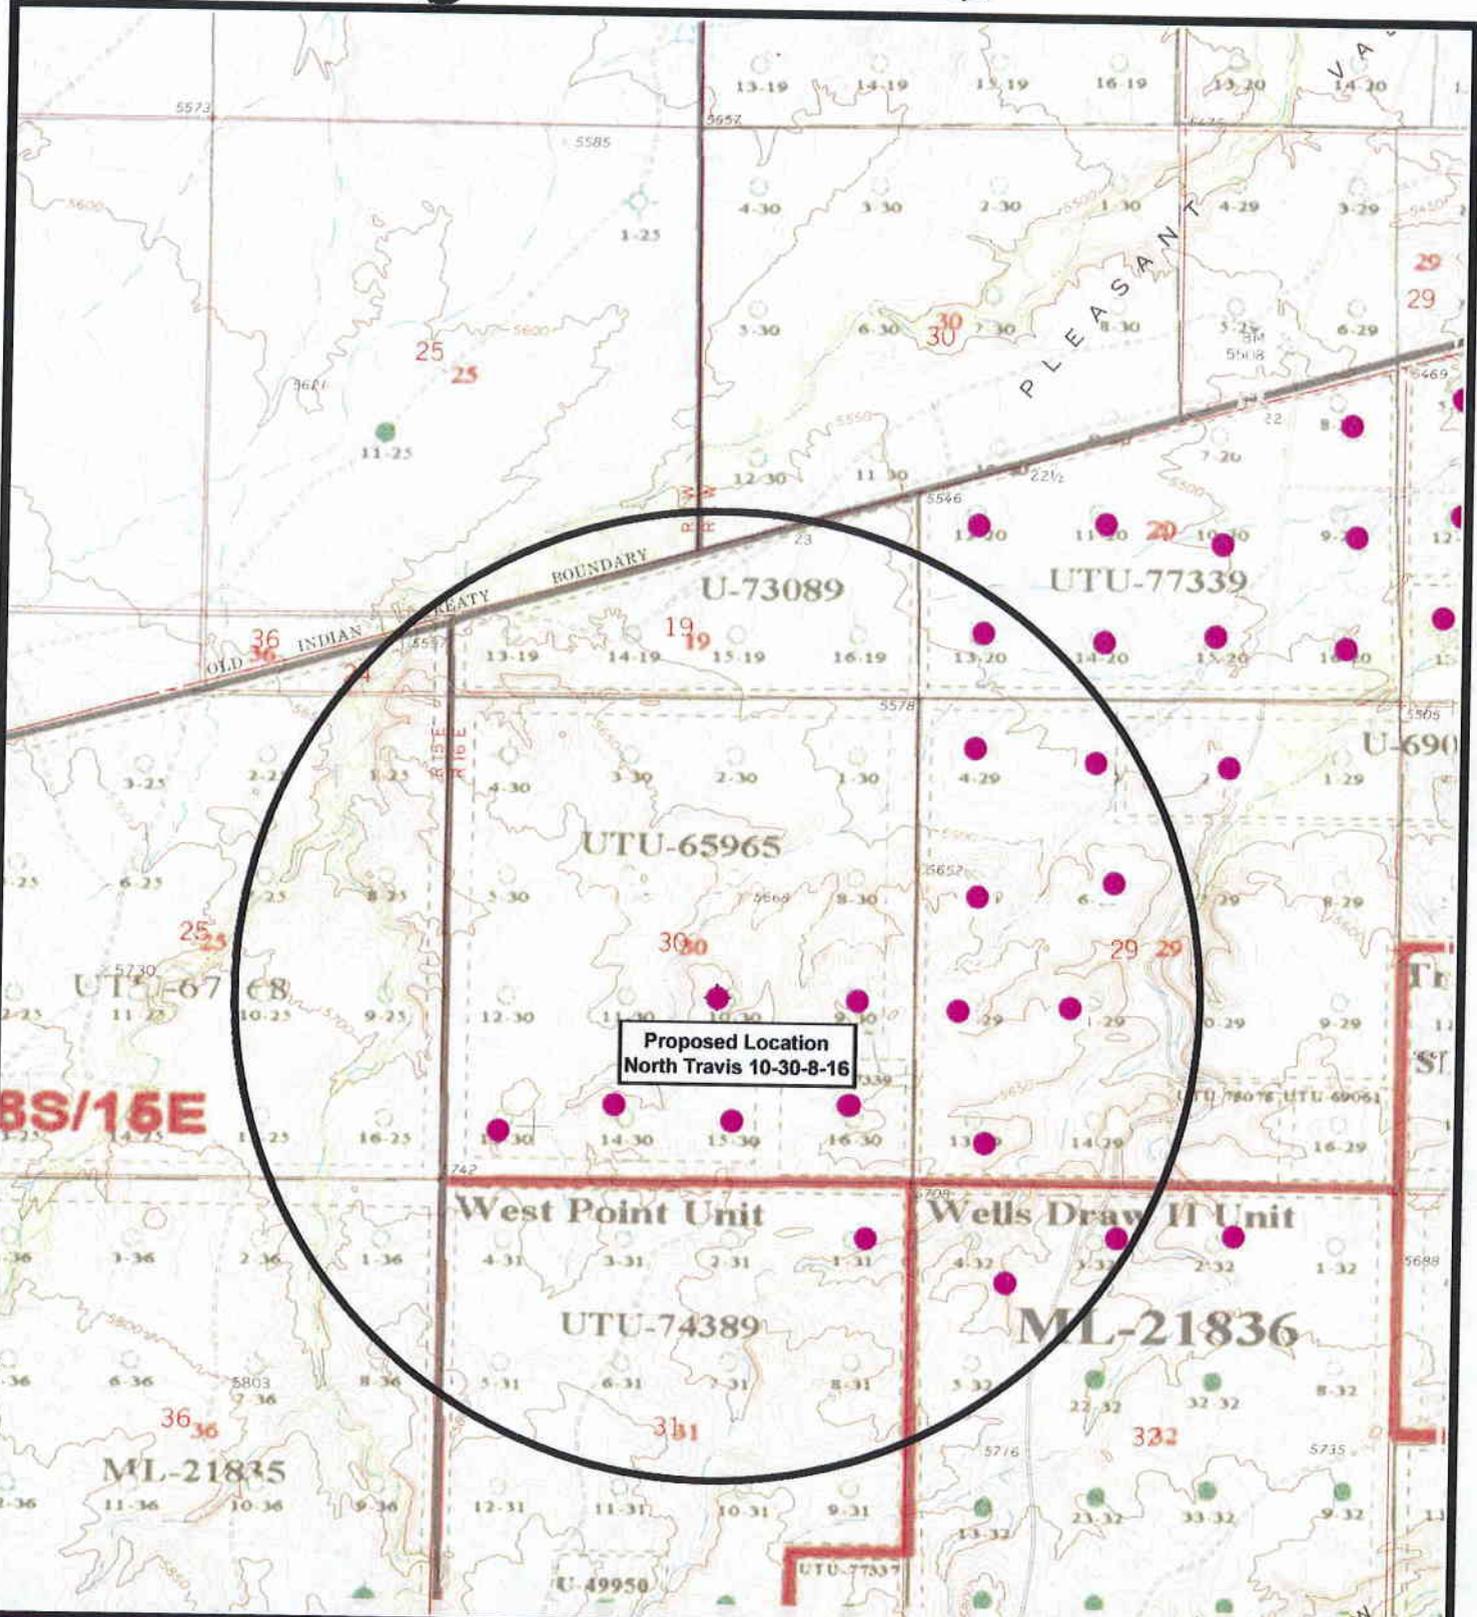

Proposed Location
North Travis 10-30-8-16

NEWFIELD
Exploration Company

North Travis 10-30-8-16
SEC. 30, T8S, R16E, S.L.B.&M.



Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 10-29-2008

Legend

- Location
- One-Mile Radius

Exhibit "B"

2-M SYSTEM
Blowout Prevention Equipment Systems

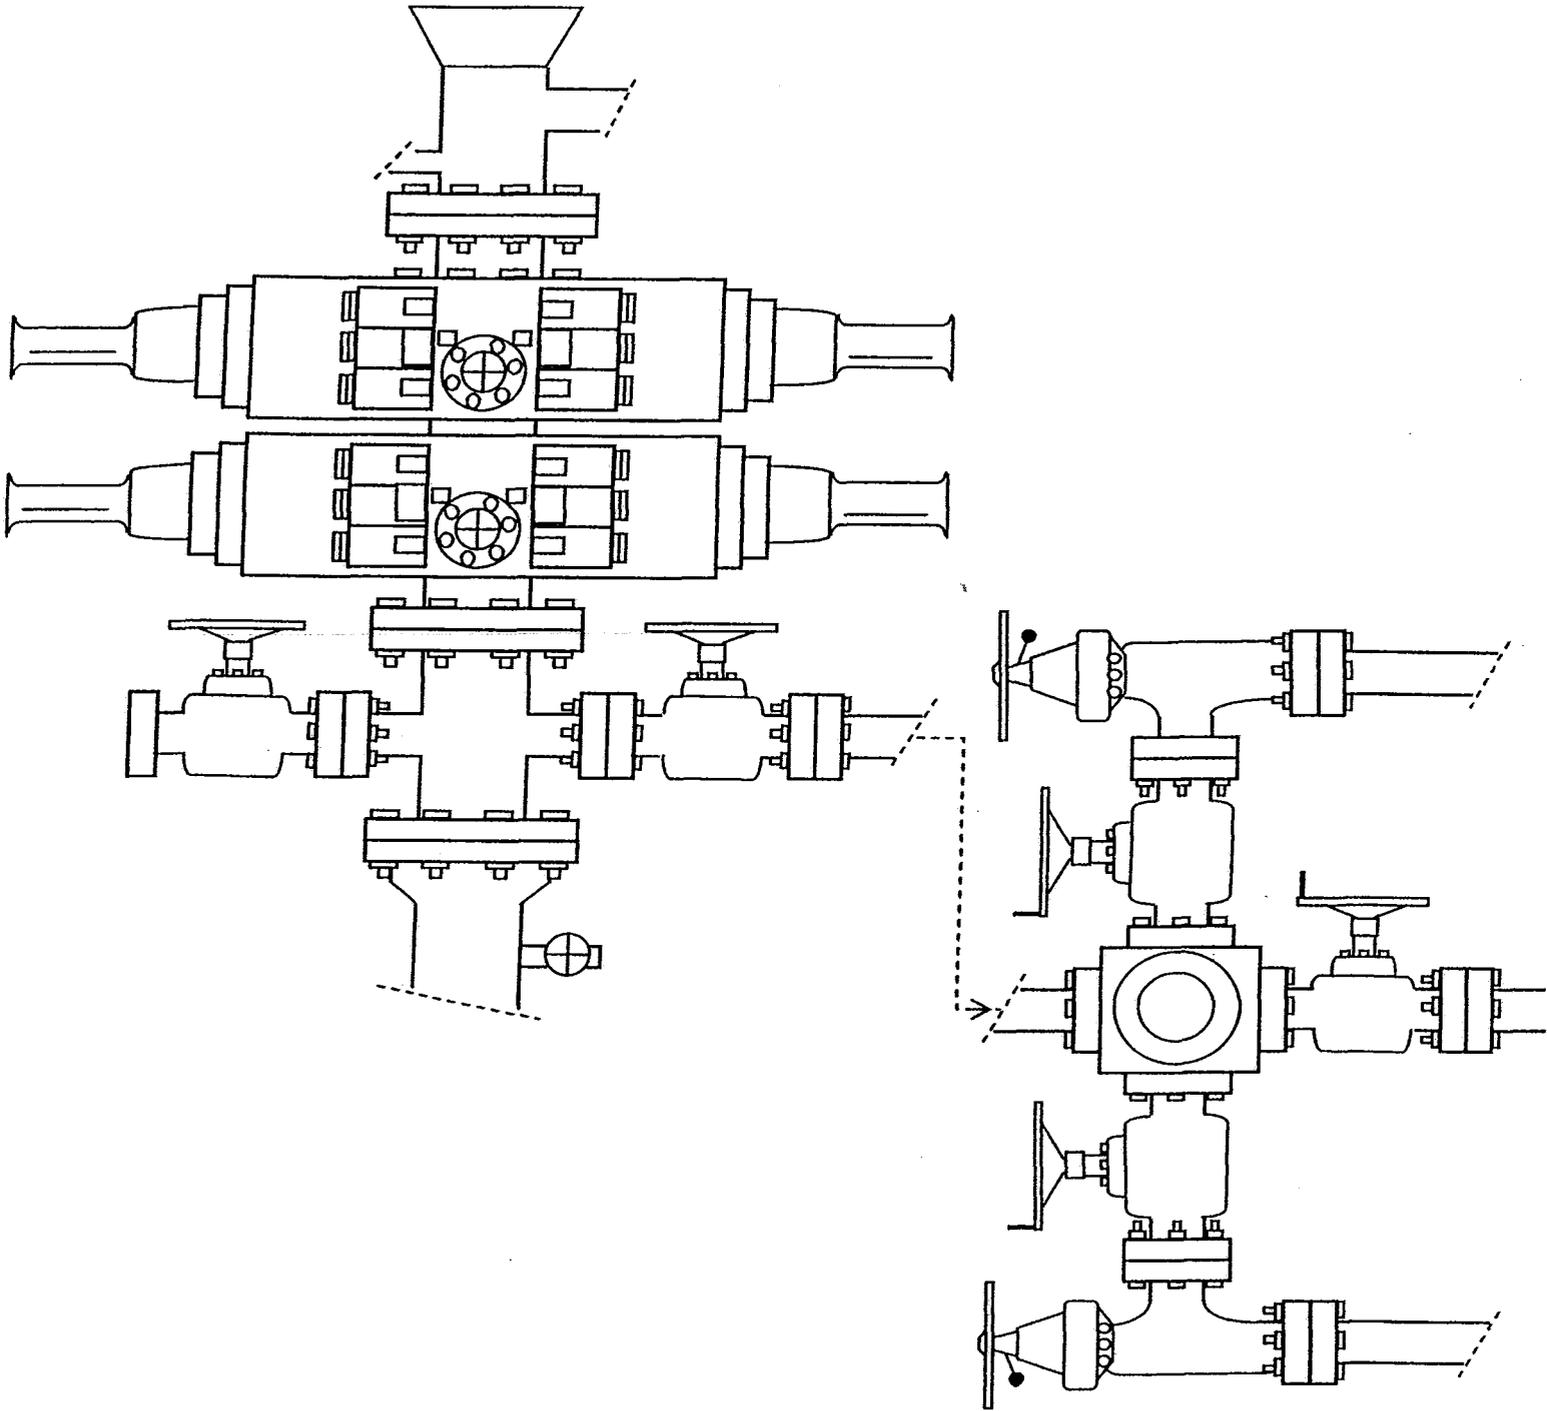


EXHIBIT C

**WORKSHEET
APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 01/14/2009

API NO. ASSIGNED: 43-013-34184

WELL NAME: FEDERAL 10-30-8-16

OPERATOR: NEWFIELD PRODUCTION (N2695)

PHONE NUMBER: 435-646-3721

CONTACT: MANDIE CROZIER

PROPOSED LOCATION:

NWSE 30 080S 160E

SURFACE: 1959 FSL 2153 FEL

BOTTOM: 1959 FSL 2153 FEL

COUNTY: DUCHESNE

LATITUDE: 40.08716 LONGITUDE: -110.1597

UTM SURF EASTINGS: 571641 NORTHINGS: 4437560

FIELD NAME: UNDESIGNATED (2)

INSPECT LOCATN BY: / /		
Tech Review	Initials	Date
Engineering		
Geology		
Surface		

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-81000

SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: GRRV

COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:

- Plat
- Bond: Fed[1] Ind[] Sta[] Fee[]
(No. WYB000493)
- Potash (Y/N)
- Oil Shale 190-5 (B) or 190-3 or 190-13
- Water Permit
(No. 43-7478)
- RDCC Review (Y/N)
(Date: _____)
- Fee Surf Agreement (Y/N)
- Intent to Commingle (Y/N)

LOCATION AND SITING:

- R649-2-3.
- Unit: _____
- R649-3-2. General
Siting: 460 From Qtr/Qtr & 920' Between Wells
- R649-3-3. Exception
- Drilling Unit
- Board Cause No: _____
- Eff Date: _____
- Siting: _____
- R649-3-11. Directional Drill

COMMENTS:

Sup, Separate Rev




STIPULATIONS:

*1. Federal Approval
2. Spacing Strip*

API Number: 4301334184
Well Name: FEDERAL 10-30-8-16
Township 08.0 S Range 16.0 E Section 30
Meridian: SLBM
Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
 Map Produced by Diana Mason

- | Units | Wells Query Events |
|--------------|----------------------|
| STATUS | ✕ <all other values> |
| ACTIVE | GIS_STAT_TYPE |
| EXPLORATORY | <Null> |
| GAS STORAGE | APD |
| NF PP OIL | DRL |
| NF SECONDARY | GI |
| PI OIL | GS |
| PP GAS | LA |
| PP GEOTHERML | NEW |
| PP OIL | OPS |
| SECONDARY | PA |
| TERMINATED | PGW |
| Fields | POW |
| STATUS | RET |
| ACTIVE | SGW |
| COMBINED | SOW |
| Sections | TA |
| | TW |
| | WD |
| | WI |
| | WS |

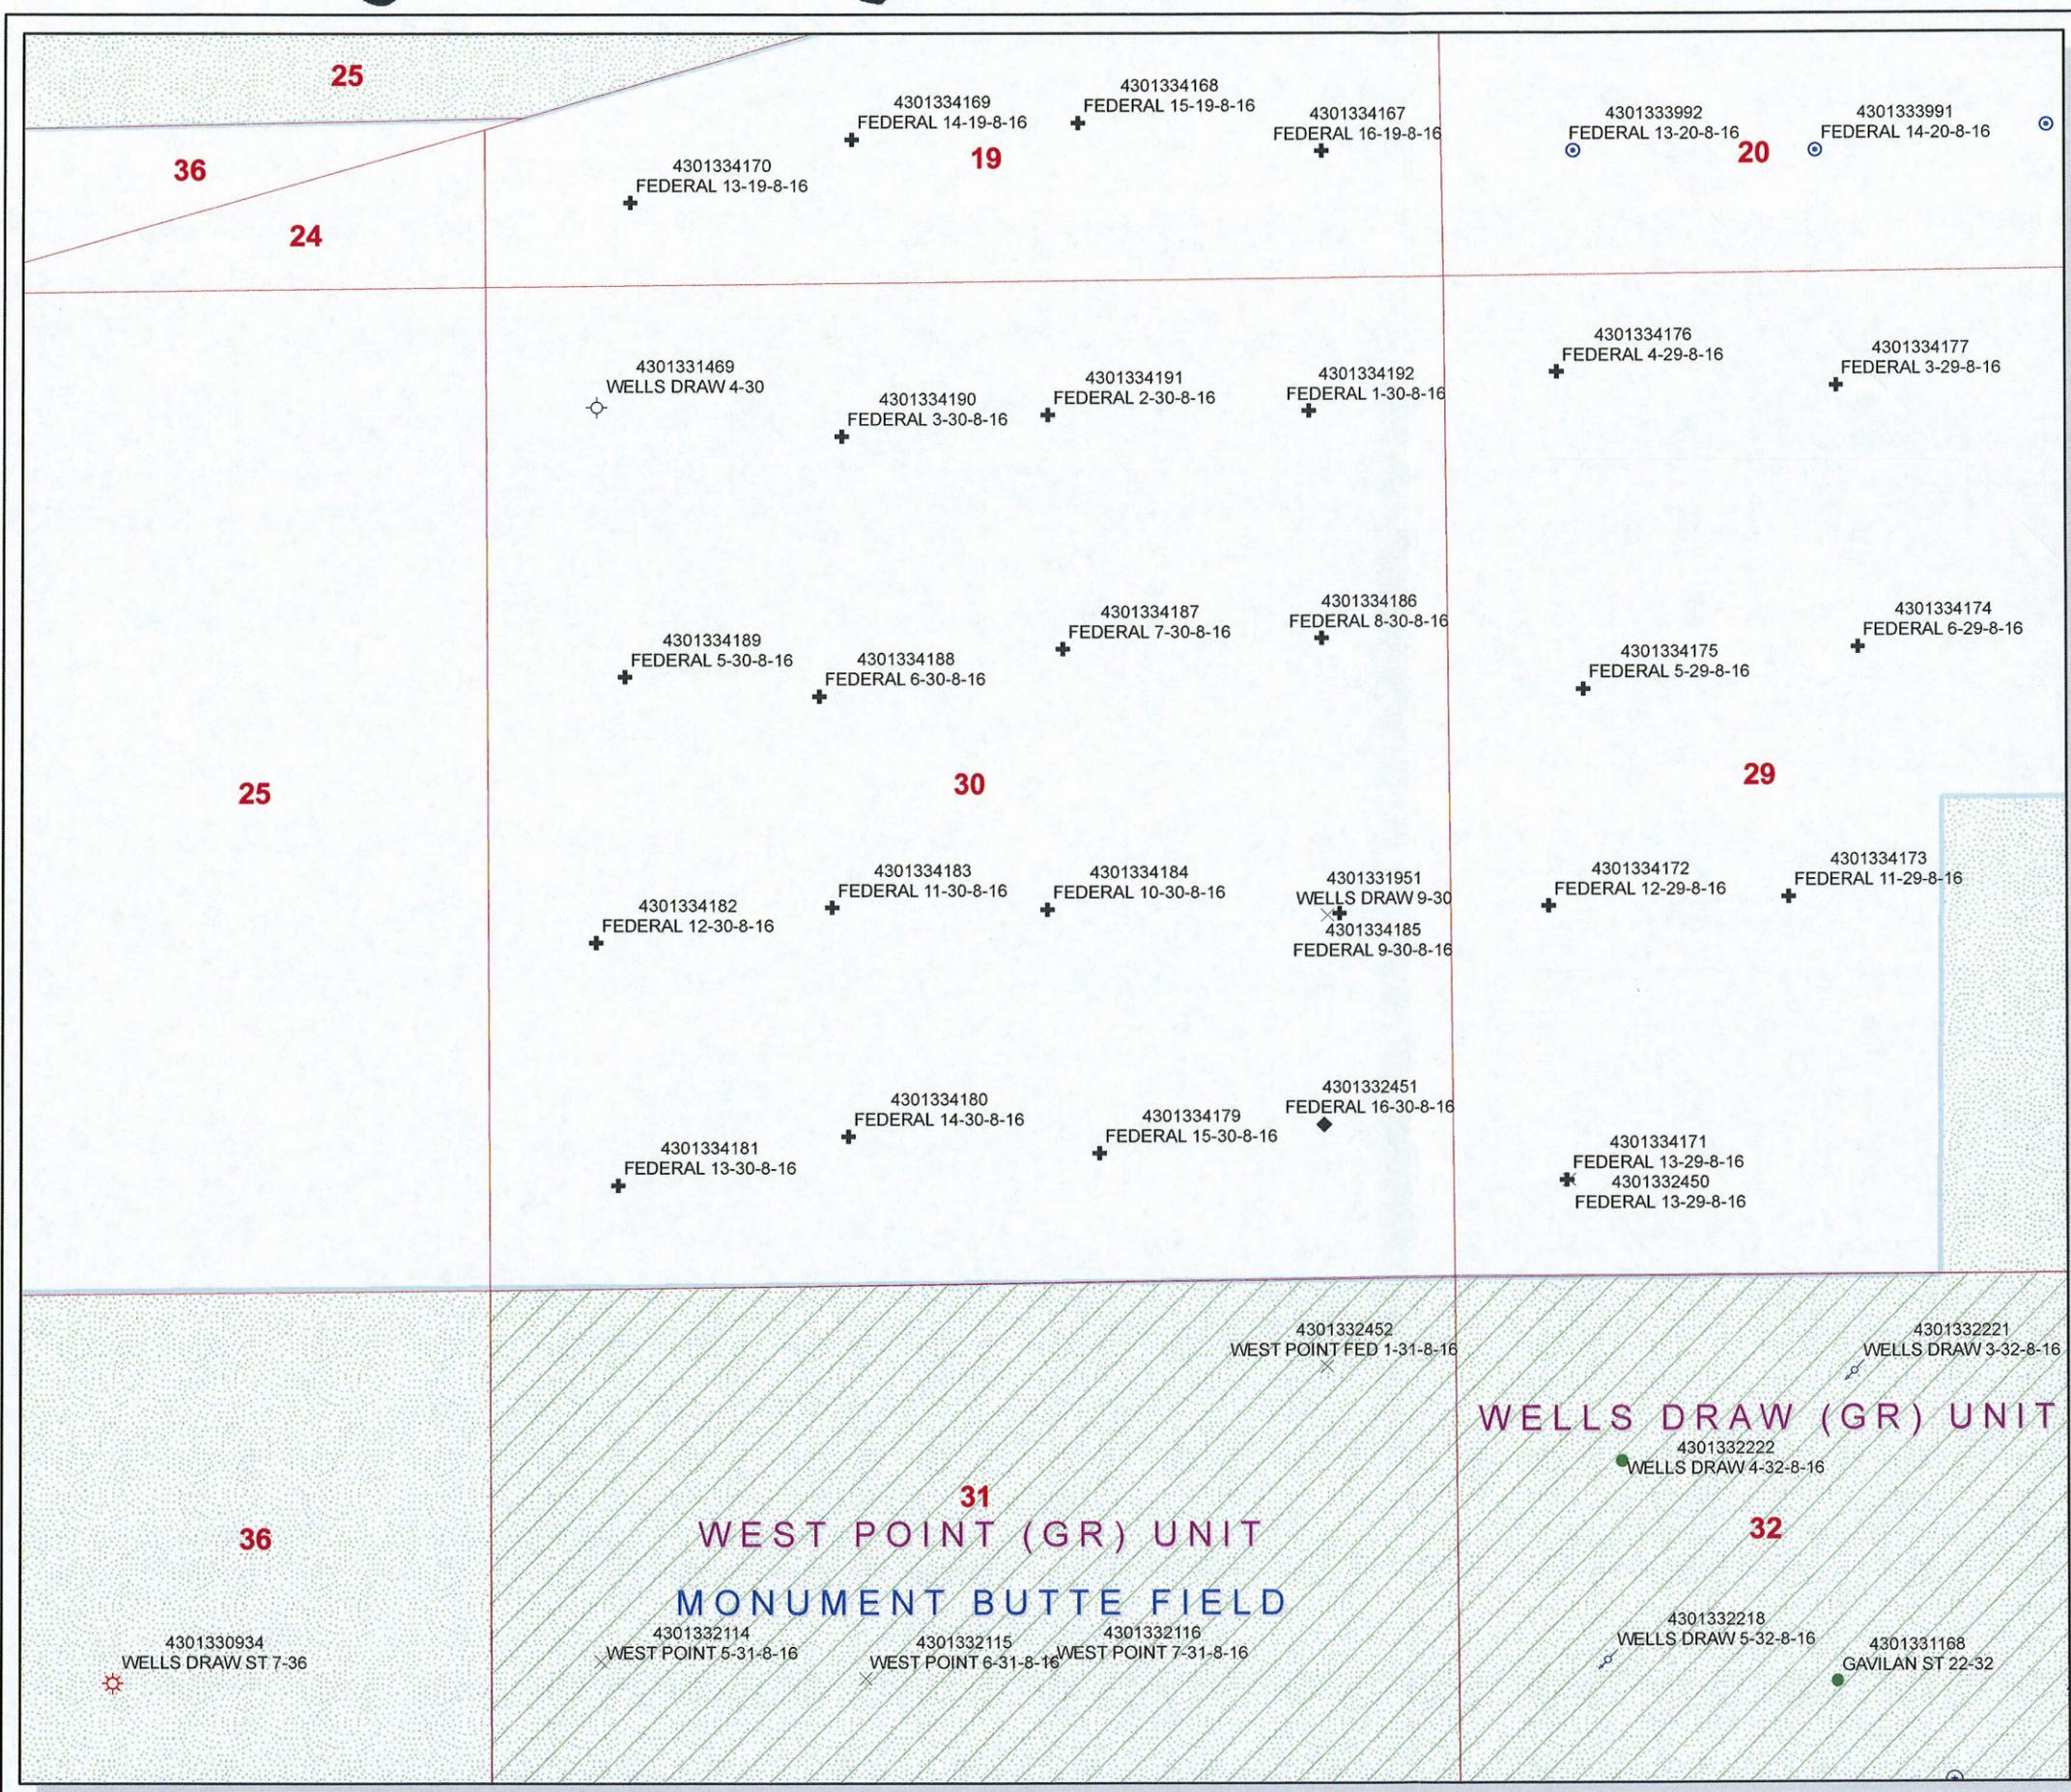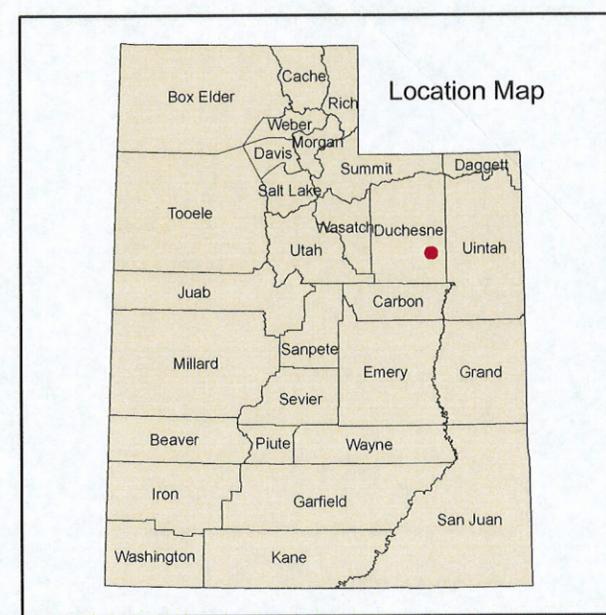



JON M. HUNTSMAN, JR.
Governor

GARY R. HERBERT
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

January 22, 2009

Newfield Production Company
Rt. 3, Box 3630
Myton, UT 84052

Re: Federal 10-30-8-16 Well, 1959' FSL, 2153' FEL, NW SE, Sec. 30, T. 8 South, R. 16 East, Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-34184.

Sincerely,

Gil Hunt
Associate Director

pab
Enclosures

cc: Duchesne County Assessor
Bureau of Land Management, Vernal Office



Operator: Newfield Production Company

Well Name & Number Federal 10-30-8-16

API Number: 43-013-34184

Lease: UTU-81000

Location: NW SE Sec. 30 T. 8 South R. 16 East

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

2. Notification Requirements

Notify the division within 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dustin Doucet at (801) 538-5281 (801) 733-0983 home

3. Reporting Requirements

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.

5. This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU-81000
6a. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name NA
2. Name of Operator Newfield Production Company		7. If Unit or CA Agreement, Name and No. NA Greater Mon. Butte
3a. Address Route #3 Box 3630, Myton UT 84052		8. Lease Name and Well No. Federal 10-30-8-16
3b. Phone No. (include area code) (435) 646-3721		9. API Well No. 43 013 34184
4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NW/SE 1959' FSL 2153' FEL At proposed prod. zone		10. Field and Pool, or Exploratory Monument Butte
14. Distance in miles and direction from nearest town or post office* Approximately 10.2 miles southwest of Myton, UT		11. Sec., T. R. M. or Blk. and Survey or Area Sec. 30, T8S R16E
15. Distance from proposed* location to nearest property or lease line, ft. Approx. 1959' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)	16. No. of acres in lease 580.24	17. Spacing Unit dedicated to this well 40 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1335'	19. Proposed Depth 6,570'	20. BLM/BIA Bond No. on file WYB000493
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5713' GL	22. Approximate date work will start* 2nd Qtr. 2009	23. Estimated duration (7) days from SPUD to rig release
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification
- Such other site specific information and/or plans as may be required by the BLM.

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 12/29/08
Title Regulatory Specialist		

Approved by (Signature) <i>Stephanie J Howard</i>	Name (Printed/Typed) Stephanie J Howard	Date 12/16/09
Title Acting Assistant Field Manager Lands & Mineral Resources	Office VERNAL FIELD OFFICE	

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached. **CONDITIONS OF APPROVAL ATTACHED**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

(Instructions on page 2)

NOTICE OF APPROVAL

NOS 11/6/08
AFMSS# 095X5024A

RECEIVED
DEC 31 2009



**UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE**

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company:	Newfield Production Company	Location:	NWSE, Sec. 30, T8S, R16E
Well No:	Federal 10-30-8-16	Lease No:	UTU-81000
API No:	43-013-34184	Agreement:	Greater Monument Butte (GR) Unit

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

RECEIVED

DEC 31 2009

DIV. OF OIL, GAS & MINING

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings to: ut_vn_opreport@blm.gov .
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

**SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.
- Construction and drilling is not allowed from May 1 – June 15 to minimize impacts during mountain plover nesting.
- If it is anticipated that construction or drilling will occur during any of the given timing restrictions, a BLM or qualified biologist shall be notified so surveys can be conducted. Depending upon the results of the surveys, permission to proceed may or may not be granted by the BLM Authorized Officer.

Reclamation:

Interim Reclamation:

- Interim reclamation of the surface environment shall take place after drilling and completion and the well is placed into production. At a minimum, this will include the stabilization of the soil surface during construction, recontouring of the unused pad area, and the reserve pit to the original contour to the extent possible, and the re-spreading of the top soil after recontouring takes place, up to the rig anchor points and any area not needed for production. Buried pipelines will be recontoured, the salvaged topsoil redistributed and reseeded. The outside borrow of the access road will have the top soil salvaged and re-spread and reseeded. The area will be reseeded using appropriate seeding methods, which includes, but is not limited to, the drill seeding method (see below). Any adjustments, due to site specific production concerns, to the reclamation COAs in this document can be submitted on Sundry form 3160-5.
- The reclamation objective is to establish a desired self-perpetuating diverse plant community. The objective is to attain **75% basal cover** based on similar undisturbed adjacent native vegetative community, and comprised of desired species and/or seeded species within 5 years of initial reclamation action. However if after three (3) growing seasons there is less than **30%** of the basal cover based on similar undisturbed native vegetative community, then the Authorized Officer may require additional seeding efforts.
- Topsoil will be segregated from the subsoil (without mixing them), stockpiled separately from other soil materials, and maintained for future use in rehabilitating the locations.

RECEIVED

DEC 31 2009

- Topsoil piles stored beyond one growing season will be stabilized and seeded to prevent erosion.
- Topsoil storage areas will be identified with appropriate signage, so it is easily identifiable where topsoil is on location.
- Noxious and invasive weeds will be inventoried and monitored. Noxious and invasive weeds will be controlled through integrated weed management including chemical, mechanical, and biological control methods. An approved Pesticide Use Proposal (PUP) is required for all herbicide applications.
- All trash and waste materials not needed for production will be removed immediately.
- Earth work for interim and final reclamation must be completed within 6 months following well completion or well plugging (weather permitting).
- Salvaged topsoil will be re-distributed evenly, and to pre-disturbance depths, over the surfaces to be revegetated.
- The soil surface will be prepared to provide a seedbed for re-establishment of desirable vegetation. Site preparation may include gouging, scarifying, dozer track-walking, mulching, hydro mulching, contour furrowing, water terracing, fertilizing, disking, soil additives or other approved methods. The seedbed preparations will be determined to accomplish the reclamation objectives above.
- The seeding contractor will provide all seed tags to the appropriate SMA prior to seeding efforts.
- Seeding will occur after August 15 and prior to winter freezing of the soil.
- Drill seeding will be used except in areas where topography or substrate composition (rock) precludes the use of the drill. If drill seeding is not possible, broadcast seeding will be implemented. If the broadcast method is used (such as on slopes of 40 percent or greater), the seed rates established for drill seeding will be doubled and seed will be immediately covered to prevent seed desiccation or predation by birds or rodents. The seeds can be covered in several ways including spreading and crimping straw over the seeded area, raking the area by hand, or dragging a chain or chain-linked fence over the seeded area.
- Any altered drainages or water courses will be stabilized through rip rap, berming, seeding, matting, or other approved methods, and will be reconstructed to have the characteristics and features of nearby functional drainages. Any disturbance to "dashed line" drainages as depicted on USGS 1:24,000 topographic maps will be coordinated with the corps of engineers prior to disturbance.

Final Reclamation:

- Final Reclamation will be similar to interim reclamation except, all disturbance associated with the well location, access road and pipeline will be reclaimed. The seed mix may include more shrubs and native species. The visual composition will be reestablished to blend with the natural surroundings through recontouring and reseeding.
- After pipeline installation is complete, all disturbed areas will be reseeded. The seed mixtures to be used will be similar to the vegetation of the surrounding areas and may consist of grasses, forbs, or shrubs. A recommended seed mixture is provided in the table below.

RECEIVED

DEC 31 2009

Monitoring:

- The initial monitoring report will include but is not limited to: when the recontouring and seeding was completed. The seed applied, the amounts, and the depth of application. Seedbed preparation such as disking , mulching, etc. Seed application such as drilling or broadcast seeding. Are there any soil amendments, fertilizers, watering, etc. The amounts of noxious and invasive weeds. Are any fencing requirements needed.
- Prior to any surface disturbance, vegetative monitoring locations and reference sites will be identified by the operator and approved by the BLM Authorized Officer.
- Vegetation monitoring protocol will be developed by the operator and approved by the BLM Authorized Officer prior to implementation of revegetation techniques and will be designed to monitor % basal vegetative cover.
- Reclamation areas will be inspected annually and monitored to document location and extent of areas with successful revegetation. Monitoring will continue until the site is considered a success by the authorized officer and the objectives established in the Green River District Guidelines. A reclamation report will be submitted electronically to the Authorized Officer by March 31 of each year.
- On Federal lands, the reclamation objective will be a vegetation community that within 5 years is comprised of desired and/or seeded species, where the basal vegetative cover is 75 percent of a similar undisturbed adjacent native vegetation community. If after 3 years basal cover is less than 30 percent, then additional seeding and reclamation efforts may be required.

Seed mix (Interim and Final Reclamation):

Common name	Latin name	lbs/acre	Recommended seed planting depth
Squirreltail grass	<i>Elymus elymoides</i>	3.0	¼ - ½"
Siberian wheatgrass	<i>Agropyron fragile</i>	1.0	½"
Shadscale saltbush	<i>Atriplex confertifolia</i>	2.0	½"
Four-wing saltbush	<i>Atriplex canescens</i>	2.0	½"
Gardner's saltbush	<i>Atriplex gardneri</i>	2.0	½"
Scarlet globemallow	<i>Sphaeralcea coccinea</i>	1.0	⅛ - ¼"

- All pounds are pure live seed.
- All seed and mulch will be certified weed free.
- Rates are set for drill seeding; double rate if broadcasting.
- Reseeding may be required if initial seeding is not successful.

RECEIVED

DEC 31 2009

DIV. OF OIL, GAS & MINING

RECEIVED

DEC 31 2009

DIV. OF OIL, GAS & MINING

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

Page 5 of 8
Well: Federal 10-30-8-16
10/27/2009

SITE SPECIFIC DOWNHOLE COAs:

- Newfield Production Co. shall adhere to all referenced requirements in the SOP (version: June 24, 2008) along with all Oil and Gas rules and requirements listed in the Code of Federal Regulations and all Federal Onshore Oil and Gas Orders.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

RECEIVED

DEC 31 2009

DIV. OF OIL, GAS & MINING

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4.

RECEIVED

DEC 31 2009

DIV. OF OIL, GAS & MINING

Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

RECEIVED

DEC 31 2009

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-81000
---	--

SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
--	---

1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: FEDERAL 10-30-8-16
------------------------------------	---

2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	9. API NUMBER: 43013341840000
--	---

3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext	9. FIELD and POOL or WILDCAT: UNDESIGNATED
--	--	--

4. LOCATION OF WELL FOOTAGES AT SURFACE: 1959 FSL 2153 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSE Section: 30 Township: 08.0S Range: 16.0E Meridian: S	COUNTY: DUCHESNE STATE: UTAH
---	---

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 1/22/2010 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input checked="" type="checkbox"/> APD EXTENSION OTHER:

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Newfield requests to extend the permit to drill this well for one year.

Approved by the Utah Division of Oil, Gas and Mining

Date: January 28, 2010

By:

NAME (PLEASE PRINT) Mandie Crozier	PHONE NUMBER 435 646-4825	TITLE Regulatory Tech
SIGNATURE N/A	DATE 1/26/2010	



The Utah Division of Oil, Gas, and Mining

- State of Utah
- Department of Natural Resources
Electronic Permitting System - Sundry Notices

Request for Permit Extension Validation Well Number 43013341840000

API: 43013341840000

Well Name: FEDERAL 10-30-8-16

Location: 1959 FSL 2153 FEL QTR NWSE SEC 30 TWP 080S RNG 160E MER S

Company Permit Issued to: NEWFIELD PRODUCTION COMPANY

Date Original Permit Issued: 1/22/2009

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision. Following is a checklist of some items related to the application, which should be verified.

- If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes No
- Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes No
- Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes No
- Have there been any changes to the access route including ownership, or rightof- way, which could affect the proposed location? Yes No
- Has the approved source of water for drilling changed? Yes No
- Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes No
- Is bonding still in place, which covers this proposed well? Yes No

**Approved by the
Utah Division of
Oil, Gas and Mining**

Signature: Mandie Crozier **Date:** 1/26/2010

Title: Regulatory Tech **Representing:** NEWFIELD PRODUCTION COMPANY **Date:** January 28, 2010

By: 

BLM - Vernal Field Office - ^{spud} Notification Form

Operator Newfield Exploration Rig Name/# Ross Rig # 26
Submitted By Don Bastian Phone Number 435-823-
6012

Well Name/Number Federal 10-30-8-16
Qtr/Qtr NW/SE Section 30 Township 8S Range 16E
Lease Serial Number UTU 81000
API Number 43-013-34184

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 11/15/10 8:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 11/15/10 2:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time 11/5/10 2:00 AM PM

Remarks Spud With Ross Rig #26 On 11/15/10 @ 8:00 AM Run 8
5/8" Casing On 11/15/10 @ 2:00 PM

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM -FORM 6

OPERATOR: **NEWFIELD PRODUCTION COMPANY**
ADDRESS: **RT. 3 BOX 3630**
MYTON, UT 84052

OPERATOR ACCT. NO. **N2695**

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION				COUNTY	SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG			
A	99999	17865	4301350339	UTE TRIBAL 9-15-4-3W	NESE	15	4S	3W	DUCHESNE	11/12/2010	11/29/10
WELL 1 COMMENTS: <i>GRRV Correction</i>											
B	99999	17400	4301350255	GREATER MON BUTTE F-2-9-16	SENE SWNW	3 2	9S	16E	DUCHESNE	11/18/2010	11/29/10
<i>GRRV Correction BML - Sec 2 SWNW</i>											
A	99999	17884	4301350355	UTE TRIBAL 10-7-4-2	NWSE	7	4S	2W 2E	DUCHESNE	11/17/2010	12/14/10
<i>GR-WS</i>											
B	99999	17400	4301350137	FEDERAL 1-28-8-16	NENE	28	8S	16E	DUCHESNE	9/20/2010	12/14/10
<i>GRRV</i>											
A	99999	17885	4301350173	UTE TRIBAL 9-24-4-3	NESE	24	4S	3W	DUCHESNE	11/12/2010	12/14/10
<i>GRRV</i>											
B	99999	17400	4301334184	FEDERAL 10-30-8-16	NWSE	30	8S	16E	DUCHESNE	11/15/2010	12/14/10
<i>GRRV</i>											

ACTION CODES (See instructions on back of form)

- A - 1 new entity for new well (single well only)
- B - well to existing entity (group or unit well)
- C - from one existing entity to another existing entity
- D - well from one existing entity to a new entity
- E - other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.

RECEIVED
DEC 06 2010

Signature *Jentri Park*
Jentri Park
Production Clerk
11/30/10

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
 NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
 Myton, UT 84052

3b. Phone (include are code)
 435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
 NWSE Section 30 T8S R16E

5. Lease Serial No.
 USA UTU-81000

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or
 GMBU

8. Well Name and No.
 FEDERAL 10-30-8-16

9. API Well No.
 4301334184

10. Field and Pool, or Exploratory Area
 GREATER MB UNIT

11. County or Parish, State
 DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 11-29-10 MIRU ROSS spud rig #21. Drill 310' of 12 1/4" hole with air mist. TIH W/7 Jt's 8 5/8" J-55 24# csgn. Set @ 312.4.
 On 12-1-10 Cement with 160 sks of Class "G" w/ 2% CaCL+ 1/4# Cello Flake. Mixed @ 15.8 ppg> 1.17 cf/sk yeild. Returned 4 bbls cement to pit.

RECEIVED
DEC 07 2010

DIV. OF OIL, GAS & MINING

I hereby certify that the foregoing is true and correct (Printed/ Typed) Xabier Lasa	Title Drilling Foreman
Signature 	Date 12/01/2010

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____	Title _____	Date _____
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.		
Office _____		

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
USA UTU-81000

SUNDRY NOTICES AND REPORTS ON WELLS

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

7. UNIT or CA AGREEMENT NAME:
GMBU

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

8. WELL NAME and NUMBER:
FEDERAL 10-30-8-16

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:
4301334184

3. ADDRESS OF OPERATOR: PHONE NUMBER
Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 435.646.3721

10. FIELD AND POOL, OR WILDCAT:
GREATER MB UNIT

4. LOCATION OF WELL:
FOOTAGES AT SURFACE:

COUNTY: DUCHESNE

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NWSE, 30, T8S, R16E

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 01/06/2011	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was completed on 01-06-11, attached is a daily completion status report.

NAME (PLEASE PRINT) Lucy Chavez-Naupoto

TITLE Administrative Assistant

SIGNATURE



DATE 01/10/2011

(This space for State use only)

RECEIVED

JAN 12 2011

DIV. OF OIL, GAS & MINING

Daily Activity Report**Format For Sundry****FEDERAL 10-30-8-16****11/1/2010 To 3/28/2011****12/22/2010 Day: 1****Completion**

Rigless on 12/22/2010 - Ran cement bond log and perforated 1st stage. - NU frac head & BOP's. RU D&M Hot Oiler & test casing, frac head, frac valves & BOP to 4500 psi. RU Perforators WLT w/ mast & pack off tool. Run CBL under pressure. WLTD was 6467' w/ TOC @ 360'. RIH w/ 3-1/8" ported guns & perforate CP5 and CP4 sands w/ (11 gram, .36"EH, 16.82¢ pen. 120°) 3 spf for a total of 42 shots. RD Perforators WLT & D&M Hot Oiler. SWIFN w/ 154 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$15,669**12/28/2010 Day: 2****Completion**

Rigless on 12/28/2010 - Frac stgs. 1-5. Flowback to pit. - Crew travel and safety meeting. RU BJ Services. Frac Stg 1- CP4/CP2/CP1 sds as shown in stimulation report. 691.9 BWTR. - Open well to pit for immediate flowback @ approx. 3 bpm. Well flowed for 3 hrs. Recovered 540 bbls. SWIFN. - RU PSI wireline. Set CFTP @ 4795' & perf PB8/GB6 sds as shown in perforation report. RU BJ Services. Frac Stg 5- PB8/GB6 sds as shown in stimulation report. 2869.9 BWTR. - RU PSI wireline. Set CFTP @ 5230' & perf D3/D1 sds as shown in perforation report. RU BJ Services. Frac Stg 4- D3/D1 sds as shown in stimulation report. 2313.9 BWTR. - RU PSI wireline. Set CFTP @ 5470' & perf B2 sds as shown in perforation report. RU BJ Services. Frac Stg 3- B2 sds as shown in stimulation report. 1776.5 BWTR. - RU PSI wireline. Set CFTP @ 5930' & perf LODC sds as shown in perforation report. RU BJ Services. Frac Stg 2- LODC sds as shown in stimulation report. 1471.8 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$126,443**12/30/2010 Day: 3****Completion**

WWS #5 on 12/30/2010 - MIRU Western rig #5. Set kill plug. Change out wellhead & BOP. Start PU & TIH W/ bit and tbg. - MIRU Western rig #5. RU HO trk & bullhead 20 BW dn casing @ 250°F. RU Perforators LLC WLT, lubricator & flange. RIH W/ Weatherford solid composite bridge plug & set @ 4640'. Bleed well off. RD WLT. ND cameron BOP & 5M frac flange. Install 3M production tbg head & NU Schaeffer BOP. Talley, drift, PU & TIH W/ used Weatherford 4 3/4" "Chomp" bit, bit sub & new 2 7/8 8rd 6.5# J-55 tbg to 1855'. SIFN W/ est 2349 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$177,581**1/3/2011 Day: 4****Completion**

WWS #5 on 1/3/2011 - TIH and DO/ CO. - Crew travel and safety meeting. MIRUHO, thaw well. SICP/ SITP @ 0 psi. Cont. RIH w/ 92 jts 2-7/8" tbg. Tag KP @ 4680'. RU drill equip and DO plg in 47 min. Tag sand @ 4745'. CO to plg @ 4850'. DO plg in 23 min. TIH to Tag plg @ 5410'. DO plg in 45 min. Circ. Well clean. EOT @ 5430'. Drain pump and lines. CWIFW.

Daily Cost: \$0**Cumulative Cost:** \$183,054

1/4/2011 Day: 5**Completion**

WWS #5 on 1/4/2011 - Drilled out remaining plugs and cleaned out well to PBTD. - Crew travel and safety meeting. Thaw well. Casing pressure at 0 psi and tubing pressure at 0 psi. Spent 2 hours to get power swivel started. Tag sand at 5757', clean out to plug at 5800', and drill out plug for 32 minutes. Tag plug at 6010' and drill out plug for 55 minutes. Tag sand at 6414', clean out to PBTD at 6496', and circulate well clean. Rig down and rack out drilling equipment. Lay down 3 joints of tubing to place end of tubing at 6421'. Drain pump and lines and CWI at 5:30 pm. 2349 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$189,083

1/5/2011 Day: 6**Completion**

WWS #5 on 1/5/2011 - Finished swabbing well and ran production tubing. - Crew travel and safety meeting. Thaw well. No pressure on casing or tubing. Rig up and run into hole with swabbing equipment. Initial shut in fluid level at 300'. Make 12 swab runs and recover 134 bbls with traces of oil and no sand. Final fluid level at 2600'. Rig down and rack out swab equipment. Pick up 3 joints and tag PBTD at 6496'. Circulate well clean, lay down 6 joints, trip out of hole with (204) joints of 2-7/8" tubing, and lay down 4-3/4" bit. Trip into hole with notched collar, (2) joints of 2-7/8" J-55 tubing, seat nipple, (1) joint of 2-7/8" J-55 tubing, tubing anchor, and (201) joints of 2-7/8" J-55 tubing. Strip off 5000 lbs BOPs and set 5-1/2" B-2 tubing anchor with 18,000 lbs of tension. End of tubing at 6336', top of seat nipple at 6271.6', and top of tubing anchor at 6237.4'. Flange up wellhead and cross-over to rod equipment. SWIFN with 2215 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$195,201

1/6/2011 Day: 7**Completion**

WWS #5 on 1/6/2011 - Tripped into hole with rod string and Central Hydraulic pump. Seated pump and tested to 800 psi. Pump tested good. PWOP with 5 spm and 122" stroke length at 12:30 pm on 1/5/11. - Crew travel and safety meeting. Thaw well. Pressure on tubing at 0 psi and pressure on casing at 0 psi. Pick up and prime 2-1/2" x 1-1/2" x 16' x 20' RHAC Central Hydraulic pump with 183" stroke. Trip into hole with (6) 1-1/2" weight bars, (20) 3/4" 4per guided rods, (124) 3/4" sucker rods, (99) 7/8" 4per guided rods, (1) 7/8" x 8' pony rod, (1) 7/8" x 4' pony rod, (1) 7/8" x 2' pony rod, and (1) 1-1/2" x 26' polish rod. Seat pump and stroke pump with unit to 800 psi. Pump tested good. Put well on production with 5 spm and 122" stroke length at 12:30 pm on 1/5/11. **Finalized**

Daily Cost: \$0**Cumulative Cost:** \$224,715

Pertinent Files: Go to File List
