

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No. UTU-81000	
6. If Indian, Allottee or Tribe Name NA	
7. If Unit or CA Agreement, Name and No. NA	
8. Lease Name and Well No. Federal 9-30-8-16	
9. API Well No. 43013-34185	
10. Field and Pool, or Exploratory <del>Monument</del> <i>Undesignated</i>	
11. Sec., T. R. M. or Blk. and Survey or Area Sec. 30, T8S R16E	
12. County or Parish Duchesne	13. State UT
14. Distance in miles and direction from nearest town or post office* Approximately 9.5 miles southwest of Myton, UT	
15. Distance from proposed* location to nearest property or lease line, ft. <i>Approx. 596' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)</i>	16. No. of acres in lease 580.24
17. Spacing Unit dedicated to this well 40 Acres	
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. <i>Approx. 1555'</i>	19. Proposed Depth 6,565'
20. BLM/BIA Bond No. on file WYB000493	
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5696' GL	22. Approximate date work will start* <i>22d Jntr. 2009</i>
	23. Estimated duration (7) days from SPUD to rig release
24. Attachments	

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- |  |   |
|--|---|
| 1. Well plat certified by a registered surveyor.   | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan.  | 5. Operator certification   |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM.             |

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date <i>12/29/08</i>
Title Regulatory Specialist		
Approved by (Signature) <i>Bradley G. Hill</i>	Name (Printed/Typed) BRADLEY G. HILL	Date <i>01-22-09</i>
Title ENVIRONMENTAL MANAGER		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

\*(Instructions on page 2)

Federal Approval of this  
Action is Necessary


RECEIVED  
JAN 14 2009  
DIV. OF OIL, GAS & MINING

# T8S, R16E, S.L.B.&M.

# NEWFIELD PRODUCTION COMPANY


S89°56'E - 77.49 (G.L.O.) 2645.49' (Measured)

N89°46'50"E - 2475.63' (Meas.) S89°56'E G.L.O. (Basis of Bearings)

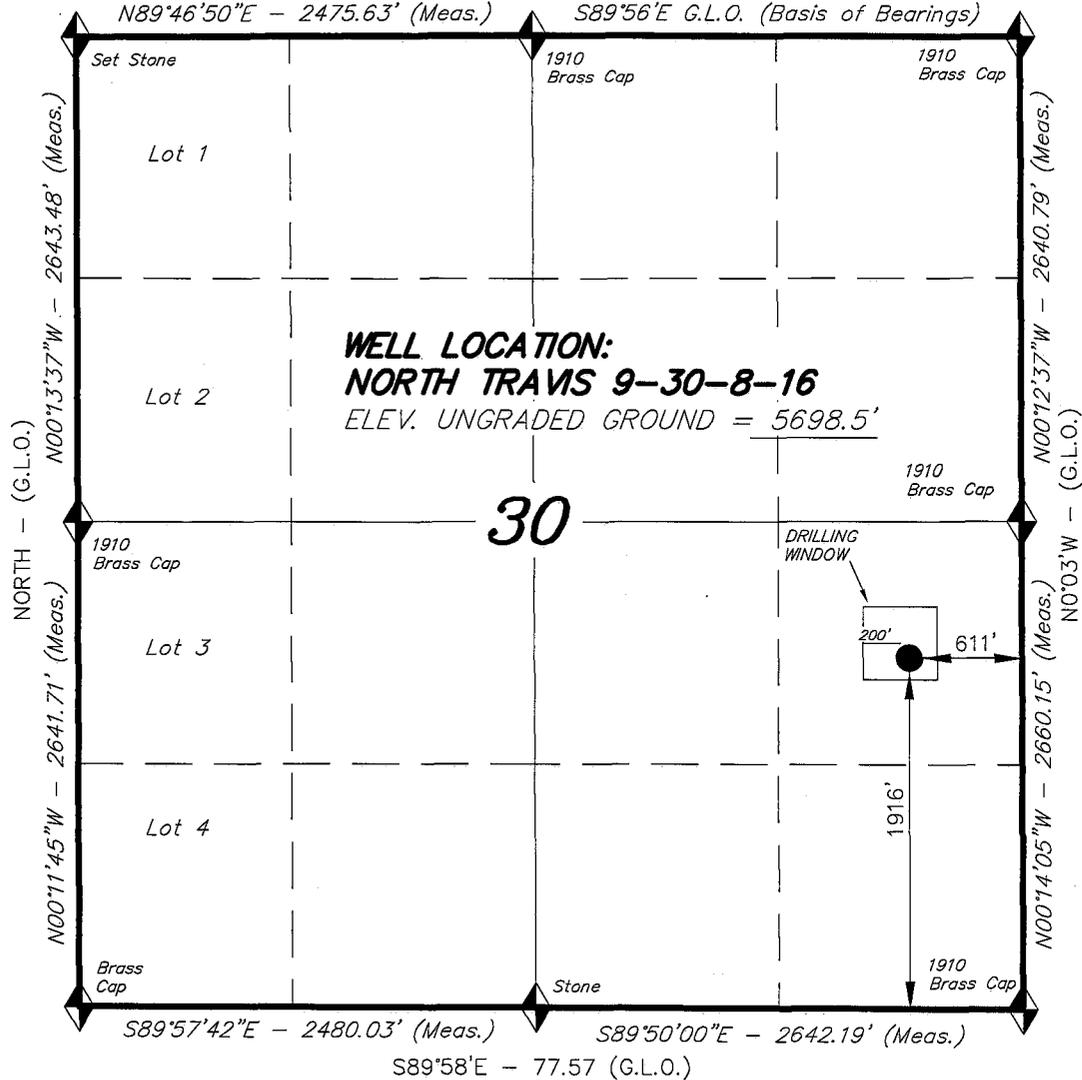


**WELL LOCATION:**  
**NORTH TRAVIS 9-30-8-16**  
 ELEV. UNGRADED GROUND = 5698.5'

WELL LOCATION, NORTH TRAVIS 9-30-8-16,  
 LOCATED AS SHOWN IN THE NE 1/4 SE 1/4  
 OF SECTION 30, T8S, R16E, S.L.B.&M.  
 DUCHESNE COUNTY, UTAH.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS  
 PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS  
 MADE BY ME OR UNDER MY SUPERVISION AND THAT  
 THE SAME ARE TRUE AND CORRECT TO THE BEST OF  
 MY KNOWLEDGE AND BELIEF. No. 189377



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV;  
 U.S.G.S. 7-1/2 min QUAD (MYTON SW)

**NORTH TRAVIS 9-30-8-16**  
 (Surface Location) NAD 83  
 LATITUDE = 40° 05' 12.80"  
 LONGITUDE = 110° 09' 17.68"

## TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078  
 (435) 781-2501

DATE SURVEYED: 10-23-08	SURVEYED BY: T.H.
DATE DRAWN: 10-27-08	DRAWN BY: F.T.M.
REVISED:	SCALE: 1" = 1000'

NEWFIELD PRODUCTION COMPANY  
FEDERAL 9-30-8-16  
NE/SE SECTION 30, T8S, R16E  
DUCHESNE COUNTY, UTAH

ONSHORE ORDER NO. 1

DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta                    0' – 1730'  
Green River            1730'  
Wasatch                6565'  
Base of Moderately Saline Ground Water @ 5250'

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation 1730' – 6565' - Oil

4. PROPOSED CASING PROGRAM

Please refer to the Monument Butte Field Standard Operation Procedure (SOP).

5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:

Please refer to the Monument Butte Field SOP. See Exhibit "C".

6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:

Please refer to the Monument Butte Field SOP.

7. AUXILIARY SAFETY EQUIPMENT TO BE USED:

Please refer to the Monument Butte Field SOP.

8. TESTING, LOGGING AND CORING PROGRAMS:

Please refer to the Monument Butte Field SOP.

9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:

The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered.

10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:

Please refer to the Monument Butte Field SOP.

NEWFIELD PRODUCTION COMPANY  
FEDERAL 9-30-8-16  
NE/SE SECTION 30, T8S, R16E  
DUCHESNE COUNTY, UTAH

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Federal 9-30-8-16 located in the NE 1/4 SE 1/4 Section 30, T8S, R16E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.4 miles  $\pm$  to the junction of this highway and UT State Hwy 53; proceed southwesterly - 7.0 miles  $\pm$  to its junction with the beginning of the proposed access road to the southwest; proceed southwesterly along the proposed access road - 5670'  $\pm$ ; turn and proceed in a northwesterly direction along the proposed access road - 160'  $\pm$  to the proposed well location.

2. PLANNED ACCESS ROAD

See Topographic Map "B" for the location of the proposed access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

All permanent surface equipment will be painted Carlsbad Canyon.  
Please refer to the Monument Butte Field Standard Operating Procedure (SOP).

5. LOCATION AND TYPE OF WATER SUPPLY

Newfield Production will transport water by truck for drilling purposes from the following water sources:

Johnson Water District  
Water Right : 43-7478

Neil Moon Pond  
Water Right: 43-11787

Maurice Harvey Pond  
Water Right: 47-1358

Newfield Collector Well  
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

Please refer to the Monument Butte Field SOP. See Exhibit "A".

6. SOURCE OF CONSTRUCTION MATERIALS

Please refer to the Monument Butte Field SOP.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

Please refer to the Monument Butte Field SOP.

8. **ANCILLARY FACILITIES**

Please refer to the Monument Butte Field SOP.

9. **WELL SITE LAYOUT**

See attached Location Layout Diagram.

10. **PLANS FOR RESTORATION OF SURFACE**

Please refer to the Monument Butte Field SOP.

11. **SURFACE OWNERSHIP** - Bureau Of Land Management (Proposed location and access roads leading to).

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Surveys have been completed the reports will be forthcoming.

Newfield Production Company requests a 1490' ROW in Lease UTU-69061, a 3480' ROW in Lease UTU-69060, a 130' ROW in Lease UTU-77339, and 730' of disturbed area be granted in Lease UTU-81000 to allow for construction of the planned access road. **Refer to Topographic Map "B"**. A permanent width of 30' and a running surface of 18' is proposed for the planned access road. The construction phase of the planned access road will last approximately (5) days. The planned access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 160' of disturbed area be granted in Lease UTU-81000 to allow for construction of the proposed surface gas lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a 10" or smaller gas gathering line, and a 3" poly fuel gas line, with a permanent width of 30' upon completion of the proposed gas lines. The construction phase of the proposed gas lines will last approximately (5) days. Both lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Newfield Production Company requests 160' of disturbed area be granted in Lease UTU-81000 to allow for construction of the proposed water lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line, with a permanent width of 30' upon completion of the proposed water return line. The construction phase of the proposed water lines will last approximately (5) days. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP. In the event that the proposed well is converted to a water injection well, a separate injection permit will be applied for through the proper agencies.

### Water Disposal

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), State of Utah approved surface disposal facilities, or Federally approved surface disposal facilities.

### Threatened, Endangered, And Other Sensitive Species

**Mountain Plover:** If new construction or surface disturbing activities are scheduled to occur between May 15 and June 15, detailed surveys of the area within 0.5 mile of the proposed location and within 300 feet of proposed access routes must be conducted to detect the presence of mountain plovers. All surveys must be conducted in accordance with the survey protocols outlined in the most recent USFWS Survey Protocol. Surveys must be completed prior to initiating new construction or surface disturbing activities. No new construction or surface disturbing activities will be allowed between May 15 and June 15 within a 0.5 mile radius of any documented mountain plover nest site.

### Reserve Pit Liner

A 16 mil liner with felt is required. Please refer to the Monument Butte Field SOP.

### Location and Reserve Pit Reclamation

Please refer to the Monument Butte Field SOP.

The following seed mixture will be used on the topsoil stockpile, to the recontoured surface of the reserve pit, and for final reclamation: (All poundages are in pure live seed)

Squirrel Tail	<i>Elymus Elymoides</i>	6 lbs/acre
Siberian Wheatgrass	<i>Agropyron Fragile</i>	2 lbs/acre
Gardner Saltbush	<i>Atriplex Gardneri</i>	1 lbs/acre
Shadscale	<i>Atriplex Confertifolia</i>	1 lbs/acre
Fourwing Saltbush	<i>Atriplex Canescens</i>	1 lbs/acre
Scarlet Globemallow	<i>Sphaeralcea Conccinea</i>	0.20 lbs/acre
Forage Kochia	<i>Kochia Prostrata</i>	0.20 lbs/acre

### Details of the On-Site Inspection

The proposed Federal 9-30-8-16 was on-sited on 11/13/08. The following were present; Dave Allred (Newfield Production ), Tim Eaton (Newfield Production ), James Herford (Bureau of Land Management), Brandon McDonald (Bureau of Land Management), and Dave Gordon (Bureau of Land Management). Weather conditions were clear and ground cover was 100% open.

### LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION

#### Representative

Name: Dave Allred  
Address: Route #3 Box 3630  
Myton, UT 84052  
Telephone: (435) 646-3721

#### Certification


Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #9-30-8-16 NE/SE Section 30, Township 8S, Range 16E: Lease UTU-81000 Duchesne County, Utah: and is responsible under the terms and conditions of the lease for the

operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

12/29/08

Date



Mandie Crozier





Regulatory Specialist

Newfield Production Company



# NEWFIELD PRODUCTION COMPANY

## CROSS SECTIONS NORTH TRAVIS 9-30-8-16

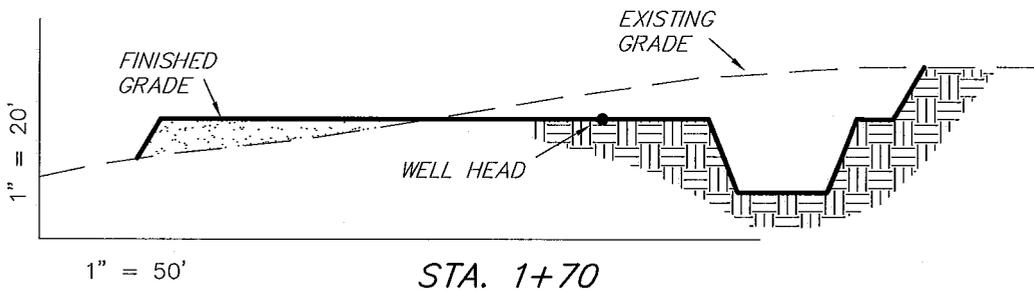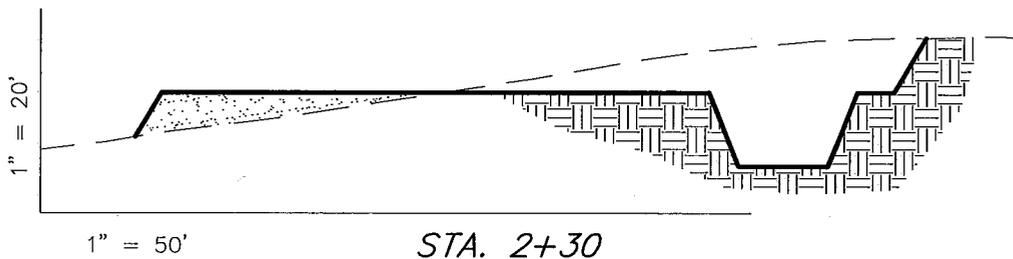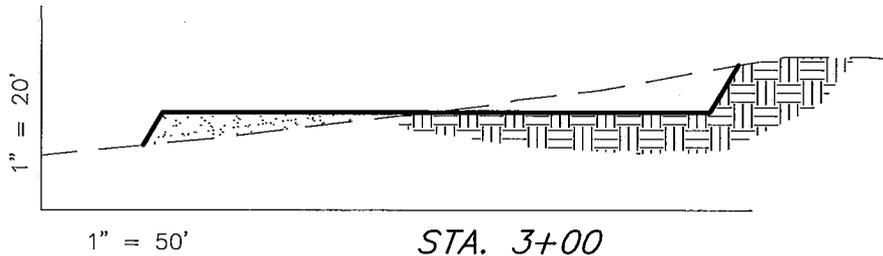

NOTE:  
UNLESS OTHERWISE  
NOTED ALL CUT/FILL  
SLOPES ARE AT 1.5:1

### ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	2,390	2,390	Topsoil is not included in Pad Cut	0
PIT	640	0		640
TOTALS	3,030	2,390	1,040	640



SURVEYED BY: T.H.	DATE SURVEYED: 10-23-08
DRAWN BY: F.T.M.	DATE DRAWN: 10-28-08
SCALE: 1" = 50'	REVISED:

**Tri State**  
Land Surveying, Inc.  
180 NORTH VERNAL AVE. VERNAL, UTAH 84078  
(435) 781-2501

# NEWFIELD PRODUCTION COMPANY

## TYPICAL RIG LAYOUT NORTH TRAVIS 9-30-8-16

PROPOSED ACCESS ROAD (Max. 6% Grade)

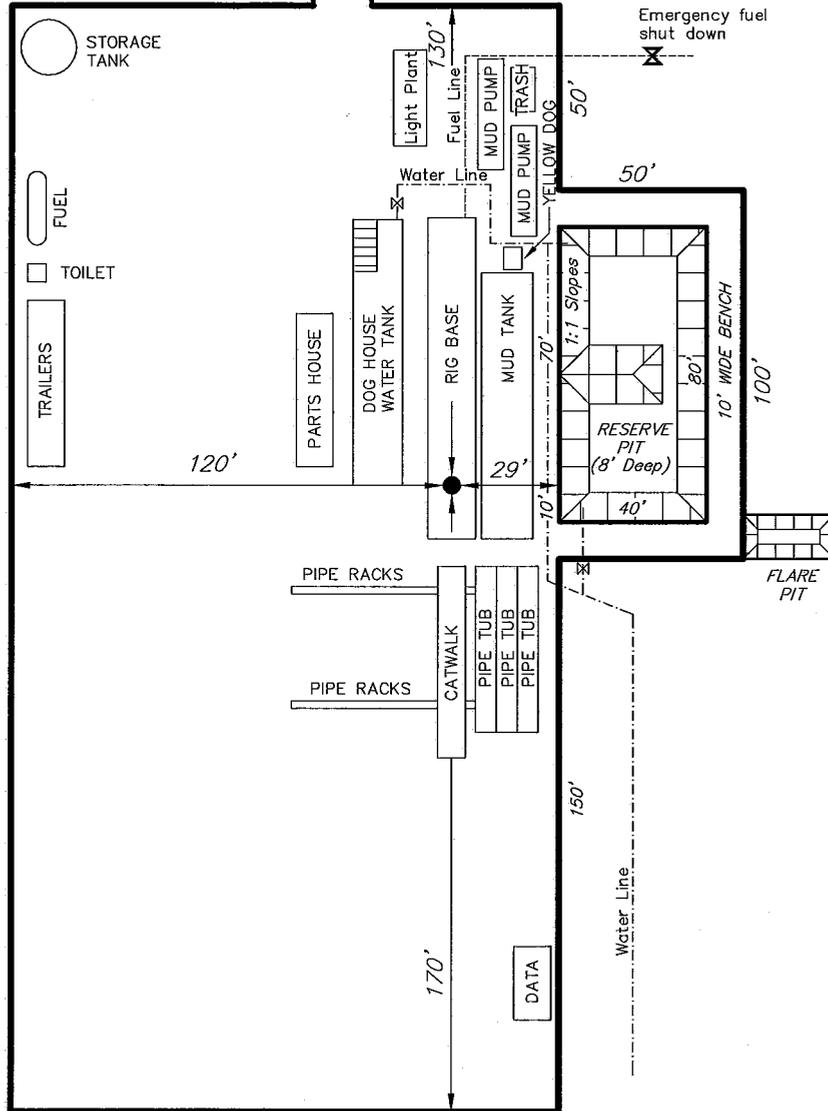

SURVEYED BY: T.H.	DATE SURVEYED: 10-23-08
DRAWN BY: F.T.M.	DATE DRAWN: 10-28-08
SCALE: 1" = 50'	REVISED:

**Tri State**  
Land Surveying, Inc. (435) 781-2501  
180 NORTH VERNAL AVE. VERNAL, UTAH 84078


# Lowfield Production Company Proposed Site Facility Diagram

Federal 9-30-8-16

NE/SE Sec. 30, T8S, R16E

Duchesne County, Utah

UTU-81000

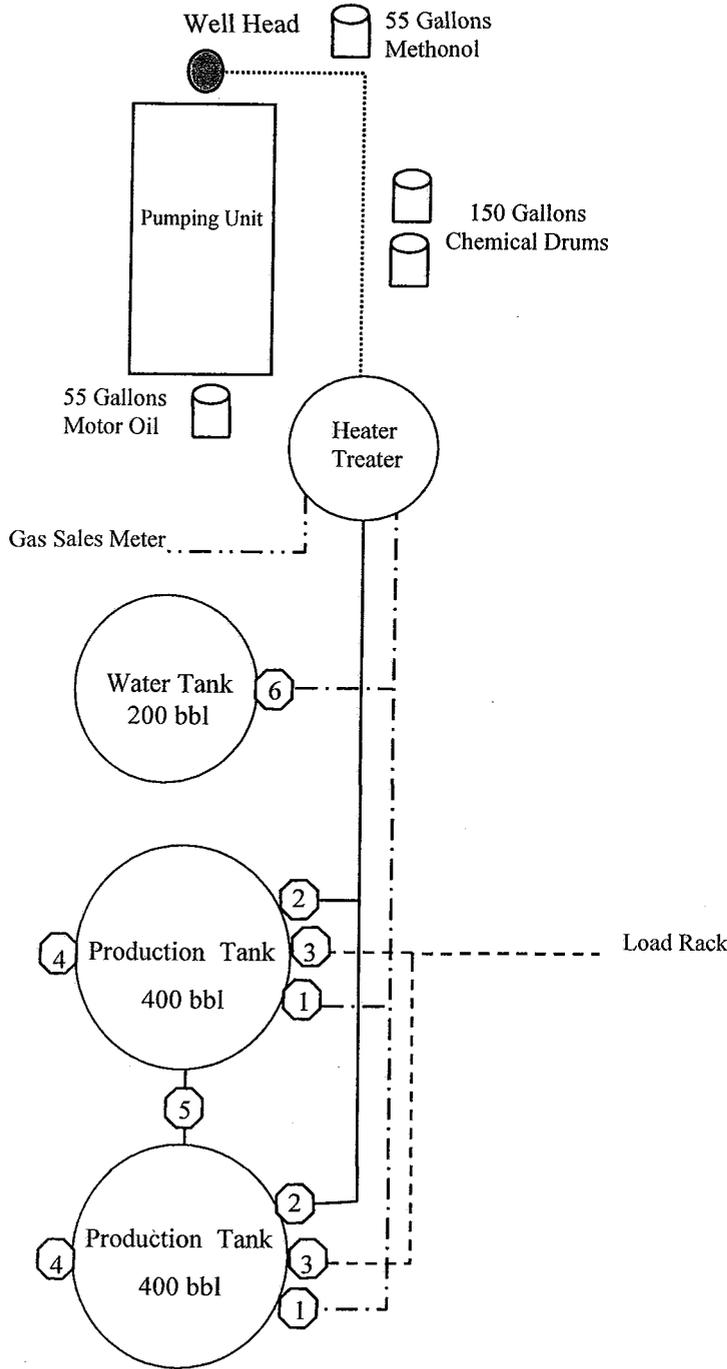

## Legend

Emulsion Line	.....
Load Rack	-----
Water Line	-----
Gas Sales	.....
Oil Line	_____

### Production Phase:

- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open

### Sales Phase:


- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

### Draining Phase:

- 1) Valves 1 and 6 open

Diked Section



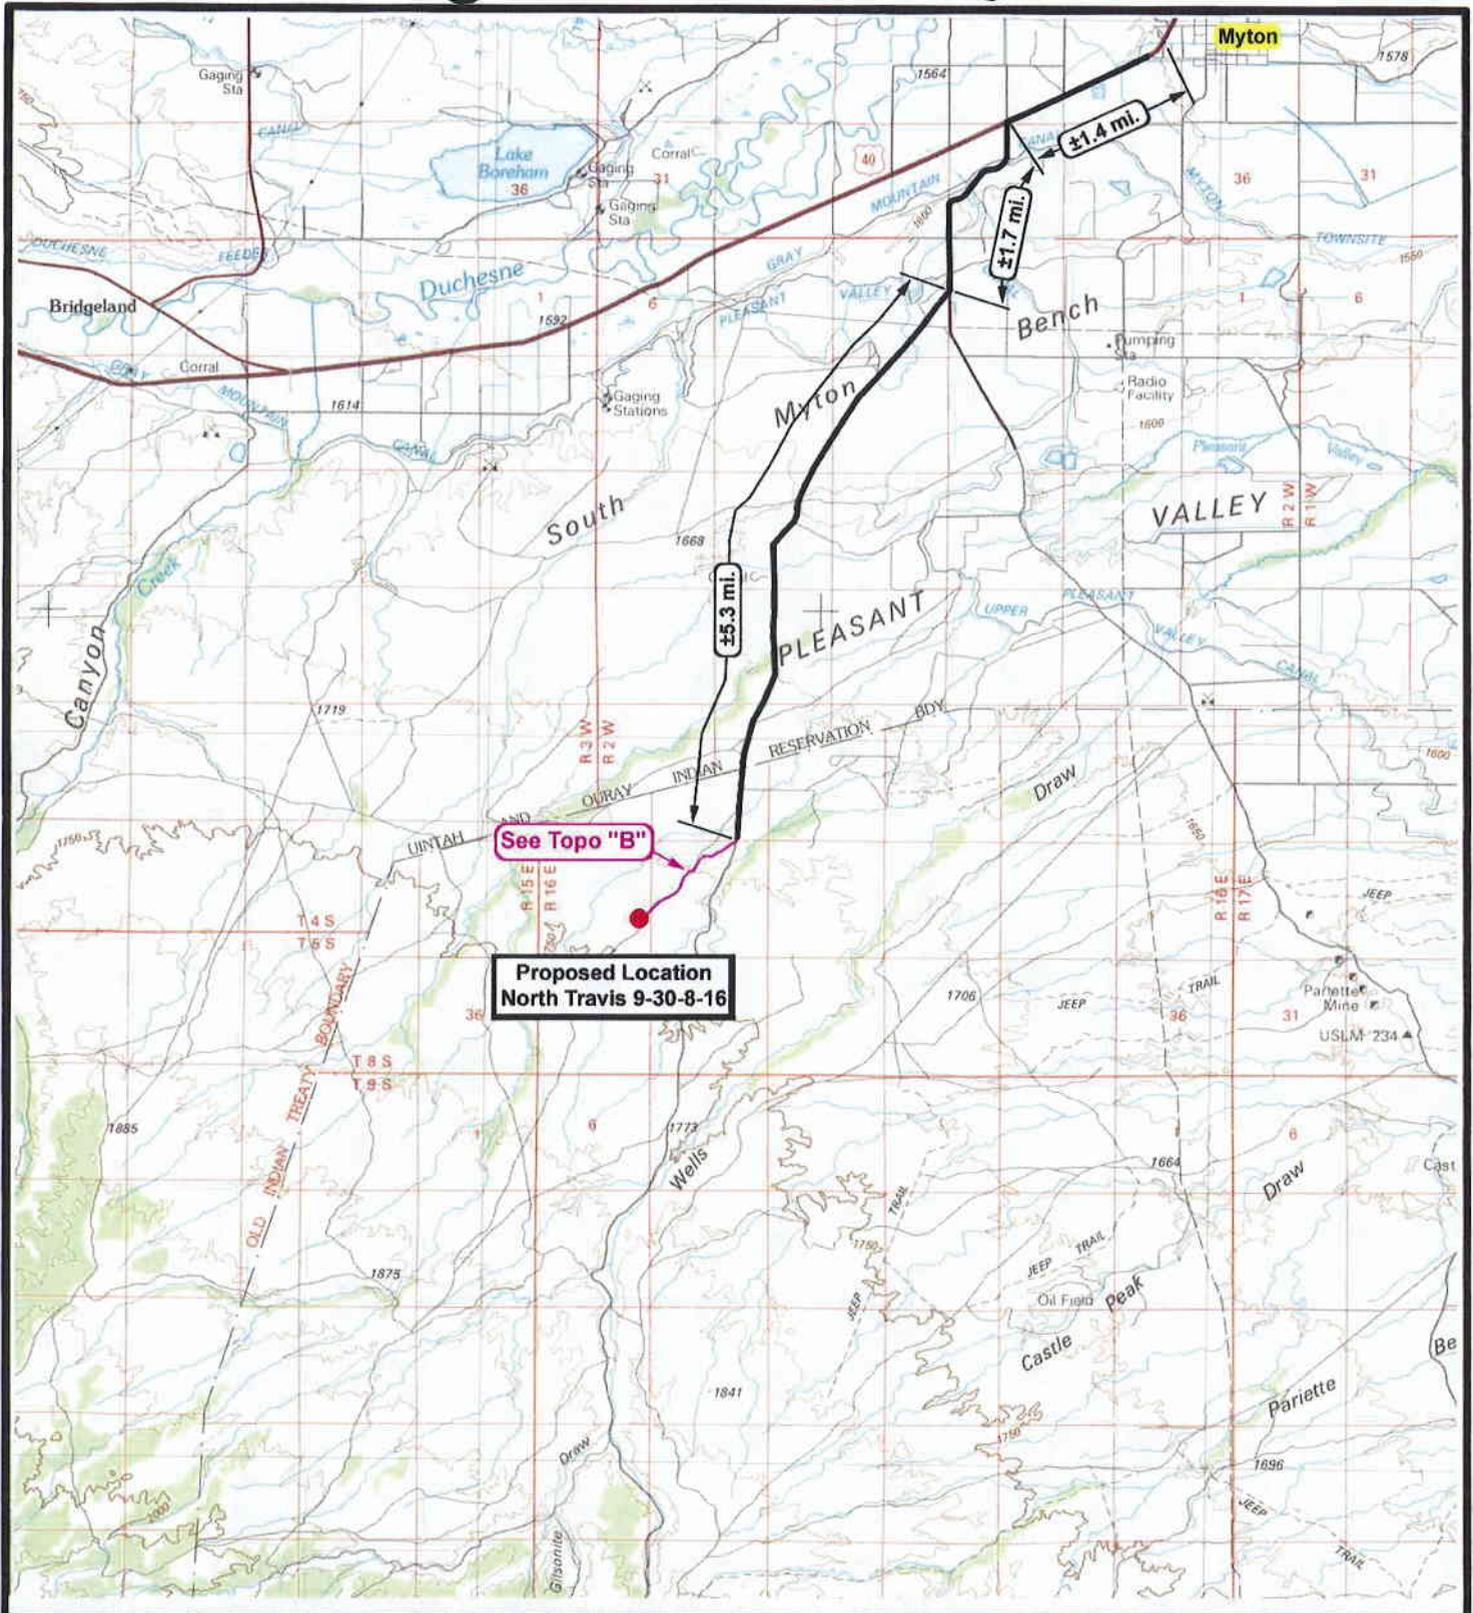


  
**NEWFIELD**  
 Exploration Company

---

**North Travis 9-30-8-16**  
**SEC. 30, T8S, R16E, S.L.B.&M.**




  
**Tri-State**  
 Land Surveying Inc.  
 (435) 781-2501  
 180 North Vernal Ave. Vernal, Utah 84078

---


**SCALE: 1 = 100,000**  
**DRAWN BY: mw**  
**DATE: 10-29-2008**

**Legend**

 Existing Road  
 Proposed Access

---

**TOPOGRAPHIC MAP**  
"A"

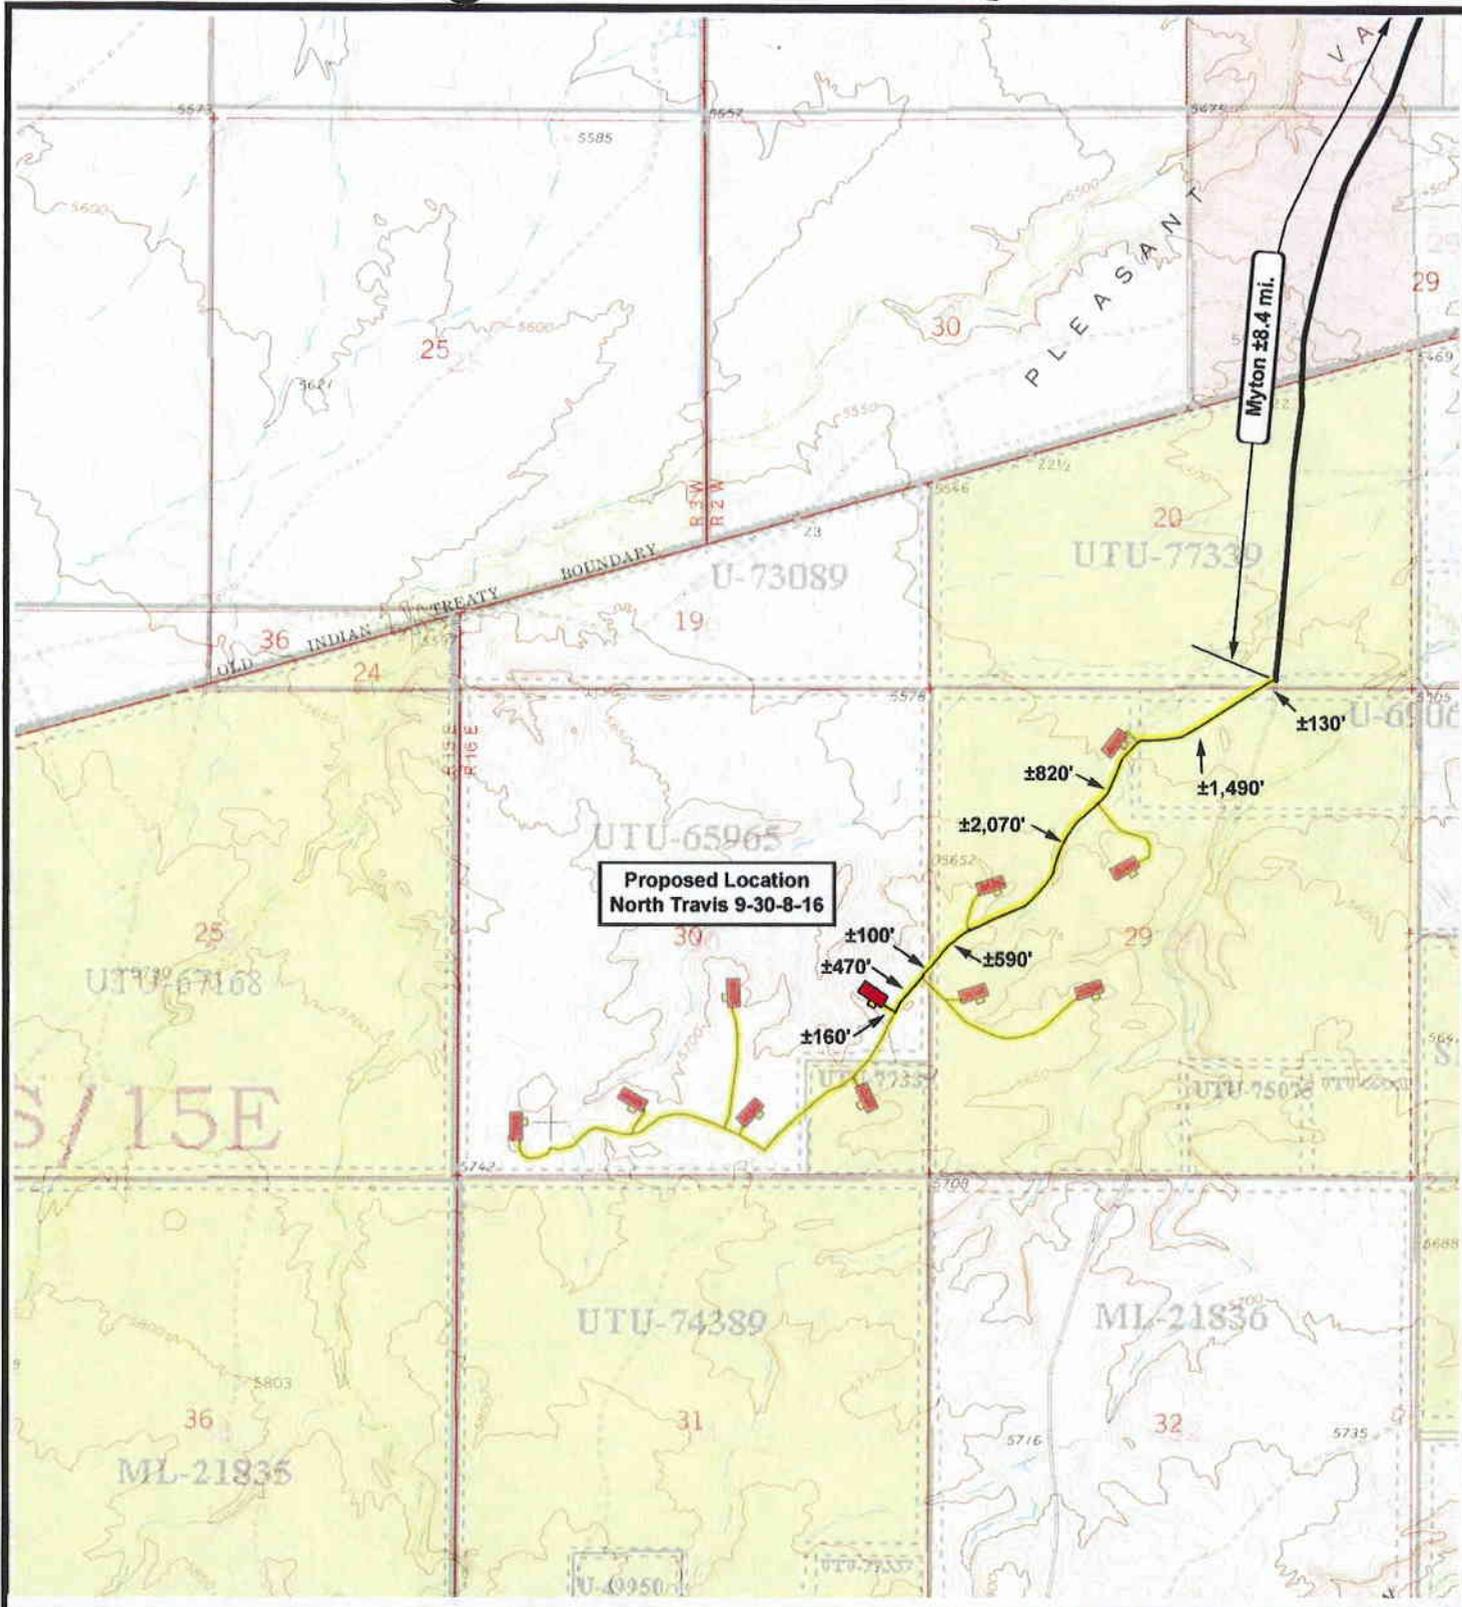

**Proposed Location  
North Travis 9-30-8-16**

**Myton ±8.4 mi.**

**NEWFIELD**  
Exploration Company

**North Travis 9-30-8-16  
SEC. 30, T8S, R16E, S.L.B.&M.**




**Tri-State**  
Land Surveying Inc.  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'  
DRAWN BY: mw  
DATE: 10-29-2008

**Legend**

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP  
**"B"**

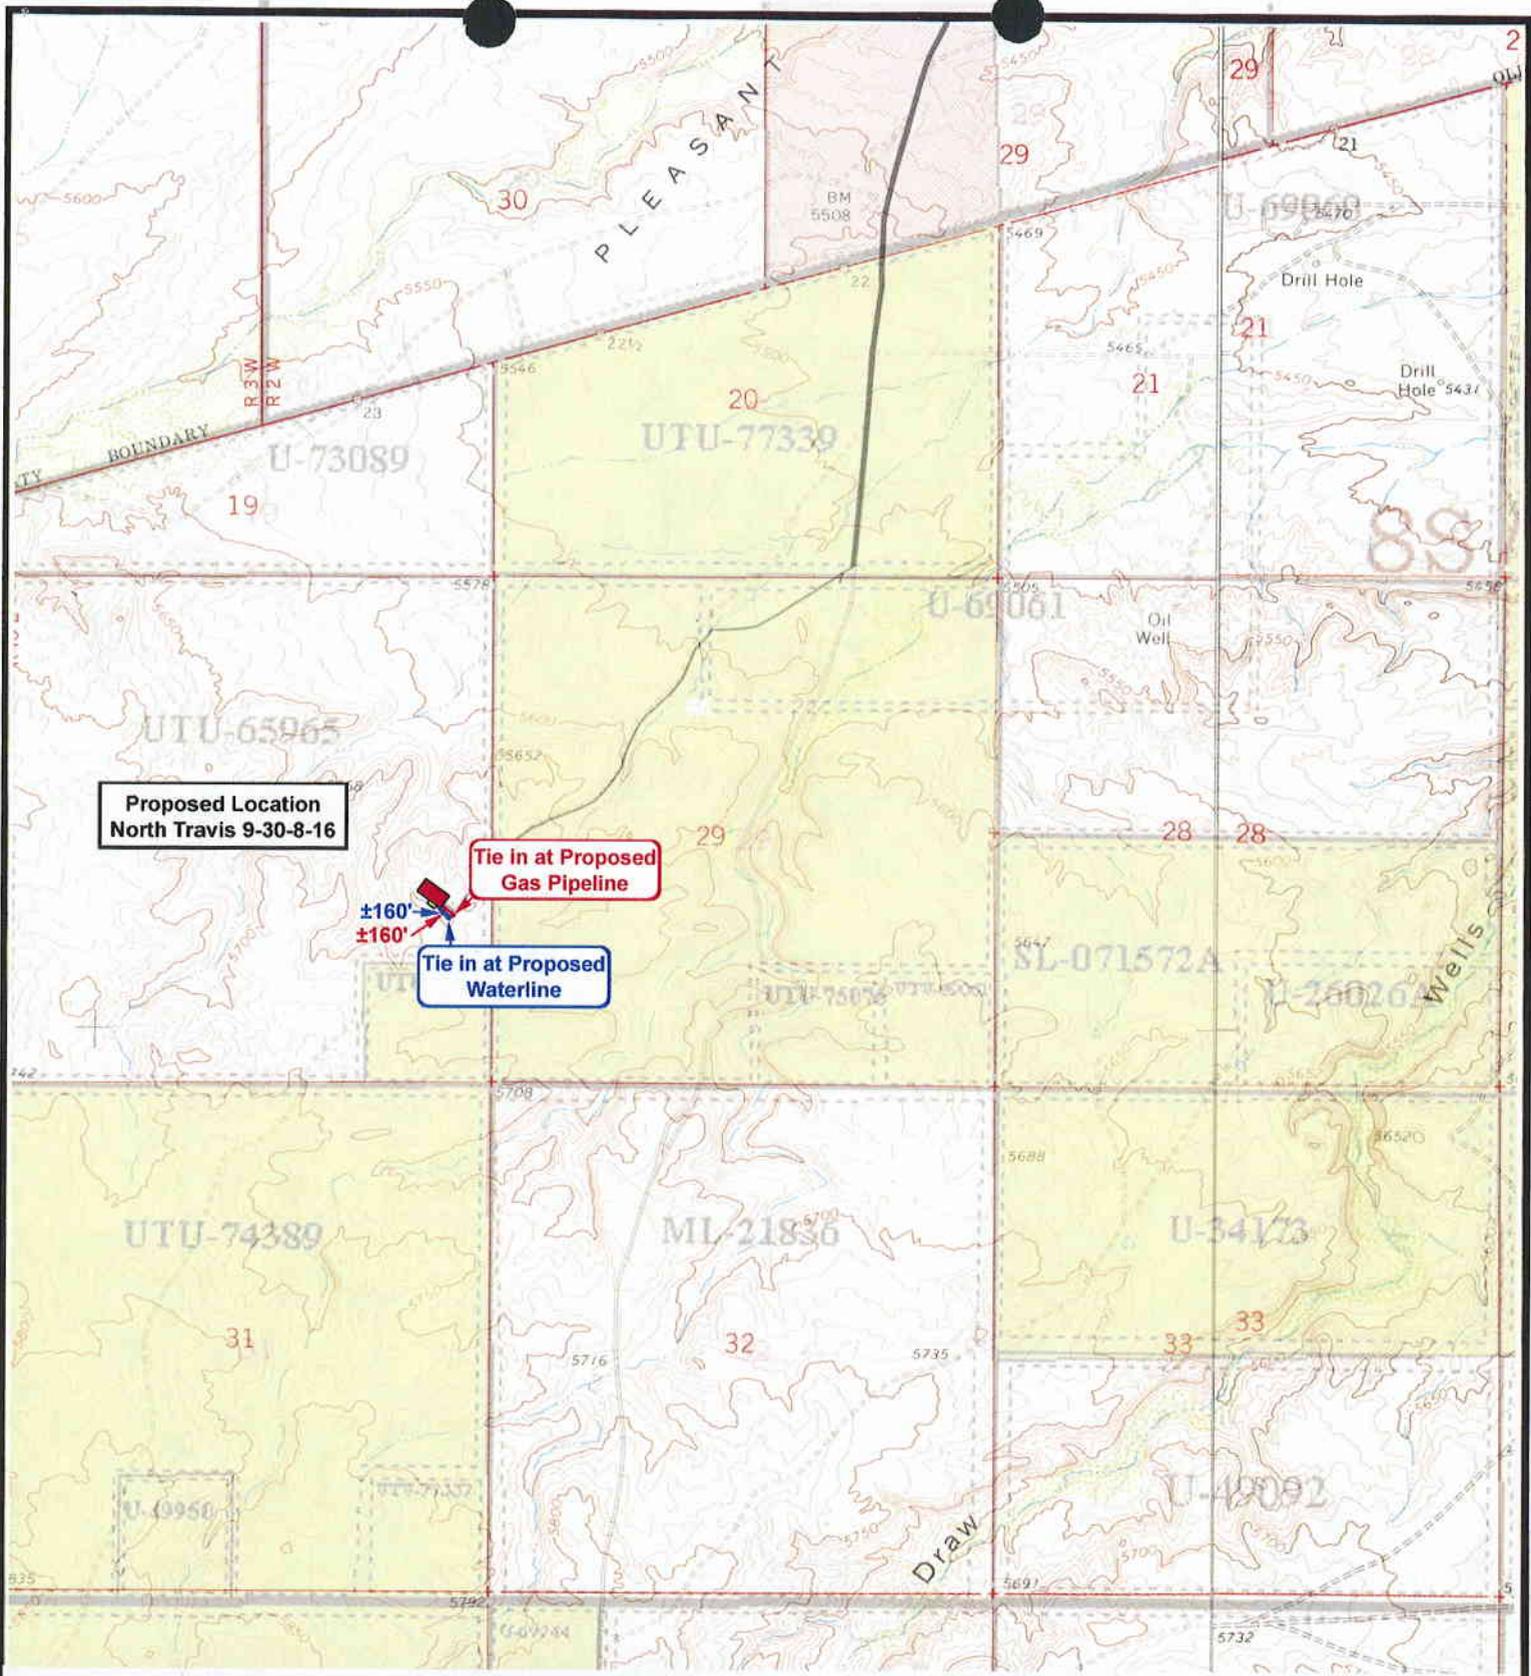


**NEWFIELD**  
Exploration Company

---

**North Travis 9-30-8-16**  
**SEC. 30, T8S, R16E, S.L.B.&M.**





**Tri-State**  
*Land Surveying Inc.*  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

---

SCALE: 1" = 2,000'  
DRAWN BY: mw  
DATE: 11-20-2008


**Legend**

-  Roads
-  Proposed Gas Line
-  Proposed Water Line

---

TOPOGRAPHIC MAP

"C"

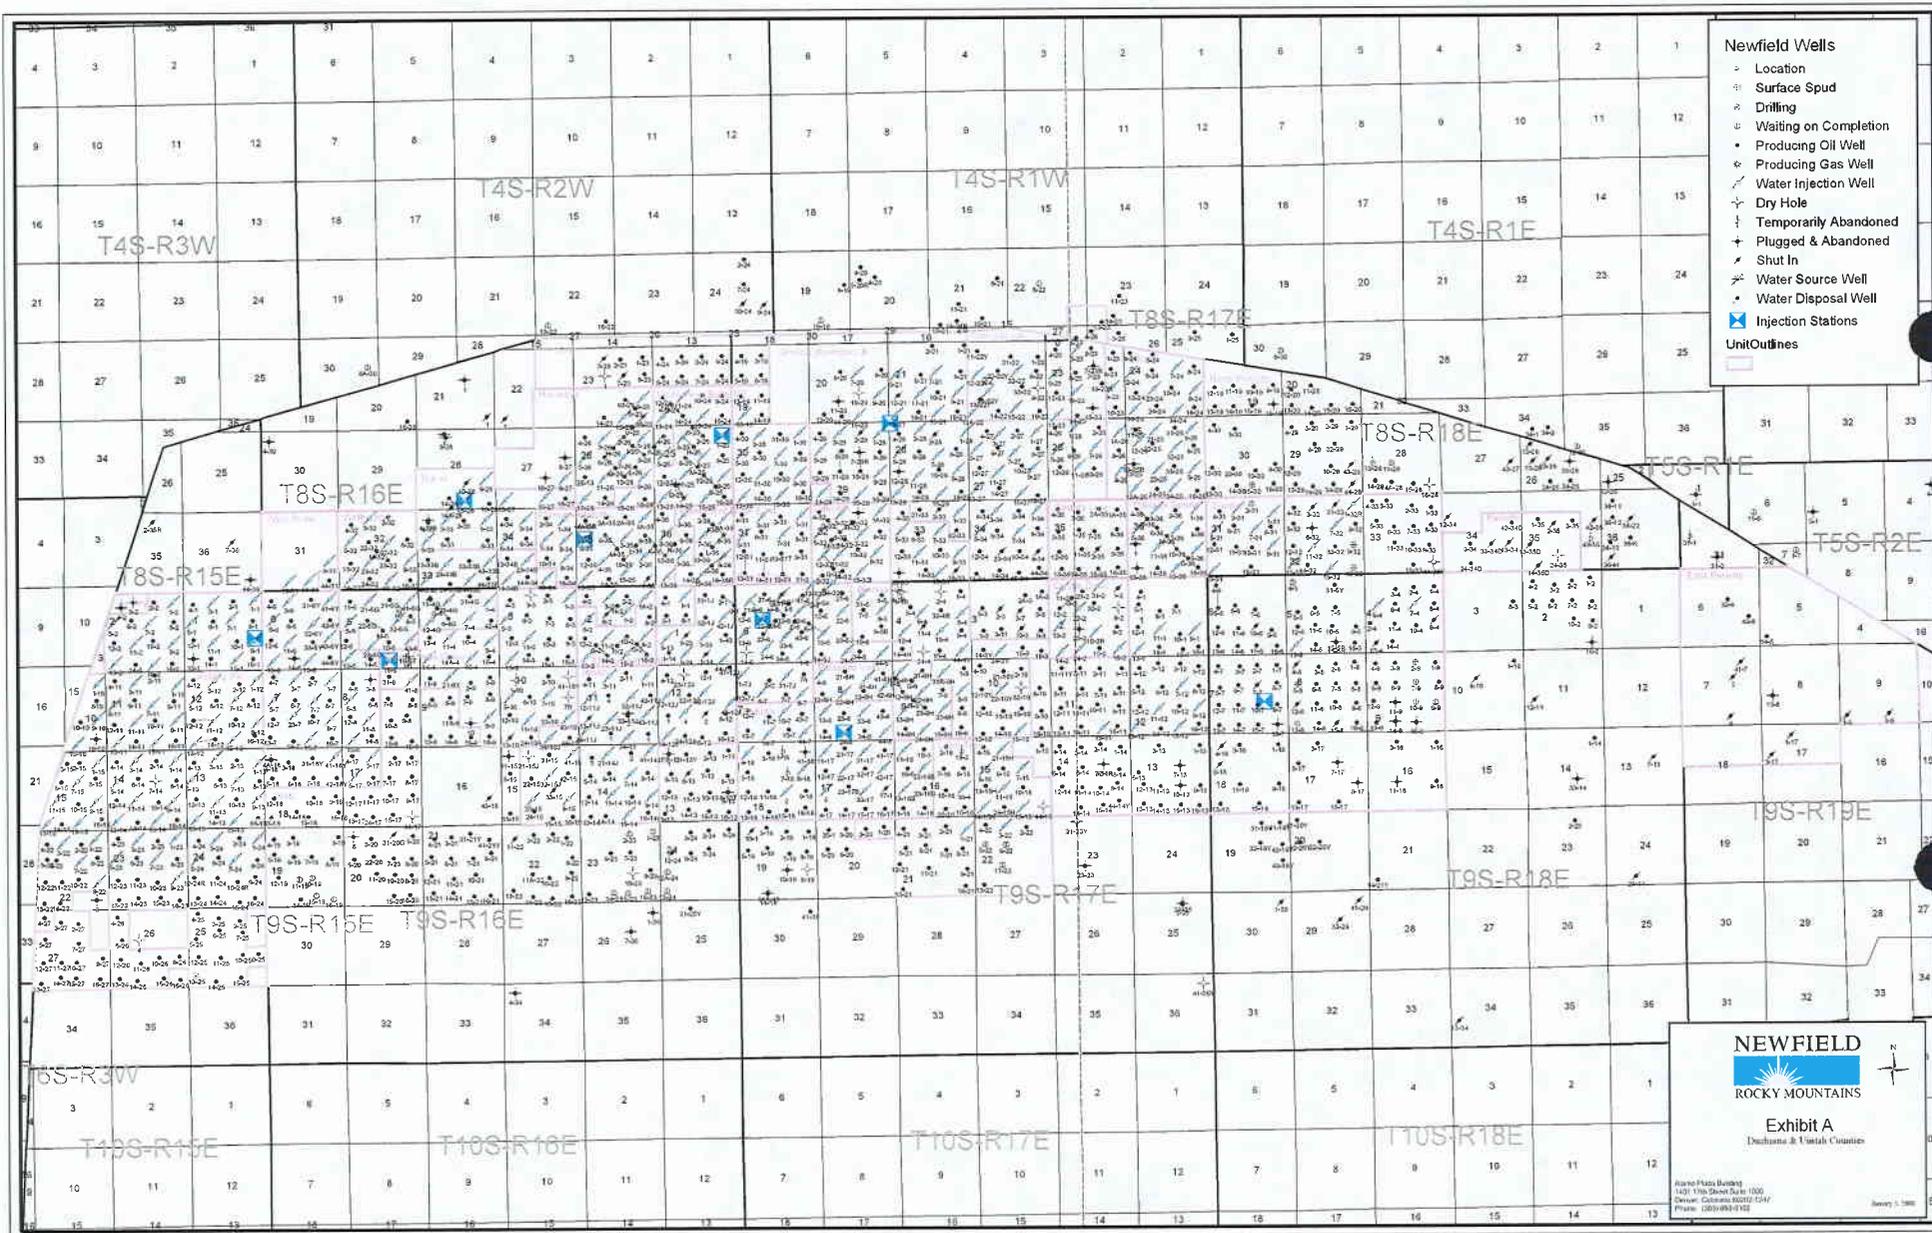


- Newfield Wells**
- Location
  - ⊕ Surface Spud
  - ⊛ Drilling
  - ⊖ Waiting on Completion
  - ⊙ Producing Oil Well
  - ⊙ Producing Gas Well
  - ⊙ Water Injection Well
  - ⊙ Dry Hole
  - ⊙ Temporarily Abandoned
  - ⊕ Plugged & Abandoned
  - ⊙ Shut In
  - ⊕ Water Source Well
  - ⊙ Water Disposal Well
  - ⊗ Injection Stations
- Unit Outlines**
- Unit Outline

**NEWFIELD**  
 ROCKY MOUNTAINS

Exhibit A  
 Duchesne & Uintah Counties

Alvord Plaza Building  
 1401 15th Street Suite 1000  
 Denver, Colorado 80202-1547  
 Phone: 303.955.6100

January 7, 2008

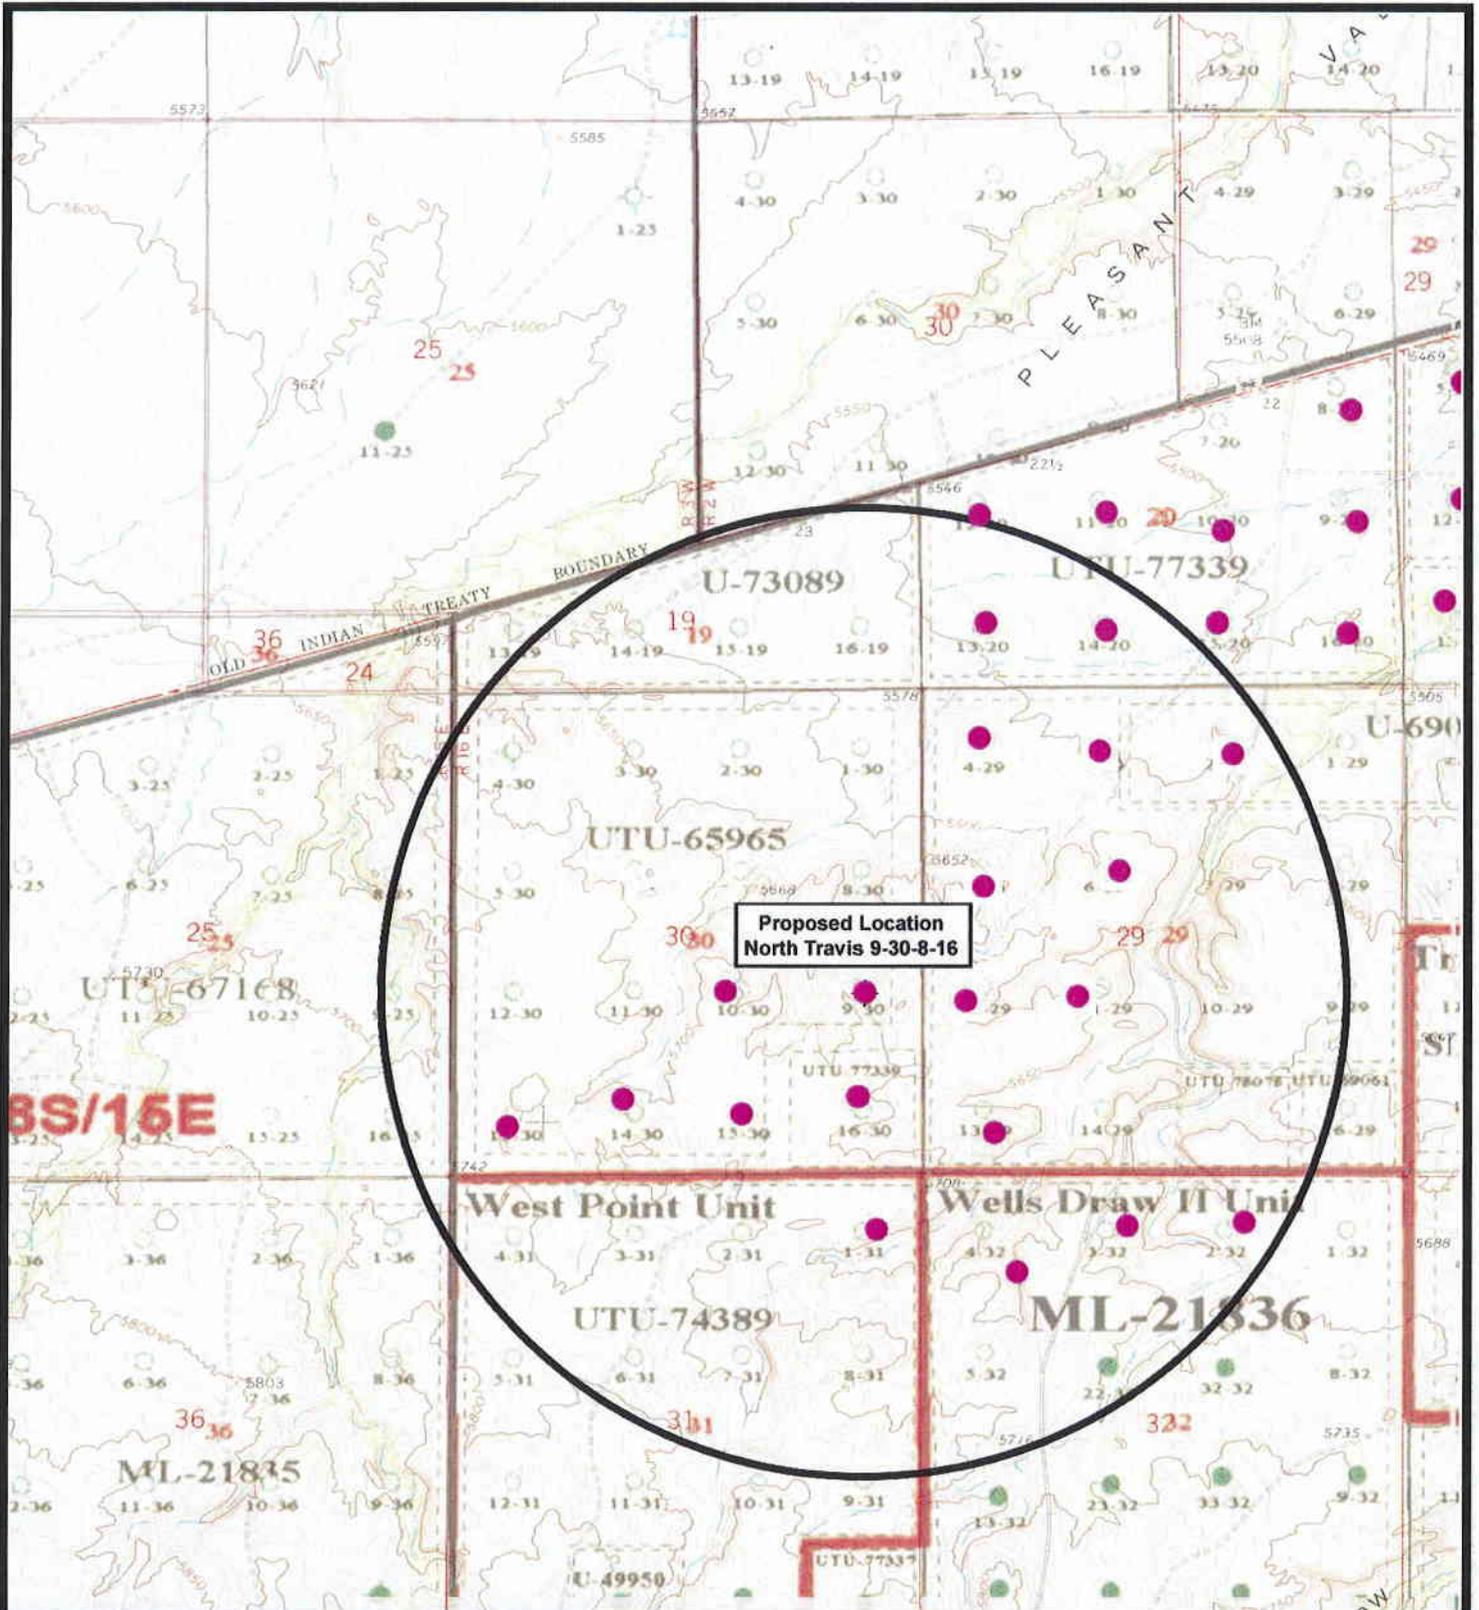

**North Travis 9-30-8-16  
SEC. 30, T8S, R16E, S.L.B.&M.**



**Tri-State  
Land Surveying Inc.**  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'  
DRAWN BY: mw  
DATE: 10-29-2008

**Legend**

- Location
- One-Mile Radius

**Exhibit "B"**

# 2-M SYSTEM

Blowout Prevention Equipment Systems

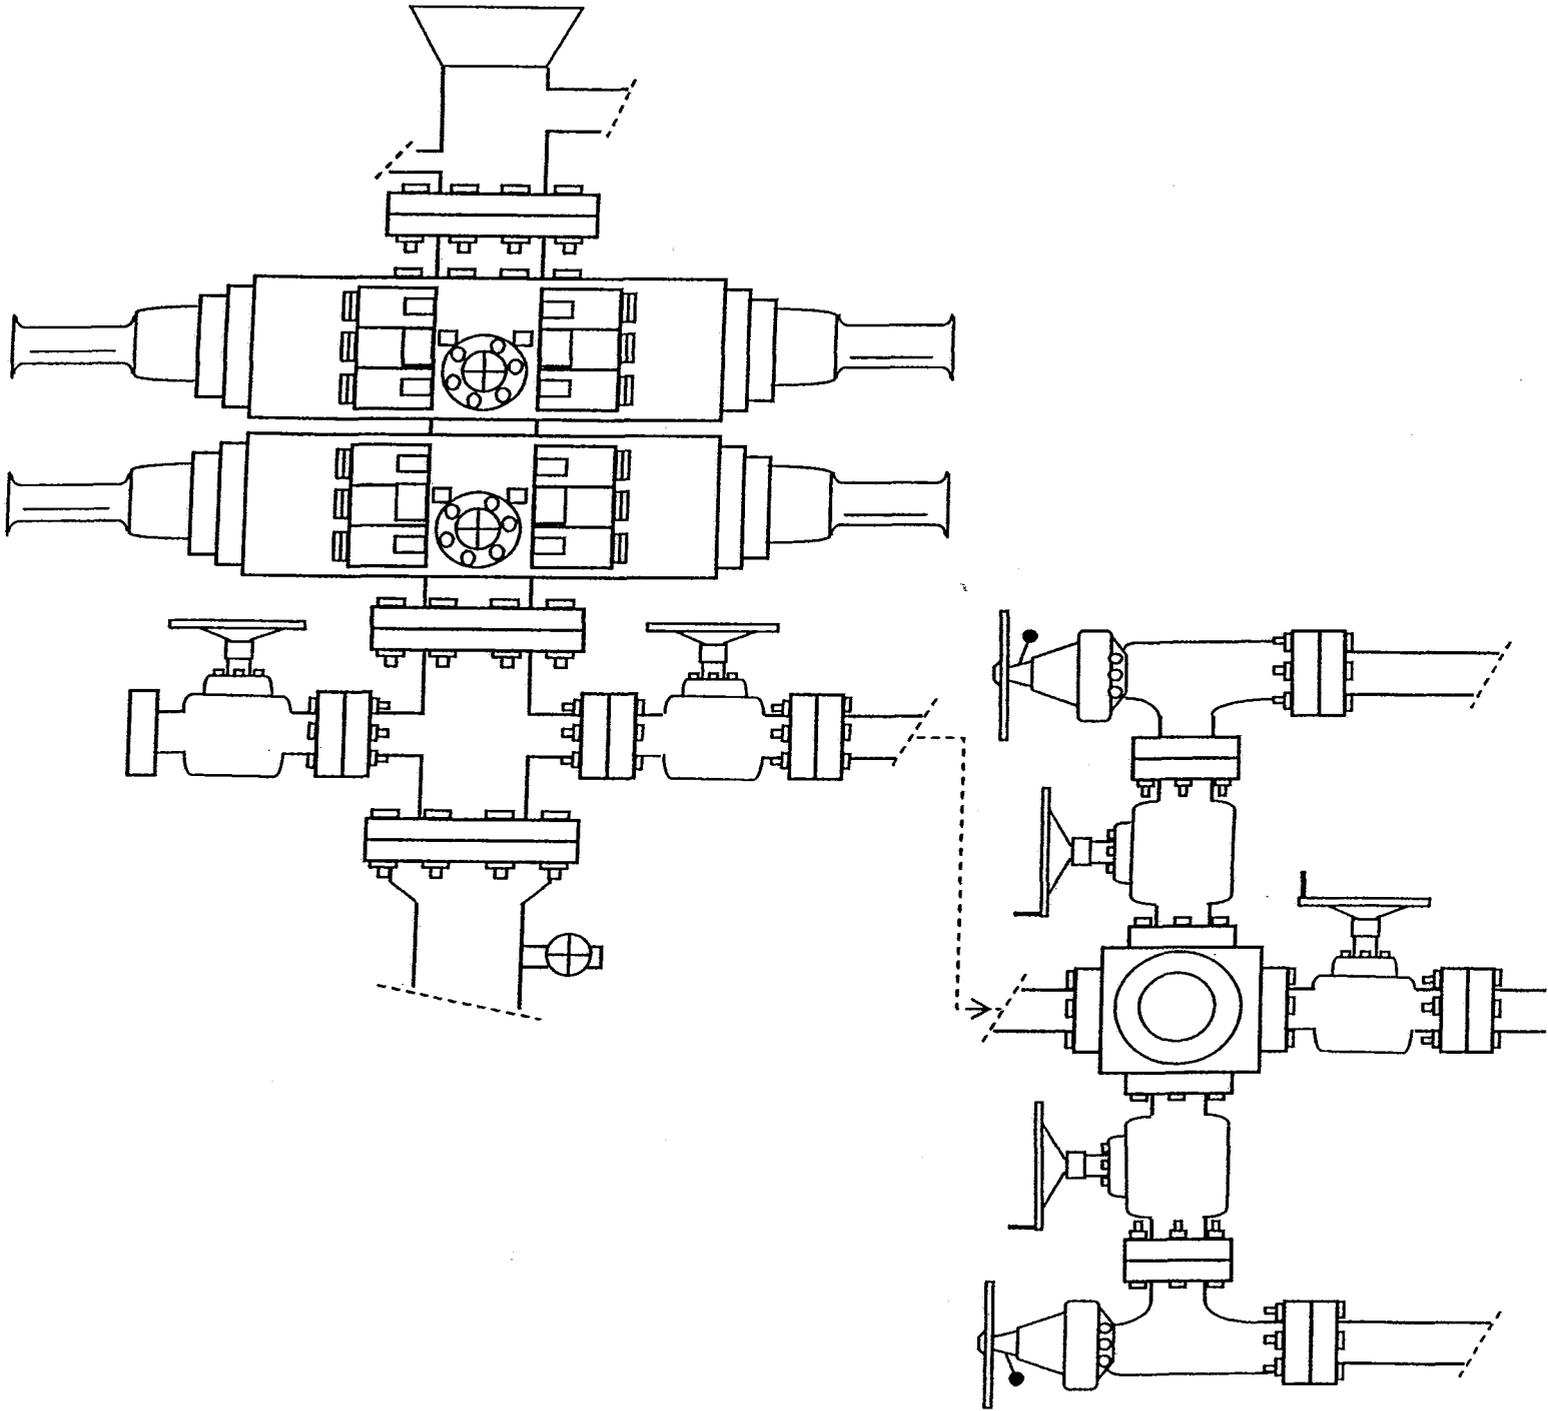


EXHIBIT C

**WORKSHEET  
APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 01/14/2009

API NO. ASSIGNED: 43-013-34185

WELL NAME: FEDERAL 9-30-8-16  
 OPERATOR: NEWFIELD PRODUCTION ( N2695 )  
 CONTACT: MANDIE CROZIER

PHONE NUMBER: 435-646-3721

PROPOSED LOCATION:  
 NESE 30 080S 160E  
 SURFACE: 1916 FSL 0611 FEL  
 BOTTOM: 1916 FSL 0611 FEL  
 COUNTY: DUCHESNE  
 LATITUDE: 40.08707 LONGITUDE: -110.1542  
 UTM SURF EASTINGS: 572112 NORTHINGS: 4437553  
 FIELD NAME: UNDESIGNATED ( 2 )

INSPECT LOCATN BY: / /		
Tech Review	Initials	Date
Engineering		
Geology		
Surface		

LEASE TYPE: 1 - Federal  
 LEASE NUMBER: UTU-81000  
 SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: GRRV  
 COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:

Plat

Bond: Fed[1] Ind[] Sta[] Fee[]  
 (No. WYB000493 )

nl Potash (Y/N)

nl Oil Shale 190-5 (B) or 190-3 or 190-13

Water Permit  
 (No. 43-7478 )

nl RDCC Review (Y/N)  
 (Date: \_\_\_\_\_ )

na Fee Surf Agreement (Y/N)

na Intent to Commingle (Y/N)

LOCATION AND SITING:

\_\_\_ R649-2-3.

Unit: \_\_\_\_\_

R649-3-2. General  
 Siting: 460 From Qtr/Qtr & 920' Between Wells

\_\_\_ R649-3-3. Exception

\_\_\_ Drilling Unit

Board Cause No: \_\_\_\_\_

Eff Date: \_\_\_\_\_

Siting: \_\_\_\_\_

\_\_\_ R649-3-11. Directional Drill

COMMENTS: Sup, Separate file

STIPULATIONS: 1- Federal Approval  
2- Spacing Strip

API Number: 4301334185

Well Name: FEDERAL 9-30-8-16


Township 08.0 S Range 16.0 E Section 30

Meridian: SLBM


Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:  
Map Produced by Diana Mason

Units	Wells Query Events
<b>STATUS</b>	✕ <all other values>
ACTIVE	GIS_STAT_TYPE
EXPLORATORY	<Null>
GAS STORAGE	APD
NF PP OIL	DRL
NF SECONDARY	GI
PI OIL	GS
PP GAS	LA
PP GEOTHERML	NEW
PP OIL	OPS
SECONDARY	PA
TERMINATED	PGW
<b>Fields</b>	POW
ACTIVE	RET
COMBINED	SGW
Sections	SOW
	TA
	TW
	WD
	WI
	WS



1:11,343

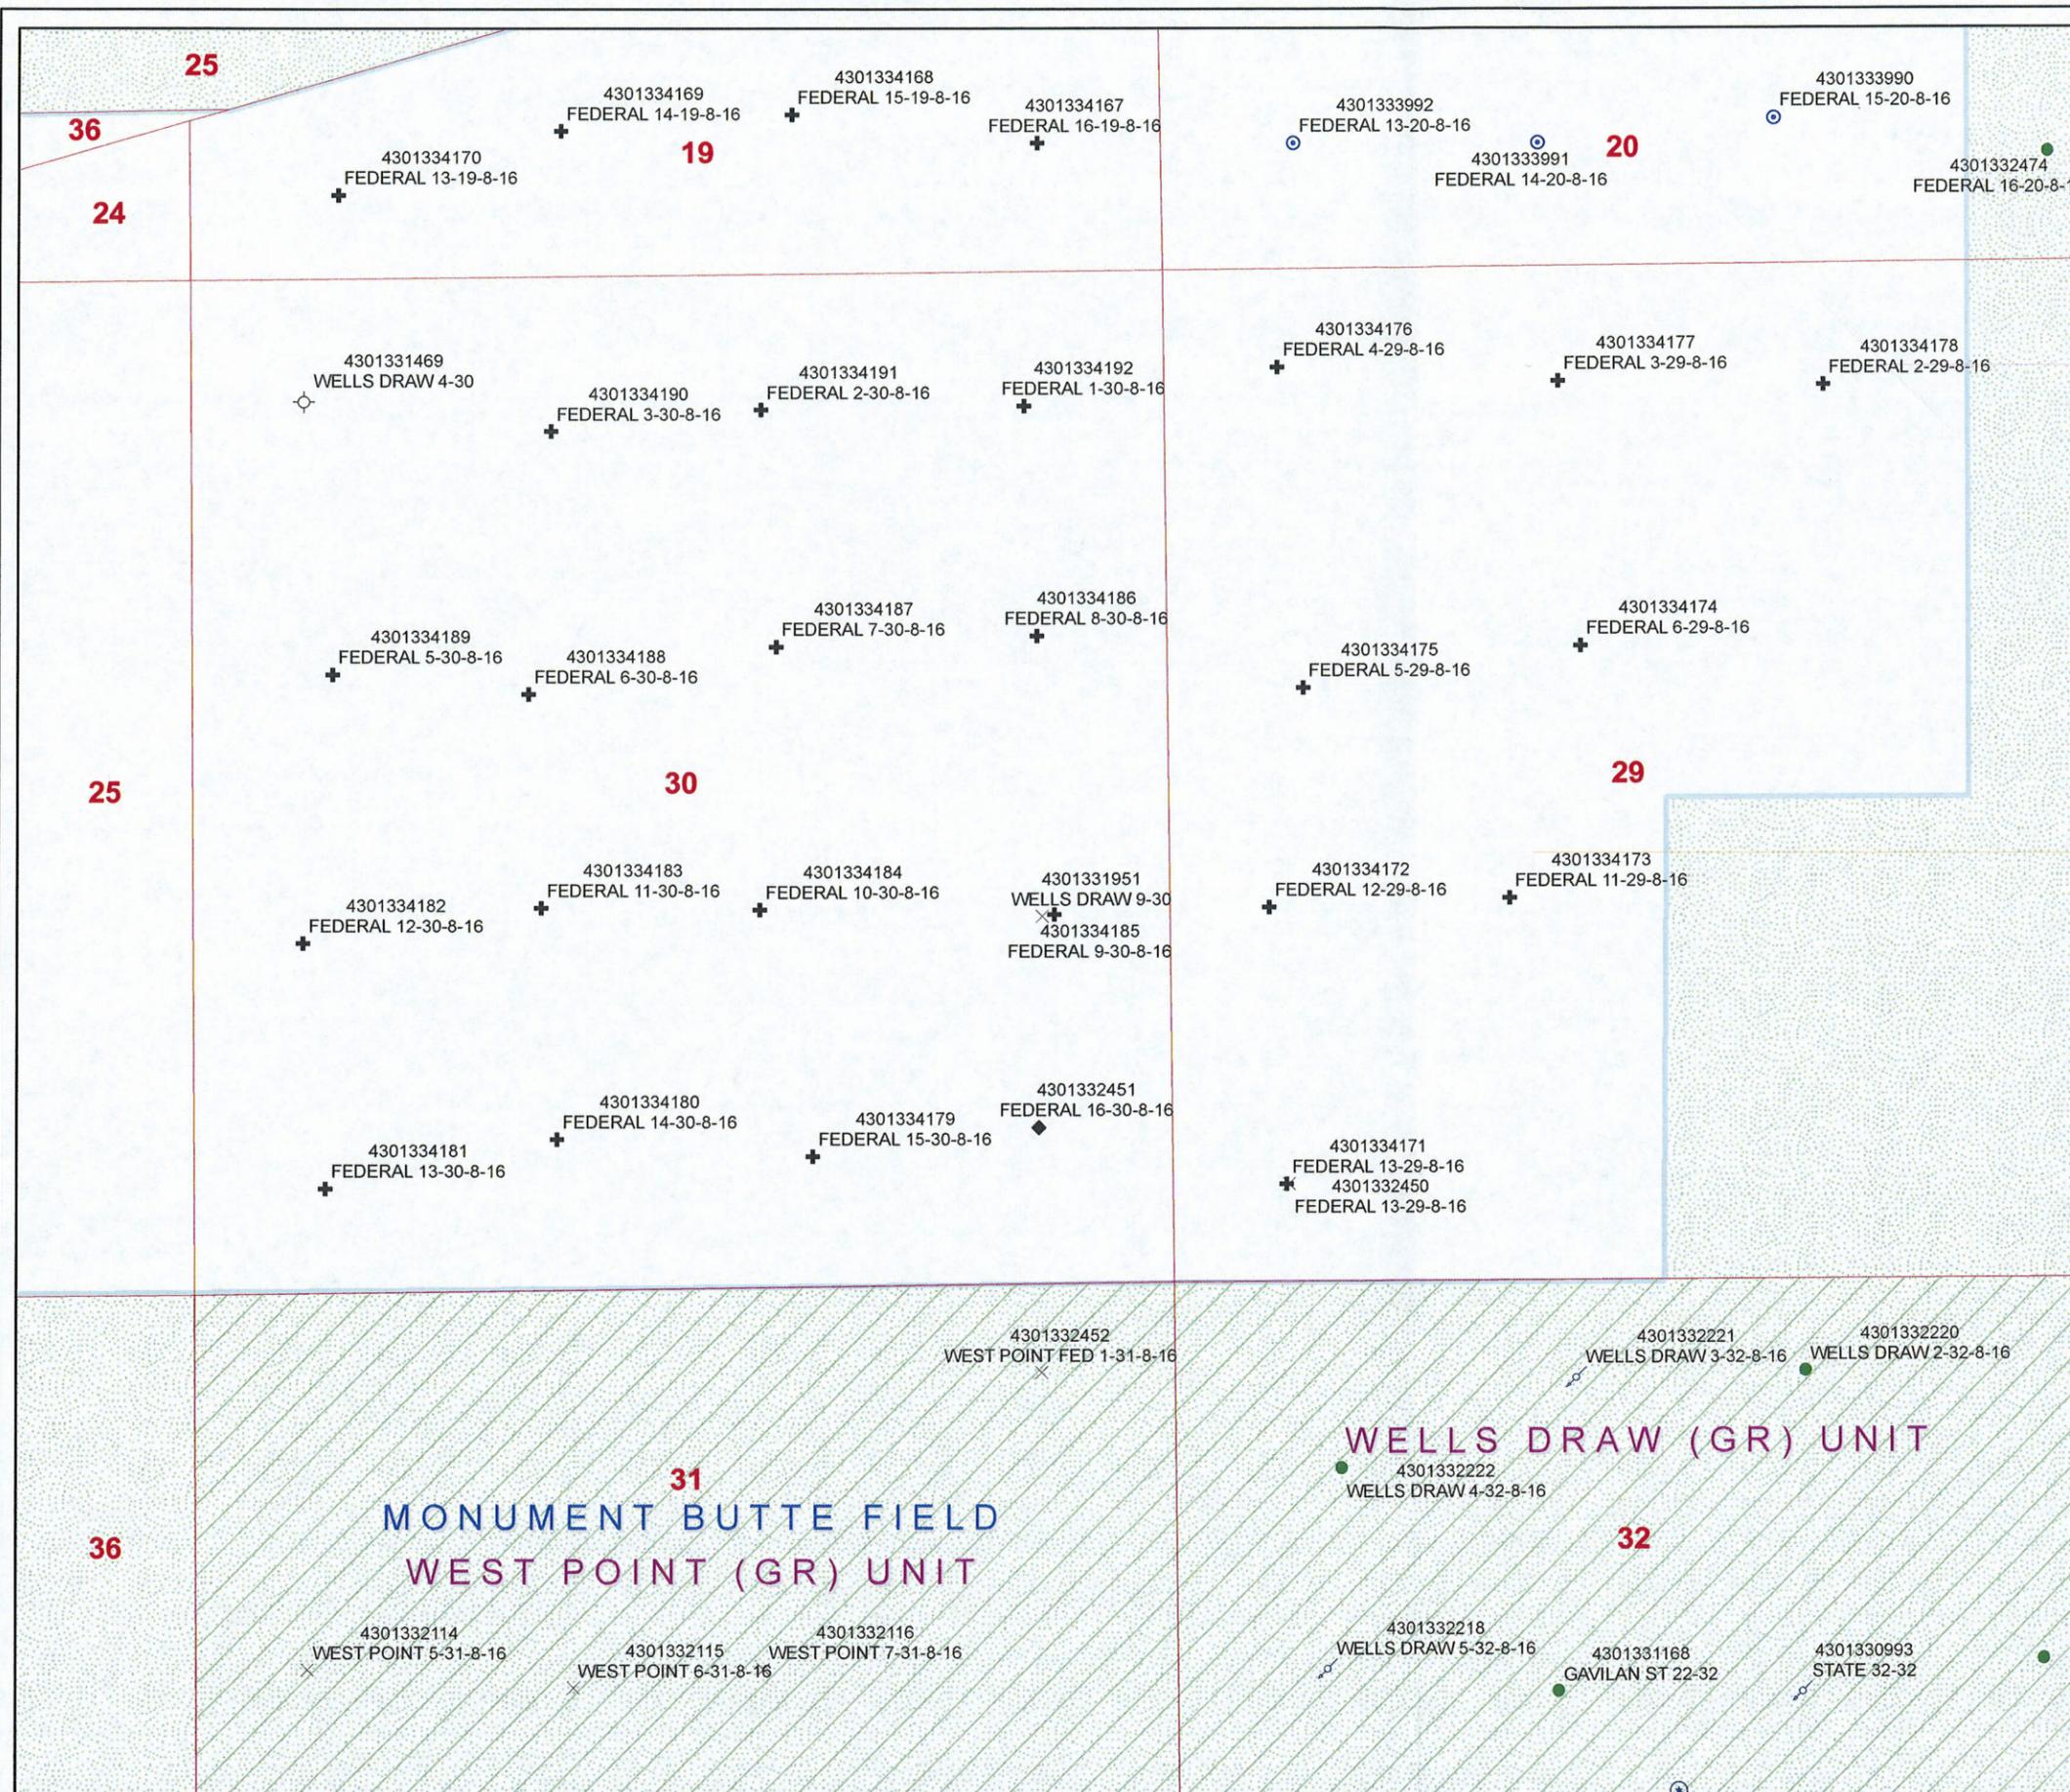



JON M. HUNTSMAN, JR.  
Governor

GARY R. HERBERT  
Lieutenant Governor

# State of Utah

## DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER  
Executive Director

### Division of Oil, Gas and Mining

JOHN R. BAZA  
Division Director

January 22, 2009

Newfield Production Company  
Rt. 3, Box 3630  
Myton, UT 84052

Re: Federal 9-30-8-16 Well, 1916' FSL, 611' FEL, NE SE, Sec. 30, T. 8 South, R. 16 East, Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-34185.

Sincerely,

Gil Hunt  
Associate Director

pab  
Enclosures

cc: Duchesne County Assessor  
Bureau of Land Management, Vernal Office



Operator: Newfield Production Company  
Well Name & Number Federal 9-30-8-16  
API Number: 43-013-34185  
Lease: UTU-81000

Location: NE SE                      Sec. 30                      T. 8 South                      R. 16 East

### Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

2. Notification Requirements

Notify the division within 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dustin Doucet at (801) 538-5281      (801) 733-0983 home

3. Reporting Requirements

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.

5. This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**APPLICATION FOR PERMIT TO DRILL OR REENTER**

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU-81000
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name NA
2. Name of Operator Newfield Production Company		7. If Unit or CA Agreement, Name and No. NA
3a. Address Route #3 Box 3630, Myton UT 84052		8. Lease Name and Well No. Federal 9-30-8-16
3b. Phone No. (include area code) (435) 646-3721		9. API Well No. 43 013 34185
4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NE/SE 1916' FSL 611' FEL At proposed prod. zone		10. Field and Pool, or Exploratory Monument Butte
14. Distance in miles and direction from nearest town or post office* Approximately 9.5 miles southwest of Myton, UT		11. Sec., T. R. M. or Blk. and Survey or Area Sec. 30, T8S R16E
15. Distance from proposed* location to nearest property or lease line, ft. Approx. 596' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)	16. No. of acres in lease 580.24	17. Spacing Unit dedicated to this well 40 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1555'	19. Proposed Depth 6,565'	20. BLM/BIA Bond No. on file. WYB000493
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5696' GL	22. Approximate date work will start* 2nd Qtr. 2009	23. Estimated duration (7) days from SPUD to rig release

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- |  |   |
|--|---|
| 1. Well plat certified by a registered surveyor.   | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan.  | 5. Operator certification   |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM.             |

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 12/29/08
Title Regulatory Specialist		

Approved by (Signature) <i>Stephanie J Howard</i>	Name (Printed/Typed) Stephanie J Howard	Date 12/16/09
Title Acting Assistant Field Manager Lands & Mineral Resources		
Office VERNAL FIELD OFFICE		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

**CONDITIONS OF APPROVAL ATTACHED**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

\*(Instructions on page 2)

NOTICE OF APPROVAL

RECEIVED

RECEIVED

JAN 13 2009

NOS 11-6-08

DEC 31 2009

BLM VERNAL, UTAH

AFMSS# 09SX50122A





**UNITED STATES DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
VERNAL FIELD OFFICE**

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



**CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL**

<b>Company:</b>	Newfield Production Company	<b>Location:</b>	NESE, Sec. 30, T8S, R16E
<b>Well No:</b>	Federal 9-30-8-16	<b>Lease No:</b>	UTU-81000
<b>API No:</b>	43-013-34185	<b>Agreement:</b>	Greater Monument Butte (GR) Unit

**OFFICE NUMBER: (435) 781-4400**

**OFFICE FAX NUMBER: (435) 781-3420**

**RECEIVED**

**DEC 31 2009**

**DIV. OF OIL, GAS & MINING**

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR  
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

**NOTIFICATION REQUIREMENTS**

Location Construction (Notify Environmental Scientist)	- Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	- Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: <a href="mailto:ut_vn_opreport@blm.gov">ut_vn_opreport@blm.gov</a> .
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

RECEIVED

DEC 31 2009

Page 2 of 8  
Well: Federal 9-30-8-16  
10/27/2009

DIV. OF OIL, GAS & MINING

**SURFACE USE PROGRAM  
CONDITIONS OF APPROVAL (COAs)**

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO<sub>x</sub> per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO<sub>x</sub> per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.
- Construction and drilling is not allowed from May 1 – June 15 to minimize impacts during mountain plover nesting.
- If it is anticipated that construction or drilling will occur during any of the given timing restrictions, a BLM or qualified biologist shall be notified so surveys can be conducted. Depending upon the results of the surveys, permission to proceed may or may not be granted by the BLM Authorized Officer.

**Reclamation:**

**Interim Reclamation:**

- Interim reclamation of the surface environment shall take place after drilling and completion and the well is placed into production. At a minimum, this will include the stabilization of the soil surface during construction, recontouring of the unused pad area, and the reserve pit to the original contour to the extent possible, and the re-spreading of the top soil after recontouring takes place, up to the rig anchor points and any area not needed for production. Buried pipelines will be recontoured, the salvaged topsoil redistributed and reseeded. The outside borrow of the access road will have the top soil salvaged and re-spread and reseeded. The area will be reseeded using appropriate seeding methods, which includes, but is not limited to, the drill seeding method (see below). Any adjustments, due to site specific production concerns, to the reclamation COAs in this document can be submitted on Sundry form 3160-5.
- The reclamation objective is to establish a desired self-perpetuating diverse plant community. The objective is to attain **75% basal cover** based on similar undisturbed adjacent native vegetative community, and comprised of desired species and/or seeded species within 5 years of initial reclamation action. However if after three (3) growing seasons there is less than **30%** of the basal cover based on similar undisturbed native vegetative community, then the Authorized Officer may require additional seeding efforts.
- Topsoil will be segregated from the subsoil (without mixing them), stockpiled separately from other soil materials, and maintained for future use in rehabilitating the locations.

- Topsoil piles stored beyond one growing season will be stabilized and seeded to prevent erosion.
- Topsoil storage areas will be identified with appropriate signage, so it is easily identifiable where topsoil is on location.
- Noxious and invasive weeds will be inventoried and monitored. Noxious and invasive weeds will be controlled through integrated weed management including chemical, mechanical, and biological control methods. An approved Pesticide Use Proposal (PUP) is required for all herbicide applications.
- All trash and waste materials not needed for production will be removed immediately.
- Earth work for interim and final reclamation must be completed within 6 months following well completion or well plugging (weather permitting).
- Salvaged topsoil will be re-distributed evenly, and to pre-disturbance depths, over the surfaces to be revegetated.
- The soil surface will be prepared to provide a seedbed for re-establishment of desirable vegetation. Site preparation may include gouging, scarifying, dozer track-walking, mulching, hydro mulching, contour furrowing, water terracing, fertilizing, disking, soil additives or other approved methods. The seedbed preparations will be determined to accomplish the reclamation objectives above.
- The seeding contractor will provide all seed tags to the appropriate SMA prior to seeding efforts.
- Seeding will occur after August 15 and prior to winter freezing of the soil.
- Drill seeding will be used except in areas where topography or substrate composition (rock) precludes the use of the drill. If drill seeding is not possible, broadcast seeding will be implemented. If the broadcast method is used (such as on slopes of 40 percent or greater), the seed rates established for drill seeding will be doubled and seed will be immediately covered to prevent seed desiccation or predation by birds or rodents. The seeds can be covered in several ways including spreading and crimping straw over the seeded area, raking the area by hand, or dragging a chain or chain-linked fence over the seeded area.
- Any altered drainages or water courses will be stabilized through rip rap, berming, seeding, matting, or other approved methods, and will be reconstructed to have the characteristics and features of nearby functional drainages. Any disturbance to "dashed line" drainages as depicted on USGS 1:24,000 topographic maps will be coordinated with the corps of engineers prior to disturbance.

**Final Reclamation:**

- Final Reclamation will be similar to interim reclamation except, all disturbance associated with the well location, access road and pipeline will be reclaimed. The seed mix may include more shrubs and native species. The visual composition will be reestablished to blend with the natural surroundings through recontouring and reseeding.
- After pipeline installation is complete, all disturbed areas will be reseeded. The seed mixtures to be used will be similar to the vegetation of the surrounding areas and may consist of grasses, forbs, or shrubs. A recommended seed mixture is provided in the table below.

**RECEIVED**

**DEC 31 2009**

**Monitoring:**

- The initial monitoring report will include but is not limited to: when the recontouring and seeding was completed. The seed applied, the amounts, and the depth of application. Seedbed preparation such as disking , mulching, etc. Seed application such as drilling or broadcast seeding. Are there any soil amendments, fertilizers, watering, etc. The amounts of noxious and invasive weeds. Are any fencing requirements needed.
- Prior to any surface disturbance, vegetative monitoring locations and reference sites will be identified by the operator and approved by the BLM Authorized Officer.
- Vegetation monitoring protocol will be developed by the operator and approved by the BLM Authorized Officer prior to implementation of revegetation techniques and will be designed to monitor % basal vegetative cover.
- Reclamation areas will be inspected annually and monitored to document location and extent of areas with successful revegetation. Monitoring will continue until the site is considered a success by the authorized officer and the objectives established in the Green River District Guidelines. A reclamation report will be submitted electronically to the Authorized Officer by March 31 of each year.
- On Federal lands, the reclamation objective will be a vegetation community that within 5 years is comprised of desired and/or seeded species, where the basal vegetative cover is 75 percent of a similar undisturbed adjacent native vegetation community. If after 3 years basal cover is less than 30 percent, then additional seeding and reclamation efforts may be required.

**Seed mix (Interim and Final Reclamation):**

Common name	Latin name	lbs/acre	Recommended seed planting depth
Squirreltail grass	<i>Elymus elymoides</i>	3.0	¼ - ½"
Siberian wheatgrass	<i>Agropyron fragile</i>	1.0	½"
Shadscale saltbush	<i>Atriplex confertifolia</i>	2.0	½"
Four-wing saltbush	<i>Atriplex canescens</i>	2.0	½"
Gardner's saltbush	<i>Atriplex gardneri</i>	2.0	½"
Scarlet globemallow	<i>Sphaeralcea coccinea</i>	1.0	⅛ - ¼"

- All pounds are pure live seed.
- All seed and mulch will be certified weed free.
- Rates are set for drill seeding; double rate if broadcasting.
- Reseeding may be required if initial seeding is not successful.

**RECEIVED**

**DEC 31 2009**

**DIV. OF OIL, GAS & MINING**

RECEIVED

DEC 31 2009

DIV. OF OIL, GAS & MINING

**DOWNHOLE PROGRAM  
CONDITIONS OF APPROVAL (COAs)**

Page 5 of 8  
Well: Federal 9-30-8-16  
10/27/2009

**SITE SPECIFIC DOWNHOLE COAs:**

- Newfield Production Co. shall adhere to all referenced requirements in the SOP (version: June 24, 2008) along with all Oil and Gas rules and requirements listed in the Code of Federal Regulations and all Federal Onshore Oil and Gas Orders.

**All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to.** The following items are emphasized:

**DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS**

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT\_VN\_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

RECEIVED

DEC 31 2009

DIV. OF OIL, GAS & MINING

RECEIVED

DEC 31 2009

Page 7 of 8  
Well: Federal 9-30-8-16  
10/27/2009

DIV. OF OIL, GAS & MINING

**OPERATING REQUIREMENT REMINDERS:**

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
  - Operator name, address, and telephone number.
  - Well name and number.
  - Well location ( $\frac{1}{4}$ , Sec., Twn, Rng, and P.M.).
  - Date well was placed in a producing status (date of first production for which royalty will be paid).
  - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
  - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
  - Unit agreement and/or participating area name and number, if applicable.
  - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4.

Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

**RECEIVED**  
**DEC 31 2009**  
DIV. OF OIL, GAS & MINING

<b>STATE OF UTAH</b> DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	<b>FORM 9</b>  <b>5. LEASE DESIGNATION AND SERIAL NUMBER:</b> UTU-81000
---	--

<b>SUNDRY NOTICES AND REPORTS ON WELLS</b>  Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	<b>6. IF INDIAN, ALLOTTEE OR TRIBE NAME:</b>  <b>7. UNIT or CA AGREEMENT NAME:</b> GMBU (GRRV)
--	---

<b>1. TYPE OF WELL</b> Oil Well	<b>8. WELL NAME and NUMBER:</b> FEDERAL 9-30-8-16
------------------------------------	--

<b>2. NAME OF OPERATOR:</b> NEWFIELD PRODUCTION COMPANY	<b>9. API NUMBER:</b> 43013341850000
--	---

<b>3. ADDRESS OF OPERATOR:</b> Rt 3 Box 3630 , Myton, UT, 84052	<b>PHONE NUMBER:</b> 435 646-4825 Ext	<b>9. FIELD and POOL or WILDCAT:</b> UNDESIGNATED
--	--	--

<b>4. LOCATION OF WELL</b> <b>FOOTAGES AT SURFACE:</b> 1916 FSL 0611 FEL <b>QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN:</b> Qtr/Qtr: NESE Section: 30 Township: 08.0S Range: 16.0E Meridian: S	<b>COUNTY:</b> DUCHESNE  <b>STATE:</b> UTAH
---	---

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> <b>NOTICE OF INTENT</b> Approximate date work will start: 1/22/2010  <input type="checkbox"/> <b>SUBSEQUENT REPORT</b> Date of Work Completion:  <input type="checkbox"/> <b>SPUD REPORT</b> Date of Spud:  <input type="checkbox"/> <b>DRILLING REPORT</b> Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input checked="" type="checkbox"/> APD EXTENSION OTHER:

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Newfield requests to extend the permit to drill this well for one year.

**Approved by the Utah Division of Oil, Gas and Mining**

**Date:** January 28, 2010

**By:**

<b>NAME (PLEASE PRINT)</b> Mandie Crozier	<b>PHONE NUMBER</b> 435 646-4825	<b>TITLE</b> Regulatory Tech
<b>SIGNATURE</b> N/A	<b>DATE</b> 1/26/2010	



**The Utah Division of Oil, Gas, and Mining**

- State of Utah
- Department of Natural Resources

**Electronic Permitting System - Sundry Notices**

**Request for Permit Extension Validation Well Number 43013341850000**

**API:** 43013341850000

**Well Name:** FEDERAL 9-30-8-16

**Location:** 1916 FSL 0611 FEL QTR NESE SEC 30 TWNP 080S RNG 160E MER S

**Company Permit Issued to:** NEWFIELD PRODUCTION COMPANY

**Date Original Permit Issued:** 1/22/2009

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision. Following is a checklist of some items related to the application, which should be verified.

- If located on private land, has the ownership changed, if so, has the surface agreement been updated?  Yes  No
- Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location?  Yes  No
- Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well?  Yes  No
- Have there been any changes to the access route including ownership, or rightof- way, which could affect the proposed location?  Yes  No
- Has the approved source of water for drilling changed?  Yes  No
- Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation?  Yes  No
- Is bonding still in place, which covers this proposed well?  Yes  No

**Approved by the  
Utah Division of  
Oil, Gas and Mining**

**Signature:** Mandie Crozier

**Date:** 1/26/2010

**Title:** Regulatory Tech **Representing:** NEWFIELD PRODUCTION COMPANY

**Date:** January 28, 2010

**By:** 

Spud

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross # 29 Submitted  
By Jim Smith Phone Number 823-  
2072

Well Name/Number Federal 9-30-8-16  
Qtr/Qtr NE/SE Section 30 Township 8S Range 16E  
Lease Serial Number UTU-81000  
API Number 43-013-34185

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 9/13/10 8:00 AM  PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 09/13/10 2:00 AM  PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time \_\_\_\_\_ AM  PM

Remarks \_\_\_\_\_

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

FORM APPROVED  
OMB No. 1004-0137  
Expires: July 31, 2010

**SUNDRY NOTICES AND REPORTS ON WELLS**  
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

**SUBMIT IN TRIPLICATE - Other Instructions on page 2**

1. Type of Well  
 Oil Well    Gas Well    Other

2. Name of Operator  
 NEWFIELD PRODUCTION COMPANY

3a. Address    Route 3 Box 3630  
                   Myton, UT 84052

3b. Phone    (include are code)  
                   435.646.3721

4. Location of Well    (Footage, Sec., T., R., M., or Survey Description)  
 1914 FSL 0611 FEL  
 NESE Section 30 T8S R16E

5. Lease Serial No.  
 USA UTU-81000

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or  
 GMBU

8. Well Name and No.  
 FEDERAL 9-30-8-16

9. API Well No.  
 4301334185

10. Field and Pool, or Exploratory Area  
 GREATER MB UNIT

11. County or Parish, State  
 DUCHESNE, UT

**12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation; (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleation in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 9/13/10 MIRU Ross # 29. Spud well @ 8:00 AM. Drill 355' of 12 1/4" hole with air mist. TIH W/ 8 Jt's 8 5/8" J-55 24# casing. Set @ 355.34' KB. On 9/19/10 cement with 170 sks of class "G" w/ 2% CaCL2 + 1/4# per sk Cello Flake mixed @ 15.8 ppg with 1.17 cf/sk yield. Returned 2 bbls cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed) Mitch Benson	Title Drilling Foreman
Signature 	Date 09/19/2010

**THIS SPACE FOR FEDERAL OR STATE OFFICE USE**

Approved by _____	Title _____	Date _____
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office _____	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on page 2)

**RECEIVED**

SEP 22 2010

DIV. OF OIL, GAS & MINING





STATE OF UTAH  
 DIVISION OF OIL, GAS AND MINING  
 ENTITY ACTION FORM -FORM 6

OPERATOR: NEWFIELD PRODUCTION COMPANY  
 ADDRESS: RT. 3 BOX 3630  
MYTON, UT 84052

OPERATOR ACCT. NO. N2695

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4301334175	FEDERAL 5-29-8-16	SWNW	29	8S	16E	DUCHESNE	9/14/2010	10/11/10
WELL 1 COMMENTS: GRRV											
B	99999	17400	4301334185	FEDERAL 9-30-8-16	NESE	30	8S	16E	DUCHESNE	9/13/2010	10/11/10
GRRV											
B	99999	17400	4301350046	FEDERAL 7-25-8-15	SWNE	25	8S	15E	DUCHESNE	9/14/2010	10/11/10
GRRV											
B	99999	17400	4301350050	FEDERAL 14-25-8-15	SESW	25	8S	15E	DUCHESNE	9/9/2010	10/11/10
GRRV											
A	99999	17794	4301350340	UTE TRIBAL 9-22-4-3	NESE	22	4S	3W	DUCHESNE	9/13/2010	10/11/10
WELL 5 COMMENTS: GRRV											
A	99999	17795	4301350345	UTE TRIBAL 8-23-4-3	SENE	23	4S	3W	DUCHESNE	9/15/2010	10/11/10
WELL 5 COMMENTS: GRRV											

- ACTION CODES (See instructions on back of form)
- A - new entity for new well (single well only)
  - B - well to existing entity (group or unit well)
  - C - from one existing entity to another existing entity
  - D - well from one existing entity to a new entity
  - E - other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.

RECEIVED  
 SEP 23 2010

DIV. OF OIL, GAS & MINING

Signature: Jentri Park  
 Production Clerk  
 Date: 09/22/10

**STATE OF UTAH**  
DEPARTMENT OF NATURAL RESOURCES  
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:  
USA UTU-81000

**SUNDRY NOTICES AND REPORTS ON WELLS**

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:  
GMBU

1. TYPE OF WELL: OIL WELL  GAS WELL  OTHER

8. WELL NAME and NUMBER:  
FEDERAL 9-30-8-16

2. NAME OF OPERATOR:  
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:  
4301334185

3. ADDRESS OF OPERATOR:  
Route 3 Box 3630 CITY Myton STATE UT ZIP 84052

PHONE NUMBER  
435.646.3721

10. FIELD AND POOL, OR WILDCAT:  
GREATER MB UNIT

4. LOCATION OF WELL:

FOOTAGES AT SURFACE:

COUNTY: DUCHESNE

OTR/OTR. SECTION, TOWNSHIP, RANGE, MERIDIAN: NESE, 30, T8S, R16E

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate)  Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only)  Date of Work Completion: 10/13/2010	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was completed on 10/13/2010, attached is a daily completion status report.

NAME (PLEASE PRINT) Lucy Chavez-Naupoto

TITLE Administrative Assistant

SIGNATURE



DATE 10/14/2010

(This space for State use only)

**RECEIVED**

**OCT 25 2010**

**DIV. OF OIL, GAS & MINING**

## Daily Activity Report

Format For Sundry

**FEDERAL 9-30-8-16**

**8/1/2010 To 12/30/2010**

**10/4/2010 Day: 1**

**Completion**

Rigless on 10/4/2010 - Ran CBL & shot 1st stage - Install 5m frac head. NU 6" 5K Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head, csg & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 6632' & cement top @ 240'. Perforate stage #1, LODC sds @ 5732-35', 5724-26', 5704-06', 5695-97', 5685-87', 5674-76', 5664-66' & 5642-44" w/ 3 1/8" Port plug guns ( 11 gram .36" EH 16.82" pen) w/ 3 spf for total of 51 shots. 158 BWTR. SWIFN.

**Daily Cost:** \$0

**Cumulative Cost:** \$16,187

**10/6/2010 Day: 2**

**Completion**

Stone #8 on 10/6/2010 - Perforate, frac & flowback well. - Perforate & frac well as detailed. 3264 BWTR. Open for immediate flowback @ approx 3 BPM. Well flowed for 3 1/2 hours & died. Recovered 500 bbls. MIRUSU. 2764 BWTR.

**Daily Cost:** \$0

**Cumulative Cost:** \$147,553

**10/8/2010 Day: 3**

**Completion**

Stone #8 on 10/8/2010 - MIRUSU. PU tbg & drill first 3 plugs. - Check pressure on well, 50 psi. Bleed pressure off well. Unload tbg. ND frac BOPs & wellhead. NU production wellhead & BOPs. Talley & PU 4 3/4" chomp bit, bit sub & 2 7/8" J-55 8rd EUE tbg. Tag fill @ 4519'. RU power swivel. Clean out to plug @ 4600'. Drill out plug in 30 min. Continue PU tbg & tag fill @ 4659'. Clean out to PBTD @ 4850'. Drill out plug in 65 min. Continue PU tbg & tag plug @ 5150'. Drill out plug in 30 min. Continue PU tbg & tag plug @ 5500'. Circulate well clean. POOH w/ 2- jts, EOT @ 5450'. SWIFN. 2764 BWTR.

**Daily Cost:** \$0

**Cumulative Cost:** \$154,608

**10/11/2010 Day: 4**

**Completion**

Stone #8 on 10/11/2010 - Clean out to PBTD, swab & flow well. - Check pressure on well, 300 psi csg & 250 psi tbg. Transfer oil to production tanks. Bleed pressure off well. Pump 30 bbls down tbg. RD Power swivel. PU tbg & tag fill @ 6072'. Clean out to PBTD @ 6660'. Circulate well clean. Well was still making a lot of sand. LD 3- jts tbg. RU swab equipment. Made 4 swab runs & well started flowing. Recovered 245 bbls with approx 10% oil cut, show of gas & sand. 2519 BWTR.

**Daily Cost:** \$0

**Cumulative Cost:** \$160,812

**10/12/2010 Day: 5**

**Completion**

Stone #8 on 10/12/2010 - Clean out to PBTD, flow well & round trip tbg. - Check pressure on well, 650 psi csg & 550 psi tbg. Bleed pressure off well. Well was flowing oil. Pump 25 BW

down tbg. TIH & tag fill @ 6627'. Csg was flowing, let flow to production tanks while waiting on brine water. Clean out to PBTD @ 6660'. Circulate well clean w/ 10# brine water. LD 27-jts tbg not needed for production. TOOH w/ tbg & LD BHA. TIH w/ production tbg as detailed. Set TA @ 5755' w/ 18,000#s tension. RD rig floor. ND BOPs. NU wellhead. X-over for rods. SWIFN. Recovered 250 bbls oil. 2269 BWTR.

**Daily Cost:** \$0

**Cumulative Cost:** \$166,375

---

**10/13/2010 Day: 6**

**Completion**

Stone #8 on 10/13/2010 - PU rods & PWOP - Flush tbg w/ 60 BW. PU & prime Central Hydraulic 2 1/2" X 1 1/2" X 24' RHAC rod pump. PU rods as detailed. RU pumping unit. Stoke test pump w/ unit to 800 psi. RDMOSU. Could not PWOP due to no gas lines to treater. PWOP @ 8:00 am 10/13/2010 w/ 122" SL & 5 SPM. 2269 BWTR. **Finalized**

**Daily Cost:** \$0

**Cumulative Cost:** \$231,764

---

**Pertinent Files: Go to File List**

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

FORM APPROVED  
OMB NO. 1004-0137  
Expires: July 31, 2010

**WELL COMPLETION OR RECOMPLETION REPORT AND LOG**

5. Lease Serial No.  
UTU-81000

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.  
GMBU

8. Lease Name and Well No.  
FEDERAL 9-30-8-16

9. AFI Well No.  
43-013-34185

10. Field and Pool or Exploratory  
GREATER MB UNIT

11. Sec., T., R., M., on Block and Survey or Area  
SEC. 30, T8S, R16E

12. County or Parish  
DUCHESNE

13. State  
UT

14. Date Spudded  
09/13/2010

15. Date T.D. Reached  
09/27/2010

16. Date Completed  
10/12/2010  
 D & A  Ready to Prod.

17. Elevations (DF, RKB, RT, GL)\*  
5699' GL 5711' KB

18. Total Depth: MD 6725'  
TVD

19. Plug Back T.D.: MD 6660'  
TVD

20. Depth Bridge Plug Set: MD  
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)  
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored?  No  Yes (Submit analysis)  
Was DST run?  No  Yes (Submit report)  
Directional Survey?  No  Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	355'		170 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	6705'		300 PRIMLITE		240'	
						450 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 5851'	TA @ 5753'						

25. Producing Intervals

Formation	Top	Bottom	Perforation Record	Size	No. Holes	Perf. Status
A) Green River			5642-5735' LODC	.36"	3	51
B) Green River			5414-5425' A1	.36"	3	15
C) Green River			5058-5073' D2	.36"	3	30
D) Green River			4738-4779' PB10 PB11	.36"	3	24

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
5642-5735'	Frac w/ 199624#s 20/40 sand in 1245 bbls of Lightning 17 fluid.
5414-5425'	Frac w/ 34702#s 20/40 sand in 228 bbls of Lightning 17 fluid.
5058-5073'	Frac w/ 55133#s 20/40 sand in 349 bbls of Lightning 17 fluid.
4738-4779'	Frac w/ 23523#s 20/40 sand in 214 bbls of Lightning 17 fluid.

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
10-13-10	10-26-10	24	→	113	60	30			2-1/2" x 1-1/2" x 20' x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

**RECEIVED**  
NOV 08 2010

DIV. OF OIL, GAS & MINING

\*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production ➔	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate ➔	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production ➔	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate ➔	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD & USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
GREEN RIVER	4430'	5735'		GARDEN GULCH MRK	3942'
				GARDEN GULCH 1	4166'
				GARDEN GULCH 2	4281'
				POINT 3	4554'
				X MRKR	4815'
				Y MRKR	4852'
				DOUGALS CREEK MRK	4968'
				BI CARBONATE MRK	5215'
				B LIMESTON MRK	5335'
				CASTLE PEAK	5888'
				BASAL CARBONATE	6320'
				WASATCH	6447'

32. Additional remarks (include plugging procedure):

Stage 5: Green River Formation (GB2 & GB6) 4430-4521', .36" 3/00 Frac w/ 33056#s of 20/40 sand in 223 bbls of Lightning 17 fluid


33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)     
  Geologic Report     
  DST Report     
  Directional Survey  
 Sundry Notice for plugging and cement verification     
  Core Analysis     
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)\*

Name (please print) Lucy Chavez-Naupoto

Title Administrative Assistant

Signature 

Date 11/02/2010

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 3)

RECEIVED

NOV 08 2010

DIV. OF OIL, GAS & MINING

**Daily Activity Report**

Format For Sundry

**FEDERAL 9-30-8-16****7/1/2010 To 11/30/2010****FEDERAL 9-30-8-16****Waiting on Cement****Date:** 9/19/2010

Ross #29 at 355. Days Since Spud - On 9/13/10 Ross Rig #29 spud Federal 9-30-8-16, drilled 355' of 12 1/4" hole, and ran 8 jts 8 5/8" - Returned 2 bbls to pit. - 8 5/8" casing w/ 170 sks Class "G" + 2% CaCl<sub>2</sub> + 0.25#/sk Cello Flake at 15.8 ppg w/ 1.17 yield. - casing (guide shoe, shoe jt, baffle plate, 7 jts) set @ 355.34' KB. On 9/19/10 BJ Services cemented

**Daily Cost:** \$0**Cumulative Cost:** \$48,070**FEDERAL 9-30-8-16****Drill 7 7/8" hole with fresh water****Date:** 9/24/2010

Capstar #328 at 2067. 1 Days Since Spud - or valve Pipe rams inside choke valves & Blind rams & Outside choke valves to 2000#s f/ 10 min - & Casing to 1500#s f/ 30 min - PU MI 616 Smith PDC & Hunting 4.8 stg 7/8 mil .33 MM NMDC, Gap sub, Index sub, 24 4.5" HWDP & Tag @ - 284' - Drill F/ 284' to 2067' WOB= 10/20 RPMS= 184 GPM= 409 ROP= 178' pr hr - Accept rig @ 4:00 PM on 9/23/10 & Held safety mtg w/ B&C Quick test Tested top drive upper kelly flo - Nipple up bops - Rig up - Move rig w/ Howcroft Trucking 1/4 of a mile to the Federal 9-30-8-16 on 9/23/10 - Do safety Insp & Strap BHA & Hook up flair lines

**Daily Cost:** \$0**Cumulative Cost:** \$117,286**FEDERAL 9-30-8-16****Drill 7 7/8" hole with salt water****Date:** 9/25/2010

Capstar #328 at 4468. 2 Days Since Spud - Circ gas out & disp hole w/ brine wtr - Drill F/2429' to 2793' WOB= 10/20 RPMS= 184 GPM= 409 ROP= 121' pr hr - Rig serv - Drill F/2793' to 4468' WOB= 10/20 RPMS= 184 GPM= 409 ROP= 115' pr hr - Drill F/2067' to 2429' WOB= 10/20 RPMS= 184 GPM= 409 ROP= 362' pr hr

**Daily Cost:** \$0**Cumulative Cost:** \$133,061**FEDERAL 9-30-8-16****Drill 7 7/8" hole with salt water****Date:** 9/26/2010

Capstar #328 at 5737. 3 Days Since Spud - Drill F/4468' to 4916' WOB= 10/20 RPMS= 184 GPM= 409 ROP= 92' pr hr - Circ & Pump pill for bit trip - TIH - Drill F/4916' to 5736' WOB= 10/20 RPMS= 184 GPM= 409 ROP= 80' pr hr - TOOH for bit

**Daily Cost:** \$0**Cumulative Cost:** \$152,606**RECEIVED****NOV 08 2010****FEDERAL 9-30-8-16****DIV. OF OIL, GAS & MINING  
Running casing****Date:** 9/27/2010

Capstar #328 at 6725. 4 Days Since Spud - Transf 4 jts to the Ute Tribe 10-22-4-2W 168.03' - Test 5.5" casing rams & RU & Run 159 jts 5.5" J55 15.5# LTC shoe @ 6705.31' Float Coller @ 6660.34' - ted Neutron Gamma Ray Loggers TD 6720' - Held safety mtg w/ Phoenix Survey Inc & Log W/ Duel Guard Log Gamma Ray Compensated Density Compensa - Drill F/5736' to 6551' WOB= 20/25 RPMS= 184 GPM= 409 ROP= 90' pr hr - Circ & Pump pill for LDDP & BHA - Drill F/6551' to 6725' WOB= 20/25 RPMS= 184 GPM= 409 ROP= 87' pr hr - Rig serv - LDDP

&amp; BHA

**Daily Cost:** \$0**Cumulative Cost:** \$278,867

---

**FEDERAL 9-30-8-16****Rigging down****Date:** 9/28/2010

Capstar #328 at 6725. 5 Days Since Spud - Release rig @ 8:30 PM on 9/27/10 - Clean Mud pits - Nipple Down & set 5.5 casing slips w/ 110,000#s - Displ w/ 158 bbls & returned 28 bbls to pit - .5SMS+FP+SF & 450 sks mixed w/14.4 ppg 1.24 yeild 50:50:2+3%KCL+0.5%EC-1+.25#CF+.05#SF+.3SMS+FP-6L - Held Saftey mtg & RU BJ & cementw/300 sks mixed W/11 ppg 3.53 yeild PLII+3%KCL+5#CSE+0.5#CF+2#KOL+ - Circ f/ Cement Job - Transf 4 jts to the Ute Tribe 10-22-4-2W 168.03' Hit a Bridge & Wash f/5451' to 5500' - Test 5.5" casing rams & RU & Run 159 jts 5.5" J55 15.5# LTC shoe @ 6705.31' Float Coller @ 6660.34'

**Finalized****Daily Cost:** \$0**Cumulative Cost:** \$343,804

---

**Pertinent Files: Go to File List**

RECEIVED

NOV 08 2010

DIV. OF OIL, GAS &amp; MINING
