

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No.
UTU-67168

6. If Indian, Allottee or Tribe Name
NA

7. If Unit or CA Agreement, Name and No.
NA

8. Lease Name and Well No.
Federal 10-26-8-15

1a. Type of work: DRILL REENTER

1b. Type of Well: Oil Well Gas Well Other Single Zone Multiple Zone

2. Name of Operator Newfield Production Company

9. API Well No.
43013-34216

3a. Address Route #3 Box 3630, Myton UT 84052

3b. Phone No. (include area code)
(435) 646-3721

10. Field and Pool, or Exploratory
~~Monument Butte~~ Undesignated

4. Location of Well (Report location clearly and in accordance with any State requirements.)* 40.08715
At surface NW/SE (LOT #3) 1958' FSL 1443' FEL 568681X
At proposed prod. zone 4437531Y -110.19439

11. Sec., T. R. M. or Blk. and Survey or Area
Sec. 26, T8S R15E

14. Distance in miles and direction from nearest town or post office*
Approximately 11.5 miles southwest of Myton, UT

12. County or Parish Duchesne

13. State UT

15. Distance from proposed* location to nearest property or lease line, ft. Approx. 533' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)

16. No. of acres in lease 1,285.960

17. Spacing Unit dedicated to this well 40 Acres

18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1035'

19. Proposed Depth 6,385'

20. BLM/BIA Bond No. on file WYB000493

21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5791' GL

22. Approximate date work will start* 3rd Qtr. 2009

23. Estimated duration (7) days from SPUD to rig release

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- 1. Well plat certified by a registered surveyor.
- 2. A Drilling Plan.
- 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- 5. Operator certification
- 6. Such other site specific information and/or plans as may be required by the BLM.

25. Signature *Mandie Crozier* Name (Printed/Typed) Mandie Crozier Date 2/20/09

Title Regulatory Specialist

Approved by Signature *Bradley G. Hill* Name (Printed/Typed) BRADLEY G. HILL Date 03-02-09

Title Office ENVIRONMENTAL MANAGER

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)




**Federal Approval of this
Action is Necessary**

RECEIVED
FEB 26 2009
DIV. OF OIL, GAS & MINING

T8S, R15E, S.L.B.&M.


NEWFIELD PRODUCTION COMPANY

WELL LOCATION, FEDERAL 10-26-8-15,
 LOCATED AS SHOWN IN THE NW 1/4 SE
 1/4 (LOT 3) OF SECTION 26, T8S, R15E,
 S.L.B.&M. DUCHESNE COUNTY, UTAH.

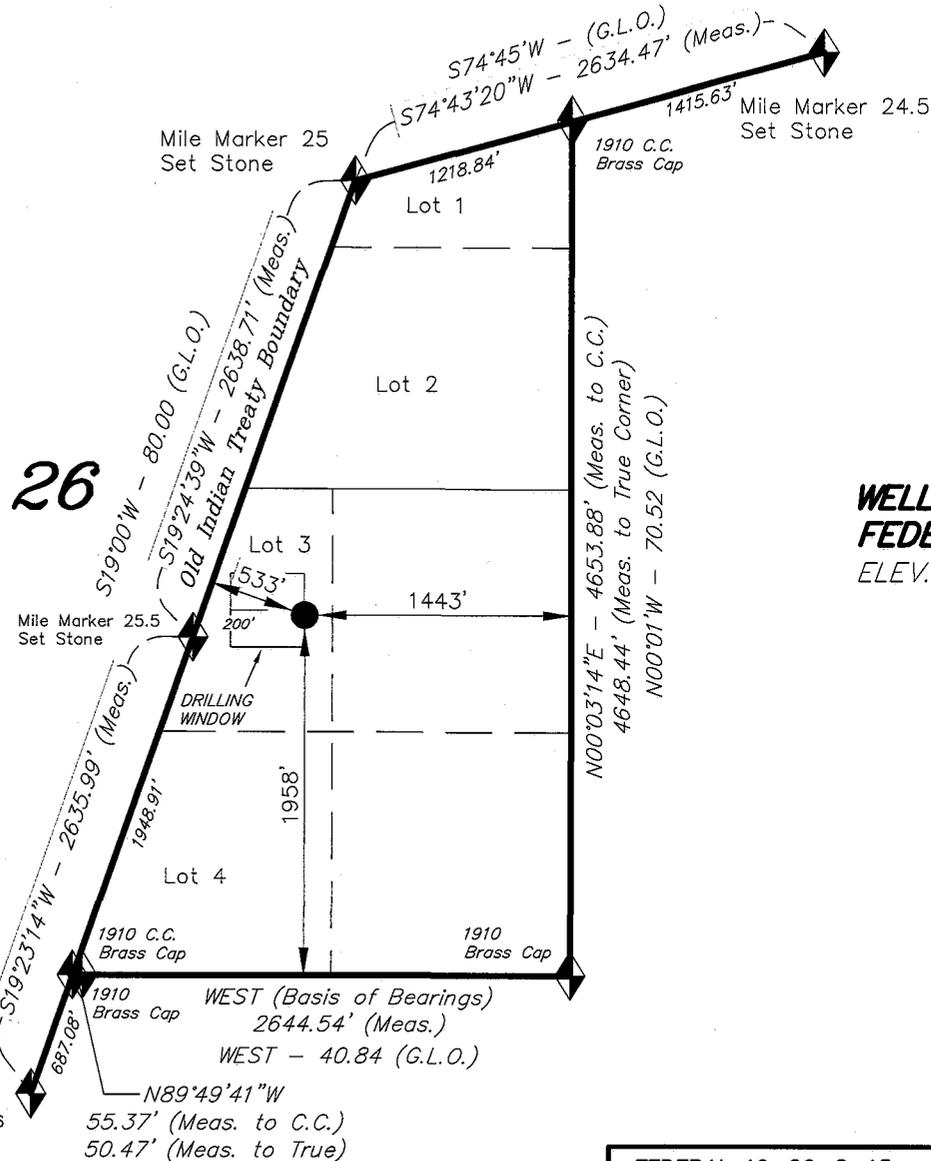

WELL LOCATION:
FEDERAL 10-26-8-15
 ELEV. UNGRADED GROUND = 5791.4'

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
 PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
 MADE BY ME OR UNDER MY SUPERVISION AND THAT
 THE SAME ARE TRUE AND CORRECT TO THE BEST OF
 MY KNOWLEDGE AND BELIEF. No. 189377



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV;
 U.S.G.S. 7-1/2 min QUAD (MYTON SW)

FEDERAL 10-26-8-15
 (Surface Location) NAD 83
 LATITUDE = 40° 05' 13.51"
 LONGITUDE = 110° 11' 42.29"

TRI STATE LAND SURVEYING & CONSULTING	
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078 (435) 781-2501	
DATE SURVEYED: 11-18-08	SURVEYED BY: T.H.
DATE DRAWN: 11-27-08	DRAWN BY: F.T.M.
REVISED:	SCALE: 1" = 1000'

NEWFIELD PRODUCTION COMPANY
FEDERAL 10-26-8-15
NW/SE (LOT #3) SECTION 26, T8S, R15E
DUCHESNE COUNTY, UTAH

ONSHORE ORDER NO. 1

DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta 0' – 1625'
Green River 1625'
Wasatch 6385'
Base of Moderately Saline Ground Water @ 5550'

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation 1625' – 6385' - Oil

4. PROPOSED CASING PROGRAM

Please refer to the Monument Butte Field Standard Operation Procedure (SOP).

5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:

Please refer to the Monument Butte Field SOP. See Exhibit "C".

6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:

Please refer to the Monument Butte Field SOP.

7. AUXILIARY SAFETY EQUIPMENT TO BE USED:

Please refer to the Monument Butte Field SOP.

8. TESTING, LOGGING AND CORING PROGRAMS:

Please refer to the Monument Butte Field SOP.

9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:

The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered.

10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:

Please refer to the Monument Butte Field SOP.

NEWFIELD PRODUCTION COMPANY
FEDERAL 10-26-8-15
NW/SE (LOT #3) SECTION 26, T8S, R15E
DUCHESNE COUNTY, UTAH

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Federal 10-26-8-15 located in the NW 1/4 SE 1/4 Section 26, T8S, R15E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.4 miles \pm to the junction of this highway and UT State Hwy 53; proceed southwesterly - 6.4 miles \pm ; turn and proceed in a southwesterly direction - 2.8 miles \pm to its junction with an existing road to the south; proceed in a southeasterly direction - 0.1 miles \pm to its junction with the beginning of the proposed access road; proceed in a southwesterly direction along the proposed access road - 3160' \pm to the proposed well location.

2. PLANNED ACCESS ROAD

See Topographic Map "B" for the location of the proposed access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

All permanent surface equipment will be painted Carlsbad Canyon.
Please refer to the Monument Butte Field Standard Operating Procedure (SOP).

5. LOCATION AND TYPE OF WATER SUPPLY

Newfield Production will transport water by truck for drilling purposes from the following water sources:

Johnson Water District
Water Right : 43-7478

Neil Moon Pond
Water Right: 43-11787

Maurice Harvey Pond
Water Right: 47-1358

Newfield Collector Well
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

Please refer to the Monument Butte Field SOP. See Exhibit "A".

6. SOURCE OF CONSTRUCTION MATERIALS

Please refer to the Monument Butte Field SOP.

7. METHODS FOR HANDLING WASTE DISPOSAL

Please refer to the Monument Butte Field SOP.

8. ANCILLARY FACILITIES

Please refer to the Monument Butte Field SOP.

9. WELL SITE LAYOUT

See attached Location Layout Diagram.

10. PLANS FOR RESTORATION OF SURFACE

Please refer to the Monument Butte Field SOP.

11. SURFACE OWNERSHIP - Bureau Of Land Management (Proposed location and access roads leading to).

12. OTHER ADDITIONAL INFORMATION

The Archaeological Resource Survey for this area is attached. MOAC Report #08-301, 1/26/09. The Paleontological Resource Survey will be forthcoming. See attached report cover page, Exhibit "D".

Newfield Production Company requests 3160' of disturbed area be granted in Lease UTU-67168 to allow for construction of the planned access road. **Refer to Topographic Map "B"**. A permanent width of 30' and a running surface of 18' is proposed for the planned access road. The construction phase of the planned access road will last approximately (5) days. The planned access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 3160' of disturbed area be granted in Lease UTU-67168 to allow for construction of the proposed surface gas lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a 10" or smaller gas gathering line, and a 3" poly fuel gas line, with a permanent width of 30' upon completion of the proposed gas lines. The construction phase of the proposed gas lines will last approximately (5) days. Both lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Newfield Production Company requests 3160' of disturbed area be granted in Lease UTU-67168 to allow for construction of the proposed water lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line, with a permanent width of 30' upon completion of the proposed water return line. The construction phase of the proposed water lines will last approximately (5) days. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP. In the event that the proposed well is converted to a water injection well, a separate injection permit will be applied for through the proper agencies.

Water Disposal

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), State of Utah approved surface disposal facilities, or Federally approved surface disposal facilities.

Threatened, Endangered, And Other Sensitive Species

Mountain Plover: If new construction or surface disturbing activities are scheduled to occur between May 15 and June 15, detailed surveys of the area within 0.5 mile of the proposed location and within 300 feet of proposed access routes must be conducted to detect the presence of mountain plovers. All surveys must be conducted in accordance with the survey protocols outlined in the most recent USFWS Survey Protocol. Surveys must be completed prior to initiating new construction or surface disturbing activities. No new construction or surface disturbing activities will be allowed between May 15 and June 15 within a 0.5 mile radius of any documented mountain plover nest site.

Reserve Pit Liner

A 16 mil liner with felt is required. Please refer to the Monument Butte Field SOP.

Location and Reserve Pit Reclamation

Please refer to the Monument Butte Field SOP.

The following seed mixture will be used on the topsoil stockpile, to the recontoured surface of the reserve pit, and for final reclamation: (All poundages are in pure live seed)

Squirrell Tail	<i>Elymus Elymoides</i>	6 lbs/acre
Siberian Wheatgrass	<i>Agropyron Fragile</i>	2 lbs/acre
Gardner Saltbush	<i>Atriplex Gardneri</i>	1 lbs/acre
Shadscale	<i>Atriplex Confertifolia</i>	1 lbs/acre
Fourwing Saltbush	<i>Atriplex Canescens</i>	1 lbs/acre
Scarlet Globemallow	<i>Sphaeralcea Conccinea</i>	0.20 lbs/acre
Forage Kochia	<i>Kochia Prostrata</i>	0.20 lbs/acre

Details of the On-Site Inspection

The proposed Federal 10-26-8-15 was on-sited on 12/10/08. The following were present; Tim Eaton (Newfield Production), Christine Cimiluca (Bureau of Land Management), and James Herford (Bureau of Land Management). Weather conditions were clear and ground cover was 30% open.

LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION

Representative

Name: Dave Allred
Address: Route #3 Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification


Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #10-26-8-15 NW/SE Section 26, Township 8S, Range 15E: Lease UTU-67168 Duchesne County, Utah: and is responsible under the terms and conditions of the lease for the

operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

2/20/09

Date





Mandie Crozier
Regulatory Specialist
Newfield Production Company

NEWFIELD PRODUCTION COMPANY

FEDERAL 10-26-8-15

Section 26, T8S, R15E, S.L.B.&M.



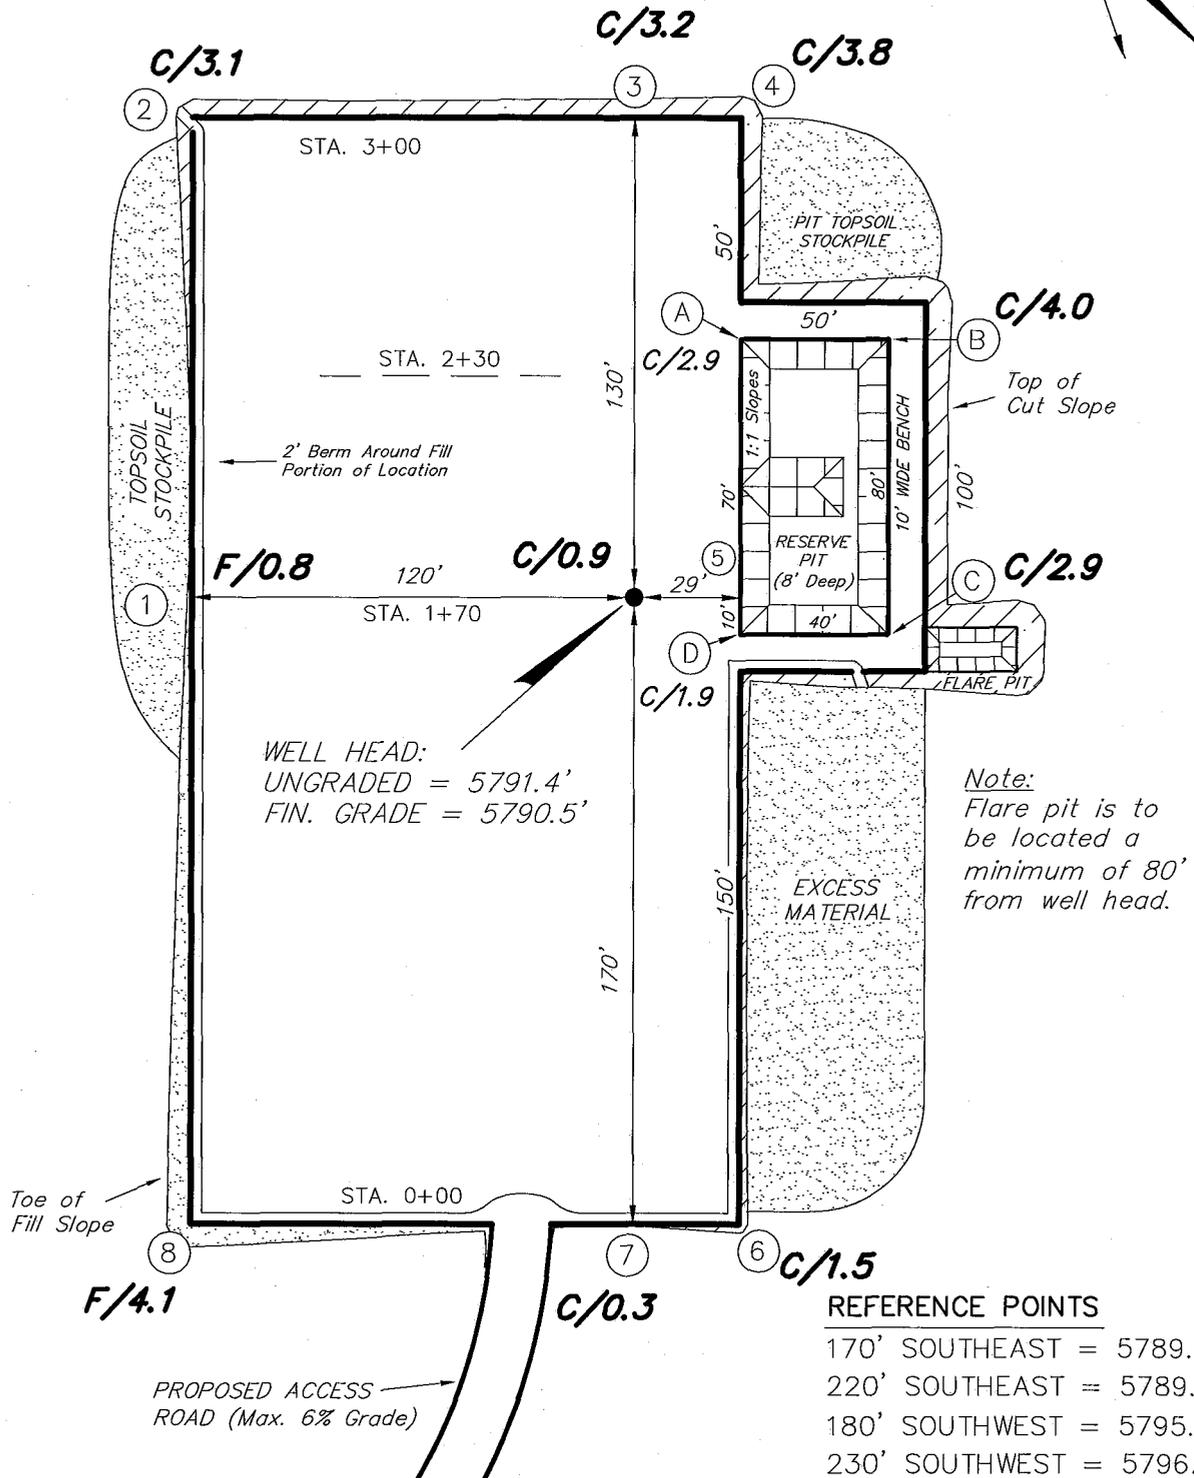



SURVEYED BY: T.H.	DATE SURVEYED: 11-18-08
DRAWN BY: F.T.M.	DATE DRAWN: 11-27-08
SCALE: 1" = 50'	REVISED:

Tri State
Land Surveying, Inc.
(435) 781-2501
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

CROSS SECTIONS FEDERAL 10-26-8-15

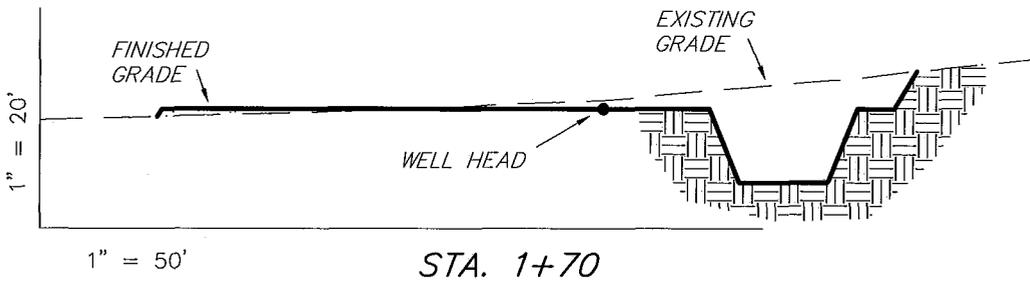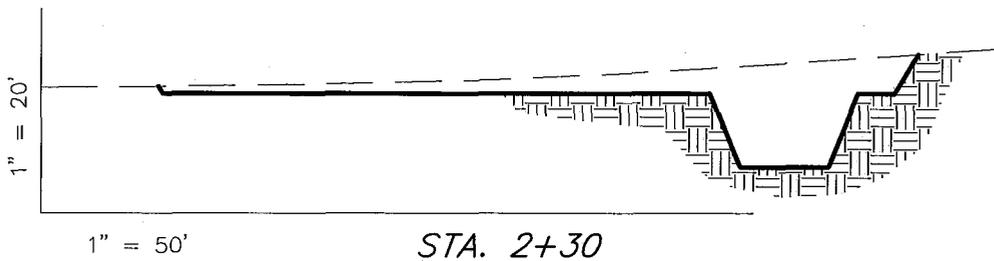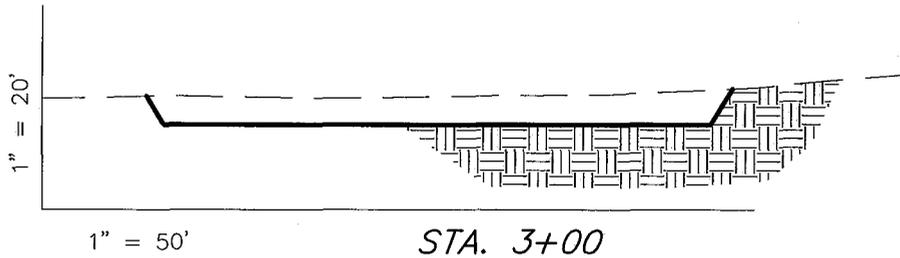

NOTE:
UNLESS OTHERWISE
NOTED ALL CUT/FILL
SLOPES ARE AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards)



ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	1,600	1,600	Topsoil is not included in Pad Cut	0
PIT	640	0		640
TOTALS	2,240	1,600	1,010	640

SURVEYED BY: T.H.	DATE SURVEYED: 11-18-08
DRAWN BY: F.T.M.	DATE DRAWN: 11-27-08
SCALE: 1" = 50'	REVISED:

Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

TYPICAL RIG LAYOUT FEDERAL 10-26-8-15

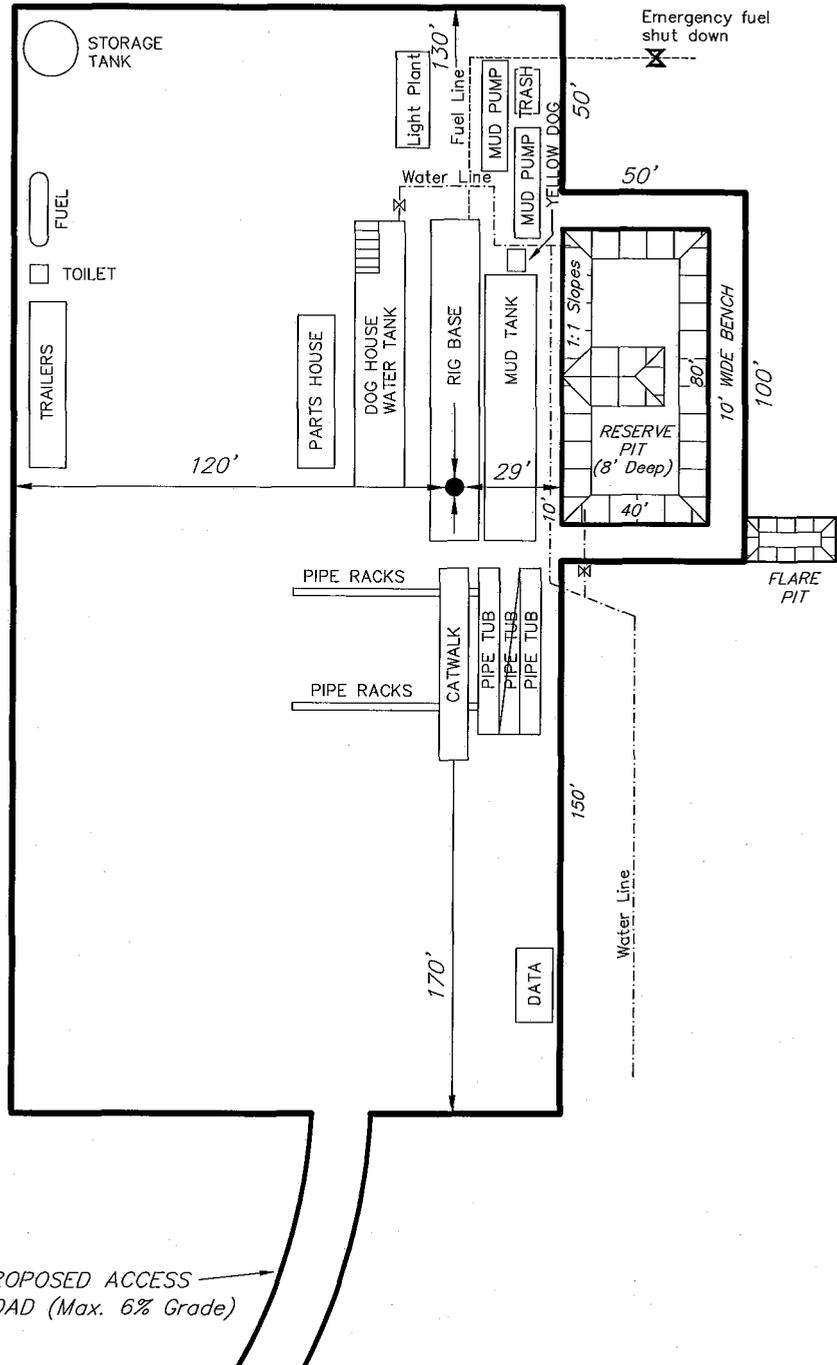

SURVEYED BY: T.H.	DATE SURVEYED: 11-18-08
DRAWN BY: F.T.M.	DATE DRAWN: 11-27-08
SCALE: 1" = 50'	REVISED:

Tri State
Land Surveying, Inc. (435) 781-2501
180 NORTH VERNAL AVE. VERNAL, UTAH 84078


Newfield Production Company Proposed Site Facility Diagram

Federal 10-26-8-15

NW/SE (Lot #3) Sec. 26, T8S, R15E

Duchesne County, Utah

UTU-67168

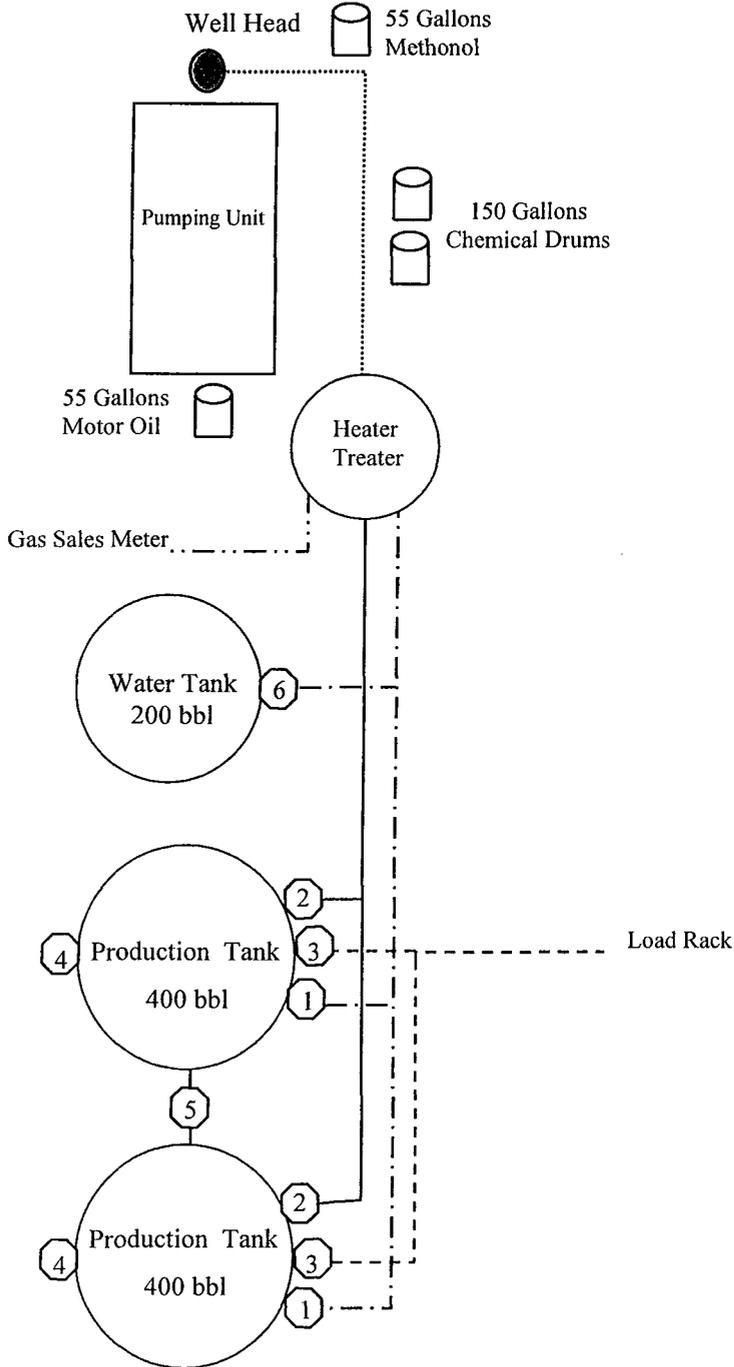

Legend

Emulsion Line
Load Rack	-----
Water Line	-----
Gas Sales	-----
Oil Line	-----

Production Phase:

- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open

Sales Phase:


- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

Draining Phase:

- 1) Valves 1 and 6 open

Diked Section



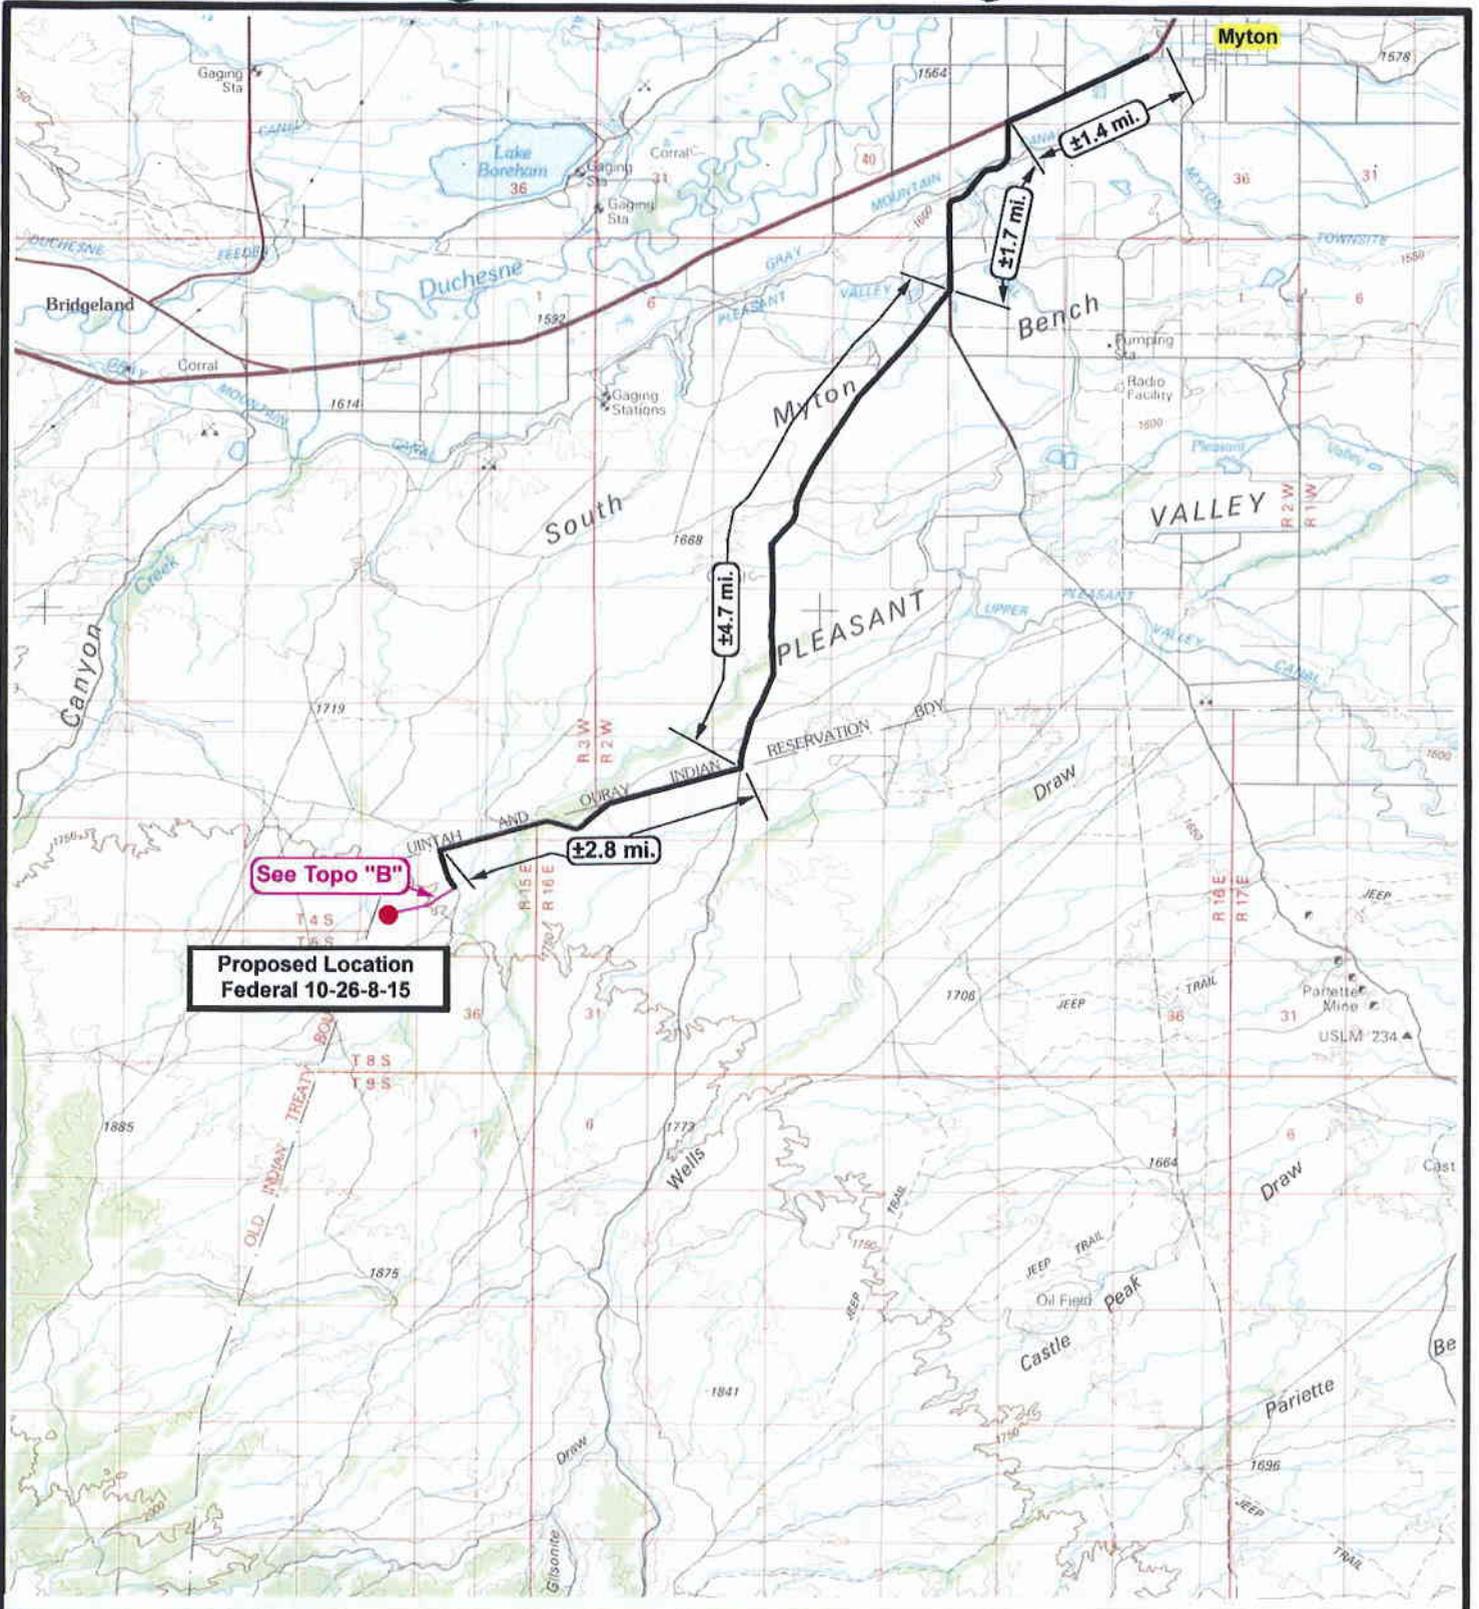

**Proposed Location
Federal 10-26-8-15**

See Topo "B"

NEWFIELD
Exploration Company

**Federal 10-26-8-15
SEC. 26, T8S, R15E, S.L.B.&M.**




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1 = 100,000
DRAWN BY: mw
DATE: 12-02-2008

Legend

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP
"A"

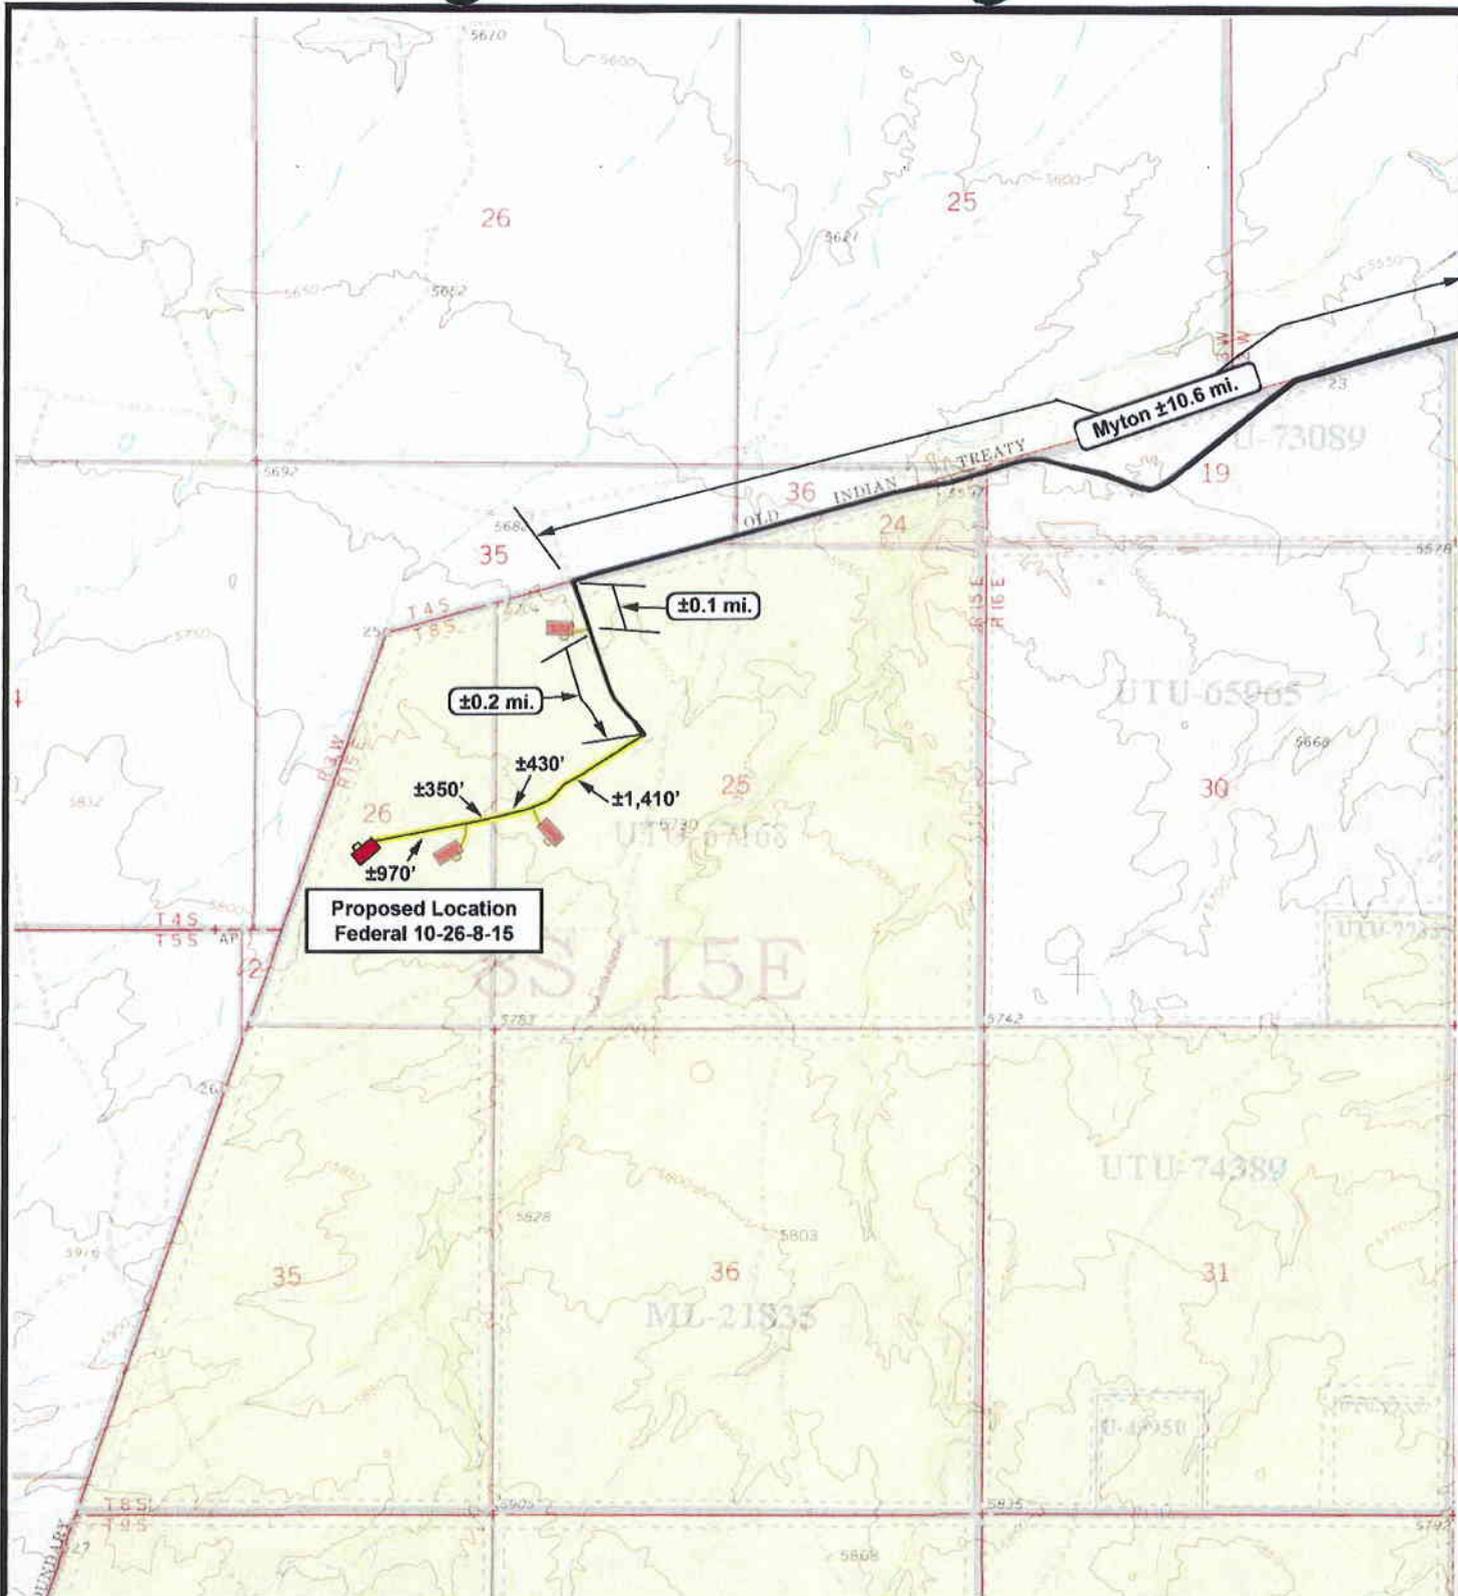


NEWFIELD
Exploration Company


Federal 10-26-8-15
SEC. 26, T8S, R15E, S.L.B.&M.





Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 12-02-2008

Legend

-  Existing Road
-  Proposed Access

TOPOGRAPHIC MAP
"B"

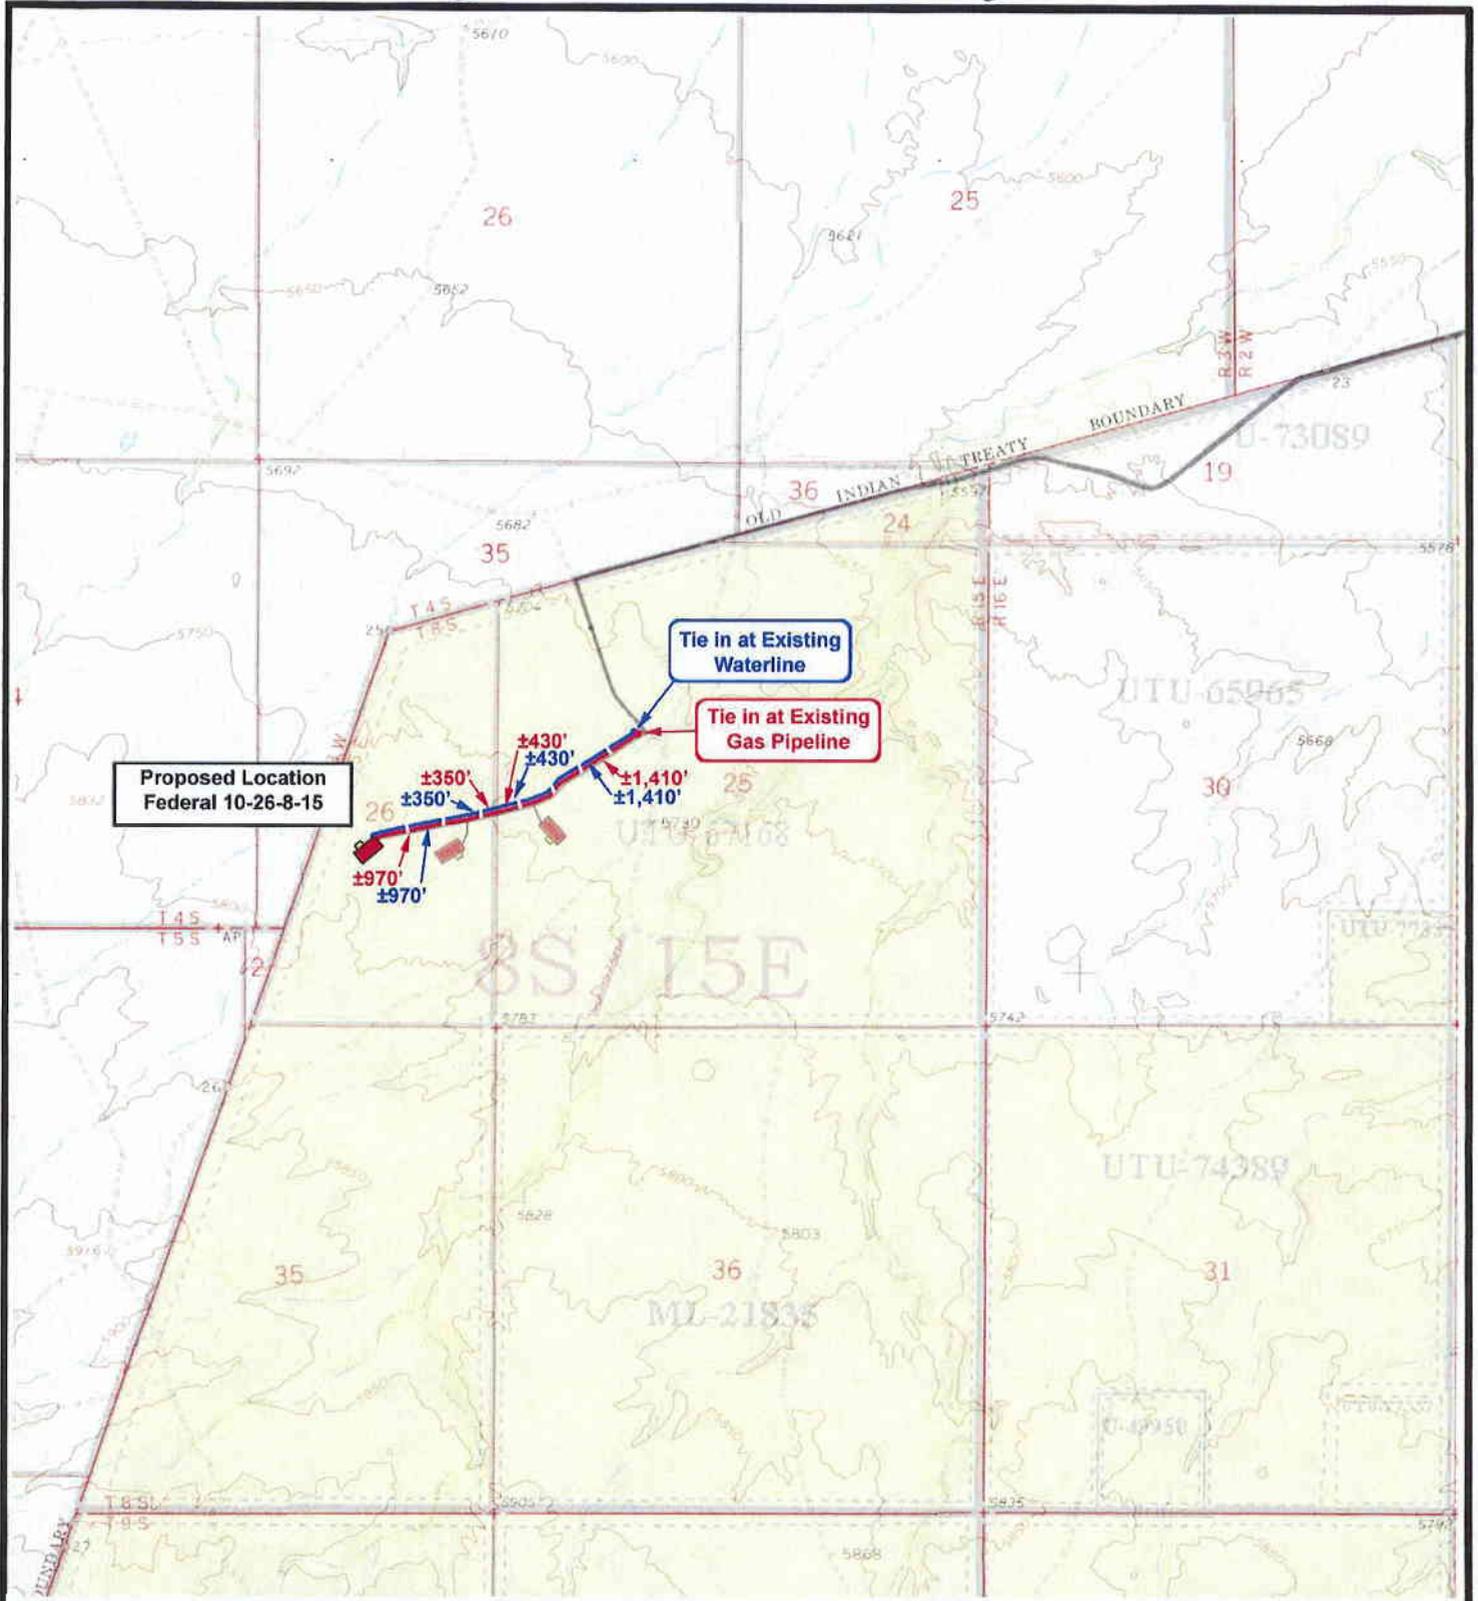

NEWFIELD
Exploration Company

Federal 10-26-8-15
SEC. 26, T8S, R15E, S.L.B.&M.




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 12-02-2008

Legend

- Roads
- Proposed Gas Line
- Proposed Water Line

TOPOGRAPHIC MAP
"C"

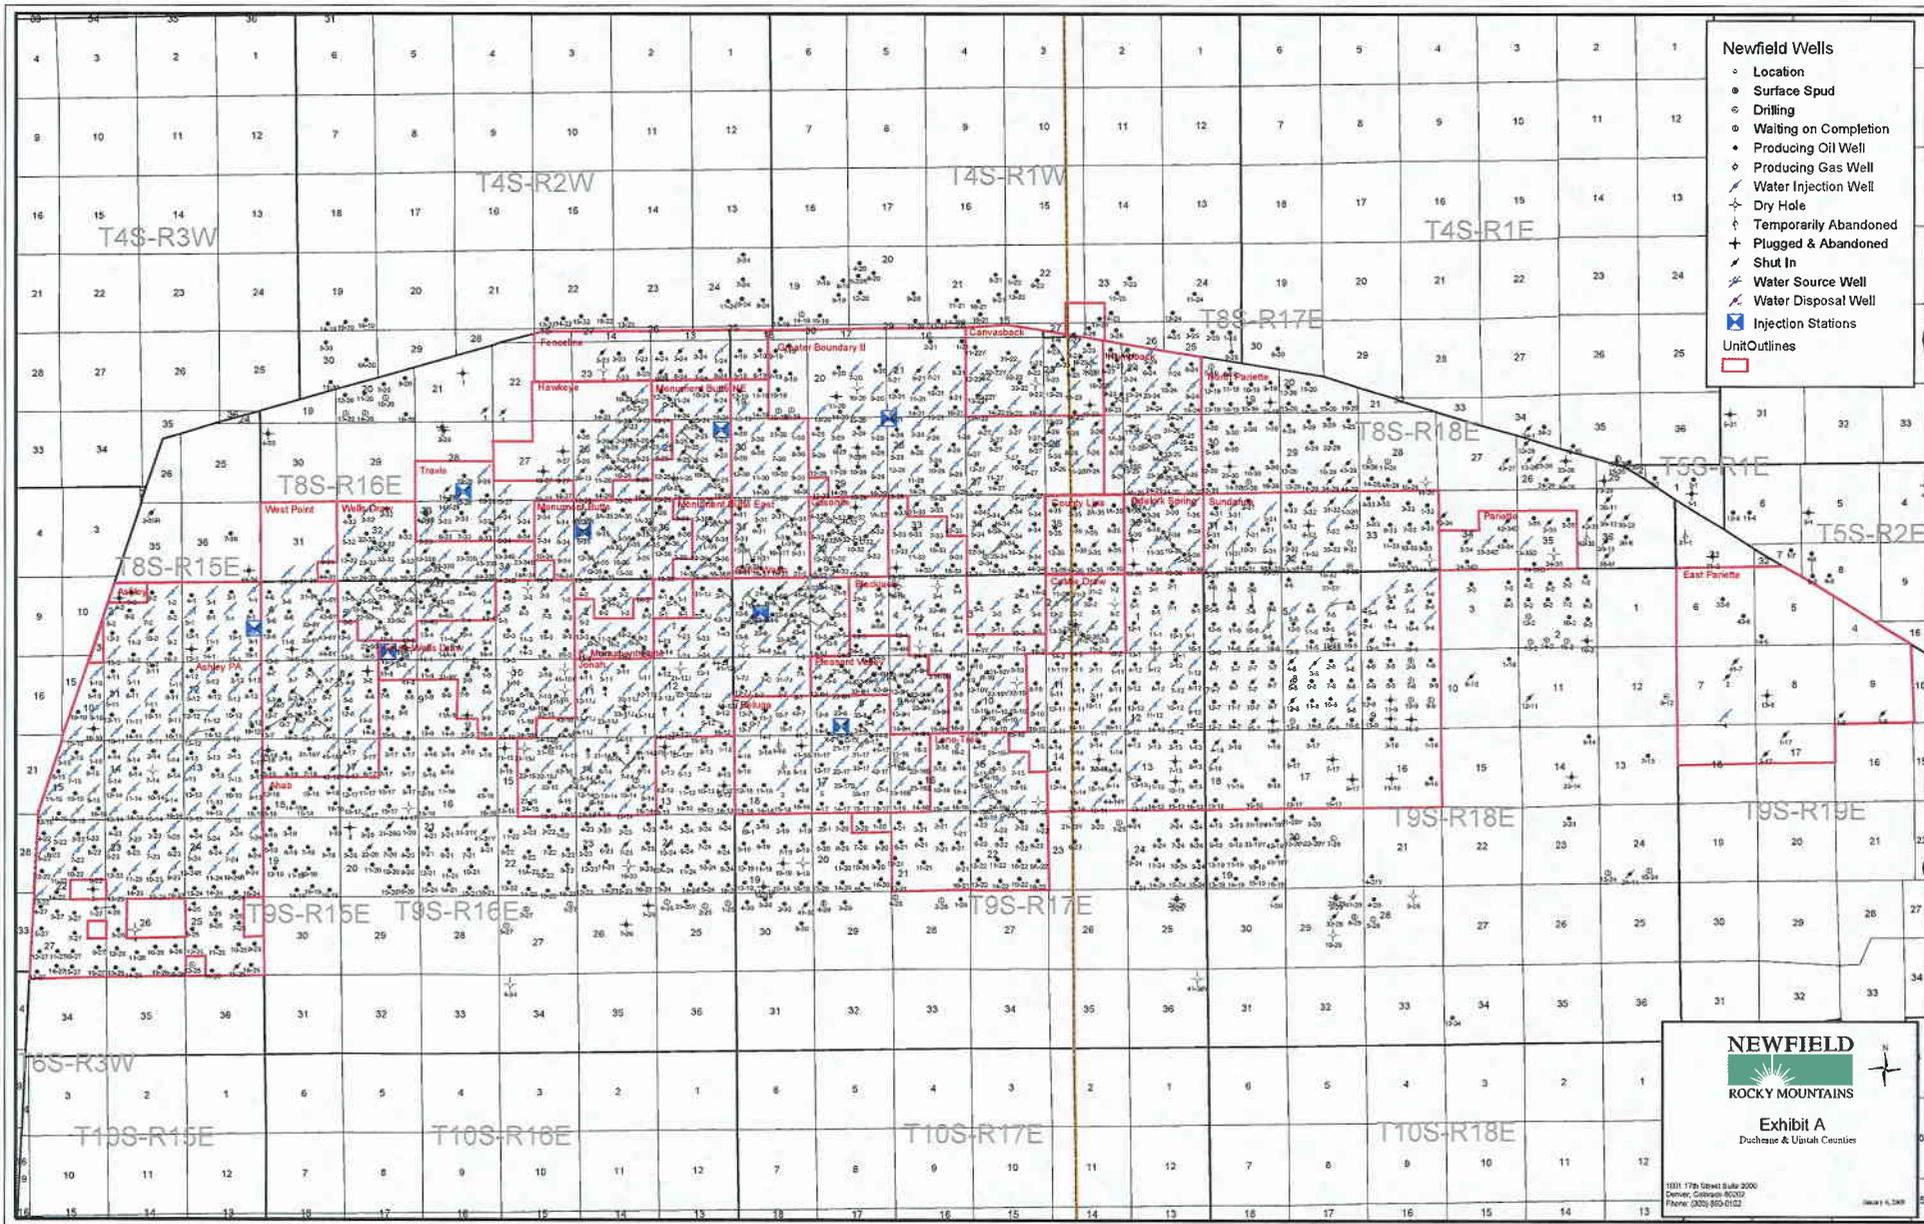

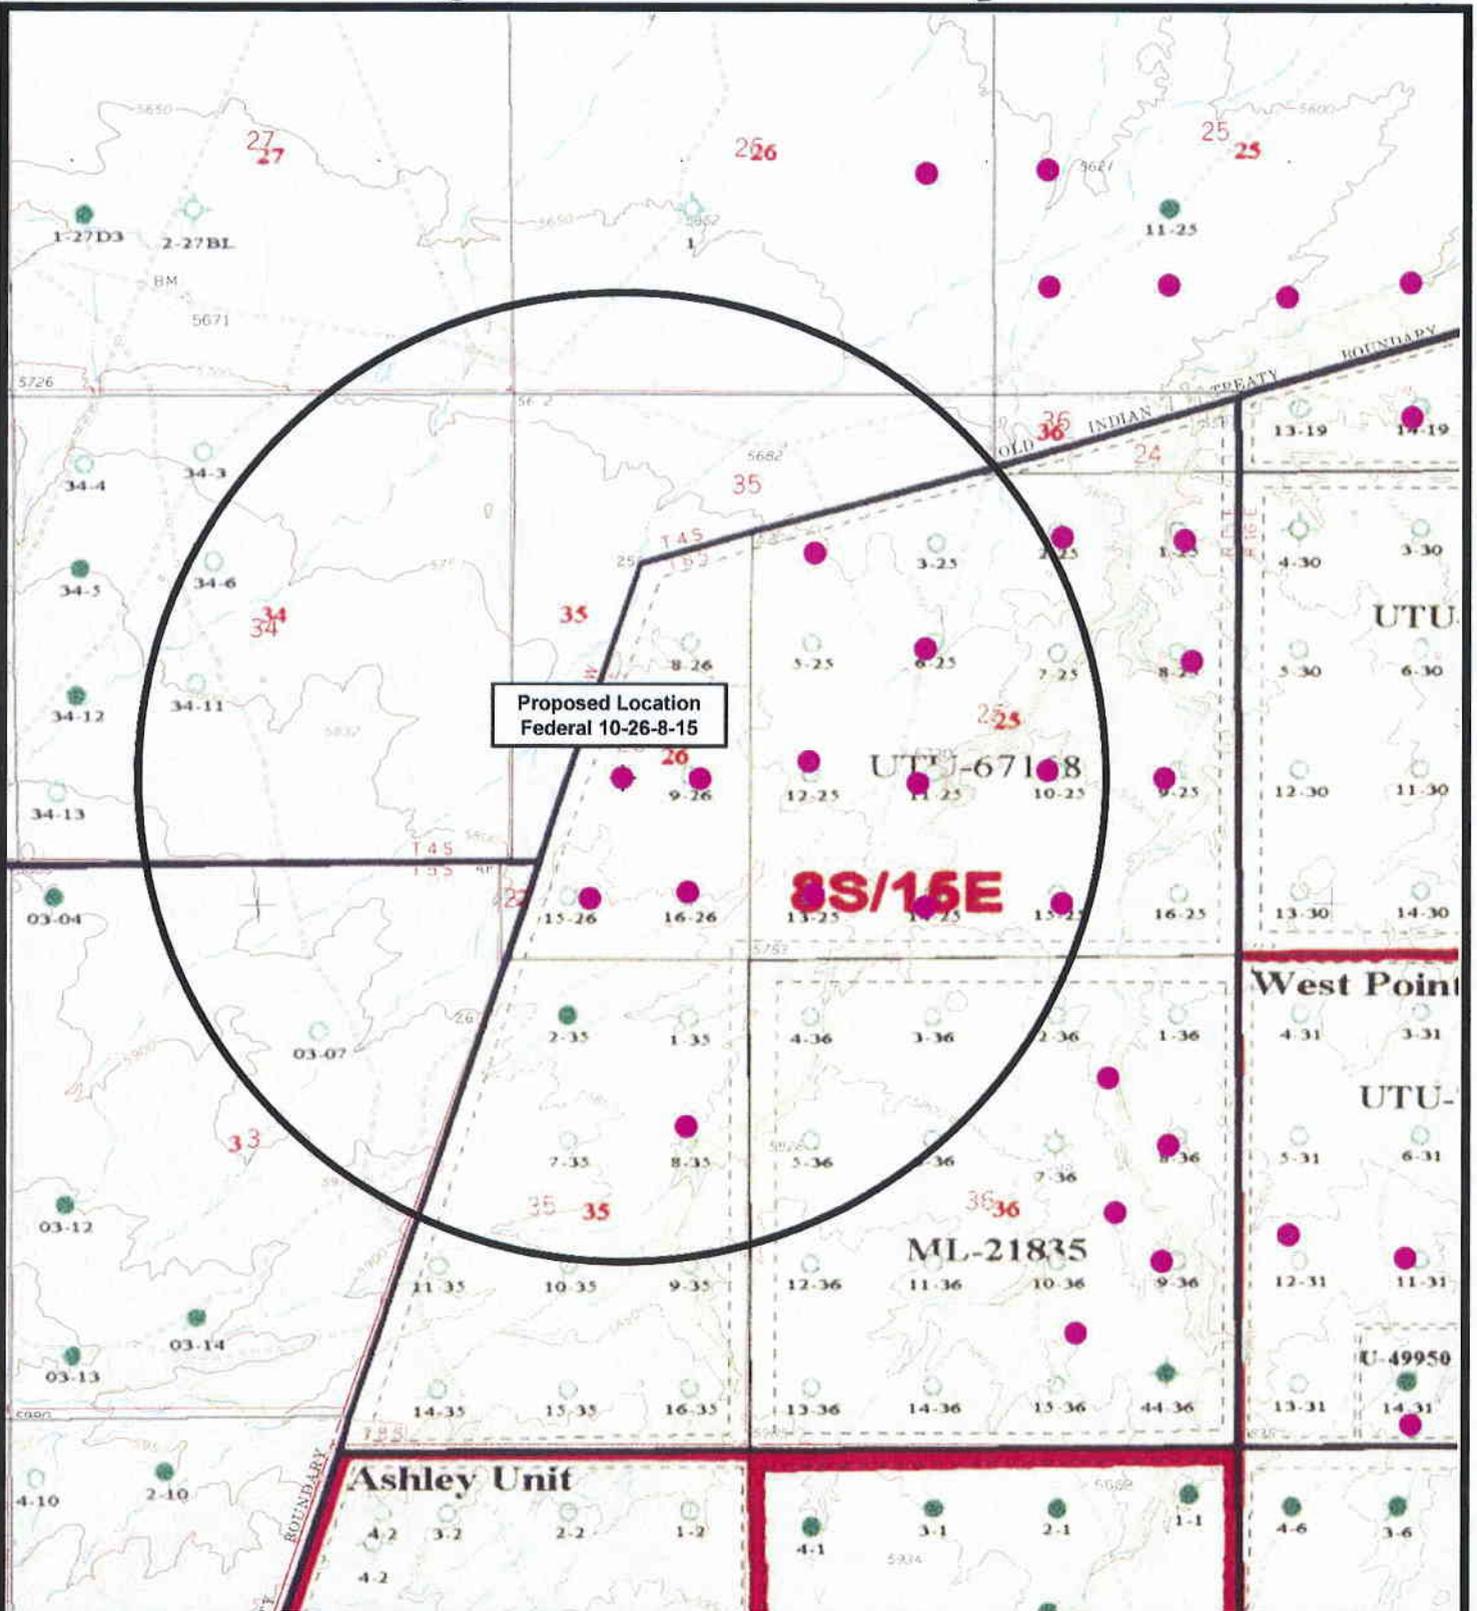

Proposed Location
Federal 10-26-8-15

Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

Legend

- Location
- One-Mile Radius

SCALE: 1" = 2,000'
DRAWN BY: mw
DATE: 12-02-2008

Exhibit "B"

NEWFIELD
Exploration Company

Federal 10-26-8-15
SEC. 26, T8S, R15E, S.L.B.&M.

2-M SYSTEM

Blowout Prevention Equipment Systems

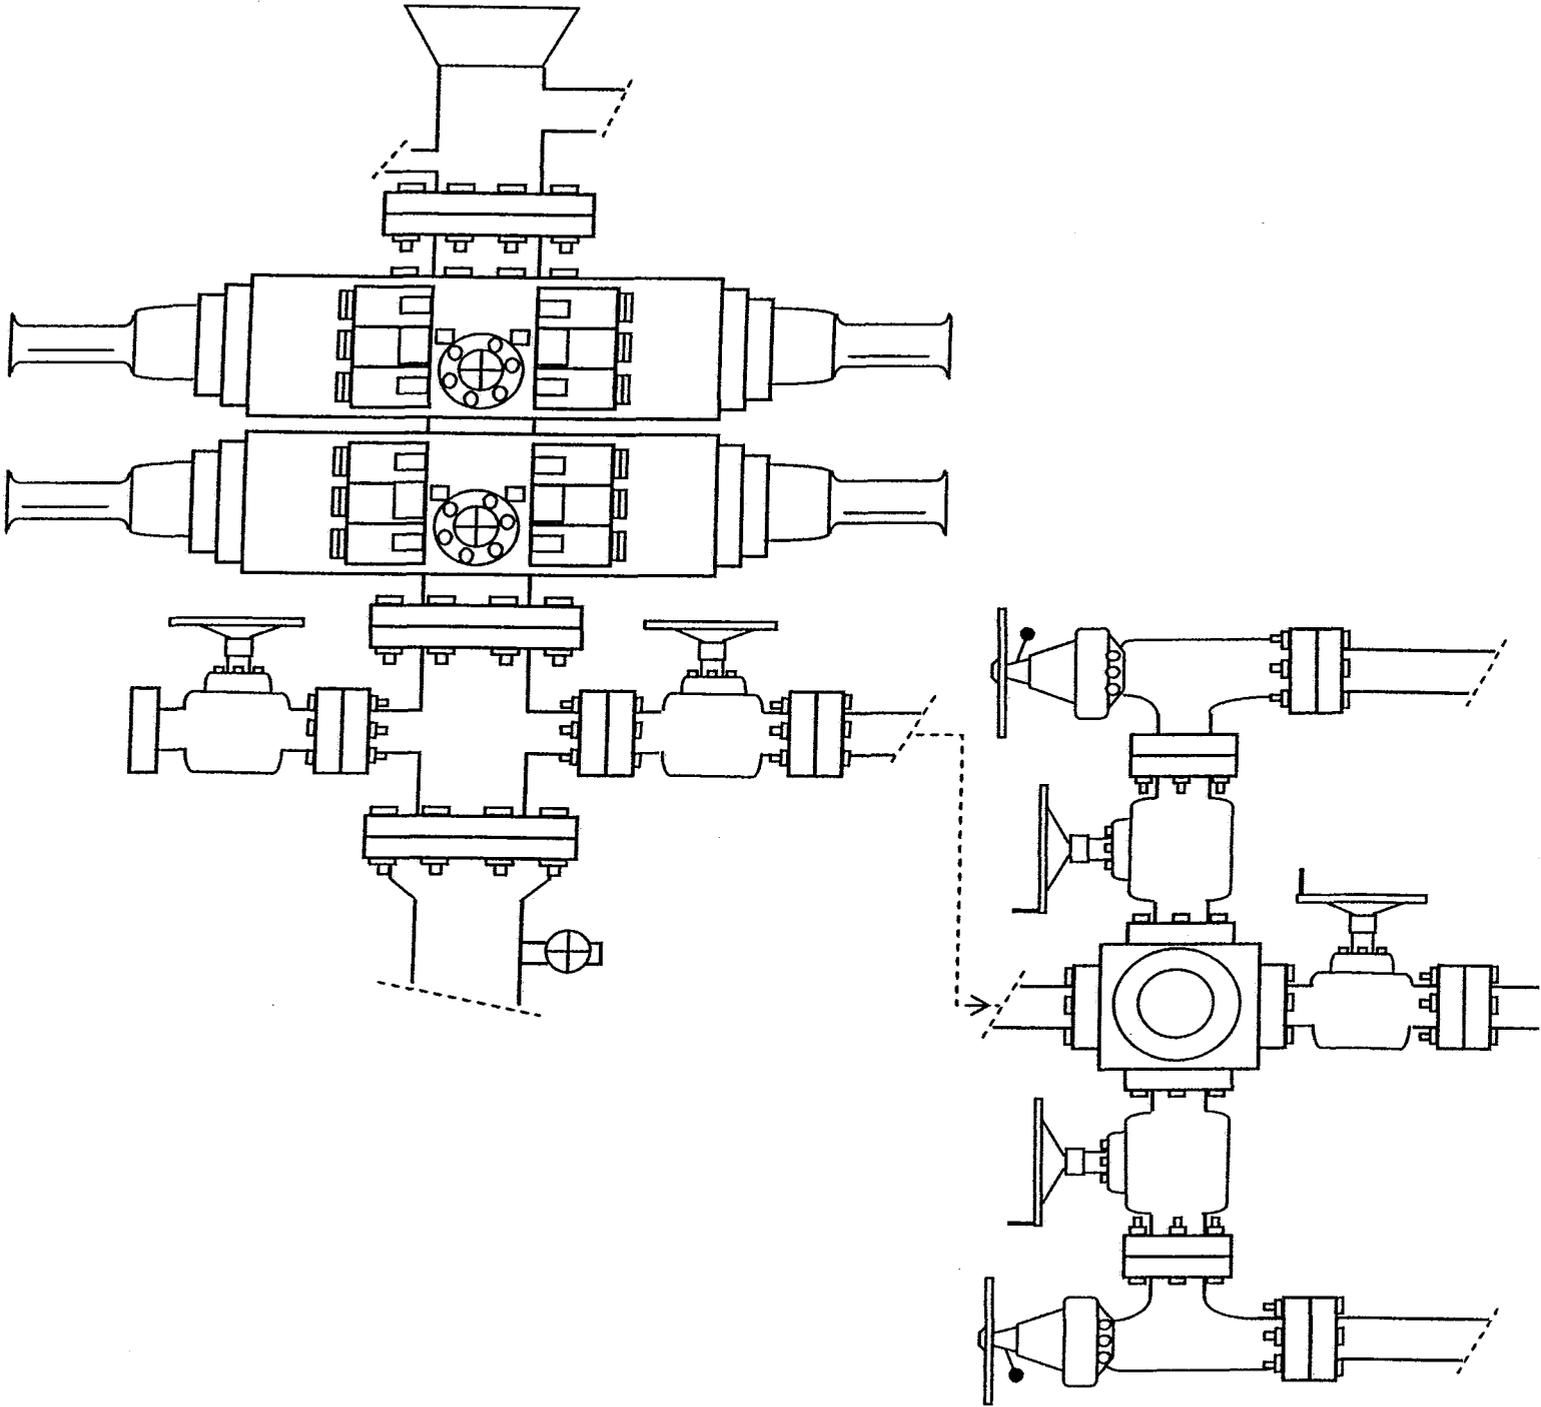


EXHIBIT C

CULTURAL RESOURCE INVENTORY OF
NEWFIELD EXPLORATION'S FOUR BLOCK PARCELS
(T8S, R15E, SECTIONS 25, 26, 35, AND 36)
DUCHESNE COUNTY, UTAH

By:

Nicole Shelnut

Prepared For:

Bureau of Land Management
Vernal Field Office
and
School & Institutional
Trust Lands Administration

Prepared Under Contract With:

Newfield Exploration Company
Rt. 3 Box 3630
Myton, UT 84052

Prepared By:

Montgomery Archaeological Consultants, Inc.
P.O. Box 219
Moab, Utah 84532

MOAC Report No. 08-301

January 26, 2009

United States Department of Interior (FLPMA)
Permit No. 08-UT-60122

State of Utah Antiquities Project (Survey)
Permit No. U-08-MQ-1227b,s

**WORKSHEET
APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 02/26/2009

API NO. ASSIGNED: 43-013-34216

WELL NAME: FEDERAL 10-26-8-15

OPERATOR: NEWFIELD PRODUCTION (N2695)

PHONE NUMBER: 435-646-3721

CONTACT: MANDIE CROZIER

PROPOSED LOCATION:

NWSE 26 080S 150E
 SURFACE: 1958 FSL 1443 FEL
 BOTTOM: 1958 FSL 1443 FEL
 COUNTY: DUCHESNE
 LATITUDE: 40.08715 LONGITUDE: -110.19439
 UTM SURF EASTINGS: 568681 NORTHINGS: 4437531
 FIELD NAME: UNDESIGNATED (2)

INSPECT LOCATN BY: / /		
Tech Review	Initials	Date
Engineering		
Geology		
Surface		

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-67168

SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: GRRV

COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:

- Plat
- Bond: Fed[1] Ind[] Sta[] Fee[]
(No. WYB000493)
- Potash (Y/N)
- Oil Shale 190-5 (B) or 190-3 or 190-13
- Water Permit
(No. 43-7478)
- RDCC Review (Y/N)
(Date: _____)
- Fee Surf Agreement (Y/N)
- Intent to Commingle (Y/N)

LOCATION AND SITING:

- R649-2-3.
- Unit: _____
- R649-3-2. General
Siting: 460 From Qtr/Qtr & 920' Between Wells
- R649-3-3. Exception
- Drilling Unit
Board Cause No: _____
Eff Date: _____
Siting: _____
- R649-3-11. Directional Drill

COMMENTS: Sup, Deposit Site

STIPULATIONS: 1. Federal Approval
2. Spacing Strip

API Number: 4301334216

Well Name: FEDERAL 10-26-8-15




Township 08.0 S Range 15.0 E Section 26

Meridian: SLBM

Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
Map Produced by Diana Mason

Units	Wells Query Events
STATUS	✕ <all other values>
ACTIVE	GIS_STAT_TYPE
EXPLORATORY	◆ <Null>
GAS STORAGE	◆ APD
NF PP OIL	◆ DRL
NF SECONDARY	◆ GI
PI OIL	◆ GS
PP GAS	◆ LA
PP GEOTHERML	◆ NEW
PP OIL	◆ OPS
SECONDARY	◆ PA
TERMINATED	◆ PGW
Fields	◆ POW
STATUS	◆ RET
ACTIVE	◆ SGW
COMBINED	◆ SOW
Sections	◆ TA
Township	○ TW
	◆ WD
	◆ WI
	◆ WS

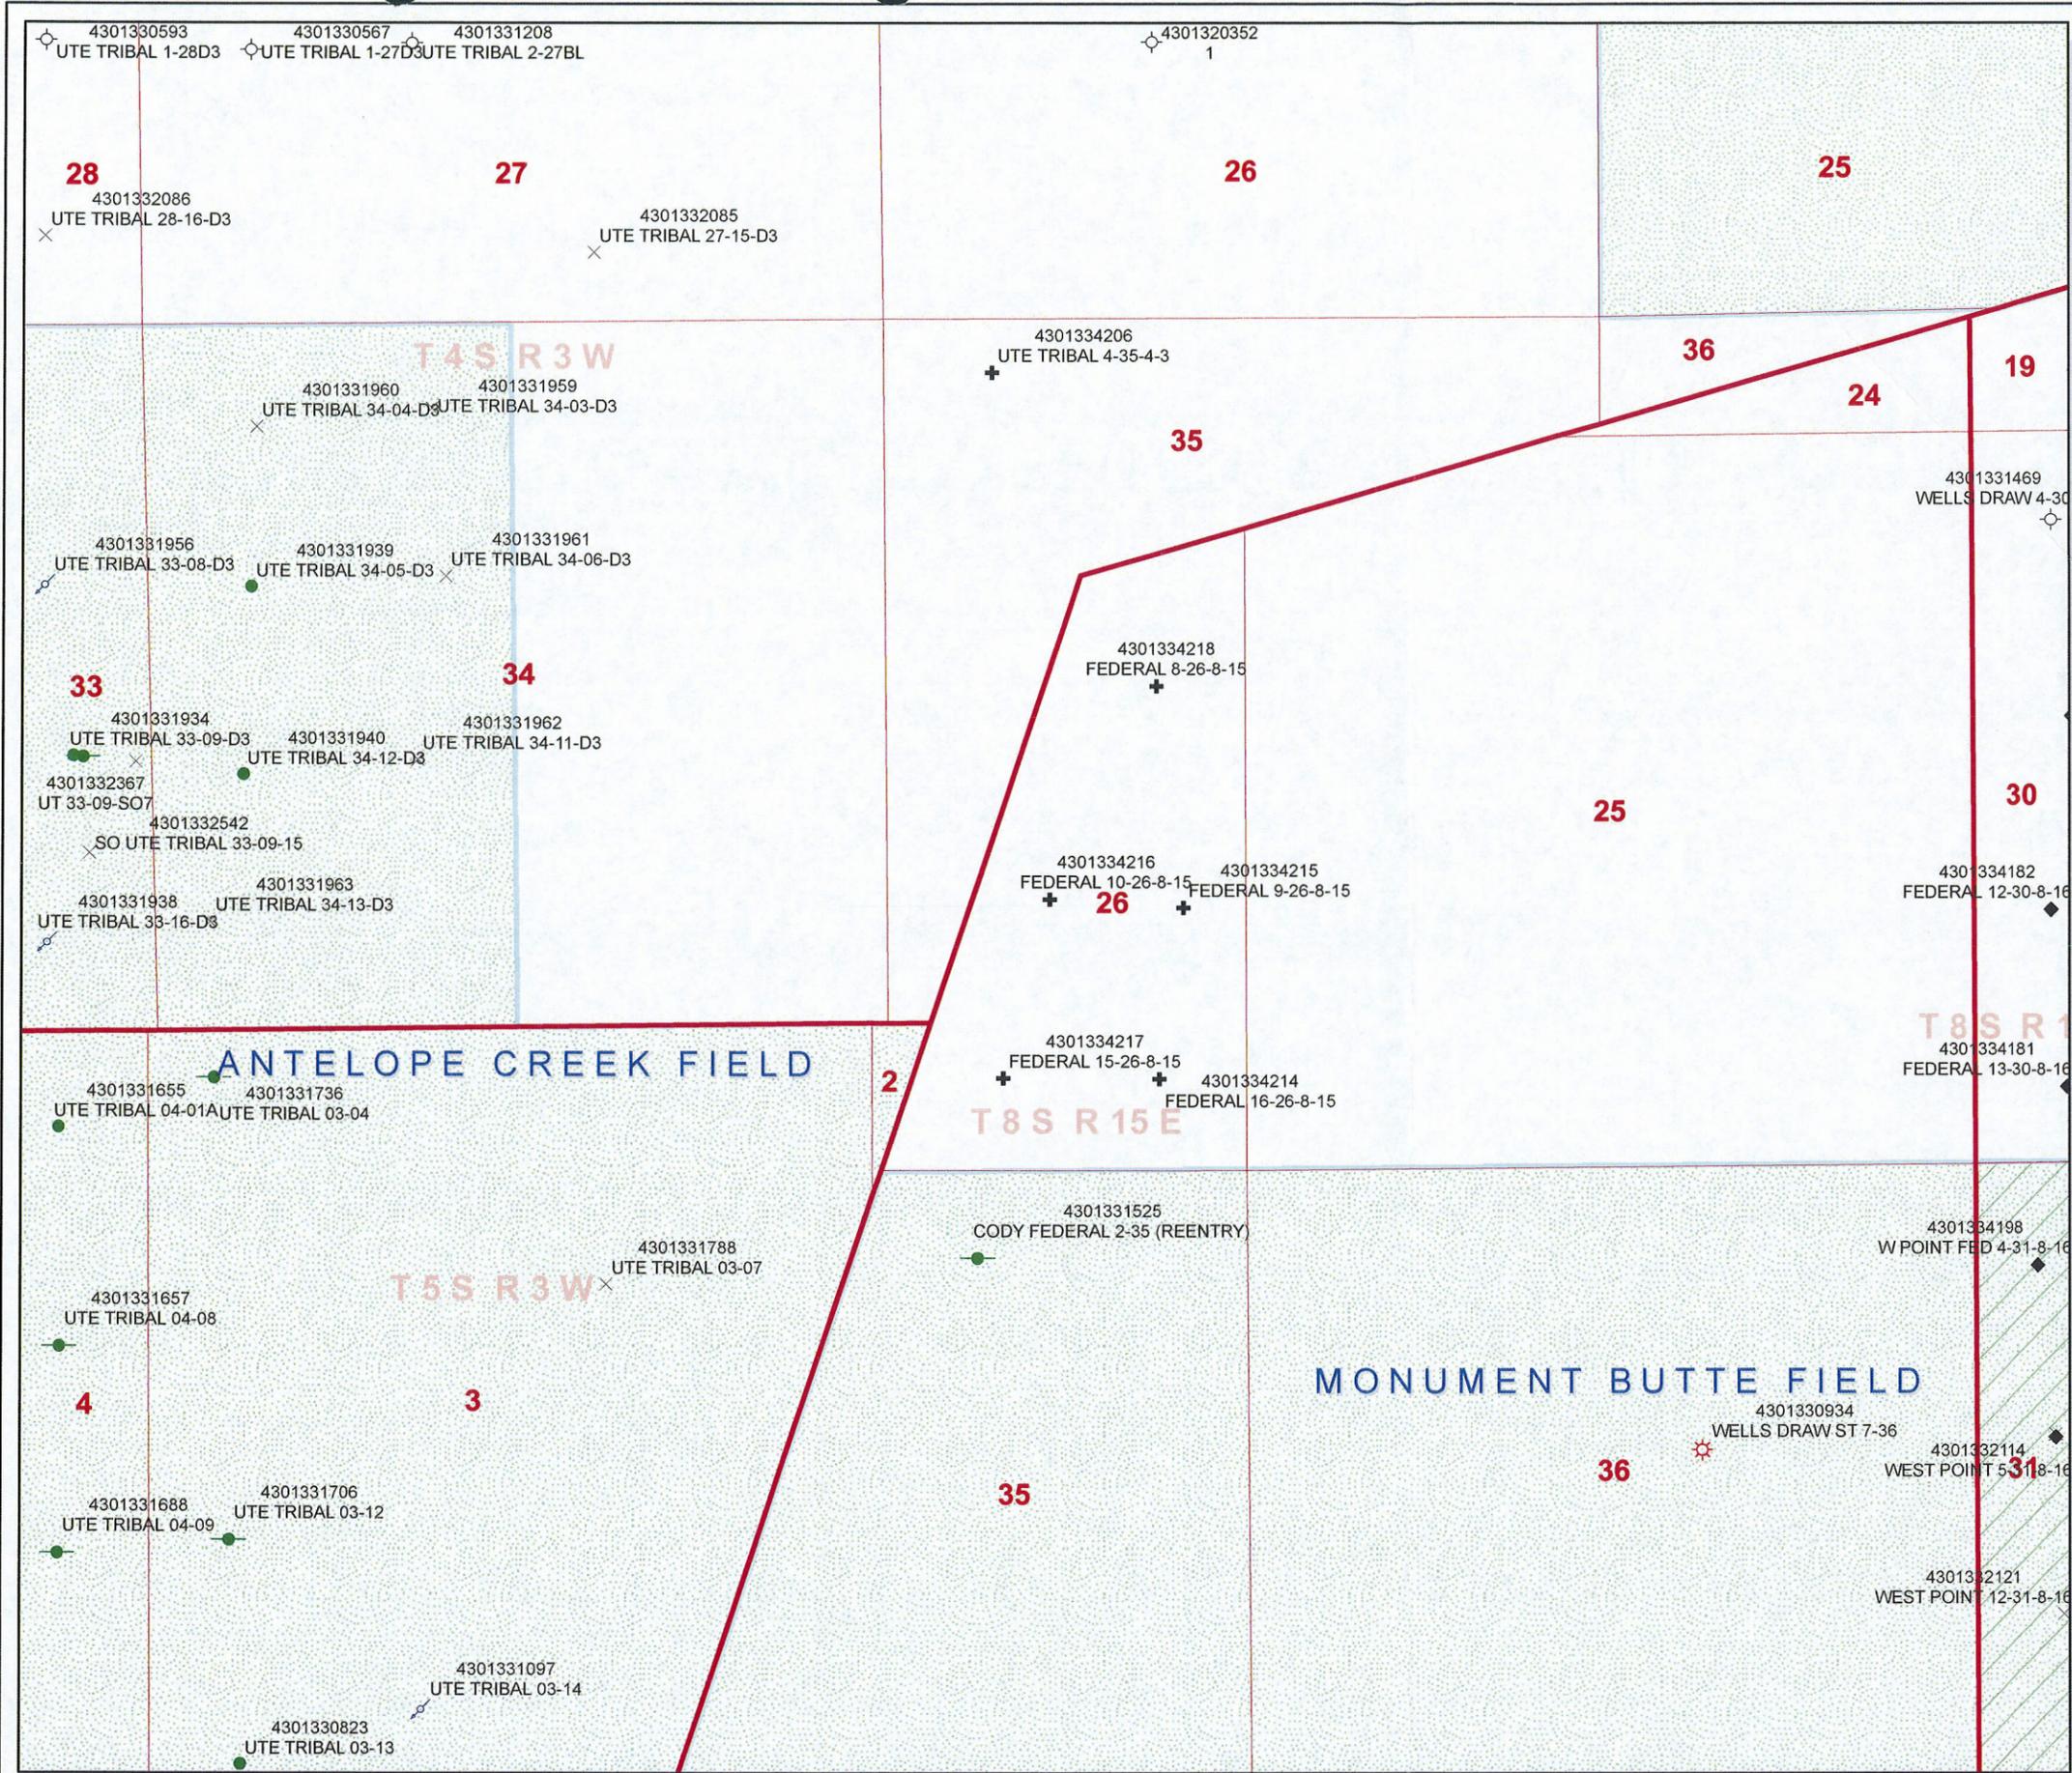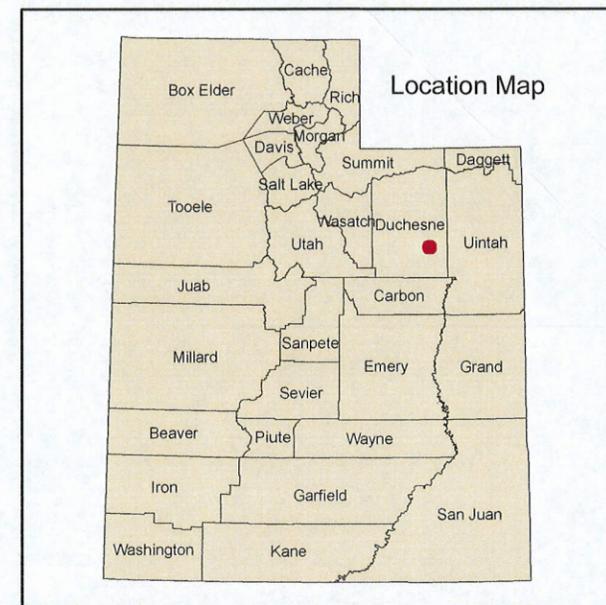



JON M. HUNTSMAN, JR.
Governor

GARY R. HERBERT
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

March 2, 2009

Newfield Production Company
Rt. #3, Box 3630
Myton, UT 84052

Re: Federal 10-26-8-15 Well, 1958' FSL, 1443' FEL, NW SE, Sec. 26, T. 8 South, R. 15 East, Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-34216.

Sincerely,

Gil Hunt
Associate Director

pab
Enclosures

cc: Duchesne County Assessor
Bureau of Land Management, Vernal Office



Operator: Newfield Production Company
Well Name & Number Federal 10-26-8-15
API Number: 43-013-34216
Lease: UTU-67168

Location: NW SE Sec. 26 T. 8 South R. 15 East

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

2. Notification Requirements

Notify the division within 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dustin Doucet at (801) 538-5281 (801) 733-0983 home

3. Reporting Requirements

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.

5. This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67168
---	--

SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
--	---

1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: FEDERAL 10-26-8-15
------------------------------------	---

2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	9. API NUMBER: 43013342160000
--	---

3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext	9. FIELD and POOL or WILDCAT: UNDESIGNATED
--	--	--

4. LOCATION OF WELL FOOTAGES AT SURFACE: 1958 FSL 1443 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSE Section: 26 Township: 08.0S Range: 15.0E Meridian: S	COUNTY: DUCHESNE STATE: UTAH
---	---

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 3/2/2010 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input checked="" type="checkbox"/> APD EXTENSION OTHER:

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Newfield proposes to extend the permit to drill for one more year.

Approved by the Utah Division of Oil, Gas and Mining

Date: March 04, 2010

By:

NAME (PLEASE PRINT) Mandie Crozier	PHONE NUMBER 435 646-4825	TITLE Regulatory Tech
SIGNATURE N/A	DATE 3/4/2010	



The Utah Division of Oil, Gas, and Mining

- State of Utah
- Department of Natural Resources

Electronic Permitting System - Sundry Notices

Request for Permit Extension Validation Well Number 43013342160000

API: 43013342160000

Well Name: FEDERAL 10-26-8-15

Location: 1958 FSL 1443 FEL QTR NWSE SEC 26 TWNP 080S RNG 150E MER S

Company Permit Issued to: NEWFIELD PRODUCTION COMPANY

Date Original Permit Issued: 3/2/2009

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision. Following is a checklist of some items related to the application, which should be verified.

- If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes No
- Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes No
- Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes No
- Have there been any changes to the access route including ownership, or rightof- way, which could affect the proposed location? Yes No
- Has the approved source of water for drilling changed? Yes No
- Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes No
- Is bonding still in place, which covers this proposed well? Yes No

**Approved by the
Utah Division of
Oil, Gas and Mining**

Signature: Mandie Crozier

Date: 3/4/2010

Title: Regulatory Tech **Representing:** NEWFIELD PRODUCTION COMPANY

Date: March 04, 2010

By:

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67168
---	--

SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
--	---

1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: FEDERAL 10-26-8-15
------------------------------------	---

2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	9. API NUMBER: 43013342160000
--	---

3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext	9. FIELD and POOL or WILDCAT: UNDESIGNATED
--	--	--

4. LOCATION OF WELL FOOTAGES AT SURFACE: 1958 FSL 1443 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSE Section: 26 Township: 08.0S Range: 15.0E Meridian: S	COUNTY: DUCHESNE STATE: UTAH
---	---

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 3/2/2010 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input checked="" type="checkbox"/> APD EXTENSION OTHER:

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Newfield proposes to extend the permit to drill for one more year.

Approved by the Utah Division of Oil, Gas and Mining

Date: March 04, 2010

By:

NAME (PLEASE PRINT) Mandie Crozier	PHONE NUMBER 435 646-4825	TITLE Regulatory Tech
SIGNATURE N/A	DATE 3/4/2010	



The Utah Division of Oil, Gas, and Mining

- State of Utah
- Department of Natural Resources

Electronic Permitting System - Sundry Notices

Request for Permit Extension Validation Well Number 43013342160000

API: 43013342160000

Well Name: FEDERAL 10-26-8-15

Location: 1958 FSL 1443 FEL QTR NWSE SEC 26 TWNP 080S RNG 150E MER S

Company Permit Issued to: NEWFIELD PRODUCTION COMPANY

Date Original Permit Issued: 3/2/2009

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision. Following is a checklist of some items related to the application, which should be verified.

- If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes No
- Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes No
- Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes No
- Have there been any changes to the access route including ownership, or rightof- way, which could affect the proposed location? Yes No
- Has the approved source of water for drilling changed? Yes No
- Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes No
- Is bonding still in place, which covers this proposed well? Yes No

**Approved by the
Utah Division of
Oil, Gas and Mining**

Signature: Mandie Crozier

Date: 3/4/2010

Title: Regulatory Tech **Representing:** NEWFIELD PRODUCTION COMPANY

Date: March 04, 2010

By:

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

5. Lease Serial No.
UTU-67168

6. If Indian, Allottee or Tribe Name
NA

7. If Unit or CA Agreement, Name and No.
~~NA~~ *Greater Mon. Butte*

8. Lease Name and Well No.
Federal 10-26-8-15

9. API Well No.
43-013-34216

1a. Type of work: DRILL REENTER
1b. Type of Well: Oil Well Gas Well Other Single Zone Multiple Zone

2. Name of Operator
Newfield Production Company

3a. Address
Route #3 Box 3630, Myton UT 84052

3b. Phone No. (include area code)
(435) 646-3721

10. Field and Pool, or Exploratory
Monument Butte

4. Location of Well (Report location clearly and in accordance with any State requirements. *)
At surface NW/SE (LOT #3) 1958' FSL 1443' FEL
At proposed prod. zone

11. Sec., T. R. M. or Blk. and Survey or Area
Sec. 26, T8S R15E

14. Distance in miles and direction from nearest town or post office*
Approximately 11.5 miles southwest of Myton, UT

12. County or Parish
Duchesne

13. State
UT

15. Distance from proposed* location to nearest property or lease line, ft. Approx. 533' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)

16. No. of acres in lease
1,285.960

17. Spacing Unit dedicated to this well
40 Acres

18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1035'

19. Proposed Depth
6,385'

20. BLM/BIA Bond No. on file
WYB000493

21. Elevations (Show whether DF, KDB, RT, GL, etc.)
5791' GL

22. Approximate date work will start*
3rd Qtr. 2009

23. Estimated duration
(7) days from SPUD to rig release

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- 1. Well plat certified by a registered surveyor.
- 2. A Drilling Plan.
- 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- 5. Operator certification
- 6. Such other site specific information and/or plans as may be required by the BLM.

25. Signature *Mandie Crozier* Name (Printed/Typed) Mandie Crozier Date *2/20/09*
Title Regulatory Specialist

Approved by (Signature) *James H. Sparger* Name (Printed/Typed) James H. Sparger Date JUN 09 2010
Title ACTING Assistant Field Manager Office VERNAL FIELD OFFICE
Lands & Mineral Resources

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached. **CONDITIONS OF APPROVAL ATTACHED**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

RECEIVED
FEB 25 2009
RECEIVED
JUN 23 2010
BLM VERNAL FIELD OFFICE
DIV. OF OIL, GAS & MINING
NOS 12/04/2008
AFMSS# 09SX30270A

NOTICE OF APPROVAL
UDOGM



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company:	Newfield Production Company	Location:	NWSE (Lot #3), Sec. 26, T8S, R15E
Well No:	Federal 10-26-8-15	Lease No:	UTU-67168
API No:	43-013-34216	Agreement:	Greater Monument Butte Unit

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction
(Notify Environmental Scientist)

- Forty-Eight (48) hours prior to construction of location and access roads.

Location Completion
(Notify Environmental Scientist)

- Prior to moving on the drilling rig.

Spud Notice
(Notify Petroleum Engineer)

- Twenty-Four (24) hours prior to spudding the well.

Casing String & Cementing
(Notify Supv. Petroleum Tech.)

- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: ut_vn_opreport@blm.gov.

BOP & Related Equipment Tests
(Notify Supv. Petroleum Tech.)

- Twenty-Four (24) hours prior to initiating pressure tests.

First Production Notice
(Notify Petroleum Engineer)

- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

**SURFACE USE PROGRAM
 CONDITIONS OF APPROVAL (COAs)**

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.
- Construction and drilling is not allowed from May 1st – June 15th to minimize impacts during Mountain plover nesting.
- If it is anticipated that construction or drilling will occur during the given timing restriction, a BLM or qualified biologist shall be notified so surveys can be conducted. Depending upon the results of the surveys, permission to proceed may or may not be recommended or granted by the BLM biologist.
- Prior to construction, an invasive plants/noxious weeds inventory will be completed for all areas where surface disturbance will occur, and a completed Weed Inventory Form will be submitted to the BLM Authorized Officer.

Reclamation

- Reclamation will be completed in accordance with the Newfield Exploration Company Castle Peak and Eight Mile Flat Reclamation Plan on file with the Vernal Field Office of the BLM.

Seed Mix (Interim and Final Reclamation)

Common name	Latin name	lbs/acre	Recommended seed planting depth
Squirreltail grass	<i>Elymus elymoides</i>	2.0	¼ - ½"
Bluebunch wheatgrass	<i>Pseudoroegneria spicata</i>	1.0	½"
Shadscale saltbush	<i>Atriplex confertifolia</i>	2.0	½"
Four-wing saltbush	<i>Atriplex canescens</i>	3.0	½"
Gardner's saltbush	<i>Atriplex gardneri</i>	1.0	½"
Scarlet globemallow	<i>Sphaeralcea coccinea</i>	1.0	⅛ - ¼"

- All pounds are pure live seed.
- All seed and mulch will be certified weed free.
- Rates are set for drill seeding; double rate if broadcasting.

Monitoring and Reporting

- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) that designates the proposed site-specific monitoring and reference sites chosen for the location. A description of the proposed sites shall be included, as well as a map showing the locations of the proposed sites.
- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) 3 growing seasons after reclamation efforts have occurred evaluating the status of the reclaimed areas in order to determine whether the BLM standards set forth in the Green River District Reclamation Guidelines have been met (30% or greater basal cover).

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Newfield Production Co. shall adhere to all referenced requirements in the SOP (version: June 24, 2008)) along with all Oil and Gas rules and requirements listed in the Code of Federal Regulations and all Federal Onshore Oil and Gas Orders.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4.

Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

Spud
BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross Rig # 29

Submitted By Don Bastian Phone Number 435-823-6012

Well Name/Number Federal 10-26-8-15

Qtr/Qtr NW/SE Section 26 Township 8S Range 15E

Lease Serial Number UTU-67168

API Number 43-013-34216

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 10/8/10 8:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 10/8/10 2:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks Ross Rig #29 Will Spud To The Federal 10-26-8-15 On
10/8/10 @ 8:00 AM. Run 8 5/8" Casing @ 2:00 PM On 10/8/10

Amended Spud
BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross Rig # 29
Submitted By Xabier Lasa Phone Number 435-823-6014
Well Name/Number Federal 10-26-8-15
Qtr/Qtr NW/SE Section 26 Township 8S Range 15E
Lease Serial Number UTU-67168
API Number 43-013-34216

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 10-15-10 8:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 10-15-10 4:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks Spud With Ross Rig #29 At 8:00 AM Run Csg @ 4:00 PM 10/15/10

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
 NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630 3b. Phone (include are code)
 Myton, UT 84052 435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
 1958 FSL 1443 FEL
 NWSE Section 26 T8S R15E

5. Lease Serial No.
 UTU-67168

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or
 GMBU

8. Well Name and No.
 FEDERAL 10-26-8-15

9. API Well No.
 4301334216

10. Field and Pool, or Exploratory Area
 GREATER MB UNIT

11. County or Parish, State
 DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 10/8/10 MIRU Ross #21. Spud well @ 8:00am. Drill 345' of 121/4" hole with air mist. TIH w/8 jt's 85/8" j-55 24# csgn. set @ 347KB On 10/12/10 cement with 170 sks of class "G" w/ 2% Calcium Chloride mixed @ 15.8 ppg > 1.17 cf/sk yeild. Returned 4 bbls cement to pit. Woc.

I hereby certify that the foregoing is true and correct (Printed/Typed)
 Jav Burton
 Signature *Jav E. Burton*

Title
 Drilling Foreman

Date
 10/26/2010

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

RECEIVED
 NOV 01 2010
 DIV. OF OIL, GAS & MINING

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM - FORM 6


OPERATOR: **NEWFIELD PRODUCTION COMPANY**
ADDRESS: **RT. 3 BOX 3630**
MYTON, UT 84052

OPERATOR ACCT. NO. **N2695**

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400 ✓	4301334214	FEDERAL 16-26-8-15	SESE	26	8S	15E	DUCHESNE	10/16/2010	11/10/10
WELL 1 COMMENTS: GRRV											
B	99999	17400 ✓	4301334216	FEDERAL 10-26-8-15	NWSE	26	8S	15E	DUCHESNE	10/15/2010	11/10/10
WELL 2 COMMENTS: GRRV											
B	99999	17400 ✓	4301334217	FEDERAL 15-26-8-15	SWSE	26	8S	15E	DUCHESNE	10/15/2010	11/10/10
WELL 3 COMMENTS: GRRV											
B	99999	17400 ✓	4301350189	WELLS DRW FED L-5-9-16	SENW	5	9S	16E	DUCHESNE	10/16/2010	11/10/10
WELL 4 COMMENTS: GRRV SENE BHL = NESE											
A	99999	17855 ✓	4301350378	UTE TRIBAL 11-14-4-3	NESW	14	4S	3W	DUCHESNE	10/14/2010	11/10/10
WELL 5 COMMENTS: GRRV											
B	99999	17400 ✓	4301350197	HAWKEYE FED N-26-8-16	NWSW	26	8S	16E	DUCHESNE	10/25/2010	11/10/10
WELL 6 COMMENTS: GRRV BHL = NWSW											

- ACTION CODES (See instructions on back of form)
- A - new entity for new well (single well only)
 - B - well to existing entity (group or unit well)
 - C - from one existing entity to another existing entity
 - D - well from one existing entity to a new entity
 - E - other (explain in comments section)

RECEIVED
NOV 08 2010

Signature 
Production Clerk **Jentri Park**
10/26/10

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
UTU-67168

SUNDRY NOTICES AND REPORTS ON WELLS

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

7. UNIT or CA AGREEMENT NAME:
GMBU

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

8. WELL NAME and NUMBER:
FEDERAL 10-26-8-15

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:
4301334216

3. ADDRESS OF OPERATOR:
Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

10. FIELD AND POOL, OR WILDCAT:
GREATER MB UNIT

4. LOCATION OF WELL:
FOOTAGES AT SURFACE: 1958 FSL 1443 FEL
OTR/OTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: NWSE, 26, T8S, R15E

COUNTY: DUCHESNE
STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 11/19/2010	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
The above subject well was completed on 11-19-10, attached is a daily completion status report.

NAME (PLEASE PRINT) Lucy Chavez-Naupoto TITLE Administrative Assistant
SIGNATURE  DATE 11/22/2010

(This space for State use only)

RECEIVED
NOV 23 2010
DIV. OF OIL, GAS & MINING

Daily Activity Report

Format For Sundry

FEDERAL 10-26-8-15**9/1/2010 To 1/30/2011****11/10/2010 Day: 1****Completion**

Rigless on 11/10/2010 - Ran CBL & perforated 1st stage. SIWFN w/ 151 BWTR. - NU frac head & Cameron BOP's. RU Hot oiler & test casing, frac head, frac valves & BOP to 4500 psi. RU WLT w/ mast & pack off tool. Run CBL under pressure. WLTD was 6279' w/ TOC @ 220'. RIH w/ 3 1/8" ported guns & perforate CP3 sds @ 6003- 09' & CP2 sds @ 5965- 70' w/ (11 gram, .36"EH, 16.82z pen. 120°) 3 spf for total of 33 shots. RD WLT & Hot Oiler. SIWFN w/ 151 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$14,784**11/15/2010 Day: 2****Completion**

Rigless on 11/15/2010 - Frac well. Flow well back. - Stage #2: RU Perforators LLC WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" (6K) composite flow through frac plug & perf guns. Set plug @ 5925'. Perferate CP1 sds w/ 3-1/8" Port Guns (11 gram, .36"EH, 120°, 16.82"pen) w/ 3 spf for total of 21 shots. RU BJ & open well w/ 2072 psi on casing. Perfs broke down @ 2757 psi back to 2741 psi w/ 5 bbls @ 4 bpm. Pump 30 gals of Techni Hib chemical @ 4% by volume. Frac w/ 45,225#'s of sand in 468 bbls of Lightning 17 frac fluid. Treated @ ave pressure of 2806 w/ ave rate of 27 bpm w/ 8 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 2504 w/ .86FG. 5 min was 2250. 10 min was 2194. 15 min was 2160. Leave pressure on well. 1023 bbls EWTR. - Stage #3: RU Perforators LLC WLT, crane & lubricator. RIH w/ frac plug & perf guns. Set plug @ 5560'. Perferate A3 sds w/ 3 spf for total of 21 shots. RU BJ & open well w/ 2146 psi on casing. Perfs broke down @ 3516 psi back to 2357 psi w/ 4 bbls @ 4 bpm. Pump 30 gals of Techni Hib chemical @ 4% by volume. Frac w/ 44,804#'s of sand in 471 bbls of Lightning 17 frac fluid. Treated @ ave pressure of 2652 w/ ave 27 rate of bpm w/ 8 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 2454 w/ .88FG. 5 min was 2270. 10 min was 2155. 15 min was 2075. Leave pressure on well. 1494 bbls EWTR. - Stage #1: RU BJ Services "Ram Head" frac flange. RU BJ & open well w/ 70 psi on casing. Perfs broke down @ 2353 psi back to 2168 psi w/ 3 bbls @ 3 bpm. ISIP was 2037 w/ .77FG. 1 min was 1900. 4 min was 1781. Pump 6 bbls of 15% HCL acid (rec'd 300 psi drop when hit perfs). Pump 30 gals of Techni Hib chemical @ 4% by volume. Frac w/ 24,371#'s of sand in 404 bbls of Lightning 17 frac fluid. Treated @ ave pressure of 2449 w/ ave rate of 27 bpm w/ 6 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 2240 w/ .81FG. 5 min was 2118. 10 min was 2082. 15 min was 2062. Leave pressure on well. 555 bbls EWTR. - Stage #4: RU WLT. RIH w/ frac plug & perf guns. Set plug @ 4460'. Perferate GB4 sds w/ 3 spf for total of 12 shots. RU BJ & open well w/ 1965 psi on casing. Perfs broke down @ 2206 psi back to 2198 psi w/ 3 bbls @ 4 bpm. Pump 30 gals of Techni Hib chemical @ 4% by volume. Frac w/ 14,742#'s of sand in 267 bbls of Lightning 17 frac fluid. Treated @ ave pressure of 3085 w/ ave rate of 24 bpm w/ 6 ppg of sand. ISIP was 2187 w/ .94FG. 5 min was 1966. 10 min was 1935. 15 min was 1894. 1761 bbls EWTR. RD BJ & WLT. Flow well back. Well flowed for 2 hours & died. SIFN w/ 1561 bbls EWTR.

Daily Cost: \$0**Cumulative Cost:** \$81,858**11/17/2010 Day: 3****Completion**

WWS #3 on 11/17/2010 - MIRUSU. RU BOP's. TIH w/ tbg. - MIRUSU. Open well w/ 100 psi on casing. RD Cameron BOP's & frac head. Instal 3M production tbg head & Schefer BOP's. RU 4-3/4" Chomp mill & x-over sub. Tally, drift, pickup & TIH w/ new J-55, 2-7/8", 6.5#, 8EUE tbg to tag fill @ 4366' (94' of fill). RU pump & tanks. C/O sand to plug @ 4460'. TIH w/ tbg to tag fill @ 5525' (35' of fill). C/O to plug #2 @ 5560' & drlg out. Leave EOT @ 5580'. SIFN. 1500 bbls EWTR.

Daily Cost: \$0

Cumulative Cost: \$127,590

11/18/2010 Day: 4

Completion

WWS #3 on 11/18/2010 - Continue drlg plugs. C/O to PBSD. Swab well for cleanout. TOOH w/ tbg. - Open well w/ 200 psi on casing. TIH w/ tbg to tag plug @ 5925'. Drlg out plug #3. TIH w/ tbg to tag fill @ 6258' (85'). C/O to PBSD @ 6343'. LD 2 jts tbg. RU swab equipment. Made 11 runs to rec'd 140 bbls fluid. FFL was 1100' w/ last run showing trace of oil w/ no sand. TIH w/ tbg to tag 20' new sand. Circulate well clean. TOOH w/ 60 jts tbg. SIFN. 1375 bbls EWTR.

Daily Cost: \$0

Cumulative Cost: \$134,074

11/19/2010 Day: 5

Completion

WWS #3 on 11/19/2010 - Continue TOOH w/ tbg. TIH w/ production. Put well on pump. Final Report. - Open well w/ 50 psi on casing. TOOH w/ tbg. LD mill & x-over sub. TIH w/ NC, 2 jts tbg, SN, 1 jt tbg, TA new Cntrl Hydrlic w/ 45,000# shear, 191 jts tbg, RD BOP's. Set TA @ 5995' w/ 18,000#'s tension w/ SN @ 6031' & EOT @ 6095'. Flush tbg w/ 60 bbls water. Pick-up & prime pump. TIH w/ new Cntrl Hydrlic 2-1/2" x 1-1/2" x 16' x 20' RHAC pump w/ 183"SL, 6- 1/1/2" weight rods, 20- 3/4" guided rods, 66- 3/4" plain rods. 48- 3/4" guided rods, 99- 7/8" guided rods, 2', 4', 8' x 7/8" pony rods, 1-1/2" x 26' polish rod. Space pump. Test tbg & pump to 800 psi. RDMOSU. POP @ 4PM w/ 120"SL @ 4 spm w/ 1375 bbls EWTR. Final Report.

Finalized

Daily Cost: \$0

Cumulative Cost: \$176,786

Pertinent Files: Go to File List

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
UTU-67168

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.
GMBU

8. Lease Name and Well No.
FEDERAL 10-26-8-15

9. AFI Well No.
43-013-34216

10. Field and Pool or Exploratory
GREATER MB UNIT

11. Sec., T., R., M., on Block and Survey or Area
SEC. 26, T8S, R15E

12. County or Parish
DUCHESNE

13. State
UT

14. Date Spudded
10/08/2010

15. Date T.D. Reached
10/30/2010

16. Date Completed 11/19/2010
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5791' GL 5803' KB

18. Total Depth: MD 6400' TVD

19. Plug Back T.D.: MD 6279' TVD

20. Depth Bridge Plug Set: MD TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

3. Address
1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
(435)646-3721

4. Location of Well (Report location clearly and in accordance with Federal requirements)*
At surface 1958' FSL & 1443' FEL (NW/SE) (LOT 3) SEC. 26, T8S, R15E
At top prod. interval reported below
At total depth 6400'

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sks. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	347'		170 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	6388'		300 PRIMLITE		220'	
						400 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 6096'	TA @ 5997'						

25. Producing Intervals

Formation	Top	Bottom	Perforation Interval	Size	No. Holes	Perf. Status
A) Green River	4348'	6009'	4348-6009'	.36"	87	
B)						
C)						
D)						

26. Perforation Record

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
4348-6009'	Frac w/ 129,142#s 20/40 sand in 656 bbls of Lightning 17 fluid in 4 stages

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
11/20/10	12/03/10	24	→	22	144	8.33			2-1/2" x 1-3/4" x 16' x 20' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

RECEIVED

DEC 09 2010

DIV. OF OIL, GAS & MINING

*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD & USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
GREEN RIVER	4348'	6009'		GARDEN GULCH MRK	3833'
				GARDEN GULCH 1	4068'
				GARDEN GULCH 2	4188'
				POINT 3	4472'
				X MRKR	4732'
				Y MRKR	4767'
DOUGALS CREEK MRK				BI CARBONATE MRK	4885'
					5144'
B LIMESTON MRK				CASTLE PEAK	5268'
					5797'
BASAL CARBONATE				WASATCH	6215'
					6346'

32. Additional remarks (include plugging procedure):


33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Lucy Chavez-Naupoto

Title Administrative Assistant

Signature 

Date 12/06/2010

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Daily Activity Report

Format For Sundry

FEDERAL 10-26-8-15**8/1/2010 To 12/30/2010****FEDERAL 10-26-8-15****Waiting on Cement****Date:** 10/26/2010

Ross #21 at 345. Days Since Spud - Ross # 21 spud @ 8:00am on 10/8/10. Drilled 345' of 12.25" hole. Then ran 8jts of 8 5/8 casing set @ - returned to pit. - 347'KB. Cemented on 10/12/10 w/BJ 170skts of G+2% Calcium Chloride+.25#/skCELLOFLAKE 4bbls

Daily Cost: \$0**Cumulative Cost:** \$60,037**FEDERAL 10-26-8-15****Drill 7 7/8" hole with fresh water****Date:** 10/27/2010

NDSI #3 at 1998. 1 Days Since Spud - PU BHA/Tag cmt @ 290' - 1500 psi for 30 min. - RU Quick test & test kelly, safety valve, pipe & blind rams, & choke to 2000 psi for 10 min./Csg. To - On 10/26/10 Jones trucking moved rig # 3 from Ute Tribal 16-21-4-2w to Fed. 10-26-8-15/Set equip. - Install rotating head rubber & drive bushing - Drill 7 7/8" hole from 1052' to 1998'/WOB 20/RPM 60/GPM 420/ROP 135 FPH - No slides - Drill 7 7/8" hole from 290' to 1052'/WOB 20/RPM 60/GPM 420/ROP 138.5FPH

Daily Cost: \$0**Cumulative Cost:** \$99,219**FEDERAL 10-26-8-15****Drill 7 7/8" hole with fresh water****Date:** 10/28/2010

NDSI #3 at 4235. 2 Days Since Spud - Drill 7 7/8" hole from 1998' to 3008'/WOB 20/RPM 60/GPM 420/ROP 119 FPH - Rig service/Function test BOP's & Crown-O-Matic/OK - Drill 7 7/8" hole from 3008' to 4235'/WOB 20/RPM 50/GPM 420/ROP 67FPH - No slides

Daily Cost: \$0**Cumulative Cost:** \$133,476**FEDERAL 10-26-8-15****Drill 7 7/8" hole with fresh water****Date:** 10/29/2010

NDSI #3 at 6189. 3 Days Since Spud - Drill 7 7/8" hole from 4487' to 6189'/WOB 20/RPM 50/GPM 420/ROP 97FPH - 401K Mandatory meeting - Drill 7 7/8" hole from 4487' to 4708'/WOB 20/RPM 50/GPM 420/ROP 88FPH - Rig service/Function test BOP's & Crown-O-Matic/OK - Drill 7 7/8" hole from 4235' to 4487'/WOB 20/RPM 50/GPM 420/ROP 84FPH - No Slides

Daily Cost: \$0**Cumulative Cost:** \$177,403**FEDERAL 10-26-8-15****Rigging down****Date:** 10/30/2010

NDSI #3 at 6400. 4 Days Since Spud - RU QT & repair power tongs/Change to csg. Rams & Test to 2000 psi/ok - Run 152 jts 5.5" J55 15.5# Csg. /Tag @ 6404'/Land Csg. @ 6387.76' - Circ with rig pump & RU BJ - Cmt Csg. With 300 sks PLI+ additives/400 sks 50:50:2+ additives/20 bbl cmt to pit - ND BOP's & set Csg slips with 110,000# tension. - Clean mud tanks - Clean mud tanks - Release rig @ 7:30 AM 10/30/10 - Surface Csg./Loggers TD 6410' - RU PSI & Log well/Run Gamma Ray, Compensated Neutron, Compensated Density & Dual Guard from TD to - Finish LDDP & BHA with Dir. Tools - Pump 320 bbls of 10# brine - LDDP to

3500' - Circ & cond. For logs - Drill 7 7/8" hole from 6189' to 6400'/WOB 20/RPM 50/GPM 420/ROP 105FPH/ T.D. - Release rig @ 7:30 AM 10/30/10 - Clean mud tanks - Clean mud tanks - ND BOP's & set Csg slips with 110,000# tension. - Cmt Csg. With 300 sks PLII+ additives/400 sks 50:50:2+ additives/20 bbl cmt to pit - Circ with rig pump & RU BJ - Run 152 jts 5.5" J55 15.5# Csg. /Tag @ 6404'/Land Csg. @ 6387.76' - RU QT & repair power tongs/Change to csg. Rams & Test to 2000 psi/ok - Surface Csg./Loggers TD 6410' - RU PSI & Log well/Run Gamma Ray,Compensated Neutron,Compensated Density & Dual Guard from TD to - Finish LDDP & BHA with Dir. Tools - Pump 320 bbls of 10# brine - LDDP to 3500' - Drill 7 7/8" hole from 6189' to 6400'/WOB 20/RPM 50/GPM 420/ROP 105FPH/ T.D. - Circ & cond. For logs **Finalized**

Daily Cost: \$0

Cumulative Cost: \$322,217

Pertinent Files: Go to File List
