

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL				1. WELL NAME and NUMBER Hawkeye Federal 13-23-8-16		
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>				3. FIELD OR WILDCAT MONUMENT BUTTE		
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO				5. UNIT or COMMUNITIZATION AGREEMENT NAME HAWKEYE (GRRV)		
6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY				7. OPERATOR PHONE 435 646-4825		
8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052				9. OPERATOR E-MAIL mcrozier@newfield.com		
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU-73088		11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>		12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>		
13. NAME OF SURFACE OWNER (if box 12 = 'fee')				14. SURFACE OWNER PHONE (if box 12 = 'fee')		
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')				16. SURFACE OWNER E-MAIL (if box 12 = 'fee')		
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')		18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>		19. SLANT VERTICAL <input checked="" type="checkbox"/> DIRECTIONAL <input type="checkbox"/> HORIZONTAL <input type="checkbox"/>		
20. LOCATION OF WELL	FOOTAGES	QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN
LOCATION AT SURFACE	359 FSL 730 FWL	SWSW	23	8.0 S	16.0 E	S
Top of Uppermost Producing Zone	359 FSL 730 FWL	SWSW	23	8.0 S	16.0 E	S
At Total Depth	359 FSL 730 FWL	SWSW	23	8.0 S	16.0 E	S
21. COUNTY DUCHESNE		22. DISTANCE TO NEAREST LEASE LINE (Feet) 1910		23. NUMBER OF ACRES IN DRILLING UNIT 40		
		25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 1800		26. PROPOSED DEPTH MD: 6695 TVD: 6695		
27. ELEVATION - GROUND LEVEL 5513		28. BOND NUMBER WYB000493		29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 43-7478		

ATTACHMENTS

VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES

<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER	<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)	<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER
<input type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)	<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP

NAME Mandie Crozier	TITLE Regulatory Tech	PHONE 435 646-4825
SIGNATURE	DATE 09/04/2009	EMAIL mcrozier@newfield.com
API NUMBER ASSIGNED 43013501320000	APPROVAL  Permit Manager	

Proposed Hole, Casing, and Cement

String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Prod	7.875	5.5	0	6695		
Pipe	Grade	Length	Weight			
	Grade J-55 LT&C	6695	15.5			


Proposed Hole, Casing, and Cement

String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Surf	12.25	8.625	0	300		
Pipe	Grade	Length	Weight			
	Grade J-55 ST&C	300	24.0			



T8S, R16E, S.L.B.&M.

NEWFIELD PRODUCTION COMPANY

WELL LOCATION, HAWKEYE 13-23-8-16,
 LOCATED AS SHOWN IN THE SW 1/4 SW
 1/4 OF SECTION 23, T8S, R16E,
 S.L.B.&M. DUCHESNE COUNTY, UTAH.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
 PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
 MADE BY ME OR UNDER MY SUPERVISION AND THAT
 THE SAME ARE TRUE AND CORRECT TO THE BEST OF
 MY KNOWLEDGE AND BELIEF. No. 189377

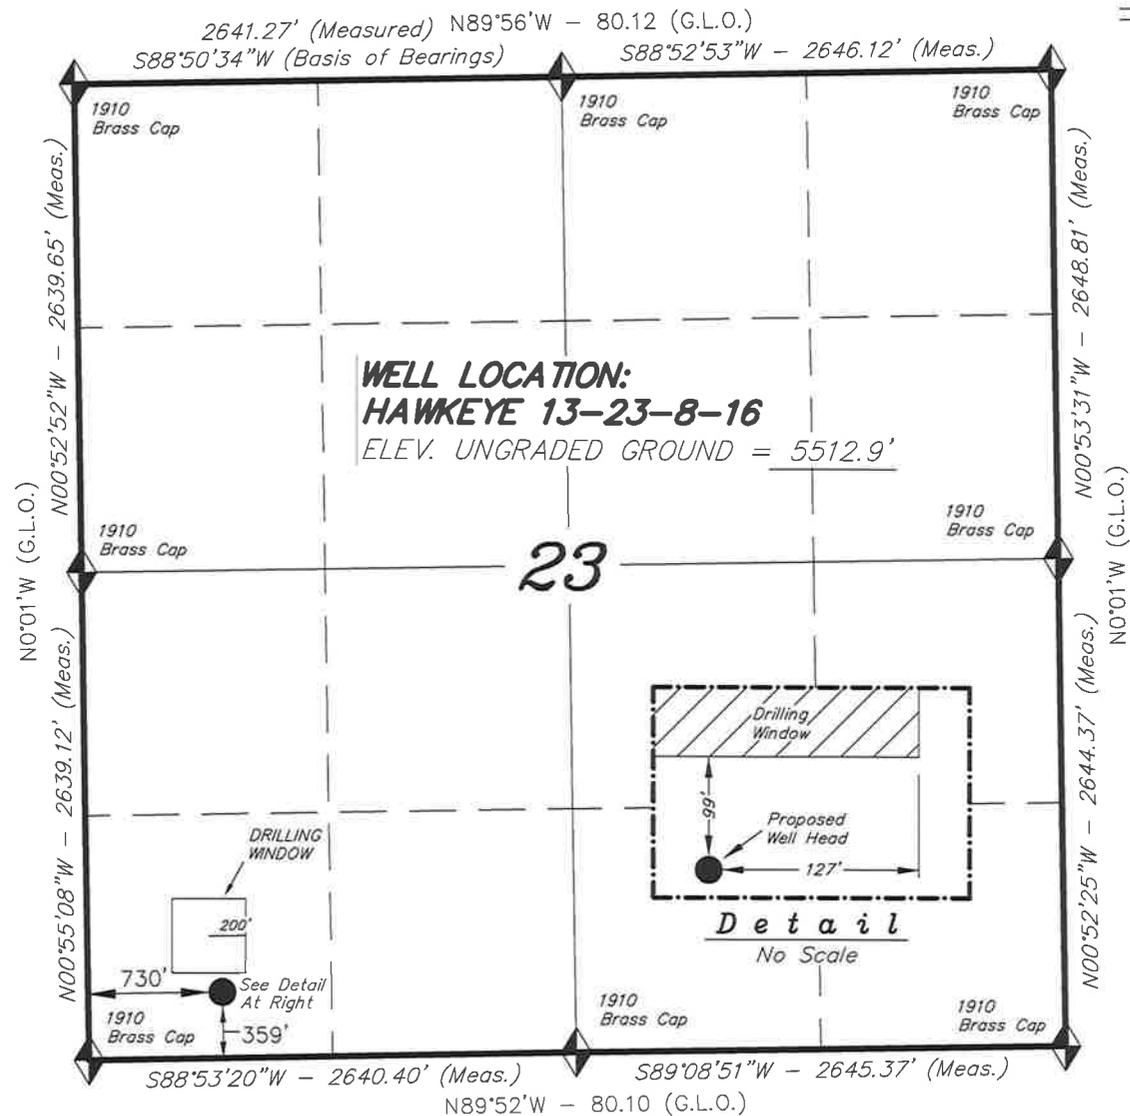

◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are base on
 an N.G.S. OPUS Correction. LOCATION:
 LAT. 40°04'09.56" LONG. 110°00'43.28"
 Elev. 5281.57' (Tristate Aluminum Cap)

HAWKEYE 13-23-8-16
 (Surface Location) NAD 83
 LATITUDE = 40° 05' 49.91"
 LONGITUDE = 110° 05' 36.66"

TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
 (435) 781-2501

DATE SURVEYED: 02-10-09	SURVEYED BY: T.H.
DATE DRAWN: 02-18-09	DRAWN BY: F.T.M.
REVISED: 03-31-09	SCALE: 1" = 1000'

NEWFIELD PRODUCTION COMPANY
HAWKEYE FEDERAL 13-23-8-16
SW/SW SECTION 23, T8S, R16E
DUCHESNE COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0 – 1,900'
Green River	1,900'
Wasatch	6,695'

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil) 1,900' – 6,695'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sampled Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO ₃) (mg/l)
Dissolved Bicarbonate (NaHCO ₃) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO ₄) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: Hawkeye Federal 13-23-8-16**

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950	1,370	244,000
						17.53	14.35	33.89
Prod casing 5-1/2"	0'	6,695'	15.5	J-55	LTC	4,810	4,040	217,000
						2.26	1.90	2.09

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg
 Pore pressure at surface casing shoe = 8.33 ppg
 Pore pressure at prod casing shoe = 8.33 ppg
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: Hawkeye Federal 13-23-8-16**

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft ³ /sk)
			ft ³			
Surface casing	300'	Class G w/ 2% CaCl	138	30%	15.8	1.17
			161			
Prod casing Lead	4,695'	Prem Lite II w/ 10% gel + 3% KCl	324	30%	11.0	3.26
			1058			
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363	30%	14.3	1.24
			451			

- * Actual volume pumped will be 15% over the caliper log
- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ±350 feet will be drilled with an air/mist system. The air rig is equipped with a 6 ½" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ±350 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated

bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.

10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the first quarter of 2010, and take approximately seven (7) days from spud to rig release.

2-M SYSTEM

Blowout Prevention Equipment Systems


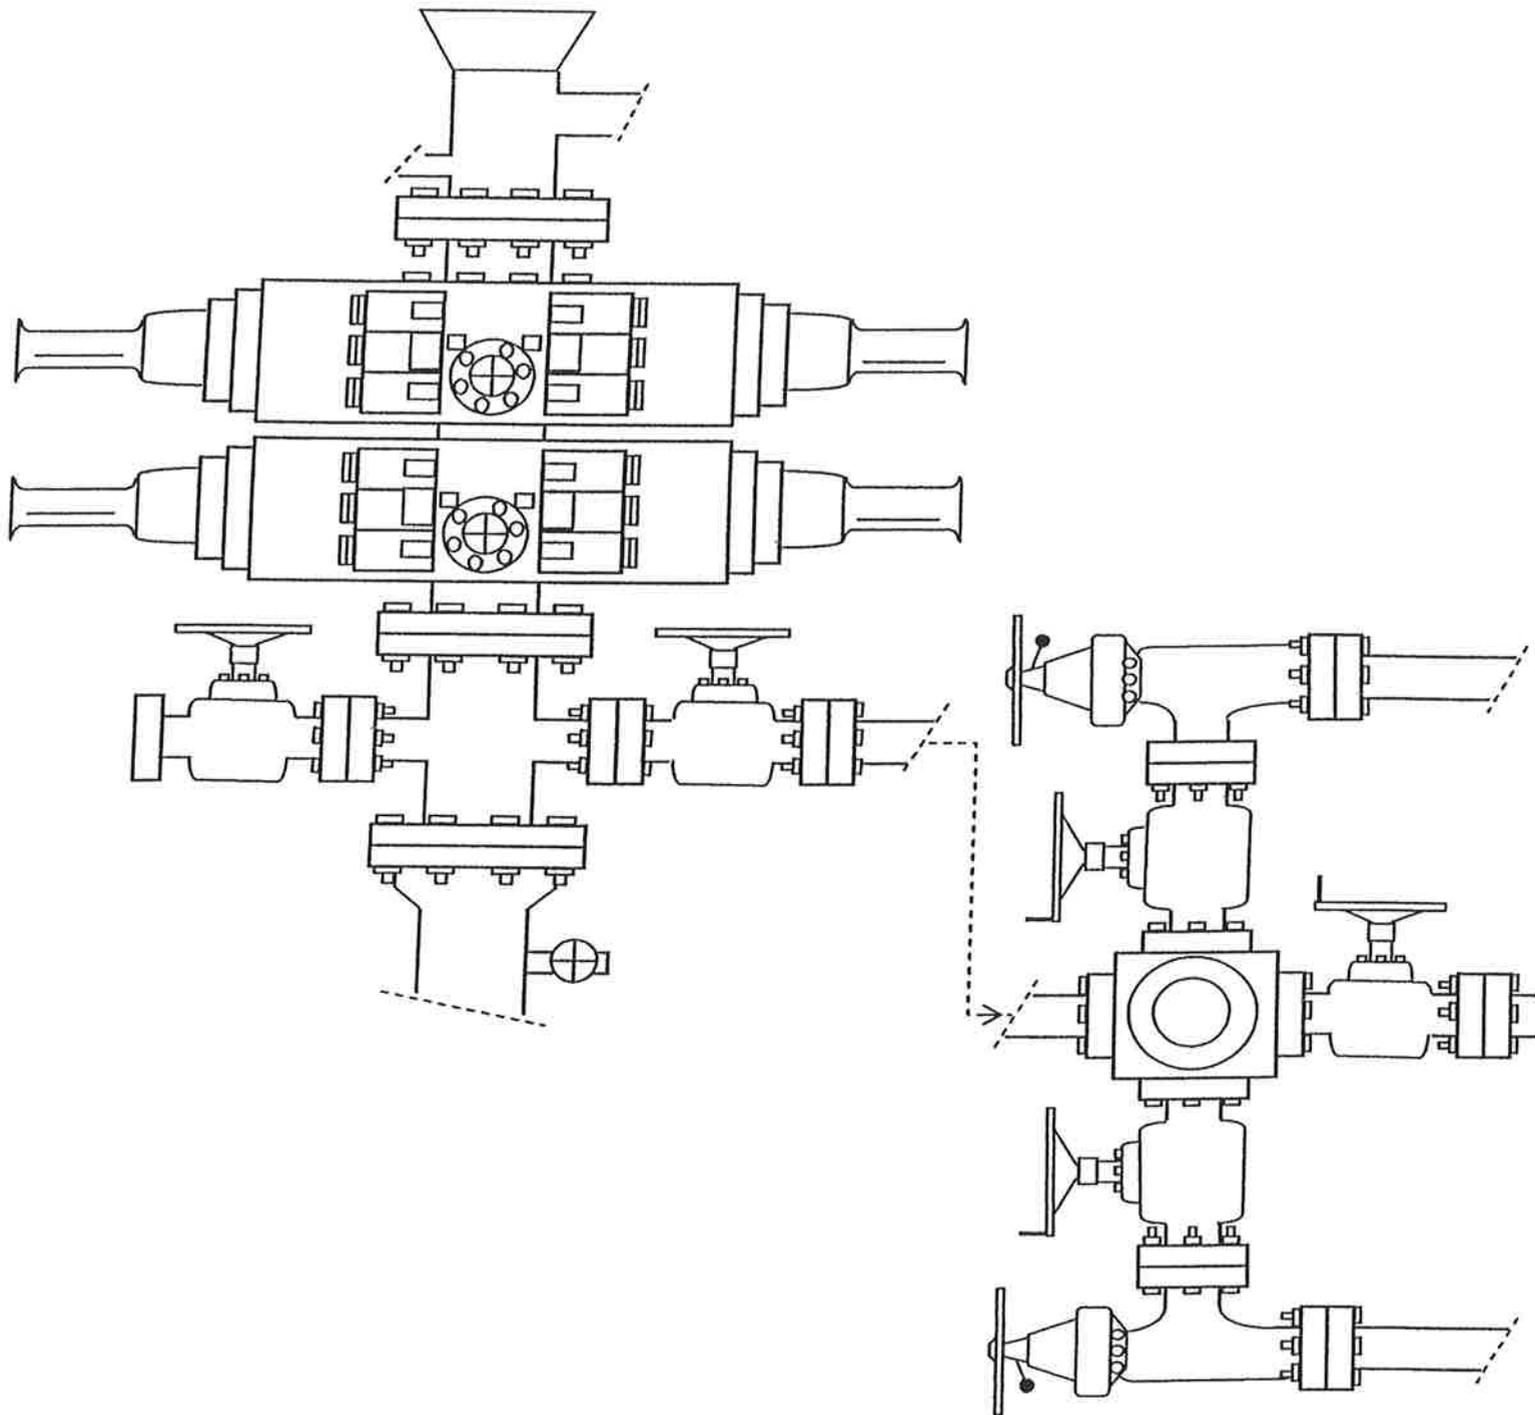


EXHIBIT C

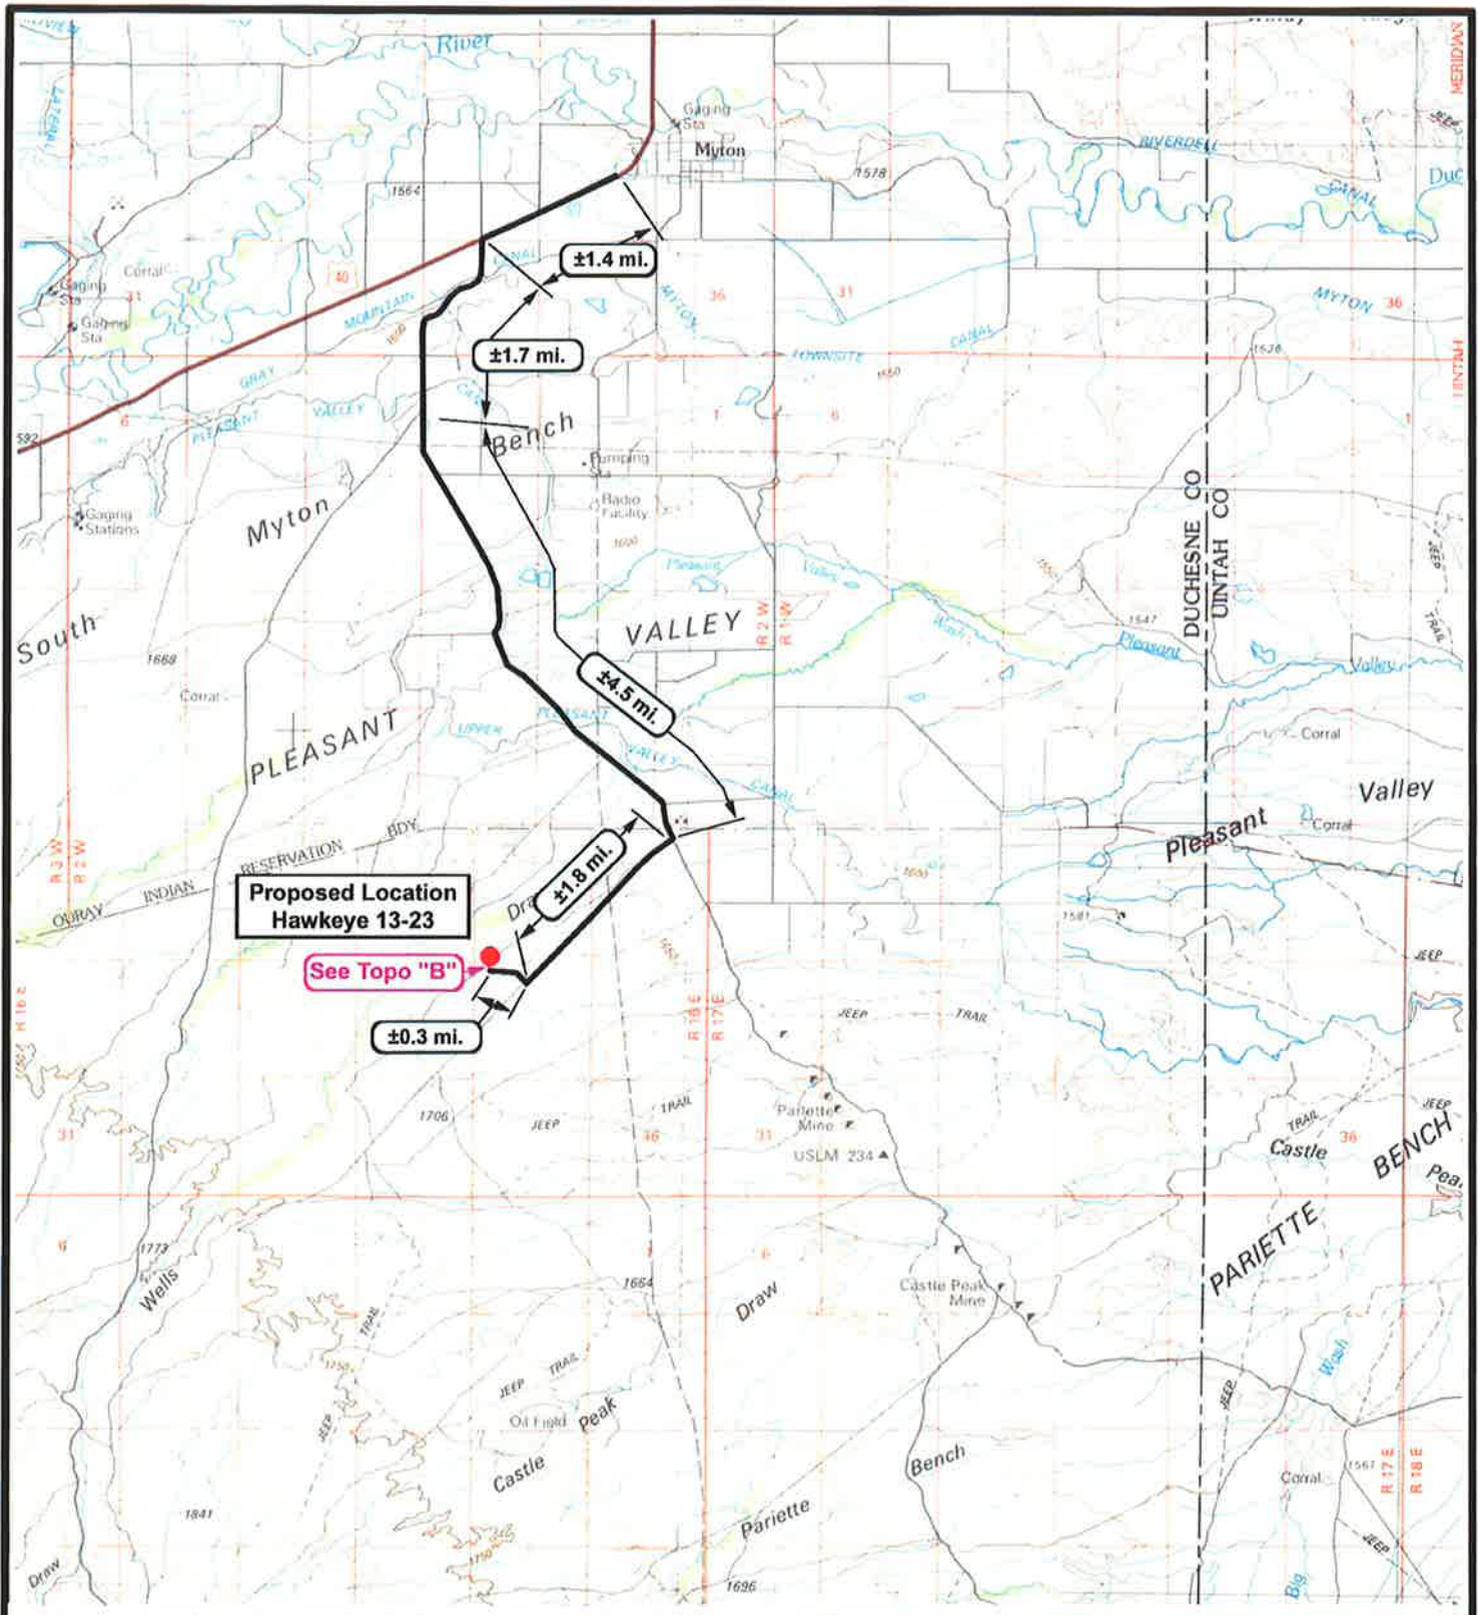

 **NEWFIELD**
Exploration Company

Hawkeye 13-23-8-16
SEC. 23, T8S, R16E, S.L.B.&M.

 **Tri-State**
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1 = 100,000
DRAWN BY: JAS
DATE: 03-31-2009

Legend

-  Existing Road
-  Proposed Access

TOPOGRAPHIC MAP

"A"

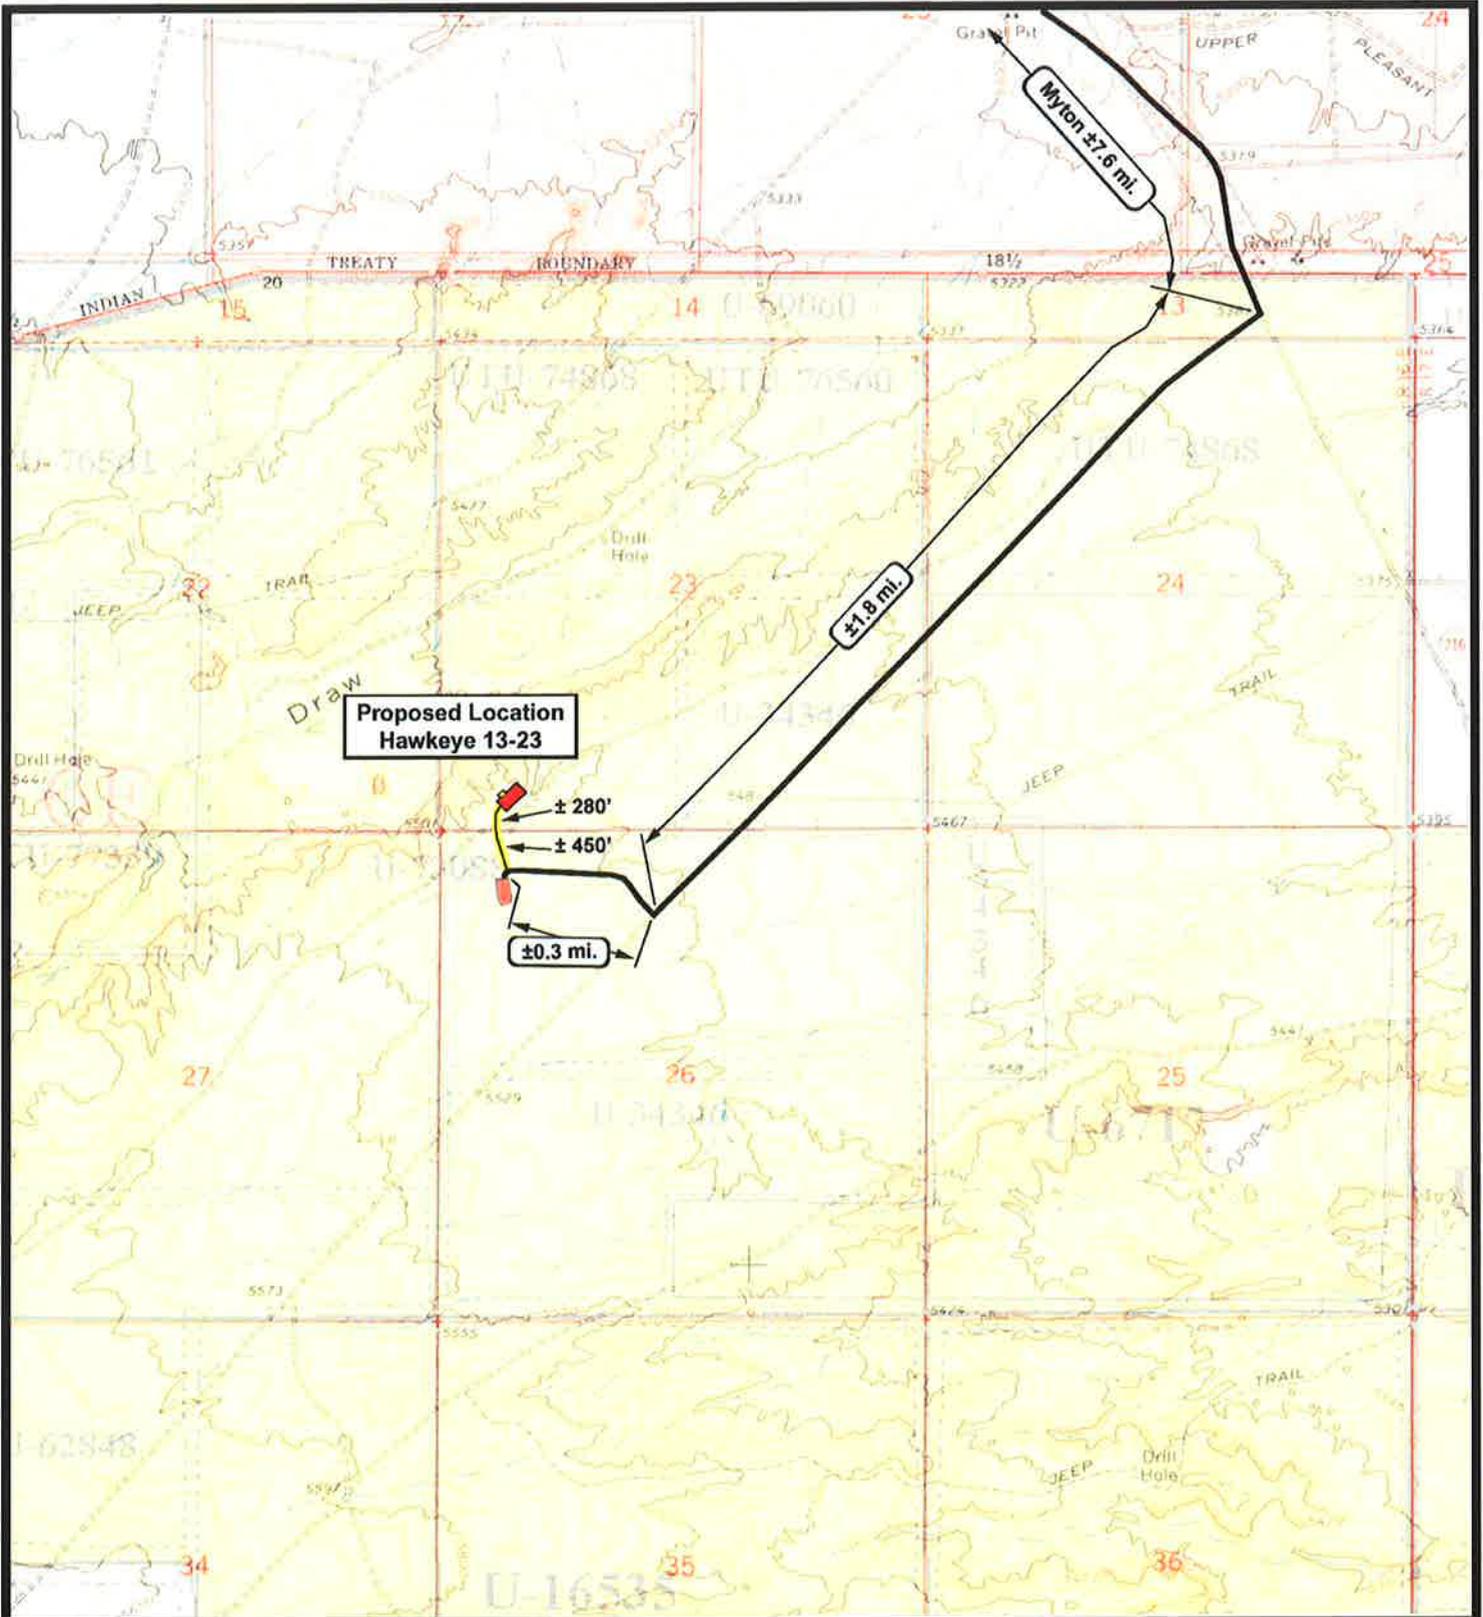

 **NEWFIELD**
Exploration Company

Hawkeye 13-23-8-16
SEC. 23, T8S, R16E, S.L.B.&M.

 **Tri-State**
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'
DRAWN BY: JAS
DATE: 03-31-2009

Legend

-  Existing Road
-  Proposed Access

TOPOGRAPHIC MAP

"B"

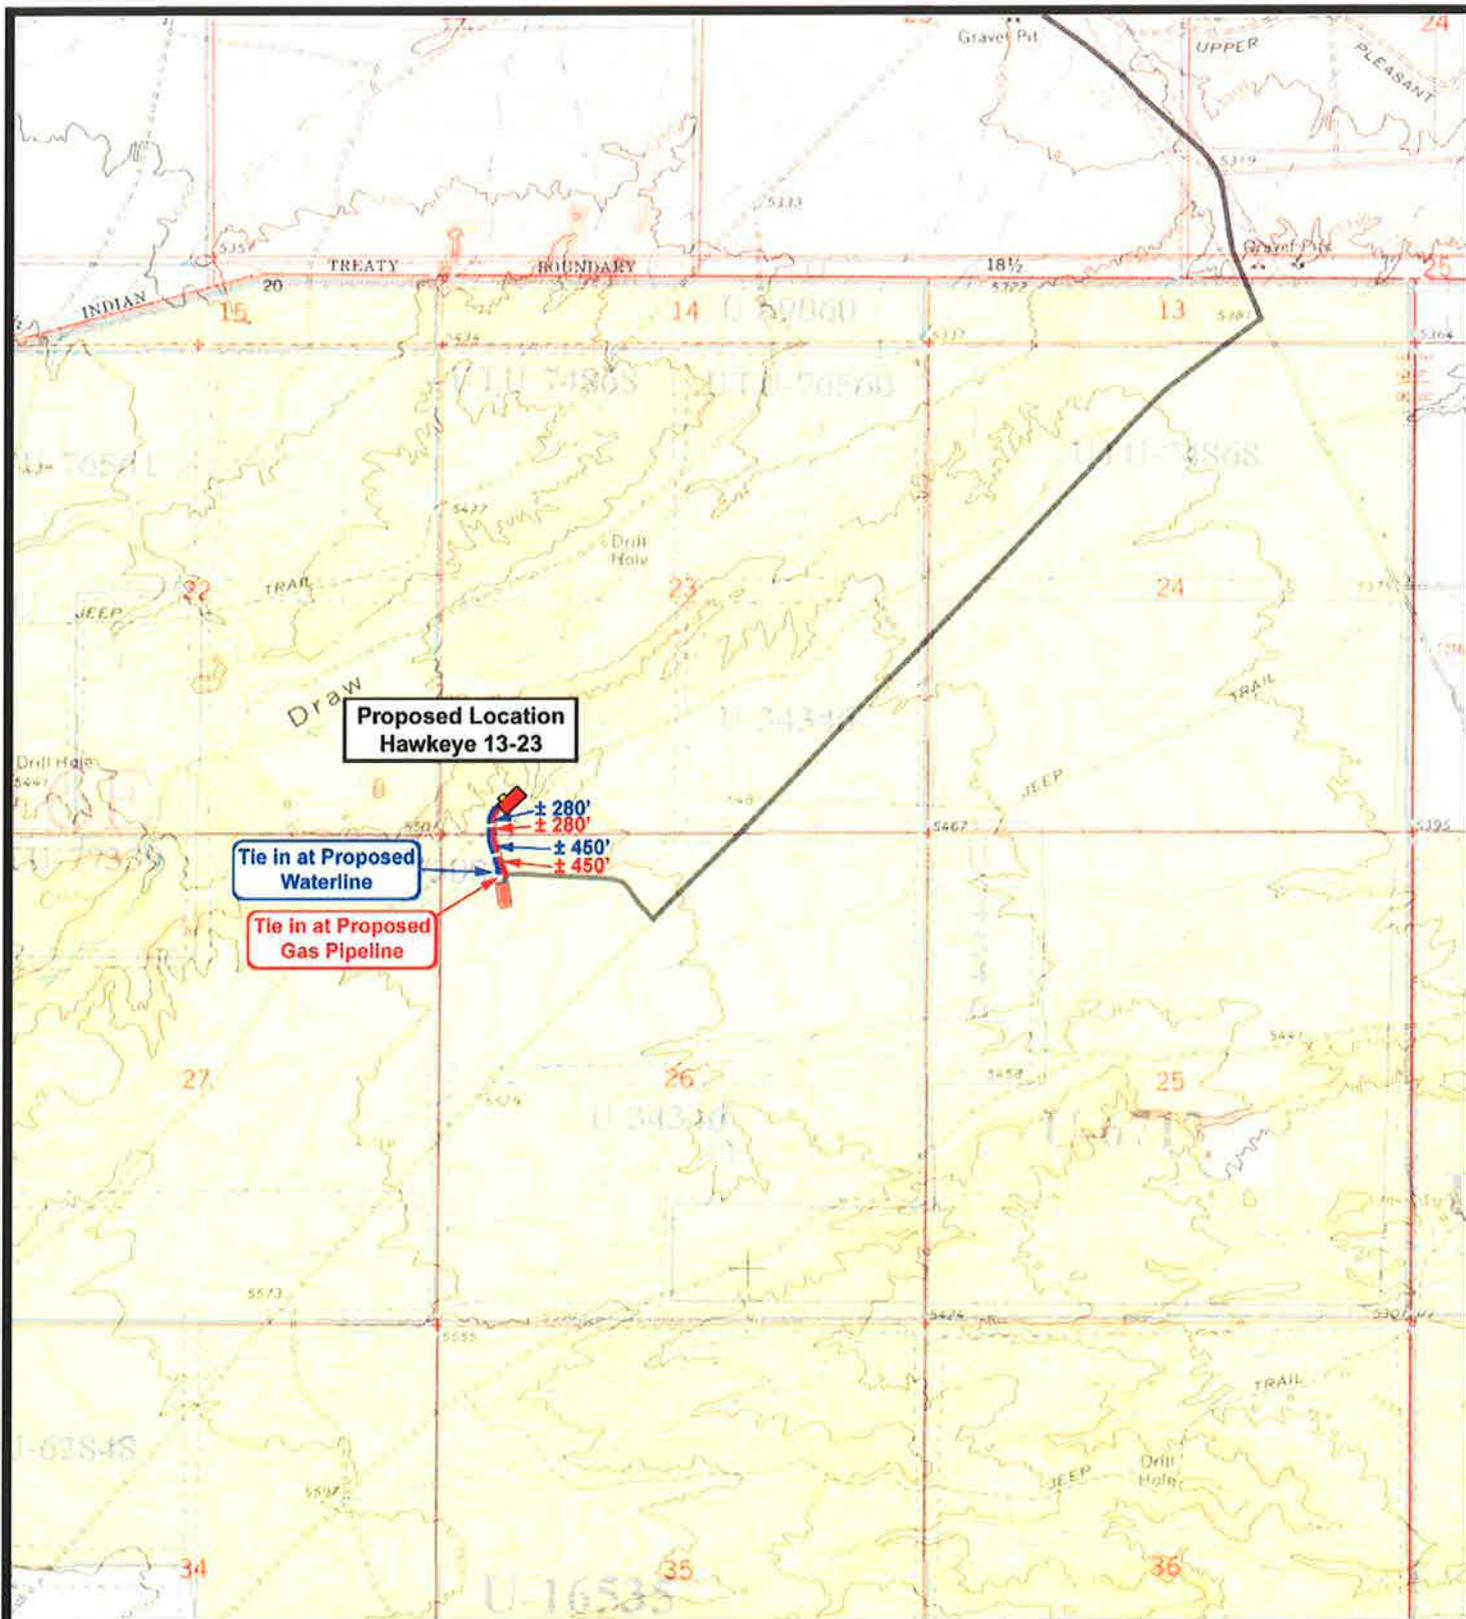

 **NEWFIELD**
Exploration Company

Hawkeye 13-23-8-16
SEC. 23, T8S, R16E, S.L.B.&M.




 **Tri-State**
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'
DRAWN BY: JAS
DATE: 03-31-2009

Legend

-  Roads
-  Proposed Gas Line
-  Proposed Water Line

TOPOGRAPHIC MAP
"C"

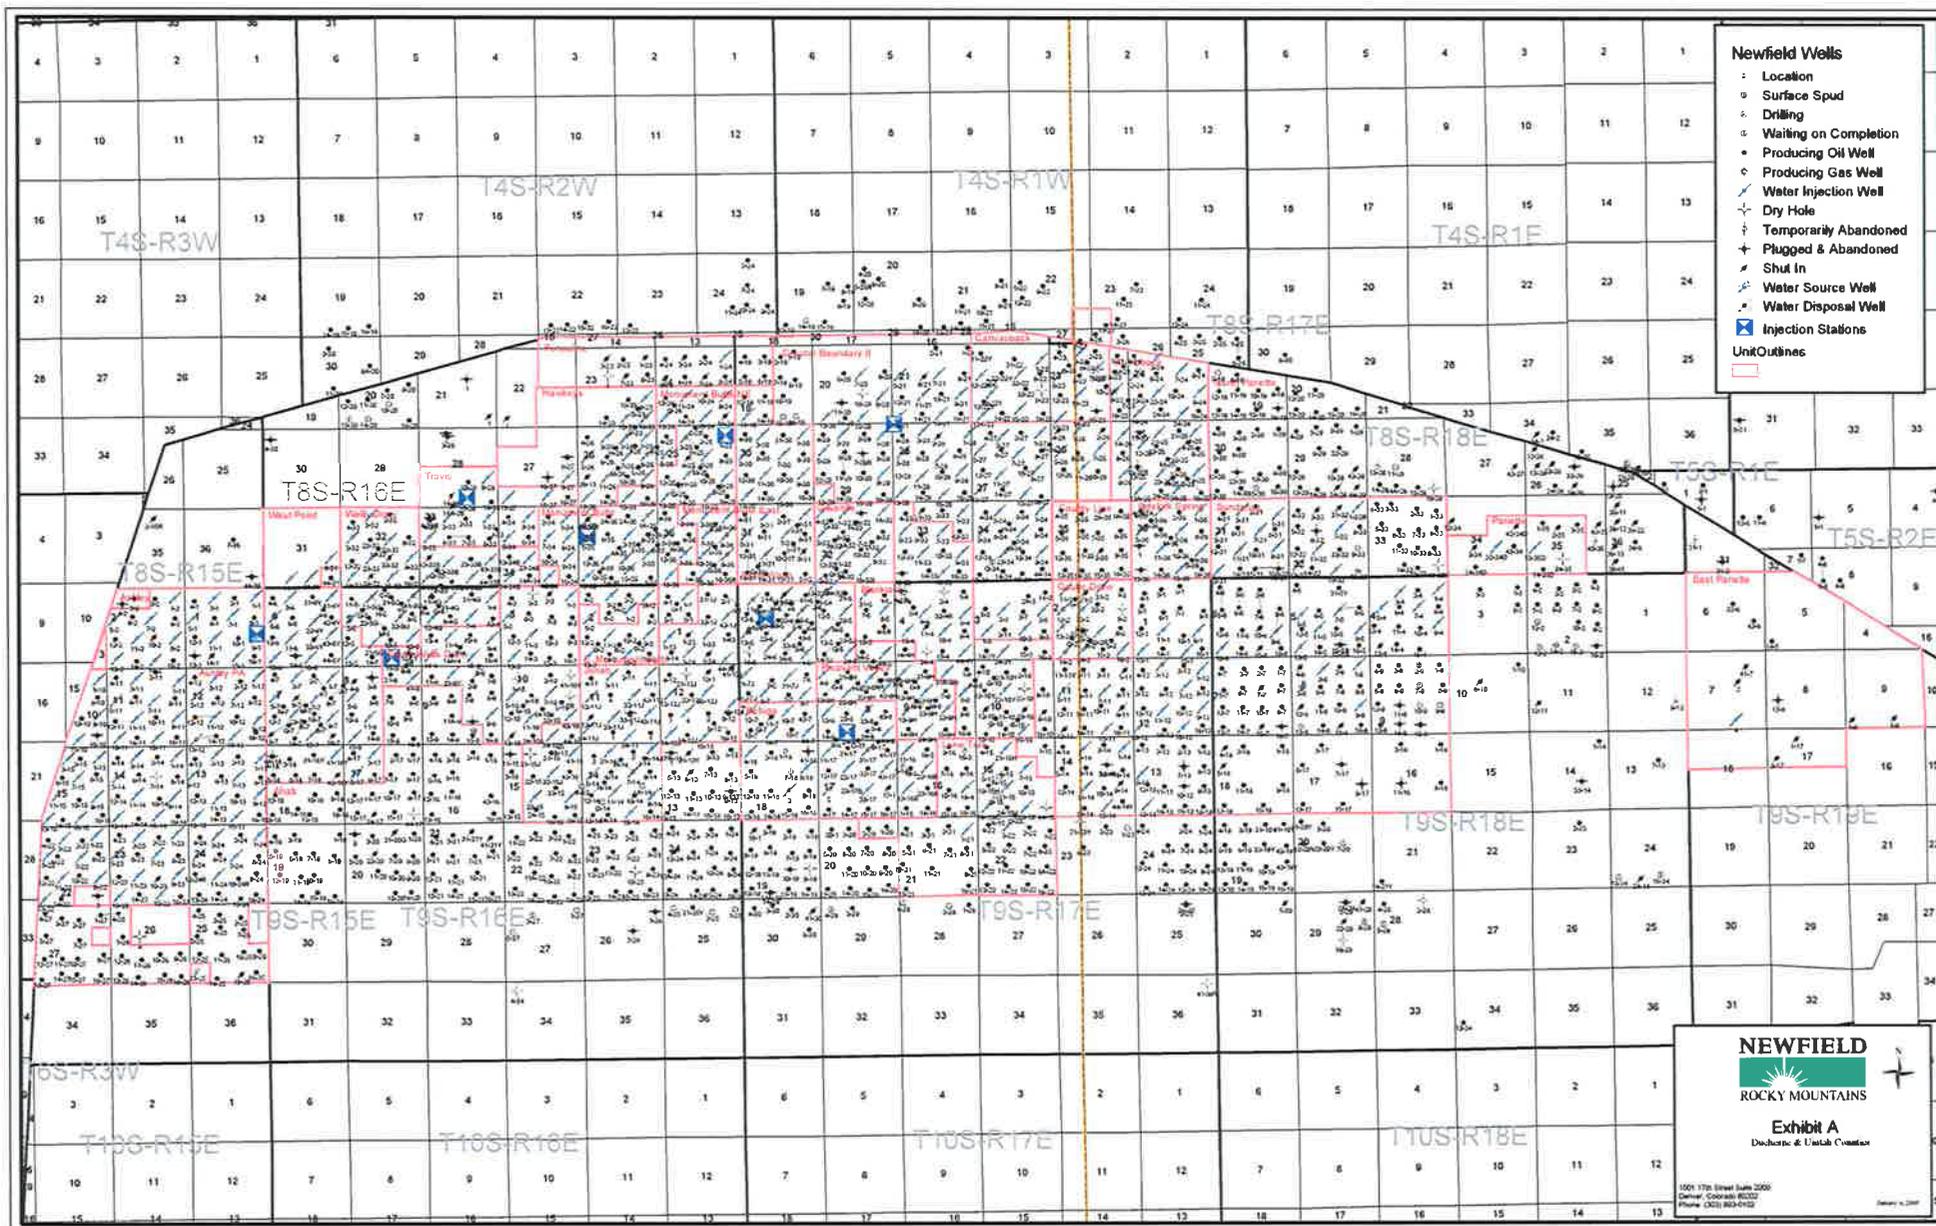

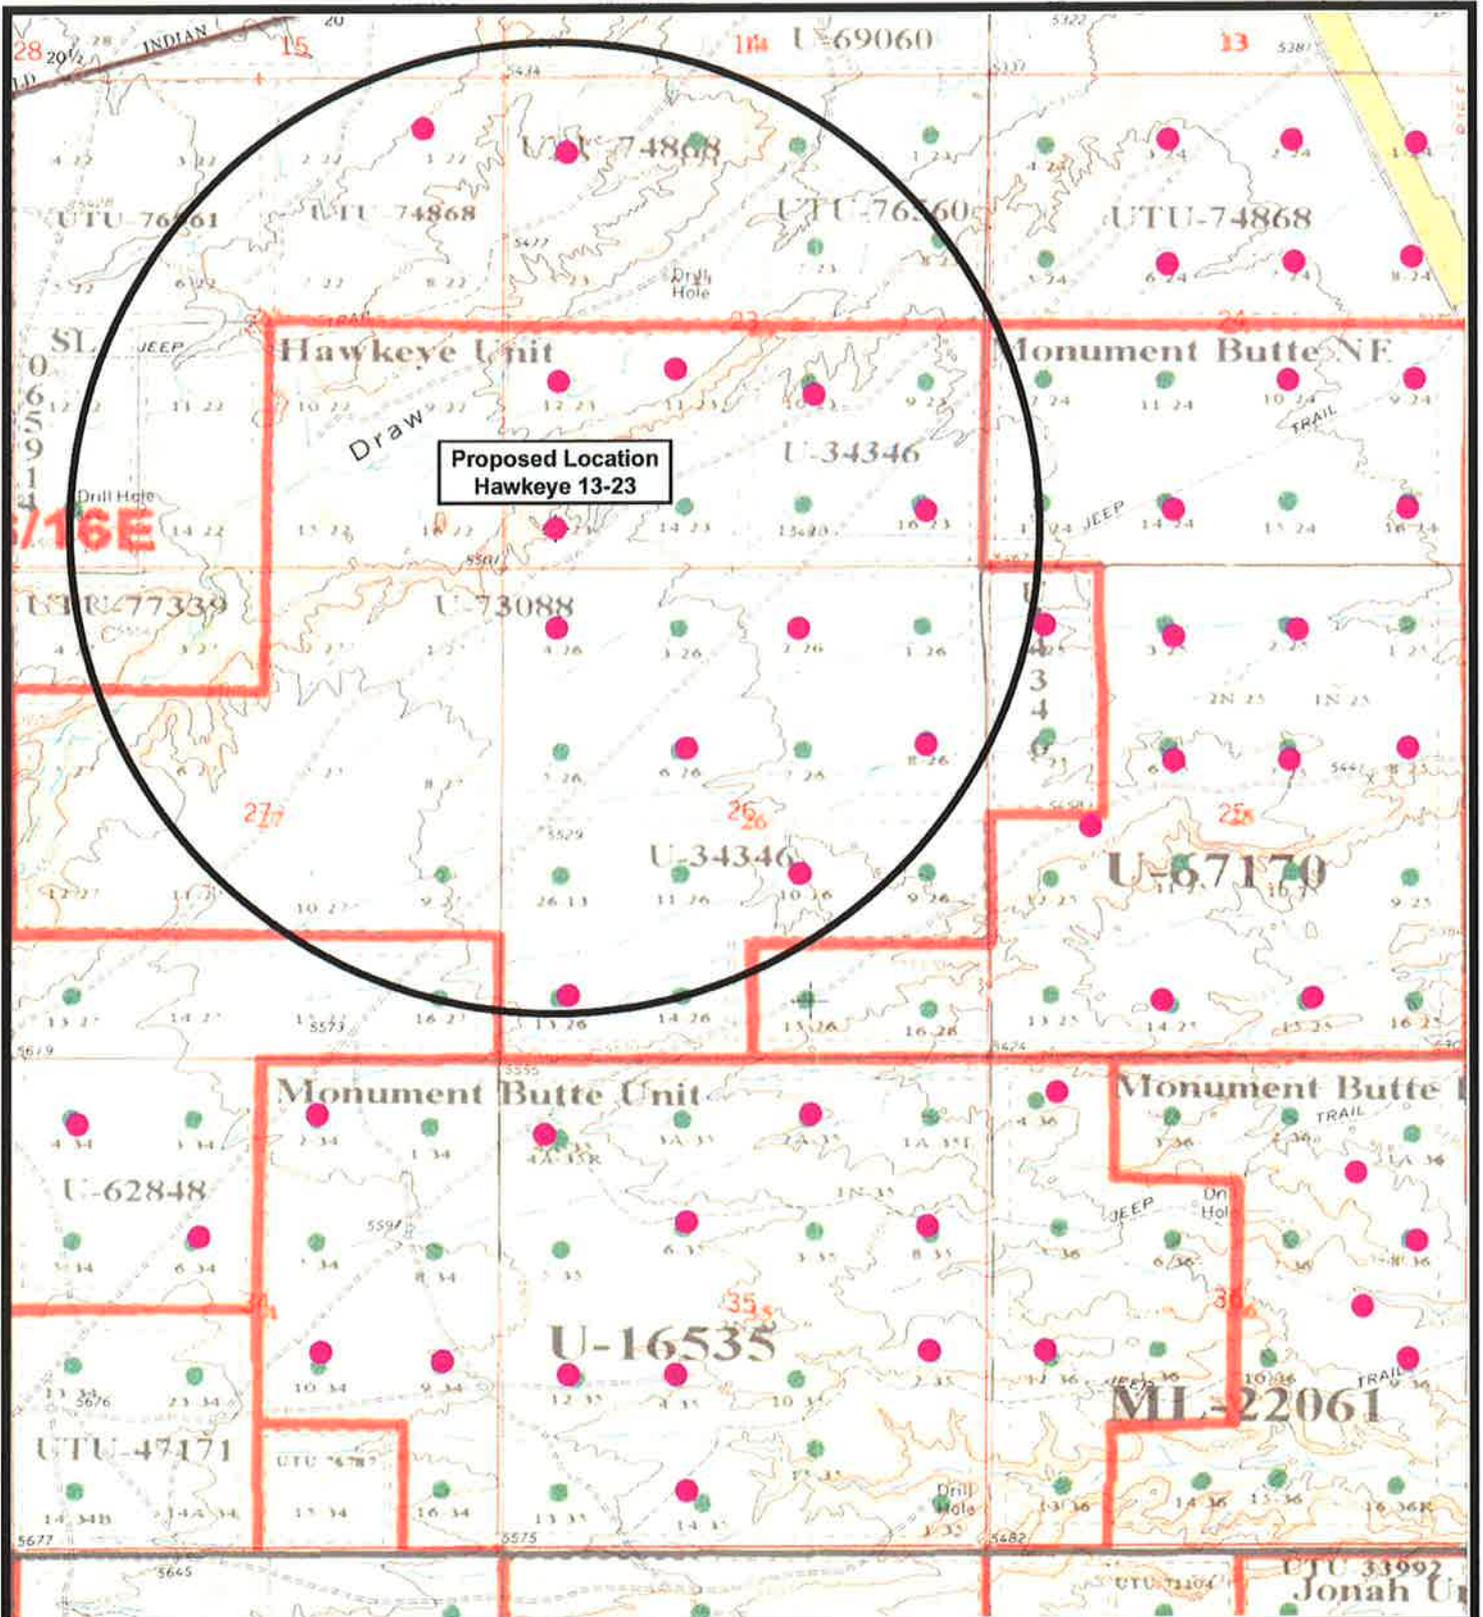

**Proposed Location
Hawkeye 13-23**



NEWFIELD
Exploration Company

**Hawkeye 13-23-8-16
SEC. 23, T8S, R16E, S.L.B.&M.**



Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: JAS
DATE: 03-31-2009

Legend

- Location
- One-Mile Radius

Exhibit "B"

NEWFIELD PRODUCTION COMPANY
HAWKEYE FEDERAL 13-23-8-16
SW/SW SECTION 23, T8S, R16E
DUCHESNE COUNTY, UTAH

THIRTEEN POINT SURFACE PROGRAM

1. **EXISTING ROADS**

See attached **Topographic Map "A"**

To reach Newfield Production Company well location site Hawkeye Federal 13-23-8-16 located in the SW¼ SW¼ Section 23, T8S, R16W, S.L.B. & M., Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.4 miles ± to the junction of this highway and UT State Hwy 53; proceed southeasterly – 6.2 miles ± to it's junction with an existing road to the southwest; proceed southwesterly – 1.8 miles ± to it's junction with an existing road to the northwest; proceed northwesterly – 0.3 miles ± to it's junction with the beginning of the proposed access road to the north; proceed northerly along the proposed access road - 730' ± to the proposed well location.

The highways mentioned in the foregoing paragraph are bituminous surfaced roads to the point where Highway 216 exists to the South, thereafter the roads are constructed with existing materials and gravel. The highways are maintained by Utah State road crews. All other roads are maintained by County crews.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal.

2. **PLANNED ACCESS ROAD**

Approximately 730' of access road is proposed. See attached **Topographic Map "B"**.

The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%.

There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. **LOCATION OF EXISTING WELLS**

Refer to **EXHIBIT B**.

4. **LOCATION OF EXISTING AND/OR PROPOSED FACILITIES**

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck for drilling purposes from the following water sources:

Johnson Water District
Water Right: 43-7478

Neil Moon Pond
Water Right: 43-11787

Maurice Harvey Pond
Water Right: 47-1358

Newfield Collector Well
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous

will be placed in this pit. A 16 mil liner with felt will be required. Newfield requests approval that a flare pit be constructed and utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

8. **ANCILLARY FACILITIES:**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT:**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

10. **PLANS FOR RESTORATION OF SURFACE:**

a) **Producing Location**

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) **Dry Hole Abandoned Location**

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP:** Bureau Of Land Management (Proposed location and access roads leading to).

12. **OTHER ADDITIONAL INFORMATION:**

- a) Newfield Production Company is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, Newfield is to immediately stop work that might further disturb such materials and contact the Authorized Officer.
- b) Newfield Production will control noxious weeds along rights-of-way for roads, pipelines, well sites or other applicable facilities. On State administered land it is required that a Pesticide Use Proposal shall be submitted and given approval prior to the application of herbicides or other possible hazardous chemicals.
- c) Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on State Lands after the conclusion of drilling operations or at any other time without State authorization. However, if State authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the Hawkeye Federal 13-23-8-16, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Hawkeye Federal 13-23-8-16 Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

The State office shall be notified upon site completion prior to moving on the drilling rig.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

Representative


Name: Tim Eaton
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that Newfield Production Company is considered to be the operator of well #13-23-8-16, SW/SW Section 23, T8S, R16E, Duchesne County, Utah and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.


9/4/09
Date _____


Mandie Crozier
Regulatory Specialist
Newfield Production Company

NEWFIELD PRODUCTION COMPANY

HAWKEYE 13-23-8-16

Section 23, T8S, R16E, S.L.B.&M.

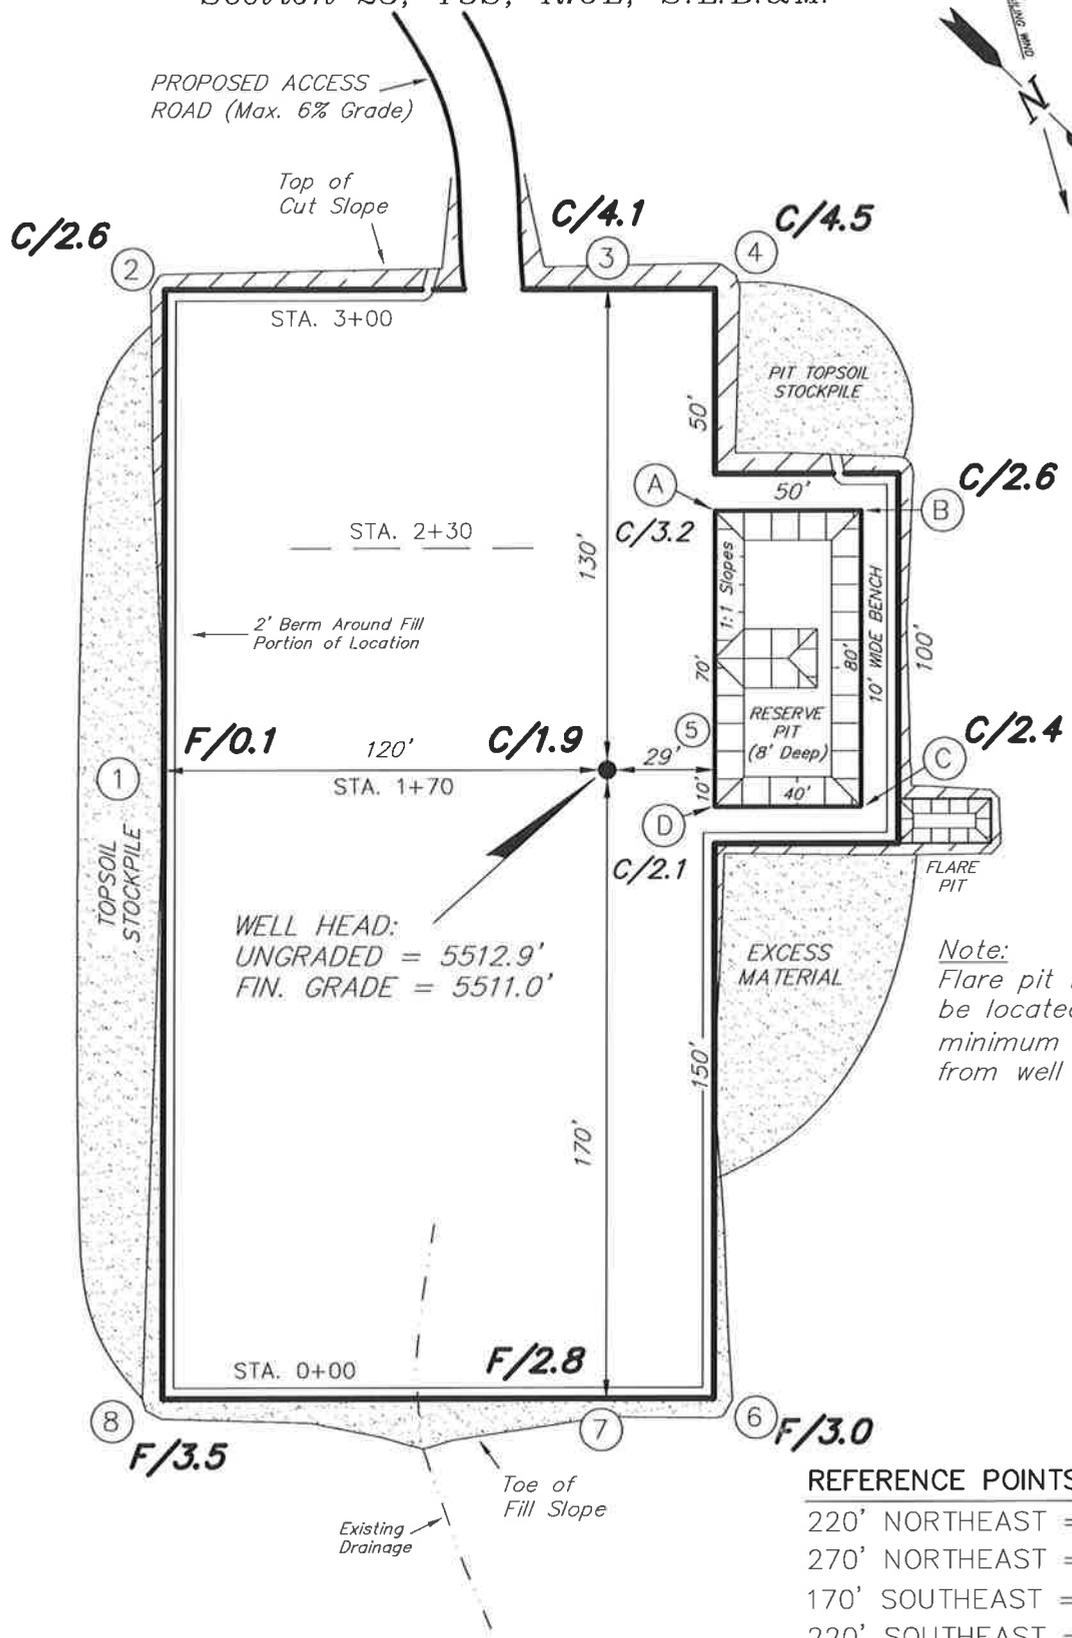

WELL HEAD:
UNGRADED = 5512.9'
FIN. GRADE = 5511.0'

Note:
Flare pit is to
be located a
minimum of 80'
from well head.





REFERENCE POINTS

- 220' NORTHEAST = 5504.0'
- 270' NORTHEAST = 5494.2'
- 170' SOUTHEAST = 5510.0'
- 220' SOUTHEAST = 5510.4'

SURVEYED BY: T.H.	DATE SURVEYED: 02-10-09
DRAWN BY: F.T.M.	DATE DRAWN: 02-18-09
SCALE: 1" = 50'	REVISED: 03-31-09

Tri State
Land Surveying, Inc.
(435) 781-2501
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY
CROSS SECTIONS
HAWKEYE 13-23-8-16

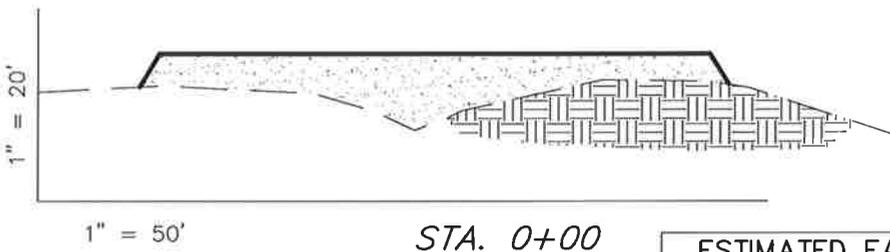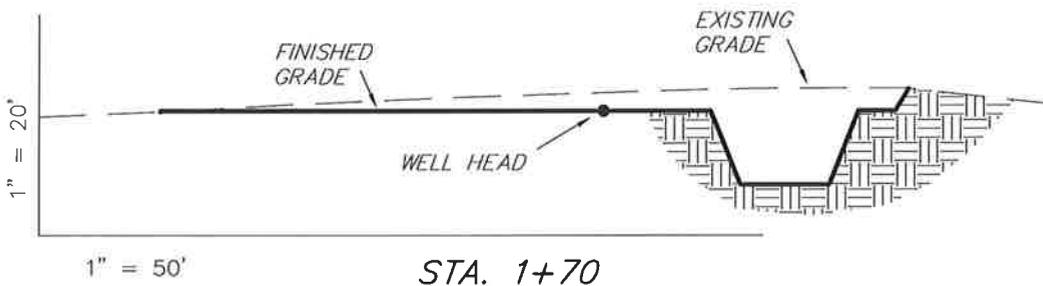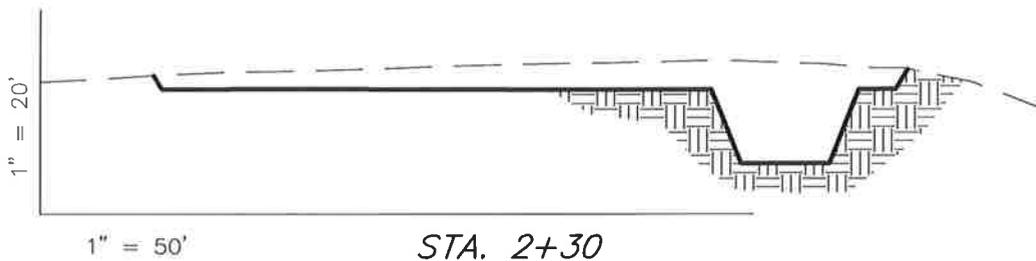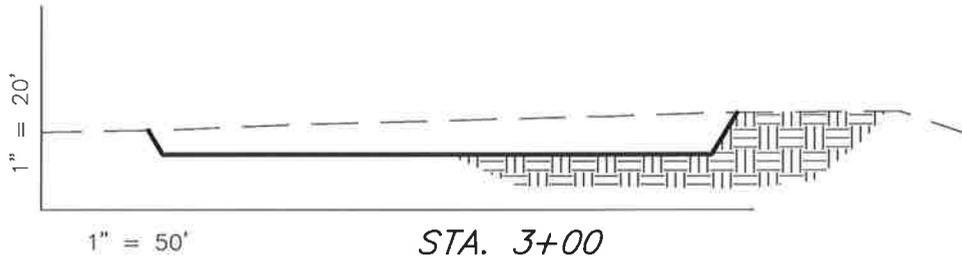

NOTE:
 UNLESS OTHERWISE
 NOTED ALL CUT/FILL
 SLOPES ARE AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES
 (No Shrink or swell adjustments have been used)
 (Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	2,010	2,010	Topsoil is not included in Pad Cut	0
PIT	640	0		640
TOTALS	2,650	2,010	1,010	640



SURVEYED BY: T.H.	DATE SURVEYED: 02-10-09
DRAWN BY: F.T.M.	DATE DRAWN: 02-18-09
SCALE: 1" = 50'	REVISED: 03-31-09

Tri State (435) 781-2501
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

TYPICAL RIG LAYOUT HAWKEYE 13-23-8-16

PROPOSED ACCESS ROAD (Max. 6% Grade)

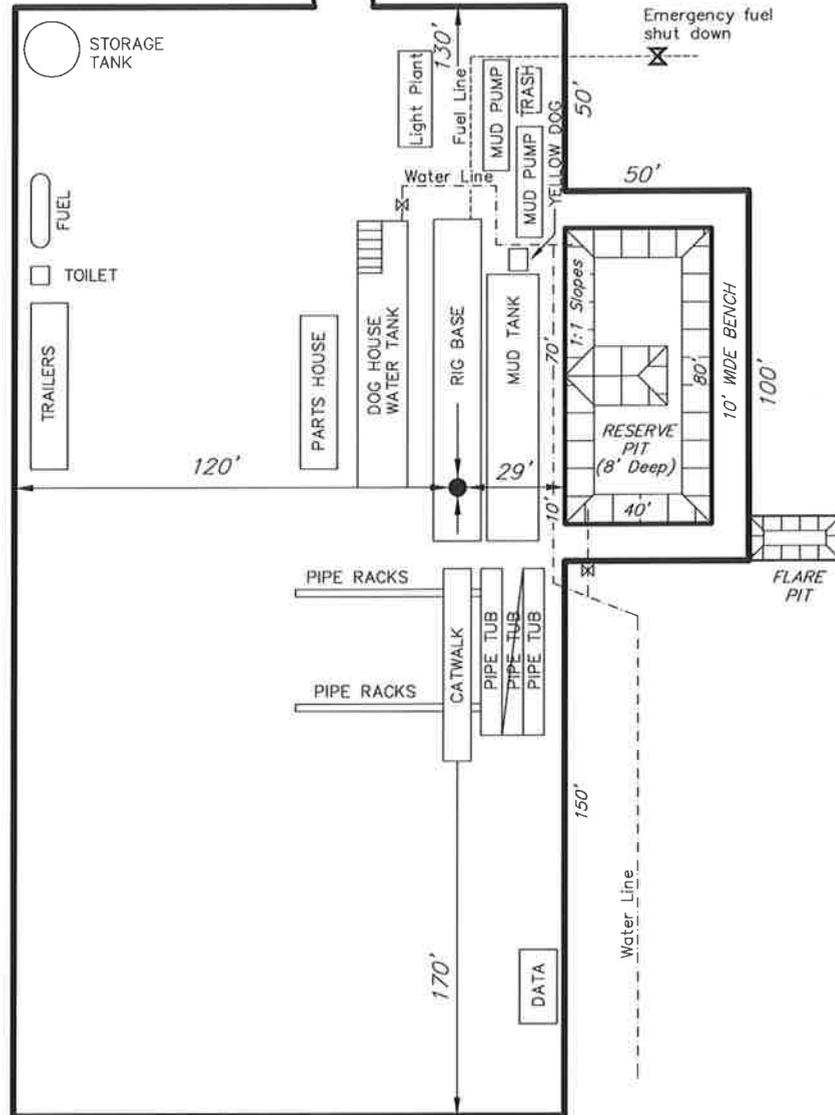

SURVEYED BY: T.H.	DATE SURVEYED: 02-10-09
DRAWN BY: F.T.M.	DATE DRAWN: 02-18-09
SCALE: 1" = 50'	REVISED: 03-31-09

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078


Newfield Production Company Proposed Site Facility Diagram

Hawkeye Federal 13-23-8-16

SW/SW Sec. 23, T8S, R16E

Duchesne County, Utah

UTU-73088

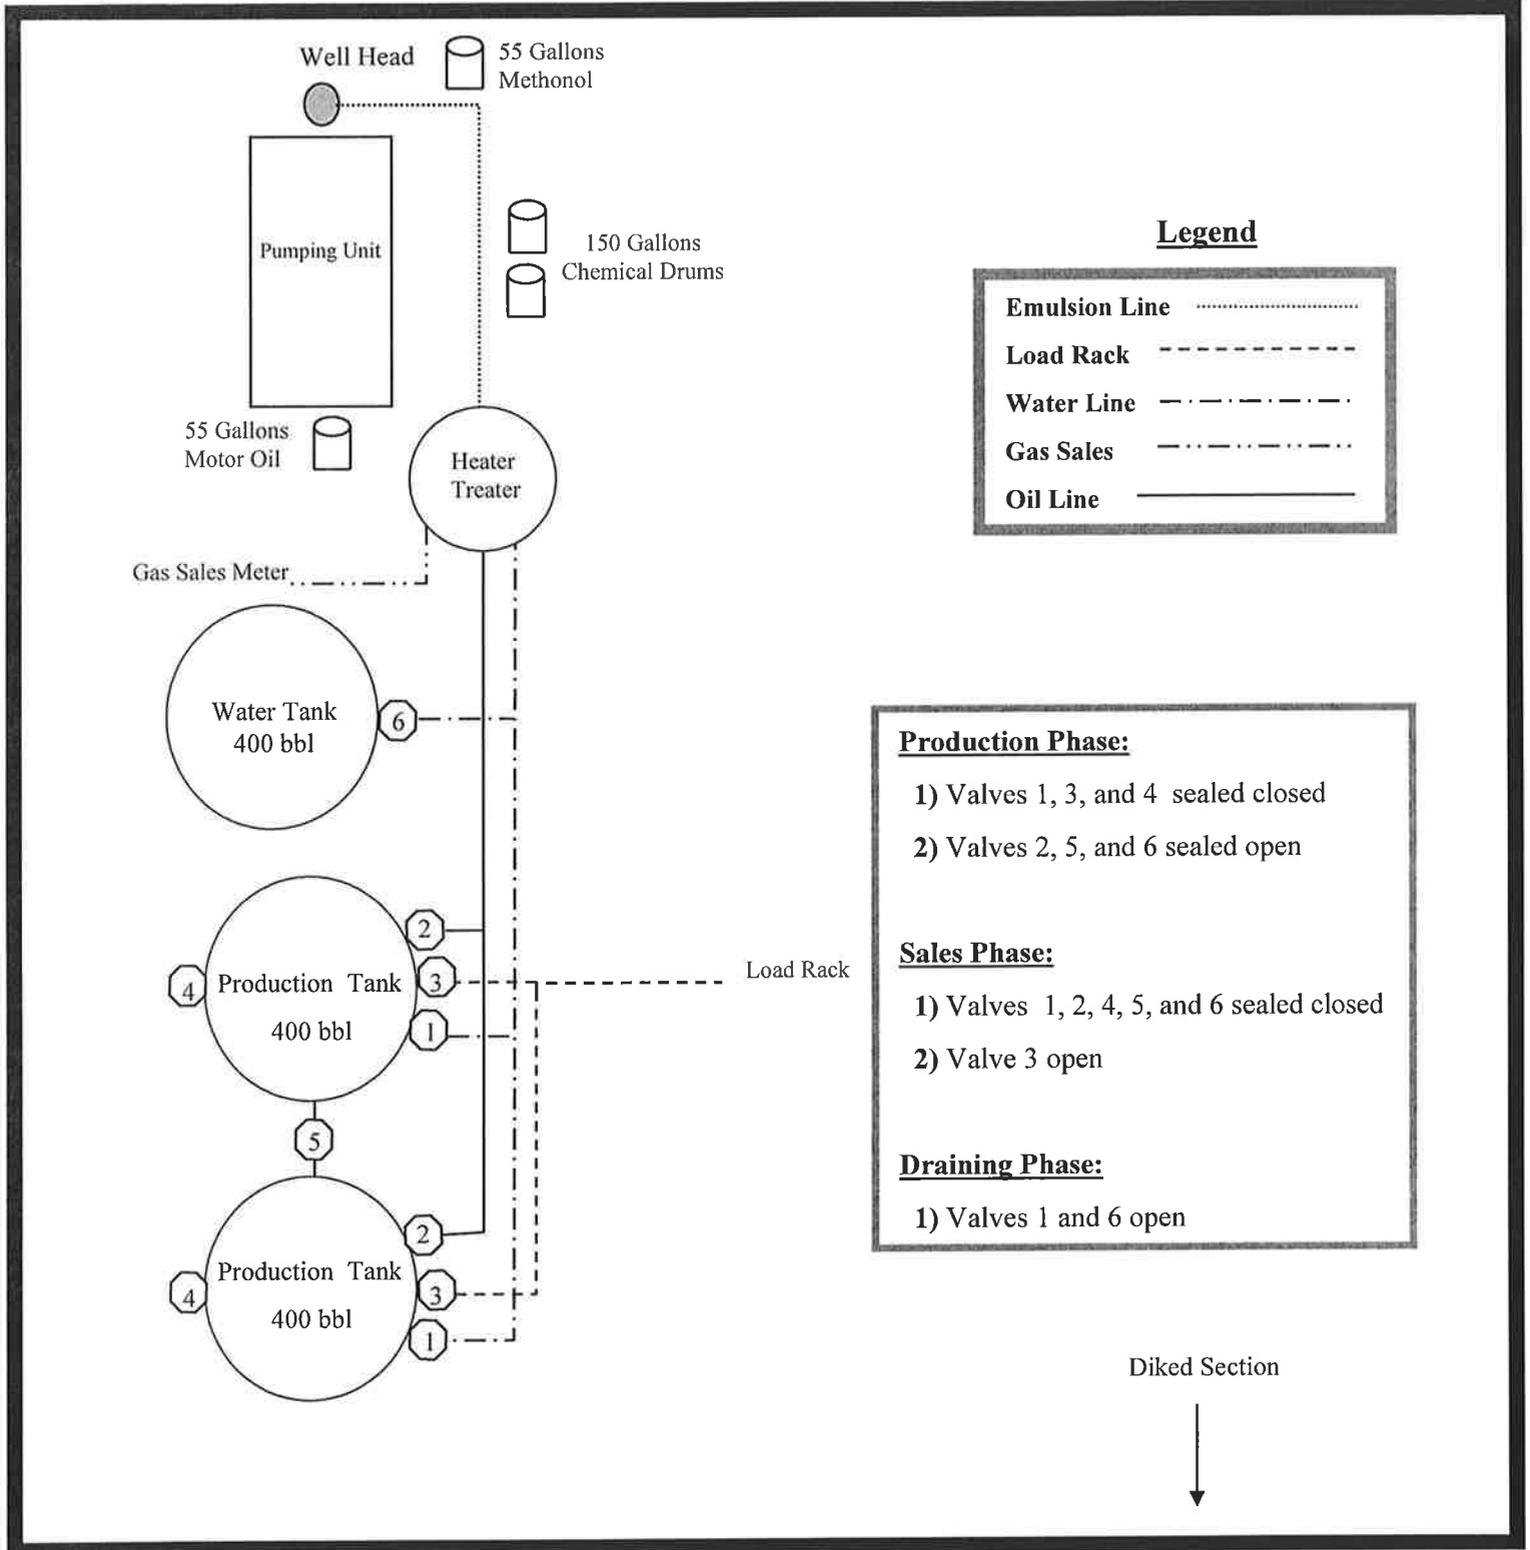

Legend

Emulsion Line
Load Rack	- - - - -
Water Line	- . - . - .
Gas Sales	- . - . - .
Oil Line	—————

Production Phase:

- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open

Sales Phase:

- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

Draining Phase:

- 1) Valves 1 and 6 open

Diked Section



Exhibit "D"

1 of 2

CULTURAL RESOURCE INVENTORY OF
NEWFIELD EXPLORATION'S THREE BLOCK PARCELS
(T8S, R16E, SECTIONS 21, 22 AND 23)
DUCHESNE COUNTY, UTAH

By:

Nicole Shelnut

Prepared For:

Bureau of Land Management
Vernal Field Office

Prepared Under Contract With:

Newfield Exploration Company
Rt. 3 Box 3630
Myton, UT 84052

Prepared By:

Montgomery Archaeological Consultants, Inc.
P.O. Box 219
Moab, Utah 84532

MOAC Report No. 08-295

February 5, 2009

United States Department of Interior (FLPMA)
Permit No. 08-UT-60122

State of Utah Antiquities Project (Survey)
Permit No. U-08-MQ-1191b

2 of 2

NEWFIELD EXPLORATION COMPANY

**PALEONTOLOGICAL SURVEY OF PROPOSED
PRODUCTION DEVELOPMENT AREAS,
DUCHESNE COUNTY, UTAH**

SE1/4, SW1/4 & SW1/4 & SE1/4, SE1/4, Sec. 2, T 9 S, R 16 E [14, 15 & 16-2-9-16];
SW1/4 & SE1/4, SW1/4 & SW1/4 & SE1/4, SE1/4; Sec.19, T 8 S, R 16 E [13,14,15 &16-19-8-
16]; Section 22, T 8 S, R 16 E (excluding SW1/4, SW1/4 [13-22-8-16]); NW1/4 & SW1/4,NW
1/4 & NE1/4, NW1/4 & SW1/4, SW1/4; Section 23, T 8 S, R 16 E 4,5,11,12 & 13-23-8-16];
NE1/4 & NW1/4, NE1/4, All of the NW1/4; SW1/4, NE1/4; NE1/4, NW1/4 & SE1/4, SW1/4;
Sec. 27, T 8 S, R 16 E [1,2,3,4,5,6,7,11,12 & 14-27-8-16]; All of the NE1/4; NW1/4, SW1/4 &
SE1/4, NE1/4; NW1/4 & SW1/4, SW1/4; Sec. 28, T 8 S, R 16 E [1,2,4,5,6,7,11,12 &14-28-8-
16]; All of Section 29, T 8 S, R 16 E (excluding SW1/4 & SE1/4, SW1/4 [13 & 14-29-8-16])

REPORT OF SURVEY


Prepared for:

Newfield Exploration Company

Prepared by:

Wade E. Miller
Consulting Paleontologist
November 11, 2008

NEWFIELD



Route #3 Box 3630
Myton, Utah 84052
(435) 646-4825, FAX: (435) 646-3031

September 4, 2009

State of Utah
Division of Oil, Gas & Mining
Attn: Diana Mason
1594 West North Temple - Suite 1210
P.O. Box 145801
Salt Lake City, Utah 84114-5801

RE: Application for Permit to Drill
Hawkeye Federal 13-23-8-16

Dear Diana:

The above mentioned location is an **Exception Location**. Our Land Department will send you the required exception location letter. If you have any questions, feel free to give either Tim Eaton or myself a call.

Sincerely,

A handwritten signature in blue ink that reads "Mandie Crozier". The signature is written in a cursive, flowing style.

Mandie Crozier
Regulatory Specialist

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office
P.O. Box 45155
Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:
3160
(UT-922)

September 11, 2009

Memorandum

To: Assistant District Manager Minerals, Vernal District
From: Michael Coulthard, Petroleum Engineer
Subject: 2009 Plan of Development Hawkeye Unit,
Duchesne County, Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2009 within the Hawkeye Unit, Duchesne County, Utah.

API#	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-50131	Hawkeye Federal	11-23-8-16 Sec 23 T08S R16E 2101 FSL 1955 FWL
43-013-50132	Hawkeye Federal	13-23-8-16 Sec 23 T08S R16E 0359 FSL 0730 FWL

This office has no objection to permitting the wells at this time.

/s/ Michael L. Coulthard

bcc: File - Hawkeye Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:9-11-09



September 8, 2009

State of Utah, Division of Oil, Gas & Mining
ATTN: Diana Mason
PO Box 145801
Salt Lake City, UT 84114-5801

2003

RE: Exception Location
Federal 13-23-8-16
T8S R16E, Section 23: SW4SW4
359'FSL 730' FWL
Duchesne County, Utah

Dear Ms. Mason;

Pursuant to Rule 649-3-3 of the Oil & Gas Rules and Regulations of the State of Utah, Newfield Production Company ("NPC") hereby requests an exception location for the drilling of the captioned well. The proposed drillsite for this well is located 99' south of the drilling window required by Rule R649-3-2, which requires a well to be located in the center of a forty (40) acre quarter-quarter section, or a substantially equivalent lot or tract, with a tolerance of two hundred (200) feet in any direction from the center.

The attached plat depicts the proposed location. The requested location is outside of the required drilling window due to terrain. Please note the drillsite and all acreage within 460' is on U-73088, which is owned by NPC 100%.

If you have any questions or require further information, please do not hesitate to contact the undersigned at 303-382-4137 or by email at awild@newfield.com. Your consideration of this matter is greatly appreciated


Sincerely,

A handwritten signature in blue ink, appearing to read "Alan D. Wild", is written over a circular stamp.

Alan D. Wild
Land Associate

Attachment


RECEIVED
SEP 14 2009
DIV. OF OIL, GAS & MINING

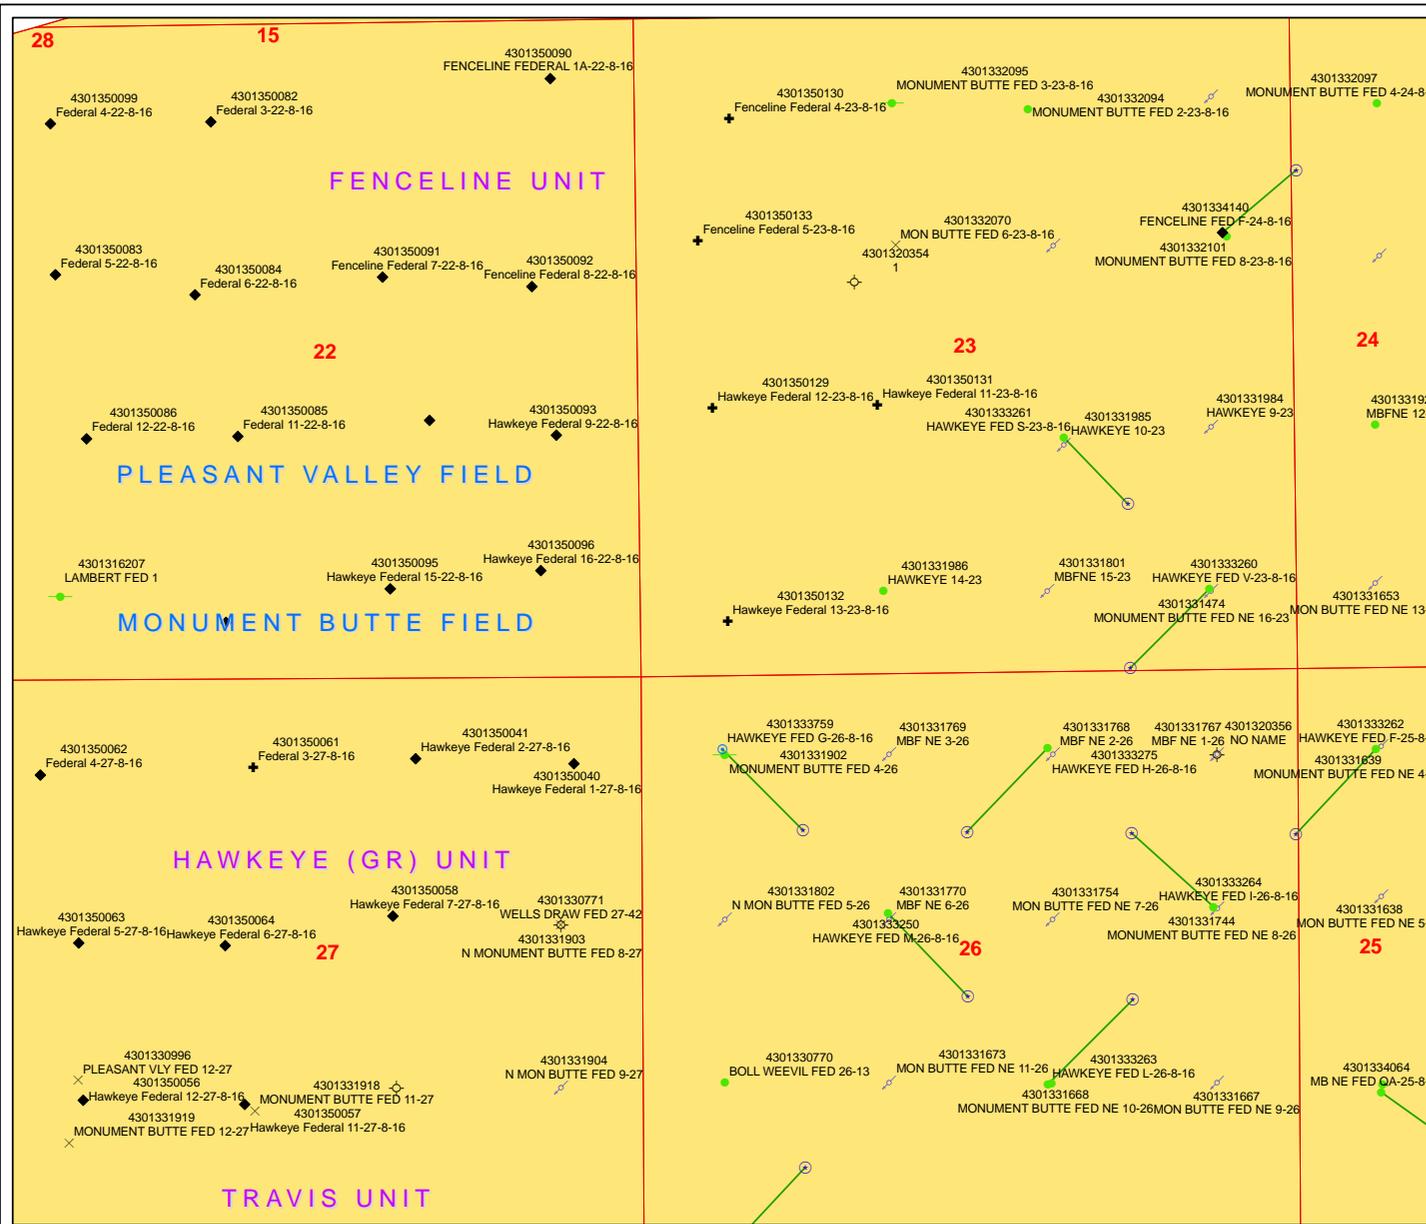

API Number: 4301350132
Well Name: Hawkeye Federal 13-23-8-16
Township 08.0 S Range 16.0 E Section 23
Meridian: SLBM
Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
 Map Produced by Diana Mason

Units	Wells Query Events
STATUS	<-all other values>
ACTIVE	GIS_STAT_TYPE
EXPLORATORY	<Null>
GAS STORAGE	APD
NF PP OIL	DRL
NF SECONDARY	GI
PI OIL	GS
PP GAS	LA
PP GEOTHERMIL	NEW
PP OIL	OPS
SECONDARY	PA
TERMINATED	PGW
Fields	POW
ACTIVE	RET
COMBINED	SGW
SECTIONS	SOW
	TA
	TW
	WI
	WS



WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 9/4/2009

API NO. ASSIGNED: 43013501320000

WELL NAME: Hawkeye Federal 13-23-8-16

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: SWSW 23 080S 160E

Permit Tech Review:

SURFACE: 0359 FSL 0730 FWL

Engineering Review:

BOTTOM: 0359 FSL 0730 FWL

Geology Review:

COUNTY: DUCHESNE

LATITUDE: 40.09732

LONGITUDE: -110.09270

UTM SURF EASTINGS: 577340.00

NORTHINGS: 4438742.00

FIELD NAME: MONUMENT BUTTE

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-73088

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 1 - Federal

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: FEDERAL - WYB000493
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 43-7478
- RDCC Review:
- Fee Surface Agreement
- Intent to Commingle


Commingling Approved

LOCATION AND SITING:

- R649-2-3.
Unit: HAWKEYE (GRRV)
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
Board Cause No: Cause 213-05(A)
Effective Date: 10/25/2006
Siting: Suspends General Siting
- R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason



State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Hawkeye Federal 13-23-8-16
API Well Number: 43013501320000
Lease Number: UTU-73088
Surface Owner: FEDERAL
Approval Date: 9/21/2009

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 213-05(A). The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)
- OR
- submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <https://oilgas.ogm.utah.gov>


Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month

- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "Gil Hunt". The signature is fluid and cursive, with a long horizontal stroke extending to the right.

Gil Hunt
Associate Director, Oil & Gas

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No. UTU-73088	
6. If Indian, Allottee or Tribe Name NA	
7. If Unit or CA Agreement, Name and No. Hawkeye GMB	
8. Lease Name and Well No. Hawkeye Federal 13-23-8-16	
9. API Well No. 43 013 50132	
10. Field and Pool, or Exploratory Monument Butte	
11. Sec., T. R. M. or Blk. and Survey or Area Sec. 23, T8S R16E	
12. County or Parish Duchesne	
13. State UT	
14. Distance in miles and direction from nearest town or post office* Approximately 9.5 miles southwest of Myton, UT	
15. Distance from proposed* location to nearest property or lease line, ft. Approx. 1910' f/lease, 2281' f/unit (Also to nearest drig. unit line, if any)	
16. No. of acres in lease 1040.00	
17. Spacing Unit dedicated to this well 40 Acres	
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1800'	
19. Proposed Depth 6,695'	
20. BLM/BIA Bond No. on file WYB000493	
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5513' GL	
22. Approximate date work will start* 1st Qtr. 2010	
23. Estimated duration (7) days from SPUD to rig release	
24. Attachments	

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 9/4/09
Title Regulatory Specialist		
Approved by (Signature) <i>James H. Sparger</i>	Name (Printed/Typed) James H. Sparger	Date MAY 18 2010
Title ACTING Assistant Field Manager Lands & Mineral Resources	Office VERNAL FIELD OFFICE	

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached. **CONDITIONS OF APPROVAL ATTACHED**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

*(Instructions on page 2)

RECEIVED

RECEIVED

SEP 9 - 2009

MAY 24 2010

UDOGM

NOTICE OF APPROVAL

DIV. OF OIL, GAS & MINING

BLM VERNAL, UT



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company:	Newfield Production Company	Location:	SWSW, Sec. 23, T8S, R16E
Well No:	Hawkeye Federal 13-23-8-16	Lease No:	UTU-73088
API No:	43-013-50132	Agreement:	Greater Monument Butte Unit

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings to: ut_vn_opreport@blm.gov .
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

**SURFACE USE PROGRAM
 CONDITIONS OF APPROVAL (COAs)**

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

CONDITIONS OF APPROVAL:

- Construction and drilling is not allowed from May 1 – June 15 to minimize impacts during mountain plover nesting.
- Construction and drilling is not allowed from March 1 – August 31 to minimize impacts during burrowing owl nesting.
- If it is anticipated that construction or drilling will occur during any of the given timing restrictions, a BLM or qualified biologist shall be notified so surveys can be conducted. Depending upon the results of the surveys, permission to proceed may or may not be granted by the BLM Authorized Officer.
- Prior to construction, an invasive plants/noxious weeds inventory will be completed for all areas where surface disturbance will occur, and a completed Weed Inventory Form will be submitted to the BLM Authorized Officer.

Reclamation

- Reclamation will be completed in accordance with the Newfield Exploration Company Castle Peak and Eight Mile Flat Reclamation Plan on file with the Vernal Field Office of the BLM.

Seed Mix (Interim and Final Reclamation)

Common name	Latin name	lbs/acre	Recommended seed planting depth
Squirreltail grass	<i>Elymus elymoides</i>	2.0	¼ - ½"
Bluebunch wheatgrass	<i>Pseudoroegneria spicata</i>	1.0	½"
Shadscale saltbush	<i>Atriplex confertifolia</i>	2.0	½"
Four-wing saltbush	<i>Atriplex canescens</i>	3.0	½"

Gardner's saltbush	<i>Atriplex gardneri</i>	1.0	1/2"
Scarlet globemallow	<i>Sphaeralcea coccinea</i>	1.0	1/8 - 1/4"

- All pounds are pure live seed.
- All seed and mulch will be certified weed free.
- Rates are set for drill seeding; double rate if broadcasting.

Monitoring and Reporting

- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) that designates the proposed site-specific monitoring and reference sites chosen for the location. A description of the proposed sites shall be included, as well as a map showing the locations of the proposed sites.
- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) 3 growing seasons after reclamation efforts have occurred evaluating the status of the reclaimed areas in order to determine whether the BLM standards set forth in the Green River District Reclamation Guidelines have been met (30% or greater basal cover).

***DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

SITE SPECIFIC DOWNHOLE COAs:

- Production casing cement shall be brought up and into the surface.
- Logging: A Gamma Ray well Log shall be run from the well Total Depth to the surface. A copy of the Gamma Ray well Log shall be submitted to the BLM Vernal Field Office.
- A copy of Newfield's Standard Operating Practices (SOP version: dated 4/18/08 and approved 5/12/08) shall be on location.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**

- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.
- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location ($\frac{1}{4}\frac{1}{4}$, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.

- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.
- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.

- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-73088
---	--

SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
--	---

1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: Hawkeye Federal 13-23-8-16
------------------------------------	---

2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	9. API NUMBER: 43013501320000
--	---

3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext	9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
--	--	--

4. LOCATION OF WELL FOOTAGES AT SURFACE: 0359 FSL 0730 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SWSW Section: 23 Township: 08.0S Range: 16.0E Meridian: S	COUNTY: DUCHESNE STATE: UTAH
---	---

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 9/21/2010	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input checked="" type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
 Newfield proposes to extend the Application for Permit to Drill this well for one year.

Approved by the
 Utah Division of
 Oil, Gas and Mining

Date: September 20, 2010
 By:

NAME (PLEASE PRINT) Mandie Crozier	PHONE NUMBER 435 646-4825	TITLE Regulatory Tech
SIGNATURE N/A	DATE 9/13/2010	



The Utah Division of Oil, Gas, and Mining

- State of Utah
- Department of Natural Resources

Electronic Permitting System - Sundry Notices

Request for Permit Extension Validation Well Number 43013501320000

API: 43013501320000

Well Name: Hawkeye Federal 13-23-8-16

Location: 0359 FSL 0730 FWL QTR SWSW SEC 23 TWP 080S RNG 160E MER S

Company Permit Issued to: NEWFIELD PRODUCTION COMPANY

Date Original Permit Issued: 9/21/2009

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision. Following is a checklist of some items related to the application, which should be verified.

- If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes No
- Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes No
- Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes No
- Have there been any changes to the access route including ownership, or rightof- way, which could affect the proposed location? Yes No
- Has the approved source of water for drilling changed? Yes No
- Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes No
- Is bonding still in place, which covers this proposed well? Yes No

Approved by the Utah Division of Oil, Gas and Mining

Signature: Mandie Crozier

Date: 9/13/2010

Title: Regulatory Tech Representing: NEWFIELD PRODUCTION COMPANY

Date: September 20, 2010

By: [Signature]

Spud
BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross # 29 Submitted
By Ryan Crum Phone Number 823-7065
Well Name/Number Federal 13-23-8-16
Qtr/Qtr SW/SW Section 23 Township 8s Range 16e
Lease Serial Number UTU-73088
API Number 43-013-50132

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 9/24/10 8:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 9/24/10 2:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks _____

STATE OF UTAH
 DIVISION OF OIL, GAS AND MINING
 ENTITY ACTION FORM -FORM 6

OPERATOR: **NEWFIELD PRODUCTION COMPANY**
 ADDRESS: **RT. 3 BOX 3630**
MYTON, UT 84052

OPERATOR ACCT. NO. **N2695**

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION				SPUD DATE	EFFECTIVE DATE	
					QQ	SC	TP	RG			COUNTY
A	99999	17799	4301350357	UTE TRIBAL 5-23-4-3	SWNW	23	4S	3W	DUCHESNE	9/21/2010	10/11/10
WELL 1 COMMENTS: GRRV											
B	99999	17400	4301334215	FEDERAL 9-26-8-15	NESE	26	8S	15E	DUCHESNE	9/16/10* 9/17/2010	
Duplicate - *processed 9/21/10											
B	99999	17400	4301350187	MONUMENT BUTTE FEDERAL S-35-8-16	NWSE	35	8S	16E	DUCHESNE	9/22/2010	10/11/10
GRRV BHL=NESE											
B	99999	17400	4301350186	MONUMENT BUTTE FEDERAL R-35-8-16	NESW	35	8S	16E	DUCHESNE	9/22/2010	10/11/10
GRRV BHL=SWSE											
B	99999	17400	4301350132	FEDERAL 13-23-8-16	SWSW	23	8S	16E	DUCHESNE	9/24/2010	10/11/10
WELL 5 COMMENTS: GRRV											
WELL 5 COMMENTS:											

- ACTION CODES (See instructions on back of form)
- A - 1 new entity for new well (single well only)
 - B - well to existing entity (group or unit well)
 - C - from one existing entity to another existing entity
 - D - well from one existing entity to a new entity
 - E - other (explain in comments section)

RECEIVED
 SEP 27 2010

Signature Jentri Park
 Production Clerk
 Date 09/27/10

NOTE: Use COMMENT section to explain why each Action Code was selected.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include are code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

0359 FSL 0730 FWL

SWSW Section 23 T8S R16E

5. Lease Serial No.

USA UTU-73088

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

GMBU

8. Well Name and No.

HAWKEYE 13-23-8-16

9. API Well No.

4301350132

10. Field and Pool, or Exploratory Area

GREATER MB UNIT

11. County or Parish, State

DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 9/24/10 MIRU Ross # 29. Spud well @ 8:00 AM. Drill 355' of 12 1/4" hole with air mist. TIH W/ 8 Jt's 8 5/8" J-55 24# casing. Set @ 354.65' KB. On 10/3/10 cement with 180 sks of class "G" w/ 2% CaCL2 + 1/4# per sk Cello Flake mixed @ 15.8 ppg with 1.17 cf/sk yield. Returned 5 bbls cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Title

Drilling Foreman

Signature

Mitch Benson

Date

10/16/2010

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

RECEIVED

NOV 01 2010

DIV. OF OIL, GAS & MINING

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
USA UTU-73088

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:
GMBU

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

8. WELL NAME and NUMBER:
HAWKEYE 13-23-8-16

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:
4301350132

3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

10. FIELD AND POOL, OR WILDCAT:
GREATER MB UNIT

4. LOCATION OF WELL:
FOOTAGES AT SURFACE:

COUNTY: DUCHESNE

OTR/OTR. SECTION, TOWNSHIP, RANGE, MERIDIAN: SWSW, 23, T8S, R16E

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 12/01/2010	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was completed on 12-01-10, attached is a daily completion status report.

NAME (PLEASE PRINT) Lucy Chavez-Naupoto

TITLE Administrative Assistant

SIGNATURE



DATE 12/06/2010

(This space for State use only)

RECEIVED

DEC 09 2010

DIV. OF OIL, GAS & MINING

Daily Activity Report

Format For Sundry

HAWKEYE 13-23-8-16

9/1/2010 To 1/30/2011

11/17/2010 Day: 1

Completion

Rigless on 11/17/2010 - Run CBL & perforate stg #1 - Install 5m frac head. NU 6" 5K Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head, csg & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 6606' & cement top @ 306'. Perforate stage #1, CP5 sds @ (6403'-06') w/ 3 1/8" Port plug guns (11 gram .36" EH 16.82" pen) w/ 3 spf for total of 18 shots. CP4 sds @ (6315'-18') w/ 3 1/8" Port plug guns (11 gram .36" EH 16.82" pen) w/ 3 spf for total of 18 shots. RD H/O truck & The Perforators WLT & mast. Wait on frac crew EWTR 158 BBLs

Daily Cost: \$0

Cumulative Cost: \$15,390

11/23/2010 Day: 2

Completion

Rigless on 11/23/2010 - Frac stgs 1-5. Flowback. - RU BJ Services. Frac Stg 1- CP5/CP4 sds as shown in stimulation report. 567 BWTR. - Open well to pit for immediate flowback @ approx. 3 bpm. Well flowed for 2 hrs. Recovered 360 bbls. SWIFN. - RU PSI wireline. Set CFTP @ 5015' & perf PB11 sds as shown in perforation report. RU BJ Services. Frac Stg 5- PB11 sds as shown in stimulation report. 1958.6 BWTR. - RU PSI wireline. Set CFTP @ 5315' & perf D2/D1 sds as shown in perforation report. RU BJ Services. Frac Stg 4- D2/D1 sds as shown in stimulation report. 1663.1 BWTR. - RU PSI wireline. Set CFTP @ 5520' & perf B.5 sds as shown in perforation report. RU BJ Services. Frac Stg 3- B.5 sds as shown in stimulation report. 1249.6 BWTR. - RU PSI wireline. Set CFTP @ 6245' & perf CP2/CP1 sds as shown in perforation report. RU BJ Services. Frac Stg 2- CP2/CP1 sds as shown in stimulation report. 952.3 BWTR.

Daily Cost: \$0

Cumulative Cost: \$98,125

11/24/2010 Day: 3

Completion

Rigless on 11/24/2010 - Set Kill Plg and BO well. - MIRUWLU. Equalize lubricator and RIH w/ Kill plug. Set Kill Plg @ 4890'. BO well and POOH. Close BOPS, BO Lubricator and RDMOWLU.

Daily Cost: \$0

Cumulative Cost: \$103,058

11/30/2010 Day: 4

Completion

NC #3 on 11/30/2010 - MIRUSU. TIH w/ tbg & start drilling CBP's. - RU hot oil truck & thaw well. 400 psi on tbg & 325 psi on csg. TIH w/ tbg to CBP @ 5315'. Drill out CBP. TIH w/ tbg to CBP @ 5520'. Drill out CBP. TIH w/ tbg to CBP @ 6245'. Drill out CBP. TIH w/ tbg to fill @ 6525'. Clean out fill to PBSD @ 6640'. CWC. LD 3- jts 2 7/8. RU sandline to swab. IFL @ surface. Made 10 swab runs & recovered 125 bbls fluid w/ 60% oil w/ no sand. FFL @ 700'. RD sandline. TIH w/ 3- jts 2 7/8. Tag PBSD @ 6640'. No new fill. CWC. LD 6- jts 2 7/8. TOH w/ 60- jts 2 7/8. SDFD. - MIRUSU. ND BOP & frac head. NU production head & BOP. RU rig floor. X- over to tbg eq. PU TIH w/ 4 3/4 chomp bit & 156- jts 2 7/8. Tag kill plg @ 4890'. RU Weatherford power swivel. Drill out kill plg. TIH w/ tbg to CBP @ 5015'. Drill out CBP. SDFD. - RU hot oil truck & thaw well. 400 psi on tbg & 325 psi on csg. TIH w/ tbg to CBP @ 5315'. Drill

out CBP. TIH w/ tbg to CBP @ 5520'. Drill out CBP. TIH w/ tbg to CBP @ 6245'. Drill out CBP. TIH w/ tbg to fill @ 6525'. Clean out fill to PBSD @ 6640'. CWC. LD 3- jts 2 7/8. RU sandline to swab. IFL @ surface. Made 10 swab runs & recovered 125 bbls fluid w/ 60% oil w/ no sand. FFL @ 700'. RD sandline. TIH w/ 3- jts 2 7/8. Tag PBSD @ 6640'. No new fill. CWC. LD 6- jts 2 7/8. TOH w/ 60- jts 2 7/8. SDFD. - MIRUSU. ND BOP & frac head. NU production head & BOP. RU rig floor. X- over to tbg eq. PU TIH w/ 4 3/4 chomp bit & 156- jts 2 7/8. Tag kill plg @ 4890'. RU Weatherford power swivel. Drill out kill plg. TIH w/ tbg to CBP @ 5015'. Drill out CBP. SDFD.

Daily Cost: \$0

Cumulative Cost: \$116,726

12/1/2010 Day: 6

Completion

NC #3 on 12/1/2010 - Trip tbg for production. TIH w/ rods. - RU hot oil truck & thaw well. 150 psi on tbg & 350 psi on csg. RU rig pump & CWC. TOH w/ 146- jts 2 7/8, & chomp bit. PU TIH w/ NC, 2- jts 2 7/8, SN, 1- jt 2 7/8, TA, 203- jts 2 7/8. RD rig floor. ND BOP. Set TA w/ 18000 tension. NU wellhead. X- over to rod eq. PU TIH w/ 2 1/2 x 1 1/2 x 20 x 24 RHAC, 6- 1 1/2 wt bars, 30- 3/4 guided rods, 96- 3/4 plain rods, 24- 3/4 guided rods, 99- 7/8 guided rods, 2' x 7/8 pony rod, 1 1/2 x 26' polish rod. W/ tbg full stroke test rod pump to 800 psi. Good test. RD MOSU. POP @ 6:00 W/ 122" SL @ 5 SPM FINAL REPORT!! **Finalized**

Daily Cost: \$0

Cumulative Cost: \$191,839

Pertinent Files: Go to File List

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
UTU-73088

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.

8. Lease Name and Well No.
HAWKEYE FEDERAL 13-23-8-16

9. AFI Well No.
43-013-50132

10. Field and Pool or Exploratory
Greater Monument Butte

11. Sec., T., R., M., on Block and Survey or Area
SEC.23, T8S, R16

12. County or Parish
DUCHESNE

13. State
UT

14. Date Spudded
09/24/2010

15. Date T.D. Reached
11/09/2010

16. Date Completed
12/01/2010
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5513 GL 5525' KB

18. Total Depth: MD **6690'**
TVD

19. Plug Back T.D.: MD **7333'**
TVD

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
**SD, DSN, DL, MSF
DUAL IND CRD, SP, COMP, DENSITY, COMP, NEUTRON, GR, CALIPER, CMT BOND**

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sks. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	342.8	354.65		180 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	6627.85	6683.12		310 PRIMLITE		306'	
NEW						440 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 6486'	TA @6388'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Green River	4960	6406	4960-6406	.36"	123	
B)						
C)						
D)						

26. Perforation Record

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
Green River	Frac w/ 110190#'s of 20/40 sand in 975 bbls of Lightning 17 fluid # 5 stages.

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
12-2-10	12-20-10	24	→	60.00	31.82	1.67			2-1/2" x 1-1/2" x 20'x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
	SI		→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
	SI		→						

RECEIVED
JAN 12 2011

(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
		24	→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD AND USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
Green River	4960	6406		GARDEN GULCH MRK	4131
				GARDEN GULCH 1	4344
				GARDEN GULCH 2	4471
				POINT 3	4751
				X MRKR	5003
				Y MRKR	5035
				DOUGALS CREEK MRK	5163
				BI CARBONATE MRK	5429
				B LIMESTON MRK	5576
				CASTLE PEAK	6074
				BASAL CARBONATE	6478
				WASATCH	6608

32. Additional remarks (include plugging procedure):

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Monica Bradley Title Office Services Assistant
 Signature Monica Bradley Date 12/22/2010

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Daily Activity Report

Format For Sundry

HAWKEYE 13-23-8-16**8/1/2010 To 12/30/2010****HAWKEYE 13-23-8-16****Waiting on Cement****Date:** 10/16/2010

Ross #29 at 355. Days Since Spud - 8 5/8" casing w/ 180 sks Class "G" + 2% CaCl2 + 0.25#/sk Cello Flake at 15.8 ppg w/ 1.17 yield. - On 9/24/10 Ross Rig #29 spud Hawkeye 13-23-8-16, drilled 355' of 12 1/4" hole, and ran 8 jts 8 5/8" - Returned 5 bbls to pit. - casing (guide shoe, shoe jt, baffle plate, 7 jts) set @ 354.65' KB. On 10/3/10 BJ Services cemented

Daily Cost: \$0**Cumulative Cost:** \$49,685**HAWKEYE 13-23-8-16****Drill 7 7/8" hole with fresh water****Date:** 11/6/2010

NDSI SS #1 at 1043. 1 Days Since Spud - MIRU W/ Liddell Trucking 4 miles - R/U B&C quickestest Test Kelly,safty valve,choke manifold,Pipe and blind rams @ 2000 PSI - P/U Smith PDC 7 7/8" BIT,.33 MM,Hathaway dir. Tools, 6" DC - Drill 7 7/8" Hole F/290' 1043' w/12 WOB, 170 TRPM, 370 GPM, 75 ROP - Surface csg @ 1500 PSI - test good

Daily Cost: \$0**Cumulative Cost:** \$85,664**HAWKEYE 13-23-8-16****Drill 7 7/8" hole with fresh water****Date:** 11/7/2010

NDSI SS #1 at 4431. 2 Days Since Spud - Rig sevice funtion test pipe rams - Drill 7 7/8" Hole F/1043' - 1307' w/20 WOB, 170 TRPM, 350 GPM, 175 ROP - Drill 7 7/8" Hole F/1307' - 4431' w/20 WOB, 170 TRPM, 350 GPM, 142 ROP

Daily Cost: \$0**Cumulative Cost:** \$111,664**HAWKEYE 13-23-8-16****Drill 7 7/8" hole with fresh water****Date:** 11/8/2010

NDSI SS #1 at 6455. 3 Days Since Spud - Drill 7 7/8" Hole F/4431' - 6430' w/20 WOB, 170 TRPM, 350 GPM, 96 ROP - Drill 7 7/8" Hole F/6430' - 6455' w/20 WOB, 170 TRPM, 350 GPM, 96 ROP - Work on Top drive hoses

Daily Cost: \$0**Cumulative Cost:** \$152,564**HAWKEYE 13-23-8-16****Running casing****Date:** 11/9/2010

NDSI SS #1 at 6690. 4 Days Since Spud - R/U and start running csg - R/U Halliburton run DISGL/SP/GR suite TD to surface- DSN/SDL/GR/CAL suite TD to 3000' (LTD 6686') - Test csg rams @ 2000 psi - Lay down DP,BHA and Dir tools - Drill 7 7/8" Hole F/6455' - 6690' w/20 WOB, 170 TRPM, 350 GPM, 96 ROP - Circulate for logs

Daily Cost: \$0**Cumulative Cost:** \$201,936**HAWKEYE 13-23-8-16****Wait on Completion****Date:** 11/10/2010

NDSI SS #1 at 6690. 5 Days Since Spud - CMT w/BJ Pump 310 sks PL II +3% KCL +5#CSE+0.5#CF+2#KOL+.5SMS+FP+SF mixed @ 11ppg - yield @ 3.54 Then tail of 440 sk 50:50:2+3%KCL+0.5%EC-1+.25# SK CF+.05#SF+.3SMS+FP-6L - Mixed @ 14.4 ppg yeild @ 1.24 return 38 bbls to pit Bump plug to 2440 psi - Nipple down set 5.5 csg slips w/ 110,000# tention - Release rig @ 7:00 pm on 11/9/10 - R/U run 159 jt 5.5 15.5# j-55 LTC-tag -GS set @ 6683.12' KB -FC set @ 6639.35' KB(TAGGED @ 6680') - Circulate csg w/rig pump - Clean Mud tanks - Tear down **Finalized**

Daily Cost: \$0

Cumulative Cost: \$323,734

Pertinent Files: Go to File List
