

**STATE OF UTAH**  
DEPARTMENT OF NATURAL RESOURCES  
DIVISION OF OIL, GAS AND MINING

FORM 3  
AMENDED REPORT

<b>APPLICATION FOR PERMIT TO DRILL</b>		<b>1. WELL NAME and NUMBER</b> Ute Tribal 6-26-4-3
<b>2. TYPE OF WORK</b> DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>		<b>3. FIELD OR WILDCAT</b> UNDESIGNATED
<b>4. TYPE OF WELL</b> Oil Well Coalbed Methane Well: NO		<b>5. UNIT or COMMUNITIZATION AGREEMENT NAME</b>
<b>6. NAME OF OPERATOR</b> NEWFIELD PRODUCTION COMPANY		<b>7. OPERATOR PHONE</b> 435 646-4825
<b>8. ADDRESS OF OPERATOR</b> Rt 3 Box 3630 , Myton, UT, 84052		<b>9. OPERATOR E-MAIL</b> mcrozier@newfield.com
<b>10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE)</b> 14-20-H62-6154	<b>11. MINERAL OWNERSHIP</b> FEDERAL <input type="checkbox"/> INDIAN <input checked="" type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>	
<b>12. SURFACE OWNERSHIP</b> FEDERAL <input type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input checked="" type="checkbox"/>		<b>13. NAME OF SURFACE OWNER (if box 12 = 'fee')</b> Kenneth and Nancy Moon
<b>14. SURFACE OWNER PHONE (if box 12 = 'fee')</b>		<b>15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')</b> 20458 West East River Rd., Duchesne, UT 84021
<b>16. SURFACE OWNER E-MAIL (if box 12 = 'fee')</b>		<b>17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')</b>
<b>18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS</b> YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>		<b>19. SLANT</b> VERTICAL <input checked="" type="checkbox"/> DIRECTIONAL <input type="checkbox"/> HORIZONTAL <input type="checkbox"/>

20. LOCATION OF WELL	FOOTAGES	QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN
<b>LOCATION AT SURFACE</b>	1981 FNL 1998 FWL	SE	26	4.0 S	3.0 W	U
<b>Top of Uppermost Producing Zone</b>	1981 FNL 1998 FWL	SE	26	4.0 S	3.0 W	U
<b>At Total Depth</b>	1981 FNL 1998 FWL	SE	26	4.0 S	3.0 W	U

<b>21. COUNTY</b> DUCHESNE	<b>22. DISTANCE TO NEAREST LEASE LINE (Feet)</b> 1981	<b>23. NUMBER OF ACRES IN DRILLING UNIT</b> 40
	<b>25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed)</b> 1335	<b>26. PROPOSED DEPTH</b> MD: 6840 TVD: 6840
<b>27. ELEVATION - GROUND LEVEL</b> 5626	<b>28. BOND NUMBER</b> RLB0010462	<b>29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE</b> 43-7478

**ATTACHMENTS**

**VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES**

<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER	<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN
<input checked="" type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)	<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER
<input type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)	<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP

<b>NAME</b> Mandie Crozier	<b>TITLE</b> Regulatory Tech	<b>PHONE</b> 435 646-4825
<b>SIGNATURE</b>	<b>DATE</b> 04/21/2010	<b>EMAIL</b> mcrozier@newfield.com
<b>API NUMBER ASSIGNED</b> 43013503150000	<b>APPROVAL</b>  Permit Manager	

**Proposed Hole, Casing, and Cement**

<b>String</b>	<b>Hole Size</b>	<b>Casing Size</b>	<b>Top (MD)</b>	<b>Bottom (MD)</b>		
Prod	7.875	5.5	0	6840		
<b>Pipe</b>	<b>Grade</b>	<b>Length</b>	<b>Weight</b>			
	Grade J-55 LT&C	6840	15.5			


**Proposed Hole, Casing, and Cement**

<b>String</b>	<b>Hole Size</b>	<b>Casing Size</b>	<b>Top (MD)</b>	<b>Bottom (MD)</b>		
Surf	12.25	8.625	0	300		
<b>Pipe</b>	<b>Grade</b>	<b>Length</b>	<b>Weight</b>			
	Grade J-55 ST&C	300	24.0			


# T4S, R3W, U.S.B.&M.

## NEWFIELD EXPLORATION COMPANY

WELL LOCATION, 6-26-4-3, LOCATED AS SHOWN IN THE SE 1/4 NW 1/4 OF SECTION 26, T4S, R3W, U.S.B.&M. DUCHESNE COUNTY, UTAH.

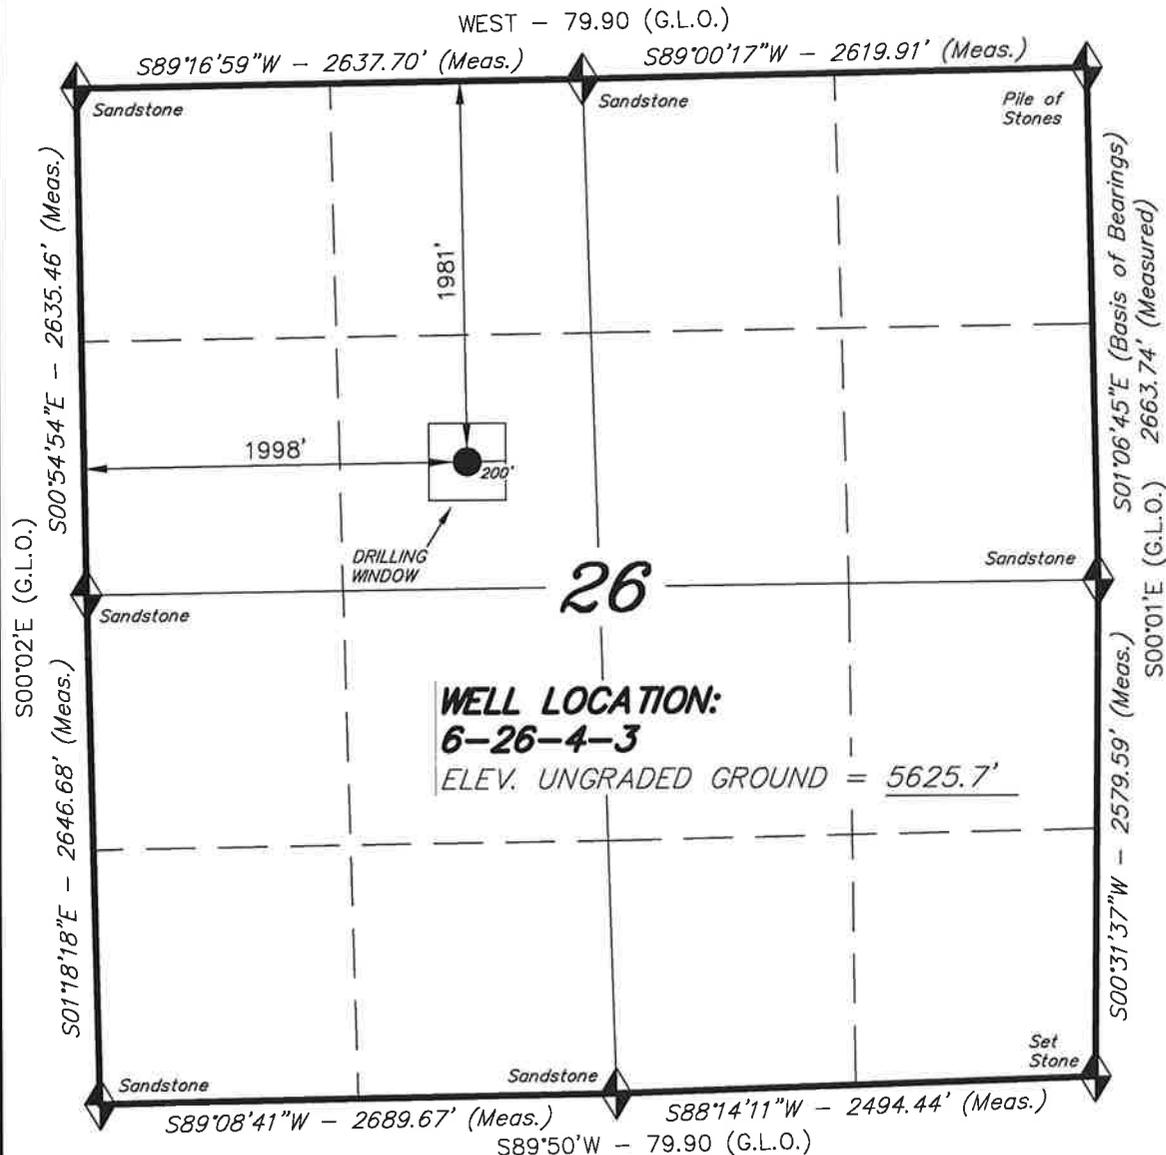

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF. 189377



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are base on LOCATION: an N.G.S. OPUS Correction. LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'

6-26-4-3  
(Surface Location) NAD 83  
LATITUDE = 40° 06' 27.77"  
LONGITUDE = 110° 11' 31.53"

### TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078  
(435) 781-2501

DATE SURVEYED: 03-15-10	SURVEYED BY: C.D.S.
DATE DRAWN: 03-16-10	DRAWN BY: F.T.M.
REVISED:	SCALE: 1" = 1000'

MEMORANDUM Ent 413009 Bk A562 Pg 88  
of Date: 27-FEB-2009 9:09AM  
EASEMENT, RIGHT-OF-WAY Fee: \$14.00 Check  
and Filed By: CBM  
SURFACE USE AGREEMENT CAROLYNE MADSEN, Recorder  
DUCHESNE COUNTY CORPORATION  
Fr: NEWFIELD ROCKY MOUNTAIN

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 20th day of January, 2009 by and between Kenneth and Nancy Moon, whose address is 20458 West East River Rd, Duchesne, UT 84021, ("Surface Owner," whether one or more) and Newfield Production Company, a Texas corporation ("NEWFIELD"), with offices at 1001 17th Street, Suite 2000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Duchesne County, Utah described as follows:

Township 4 South, Range 3 West

Section 13 All

Section 23 NW ¼, NWSW, NESW, & SWSW

Section 26 Beg. at the SW corner of said section 26 and running thence N 89° 58' 29" E 3,072.57 feet M/L; thence N 15° 26' 04" W 1681.90 feet M/L; thence N 74° 42' 37" E 2718.06 feet M/L to the East line of section 26; thence following the East line of section 26 to the NE corner of said section; thence West along the North line of section 26 to the NW corner of said section; thence South along the West line of said section 26 to the point of beg. Excluding the acre parcel in the NENW quarter quarter being approximately described as follows: Beg. at a point which is S 49° 00' 00" W 300 feet M/L from the North quarter corner of said section 26; thence South 208 feet M/L; thence West 208 feet M/L; thence North 208 feet M/L; thence East 208 feet M/L to the point of beg.

Duchesne County, Utah  
being 1447.89 acres, more or less

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

1. Compensation for Well; Release of All Claims

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated January 20th 2009, as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

2. Grant of Right of Way and Easement

Surface Owner hereby grants, bargains, leases, assigns, and conveys to NEWFIELD an easement and right-of-way for the purpose of construction, using and maintaining access roads, locations for surface equipment and subsurface gathering lines for each well drilled upon the Lands, pipelines, and pipeline interconnections for two years from date of this agreement and so long thereafter as NEWFIELD's oil and gas leases remain in effect.


This Agreement shall be binding upon the respective heirs, executors, administrators, successors, and assigns of the undersigned. This agreement replaces and supersedes any and all prior agreements covering the lands described herein.


These Parties hereto have executed this document effective as of the day first above written.

SURFACE OWNER

By:   
Kenneth Moon

NEWFIELD PRODUCTION COMPANY

By:   
Gary D. Packer, President

By:   
Nancy Moon



NEWFIELD PRODUCTION COMPANY  
UTE TRIBAL 6-26-4-3  
SE/NW SECTION 26, T4S, R3W  
DUCHESNE COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0' – 1,720'
Green River	1,720'
Wasatch	6,590'
Proposed TD	6,840'

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil) 1,720' – 6,590'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sample Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO <sub>3</sub> ) (mg/l)
Dissolved Bicarbonate (NaHCO <sub>3</sub> ) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO <sub>4</sub> ) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: Ute Tribal 6-26-4-3**

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950	1,370	244,000
						17.53	14.35	33.89
Prod casing 5-1/2"	0'	6,840'	15.5	J-55	LTC	4,810	4,040	217,000
						2.21	1.86	2.05

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg  
 Pore pressure at surface casing shoe = 8.33 ppg  
 Pore pressure at prod casing shoe = 8.33 ppg  
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: Ute Tribal 6-26-4-3**

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft <sup>3</sup> /sk)
			ft <sup>3</sup>			
Surface casing	300'	Class G w/ 2% CaCl	138	30%	15.8	1.17
			161			
Prod casing Lead	4,840'	Prem Lite II w/ 10% gel + 3% KCl	334	30%	11.0	3.26
			1090			
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363	30%	14.3	1.24
			451			

- \*Actual volume pumped will be 15% over the caliper log
- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ±350 feet will be drilled with an air/mist system. The air rig is equipped with a 6 ½" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ±350 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTB to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated

bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.

10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the third quarter of 2010, and take approximately seven (7) days from spud to rig release.

# 2-M SYSTEM

Blowout Prevention Equipment Systems


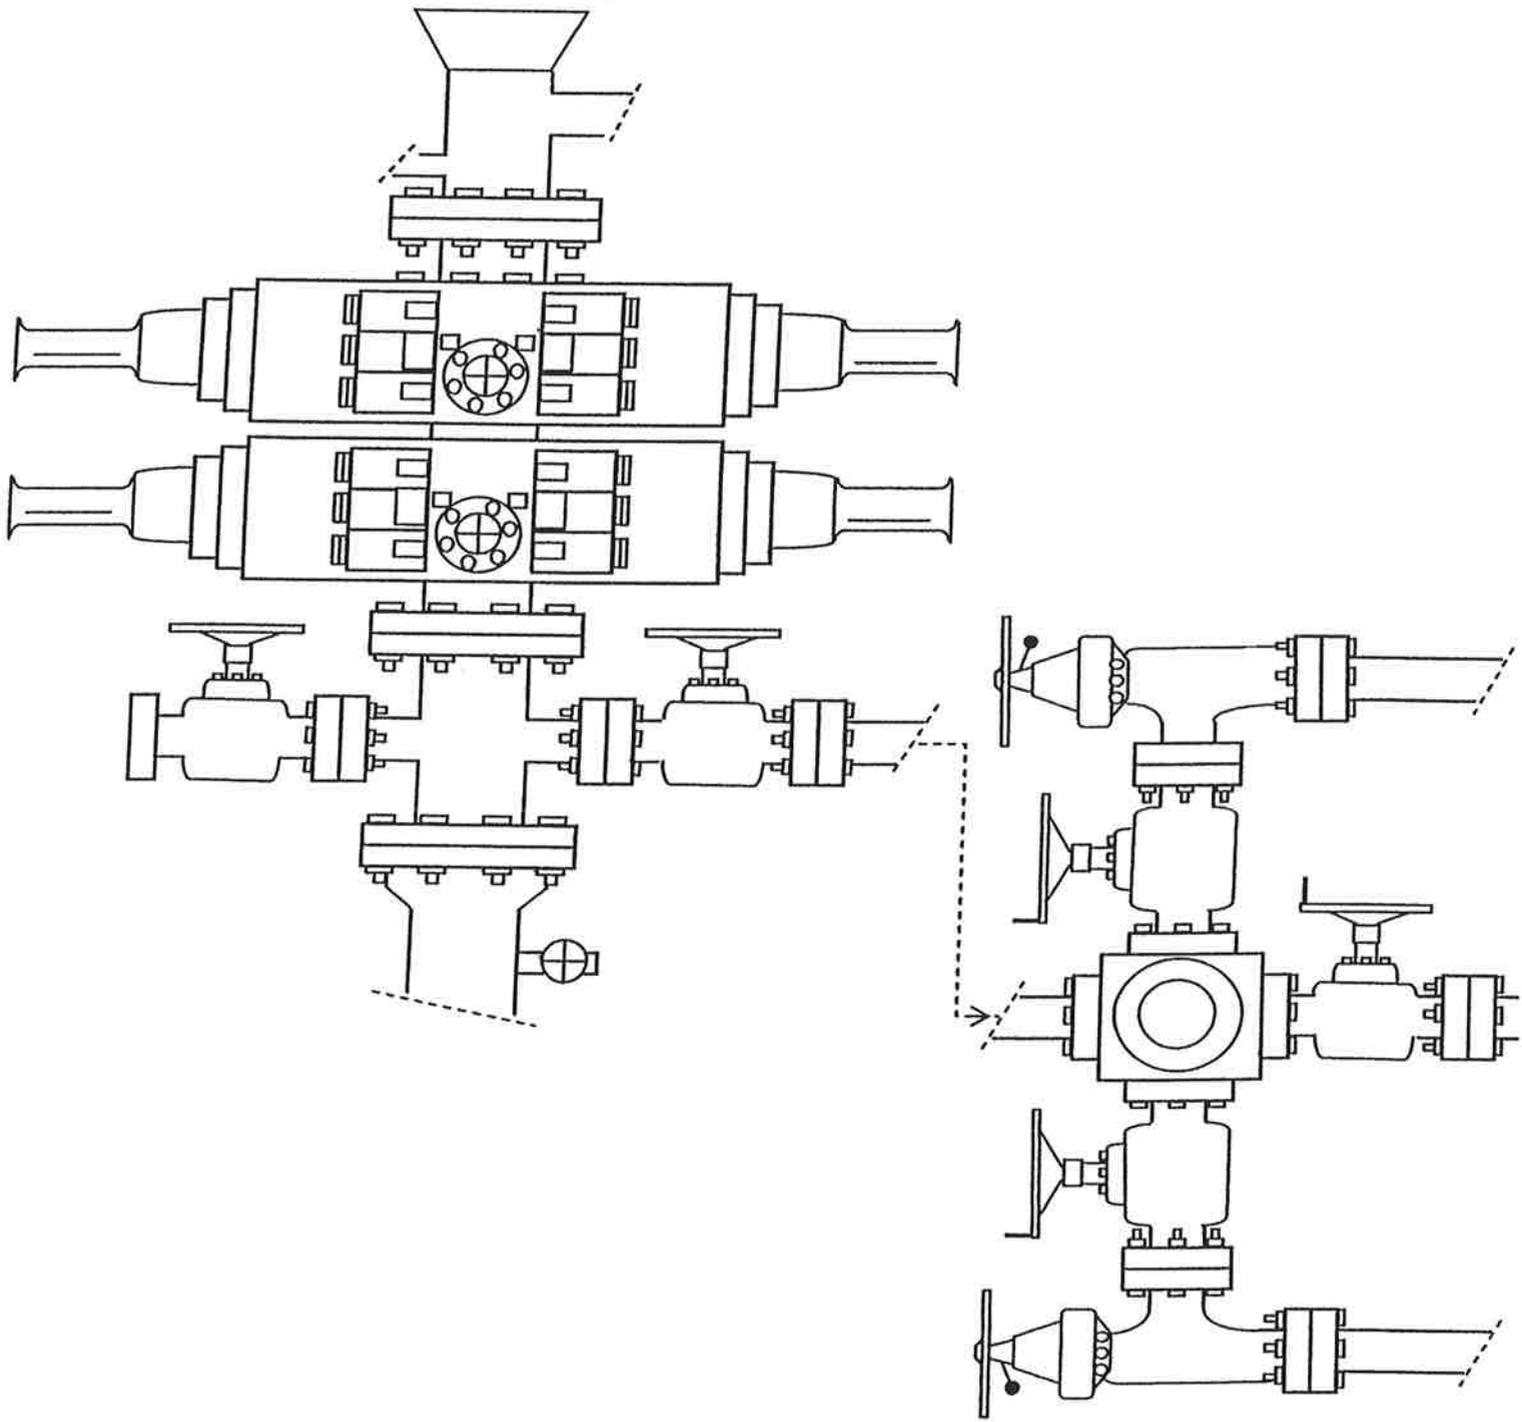


EXHIBIT C



**NEWFIELD**  
Exploration Company

**6-26-4-3**  
**SEC. 26, T4S, R3W, U.S.B.&M.**

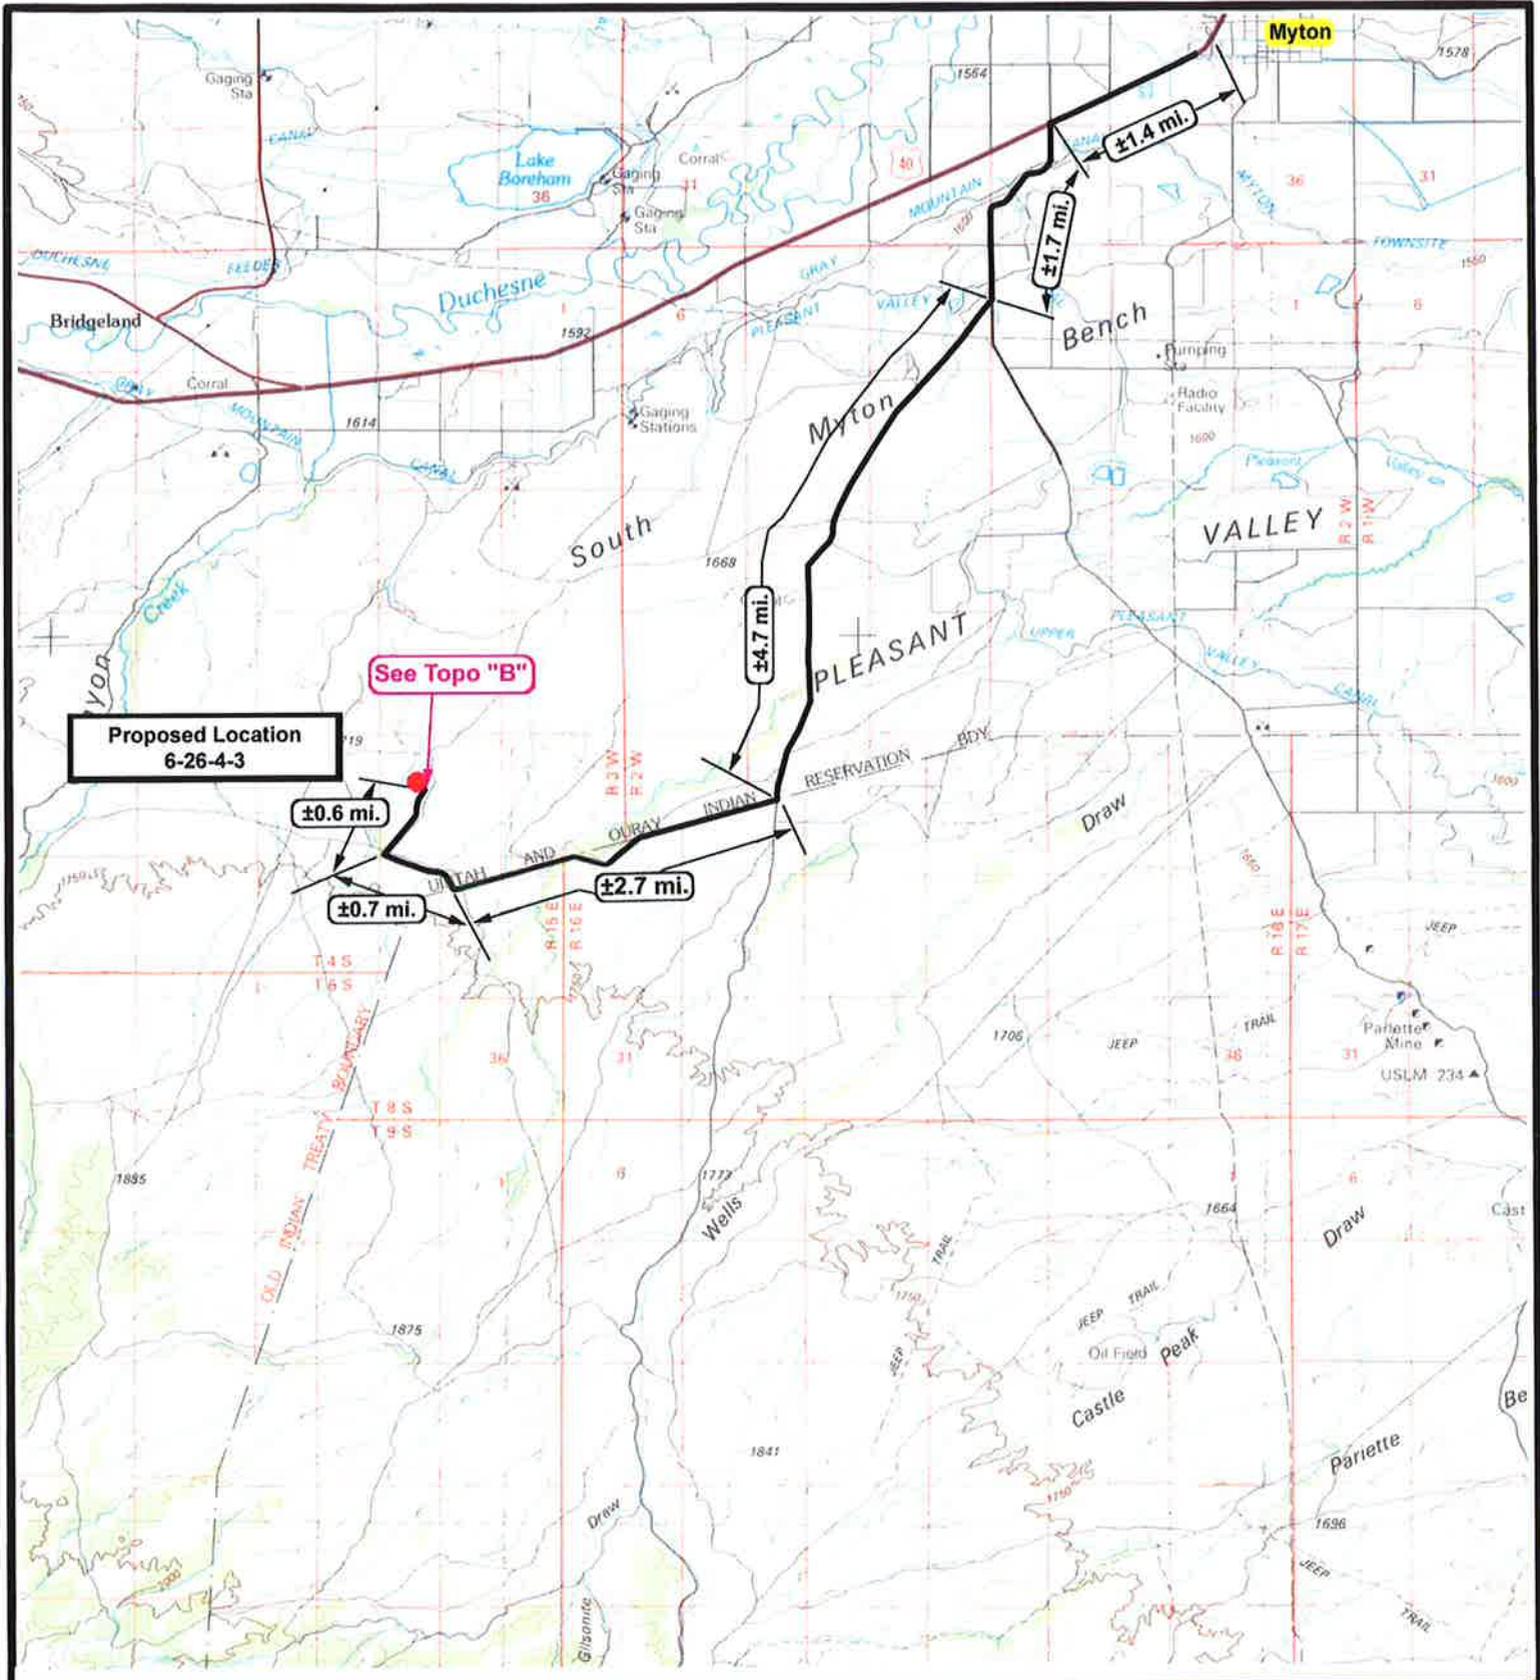


**Tri-State**  
*Land Surveying Inc.*  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

**SCALE: 1 : 100,000**  
**DRAWN BY: JAS**  
**DATE: 03-16-2010**

**Legend**

- Existing Road
- Proposed Access

**TOPOGRAPHIC MAP**  
**"A"**

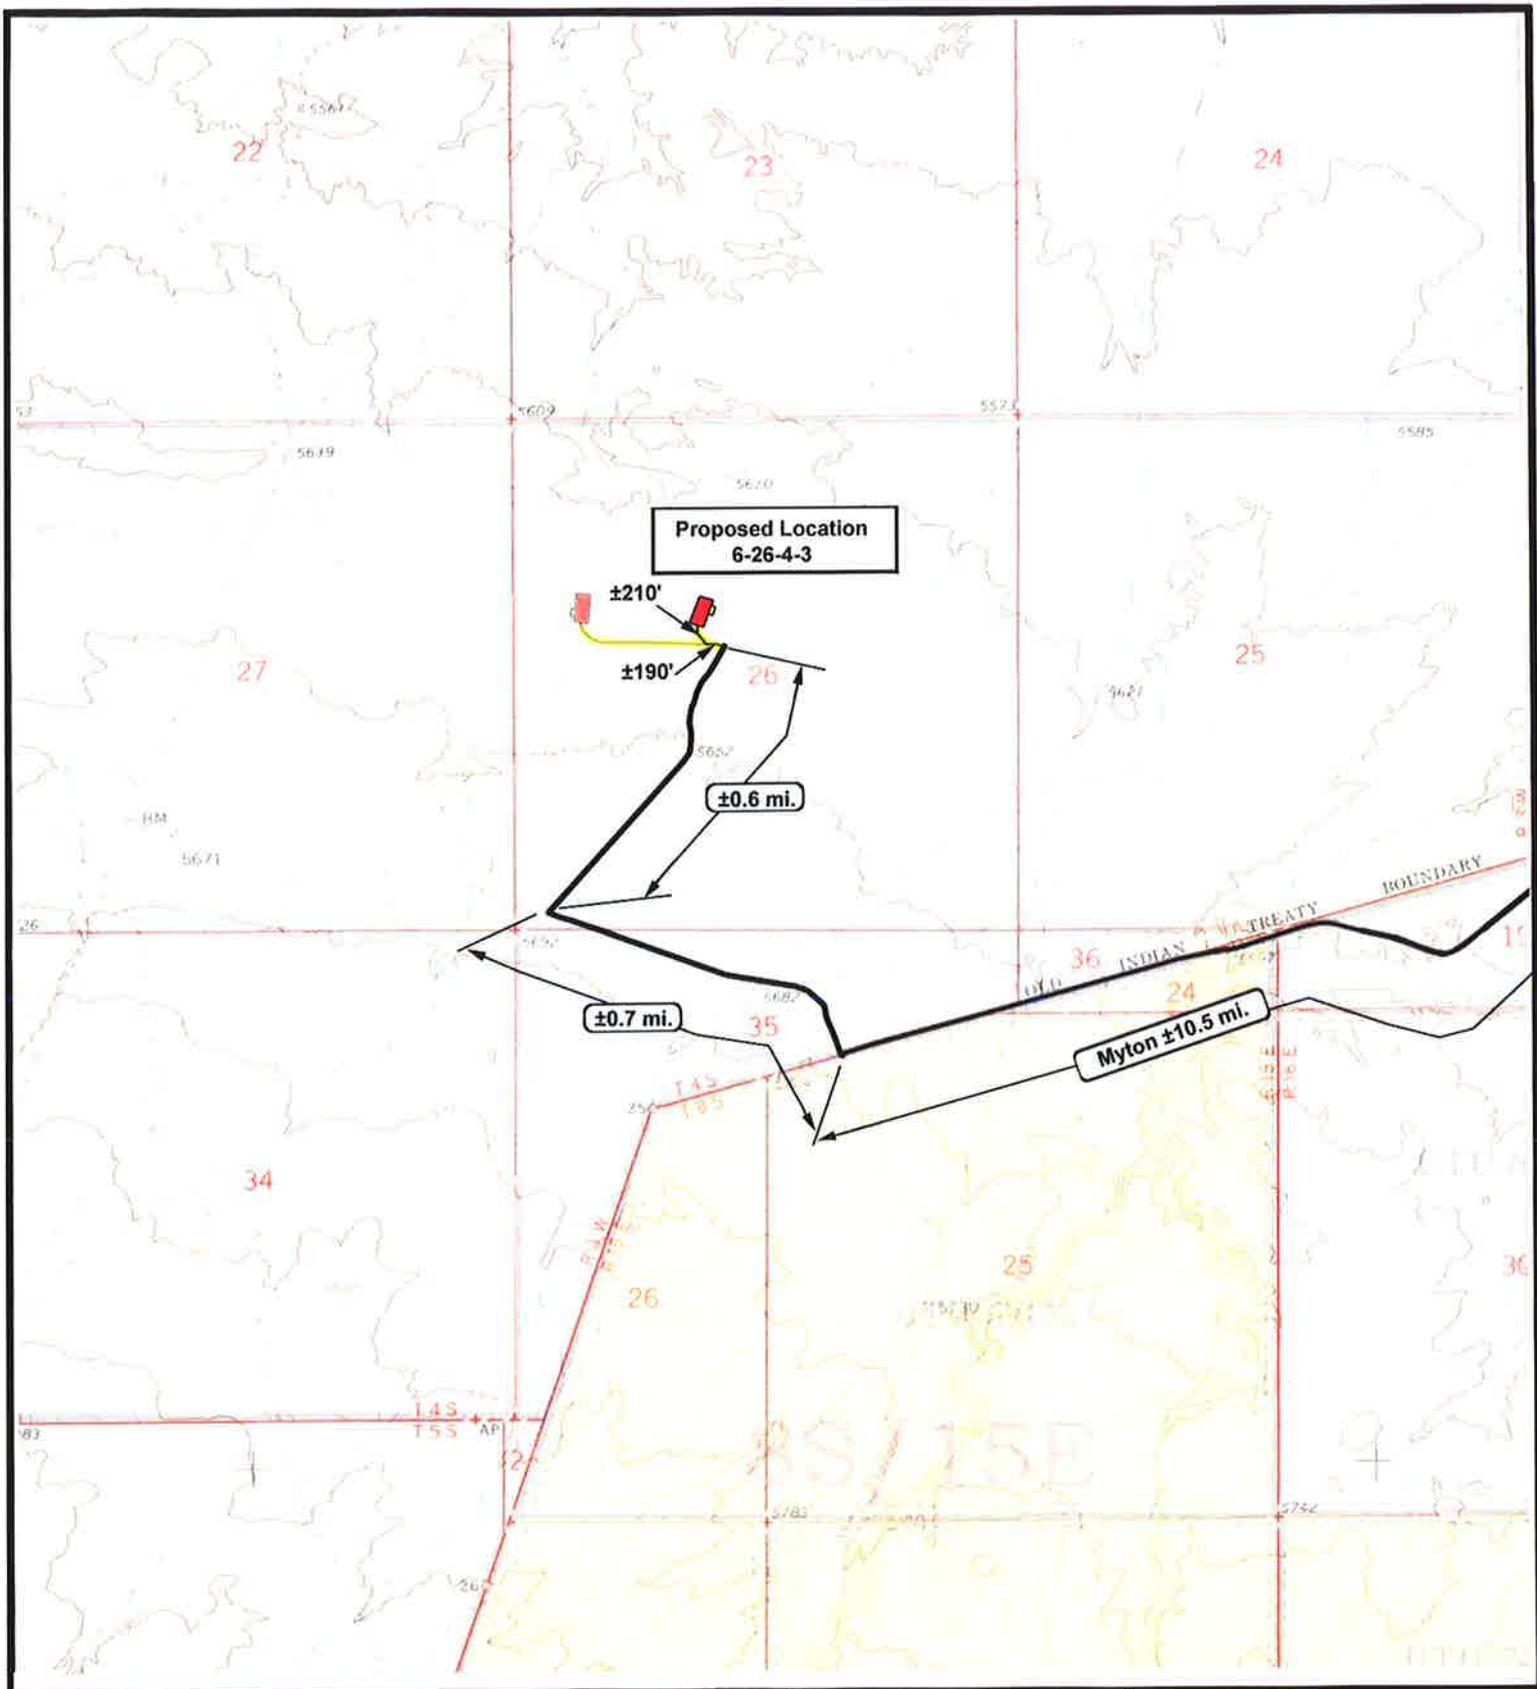

**6-26-4-3**  
**SEC. 26, T4S, R3W, U.S.B.&M.**




*Tri-State*  
Land Surveying Inc.  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

**SCALE: 1" = 2,000'**  
**DRAWN BY: JAS**  
**DATE: 03-16-2010**


**Legend**

- Existing Road
- Proposed Access

**TOPOGRAPHIC MAP**  
**"B"**

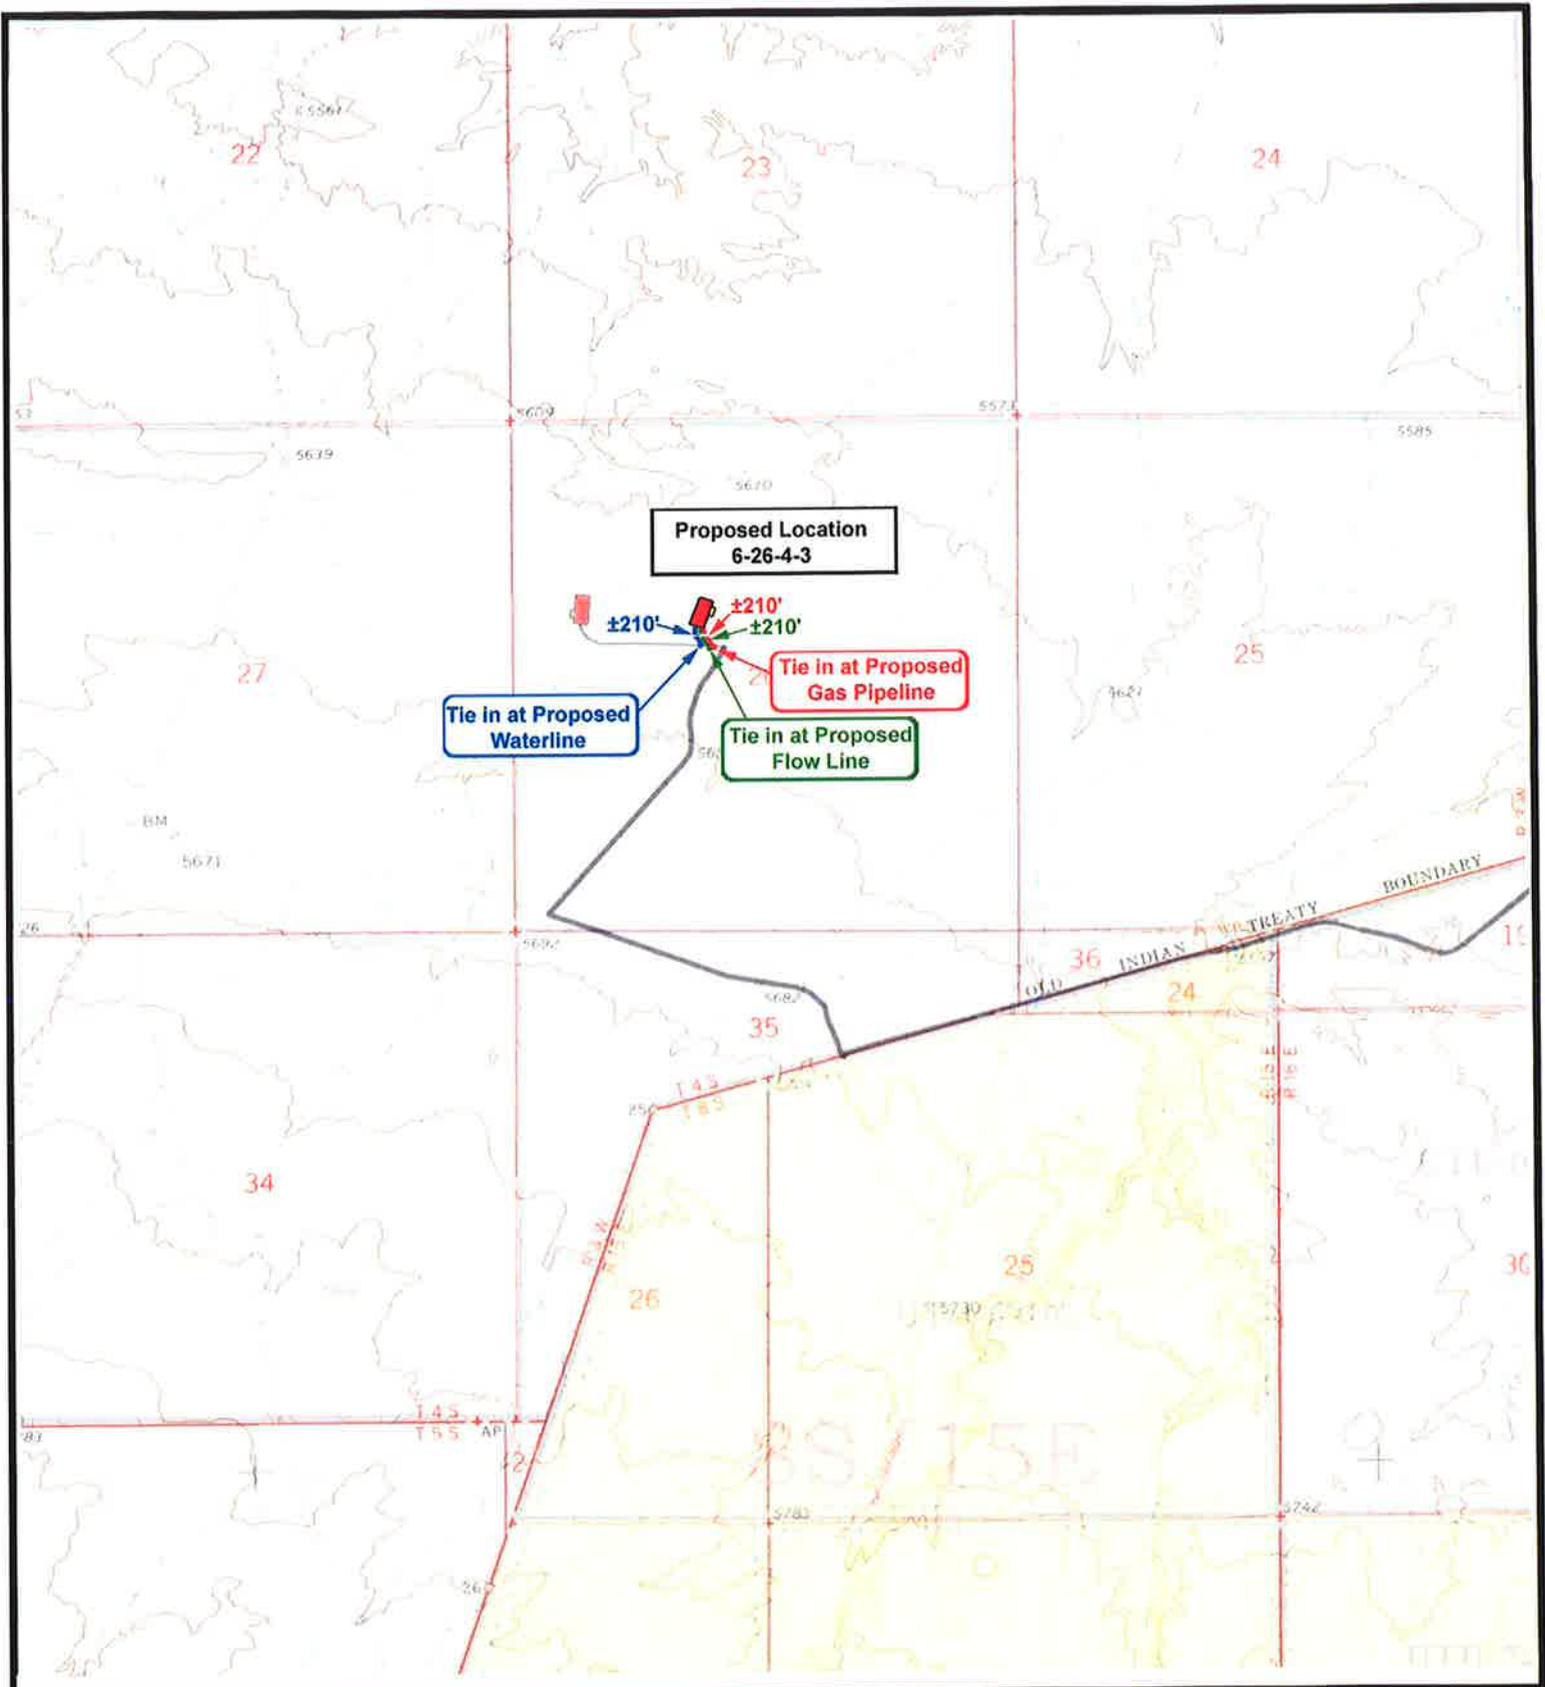

**6-26-4-3**  
**SEC. 26, T4S, R3W, U.S.B.&M.**




*Tri-State*  
*Land Surveying Inc.*  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

**SCALE: 1" = 2,000'**  
**DRAWN BY: JAS**  
**DATE: 03-16-2010**

Legend	
	Roads
	Proposed Gas Line
	Proposed Water Line
	Proposed Flow Line

**TOPOGRAPHIC MAP**  
**"C"**



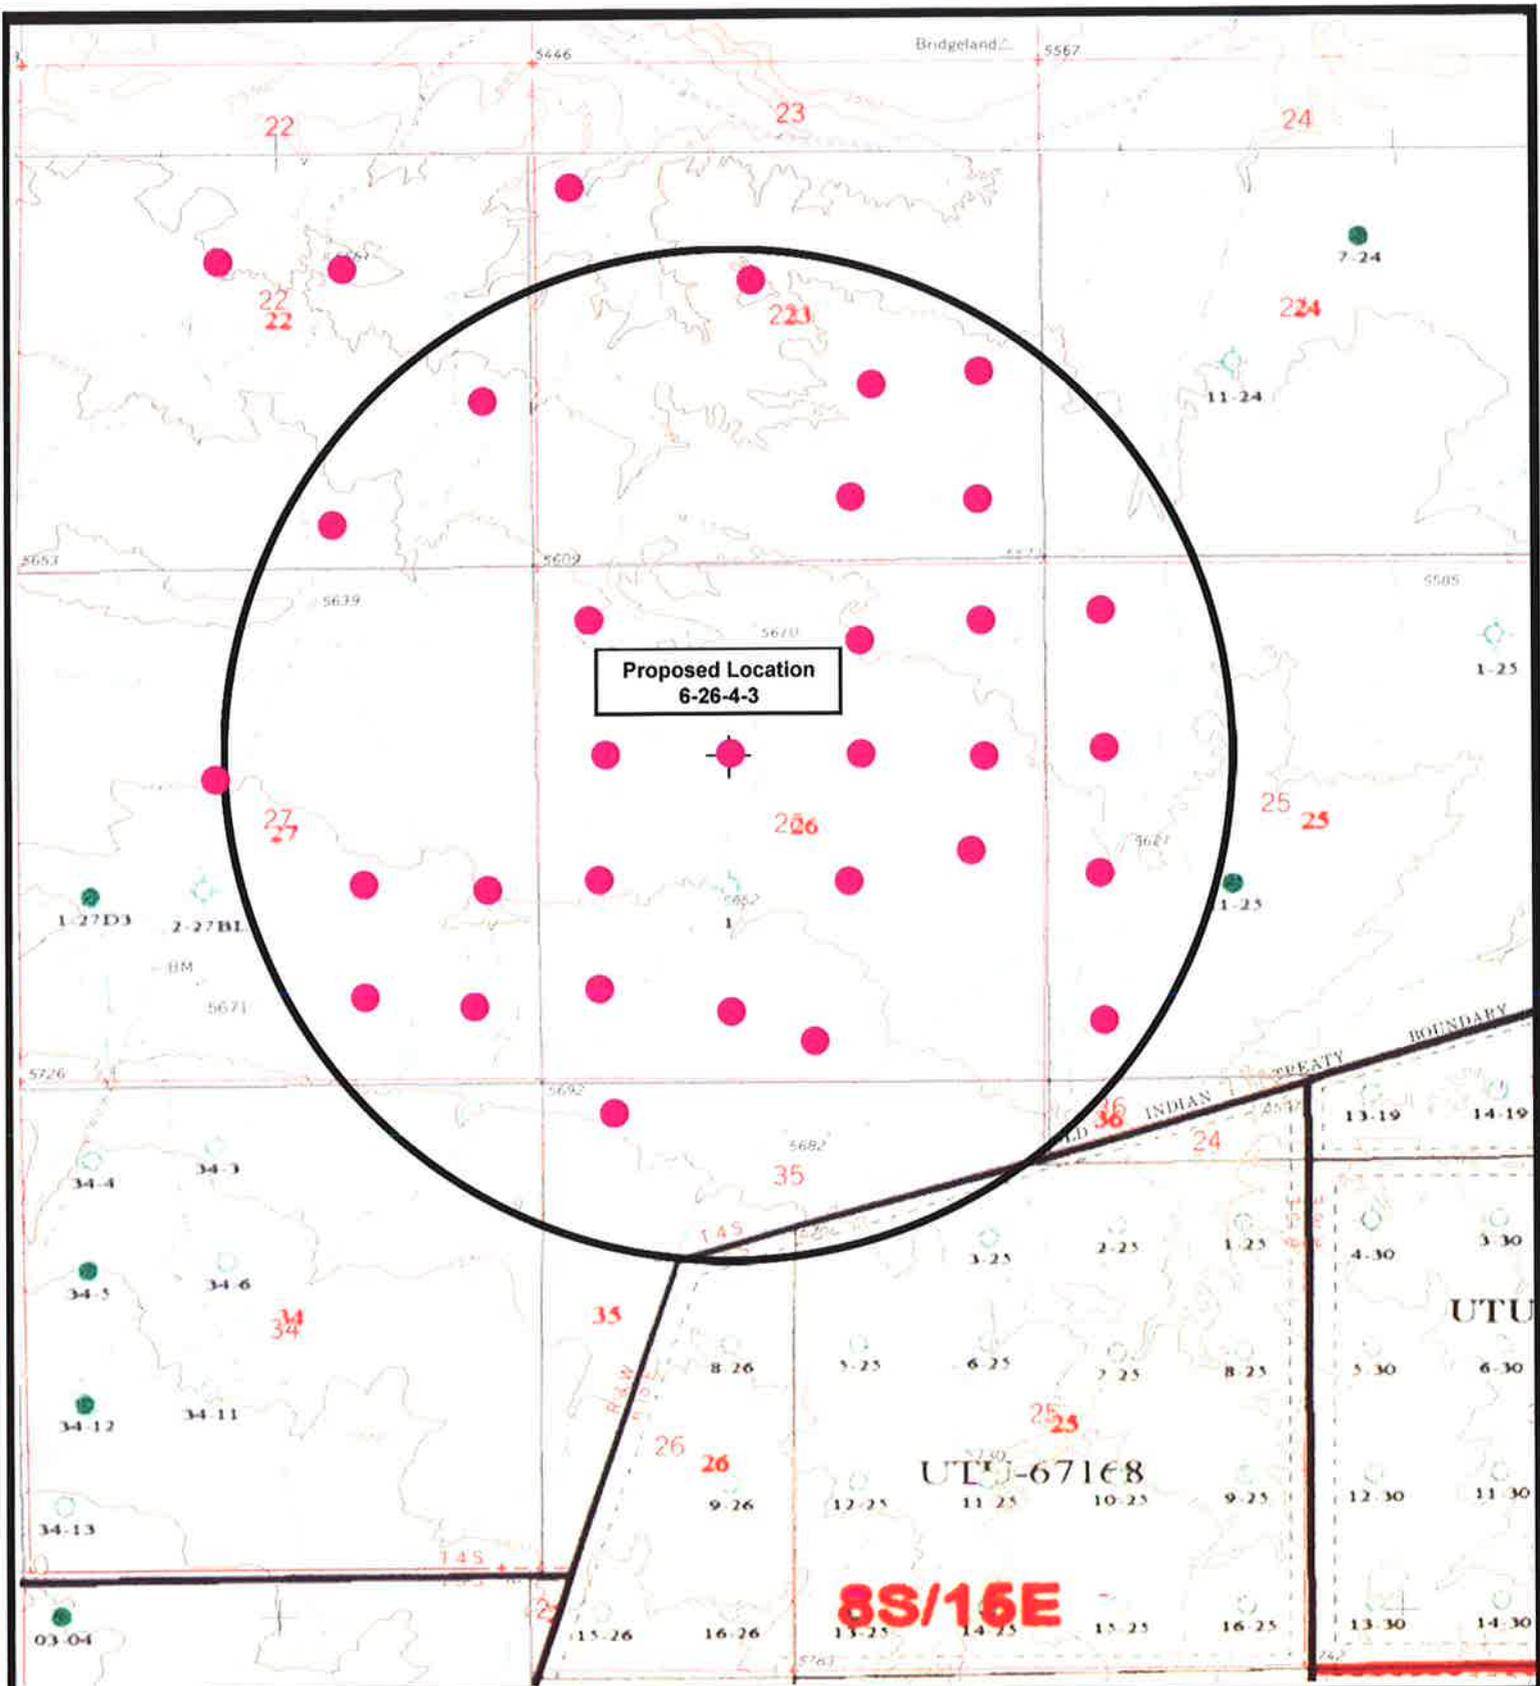

Proposed Location  
6-26-4-3

UTU-67168

**8S/16E**



**NEWFIELD**  
Exploration Company

**6-26-4-3**  
**SEC. 26, T4S, R3W, U.S.B.&M.**



*Tri-State*  
Land Surveying Inc.  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

**SCALE: 1" = 2,000'**  
**DRAWN BY: JAS**  
**DATE: 03-16-2010**

**Legend**

- Pad Location
- One-Mile Radius

**Exhibit "B"**

**NEWFIELD PRODUCTION COMPANY  
UTE TRIBAL 6-26-4-3  
SE/NW SECTION 26, T4S, R3W  
DUCHESNE COUNTY, UTAH**

**ONSHORE ORDER NO. 1**

**MULTI-POINT SURFACE USE & OPERATIONS PLAN**

**1. EXISTING ROADS**

See attached Topographic Map "A"

To reach Newfield Production Company well location site Ute Tribal 6-26-4-3 located in the SE 1/4 NW 1/4 Section 26, T4S, R3W, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 approximately 1.4 miles  $\pm$  to the junction of this highway and UT State Hwy 53; proceed southwesterly approximately 6.4 miles  $\pm$  to it's junction with an existing road to the southwest; proceed southwesterly approximately 2.7 miles to it's junction with an existing road to the northwest; proceed northwesterly approximately 0.7 miles  $\pm$  to it's junction with an existing road to the northeast; proceed in a northeasterly direction approximately 0.6 miles  $\pm$  to it's junction with the beginning of the proposed access road to the west; proceed northwesterly along the proposed access road approximately 400' to the proposed well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

**2. PLANNED ACCESS ROAD**

Approximately 400' of access road is proposed for the proposed well. See attached **Topographic Map "B"**.

The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

**3. LOCATION OF EXISTING WELLS**

Refer to Exhibit "B".

4. **LOCATION OF EXISTING AND/OR PROPOSED FACILITIES**

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District  
Water Right : 43-7478

Neil Moon Pond  
Water Right: 43-11787

Newfield Collector Well  
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), State of Utah approved surface disposal facilities, or Federally approved surface disposal facilities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

**Fencing Requirements**

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be

reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – Kenneth and Nancy Moon.  
See attached Memorandum of Surface Use Agreement and Easement ROW.

12. **OTHER ADDITIONAL INFORMATION**

Newfield Production Company requests 400' of disturbed area be granted to allow for construction of the planned access road. **Refer to Topographic Map "B"**. A permanent width of 30' and a running surface of 18' is proposed for the planned access road. The construction phase of the planned access road will last approximately (5) days. The planned access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 210' of disturbed area be granted for construction of the proposed gas lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a 6" gas gathering line, and a 3" poly fuel gas line, with a permanent width of 30' upon completion of the proposed gas lines. The construction phase of the proposed gas lines will last approximately (5) days. Both proposed lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."**

Newfield Production Company requests 210' of disturbed area be granted to allow for construction of the proposed water lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line and 30' wide upon completion of the proposed water lines. Both proposed lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** In the event that the proposed well is converted to a water injection well, a separate injection permit will be applied for through the proper agencies.

**Surface Flow Line**

Newfield Production Company requests 210' of disturbed area be granted for construction of a surface flow line bundle. For all new wells, Newfield requests that a 30' Right of way be granted to allow for construction of up to a 14" bundled pipe consisting of 2-2" poly glycol lines and 1-3" production line. Refer to Topographic Map "C" for the proposed location of the proposed flow line. Flow lines will be tan and will be constructed using the following procedures:

Clearing and Grading: the proposed flow line will be placed on the surface of the ground. As such no grading or clearing will be needed. The flow line will be centered staked every 200 feet prior to the installation. The flow line will be as close to the access road as possible without interfering with the normal road travel, or road maintenance

Installation for portions along existing roads, lengths of pipe will be laid in the barrow ditch, welded together and moved into place. For lines that go cross-country minimal access will be needed only for maintenance purpose. It is in the best interest of Newfield Exploration to avoid wet and saturated ground that would cause ruts greater than 3 inches in depth. Disturbed areas will be reclaimed with in 120 days of the end of the installation.

- a) Newfield Production Company is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, Newfield is to immediately stop work that might further disturb such materials and contact the Authorized Officer.
- b) Newfield Production will control noxious weeds along rights-of-way for roads, pipelines, well sites or other applicable facilities. On State administered land it is required that a Pesticide Use Proposal shall be submitted and given approval prior to the application of herbicides or other possible hazardous chemicals.
- c) Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on State Lands after the conclusion of drilling operations or at any other time without State authorization. However, if State authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

The Archaeological and Paleontological Report Waiver is attached.

#### **Additional Surface Stipulations**

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

#### **Hazardous Material Declaration**

Newfield Production Company guarantees that during the drilling and completion of the Ute Tribal 6-26-4-3, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Ute Tribal 6-26-4-3, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

The State office as well as the Ute Tribe Energy and Mineral Department shall be notified upon site completion prior to moving on the drilling rig.

#### 13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

##### Representative

Name: Tim Eaton  
Address: Newfield Production Company  
Route 3, Box 3630  
Myton, UT 84052  
Telephone: (435) 646-3721

Certification

Please be advised that Newfield Production Company is considered to be the operator of well #6-26-4-3, SE/NW Section 26, T4S, R3W, Duchesne County, Utah and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage for this well is covered by the Bureau of Indian Affairs Bond #RLB0010462.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

4/21/10

Date




Mandie Crozier  
Regulatory Specialist  
Newfield Production Company

# NEWFIELD EXPLORATION COMPANY

## LOCATION LAYOUT

6-26-4-3

Section 26, T4S, R3W, U.S.B.&M.

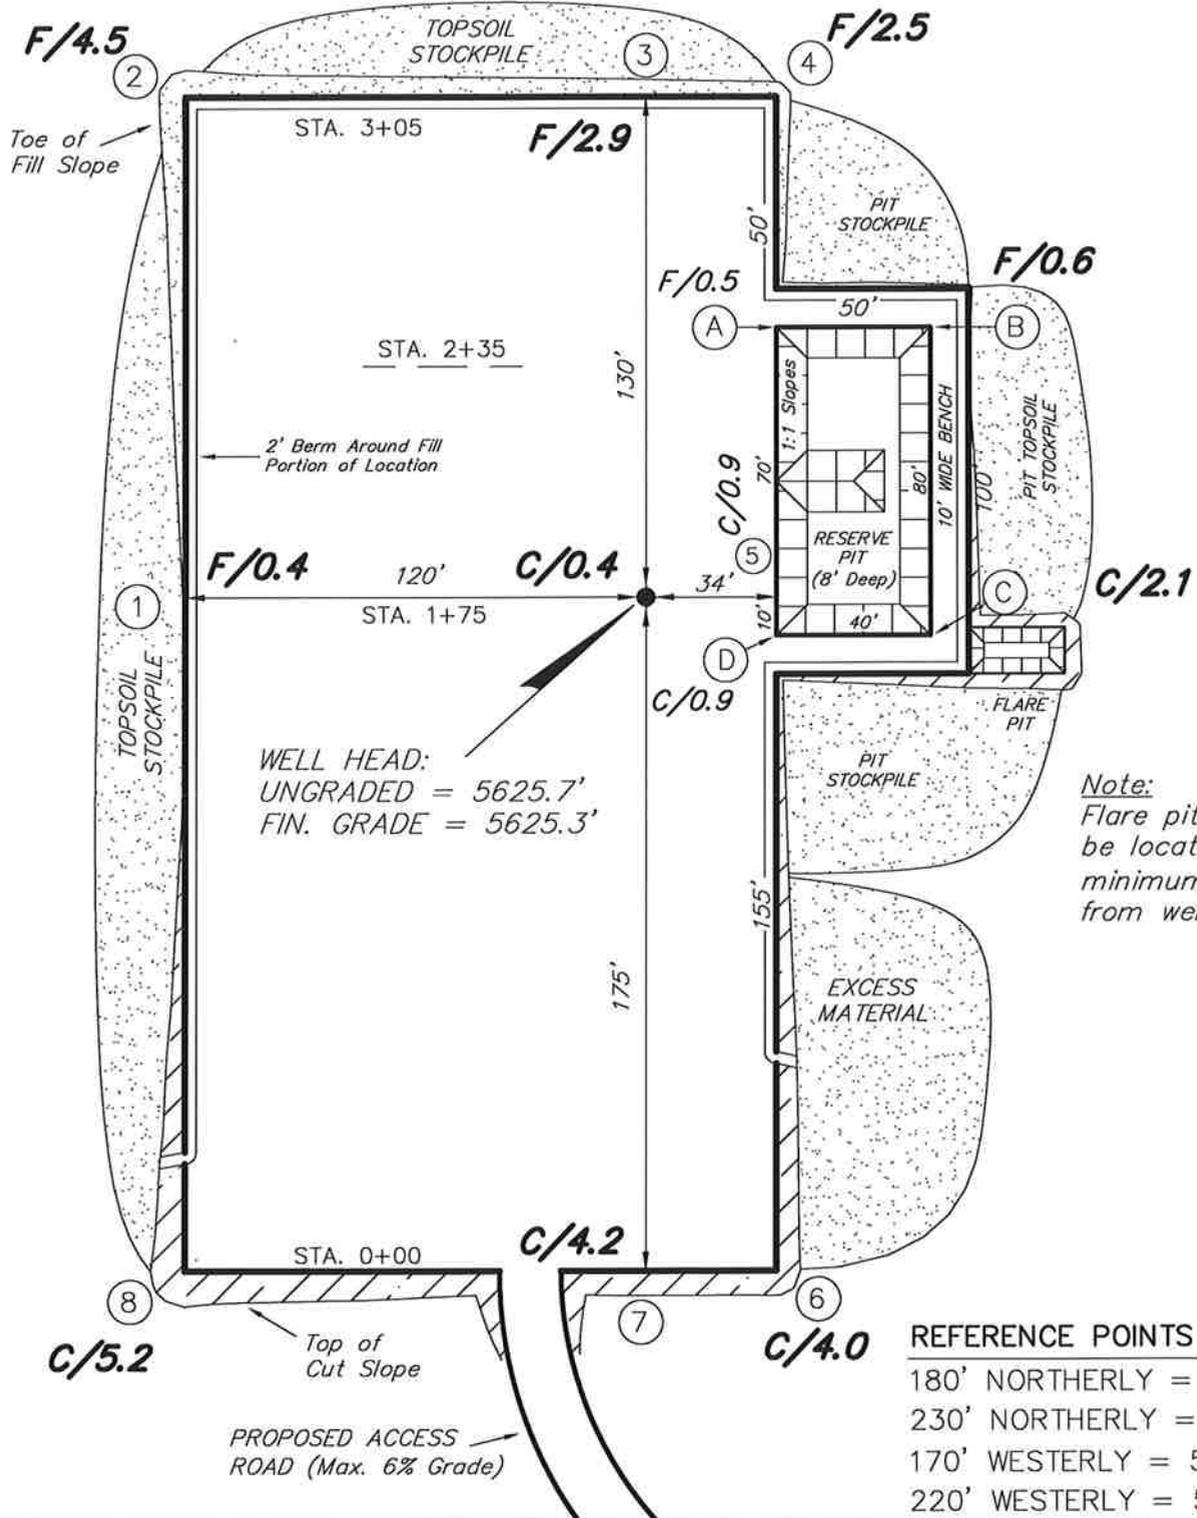

WELL HEAD:  
UNGRADED = 5625.7'  
FIN. GRADE = 5625.3'

*Note:*  
Flare pit is to be located a minimum of 80' from well head.

**REFERENCE POINTS**

180' NORTHERLY	= 5621.9'
230' NORTHERLY	= 5624.3'
170' WESTERLY	= 5624.2'
220' WESTERLY	= 5623.4'

SURVEYED BY: C.D.S.	DATE SURVEYED: 03-15-10
DRAWN BY: F.T.M.	DATE DRAWN: 03-16-10
SCALE: 1" = 50'	REVISED:





**Tri State** (435) 781-2501  
**Land Surveying, Inc.**  
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

# NEWFIELD EXPLORATION COMPANY

## CROSS SECTIONS

**6-26-4-3**

*Section 26, T4S, R3W, U.S.B.&M.*

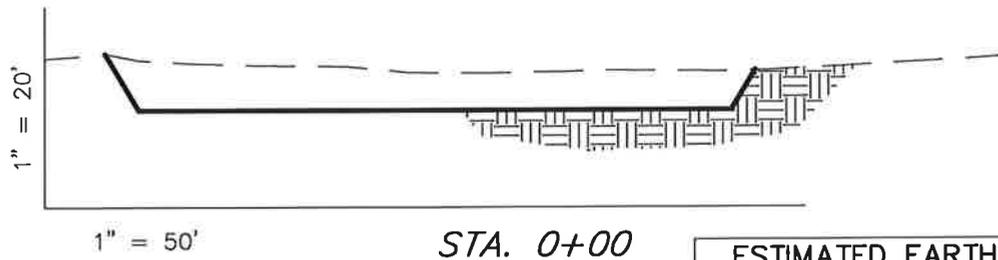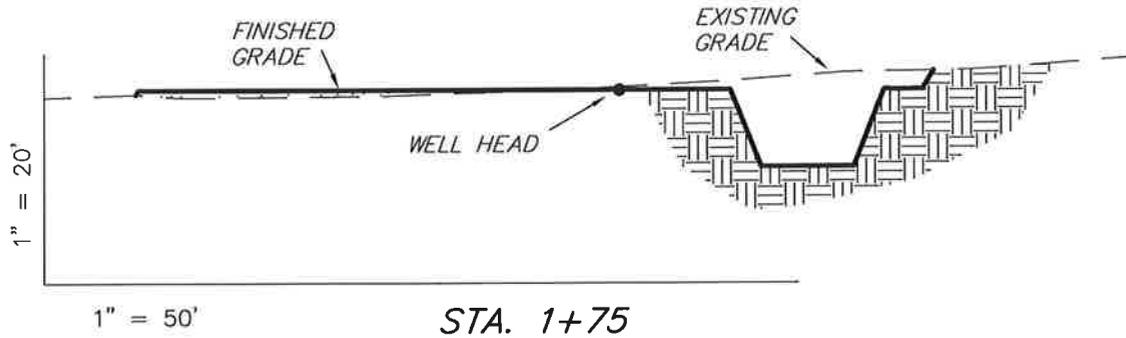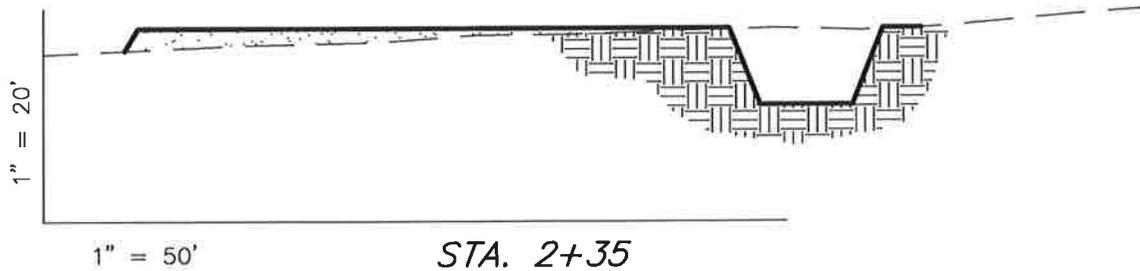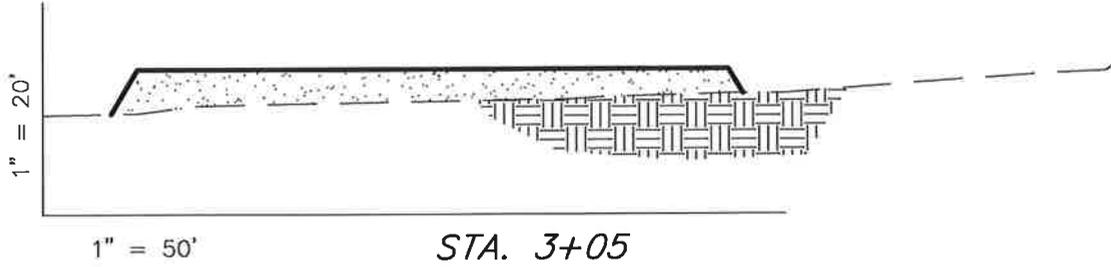

NOTE:  
UNLESS OTHERWISE  
NOTED ALL CUT/FILL  
SLOPES ARE AT 1.5:1

**ESTIMATED EARTHWORK QUANTITIES**  
(No Shrink or swell adjustments have been used)  
(Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	1,740	1,740	Topsoil is not included in Pad Cut	0
PIT	640	0		640
<b>TOTALS</b>	<b>2,380</b>	<b>1,740</b>	<b>1,050</b>	<b>640</b>

SURVEYED BY: C.D.S.	DATE SURVEYED: 03-15-10	
DRAWN BY: F.T.M.	DATE DRAWN: 03-16-10	
SCALE: 1" = 50'	REVISED:	


*Tri State* (435) 781-2501  
**Land Surveying, Inc.**  
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

# NEWFIELD EXPLORATION COMPANY

## TYPICAL RIG LAYOUT

6-26-4-3

Section 26, T4S, R3W, U.S.B.&M.

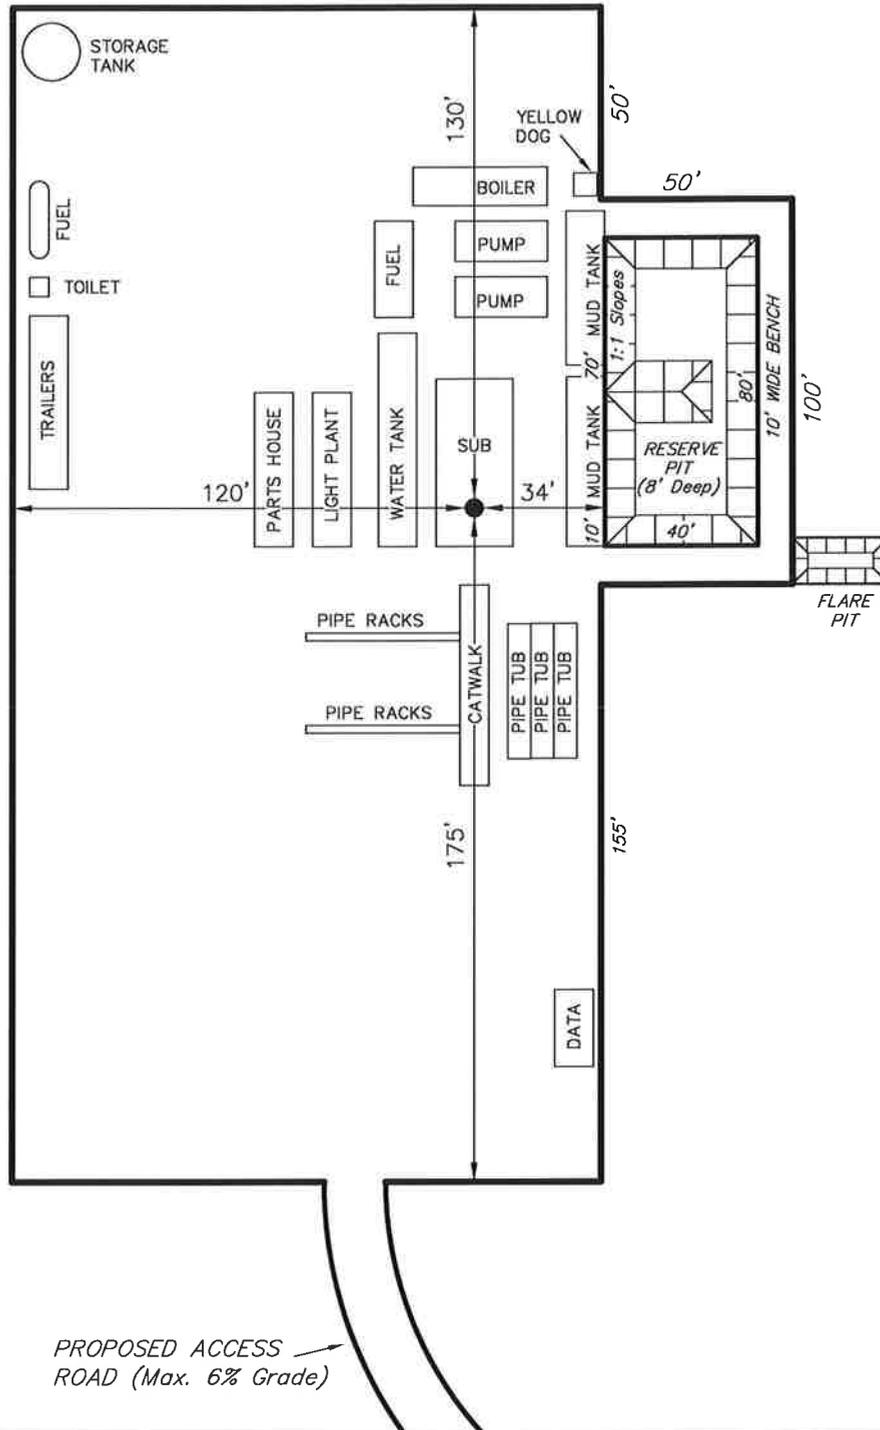

SURVEYED BY: C.D.S.	DATE SURVEYED: 03-15-10
DRAWN BY: F.T.M.	DATE DRAWN: 03-16-10
SCALE: 1" = 50'	REVISED:

**Tri State** (435) 781-2501  
 Land Surveying, Inc.  
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078


# Newfield Production Company Proposed Site Facility Diagram

Ute Tribal 6-26-4-3

SE/NW Sec. 26, T4S, R3W

Duchesne County, Utah

14-20-H62-6154

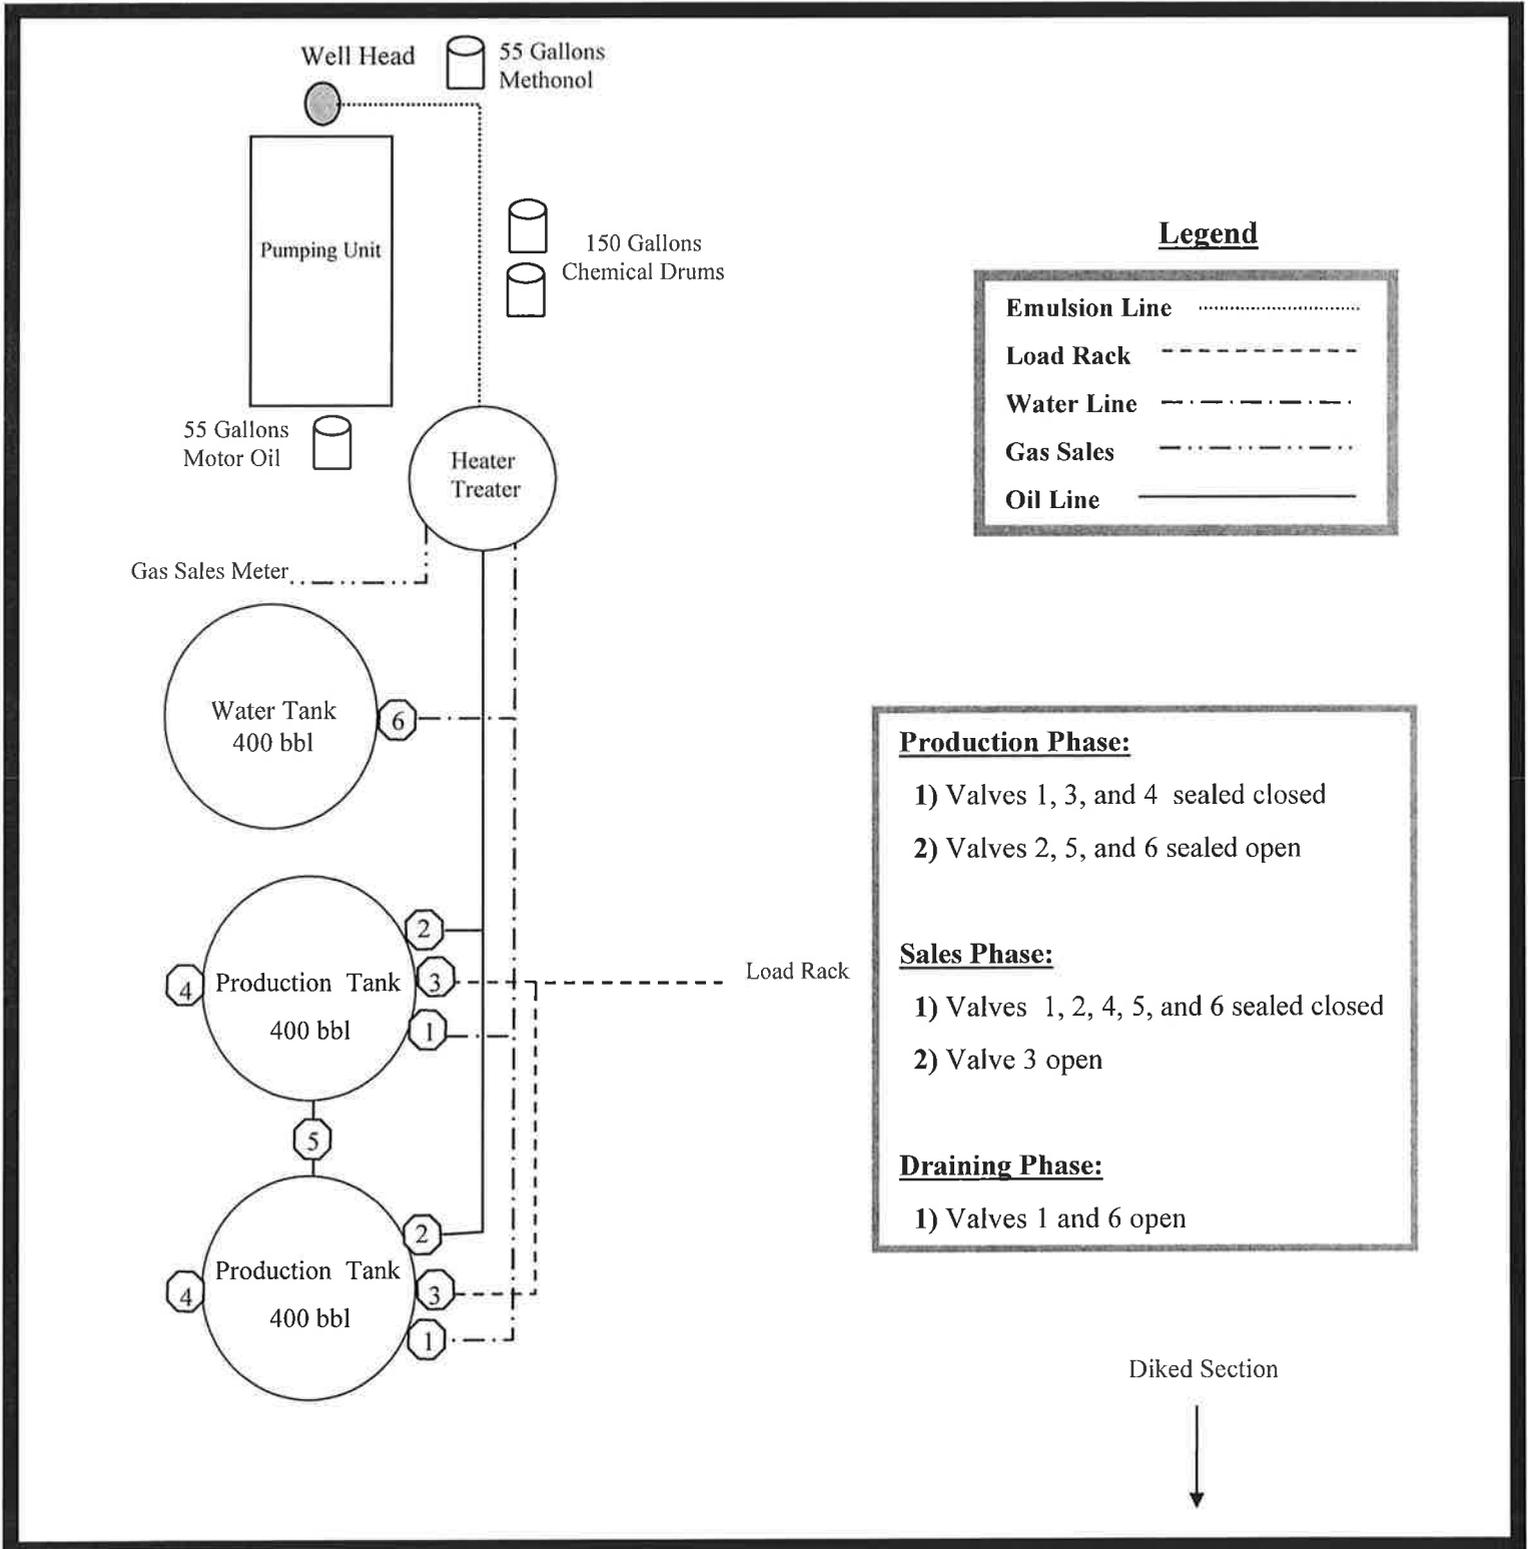

### Legend

Emulsion Line	.....
Load Rack	-----
Water Line	-.-.-.-
Gas Sales	-.-.-.-
Oil Line	————

### Production Phase:

- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open

### Sales Phase:

- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

### Draining Phase:

- 1) Valves 1 and 6 open

**EXHIBIT D**

Township 4 South, Range 3 West

Section 13 All

Section 23 NW ¼, NWSW, NESW, & SWSW

Section 26 Beg. at the SW corner of said section 26 and running thence N 89° 58' 29" E 3,072.57 feet M/L; thence N 15° 26' 04" W 1681.90 feet M/L; thence N 74° 42' 37" E 2718.06 feet M/L to the East line of section 26; thence N following the East line of section 26 to the NE corner of said section; thence West along the North line of section 26 to the NW corner of said section; thence South along the West line of said section 26 to the point of beg. Excluding the 1 acre parcel in the NENW quarter quarter being approximately described as follows: Beg. at a point which is S 49° 00' 00" W 300 feet M/L from the North quarter corner of said section 26: thence South 208 feet M/L; thence West 208 feet M/L; thence North 208 feet M/L; thence East 208 feet M/L to the point of beg.


Duchesne County, Utah


**ARCHAEOLOGICAL & PALEOTOLOGICAL REPORT WAIVER**

For the above referenced location; Kenneth and Nancy Moon, the Private Surface Owner.  
(Having a Surface Owner Agreement with Newfield Production Company)

Kenneth and Nancy Moon, representing this entity does agree to waive the request from the State of Utah and Bureau of Land Management for an Archaeological/Cultural and Paleotological Resource Survey for any wells covered by the Surface Use Agreement dated 1/20/09 between the above said private land owner and Newfield Production. This waiver hereby releases Newfield Production Company from this request.

  
\_\_\_\_\_  
Kenneth Moon                      Date  
Private Surface Owner                      1-20-09



  
\_\_\_\_\_  
Brad Meham                      Date  
Newfield Production Company                      1-20-09

  
\_\_\_\_\_  
Nancy Moon                      Date  
Private Surface Owner                      1-20-09

**API Number: 4301350315**  
**Well Name: Ute Tribal 6-26-4-3**  
**Township 04.0 S Range 03.0 W Section 26**  
**Meridian: UBM**  
 Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:  
 Map Produced by Diana Mason

<b>Units</b>	<b>Wells Query</b>
<b>STATUS</b>	<-all other values>
ACTIVE	APD - Approved Permit
EXPLORATORY	DRL - Spudded (Drilling Commenced)
GAS STORAGE	GIW - Gas Injection
NF PP OIL	GS - Gas Storage
NF SECONDARY	LA - Location Abandoned
PI OIL	LOC - New Location
PP GAS	OPS - Operation Suspended
PP GEOTHERM	PA - Plugged Abandoned
PP OIL	PGW - Producing Gas Well
SECONDARY	POW - Producing Oil Well
TERMINATED	RET - Returned APD
<b>Fields</b>	SGW - Shut-in Gas Well
Sections	SOW - Shut-in Oil Well
Township	TA - Temp. Abandoned
	TW - Test Well
	WDW - Water Disposal
	WIW - Water Injection Well
	WSW - Water Supply Well

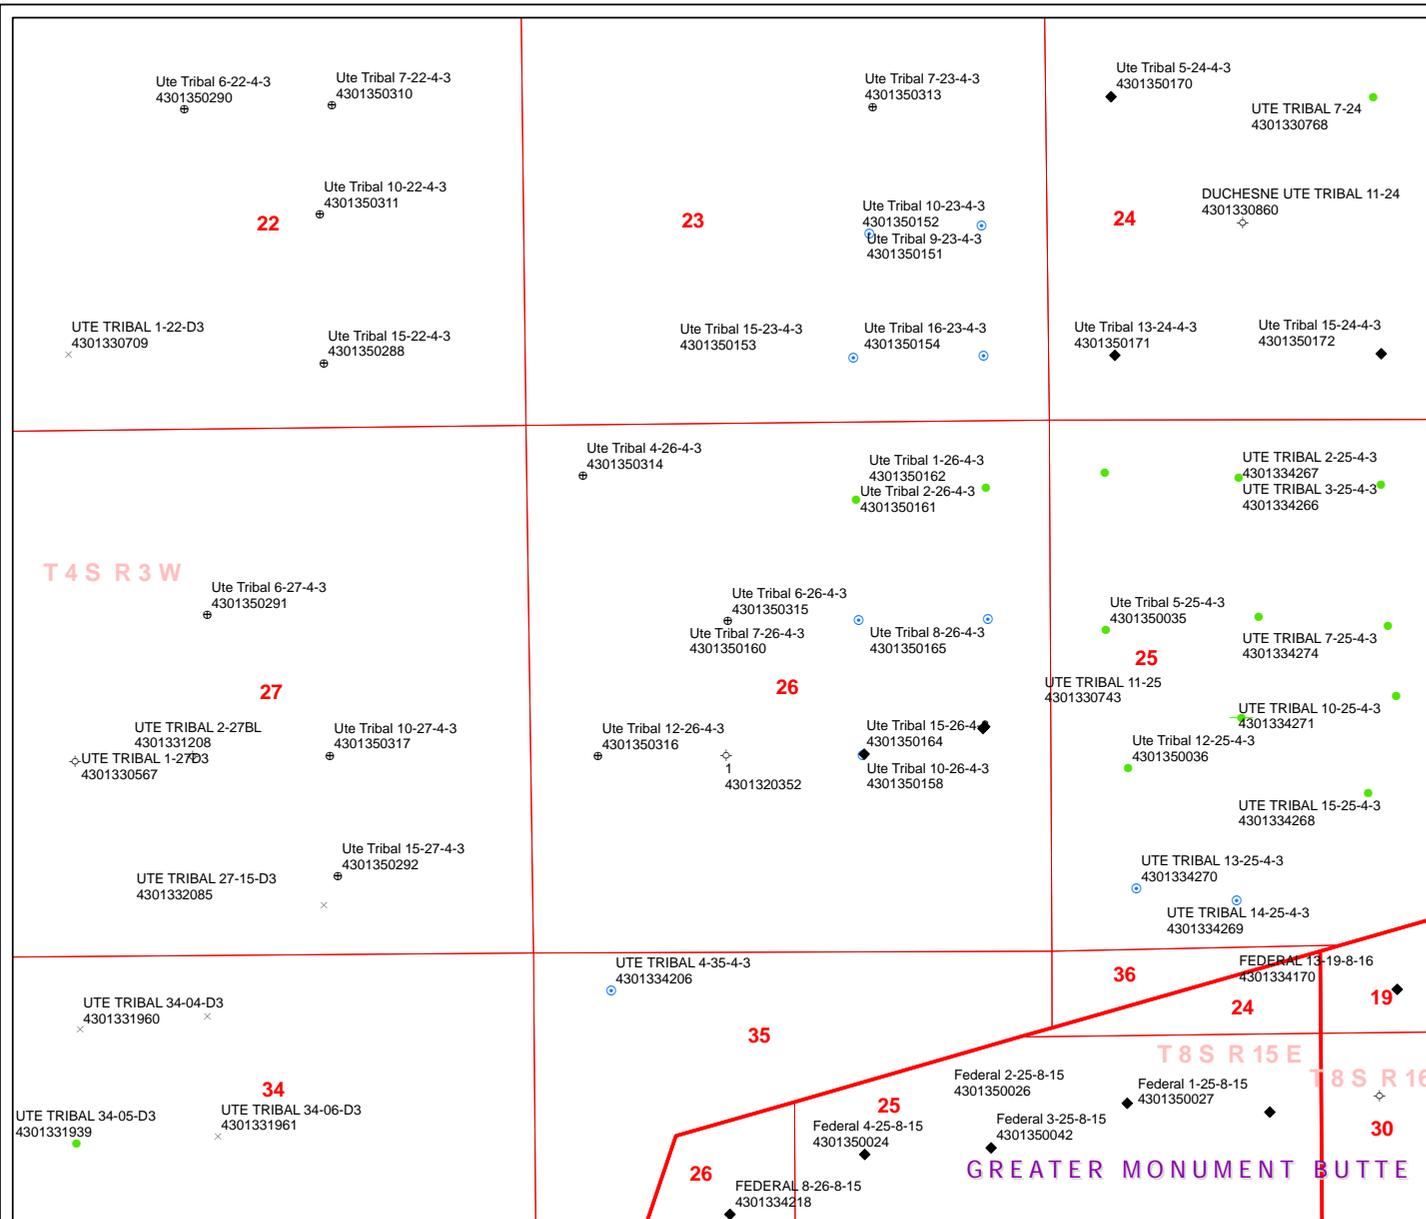

GREATER MONUMENT BUTTE

# ON-SITE PREDRILL EVALUATION

## Utah Division of Oil, Gas and Mining

**Operator** NEWFIELD PRODUCTION COMPANY  
**Well Name** Ute Tribal 6-26-4-3  
**API Number** 43013503150000      **APD No** 2572      **Field/Unit** UNDESIGNATED  
**Location: 1/4,1/4** SENW      **Sec** 26      **Tw** 4.0S      **Rng** 3.0W      1981 FNL 1998 FWL  
**GPS Coord (UTM)** 568919 4439812      **Surface Owner** Kenneth and Nancy Moon

**Participants**

Floyd Bartlett (DOGM), Joe Pippy (Newfield Permitting), Scott Vernon (Tri-State Land Surveying), Christine Cimiluca and Cheryl Laroque (BLM).

**Regional/Local Setting & Topography**

The proposed location is approximately 11.8 road miles southwest of Myton, UT in the South Myton Bench/Antelope Creek area. Drainages in the area run northerly toward the Duchesne River about 4 miles away but are intercepted by the Gray Mountain or Pleasant Valley Irrigation Canals. Broad flats and rolling hills with those near the edge of the benches becoming steep and intersected with draws, characterize the area. Access is by State, County and planned or existing oil field development roads. Approximately 400 feet of new construction across Moon’s private land will be required to reach the location.

The proposed Ute Tribal 6-26-4-3 oil well pad is laid out in a north to south direction on a flat with a gentle north slope. Some minor overland flow is occurring but no drainages are needed. A 5.2-foot cut is required at corner 8. No springs, streams or seeps are known to exist in the immediate area. The selected site appears to be a suitable location for constructing a pad, drilling and operating a well.

Kenneth Moon and Nancy Moon own the surface of the location. The BLM contacted Mr. Moon by telephone and invited him to the pre-site visit. He said he would not attend. A signed landowner agreement exists. The minerals are owned by the United States Government and held in trust for the Ute Indian Tribe.

**Surface Use Plan**

**Current Surface Use**  
 Grazing  
 Wildlife Habitat

<b>New Road Miles</b>	<b>Well Pad</b>	<b>Src Const Material</b>	<b>Surface Formation</b>
0.096	<b>Width</b> 204 <b>Length</b> 305	Onsite	UNTA

**Ancillary Facilities** N

**Waste Management Plan Adequate?**

**Environmental Parameters**

**Affected Floodplains and/or Wetlands** N

**Flora / Fauna**

A desert shrub type vegetation covers the area. Principal plants consist of mat saltbrush, Gardiner saltbrush, shadscale, curly mesquite, horse brush and annuals.

Cattle, deer, prairie dogs, small mammals and birds.

**Soil Type and Characteristics**

Deep sandy loam.

**Erosion Issues** N

**Sedimentation Issues** N

**Site Stability Issues** N

**Drainage Diversion Required?** N

**Berm Required?** Y

**Erosion Sedimentation Control Required?** N

**Paleo Survey Run?** N **Paleo Potential Observed?** N **Cultural Survey Run?** N **Cultural Resources?**

**Reserve Pit**

**Site-Specific Factors**

**Site Ranking**

<b>Distance to Groundwater (feet)</b>	100 to 200	5
<b>Distance to Surface Water (feet)</b>	>1000	0
<b>Dist. Nearest Municipal Well (ft)</b>	>5280	0
<b>Distance to Other Wells (feet)</b>	300 to 1320	10
<b>Native Soil Type</b>	Mod permeability	10
<b>Fluid Type</b>	Fresh Water	5
<b>Drill Cuttings</b>	Normal Rock	0
<b>Annual Precipitation (inches)</b>		0
<b>Affected Populations</b>		
<b>Presence Nearby Utility Conduits</b>	Not Present	0
<b>Final Score</b>		30

1 Sensitivity Level

**Characteristics / Requirements**

A reserve pit 40' x 80' x 8' deep will be located mostly in an area of cut on the northeast side of the location. Corner C has a 2.1-foot cut. With the pit stockpiles, a 10-foot bench around the edge and a 2-foot freeboard, it should be stable. A pit liner is required. Newfield commonly uses a 16-mil liner.

**Closed Loop Mud Required?** N **Liner Required?** Y **Liner Thickness** 16 **Pit Underlayment Required?** Y

**Other Observations / Comments**

ATV's were used to reach the site.

Floyd Bartlett  
**Evaluator**

5/12/2010  
**Date / Time**

# Application for Permit to Drill

## Statement of Basis

5/25/2010

### Utah Division of Oil, Gas and Mining

Page 1

<b>APD No</b>	<b>API WellNo</b>	<b>Status</b>	<b>Well Type</b>	<b>Surf Owner</b>	<b>CBM</b>
2572	43013503150000	LOCKED	OW	P	No
<b>Operator</b>	NEWFIELD PRODUCTION COMPANY		<b>Surface Owner-APD</b>	Kenneth and Nancy Moon	
<b>Well Name</b>	Ute Tribal 6-26-4-3		<b>Unit</b>		
<b>Field</b>	UNDESIGNATED		<b>Type of Work</b>	DRILL	
<b>Location</b>	SEW 26 4S 3W U 1981 FNL 1998 FWL GPS Coord (UTM) 568910E 4439819N				

#### Geologic Statement of Basis

The mineral rights for the proposed well are owned by the Ute Tribe. The BLM will be the agency responsible for evaluating and approving the drilling, casing and cement programs.

Brad Hill  
APD Evaluator

5/24/2010  
Date / Time

#### Surface Statement of Basis

The proposed location is approximately 11.8 road miles southwest of Myton, UT in the South Myton Bench/Antelope Creek area. Drainages in the area run northerly toward the Duchesne River about 4 miles away but are intercepted by the Gray Mountain or Pleasant Valley Irrigation Canals. Broad flats and rolling hills with those near the edge of the benches becoming steep and intersected with draws, characterize the area. Access is by State, County and planned or existing oil field development roads. Approximately 400 feet of new construction across Moon's private land will be required to reach the location.

The proposed Ute Tribal 6-26-4-3 oil well pad is laid out in a north to south direction on a flat with a gentle north slope. Some minor overland flow is occurring but no drainages are needed. A 5.2-foot cut is required at corner 8. No springs, streams or seeps are known to exist in the immediate area. The selected site appears to be a suitable location for constructing a pad, drilling and operating a well.

Kenneth Moon and Nancy Moon own the surface of the location. The BLM contacted Mr. Moon by telephone and invited him to the pre-site visit. He said he would not attend. A signed landowner agreement exists. The minerals are owned by the United States Government and held in trust for the Ute Indian Tribe. Acting for the Ute Indian Tribe, Ms. Christine Cimiluca and Ms. Cheryl Laroque of the BLM attended the pre-site evaluation. They specified the color of paint the facilities were to be painted and had no other surface concerns except as noted above. Reclamation of the site will be as directed in the Multi-point Operating Plan.

A reserve pit 40' x 80' x 8' deep will be located mostly in an area of cut on the northeast side of the location. Corner C has a 2.1-foot fill. With the pit stockpiles, a 10-foot bench around the edge and a 2-foot freeboard, it should be stable. A pit liner is required.

Floyd Bartlett  
Onsite Evaluator

5/12/2010  
Date / Time

#### Conditions of Approval / Application for Permit to Drill

<b>Category</b>	<b>Condition</b>
Pits	A synthetic liner with a minimum thickness of 16 mils shall be properly installed and maintained in the reserve pit.
Surface	The well site shall be bermed to prevent fluids from leaving the pad.
Surface	The reserve pit shall be fenced upon completion of drilling operations.

# WORKSHEET APPLICATION FOR PERMIT TO DRILL

**APD RECEIVED:** 4/21/2010

**API NO. ASSIGNED:** 43013503150000

**WELL NAME:** Ute Tribal 6-26-4-3

**OPERATOR:** NEWFIELD PRODUCTION COMPANY (N2695)

**PHONE NUMBER:** 435 646-4825

**CONTACT:** Mandie Crozier

**PROPOSED LOCATION:** SENW 26 040S 030W

**Permit Tech Review:**

**SURFACE:** 1981 FNL 1998 FWL

**Engineering Review:**

**BOTTOM:** 1981 FNL 1998 FWL

**Geology Review:**

**COUNTY:** DUCHESNE

**LATITUDE:** 40.10775

**LONGITUDE:** -110.19146

**UTM SURF EASTINGS:** 568910.00

**NORTHINGS:** 4439819.00

**FIELD NAME:** UNDESIGNATED

**LEASE TYPE:** 2 - Indian

**LEASE NUMBER:** 14-20-H62-6154

**PROPOSED PRODUCING FORMATION(S):** GREEN RIVER

**SURFACE OWNER:** 4 - Fee

**COALBED METHANE:** NO

## RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: INDIAN - RLB0010462
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 43-7478
- RDCC Review:
- Fee Surface Agreement
- Intent to Commingle


Commingle Approved

## LOCATION AND SITING:

- R649-2-3.
- Unit:
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
- Board Cause No: R649-3-2
- Effective Date:
- Siting:
- R649-3-11. Directional Drill

**Comments:** Presite Completed

**Stipulations:** 4 - Federal Approval - dmason  
5 - Statement of Basis - bhill  
23 - Spacing - dmason



# State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER  
*Executive Director*

Division of Oil, Gas and Mining

JOHN R. BAZA  
*Division Director*

## Permit To Drill

\*\*\*\*\*

**Well Name:** Ute Tribal 6-26-4-3  
**API Well Number:** 43013503150000  
**Lease Number:** 14-20-H62-6154  
**Surface Owner:** FEE (PRIVATE)  
**Approval Date:** 6/1/2010

### Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

### Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of R649-3-2. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

### Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

### General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

### Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.

Compliance with the Conditions of Approval/Application for Permit to Drill outlined in the Statement of Basis (copy attached).

### Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during

drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)
- OR
- submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <https://oilgas.ogm.utah.gov>

**Reporting Requirements:**

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

**Approved By:**



Acting Associate Director, Oil & Gas

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**APPLICATION FOR PERMIT TO DRILL OR REENTER**

FORM APPROVED  
OMB No. 1004-0137  
Expires July 31, 2010

5. Lease Serial No. 14-20-H62-6154	
6. If Indian, Allottee or Tribe Name UTE	
7. If Unit or CA Agreement, Name and No. NA	
8. Lease Name and Well No. Ute Tribal 6-26-4-3	
9. API Well No. 43-013-50315	
10. Field and Pool, or Exploratory Undesignated	11. Sec., T. R. M. or Blk. and Survey or Area Sec. 26, T4S R3W
12. County or Parish Duchesne	13. State UT
14. Distance in miles and direction from nearest town or post office* Approximately 11.9 miles southwest of Myton, UT	15. Distance from proposed* location to nearest property or lease line, ft. Approx. 1981' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)
16. No. of acres in lease NA	17. Spacing Unit dedicated to this well 40 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1335'	19. Proposed Depth 6,840'
20. BLM/BIA Bond No. on file RLB0010462	21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5626' GL
22. Approximate date work will start* 3rd Qtr. 2010	23. Estimated duration (7) days from SPUD to rig release
24. Attachments	

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- |  |   |
|--|---|
| 1. Well plat certified by a registered surveyor.   | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan.  | 5. Operator certification   |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM.             |

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 4/2/10
Title Regulatory Specialist		

Approved by (Signature) <i>James H. Sparger</i>	Name (Printed/Typed) James H. Sparger	Date JUN 10 2010
Title ACTING Assistant Field Manager Lands & Mineral Resources	Office VERNAL FIELD OFFICE	

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached. **CONDITIONS OF APPROVAL ATTACHED**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

\*(Instructions on page 2)

**UDOGM**

**NOTICE OF APPROVAL**

RECEIVED  
GREEN RIVER DISTRICT  
VERNAL FIELD OFFICE  
JUN 15 2010

**NOS 4-12-2010**

**RECEIVED AFMSS# 10550209A**

**JUN 15 2010**



**UNITED STATES DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
VERNAL FIELD OFFICE**

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



**CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL**

<b>Company:</b>	<b>Newfield Production Company</b>	<b>Location:</b>	<b>NWSW, Sec. 26, T4S, R3W</b>
<b>Well No:</b>	<b>Ute Tribal 12-26-4-3</b>	<b>Lease No:</b>	<b>14-20-H62-6154</b>
<b>API No:</b>	<b>43-013-50316</b>	<b>Agreement:</b>	<b>N/A</b>

**OFFICE NUMBER: (435) 781-4400**

**OFFICE FAX NUMBER: (435) 781-3420**

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR  
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

**NOTIFICATION REQUIREMENTS**

Construction Activity (Notify Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist)	- The Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist shall be notified at least 48 hours in advance of any construction activity. The Ute Tribal office is open Monday through Thursday.
Construction Completion (Notify Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist)	- Upon completion of the pertinent APD/ROW construction, notify the Ute Tribe Energy & Minerals Dept. for a Tribal Technician to verify the Affidavit of Completion. Notify the BLM Environmental Scientist prior to moving on the drilling rig.
Spud Notice (Notify BLM Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify BLM Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: <a href="mailto:ut_vn_opreport@blm.gov">ut_vn_opreport@blm.gov</a> .
BOP & Related Equipment Tests (Notify BLM Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify BLM Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM  
CONDITIONS OF APPROVAL (COAs)***

- Private surface.  
Private surface use agreement submitted.

***DOWNHOLE PROGRAM  
CONDITIONS OF APPROVAL (COAs)***

**SITE SPECIFIC DOWNHOLE COAs:**

- Variance on using a diverter bowl in place of a rotating head. The diverter bowl forces the air and cutting returns to the reserve pit and is used to drill the surface casing (surface to a total depth of 350 feet). The surface casing occurs within the Uinta Formation which is a non-hydrocarbon bearing zone and thus has no possibility of gas pressure.
- Variance is granted on using a blooie line with a discharge less than 100 feet from the wellbore in order to minimize the size of the well pads and direct the cuttings and circulating mediums into the reserve pit. The well bore is located approximately 35 feet from the reserve pit which is 40 feet wide; a 100 feet blooie line will discharge the cuttings and circulating mediums across the reserve pit and off the location. The requested length of the blooie line to drill the surface casing (surface to a total depth of 350 feet) is 35 feet. The surface casing occurs within the Uinta Formation which is a non-hydrocarbon bearing zone and thus has no possibility of gas pressure.
- Variance is granted on operating without an automatic igniter or continuous pilot light on the blooie line due to the fact the air rig is only used to drill the surface casing (surface to a total depth of 350 feet). The surface casing occurs within the Uinta Formation which is a non-hydrocarbon bearing zone and thus has no possibility of gas pressure.
- Variance granted permission to use a trailer mounted compressor located less than 100 feet from the well bore in order to minimize the well pad size. The trailer mounted compressor is located 50 feet from the wellbore and in an opposite direction of the blooie line. The compressor has the following safety features: (1) shut off valve on the trailer that is located approximately 15 ft from the air rig, (2) pressure relief valve on the compressor, and (3) Spark arresters on the motors. The compressor only used in the drilling of the surface casing (surface to a total depth of 350 feet). The surface casing occurs within the Uinta Formation which is a non-hydrocarbon bearing zone and thus has no possibility of gas pressure.

**All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to.** The following items are emphasized:

**DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS**

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.

- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.
- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.

- **Please submit an electronic copy of all other logs run on this well in LAS format to UT\_VN\_Wellogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

## **OPERATING REQUIREMENT REMINDERS:**

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
  - Operator name, address, and telephone number.
  - Well name and number.
  - Well location (¼¼, Sec., Twn, Rng, and P.M.).
  - Date well was placed in a producing status (date of first production for which royalty will be paid).
  - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
  - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
  - Unit agreement and/or participating area name and number, if applicable.
  - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.

- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.
- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.

- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

Spud  
BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross #29 Submitted  
By Ryan Crum Phone Number 823-7065  
Well Name/Number Ute Tribal 6-26-4-3  
Qtr/Qtr SE/NW Section 26 Township 4s Range 3w  
Lease Serial Number 14-20-H62-6154  
API Number 43-013-50315

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 7/24/10      8:00 AM  PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 7/24/10      1:00 AM  PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time \_\_\_\_\_ AM  PM

Remarks \_\_\_\_\_

---

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**SUNDRY NOTICES AND REPORTS ON WELLS**  
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

**SUBMIT IN TRIPLICATE - Other Instructions on page 2**

1. Type of Well  
 Oil Well  Gas Well  Other

2. Name of Operator  
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630  
Myton, UT 84052

3b. Phone (include area code)  
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)  
**1981 FNL 1998 FWL**  
SENW Section 26 T4S R3W

5. Lease Serial No.  
UTE TR EDA 14-20-H62-6154

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.  
UTE TRIBAL 6-26-4-3

9. API Well No.  
4301350315

10. Field and Pool, or Exploratory Area  
MYTON-TRIBAL EDA

11. County or Parish, State  
DUCHESNE, UT

**12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 7/26/10 MIRU Ross # 29. Spud well @ 8:00 AM. Drill 315' of 12 1/4" hole with air mist. TIH W/ 7 Jt's 8 5/8" J-55 24# casing. Set @ 314.56' KB. On 7/31/10 cement with 160 sks of class "G" w/ 2% CaCL2 + 1/4# per sk Cello Flake mixed @ 15.8 ppg with 1.17 cf/sk yield. Returned 6.5 bbls cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Mitch Benson

Signature *Mitch Benson*

Title  
Drilling Foreman

Date  
07/31/2010

**THIS SPACE FOR FEDERAL OR STATE OFFICE USE**

Approved by \_\_\_\_\_  
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title \_\_\_\_\_ Date \_\_\_\_\_  
Office \_\_\_\_\_

RECEIVED

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

**AUG 10 2010**

(Instructions on page 2)





ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION				COUNTY	SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG			
B	99999	17400	4301350128	GREATER BOUNDARY II FEDERAL S-21-8-17	SESE NWSE	21	8S	17E	DUCHESNE	7/29/2010	8/19/10
WELL 1 COMMENTS: GRRV BHL = NWSE											
B	99999	17400	50183 4301350813	SANDWASH FEDERAL S-31-8-17	NESE	31	8S	17E	DUCHESNE	7/27/2010	8/19/10
WELL 2 COMMENTS: GRRV BHL = NESE											
A	99999	17732	4301350315	UTE TRIBAL 6-26-4-3	SENW	26	4S	3W	DUCHESNE	7/24/2010	8/19/10
WELL 3 COMMENTS: GRRV											
B	99999	17400	4301333987	ASHLEY FEDERAL H-15-9-15	SENW	15	9S	15E	DUCHESNE	7/28/2010	8/19/10
WELL 4 COMMENTS: GRRV BHL = SWNE											
A	99999	17733	4301350314	UTE TRIBAL 4-26-4-3	NWNW	26	4S	3W	DUCHESNE	7/28/2010	8/19/10
WELL 5 COMMENTS: GRRV											
B	99999	17400	4301334198	WEST POINT FEDERAL 4-31-8-16	NWNW	31	8S	16E	DUCHESNE	8/3/2010	8/19/10
WELL 6 COMMENTS: GRRV											


ACTION CODES (See instructions on back of form)

- A - 1 new entity for new well (single well only)
- B - well to existing entity (group or unit well)
- C - from one existing entity to another existing entity
- D - well from one existing entity to a new entity
- E - other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.

RECEIVED  
 AUG 10 2010

DIV. OF OIL, GAS & MINING

  
 Signature  
 Jentri Park  
 Production Clerk  
 08/10/10  
 Date

**STATE OF UTAH**  
DEPARTMENT OF NATURAL RESOURCES  
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:  
UTE TR EDA 14-20-H62-6154

**SUNDRY NOTICES AND REPORTS ON WELLS**

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:

1. TYPE OF WELL: OIL WELL  GAS WELL  OTHER

8. WELL NAME and NUMBER:  
UTE TRIBAL 6-26-4-3

2. NAME OF OPERATOR:  
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:  
4301350315

3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

10. FIELD AND POOL, OR WILDCAT:  
MYTON-TRIBAL EDA

4. LOCATION OF WELL: FOOTAGES AT SURFACE: COUNTY: DUCHESNE

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: SENW, 26, T4S, R3W STATE: UT

**CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate)  Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only)  Date of Work Completion: 09/07/2010	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was completed on 09-07-10, attached is a daily completion status report.

NAME (PLEASE PRINT) Lucy Chavez-Naupoto TITLE Administrative Assistant

SIGNATURE  DATE 09/08/2010

(This space for State use only)

**RECEIVED**

**SEP 13 2010**

**DIV. OF OIL, GAS & MINING**

## Daily Activity Report

Format For Sundry

**UTE TRIBAL 6-26-4-3**

**7/1/2010 To 11/30/2010**

**8/23/2010 Day: 1**

**Completion**

Rigless on 8/23/2010 - Run CBL & shoot first stage. - Install 5M frac head. NU 6" 5M Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 6747' cement top @ 0'. Perforate CP5/CP4 sds as shown in perforation report. 162 BWTR. SWIFN.

**Daily Cost:** \$0

**Cumulative Cost:** \$12,868

**8/30/2010 Day: 2**

**Completion**

Rigless on 8/30/2010 - Frac well. Flowback well - RU PSI WLT & crane. RU BJ Services frac equipment. Frac stg #1. Perforate & frac stgs #2-5. RD WLT & crane. RD BJ frac equipment. EWTR 2230 BBLs. RU flowback equipment. Open well to pit @ 12:05 PM. Flowback well for 3 hrs to recover 360 BBLs. EWTR 1870 BBLs

**Daily Cost:** \$0

**Cumulative Cost:** \$106,279

**8/31/2010 Day: 3**

**Completion**

Nabors #147 on 8/31/2010 - MIRUSU Nabors #147. Pick up tbg for cleanout operations - MIRUSU Nabors #147. Open well. CSG 400 psi. Bleed off well. ND Cameron BOP. Break out frac head. MU production head. NU Schaffer BOP. RU workflow. Prep & tally tbg. MU 4 3/4" Weatherford chomp bit & bit sub. TIH picking up & drifting tbg. Get in hole w/ 156 jts tbg. RU pump lines. SDFN

**Daily Cost:** \$0

**Cumulative Cost:** \$151,870

**9/2/2010 Day: 4**

**Completion**

Nabors #147 on 9/2/2010 - Drill out plugs. Clean out to PBTD. Swab & flow well. - Open well. TBG 0 psi. CSG 200 psi. RU Nabors power swivel. Catch circulation. Tag 1st CBP @ 4875'. Drill out plug. Continue picking up tbg to tag sand @ 5415'. 75' sand. Clean out sand to next CBP @ 5490'. Drill out plug. Circulate out gas. Continue picking up tbg to tag next plug @ 5620'. Drill out plug. Continue picking up tbg to tag next plug @ 5815'. Drill out plug. Continue picking up tbg to tag sand @ 6600'. 190' sand. Clean out sand to PBTD @ 6790'. RU swab equipment. Make up swab equipment. RIH w/ swab. IFL @ surface. Make 1 swab run. Well started to flow. Flowed back 180 bbls in 2 hrs w/ trace of oil & no sand. Pump 20 bbls to kill tbg. TIH w/ tbg to tag PBTD no new fill. Circulate clean w/ 140 bbls wtr. LD 13 jts tbg. SDFN

**Daily Cost:** \$0

**Cumulative Cost:** \$160,650

**9/3/2010 Day: 5**

**Completion**

Nabors #147 on 9/3/2010 - Kill well. Trip tbg. TAC would not set - Open well. TBG 450 psi. CSG 600 psi. Circulate well w/ 180 bbls 10# brine wtr. TOOH w/ 203 jts tbg. Get out of hole

tbg. LD bit & bit sub. MU btm hole assembly. TIH w/ tbg detail @ follows. NC, 2 jts tbg, PSN, 1 jt tbg, TAC, & 200 jts tbg. Attempt to set TAC. TAC would not set. Work TAC to try to get set. Would not set. Well began to flow. SDFN

**Daily Cost:** \$0

**Cumulative Cost:** \$166,006

---

**9/7/2010 Day: 6**

**Completion**

Nabors #147 on 9/7/2010 - Kill well. Trip tbg to replace TAC. PU rod detail. PWOP - Open well. TBG 0 psi. CSG 450 psi. Pump 140 bbls 10# brine to kill well. Re-attempt to set anchor w/out success. TOOH w/ 200 jts tbg. Change out TAC. TIH w/ tbg detail. Get in hole w/ tbg. RD workflow. ND BOP. Set TAC. MU B-1 adapter flange. Land tbg on wellhead w/ 18000# tension. X-over to rod equipment. PU & prime new Central Hydraulic 2 1/2" x 1 1/2" x 21' x 24' RHAC pump. TIH picking up rod detail @ follows. 6 - 1 1/2" wt bars, 146 - 3/4" guided rods, & 100 - 7/8" guided rods. Space out pump w/ 1 - 2' x 7/8" pony sub. PU new 1 1/2" x 26' polished rod. RU pumping unit. Fill & test tbg to 200 psi w/ 5 bw. Stoke test pump to 800 psi w/ unit. Good pump action. RDMOSU Nabors #147. PWOP @ 8:30 PM w/ 124" SL @ 5 SPM  
FINAL REPORT! EWTR 1682 BBLs **Finalized**

**Daily Cost:** \$0

**Cumulative Cost:** \$211,685

---

**Pertinent Files: Go to File List**

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

FORM APPROVED  
OMB NO. 1004-0137  
Expires: July 31, 2010

**WELL COMPLETION OR RECOMPLETION REPORT AND LOG**

5. Lease Serial No.  
14-20-H62-6154

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.

8. Lease Name and Well No.  
UTE TRIBAL 6-26-4-3

9. AFI Well No.  
43-013-50315

10. Field and Pool or Exploratory  
MYTON-TRIBAL EDA

11. Sec., T., R., M., on Block and  
Survey or Area  
SEC. 26, T4S, R3W

12. County or Parish  
DUCHESNE

13. State  
UT

14. Date Spudded  
07/26/2010

15. Date T.D. Reached  
08/14/2010

16. Date Completed  
09/03/2010  
 D & A  Ready to Prod.

17. Elevations (DF, RKB, RT, GL)\*  
5626' GL 5638' KB

18. Total Depth: MD 6845'  
TVD

19. Plug Back T.D.: MD 6790'  
TVD

20. Depth Bridge Plug Set: MD  
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)  
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored?  No  Yes (Submit analysis)  
Was DST run?  No  Yes (Submit report)  
Directional Survey?  No  Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sks. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	315'		160 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	6835'		275 PRIMLITE		00'	
						400 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 6390'	TA @ 6291'						

25. Producing Intervals

Formation	Top	Bottom	Perforation Record	Size	No. Holes	Perf. Status
A) Green River			6222-6332' CP4 CP5	.36"	3	21
B) Green River			5646-5730' LODC	.34"	3	48
C) Green River			5567-5571' A3	.34"	3	12
D) Green River			5410-5423' B2	.34"	3	21

26. Perforation Record 4775

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
6222-6332'	Frac w/ 24711#'s 20/40 sand in 208 bbls of Lightning 17 fluid.
5646-5730'	Frac w/ 99051#'s 20/40 sand in 482 bbls of Lightning 17 fluid.
5567-5571'	Frac w/ 24580#'s 20/40 sand in 210 bbls of Lightning 17 fluid.
5410-5423'	Frac w/ 34670#'s 20/40 sand in 292 bbls of Lightning 17 fluid.

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
9-2-10	9-14-10	24	→	17	35	17			2-1/2" x 1-1/2" x 21' x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

\*(See instructions and spaces for additional data on page 2)

RECEIVED  
SEP 30 2010

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD & USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
				GARDEN GULCH MRK GARDEN GULCH 1	3967' 4204'
				GARDEN GULCH 2 POINT 3	4336' 4631'
				X MRKR Y MRKR	4888' 4920'
				DOUGALS CREEK MRK BI CARBONATE MRK	5036' 5299'
				B LIMESTON MRK CASTLE PEAK	5434' 5972'
				BASAL CARBONATE WASATCH	6396' 6530'


32. Additional remarks (include plugging procedure):

Stage 5: Green River Formation (PB10) 4775-4790', .34" 3/30 Frac w/ 54497#'s of 20/40 sand in 323 bbls of Lightning 17 fluid

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)     
  Geologic Report     
  DST Report     
  Directional Survey  
 Sundry Notice for plugging and cement verification     
  Core Analysis     
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)\*

Name (please print) Lucy Chavez-Naupoto Title Administrative Assistant  
 Signature  Date 09/27/2010

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

**Daily Activity Report**

Format For Sundry

**UTE TRIBAL 6-26-4-3****5/1/2010 To 9/30/2010****UTE TRIBAL 6-26-4-3****Waiting on Cement****Date:** 7/31/2010

Ross #29 at 315. Days Since Spud - Returned 6.5 bbls to pit. - On 7/26/10 Ross Rig #29 spud Ute Tribal 6-26-4-3, drilled 315' of 12 1/4" hole, and ran 7 jts 8 5/8" - casing (guide shoe, shoe jt, baffle plate, 6 jts) set @ 314.56' KB. On 7/31/10 BJ Services cemented - 8 5/8" casing w/ 160 sks Class "G" + 2% CaCl<sub>2</sub> + 0.25#/sk Cello Flake at 15.8 ppg w/ 1.17 yield.

**Daily Cost:** \$0**Cumulative Cost:** \$46,329**UTE TRIBAL 6-26-4-3****Rigging down****Date:** 8/8/2010

NDSI #3 at 315. 0 Days Since Spud - RD & prepare to move to Ute Tribal 6-26-4-3W with Jones trucking

**Daily Cost:** \$0**Cumulative Cost:** \$49,064**UTE TRIBAL 6-26-4-3****Drill 7 7/8" hole with fresh water****Date:** 8/9/2010

NDSI #3 at 1959. 1 Days Since Spud - Pickup BHA, Smith. 7 7/8" PDC Bit, 1X26.82' 6.5" Hunting 4/5 6.0St 1.5° Mud Motor, 1X29.94' Monel, - Test Srfce casing to 1,500PSI F/ 30min - Test Kelly, Choke, Pipe, and Blind Rams, Safety Valve to 2,000 PSI F/ Ten Minutes. - Move Rig to the Ute Tribal 6-26-4-3 - 1X1.74 X-Over, 17 Drill Collars 496.64' Tag Cmt @ 265' - Work on Pump - Install rotating head rubber and Drive bushing - Drill 7 7/8" hole F/ 1644' to 1959' W/20,000 WOB, 151TRPM, 395GPM, 178fph - Circulate wait on Directional tools - Drill 7 7/8" hole F/ 265' to 1644' W/20,000 WOB, 151TRPM, 395GPM, 178fph

**Daily Cost:** \$0**Cumulative Cost:** \$68,889**UTE TRIBAL 6-26-4-3****Drill 7 7/8" hole with fresh water****Date:** 8/10/2010

NDSI #3 at 4103. 2 Days Since Spud - Drill 7 7/8" hole F/ 2243' to 2306' W/20,000 WOB, 151TRPM, 395GPM, 170fph - Drill 7 7/8" hole F/ 3630' to 4103' W/20,000 WOB, 151TRPM, 395GPM, 170fph - Change Swivel Packing - Drill 7 7/8" hole F/ 2306' to 3630' W/20,000 WOB, 151TRPM, 395GPM, 170fph - Trip in hole - Trip in Hole W/ BHA do shallow hole test - Trip out of hole F/ Directonal tools, Make up and check MWD tool - Wait on Brine - Rig Service Function test BOP, and Crown-O-Matic Grease Crown, Swivel and Kelly Spinner - Circulate Wait on Orders ( Directional Tools ) - Drill 7 7/8" hole F/ 1959' to 2243' W/20,000 WOB, 151TRPM, 395GPM, 170fph

**Daily Cost:** \$0**Cumulative Cost:** \$90,604**UTE TRIBAL 6-26-4-3****Drill 7 7/8" hole with fresh water****Date:** 8/11/2010

NDSI #3 at 6561. 3 Days Since Spud - Rig Service, Function Test BOP and Crown-O-Matic, Grease Crown, Blocks, and Swivel - Drill 7 7/8" hole F/ 4103' to 4702' W/23,000 WOB, 151TRPM, 395GPM, 137fph - Drill 7 7/8" hole F/ 4702' to 6561' W/23,000 WOB, 151TRPM,

395GPM, 137fph

**Daily Cost:** \$0

**Cumulative Cost:** \$124,189

---

**UTE TRIBAL 6-26-4-3**

**Logging**

**Date:** 8/12/2010

NDSI #3 at 6845. 4 Days Since Spud - TOOH - Log descent # 1, Start on descent # 2. - Drill 7 7/8" hole F/ 6561' to 6845' W/23,000 WOB, 151TRPM, 395GPM, 137fph - Mud up for logs

**Daily Cost:** \$0

**Cumulative Cost:** \$138,174

---

**UTE TRIBAL 6-26-4-3**

**TOOH**

**Date:** 8/13/2010

NDSI #3 at 6845. 5 Days Since Spud - TIH - LDDP - Finish logging - Ream 120' to bottom & circulate bottoms up

**Daily Cost:** \$0

**Cumulative Cost:** \$238,093

---

**UTE TRIBAL 6-26-4-3**

**Wait on Completion**

**Date:** 8/14/2010

NDSI #3 at 6845. 6 Days Since Spud - Release Rig @ 12:00am 8/14/10 - Clean mud tanks - Nipple down set slips w/110,000# Tension - 400sks tail;50:50:2 Class G+.05SF+3%KCL+.5% EC+.25#CF+3%SM - LDDP & BHA - Change and test casing rams 2000psi for 10min - Run 161jts of 5.5" casing set @ 6835.37'KB - Cement w/BJ 275sks lead; PLII3% KCL+.5#CF2#KS.002FP-6L+5#CSE-2 - Circulate w/rig pump **Finalized**

**Daily Cost:** \$0

**Cumulative Cost:** \$398,726

---

**Pertinent Files: Go to File List**
