

STATE OF UTAH
 DEPARTMENT OF NATURAL RESOURCES
 DIVISION OF OIL, GAS AND MINING

FORM 3
 AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL				1. WELL NAME and NUMBER Ute Tribal 1-27-4-3		
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>				3. FIELD OR WILDCAT UNDESIGNATED		
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO				5. UNIT or COMMUNITIZATION AGREEMENT NAME		
6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY				7. OPERATOR PHONE 435 646-4825		
8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052				9. OPERATOR E-MAIL mcrozier@newfield.com		
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) 14-20-H62-6154		11. MINERAL OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input checked="" type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>		12. SURFACE OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input checked="" type="checkbox"/>		
13. NAME OF SURFACE OWNER (if box 12 = 'fee') Moon Live Stock LLC				14. SURFACE OWNER PHONE (if box 12 = 'fee')		
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee') HC 64 Box 102, Duchesne, UT 84021				16. SURFACE OWNER E-MAIL (if box 12 = 'fee')		
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')		18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>		19. SLANT VERTICAL <input checked="" type="checkbox"/> DIRECTIONAL <input type="checkbox"/> HORIZONTAL <input type="checkbox"/>		
20. LOCATION OF WELL	FOOTAGES	QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN
LOCATION AT SURFACE	515 FNL 728 FEL	NENE	27	4.0 S	3.0 W	U
Top of Uppermost Producing Zone	515 FNL 728 FEL	NENE	27	4.0 S	3.0 W	U
At Total Depth	515 FNL 728 FEL	NENE	27	4.0 S	3.0 W	U
21. COUNTY DUCHESNE		22. DISTANCE TO NEAREST LEASE LINE (Feet) 515		23. NUMBER OF ACRES IN DRILLING UNIT 40		
		25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 1370		26. PROPOSED DEPTH MD: 6905 TVD: 6905		
27. ELEVATION - GROUND LEVEL 5623		28. BOND NUMBER RLB0010462		29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 43-7478		

ATTACHMENTS

VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES

<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER	<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN
<input checked="" type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)	<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER
<input type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)	<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP

NAME Mandie Crozier	TITLE Regulatory Tech	PHONE 435 646-4825
SIGNATURE	DATE 04/29/2010	EMAIL mcrozier@newfield.com
API NUMBER ASSIGNED 43013503310000	APPROVAL  Permit Manager	

Proposed Hole, Casing, and Cement


String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Prod	7.875	5.5	0	6905		
Pipe	Grade	Length	Weight			
	Grade J-55 LT&C	6905	15.5			

Proposed Hole, Casing, and Cement


String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Surf	12.25	8.625	0	300		
Pipe	Grade	Length	Weight			
	Grade J-55 ST&C	300	24.0			

T4S, R3W, U.S.B.&M.


NEWFIELD EXPLORATION COMPANY

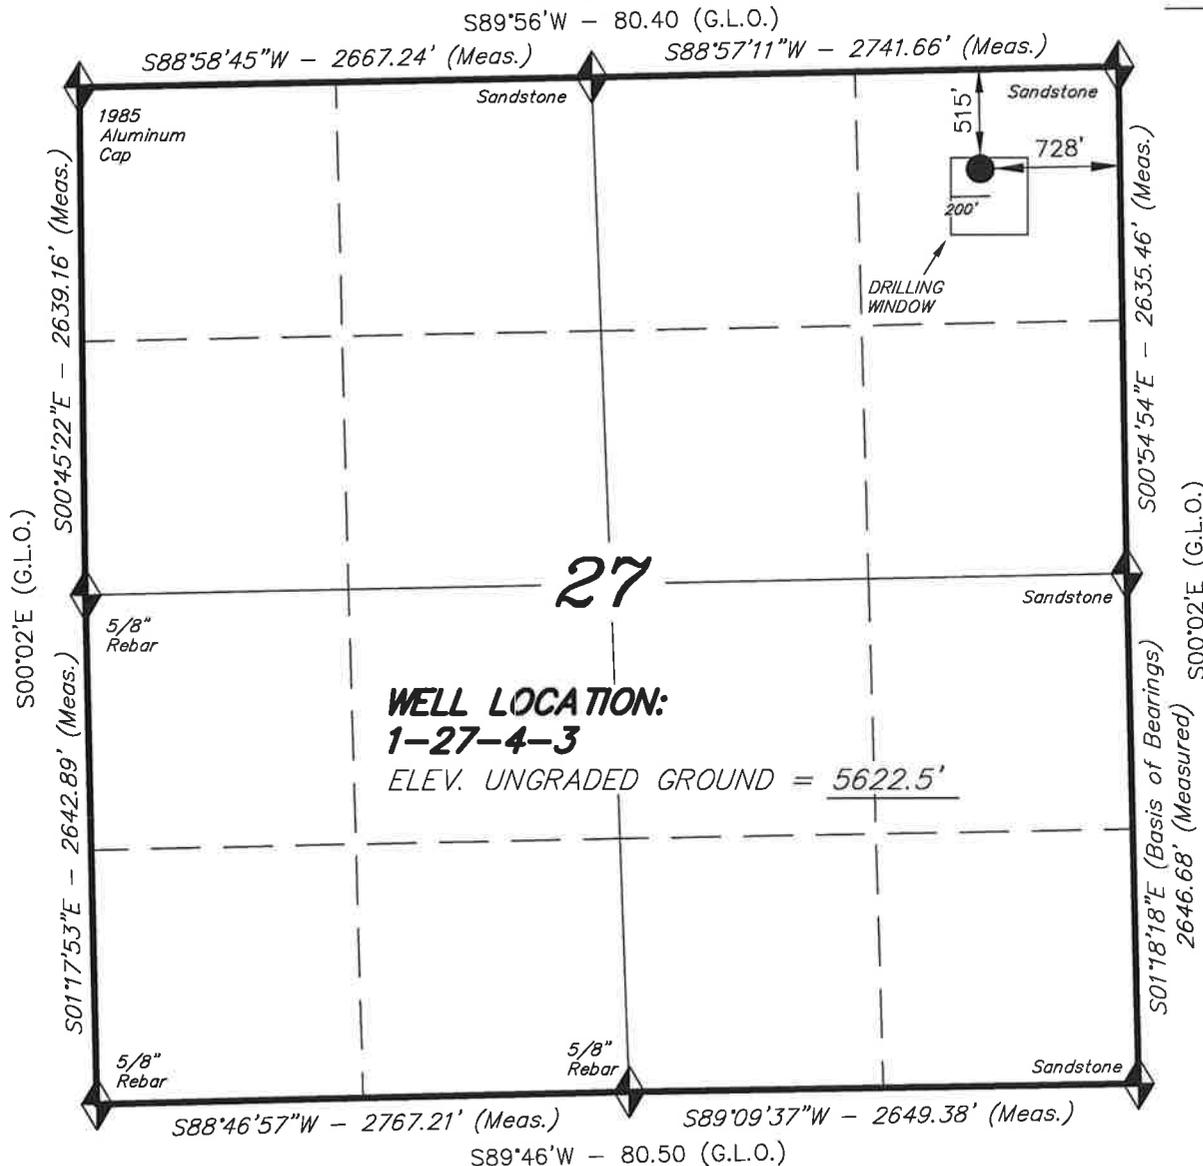

WELL LOCATION, 1-27-4-3, LOCATED AS SHOWN IN THE NE 1/4 NE 1/4 OF SECTION 27, T4S, R3W, U.S.B.&M. DUCHESNE COUNTY, UTAH.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF. 189377



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are base on LOCATION: an N.G.S. OPUS Correction. LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'

1-27-4-3
(Surface Location) NAD 83
 LATITUDE = 40° 06' 42.26"
 LONGITUDE = 110° 12' 06.63"

TRI STATE LAND SURVEYING & CONSULTING
 180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
 (435) 781-2501

DATE SURVEYED: 03-12-10	SURVEYED BY: C.D.S.
DATE DRAWN: 03-13-10	DRAWN BY: F.T.M.
REVISED:	SCALE: 1" = 1000'

**MEMORANDUM
of
EASEMENT, RIGHT-OF-WAY
and
SURFACE USE AGREEMENT**

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 17th day of March, 2010 by and between **Moon Live Stock, LLC, whose address is HC 64 box 102, Duchesne, Utah 84021**, ("Surface Owner," whether one or more) and Newfield Production Company, a Texas corporation ("NEWFIELD"), with offices at 1001 Seventeenth Street, Suite 2000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Duchesne County, Utah described as follows:

Township 4 South, Range 3 West

Section 27: All, being 640 acres more or less.

Duchesne County, Utah

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

1. **Compensation for Well; Release of All Claims**

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated March 17, 2010 as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

2. **Grant of Right of Way and Easement**

Surface Owner hereby grants, bargains, leases, assigns, and conveys to NEWFIELD an easement and right-of-way for the purpose of construction, using and maintaining access roads, locations for surface equipment and subsurface gathering lines for each well drilled upon the Lands, pipelines, and pipeline interconnections for two years from date of this agreement and so long thereafter as NEWFIELD's oil and gas leases remain in effect.

This Agreement shall be binding upon the respective heirs, executors, administrators, successors, and assigns of the undersigned.

These Parties hereto have executed this document effective as of the day first above written.

MOON LIVE STOCK, LLC

NEWFIELD PRODUCTION COMPANY

By: [Signature]
Ken Moon, private surface owner

By: _____
Daniel W. Shewmake,
Vice President-Development

By: [Signature]
Todd Moon, private surface owner


By: [Signature]
Russell Moon

STATE OF UTAH)
)ss
COUNTY OF Duchesne)

This instrument was acknowledged before me this 24th day of March, 2010 by **Moon Live Stock LLC, private surface owners.**

Witness my hand and official seal.

My commission expires 9/8/2013

[Signature]
Notary Public


STATE OF COLORADO)
)ss
COUNTY OF Denver)

This instrument was acknowledged before me this _____, 2010 by **Daniel W. Shewmake, Vice President-Development** a Texas corporation, on behalf of the corporation.

Witness my hand and official seal.

Notary Public

My commission expires _____

NEWFIELD PRODUCTION COMPANY
UTE TRIBAL 1-27-4-3
NE/NE SECTION 27, T4S, R3W
DUCHESNE COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0' – 1715'
Green River	1715'
Wasatch	6605'
Proposed TD	6905'

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil) 1715' – 6605'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sampled Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO ₃) (mg/l)
Dissolved Bicarbonate (NaHCO ₃) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO ₄) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: Ute Tribal 1-27-4-3**

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950	1,370	244,000
						17.53	14.35	33.89
Prod casing 5-1/2"	0'	6,905'	15.5	J-55	LTC	4,810	4,040	217,000
						2.19	1.84	2.03

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg
 Pore pressure at surface casing shoe = 8.33 ppg
 Pore pressure at prod casing shoe = 8.33 ppg
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: Ute Tribal 1-27-4-3**

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft ³ /sk)
			ft ³			
Surface casing	300'	Class G w/ 2% CaCl	138	30%	15.8	1.17
			161			
Prod casing Lead	4,905'	Prem Lite II w/ 10% gel + 3% KCl	339	30%	11.0	3.26
			1105			
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363	30%	14.3	1.24
			451			

- *Actual volume pumped will be 15% over the caliper log
- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
 - Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ± 350 feet will be drilled with an air/mist system. The air rig is equipped with a 6 1/2" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ± 350 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBDT to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated

bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.

10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the third quarter of 2010, and take approximately seven (7) days from spud to rig release.

2-M SYSTEM

Blowout Prevention Equipment Systems


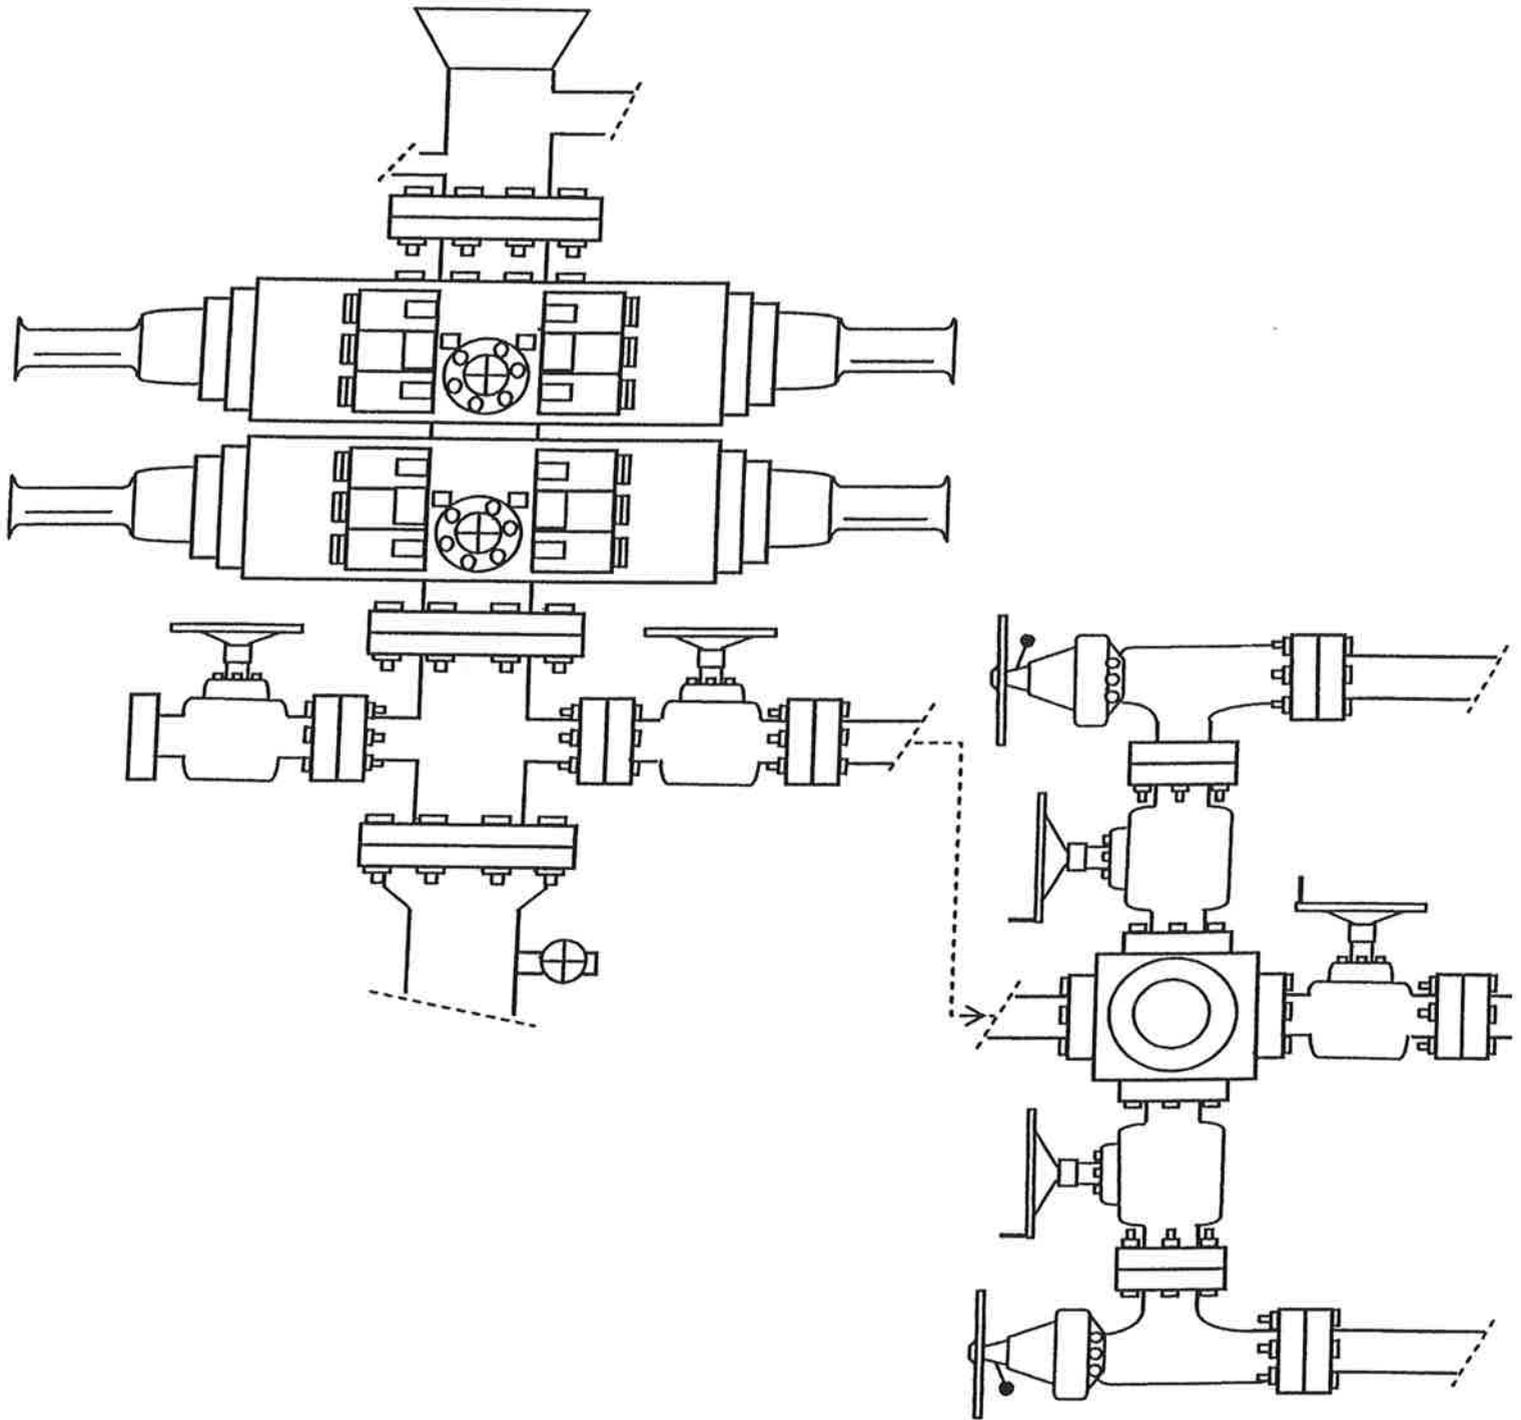


EXHIBIT C

Access Road Map

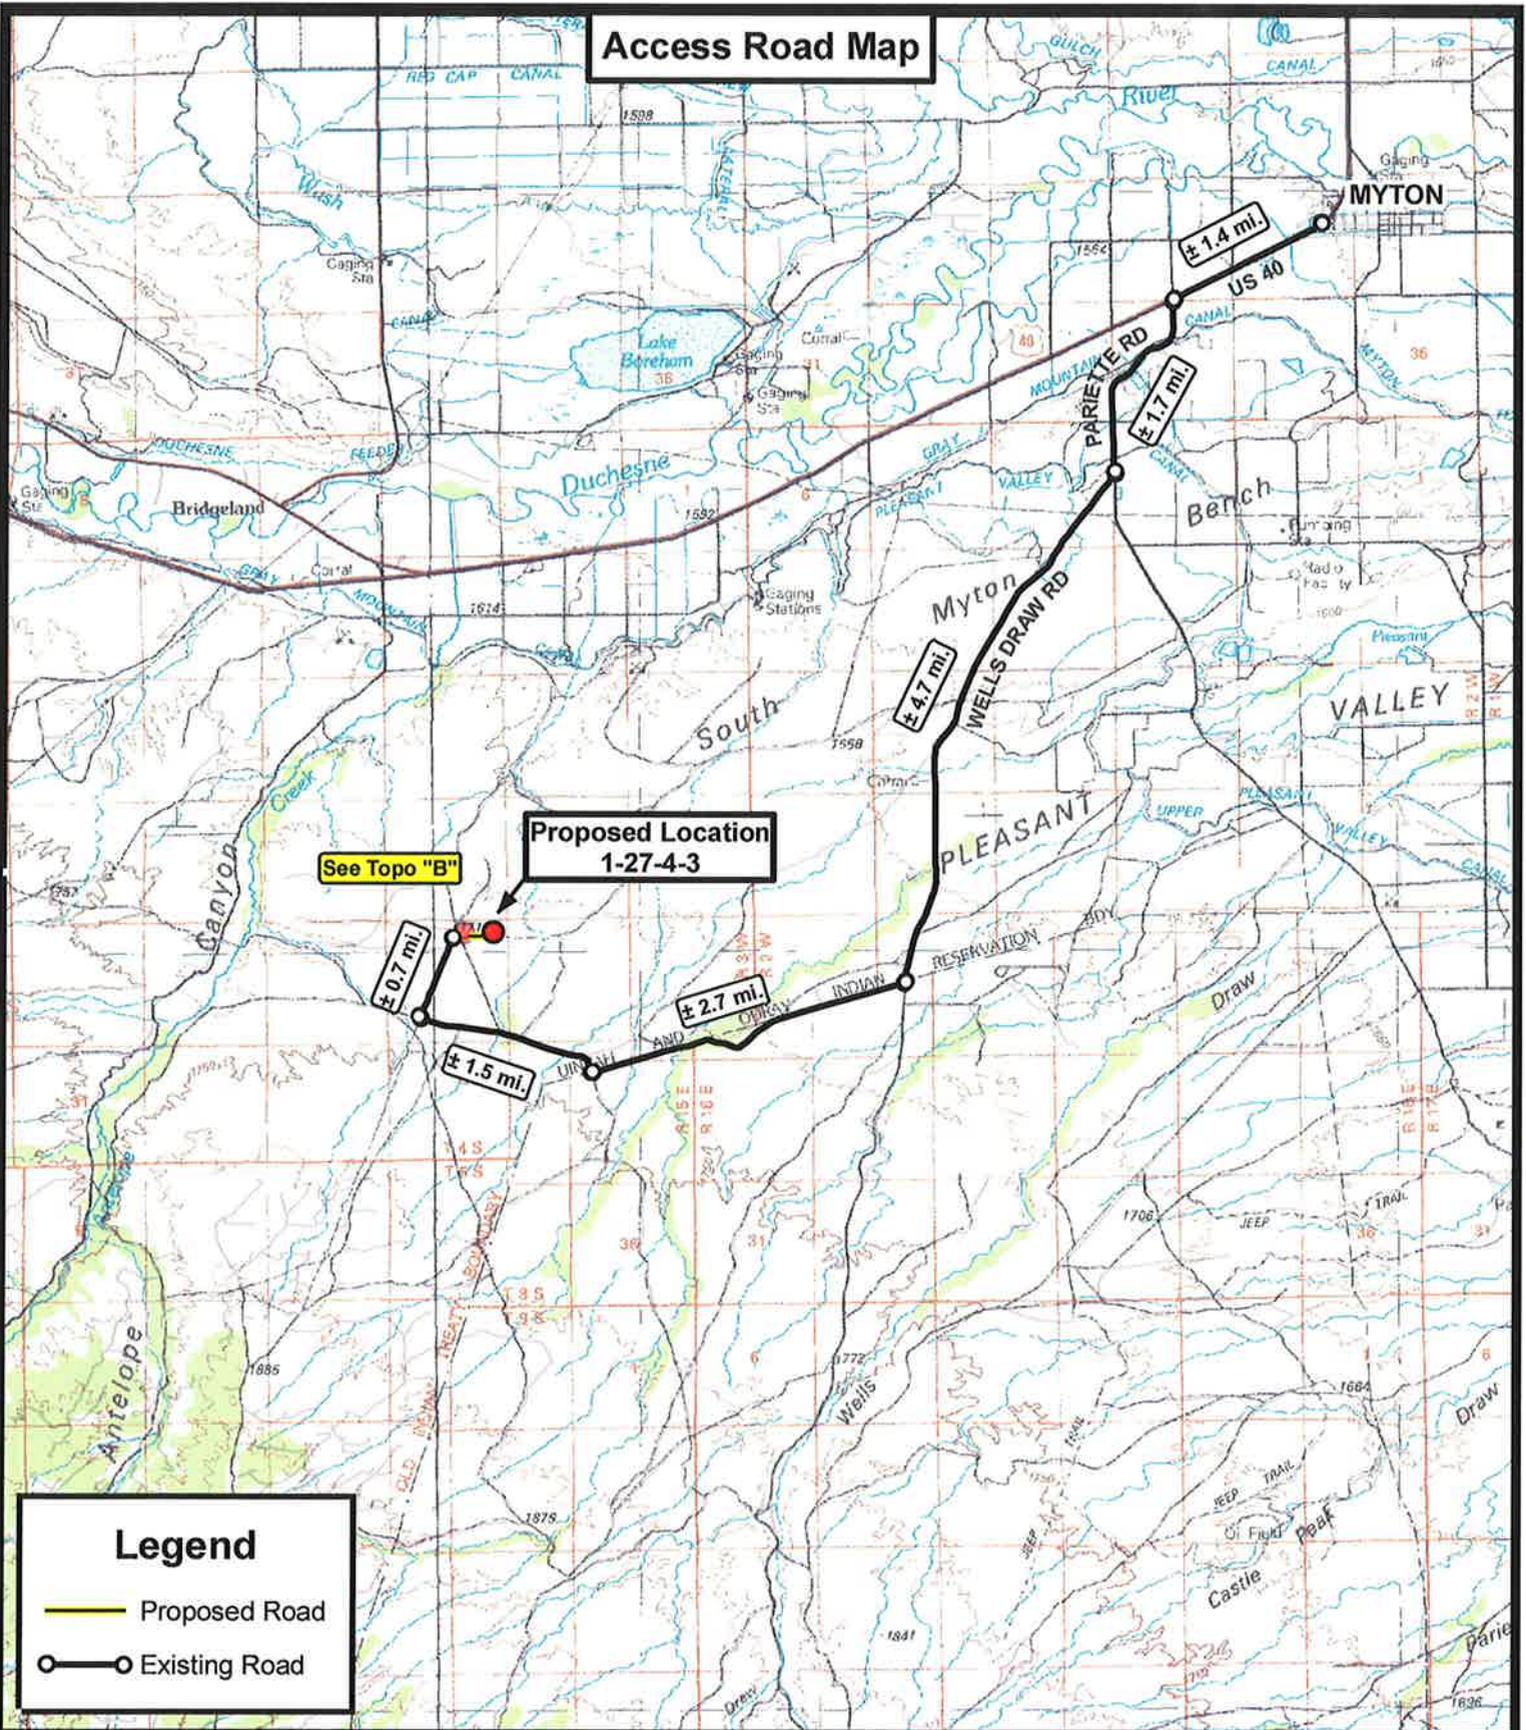

Legend

- Proposed Road
- Existing Road

Tri State
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY


1-27-4-3
 SEC. 27, T4S, R3W, U.S.B.&M.
 Duchesne County, UT.

DRAWN BY:	C.H.M.
DATE:	03-25-2010
SCALE:	1:100,000

TOPOGRAPHIC MAP

SHEET
A

Access Road Map

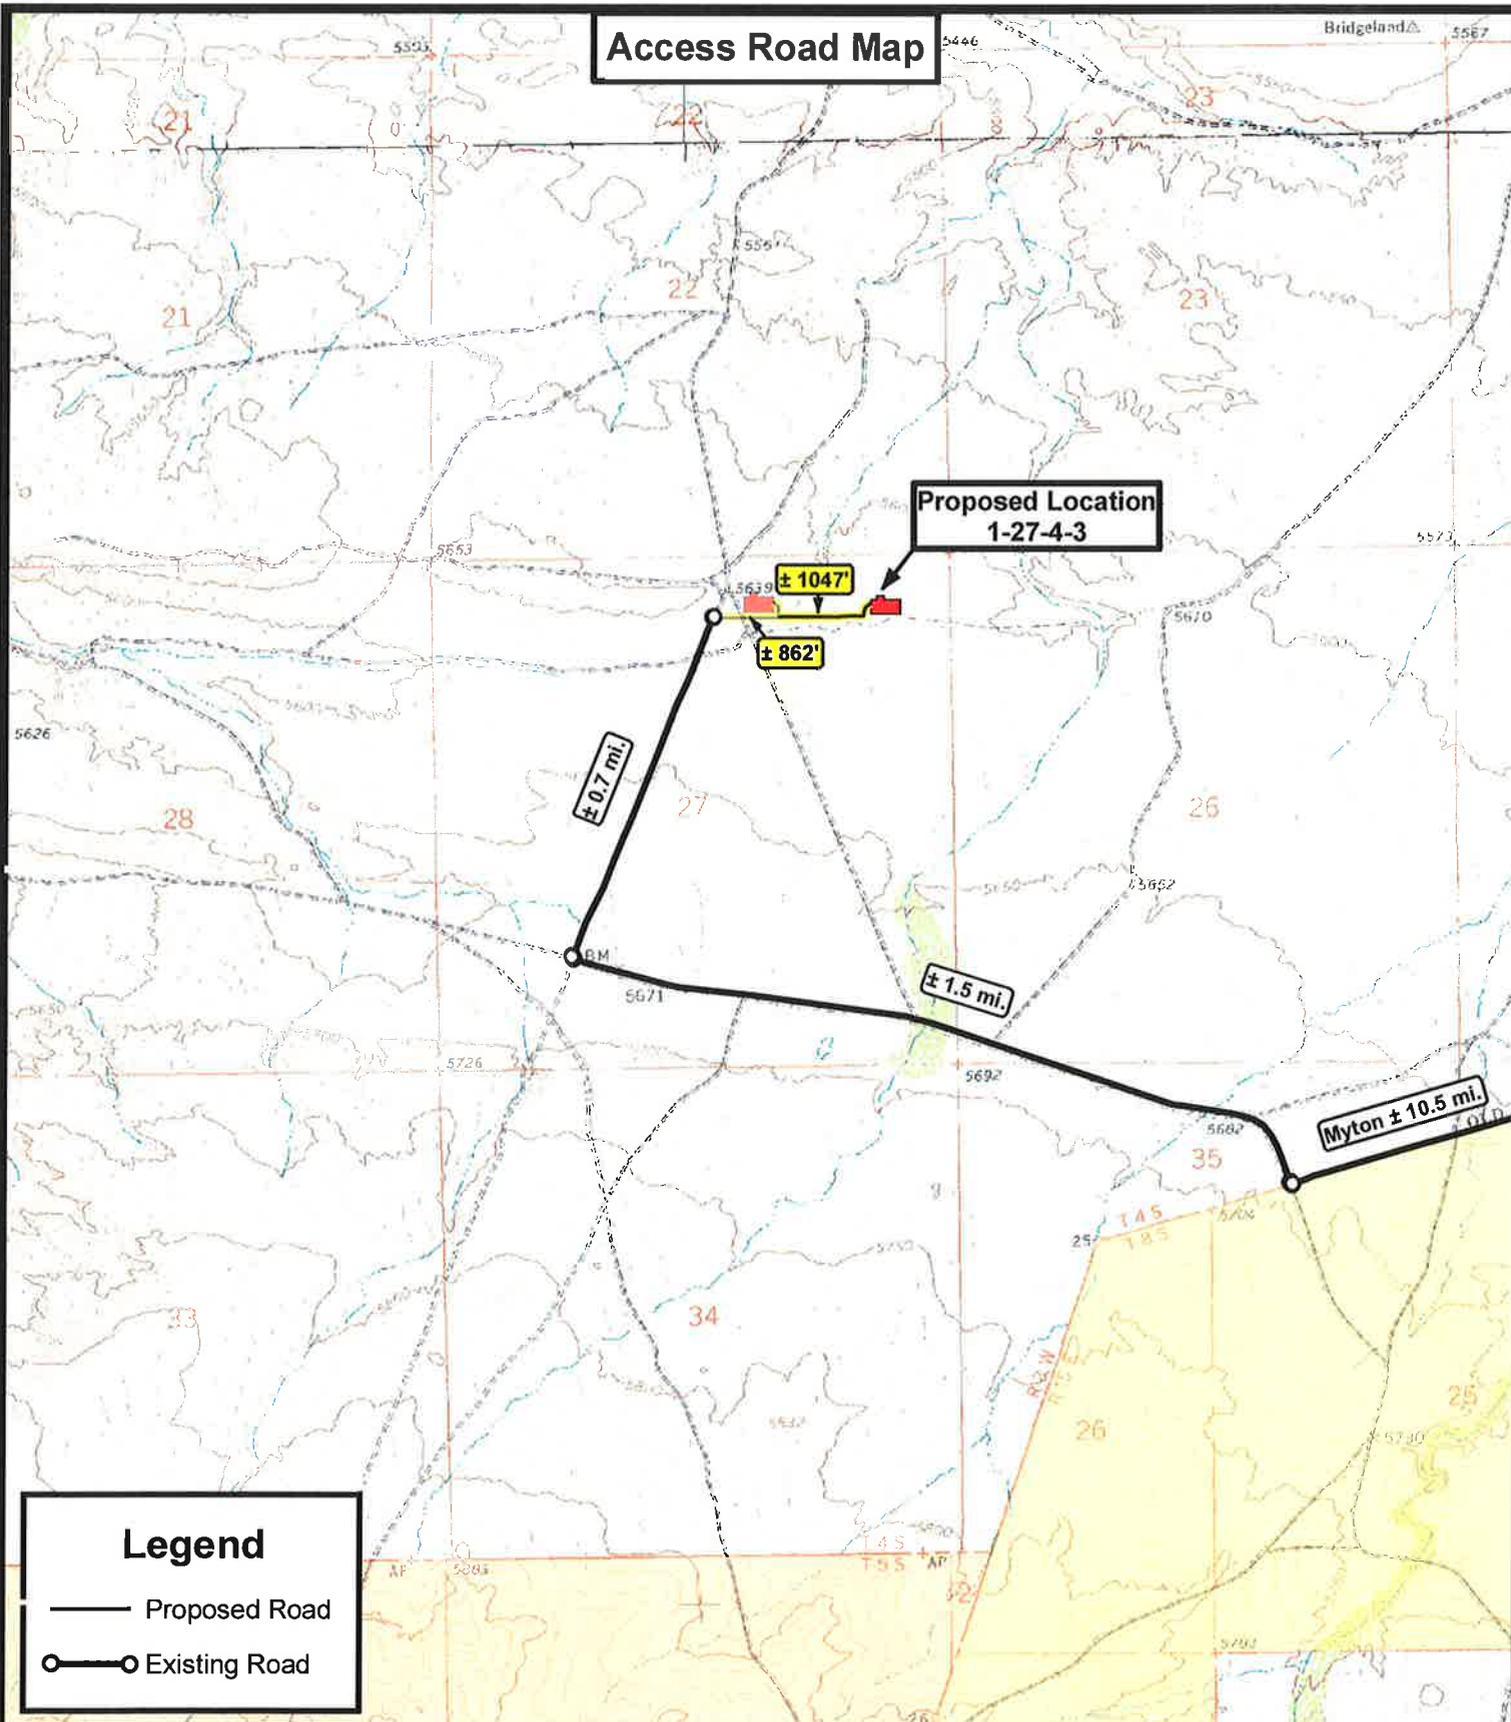

**Proposed Location
1-27-4-3**

± 1047'

± 862'

± 0.7 mi.

± 1.5 mi.

Myton ± 10.5 mi.

Legend

- Proposed Road
- Existing Road



**Tri State
Land Surveying, Inc.**
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY


1-27-4-3
SEC. 27, T4S, R3W, U.S.B.&M.
Duchesne County, UT.

DRAWN BY:	C.H.M.
DATE:	03-25-2010
SCALE:	1" = 2,000'

TOPOGRAPHIC MAP

SHEET
B

Proposed Pipeline Map

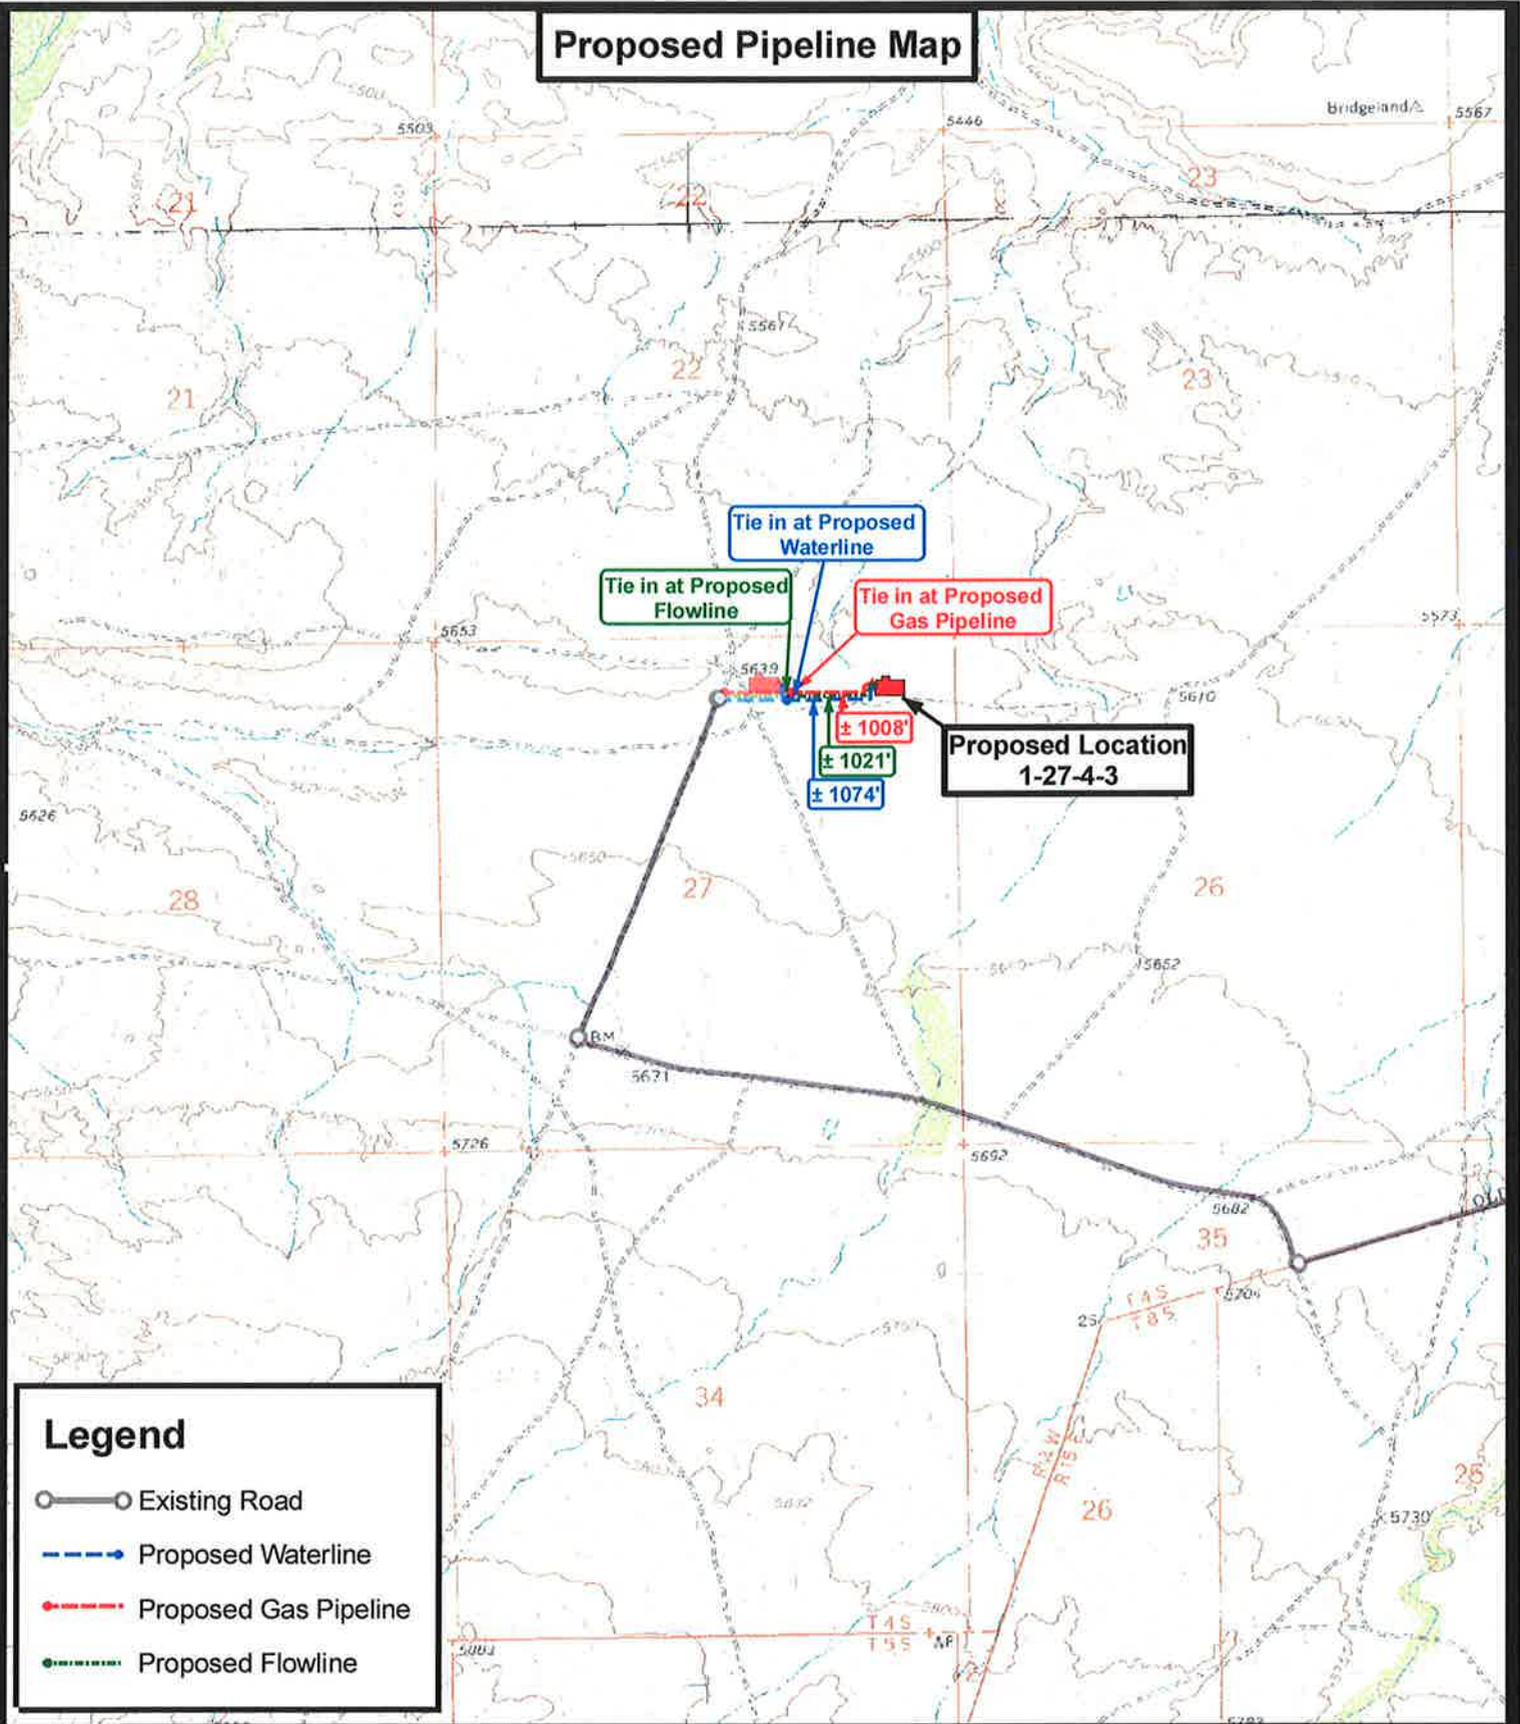

Legend

- Existing Road
- Proposed Waterline
- Proposed Gas Pipeline
- Proposed Flowline

Tri State Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY
1-27-4-3
SEC. 27, T4S, R3W, U.S.B.&M.
Duchesne County, UT.

DRAWN BY:	C.H.M.
DATE:	03-25-2010
SCALE:	1" = 2,000'

TOPOGRAPHIC MAP SHEET **C**


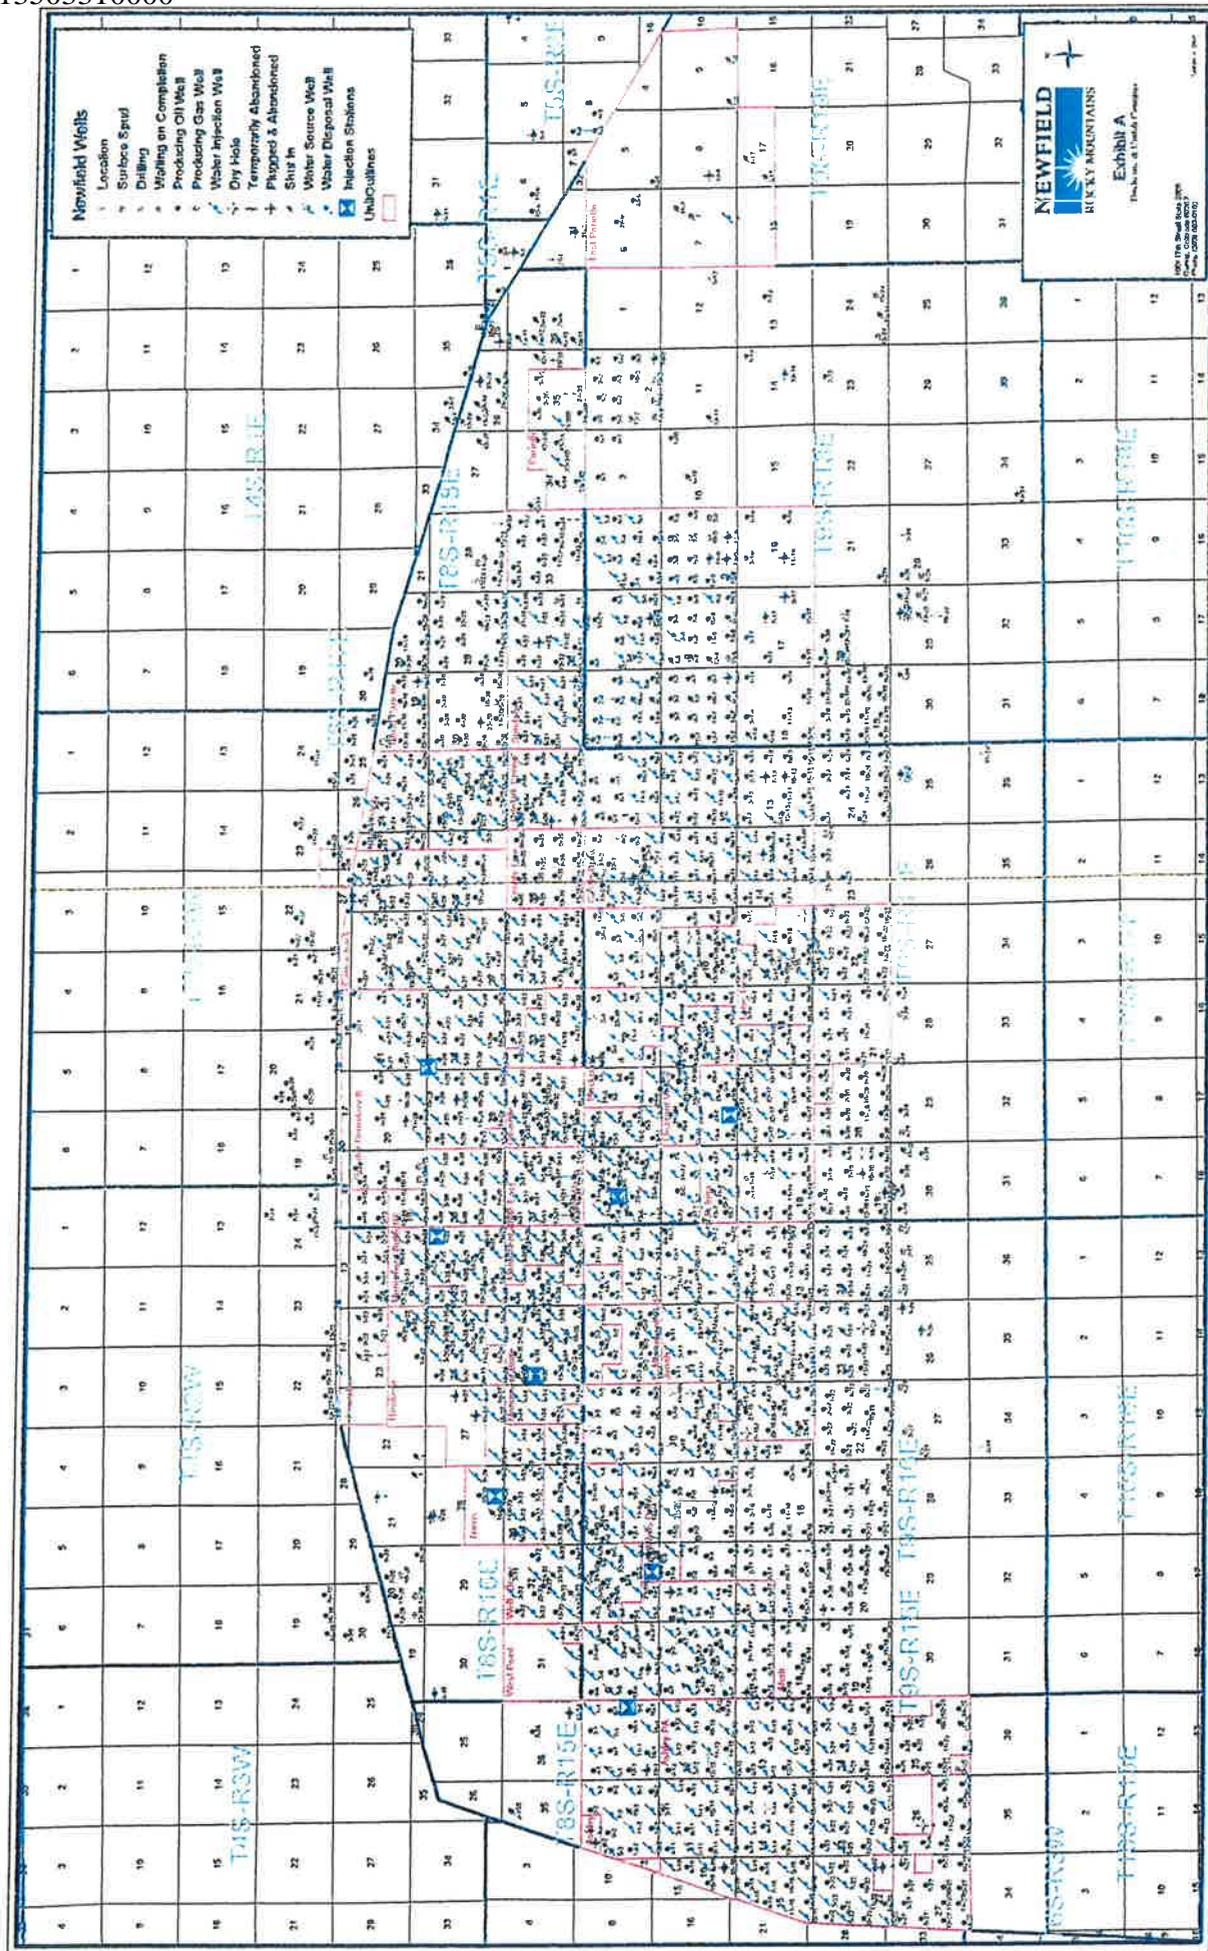


Exhibit "B" Map

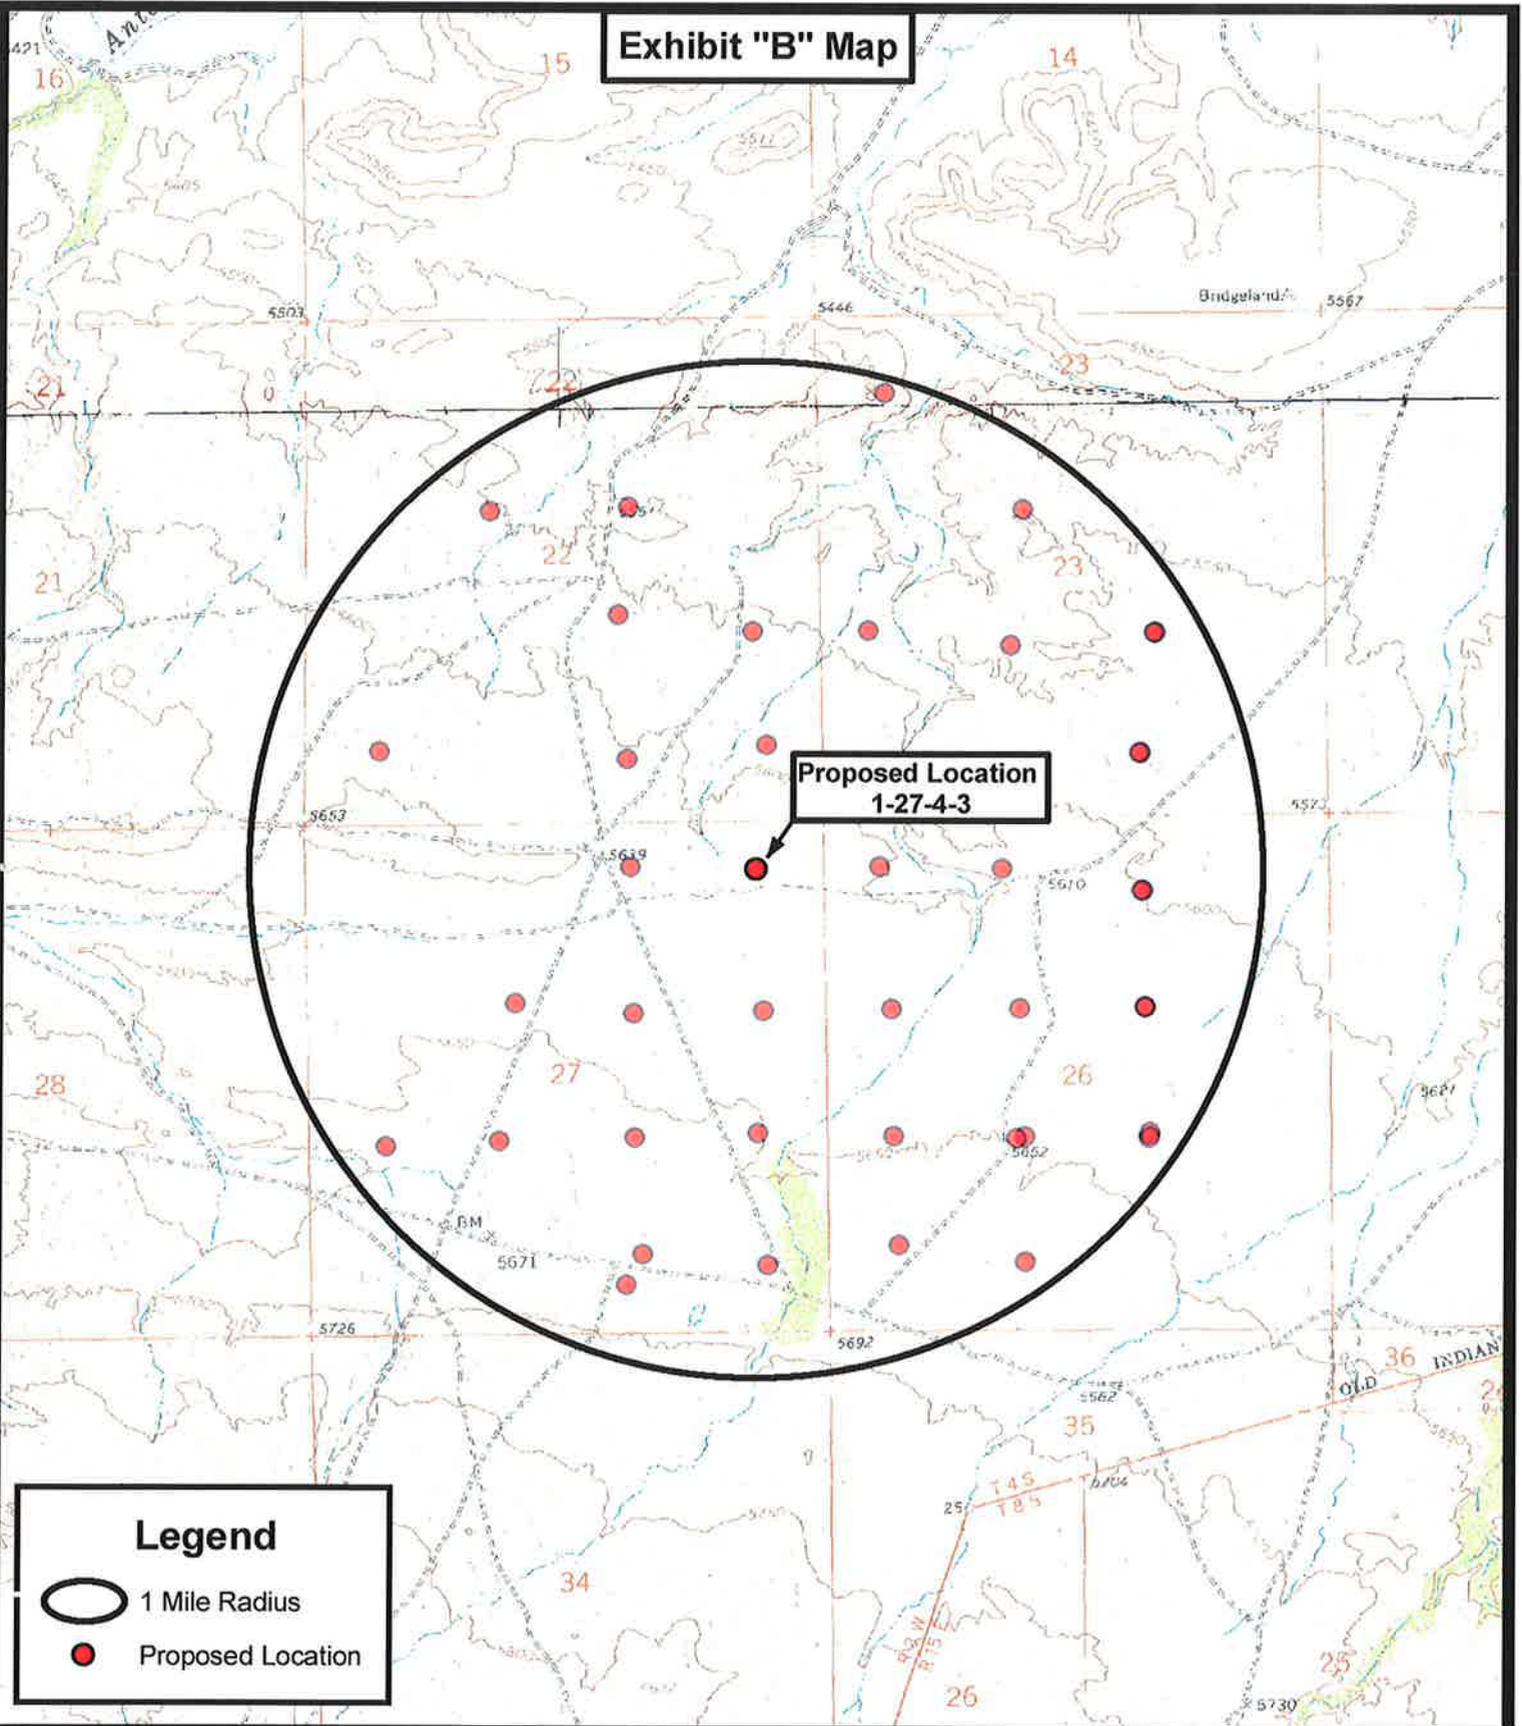

**Proposed Location
1-27-4-3**

Legend

-  1 Mile Radius
-  Proposed Location



**Tri State
Land Surveying, Inc.**
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

**1-27-4-3
SEC. 27, T4S, R3W, U.S.B.&M.
Duchesne County, UT.**

DRAWN BY:	C.H.M.
DATE:	03-25-2010
SCALE:	1" = 2,000'

TOPOGRAPHIC MAP

SHEET
D

**NEWFIELD PRODUCTION COMPANY
UTE TRIBAL 1-27-4-3
NE/NE SECTION 27, T4S, R3W
DUCHESNE COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Ute Tribal 1-27-4-3 located in the NE 1/4 NE 1/4 Section 27, T4S, R3W, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.4 miles ± to the junction of this highway and UT State Hwy 53; proceed in a southwesterly direction approximately 6.4 miles to it's junction with an existing road to the southwest; proceed in a southwesterly direction approximately 2.7 miles to it's junction with an existing road to the northwest; proceed in a northwesterly direction approximately 1.5 miles to it's junction with an existing road to the northeast; proceed northeasterly approximately 0.7 miles to it's junction with the beginning of the proposed access road to the east; proceed easterly along the proposed access road approximately 1,909' to the proposed well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

Approximately 1,909' of access road is proposed for the proposed well. See attached Topographic Map "B".

The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. **LOCATION OF EXISTING AND/OR PROPOSED FACILITIES**

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District
Water Right : 43-7478

Neil Moon Pond
Water Right: 43-11787

Newfield Collector Well
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), State of Utah approved surface disposal facilities, or Federally approved surface disposal facilities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be

reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – Moon Live Stock LLC.

See attached Memorandum of Surface Use Agreement and Easement ROW.

12. **OTHER ADDITIONAL INFORMATION**

Newfield Production Company requests 1,909' of disturbed area be granted to allow for construction of the planned access road. **Refer to Topographic Map "B"**. A permanent width of 30' and a running surface of 18' is proposed for the planned access road. The construction phase of the planned access road will last approximately (5) days. The planned access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 1,008' of disturbed area be granted for construction of the proposed gas lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a 6" gas gathering line, and a 3" poly fuel gas line, with a permanent width of 30' upon completion of the proposed gas lines. The construction phase of the proposed gas lines will last approximately (5) days. Both proposed lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."**

Newfield Production Company requests 1,074' of disturbed area be granted to allow for construction of the proposed water lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line and 30' wide upon completion of the proposed water lines. Both proposed lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** In the event that the proposed well is converted to a water injection well, a separate injection permit will be applied for through the proper agencies.

Surface Flow Line

Newfield Production Company requests 1,021' of disturbed area be granted for construction of a surface flow line bundle. For all new wells, Newfield requests that a 30' Right of way be granted to allow for construction of up to a 14" bundled pipe consisting of 2-2" poly glycol lines and 1-3" production line. Refer to Topographic Map "C" for the proposed location of the proposed flow line. Flow lines will be tan and will be constructed using the following procedures:

Clearing and Grading: the proposed flow line will be placed on the surface of the ground. As such no grading or clearing will be needed. The flow line will be centered staked every 200 feet prior to the installation. The flow line will be as close to the access road as possible without interfering with the normal road travel, or road maintenance

Installation for portions along existing roads, lengths of pipe will be laid in the barrow ditch, welded together and moved into place. For lines that go cross-country minimal access will be needed only for maintenance purpose. It is in the best interest of Newfield Exploration to avoid wet and saturated ground that would cause ruts greater than 3 inches in depth. Disturbed areas will be reclaimed with in 120 days of the end of the installation.

- a) Newfield Production Company is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, Newfield is to immediately stop work that might further disturb such materials and contact the Authorized Officer.
- b) Newfield Production will control noxious weeds along rights-of-way for roads, pipelines, well sites or other applicable facilities. On State administered land it is required that a Pesticide Use Proposal shall be submitted and given approval prior to the application of herbicides or other possible hazardous chemicals.
- c) Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on State Lands after the conclusion of drilling operations or at any other time without State authorization. However, if State authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

The Archaeological and Paleontological Report Waiver is attached.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the Ute Tribal 1-27-4-3, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Ute Tribal 1-27-4-3, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

The State office as well as the Ute Tribe Energy and Mineral Department shall be notified upon site completion prior to moving on the drilling rig.

13. LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:

Representative

Name: Tim Eaton
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that Newfield Production Company is considered to be the operator of well #1-27-4-3, NE/NE Section 27, T4S, R3W, Duchesne County, Utah and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage for this well is covered by the Bureau of Indian Affairs Bond #RLB0010462.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

4/28/10

Date




Mandie Crozier
Regulatory Specialist
Newfield Production Company

NEWFIELD EXPLORATION COMPANY

LOCATION LAYOUT

1-27-4-3

Section 27, T4S, R3W, U.S.B.&M.

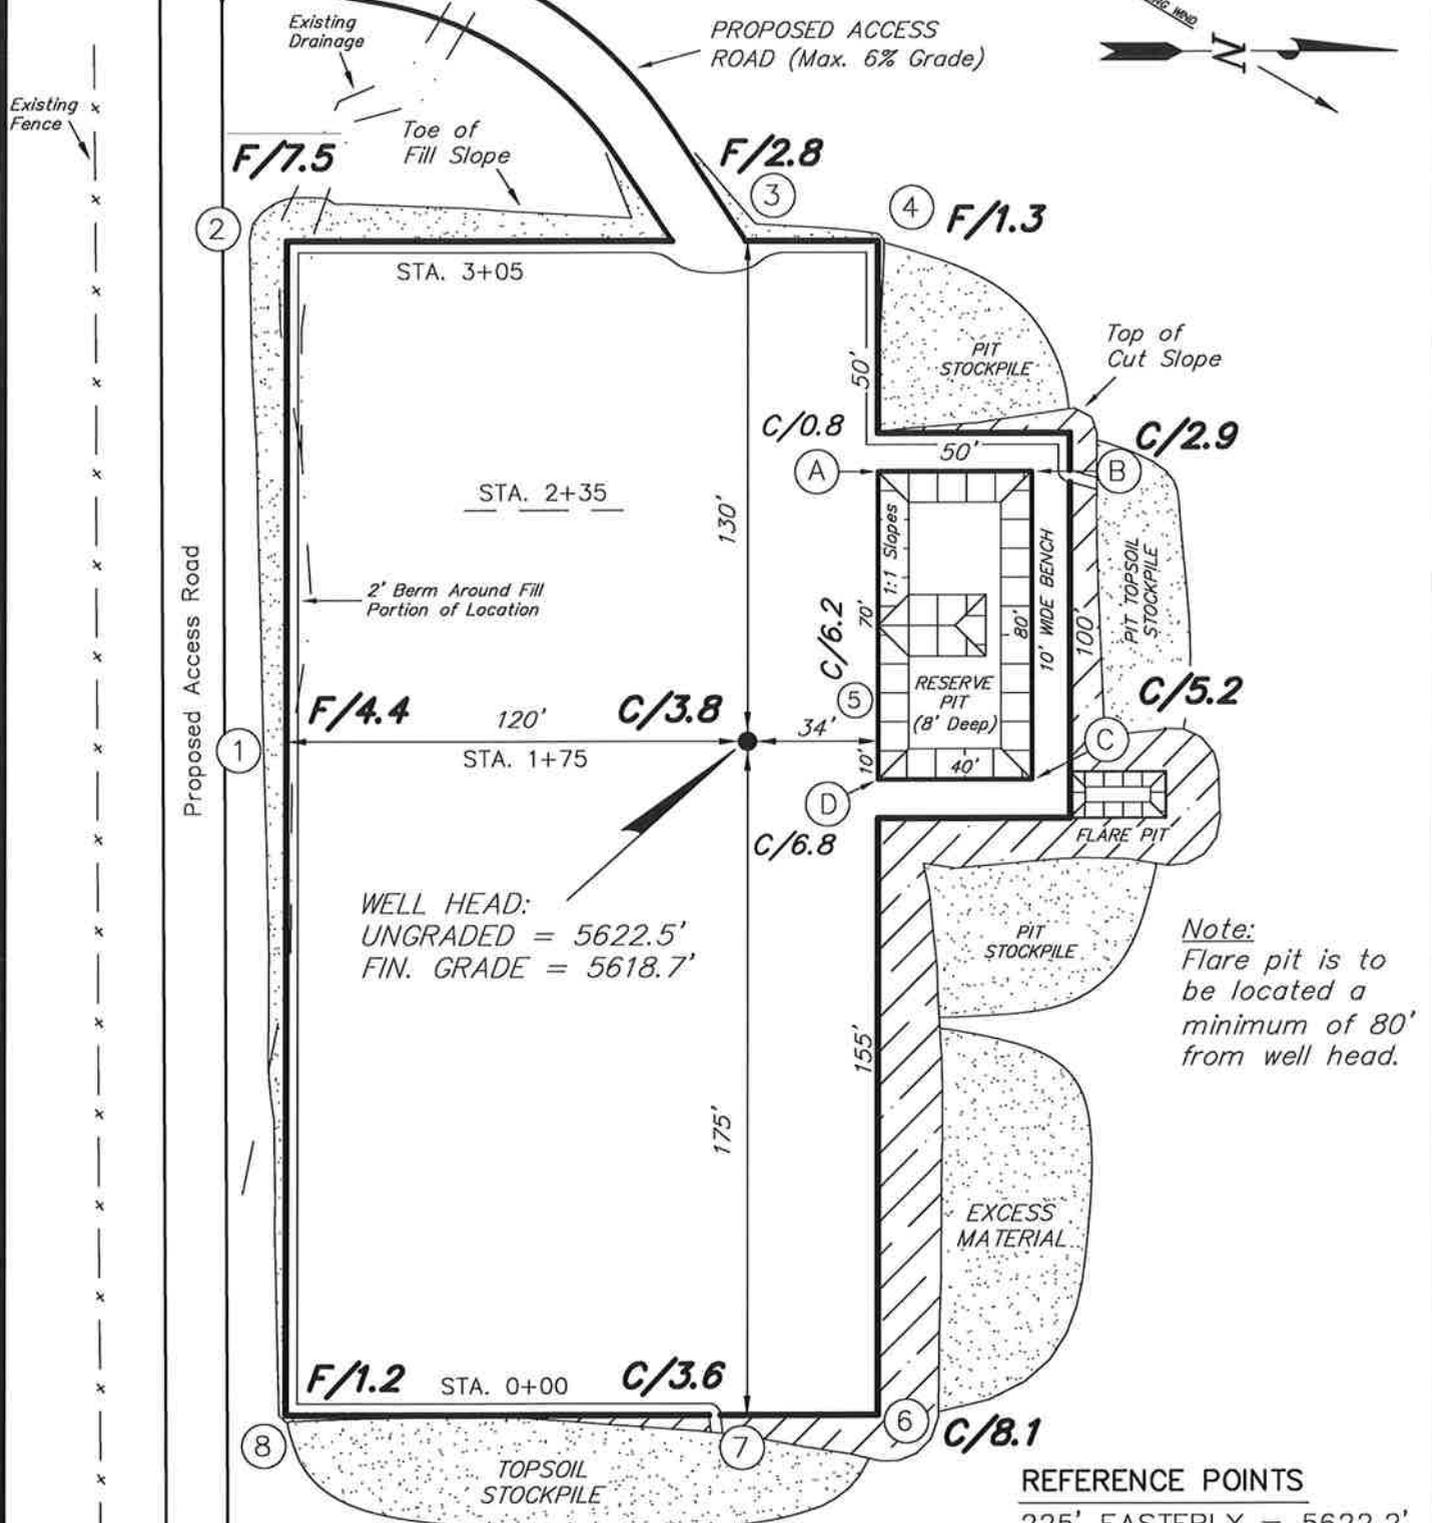

WELL HEAD:
UNGRADED = 5622.5'
FIN. GRADE = 5618.7'

Note:
Flare pit is to be located a minimum of 80' from well head.

- REFERENCE POINTS**
- 225' EASTERLY = 5622.2'
 - 275' EASTERLY = 5623.2'
 - 170' SOUTHERLY = 5615.0'
 - 220' SOUTHERLY = 5615.8'

SURVEYED BY: C.D.S.	DATE SURVEYED: 03-12-10
DRAWN BY: F.T.M.	DATE DRAWN: 03-13-10
SCALE: 1" = 50'	REVISED:





Tri State (435) 781-2501
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD EXPLORATION COMPANY

CROSS SECTIONS

1-27-4-3

Section 27, T4S, R3W, U.S.B.&M.

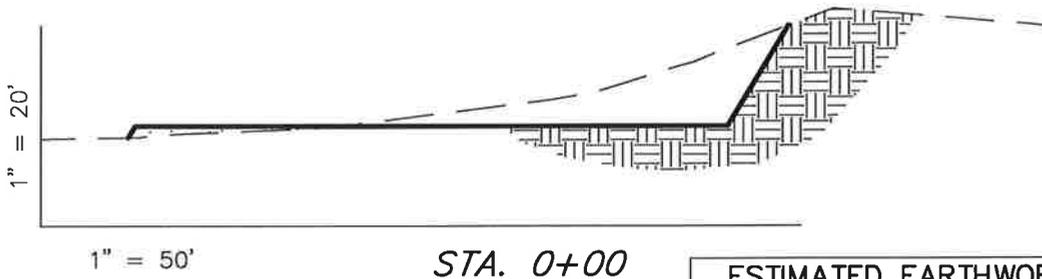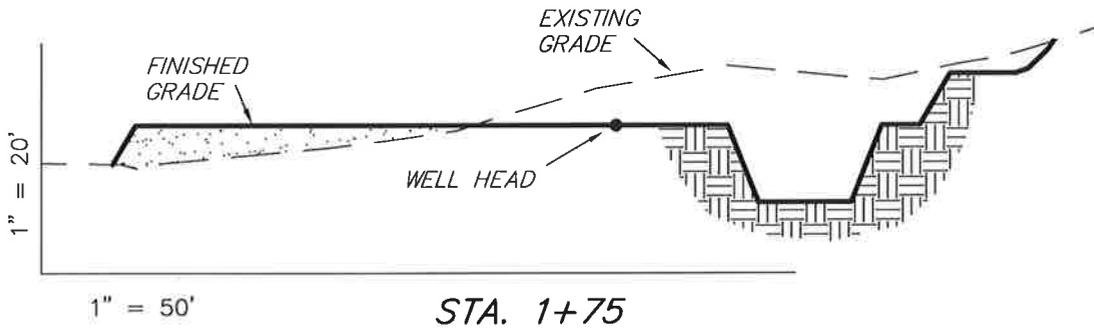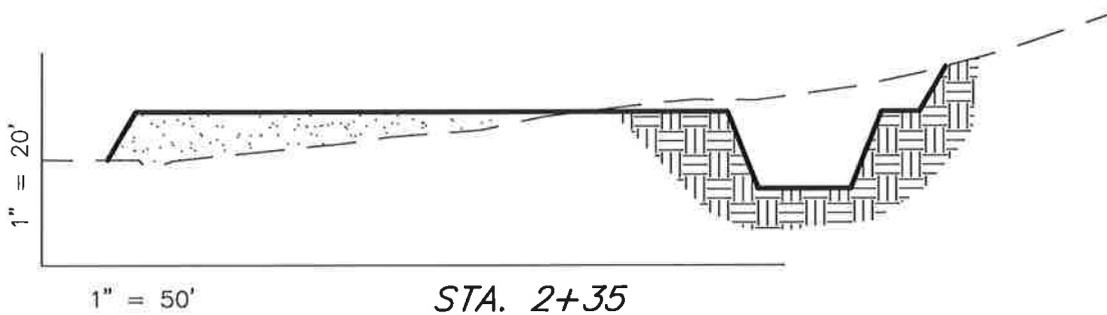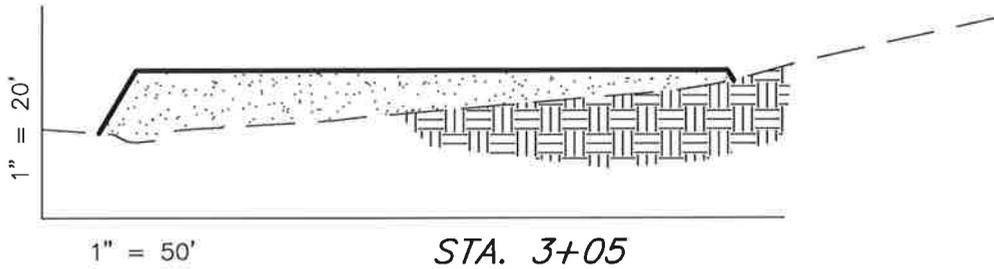

NOTE:
UNLESS OTHERWISE
NOTED ALL CUT/FILL
SLOPES ARE AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES
(No Shrink or swell adjustments have been used)
(Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	3,370	3,360	Topsoil is not included in Pad Cut	10
PIT	640	0		640
TOTALS	4,010	3,360	1,120	650

SURVEYED BY: C.D.S.	DATE SURVEYED: 03-12-10	
DRAWN BY: F.T.M.	DATE DRAWN: 03-13-10	
SCALE: 1" = 50'	REVISED:	

Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078


NEWFIELD EXPLORATION COMPANY

TYPICAL RIG LAYOUT

1-27-4-3


Section 27, T4S, R3W, U.S.B.&M.

PROPOSED ACCESS ROAD (Max. 6% Grade)



Existing Fence

Proposed Access Road

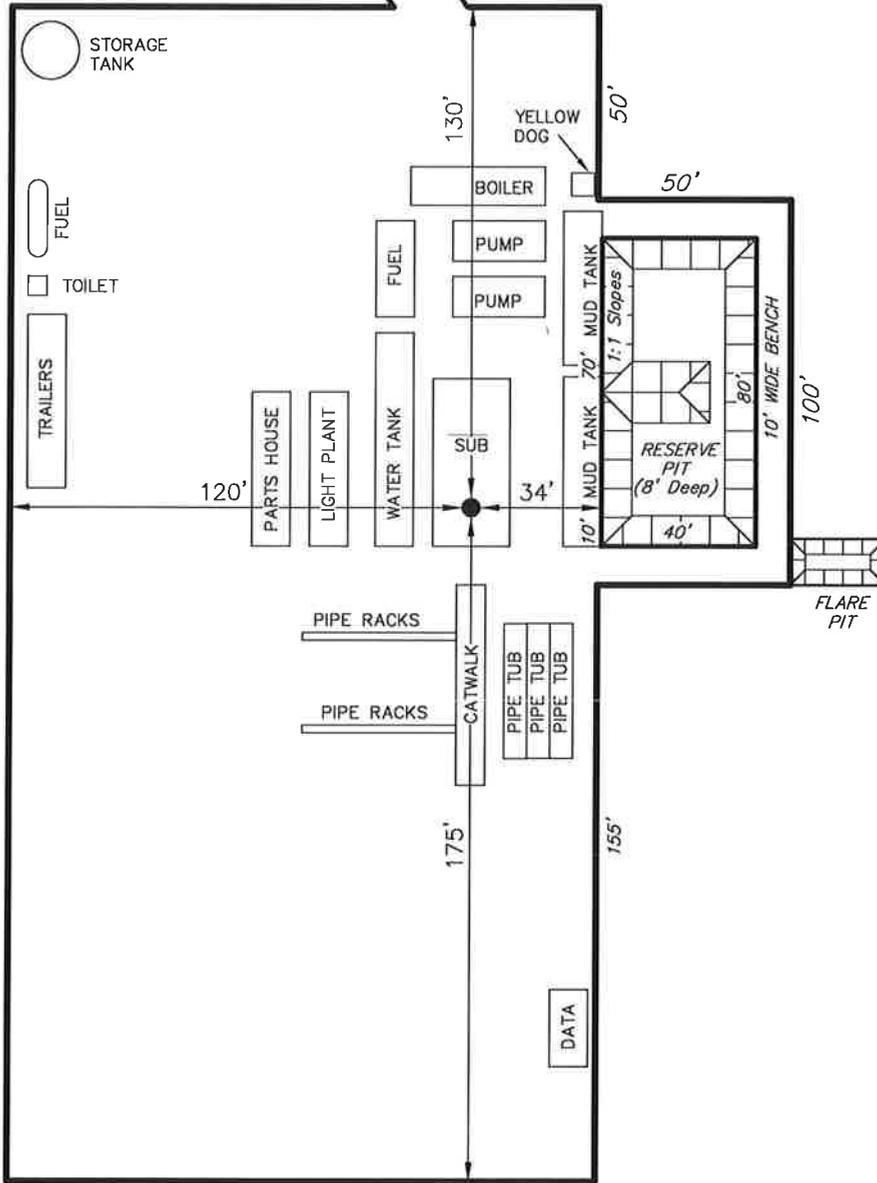

SURVEYED BY: C.D.S.

DATE SURVEYED: 03-12-10

DRAWN BY: F.T.M.

DATE DRAWN: 03-13-10

SCALE: 1" = 50'

REVISED:

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078


Newfield Production Company Proposed Site Facility Diagram

Ute Tribal 1-27-4-3

NE/NE Sec. 27, T4S, R3W

Duchesne County, Utah

14-20-H62-6154

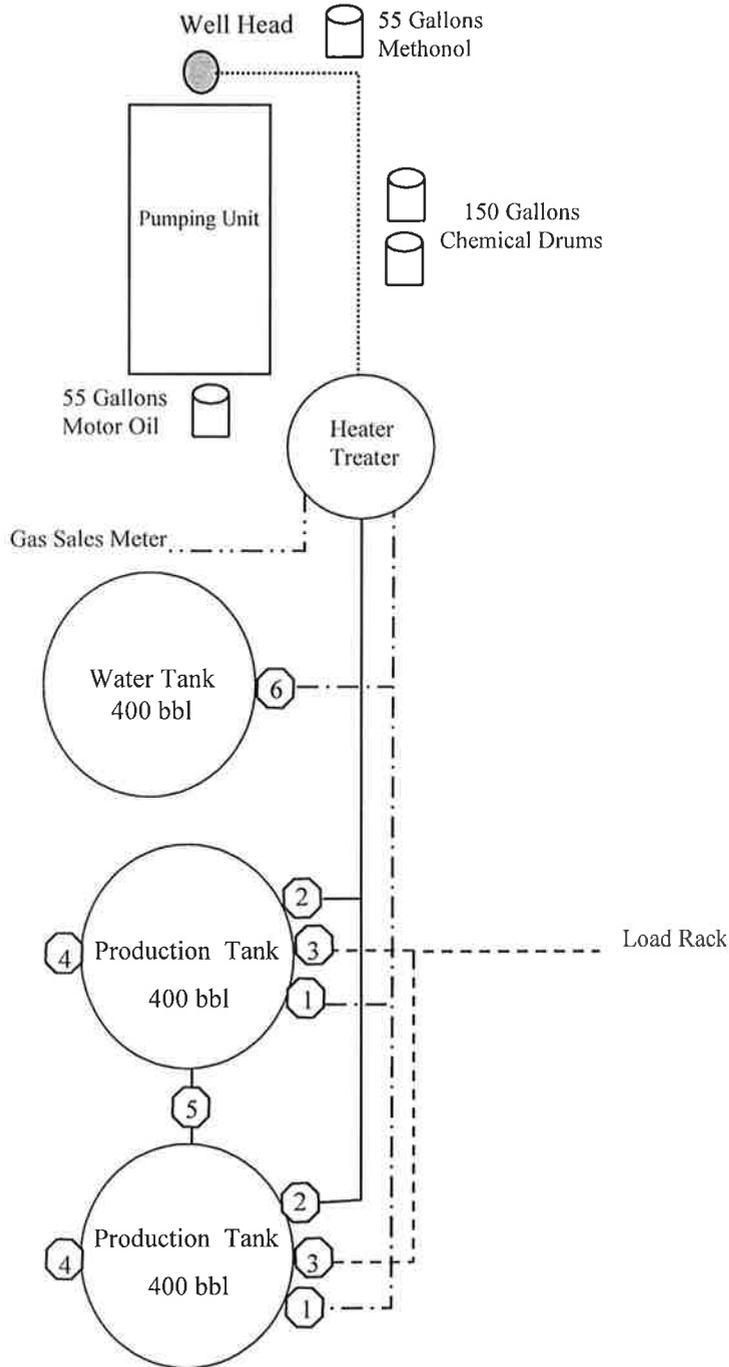

55 Gallons
Methanol

150 Gallons
Chemical Drums

55 Gallons
Motor Oil

Legend

Emulsion Line
Load Rack	- - - - -
Water Line	- . - . -
Gas Sales	-
Oil Line	—————

Production Phase:

- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open

Sales Phase:

- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

Draining Phase:

- 1) Valves 1 and 6 open

Diked Section



EXHIBIT D

Township 4 South, Range 3 West
Section 27: All, being 640 acres more or less.


Duchesne County, Utah

ARCHAEOLOGICAL & PALEOTOLOGICAL REPORT WAIVER

For the above referenced location; Moon Live Stock, LLC; the private surface owners.
(Having a Surface Owner Agreement with Newfield Production Company)

Ken Moon, representing this entity does agree to waive the request from the State of Utah and Bureau of Land Management for an Archaeological/Cultural and Paleotological Resource Survey for any wells covered by the Surface Use Agreement dated 3/17/2010 between the above said private land owner and Newfield Production. This waiver hereby releases Newfield Production Company from this request.




Ken Moon Date
Moon Live Stock, LLC 3-24-2010


Brad Mecham Date
Newfield Production Company 3-25-2010

API Number: 4301350331
Well Name: Ute Tribal 1-27-4-3
Township 04.0 S Range 03.0 W Section 27
Meridian: UBM
 Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
 Map Produced by Diana Mason

- | | |
|---------------------|------------------------------------|
| Units STATUS | Wells Query |
| ACTIVE | <-all other values> |
| EXPLORATORY | APD - Approved Permit |
| GAS STORAGE | DRL - Spudded (Drilling Commenced) |
| NF PP OIL | GIW - Gas Injection |
| NF SECONDARY | GS - Gas Storage |
| PI OIL | LA - Location Abandoned |
| PP GAS | LOC - New Location |
| PP GEOTHERMAL | OPS - Operation Suspended |
| PP OIL | PA - Plugged Abandoned |
| SECONDARY | PGW - Producing Gas Well |
| TERMINATED | POW - Producing Oil Well |
| Fields | RET - Returned APD |
| Sections | SGW - Shut-in Gas Well |
| Township | SOW - Shut-in Oil Well |
| | TA - Temp. Abandoned |
| | TW - Test Well |
| | WDW - Water Disposal |
| | WW - Water Injection Well |
| | WSW - Water Supply Well |

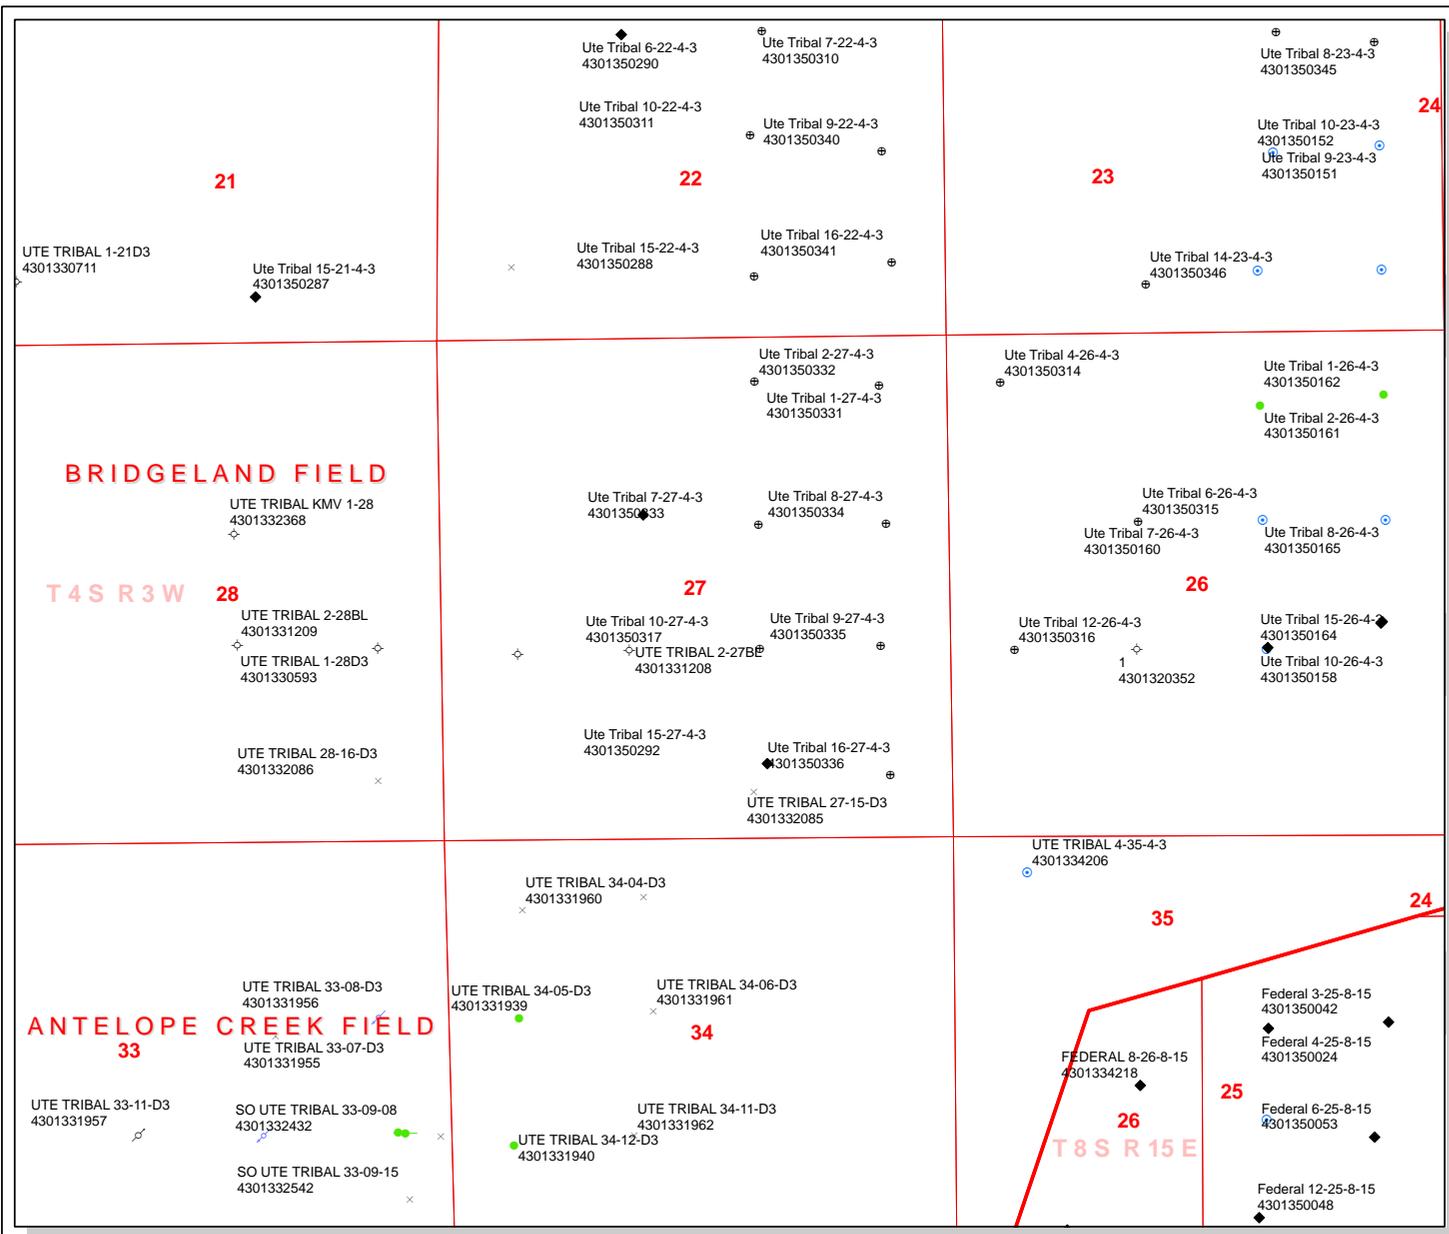

ON-SITE PREDRILL EVALUATION

Utah Division of Oil, Gas and Mining

Operator	NEWFIELD PRODUCTION COMPANY				
Well Name	Ute Tribal 1-27-4-3				
API Number	43013503310000	APD No	2624	Field/Unit	UNDESIGNATED
Location: 1/4,1/4	NENE	Sec	27	Tw	4.0S Rng 3.0W 515 FNL 728 FEL
GPS Coord (UTM)	568074 4440261	Surface Owner	Moon Live Stock LLC		

Participants

Floyd Bartlett (DOGM), Joe Pippy (Newfield Permitting), Scott Vernon (Tri-State Land Surveying), Christine Cimiluca and Cheryl Laroque (BLM).

Regional/Local Setting & Topography

The proposed location is approximately 12.7 road miles southwest of Myton, UT in the South Myton Bench/Antelope Creek area. Drainages in the area run northerly toward the Duchesne River about 4 miles away but are intercepted by the Pleasant Valley Irrigation Canal. Broad flats and rolling hills with those near the edge of the bench becoming steep and intersected with draws, characterize the area. Access is by State, County and planned or existing oil field development roads. Approximately 1047 feet of new construction across Moon’s private land will be required to reach the location.

The proposed Ute Tribal 1-27-4-3 oil well pad laid out in a west to east direction on the south slope of a ridge. It extends south into a flat which is north of a wire fence. The location was moved to the ridge edge so as to avoid the fence and leave room for a road to parallel the location side of the fence. A swale runs through the site in the pit area but will not require a diversion. An 8.1-foot fill is required on corner 2. No springs, streams or seeps are known to exist in the immediate area. The selected site appears to be a good location for constructing a pad, drilling and operating a well.

Moon Livestock own the surface of the location. Mr. Ken Moon is the contact person. . The BLM contacted Mr. Moon by telephone and invited him to the pre-site visit. He said he would not attend. A signed landowner agreement exists. The minerals are owned by the United States Government and held in trust for the Ute Indian Tribe.

Surface Use Plan

Current Surface Use

Grazing
Wildlfe Habitat

New Road Miles	Well Pad	Src Const Material	Surface Formation
0.2	Width 204 Length 305	Onsite	UNTA

Ancillary Facilities N

Waste Management Plan Adequate?

Environmental Parameters

Affected Floodplains and/or Wetlands N

Flora / Fauna

A desert shrub type vegetation covers the area. Principal plants consist of sagebrush, horsebrush, fringe sage, cheatgrass, halogeton, globe mallows, shadscale, curly mesquite, and spring annuals.

Cattle, deer, prairie dogs, small mammals and birds.

Soil Type and Characteristics

Deep sandy loam with some shaley rock outcrops.

Erosion Issues N

Sedimentation Issues N

Site Stability Issues N

Drainage Diverson Required? N

Berm Required? Y

Erosion Sedimentation Control Required? Y

Paleo Survey Run? **Paleo Potental Observed?** N **Cultural Survey Run?** N **Cultural Resources?**

Reserve Pit

Site-Specific Factors

Site Ranking

Distance to Groundwater (feet)	100 to 200	5
Distance to Surface Water (feet)	>1000	0
Dist. Nearest Municipal Well (ft)	>5280	0
Distance to Other Wells (feet)	300 to 1320	10
Native Soil Type	Mod permeability	10
Fluid Type	Fresh Water	5
Drill Cuttings	Normal Rock	0
Annual Precipitation (inches)		0
Affected Populations		
Presence Nearby Utility Conduits	Not Present	0
	Final Score	30

1 Sensitivity Level

Characteristics / Requirements

A reserve pit 40' x 80' x 8' deep will be located in an area of cut on the northwest side of the location. A pit liner is required. Newfield commonly uses a 16-mil liner.

Closed Loop Mud Required? N **Liner Required?** Y **Liner Thickness** 16 **Pit Underlayment Required?** Y

Other Observations / Comments

ATV's were used to reach the site.

Floyd Bartlett
Evaluator

5/12/2010
Date / Time

Application for Permit to Drill

Statement of Basis

5/26/2010

Utah Division of Oil, Gas and Mining

Page 1

APD No	API WellNo	Status	Well Type	Surf Owner	CBM
2624	43013503310000	LOCKED	OW	P	No
Operator	NEWFIELD PRODUCTION COMPANY		Surface Owner-APD	Moon Live Stock LLC	
Well Name	Ute Tribal 1-27-4-3		Unit		
Field	UNDESIGNATED		Type of Work	DRILL	
Location	NENE 27 4S 3W U 515 FNL 728 FEL		GPS Coord (UTM)	568073E	4440257N

Geologic Statement of Basis

The mineral rights for the proposed well are owned by the Ute Tribe. The BLM will be the agency responsible for evaluating and approving the drilling, casing and cement programs.

Brad Hill
APD Evaluator

5/24/2010
Date / Time

Surface Statement of Basis

The proposed location is approximately 12.7 road miles southwest of Myton, UT in the South Myton Bench/Antelope Creek area. Drainages in the area run northerly toward the Duchesne River about 4 miles away but are intercepted by the Pleasant Valley Irrigation Canal. Broad flats and rolling hills with those near the edge of the bench becoming steep and intersected with draws, characterize the area. Access is by State, County and planned or existing oil field development roads. Approximately 1047 feet of new construction across Moon's private land will be required to reach the location.

The proposed Ute Tribal 1-27-4-3 oil well pad laid out in a west to east direction on the south slope of a ridge. It extends south into a flat which is north of a wire fence. The location was moved to the ridge edge so as to avoid the fence and leave room for a road to parallel the location side of the fence. A swale runs through the site in the pit area but will not require a diversion. An 8.1-foot fill is required on corner 2. No springs, streams or seeps are known to exist in the immediate area. The selected site appears to be a good location for constructing a pad, drilling and operating a well.

Moon Livestock own the surface of the location. Mr. Ken Moon is the contact person. The BLM contacted Mr. Moon by telephone and invited him to the pre-site visit. He said he would not attend. A signed landowner agreement exists. The minerals are owned by the United States Government and held in trust for the Ute Indian Tribe. Acting for the Ute Indian Tribe, Ms. Christine Cimiluca and Ms. Cheryl Laroque of the BLM attended the pre-site evaluation. They specified the color of paint the facilities were to be painted and had no surface concerns. Reclamation of the site will be as directed in the Multi-point Operating Plan.

Floyd Bartlett
Onsite Evaluator

5/12/2010
Date / Time

Conditions of Approval / Application for Permit to Drill

Category	Condition
Pits	A synthetic liner with a minimum thickness of 16 mils with a felt subliner shall be properly installed and maintained in the reserve pit.
Surface	The well site shall be bermed to prevent fluids from leaving the pad.
Surface	The reserve pit shall be fenced upon completion of drilling operations.

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 4/29/2010

API NO. ASSIGNED: 43013503310000

WELL NAME: Ute Tribal 1-27-4-3

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: NENE 27 040S 030W

Permit Tech Review:

SURFACE: 0515 FNL 0728 FEL

Engineering Review:

BOTTOM: 0515 FNL 0728 FEL

Geology Review:

COUNTY: DUCHESNE

LATITUDE: 40.11176

LONGITUDE: -110.20124

UTM SURF EASTINGS: 568073.00

NORTHINGS: 4440257.00

FIELD NAME: UNDESIGNATED

LEASE TYPE: 2 - Indian

LEASE NUMBER: 14-20-H62-6154

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 4 - Fee

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: INDIAN - RLB0010462
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 43-7478
- RDCC Review:
- Fee Surface Agreement
- Intent to Commingle


Commingle Approved

LOCATION AND SITING:

- R649-2-3.
- Unit:
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
- Board Cause No: R649-3-2
- Effective Date:
- Siting:
- R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason
5 - Statement of Basis - bhill
23 - Spacing - dmason



State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Ute Tribal 1-27-4-3
API Well Number: 43013503310000
Lease Number: 14-20-H62-6154
Surface Owner: FEE (PRIVATE)
Approval Date: 6/1/2010

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of R649-3-2. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.

Compliance with the Conditions of Approval/Application for Permit to Drill outlined in the Statement of Basis (copy attached).

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during

drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)
- OR
- submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <https://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:



Acting Associate Director, Oil & Gas

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

5a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		7. If Unit or CA Agreement, Name and No. NA
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		8. Lease Name and Well No. Ute Tribal 1-27-4-3
2. Name of Operator Newfield Production Company		9. API Well No. 43-013-50331
3a. Address Route #3 Box 3630, Myton UT 84052	3b. Phone No. (include area code) (435) 646-3721	10. Field and Pool, or Exploratory Undesignated
4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NE/NE 515' FNL 728' FEL At proposed prod. zone		11. Sec., T. R. M. or Blk. and Survey or Area Sec. 27, T4S R3W
14. Distance in miles and direction from nearest town or post office* Approximately 13.1 miles southwest of Myton, UT		12. County or Parish Duchesne
15. Distance from proposed* location to nearest property or lease line, ft. Approx. 515' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)		13. State UT
16. No. of acres in lease NA		17. Spacing Unit dedicated to this well 40 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1370'		20. BLM/BIA Bond No. on file RLB0010462
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5623' GL		22. Approximate date work will start* 3rd Qtr. 2010
		23. Estimated duration (7) days from SPUD to rig release

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 4/28/10
Title Regulatory Specialist		

Approved by (Signature) <i>James H. Sparger</i>	Name James H. Sparger	Date SEP 10 2010
Title Acting Assistant Field Manager Lands & Mineral Resources		
Office VERNAL FIELD OFFICE		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)



RECEIVED
OCT 14 2010
DIV. OF OIL, GAS & MINING

RECEIVED NOS 04/29/10
AFMSS# 10550261A
MAY 03 2010

*(Instructions on page 2)

NOTICE OF APPROVAL

BLM VERNAL, UTAH

CONDITIONS OF APPROVAL ATTACHED



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company Location: NENE, Sec.27, T4S R3W
Well No: Ute Tribal 1-27-4-3 Lease No: 14-20-H62-6154
API No: 43-013-50331 Agreement: N/A

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Construction Activity (Notify Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist)	- The Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist shall be notified at least 48 hours in advance of any construction activity. The Ute Tribal office is open Monday through Thursday.
Construction Completion (Notify Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist)	- Upon completion of the pertinent APD/ROW construction, notify the Ute Tribe Energy & Minerals Dept. for a Tribal Technician to verify the Affidavit of Completion. Notify the BLM Environmental Scientist prior to moving on the drilling rig.
Spud Notice (Notify BLM Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify BLM Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: ut_vn_opreport@blm.gov .
BOP & Related Equipment Tests (Notify BLM Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify BLM Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

Site Specific Conditions of Approval

- No BLM surface COA's, private surface.

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- The operator shall comply with all applicable requirement in the SOP (version: "Ute Tribe Green River Development Program", April 17, 2008). The operator shall also comply with applicable laws and regulations; with the lease terms, Onshore Oil and Gas Orders, NTL's; and with other orders and instructions of the authorized officer.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth

(from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location ($\frac{1}{4}$ $\frac{1}{4}$, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or

data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

Spud
BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross Rig # 21
Submitted By Ryan Crum Phone Number 823-7065
Well Name/Number Ute Tribal 1-27-4-3
Qtr/Qtr NE/NE Section 27 Township 4s Range 3w
Lease Serial Number 14-20-H62-6154
API Number 43-013-50331

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 11/23/10 8:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 11/23/10 2:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks _____

STATE OF UTAH
 DIVISION OF OIL, GAS AND MINING
 ENTITY ACTION FORM -FORM 6

OPERATOR: **NEWFIELD PRODUCTION COMPANY**
 ADDRESS: **RT. 3 BOX 3630**
MYTON, UT 84052

OPERATOR ACCT. NO. **N2695**


ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION				COUNTY	SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG			
A	99999	17874	4304751125	UTE TRIBAL 11-12-4-1E	NESW	12	4S	1E	UINTAH	11/23/2010	11/29/10
WELL 1 COMMENTS: GRRV											
A	99999	17875	4301350331	UTE TRIBAL 1-27-4-3	NENE	27	4S	3W	DUCHESNE	11/23/2010	11/29/10
WELL 1 COMMENTS: GRRV											

ACTION CODES (See instructions on back of form)
 A - new entity for new well (single well only)
 B - well to existing entity (group or unit well)
 C - from one existing entity to another existing entity
 D - well from one existing entity to a new entity
 E - other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.

RECEIVED
 NOV 23 2010

DIV. OF OIL, GAS & MINING

Signature 
 Jentri Park
 Production Clerk
 11/23/10

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include area code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
0515 FNL 0728 FEL
NENE Section 27 T4S R3W

5. Lease Serial No.
UTE TR EDA 14-20-H62-6154

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.
UTE TRIBAL 1-27-4-3

9. API Well No.
4301350331

10. Field and Pool, or Exploratory Area
MYTON-TRIBAL EDA

11. County or Parish, State
DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

(A) TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 11/23/10 MIRU Ross #21. Spud well @ 8:00am. Drill 310' of 121/4" hole with air mist. TIH w/7 jt's 85/8" j-55 24# csgn. set @ 313.81KB On 12/1/10 cement with 160 sks of class "G" w/ 2% Calcium Chloride mixed @ 15.8 ppg > 1.17 cf/sk yeild. Returned 4 bbls cement to pit. Woc.

RECEIVED
JAN 10 2011

DIV. OF OIL, GAS & MINING

I hereby certify that the foregoing is true and correct (Printed/ Typed)
Jay Burton
Signature *Jay E. Burton*
Title Drilling Foreman
Date 12/04/2010

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
UTE TR EDA 14-20-H62-6154

SUNDRY NOTICES AND REPORTS ON WELLS

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

8. WELL NAME and NUMBER:
UTE TRIBAL 1-27-4-3

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:
4301350331

3. ADDRESS OF OPERATOR:
Route 3 Box 3630 CITY Myton STATE UT ZIP 84052

PHONE NUMBER
435.646.3721

10. FIELD AND POOL, OR WILDCAT:
MYTON-TRIBAL EDA

4. LOCATION OF WELL:

FOOTAGES AT SURFACE:

COUNTY: DUCHESNE

OTR/OTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: NENE, 27, T4S, R3W

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 01/19/2011	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	


12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was completed on 01-19-11, attached is a daily completion status report.

NAME (PLEASE PRINT) Lucy Chavez-Naupoto

TITLE Administrative Assistant

SIGNATURE



DATE 01/21/2011

(This space for State use only)

RECEIVED

JAN 25 2011

DIV. OF OIL, GAS & MINING

Daily Activity Report

Format For Sundry

UTE TRIBAL 1-27-4-3**11/1/2010 To 3/28/2011****1/10/2011 Day: 1****Completion**

Rigless on 1/10/2011 - Test casing to 4500 psi. CBL/Perferate 1st stage. - RU Frac head & Cameron BOP's. RU Hot Oiler & test casing, frac head w/ valves & BOP's to 4500 psi. RU Perforators WLT w/ mast & run CBL under pressure. WLTD wasw 6741' w/ cement top @ 180'. RIH w/ 3-1/8" Port Guns (11 gram, .36"EH, 120°, 16.82"pen) & perferate CP4 sds @ 6213-20' w/ 3 spf for total of 21 shots. RD WLT & Hot Oiler. SIFN w/ 161 bbls EWTR.

Daily Cost: \$0**Cumulative Cost:** \$12,695**1/12/2011 Day: 2****Completion**

Rigless on 1/12/2011 - Frac well. Flowback frac. - RU The Perforators wireline. Set CBP & perf A3 sds as shown in perforation report. RU BJ Services. Frac A3 sds as shown in stimulation report. 803 BWTR. - RU The Perforators wireline. Set CBP & perf B2/C sds as shown in perforation report. RU BJ Services. Frac B2/C sds as shown in stimulation report. 1289 BWTR. - RU BJ Services. Frac CP4 sds as shown in stimulation report. 482 BWTR. - RU The Perforators wireline. Set CBP & perf D1/PB10 sds as shown in perforation report. RU BJ Services. Frac D1/PB10 sds as shown in stimulation report. 1562 BWTR. RD BJ Services & The Perforators wireline. Open well to pit for immediate flowback @ approx. 3 bpm. Well flowed for 5 hrs & died. Recovered 650 bbls. SWIFN. 912 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$81,707**1/14/2011 Day: 3****Completion**

Stone #8 on 1/14/2011 - MIRU Stone #8. Thaw out BOP & WH. ND Cameron BOP. NU Schaeffer BOP. SIWFN w/ 1279 BWTR. - MIRU Stone #8. Thaw out BOP & WH. ND Cameron BOP. NU Schaeffer BOP. SIWFN w/ 1279 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$84,787**1/17/2011 Day: 4****Completion**

Stone #8 on 1/17/2011 - Hot oiler steamed and thawed out BOP & WH. 400 psi on well. Bleed off pressure. Continue PU & RIH w/ tbg. Tagged plug @ 5170'. RU RBS power swivel. Drill out 3 CBP's. Circulate well clean. SIWFN w/ 1304 BWTR. - Hot oiler steamed and thawed out BOP & WH. 400 psi on well. Bleed off pressure. Continue PU & RIH w/ tbg. Tagged plug @ 5170'. RU RBS power swivel. Drill out 3 CBP's. Circulate well clean. SIWFN w/ 1304 BWTR.

Daily Cost: \$0**Cumulative Cost:** \$91,134**1/18/2011 Day: 5****Completion**

Stone #8 on 1/18/2011 - C/O to PBTD. Swab, Flow. C/O PBTD. LD 18 tjs of tbg. TOH w/ bit. TIH w/ production tbg. EOT @ 3255'. SIWFN w/ 1229 BWTR. - Hot oiler steamed and thawed

out BOP & WH. PU 28 jts of tbg. Tagged sand @ 6647'. C/o to PBD @ 6803'. LD 3 jts of tbg. RU swab equipment. Made 7 runs. Well started flowing. Rec 160 BTF. RD swab equipment. Pumped 30 BW down tbg. PU 3 jts of tbg. Tagged sand @ 6798'. C/O to PBD @ 6803'. Circulate clean w/ 170 BW. LD 18 jts of tbg. TOH w/ 201 jts of tbg. TIH w/ NC, 2- jts, SN, 1 jts, TA, 100 jts of tbg. EOT @ 3255'. SIWFW w/ 1229 BWTR.

Daily Cost: \$0

Cumulative Cost: \$105,412

1/19/2011 Day: 6

Completion

Stone #8 on 1/19/2011 - Continue TIH w/ production tbg. ND BOP, Set TA. NU WH. Flush tbg w/ 60 BW. PU & RIH w/ "A" grade rod string. Hang head, Space out rods. Pressure test to 800 psi. RDMOSU. POP @ 5:00 PM w/ 122" SL @ 4 SPM. 1212 BWTR. FINAL REPORT!! - Hot oiler steamed and thawed out WH and BOP. 350 psi on tbg, 600 psi on csg. Circulate well w/ 90 BW. Continue TIH w/ production tbg. Detail as follows: NC, 2- jts, SN, 1- jt, TA, 198 jts of 2 7/8" J-55 tbg. ND BOP. Set TA w/ 18,000#'s of tension. NU WH. Flush tbg w/ 60 BW. PU & RIH w/ "A" grade rod string as follows: Central hydraulic rod pump 2 1/2" X 1 1/2" X 21' X 24' RHAC, 6- 1 1/2" wt bars, 141- 3/4" guided rods, 100- 7/8" guided rods, 1- 8', 1- 4' X 7/8" pony rods, 1 1/2" X 30' polish rod. Hang head, Space out rods. Pressure test to 800 psi. RDMOSU. POP @ 5:00 PM w/ 122" SL @ 4 SPM. 1212 BWTR. FINAL REPORT!! **Finalized**

Daily Cost: \$0

Cumulative Cost: \$177,109

Pertinent Files: Go to File List

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
14-20-H62-6154

1a. Type of Well Oil Well Gas Well Dry Other
 b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Resvr.,
 Other: _____

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

8. Lease Name and Well No.
UTE TRIBAL 1-27-4-3

3. Address
1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
(435)646-3721

9. AFI Well No.
43-013-50331

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

10. Field and Pool or Exploratory
MYTON-TRIBAL EDA

At surface 515' FNL & 728' FEL (NE/NE) SEC. 27, T4S, R3W

11. Sec., T., R., M., on Block and Survey or Area
SEC. 27, T4S, R3W

At top prod. interval reported below

12. County or Parish
DUCHESNE

13. State
UT

At total depth 6865'

14. Date Spudded
11/23/2010

15. Date T.D. Reached
12/26/2010

16. Date Completed 01/18/2011
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5623' GL 5635' KB

18. Total Depth: MD 6865'
TVD

19. Plug Back T.D.: MD 6803'
TVD

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
 Was DST run? No Yes (Submit report)
 Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	314'		160 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	6849'		300 PRIMLITE		180'	
						425 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 6298'	TA @ 6201'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Green River	4824'	6220'	4824-6220'	.36"	90	
B)						
C)						
D)						

26. Perforation Record

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
4824-6220'	Frac w/ 116874#'s 20/40 sand in 840 bbls of Lightning 17 fluid in 4 stages

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
01/18/11	01/27/11	24	→	269	110	98			2-1/2" x 1-1/2" x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

*(See instructions and spaces for additional data on page 2)

RECEIVED

FEB 03 2011

DIV. OF OIL, GAS & MINING

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD & USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
GREEN RIVER	4824'	6220'		GARDEN GULCH MRK GARDEN GULCH 1	3982' 4227'
				GARDEN GULCH 2 POINT 3	4355' 4648'
				X MRKR Y MRKR	4909' 4940'
				DOUGALS CREEK MRK BI CARBONATE MRK	5057' 5331'
				B LIMESTON MRK CASTLE PEAK	5474' 6003'
				BASAL CARBONATE WASATCH	6418' 6553'

32. Additional remarks (include plugging procedure):


33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Lucy Chavez-Naupoto

Title Administrative Assistant

Signature 

Date 01/31/2011

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Daily Activity Report**Format For Sundry****UTE TRIBAL 1-27-4-3****10/1/2010 To 2/28/2011****UTE TRIBAL 1-27-4-3****Waiting on Cement****Date:** 12/2/2010

Ross #21 at 310. Days Since Spud - @ 313.81'KB. On 12/1/10 cemented w/BJ 160sks of Class G+2% Calcium Chloride. 4BBLS returned to - Pit. Cement Mixed @ 15.8ppg W/1.17 yeild. - On 11/23/10 Ross # 21 spud @ 8:00am. Drilled 310' of 12.25" hole. Then ran 7jts of 8 5/8" casing set

Daily Cost: \$0**Cumulative Cost:** \$47,885**UTE TRIBAL 1-27-4-3****Rigging Up****Date:** 12/20/2010

Aztec #184 at 310. 0 Days Since Spud - of BOP test on 12/19/2010 at 6:00 PM. All notifacations made by email. - Contact BLM and state on 12/18/2010 of rig move on 12/19/2010 at 7:00 AM. Also notify 12/18/2010 - Safety meeting held w/ Jones trucking, myself and rig crew of proper body placement while picking eq - Hook up flow line and finish rigging up. - Hook up pumps and nipple up BOP and choke manifold. - Move rig and set all equipment with Jones Trucking. (.75 mile rig move from the UT 13-22-4-3w) - Then test the surface casing at 1500 psi for 30 minutes. Tested ok. - kill line, choke line and manifold. Ten min at 2000 psi. all tests ok. - Accept rig and test the upper kelly valve, safety valve, pipe rams and out side valve. Blind ram,

Daily Cost: \$0**Cumulative Cost:** \$96,374**UTE TRIBAL 1-27-4-3****Drill 7 7/8" hole with fresh water****Date:** 12/21/2010

Aztec #184 at 1194. 0 Days Since Spud - Rig up flow line, move BHA over to pipe racks and strap. - Drill 7-7/8" hole with water from 271' to 1194' with 15,000# WOB, 150 TRPM 400 GPMS 51.3 TROP - P/U BHA and directional tools. Scribe directional tool and mud motor

Daily Cost: \$0**Cumulative Cost:** \$114,374**UTE TRIBAL 1-27-4-3****Drill 7 7/8" hole with fresh water****Date:** 12/22/2010

Aztec #184 at 2600. 1 Days Since Spud - Drill 7-7/8" hole with water from 2255' to 2600' with 15,000# WOB, 150 TRPM 400 GPMS 69 TROP - Rig service. Function test BOP and crown-o-matic - Drill 7-7/8" hole with water from 1194' to 1844' with 15,000# WOB, 150 TRPM 400 GPMS 72.2 TROP - Work on brakes - Drill 7-7/8" hole with water from 1844' to 2255' with 15,000# WOB, 150 TRPM 400 GPMS 58 TROP - Rig repair. Change out Hydraulic hose on unit.

Daily Cost: \$0**Cumulative Cost:** \$133,075**UTE TRIBAL 1-27-4-3****Drill 7 7/8" hole with fresh water****Date:** 12/23/2010

Aztec #184 at 4375. 2 Days Since Spud - Rig service. Function test BOP and crown-o-matic - Drill 7-7/8" hole with water from 3420' to 4375' with 15,000# WOB, 150 TRPM 400 GPMS 79.6 TROP - Drill 7-7/8" hole with water from 2600' to 3420' with 15,000# WOB, 150 TRPM

400 GPMS 71.3 TROP

Daily Cost: \$0**Cumulative Cost:** \$175,670**UTE TRIBAL 1-27-4-3****Drill 7 7/8" hole with fresh water****Date:** 12/24/2010

Aztec #184 at 5900. 3 Days Since Spud - Drill 7-7/8" hole with water from 4372' to 5123' with 15,000# WOB, 150 TRPM 400 GPMS 68.3 TROP - Rig service - Drill 7-7/8" hole with water from 5123' to 5900' with 15,000# WOB, 150 TRPM 400 GPMS 62.16 TROP

Daily Cost: \$0**Cumulative Cost:** \$207,825**UTE TRIBAL 1-27-4-3****Lay Down Drill Pipe/BHA****Date:** 12/25/2010

Aztec #184 at 6865. 4 Days Since Spud - Hold safety meeting with rig crew, RNI and rig crew - Circulate and rig up BJ hard lines. - Wait on elevators - Test 5 1/2" pipe rams to 2000 psi. - Run GR/DSN/SDL/DLL/MSFL suite. From TD to 4385' 30'/min. 4385' to surface at 60'/min - R/U Halliburton Wireline. Tool failur at surface. Change out the density tool. - Finish pipe lay down - Continue to lay down pipe. - Pump 200 bbls of 10# brine. Check flow no flow. - Lay down pipe to 3505'. Check flow. Well flowing at 30 gal/min. Pump 200 bbls of 10# brine. Check - Circulate - Drill 7-7/8" hole with water from 5900' to 6865' with 15,000# WOB, 150 TRPM 400 GPMS 56 TROP - Hold safety meeting with rig crew, RNI and rig crew - Circulate and rig up BJ hard lines. - R/U and run 161 jts 5 1/2" 15.50# casing set at 6860'. - Wait on elevators - Test 5 1/2" pipe rams to 2000 psi. - Run GR/DSN/SDL/DLL/MSFL suite. From TD to 4385' 30'/min. 4385' to surface at 60'/min - R/U Halliburton Wireline. Tool failur at surface. Change out the density tool. - Finish pipe lay down - Continue to lay down pipe. - Pump 200 bbls of 10# brine. Check flow no flow. - Lay down pipe to 3505'. Check flow. Well flowing at 30 gal/min. Pump 200 bbls of 10# brine. Check - Circulate - Drill 7-7/8" hole with water from 5900' to 6865' with 15,000# WOB, 150 TRPM 400 GPMS 56 TROP - R/U and run 161 jts 5 1/2" 15.50# casing set at 6860'.

Daily Cost: \$0**Cumulative Cost:** \$243,873**UTE TRIBAL 1-27-4-3****Wait on Completion****Date:** 12/27/2010

Aztec #184 at 6840. 6 Days Since Spud - Clean mud tanks - Nipple down, Hang BOP, set slips W/ 90,000 tension - W/1.24YLD Returned 40bbls to Pit - 425SKS 50:50:2+3%KCL+.5%EC-1+.25#CF+.05#SF+.3SMS+FP-6L Mixed @14.4PPG - Pump 300sks PL11+3% KCL+5#CSE+.5CF+.5SMS+FP+SF Mix @ 11ppg W/3.53YLD - Release Rig @ 3:00 PM 12-26-10 Greg Stutzman **Finalized**

Daily Cost: \$0**Cumulative Cost:** \$389,662**Pertinent Files: Go to File List**

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
14-20-H62-6154

1a. Type of Well Oil Well Gas Well Dry Other
b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Resvr.,
Other: _____

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

8. Lease Name and Well No.
UTE TRIBAL 1-27-4-3

3. Address
1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
(435)646-3721

9. AFI Well No.
43-013-50331

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

10. Field and Pool or Exploratory
MYTON-TRIBAL EDA

At surface 515' FNL & 728' FEL (NE/NE) SEC. 27, T4S, R3W

11. Sec., T., R., M., on Block and Survey or Area
SEC. 27, T4S, R3W

At top prod. interval reported below

12. County or Parish
DUCHESNE

13. State
UT

At total depth 6865'

14. Date Spudded
11/23/2010

15. Date T.D. Reached
12/26/2010

16. Date Completed 01/18/2011
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5623' GL 5635' KB

18. Total Depth: MD 6865'
TVD

19. Plug Back T.D.: MD 6803'
TVD

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sks. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	314'		160 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	6849'		300 PRIMLITE		180'	
						425 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 6298'	TA @ 6201'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Green River	4824'	6220'	4824-6220'	.36"	90	
B)						
C)						
D)						

26. Perforation Record

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
4824-6220'	Frac w/ 116874#'s 20/40 sand in 840 bbls of Lightning 17 fluid in 4 stages

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
01/18/11	01/27/11	24	→	269	110	98			2-1/2" x 1-1/2" x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

*(See instructions and spaces for additional data on page 2)

RECEIVED

FEB 03 2011

DIV. OF OIL, GAS & MINING

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD & USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
GREEN RIVER	4824'	6220'		GARDEN GULCH MRK	3982'
				GARDEN GULCH 1	4227'
				GARDEN GULCH 2	4355'
				POINT 3	4648'
				X MRKR	4909'
				Y MRKR	4940'
DOUGALS CREEK MRK				BI CARBONATE MRK	5057'
					5331'
B LIMESTON MRK				CASTLE PEAK	5474'
					6003'
BASAL CARBONATE				WASATCH	6418'
					6553'

32. Additional remarks (include plugging procedure):


33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Lucy Chavez-Naupoto

Title Administrative Assistant

Signature 

Date 01/31/2011

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Daily Activity Report**Format For Sundry****UTE TRIBAL 1-27-4-3****10/1/2010 To 2/28/2011****UTE TRIBAL 1-27-4-3****Waiting on Cement****Date:** 12/2/2010

Ross #21 at 310. Days Since Spud - @ 313.81'KB. On 12/1/10 cemented w/BJ 160sks of Class G+2% Calcium Chloride. 4BBLS returned to - Pit. Cement Mixed @ 15.8ppg W/1.17 yeild. - On 11/23/10 Ross # 21 spud @ 8:00am. Drilled 310' of 12.25" hole. Then ran 7jts of 8 5/8" casing set

Daily Cost: \$0**Cumulative Cost:** \$47,885**UTE TRIBAL 1-27-4-3****Rigging Up****Date:** 12/20/2010

Aztec #184 at 310. 0 Days Since Spud - of BOP test on 12/19/2010 at 6:00 PM. All notifacations made by email. - Contact BLM and state on 12/18/2010 of rig move on 12/19/2010 at 7:00 AM. Also notify 12/18/2010 - Safety meeting held w/ Jones trucking, myself and rig crew of proper body placement while picking eq - Hook up flow line and finish rigging up. - Hook up pumps and nipple up BOP and choke manifold. - Move rig and set all equipment with Jones Trucking. (.75 mile rig move from the UT 13-22-4-3w) - Then test the surface casing at 1500 psi for 30 minutes. Tested ok. - kill line, choke line and manifold. Ten min at 2000 psi. all tests ok. - Accept rig and test the upper kelly valve, safety valve, pipe rams and out side valve. Blind ram,

Daily Cost: \$0**Cumulative Cost:** \$96,374**UTE TRIBAL 1-27-4-3****Drill 7 7/8" hole with fresh water****Date:** 12/21/2010

Aztec #184 at 1194. 0 Days Since Spud - Rig up flow line, move BHA over to pipe racks and strap. - Drill 7-7/8" hole with water from 271' to 1194' with 15,000# WOB, 150 TRPM 400 GPMS 51.3 TROP - P/U BHA and directional tools. Scribe directional tool and mud motor

Daily Cost: \$0**Cumulative Cost:** \$114,374**UTE TRIBAL 1-27-4-3****Drill 7 7/8" hole with fresh water****Date:** 12/22/2010

Aztec #184 at 2600. 1 Days Since Spud - Drill 7-7/8" hole with water from 2255' to 2600' with 15,000# WOB, 150 TRPM 400 GPMS 69 TROP - Rig service. Function test BOP and crown-o-matic - Drill 7-7/8" hole with water from 1194' to 1844' with 15,000# WOB, 150 TRPM 400 GPMS 72.2 TROP - Work on brakes - Drill 7-7/8" hole with water from 1844' to 2255' with 15,000# WOB, 150 TRPM 400 GPMS 58 TROP - Rig repair. Change out Hydraulic hose on unit.

Daily Cost: \$0**Cumulative Cost:** \$133,075**UTE TRIBAL 1-27-4-3****Drill 7 7/8" hole with fresh water****Date:** 12/23/2010

Aztec #184 at 4375. 2 Days Since Spud - Rig service. Function test BOP and crown-o-matic - Drill 7-7/8" hole with water from 3420' to 4375' with 15,000# WOB, 150 TRPM 400 GPMS 79.6 TROP - Drill 7-7/8" hole with water from 2600' to 3420' with 15,000# WOB, 150 TRPM

400 GPMS 71.3 TROP

Daily Cost: \$0**Cumulative Cost:** \$175,670**UTE TRIBAL 1-27-4-3****Drill 7 7/8" hole with fresh water****Date:** 12/24/2010

Aztec #184 at 5900. 3 Days Since Spud - Drill 7-7/8" hole with water from 4372' to 5123' with 15,000# WOB, 150 TRPM 400 GPMS 68.3 TROP - Rig service - Drill 7-7/8" hole with water from 5123' to 5900' with 15,000# WOB, 150 TRPM 400 GPMS 62.16 TROP

Daily Cost: \$0**Cumulative Cost:** \$207,825**UTE TRIBAL 1-27-4-3****Lay Down Drill Pipe/BHA****Date:** 12/25/2010

Aztec #184 at 6865. 4 Days Since Spud - Hold safety meeting with rig crew, RNI and rig crew - Circulate and rig up BJ hard lines. - Wait on elevators - Test 5 1/2" pipe rams to 2000 psi. - Run GR/DSN/SDL/DLL/MSFL suite. From TD to 4385' 30'/min. 4385' to surface at 60'/min - R/U Halliburton Wireline. Tool failur at surface. Change out the density tool. - Finish pipe lay down - Continue to lay down pipe. - Pump 200 bbls of 10# brine. Check flow no flow. - Lay down pipe to 3505'. Check flow. Well flowing at 30 gal/min. Pump 200 bbls of 10# brine. Check - Circulate - Drill 7-7/8" hole with water from 5900' to 6865' with 15,000# WOB, 150 TRPM 400 GPMS 56 TROP - Hold safety meeting with rig crew, RNI and rig crew - Circulate and rig up BJ hard lines. - R/U and run 161 jts 5 1/2" 15.50# casing set at 6860'. - Wait on elevators - Test 5 1/2" pipe rams to 2000 psi. - Run GR/DSN/SDL/DLL/MSFL suite. From TD to 4385' 30'/min. 4385' to surface at 60'/min - R/U Halliburton Wireline. Tool failur at surface. Change out the density tool. - Finish pipe lay down - Continue to lay down pipe. - Pump 200 bbls of 10# brine. Check flow no flow. - Lay down pipe to 3505'. Check flow. Well flowing at 30 gal/min. Pump 200 bbls of 10# brine. Check - Circulate - Drill 7-7/8" hole with water from 5900' to 6865' with 15,000# WOB, 150 TRPM 400 GPMS 56 TROP - R/U and run 161 jts 5 1/2" 15.50# casing set at 6860'.

Daily Cost: \$0**Cumulative Cost:** \$243,873**UTE TRIBAL 1-27-4-3****Wait on Completion****Date:** 12/27/2010

Aztec #184 at 6840. 6 Days Since Spud - Clean mud tanks - Nipple down, Hang BOP, set slips W/ 90,000 tension - W/1.24YLD Returned 40bbls to Pit - 425SKS 50:50:2+3%KCL+.5%EC-1+.25#CF+.05#SF+.3SMS+FP-6L Mixed @14.4PPG - Pump 300sks PL11+3% KCL+5#CSE+.5CF+.5SMS+FP+SF Mix @ 11ppg W/3.53YLD - Release Rig @ 3:00 PM 12-26-10 Greg Stutzman **Finalized**

Daily Cost: \$0**Cumulative Cost:** \$389,662**Pertinent Files: Go to File List**
