

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3
AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL						1. WELL NAME and NUMBER Greater Monument Butte R-6-9-17		
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT MONUMENT BUTTE		
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO						5. UNIT or COMMUNITIZATION AGREEMENT NAME GMBU (GRRV)		
6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY						7. OPERATOR PHONE 435 646-4825		
8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052						9. OPERATOR E-MAIL mcrozier@newfield.com		
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU-020252A			11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>		
13. NAME OF SURFACE OWNER (if box 12 = 'fee')						14. SURFACE OWNER PHONE (if box 12 = 'fee')		
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')		
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>			19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/>		
20. LOCATION OF WELL		FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN
LOCATION AT SURFACE		1108 FSL 2123 FWL		SESW	6	9.0 S	17.0 E	S
Top of Uppermost Producing Zone		1583 FSL 2576 FWL		NESW	6	9.0 S	17.0 E	S
At Total Depth		1775 FSL 2379 FEL		NWSE	6	9.0 S	17.0 E	S
21. COUNTY DUCHESNE			22. DISTANCE TO NEAREST LEASE LINE (Feet) 1775			23. NUMBER OF ACRES IN DRILLING UNIT 20		
			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 725			26. PROPOSED DEPTH MD: 6183 TVD: 6183		
27. ELEVATION - GROUND LEVEL 5306			28. BOND NUMBER WYB000493			29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 437478		
ATTACHMENTS								
VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES								
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER				<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN				
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)				<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER				
<input checked="" type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)				<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP				
NAME Mandie Crozier			TITLE Regulatory Tech			PHONE 435 646-4825		
SIGNATURE			DATE 01/11/2011			EMAIL mcrozier@newfield.com		
API NUMBER ASSIGNED 43013505810000			APPROVAL			 Permit Manager		

Proposed Hole, Casing, and Cement						
String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Prod	7.875	5.5	0	6183		
Pipe	Grade	Length	Weight			
	Grade J-55 LT&C	6183	15.5			

Proposed Hole, Casing, and Cement						
String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Surf	12.25	8.625	0	300		
Pipe	Grade	Length	Weight			
	Grade J-55 ST&C	300	24.0			

NEWFIELD PRODUCTION COMPANY
GREATER MONUMENT BUTTE R-6-9-17
AT SURFACE: SE/SW SECTION 6, T9S, R17E
DUCHESNE COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0' – 1425'
Green River	1425'
Wasatch	6050'
Proposed TD	6183'

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil) 1425' – 6050'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sampled Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO ₃) (mg/l)
Dissolved Bicarbonate (NaHCO ₃) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO ₄) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: Greater Monument Butte R-6-9-17**

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950 17.53	1,370 14.35	244,000 33.89
Prod casing 5-1/2"	0'	6,183'	15.5	J-55	LTC	4,810 2.45	4,040 2.05	217,000 2.26

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg
 Pore pressure at surface casing shoe = 8.33 ppg
 Pore pressure at prod casing shoe = 8.33 ppg
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: Greater Monument Butte R-6-9-17**

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft ³ /sk)
			ft ³			
Surface casing	300'	Class G w/ 2% CaCl	138	30%	15.8	1.17
			161			
Prod casing Lead	4,183'	Prem Lite II w/ 10% gel + 3% KCl	289	30%	11.0	3.26
			942			
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363	30%	14.3	1.24
			451			

- *Actual volume pumped will be 15% over the caliper log
- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ±350 feet will be drilled with an air/mist system. The air rig is equipped with a 6 ½" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ±350 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.

10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**



It is anticipated that the drilling operations will commence the second quarter of 2011, and take approximately seven (7) days from spud to rig release.

T9S, R17E, S.L.B.&M.

NEWFIELD EXPLORATION COMPANY

WELL LOCATION, R-6-9-17, LOCATED AS SHOWN IN THE SE 1/4 SW 1/4 OF SECTION 6, T9S, R7E, S.L.B.&M. DUCHESNE COUNTY, UTAH.


TARGET BOTTOM HOLE, R-6-9-17, LOCATED AS SHOWN IN THE NW 1/4 SE 1/4 OF SECTION 6, T9S, R7E, S.L.B.&M. DUCHESNE COUNTY, UTAH.

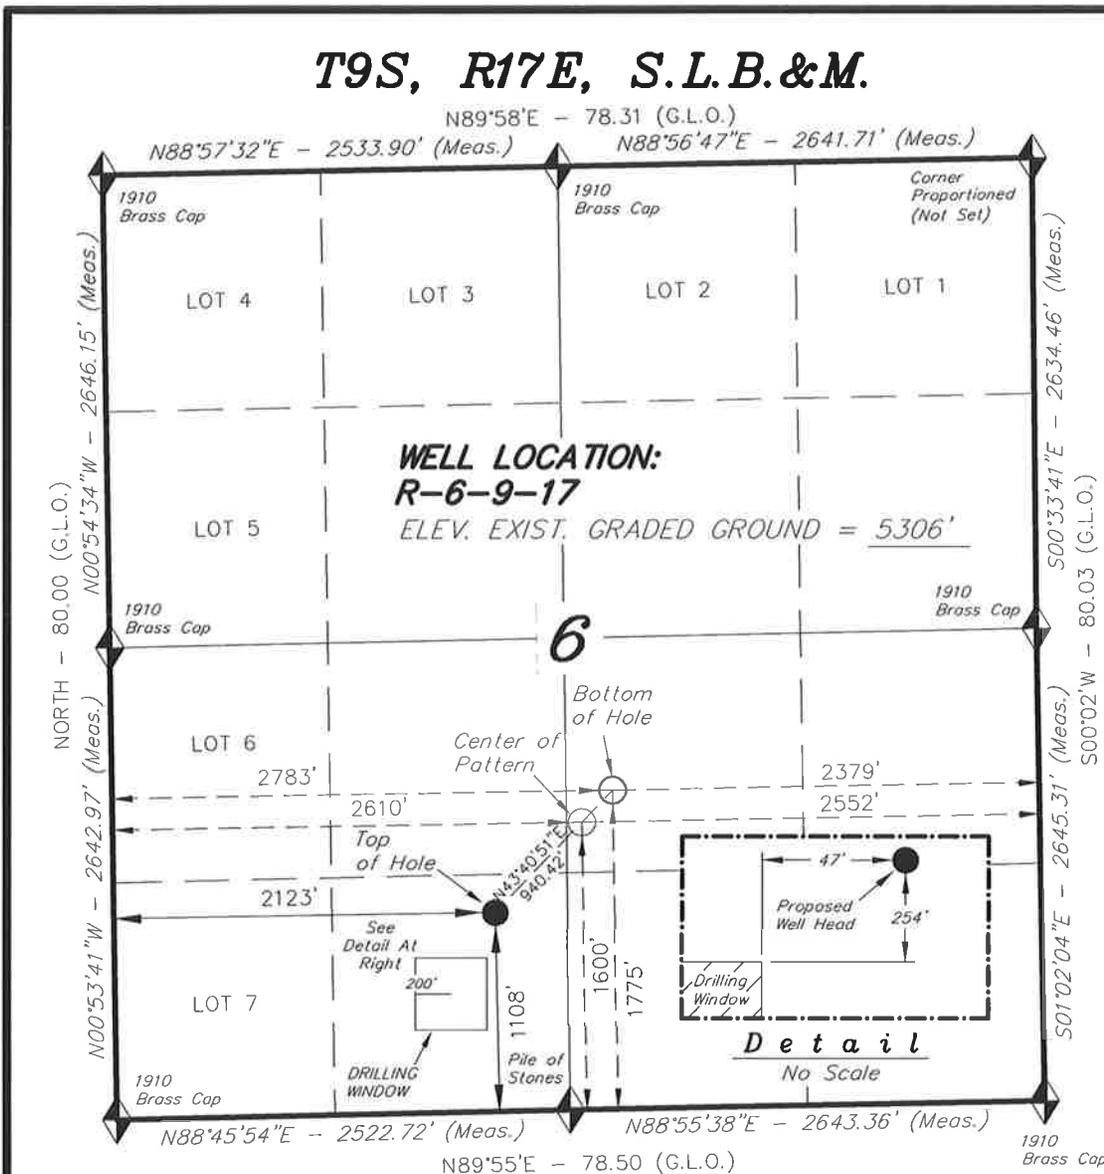

NOTES:

1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.

THIS IS TO CERTIFY THAT THE ABOVE PLAN WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are base on LOCATION: on N.G.S. OPUS Correction. LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'


R-6-9-17
(Surface Location) NAD 83
LATITUDE = 40° 03' 20.39"
LONGITUDE = 110° 03' 02.76"

TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

DATE SURVEYED: 08-09-10	SURVEYED BY: D.G.
DATE DRAWN: 11-12-10	DRAWN BY: M.W.
REVISED:	SCALE: 1" = 1000'

Access Road Map

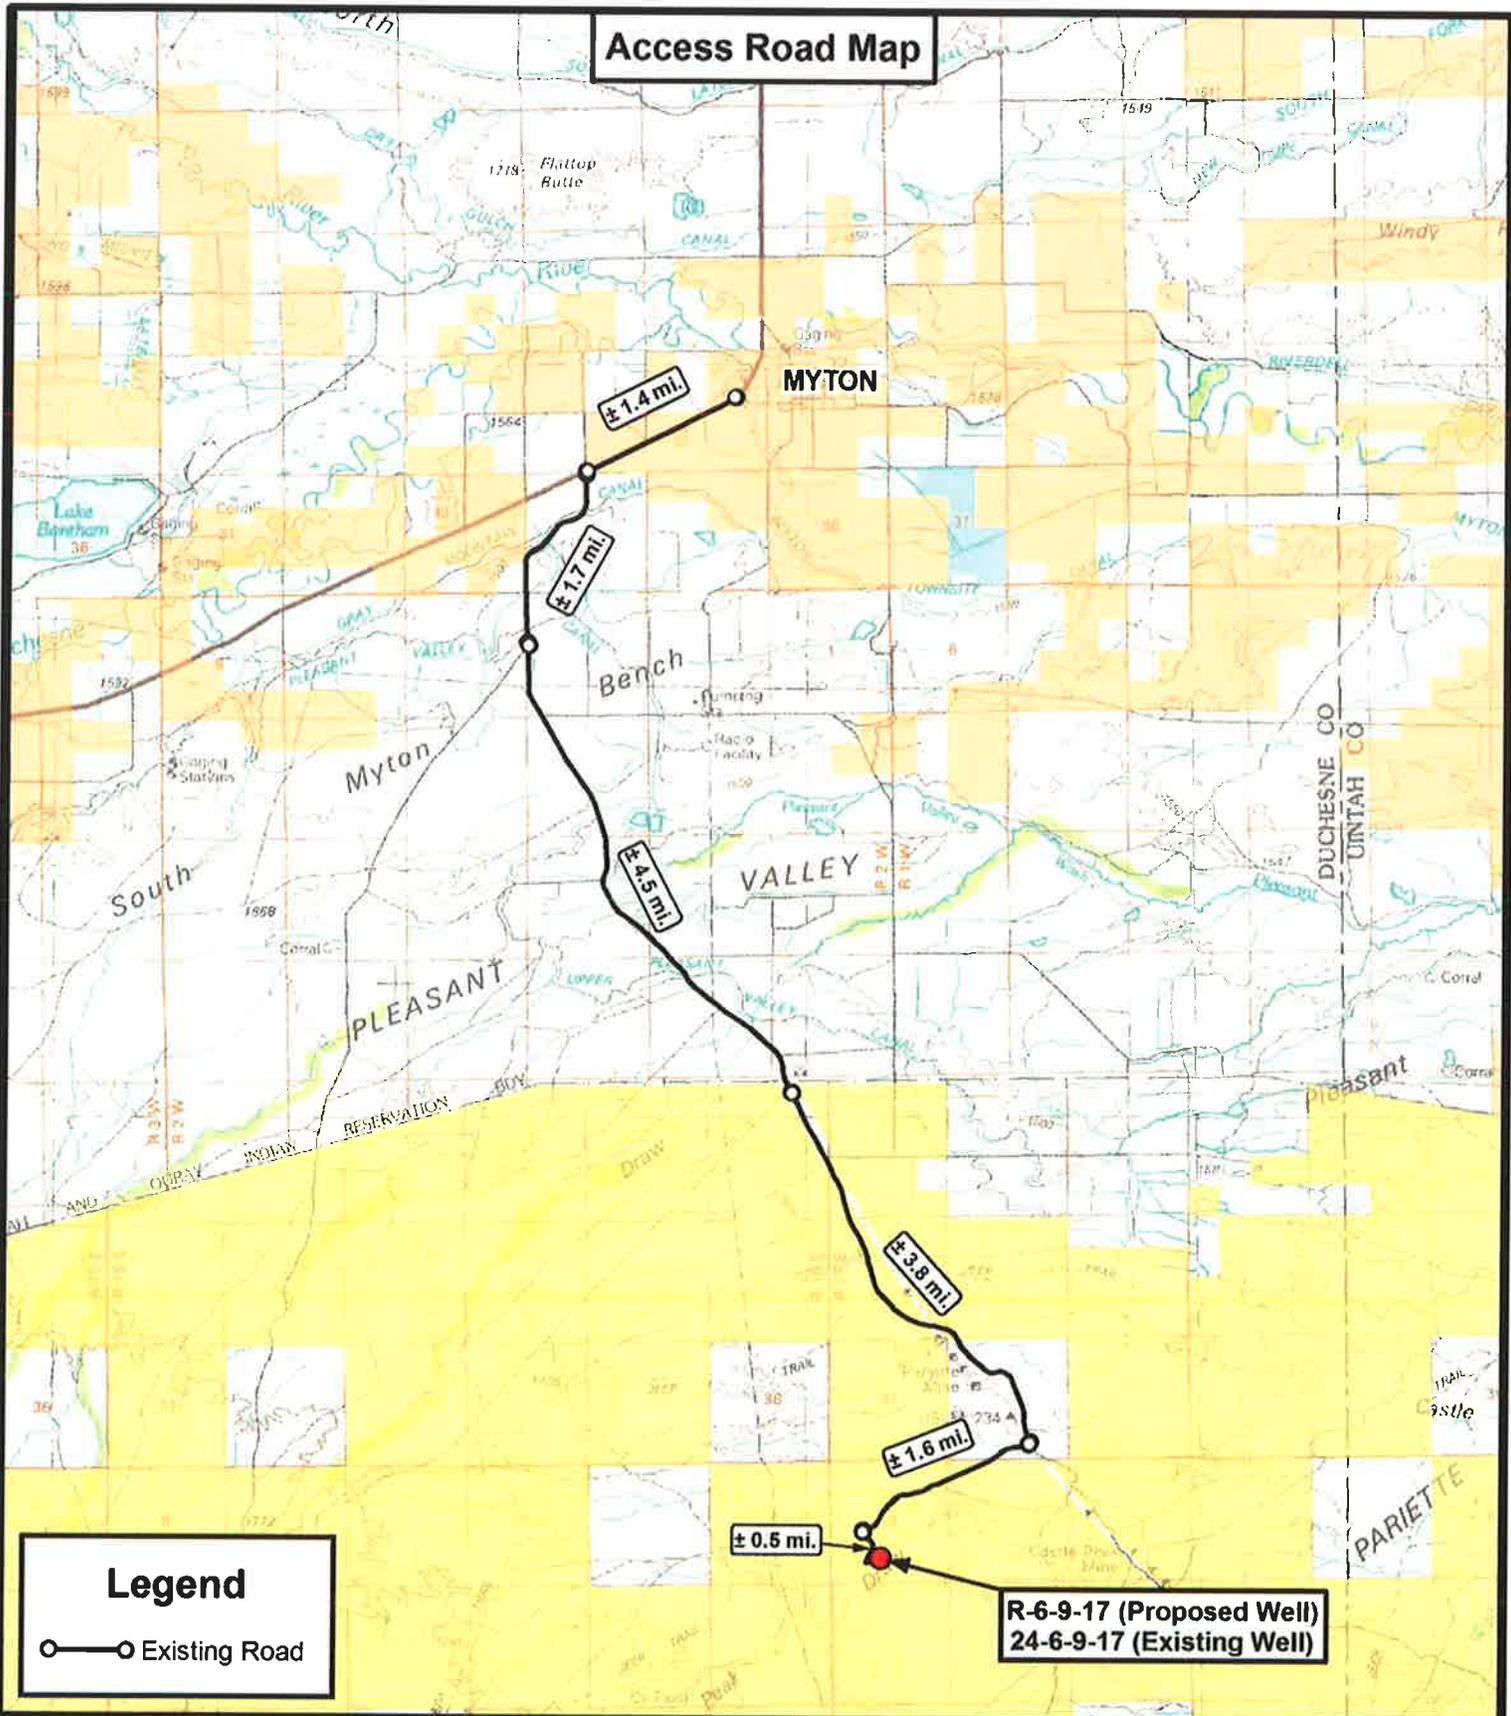

Legend

○—○ Existing Road

R-6-9-17 (Proposed Well)
24-6-9-17 (Existing Well)

Tri State
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY


R-6-9-17 (Proposed Well)
24-6-9-17 (Existing Well)
SEC. 6, T9S, R17E, S.L.B.&M.
Duchesne County, UT.

DRAWN BY: C.H.M.
DATE: 09-20-2010
SCALE: 1:100,000

TOPOGRAPHIC MAP

SHEET
A

Access Road Map

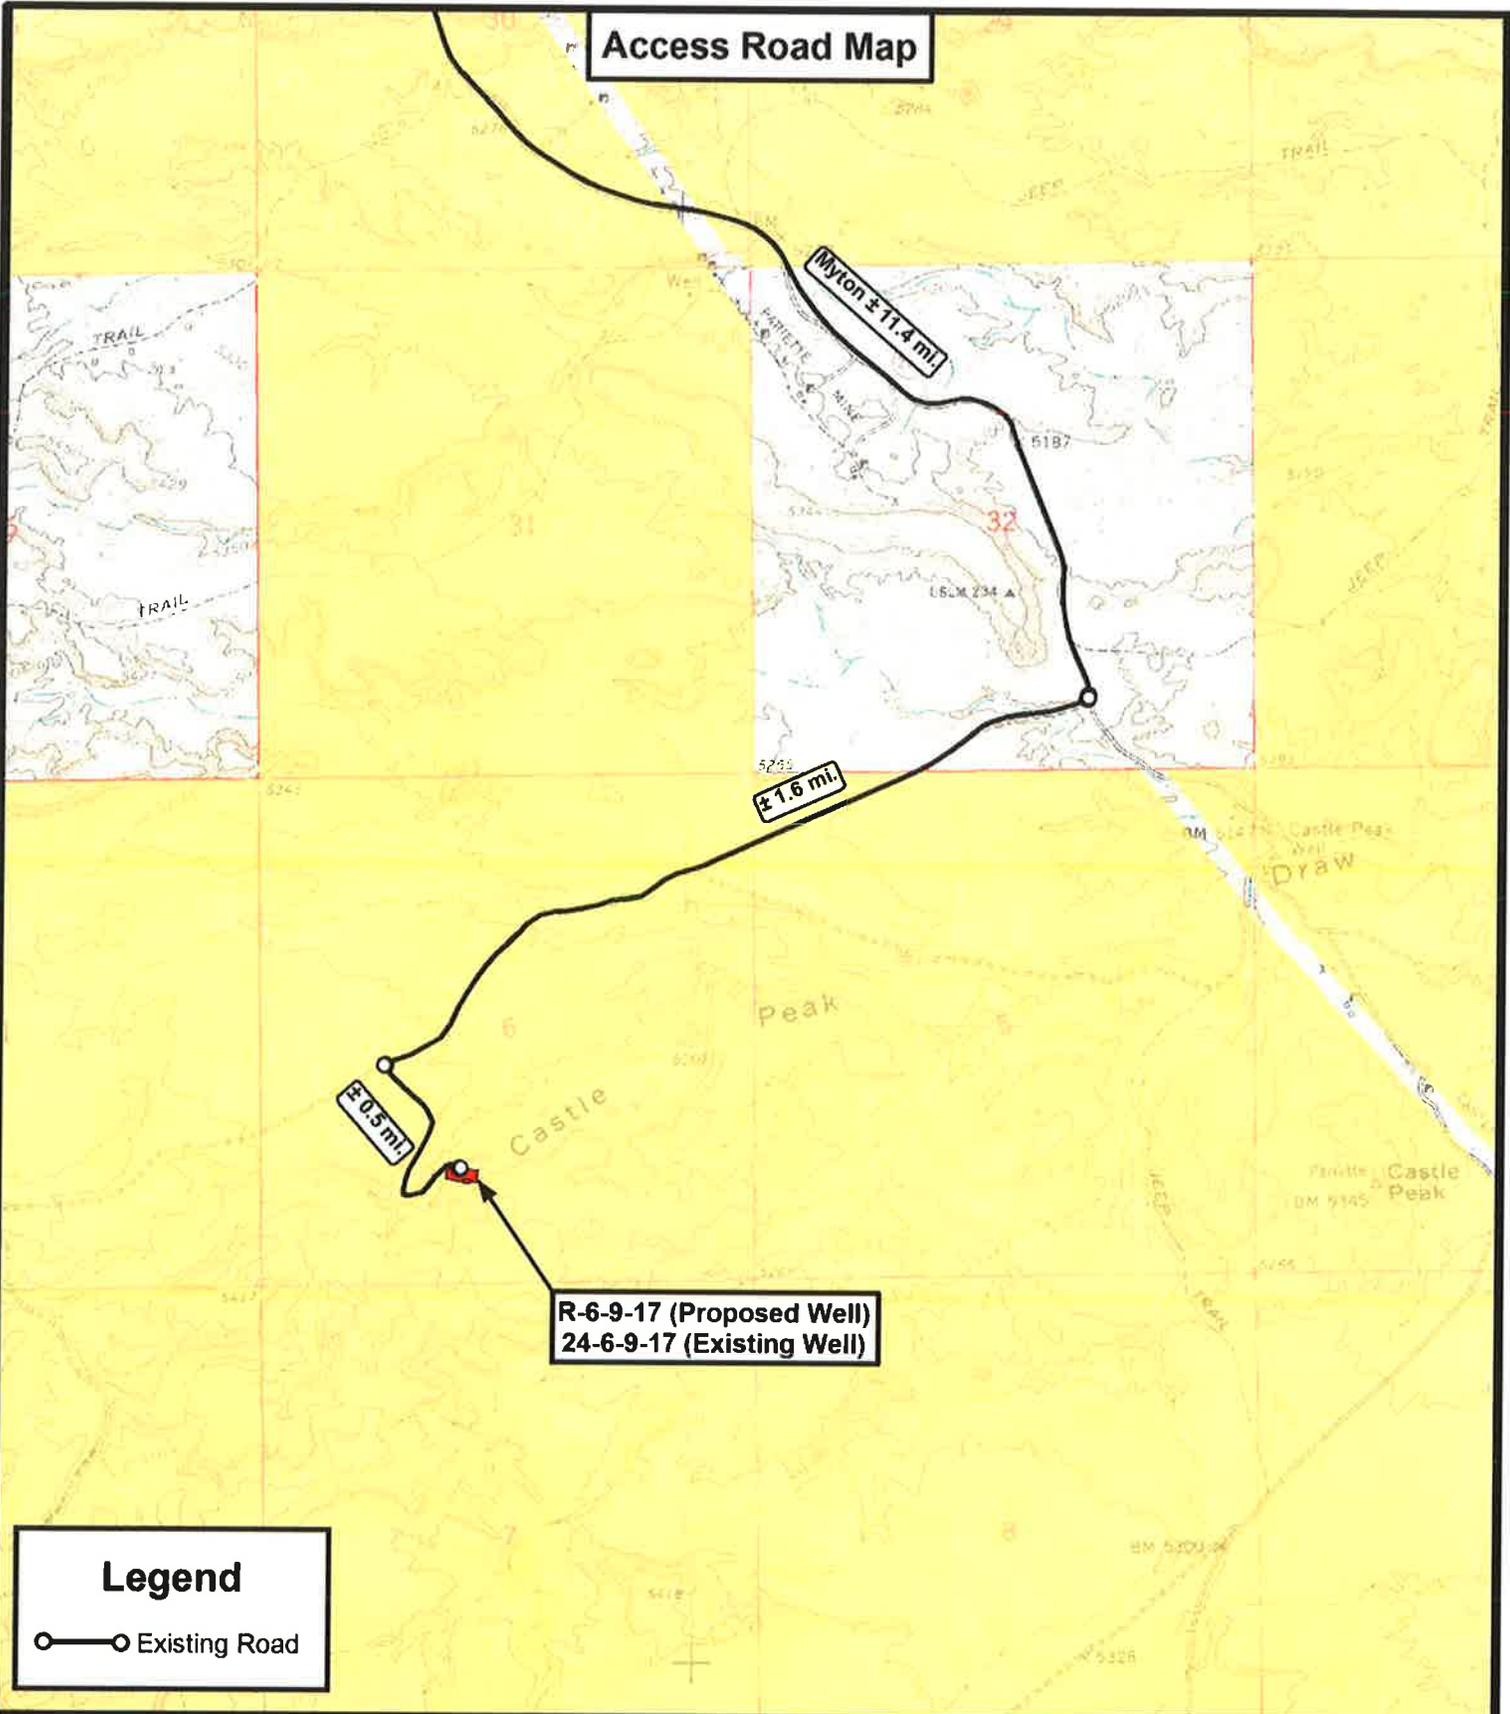

Legend

○—○ Existing Road

Tri State
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY


R-6-9-17 (Proposed Well)
 24-6-9-17 (Existing Well)
 SEC. 6, T9S, R17E, S.L.B.&M.
 Duchesne County, UT.

DRAWN BY:	C.H.M.
DATE:	09-20-2010
SCALE:	1" = 2,000'

TOPOGRAPHIC MAP

SHEET
B

Proposed Pipeline Map

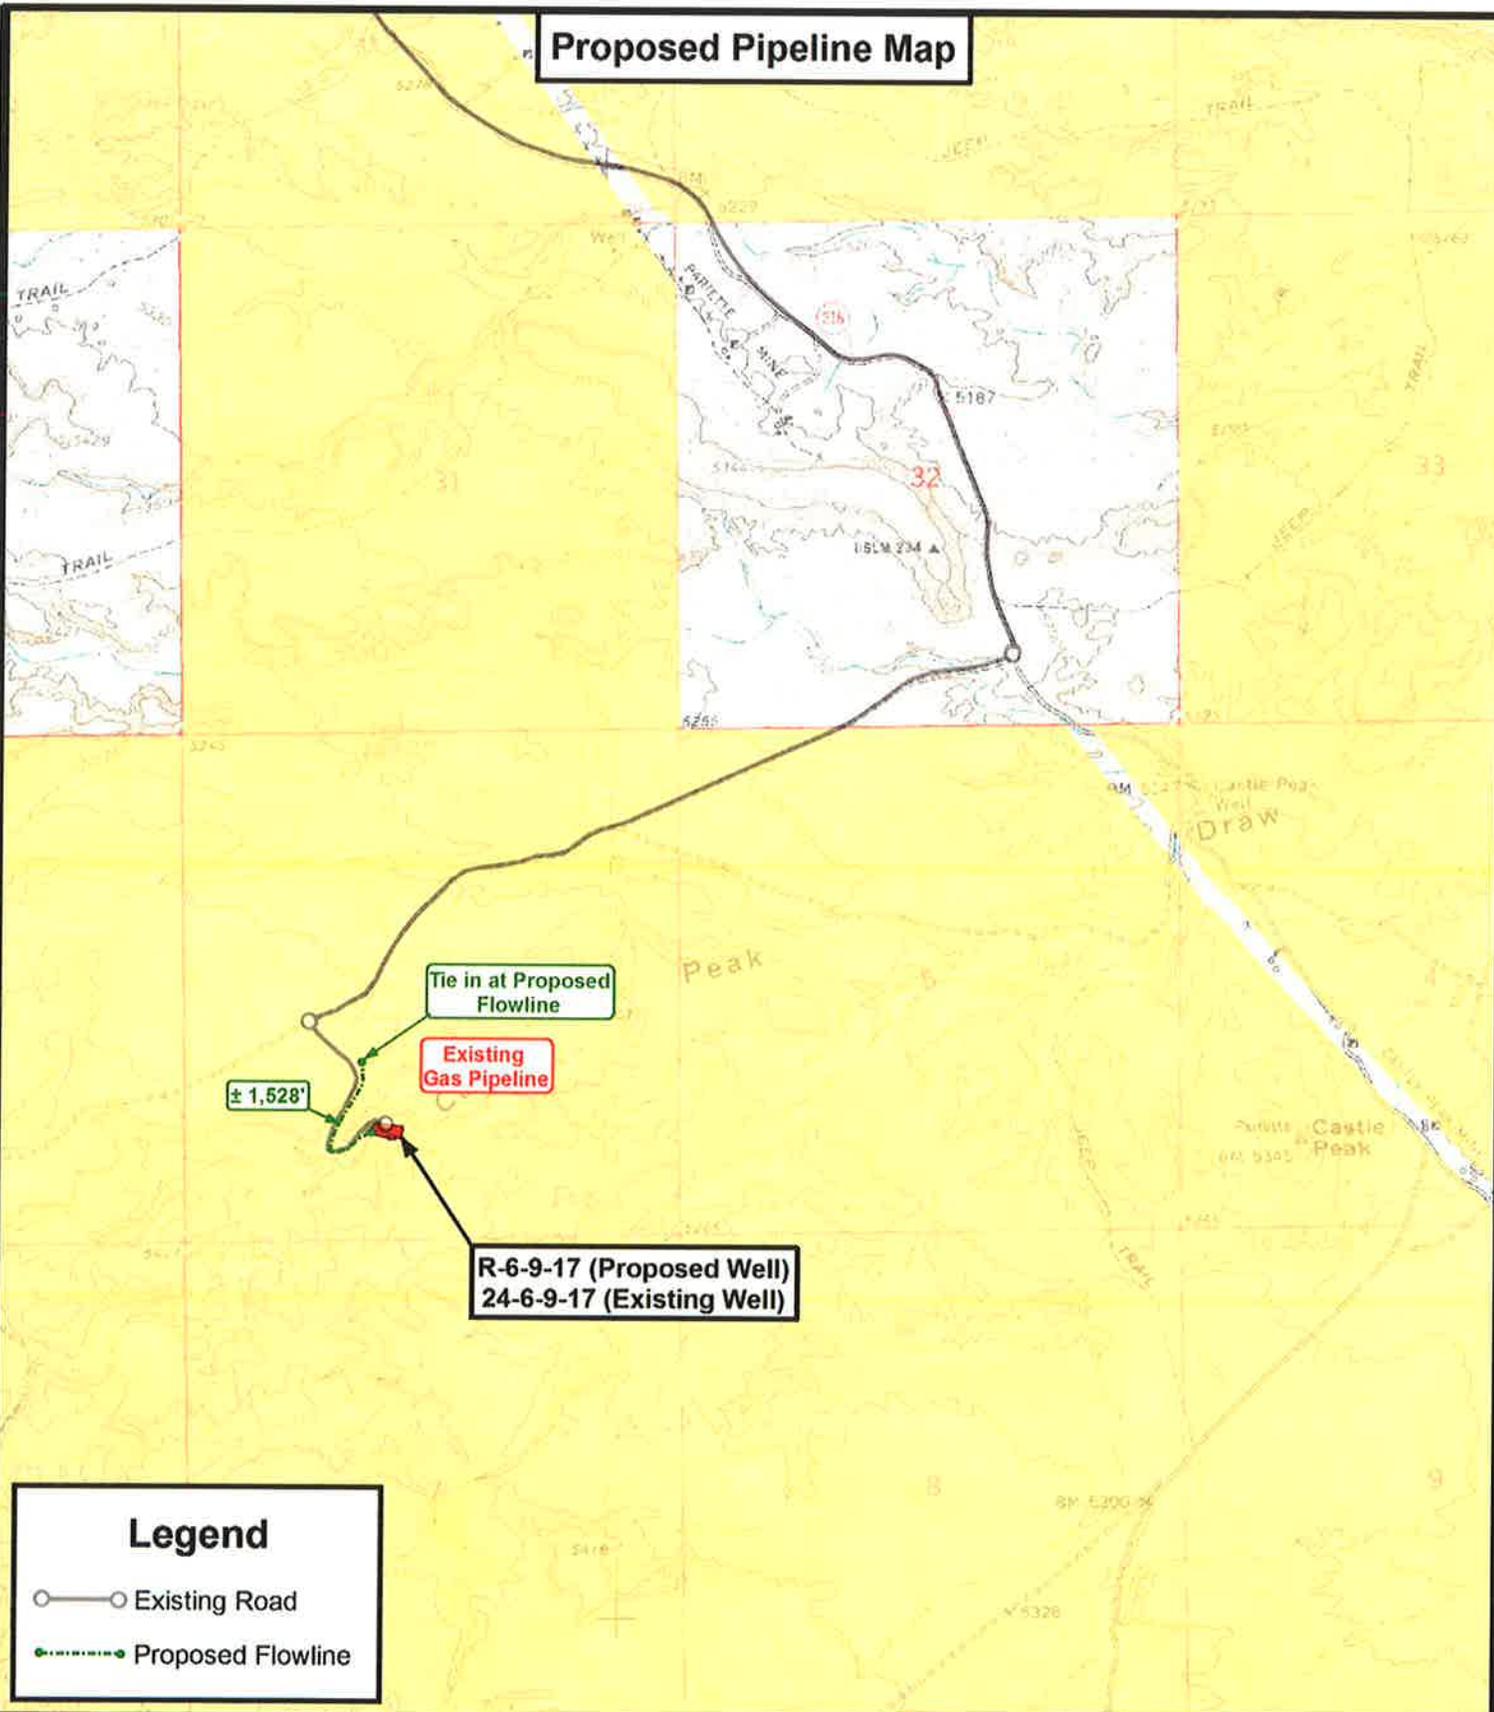

Legend

- Existing Road
- Proposed Flowline

Tri State Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

R-6-9-17 (Proposed Well)
 24-6-9-17 (Existing Well)
 SEC. 6, T9S, R17E, S.L.B.&M.
 Duchesne County, UT.

DRAWN BY:	C.H.M
DATE:	09-20-2010
SCALE:	1" = 2,000'

TOPOGRAPHIC MAP

SHEET
C


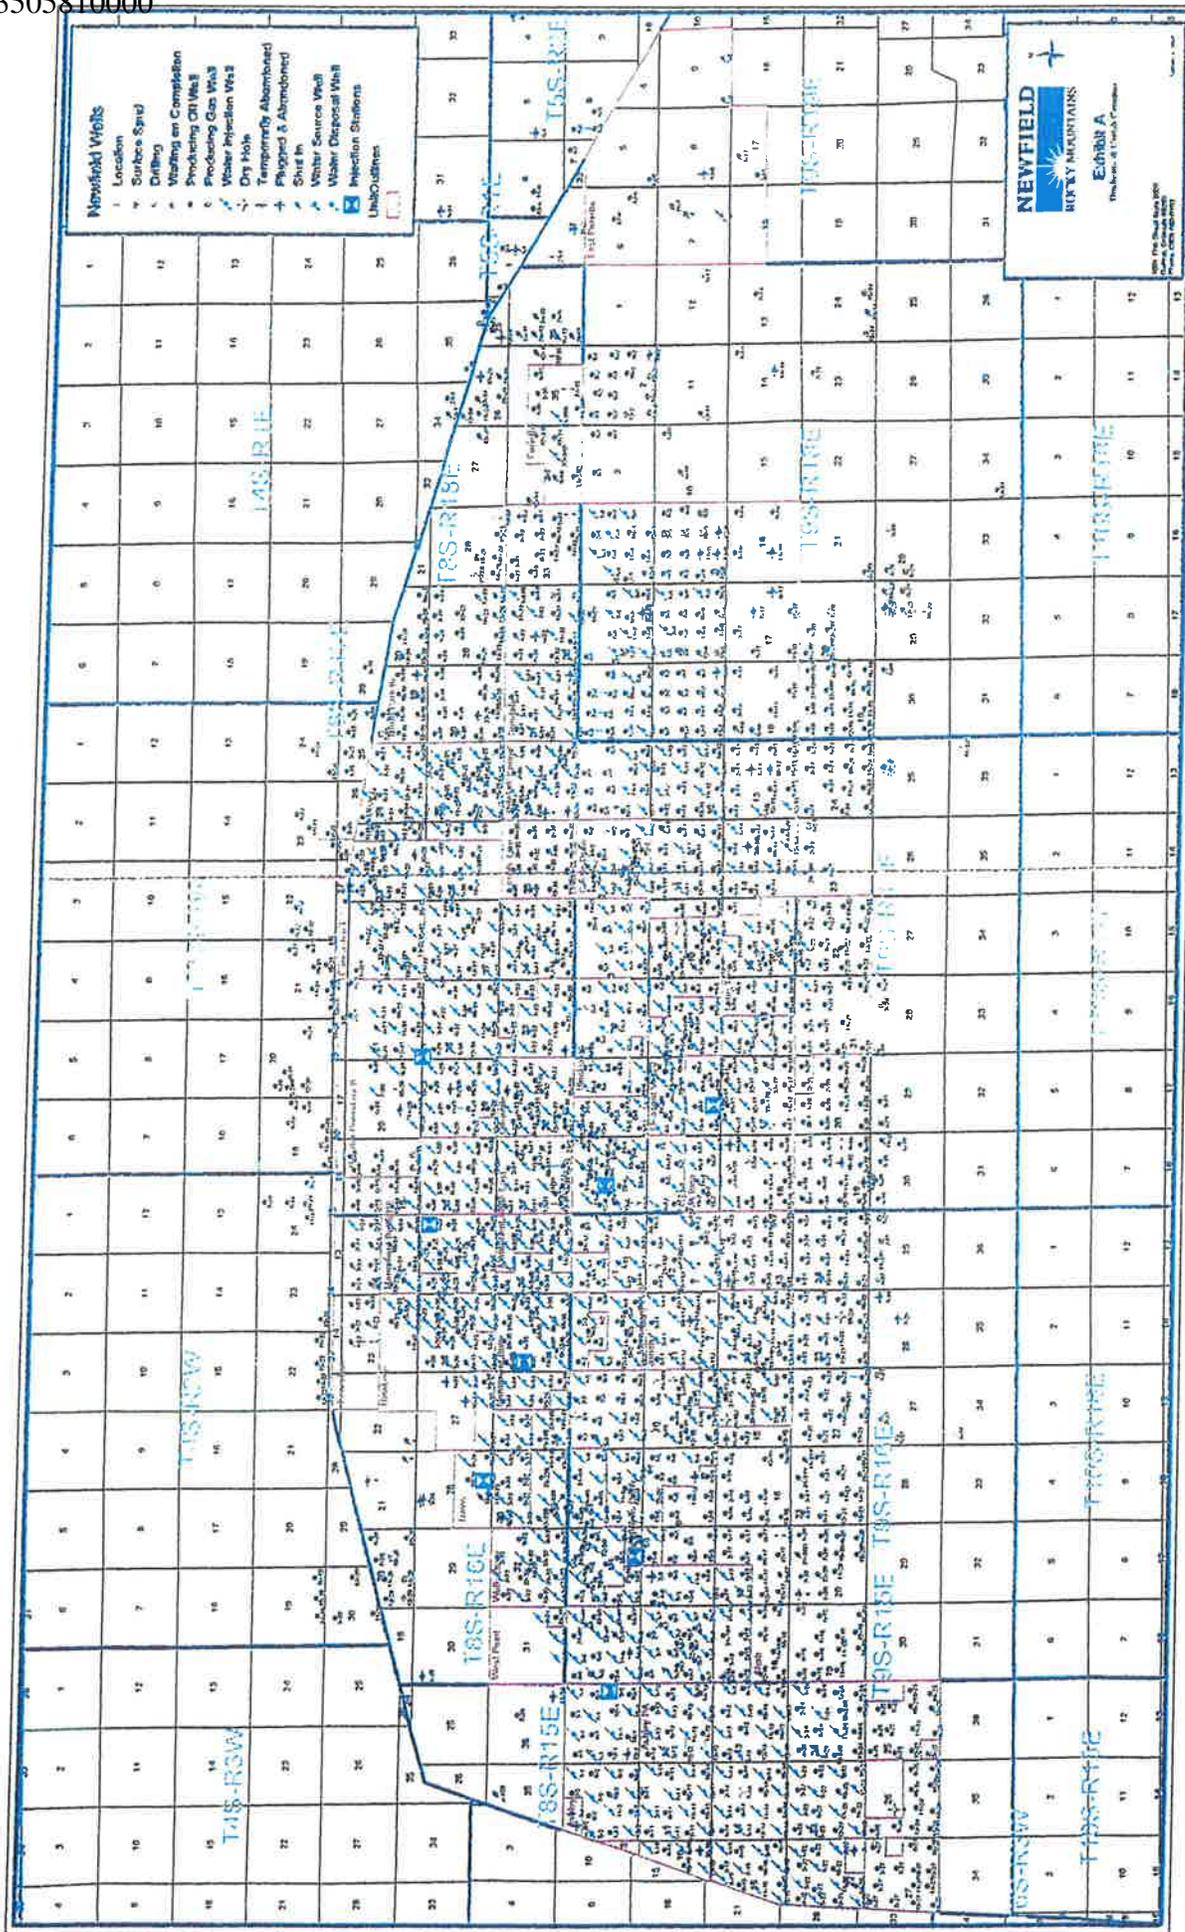


Exhibit "B" Map

R-6-9-17 (Proposed Well)
24-6-9-17 (Existing Well)

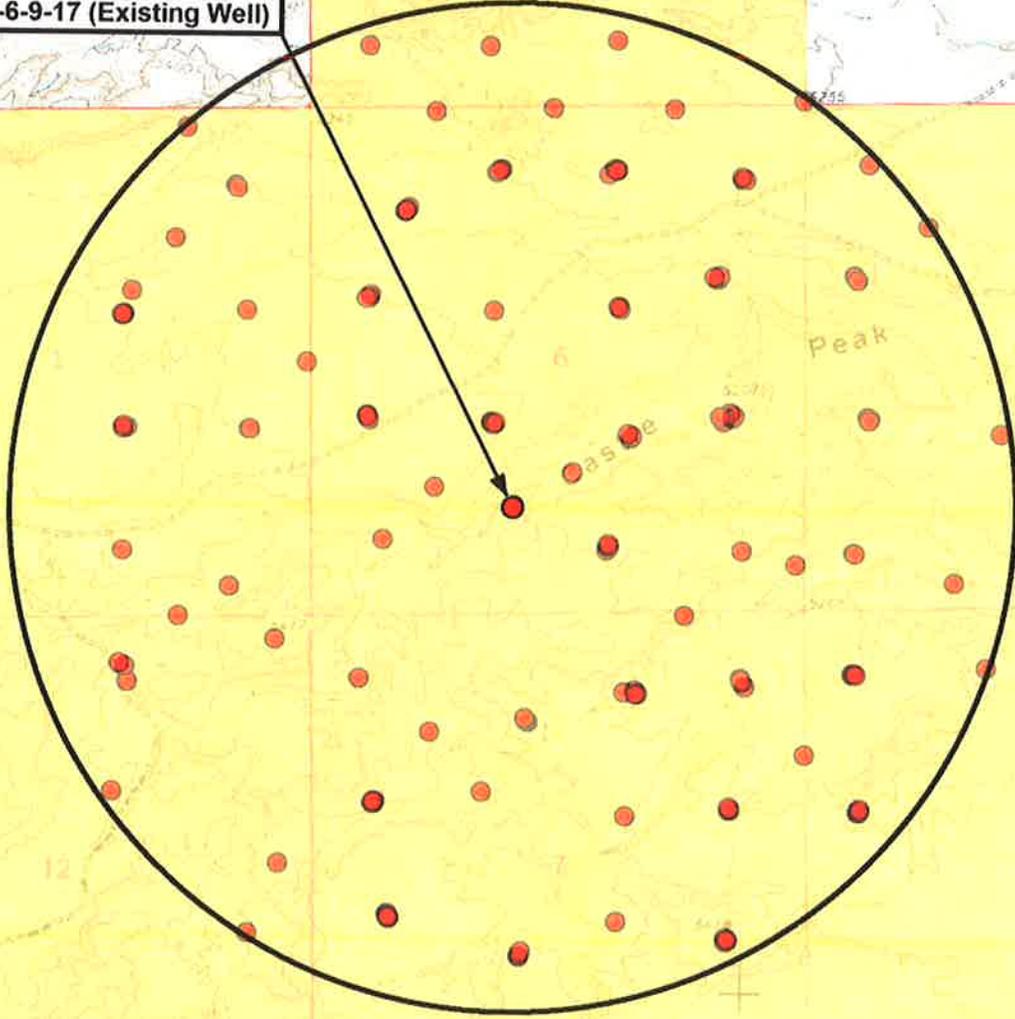

Legend

-  1 Mile Radius
-  Proposed Location

Tri State
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

R-6-9-17 (Proposed Well)
24-6-9-17 (Existing Well)
SEC. 6, T9S, R17E, S.L.B.&M.
Duchesne County, UT.

DRAWN BY:	C.H.M
DATE:	09-20-2010
SCALE:	1" = 2,000

TOPOGRAPHIC MAP

SHEET
D

NEWFIELD



NEWFIELD EXPLORATION

USGS Myton SW (UT)

SECTION 6 T9S, R17E

R-6-9-17

Wellbore #1

Plan: Design #1

Standard Planning Report

11 November, 2010



PayZone Directional Services, LLC.
 Planning Report



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well R-6-9-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	R-6-9-17 @ 5318.0ft (Original Well Elev)
Project:	USGS Myton SW (UT)	MD Reference:	R-6-9-17 @ 5318.0ft (Original Well Elev)
Site:	SECTION 6 T9S, R17E	North Reference:	True
Well:	R-6-9-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Project	USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Utah Central Zone		

Site	SECTION 6 T9S, R17E				
Site Position:		Northing:	7,195,000.00 ft	Latitude:	40° 3' 47.061 N
From:	Lat/Long	Easting:	2,047,000.00 ft	Longitude:	110° 2' 50.009 W
Position Uncertainty:	0.0 ft	Slot Radius:	"	Grid Convergence:	0.93 °

Well	R-6-9-17, SHL LAT: 40° 03' 20.39, LONG: -110° 03' 02.76					
Well Position	+N/-S	-2,698.6 ft	Northing:	7,192,285.67 ft	Latitude:	40° 3' 20.390 N
	+E/-W	-991.3 ft	Easting:	2,046,052.57 ft	Longitude:	110° 3' 2.760 W
Position Uncertainty		0.0 ft	Wellhead Elevation:	5,318.0 ft	Ground Level:	5,306.0 ft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010	2010/11/11	11.39	65.82	52,338

Design	Design #1				
Audit Notes:					
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0	
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)	
	0.0	0.0	0.0	43.68	

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.00	0.00	0.00	0.00	
1,289.4	10.34	43.68	1,285.6	44.9	42.8	1.50	1.50	0.00	43.68	
4,810.9	10.34	43.68	4,750.0	502.0	479.4	0.00	0.00	0.00	0.00	
6,183.2	10.34	43.68	6,100.0	680.1	649.5	0.00	0.00	0.00	0.00	



PayZone Directional Services, LLC.
 Planning Report



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well R-6-9-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	R-6-9-17 @ 5318.0ft (Original Well Elev)
Project:	USGS Myton SW (UT)	MD Reference:	R-6-9-17 @ 5318.0ft (Original Well Elev)
Site:	SECTION 6 T9S, R17E	North Reference:	True
Well:	R-6-9-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00	
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00	
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00	
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00	
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00	
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00	
700.0	1.50	43.68	700.0	0.9	0.9	1.3	1.50	1.50	0.00	
800.0	3.00	43.68	799.9	3.8	3.6	5.2	1.50	1.50	0.00	
900.0	4.50	43.68	899.7	8.5	8.1	11.8	1.50	1.50	0.00	
1,000.0	6.00	43.68	999.3	15.1	14.5	20.9	1.50	1.50	0.00	
1,100.0	7.50	43.68	1,098.6	23.6	22.6	32.7	1.50	1.50	0.00	
1,200.0	9.00	43.68	1,197.5	34.0	32.5	47.0	1.50	1.50	0.00	
1,289.4	10.34	43.68	1,285.6	44.9	42.8	62.0	1.50	1.50	0.00	
1,300.0	10.34	43.68	1,296.1	46.2	44.2	63.9	0.00	0.00	0.00	
1,400.0	10.34	43.68	1,394.5	59.2	56.6	81.9	0.00	0.00	0.00	
1,500.0	10.34	43.68	1,492.8	72.2	69.0	99.8	0.00	0.00	0.00	
1,600.0	10.34	43.68	1,591.2	85.2	81.4	117.8	0.00	0.00	0.00	
1,700.0	10.34	43.68	1,689.6	98.2	93.7	135.7	0.00	0.00	0.00	
1,800.0	10.34	43.68	1,788.0	111.2	106.1	153.7	0.00	0.00	0.00	
1,900.0	10.34	43.68	1,886.3	124.1	118.5	171.6	0.00	0.00	0.00	
2,000.0	10.34	43.68	1,984.7	137.1	130.9	189.6	0.00	0.00	0.00	
2,100.0	10.34	43.68	2,083.1	150.1	143.3	207.5	0.00	0.00	0.00	
2,200.0	10.34	43.68	2,181.5	163.1	155.7	225.5	0.00	0.00	0.00	
2,300.0	10.34	43.68	2,279.9	176.1	168.1	243.4	0.00	0.00	0.00	
2,400.0	10.34	43.68	2,378.2	189.0	180.5	261.4	0.00	0.00	0.00	
2,500.0	10.34	43.68	2,476.6	202.0	192.9	279.3	0.00	0.00	0.00	
2,600.0	10.34	43.68	2,575.0	215.0	205.3	297.3	0.00	0.00	0.00	
2,700.0	10.34	43.68	2,673.4	228.0	217.7	315.2	0.00	0.00	0.00	
2,800.0	10.34	43.68	2,771.7	241.0	230.1	333.2	0.00	0.00	0.00	
2,900.0	10.34	43.68	2,870.1	253.9	242.5	351.1	0.00	0.00	0.00	
3,000.0	10.34	43.68	2,968.5	266.9	254.9	369.1	0.00	0.00	0.00	
3,100.0	10.34	43.68	3,066.9	279.9	267.3	387.0	0.00	0.00	0.00	
3,200.0	10.34	43.68	3,165.2	292.9	279.7	405.0	0.00	0.00	0.00	
3,300.0	10.34	43.68	3,263.6	305.9	292.1	422.9	0.00	0.00	0.00	
3,400.0	10.34	43.68	3,362.0	318.9	304.5	440.9	0.00	0.00	0.00	
3,500.0	10.34	43.68	3,460.4	331.8	316.9	458.8	0.00	0.00	0.00	
3,600.0	10.34	43.68	3,558.7	344.8	329.3	476.8	0.00	0.00	0.00	
3,700.0	10.34	43.68	3,657.1	357.8	341.7	494.7	0.00	0.00	0.00	
3,800.0	10.34	43.68	3,755.5	370.8	354.1	512.7	0.00	0.00	0.00	
3,900.0	10.34	43.68	3,853.9	383.8	366.5	530.6	0.00	0.00	0.00	
4,000.0	10.34	43.68	3,952.2	396.7	378.9	548.6	0.00	0.00	0.00	
4,100.0	10.34	43.68	4,050.6	409.7	391.3	566.5	0.00	0.00	0.00	
4,200.0	10.34	43.68	4,149.0	422.7	403.7	584.5	0.00	0.00	0.00	
4,300.0	10.34	43.68	4,247.4	435.7	416.1	602.4	0.00	0.00	0.00	
4,400.0	10.34	43.68	4,345.7	448.7	428.5	620.4	0.00	0.00	0.00	
4,500.0	10.34	43.68	4,444.1	461.6	440.8	638.3	0.00	0.00	0.00	
4,600.0	10.34	43.68	4,542.5	474.6	453.2	656.3	0.00	0.00	0.00	
4,700.0	10.34	43.68	4,640.9	487.6	465.6	674.2	0.00	0.00	0.00	
4,800.0	10.34	43.68	4,739.2	500.6	478.0	692.2	0.00	0.00	0.00	
4,810.9	10.34	43.68	4,750.0	502.0	479.4	694.1	0.00	0.00	0.00	
R-6-9-17										
4,900.0	10.34	43.68	4,837.6	513.6	490.4	710.1	0.00	0.00	0.00	
5,000.0	10.34	43.68	4,936.0	526.6	502.8	728.1	0.00	0.00	0.00	



PayZone Directional Services, LLC.
 Planning Report



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well R-6-9-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	R-6-9-17 @ 5318.0ft (Original Well Elev)
Project:	USGS Myton SW (UT)	MD Reference:	R-6-9-17 @ 5318.0ft (Original Well Elev)
Site:	SECTION 6 T9S, R17E	North Reference:	True
Well:	R-6-9-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
5,100.0	10.34	43.68	5,034.4	539.5	515.2	746.0	0.00	0.00	0.00	
5,200.0	10.34	43.68	5,132.8	552.5	527.6	764.0	0.00	0.00	0.00	
5,300.0	10.34	43.68	5,231.1	565.5	540.0	781.9	0.00	0.00	0.00	
5,400.0	10.34	43.68	5,329.5	578.5	552.4	799.9	0.00	0.00	0.00	
5,500.0	10.34	43.68	5,427.9	591.5	564.8	817.8	0.00	0.00	0.00	
5,600.0	10.34	43.68	5,526.3	604.4	577.2	835.8	0.00	0.00	0.00	
5,700.0	10.34	43.68	5,624.6	617.4	589.6	853.7	0.00	0.00	0.00	
5,800.0	10.34	43.68	5,723.0	630.4	602.0	871.7	0.00	0.00	0.00	
5,900.0	10.34	43.68	5,821.4	643.4	614.4	889.6	0.00	0.00	0.00	
6,000.0	10.34	43.68	5,919.8	656.4	626.8	907.6	0.00	0.00	0.00	
6,100.0	10.34	43.68	6,018.1	669.3	639.2	925.5	0.00	0.00	0.00	
6,183.2	10.34	43.68	6,100.0	680.1	649.5	940.5	0.00	0.00	0.00	

Targets										
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (ft)	Easting (ft)	Latitude	Longitude	
R-6-9-17 - hit/miss target - Shape	0.00	0.00	4,750.0	502.0	479.4	7,192,795.38	2,046,523.77	40° 3' 25.351 N	110° 2' 56.594 W	
- plan hits target										
- Circle (radius 75.0)										





Project: USGS Myton SW (UT)
 Site: SECTION 6 T9S, R17E
 Well: R-6-9-17
 Wellbore: Wellbore #1
 Design: Design #1



Azimuths to True North
 Magnetic North: 11.39°

Magnetic Field
 Strength: 52338.0snT
 Dip Angle: 65.82°
 Date: 2010/11/11
 Model: IGRF2010

KOP @ 600'
 DOGLEG RATE 1.5 DEG/100
 TARGET RADIUS IS 75'

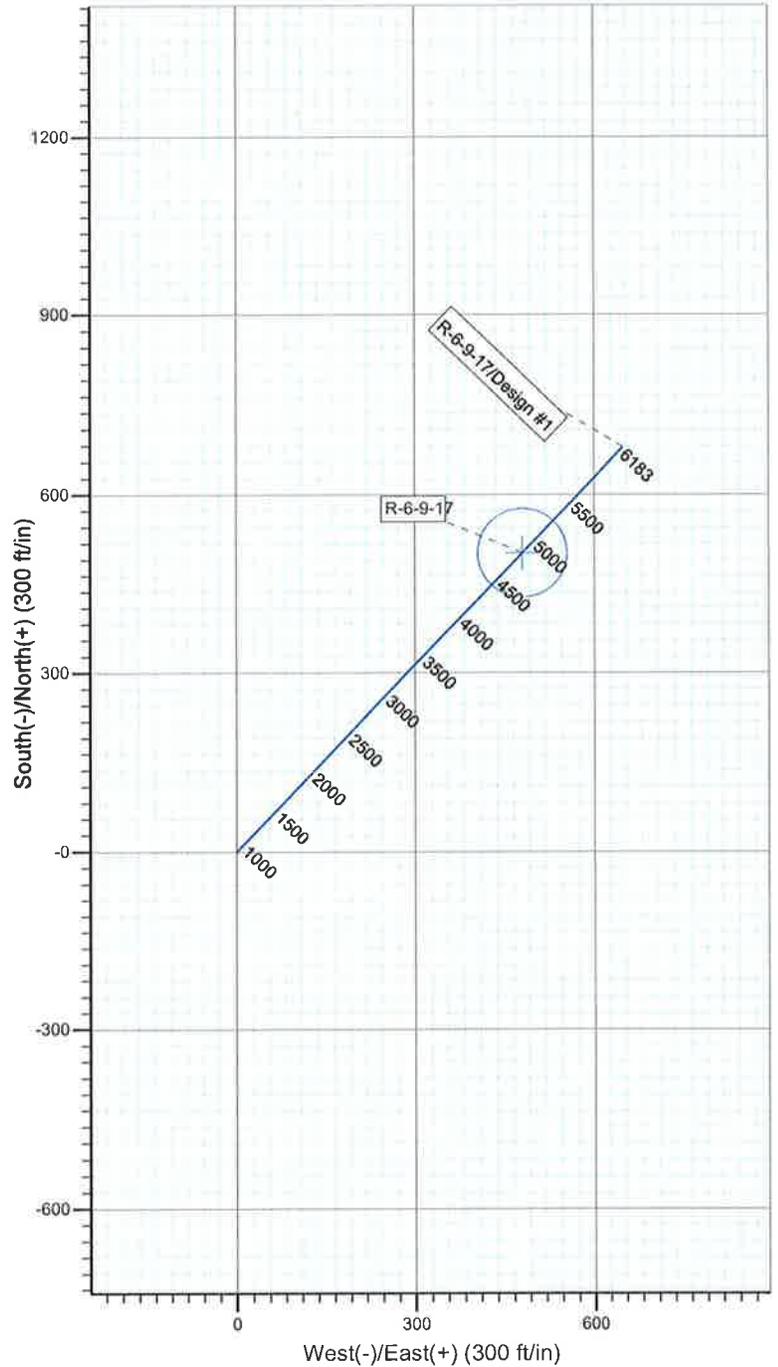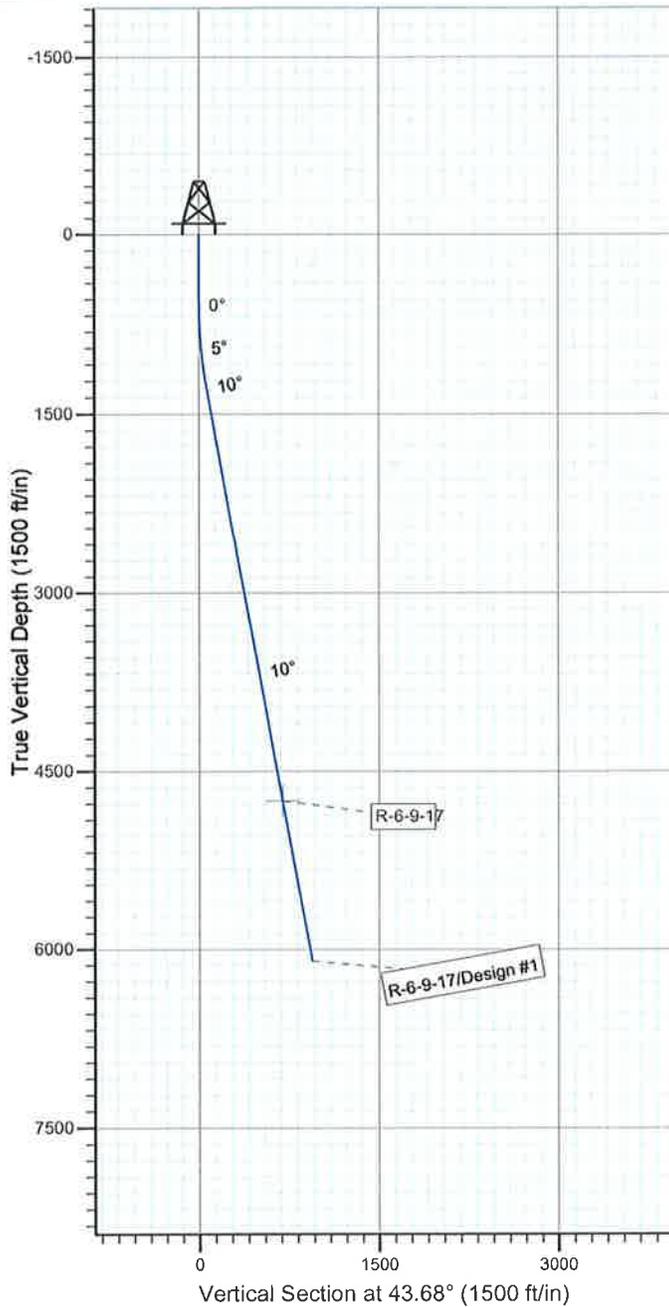

WELLBORE TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Shape
R-6-9-17	4750.0	502.0	479.4	Circle (Radius: 75.0)

SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	DLeg	TFace	VSec	Target
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	



**NEWFIELD PRODUCTION COMPANY
GREATER MONUMENT BUTTE R-6-9-17
AT SURFACE: SE/SW SECTION 6, T9S, R17E
DUCHESNE COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Greater Monument Butte R-6-9-17 located in the SE 1/4 SW 1/4 Section 6, T9S, R17E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 – 1.4 miles ± to the junction of this highway and UT State Hwy 53; proceed southeasterly – 10.0 miles ± to it's junction with an existing road to the southwest; proceed in a southwesterly direction - 1.6 miles ± to it's junction with an existing road to the southeast; proceed in a southeasterly direction – 0.5 miles ± to the existing 24-6-9-17 well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

There is no proposed access road for this location. The proposed well will be drilled directionally off of the existing 24-6-9-17 well pad. See attached **Topographic Map "B"**.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District
Water Right : 43-10136

Maurice Harvey Pond
Water Right: 47-1358

Neil Moon Pond
Water Right: 43-11787

Newfield Collector Well
Water Right: 47-1817 (A30414DVA, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

8. ANCILLARY FACILITIES

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. WELL SITE LAYOUT

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. PLANS FOR RESTORATION OF SURFACE:

a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. SURFACE OWNERSHIP – Bureau of Land Management.

12. OTHER ADDITIONAL INFORMATION

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. MOAC Report #10-171, 11/1/10. Paleontological Resource Survey prepared by, Wade E. Miller, 11/22/10. See attached report cover pages, Exhibit "D".

Surface Flow Line

Newfield requests 1,528' of surface flow line be granted. The Surface Flow Line will consist of up to a 14" bundled pipe consisting of 2-2" poly glycol lines and 1-3" production line. For all new wells, Newfield. **Refer to Topographic Map "D"** for the proposed location of the proposed flow line. Flow lines will be tan and will be constructed using the following procedures:

Clearing and Grading: No clearing or grading of the ROW will be required. The centerline of the proposed route will be staked prior to installation. Flow lines shall be placed as close to existing roads as possible without interfering with normal road travel or road maintenance activities. Due to the proximity of existing facilities, no temporary use or construction/storage areas are anticipated. If necessary, temporary use or construction/storage areas will be identified on a topographic map included in the approved permit.

Installation: The proposed flow lines will be installed 4-6" above the ground. For portions along existing two-track and primary access roads, lengths of pipe will be strung out in the borrow ditch, welded together, and rolled or dragged into place with heavy equipment. For pipelines that are installed cross-country (not along existing or proposed roads), travel along the lines will be infrequent and for maintenance needs only. No installation activities will be performed during periods when the soil is too wet to adequately support installation equipment. If such equipment creates ruts in excess of three (3) inches deep, the soil will be deemed too wet to adequately support the equipment.

Water Disposal

After first production, if the production water meets quality guidelines, it will be transported to the Ashley, Monument Butte, Jonah, South Wells Draw and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project. Water not meeting quality criteria, will be disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), Federally approved surface disposal facilities or at a State of Utah approved surface disposal facilities.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Details of the On-Site Inspection

The proposed Greater Monument Butte R-6-9-17 was on-sited on 12/13/10. The following were present; Tim Eaton (Newfield Production and Janna Simonsen (Bureau of Land Management).

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the Greater Monument Butte R-6-9-17, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Greater Monument Butte R-6-9-17, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

Representative


Name: Tim Eaton
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #R-6-9-17, Section 6, Township 9S, Range 17E: Lease UTU-020252A Duchesne County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

1/7/11
Date


Mandie Crozier
Regulatory Specialist
Newfield Production Company

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office

P.O. Box 45155

Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:

3160

(UT-922)

January 13, 2011

Memorandum

To: Assistant District Manager Minerals, Vernal District

From: Michael Coulthard, Petroleum Engineer

Subject: 2011 Plan of Development Greater Monument
Butte Unit, Duchesne and Uintah Counties,
Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2011 within the Greater Monument Butte Unit, Duchesne and Uintah Counties, Utah.

API#	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-047-51479	GMBU I-23-8-17	Sec 23 T08S R17E 0442 FNL 2172 FEL BHL Sec 23 T08S R17E 1151 FNL 1328 FEL
43-047-51480	GMBU L-23-8-17	Sec 23 T08S R17E 1580 FNL 2045 FEL BHL Sec 23 T08S R17E 2163 FNL 1384 FEL
43-047-51481	GMBU S-23-8-17	Sec 23 T08S R17E 2114 FSL 0823 FEL BHL Sec 23 T08S R17E 1100 FSL 1449 FEL
43-047-51482	GMBU K-23-8-17	Sec 23 T08S R17E 2135 FSL 0818 FEL BHL Sec 23 T08S R17E 1817 FNL 0286 FEL
43-013-50576	GMBU M-30-8-17	Sec 30 T08S R17E 1999 FNL 1991 FEL BHL Sec 30 T08S R17E 2548 FSL 2393 FWL
43-013-50577	GMBU M-11-9-16	Sec 11 T09S R16E 1825 FSL 2167 FWL BHL Sec 11 T09S R16E 2236 FNL 2482 FEL
43-013-50578	GMBU N-11-9-16	Sec 11 T09S R16E 1806 FSL 2158 FWL BHL Sec 11 T09S R16E 2604 FNL 1158 FWL
43-013-50579	GMBU R-11-9-16	Sec 11 T09S R16E 0799 FSL 2047 FWL BHL Sec 11 T09S R16E 1383 FSL 2303 FEL

API#	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-50580	GMBU B-14-9-16	Sec 11 T09S R16E 0730 FSL 0731 FEL BHL Sec 14 T09S R16E 0248 FNL 1467 FEL
43-013-50581	GMBU R-6-9-17	Sec 06 T09S R17E 1108 FSL 2123 FWL BHL Sec 06 T09S R17E 1775 FSL 2379 FEL

This office has no objection to permitting the wells at this time.

Michael L. Coulthard

Digitally signed by Michael L. Coulthard
DN: cn=Michael L. Coulthard, o=Bureau of Land Management, ou=Branch of Minerals,
email=Michael_Coulthard@blm.gov, c=US
Date: 2011.01.13 11:01:09 -07'00'

bcc: File - Greater Monument Butte Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:1-13-11

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office

P.O. Box 45155

Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:

3160

(UT-922)

January 13, 2011

Memorandum

To: Assistant District Manager Minerals, Vernal District

From: Michael Coulthard, Petroleum Engineer

Subject: 2011 Plan of Development Greater Monument
Butte Unit, Duchesne and Uintah Counties,
Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2011 within the Greater Monument Butte Unit, Duchesne and Uintah Counties, Utah.

API#	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-047-51479	GMBU I-23-8-17	Sec 23 T08S R17E 0442 FNL 2172 FEL BHL Sec 23 T08S R17E 1151 FNL 1328 FEL
43-047-51480	GMBU L-23-8-17	Sec 23 T08S R17E 1580 FNL 2045 FEL BHL Sec 23 T08S R17E 2163 FNL 1384 FEL
43-047-51481	GMBU S-23-8-17	Sec 23 T08S R17E 2114 FSL 0823 FEL BHL Sec 23 T08S R17E 1100 FSL 1449 FEL
43-047-51482	GMBU K-23-8-17	Sec 23 T08S R17E 2135 FSL 0818 FEL BHL Sec 23 T08S R17E 1817 FNL 0286 FEL
43-013-50576	GMBU M-30-8-17	Sec 30 T08S R17E 1999 FNL 1991 FEL BHL Sec 30 T08S R17E 2548 FSL 2393 FWL
43-013-50577	GMBU M-11-9-16	Sec 11 T09S R16E 1825 FSL 2167 FWL BHL Sec 11 T09S R16E 2236 FNL 2482 FEL
43-013-50578	GMBU N-11-9-16	Sec 11 T09S R16E 1806 FSL 2158 FWL BHL Sec 11 T09S R16E 2604 FNL 1158 FWL
43-013-50579	GMBU R-11-9-16	Sec 11 T09S R16E 0799 FSL 2047 FWL BHL Sec 11 T09S R16E 1383 FSL 2303 FEL

API#	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-50580	GMBU B-14-9-16	Sec 11 T09S R16E 0730 FSL 0731 FEL BHL Sec 14 T09S R16E 0248 FNL 1467 FEL
43-013-50581	GMBU R-6-9-17	Sec 06 T09S R17E 1108 FSL 2123 FWL BHL Sec 06 T09S R17E 1775 FSL 2379 FEL

This office has no objection to permitting the wells at this time.

Michael L. Coulthard

Digitally signed by Michael L. Coulthard
DN: cn=Michael L. Coulthard, o=Bureau of Land Management, ou=Branch of Minerals,
email=Michael_Coulthard@blm.gov, c=US
Date: 2011.01.13 11:01:09 -07'00'

bcc: File - Greater Monument Butte Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:1-13-11

**WORKSHEET
APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 1/11/2011

API NO. ASSIGNED: 43013505810000

WELL NAME: Greater Monument Butte R-6-9-17

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: SESW 06 090S 170E

Permit Tech Review:

SURFACE: 1108 FSL 2123 FWL

Engineering Review:

BOTTOM: 1775 FSL 2379 FEL

Geology Review:

COUNTY: DUCHESNE

LATITUDE: 40.05562

LONGITUDE: -110.05007

UTM SURF EASTINGS: 581023.00

NORTHINGS: 4434153.00

FIELD NAME: MONUMENT BUTTE

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-020252A

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 1 - Federal

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT**
- Bond:** FEDERAL - WYB000493
- Potash**
- Oil Shale 190-5**
- Oil Shale 190-3**
- Oil Shale 190-13**
- Water Permit:** 437478
- RDCC Review:**
- Fee Surface Agreement**
- Intent to Commingle**

Commingle Approved

LOCATION AND SITING:

- R649-2-3.**
Unit: GMBU (GRRV)
- R649-3-2. General**
- R649-3-3. Exception**
- Drilling Unit**
Board Cause No: Cause 213-11
- Effective Date:** 11/30/2009
- Siting:** Suspends General Siting
- R649-3-11. Directional Drill**

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason
15 - Directional - dmason
27 - Other - bhill



GARY R. HERBERT
Governor

GREGORY S. BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Greater Monument Butte R-6-9-17
API Well Number: 43013505810000
Lease Number: UTU-020252A
Surface Owner: FEDERAL
Approval Date: 1/19/2011

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 213-11. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Production casing cement shall be brought up to or above the top of the unitized interval for the Greater Monument Butte Unit (Cause No. 213-11).

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)
OR
submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <https://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "John Rogers", written in a cursive style.

For John Rogers
Associate Director, Oil & Gas

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No. UTU-020252A	
6. If Indian, Allottee or Tribe Name NA	
7. If Unit or CA Agreement, Name and No. Greater Monument Butte	
8. Lease Name and Well No. Greater Monument Butte R-6-9-17	
9. API Well No. 43-013-50581	
10. Field and Pool, or Exploratory Monument Butte	11. Sec., T, R, M. or Blk. and Survey or Area Sec. 6, T9S R17E
12. County or Parish Duchesne	13. State UT
14. Distance in miles and direction from nearest town or post office* Approximately 13.5 miles southeast of Myton, UT	
15. Distance from proposed* location to nearest property or lease line, ft. Approx. 1775' f/lse, NA f/unit (Also to nearest drig. unit line, if any)	
16. No. of acres in lease 320.13	
17. Spacing Unit dedicated to this well 20 Acres	
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 725'	
19. Proposed Depth 6,183'	
20. BLM/BIA Bond No. on file WYB000493	
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5306' GL	
22. Approximate date work will start* 2nd Qtr. 2011	
23. Estimated duration (7) days from SPUD to rig release	

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

25. Signature <i>Mandle Crozier</i>	Name (Printed/Typed) Mandle Crozier	Date 1/7/11
Title Regulatory Specialist		

Approved by (Signature) <i>Jerry Kenczka</i>	Name (Printed/Typed) Jerry Kenczka	Date DEC 15 2011
Title Assistant Field Manager Lands & Mineral Resources		
Office VERNAL FIELD OFFICE		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

CONDITIONS OF APPROVAL ATTACHED

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

RECEIVED
DEC 21 2011

(Continued on page 2)

*(Instructions on page 2)

UDOGM

NOS 12-3-10

AFMSS# 11SXSO142A

DIV. OF OIL, GAS & MINING

RECEIVED

JAN 12 2011

NOTICE OF APPROVAL

BLM VERNAL, UTAH



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company
Well No: GMBU R-6-9-17
API No: 43-013-50581

Location: SESW, Sec. 6, T9S, R17E
Lease No: UTU-020252A
Agreement:

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	- Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	- Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: blm ut vn opreport@blm.gov
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

**SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.
- After cessation of drilling and completion operations, any visible or measurable layer of oil must be removed from the surface of the reserve pit and the pit kept free of oil.
- Pits must be free of oil and other liquid and solid wastes prior to filling. Pit liners must not be breached (cut) or filled (squeezed) while still containing fluids. The pit liner must be removed to the solids level or treated to prevent its reemergence to the surface or its interference with long-term successful revegetation.

If construction and drilling is anticipated during any of the following wildlife seasonal or spatial restrictions, a qualified consulting firm biologist must be contacted 2 weeks prior in order to conduct applicable surveys using an accepted protocol prior to any ground disturbing activities.

- Three raptor nest surveys must be conducted during the nesting season within ½ mile of the project area(s). It is recommended that these surveys be spaced 3 weeks apart, so nesting status and reproductive success can be verified and documented.
- Mountain plover surveys will be conducted to protocol by a professional Environmental Consulting Firm biologist prior to any ground disturbing activities. Reports from survey results must be reviewed by a BLM minerals biologist prior to proceeding with the proposed project. A seasonal restriction for all ground disturbing activities in mountain plover habitat from May 1-June 15 is required.
- White-tailed prairie dog burrows and animals sighted will be recorded/mapped while conducting (to protocol) burrowing owl surveys. If burrowing owls/burrows are located, a seasonal restriction from March 1-August 31 within .25 miles is required.
- Install hospital mufflers where possible to reduce noise impacts to wildlife.

Reclamation

- Reclamation will be completed in accordance with the Newfield Exploration Company Castle Peak and Eight Mile Flat Reclamation Plan on file with the Vernal Field Office of the BLM.

- The reclamation seed mix will incorporate low growing grasses, instead of crested wheatgrass, which negatively impacts mountain plover habitat.
- Appropriate erosion control and revegetation measures will be employed. In areas with unstable soils where seeding alone may not adequately control erosion, grading will be used to minimize slopes and water bars will be installed on disturbed slopes. Erosion control efforts will be monitored by Newfield and, if necessary, modifications will be made to control erosion.

Monitoring and Reporting

- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) that designates the proposed site-specific monitoring and reference sites chosen for the location. A description of the proposed sites shall be included, as well as a map showing the locations of the proposed sites.
- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) 3 growing seasons after reclamation efforts have occurred evaluating the status of the reclaimed areas in order to determine whether the BLM standards set forth in the Green River District Reclamation Guidelines have been met (30% or greater basal cover).

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Newfield Production Co. shall comply with all applicable requirements in the SOP (version: "Greater Monument Butte Green River Development Program", June 24, 2008). The operator shall also comply with applicable laws and regulations; with lease terms, Onshore Oil and Gas Orders, NTL's; and with other orders and instructions of the authorized officer.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each

encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to BLM_UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs,

core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9
5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-020252A	
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	
6. IF INDIAN, ALLOTTEE OR TRIBE NAME:	
7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)	
8. WELL NAME and NUMBER: GREATER MON BUTTE R-6-9-17	
9. API NUMBER: 43013505810000	
9. FIELD and POOL or WILDCAT: MONUMENT BUTTE	
9. COUNTY: DUCHESNE	
9. STATE: UTAH	
1. TYPE OF WELL Oil Well	
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	
PHONE NUMBER: 435 646-4825 Ext	
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1108 FSL 2123 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SESW Section: 06 Township: 09.0S Range: 17.0E Meridian: S	

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 1/19/2012	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input checked="" type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Newfield proposes to extend the Application for Permit to Drill this well for one year.

Approved by the Utah Division of Oil, Gas and Mining

Date: January 12, 2012

By:

NAME (PLEASE PRINT) Mandie Crozier	PHONE NUMBER 435 646-4825	TITLE Regulatory Tech
SIGNATURE N/A	DATE 1/9/2012	



The Utah Division of Oil, Gas, and Mining

- State of Utah
- Department of Natural Resources

Electronic Permitting System - Sundry Notices

Request for Permit Extension Validation Well Number 43013505810000

API: 43013505810000

Well Name: GREATER MON BUTTE R-6-9-17

Location: 1108 FSL 2123 FWL QTR SESW SEC 06 TWP 090S RNG 170E MER S

Company Permit Issued to: NEWFIELD PRODUCTION COMPANY

Date Original Permit Issued: 1/19/2011

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision. Following is a checklist of some items related to the application, which should be verified.

- If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes No
- Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes No
- Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes No
- Have there been any changes to the access route including ownership, or rightof- way, which could affect the proposed location? Yes No
- Has the approved source of water for drilling changed? Yes No
- Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes No
- Is bonding still in place, which covers this proposed well? Yes No

Signature: Mandie Crozier

Date: 1/9/2012

Title: Regulatory Tech Representing: NEWFIELD PRODUCTION COMPANY

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross 29 Submitted By
Branden Arnold Phone Number 435-401-0223

Well Name/Number GMB R-6-9-17

Qtr/Qtr SE/SW Section 6 Township 9S Range 17E

Lease Serial Number UTU-0202252A

API Number 43-013-50581

Spud Notice – Spud is the initial spudding of the well, not drilling
out below a casing string.

Date/Time 4/5/12 9:00 AM PM

Casing – Please report time casing run starts, not cementing
times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 4/5/12 3:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks _____

STATE OF UTAH
 DIVISION OF OIL, GAS AND MINING
 ENTITY ACTION FORM -FORM 6


OPERATOR: NEWFIELD PRODUCTION COMPANY
 ADDRESS: RT. 3 BOX 3630
MYTON, UT 84052

OPERATOR ACCT. NO. N2695

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4304751649	GMBU N-25-8-17	NWSW	25	8S	17E	Uintah	4/4/2012	4/24/12
WELL 1 COMMENTS: GRRV											
B	16361	17400	4304734943	GMBU 3-14-9-18H	NENW	14	9S	18E	Uintah	4/4/2012	4/24/12
GRRV CONFIDENTIAL											
B	99999	17400	4301350745	GMBU F-8-9-17	NENE	7	9S	17E	Duchesne	4/4/2012	4/24/12
GRRV											
B	99999	17400	4301350581	GMBU R-6-9-17	SESW	6	9S	17E	Duchesne	4/5/2012	4/24/12
GRRV											
B	99999	17400	4301350684	GMBU V-6-9-17	NENE	7	9S	17E	Duchesne	4/4/2012	4/24/12
GRRV											

ACTION CODES (See instructions on back of form)
 A - 1 new entity for new well (single well only)
 B - 1 well to existing entity (group or unit well)
 C - from one existing entity to another existing entity
 D - well from one existing entity to a new entity
 E - ther (explain in comments section)

RECEIVED
 APR 18 2012


 Signature
 Tabitha Timothy
 Production Clerk
 04/11/12

NOTE: Use COMMENT section to explain why each Action Code was selected.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

5. Lease Serial No.

USA UTU-020252-A

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

GMBU

8. Well Name and No.

GRTR MON BUTTE R-6-9-17

9. API Well No.

4301350581

10. Field and Pool, or Exploratory Area

GREATER MB UNIT

11. County or Parish, State

DUCHESNE, UT

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630

Myton, UT 84052

3b. Phone (include are code)

435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

1108 FSL 2123 FWL

Section 6 T9S R17E

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 4/5/12 MIRU Ross #29. Spud well @9:00 AM. Drill 340' of 12 1/4" hole with air mist. TIH W/ 8 Jt's 8 5/8" J-55 24# csgn. Set @ 341.17'. On 4/9/12 cement with 170 sks of class "G" w/ 2% CaCL2 + 0.25#/sk Cello- Flake Mixed @ 15.8ppg w/ 1.17ft3/sk yield. Returned 5 barrels cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Branden Arnold

Signature

Branden Arnold

Title

Date

04/11/2012

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

RECEIVED

APR 19 2012

DIV. OF OIL, GAS & MINING

Casing / Liner Detail

Well GMBU R-6-9-17
Prospect Monument Butte
Foreman _____
Run Date: _____
String Type Surface, 8.625", 24#, J-55, STC (Generic)

- Detail From Top To Bottom -

Depth	Length	JTS	Description	OD	ID
341.75	1.42		Wellhead		
343.17	-2.00		Cutoff		
10.00	42.30	1	Shoe Joint	8.625	
52.30	288.55	7	8 5/8" Casing	8.625	
340.85	0.90	1	Guide Shoe	8.625	
341.17			KB		

Cement Detail

Cement Company: BJ					
Slurry	# of Sacks	Weight (ppg)	Yield	Volume (ft³)	Description - Slurry Class and Additives
Slurry 1	170	15.8	1.17	198.9	Class "G"+2%CaCl

Stab-In-Job?	No
BHT:	0
Initial Circulation Pressure:	
Initial Circulation Rate:	
Final Circulation Pressure:	
Final Circulation Rate:	
Displacement Fluid:	Water
Displacement Rate:	
Displacement Volume:	19.1
Mud Returns:	
Centralizer Type And Placement:	
Middle of first, top of second and third for a total of three.	

Cement To Surface?	Yes
Est. Top of Cement:	0
Plugs Bumped?	Yes
Pressure Plugs Bumped:	115
Floats Holding?	No
Casing Stuck On / Off Bottom?	No
Casing Reciprocated?	No
Casing Rotated?	No
CIP:	13:30
Casing Wt Prior To Cement:	
Casing Weight Set On Slips:	

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# NDSI SS # 1
Submitted By Xabier Lasa Phone Number 435-823-6014
Well Name/Number GMBU R-6-9-17
Qtr/Qtr NW/SE Section 6 Township 9S Range 17E
Lease Serial Number UTU-020252A
API Number 43-013-50581

TD Notice – TD is the final drilling depth of hole.

Date/Time 5-22-12 3:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 5-22-12 4:00 AM PM

RECEIVED

MAY 22 2012

DIV. OF OIL, GAS & MINING

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-020252A
1. TYPE OF WELL Oil Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052		8. WELL NAME and NUMBER: GREATER MON BUTTE R-6-9-17
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1108 FSL 2123 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SESW Section: 06 Township: 09.0S Range: 17.0E Meridian: S		9. API NUMBER: 43013505810000
PHONE NUMBER: 435 646-4825 Ext		9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
COUNTY: DUCHESNE		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 6/6/2012	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE TUBING	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CHANGE WELL NAME	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER	
	OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. The above well was placed on production on 06/06/2012 at 17:00 hours. Production Start Sundry resent 10/05/2012.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY October 09, 2012		
NAME (PLEASE PRINT) Kaci Deveraux	PHONE NUMBER 435 646-4867	TITLE Production Technician
SIGNATURE N/A	DATE 10/5/2012	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-020252A
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Oil Well	7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	8. WELL NAME and NUMBER: GREATER MON BUTTE R-6-9-17
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1108 FSL 2123 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SESW Section: 06 Township: 09.0S Range: 17.0E Meridian: S	9. API NUMBER: 43013505810000
	9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
	COUNTY: DUCHESENE
	STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 6/6/2012	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
 The above well was placed on production on 06/06/2012 at 17:00 hours. Production Start Sundry resent 10/05/2012.

NAME (PLEASE PRINT) Kaci Deveraux	PHONE NUMBER 435 646-4867	TITLE Production Technician
SIGNATURE N/A	DATE 10/5/2012	

Daily Activity Report

Format For Sundry

GMBU R-6-9-17

4/1/2012 To 8/30/2012

6/1/2012 Day: 1

Completion

Rigless on 6/1/2012 - Run CBL Press test BOPs ,Valves & Csg. Perforate 1st Stage - Safety meeting. JSA Press Test Lines to 5000psi. Open well 1308 psi break down A3 formation (15 holes) @ 2790 psi w/ 1.2 bbls 7% KCL @ 2.2 BPM. 37 bbls 7% KCL to get Rate, 15 bbls to get X link. Pump 471 bbls 1# to 5# 20/40 sand (ramped) 61 BBls 20/40 6# sand, 12 BBls 15% HCL, 125 BBls 7% KCL Flush. ISIP 2183 psi FG .87, Max press 3462 psi Avg press 2964 psi. Max rate 34.7 BPM Avg rate 34.4 BPM. 98,225# 20/40 Sand in formation. 720 total BBls Pumped. CWI - Safety meeting. JSA Press Test Lines to 5000psi. Open well 1834 psi break down D formation (12 holes) @ 2627 psi w/ 1 bbls 7% KCL @ 2.8 BPM.Pump 95 bbls 7% KCL to get Rate, 15 bbls to get X link. Pump 67 bbls 1# to 5# 20/40 sand (ramped) 155 BBls 6# 20/40 sand, 113 BBls 7% KCL Flush. ISIP 2180 psi FG .91, Max press 3744 psi Avg press 2900 psi. Max rate 29.6 BPM Avg rate 29.5 BPM. 26577# 20/40 Sand in formation. 444 total BBls Pumped. CWI - RU Extreme WL & Weatherford press Tester. Press test Lub to 5000 psi. Open Well @ 1834 psi RIH w/ CFT Plug & 3-1/3 Csg guns. Set CFT Plug @ 4880' & Perforate the D formation @ 4820-21', 4817-18', 4765-66', 4749-50', w/ 3-1/8 Csg guns 3SPF (12 holes) POOH CWI RD WL - RU Extreme WL & Weatherford press Tester. Press test Lub to 5000 psi. Open Well @ 1834 psi RIH w/ CFT Plug & 3-1/3 Csg guns. Set CFT Plug @ 4880' & Perforate the D formation @ 4820-21', 4817-18', 4765-66', 4749-50', w/ 3-1/8 Csg guns 3SPF (12 holes) POOH CWI RD WL - Safety meeting. JSA Press Test Lines to 5000psi. Open well 1835 psi break down B&C formations (18 holes) @ 2054 psi w/ 1.2 bbls 7% KCL @ 2.4 BPM. 91 bbls 7% KCL to get Rate, 15 bbls to get X link. Pump 360 bbls 1# to 5# 20/40 sand (ramped) 32 BBls 20/40 6# sand, 12 BBls 15% HCL, 117 BBls 7% KCL Flush. ISIP 2399 psi FG .93, Max press 3626 psi Avg press 3114 psi. Max rate 43.7 BPM Avg rate 43.5 BPM. 71,864# 20/40 Sand in formation. 626 total BBls Pumped. CWI - Safety meeting. JSA Press Test Lines to 5000psi. Open well 1835 psi break down B&C formations (18 holes) @ 2054 psi w/ 1.2 bbls 7% KCL @ 2.4 BPM. 91 bbls 7% KCL to get Rate, 15 bbls to get X link. Pump 360 bbls 1# to 5# 20/40 sand (ramped) 32 BBls 20/40 6# sand, 12 BBls 15% HCL, 117 BBls 7% KCL Flush. ISIP 2399 psi FG .93, Max press 3626 psi Avg press 3114 psi. Max rate 43.7 BPM Avg rate 43.5 BPM. 71,864# 20/40 Sand in formation. 626 total BBls Pumped. CWI - RU Extreme WL & Weatherford press Tester. Press test Lub to 5000 psi. Open Well @ 1835 psi RIH w/ CFT Plug & 3-1/3 Csg guns. Set CFT Plug @ 5150' & Perforate the B&C formations @ 5065-66', 5062-63', 5043-44', 5038-39', 4930-31', 4920-21', w/ 3-1/8 Csg guns 3SPF (18 holes) POOH CWI RD WL - RU Extreme WL & Weatherford press Tester. Press test Lub to 5000 psi. Open Well @ 1835 psi RIH w/ CFT Plug & 3-1/3 Csg guns. Set CFT Plug @ 5150' & Perforate the B&C formations @ 5065-66', 5062-63', 5043-44', 5038-39', 4930-31', 4920-21', w/ 3-1/8 Csg guns 3SPF (18 holes) POOH CWI RD WL - Safety meeting. JSA Press Test Lines to 5000psi. Open well 1308 psi break down A3 formation (15 holes) @ 2790 psi w/ 1.2 bbls 7% KCL @ 2.2 BPM. 37 bbls 7% KCL to get Rate, 15 bbls to get X link. Pump 471 bbls 1# to 5# 20/40 sand (ramped) 61 BBls 20/40 6# sand, 12 BBls 15% HCL, 125 BBls 7% KCL Flush. ISIP 2183 psi FG .87, Max press 3462 psi Avg press 2964 psi. Max rate 34.7 BPM Avg rate 34.4 BPM. 98,225# 20/40 Sand in formation. 720 total BBls Pumped. CWI - Safety meeting. JSA Press Test Lines to 5000psi. Open well 1834 psi break down D formation (12 holes) @ 2627 psi w/ 1 bbls 7% KCL @ 2.8 BPM.Pump 95 bbls 7% KCL to get Rate, 15 bbls to get X link. Pump 67 bbls 1# to 5# 20/40 sand (ramped) 155 BBls 6# 20/40 sand, 113 BBls 7% KCL Flush. ISIP 2180 psi FG .91, Max press 3744 psi Avg press 2900 psi. Max rate 29.6 BPM Avg rate 29.5 BPM. 26577# 20/40 Sand in formation. 444 total BBls Pumped. CWI - SICP 1835 psi open well to flow back on 20/64 choke @ 3 BPM - SICP 1835 psi open well to flow back on 20/64 choke @ 3 BPM - MAINTENANCE ON RIG WHILE WAITING FOR FRAC TO FINISH UP AND MOVE OFF MOVE RIG AND EQUIPTMENT ONTO THE R -6-9-17 SIRU/ DERRICK

INSPECTION X-O TBG EQUIPMENT, SPOT IN PIPE RACKS, CLEAN UP SDFN - MAINTENANCE ON RIG WHILE WAITING FOR FRAC TO FINISH UP AND MOVE OFF MOVE RIG AND EQUIPMENT ONTO THE R -6-9-17 SIRU/ DERRICK INSPECTION X-O TBG EQUIPMENT, SPOT IN PIPE RACKS, CLEAN UP SDFN - NU 6" 5K Cameron BOP & Weatherford Frac Valve. RU Perforators LLC WLT w/ Crane & run CBL. WLTD @ 6099' & cement top @ 262'.RU H/O truck & Weatherford Press Testing Unit pressure test casing, blind rams, csg & casing valves to 4300 psi. Press test Top of Frac Valve & Lubricator to 5000 psi Perforate stage #1, CP sds @ (5803-04', 5791-92', 5772-73', 5763-64', 5693-94', 5682-83') w/ 3 1/8" Disposable guns (16 gram .34" EH 22" pen w/120° phasing) w/ 3 spf for total of 18 shots. RD H/O truck, Weatherford & The Perforators WLT & mast. Wait on frac crew EWTR 135 BBLS - NU 6" 5K Cameron BOP & Weatherford Frac Valve. RU Perforators LLC WLT w/ Crane & run CBL. WLTD @ 6099' & cement top @ 262'.RU H/O truck & Weatherford Press Testing Unit pressure test casing, blind rams, csg & casing valves to 4300 psi. Press test Top of Frac Valve & Lubricator to 5000 psi Perforate stage #1, CP sds @ (5803-04', 5791-92', 5772-73', 5763-64', 5693-94', 5682-83') w/ 3 1/8" Disposable guns (16 gram .34" EH 22" pen w/120° phasing) w/ 3 spf for total of 18 shots. RD H/O truck, Weatherford & The Perforators WLT & mast. Wait on frac crew EWTR 135 BBLS - Safety meeting. JSA Press Test Lines to 5000psi. Open well 60 psi break down CP formation (18 holes) @ 3645 psi w/ 6.9 bbls 7% KCL @ 6.5 BPM. Pump 6 bbls 15% HCL, 172 bbls 7% KCL to get Rate, 15 bbls to get X link. Pump 388 bbls 1# to 5# 20/40 sand (ramped) 58 BBls 20/40 6# sand, 12 BBls 15% HCL, 135 BBls 7% KCL Flush. ISIP 1746 psi FG .76, Max press 4109 psi Avg press 2495 psi. Max rate 44 BPM Avg rate 24 BPM. 82,539# 20/40 Sand in formation. 794 total BBls Pumped. CWI - Safety meeting. JSA Press Test Lines to 5000psi. Open well 60 psi break down CP formation (18 holes) @ 3645 psi w/ 6.9 bbls 7% KCL @ 6.5 BPM. Pump 6 bbls 15% HCL, 172 bbls 7% KCL to get Rate, 15 bbls to get X link. Pump 388 bbls 1# to 5# 20/40 sand (ramped) 58 BBls 20/40 6# sand, 12 BBls 15% HCL, 135 BBls 7% KCL Flush. ISIP 1746 psi FG .76, Max press 4109 psi Avg press 2495 psi. Max rate 44 BPM Avg rate 24 BPM. 82,539# 20/40 Sand in formation. 794 total BBls Pumped. CWI - RU Extreme WL & Weatherford press Tester. Press test Lub to 5000 psi. Open Well @ 1308 psi RIH w/ CFT Plug & 3-1/3 Csg guns. Set CFT Plug @ 5330' & Perforate the A3 formation @ 5268-69', 5262-63', 5255-56', 5247-48', 5231-32', w/ 3-1/8 Csg guns 3SPF (15 holes) POOH CWI RD WL - RU Extreme WL & Weatherford press Tester. Press test Lub to 5000 psi. Open Well @ 1308 psi RIH w/ CFT Plug & 3-1/3 Csg guns. Set CFT Plug @ 5330' & Perforate the A3 formation @ 5268-69', 5262-63', 5255-56', 5247-48', 5231-32', w/ 3-1/8 Csg guns 3SPF (15 holes) POOH CWI RD WL

Daily Cost: \$0

Cumulative Cost: \$25,702

6/5/2012 Day: 3

Completion

Rigless on 6/5/2012 - Set Kill Plug Press test BOPs PU & TIH w/ Bit & Tbg Tag Kill Plug. RU Pump & Lines - NU BOP PRESS TEST 5000 PSI, RU WORK FLOOR, X -O TBG EQUIPMENT, RU TBG TONGS, PREP TALLEY TBG, RU LIFTING CYLINDER - RU EXTREME WIRELINE, RIH SET KILL PLUG @4670, POOH W/ WIRELINE, BLEED OFF WELL, RD WIRELINE - CREW TRAVEL, JSA, JSP, START EQUIPMENT - PU RIH W/ MILL, POBS, 149 JNTS 2 7/8" J -55 TBG, TAG KILL PLUG, LD 1 JNT - RU POWER SWIVEL, FINISH BUILDING PUMP LINES AND RETURN LINES, HAVE EVERYTHING READY TO START DRILLING IN MORNING, SWIFN, CLEAN UP SDFN

Daily Cost: \$0

Cumulative Cost: \$252,271

6/6/2012 Day: 4

Completion

Nabors #1450 on 6/6/2012 - Drill Out Plugs Clean out to PBD @ 6127' Flow well To Batt. - CREW TRAVEL, JSA, JSP, START EQUIPMENT - POOH W/ 50 JNTS TO DERRICK, SWIFN EOT @4662, CLEAN UP OPEN UP CSG TO TANK BATTERY FOR NIGHT, SDFN - RD POWER SWIVEL -

ROLL 140 BBLS OF 7% DWN TBG AND UP CSG, WELL STILL FLOWING - DRILL OUT KILL PLUG JNT 149 @ 4670, 1000PSI UNDER PLUG, SWIVEL DWN 7 JNTS, DRILL PLUG @ 4880 JNT 156, SWIVEL DWN 8 JNTS, DRILL PLUG @ 5150, JNT 164, SWIVEL DWN TO PLUG @ 5330 CLEANING OUT 60 FT OF FILL ON PLUG, HANG SWIVEL BACK RIH W/ 22 JNTS TAGGING 90 FT OF FILL ON PBTD, RU POWER SWIVEL, CLEAN OUT TO PBTD @ 6127

Daily Cost: \$0

Cumulative Cost: \$260,376

6/7/2012 Day: 5

Completion

Nabors #1450 on 6/7/2012 - Land tbg @ 4725.42' NU WH RD Rig Trun Well Over to Production - RACK OUT PUMP, CLEAN UP LOCATION WAITING FOR BAKER HUGHES TO PULL OFF NEXT LOCATION - CREW TRAVEL, JSA, JSP, START EQUIPMENT - TBG 250 PSI, CSG 150 PSI MADE 300 BBLS FLOWING UP CSP OVER NIGHT, WAIT FOR DECISION ON HOW TO PROCEED. WAIT FOR WELL HEAD - RU PUMP LINES, PUMP 30 BBLS DWN TBG, KILL TBG - RIH W/ 24 STANDS OUT OF DERRICK, LD 50 TOTAL JNTS ON GROUND LEAVING 150 IN WELL - RIG DWN - LAND WELL, @ 4725.42, ND BOP, RD WORKFLOOR, NU WELL HEAD, BUILD FLOW LINES

Daily Cost: \$0

Cumulative Cost: \$269,531

6/21/2012 Day: 7

Completion

Stone #10 on 6/21/2012 - Circ 260 Bbls 7% KCL. Kill well. TIH W/production Tbg and BHA. - MIRU. RU work floor. Wait most of the day for 7% KCL. Flush tubing W/25 Bbl 7% KCL. NUBOP. Flush casing W/25 Bbl 7% KCL. RU floor. Stab wash rubber. Set pipe racks. - SITP 0 Psi. SICP 200 Psi. PU 45 Jts. Tag fill @ 6127'. RU rig pump, circ 150 Bbls 7%KCL, well was not dead, circ 110 Bbls 7% KCL. LD 9 Jts. TOOH & tally 186 Jts, POBS, and bit. TIH W/production. Set TAC W/18,000# tension. NDBOP. TIH W/183 Jts Tbg, TAC, 1 Jt, SN, BN, 2 Jts. NC. EOT @ 5852.51. NUWH. PREP rods. - SITP 0 Psi. SICP 200 Psi. PU 45 Jts. Tag fill @ 6127'. RU rig pump, circ 150 Bbls 7%KCL, well was not dead, circ 110 Bbls 7% KCL. LD 9 Jts. TOOH & tally 186 Jts, POBS, and bit. TIH W/production. Set TAC W/18,000# tension. NDBOP. TIH W/183 Jts Tbg, TAC, 1 Jt, SN, BN, 2 Jts. NC. EOT @ 5852.51. NUWH. PREP rods. - MIRU. RU work floor. Wait most of the day for 7% KCL. Flush tubing W/25 Bbl 7% KCL. NUBOP. Flush casing W/25 Bbl 7% KCL. RU floor. Stab wash rubber. Set pipe racks.

Daily Cost: \$0

Cumulative Cost: \$282,079

6/22/2012 Day: 8

Completion

Stone #10 on 6/22/2012 - TIH W/rods, stroke test to 800 Psi. PWOP. RDMO. - Flush Tbg W/40 Bbls 7% KCL W/hot oiler. Prime rod pump, PU and RIH W/ pump and rods. 30' X 1-1/2" polish rod/ 2' 4' 6' X 7/8" ponies, 72 7/8" - 4 per. 153 3/4' - 4 per. 5 1-1/2" K bars W/ stabilizers. 2.5X1.75X24' RHAC. Stroke test to 800 Psi. RUPU. RDMO. PWOP @ 1:00 pm W/144' SL @ 5 SPM. FINAL REPORT. **Finalized**

Daily Cost: \$0

Cumulative Cost: \$354,510

Pertinent Files: Go to File List

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
UTU-020252A

1a. Type of Well Oil Well Gas Well Dry Other
 b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Resrv.,
 Other: _____

6. If Indian, Allottee or Tribe Name
NA

7. Unit or CA Agreement Name and No.
GMBU (GRRV)

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

8. Lease Name and Well No.
GMBU R-6-9-17

3. Address
1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
(435) 646-3721

9. AFI Well No.
43-013-50581

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

At surface 1108' FSL & 2123' FWL (SE/SW) SEC. 6, T9S, R17E (UTU-020252A)

At top prod. interval reported below 1623' FSL & 2598' FWL (NE/SW) SEC. 6, T9S, R17E (UTU-020252A)

At total depth 1765' FSL & 2524' FEL (NW/SE) SEC. 6, T9S, R17E (UTU-020252A) *BHL by HSM*

10. Field and Pool or Exploratory
MONUMENT BUTTE

11. Sec., T., R., M., on Block and
Survey or Area SEC. 6, T9S, R17E

12. County or Parish

DUCHESNE

13. State

UT

14. Date Spudded
04/05/2012

15. Date T.D. Reached
05/23/2012

16. Date Completed 06/21/2012
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5306' GL 5316' KB

18. Total Depth: MD 6175'
TVD 6098'

19. Plug Back T.D.: MD 6127'
TVD 6051

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	341'		170 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	6171'		230 PRIMLITE		262'	
						470 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 5853'	TA @ 5753'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Green River	4749'	5804'	5749-5804'	.34"	63	
B)						
C)						
D)						

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
4749-5804'	Frac w/ 289205#s 20/40 white sand in 2167 bbls of Lightning 17 fluid, in 4 stages.

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
6/10/12	6/16/12	24	→	129	53	20			2-1/2" x 1-1/2" x 20' x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

RECEIVED

OCT 24 2012

DIV. OF OIL, GAS & MINING

*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD AND USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
GREEN RIVER	4749'	5804'		GARDEN GULCH MRK	3710'
				GARDEN GULCH 1	3912'
				GARDEN GULCH 2	4032'
				POINT 3	4293'
				X MRKR	4548'
				Y MRKR	4584'
				DOUGLAS CREEK MRK	4713'
				BI CARBONATE MRK	4964'
				B LIMESTON MRK	5097'
				CASTLE PEAK	5566'
				BASAL CARBONATE	6002'


32. Additional remarks (include plugging procedure):

The above well began flowing during the completion process, on 06/06/2012. Completion procedures were finalized on 06/21/2012 at 13:00 hours, and test data was taken ten days following, on 07/01/2012.

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other:

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name *(please print)* Jennifer Peatross Title Production Technician
 Signature  Date 07/09/2012

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

NEWFIELD

NEWFIELD EXPLORATION

**USGS Myton SW (UT)
SECTION 6 T9S, R17E
R-6-9-17**

Wellbore #1

Design: Actual

Standard Survey Report

23 May, 2012





Payzone Directional Survey Report



Company: NEWFIELD EXPLORATION	Local Co-ordinate Reference: Well R-6-9-17
Project: USGS Myton SW (UT)	TVD Reference: R-6-9-17 @ 5316.0ft (NDSI SS #1)
Site: SECTION 6 T9S, R17E	MD Reference: R-6-9-17 @ 5316.0ft (NDSI SS #1)
Well: R-6-9-17	North Reference: True
Wellbore: Wellbore #1	Survey Calculation Method: Minimum Curvature
Design: Actual	Database: EDM 2003.21 Single User Db

Project USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA			
Map System: US State Plane 1983	System Datum: Mean Sea Level		
Geo Datum: North American Datum 1983			
Map Zone: Utah Central Zone			

Site SECTION 6 T9S, R17E			
Site Position:	Northing: 7,195,000.00 ft	Latitude: 40° 3' 47.061 N	
From: Lat/Long	Easting: 2,047,000.00 ft	Longitude: 110° 2' 50.009 W	
Position Uncertainty: 0.0 ft	Slot Radius: "	Grid Convergence: 0.93 °	

Well R-6-9-17, SHL LAT: 40° 03' 20.39, LONG: -110° 03' 02.76			
Well Position	+N/-S 0.0 ft	Northing: 7,192,285.67 ft	Latitude: 40° 3' 20.390 N
	+E/-W 0.0 ft	Easting: 2,046,052.57 ft	Longitude: 110° 3' 2.760 W
Position Uncertainty	0.0 ft	Wellhead Elevation: 5,316.0 ft	Ground Level: 5,306.0 ft

Wellbore Wellbore #1					
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010	11/11/2010	11.39	65.82	52,338

Design Actual					
Audit Notes:					
Version: 1.0	Phase: ACTUAL	Tie On Depth: 0.0			
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)	
	0.0	0.0	0.0	43.91	

Survey Program Date 5/23/2012					
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description	
347.0	6,175.0	Survey #1 (Wellbore #1)	MWD	MWD - Standard	

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
347.0	1.50	14.90	347.0	4.4	1.2	4.0	0.43	0.43	0.00
377.0	1.60	12.00	376.9	5.2	1.4	4.7	0.42	0.33	-9.67
408.0	1.60	15.60	407.9	6.0	1.6	5.4	0.32	0.00	11.61
438.0	1.80	27.40	437.9	6.8	1.9	6.2	1.34	0.67	39.33
468.0	2.10	29.10	467.9	7.7	2.4	7.2	1.02	1.00	5.67
500.0	2.10	33.30	499.9	8.7	3.0	8.4	0.48	0.00	13.13
530.0	2.50	40.70	529.9	9.7	3.7	9.6	1.66	1.33	24.67
561.0	2.60	44.70	560.8	10.7	4.6	10.9	0.66	0.32	12.90
592.0	2.70	48.10	591.8	11.7	5.7	12.4	0.60	0.32	10.97
622.0	2.70	47.70	621.8	12.6	6.7	13.8	0.06	0.00	-1.33
653.0	3.00	49.40	652.7	13.7	7.9	15.3	1.01	0.97	5.48
683.0	3.20	49.80	682.7	14.7	9.1	16.9	0.67	0.67	1.33

Payzone Directional
Survey Report



Company: NEWFIELD EXPLORATION
Project: USGS Myton SW (UT)
Site: SECTION 6 T9S, R17E
Well: R-6-9-17
Wellbore: Wellbore #1
Design: Actual

Local Co-ordinate Reference: Well R-6-9-17
TVD Reference: R-6-9-17 @ 5316.0ft (NDSI SS #1)
MD Reference: R-6-9-17 @ 5316.0ft (NDSI SS #1)
North Reference: True
Survey Calculation Method: Minimum Curvature
Database: EDM 2003.21 Single User Db

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
714.0	3.40	48.50	713.6	15.9	10.5	18.7	0.69	0.65	-4.19
744.0	3.80	49.50	743.6	17.1	11.9	20.6	1.35	1.33	3.33
775.0	4.40	50.00	774.5	18.5	13.6	22.8	1.94	1.94	1.61
805.0	4.60	48.70	804.4	20.1	15.4	25.1	0.75	0.67	-4.33
836.0	5.20	47.20	835.3	21.9	17.3	27.8	1.98	1.94	-4.84
866.0	6.10	48.20	865.1	23.8	19.5	30.7	3.02	3.00	3.33
896.0	6.30	47.40	895.0	26.0	21.9	34.0	0.73	0.67	-2.67
926.0	6.60	47.30	924.8	28.3	24.4	37.3	1.00	1.00	-0.33
957.0	7.00	46.80	955.6	30.8	27.1	41.0	1.30	1.29	-1.61
987.0	7.60	46.20	985.3	33.4	29.9	44.8	2.02	2.00	-2.00
1,018.0	8.30	46.50	1,016.0	36.4	33.0	49.1	2.26	2.26	0.97
1,063.0	8.80	45.60	1,060.5	41.0	37.8	55.8	1.15	1.11	-2.00
1,109.0	9.00	44.00	1,106.0	46.1	42.8	62.9	0.69	0.43	-3.48
1,155.0	9.40	43.00	1,151.4	51.4	47.8	70.2	0.94	0.87	-2.17
1,199.0	10.10	42.20	1,194.7	56.9	52.9	77.7	1.62	1.59	-1.82
1,244.0	10.50	41.40	1,239.0	62.9	58.3	85.7	0.94	0.89	-1.78
1,290.0	10.60	41.71	1,284.2	69.2	63.8	94.1	0.25	0.22	0.67
1,334.0	10.70	42.30	1,327.5	75.2	69.3	102.3	0.34	0.23	1.34
1,380.0	10.80	41.10	1,372.7	81.7	75.0	110.8	0.53	0.22	-2.61
1,425.0	10.60	40.90	1,416.9	88.0	80.5	119.2	0.45	-0.44	-0.44
1,469.0	10.50	40.10	1,460.1	94.1	85.7	127.2	0.40	-0.23	-1.82
1,515.0	10.40	39.70	1,505.4	100.5	91.1	135.5	0.27	-0.22	-0.87
1,559.0	9.90	41.20	1,548.7	106.4	96.1	143.3	1.29	-1.14	3.41
1,603.0	9.40	41.50	1,592.1	111.9	101.0	150.6	1.14	-1.14	0.68
1,649.0	8.90	42.30	1,637.5	117.4	105.8	158.0	1.12	-1.09	1.74
1,694.0	8.60	44.30	1,682.0	122.4	110.5	164.8	0.95	-0.67	4.44
1,740.0	8.50	45.20	1,727.4	127.2	115.3	171.6	0.36	-0.22	1.96
1,784.0	8.30	44.50	1,771.0	131.8	119.9	178.1	0.51	-0.45	-1.59
1,828.0	8.00	43.60	1,814.5	136.2	124.2	184.3	0.74	-0.68	-2.05
1,872.0	8.40	44.30	1,858.1	140.8	128.6	190.6	0.94	0.91	1.59
1,916.0	8.70	45.80	1,901.6	145.4	133.2	197.1	0.85	0.68	3.41
1,960.0	8.90	41.40	1,945.1	150.3	137.8	203.8	1.60	0.45	-10.00
2,004.0	9.30	42.40	1,988.5	155.4	142.5	210.8	0.98	0.91	2.27
2,048.0	9.70	42.80	2,031.9	160.8	147.4	218.1	0.92	0.91	0.91
2,091.0	9.90	41.10	2,074.3	166.2	152.3	225.4	0.82	0.47	-3.95
2,136.0	9.50	38.10	2,118.6	172.1	157.1	232.9	1.43	-0.89	-6.67
2,180.0	9.00	39.40	2,162.1	177.6	161.6	240.0	1.23	-1.14	2.95
2,224.0	8.60	39.20	2,205.6	182.8	165.8	246.7	0.91	-0.91	-0.45
2,268.0	9.20	38.80	2,249.0	188.1	170.1	253.5	1.37	1.36	-0.91
2,313.0	9.80	39.90	2,293.4	193.8	174.8	260.9	1.39	1.33	2.44
2,357.0	9.90	45.60	2,336.8	199.3	179.9	268.4	2.23	0.23	12.95
2,403.0	9.80	44.00	2,382.1	204.9	185.5	276.3	0.63	-0.22	-3.48
2,449.0	9.80	40.80	2,427.4	210.7	190.7	284.1	1.18	0.00	-6.96
2,495.0	9.50	38.40	2,472.8	216.6	195.7	291.8	1.09	-0.65	-5.22
2,541.0	9.50	36.30	2,518.1	222.7	200.3	299.3	0.75	0.00	-4.57
2,586.0	9.70	38.30	2,562.5	228.6	204.8	306.8	0.86	0.44	4.44
2,632.0	9.60	42.70	2,607.8	234.5	209.8	314.5	1.62	-0.22	9.57
2,676.0	10.90	43.40	2,651.1	240.2	215.2	322.3	2.97	2.95	1.59
2,720.0	12.20	43.30	2,694.3	246.6	221.2	331.1	2.95	2.95	-0.23
2,764.0	13.00	43.70	2,737.2	253.6	227.8	340.7	1.83	1.82	0.91
2,808.0	13.80	45.60	2,780.0	260.8	235.0	350.9	2.08	1.82	4.32
2,851.0	13.80	45.30	2,821.8	268.0	242.3	361.1	0.17	0.00	-0.70
2,897.0	13.80	45.10	2,866.4	275.8	250.1	372.1	0.10	0.00	-0.43
2,943.0	12.80	44.10	2,911.2	283.3	257.5	382.7	2.23	-2.17	-2.17



Payzone Directional Survey Report



Company: NEWFIELD EXPLORATION
 Project: USGS Myton SW (UT)
 Site: SECTION 6 T9S, R17E
 Well: R-6-9-17
 Wellbore: Wellbore #1
 Design: Actual

Local Co-ordinate Reference: Well R-6-9-17
 TVD Reference: R-6-9-17 @ 5316.0ft (NDSI SS #1)
 MD Reference: R-6-9-17 @ 5316.0ft (NDSI SS #1)
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Database: EDM 2003.21 Single User Db

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
2,989.0	12.30	42.80	2,956.1	290.6	264.4	392.7	1.25	-1.09	-2.83
3,035.0	12.90	41.20	3,001.0	298.0	271.1	402.7	1.51	1.30	-3.48
3,078.0	12.20	38.50	3,043.0	305.2	277.1	412.0	2.12	-1.63	-6.28
3,124.0	11.50	37.10	3,088.0	312.6	282.9	421.4	1.64	-1.52	-3.04
3,170.0	12.10	38.40	3,133.0	320.1	288.6	430.8	1.43	1.30	2.83
3,216.0	12.20	38.30	3,178.0	327.7	294.6	440.4	0.22	0.22	-0.22
3,262.0	12.00	37.00	3,223.0	335.3	300.5	450.0	0.73	-0.43	-2.83
3,306.0	11.70	35.70	3,266.0	342.6	305.9	458.9	0.91	-0.68	-2.95
3,349.0	11.80	35.70	3,308.1	349.7	311.0	467.6	0.23	0.23	0.00
3,393.0	12.00	36.10	3,351.2	357.0	316.3	476.6	0.49	0.45	0.91
3,437.0	12.10	37.60	3,394.2	364.4	321.8	485.7	0.75	0.23	3.41
3,483.0	12.20	39.60	3,439.2	372.0	327.9	495.4	0.94	0.22	4.35
3,527.0	12.10	39.70	3,482.2	379.1	333.8	504.6	0.23	-0.23	0.23
3,573.0	11.90	40.40	3,527.2	386.4	339.9	514.1	0.54	-0.43	1.52
3,619.0	11.30	40.30	3,572.2	393.5	345.9	523.4	1.31	-1.30	-0.22
3,663.0	10.80	41.80	3,615.4	399.8	351.5	531.8	1.31	-1.14	3.41
3,706.0	10.40	41.60	3,657.7	405.7	356.7	539.7	0.93	-0.93	-0.47
3,750.0	10.00	41.30	3,701.0	411.6	361.9	547.5	0.92	-0.91	-0.68
3,794.0	9.40	41.40	3,744.4	417.1	366.8	554.9	1.36	-1.36	0.23
3,838.0	9.40	45.40	3,787.8	422.3	371.7	562.1	1.48	0.00	9.09
3,884.0	9.20	47.80	3,833.2	427.5	377.1	569.5	0.95	-0.43	5.22
3,929.0	9.40	46.40	3,877.6	432.4	382.4	576.7	0.67	0.44	-3.11
3,975.0	9.50	46.70	3,923.0	437.6	387.9	584.3	0.24	0.22	0.65
4,021.0	9.40	48.20	3,968.3	442.7	393.5	591.8	0.58	-0.22	3.26
4,067.0	9.20	46.30	4,013.7	447.7	398.9	599.2	0.80	-0.43	-4.13
4,113.0	8.60	45.40	4,059.2	452.7	404.0	606.4	1.34	-1.30	-1.96
4,158.0	8.30	46.60	4,103.7	457.3	408.8	613.0	0.77	-0.67	2.67
4,204.0	8.00	47.60	4,149.2	461.7	413.6	619.5	0.72	-0.65	2.17
4,250.0	7.60	48.60	4,194.8	465.9	418.2	625.7	0.92	-0.87	2.17
4,296.0	7.40	49.70	4,240.4	469.8	422.8	631.7	0.54	-0.43	2.39
4,342.0	7.50	53.00	4,286.0	473.6	427.4	637.6	0.96	0.22	7.17
4,387.0	7.60	52.70	4,330.6	477.1	432.1	643.4	0.24	0.22	-0.67
4,433.0	8.00	50.90	4,376.2	481.0	437.0	649.6	1.02	0.87	-3.91
4,479.0	8.60	51.60	4,421.7	485.1	442.2	656.2	1.32	1.30	1.52
4,525.0	9.20	51.50	4,467.2	489.6	447.8	663.3	1.30	1.30	-0.22
4,570.0	9.50	50.10	4,511.6	494.2	453.5	670.5	0.84	0.67	-3.11
4,616.0	9.60	46.40	4,556.9	499.3	459.1	678.1	1.35	0.22	-8.04
4,662.0	9.40	46.30	4,602.3	504.5	464.6	685.7	0.44	-0.43	-0.22
4,708.0	9.20	46.60	4,647.7	509.6	470.0	693.1	0.45	-0.43	0.65
4,753.0	9.30	46.70	4,692.1	514.6	475.3	700.4	0.23	0.22	0.22
4,797.0	9.40	47.50	4,735.5	519.5	480.5	707.5	0.37	0.23	1.82
4,809.4	9.34	47.75	4,747.8	520.8	482.0	709.5	0.56	-0.46	2.01
R-6-9-17 TGT									
4,841.0	9.20	48.40	4,778.9	524.2	485.8	714.6	0.56	-0.45	2.06
4,885.0	9.20	47.40	4,822.4	528.9	491.0	721.6	0.36	0.00	-2.27
4,929.0	8.80	46.00	4,865.8	533.7	496.0	728.5	1.04	-0.91	-3.18
4,974.0	8.50	45.30	4,910.3	538.4	500.9	735.2	0.71	-0.67	-1.56
5,020.0	8.50	44.00	4,955.8	543.2	505.6	742.0	0.42	0.00	-2.83
5,064.0	8.70	45.80	4,999.3	547.9	510.3	748.6	0.76	0.45	4.09
5,108.0	9.20	46.30	5,042.8	552.6	515.2	755.5	1.15	1.14	1.14
5,152.0	9.10	46.80	5,086.2	557.5	520.3	762.5	0.29	-0.23	1.14
5,195.0	9.00	47.10	5,128.7	562.1	525.2	769.2	0.26	-0.23	0.70
5,239.0	9.00	50.10	5,172.1	566.6	530.4	776.1	1.07	0.00	6.82
5,283.0	9.40	50.70	5,215.6	571.1	535.8	783.1	0.93	0.91	1.36



Payzone Directional Survey Report



Company: NEWFIELD EXPLORATION
Project: USGS Myton SW (UT)
Site: SECTION 6 T9S, R17E
Well: R-6-9-17
Wellbore: Wellbore #1
Design: Actual

Local Co-ordinate Reference: Well R-6-9-17
TVD Reference: R-6-9-17 @ 5316.0ft (NDSI SS #1)
MD Reference: R-6-9-17 @ 5316.0ft (NDSI SS #1)
North Reference: True
Survey Calculation Method: Minimum Curvature
Database: EDM 2003.21 Single User Db

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
5,329.0	9.10	50.60	5,261.0	575.8	541.5	790.4	0.65	-0.65	-0.22
5,375.0	8.30	52.50	5,306.5	580.1	547.0	797.3	1.85	-1.74	4.13
5,421.0	7.70	54.70	5,352.0	583.9	552.1	803.6	1.46	-1.30	4.78
5,466.0	7.80	54.50	5,396.6	587.4	557.1	809.6	0.23	0.22	-0.44
5,512.0	8.10	54.10	5,442.2	591.2	562.3	815.8	0.66	0.65	-0.87
5,558.0	7.80	48.70	5,487.7	595.1	567.2	822.1	1.75	-0.65	-11.74
5,604.0	8.30	48.80	5,533.3	599.4	572.1	828.5	1.09	1.09	0.22
5,650.0	8.70	48.80	5,578.8	603.8	577.2	835.3	0.87	0.87	0.00
5,695.0	8.40	49.50	5,623.3	608.2	582.2	842.0	0.71	-0.67	1.56
5,741.0	8.50	48.70	5,668.8	612.6	587.4	848.7	0.34	0.22	-1.74
5,787.0	9.10	48.20	5,714.2	617.3	592.6	855.7	1.31	1.30	-1.09
5,833.0	8.80	47.00	5,759.7	622.1	597.9	862.9	0.77	-0.65	-2.61
5,878.0	8.60	47.00	5,804.1	626.8	602.9	869.7	0.44	-0.44	0.00
5,922.0	8.60	46.30	5,847.6	631.3	607.7	876.2	0.24	0.00	-1.59
5,966.0	8.30	44.90	5,891.2	635.8	612.3	882.7	0.83	-0.68	-3.18
6,010.0	8.50	44.50	5,934.7	640.4	616.8	889.1	0.47	0.45	-0.91
6,054.0	8.70	42.60	5,978.2	645.2	621.3	895.7	0.79	0.45	-4.32
6,097.0	8.10	43.00	6,020.7	649.8	625.6	902.0	1.40	-1.40	0.93
6,121.0	7.60	43.30	6,044.5	652.2	627.8	905.3	2.09	-2.08	1.25
6,175.0	7.60	43.30	6,098.0	657.4	↔ 632.7	912.4	0.00	0.00	0.00

Checked By: _____ Approved By: _____ Date: _____





Project: USGS Myton SW (UT)
 Site: SECTION 6 T9S, R17E
 Well: R-6-9-17
 Wellbore: Wellbore #1
 Design: Actual




Azimuths to True North
 Magnetic North: 11.39°

Magnetic Field
 Strength: 52338.0snT
 Dip Angle: 65.82°
 Date: 11/11/2010
 Model: IGRF2010

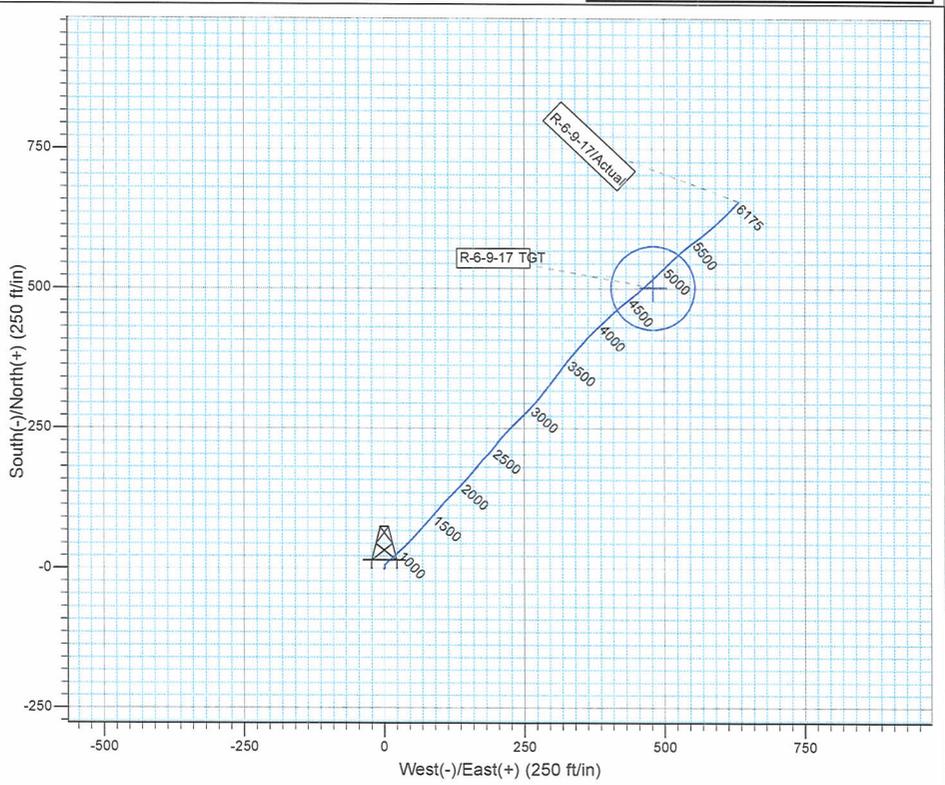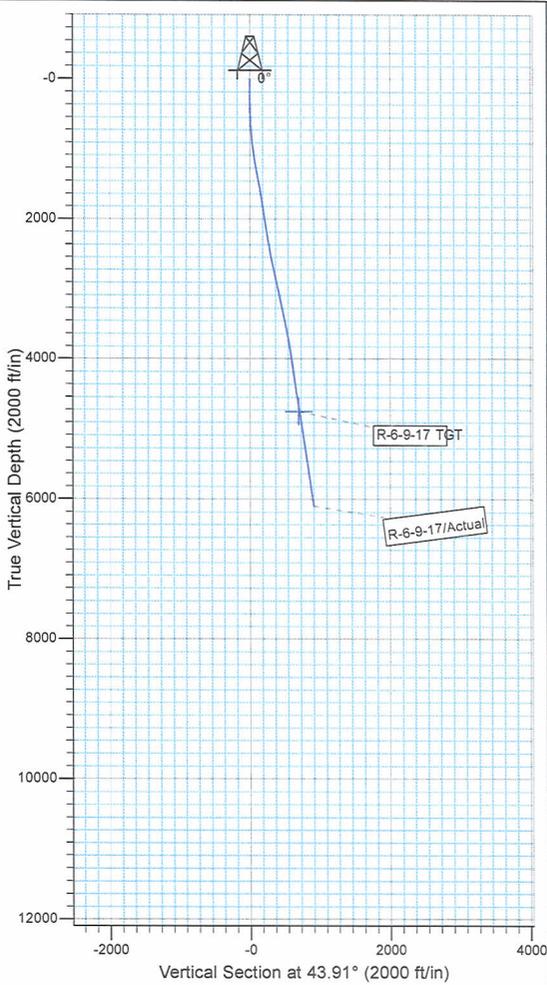

Design: Actual (R-6-9-17/Wellbore #1)
 Created By: Sarah Webb Date: 18:11, May 23 2012
 THIS SURVEY IS CORRECT TO THE BEST OF
 MY KNOWLEDGE AND IS SUPPORTED
 BY ACTUAL FIELD DATA

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9	
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-020252A	
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:	
1. TYPE OF WELL Oil Well		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)	
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		8. WELL NAME and NUMBER: GREATER MON BUTTE R-6-9-17	
3. ADDRESS OF OPERATOR: 1001 17th Street, Suite 2000 , Denver, CO, 80202		9. API NUMBER: 43013505810000	
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1108 FSL 2123 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SESW Section: 06 Township: 09.0S Range: 17.0E Meridian: S		9. FIELD and POOL or WILDCAT: MONUMENT BUTTE	
		COUNTY: DUCHESNE	
		STATE: UTAH	
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA			
TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: <input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 6/24/2013 <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input checked="" type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text" value="Site Facility/Site Security"/>
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.			
SEE ATTACHED REVISED SITE FACILITY DIAGRAM			
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY August 09, 2013			
NAME (PLEASE PRINT) Jill L Loyle		PHONE NUMBER 303 383-4135	TITLE Regulatory Technician
SIGNATURE N/A		DATE 6/24/2013	

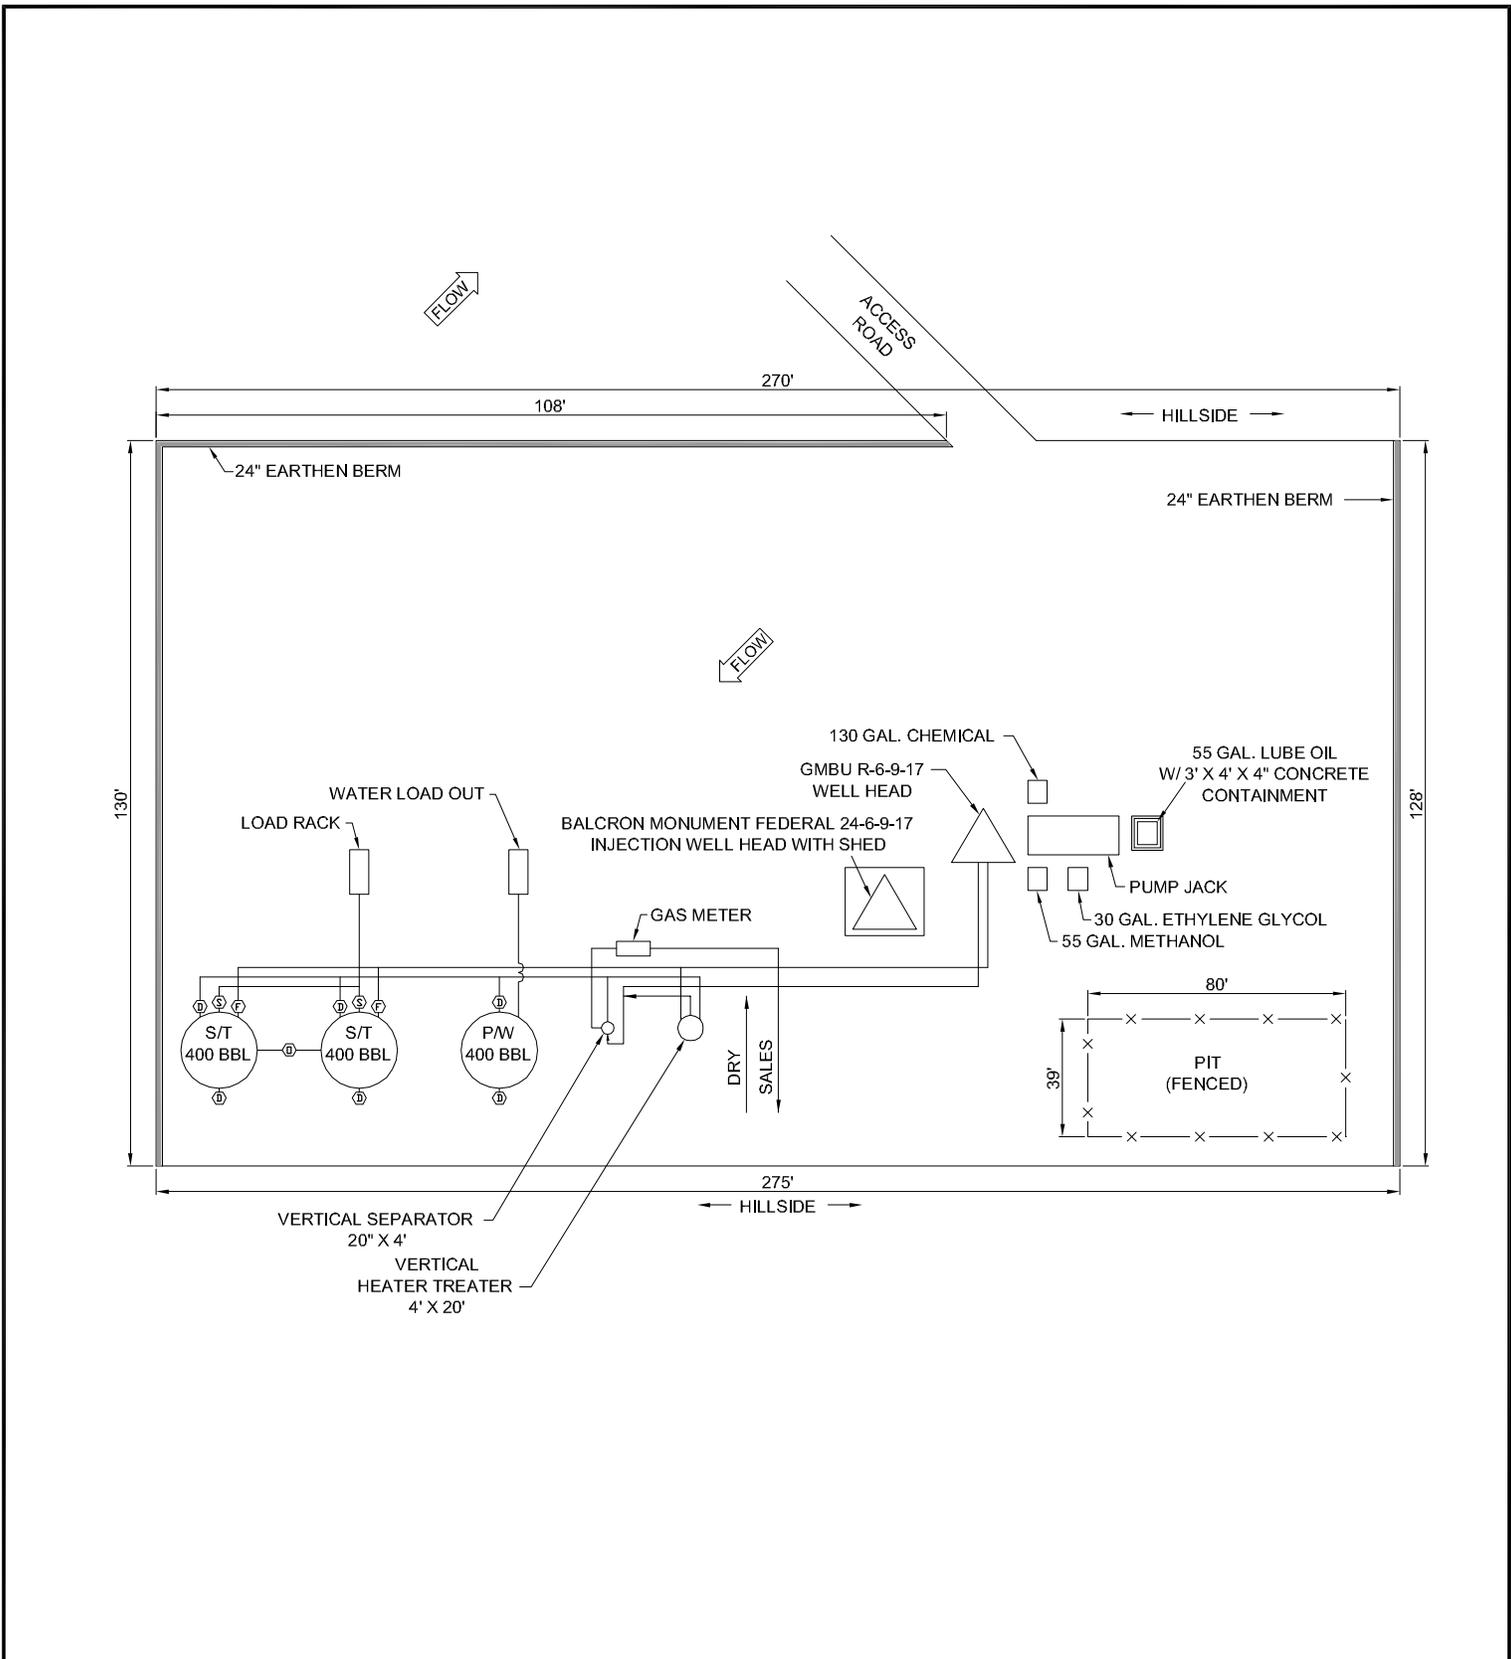

POSITION OF VALVES AND USE OF SEALS DURING PRODUCTION			
Valve	Line Purpose	Position	Seal Installed
D	Drain	Closed	Yes
F	Oil, Gas, Water	Open	No
O	Overflow	Open/Closed	No
V	Vent	Open	No
R	Recycle	Closed	Yes
B	Blowdown	Open/Closed	No
S	Sales	Closed	Yes

Valve Type	
D	- Drain Valve
F	- Flow Valve
O	- Overflow
V	- Vent
R	- Recycle
B	- Blow Down
S	- Sales Valve

Federal Lease #: UTU-87538X
 API #:
 This lease is subject to the
 Site Security Plan for:
 Newfield Exploration Company
 19 East Pine Street
 Pinedale, WY 82941



**BALCRON MONUMENT FEDERAL 24-6-9-17
 AND GMBU R-6-9-17**

**Newfield Exploration Company
 SESW Sec 6, T9S, R17E
 Duchesne County, UT**

POSITION OF VALVES AND USE OF SEALS DURING SALES			
Valve	Line Purpose	Position	Seal Installed
D	Drain	Closed	Yes
F	Oil, Gas, Water	Closed	Yes
O	Overflow	Closed	Yes
V	Vent	Open	No
R	Recycle	Closed	Yes
B	Blowdown	Closed	No
S	Sales	Open	No

POSITION OF VALVES AND USE OF SEALS DURING WATER DRAIN			
Valve	Line Purpose	Position	Seal Installed
D	Drain	Open	No
F	Oil, Gas, Water	Closed	No
O	Overflow	Closed	No
V	Vent	Open	No
R	Recycle	Closed	Yes
B	Blowdown	Closed	No
S	Sales	Closed	Yes

M.G.

SEPT 2012

Note: This drawing represents approximate sizes and distances. Underground pipeline locations are also approximated.



STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-020252A
---	--

SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
--	---

1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: GREATER MON BUTTE R-6-9-17
-----------------------------	--

2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	9. API NUMBER: 43013505810000
---	----------------------------------

3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext	9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
---	-----------------------------------	---

4. LOCATION OF WELL FOOTAGES AT SURFACE: 1108 FSL 2123 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SESW Section: 06 Township: 09.0S Range: 17.0E Meridian: S	COUNTY: DUCHESNE STATE: UTAH
--	---

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 11/19/2013 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input checked="" type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input type="text" value="OAP to Current Formation"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Newfield proposes to perforate and fracture stimulate the following:
 B-2 5034-5046 and A-3 5228-5272 with in the current production formation (Green River).

Accepted by the Utah Division of Oil, Gas and Mining

Date: December 16, 2013

By: *Derek Quist*

NAME (PLEASE PRINT) Mandie Crozier	PHONE NUMBER 435 646-4825	TITLE Regulatory Tech
SIGNATURE N/A	DATE 11/19/2013	
