


STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS AND MINING						FORM 3 AMENDED REPORT <input type="checkbox"/>				
<b>APPLICATION FOR PERMIT TO DRILL</b>						1. WELL NAME and NUMBER GMBU I-12-9-15				
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT MONUMENT BUTTE				
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO						5. UNIT or COMMUNITIZATION AGREEMENT NAME GMBU (GRRV)				
6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY						7. OPERATOR PHONE 435 646-4825				
8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052						9. OPERATOR E-MAIL mcrozier@newfield.com				
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU-74826			11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>				
13. NAME OF SURFACE OWNER (if box 12 = 'fee')						14. SURFACE OWNER PHONE (if box 12 = 'fee')				
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')				
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>			19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/>				
20. LOCATION OF WELL	FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN			
LOCATION AT SURFACE	1869 FNL 1870 FEL		SWNE	12	9.0 S	15.0 E	S			
Top of Uppermost Producing Zone	1509 FNL 1320 FEL		SWNE	12	9.0 S	15.0 E	S			
At Total Depth	1205 FNL 818 FEL		NENE	12	9.0 S	15.0 E	S			
21. COUNTY DUCHESNE			22. DISTANCE TO NEAREST LEASE LINE (Feet) 818		23. NUMBER OF ACRES IN DRILLING UNIT 20					
			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 949		26. PROPOSED DEPTH MD: 6247 TVD: 6100					
27. ELEVATION - GROUND LEVEL 6017			28. BOND NUMBER WYB000493		29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 437478					
<b>Hole, Casing, and Cement Information</b>										
String	Hole Size	Casing Size	Length	Weight	Grade & Thread	Max Mud Wt.	Cement	Sacks	Yield	Weight
Surf	12.25	8.625	0 - 300	24.0	J-55 ST&C	8.3	Class G	138	1.17	15.8
Prod	7.875	5.5	0 - 6247	15.5	J-55 LT&C	8.3	Premium Lite High Strength	293	3.26	11.0
							50/50 Poz	363	1.24	14.3
<b>ATTACHMENTS</b>										
<b>VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES</b>										
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER					<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN					
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)					<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER					
<input checked="" type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)					<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP					
NAME Mandie Crozier				TITLE Regulatory Tech			PHONE 435 646-4825			
SIGNATURE				DATE 10/04/2012			EMAIL mcrozier@newfield.com			
API NUMBER ASSIGNED 43013517540000				APPROVAL  Permit Manager						

NEWFIELD PRODUCTION COMPANY  
GMBU I-12-9-15  
AT SURFACE: SW/NE SECTION 12, T9S R15E  
DUCHESNE COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0' – 1680'
Green River	1680'
Wasatch	6360'
<b>Proposed TD</b>	<b>6247'</b>

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil)      1680' – 6360'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sampled Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO <sub>3</sub> ) (mg/l)
Dissolved Bicarbonate (NaHCO <sub>3</sub> ) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO <sub>4</sub> ) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

#### 4. **PROPOSED CASING PROGRAM**

##### a. Casing Design: GMBU I-12-9-15

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950 17.53	1,370 14.35	244,000 33.89
Prod casing 5-1/2"	0'	6,247'	15.5	J-55	LTC	4,810 2.42	4,040 2.03	217,000 2.24

##### Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg  
 Pore pressure at surface casing shoe = 8.33 ppg  
 Pore pressure at prod casing shoe = 8.33 ppg  
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

##### b. Cementing Design: GMBU I-12-9-15

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft <sup>3</sup> /sk)
			ft <sup>3</sup>			
Surface casing	300'	Class G w/ 2% CaCl	138 161	30%	15.8	1.17
Prod casing Lead	4,247'	Prem Lite II w/ 10% gel + 3% KCl	293 957	30%	11.0	3.26
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363 451	30%	14.3	1.24

\*Actual volume pumped will be 15% over the caliper log

- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

#### 5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to  $\pm 300$  feet will be drilled with an air/mist system. The air rig is equipped with a 6 1/2" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about  $\pm 300$  feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated

bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.


10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the first quarter of 2013, and take approximately seven (7) days from spud to rig release.

**T9S, R15E, S.L.B.&M.****NEWFIELD EXPLORATION COMPANY**


WELL LOCATION, I-12-9-15, LOCATED AS SHOWN IN THE SW 1/4 NE 1/4 OF SECTION 12, T9S, R15E, S.L.B.&M. DUCHESNE COUNTY, UTAH.

TARGET BOTTOM HOLE, I-12-9-15, LOCATED AS SHOWN IN THE NE 1/4 NE 1/4 OF SECTION 12, T9S, R15E, S.L.B.&M. DUCHESNE COUNTY, UTAH.

**NOTES:**


1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

**TRI STATE LAND SURVEYING & CONSULTING**

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078  
(435) 781-2501

DATE SURVEYED: 03-07-12	SURVEYED BY: M.C.	VERSION:
DATE DRAWN: 07-06-12	DRAWN BY: F.T.M.	V2
REVISED:	SCALE: 1" = 1000'	

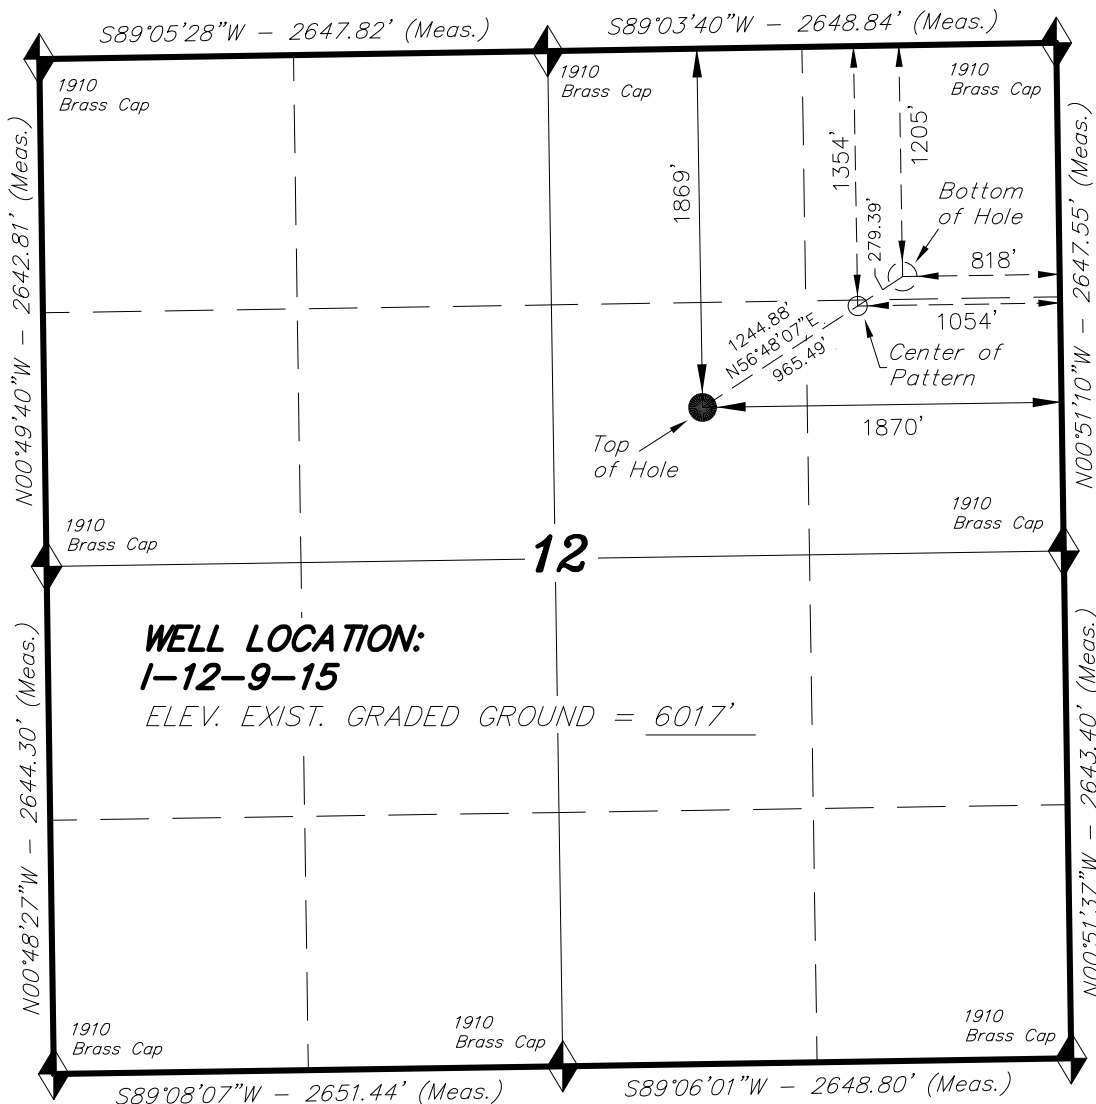


= SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are based on an N.G.S. OPUS Correction. LOCATION: LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'

<b>NAD 83 (SURFACE LOCATION)</b>
LATITUDE = 40°02'51.25"
LONGITUDE = 110°10'39.78"
<b>NAD 27 (SURFACE LOCATION)</b>
LATITUDE = 40°02'51.39"
LONGITUDE = 110°10'37.23"
<b>NAD 83 (BOTTOM HOLE LOCATION)</b>
LATITUDE = 40°02'57.83"
LONGITUDE = 110°10'26.26"
<b>NAD 27 (BOTTOM HOLE LOCATION)</b>
LATITUDE = 40°02'57.97"
LONGITUDE = 110°10'23.71"



## Access Road Map

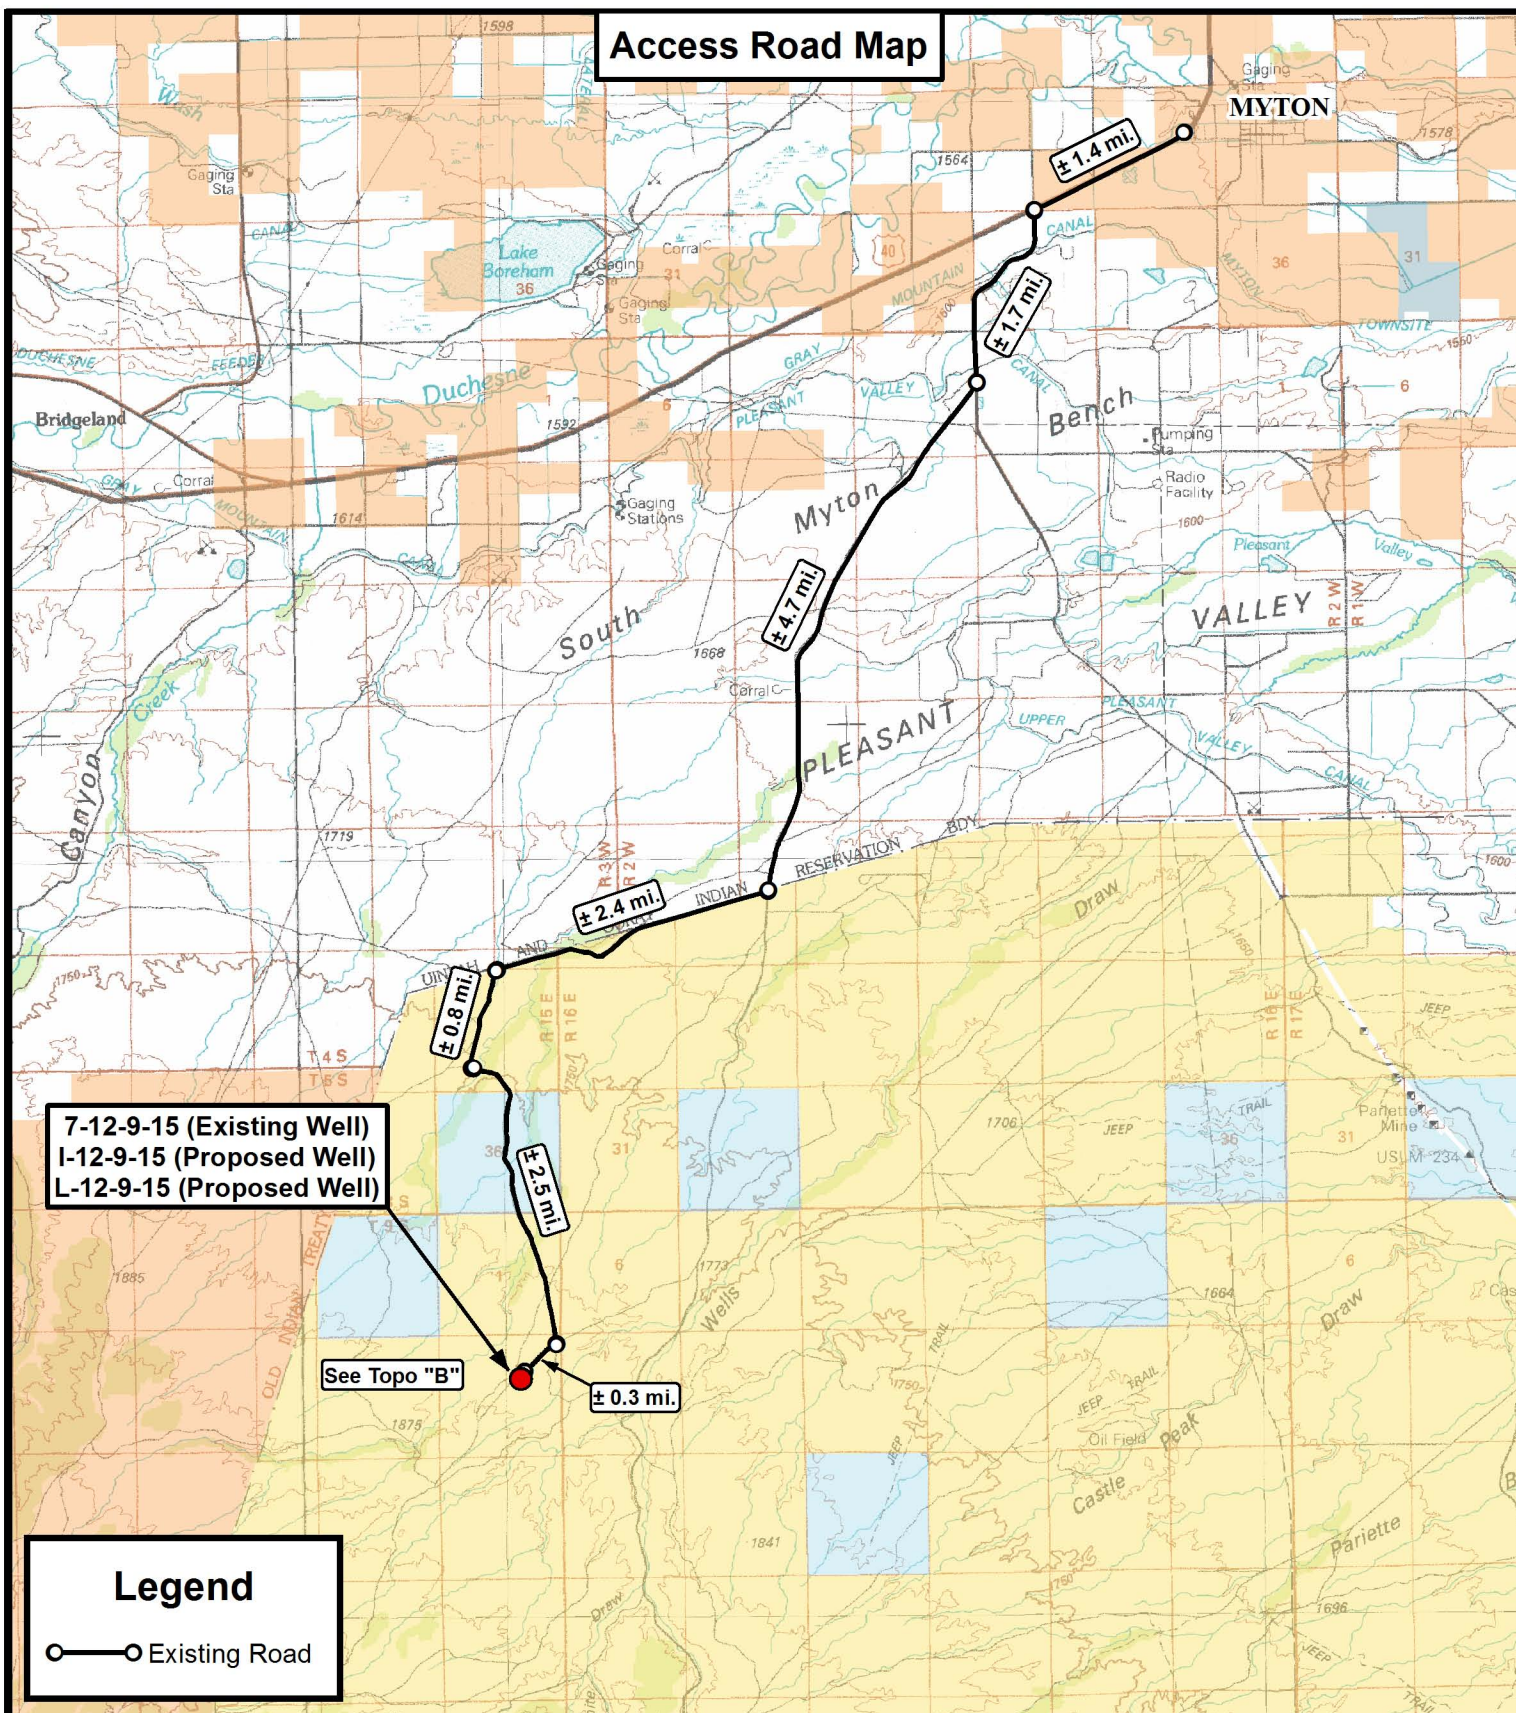

**Tri State  
Land Surveying, Inc.**

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501  
F: (435) 781-2518



## NEWFIELD EXPLORATION COMPANY

7-12-9-15 (Existing Well)

I-12-9-15 (Proposed Well)

L-12-9-15 (Proposed Well)

SEC. 12, T9S, R15E, S.L.B.&M. Duchesne County, UT.


DRAWN BY:	A.P.C.	REVISED:	VERSION:
DATE:	07-06-2012		V2
SCALE:	1:100,000		

**TOPOGRAPHIC MAP**

SHEET

**A**



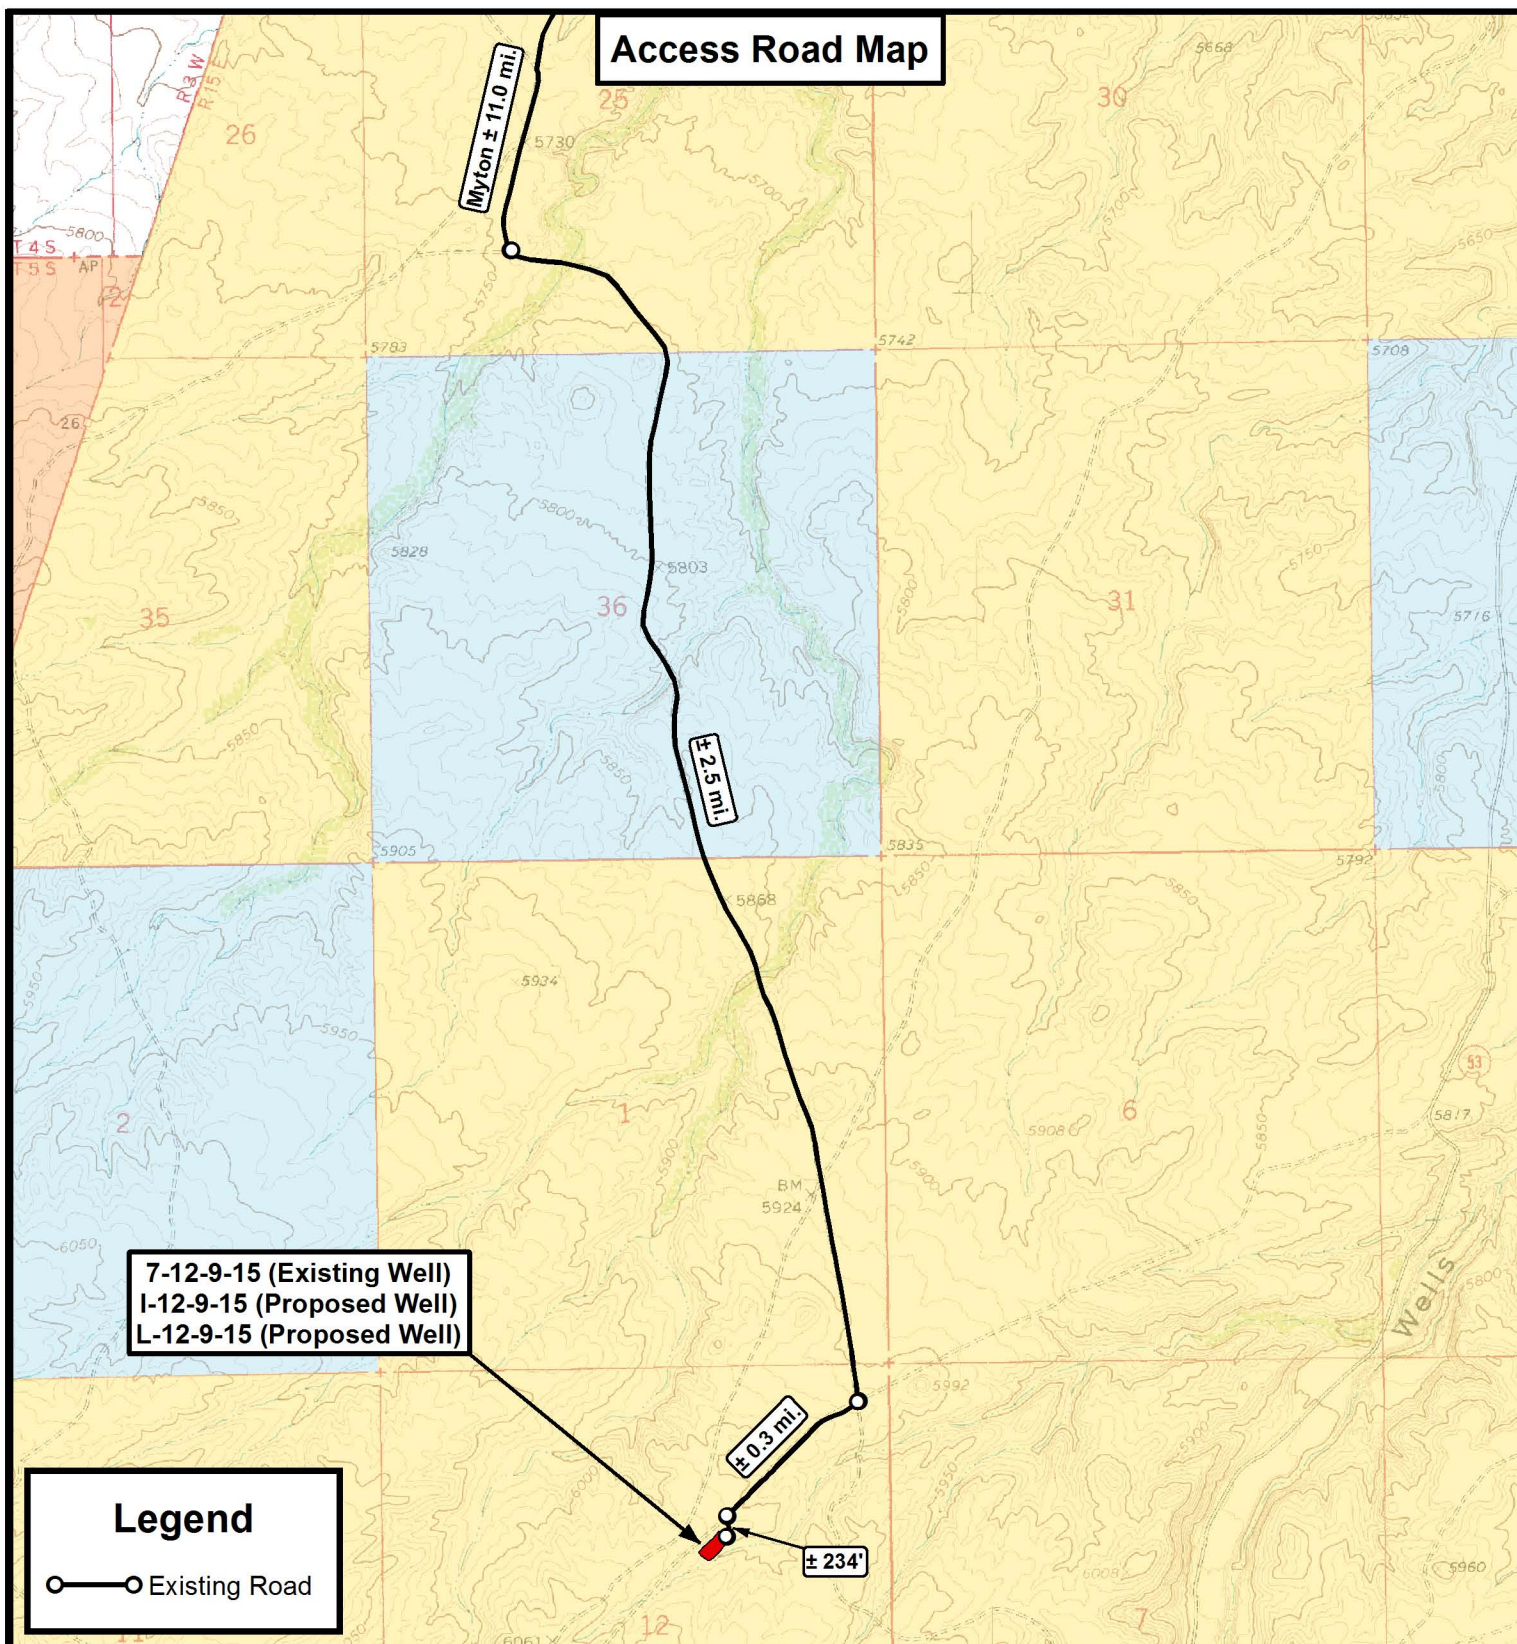

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.

**Tri State**  
Land Surveying, Inc.  
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501  
F: (435) 781-2518



## NEWFIELD EXPLORATION COMPANY

7-12-9-15 (Existing Well)  
I-12-9-15 (Proposed Well)  
L-12-9-15 (Proposed Well)  
SEC. 12, T9S, R15E, S.L.B.&M. Duchesne County, UT.


DRAWN BY:	A.P.C.	REVISED:	07-06-12 A.P.C.	VERSION:
DATE:	03-12-2012			V2
SCALE:	1" = 2,000'			

**TOPOGRAPHIC MAP**

SHEET  
**B**



# Proposed Pipeline Map

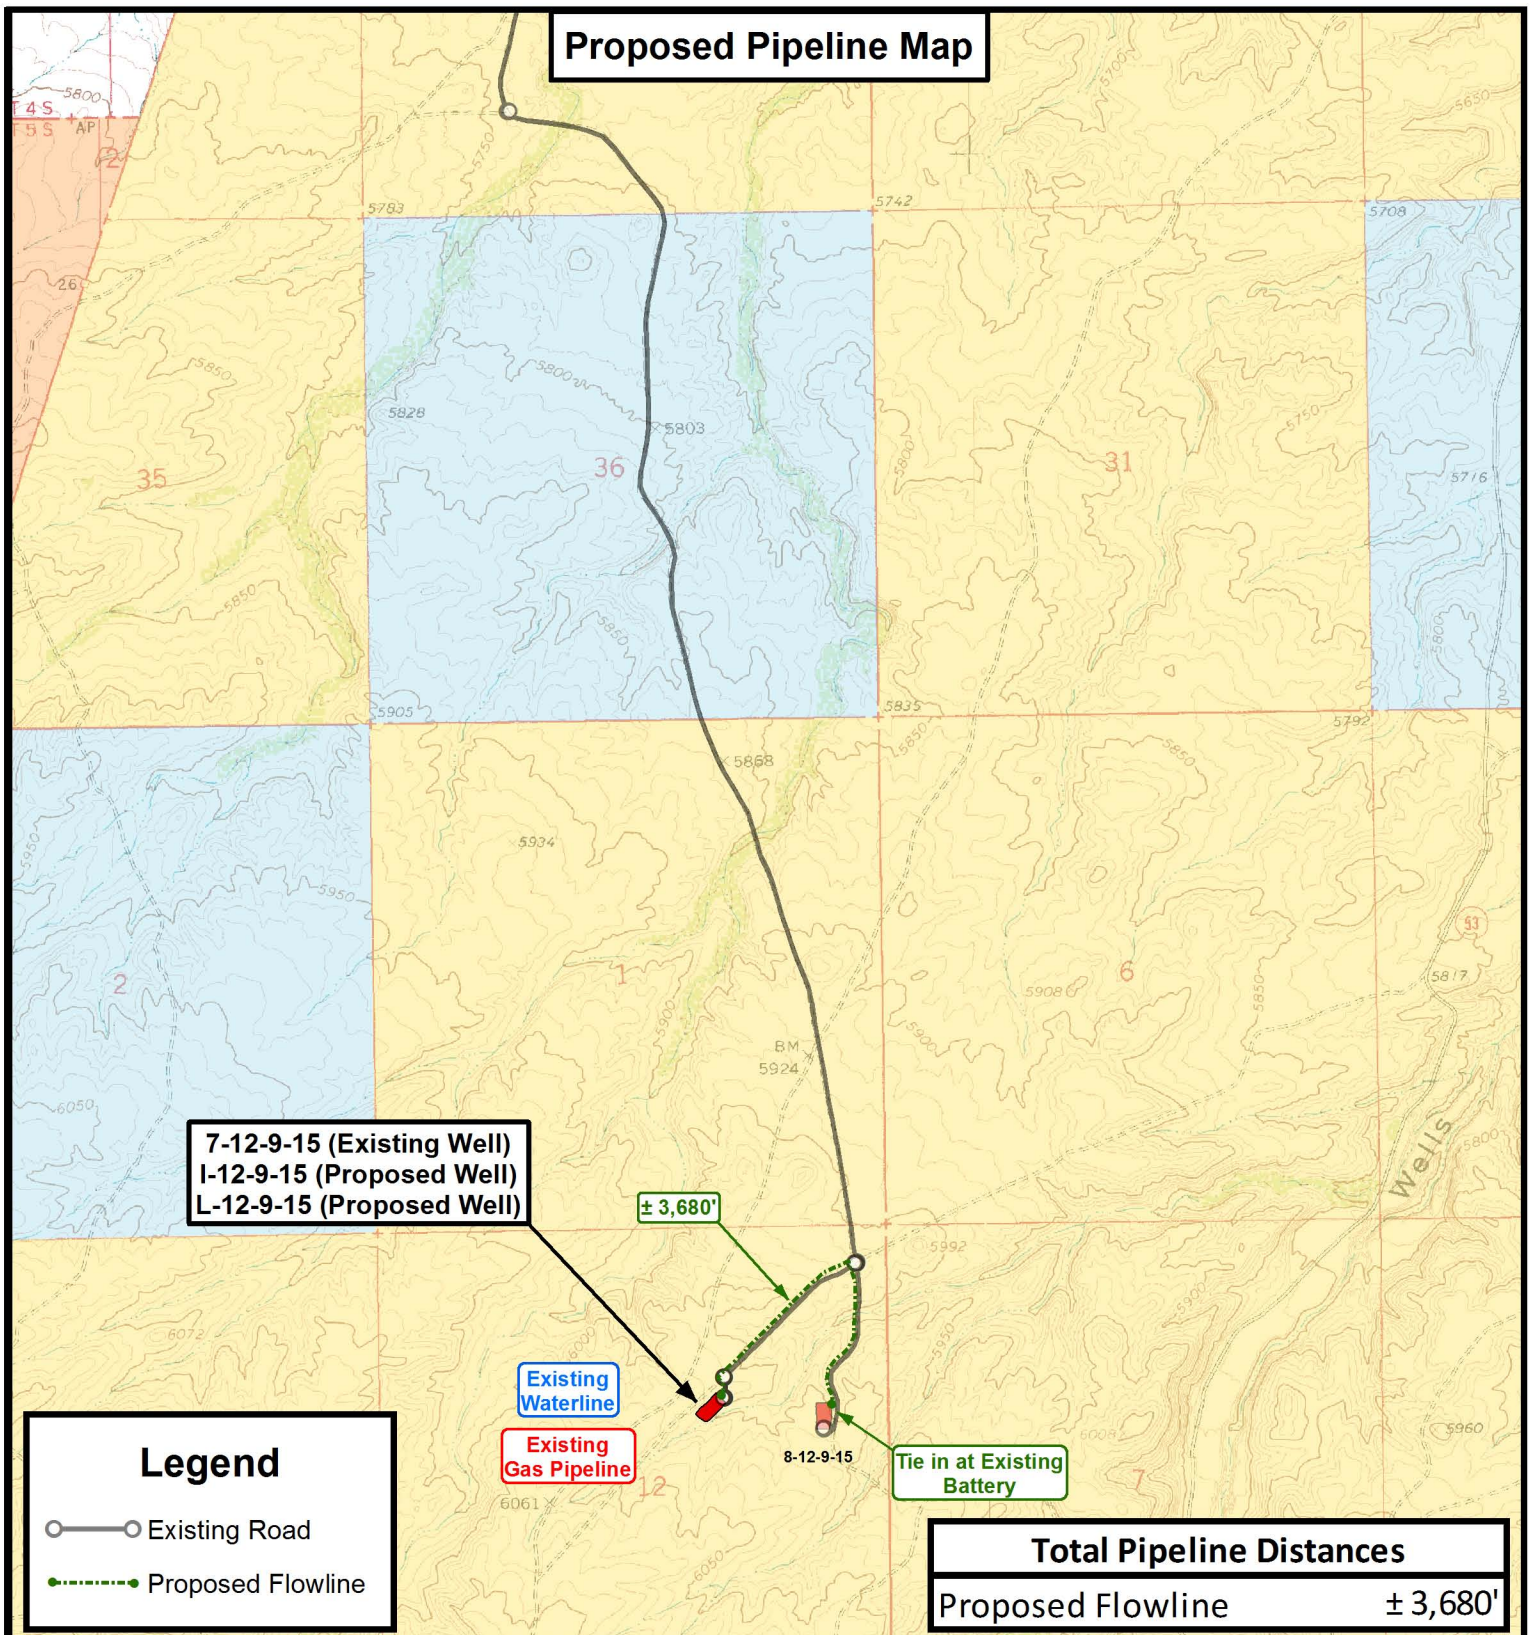

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.

**Tri State**  
**Land Surveying, Inc.**  
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501  
 F: (435) 781-2518



## NEWFIELD EXPLORATION COMPANY

7-12-9-15 (Existing Well)  
 I-12-9-15 (Proposed Well)  
 L-12-9-15 (Proposed Well)  
 SEC. 12, T9S, R15E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	A.P.C.	REVISED:	07-06-12 A.P.C.	VERSION:
DATE:	03-12-2012			V2
SCALE:	1" = 2,000'			

**TOPOGRAPHIC MAP**


SHEET

**C**



**Exhibit "B" Map**

7-12-9-15 (Existing Well)  
 I-12-9-15 (Proposed Well)  
 L-12-9-15 (Proposed Well)

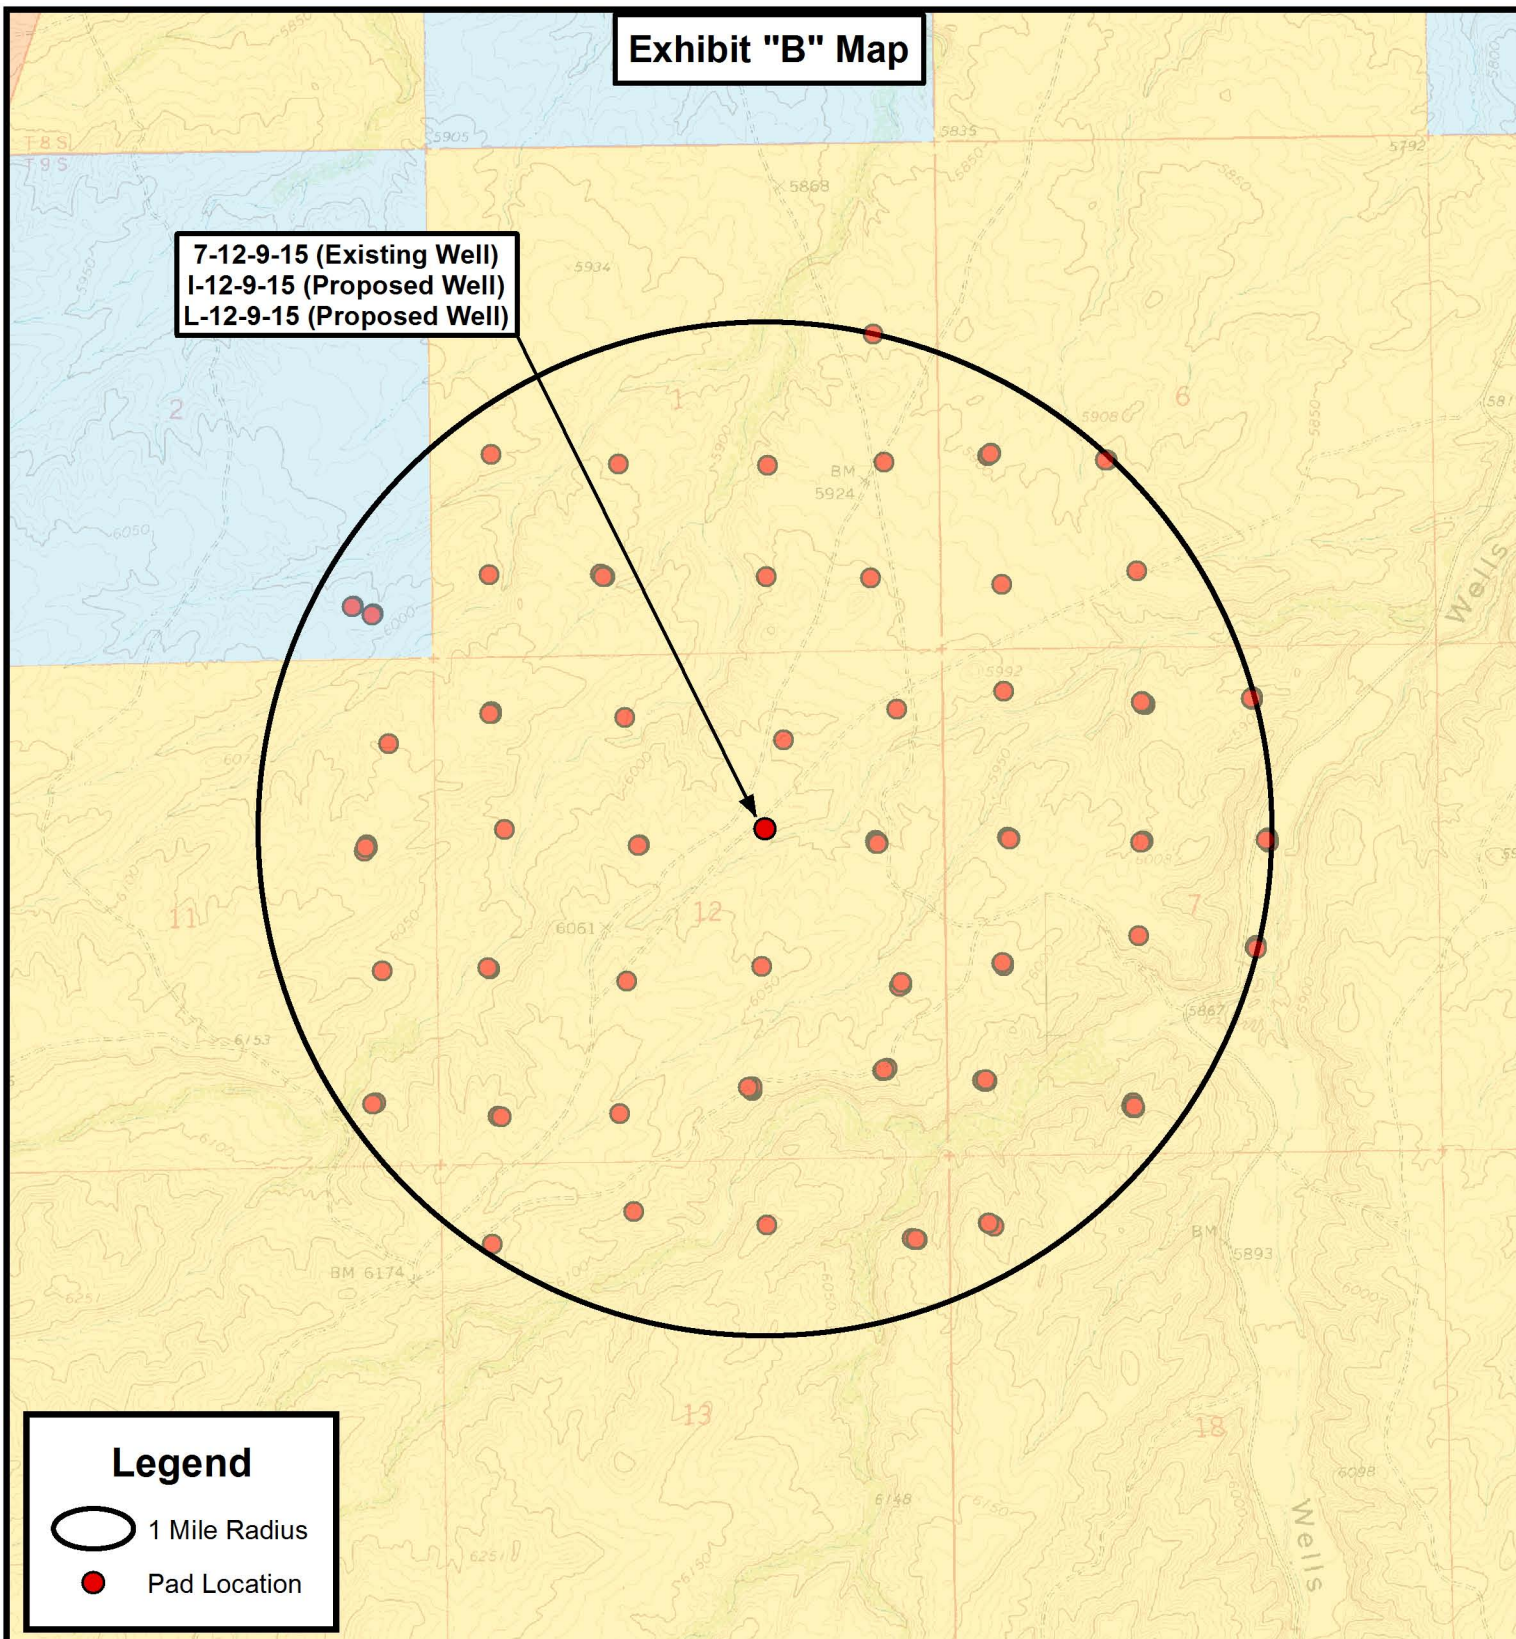

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501  
 F: (435) 781-2518

**NEWFIELD EXPLORATION COMPANY**

7-12-9-15 (Existing Well)  
 I-12-9-15 (Proposed Well)  
 L-12-9-15 (Proposed Well)  
 SEC. 12, T9S, R15E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	A.P.C.	REVISED:	VERSION:
DATE:	07-06-2012		<b>V2</b>
SCALE:	1" = 2,000'		

**TOPOGRAPHIC MAP**

SHEET

**D**



# **NEWFIELD EXPLORATION**

**USGS Myton SW (UT)  
SECTION 12 T9S, R15E  
I-12-9-15**

**Wellbore #1**

**Plan: Design #1**

## **Standard Planning Report**

**27 June, 2012**







## Payzone Directional Planning Report



<b>Database:</b>	EDM 2003.21 Single User Db	<b>Local Co-ordinate Reference:</b>	Well I-12-9-15
<b>Company:</b>	NEWFIELD EXPLORATION	<b>TVD Reference:</b>	I-12-9-15 @ 6029.0ft (Original Well Elev)
<b>Project:</b>	USGS Myton SW (UT)	<b>MD Reference:</b>	I-12-9-15 @ 6029.0ft (Original Well Elev)
<b>Site:</b>	SECTION 12 T9S, R15E	<b>North Reference:</b>	True
<b>Well:</b>	I-12-9-15	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

<b>Project</b>	USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA		
<b>Map System:</b>	US State Plane 1983	<b>System Datum:</b>	Mean Sea Level
<b>Geo Datum:</b>	North American Datum 1983		
<b>Map Zone:</b>	Utah Central Zone		

<b>Site</b>	SECTION 12 T9S, R15E			
<b>Site Position:</b>		<b>Northing:</b>	7,188,000.00 ft	<b>Latitude:</b> 40° 2' 43.749 N
<b>From:</b> Map		<b>Easting:</b>	2,008,669.32 ft	<b>Longitude:</b> 110° 11' 4.317 W
<b>Position Uncertainty:</b>	0.0 ft	<b>Slot Radius:</b>	"	<b>Grid Convergence:</b> 0.84 °

<b>Well</b>	I-12-9-15, SHL LAT: 40 02 51.25 LONG: -110 10 39.78			
<b>Well Position</b>	<b>+N/-S</b>	758.9 ft	<b>Northing:</b>	7,188,787.04 ft
	<b>+E/-W</b>	1,908.1 ft	<b>Easting:</b>	2,010,565.96 ft
<b>Position Uncertainty</b>		0.0 ft	<b>Wellhead Elevation:</b>	6,029.0 ft
			<b>Ground Level:</b>	6,017.0 ft

<b>Wellbore</b>	Wellbore #1				
<b>Magnetics</b>	<b>Model Name</b>	<b>Sample Date</b>	<b>Declination (°)</b>	<b>Dip Angle (°)</b>	<b>Field Strength (nT)</b>
	IGRF2010	6/27/2012	11.23	65.75	52,149

<b>Design</b>	Design #1			
<b>Audit Notes:</b>				
<b>Version:</b>	<b>Phase:</b>	PROTOTYPE	<b>Tie On Depth:</b>	0.0
<b>Vertical Section:</b>	<b>Depth From (TVD) (ft)</b>	<b>+N/-S (ft)</b>	<b>+E/-W (ft)</b>	<b>Direction (°)</b>
	0.0	0.0	0.0	56.80

<b>Plan Sections</b>										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.00	0.00	0.00	0.00	
1,525.9	13.89	56.80	1,516.9	61.1	93.4	1.50	1.50	0.00	56.80	
5,083.0	13.89	56.80	4,970.0	528.6	807.9	0.00	0.00	0.00	0.00	I-12-9-15 TGT
6,247.1	13.89	56.80	6,100.0	681.6	1,041.7	0.00	0.00	0.00	0.00	



## Payzone Directional

## Planning Report



<b>Database:</b>	EDM 2003.21 Single User Db	<b>Local Co-ordinate Reference:</b>	Well I-12-9-15
<b>Company:</b>	NEWFIELD EXPLORATION	<b>TVD Reference:</b>	I-12-9-15 @ 6029.0ft (Original Well Elev)
<b>Project:</b>	USGS Myton SW (UT)	<b>MD Reference:</b>	I-12-9-15 @ 6029.0ft (Original Well Elev)
<b>Site:</b>	SECTION 12 T9S, R15E	<b>North Reference:</b>	True
<b>Well:</b>	I-12-9-15	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	1.50	56.80	700.0	0.7	1.1	1.3	1.50	1.50	0.00
800.0	3.00	56.80	799.9	2.9	4.4	5.2	1.50	1.50	0.00
900.0	4.50	56.80	899.7	6.4	9.9	11.8	1.50	1.50	0.00
1,000.0	6.00	56.80	999.3	11.5	17.5	20.9	1.50	1.50	0.00
1,100.0	7.50	56.80	1,098.6	17.9	27.3	32.7	1.50	1.50	0.00
1,200.0	9.00	56.80	1,197.5	25.7	39.4	47.0	1.50	1.50	0.00
1,300.0	10.50	56.80	1,296.1	35.0	53.5	64.0	1.50	1.50	0.00
1,400.0	12.00	56.80	1,394.2	45.7	69.8	83.5	1.50	1.50	0.00
1,500.0	13.50	56.80	1,491.7	57.8	88.3	105.5	1.50	1.50	0.00
1,525.9	13.89	56.80	1,516.9	61.1	93.4	111.7	1.50	1.50	0.00
1,600.0	13.89	56.80	1,588.8	70.9	108.3	129.5	0.00	0.00	0.00
1,700.0	13.89	56.80	1,685.9	84.0	128.4	153.5	0.00	0.00	0.00
1,800.0	13.89	56.80	1,782.9	97.2	148.5	177.5	0.00	0.00	0.00
1,900.0	13.89	56.80	1,880.0	110.3	168.6	201.5	0.00	0.00	0.00
2,000.0	13.89	56.80	1,977.1	123.5	188.7	225.5	0.00	0.00	0.00
2,100.0	13.89	56.80	2,074.2	136.6	208.8	249.5	0.00	0.00	0.00
2,200.0	13.89	56.80	2,171.3	149.7	228.8	273.5	0.00	0.00	0.00
2,300.0	13.89	56.80	2,268.3	162.9	248.9	297.5	0.00	0.00	0.00
2,400.0	13.89	56.80	2,365.4	176.0	269.0	321.5	0.00	0.00	0.00
2,500.0	13.89	56.80	2,462.5	189.2	289.1	345.5	0.00	0.00	0.00
2,600.0	13.89	56.80	2,559.6	202.3	309.2	369.5	0.00	0.00	0.00
2,700.0	13.89	56.80	2,656.6	215.4	329.3	393.5	0.00	0.00	0.00
2,800.0	13.89	56.80	2,753.7	228.6	349.4	417.5	0.00	0.00	0.00
2,900.0	13.89	56.80	2,850.8	241.7	369.4	441.5	0.00	0.00	0.00
3,000.0	13.89	56.80	2,947.9	254.9	389.5	465.5	0.00	0.00	0.00
3,100.0	13.89	56.80	3,044.9	268.0	409.6	489.5	0.00	0.00	0.00
3,200.0	13.89	56.80	3,142.0	281.2	429.7	513.5	0.00	0.00	0.00
3,300.0	13.89	56.80	3,239.1	294.3	449.8	537.5	0.00	0.00	0.00
3,400.0	13.89	56.80	3,336.2	307.4	469.9	561.5	0.00	0.00	0.00
3,500.0	13.89	56.80	3,433.2	320.6	489.9	585.5	0.00	0.00	0.00
3,600.0	13.89	56.80	3,530.3	333.7	510.0	609.5	0.00	0.00	0.00
3,700.0	13.89	56.80	3,627.4	346.9	530.1	633.5	0.00	0.00	0.00
3,800.0	13.89	56.80	3,724.5	360.0	550.2	657.5	0.00	0.00	0.00
3,900.0	13.89	56.80	3,821.6	373.2	570.3	681.5	0.00	0.00	0.00
4,000.0	13.89	56.80	3,918.6	386.3	590.4	705.5	0.00	0.00	0.00
4,100.0	13.89	56.80	4,015.7	399.4	610.5	729.5	0.00	0.00	0.00
4,200.0	13.89	56.80	4,112.8	412.6	630.5	753.5	0.00	0.00	0.00
4,300.0	13.89	56.80	4,209.9	425.7	650.6	777.5	0.00	0.00	0.00
4,400.0	13.89	56.80	4,306.9	438.9	670.7	801.5	0.00	0.00	0.00
4,500.0	13.89	56.80	4,404.0	452.0	690.8	825.5	0.00	0.00	0.00
4,600.0	13.89	56.80	4,501.1	465.2	710.9	849.5	0.00	0.00	0.00
4,700.0	13.89	56.80	4,598.2	478.3	731.0	873.6	0.00	0.00	0.00
4,800.0	13.89	56.80	4,695.2	491.4	751.1	897.6	0.00	0.00	0.00
4,900.0	13.89	56.80	4,792.3	504.6	771.1	921.6	0.00	0.00	0.00
5,000.0	13.89	56.80	4,889.4	517.7	791.2	945.6	0.00	0.00	0.00
5,083.0	13.89	56.80	4,970.0	528.6	807.9	965.5	0.00	0.00	0.00
5,100.0	13.89	56.80	4,986.5	530.9	811.3	969.6	0.00	0.00	0.00



## Payzone Directional

## Planning Report



<b>Database:</b>	EDM 2003.21 Single User Db	<b>Local Co-ordinate Reference:</b>	Well I-12-9-15
<b>Company:</b>	NEWFIELD EXPLORATION	<b>TVD Reference:</b>	I-12-9-15 @ 6029.0ft (Original Well Elev)
<b>Project:</b>	USGS Myton SW (UT)	<b>MD Reference:</b>	I-12-9-15 @ 6029.0ft (Original Well Elev)
<b>Site:</b>	SECTION 12 T9S, R15E	<b>North Reference:</b>	True
<b>Well:</b>	I-12-9-15	<b>Survey Calculation Method:</b>	Minimum Curvature
<b>Wellbore:</b>	Wellbore #1		
<b>Design:</b>	Design #1		


Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
5,200.0	13.89	56.80	5,083.5	544.0	831.4	993.6	0.00	0.00	0.00
5,300.0	13.89	56.80	5,180.6	557.2	851.5	1,017.6	0.00	0.00	0.00
5,400.0	13.89	56.80	5,277.7	570.3	871.6	1,041.6	0.00	0.00	0.00
5,500.0	13.89	56.80	5,374.8	583.4	891.7	1,065.6	0.00	0.00	0.00
5,600.0	13.89	56.80	5,471.9	596.6	911.7	1,089.6	0.00	0.00	0.00
5,700.0	13.89	56.80	5,568.9	609.7	931.8	1,113.6	0.00	0.00	0.00
5,800.0	13.89	56.80	5,666.0	622.9	951.9	1,137.6	0.00	0.00	0.00
5,900.0	13.89	56.80	5,763.1	636.0	972.0	1,161.6	0.00	0.00	0.00
6,000.0	13.89	56.80	5,860.2	649.2	992.1	1,185.6	0.00	0.00	0.00
6,100.0	13.89	56.80	5,957.2	662.3	1,012.2	1,209.6	0.00	0.00	0.00
6,200.0	13.89	56.80	6,054.3	675.4	1,032.3	1,233.6	0.00	0.00	0.00
6,247.1	13.89	56.80	6,100.0	681.6	1,041.7	1,244.9	0.00	0.00	0.00



API Well Number: 43013517540000





Project: USGS Myton SW (UT)  
 Site: SECTION 12 T9S, R15E  
 Well: I-12-9-15  
 Wellbore: Wellbore #1  
 Design: Design #1



Azimuths to True North  
 Magnetic North: 11.23°

Magnetic Field  
 Strength: 52149.3snT  
 Dip Angle: 65.75°  
 Date: 6/27/2012  
 Model: IGRF2010

KOP @ 600'  
 DOGLEG RATE 1.5 DEG/100  
 TARGET RADIUS IS 75'

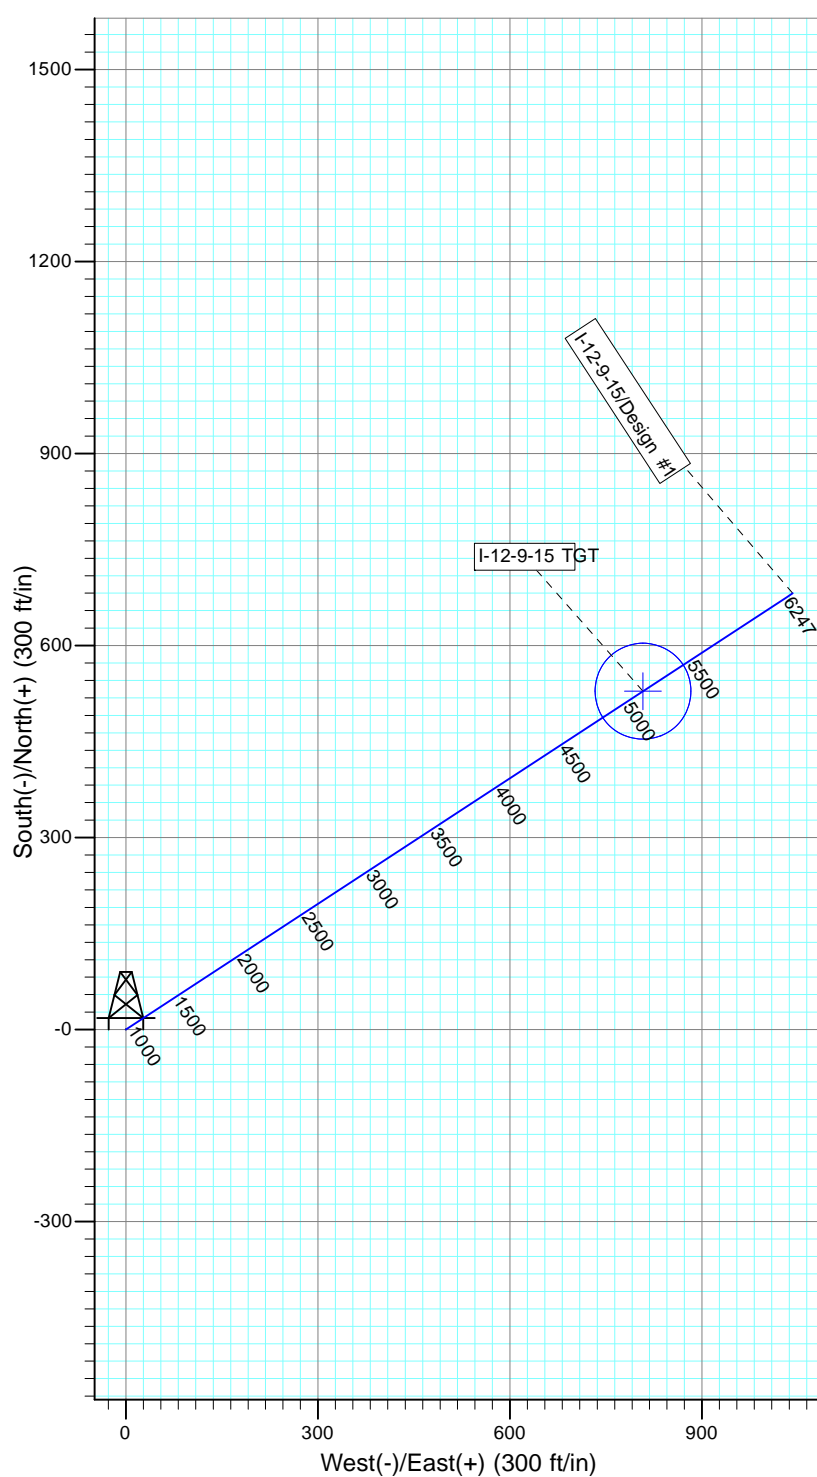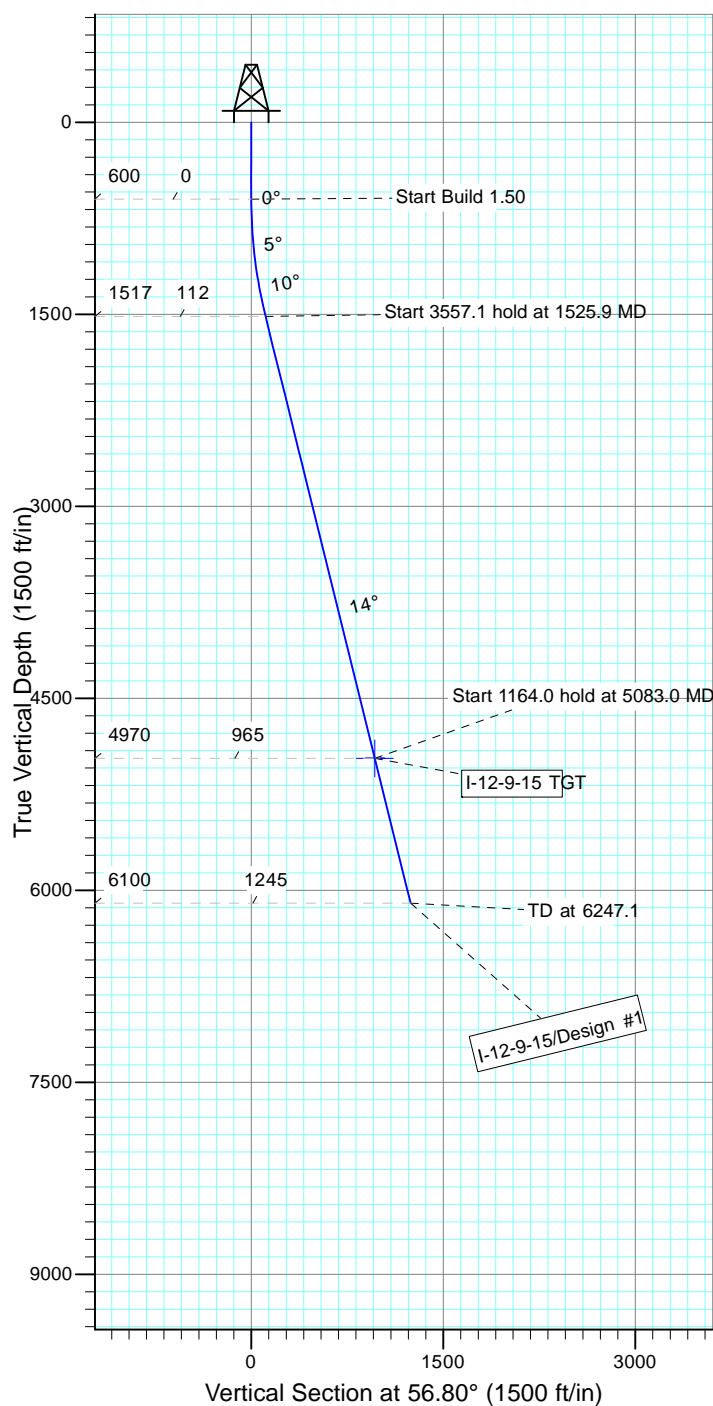

## WELLBORE TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Shape
I-12-9-15 TGT	4970.0	528.6	807.9	Circle (Radius: 75.0)

## SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	DLeg	TFace	VSec	Target
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2	600.0	0.00	0.00	600.0	0.0	0.0	0.00	0.00	0.0	
3	1525.9	13.89	56.80	1516.9	61.1	93.4	1.50	56.80	111.7	
4	5083.0	13.89	56.80	4970.0	528.6	807.9	0.00	0.00	965.5	I-12-9-15 TGT
5	6247.1	13.89	56.80	6100.0	681.6	1041.7	0.00	0.00	1244.9	



**NEWFIELD PRODUCTION COMPANY  
GMBU I-12-9-15  
AT SURFACE: SW/NE SECTION 12, T9S R15E  
DUCHESNE COUNTY, UTAH**

**ONSHORE ORDER NO. 1**

**MULTI-POINT SURFACE USE & OPERATIONS PLAN**

**1. EXISTING ROADS**

See attached Topographic Map "A"

To reach Newfield Production Company well location site GMBU I-12-9-15 located in the SW 1/4 NE 1/4 Section 12, T9S, R15E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 – 1.4 miles  $\pm$  to the junction of this highway and UT State Hwy 53; proceed in a southwesterly direction – 6.4 miles  $\pm$  to it's junction with an existing road to the southwest; proceed in a southwesterly direction – 2.4 miles  $\pm$  to it's junction with an existing road to the southwest; proceed in a southwesterly direction – 0.8 miles  $\pm$  to it's junction with an existing road to the east; proceed in a southeasterly direction – 2.5 miles  $\pm$  to it's junction with an existing road to the southwest; proceed in southwesterly direction – 0.3 miles  $\pm$  to it's junction with the beginning of the access road to the existing 7-12-9-15 well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

**2. PLANNED ACCESS ROAD**

There is no proposed access road for this location. The proposed well will be drilled directionally off of the existing 7-12-9-15 well pad. See attached **Topographic Map "B"**.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

**3. LOCATION OF EXISTING WELLS**

Refer to Exhibit "B".

**4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES**

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District  
Water Right : 43-10136

Maurice Harvey Pond  
Water Right: 47-1358

Neil Moon Pond  
Water Right: 43-11787

Newfield Collector Well  
Water Right: 47-1817 (A30414DVA, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.



A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

**Fencing Requirements**

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – Bureau of Land Management.

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. State of Utah Antiquities Project Permit #U-12-MQ-0413b 5/29/12, prepared by Montgomery Archaeological Consultants. Paleontological Resource Survey prepared by, Wade E. Miller, 7/27/00. See attached report cover pages, Exhibit "D".

#### **Surface Flow Line**

Newfield requests 3,680' of surface flow line be granted. The Surface Flow Line will consist of up to a 14" bundled pipe consisting of 2-2" poly glycol lines and 1-3" production line. Refer to Topographic Map "C" for the proposed location of the proposed flow line. Flow lines will be tan and will be constructed using the following procedures as outlined in the Greater Monument Butte Green River Development SOP.

#### **Water Disposal**

After first production, if the production water meets quality guidelines, it will be transported to the Ashley, Monument Butte, Jonah, South Wells Draw and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project. Water not meeting quality criteria, will be disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), Federally approved surface disposal facilities or at a State of Utah approved surface disposal facilities.

#### **Additional Surface Stipulations**

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

#### **Details of the On-Site Inspection**

The proposed GMBU I-12-9-15 was on-sited on 7/11/12. The following were present; Corie Miller (Newfield Production) and Janna Simonsen (Bureau of Land Management).

#### **Hazardous Material Declaration**

Newfield Production Company guarantees that during the drilling and completion of the GMBU I-12-9-15, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the GMBU I-12-9-15, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

#### **13. LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

##### Representative

Name: Corie Miller  
Address: Newfield Production Company  
Route 3, Box 3630  
Myton, UT 84052  
Telephone: (435) 646-3721

##### Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #I-12-9-15, Section 12, Township 9S, Range 15E: Lease UTU-74826 Duchesne County, Utah: and is

responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.


I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

10/2/12  
Date

\_\_\_\_\_  
Mandie Crozier  
Regulatory Analyst  
Newfield Production Company




## Typical 2M BOP stack configuration

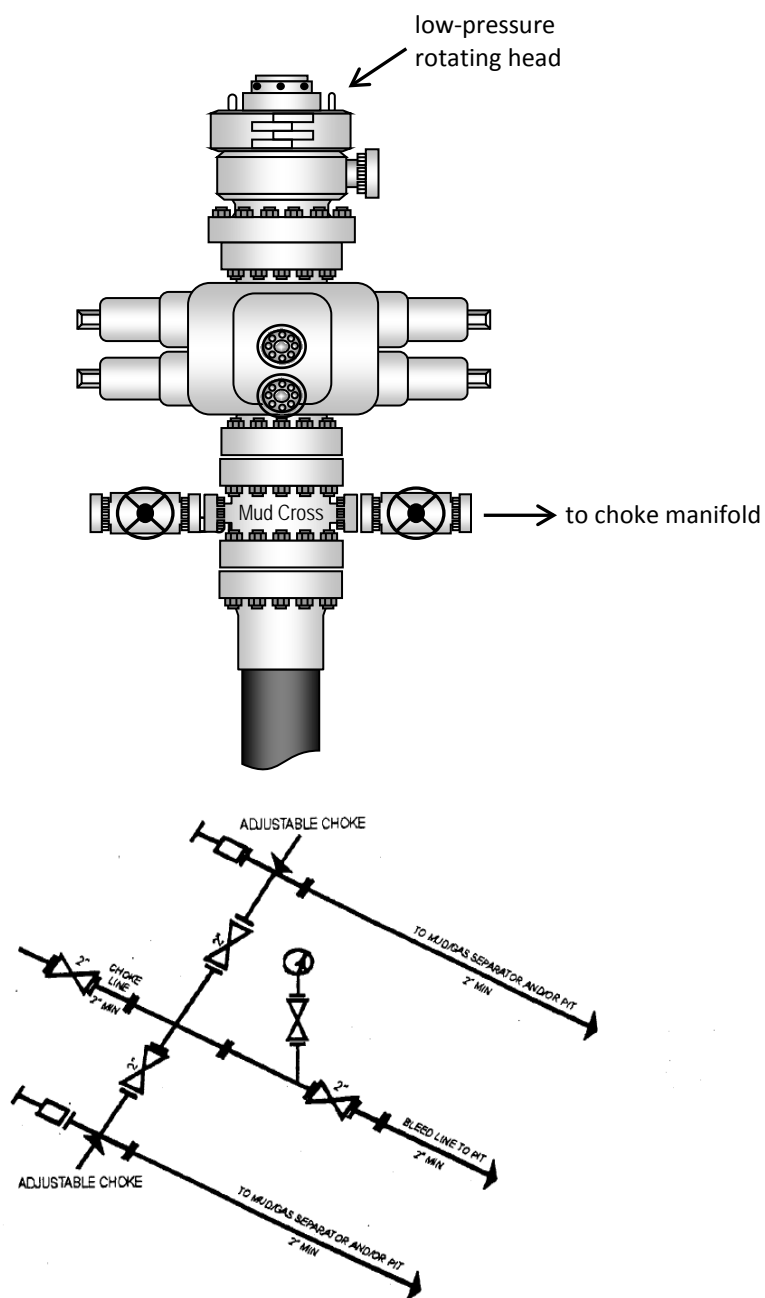

2M CHOKE MANIFOLD EQUIPMENT - CONFIGURATION OF CHOKES MAY VARY

RECEIVED: October 04, 2012




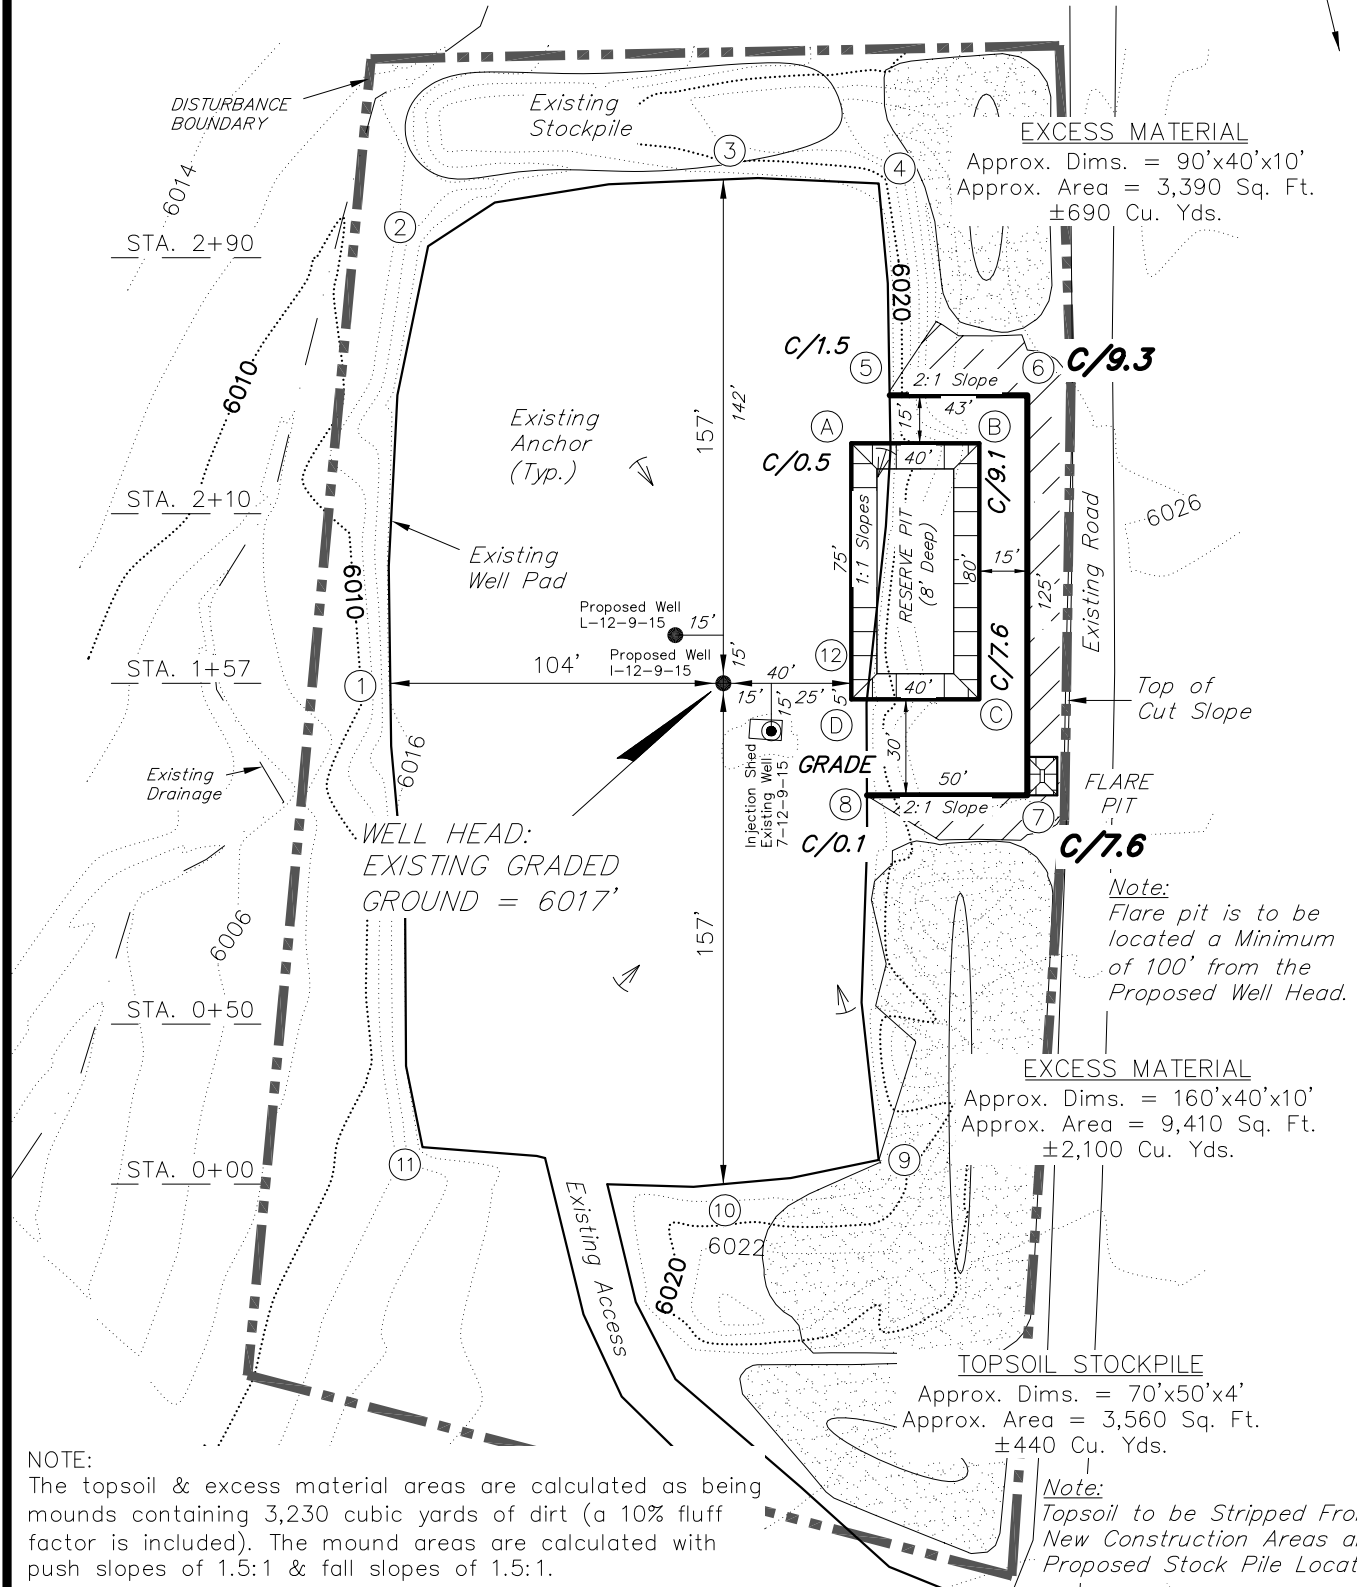
**NEWFIELD EXPLORATION COMPANY****LOCATION LAYOUT****7-12-9-15 (Existing Well)****I-12-9-15 (Proposed Well)****L-12-9-15 (Proposed Well)****Pad Location: SWNE Section 12, T9S, R15E, S.L.B.&M.**

SURVEYED BY: M.C.	DATE SURVEYED: 03-07-12	VERSION:
DRAWN BY: M.W.	DATE DRAWN: 03-09-12	V2
SCALE: 1" = 60'	REVISED: F.T.M. 07-06-12	

**Tri State** (435) 781-2501  
**Land Surveying, Inc.**  
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

RECEIVED: October 04, 2012

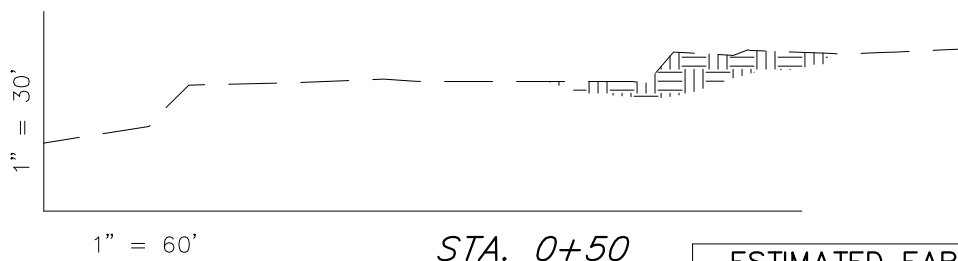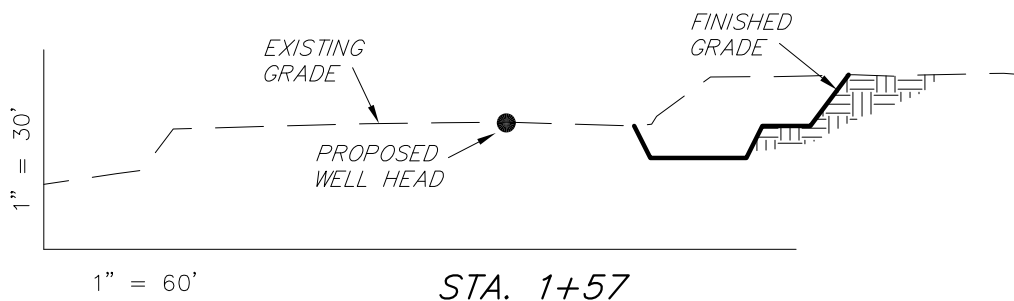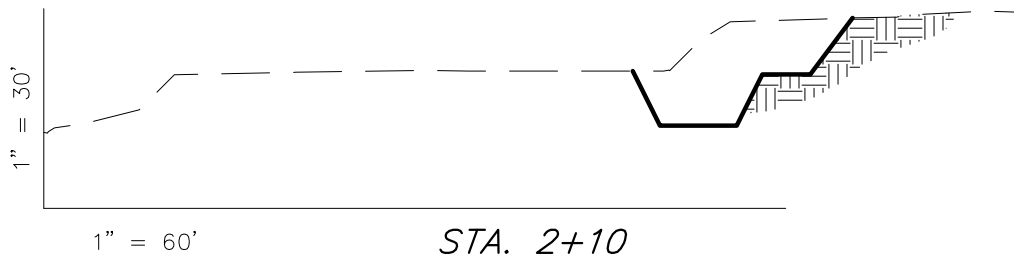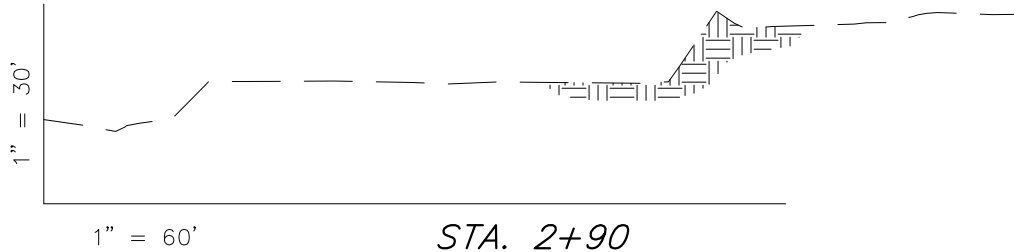

***NEWFIELD EXPLORATION COMPANY******CROSS SECTIONS******7-12-9-15 (Existing Well)******I-12-9-15 (Proposed Well)******L-12-9-15 (Proposed Well)****Pad Location: SWNE Section 12, T9S, R15E, S.L.B.&M.*

NOTE:  
UNLESS OTHERWISE  
NOTED ALL CUT/FILL  
SLOPES ARE AT 1.5:1

**ESTIMATED EARTHWORK QUANTITIES**  
(No Shrink or swell adjustments have been used)  
(Expressed in Cubic Yards)


ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	1,850	0	Topsoil is not included in Pad Cut	1,850
PIT	690	0		690
TOTALS	2,540	0	400	2,540

SURVEYED BY: M.C.	DATE SURVEYED: 03-07-12	VERSION:
DRAWN BY: M.W.	DATE DRAWN: 03-09-12	V2
SCALE: 1" = 60'	REVISED: F.T.M. 07-06-12	

**Tri State**  
*Land Surveying, Inc.*  
180 NORTH VERNAL AVE. VERNAL, UTAH 84078  
(435) 781-2501

**RECEIVED:** October 04, 2012

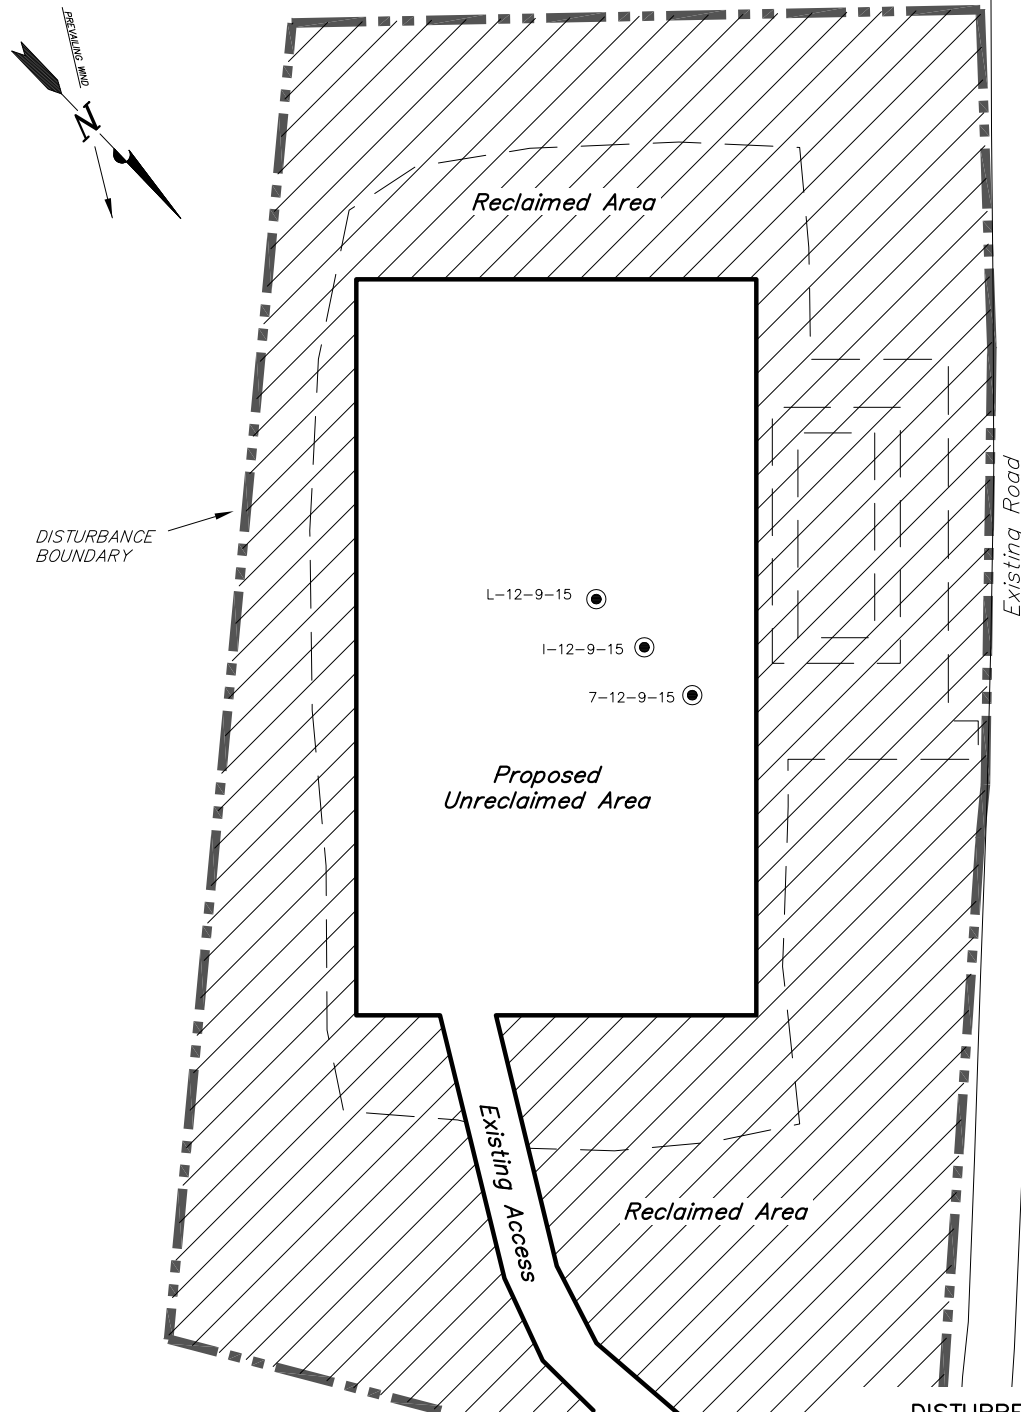

**NEWFIELD EXPLORATION COMPANY****RECLAMATION LAYOUT****7-12-9-15 (Existing Well)****I-12-9-15 (Proposed Well)****L-12-9-15 (Proposed Well)***Pad Location: SWNE Section 12, T9S, R15E, S.L.B.&M.***Notes:**

1. Reclaimed Area to Include Seeding of Approved Vegetation and Sufficient Storm Water Management System.
2. Actual Equipment Layout and Reclaimed Pad Surface Area May Change due to Production Requirements or Site Conditions.

**DISTURBED AREA:**

TOTAL DISTURBED AREA = 2.39 ACRES  
 TOTAL RECLAIMED AREA = 1.66 ACRES  
 UNRECLAIMED AREA = 0.73 ACRES

SURVEYED BY: M.C.	DATE SURVEYED: 03-07-12	VERSION:
DRAWN BY: F.T.M.	DATE DRAWN: 07-06-12	V2
SCALE: 1" = 60'	REVISED:	

**Tri State**


(435) 781-2501

**Land Surveying, Inc.**

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

**RECEIVED:** October 04, 2012

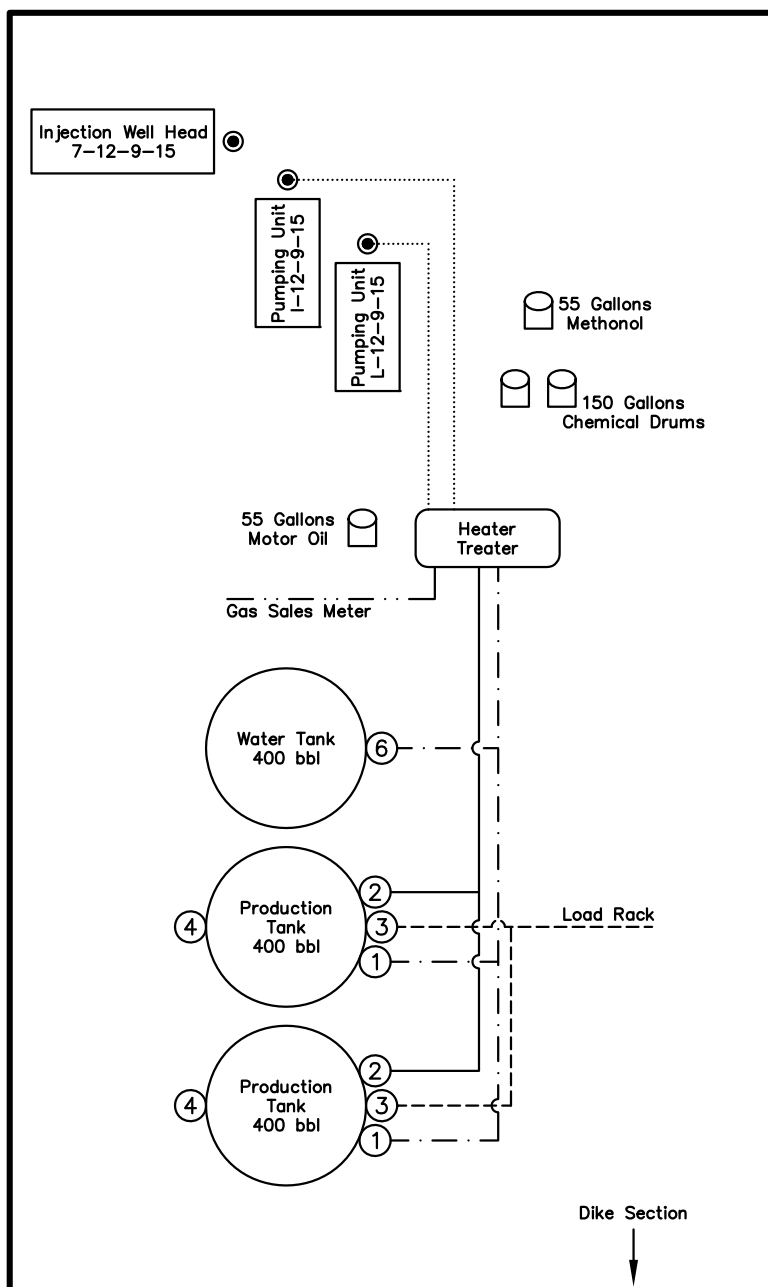

**NEWFIELD EXPLORATION COMPANY****PROPOSED SITE FACILITY DIAGRAM****7-12-9-15 (Existing Well)****I-12-9-15 (Proposed Well) UTU-74826****L-12-9-15 (Proposed Well) UTU-74826***Pad Location: SWNE Section 12, T9S, R15E, S.L.B.&M.  
Duchesne County, Utah***Legend**


Emulsion Line .....  
 Load Rack - - - - -  
 Water Line - . - . -  
 Gas Sales - . . . .  
 Oil Line - - - - -

NOT TO SCALE

SURVEYED BY: M.C.	DATE SURVEYED: 03-07-12	VERSION:
DRAWN BY: F.T.M.	DATE DRAWN: 07-06-12	V2
SCALE: NONE	REVISED:	


**Tri State** (435) 781-2501  
*Land Surveying, Inc.*  
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

RECEIVED: October 04, 2012

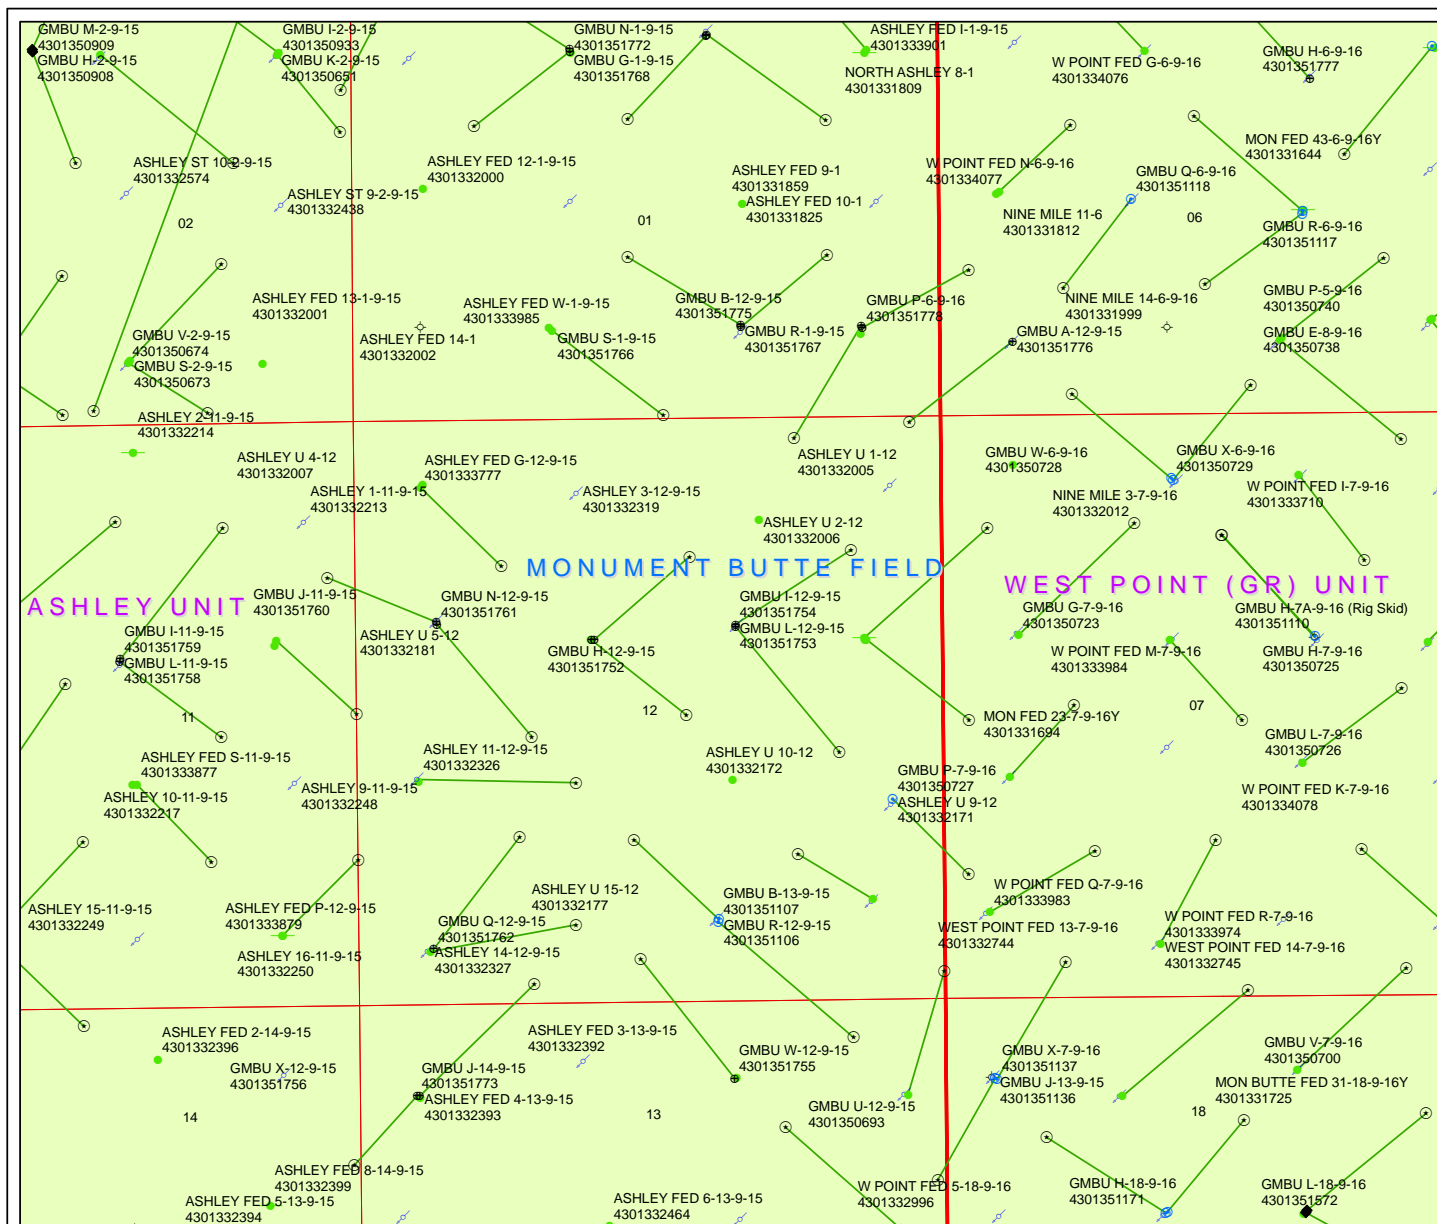

**API Number: 4301351754**  
**Well Name: GMBU I-12-9-15**  
**Township T09.0S Range R15.0E Section 12**  
**Meridian: SLBM**  
**Operator: NEWFIELD PRODUCTION COMPANY**  
 Map Prepared:  
 Map Produced by Diana Mason

Units	Wells Query
STATUS	APD - Approved Permit
ACTIVE	DRL - Spudded (Drilling Commenced)
EXPLORATORY	GIW - Gas Injection
GAS STORAGE	GS - Gas Storage
NP PP OIL	LOC - New Location
NP SECONDARY	OPS - Operation Suspended
PI OIL	PA - Plugged Abandoned
PP GAS	PPG - Producing Gas Well
PP GEOTHERM	POW - Producing Oil Well
PP OIL	SGW - Shut-in Gas Well
SECONDARY	SOW - Shut-in Oil Well
TERMINATED	TA - Temp. Abandoned
	TW - Test Well
	WDW - Water Disposal
	WW - Water Injection Well
	WSW - Water Supply Well
	Bottom Hole Location - Oil/Gas/Oil
Fields	
Unknown	
ABANDONED	
ACTIVE	
COMBINED	
INACTIVE	
STORAGE	
TERMINATED	



# United States Department of the Interior

## BUREAU OF LAND MANAGEMENT

Utah State Office  
P.O. Box 45155  
Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:  
3160  
(UT-922)

October 15, 2012

Memorandum

To: Assistant Field Manager Minerals, Vernal Field Office

From: Michael Coulthard, Petroleum Engineer

Subject: 2012 Plan of Development Greater Monument  
Butte Unit, Duchesne and Uintah Counties,  
Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2012 within the Greater Monument Butte Unit, Duchesne and Uintah Counties, Utah.

API #	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-51751	GMBU M-12-9-15	Sec 12 T09S R15E 1999 FNL 2133 FWL
	BHL	Sec 12 T09S R15E 2595 FSL 2324 FEL
43-013-51752	GMBU H-12-9-15	Sec 12 T09S R15E 1996 FNL 2154 FWL
	BHL	Sec 12 T09S R15E 1252 FNL 2274 FEL
43-013-51753	GMBU L-12-9-15	Sec 12 T09S R15E 1891 FNL 1870 FEL
	BHL	Sec 12 T09S R15E 2242 FSL 0941 FEL
43-013-51754	GMBU I-12-9-15	Sec 12 T09S R15E 1869 FNL 1870 FEL
	BHL	Sec 12 T09S R15E 1205 FNL 0818 FEL
43-013-51755	GMBU W-12-9-15	Sec 13 T09S R15E 0701 FNL 1912 FEL
	BHL	Sec 12 T09S R15E 0389 FSL 2545 FWL
43-013-51756	GMBU X-12-9-15	Sec 13 T09S R15E 0824 FNL 0535 FWL
	BHL	Sec 12 T09S R15E 0176 FSL 1580 FWL
43-013-51757	GMBU R-11-9-15	Sec 11 T09S R15E 0654 FSL 1992 FWL
	BHL	Sec 11 T09S R15E 1514 FSL 2481 FEL
43-013-51758	GMBU L-11-9-15	Sec 11 T09S R15E 2143 FNL 2131 FEL
	BHL	Sec 11 T09S R15E 2443 FSL 1221 FEL

RECEIVED: October 16, 2012



API #	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-51759	GMBU I-11-9-15	Sec 11 T09S R15E 2122 FNL 2129 FEL BHL Sec 11 T09S R15E 0948 FNL 1189 FEL
43-013-51760	GMBU J-11-9-15	Sec 12 T09S R15E 1822 FNL 0728 FWL BHL Sec 11 T09S R15E 1408 FNL 0251 FEL
43-013-51761	GMBU N-12-9-15	Sec 12 T09S R15E 1841 FNL 0737 FWL BHL Sec 12 T09S R15E 2415 FSL 1581 FWL
43-013-51762	GMBU Q-12-9-15	Sec 12 T09S R15E 0502 FSL 0675 FWL BHL Sec 12 T09S R15E 1506 FSL 1464 FWL
43-013-51763	GMBU C-14-9-15	Sec 11 T09S R15E 0639 FSL 2006 FWL BHL Sec 14 T09S R15E 0155 FNL 2490 FEL
43-013-51764	GMBU M-14-9-15	Sec 14 T09S R15E 1811 FNL 2069 FWL BHL Sec 14 T09S R15E 2466 FSL 2503 FEL
43-013-51765	GMBU G-14-9-15	Sec 14 T09S R15E 1801 FNL 2050 FWL BHL Sec 14 T09S R15E 1158 FNL 1215 FWL
43-013-51766	GMBU S-1-9-15	Sec 01 T09S R15E 0820 FSL 1795 FEL BHL Sec 01 T09S R15E 1466 FSL 1013 FEL
43-013-51767	GMBU R-1-9-15	Sec 01 T09S R15E 0840 FSL 1801 FEL BHL Sec 01 T09S R15E 1463 FSL 2488 FWL
43-013-51768	GMBU G-1-9-15	Sec 01 T09S R15E 1940 FNL 1975 FWL BHL Sec 01 T09S R15E 1320 FNL 1023 FWL
43-013-51769	GMBU L-1-9-15	Sec 01 T09S R15E 1814 FNL 2084 FEL BHL Sec 01 T09S R15E 2601 FNL 1017 FEL
43-013-51770	GMBU M-1-9-15	Sec 01 T09S R15E 1833 FNL 2093 FEL BHL Sec 01 T09S R15E 2577 FNL 2497 FWL
43-013-51771	GMBU H-1-9-15	Sec 01 T09S R15E 0686 FNL 2008 FWL BHL Sec 01 T09S R15E 1392 FNL 2545 FEL
43-013-51772	GMBU N-1-9-15	Sec 01 T09S R15E 1961 FNL 1978 FWL BHL Sec 01 T09S R15E 2634 FNL 1108 FWL
43-013-51773	GMBU J-14-9-15	Sec 13 T09S R15E 0818 FNL 0515 FWL BHL Sec 14 T09S R15E 1446 FNL 0062 FEL
43-013-51774	GMBU J-10-9-15	Sec 11 T09S R15E 0568 FNL 0619 FWL BHL Sec 10 T09S R15E 1532 FNL 0044 FEL
43-013-51775	GMBU B-12-9-15	Sec 01 T09S R15E 0824 FSL 0711 FEL BHL Sec 12 T09S R15E 0188 FNL 1324 FEL

API #	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-51776	GMBU A-12-9-15	Sec 06 T09S R16E 0669 FSL 0653 FWL BHL Sec 12 T09S R15E 0052 FNL 0283 FEL
43-013-51777	GMBU H-6-9-16	Sec 06 T09S R16E 2258 FNL 1777 FEL BHL Sec 06 T09S R16E 1111 FNL 2329 FWL
43-013-51778	GMBU P-6-9-16	Sec 01 T09S R15E 0804 FSL 0702 FEL BHL Sec 06 T09S R16E 1321 FSL 0267 FWL
43-013-51779	GMBU T-32-8-16	Sec 33 T08S R16E 0615 FSL 0485 FWL BHL Sec 32 T08S R16E 1494 FSL 0116 FEL
43-013-51780	GMBU W-36-8-15	Sec 01 T09S R15E 0672 FNL 1992 FWL BHL Sec 36 T08S R15E 0201 FSL 2368 FEL

This office has no objection to permitting the wells at this time.

**Michael L. Coulthard**  
Digitally signed by Michael L. Coulthard  
DN: cn=Michael L. Coulthard, o=Bureau of Land Management,  
ou=Branch of Minerals, email=Michael\_Coulthard@blm.gov, c=US  
Date: 2012.10.15 15:29:00 -06'00'

bcc: File - Greater Monument Butte Unit  
Division of Oil Gas and Mining  
Central Files  
Agr. Sec. Chron  
Fluid Chron

MCoulthard:mc:10-15-12

RECEIVED: October 16, 2012

VIA ELECTRONIC DELIVERY



October 11, 2012

State of Utah, Division of Oil, Gas and Mining  
ATTN: Diana Mason  
P.O. Box 145801  
Salt Lake City, UT 84114-5801

RE: Directional Drilling  
**GMBU I-12-9-15**  
Greater Monument Butte (Green River) Unit

Surface Hole: T9S-R15E Section 12: SWNE (UTU-74826)  
1869' FNL 1870' FEL

At Target: T9S-R15E Section 12: NENE (UTU-74826)  
1205' FNL 818' FEL

Duchesne County, Utah

Dear Ms. Mason:

Pursuant to the filing by Newfield Production Company (NPC) of an Application for Permit to Drill the above referenced well dated 10/4/2012, a copy of which is attached, and in accordance with Oil and Gas Conservation Rule R649-3-11, NPC hereby submits this letter as notice of our intention to directionally drill this well.

The surface hole and target locations of this well are both within the boundaries of the Greater Monument Butte Unit (UTU-87538X), of which Newfield certifies that it is the operator. Further, Newfield certifies that all lands within 460 feet of the entire directional well bore are within the Greater Monument Butte Unit.

NPC is permitting this well as a directional well in order to mitigate surface disturbance by utilizing pre-existing roads and pipelines.

NPC hereby requests our application for permit to drill be granted pursuant to R649-3-11. If you have any questions or require further information, please contact the undersigned at 303-383-4121 or by email at [lburget@newfield.com](mailto:lburget@newfield.com). Your consideration in this matter is greatly appreciated.

Sincerely,  
Newfield Production Company

A handwritten signature in blue ink that reads "Leslie Burget".

Leslie Burget  
Land Associate

Form 3160-3  
(August 2007)UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENTFORM APPROVED  
OMB No. 1004-0136  
Expires July 31, 2010

## APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU74826
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator NEWFIELD PRODUCTION COMPANY Contact: MANDIE CROZIER Email: mcrozier@newfield.com		7. If Unit or CA Agreement, Name and No. GREATER MONUMENT
3a. Address ROUTE #3 BOX 3630 MYTON, UT 84052	3b. Phone No. (include area code) Ph: 435-646-4825 Fx: 435-646-3031	8. Lease Name and Well No. GMBU I-12-9-15
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface SWNE 1869FNL 1870FEL At proposed prod. zone NENE 1205FNL 818FEL		9. API Well No.
14. Distance in miles and direction from nearest town or post office* 13.8 MILES SOUTHWEST OF MYTON		10. Field and Pool, or Exploratory MONUMENT BUTTE
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 818'	16. No. of Acres in Lease 2189.90	11. Sec., T., R., M., or Blk. and Survey or Area Sec 12 T9S R15E Mer SLB
18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 949'	17. Spacing Unit dedicated to this well 20.00	12. County or Parish DUCHESNE
21. Elevations (Show whether DF, KB, RT, GL, etc.) 6017 GL	19. Proposed Depth 6247 MD 6100 TVD	13. State UT
22. Approximate date work will start 01/01/2013	20. BLM/BIA Bond No. on file WYB000493	23. Estimated duration 7 DAYS

## 24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- |   |  |
|---|--|
| 1. Well plat certified by a registered surveyor.  | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).    |
| 2. A Drilling Plan.   | 5. Operator certification  |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature (Electronic Submission)	Name (Printed/Typed) MANDIE CROZIER Ph: 435-646-4825	Date 10/04/2012
Title REGULATORY ANALYST		
Approved by (Signature)	Name (Printed/Typed)	Date
Title	Office	

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

## Additional Operator Remarks (see next page)

Electronic Submission #153412 verified by the BLM Well Information System  
For NEWFIELD PRODUCTION COMPANY, sent to the Vernal


\*\* OPERATOR-SUBMITTED \*\* OPERATOR-SUBMITTED \*\* OPERATOR-SUBMITTED \*\*



API Well Number: 43013517540000

**Additional Operator Remarks:**

SURFACE LEASE: UTU-74826  
BOTTOM HOLE LEASE: UTU-74826

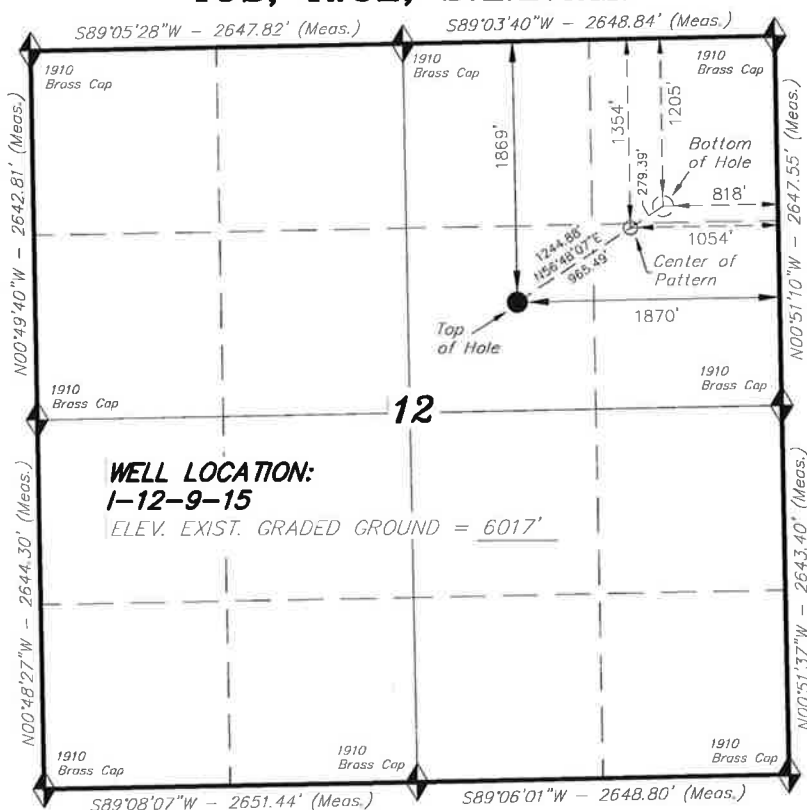**T9S, R15E, S.L.B.&M.**

**WELL LOCATION:**  
**I-12-9-15**

ELEV. EXIST. GRADED GROUND = 6017'

**NEWFIELD EXPLORATION COMPANY**

WELL LOCATION, I-12-9-15, LOCATED AS SHOWN IN THE SW 1/4 NE 1/4 OF SECTION 12, T9S, R15E, S.L.B.&M. DUCHESNE COUNTY, UTAH.

TARGET BOTTOM HOLE, I-12-9-15, LOCATED AS SHOWN IN THE NE 1/4 NE 1/4 OF SECTION 12, T9S, R15E, S.L.B.&M. DUCHESNE COUNTY, UTAH.

**NOTES:**

1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE.



◆ = SECTION CORNERS LOCATED


BASIS OF ELEV; Elevations are based on an N.G.S. OPUS Correction. LOCATION: LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'

<b>NAD 83 (SURFACE LOCATION)</b>
LATITUDE = 40°02'51.25"
LONGITUDE = 110°10'39.78"
<b>NAD 27 (SURFACE LOCATION)</b>
LATITUDE = 40°02'51.39"
LONGITUDE = 110°10'37.23"
<b>NAD 83 (BOTTOM HOLE LOCATION)</b>
LATITUDE = 40°02'57.83"
LONGITUDE = 110°10'26.26"
<b>NAD 27 (BOTTOM HOLE LOCATION)</b>
LATITUDE = 40°02'57.97"
LONGITUDE = 110°10'23.71"

**TRI STATE LAND SURVEYING & CONSULTING**

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078  
(435) 781-2501

DATE SURVEYED: 03-07-12	SURVEYED BY: M.C.	VERSION:
DATE DRAWN: 07-06-12	DRAWN BY: F.T.M.	
REVISED:	SCALE: 1" = 1000'	V2

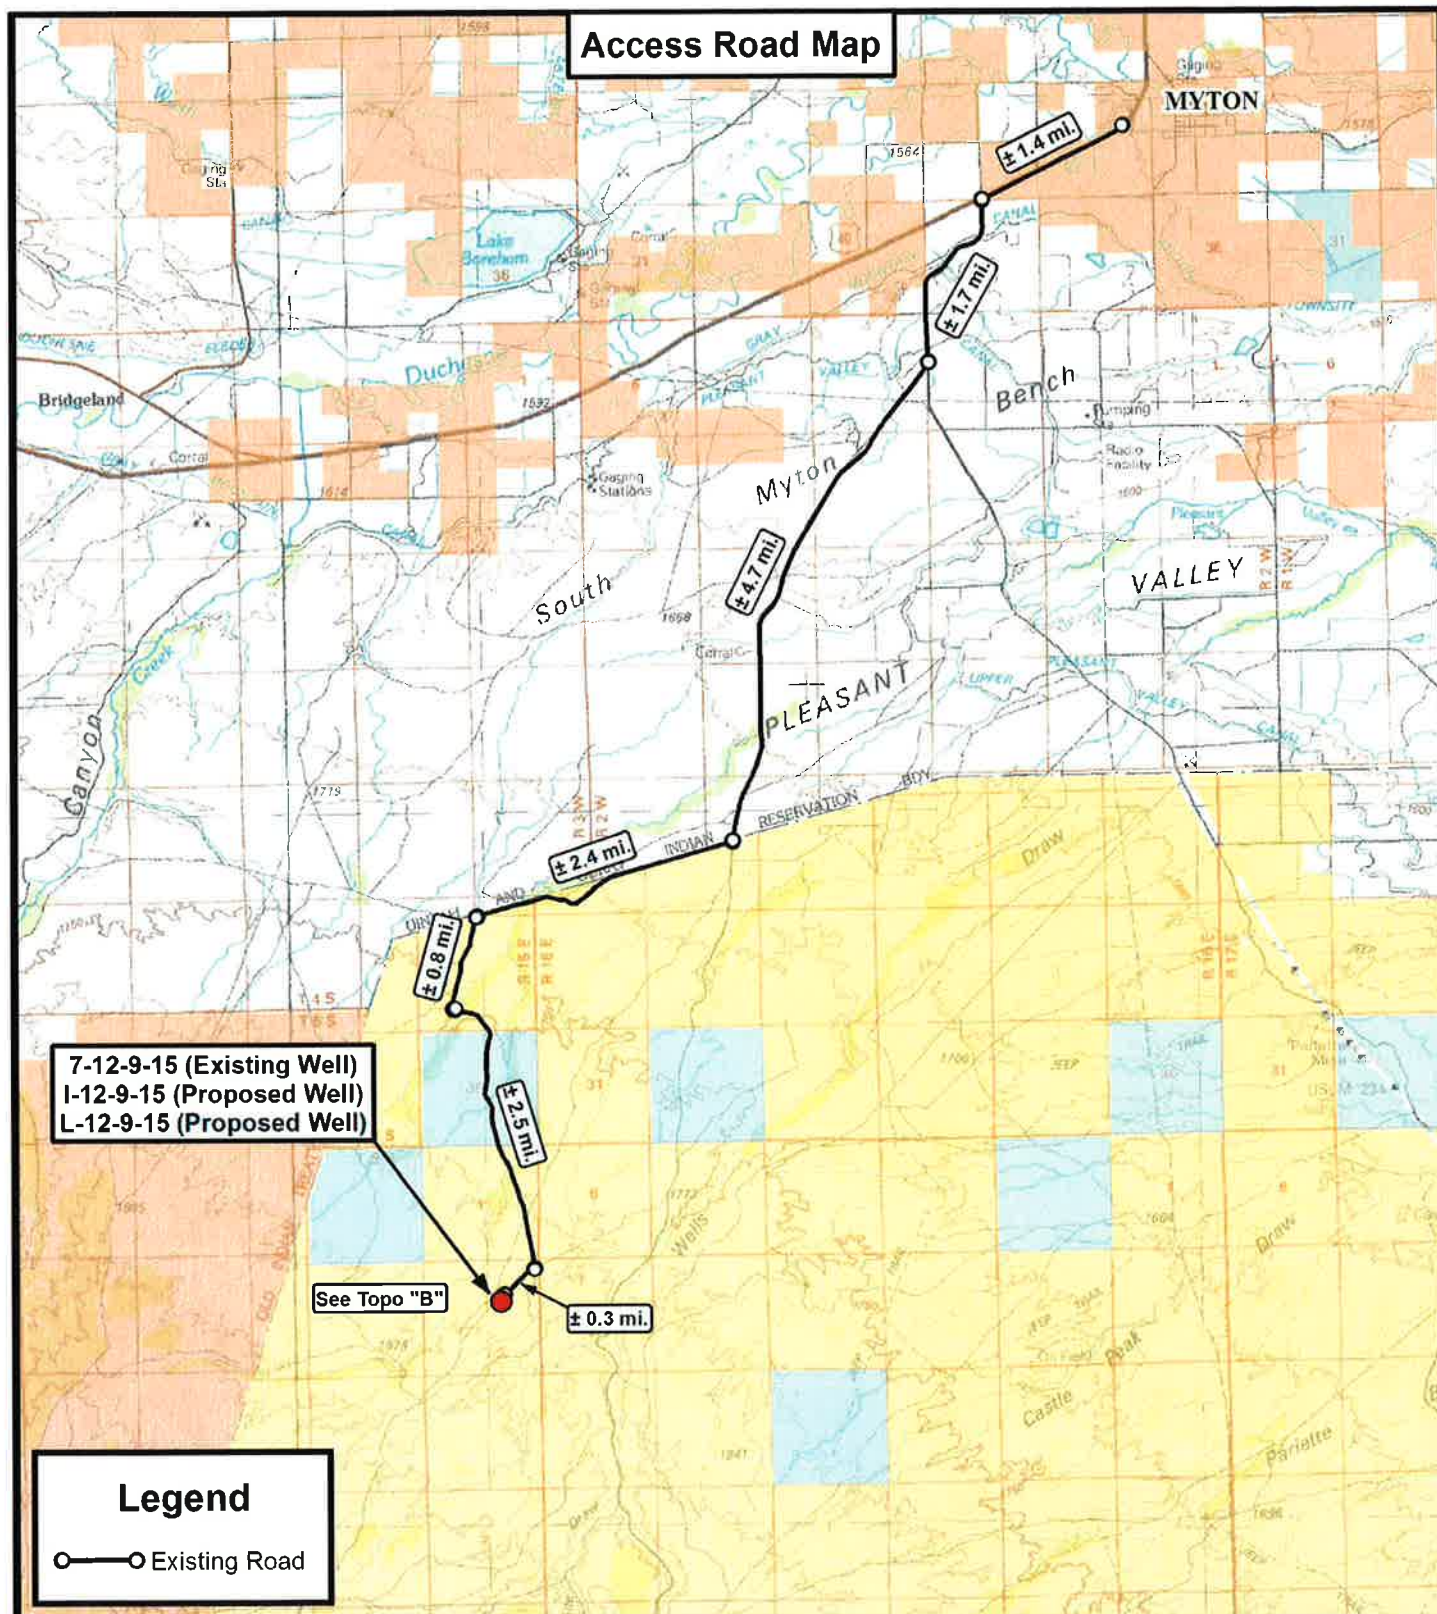

**Tri State  
Land Surveying, Inc.**

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501  
F: (435) 781-2518



**NEWFIELD EXPLORATION COMPANY**

7-12-9-15 (Existing Well)  
 I-12-9-15 (Proposed Well)  
 L-12-9-15 (Proposed Well)  
 SEC. 12, T9S, R15E, S.L.B.&M. Duchesne County, UT.


DRAWN BY:	A.P.C.	REVISED:	VERSION:
DATE:	07-06-2012		V2
SCALE:	1:100,000		

**TOPOGRAPHIC MAP**

SHEET

**A**



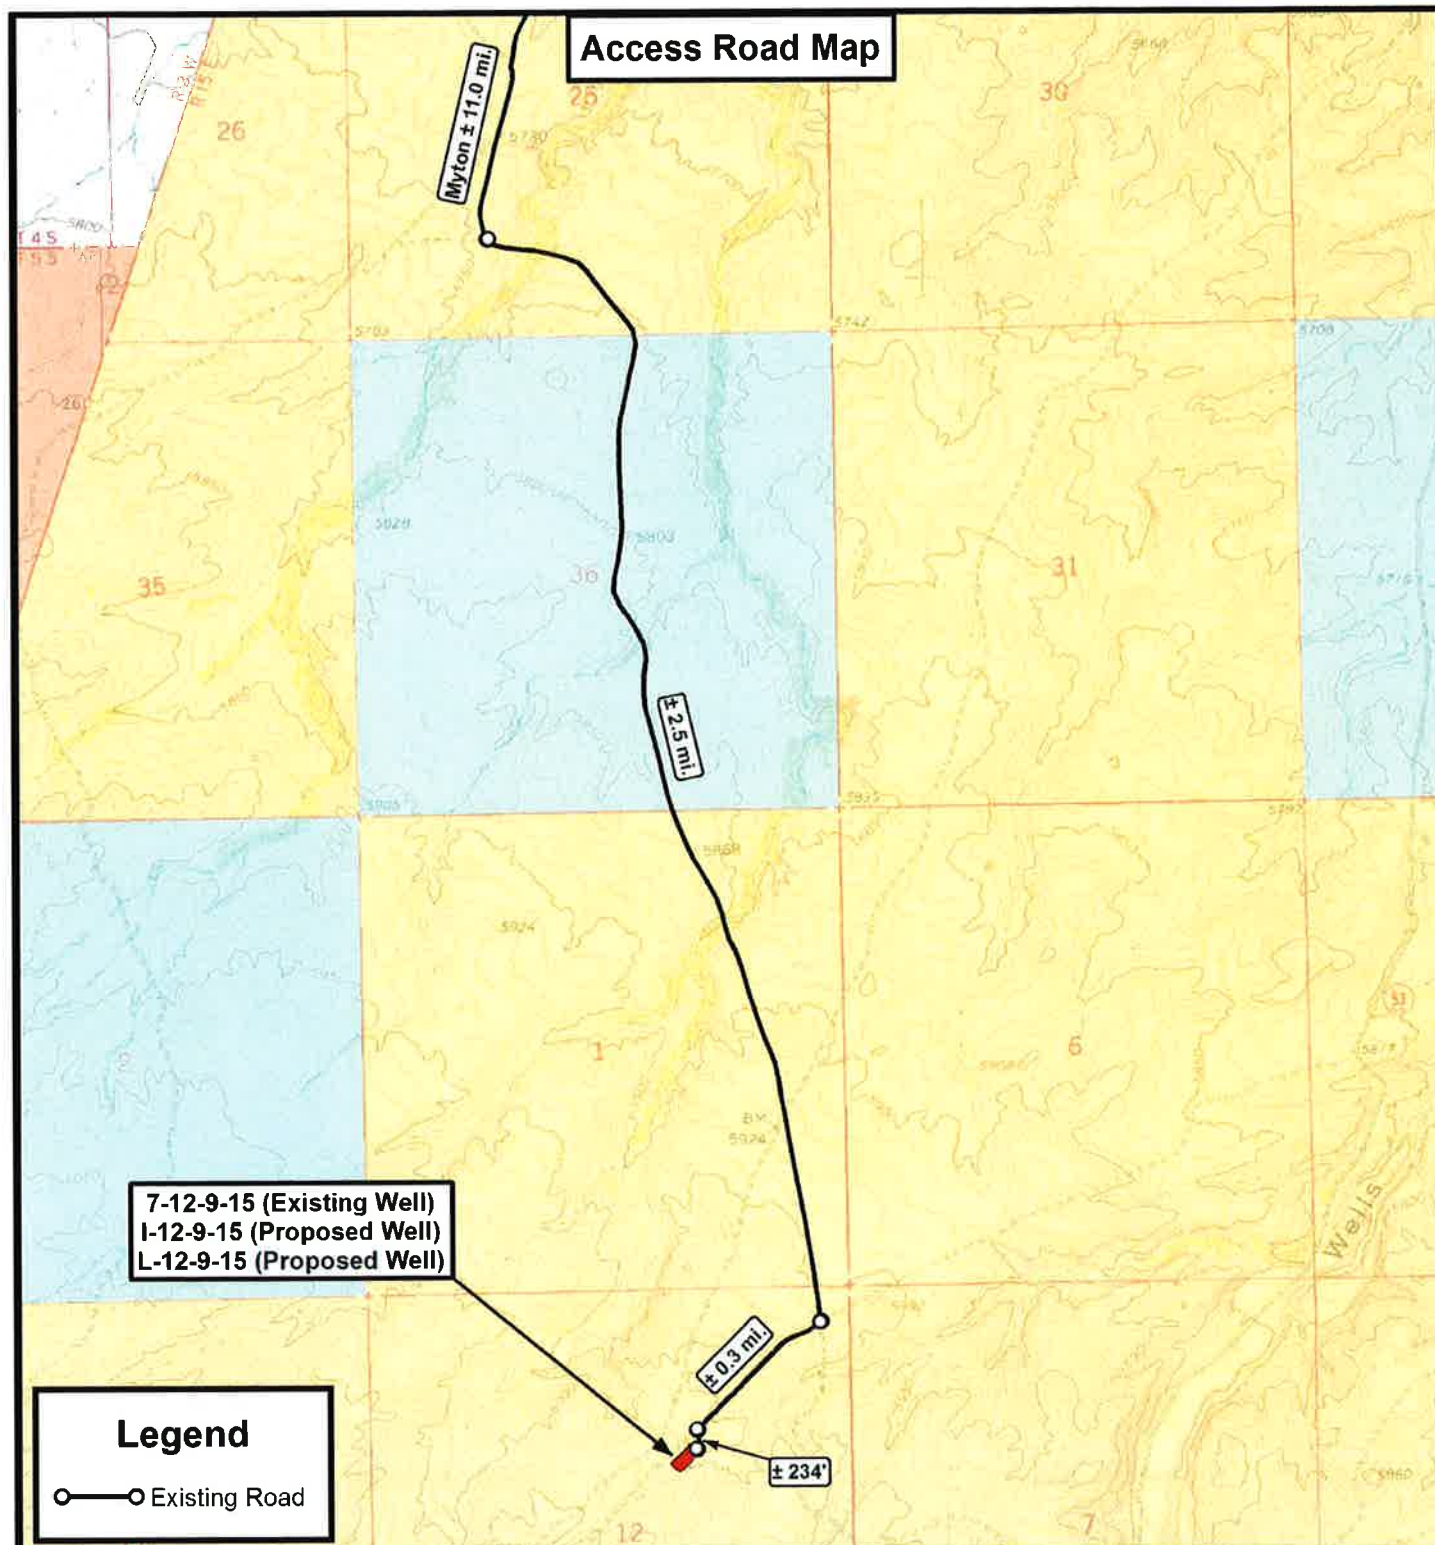

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



**Tri State  
Land Surveying, Inc.**

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501  
F: (435) 781-2518

N



## NEWFIELD EXPLORATION COMPANY

7-12-9-15 (Existing Well)  
I-12-9-15 (Proposed Well)  
L-12-9-15 (Proposed Well)  
SEC. 12, T9S, R15E, S.L.B.&M. Duchesne County, UT.


DRAWN BY:	A.P.C.	REVISED: 07-06-12 A.P.C.	VERSION:
DATE:	03-12-2012		V2
SCALE:	1" = 2,000'		

**TOPOGRAPHIC MAP**

SHEET

**B**



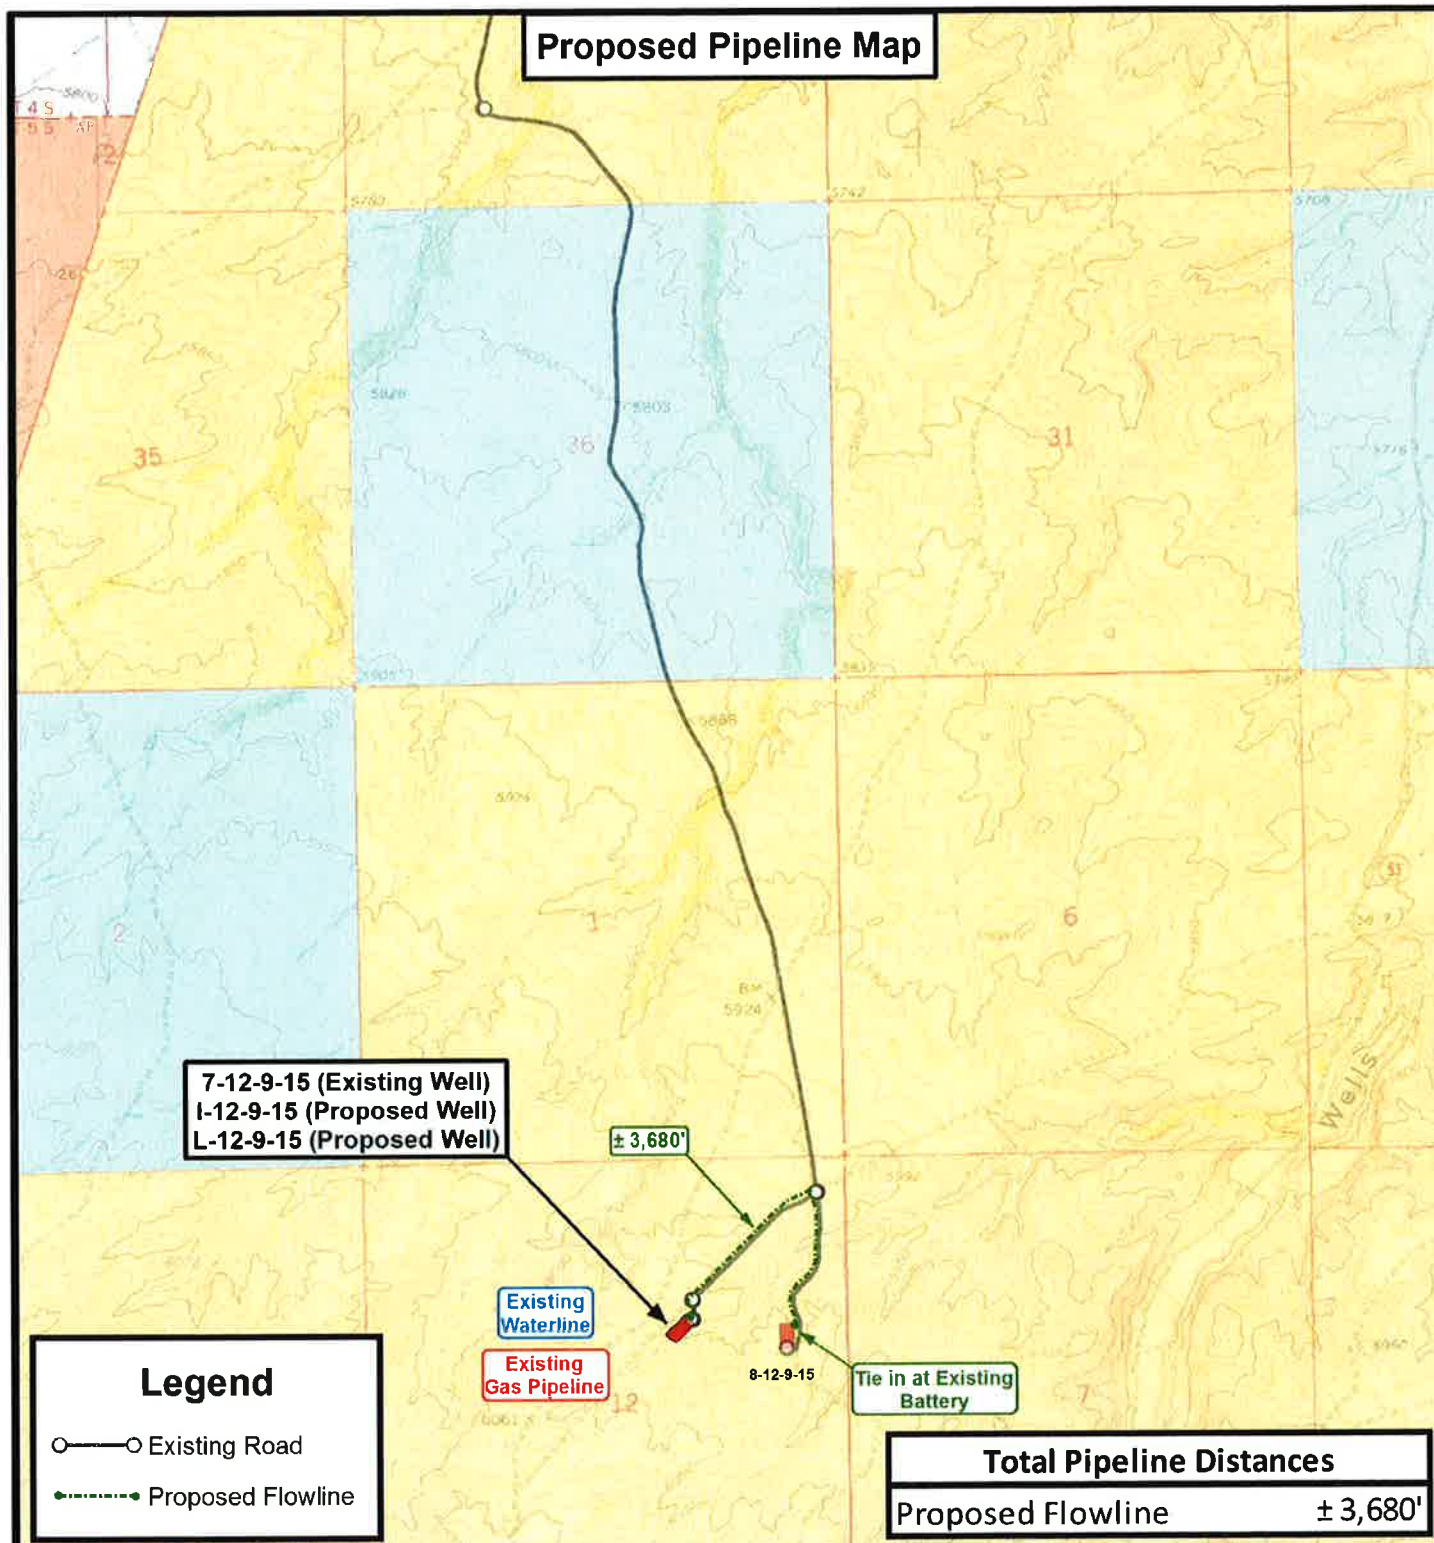

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



**Tri State**  
**Land Surveying, Inc.**

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501  
 F: (435) 781-2518

N



## NEWFIELD EXPLORATION COMPANY

7-12-9-15 (Existing Well)

I-12-9-15 (Proposed Well)

L-12-9-15 (Proposed Well)

SEC. 12, T9S, R15E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	A.P.C.	REVISED:	07-06-12 A.P.C.	VERSION:
DATE:	03-12-2012			V2
SCALE:	1" = 2,000'			


**TOPOGRAPHIC MAP**

SHEET

**C**

## Exhibit "B" Map

7-12-9-15 (Existing Well)  
 I-12-9-15 (Proposed Well)  
 L-12-9-15 (Proposed Well)

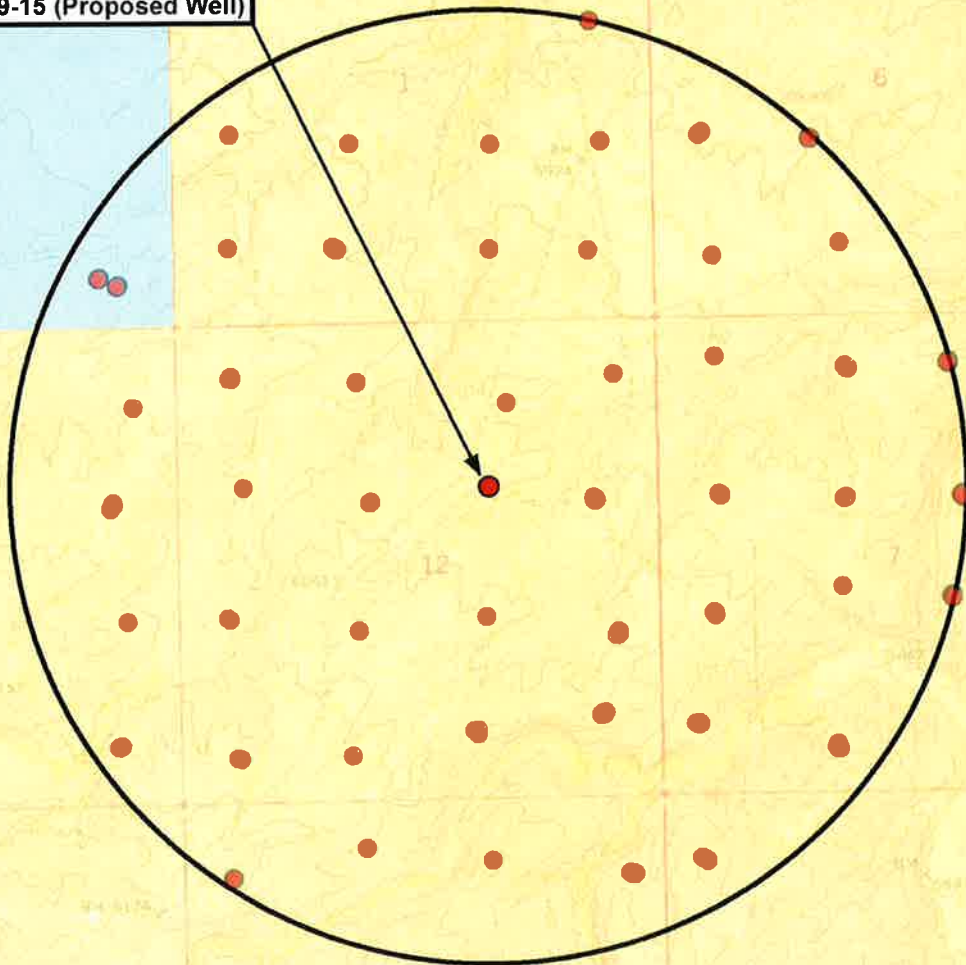

## Legend

- 1 Mile Radius  
 ● Pad Location

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



**Tri State  
 Land Surveying, Inc.**

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501  
 F: (435) 781-2518

**NEWFIELD EXPLORATION COMPANY**

7-12-9-15 (Existing Well)  
 I-12-9-15 (Proposed Well)  
 L-12-9-15 (Proposed Well)  
 SEC. 12, T9S, R15E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	A.P.C.	REVISED:	VERSION:
DATE:	07-06-2012		V2
SCALE:	1" = 2,000'		

**TOPOGRAPHIC MAP**

SHEET

**D**

## WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 10/4/2012

API NO. ASSIGNED: 43013517540000

WELL NAME: GMBU I-12-9-15

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: SWNE 12 090S 150E

Permit Tech Review: ☒

SURFACE: 1869 FNL 1870 FEL

Engineering Review: ☐

BOTTOM: 1205 FNL 0818 FEL

Geology Review: ☒

COUNTY: DUCHESNE

LATITUDE: 40.04756

LONGITUDE: -110.17776

UTM SURF EASTINGS: 570138.00

NORTHINGS: 4433360.00

FIELD NAME: MONUMENT BUTTE

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-74826

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 1 - Federal

COALBED METHANE: NO

## RECEIVED AND/OR REVIEWED:

☒ PLAT☒ Bond: FEDERAL - WYB000493☐ Potash☐ Oil Shale 190-5☐ Oil Shale 190-3☐ Oil Shale 190-13☒ Water Permit: 437478☐ RDCC Review:☐ Fee Surface Agreement☐ Intent to Commingle

Commingling Approved

## LOCATION AND SITING:

☐ R649-2-3.

Unit: GMBU (GRRV)

☐ R649-3-2. General☐ R649-3-3. Exception☒ Drilling Unit

Board Cause No: Cause 213-11

Effective Date: 11/30/2009

Siting: Suspends General Siting

☒ R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason  
15 - Directional - dmason  
27 - Other - bhill

RECEIVED: November 01, 2012





GARY R. HERBERT  
*Governor*

GREGORY S. BELL  
*Lieutenant Governor*

# State of Utah

## DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER  
*Executive Director*

### Division of Oil, Gas and Mining

JOHN R. BAZA  
*Division Director*

## Permit To Drill

\*\*\*\*\*

**Well Name:** GMBU I-12-9-15  
**API Well Number:** 43013517540000  
**Lease Number:** UTU-74826  
**Surface Owner:** FEDERAL  
**Approval Date:** 11/1/2012

### Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

### Authority:

Pursuant to Utah Code Ann. 40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 213-11. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

### Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

### General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

### Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Production casing cement shall be brought up to or above the top of the unitized interval for the Greater Monument Butte Unit (Cause No. 213-11).

### Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well - contact Carol Daniels at 801-538-5284

(please leave a voicemail message if not available)

OR

submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website  
at <http://oilgas.ogm.utah.gov>

**Reporting Requirements:**

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) - due within 5 days of spudding the well
- Monthly Status Report (Form 9) - due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) - due prior to implementation
- Written Notice of Emergency Changes (Form 9) - due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) - due prior to implementation
- Report of Water Encountered (Form 7) - due within 30 days after completion
- Well Completion Report (Form 8) - due within 30 days after completion or plugging

**Approved By:**

A handwritten signature in black ink, appearing to read "John Rogers", written over a horizontal line.

For John Rogers  
Associate Director, Oil & Gas



UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

RECEIVED

OCT 05 2012

FORM APPROVED  
OMB No. 1004-0136  
Expires July 31, 2010

APPLICATION FOR PERMIT TO DRILL OR REENTER

BLM

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU74826
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator NEWFIELD PRODUCTION COMPANY Contact: MANDIE CROZIER Email: mcrozier@newfield.com		7. If Unit or CA Agreement, Name and No. GREATER MONUMENT
3a. Address ROUTE #3 BOX 3630 MYTON, UT 84052		8. Lease Name and Well No. GMBU I-12-9-15
3b. Phone No. (include area code) Ph: 435-646-4825 Fx: 435-646-3031		9. API Well No. 43-013-51754
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface SWNE 1869FNL 1870FEL At proposed prod. zone NENE 1205FNL 818FEL		10. Field and Pool, or Exploratory MONUMENT BUTTE
14. Distance in miles and direction from nearest town or post office* 13.8 MILES SOUTHWEST OF MYTON		11. Sec., T., R., M., or Blk. and Survey or Area Sec 12 T9S R15E Mer SLB
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 818'	16. No. of Acres in Lease 2189.90	12. County or Parish DUCHESNE
17. Spacing Unit dedicated to this well 20.00	18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 949'	13. State UT
19. Proposed Depth 6247 MD 6100 TVD	20. BLM/BIA Bond No. on file WYB000493	21. Elevations (Show whether DF, KB, RT, GL, etc.) 6017 GL
22. Approximate date work will start 01/01/2013	23. Estimated duration 7 DAYS	

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

DIV. OF OIL, GAS & MINING

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature (Electronic Submission)	Name (Printed/Typed) MANDIE CROZIER Ph: 435-646-4825	Date 10/04/2012
Title REGULATORY ANALYST		
Approved by (Signature)	Name (Printed/Typed) Jerry Kenczka	Date SEP 12 2013
Title Assistant Field Manager Lands & Mineral Resources	Office VERNAL FIELD OFFICE	

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.  
Conditions of approval, if any, are attached.

CONDITIONS OF APPROVAL ATTACHED

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

Electronic Submission #153412 verified by the BLM Well Information System  
For NEWFIELD PRODUCTION COMPANY, sent to the Vernal  
Committed to AFMSS for processing by JOHNETTA MAGEE on 10/18/2012 ()

NOTICE OF APPROVAL

UDOGM

\*\* OPERATOR-SUBMITTED \*\* OPERATOR-SUBMITTED \*\* OPERATOR-SUBMITTED \*\*




UNITED STATES DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



**CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL**

Company: Newfield Production Company  
Well No: GMBU I-12-9-15  
API No: 43-013-51754

Location: SWNE, Sec. 12, T9S, R15E  
Lease No: UTU-74826  
Agreement:

**OFFICE NUMBER: (435) 781-4400**

**OFFICE FAX NUMBER: (435) 781-3420**

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR  
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

**NOTIFICATION REQUIREMENTS**

Location Construction (Notify Environmental Scientist)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings to: <a href="mailto:blm_ut_vn_opreport@blm.gov">blm_ut_vn_opreport@blm.gov</a>
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM  
CONDITIONS OF APPROVAL (COAs)***

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO<sub>x</sub> per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO<sub>x</sub> per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

The Operator will comply with the requirements of the ***Green River District (GRD) Reclamation Guidelines*** formalized by Green River District Instructional Memo UTG000-2011-003 on March 28, 2011. Documentation of the compliance will be as follows:

- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) that designates the proposed site-specific monitoring and reference sites chosen for the location. A description of the proposed sites shall be included, as well as a map showing the locations of the proposed sites.
- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) 3 growing seasons after reclamation efforts have occurred evaluating the status of the reclaimed areas in order to determine whether the BLM standards set forth in the GRD Reclamation Guidelines have been met (30% or greater basal cover).
- Prior to beginning new surface disturbance, the operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) providing the results of the noxious weed inventory described in the GRD Reclamation Guidelines (2011). If weeds are found the report shall include 1) A GPS location recorded in North American Datum 1983; 2) species; 3) canopy cover or number of plants; 4) and size of infestation (estimate square feet or acres. Information shall be also documented in the reclamation report.

**CONDITIONS OF APPROVAL**

**Wildlife**

**In accordance with the Record of Decision for the Castle Peak and Eightmile Flat Oil and Gas Expansion Project, Newfield Rocky Mountains Inc., the following COA's are required:**

- WFM-1 On level or gently sloping ground (5 percent slope or less) Newfield will elevate surface pipelines (4 inches or greater in diameter) a minimum of 6 inches above the ground to allow passage of small animals beneath the pipe. This ground clearance will be achieved by placing the pipeline on blocks at intervals of 150 to 200 feet.

- WFM-4 Newfield will install noise reduction devices on all pump jacks to reduce intermittent noise to 45 dBA at 660 feet from the source.

#### **COA's derived from mitigating measures in the EA:**

**If construction and drilling is anticipated during any of the following wildlife seasonal spatial restrictions, a BLM biologist or a qualified consulting firm biologist must conduct applicable surveys using an accepted protocol prior to any ground disturbing activities.**

- There is a ferruginous hawk nest within ½ mile of the proposed project area. If construction or drilling is proposed from March 1-August 31, then a nesting survey will be conducted by a qualified biologist according to protocol. If the nest is found to be inactive, then permission to proceed may be granted by the BLM Authorized Officer. If the nest is determined to be active, then the timing restriction will remain in effect.
- The proposed project is within 0.25 mile of burrowing owl habitat. If construction or drilling is proposed from March 1-August 31, then a nesting survey will be conducted by a qualified biologist according to protocol. If no nests are located, then permission to proceed may be granted by the BLM Authorized Officer. If a nest is located, then the timing restriction will remain in effect.
- If it is anticipated that construction or drilling will occur during Mountain plover nesting season (May 1 – June 15), a BLM biologist will be notified to determine if surveys are necessary prior to beginning operations. If surveys are deemed necessary, depending on the results permission to proceed may or may not, be granted by the BLM Authorized Officer.

#### **For protection of T&E Fish if drawing water from the Green River**

- For areas of fresh water collection, an infiltration gallery will be constructed in a Service approved location. An infiltration gallery is basically a pit or trench dug within the floodplain to a depth below the water table. Water is drawn from the pit rather than from the river directly. If this is not possible, limit pumping within the river to off-channel locations that do not connect to the river during high spring flows.
- If water cannot be drawn using the measures above and the pump head will be located in the river channel where larval fish are known to occur, the following measures apply:
  - Avoid pumping from low-flow or no-flow areas as these habitats tend to concentrate larval fish
  - Avoid pumping to the greatest extent possible, during that period of the year when larval fish may be present (see previous bullet); and
  - Avoid pumping, to the greatest extent possible, during the midnight hours (10:00 p.m. to 2:00 a.m.) as larval drift studies indicate that this is a period of greatest daily activity. Dusk is the preferred pumping time, as larval drift abundance is lowest during this time.
  - Screen all pump intakes with 3/32-inch mesh material.
- Report any fish impinged on the intake screen to the FWS office (801.975.3330) and the:  
Utah Division of Wildlife Resources  
Northeastern Region  
152 East 100 North  
Vernal, UT 84078  
(435) 781-9453

### **Air Quality**

- All internal combustion equipment will be kept in good working order.
- Water or other approved dust suppressants will be used at construction sites and along roads, as determined appropriate by the Authorized Officer. Dust suppressant such as magnesium chloride or fresh water may be used, as needed, during the drilling phase.
- Open burning of garbage or refuse will not occur at well sites or other facilities.
- Drill rigs will be equipped with Tier II or better diesel engines.
- Low bleed pneumatics will be installed on separator dump valves and other controllers.
- During completion, no venting will occur, and flaring will be limited as much as possible. Production equipment and gathering lines will be installed as soon as possible.
- Telemetry will be installed to remotely monitor and control production.
- When feasible, two or more rigs (including drilling and completion rigs) will not be run simultaneously within 200 meters of each other. If two or more rigs must be run simultaneously within 200 meters of each other, then effective public health buffer zones out to 200 meters (m) from the nearest emission source will be implemented. Examples of an effective public health protection buffer zone include the demarcation of a public access exclusion zone by signage at intervals of every 250 feet that is visible from a distance of 125 feet during daylight hours, and a physical buffer such as active surveillance to ensure the property is not accessible by the public during drilling operations. Alternatively, the proponent may demonstrate compliance with the 1-hour NO<sub>2</sub> National Ambient Air Quality Standards (NAAQS) with appropriate and accepted near-field modeling. As part of this demonstration, the proponent may propose alternative mitigation that could include but is not limited to natural gas-fired drill rigs, installation of NO<sub>x</sub> controls, time/use restrictions, and/or drill rig spacing.
- Green completions will be used for all well completion activities where technically feasible.
- Employ enhanced VOC emission controls with 95% control efficiency on production equipment having a potential to emit greater than 5 tons per year.



**DOWNHOLE PROGRAM  
CONDITIONS OF APPROVAL (COAs)**

**SITE SPECIFIC DOWNHOLE COAs:**

- Newfield Production Co. shall adhere to all referenced requirements in the SOP (version: "Greater Monument Butte Green River Development Program", Feb. 16, 2012).
- The operator shall also comply with applicable laws and regulations; with lease terms Onshore Oil and Gas Orders, NTL's and with other orders and instructions of the, authorized officer.

**All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to.** The following items are emphasized:

**DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS**

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB

or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well by CD (compact disc). This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

## **OPERATING REQUIREMENT REMINDERS:**

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at [www.ONRR.gov](http://www.ONRR.gov).
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
  - Operator name, address, and telephone number.
  - Well name and number.
  - Well location (¼¼, Sec., Twn, Rng, and P.M.).
  - Date well was placed in a producing status (date of first production for which royalty will be paid).
  - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
  - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
  - Unit agreement and/or participating area name and number, if applicable.
  - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid,

and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross 29 Submitted By  
Branden Arnold Phone Number 435-401-0223  
Well Name/Number GMBU I-12-9-15  
Qtr/Qtr SW/NE Section 12 Township 9S Range 15E  
Lease Serial Number UTU-74826  
API Number 43-013-51754

Spud Notice – Spud is the initial spudding of the well, not drilling  
out below a casing string.

Date/Time 9/30/13 7:00 AM ☒ PM ☐

Casing – Please report time casing run starts, not cementing  
times.

- ☒ Surface Casing
- ☐ Intermediate Casing
- ☐ Production Casing
- ☐ Liner
- ☐ Other

Date/Time 9/30/13 3:00 AM ☐ PM ☒

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time \_\_\_\_\_ AM ☐ PM ☐

Remarks \_\_\_\_\_

---



BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross 29 Submitted By  
Branden Arnold Phone Number 435-401-0223  
Well Name/Number GMBU I-12-9-15  
Qtr/Qtr SW/NE Section 12 Township 9S Range 15E  
Lease Serial Number UTU-74826  
API Number 43-013-51754

Spud Notice – Spud is the initial spudding of the well, not drilling  
out below a casing string.

Date/Time 9/30/13 7:00 AM ☐ PM ☐

Casing – Please report time casing run starts, not cementing  
times.

- ☐ Surface Casing
- ☐ Intermediate Casing
- ☐ Production Casing
- ☐ Liner
- ☐ Other

Date/Time 9/30/13 3:00 AM ☐ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

**RECEIVED**

**SEP 27 2013**

**DIV. OF OIL, GAS & MINING**

Date/Time \_\_\_\_\_ AM ☐ PM ☐

Remarks \_\_\_\_\_

---

<b>STATE OF UTAH</b> DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		<b>FORM 9</b>
<b>SUNDRY NOTICES AND REPORTS ON WELLS</b>  Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		<b>5. LEASE DESIGNATION AND SERIAL NUMBER:</b> UTU-74826
<b>1. TYPE OF WELL</b> Oil Well		<b>6. IF INDIAN, ALLOTTEE OR TRIBE NAME:</b>
<b>2. NAME OF OPERATOR:</b> NEWFIELD PRODUCTION COMPANY		<b>7. UNIT or CA AGREEMENT NAME:</b> GMBU (GRRV)
<b>3. ADDRESS OF OPERATOR:</b> Rt 3 Box 3630 , Myton, UT, 84052		<b>8. WELL NAME and NUMBER:</b> GMBU I-12-9-15
<b>4. LOCATION OF WELL</b> <b>FOOTAGES AT SURFACE:</b> 1869 FNL 1870 FEL <b>QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN:</b> Qtr/Qtr: SWNE Section: 12 Township: 09.0S Range: 15.0E Meridian: S		<b>9. API NUMBER:</b> 43013517540000
<b>PHONE NUMBER:</b> 435 646-4825 Ext		<b>9. FIELD and POOL or WILDCAT:</b> MONUMENT BUTTE
<b>COUNTY:</b> DUCHESNE		<b>STATE:</b> UTAH
<b>11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA</b>		
<b>TYPE OF SUBMISSION</b>	<b>TYPE OF ACTION</b>	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input checked="" type="checkbox"/> SPUD REPORT Date of Spud: 9/30/2013	<input type="checkbox"/> CASING REPAIR	
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> CHANGE WELL TYPE	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/>	
<b>12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.</b> On 9/30/13 Drill and set 6' of 14" conductor. Drill F/6' to 325' KB of 12 1/4 hole R/U and run 7 joints of 8 5/8 24# J-55 casing set @ 323 KB. On 10/2/13 Cement w/200 sx of G Neat cement returned 8 bbls and bumped plug to 500 psi.		
<b>Accepted by the          Utah Division of          Oil, Gas and Mining          FOR RECORD ONLY          October 10, 2013</b>		
<b>NAME (PLEASE PRINT)</b> Cherei Neilson	<b>PHONE NUMBER</b> 435 646-4883	<b>TITLE</b> Drilling Technician
<b>SIGNATURE</b> N/A	<b>DATE</b> 10/10/2013	

**NEWFIELD****Casing****Conductor**

Legal Well Name GMBU I-12-9-15			Wellbore Name Original Hole		
API/UWI 43013517540000	Surface Legal Location SWNE	Field Name GMBU CTB2	Well Type Development	Well Configuration Type Slant	
Well RC 500347004	County Duchesne	State/Province Utah	Spud Date 9/30/2013 08:30	Final Rig Release Date 10/10/2013 06:00	

<b>Wellbore</b>					
Wellbore Name Original Hole			Kick Off Depth (ftKB)		

Section Des	Size (in)	Actual Top Depth (MD) (ftKB)	Actual Bottom Depth (MD) (ftKB)	Start Date	End Date
Conductor	14	10	16	9/30/2013	9/30/2013

<b>Wellhead</b>				
Type	Install Date	Service	Comment	

<b>Wellhead Components</b>				
Des	Make	Model	SN	WP Top (psi)

Casing			
Casing Description	Set Depth (ftKB)	Run Date	Set Tension (kips)
Conductor	16	9/30/2013	
Centralizers	Scratchers		

<b>Casing Components</b>												
Item Des	OD (in)	ID (in)	Wt (lb/ft)	Grade	Top Thread	Jts	Len (ft)	Top (ftKB)	Btm (ftKB)	Mk-up Tq (ft•lb)	Class	Max OD (in)
Conductor	14	13.500	36.75	H-40		1	6.00	10.0	16.0			

<b>Jewelry Details</b>												
<b>External Casing Packer</b>												
Type	Setting Requirement			Release Requirements			Inflation Method		Vol Inflation (gal)		Equiv Hole Sz (in)	
Inflation Fluid Type	Infl Fl Dens (lb/gal)	P AV Set (psi)		AV Acting Pressure (psi)	P ICV Set (psi)		P ICV Act (psi)		ECP Load (1000lbf)		Seal Load (1000lbf)	

Slotted Liner							
% Open Area (%)	Perforation Min Dimension (in)	Perforation Max Dimension (in)	Axial Perf Spacing (ft)	Perf Rows	Blank Top Length (ft)	Blank Bottom Length (ft)	
Slot Description		Slot Pattern		Slot Length (in)	Slot Width (in)	Slot Frequency	Screen Gauge (ga)

Liner Hanger				
Retrievable?	Elastomer Type	Element Center Depth (ft)	Polish Bore Size (in)	Polish Bore Length (ft)
Slip Description			Set Mechanics	

Setting Procedure												
-------------------	--	--	--	--	--	--	--	--	--	--	--	--

Unsetting Procedure												
---------------------	--	--	--	--	--	--	--	--	--	--	--	--

**NEWFIELD****Casing****Surface**

Legal Well Name GMBU I-12-9-15			Wellbore Name Original Hole		
API/UWI 43013517540000	Surface Legal Location SWNE	Field Name GMBU CTB2	Well Type Development	Well Configuration Type Slant	
Well RC 500347004	County Duchesne	State/Province Utah	Spud Date 9/30/2013 08:30	Final Rig Release Date 10/10/2013 06:00	

<b>Wellbore</b>					
Wellbore Name Original Hole			Kick Off Depth (ftKB)		
Section Des	Size (in)	Actual Top Depth (MD) (ftKB)	Actual Bottom Depth (MD) (ftKB)	Start Date	End Date
Conductor	14	10	16	9/30/2013	9/30/2013
Vertical	12 1/4	16	325	9/30/2013	9/30/2013

<b>Wellhead</b>				
Type	Install Date	Service	Comment	

<b>Wellhead Components</b>				
Des	Make	Model	SN	WP Top (psi)

Casing			
Casing Description	Set Depth (ftKB)	Run Date	Set Tension (kips)
Surface	323	9/30/2013	
Centralizers	Scratchers		
3			

<b>Casing Components</b>												
Item Des	OD (in)	ID (in)	Wt (lb/ft)	Grade	Top Thread	Jts	Len (ft)	Top (ftKB)	Btm (ftKB)	Mk-up Tq (ft•lb)	Class	Max OD (in)
Wellhead	8 5/8	8.097	24.00	J-55	ST&C	1	2.50	9.9	12.4			
Cut off	8 5/8	8.097	24.00	J-55	ST&C	1	42.56	12.4	54.9			
Casing Joints	8 5/8	8.097	24.00	J-55	ST&C	5	223.74	54.9	278.7			
Float Collar	8 5/8	8.097	24.00	J-55	ST&C	1	1.00	278.7	279.7			
Shoe Joint	8 5/8	8.097	24.00	J-55	ST&C	1	41.82	279.7	321.5			
Guide Shoe	8 5/8	8.097	24.00	J-55	ST&C	1	1.50	321.5	323.0			

<b>Jewelry Details</b>							
<b>External Casing Packer</b>							
Type	Setting Requirement	Release Requirements			Inflation Method	Vol Inflation (gal)	Equiv Hole Sz (in)
Inflation Fluid Type	Infl Fl Dens (lb/gal)	P AV Set (psi)	AV Acting Pressure (psi)	P ICV Set (psi)	P ICV Act (psi)	ECP Load (1000lbf)	Seal Load (1000lbf)

<b>Slotted Liner</b>							
% Open Area (%)	Perforation Min Dimension (in)	Perforation Max Dimension (in)	Axial Perf Spacing (ft)	Perf Rows	Blank Top Length (ft)	Blank Bottom Length (ft)	
Slot Description	Slot Pattern			Slot Length (in)	Slot Width (in)	Slot Frequency	Screen Gauge (ga)

Liner Hanger				
Retrievable?	Elastomer Type	Element Center Depth (ft)	Polish Bore Size (in)	Polish Bore Length (ft)
Slip Description			Set Mechanics	

Setting Procedure							
Unsetting Procedure							

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# NDSI SS #1

Submitted By Xabier Lasa Phone Number 823-6014

Well Name/Number GMBU I-12-9-15

Qtr/Qtr SW/NE Section 12 Township 9s Range 15E

Lease Serial Number UTU74826

API Number 43-013-51754

Rig Move Notice – Move drilling rig to new location.

Date/Time 10-6-13 7:00 AM ☐ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time 10-6-13 10:00 AM ☐ PM ☐

Remarks \_\_\_\_\_

---

RECEIVED  
OCT 05 2013  
DIV. OF OIL, GAS & MINING



<b>STATE OF UTAH</b> DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		<b>FORM 9</b>
<b>SUNDRY NOTICES AND REPORTS ON WELLS</b>  Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		<b>5. LEASE DESIGNATION AND SERIAL NUMBER:</b> UTU-74826
<b>1. TYPE OF WELL</b> Oil Well		<b>6. IF INDIAN, ALLOTTEE OR TRIBE NAME:</b>
<b>2. NAME OF OPERATOR:</b> NEWFIELD PRODUCTION COMPANY		<b>7. UNIT or CA AGREEMENT NAME:</b> GMBU (GRRV)
<b>3. ADDRESS OF OPERATOR:</b> Rt 3 Box 3630 , Myton, UT, 84052		<b>8. WELL NAME and NUMBER:</b> GMBU I-12-9-15
<b>4. LOCATION OF WELL</b> <b>FOOTAGES AT SURFACE:</b> 1869 FNL 1870 FEL <b>QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN:</b> Qtr/Qtr: SWNE Section: 12 Township: 09.0S Range: 15.0E Meridian: S		<b>9. API NUMBER:</b> 43013517540000
<b>PHONE NUMBER:</b> 435 646-4825 Ext		<b>9. FIELD and POOL or WILDCAT:</b> MONUMENT BUTTE
<b>COUNTY:</b> DUCHESNE		<b>STATE:</b> UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
<b>TYPE OF SUBMISSION</b>	<b>TYPE OF ACTION</b>	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 11/14/2013	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE TUBING	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. The above well was placed on production on 11/14/2013 at 17:10 hours.		
Accepted by the Utah Division of Oil, Gas and Mining <b>FOR RECORD ONLY</b> November 20, 2013		
<b>NAME (PLEASE PRINT)</b> Jennifer Peatross	<b>PHONE NUMBER</b> 435 646-4885	<b>TITLE</b> Production Technician
<b>SIGNATURE</b> N/A	<b>DATE</b> 11/20/2013	

Form 3160-4  
(March 2012)UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENTFORM APPROVED  
OMB NO. 1004-0137  
Expires: October 31, 2014

## WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. Type of Well <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Dry <input type="checkbox"/> Other b. Type of Completion: <input checked="" type="checkbox"/> New Well <input type="checkbox"/> Work Over <input type="checkbox"/> Deepen <input type="checkbox"/> Plug Back <input type="checkbox"/> Diff. Resvr., Other: _____						5. Lease Serial No. UTU74826			
2. Name of Operator NEWFIELD PRODUCTION COMPANY						6. If Indian, Allottee or Tribe Name			
3. Address ROUTE #3 BOX 3630 MYTON, UT 84052						7. Unit or CA Agreement Name and No. UTU87538X			
3a. Phone No. (include area code) Ph: 435-646-3721						8. Lease Name and Well No. GMBU I-12-9-15			
4. Location of Well (Report location clearly and in accordance with Federal requirements)*  At surface 1869' FNL 1870' FEL (SW/NE) SEC 12 T9S R15E (UTU-74826)  At top prod. interval reported below 1410' FNL 1172' FEL (SE/NE) SEC 12 T9S R15E (UTU-74826)  At total depth 1178' FNL 805' FEL (NE/NE) SEC 12 T9S R15E (UTU-74826)						9. API Well No. 43-013-51754			
14. Date Spudded 09/30/2013						10. Field and Pool or Exploratory MONUMENT BUTTE			
15. Date T.D. Reached 10/10/2013						11. Sec., T., R., M., on Block and Survey or Area SEC 12 T9S R15E Mer SLB			
16. Date Completed 11/14/2013 <input type="checkbox"/> D & A <input checked="" type="checkbox"/> Ready to Prod.						12. County or Parish DUCHESNE			
17. Elevations (DF, RKB, RT, GL)* 6017' GL 6027' KB						13. State UT			
18. Total Depth: MD 6411' TVD 6266'						19. Plug Back T.D.: MD 6359' TVD			
20. Depth Bridge Plug Set: MD TVD						21. Type Electric & Other Mechanical Logs Run (Submit copy of each) DUAL IND GRD, SP, COMP. NEUTRON, GR, CALIPER, CMT BOND			
22. Was well cored? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Submit analysis) Was DST run? <input checked="" type="checkbox"/> No <input type="checkbox"/> Yes (Submit report) Directional Survey? <input type="checkbox"/> No <input checked="" type="checkbox"/> Yes (Submit copy)									
23. Casing and Liner Record (Report all strings set in well)									
Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24	0'	323'		200 CLASS G			
7-7/8"	5-1/2" J-55	15.50	0'	6406'		290 Econocem		32'	
						480Expandacem			
24. Tubing Record									
Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	
2-7/8"	EOT@5974'	TA@5872'							
25. Producing Intervals									
Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status			
A) Green River	4452'	5916'	4452' - 5916' MD	0.34	62				
B)									
C)									
D)									
26. Perforation Record									
27. Acid, Fracture, Treatment, Cement Squeeze, etc.									
Depth Interval		Amount and Type of Material							
4452' - 5916' MD		Frac w/ 188900#s of 20/40 white sand in 2076 bbls of Lightning 17 fluid, in 4 stages.							
28. Production - Interval A									
Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
11/6/13	11/16/13	24	→	87	38	51			2.5 X 1.75 RHAC
Choke Size	Tbg. Press. Flwg. SI	Csg. Press. SI	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	
28a. Production - Interval B									
Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press. SI	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

\*(See instructions and spaces for additional data on page 2)

## 28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

## 28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

## 29. Disposition of Gas (Solid, used for fuel, vented, etc.)

## 30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers  
GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
				GARDEN GULCH MARK GARDEN GULCH 1	3852' 4083'
				GARDEN GULCH 2 POINT 3	4197' 4461'
				X MRKR Y MRKR	4729' 4763'
				DOUGLAS CREEK MRK BI CARBONATE MRK	4879' 5115'
				B LIMESTONE MRK CASTLE PEAK	5215' 5800'
				BASAL CARBONATE WASATCH	6275' 6405'

## 32. Additional remarks (include plugging procedure):

## 33. Indicate which items have been attached by placing a check in the appropriate boxes:

- ☐ Electrical/Mechanical Logs (1 full set req'd.)     
 ☐ Geologic Report     
 ☐ DST Report     
 ☒ Directional Survey  
☐ Sundry Notice for plugging and cement verification     
 ☐ Core Analysis     
 ☒ Other: Drilling daily activity

## 34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)\*

Name (please print) Heather Calder      Title Regulatory Technician  
 Signature Heather Calder      Date 11/19/2013

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 3)

(Form 3160-4, page 2)



## **NEWFIELD EXPLORATION**

**USGS Myton SW (UT)  
SECTION 12 T9S, R15E  
I-12-9-15  
Wellbore #1**

**Design: Actual**

## **End of Well Report**

**14 October, 2013**





# Payzone Directional

## End of Well Report



<b>Company:</b> NEWFIELD EXPLORATION <b>Project:</b> USGS Myton SW (UT) <b>Site:</b> SECTION 12 T9S, R15E <b>Well:</b> I-12-9-15 <b>Wellbore:</b> Wellbore #1 <b>Design:</b> Actual		<b>Local Co-ordinate Reference:</b> Well I-12-9-15 I-12-9-15 @ 6027.0ft (NDSI SS #1) I-12-9-15 @ 6027.0ft (NDSI SS #1) True Minimum Curvature EDM 2003.21 Single User Db	
<b>Project</b> USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA		<b>System Datum:</b> Mean Sea Level	
<b>Map System:</b> US State Plane 1983 <b>Geo Datum:</b> North American Datum 1983 <b>Map Zone:</b> Utah Central Zone			
<b>Site</b> SECTION 12 T9S, R15E			
<b>Site Position:</b>		<b>Latitude:</b> 40° 2' 43.749 N <b>Longitude:</b> 110° 11' 4.317 W <b>Grid Convergence:</b> 0.84 °	
<b>From:</b> Map		<b>North:</b> 7,188,000.00 ft <b>East:</b> 2,008,669.32 ft <b>Slot Radius:</b> "	
<b>Position Uncertainty:</b> 0.0 ft			
<b>Well</b> I-12-9-15, SHL LAT: 40 02 51.25 LONG: -110 10 39.78			
<b>Well Position</b>		<b>North:</b> 7,188,787.03 ft <b>East:</b> 2,010,565.96 ft <b>Wellhead Elevation:</b> 6,027.0 ft	
<b>Position Uncertainty</b>		<b>Latitude:</b> 40° 2' 51.250 N <b>Longitude:</b> 110° 10' 39.780 W <b>Ground Level:</b> 6,017.0 ft	
<b>Wellbore</b> Wellbore #1			
<b>Magnetics</b>		<b>Field Strength (nT)</b> 52,149	
<b>Model Name</b> IGRF2010		<b>Dip Angle (°)</b> 65.75	
<b>Sample Date</b> 6/27/2012		<b>Declination (°)</b> 11.23	
<b>Design</b> Actual		<b>Tie On Depth:</b> 0.0	
<b>Audit Notes:</b>		<b>Phase:</b> ACTUAL	
<b>Version:</b> 1.0		<b>Depth From (TVD) (ft)</b> 0.0	
<b>Vertical Section:</b>		<b>+N/-S (ft)</b> 0.0	
<b>From (ft)</b> 343.0		<b>+E/-W (ft)</b> 0.0	
<b>To (ft)</b> 6,411.0		<b>Direction (°)</b> 57.04	
<b>Survey Program</b>		<b>Date</b> 10/14/2013	
<b>From (ft)</b> 343.0		<b>Survey (Wellbore)</b> Survey #1 (Wellbore #1)	
<b>To (ft)</b> 6,411.0		<b>Tool Name</b> MWD	
<b>Description</b>		<b>MWD - Standard</b>	





# Payzone Directional

## End of Well Report



**Company:** NEWFIELD EXPLORATION  
**Project:** USGS Mylon SW (UT)  
**Site:** SECTION 12 T9S, R15E  
**Well:** I-12-9-15  
**Wellbore:** Wellbore #1  
**Design:** Actual

**Local Co-ordinate Reference:** Well I-12-9-15  
**TVD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**MD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**North Reference:** True  
**Survey Calculation Method:** Minimum Curvature  
**Database:** EDM 2003.21 Single User Db

Survey	MD (ft)	Inc (°)	Azi (azimuth) (°)	TVD (ft)	V. Sec (ft)	N/S (ft)	E/W (ft)	D/Leg (°/100ft)	Build (°/100ft)	Turn (°/100ft)
	0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
	343.0	1.10	87.10	343.0	2.8	0.2	3.3	0.32	0.32	0.00
	374.0	1.50	88.70	374.0	3.5	0.2	4.0	1.30	1.29	5.16
	404.0	1.30	75.00	404.0	4.1	0.3	4.7	1.30	-0.67	-45.67
	434.0	1.50	67.50	434.0	4.8	0.5	5.4	0.90	0.67	-25.00
	465.0	1.90	63.50	464.9	5.7	0.9	6.2	1.35	1.29	-12.90
	495.0	1.80	65.60	494.9	6.7	1.3	7.1	0.40	-0.33	7.00
	526.0	1.90	55.20	525.9	7.7	1.8	8.0	1.13	0.32	-33.55
	556.0	2.50	55.20	555.9	8.8	2.5	8.9	2.00	2.00	0.00
	586.0	2.50	48.80	585.9	10.1	3.3	10.0	0.93	0.00	-21.33
	617.0	3.00	56.10	616.8	11.6	4.2	11.1	1.97	1.61	23.55
	646.0	3.30	49.20	645.8	13.2	5.1	12.4	1.67	1.03	-23.79
	677.0	3.60	59.10	676.7	15.1	6.2	13.9	2.15	0.97	31.94
	707.0	3.70	53.30	706.7	17.0	7.3	15.5	1.27	0.33	-19.33
	737.0	3.90	51.10	736.6	18.9	8.5	17.1	0.82	0.67	-7.33
	767.0	4.00	53.50	766.5	21.0	9.8	18.7	0.64	0.33	8.00
	797.0	4.40	49.50	796.4	23.2	11.1	20.4	1.65	1.33	-13.33
	828.0	4.60	51.00	827.3	25.6	12.7	22.3	0.75	0.65	4.84
	858.0	5.10	54.90	857.2	28.1	14.2	24.3	2.00	1.67	13.00
	889.0	5.10	59.20	888.1	30.9	15.7	26.6	1.23	0.00	13.87
	919.0	5.70	59.20	918.0	33.7	17.2	29.0	2.00	2.00	0.00
	950.0	5.70	59.30	948.8	36.8	18.7	31.7	0.03	0.00	0.32
	980.0	6.00	60.40	978.7	39.8	20.3	34.3	1.07	1.00	3.67
	1,011.0	6.20	57.10	1,009.5	43.1	22.0	37.1	1.30	0.65	-10.65
	1,041.0	6.50	59.80	1,039.3	46.4	23.7	40.0	1.41	1.00	9.00
	1,085.0	7.30	61.60	1,083.0	51.7	26.3	44.6	1.88	1.82	4.09
	1,129.0	8.00	61.60	1,126.6	57.6	29.1	49.7	1.59	1.59	0.00



# Payzone Directional

## End of Well Report



**Company:** NEWFIELD EXPLORATION  
**Project:** USGS Mylon SW (UT)  
**Site:** SECTION 12 T9S, R15E  
**Well:** I-12-9-15  
**Wellbore:** Wellbore #1  
**Design:** Actual

**Local Co-ordinate Reference:** Well I-12-9-15  
**TVD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**MD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**North Reference:** True  
**Survey Calculation Method:** Minimum Curvature  
**Database:** EDM 2003.21 Single User Db

Survey	MD (ft)	Inc (°)	Azi (azimuth) (°)	TVD (ft)	V. Sec (ft)	N/S (ft)	E/W (ft)	D/Leg (°/100ft)	Build (°/100ft)	Turn (°/100ft)
	1,173.0	8.40	61.40	1,170.2	63.8	32.1	55.3	0.91	0.91	-0.45
	1,218.0	9.30	59.90	1,214.6	70.7	35.5	61.3	2.06	2.00	-3.33
	1,264.0	9.50	58.70	1,260.0	78.2	39.3	67.7	0.61	0.43	-2.61
	1,310.0	9.90	58.70	1,305.3	86.0	43.3	74.4	0.87	0.87	0.00
	1,364.0	10.50	58.80	1,358.5	95.5	48.3	82.5	1.11	1.11	0.19
	1,400.0	11.40	57.30	1,393.8	102.4	51.9	88.3	2.62	2.50	-4.17
	1,444.0	11.90	57.20	1,436.9	111.3	56.7	95.8	1.14	1.14	-0.23
	1,490.0	12.40	56.40	1,481.9	120.9	62.0	103.9	1.15	1.09	-1.74
	1,534.0	12.70	56.00	1,524.8	130.5	67.4	111.9	0.71	0.68	-0.91
	1,580.0	13.00	55.60	1,569.7	140.7	73.1	120.3	0.68	0.65	-0.87
	1,623.0	13.40	53.50	1,611.6	150.5	78.8	128.3	1.45	0.93	-4.88
	1,669.0	13.80	53.20	1,656.3	161.3	85.3	137.0	0.88	0.87	-0.65
	1,715.0	13.60	52.80	1,701.0	172.2	91.8	145.7	0.48	-0.43	-0.87
	1,761.0	13.80	51.70	1,745.6	183.1	98.5	154.3	0.71	0.43	-2.39
	1,805.0	13.50	49.90	1,788.4	193.4	105.0	162.4	1.18	-0.68	-4.09
	1,849.0	13.10	49.60	1,831.2	203.4	111.6	170.1	0.92	-0.91	-0.68
	1,892.0	12.90	50.30	1,873.1	213.0	117.8	177.5	0.59	-0.47	1.63
	1,936.0	13.40	51.00	1,916.0	223.0	124.2	185.2	1.19	1.14	1.59
	1,980.0	13.10	52.20	1,958.8	233.0	130.4	193.1	0.92	-0.68	2.73
	2,024.0	13.00	53.20	2,001.7	242.9	136.4	201.0	0.56	-0.23	2.27
	2,070.0	13.00	55.20	2,046.5	253.2	142.5	209.4	0.98	0.00	4.35
	2,116.0	13.20	56.40	2,091.3	263.7	148.4	218.0	0.73	0.43	2.61
	2,160.0	13.10	55.20	2,134.1	273.7	154.0	226.3	0.66	-0.23	-2.73
	2,204.0	13.20	55.80	2,177.0	283.7	159.6	234.6	0.38	0.23	1.36
	2,248.0	13.60	56.40	2,219.8	293.9	165.3	243.0	0.96	0.91	1.36
	2,293.0	13.60	57.30	2,263.5	304.5	171.1	251.9	0.47	0.00	2.00
	2,337.0	13.80	58.40	2,306.3	314.9	176.7	260.7	0.75	0.45	2.50



# Payzone Directional

## End of Well Report



**Company:** NEWFIELD EXPLORATION  
**Project:** USGS Mylon SW (UT)  
**Site:** SECTION 12 T9S, R15E  
**Well:** I-12-9-15  
**Wellbore:** Wellbore #1  
**Design:** Actual

**Local Co-ordinate Reference:** Well I-12-9-15  
**TVD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**MD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**North Reference:** True  
**Survey Calculation Method:** Minimum Curvature  
**Database:** EDM 2003.21 Single User Db

Survey	MD (ft)	Inc (°)	Azi (azimuth) (°)	TVD (ft)	V. Sec (ft)	N/S (ft)	E/W (ft)	DLeg (°/100ft)	Build (°/100ft)	Turn (°/100ft)
	2,381.0	14.20	60.50	2,349.0	325.5	182.1	269.9	1.47	0.91	4.77
	2,427.0	14.50	59.60	2,393.5	336.9	187.8	279.8	0.81	0.85	-1.96
	2,471.0	14.80	59.90	2,436.1	348.0	193.4	289.4	0.70	0.88	0.68
	2,517.0	15.00	60.10	2,480.5	359.8	199.3	299.6	0.45	0.43	0.43
	2,562.0	15.20	59.60	2,524.0	371.5	205.2	309.8	0.53	0.44	-1.11
	2,606.0	15.10	59.70	2,566.5	383.0	211.0	319.7	0.23	-0.23	0.23
	2,652.0	14.90	57.80	2,610.9	394.9	217.2	329.9	1.15	-0.43	-4.13
	2,696.0	14.40	56.00	2,653.5	406.0	223.2	339.2	1.54	-1.14	-4.09
	2,742.0	14.30	55.10	2,698.0	417.4	229.7	348.6	0.53	-0.22	-1.96
	2,786.0	14.30	55.20	2,740.7	428.3	235.9	357.5	0.06	0.00	0.23
	2,829.0	14.50	55.80	2,782.3	439.0	241.9	366.3	0.58	0.47	1.40
	2,875.0	14.80	57.00	2,826.8	450.6	248.4	376.0	0.93	0.65	2.61
	2,921.0	15.10	58.90	2,871.3	462.5	254.7	386.1	1.25	0.65	4.13
	2,965.0	15.70	59.04	2,913.7	474.2	260.7	396.1	1.37	1.36	0.32
	3,011.0	16.00	58.90	2,957.9	486.7	267.2	406.8	0.66	0.65	-0.30
	3,055.0	16.00	57.90	3,000.2	498.8	273.5	417.2	0.63	0.00	-2.27
	3,100.0	15.90	56.10	3,043.5	511.2	280.3	427.5	1.12	-0.22	-4.00
	3,144.0	15.70	56.10	3,085.8	523.2	286.9	437.5	0.45	-0.45	0.00
	3,190.0	15.90	55.60	3,130.1	535.7	294.0	447.9	0.53	0.43	-1.09
	3,234.0	15.20	55.90	3,172.5	547.5	300.6	457.6	1.60	-1.59	0.68
	3,277.0	14.40	55.60	3,214.1	558.5	306.8	466.7	1.87	-1.86	-0.70
	3,323.0	14.90	55.10	3,258.6	570.1	313.4	476.3	1.12	1.09	-1.09
	3,369.0	14.90	56.40	3,303.0	581.9	320.1	486.0	0.73	0.00	2.83
	3,415.0	14.80	55.20	3,347.5	593.7	326.7	495.8	0.70	-0.22	-2.61
	3,459.0	14.90	56.30	3,390.0	605.0	333.0	505.1	0.68	0.23	2.50
	3,504.0	14.70	56.00	3,433.5	616.5	339.4	514.6	0.48	-0.44	-0.67
	3,550.0	14.90	56.80	3,478.0	628.2	345.9	524.4	0.62	0.43	1.74



# Payzone Directional

## End of Well Report



**Company:** NEWFIELD EXPLORATION  
**Project:** USGS Myton SW (UT)  
**Site:** SECTION 12 T9S, R15E  
**Well:** I-12-9-15  
**Wellbore:** Wellbore #1  
**Design:** Actual

**Local Co-ordinate Reference:** Well I-12-9-15  
**TVD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**MD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**North Reference:** True  
**Survey Calculation Method:** Minimum Curvature  
**Database:** EDM 2003.21 Single User Db

Survey	MD (ft)	Inc (°)	Azi (azimuth) (°)	TVD (ft)	V. Sec (ft)	N/S (ft)	E/W (ft)	D/Leg (°/100ft)	Build (°/100ft)	Turn (°/100ft)
	3,594.0	14.70	56.80	3,520.5	639.5	352.1	533.8	0.45	-0.45	0.00
	3,640.0	14.40	56.70	3,565.1	651.0	358.4	543.5	0.65	-0.65	-0.22
	3,684.0	14.20	55.40	3,607.7	661.9	364.5	552.5	0.86	-0.45	-2.95
	3,729.0	13.80	55.30	3,651.4	672.8	370.7	561.5	0.89	-0.89	-0.22
	3,775.0	13.40	54.80	3,696.1	683.6	376.9	570.3	0.91	-0.87	-1.09
	3,821.0	12.60	55.50	3,740.9	693.9	382.8	578.8	1.77	-1.74	1.52
	3,867.0	12.30	56.30	3,785.8	703.9	388.4	587.0	0.75	-0.65	1.74
	3,911.0	12.00	56.00	3,828.8	713.1	393.5	594.7	0.70	-0.68	-0.68
	3,956.0	11.90	56.10	3,872.8	722.4	398.7	602.5	0.23	-0.22	0.22
	4,002.0	12.00	58.00	3,917.9	731.9	403.9	610.5	0.88	0.22	4.13
	4,046.0	12.30	59.30	3,960.9	741.2	408.7	618.4	0.92	0.68	2.95
	4,092.0	12.30	61.40	4,005.8	751.0	413.6	626.9	0.97	0.00	4.57
	4,136.0	13.10	60.30	4,048.7	760.6	418.3	635.3	1.90	1.82	-2.50
	4,180.0	13.60	60.60	4,091.5	770.8	423.3	644.2	1.15	1.14	0.68
	4,225.0	13.80	60.10	4,135.3	781.4	428.6	653.4	0.52	0.44	-1.11
	4,269.0	14.20	58.20	4,178.0	792.1	434.0	662.6	1.38	0.91	-4.32
	4,315.0	13.90	56.40	4,222.6	803.2	440.1	672.0	1.15	-0.65	-3.91
	4,359.0	13.80	55.80	4,265.3	813.8	445.9	680.7	0.40	-0.23	-1.36
	4,405.0	13.30	53.20	4,310.0	824.5	452.2	689.5	1.71	-1.09	-5.65
	4,451.0	13.10	53.10	4,354.8	835.0	458.5	697.9	0.44	-0.43	-0.22
	4,496.0	12.90	53.20	4,398.7	845.1	464.6	706.0	0.45	-0.44	0.22
	4,540.0	12.70	54.00	4,441.6	854.8	470.3	713.8	0.61	-0.45	1.82
	4,584.0	12.50	54.40	4,484.5	864.4	476.0	721.6	0.50	-0.45	0.91
	4,628.0	12.80	55.00	4,527.4	874.0	481.5	729.5	0.74	0.68	1.36
	4,672.0	13.70	55.70	4,570.3	884.1	487.3	737.8	2.08	2.05	1.59
	4,715.0	14.20	55.90	4,612.0	894.5	493.1	746.3	1.17	1.16	0.47
	4,759.0	14.10	57.50	4,654.7	905.2	499.0	755.3	0.92	-0.23	3.64



# Payzone Directional

## End of Well Report



**Company:** NEWFIELD EXPLORATION  
**Project:** USGS Mylon SW (UT)  
**Site:** SECTION 12 T9S, R15E  
**Well:** I-12-9-15  
**Wellbore:** Wellbore #1  
**Design:** Actual

**Local Co-ordinate Reference:** Well I-12-9-15  
**TVD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**MD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**North Reference:** True  
**Survey Calculation Method:** Minimum Curvature  
**Database:** EDM 2003.21 Single User Db

### Survey

MD (ft)	Inc (°)	Azi (azimuth) (°)	TVD (ft)	V. Sec (ft)	N/S (ft)	E/W (ft)	D/Leg (°/100ft)	Build (°/100ft)	Turn (°/100ft)
4,805.0	13.80	59.30	4,599.3	916.3	504.8	764.8	1.15	-0.65	3.91
4,851.0	13.30	59.50	4,744.0	927.1	510.3	774.1	1.09	-1.09	0.43
4,897.0	12.90	61.30	4,788.8	937.5	515.4	783.1	1.24	-0.87	3.91
4,944.0	12.80	64.30	4,834.6	947.9	520.2	792.4	1.44	-0.21	6.38
4,988.0	12.70	63.40	4,877.6	957.5	524.5	801.1	0.51	-0.23	-2.05
5,034.0	12.90	63.50	4,922.4	967.7	529.0	810.2	0.44	0.43	0.22
5,079.8	13.40	64.20	4,967.0	978.0	533.6	819.6	1.14	1.09	1.52
<b>I-12-9-15 TGT</b>									
5,080.0	13.40	64.20	4,967.2	978.1	533.7	819.6	1.14	1.09	1.47
5,126.0	13.10	62.70	5,012.0	988.5	538.4	829.1	0.99	-0.65	-3.26
5,171.0	12.90	59.80	5,055.8	998.6	543.2	837.9	1.52	-0.44	-6.44
5,215.0	12.30	57.80	5,098.8	1,008.2	548.2	846.2	1.69	-1.36	-4.55
5,259.0	11.90	55.90	5,141.8	1,017.4	553.2	853.9	1.28	-0.91	-4.32
5,305.0	11.60	54.40	5,186.8	1,026.8	558.6	861.6	0.93	-0.65	-3.26
5,351.0	11.30	53.10	5,231.9	1,035.9	564.0	868.9	0.86	-0.65	-2.83
5,394.0	11.50	51.80	5,274.1	1,044.4	569.2	875.7	0.76	0.47	-3.02
5,438.0	12.10	51.00	5,317.1	1,053.3	574.8	882.7	1.41	1.36	-1.82
5,482.0	12.70	53.00	5,360.1	1,062.8	580.6	890.1	1.68	1.36	4.55
5,526.0	13.00	54.00	5,403.0	1,072.5	586.4	898.0	0.85	0.68	2.27
5,572.0	13.10	56.90	5,447.8	1,082.9	592.3	906.6	1.44	0.22	6.30
5,617.0	13.70	57.90	5,491.6	1,093.3	597.9	915.3	1.43	1.33	2.22
5,661.0	13.50	61.00	5,534.4	1,103.7	603.2	924.3	1.72	-0.45	7.05
5,707.0	12.80	66.00	5,579.2	1,114.1	607.9	933.6	2.90	-1.52	10.87
5,753.0	12.40	67.50	5,624.1	1,123.9	611.8	942.8	1.12	-0.87	3.26
5,797.0	11.70	67.00	5,667.1	1,133.0	615.4	951.3	1.61	-1.59	-1.14
5,841.0	11.70	64.80	5,710.2	1,141.8	619.0	959.4	1.01	0.00	-5.00
5,887.0	12.20	61.90	5,755.2	1,151.3	623.3	967.9	1.70	1.09	-6.30





# Payzone Directional

## End of Well Report



**Company:** NEWFIELD EXPLORATION  
**Project:** USGS Mylon SW (UT)  
**Site:** SECTION 12 T9S, R15E  
**Well:** I-12-9-15  
**Wellbore:** Wellbore #1  
**Design:** Actual

**Local Co-ordinate Reference:** Well I-12-9-15  
**TVD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**MD Reference:** I-12-9-15 @ 6027.0ft (NDSI SS #1)  
**North Reference:** True  
**Survey Calculation Method:** Minimum Curvature  
**Database:** EDM 2003.21 Single User Db

Survey	MD (ft)	Inc (°)	Azi (azimuth) (°)	TVD (ft)	V. Sec (ft)	N/S (ft)	E/W (ft)	D/Leg (°/100ft)	Build (°/100ft)	Turn (°/100ft)
	5,930.0	12.80	60.60	5,797.2	1,160.5	627.8	976.1	1.54	1.40	-3.02
	5,976.0	13.40	59.20	5,842.0	1,171.0	633.0	985.1	1.48	1.30	-3.04
	6,020.0	13.40	57.20	5,884.8	1,181.1	638.4	993.8	1.05	0.00	-4.55
	6,066.0	13.90	55.60	5,929.5	1,192.0	644.4	1,002.8	1.36	1.09	-3.48
	6,112.0	13.80	53.90	5,974.1	1,203.0	650.7	1,011.8	0.91	-0.22	-3.70
	6,158.0	13.70	54.60	6,018.8	1,213.9	657.1	1,020.7	0.42	-0.22	1.52
	6,201.0	13.80	54.40	6,060.6	1,224.1	663.1	1,029.0	0.26	0.23	-0.47
	6,245.0	13.20	52.80	6,103.4	1,234.4	669.2	1,037.3	1.61	-1.36	-3.64
	6,289.0	12.50	53.30	6,146.3	1,244.1	675.0	1,045.1	1.61	-1.59	1.14
	6,333.0	11.70	52.90	6,189.3	1,253.3	680.6	1,052.5	1.83	-1.82	-0.91
	6,356.0	12.00	51.00	6,211.8	1,258.1	683.5	1,056.2	2.14	1.30	-8.26
	6,411.0	12.00	51.00	6,265.6	1,269.4	690.7	1,065.1	0.00	0.00	0.00




Checked By: \_\_\_\_\_

Approved By: \_\_\_\_\_

Date: \_\_\_\_\_

Project: USGS Myton SW (UT)  
 Site: SECTION 12 T9S, R15E  
 Well: I-12-9-15  
 Wellbore: Wellbore #1  
 Design: Actual

Azimuths to True North  
 Magnetic North: 11.23°  
 Magnetic Field  
 Strength: 52149.3snT  
 Dip Angle: 65.75°  
 Date: 6/27/2012  
 Model: IGRF2010

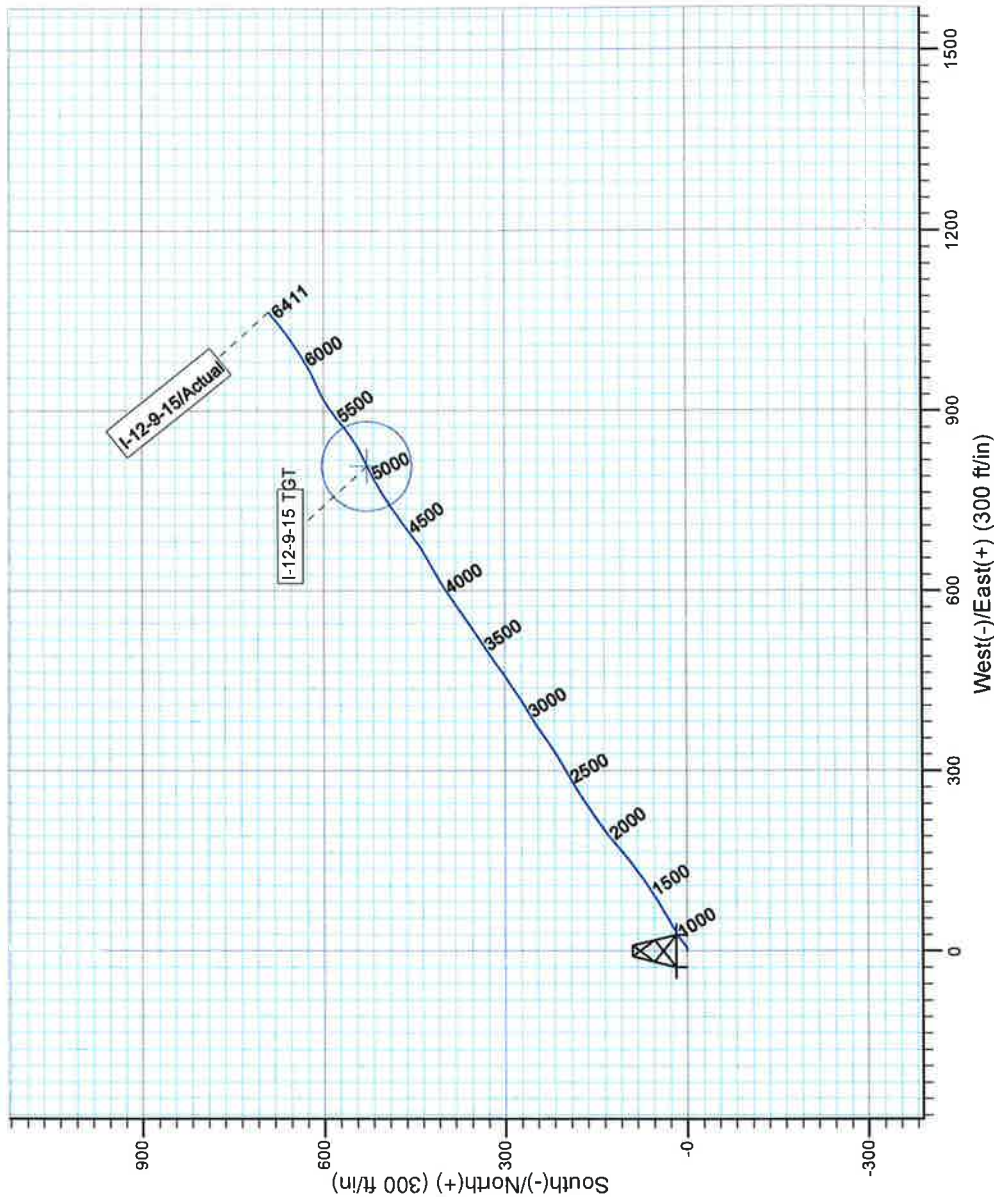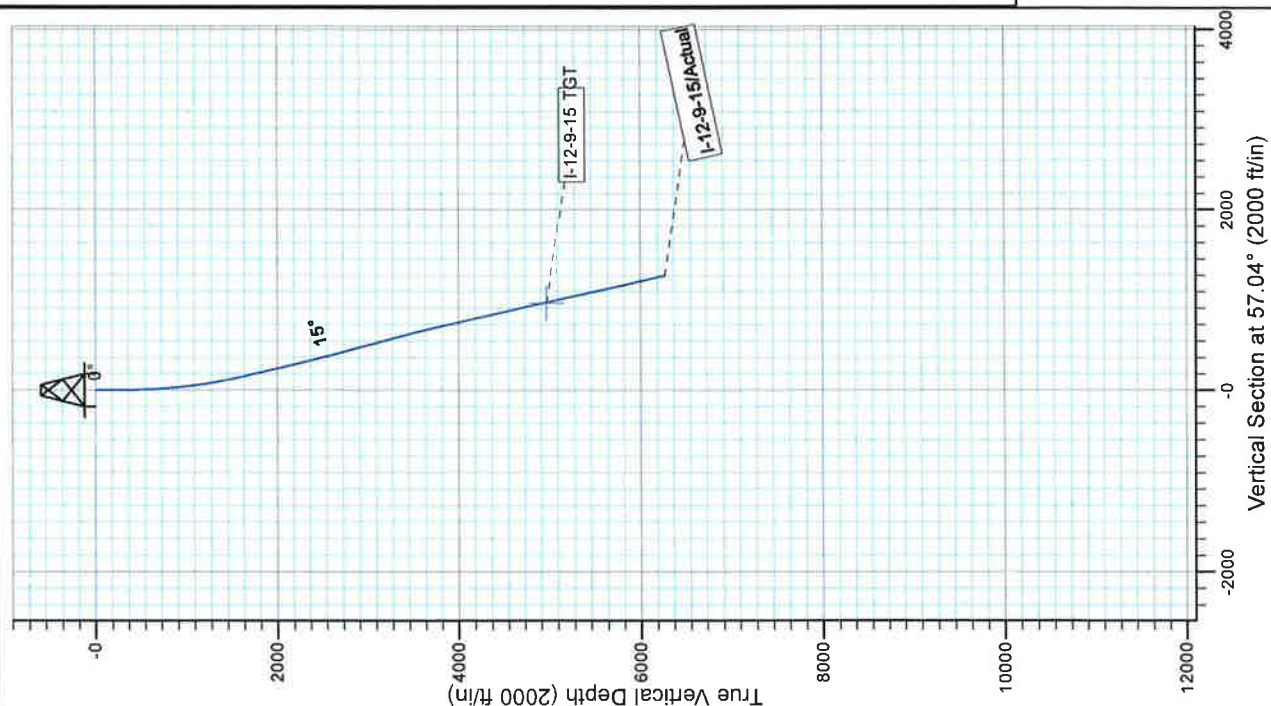

Design: Actual (I-12-9-15/Wellbore #1)

Created By: Sarah Webb

Date: 11:28, October 14 2013

THIS SURVEY IS CORRECT TO THE BEST OF  
 MY KNOWLEDGE AND IS SUPPORTED  
 BY ACTUAL FIELD DATA

NEWFIELD



Well Name: GMBU I-12-9-15

## Summary Rig Activity

Job Category	Job Start Date		Job End Date	
<b>Daily Operations</b>				
Report Start Date	Report End Date	24hr Activity Summary		
10/29/2013	10/30/2013	Run CBL, Press test Csg, Valves, BOP & Frac Valve, Perforate 1st Stage		
Start Time		End Time	Comment	
	00:00	07:00	SDFN	
Start Time		End Time	Comment	
	07:00	09:00	Run CBL Form 6316' to surface Cement Top @ 32'	
Start Time		End Time	Comment	
	09:00	11:00	Press test Csg , Csg Valves, BOP & Frac Valve 300 psi low, 4300psi high	
Start Time		End Time	Comment	
	11:00	12:00	Perforate CP-2 Sds @ 5912-16', 5902-03', 5882-83', 5870-72', CP1/2 sds @ 5837-38', W/ 3-1/8 csg guns 2SPF, (18 shots) POOH CWI Lock down BOPs	
Start Time		End Time	Comment	
	12:00	00:00	SDFN	
Report Start Date	Report End Date	24hr Activity Summary		
10/31/2013	11/1/2013	Frac & Flow back Well		
Start Time		End Time	Comment	
	00:00	06:00	SDFN	
Start Time		End Time	Comment	
	06:00	07:00	Safety Meeting JSA, Press test Pumps & Lines	
Start Time		End Time	Comment	
	07:00	07:45	Break Down CP sds @ 3592psi @ 7BPM w/ 3.5 bbls 7% kcl ISIP 308psi, W/ .50FG, Pump 55,200# 20/40 white sand ISIP 1896 psi .78FG, max rate 40bpm, avg rate 38.6bpm, max press 3129psi, avg press 2558psi. 640 Total bbls pumped	
Start Time		End Time	Comment	
	07:45	08:45	RIH W/ CFTP & 3-1/8" Csg Guns 2SPF Set CFTP @ 5630' & Perforate the LODC sds @ 5558-60', 5525-26', 5518-19', 5486-87', 5472-73', 5446-47', 5424-26', A-1 sds @ 5296-97', 20 shots total, POOH RD W/L	
Start Time		End Time	Comment	
	08:45	09:30	Break Down LODC sds @ 2748psi @ 5bpm Pump 87,400# 20/40 white sand ISIP 1779 psi .78FG, max rate 43 bpm, avg rate 42.6 bpm, max press 2776 psi, avg press 2526 psi. 1205 Total bbls pumped Cut 110,600# 500psi increase during 5 to 6# ramp	
Start Time		End Time	Comment	
	09:30	10:30	RIH W/ CFTP & 3-1/8 Csg Guns 3spf set CFTP @ 5170' perforate the C-Sand @ 5078-82', 12 shots. POOH CWI	
Start Time		End Time	Comment	
	10:30	11:00	Break Down C-Sand sds @ 3212 psi @ 4 bpm Pump 21,100# 20/40 white sand ISIP 1794 psi .81FG, max rate 24.3 bpm, avg rate 24 bpm, max press 2819 psi, avg press 2541 psi. 308 Total bbls pumped	
Start Time		End Time	Comment	
	11:00	12:00	RIH W/ CFTP & 3-1/8 Csg Guns 2spf set CFTP @ 4710' perforate the PB-10 sds @ 4642-44', 4651-53', GB-6 sds @ 4452-54', 12 shots. POOH CWI	
Start Time		End Time	Comment	
	12:00	12:30	Break Down PB-10 & GB-6 sds @ 2388 psi @ 5 bpm Pump 30,100# 20/40 white sand ISIP 2223 psi .94FG, max rate 24.4 bpm, avg rate 24 bpm, max press 2911 psi, avg press 2613 psi. 348 Total bbls pumped	
Start Time		End Time	Comment	
	12:30	14:30	SICP 1820 psi Open Well to pit on 24/64 choke flow back @ 3 bpm Flowed Back 220 bbls turned to Oil & Gas CWI	
Start Time		End Time	Comment	
	14:30	00:00	SDFN	
Report Start Date	Report End Date	24hr Activity Summary		
11/1/2013	11/2/2013	MIRUWOR, NU NOPS, Test BOPS, RIH w/ 2 7/8" drill string.		



NEWFIELD



Well Name: GMBU I-12-9-15

## Summary Rig Activity

Start Time	00:00	End Time	05:30	Comment
				SDFN
Start Time	05:30	End Time	07:00	Comment
				Crew Travel. Safety Meeting. JSA
Start Time	07:00	End Time	08:15	Comment
				Rig Move
Start Time	08:15	End Time	09:30	Comment
				Multitasking, spot rig and equipment.
Start Time	09:30	End Time	10:30	Comment
				Rig up WOR, RU workfloor, NU BOPS
Start Time	10:30	End Time	13:00	Comment
				Pressure test DO stack and vlvs.
Start Time	13:00	End Time	14:30	Comment
				Prep and tally tbq. RU pipe lifting ram, X-over to and RU pipe
Start Time	14:30	End Time	17:30	Comment
				TIH w/ bit, bit sub, 1 jnt, SN, 132 jnts tbq. Install washington rubber and divert oil to pit while TIH.
Start Time	17:30	End Time	18:30	Comment
				SD @ 4287'. RU pwr swl. Secure location and SDFN.
Start Time	18:30	End Time	00:00	Comment
				SDFN
Report Start Date 11/4/2013 Report End Date 11/5/2013 24hr Activity Summary DO/CO through KP and all frac frac plgs. Circ cln and SDFN.				
Start Time	00:00	End Time	06:30	Comment
				SDFN
Start Time	06:30	End Time	07:00	Comment
				Safety Meeting
Start Time	07:00	End Time	08:00	Comment
				RU PUMP LINES AND RETURN LINES. PUMP TO CATCH CIRC.
Start Time	08:00	End Time	17:00	Comment
				DRILL OUT KILL PLUG @ 4350' AND TOOK KICK. CIRC GASSES OUT. SWIVEL IN 11 JNTS TO TAG 2ND PLUG @ 4730'. DRILL OUT PLUG. SWIVEL IN 13 JNTS TO TAG FILL ON TOP OF 3RD PLUG @ 5170'. C/O SAND AND DRILL OUT PLUG. SWIVEL IN 10 MORE JNTS TO TAG 120' OF FILL ON TOP OF 4TH PLUG @ 5630'. DRILL OUT PLUG. SWIVEL IN 10 JNTS AND CIRC BOTTOMS UP. SWIFN.
Start Time	17:00	End Time	17:30	Comment
				DRAIN PUMP AND LINES. CLEAN LOCATION, SDFN.
Start Time	17:30	End Time	00:00	Comment
				SDFN
Report Start Date 11/5/2013 Report End Date 11/6/2013 24hr Activity Summary Finish Clean Out Trip Tbg				
Start Time	00:00	End Time	05:30	Comment
				SDFN
Start Time	05:30	End Time	07:00	Comment
				Travel time Safety Meeting JSA
Start Time	07:00	End Time	07:30	Comment
				RU PUMP AND RETURN LINES.
Start Time	07:30	End Time	08:30	Comment
				SWIVEL IN 2 JNTS AND TAG FILL. CIRC 1 JNT IN AND CIRC BOTTOMS UP.
Start Time	08:30	End Time	10:00	Comment
				FLOW BACK/ BLEED DOWN WELL AND RU NEW RETURN LINES FROM STACK TO PIT AND TO FLOW BACK TANK.

NEWFIELD



Well Name: GMBU I-12-9-15

## Summary Rig Activity

Start Time	10:00	End Time	10:30	Comment
Start Time	10:30	End Time	12:00	RU FLOW BACK IRON ON THE L-12-9-15.
Start Time	12:00	End Time	15:00	FLOW BACK L-12-9-15 TO PIT. ON STANDBY WAITING FOR WATER TO SHOW UP.
Start Time	15:00	End Time	16:00	DRILLWASH OUT SAND AND PLUG PARTS WITH 15 JNTS TO PBTD. 6359'
Start Time	16:00	End Time	17:00	CIRC BOTTOMS UP UNTIL RETURNS WERE CLEAN.
Start Time	17:00	End Time	17:30	RD/RACK OUT POWER SWIVEL, LD EXCESS TBG FROM TOP OF STRING. POOH WITH 66 JNTS TBG.
Start Time	17:30	End Time	19:00	SWIFN, CLEAN LOCATION, DRAIN PUMP AND RETURN LINES, SDFN.
Start Time	19:00	End Time	22:00	Crew Travel
Report Start Date	11/6/2013	Report End Date	11/7/2013	24hr Activity Summary Trip & Land Tbg
Start Time	00:00	End Time	05:30	SDFN
Start Time	05:30	End Time	06:00	RU PUMP AND RETURN LINES.
Start Time	06:00	End Time	09:00	PUMP TO CIRCULATE GAS OUT OF WELL. FINALLY GOT TBG KILL. CSG BLOWING TOO HARD TO GET EOT OUT OF HOLE.
Start Time	09:00	End Time	09:30	TIH WITH 50 JNTS TBG FROM DERRICK.
Start Time	09:30	End Time	10:00	POOH WITH 50 JNTS TBG, LD ON PIPE SKATE/ PIPE RACKS.
Start Time	10:00	End Time	12:30	RD WORKFLOOR AND PICKUP RAM, ND DOUBLE GATE PIPE RAMS, ND FRAC VALVE ON L-12-9-15, NU DOUBLE GATE PIPE RAMS ON L-12-9-15. FUNCTION TEST BOP. PREP TO RIG DOWN.
Start Time	12:30	End Time	13:30	RD RIG, MOVE TOOLS OVER TO L-12-9-15.
Start Time	13:30	End Time	14:30	MOVE PIPE RACKS TO NEXT WELL AND WAIT FOR PIPE TO BE LOADED ON RACKS, FORKLIFT IN WAY OF RIG.
Start Time	14:30	End Time	15:30	SPOT RIG, RU RIG.
Start Time	15:30	End Time	16:30	PREP TBG, SWIFN, CLEAN LOCATION, SDFN.
Start Time	16:30	End Time	18:00	Travel Time
Start Time	18:00	End Time	00:00	SDFN
Report Start Date	11/13/2013	Report End Date	11/14/2013	24hr Activity Summary Ck Fill Trip & Land Tbg
Start Time	00:00	End Time	05:30	SDFN
Start Time	05:30	End Time	07:00	Crew Travel. Safety Meeting. JSA



NEWFIELD



Well Name: GMBU I-12-9-15

## Summary Rig Activity

Start Time	07:00	End Time	07:30	Comment
Start Time	07:30	End Time	08:45	RU PUMP AND RETURN LINES.
Start Time	08:45	End Time	11:15	CHECK TBG AND CSG PRESSURES. TBG 140 PSI, CSG 80 PSI, PUMP AND ROLL WELL TO CLEAN UP WELL BORE.
Start Time	11:15	End Time	12:30	PRESSURE TEST BOP AND GOT BAD CHAMBER TEST DUE TO FAULTY EXTENSION LINE ON PIPE RAMS, ON STANDBY WAITING FOR NEW HOSE TO SHOW UP, CHANGE OUT HOSE AND RETEST, GOOD TEST, FINISH PT STACK, GOOD TEST.
Start Time	12:30	End Time	14:00	TIH WITH 62 JNTS TO TAG FILL @ 6344'. 15' OF NEW FILL. LD 17 JNTS EXCESS TBG FROM TOP OF STRING.
Start Time	14:00	End Time	16:00	POOH WITH TBG AND BIT, BIT SUB.
Start Time	16:00	End Time	17:00	TIH WITH TBG, TBG DETAIL AS FOLLOWS: NC, 2 JNTS, PSN, 1 JNT, TAC, 180 JNTS TBG.
Start Time	17:00	End Time	17:30	RD WORK FLOOR, ND PIPE RAMS, ND BLIND RAMS, SET TAC, LAND TBG IN 18 K TENSION, NU WH.
Start Time	17:30	End Time	19:00	SWIFN, CLEAN LOCATION, SDFN.
Start Time	19:00	End Time	00:00	Crew Travel
Start Time	00:00	End Time	05:30	SDFN
Start Time	05:30	End Time	07:00	Crew Travel. Safety Meeting. JSA
Start Time	07:00	End Time	09:30	RACK OUT TBG EQUIPMENT, XO TO RODS EQUIPMENT, PREP RODS, SPOT IN ROD TRAILER, PUMP 30 BBLs WATER DOWN TBG.
Start Time	09:30	End Time	13:30	PRIME PUMP AND TIH WITH RODS, ROD DETAIL AS FOLLOWS: 25-175-RHAC-20-4-21-24' PUMP, 29 X 7/8" 8 PER GUIDED RODS, 130 X 3/4" 4 PER GUIDED RODS, 75 X 7/8" 4 PER GUIDED RODS, 8' 6" 4', 2', 7/8" PONY SUBS, AND PR X 1.5 X 30'. SPACE OUT RODS.
Start Time	13:30	End Time	14:00	HANG OFF HORSES HEAD AND RODS.
Start Time	14:00	End Time	16:00	RACK OUT ACCUMULATOR HOSES, LOAD TRAILER TO RETURN TO RUNNERS, HAVE HOT OILER STEAM OFF RIG, MOVE PIPE RACKS OUT OF WAY. RACK OUT RIG PUMP LINES AND RETURN LINES. GARBAGE RUN ON LOCATION. WAIT FOR SHIELDS TO FINISH LOADING OIL FOR TRANSFER AND GET OUT OF WAY TO RIG DOWN.
Start Time	16:00	End Time	17:00	RD RIG, RACK OUT WINCH TRUCK AND TOOLS.
Start Time	17:00	End Time	18:00	clean location, prep to move rig in morning, sdfn.
Start Time	18:00	End Time	19:30	Crew Travel

Report Start Date 11/14/2013

Report End Date 11/15/2013

24hr Activity Summary RIH W/ Rods

NEWFIELD



**Well Name: GMBU I-12-9-15**

Start Time	End Time	Comment
19:30	00:00	SDFN
