

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL						1. WELL NAME and NUMBER Ute Tribal 07-15K				
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT ANTELOPE CREEK				
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO						5. UNIT or COMMUNITIZATION AGREEMENT NAME ANTELOPE CREEK				
6. NAME OF OPERATOR PETROGLYPH OPERATING CO						7. OPERATOR PHONE 208 685-7685				
8. ADDRESS OF OPERATOR 960 Broadway Avenue, Ste 500, Boise, ID, 83703						9. OPERATOR E-MAIL ppowell@pgei.com				
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) 1420H623506			11. MINERAL OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input checked="" type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input checked="" type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>				
13. NAME OF SURFACE OWNER (if box 12 = 'fee')						14. SURFACE OWNER PHONE (if box 12 = 'fee')				
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')				
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN') Ute Indian Tribe			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>			19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/>				
20. LOCATION OF WELL		FOOTAGES		QTR-QTR	SECTION	TOWNSHIP		RANGE	MERIDIAN	
LOCATION AT SURFACE		643 FSL 1965 FEL		SWSE	7	5.0 S		3.0 W	U	
Top of Uppermost Producing Zone		1150 FSL 1015 FEL		SESE	7	5.0 S		3.0 W	U	
At Total Depth		1150 FSL 1015 FEL		SESE	7	5.0 S		3.0 W	U	
21. COUNTY DUCHESNE			22. DISTANCE TO NEAREST LEASE LINE (Feet) 643			23. NUMBER OF ACRES IN DRILLING UNIT 640				
27. ELEVATION - GROUND LEVEL 6065			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 22			26. PROPOSED DEPTH MD: 6259 TVD: 6120				
28. BOND NUMBER LPM4138336			29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 43-8342							
Hole, Casing, and Cement Information										
String	Hole Size	Casing Size	Length	Weight	Grade & Thread	Max Mud Wt.	Cement	Sacks	Yield	Weight
Cond	20	14	0 - 54	5.0	Unknown	10.0	Class G	25	1.17	15.8
Surf	12.25	8.625	0 - 494	24.0	J-55 ST&C	10.0	Class G	227	1.17	15.8
Prod	7.875	5.5	0 - 6259	15.5	J-55 LT&C	10.0	Class G	469	1.92	12.5
							Class G	349	1.46	13.4
ATTACHMENTS										
VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES										
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER					<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN					
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)					<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER					
<input type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)					<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP					
NAME Ed Trotter				TITLE Agent			PHONE 435 789-4120			
SIGNATURE				DATE 05/31/2013			EMAIL edtrotter@easilink.com			
API NUMBER ASSIGNED 43013522110000				APPROVAL  Permit Manager						

CONFIDENTIAL
NINE POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 07-15K
SW SE, SEC 7, T5S, R3W
DUCHESNE COUNTY, UTAH

1. ESTIMATED TOPS OF IMPORTANT GEOLOGICAL MARKERS:

Formation		Subsea	TVD	MD
Rig KB~14.4' above GGL		6080	0	0
Surface Formation = Uinta				
Uinta		6065	15	15
Green River		4774	1306	1309
Trona		3438	2642	2695
Mahogany Shale		3285	2795	2854
"B" Marker	Waterflood Unit Interval	2188	3892	3999
"X" Marker		1692	4388	4516
Douglas Creek Marker		1547	4533	4664
"B" Limestone		1160	4920	5057
Base Castle Peak Limestone		608	5472	5611
BSCARB		190	5890	6173
Wasatch		-67	NDE	NDE
Rig TD		-40	6120	6259

2. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERAL FORMATIONS:

Substance	Formation	Subsea	TVD	MD
Base of moderately saline ground water*	Uinta	6000	80	80
Oil/Gas	Douglas Creek	1547	4533	4664
Oil/Gas	Castle Peak	608	5472	5611

Any water encountered during drilling shall be sampled, analyzed and reported to BLM, Vernal office using State of Utah DOGM Form 7 *Report of Water Encountered during Drilling*. The following analyses shall be performed on any water encountered:

Flow rate (or blowtest)	Temperature	pH	TDS
Dissolved Iron	Dissolved Magnesium	Dissolved Bicarb.	Dissolved Sulfate
Dissolved Calcium	Dissolved Sodium	Dissolved Carbonate	Dissolved Chloride

All depths through the "Base of moderately saline ground water"* , along with any water encountered below that depth which is less than 10,000 TDS, shall be protected by the surface casing or by lifting the cement of the production casing into the surface casing.

*Base of Moderately Saline Groundwater from Howells, Longson and Hunt, 1981, Utah State Technical Publication 92: The Base of the Moderately Saline Water in the Uinta Basin, Utah



CONFIDENTIAL
NINE POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 07-15K
SW SE, SEC 7, T5S, R3W
DUCHESNE COUNTY, UTAH

3. PROPOSED CASING PROGRAM:

String	Hole	Casing	Top - MD	Bottom - MD	Weight lb/ft	Grade	Thread
Conductor	20"	14"	surface	54'	steel	Cond'r	none
Surface	12-1/4"	8-5/8"	surface	494'	24	J-55	STC
Production	7-7/8"	5-1/2"	surface	6259'	15.5	J-55	LTC

String	Hole	Casing	Collapse	Burst	Tensile
Surface	12-1/4"	8-5/8"	1,370 psi	2,950 psi	244,000 lb
Production	7-7/8"	5-1/2"	4,040 psi	4,810 psi	248,000 lb

- All casing will be new or inspected.
- The surface and production strings shall have a minimum of one (1) centralizer on each of the bottom three (3) joints.
- The production string shall have a minimum of one (1) centralizer for every three (3) joints from TD to the top of the "B" marker at 3999'MD.

4. PROPOSED CEMENTING PROGRAM:

String	Top	Cement Description	Sacks	Excess	Weight (ppg)	Yield (ft ³ /sk)
	Bottom		Vol (ft ³)			
Conductor	0 54	Construction Grade Cement	Sufficient volumes to grout Conductor			
Surface	0 494	Class G +2% CaCl ₂ +0.25 lb/sk Cello Flake	227 265	30%	15.8	1.17
Production Lead	0 3999	EXPANDACEM (Class G +additives) + 1 lb/sk Granulite TR ¹ / ₄ (LCM)	469 901	30%	12.5	1.92
Production Tail	3999 6259	EXPANDACEM (Class G +additives) + 1 lb/sk Granulite TR ¹ / ₄ (LCM)	349 509	30%	13.4	1.46

- The 8-5/8" surface casing shall be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.
- The 5-1/2" production casing shall be cemented back to surface. In the event that during the primary cementing operation the cement does not circulate to surface, a remedial cementing operation shall be performed only if necessary to lift cement above the Trona at 2695'MD.



CONFIDENTIAL
NINE POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 07-15K
SW SE, SEC 7, T5S, R3W
DUCHESNE COUNTY, UTAH

5. MINIMUM PRESSURE CONTROL AND SAFETY EQUIPMENT:

- An 8", 2000 PSI, Double Ram BOPE with Hydraulic Closing Unit shall be used.
- The flowline shall have a minimum diameter of 10".
- Auxiliary equipment shall be a Kelly Cock, Bit Float, and a TIW valve with drill pipe threads.
- Spark arrestors shall be equipped on all engine exhausts within 100 feet of the wellbore.
- See attached 2,000 psi BOP schematic diagram.

BOPE TESTING PROCEDURE:

- The BOPE shall be tested by a professional tester to conform to Onshore Order #2.

6. MUD PROGRAM:

A. SURFACE HOLE

- The surface hole will be drilled with an air/mist system from 0' to 494'. All cutting shall be directed to pit.
- A trailer-mounted compressor with a capacity of 2000 CFM will be used. Compressor will have a safety shut-off valve located less than 15 feet from the driller's controls of the rig.
- The rat and mouse holes will be drilled with the air rig after surface casing is cemented.
- The 140 barrel water truck used with the deduster will be the source of kill fluid in the highly unlikely event of pressure being encountered during drilling of the surface hole.
- Operator requests the following variances from Onshore Order 2 part E during drilling of the surface hole. Operator will use air drilling techniques only on surface hole:
 - Operator requests a variance to regulations requiring the blooie line discharge to be 100' from the wellbore. Due to reduced location size, the blooie line discharge will be approximately 75' from the wellbore and securely anchored.
 - Operator requests a variance to regulations requiring an automatic igniter or continuous pilot light on the blooie line. A mister shall be on the end of the blooie line.
 - Operator requests a variance to regulations requiring compressors be located in the opposite direction from the blooie line; a minimum of 100' from the wellbore. Due to the reduced location size, the compressors shall be located as close as is reasonable to the opposite direction from the blooie line and 75' from the wellbore.
 - Operator requests a variance to regulations requiring a BOPE on the hole when drilling the surface hole. An air bowl shall be utilized on the diverter system in place of a BOPE.



CONFIDENTIAL
NINE POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 07-15K
SW SE, SEC 7, T5S, R3W
DUCHESNE COUNTY, UTAH

B. PRODUCTION HOLE

- The production hole shall be drilled with a freshwater polymer system from 494' to 6259'. LSND mud if conditions warrant.
- Clay inhibition and hole stability shall be achieved with a Diammonium Phosphate (DAP) additive or similar source of clay-stabilizing ions. Anticipated mud weight is 8.3-8.8 lbs/gal. although mud weight up to 10lbs/gal may be used if necessary to prevent wellbore wall instability due to the planned inclination of the well.
- All cuttings and circulating medium shall be directed into the reserve pit. Total Dissolved Solids (TDS) are anticipated to be less than 3000 PPM.
- Sufficient mud inventory will be maintained on location in either tanks or the reserve pit during the drilling of the production hole to handle any adverse conditions that may arise.
- If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite. Enough material shall be maintained on location to allow for the mudweight to be raised to 10.5 lbs/gal should need arise.
- During drilling operations, pit levels and flow from the well shall be monitored by instrumentation to include at least: a pit volume totalizer (PVT), a stroke counter, and a mud-flow indicator.
- A mud-gas separator shall be available on location. Operator does not plan on using a gas detector on the mud return due to the fact that any abnormal pressure is the result of offset water injection.

C. HAZARDOUS MATERIALS AND POLLUTANTS

- Chromate additives **shall NOT** be used in the mud system on Indian lands without prior DOGM approval to ensure adequate protection of freshwater aquifers.
- Chemicals subject to reporting under SARA Title III in an amounts equal to or greater than 10,000 pounds annually **shall NOT** be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completion of this well.
- Extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities **shall NOT** be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completion of this well.
- Hazardous substances specifically listed by the EPA as a hazardous waste, as defined in 40 CFR 261 (D), or any substances that through their use would lead to the generation of a hazardous waste, **shall NOT** be used in association with the drilling, testing, or completion of this well.

CONFIDENTIAL
NINE POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 07-15K
SW SE, SEC 7, T5S, R3W
DUCHESNE COUNTY, UTAH

7. EVALUATION PROGRAM:

Logs: Triple Combo TD to base of surface casing (AIT, DSN, CDL)
 Base of surface casing to surface (GR only)

Cores: None planned

DST: None planned

Testing: Operator plans no testing until the completion phase of the well.

8. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:


- Operator anticipates Bottom Hole Temperatures below 150°F, the maximum temperature for DAP drilling fluids.
- No H₂S has been encountered or is known to exist from previous drilling in the area at this depth.
- Maximum pressure for hydrocarbon bearing zones at native conditions in this area is approximately 1565 PSI (0.25 PSI/ft gradient).
- This well is in the vicinity of active injection wells. Nearby active injection can cause pressures up to a 0.433 PSI/ft gradient (2710 PSI).

9. DIRECTIONAL WELL PLAN:

- Well shall be drilled directionally in order to limit surface disturbance.
- A Positive Displacement Motor with a bent sub of 1.25° to 1.75° will be used to control well path.
- A directional survey shall be taken at least one (1) time per 100' of drilling.
- Anti-collision equipment will not be used as there are no existing wells in the vicinity of the proposed well path.
- While cutting the Waterflood Unit Interval from 3999' to 6173', the actual well path may be allowed to vary up to 100' horizontally from plan in order to prevent excessive slide drilling. Above and below the Waterflood Unit Interval, variances in excess 100' horizontally from plan may be allowed.
- Directional drilling plan is attached.


CONFIDENTIAL
NINE POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 07-15K
SW SE, SEC 7, T5S, R3W
DUCHESNE COUNTY, UTAH

TYPICAL 2,000 p.s.i. BLOWOUT PREVENTER

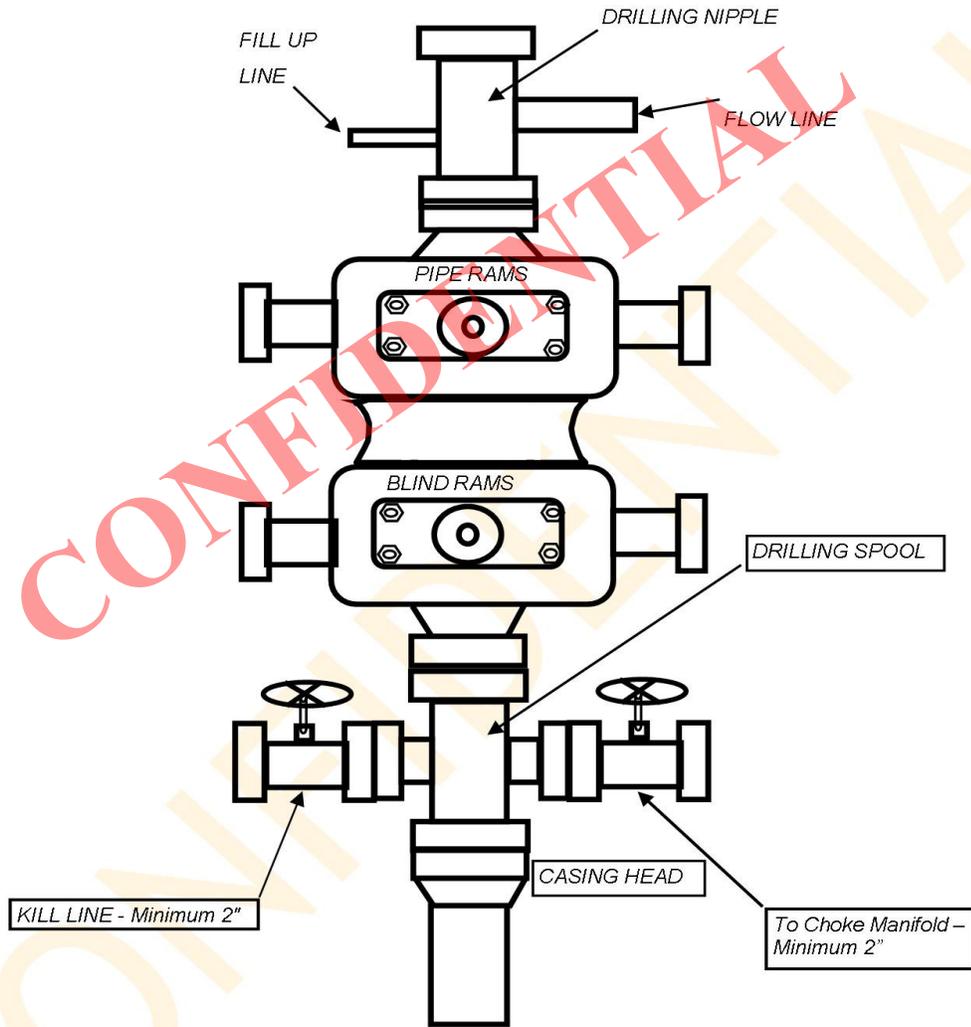

CONFIDENTIAL
NINE POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 07-15K
SW SE, SEC 7, T5S, R3W
DUCHESNE COUNTY, UTAH

TYPICAL 2,000 p.s.i. CHOKE MANIFOLD

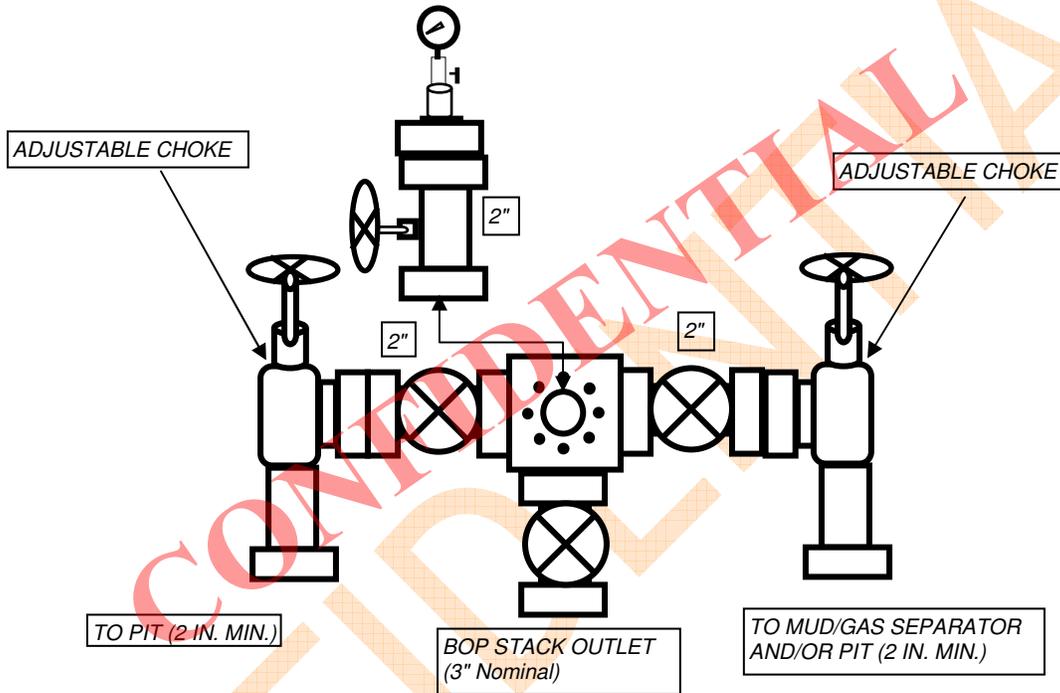



VERTICAL SECTION ON AZIMUTH 60.9 DEGREES

#	Reference	Type	MD	Inc	Azi	TVD	N	E	DLS	Vert S
0	RKB	Tie Point	0.00	0.00	0.00	0.00	0.00	0.00		0.00
1	KOP	Vertical	600.00	0.00	0.00	600.00	0.00	0.00	0.00	0.00
2	End Build	Build	1960.00	17.00	60.90	1940.13	97.41	175.00	1.25	200.28
3	Start Drop	Tangent	4100.00	17.00	60.90	3986.63	401.69	721.70	0.00	825.96
4	End Drop	Drop	5800.00	0.00	0.00	5661.79	523.45	940.45	1.00	1076.32
5	RTD	Vertical	6259.00	0.00	0.00	6120.79	523.45	940.45	0.00	1076.32

07-15K, Plan 1

Operator	Units feet, %100ft	11:12 Thursday, May 02, 2013 Page 1 of 4
Field	County Duchesne	Vertical Section Azimuth 60.9
Well Name 07-15K	State UT	Survey Calculation Method Minimum Curvature
Plan 1	Country USA	Database Access

Location SHL: 643' FSL 1965' FEL BHL: 1150' FSL 1015' FEL	MapZone	Lat Long Ref
Site	SurfaceX	Surface Long
Slot Name	SurfaceY	Surface Lat
Well Number	Z Datum	
Project	Surface Z	Ground Level

DIRECTIONAL WELL PLAN

MD*	INC*	AZI*	TVD*	N*	E*	DLS*	V. S.*	MapE*	MapN*	SysTVD*
ft	deg	deg	ft	ft	ft	%100ft	ft	ft	ft	ft
*** RKB (at MD = 0.00)										
0.00	0.00	0.0	0.00	0.00	0.00		0.00			
50.00	0.00	0.0	50.00	0.00	0.00	0.00	0.00			
100.00	0.00	0.0	100.00	0.00	0.00	0.00	0.00			
150.00	0.00	0.0	150.00	0.00	0.00	0.00	0.00			
200.00	0.00	0.0	200.00	0.00	0.00	0.00	0.00			
250.00	0.00	0.0	250.00	0.00	0.00	0.00	0.00			
300.00	0.00	0.0	300.00	0.00	0.00	0.00	0.00			
350.00	0.00	0.0	350.00	0.00	0.00	0.00	0.00			
400.00	0.00	0.0	400.00	0.00	0.00	0.00	0.00			
450.00	0.00	0.0	450.00	0.00	0.00	0.00	0.00			
500.00	0.00	0.0	500.00	0.00	0.00	0.00	0.00			
550.00	0.00	0.0	550.00	0.00	0.00	0.00	0.00			
*** KOP (at MD = 600.00)										
600.00	0.00	0.0	600.00	0.00	0.00	0.00	0.00			
650.00	0.63	60.9	650.00	0.13	0.24	1.25	0.27			
700.00	1.25	60.9	699.99	0.53	0.95	1.25	1.09			
750.00	1.88	60.9	749.97	1.19	2.14	1.25	2.45			
800.00	2.50	60.9	799.94	2.12	3.81	1.25	4.36			
850.00	3.13	60.9	849.88	3.31	5.96	1.25	6.82			
900.00	3.75	60.9	899.79	4.77	8.58	1.25	9.81			
950.00	4.38	60.9	949.66	6.50	11.67	1.25	13.36			
1000.00	5.00	60.9	999.49	8.48	15.24	1.25	17.44			
1050.00	5.63	60.9	1049.28	10.73	19.29	1.25	22.07			
1100.00	6.25	60.9	1099.01	13.25	23.80	1.25	27.24			
1150.00	6.88	60.9	1148.68	16.03	28.80	1.25	32.96			
1200.00	7.50	60.9	1198.29	19.07	34.26	1.25	39.21			
1250.00	8.13	60.9	1247.82	22.38	40.20	1.25	46.01			
1300.00	8.75	60.9	1297.28	25.94	46.61	1.25	53.35			
1350.00	9.38	60.9	1346.66	29.77	53.49	1.25	61.22			
1400.00	10.00	60.9	1395.94	33.87	60.85	1.25	69.64			
1450.00	10.63	60.9	1445.14	38.22	68.67	1.25	78.59			
1500.00	11.25	60.9	1494.23	42.83	76.96	1.25	88.07			
1550.00	11.88	60.9	1543.21	47.71	85.71	1.25	98.10			
1600.00	12.50	60.9	1592.09	52.84	94.94	1.25	108.65			
1650.00	13.13	60.9	1640.84	58.23	104.62	1.25	119.74			

07-15K, Plan 1

Operator	Units feet, %100ft	11:12 Thursday, May 02, 2013 Page 2 of 4
Field	County Duchesne	Vertical Section Azimuth 60.9
Well Name 07-15K	State UT	Survey Calculation Method Minimum Curvature
Plan 1	Country USA	Database Access

Location SHL: 643' FSL 1965' FEL BHL: 1150' FSL 1015' FEL	MapZone	Lat Long Ref
Site	SurfaceX	Surface Long
Slot Name	SurfaceY	Surface Lat
Well Number	Z Datum	
Project	Surface Z	Ground Level

DIRECTIONAL WELL PLAN

MD*	INC*	AZI*	TVD*	N*	E*	DLS*	V. S.*	MapE*	MapN*	SysTVD*
ft	deg	deg	ft	ft	ft	%100ft	ft	ft	ft	ft
1700.00	13.75	60.9	1689.47	63.88	114.78	1.25	131.36			
1750.00	14.38	60.9	1737.97	69.79	125.39	1.25	143.51			
1800.00	15.00	60.9	1786.34	75.96	136.47	1.25	156.18			
1850.00	15.63	60.9	1834.56	82.38	148.01	1.25	169.39			
1900.00	16.25	60.9	1882.64	89.06	160.00	1.25	183.12			
1950.00	16.88	60.9	1930.57	95.99	172.46	1.25	197.37			
*** END BUILD (at MD = 1960.00)										
1960.00	17.00	60.9	1940.13	97.41	175.00	1.25	200.28			
2000.00	17.00	60.9	1978.39	103.09	185.22	0.00	211.98			
2050.00	17.00	60.9	2026.20	110.20	197.99	0.00	226.60			
2100.00	17.00	60.9	2074.02	117.31	210.77	0.00	241.22			
2150.00	17.00	60.9	2121.83	124.42	223.54	0.00	255.83			
2200.00	17.00	60.9	2169.65	131.53	236.31	0.00	270.45			
2250.00	17.00	60.9	2217.46	138.64	249.09	0.00	285.07			
2300.00	17.00	60.9	2265.28	145.75	261.86	0.00	299.69			
2350.00	17.00	60.9	2313.09	152.86	274.63	0.00	314.31			
2400.00	17.00	60.9	2360.91	159.97	287.41	0.00	328.93			
2450.00	17.00	60.9	2408.72	167.08	300.18	0.00	343.55			
2500.00	17.00	60.9	2456.54	174.19	312.95	0.00	358.17			
2550.00	17.00	60.9	2504.35	181.30	325.73	0.00	372.78			
2600.00	17.00	60.9	2552.17	188.41	338.50	0.00	387.40			
2650.00	17.00	60.9	2599.98	195.52	351.27	0.00	402.02			
2700.00	17.00	60.9	2647.80	202.63	364.05	0.00	416.64			
2750.00	17.00	60.9	2695.61	209.74	376.82	0.00	431.26			
2800.00	17.00	60.9	2743.43	216.85	389.59	0.00	445.88			
2850.00	17.00	60.9	2791.24	223.96	402.37	0.00	460.50			
2900.00	17.00	60.9	2839.06	231.06	415.14	0.00	475.11			
2950.00	17.00	60.9	2886.87	238.17	427.91	0.00	489.73			
3000.00	17.00	60.9	2934.69	245.28	440.69	0.00	504.35			
3050.00	17.00	60.9	2982.51	252.39	453.46	0.00	518.97			
3100.00	17.00	60.9	3030.32	259.50	466.23	0.00	533.59			
3150.00	17.00	60.9	3078.14	266.61	479.01	0.00	548.21			
3200.00	17.00	60.9	3125.95	273.72	491.78	0.00	562.83			
3250.00	17.00	60.9	3173.77	280.83	504.55	0.00	577.44			
3300.00	17.00	60.9	3221.58	287.94	517.33	0.00	592.06			

07-15K, Plan 1

Operator	Units feet, %/100ft	11:12 Thursday, May 02, 2013 Page 3 of 4
Field	County Duchesne	Vertical Section Azimuth 60.9
Well Name 07-15K	State UT	Survey Calculation Method Minimum Curvature
Plan 1	Country USA	Database Access

Location SHL: 643' FSL 1965' FEL BHL: 1150' FSL 1015' FEL	MapZone	Lat Long Ref
Site	SurfaceX	Surface Long
Slot Name	SurfaceY	Surface Lat
Well Number	Z Datum	
Project	Surface Z	Ground Level

DIRECTIONAL WELL PLAN

MD*	INC*	AZI*	TVD*	N*	E*	DLS*	V. S.*	MapE*	MapN*	SysTVD*
ft	deg	deg	ft	ft	ft	%/100ft	ft	ft	ft	ft
3350.00	17.00	60.9	3269.40	295.05	530.10	0.00	606.68			
3400.00	17.00	60.9	3317.21	302.16	542.87	0.00	621.30			
3450.00	17.00	60.9	3365.03	309.27	555.65	0.00	635.92			
3500.00	17.00	60.9	3412.84	316.38	568.42	0.00	650.54			
3550.00	17.00	60.9	3460.66	323.49	581.19	0.00	665.16			
3600.00	17.00	60.9	3508.47	330.60	593.97	0.00	679.77			
3650.00	17.00	60.9	3556.29	337.71	606.74	0.00	694.39			
3700.00	17.00	60.9	3604.10	344.82	619.51	0.00	709.01			
3750.00	17.00	60.9	3651.92	351.93	632.29	0.00	723.63			
3800.00	17.00	60.9	3699.73	359.04	645.06	0.00	738.25			
3850.00	17.00	60.9	3747.55	366.15	657.83	0.00	752.87			
3900.00	17.00	60.9	3795.36	373.26	670.61	0.00	767.49			
3950.00	17.00	60.9	3843.18	380.36	683.38	0.00	782.10			
4000.00	17.00	60.9	3890.99	387.47	696.15	0.00	796.72			
4050.00	17.00	60.9	3938.81	394.58	708.93	0.00	811.34			
*** START DROP (at MD = 4100.00)										
4100.00	17.00	60.9	3986.63	401.69	721.70	0.00	825.96			
4150.00	16.50	60.9	4034.50	408.70	734.29	1.00	840.37			
4200.00	16.00	60.9	4082.51	415.51	746.52	1.00	854.36			
4250.00	15.50	60.9	4130.63	422.11	758.38	1.00	867.93			
4300.00	15.00	60.9	4178.87	428.50	769.87	1.00	881.08			
4350.00	14.50	60.9	4227.22	434.69	780.99	1.00	893.81			
4400.00	14.00	60.9	4275.68	440.68	791.74	1.00	906.12			
4450.00	13.50	60.9	4324.25	446.46	802.13	1.00	918.01			
4500.00	13.00	60.9	4372.92	452.03	812.14	1.00	929.47			
4550.00	12.50	60.9	4421.68	457.40	821.78	1.00	940.50			
4600.00	12.00	60.9	4470.55	462.56	831.05	1.00	951.11			
4650.00	11.50	60.9	4519.50	467.51	839.95	1.00	961.29			
4700.00	11.00	60.9	4568.54	472.25	848.47	1.00	971.05			
4750.00	10.50	60.9	4617.66	476.79	856.62	1.00	980.37			
4800.00	10.00	60.9	4666.86	481.12	864.40	1.00	989.27			
4850.00	9.50	60.9	4716.14	485.23	871.80	1.00	997.74			
4900.00	9.00	60.9	4765.49	489.14	878.82	1.00	1005.77			
4950.00	8.50	60.9	4814.91	492.84	885.46	1.00	1013.38			
5000.00	8.00	60.9	4864.39	496.33	891.73	1.00	1020.56			

07-15K, Plan 1

Operator	Units feet, %100ft	11:12 Thursday, May 02, 2013 Page 4 of 4
Field	County Duchesne	Vertical Section Azimuth 60.9
Well Name 07-15K	State UT	Survey Calculation Method Minimum Curvature
Plan 1	Country USA	Database Access

Location Site SHL: 643' FSL 1965' FEL BHL: 1150' FSL 1015' FEL	MapZone	Lat Long Ref
Slot Name	SurfaceX	Surface Long
Well Number	SurfaceY	Surface Lat
Project	Z Datum	
	Surface Z	Ground Level


DIRECTIONAL WELL PLAN

MD*	INC*	AZI*	TVD*	N*	E*	DLS*	V. S.*	MapE*	MapN*	SysTVD*
ft	deg	deg	ft	ft	ft	%100ft	ft	ft	ft	ft
5050.00	7.50	60.9	4913.93	499.61	897.62	1.00	1027.30			
5100.00	7.00	60.9	4963.53	502.68	903.14	1.00	1033.61			
5150.00	6.50	60.9	5013.19	505.54	908.27	1.00	1039.48			
5200.00	6.00	60.9	5062.89	508.19	913.03	1.00	1044.93			
5250.00	5.50	60.9	5112.64	510.62	917.41	1.00	1049.94			
5300.00	5.00	60.9	5162.43	512.85	921.40	1.00	1054.51			
5350.00	4.50	60.9	5212.25	514.86	925.02	1.00	1058.65			
5400.00	4.00	60.9	5262.12	516.66	928.26	1.00	1062.36			
5450.00	3.50	60.9	5312.01	518.25	931.12	1.00	1065.63			
5500.00	3.00	60.9	5361.93	519.63	933.59	1.00	1068.46			
5550.00	2.50	60.9	5411.87	520.80	935.69	1.00	1070.86			
5600.00	2.00	60.9	5461.83	521.75	937.40	1.00	1072.82			
5650.00	1.50	60.9	5511.81	522.50	938.74	1.00	1074.35			
5700.00	1.00	60.9	5561.80	523.03	939.69	1.00	1075.44			
5750.00	0.50	60.9	5611.79	523.34	940.26	1.00	1076.10			
*** END DROP (at MD = 5800.00)										
5800.00	0.00	0.0	5661.79	523.45	940.45	1.00	1076.32			
5850.00	0.00	0.0	5711.79	523.45	940.45	0.00	1076.32			
5900.00	0.00	0.0	5761.79	523.45	940.45	0.00	1076.32			
5950.00	0.00	0.0	5811.79	523.45	940.45	0.00	1076.32			
6000.00	0.00	0.0	5861.79	523.45	940.45	0.00	1076.32			
6050.00	0.00	0.0	5911.79	523.45	940.45	0.00	1076.32			
6100.00	0.00	0.0	5961.79	523.45	940.45	0.00	1076.32			
6150.00	0.00	0.0	6011.79	523.45	940.45	0.00	1076.32			
6200.00	0.00	0.0	6061.79	523.45	940.45	0.00	1076.32			
6250.00	0.00	0.0	6111.79	523.45	940.45	0.00	1076.32			
*** RTD (at MD = 6259.00)										
6259.00	0.00	0.0	6120.79	523.45	940.45	0.00	1076.32			

T5S, R3W, U.S.B.&M.

PETROGLYPH OPERATING CO., INC.

Well location, UTE TRIBAL #07-15K, located as shown in the SW 1/4 SE 1/4 of Section 7, T5S, R3W, U.S.B.&M., Duchesne County, Utah.

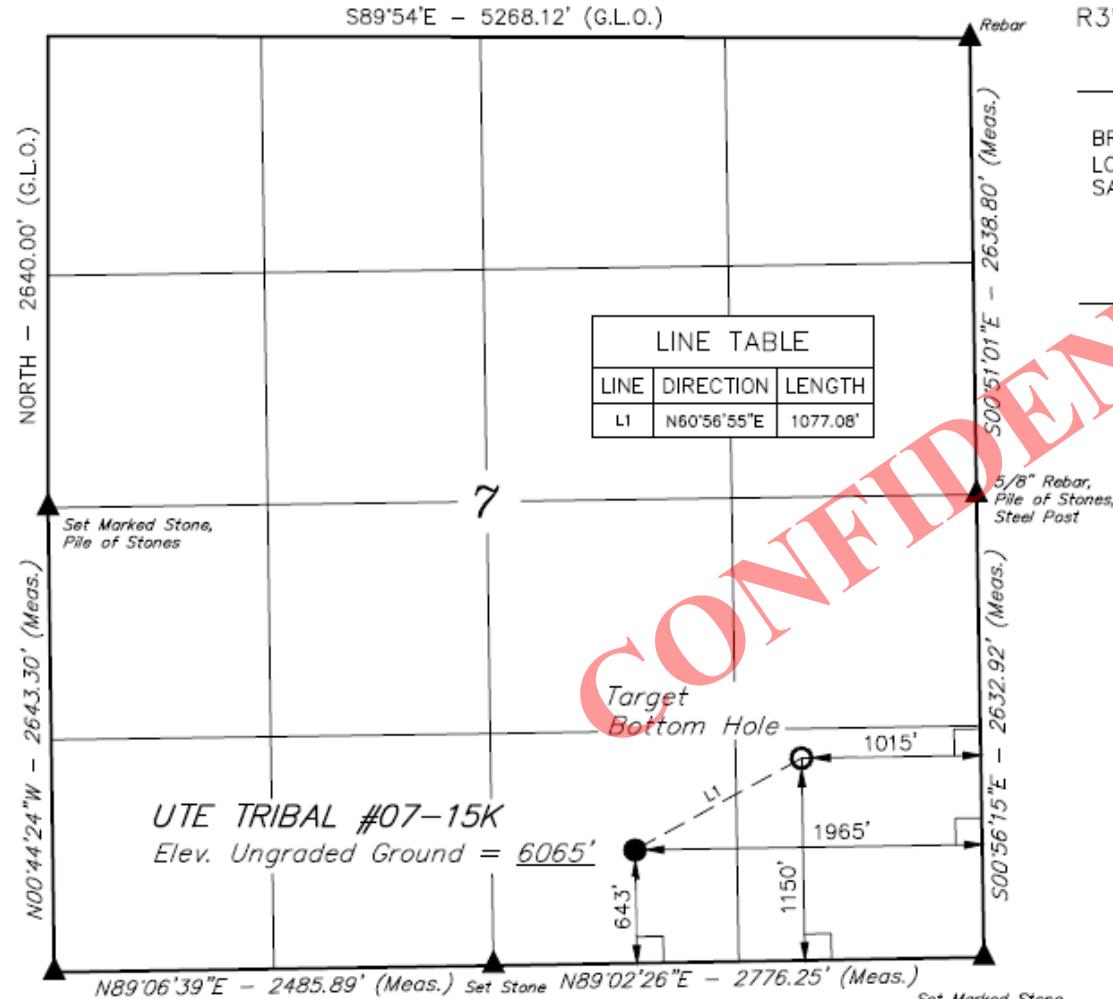

CONFIDENTIAL


LINE TABLE		
LINE	DIRECTION	LENGTH
L1	N60°56'55"E	1077.08'

BASIS OF ELEVATION

BRASS CAP SET IN CONCRETE BY SUNRISE ENGINEERING LOCATED IN THE SE 1/4 OF SECTION 16, T5S, R3W, U.S.B.&M. SAID ELEVATION IS MARKED AS BEING 6281.9 FEET.

BASIS OF BEARINGS

BASIS OF BEARINGS IS A G.P.S. OBSERVATION.

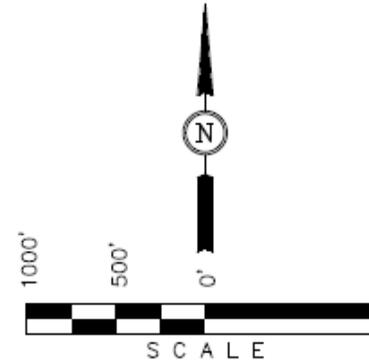

CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

REGISTERED LAND SURVEYOR
 REGISTRATION NO. 161319
 STATE OF UTAH


Position Re-Established Using Bearing Tree Information (Not Set on Ground)

LEGEND:

- └─ = 90° SYMBOL
- = PROPOSED WELL HEAD.
- ▲ = SECTION CORNERS LOCATED.

NAD 83 (TARGET BOTTOM HOLE)	NAD 83 (SURFACE LOCATION)
LATITUDE = 40°03'25.13" (40.056981)	LATITUDE = 40°03'20.09" (40.055581)
LONGITUDE = 110°15'35.40" (110.259833)	LONGITUDE = 110°15'47.61" (110.263225)
NAD 27 (TARGET BOTTOM HOLE)	NAD 27 (SURFACE LOCATION)
LATITUDE = 40°03'25.27" (40.057019)	LATITUDE = 40°03'20.23" (40.055619)
LONGITUDE = 110°15'32.85" (110.259125)	LONGITUDE = 110°15'45.06" (110.262517)

UINTAH ENGINEERING & LAND SURVEYING 85 SOUTH 200 EAST - VERNAL, UTAH 84078 (435) 789-1017		
SCALE 1" = 1000'	DATE SURVEYED: 10-23-12	DATE DRAWN: 11-01-12
PARTY G.O. D.D. A.T.		REFERENCES G.L.O. PLAT
WEATHER COLD		FILE PETROGLYPH OPERATING CO., INC.

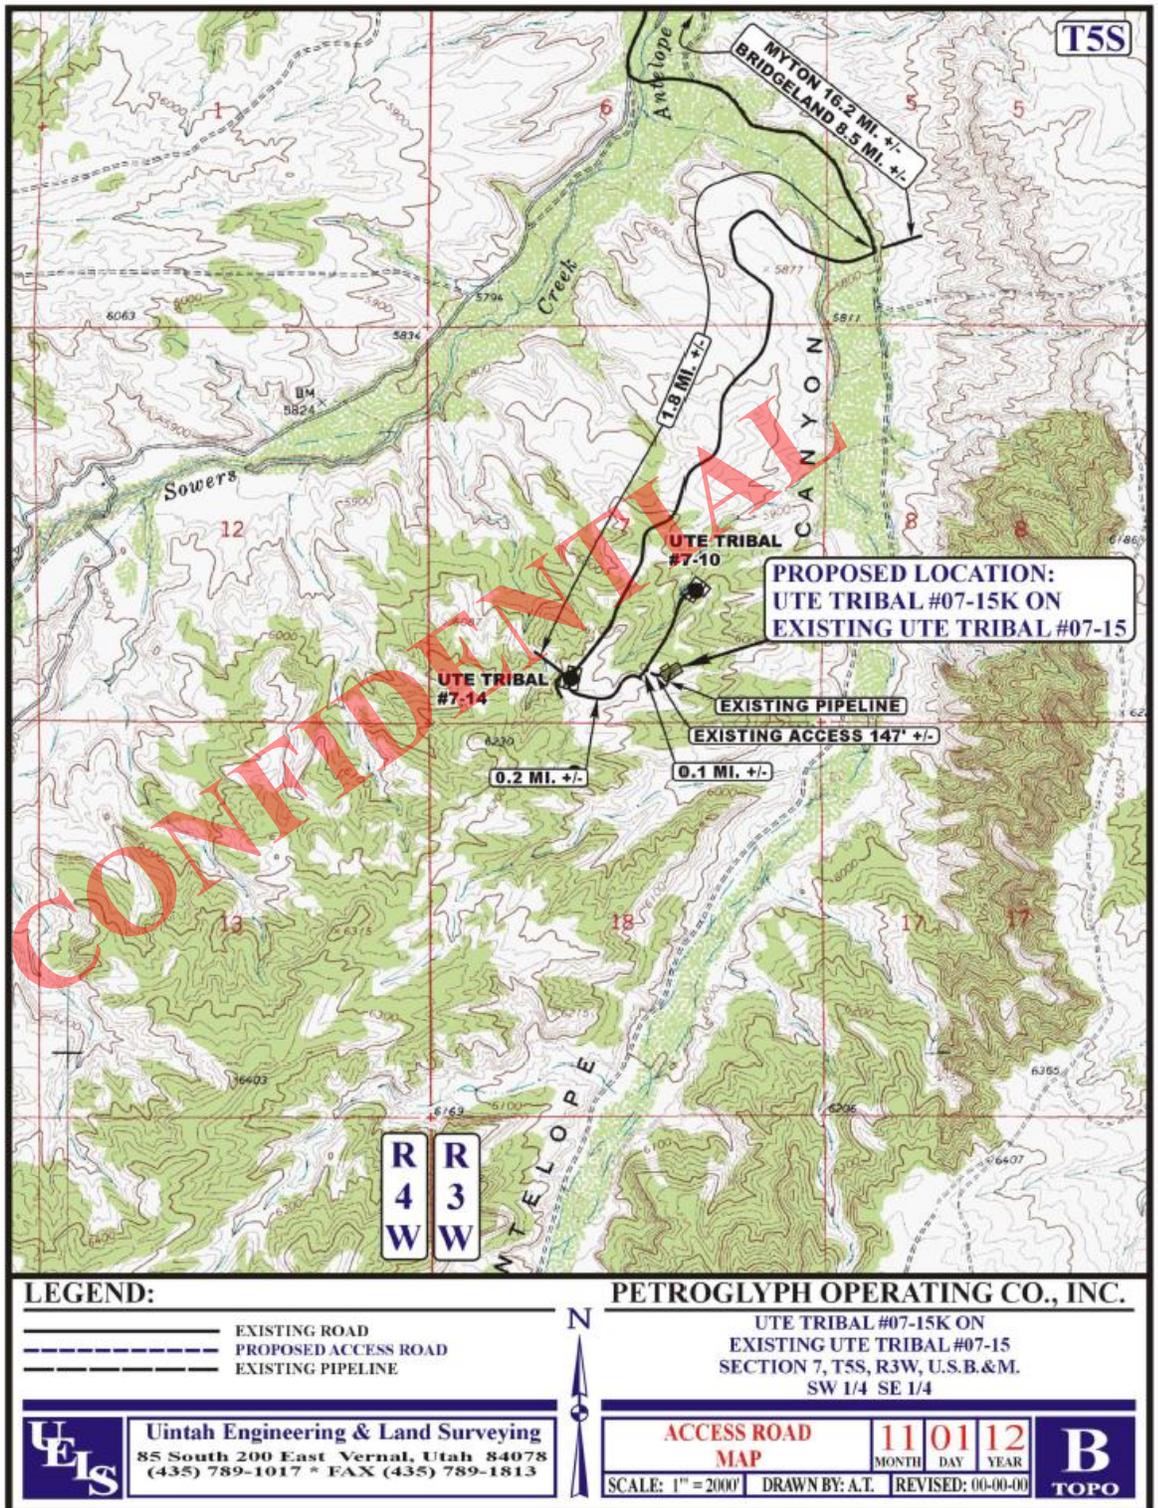

PETROGLYPH OPERATING CO., INC.
P.O. BOX 607
ROOSEVELT, UTAH 84066

May 31, 2013

Ms. Diana Mason
State of Utah
Division of Oil, Gas & Mining
1594 West North Temple, Suite 1210
P.O. Box 145801
Salt Lake City, UT 84114-5801

Re: Directional Drilling R649-3-11

Ute Tribal 07-15K: 643' FSL & 1965' FEL, SW/SE, (Surface Hole)
 1150' FSL & 1015' FEL, SE/SE, (Bottom Hole)
 Sec. 7, T5S, R3W, U.S.B.&M.,
 Duchesne County, Utah

Dear Ms. Mason,

Pursuant to the filing of Petroglyph Operating Co., Inc.'s Application for Permit to Drill regarding the above referenced well on May 31, 2013, we are hereby submitting this letter in accordance with Oil & Gas Conservation Rule R649-3-11 pertaining to the Exception to Location and Siting of Wells.

- The Ute Tribal 07-15K is located within the Antelope Creek Unit Area.
- Petroglyph Operating Co., Inc. is permitting this well as a directional well in order to minimize surface disturbance. Locating the well at the surface location and drilling directionally from this location, Petroglyph Operating Co., Inc. will be able to utilize the existing road and pipelines in the area.
- Furthermore, Petroglyph Operating Co., Inc. hereby certifies that it is the sole working interest owner within 460 feet of the entire directional well bore.

Therefore, based on the above stated information, Petroglyph Operating Co., Inc. requests the permit be granted pursuant to R649-3-11.

Respectfully Submitted,

Ed Trotter,
Agent
P.O. Box 1910
Vernal, UT 84078
Phone: (435)789-4120
Fax: (435)789-1420
E-mail: edtrotter@easilink.com

Certification


I hereby certify that I, or persons under my direct supervision, have inspected the proposed drillsite and access route; that I am familiar with the conditions that presently exist; that the statements made in the Plan are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed by Petroglyph Operating Co., Inc. and its contractors and subcontractors in conformity with this Plan and the terms and conditions under which it is approved.


Please be advised that Petroglyph Operating Co., Inc. is considered to be the operator of the **UTE TRIBAL 07-15K Well, located in the SW/SE of Section 7, T5S, R3W, Duchesne County, Utah; Lease #14-20-H62-3506;** and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond Coverage is provided under Bond #LPM4138335.

Date

Ed Trotter, as Agent for
Petroglyph Operating Co., Inc.

CONFIDENTIAL

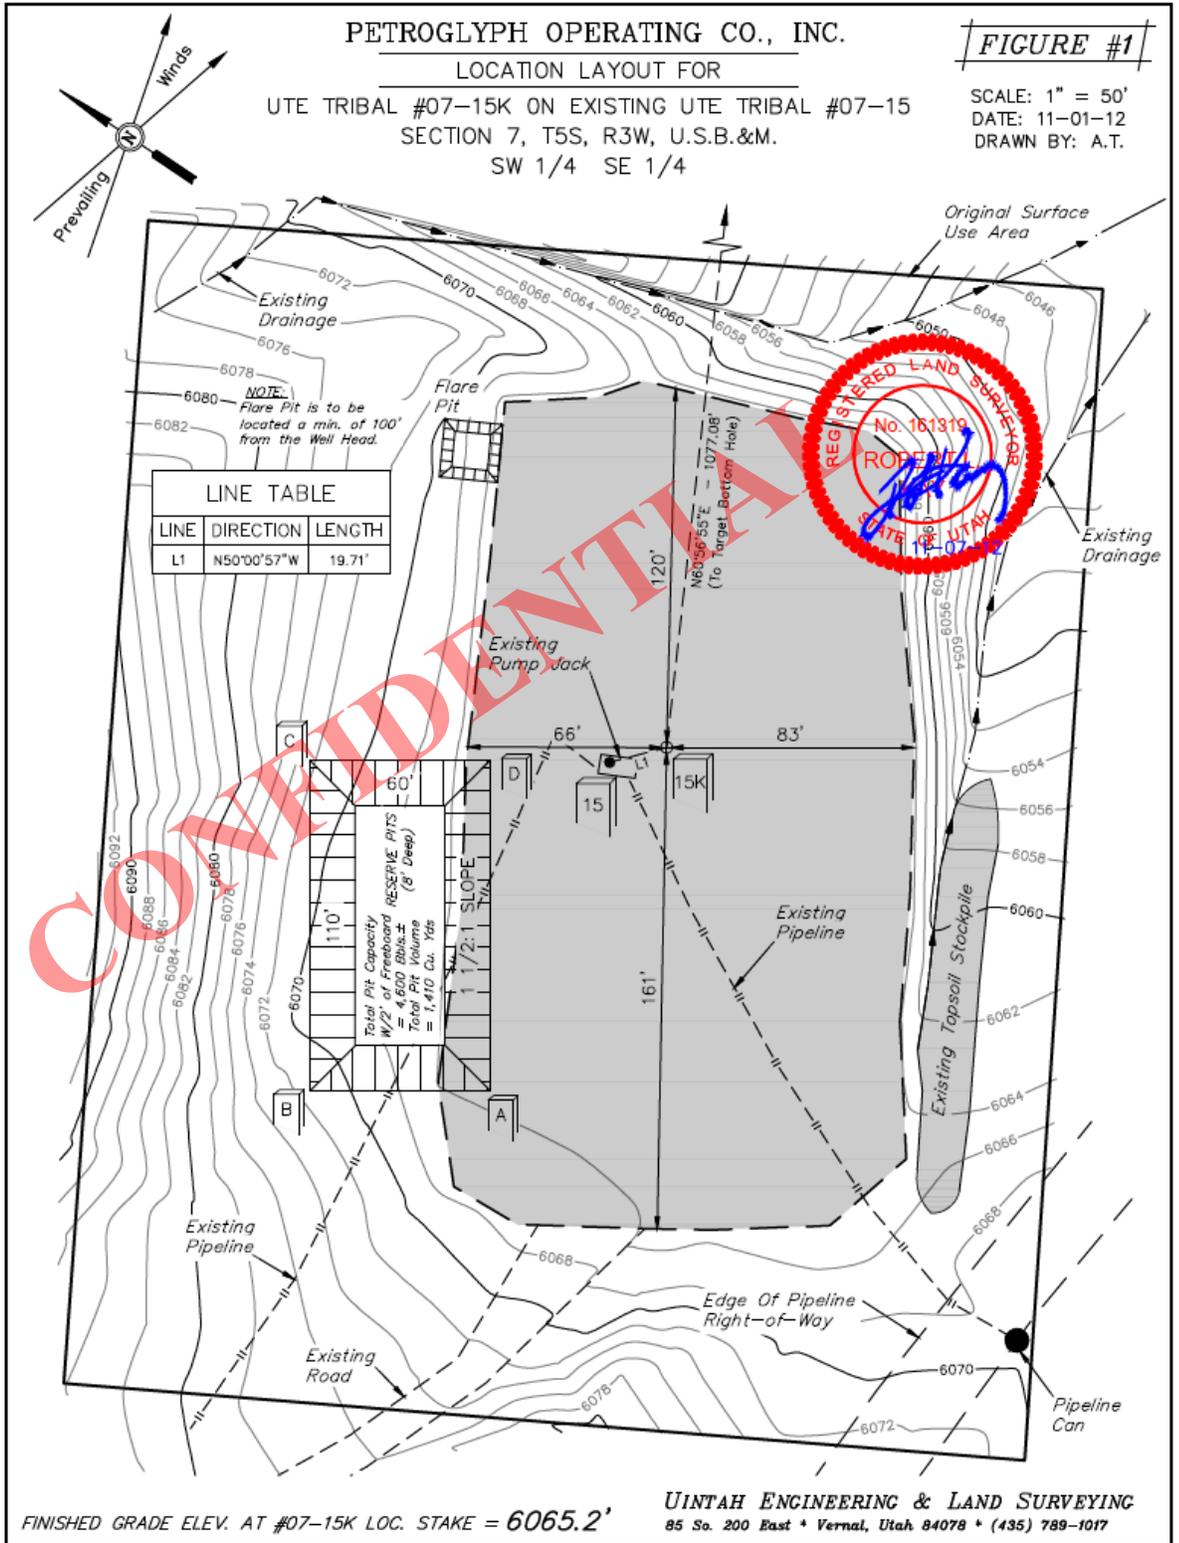


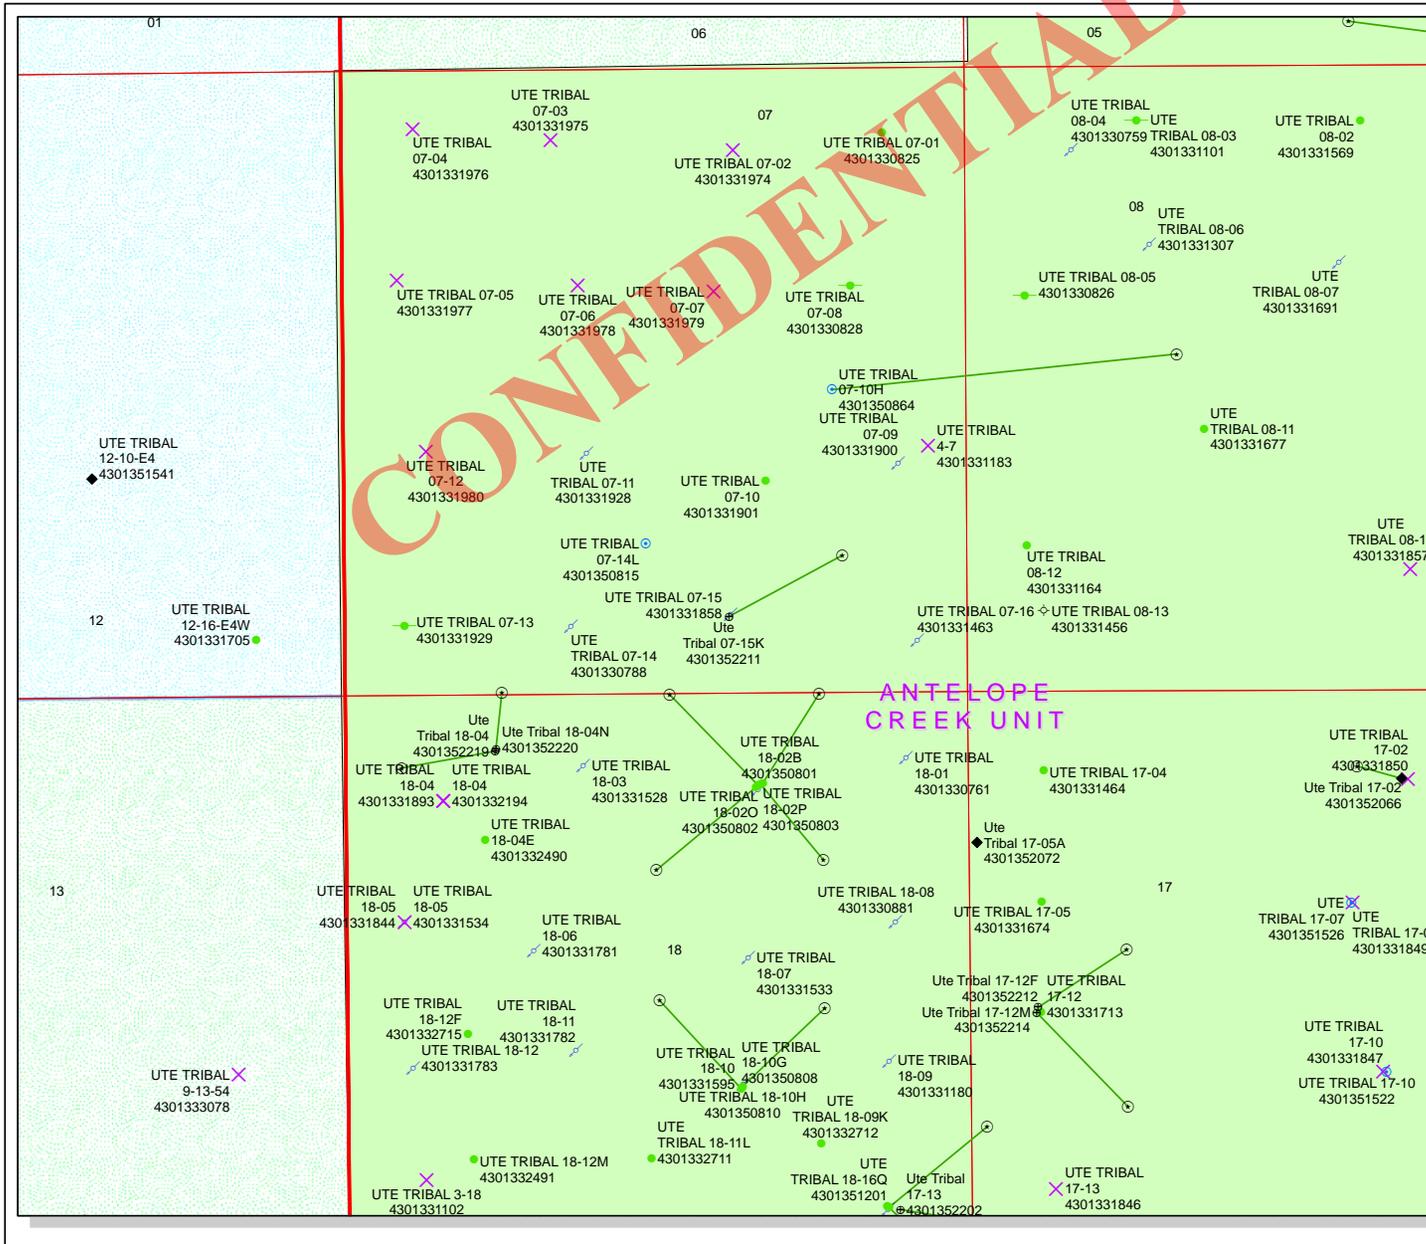

API Number: 4301352211
Well Name: Ute Tribal 07-15K
Township T05.0S Range R03.0W Section 07
Meridian: UBM
Operator: PETROGLYPH OPERATING CO

Map Prepared:
 Map Produced by Diana Mason

- Units STATUS**
- ACTIVE
 - EXPLORATORY
 - GAS STORAGE
 - NF PP OIL
 - NF SECONDARY
 - PI OIL
 - PP GAS
 - PP GEOTHERMAL
 - PP OIL
 - SECONDARY
 - TERMINATED



WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 5/31/2013

API NO. ASSIGNED: 43013522110000

WELL NAME: Ute Tribal 07-15K

OPERATOR: PETROGLYPH OPERATING CO (N3800)

PHONE NUMBER: 435 789-4120

CONTACT: Ed Trotter

PROPOSED LOCATION: SWSE 07 050S 030W

Permit Tech Review:

SURFACE: 0643 FSL 1965 FEL

Engineering Review:

BOTTOM: 1150 FSL 1015 FEL

Geology Review:

COUNTY: DUCHESNE

LATITUDE: 40.05555

LONGITUDE: -110.26344

UTM SURF EASTINGS: 562822.00

NORTHINGS: 4434183.00

FIELD NAME: ANTELOPE CREEK

LEASE TYPE: 2 - Indian

LEASE NUMBER: 1420H623506

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 2 - Indian

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: INDIAN - LPM4138336
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 43-8342
- RDCC Review:
- Fee Surface Agreement
- Intent to Commingle

Commingling Approved

LOCATION AND SITING:

- R649-2-3.
- Unit: ANTELOPE CREEK
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
- Board Cause No: Cause 214-2
- Effective Date: 6/9/2000
- Siting: Suspends General Siting
- R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason
15 - Directional - dmason



GARY R. HERBERT
Governor

GREGORY S. BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Ute Tribal 07-15K
API Well Number: 43013522110000
Lease Number: 1420H623506
Surface Owner: INDIAN
Approval Date: 6/12/2013

Issued to:

PETROGLYPH OPERATING CO, 960 Broadway Avenue, Ste 500, Boise, ID 83703

Authority:

Pursuant to Utah Code Ann. 40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 214-2. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well - contact Carol Daniels at 801-538-5284

(please leave a voicemail message if not available)

OR

submit an electronic sundry notice (pre-registration required) via the Utah Oil &

Gas website
at <http://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) - due within 5 days of spudding the well
- Monthly Status Report (Form 9) - due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) - due prior to implementation
- Written Notice of Emergency Changes (Form 9) - due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) - due prior to implementation
- Report of Water Encountered (Form 7) - due within 30 days after completion
- Well Completion Report (Form 8) - due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "John Rogers", written over a faint, illegible printed name.

For John Rogers
Associate Director, Oil & Gas

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

RECEIVED

JUN 06 2013

FORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010

BLM

APPLICATION FOR PERMIT TO DRILL OR REENTER

5. Lease Serial No.
1420H623506

6. If Indian, Allottee or Tribe Name
UINTAH AND OURAY

7. If Unit or CA Agreement, Name and No.
1420H624650

8. Lease Name and Well No.
UTE TRIBAL 07-15K

9. API Well No.
4301352211

10. Field and Pool, or Exploratory
ANTELOPE CREEK

11. Sec., T., R., M., or Blk. and Survey or Area
Sec 7 T5S R3W Mer UBM
SME: BIA

12. County or Parish
DUCHESNE

13. State
UT

17. Spacing Unit dedicated to this well

20. BLM/BIA Bond No. on file
LPM4138335

23. Estimated duration
45 DAYS

24. Attachments

NOV 15 2013

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- 1. Well plat certified by a registered surveyor.
- 2. A Drilling Plan.
- 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- 5. Operator certification
- 6. Such other site specific information and/or plans as may be required by the authorized officer.

DIV. OF OIL, GAS & MINING

25. Signature (Electronic Submission) Name (Printed/Typed) LESTER FARNSWORTH Ph: 435-722-2531 Date 05/31/2013

Title DISTRICT MANAGER

Approved by (Signature) Name (Printed/Typed) Jerry Kenczka NOV 12 2013

Title Assistant Field Manager Lands & Mineral Resources Office VERNAL FIELD OFFICE

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached. **CONDITIONS OF APPROVAL ATTACHED**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

Electronic Submission #209212 verified by the BLM Well Information System
For PETROGLYPH OPERATING CO INC, sent to the Vernal
Committed to AFMSS for processing by JOHNETTA MAGEE on 06/10/2013 (13JM1037AE)

NOTICE OF APPROVAL

UDOGM

** BLM REVISED **




**UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE**

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: PETROGLYPH OPERATING CO INC
Well No: UTE TRIBAL 07-15K
API No: 43-013-52211

Location: SWSE, Sec. 7, T5S, R3W
Lease No: 14-20-H62-3506
Agreement: N/A

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Construction Activity (Notify Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist)	- The Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist shall be notified at least 48 hours in advance of any construction activity. The Ute Tribal office is open Monday through Thursday.
Construction Completion (Notify Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist)	- Upon completion of the pertinent APD/ROW construction, notify the Ute Tribe Energy & Minerals Dept. for a Tribal Technician to verify the Affidavit of Completion. Notify the BLM Environmental Scientist prior to moving on the drilling rig.
Spud Notice (Notify BLM Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify BLM Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: blm_ut_vn_opreport@blm.gov .
BOP & Related Equipment Tests (Notify BLM Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify BLM Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

- Both existing and new infrastructure will be painted Covert Green
- Remove all tanks and production systems until drilling operations are complete.
- Remove all existing flow-lines on the new damage until drilling operations are complete.
- The damage corners will be re-staked before dirt work commences and a Tribal Compliance officer will be present to ensure that the dirt stays within the authorized areas.

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Gamma Ray Log shall be run for Total Depth to Surface.
- CBL will be run from TD to TOC.
- Cement for the surface casing will be circulated to the surface.
- Cement for the long-string shall be circulated 200' above surface casing shoe.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of

each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well by CD (compact disc). This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if

performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
		5. LEASE DESIGNATION AND SERIAL NUMBER: 1420H623506
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: Ute In
		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: Ute Tribal 07-15K	
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO	9. API NUMBER: 43013522110000	
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703	PHONE NUMBER: 208 685-7685 Ext	9. FIELD and POOL or WILDCAT: ANTELOPE CREEK
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0643 FSL 1965 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SWSE Section: 07 Township: 05.0S Range: 03.0W Meridian: U		COUNTY: DUCHESNE
		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input checked="" type="checkbox"/> SPUD REPORT Date of Spud: 12/5/2013 <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	
	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.		
This well was spud on 12/5/2013 at approximately 11:00 A.M. Using a Bucket Rig (BR 2) provided by Craig's Roustabout Service, Vernal Utah, we set 60' of 16" Conductor. For additional information please contact our staff at 435-722-2531.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY December 06, 2013		
NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 12/6/2013	

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 6

ENTITY ACTION FORM

Operator: Petroglyph Operating Company Operator Account Number: N 3800
 Address: P.O. Box 607
city Roosevelt
state UT zip 84066 Phone Number: (435) 722-2531

Well 1

API Number	Well Name	QQ	Sec	Twp	Rng	County
4301352211	Ute Tribal 07-15K	SWSE	7	5S	3W	Duchesne
Action Code	Current Entity Number	New Entity Number		Spud Date		Entity Assignment Effective Date
B	99999	09392		12/5/2013		12-20-2013
Comments: Please add well to existing Ute Tribal 07-14 Tank Battery.						CONFIDENTIAL

Well 2

API Number	Well Name	QQ	Sec	Twp	Rng	County
Action Code	Current Entity Number	New Entity Number		Spud Date		Entity Assignment Effective Date
Comments:						

Well 3

API Number	Well Name	QQ	Sec	Twp	Rng	County
Action Code	Current Entity Number	New Entity Number		Spud Date		Entity Assignment Effective Date
Comments:						

RECEIVED

ACTION CODES:

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (Explain in 'comments' section)

DEC 19 2013

Rodrigo Jurado
 Name (Please Print)

 Signature
 Regulatory Compliance Spc 12/18/2013
 Title Date

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
		5. LEASE DESIGNATION AND SERIAL NUMBER: 1420H623506
SUNDRY NOTICES AND REPORTS ON WELLS		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: UTE
Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
1. TYPE OF WELL Oil Well		8. WELL NAME and NUMBER: Ute Tribal 07-15K
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO		9. API NUMBER: 43013522110000
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703	PHONE NUMBER: 208 685-7685 Ext	9. FIELD and POOL or WILDCAT: ANTELOPE CREEK
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0643 FSL 1965 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SWSE Section: 07 Township: 05.0S Range: 03.0W Meridian: U		COUNTY: DUCHESNE
		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: <input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 3/17/2014 <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> DEEPEN <input checked="" type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> WILDCAT WELL DETERMINATION <input type="checkbox"/> OTHER	
<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input type="text"/>		
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. Please see attached.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY June 04, 2014		
NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 6/4/2014	

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 9

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.


			5. LEASE DESIGNATION AND SERIAL NUMBER: 14-20-H62-3506
			6. IF INDIAN, ALLOTTEE OR TRIBE NAME: Ute Indian Tribe
			7. UNIT or CA AGREEMENT NAME: 14-20-H62-4650
1. TYPE OF WELL OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER _____			8. WELL NAME and NUMBER: Ute Tribal 07-15K
2. NAME OF OPERATOR: Petroglyph Operating Company Inc.			9. API NUMBER: 4301352211
3. ADDRESS OF OPERATOR: P.O. Box 607		CITY Roosevelt STATE UT ZIP 84066	10. FIELD AND POOL, OR WILDCAT: Antelope Creek
4. LOCATION OF WELL			
FOOTAGES AT SURFACE: 643' FSL 1965' FEL			COUNTY: Duchesne
QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: SWSE 7 5S 3W U			STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will start: _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input checked="" type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLARE
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of work completion: 3/17/2014	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/RESUME)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: _____
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On 2/13/2014 Petroglyph Operating ran GR/CBL and found ETOC @ Surface, then on 2/20/2014 perforated the following: 5940-43, 5914-22, 5873-77, 5787-93, 5779-83, 5746-50, 5709-12, 5685-87, 5614-16, 5598-5608, 5646-58, 5530-32, 5466-69, 5455-60, 5380-82, 5358-61, 5346-48, 5323-25, 5319-21, 5278-86, 5271-73, 5243-46, 5225-29, 5208-10, 5136-38, 5131-33, 5424-26, 5110-21, 4986-5000, 4981-83, 4945-50, 4936-38, 4849-51, 4842-44, 4830-33, 4688-90, 4467-69, 4420-25, 4395-4404, 4341-44, 4216-19, 4185-98, 4166-70, 4150-54 & 4070-74. We isolated and fracture treated the following intervals: 5,685'-5,943': 928 Bbls of fluid containing 90,000#'s of sand, 5,455'-5,616': 644 Bbls of fluid containing 55,000#'s of sand, 5,208'-5,382': 1,127 Bbls of fluid containing 120,000#'s of sand, 5,110'-5,138': 366 Bbls of fluid containing 20,000#'s of sand, 4,936'-5,000': 720 Bbls of fluid containing 65,000#'s of sand, 4,688'-4,851': 467 Bbls of fluid containing 35,000#'s of sand, 4,341'-4,469': 660 Bbls of fluid containing 55,000#'s of sand, 4,070'-4,219': 624 Bbls of fluid containing 43,800#'s of sand. Isolation plugs used were Halliburton 8K Composite Plugs, fluid used was Delta 140 18# gelled fluid, sand used was 20/40 Mesh Premium White Sand and plugs used were Titan 3-1/8", containing 22.7 gram charges, 0.42" EHD, 23.54" TTP @ 4 SPF @ 120* Phased. All plugs were drilled out and cleaned out to PBSD, 6,235'. The well was swabbed until a good oil cut was see, then ran a pump on 3/17/2014 and put to pump.

NAME (PLEASE PRINT) Rodrigo Jurado TITLE Regulatory Compliance Specialist
SIGNATURE  DATE 6/2/2014

(This space for State use only)

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5.LEASE DESIGNATION AND SERIAL NUMBER: 1420H623506
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: UTE 7.UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: Ute Tribal 07-15K
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO	9. API NUMBER: 43013522110000
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703	PHONE NUMBER: 208 685-7685 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0659 FSL 1946 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SWSE Section: 07 Township: 05.0S Range: 03.0W Meridian: U	9. FIELD and POOL or WILDCAT: ANTELOPE CREEK COUNTY: DUCHESNE STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 12/6/2013	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> OTHER	OTHER: <input type="text" value="Well Head Spacing"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.


The well head spacing on the pad referenced above was revised to accommodate the footprint of the available drill rig, Capstar 334. The well's revised location is 659' FNL, 1946' FEL, SW/SE Section 7, Township 5 South, Range 3 West, Duchesne County Utah. Please see the attached revised plats.

**Approved by the
 Utah Division of
 Oil, Gas and Mining
 July 01, 2014**

Date: _____

By: 

NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 6/23/2014	

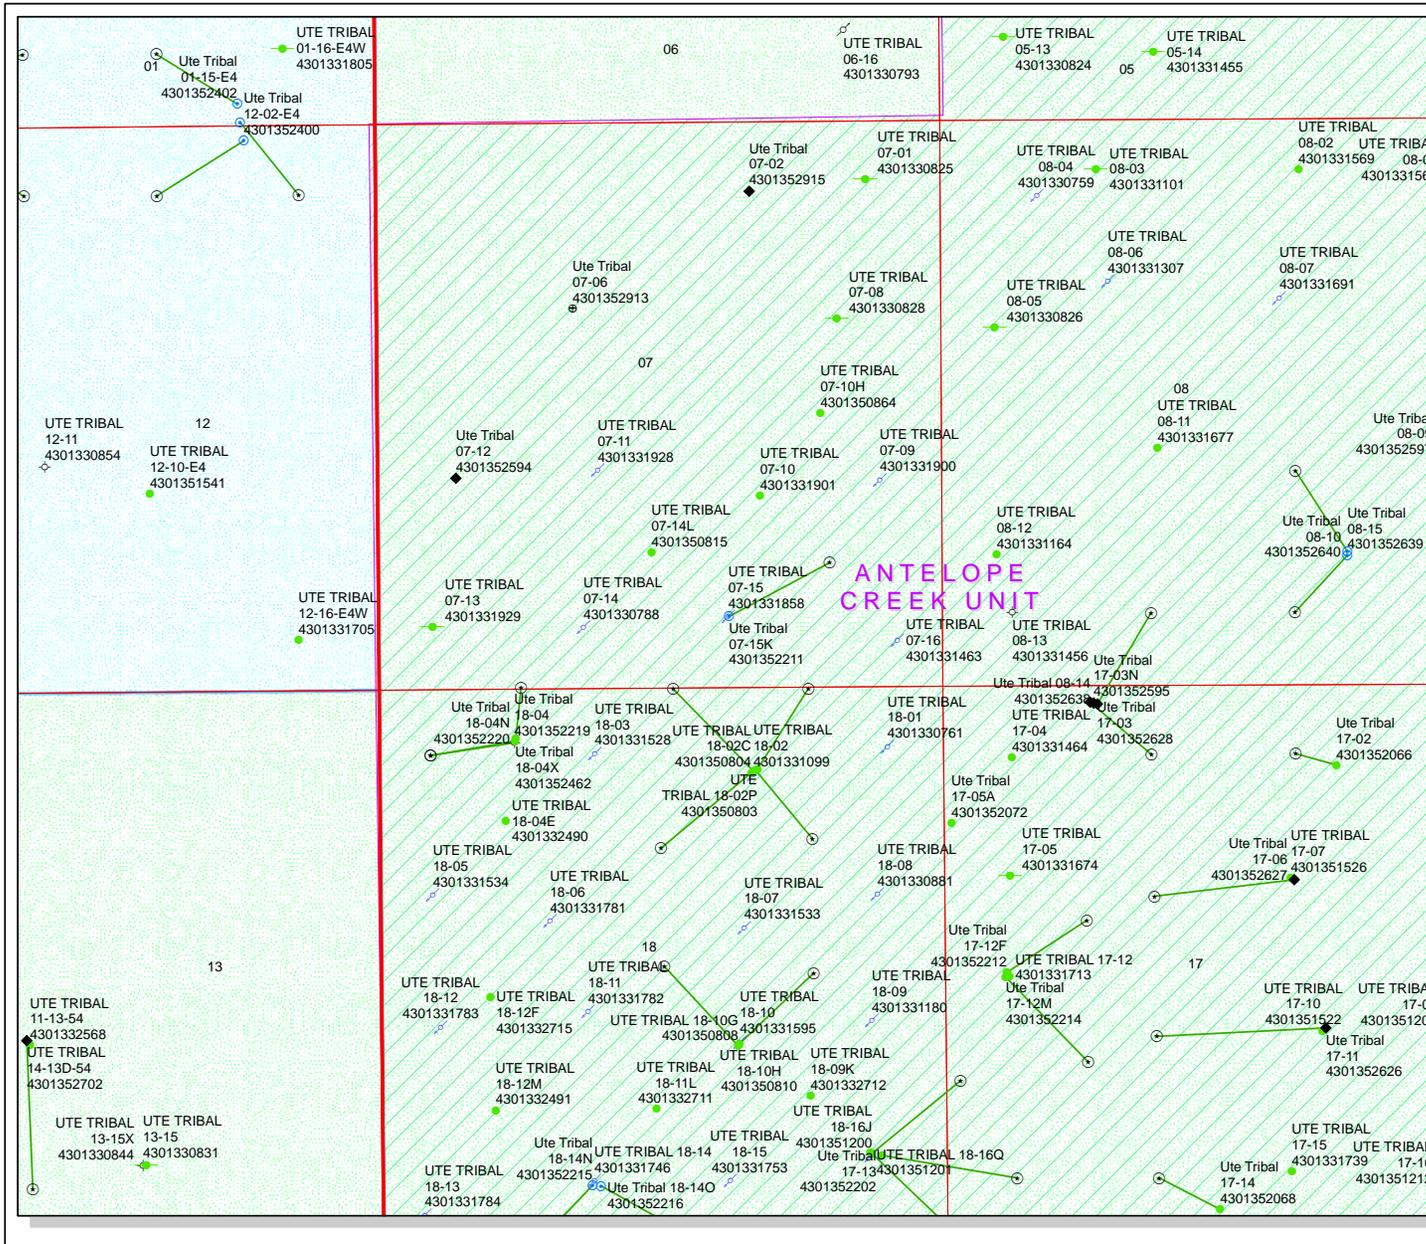

API Number: 4301352211


Well Name: Ute Tribal 07-15K

Township: T05.0S Range: R03.0W Section: 07 Meridian: U

Operator: PETROGLYPH OPERATING CO

Map Prepared: 6/27/2014
Map Produced by Diana Mason

Wells Query		Units	
Status		STATUS	
APD - Approved Permit	◆	ACTIVE	▨
DRL - Spudded (Drilling Commenced)	○	EXPLORATORY	▨
GIW - Gas Injection	⚡	GAS STORAGE	▨
GS - Gas Storage	⊕	NF PP OIL	▨
LOC - New Location	⊕	NF SECONDARY	▨
OPS - Operation Suspended	⊕	PI OIL	▨
PA - Plugged Abandoned	⊕	PP GAS	▨
PGW - Producing Gas Well	⊕	PP GEOTHERMAL	▨
POW - Producing Oil Well	⊕	PP OIL	▨
SGW - Shut-in Gas Well	⊕	SECONDARY	▨
SOW - Shut-in Oil Well	⊕	TERMINATED	▨
TA - Temp. Abandoned	⊕		
TW - Test Well	○	Fields STATUS	
WDW - Water Disposal	⊕	Unknown	▨
WW - Water Injection Well	⊕	ABANDONED	▨
WSW - Water Supply Well	⊕	ACTIVE	▨
		COMBINED	▨
		INACTIVE	▨
		STORAGE	▨
		TERMINATED	▨



PETROGLYPH OPERATING CO., INC.
UTE TRIBAL #07-15K ON EXISTING #07-15
LOCATED IN DUCHESNE COUNTY, UTAH
SECTION 7, T5S, R3W, U.S.B.&M.



LOCATION STAKE

PIT "D"

PHOTO: VIEW FROM PIT "D" TO LOCATION STAKE

CAMERA ANGLE: SOUTHEASTERLY



EXISTING ACCESS

PHOTO: VIEW FROM BEGINNING OF EXISTING ACCESS

CAMERA ANGLE: SOUTHEASTERLY



- Since 1964 -

UELS Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813

LOCATION PHOTOS

11 01 12
MONTH DAY YEAR

PHOTO

TAKEN BY: J.C.

DRAWN BY: A.T.

REVISED: 00-00-00

T5S, R3W, U.S.B.&M.

PETROGLYPH OPERATING CO., INC.


Well location, UTE TRIBAL #07-15K, located as shown in the SW 1/4 SE 1/4 of Section 7, T5S, R3W, U.S.B.&M., Duchesne County, Utah.

BASIS OF ELEVATION


BRASS CAP SET IN CONCRETE BY SUNRISE ENGINEERING LOCATED IN THE SE 1/4 OF SECTION 16, T5S, R3W, U.S.B.&M. SAID ELEVATION IS MARKED AS BEING 6281.9 FEET.

BASIS OF BEARINGS

BASIS OF BEARINGS IS A G.P.S. OBSERVATION.

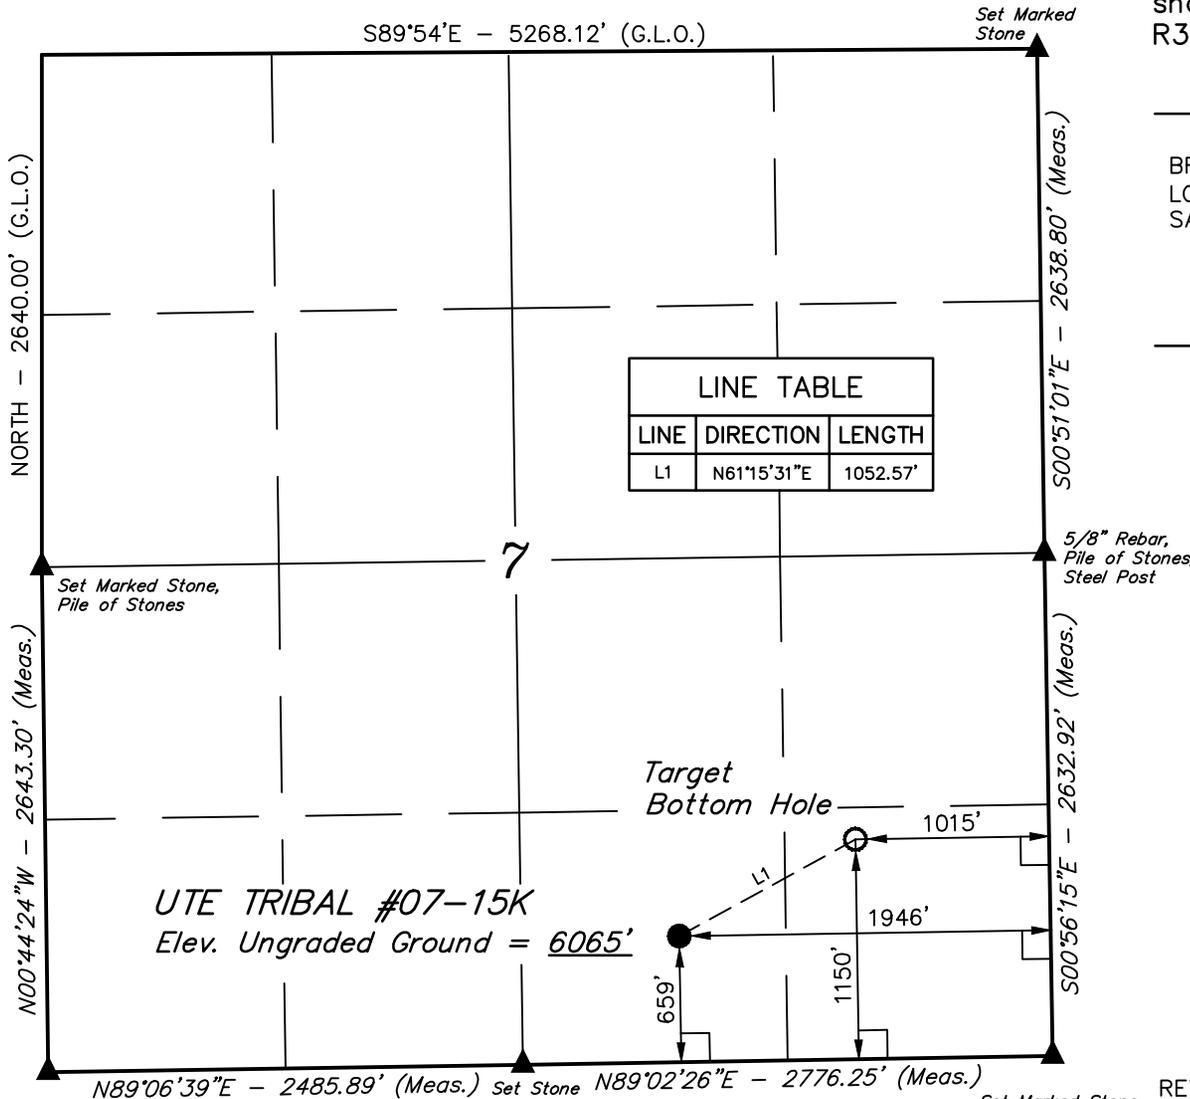

LINE TABLE		
LINE	DIRECTION	LENGTH
L1	N61°15'31"E	1052.57'

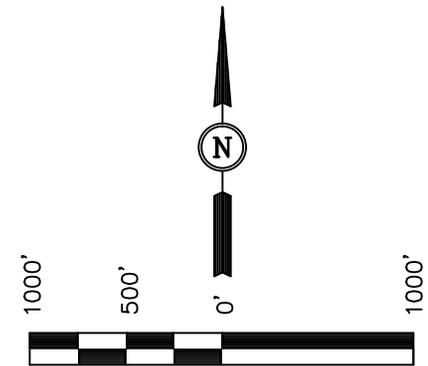

SCALE

CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

Robert KAY
 REGISTERED LAND SURVEYOR
 REGISTRATION NO. 161319
 STATE OF UTAH

REV: 12-03-13 J.J.

UINTAH ENGINEERING & LAND SURVEYING
 85 SOUTH 200 EAST - VERNAL, UTAH 84078
 (435) 789-1017

Position Re-Established Using Bearing Tree Information (Not Set on Ground)

LEGEND:

- └─┘ = 90° SYMBOL
- = PROPOSED WELL HEAD.
- ▲ = SECTION CORNERS LOCATED.

NAD 83 (TARGET BOTTOM HOLE)		NAD 83 (SURFACE LOCATION)	
LATITUDE = 40°03'25.13" (40.056981)	LONGITUDE = 110°15'35.40" (110.259833)	LATITUDE = 40°03'20.26" (40.055628)	LONGITUDE = 110°15'47.36" (110.263156)
NAD 27 (TARGET BOTTOM HOLE)		NAD 27 (SURFACE LOCATION)	
LATITUDE = 40°03'25.27" (40.057019)	LONGITUDE = 110°15'32.85" (110.259125)	LATITUDE = 40°03'20.40" (40.055667)	LONGITUDE = 110°15'44.81" (110.262447)

SCALE 1" = 1000'	DATE SURVEYED: 10-23-12	DATE DRAWN: 11-01-12
PARTY G.O. D.D. A.T.	REFERENCES G.L.O. PLAT	
WEATHER COLD	FILE PETROGLYPH OPERATING CO., INC.	



PETROGLYPH OPERATING CO., INC.

LOCATION LAYOUT FOR

**UTE TRIBAL #07-15K ON EXISTING UTE TRIBAL #07-15
SECTION 7, T5S, R3W, U.S.B.&M.
SW 1/4 SE 1/4**

FIGURE #1

SCALE: 1" = 50'
DATE: 11-01-12
DRAWN BY: A.T.
REV: 12-03-13 J.J.

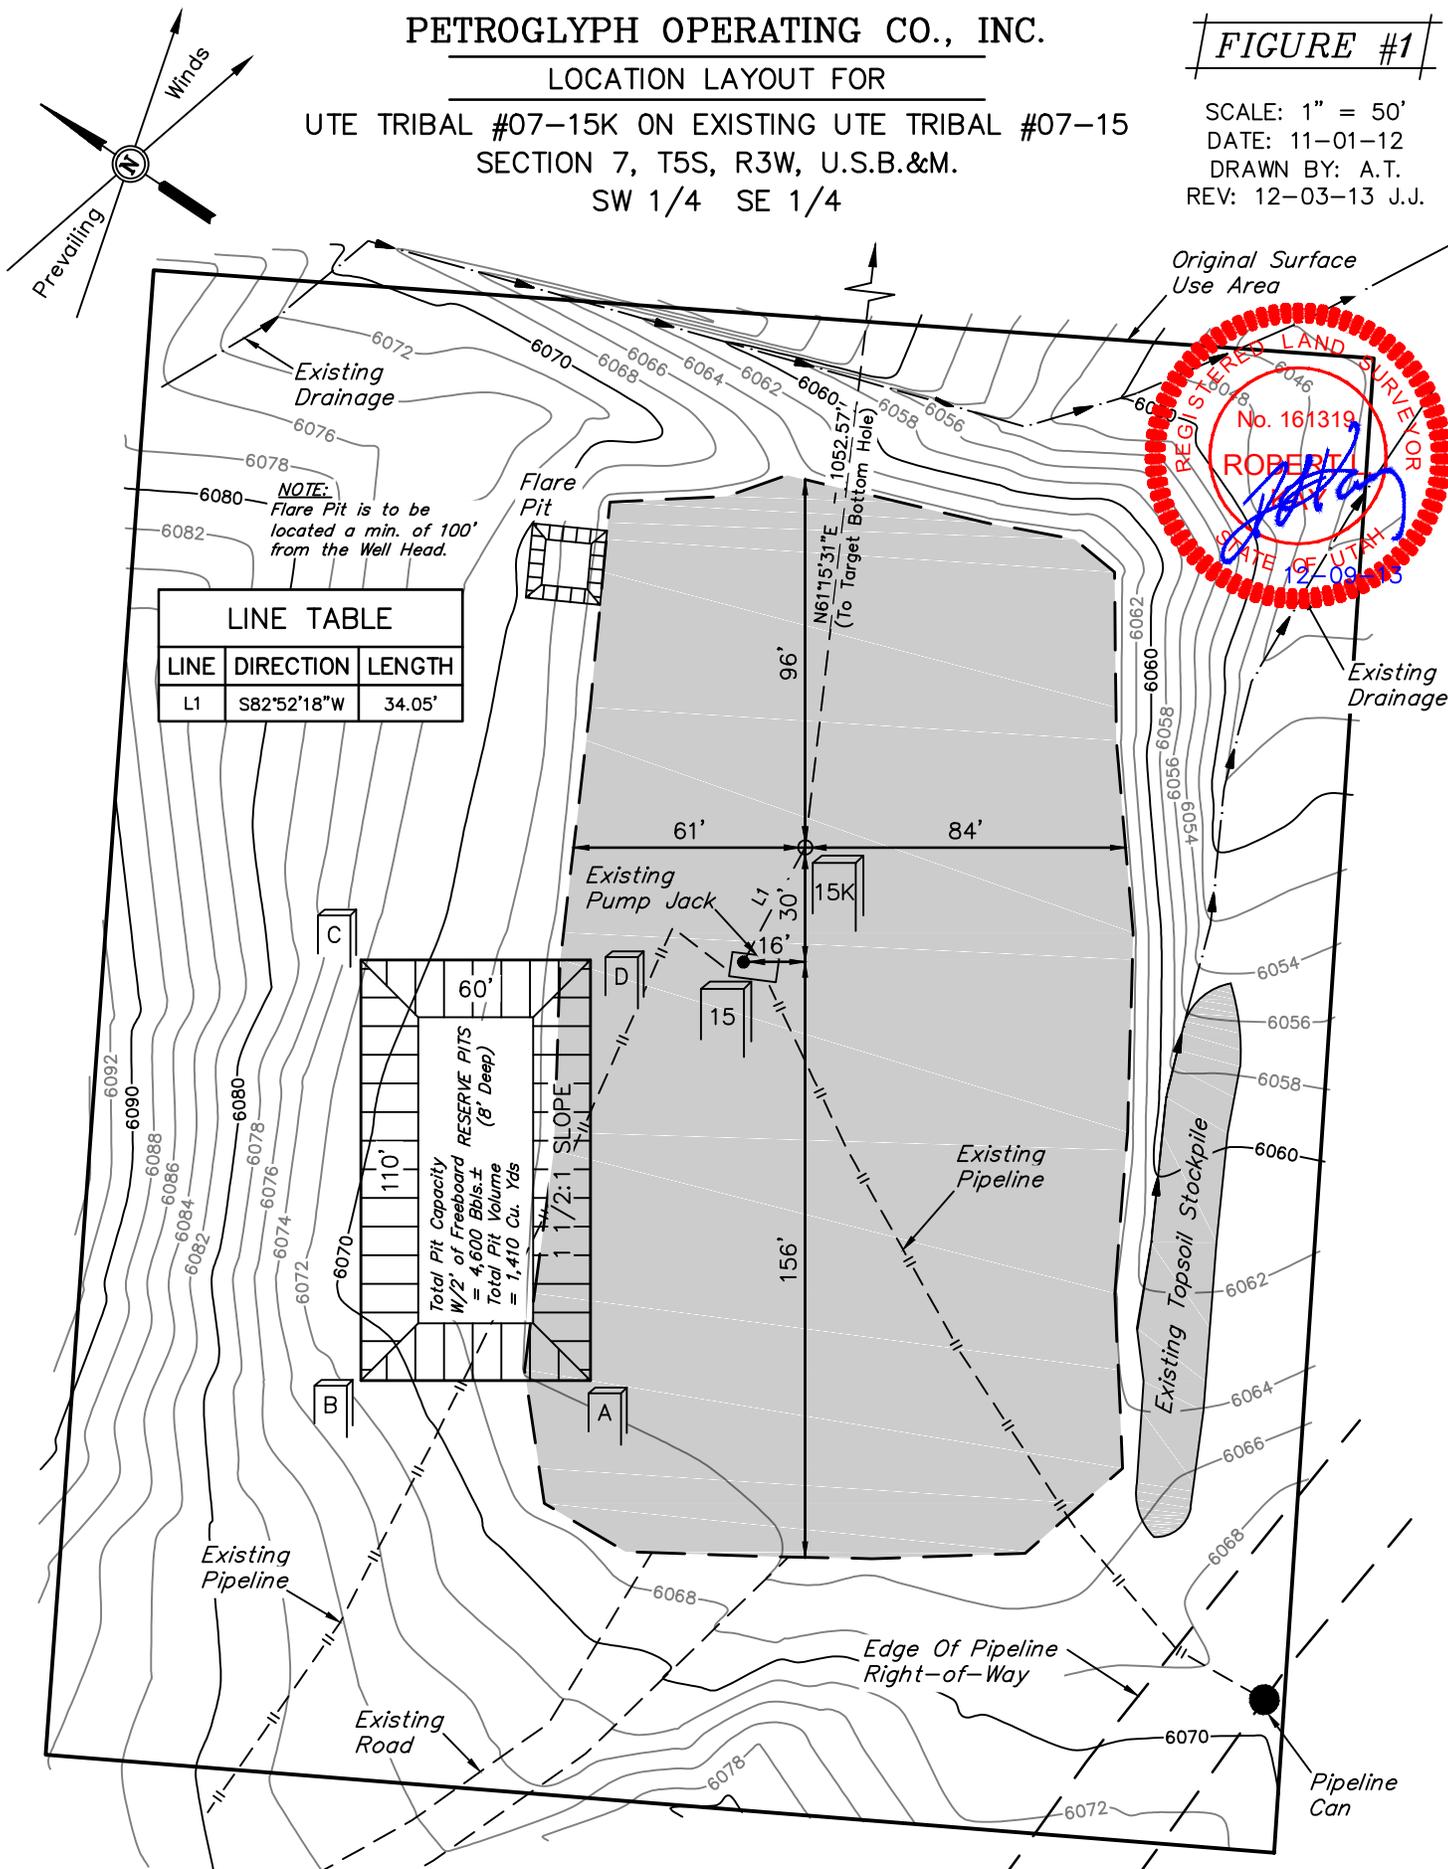

FINISHED GRADE ELEV. AT #07-15K LOC. STAKE = 6065.2'

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East * Vernal, Utah 84078 * (435) 789-1017

RECEIVED: Jun. 23, 2014



PETROGLYPH OPERATING CO., INC.

TYPICAL RIG LAYOUT FOR

UTE TRIBAL #07-15K ON EXISTING UTE TRIBAL #07-15
SECTION 7, T5S, R3W, U.S.B.&M.
SW 1/4 SE 1/4

FIGURE #2

SCALE: 1" = 50'
DATE: 11-01-12
DRAWN BY: A.T.
REV: 12-03-13 J.J.

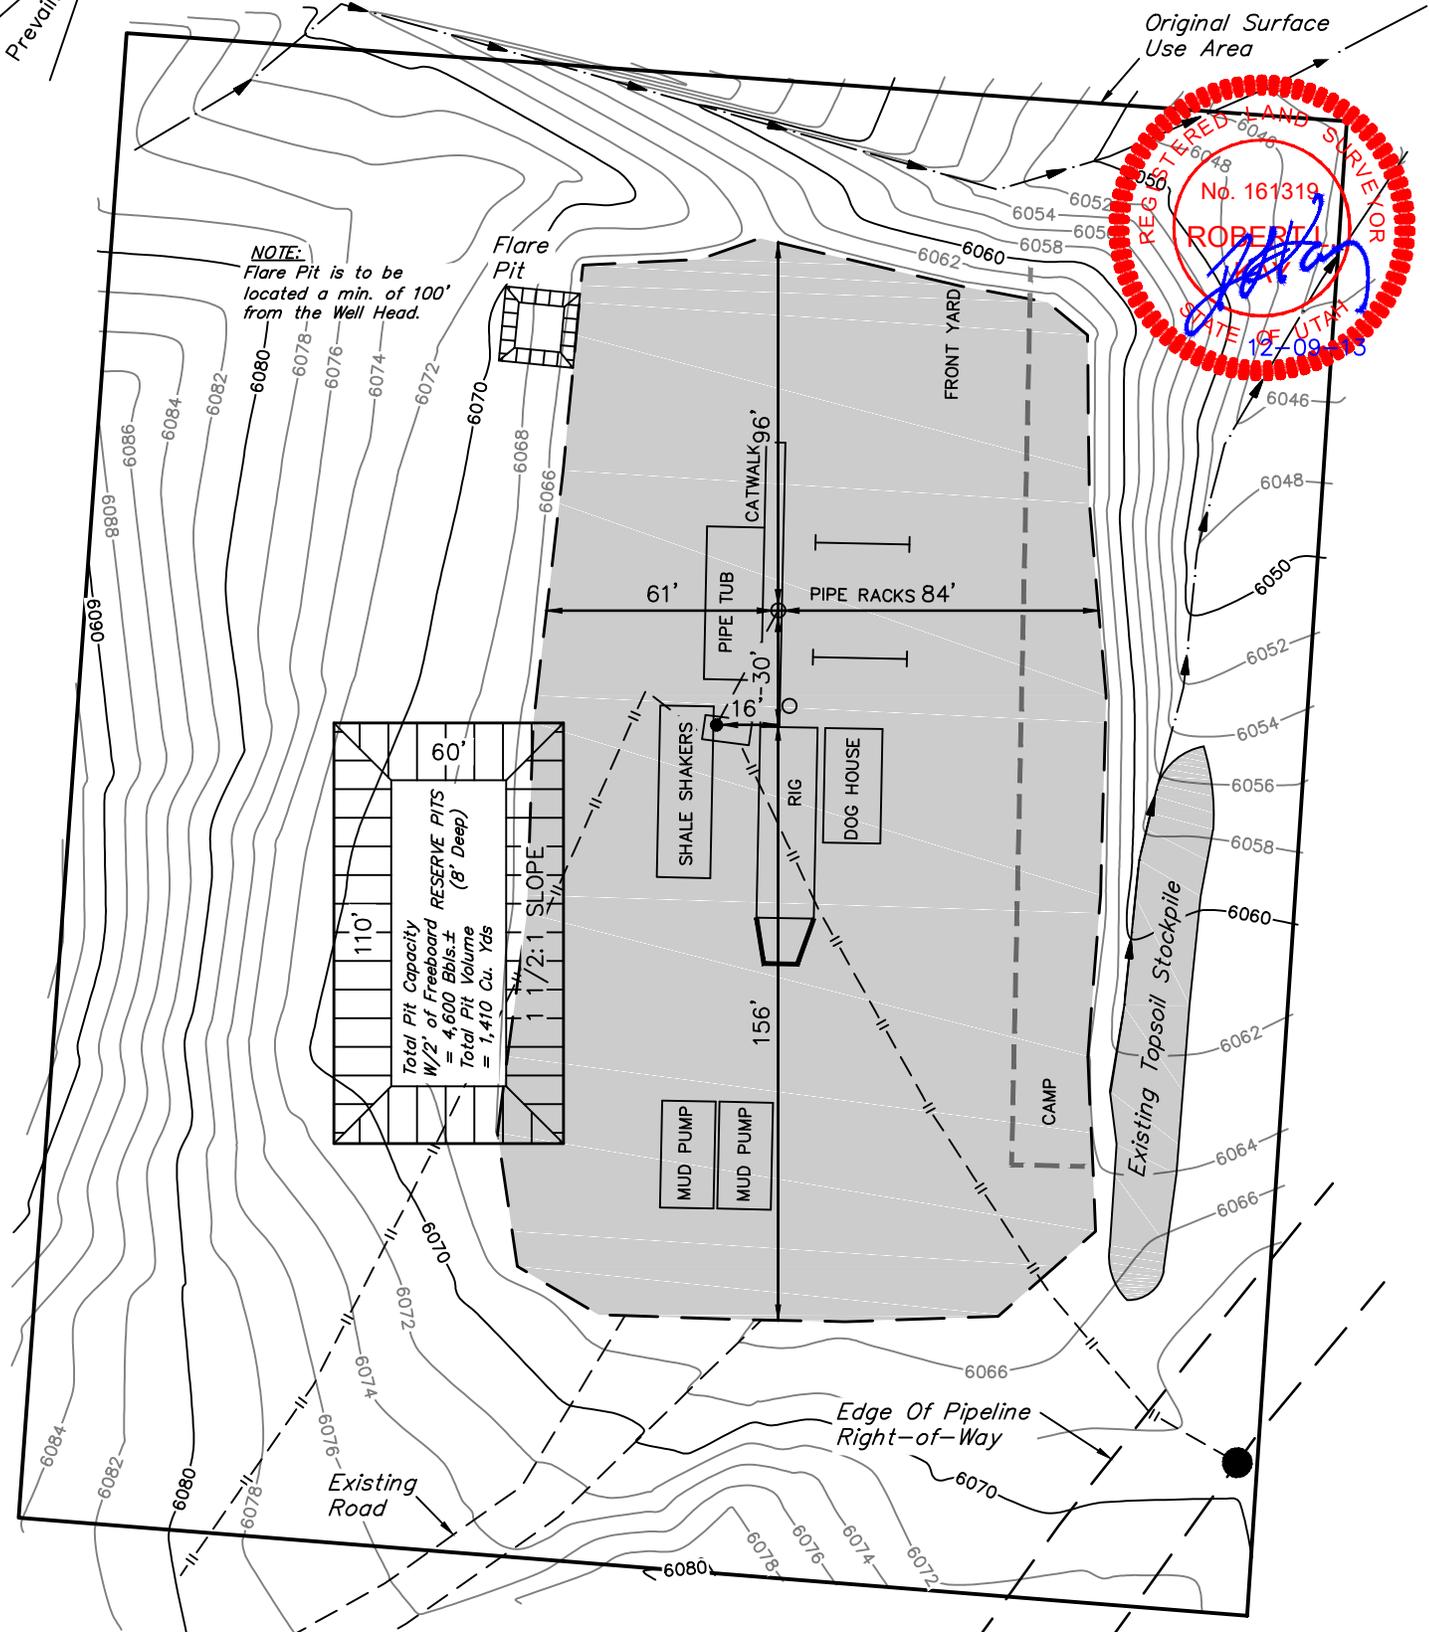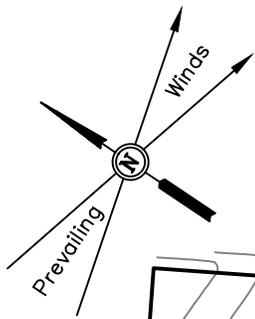

NOTE:
Flare Pit is to be located a min. of 100' from the Well Head.


110'
80'
Total Pit Capacity
W/2' of Freeboard
RESERVE PITS
= 4,600 Bbls. ±
(8' Deep)
Total Pit Volume
= 1,410 Cu. Yds
1 1/2:1 SLOPE



**PETROGLYPH OPERATING CO., INC.
UTE TRIBAL #07-15K ON EXISTING
UTE TRIBAL #07-15
SECTION 7, T5S, R3W, U.S.B.&M.**

PROCEED IN A SOUTHWESTERLY DIRECTION FROM MYTON, UTAH ALONG U.S. HIGHWAY 40 APPROXIMATELY 8.3 MILES TO THE JUNCTION OF THIS ROAD AND ANTELOPE CANYON ROAD TO THE SOUTH; TURN LEFT AND PROCEED IN A SOUTHERLY DIRECTION APPROXIMATELY 6.3 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTHEAST; TURN LEFT AND PROCEED IN A SOUTHEASTERLY DIRECTION APPROXIMATELY 0.8 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE WEST; TURN RIGHT AND PROCEED IN A WESTERLY, THEN NORTHWESTERLY, THEN SOUTHWESTERLY DIRECTION APPROXIMATELY 1.8 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING LOCATION UTE TRIBAL #7-14 AND AN EXISTING ROAD TO THE TO THE EAST; PROCEED IN AN EASTERLY DIRECTION APPROXIMATELY 0.2 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE NORTHEAST; TURN LEFT AND PROCEED IN A NORTHEASTERLY DIRECTION APPROXIMATELY 0.1 MILES TO THE BEGINNING OF THE EXISTING ACCESS TO THE SOUTHEAST; PROCEED IN A SOUTHEASTERLY DIRECTION APPROXIMATELY 147' TO THE PROPOSED LOCATION.

TOTAL DISTANCE FROM MYTON, UTAH TO THE PROPOSED WELL LOCATION IS APPROXIMATELY 17.5 MILES.

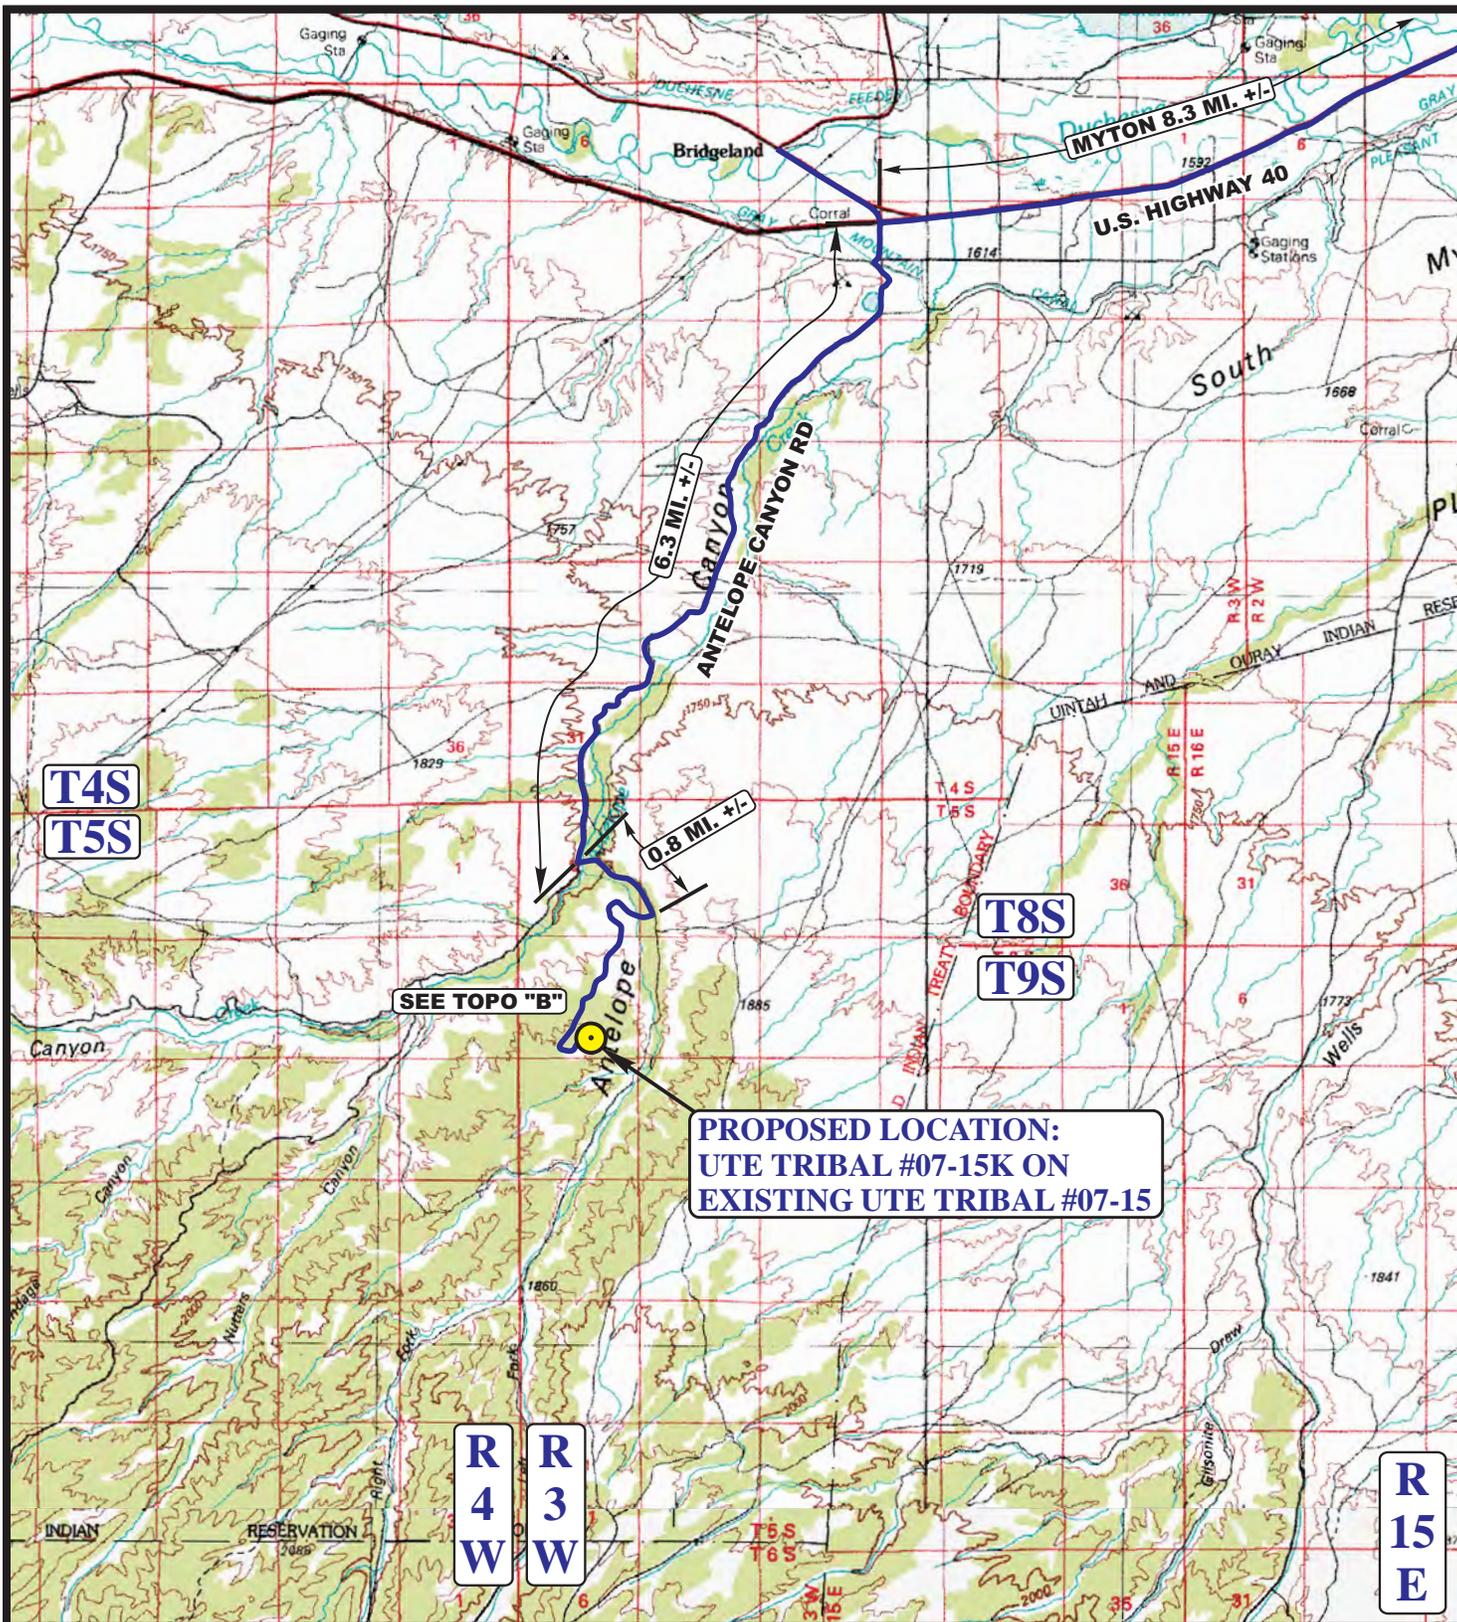

SEE TOPO "B"

**PROPOSED LOCATION:
UTE TRIBAL #07-15K ON
EXISTING UTE TRIBAL #07-15**

LEGEND:

PROPOSED LOCATION

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #07-15K ON
EXISTING UTE TRIBAL #07-15
SECTION 7, T5S, R3W, U.S.B.&M.
SW 1/4 SE 1/4



Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813




**ACCESS ROAD
MAP**

11	01	12
MONTH	DAY	YEAR



SCALE: 1:100,000 DRAWN BY: A.T. REV: 11-12-13 L.S.

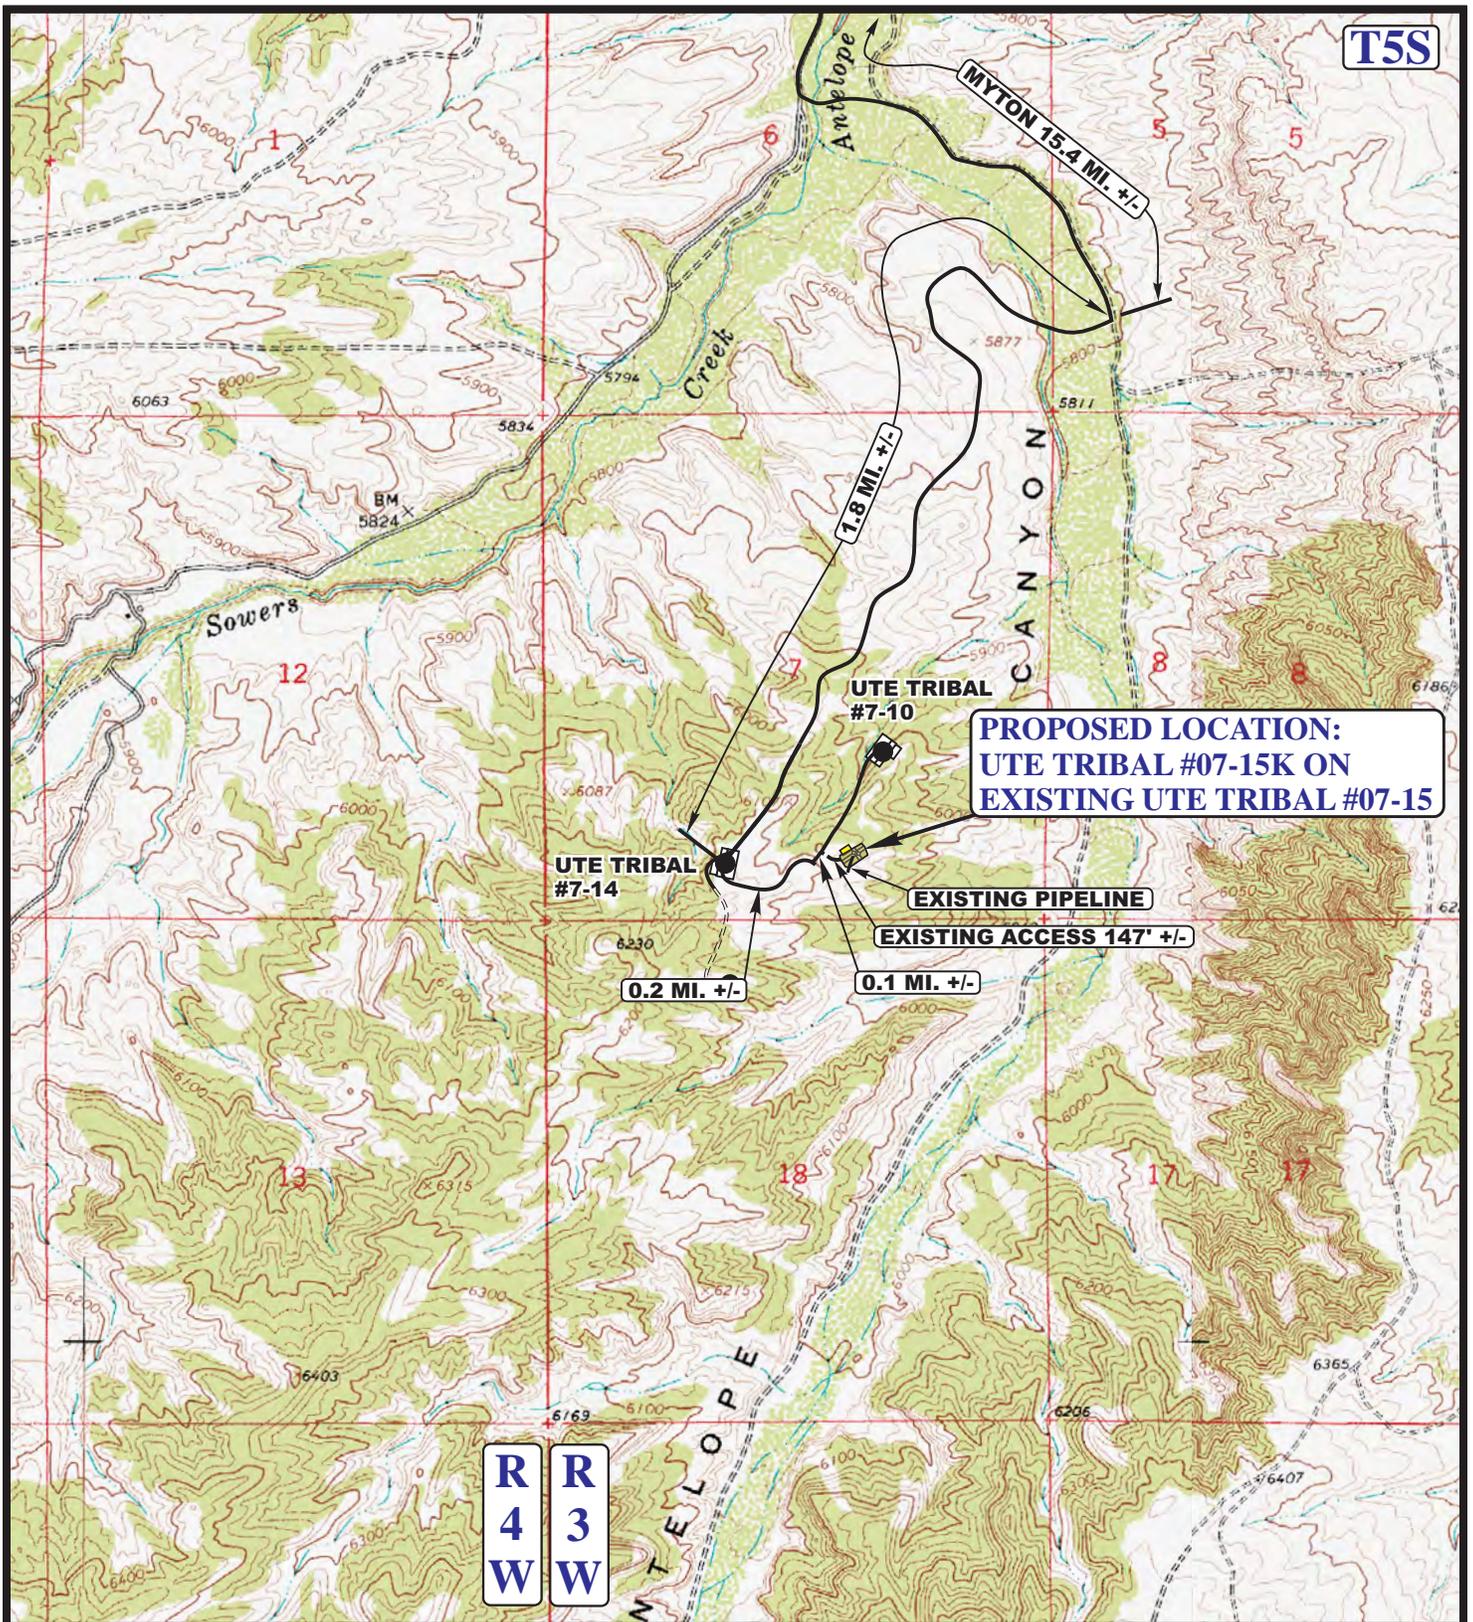

T5S

**PROPOSED LOCATION:
UTE TRIBAL #07-15K ON
EXISTING UTE TRIBAL #07-15**

**R
4
W** **R
3
W**

LEGEND:

- EXISTING ROAD
- PROPOSED ACCESS ROAD
- EXISTING PIPELINE


UES Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #07-15K ON
EXISTING UTE TRIBAL #07-15
SECTION 7, T5S, R3W, U.S.B.&M.
SW 1/4 SE 1/4

ACCESS ROAD MAP	11	01	12	B TOPO
	MONTH	DAY	YEAR	
SCALE: 1" = 2000'	DRAWN BY: A.T.		REV: 11-12-13 L.S.	



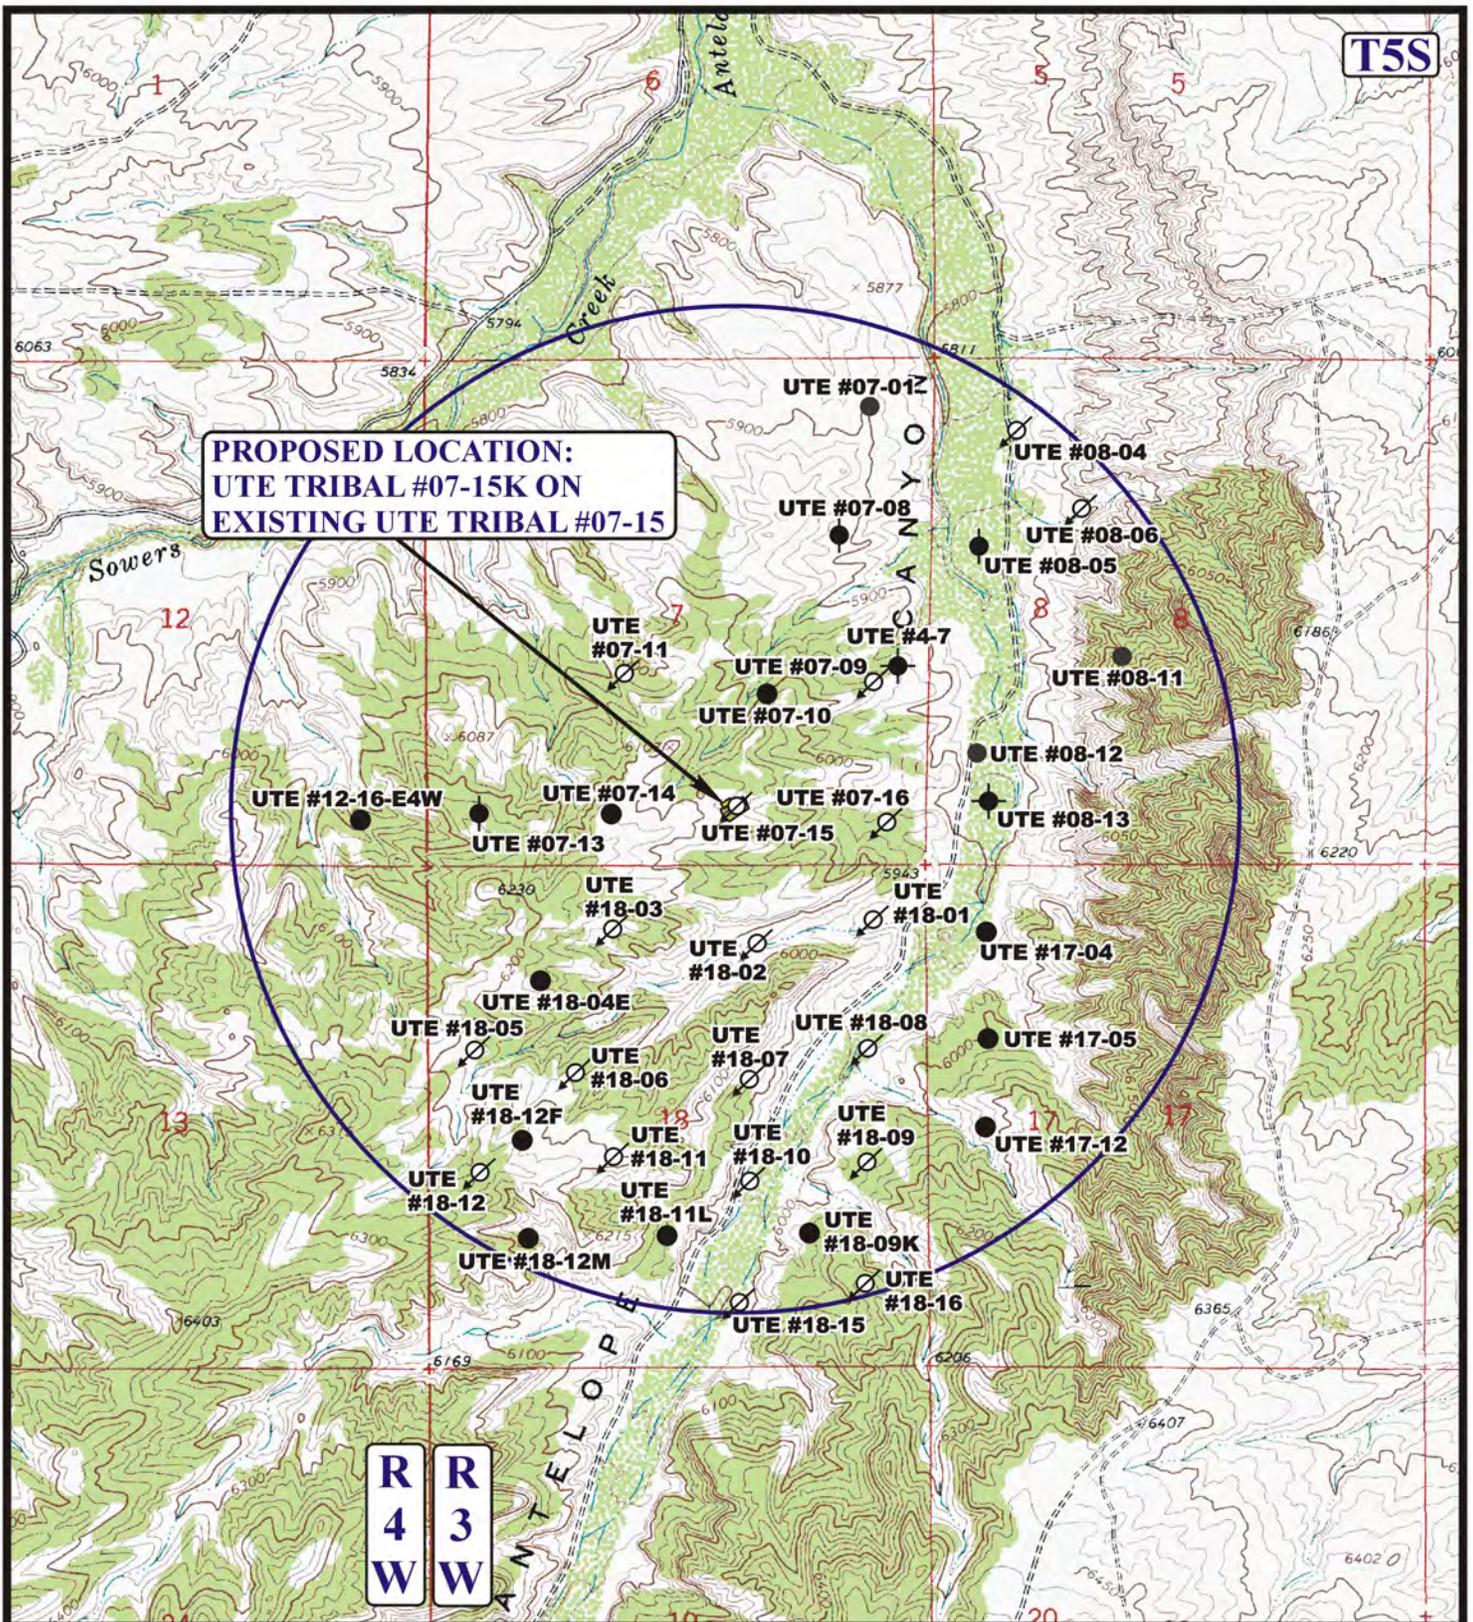

- LEGEND:**
- ⊗ DISPOSAL WELLS
 - PRODUCING WELLS
 - SHUT IN WELLS
 - ABANDONED WELLS
 - TEMPORARILY ABANDONED

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #07-15K ON
EXISTING UTE TRIBAL #07-15
SECTION 7, T5S, R3W, U.S.B.&M.
SW 1/4 SE 1/4

UELS Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813

TOPOGRAPHIC MAP 11 01 12
MONTH DAY YEAR
SCALE: 1" = 2000' DRAWN BY: A.T. REV: 11-12-13 L.S. **C TOPO**

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

AMENDED REPORT FORM 8
(highlight changes)

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. TYPE OF WELL: OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> DRY <input type="checkbox"/> OTHER _____		5. LEASE DESIGNATION AND SERIAL NUMBER: 14-20-H62-3506
b. TYPE OF WORK: NEW WELL <input checked="" type="checkbox"/> HORIZ. LATS. <input type="checkbox"/> DEEP-EN <input type="checkbox"/> RE-ENTRY <input type="checkbox"/> DIFF. RESVR <input type="checkbox"/> OTHER _____		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: Ute Indian Tribe
2. NAME OF OPERATOR: Petroglyph Operating Company, Inc.		7. UNIT OR CA AGREEMENT NAME: 14-20-H62-4650
3. ADDRESS OF OPERATOR: P.O. Box 607 CITY Roosevelt STATE UT ZIP 84066		8. WELL NAME and NUMBER: Ute Tribal 07-15K
PHONE NUMBER: (435) 722-2531		9. API NUMBER: 4301352211
4. LOCATION OF WELL (FOOTAGES): AT SURFACE: 659' FSL, 1946' FEL AT TOP PRODUCING INTERVAL REPORTED BELOW: 973' FSL, 1256' FEL SE/SE Sec. 7 T5S R3W AT TOTAL DEPTH: 1015' FSL, 1125' FEL SE/SE Sec. 7 T5S R3W		10. FIELD AND POOL, OR WLDCAT: Antelope Creek
		11. QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: SWSE 7 5S 3W U
		12. COUNTY: Duchesne 13. STATE: UTAH

14. DATE SPUNDED: 12/6/2013	15. DATE T.D. REACHED: 2/3/2014	16. DATE COMPLETED: 3/17/2014	ABANDONED <input type="checkbox"/> READY TO PRODUCE <input checked="" type="checkbox"/>	17. ELEVATIONS (DF, RKB, RT, GL): 6078' RKB
18. TOTAL DEPTH: MD 6,315 TVD 6,204	19. PLUG BACK T.D.: MD 6,235 TVD 6,124	20. IF MULTIPLE COMPLETIONS, HOW MANY? *		21. DEPTH BRIDGE MD PLUG SET: TVD
22. TYPE ELECTRIC AND OTHER MECHANICAL LOGS RUN (Submit copy of each) SDDSN, ACTR, Cement Bond Log, Borehole Volume Plot			23. WAS WELL CORED? NO <input checked="" type="checkbox"/> YES <input type="checkbox"/> (Submit analysis) WAS DST RUN? NO <input checked="" type="checkbox"/> YES <input type="checkbox"/> (Submit report) DIRECTIONAL SURVEY? NO <input type="checkbox"/> YES <input checked="" type="checkbox"/> (Submit copy)	

24. CASING AND LINER RECORD (Report all strings set in well)

HOLE SIZE	SIZE/GRADE	WEIGHT (#/ft.)	TOP (MD)	BOTTOM (MD)	STAGE CEMENTER DEPTH	CEMENT TYPE & NO. OF SACKS	SLURRY VOLUME (BBL)	CEMENT TOP **	AMOUNT PULLED
26	16 J-55	75	0	73				0	Conductor
12.25	8.625 J-55	24	0	520		G 350	72	0	
7.875	5.5 J-55	15.5	0	6,294		G 860	163	0 CBL	

25. TUBING RECORD

SIZE	DEPTH SET (MD)	PACKER SET (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)
2.875	5,987							

26. PRODUCING INTERVALS

FORMATION NAME	TOP (MD)	BOTTOM (MD)	TOP (TVD)	BOTTOM (TVD)	INTERVAL (Top/Bot - MD)	SIZE	NO. HOLES	PERFORATION STATUS
(A) Green River	4,070	5,940	3,971	5,832	4,070 5,940	0.42	776	Open <input checked="" type="checkbox"/> Squeezed <input type="checkbox"/>
(B)								Open <input type="checkbox"/> Squeezed <input type="checkbox"/>
(C)								Open <input type="checkbox"/> Squeezed <input type="checkbox"/>
(D)								Open <input type="checkbox"/> Squeezed <input type="checkbox"/>

27. PERFORATION RECORD

28. ACID, FRACTURE, TREATMENT, CEMENT SQUEEZE, ETC.

DEPTH INTERVAL	AMOUNT AND TYPE OF MATERIAL
4,070'-5,940'	5,536 Bbls of Delta 140 18# Gelled Fluid Containing 483,800#'s of 20/40 Mesh Sand.

29. ENCLOSED ATTACHMENTS:

- | | | | |
|---|--|--|--|
| <input checked="" type="checkbox"/> ELECTRICAL/MECHANICAL LOGS | <input type="checkbox"/> GEOLOGIC REPORT | <input type="checkbox"/> DST REPORT | <input checked="" type="checkbox"/> DIRECTIONAL SURVEY |
| <input type="checkbox"/> SUNDRY NOTICE FOR PLUGGING AND CEMENT VERIFICATION | <input type="checkbox"/> CORE ANALYSIS | <input checked="" type="checkbox"/> OTHER: <u>DOG M Form 7</u> | |

30. WELL STATUS:

POW

31. INITIAL PRODUCTION

INTERVAL A (As shown in item #26)

DATE FIRST PRODUCED: 3/5/2014		TEST DATE: 5/19/2014		HOURS TESTED: 24		TEST PRODUCTION RATES: →	OIL – BBL: 51	GAS – MCF: 17	WATER – BBL: 107	PROD. METHOD: Rod Pump
CHOKE SIZE: 32/64	TBG. PRESS. 82	CSG. PRESS. 82	API GRAVITY 40.90	BTU – GAS 1	GAS/OIL RATIO 333	24 HR PRODUCTION RATES: →	OIL – BBL: 51	GAS – MCF: 17	WATER – BBL: 107	INTERVAL STATUS: Open

INTERVAL B (As shown in item #26)

DATE FIRST PRODUCED:		TEST DATE:		HOURS TESTED:		TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	INTERVAL STATUS:

INTERVAL C (As shown in item #26)

DATE FIRST PRODUCED:		TEST DATE:		HOURS TESTED:		TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	INTERVAL STATUS:

INTERVAL D (As shown in item #26)

DATE FIRST PRODUCED:		TEST DATE:		HOURS TESTED:		TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	INTERVAL STATUS:

32. DISPOSITION OF GAS (Sold, Used for Fuel, Vented, Etc.)

Used for Fuel

33. SUMMARY OF POROUS ZONES (Include Aquifers):

Show all important zones of porosity and contents thereof. Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

34. FORMATION (Log) MARKERS:

Formation	Top (MD)	Bottom (MD)	Descriptions, Contents, etc.	Name	Top (Measured Depth)
				Trona	2,684
				Mahogany	2,853
				Garden Gulch	3,586
				B Marker	3,998
				X Marker	4,504
				Y Marker	4,540
				Douglas Creek	4,650
				B Lime	5,041
				Castle Peak	5,590
				Basal Carbonate	6,003

35. ADDITIONAL REMARKS (Include plugging procedure)

Sfc Footages Revised. See Sundry #52391. All Frac and Perf Info Condensed, see NOI and Sub Report Frac Sundry.

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records.

NAME (PLEASE PRINT) Rodrigo Jurado TITLE Regulatory Compliance Specialist
 SIGNATURE  DATE 6/23/2014


This report must be submitted within 30 days of

- completing or plugging a new well
- drilling horizontal laterals from an existing well bore
- recompleting to a different producing formation
- reentering a previously plugged and abandoned well
- significantly deepening an existing well bore below the previous bottom-hole depth
- drilling hydrocarbon exploratory holes, such as core samples and stratigraphic tests

* ITEM 20: Show the number of completions if production is measured separately from two or more formations.

** ITEM 24: Cement Top – Show how reported top(s) of cement were determined (circulated (CIR), calculated (CAL), cement bond log (CBL), temperature survey (TS)).

Send to: Utah Division of Oil, Gas and Mining Phone: 801-538-5340
 1594 West North Temple, Suite 1210
 Box 145801 Fax: 801-359-3940
 Salt Lake City, Utah 84114-5801



Job Number: UT141405
 Company: Petroglyph
 Lease/Well: Ute Tribal_07-15K
 Location: Sec. 7, T5S, R3W
 Rig Name: Capstar #334
 RKB: 6078
 G.L. or M.S.L.: GL_6065'

State/Country: Utah/USA
 Declination: 11.06
 Grid: True
 File name: C:\WINSERVE\UT141405.SVY
 Date/Time: 03-Feb-14 / 16:58
 Curve Name: Ute Tribal_07-15K_Actual

Payzone Directional Services LLC

WINSERVE SURVEY CALCULATIONS
 Minimum Curvature Method
 Vertical Section Plane 66.00
 Vertical Section Referenced to Wellhead
 Rectangular Coordinates Referenced to Wellhead


Measured Depth FT	Incl Angle Deg	Drift Direction Deg	True Vertical Depth	CLOSURE			Dogleg Severity Deg/100
				N-S FT	E-W FT	Vertical Section FT	
.00	.00	.00	.00	.00	.00	.00	.00
533.00	.66	228.02	532.99	-2.05	-2.28	-2.92	228.02
625.00	.30	160.00	624.99	-2.63	-2.59	-3.44	224.56
718.00	.92	90.03	717.98	-2.86	-1.76	-2.78	211.63
779.00	1.67	63.40	778.97	-2.47	-.48	-1.44	191.00
871.00	2.59	68.28	870.90	-1.10	2.65	1.98	112.46
962.00	3.47	62.56	961.77	.93	7.01	6.78	82.40
1053.00	3.96	60.19	1052.58	3.77	12.18	12.65	72.82
1144.00	5.10	65.20	1143.30	7.02	18.57	19.83	69.29
1236.00	5.80	68.98	1234.88	10.41	26.63	28.56	68.65

Measured Depth FT	Incl Angle Deg	Drift Direction Deg	True Vertical Depth	N-S FT	E-W FT	Vertical Section FT	CLOSURE		Dogleg Severity Deg/100
							Distance FT	Direction Deg	
1327.00	7.87	68.94	1325.23	14.30	36.73	39.37	39.42	68.74	2.27
1418.00	9.45	64.89	1415.19	19.70	49.31	53.06	53.10	68.22	1.86
1510.00	11.00	64.60	1505.72	26.67	64.08	69.39	69.41	67.40	1.69
1601.00	12.40	63.20	1594.83	34.80	80.64	87.83	87.83	66.66	1.57
1692.00	13.40	65.70	1683.53	43.55	98.98	108.13	108.13	66.25	1.26
1783.00	14.10	64.30	1771.93	52.70	118.58	129.76	129.76	66.04	.85
1875.00	14.80	65.80	1861.02	62.37	139.39	152.71	152.71	65.89	.86
1966.00	15.40	66.70	1948.87	71.92	161.09	176.41	176.41	65.94	.71
2057.00	16.40	68.50	2036.39	81.40	184.14	201.33	201.33	66.15	1.23
2149.00	16.60	64.50	2124.61	91.82	208.09	227.44	227.45	66.19	1.25
2240.00	16.10	66.10	2211.93	102.53	231.36	253.06	253.06	66.10	.74
2332.00	15.60	63.50	2300.43	113.22	254.09	278.17	278.17	65.98	.94
2423.00	15.90	63.80	2388.01	124.18	276.22	302.85	302.85	65.79	.34
2514.00	16.10	63.70	2475.49	135.28	298.72	327.92	327.92	65.64	.22
2605.00	16.30	62.30	2562.87	146.80	321.34	353.27	353.28	65.45	.48
2696.00	16.40	64.10	2650.19	158.35	344.20	378.85	378.88	65.30	.57
2788.00	16.60	66.30	2738.41	169.31	367.92	404.97	405.00	65.29	.71
2880.00	16.08	65.55	2826.69	179.86	391.55	430.86	430.89	65.33	.61
2971.00	16.20	64.79	2914.10	190.48	414.51	456.15	456.18	65.32	.27
3063.00	15.78	63.14	3002.54	201.60	437.28	481.47	481.52	65.25	.67
3154.00	16.44	64.15	3089.97	212.81	459.91	506.70	506.76	65.17	.79
3246.00	17.23	64.37	3178.03	224.38	483.91	533.34	533.40	65.12	.86
3337.00	16.83	63.62	3265.04	236.06	507.86	559.97	560.04	65.07	.50
3429.00	16.39	65.82	3353.20	247.30	531.64	586.26	586.34	65.05	.83
3520.00	15.95	66.21	3440.60	257.60	554.79	611.60	611.68	65.09	.50
3612.00	15.38	66.50	3529.18	267.56	577.54	636.44	636.51	65.14	.63
3703.00	15.20	68.36	3616.96	276.77	599.70	660.43	660.49	65.23	.57
3794.00	15.51	67.44	3704.71	285.84	622.02	684.51	684.56	65.32	.43
3885.00	16.26	66.91	3792.24	295.51	644.98	709.41	709.45	65.38	.84
3977.00	15.47	66.83	3880.73	305.38	668.11	734.56	734.59	65.44	.86
4068.00	14.40	67.50	3968.66	314.49	689.72	758.01	758.04	65.49	1.19
4159.00	12.90	65.90	4057.08	322.97	709.45	779.48	779.50	65.52	1.70
4251.00	11.70	64.50	4146.97	331.18	727.24	799.07	799.10	65.52	1.34
4342.00	10.20	67.60	4236.31	338.22	743.02	816.35	816.38	65.53	1.77

Measured Depth FT	Incl Angle Deg	Drift Direction Deg	True Vertical Depth	N-S FT	E-W FT	Vertical Section FT	Distance FT	CLOSURE		Dogleg Severity Deg/100
								Vertical Section FT	Distance FT	
4433.00	9.30	67.30	4326.00	344.13	757.25	831.76	831.78	65.56	.99	
4524.00	8.20	66.70	4415.94	349.53	770.00	845.60	845.62	65.58	1.21	
4616.00	7.30	68.80	4507.10	354.24	781.47	858.00	858.01	65.62	1.03	
4707.00	6.50	69.30	4597.44	358.15	791.68	868.91	868.93	65.66	.88	
4799.00	5.80	70.00	4688.91	361.58	800.92	878.75	878.76	65.70	.77	
4890.00	4.13	64.23	4779.56	364.58	808.19	886.61	886.62	65.72	1.91	
4981.00	3.16	61.38	4870.38	367.21	813.35	892.39	892.40	65.70	1.08	
5073.00	2.50	61.50	4962.26	369.38	817.34	896.91	896.93	65.68	.72	
5164.00	.95	55.01	5053.22	370.76	819.70	899.63	899.65	65.66	1.71	
5256.00	.22	41.69	5145.21	371.33	820.44	900.54	900.56	65.65	.80	
5347.00	.48	210.00	5236.21	371.13	820.37	900.39	900.41	65.66	.77	
5439.00	1.80	190.18	5328.19	369.37	819.92	899.27	899.28	65.75	1.48	
5530.00	2.30	186.40	5419.13	366.15	819.46	897.54	897.54	65.92	.57	
5621.00	1.32	168.34	5510.09	363.31	819.47	896.40	896.40	66.09	1.23	
5713.00	.50	161.80	5602.08	361.89	819.81	896.13	896.13	66.18	.90	
5804.00	.66	152.65	5693.07	361.05	820.17	896.12	896.13	66.24	.20	
5895.00	.50	145.10	5784.07	360.26	820.64	896.22	896.24	66.30	.19	
5986.00	.50	173.50	5875.06	359.54	820.92	896.18	896.20	66.35	.27	
6078.00	.70	182.30	5967.06	358.58	820.94	895.81	895.83	66.40	.24	
6169.00	.62	187.00	6058.05	357.53	820.86	895.31	895.34	66.46	.11	
6260.00	.88	185.30	6149.04	356.35	820.73	894.72	894.75	66.53	.29	
Projection to bit @TD										
6315.00	.88	185.30	6204.04	355.51	820.65	894.30	894.35	66.58	.00	

Job Number: UT141405
 Company: Petroglyph
 Lease/Well: Ute Tribal 07-15K
 Location: Sec. 7, T5S, R3W
 Rig Name: Capstar #334
 State/Country: Utah/USA

Declination: 11.06

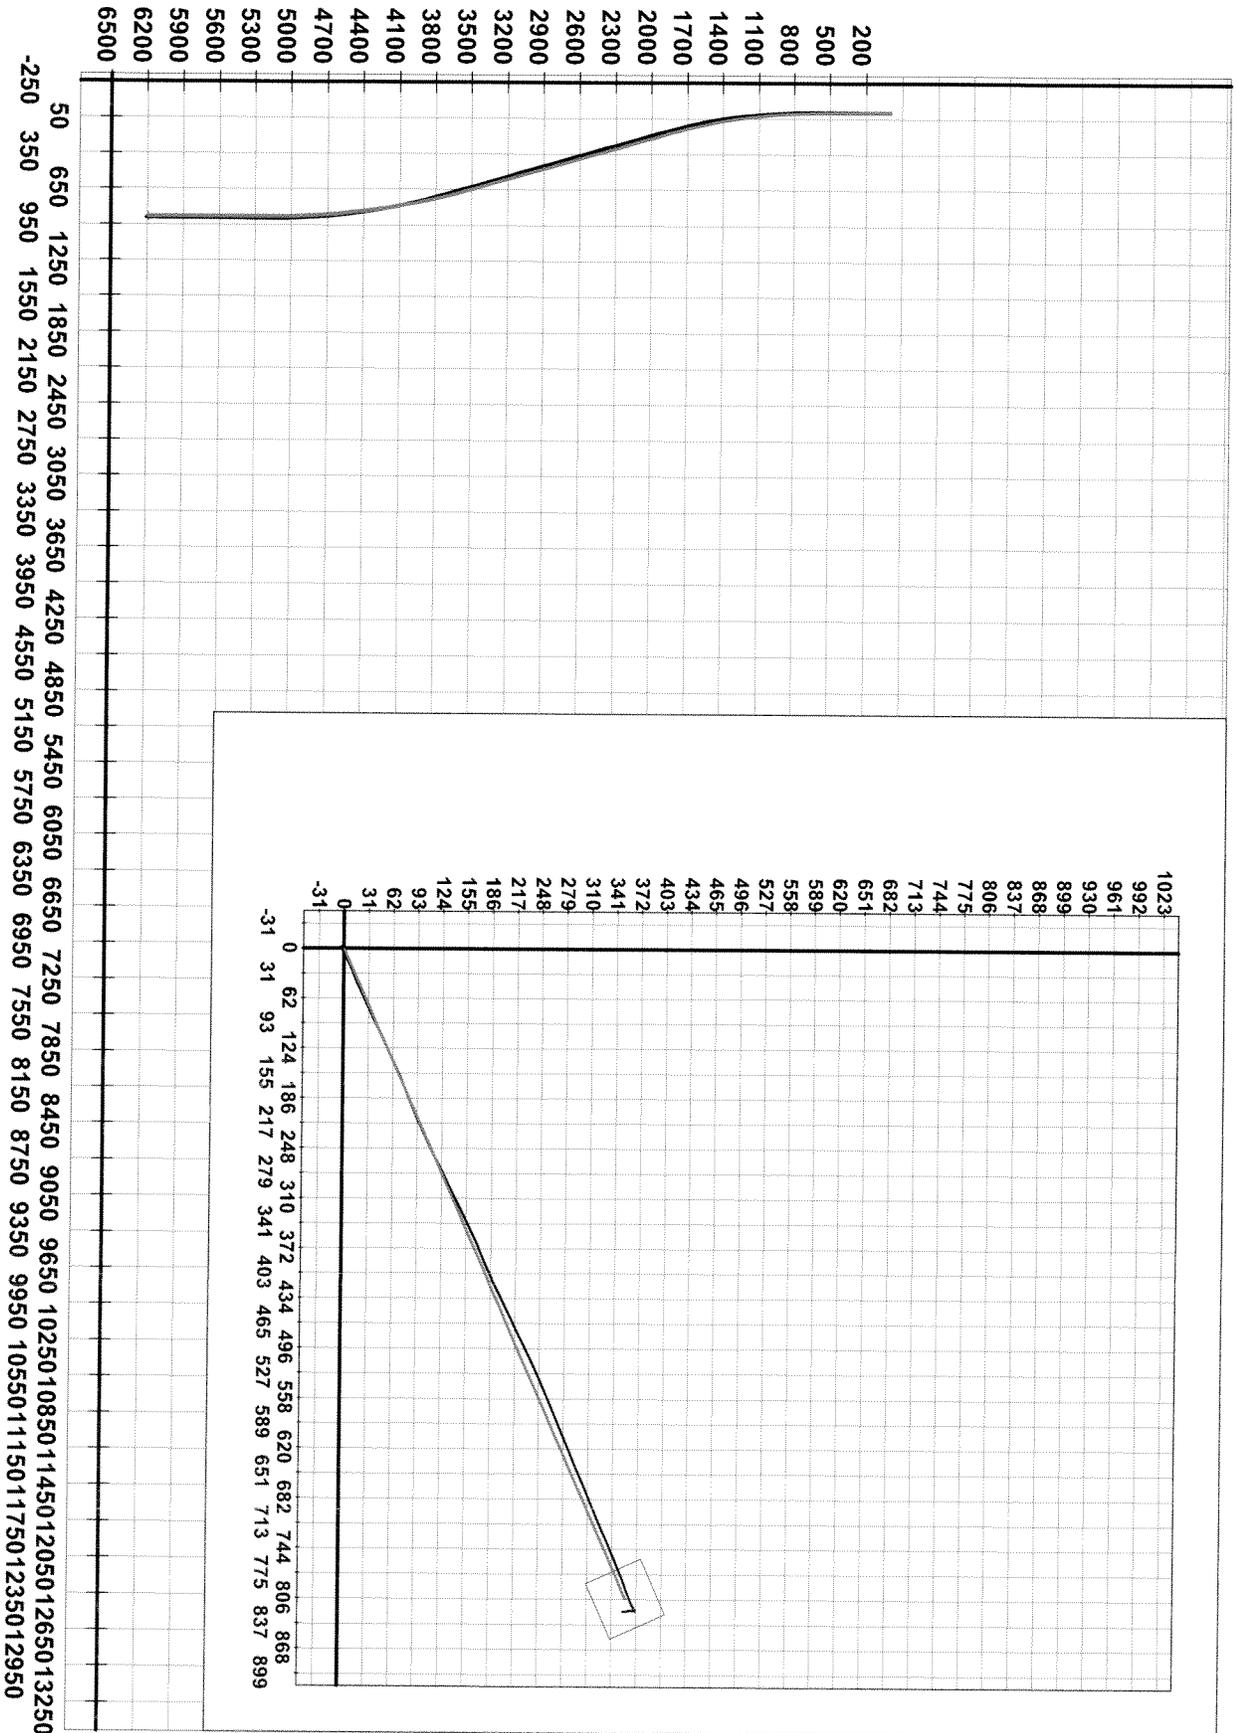

STATE OF UTAH
 DEPARTMENT OF NATURAL RESOURCES
 DIVISION OF OIL, GAS AND MINING

REPORT OF WATER ENCOUNTERED DURING DRILLING

Well name and number: Ute Tribal 07-15K

API number: 4301352211

Well Location: QQ SWSE Section 7 Township 5S Range 3W County Duchesne

Well operator: Petroglyph Operating Company, Inc.

Address: P.O. Box 607

city Roosevelt state UT zip 84066

Phone: (435) 722-2531

Drilling contractor: ProPetro Services

Address: 1422 East 1500 South

city Vernal state UT zip 84078

Phone: (435) 789-1735

Water encountered (attach additional pages as needed):

DEPTH		VOLUME (FLOW RATE OR HEAD)	QUALITY (FRESH OR SALTY)
FROM	TO		
0	520	0	No Water Encountered


Formation tops: 1 _____ 2 _____ 3 _____
 (Top to Bottom) 4 _____ 5 _____ 6 _____
 7 _____ 8 _____ 9 _____
 10 _____ 11 _____ 12 _____

If an analysis has been made of the water encountered, please attach a copy of the report to this form.

I hereby certify that this report is true and complete to the best of my knowledge.

NAME (PLEASE PRINT) Rodrigo Jurado

TITLE Regulatory Compliance Specialist

SIGNATURE 

DATE 1/17/2014
