

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL						1. WELL NAME and NUMBER Ute Tribal 31-01				
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT ANTELOPE CREEK				
4. TYPE OF WELL Oil Well <input type="checkbox"/> Coalbed Methane Well: NO <input type="checkbox"/>						5. UNIT or COMMUNITIZATION AGREEMENT NAME ANTELOPE CREEK				
6. NAME OF OPERATOR PETROGLYPH OPERATING CO						7. OPERATOR PHONE 208 685-7685				
8. ADDRESS OF OPERATOR 960 Broadway Avenue, Ste 500, Boise, ID, 83703						9. OPERATOR E-MAIL ppowell@pgei.com				
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) 1420H623520			11. MINERAL OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input checked="" type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input checked="" type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>				
13. NAME OF SURFACE OWNER (if box 12 = 'fee')						14. SURFACE OWNER PHONE (if box 12 = 'fee')				
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')				
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN') Ute Indian Tribe			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>			19. SLANT VERTICAL <input checked="" type="checkbox"/> DIRECTIONAL <input type="checkbox"/> HORIZONTAL <input type="checkbox"/>				
20. LOCATION OF WELL		FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN		
LOCATION AT SURFACE		826 FNL 690 FEL		NENE	31	5.0 S	3.0 W	U		
Top of Uppermost Producing Zone		826 FNL 690 FEL		NENE	31	5.0 S	3.0 W	U		
At Total Depth		826 FNL 690 FEL		NENE	31	5.0 S	3.0 W	U		
21. COUNTY DUCHESNE			22. DISTANCE TO NEAREST LEASE LINE (Feet) 690			23. NUMBER OF ACRES IN DRILLING UNIT 640				
25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 1290			26. PROPOSED DEPTH MD: 6217 TVD: 6217			29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 43-8342				
27. ELEVATION - GROUND LEVEL 6704			28. BOND NUMBER LPM4138336							
Hole, Casing, and Cement Information										
String	Hole Size	Casing Size	Length	Weight	Grade & Thread	Max Mud Wt.	Cement	Sacks	Yield	Weight
Cond	20	14	0 - 53	5.0	Unknown	10.0	Class G	25	1.17	15.8
Surf	12.25	8.625	0 - 493	24.0	J-55 ST&C	10.0	Class G	226	1.17	15.8
Prod	7.875	5.5	0 - 6217	15.5	J-55 LT&C	10.0	Class G	514	1.74	12.5
							Class G	347	1.46	13.4
ATTACHMENTS										
VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES										
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER					<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN					
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)					<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER					
<input type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)					<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP					
NAME Ed Trotter				TITLE Agent			PHONE 435 789-4120			
SIGNATURE				DATE 10/23/2013			EMAIL edtrotter@easilink.com			
API NUMBER ASSIGNED 43013525980000				APPROVAL  Permit Manager						

CONFIDENTIAL
EIGHT POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 31-01
NE NE, SEC 31, T5S, R3W
DUCHESNE COUNTY, UTAH

1. ESTIMATED TOPS OF IMPORTANT GEOLOGICAL MARKERS:

Formation		Subsea	MD
Rig KB=13' above GGL		6717	0
Surface Formation = Uinta			
Uinta		6704	13
Green River		5259	1458
Trona		3980	2737
Mahogany Shale		3831	2886
"B" Marker	Waterflood Unit Interval	2748	3969
"X" Marker		2270	4447
Douglas Creek Marker		2129	4588
"B" Limestone		1761	4956
Base Castle Peak Limestone		1225	5492
BSCARB		790	5927
Wasatch		533	6184
Formation at TD: Wasatch	RIG TD	500	6217

2. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERAL FORMATIONS:

<u>Substance</u>	<u>Formation</u>	<u>SUBSEA</u>	<u>MD</u>
Base of moderately saline ground water*	Uinta	5500	1217
Oil/Gas	Douglas Creek	2129	4588
Oil/Gas	Castle Peak	1225	5492

Any water encountered during drilling shall be sampled, analyzed and reported to the BLM Vernal office using State of Utah DOGM Form 7 *Report of Water Encountered during Drilling*. The following analyses shall be performed on any water encountered:

Flow rate (or blowtest)	Temperature	pH	TDS
Dissolved Iron	Dissolved Magnesium	Dissolved Bicarb.	Dissolved Sulfate
Dissolved Calcium	Dissolved Sodium	Dissolved Carbonate	Dissolved Chloride

All depths through the "Base of moderately saline ground water"*, along with any water encountered below that depth which is less than 10,000 TDS, shall be protected by the surface casing or by lifting the cement of the production casing into the surface casing.

*Base of Moderately Saline Groundwater from Howells, Longson and Hunt, 1981, Utah State Technical Publication 92: The Base of the Moderately Saline Water in the Uinta Basin, Utah



CONFIDENTIAL
EIGHT POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 31-01
NE NE, SEC 31, T5S, R3W
DUCHESNE COUNTY, UTAH

3. PROPOSED CASING PROGRAM:

String	Hole	Casing	Top - MD	Bottom - MD	Weight lb/ft	Grade	Thread
Conductor	20"	14"	surface	53'	steel	Cond'r	none
Surface	12-1/4"	8-5/8"	surface	493'	24	J-55	STC
Production	7-7/8"	5-1/2"	surface	6217'	15.5	J-55	LTC

String	Hole	Casing	Collapse	Burst	Tensile
Surface	12-1/4"	8-5/8"	1,370 psi	2,950 psi	244,000 lb
Production	7-7/8"	5-1/2"	4,040 psi	4,810 psi	248,000 lb

- All casing will be new or inspected.
- The surface and production strings shall have a minimum of one (1) centralizer on each of the bottom three (3) joints.
- The production string shall have a minimum of one (1) centralizer for every three (3) joints from TD to the top of the "B" marker at 3969' MD.

4. PROPOSED CEMENTING PROGRAM:

String	Top	Cement Description	Sacks	Excess	Weight (ppg)	Yield (ft ³ /sk)
	Bottom		Vol (ft ³)			
Conductor	0 53	Construction Grade Cement	Sufficient volumes to grout Conductor			
Surface	0 493	Class G +2% CaCl ₂ +0.25 lb/sk Cello Flake	226 264	30%	15.8	1.17
Production Lead	0 3969	EXPANDACEM (Class G +additives) + 1 lb/sk Granulite TR ¹ / ₄ (LCM)	514 894	30%	12.5	1.74
Production Tail	3969 6217	EXPANDACEM (Class G +additives) + 1 lb/sk Granulite TR ¹ / ₄ (LCM)	347 506	30%	13.5	1.46

- The 8-5/8" surface casing shall be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.
- The 5-1/2" production casing shall be cemented back to surface. In the event that during the primary cementing operation the cement does not circulate to surface, a remedial cementing operation shall be performed only if necessary to lift cement above the Surface Casing Shoe at 493' MD.

CONFIDENTIAL
EIGHT POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 31-01
NE NE, SEC 31, T5S, R3W
DUCHESNE COUNTY, UTAH

5. MINIMUM PRESSURE CONTROL AND SAFETY EQUIPMENT:

- An 8", 2000 PSI, Double Ram BOPE with Hydraulic Closing Unit shall be used.
- A 2000 PSI Working Pressure Annular shall be used.
- The flowline shall have a minimum diameter of 10".
- Auxiliary equipment shall be a Kelly Cock, Bit Float, and a TIW valve with drill pipe threads.
- Spark arrestors shall be equipped on all engine exhausts within 100 feet of the wellbore.
- See attached 2,000 psi BOP schematic diagram.

BOPE TESTING PROCEDURE:

- The BOPE shall be tested by a professional tester to conform to the standards of Onshore Order #2.

6. MUD PROGRAM:

A. SURFACE HOLE

- The surface hole will be drilled with an air/mist system from 0' to 493'. All cuttings shall be directed to pit.
- A trailer-mounted compressor with a capacity of 2000 CFM will be used. Compressor will have a safety shut-off valve located less than 15 feet from the driller's controls of the rig.
- The rat and mouse holes will be drilled with the air rig after surface casing is cemented.
- The 140 barrel water truck used with the deduster will be the source of kill fluid in the highly unlikely event of pressure being encountered during drilling of the surface hole.
- Operator requests the following variances from Onshore Order 2 part E during drilling of the surface hole. Operator will use air drilling techniques only on surface hole:
 - Operator requests a variance to regulations requiring the blooie line discharge to be 100' from the wellbore. Due to reduced location size, the blooie line discharge will be approximately 75' from the wellbore and securely anchored.
 - Operator requests a variance to regulations requiring an automatic igniter or continuous pilot light on the blooie line. A mister shall be on the end of the blooie line.
 - Operator requests a variance to regulations requiring compressors be located in the opposite direction from the blooie line; a minimum of 100' from the wellbore. Due to the reduced location size, the compressors shall be located as close as is reasonable to the opposite direction from the blooie line and 75' from the wellbore.
 - Operator requests a variance to regulations requiring a BOPE on the hole when drilling the surface hole. An air bowl shall be utilized on the diverter system in place of a BOPE.

CONFIDENTIAL
EIGHT POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 31-01
NE NE, SEC 31, T5S, R3W
DUCHESNE COUNTY, UTAH

B. PRODUCTION HOLE

- The production hole shall be drilled with a freshwater polymer system from 493' to 6217'. LSND mud if conditions warrant.
- Clay inhibition and hole stability shall be achieved with a Diammonium Phosphate (DAP) additive or similar source of clay-stabilizing ions. Anticipated mud weight is 8.3-8.4 lbs/gal.
- All cuttings and circulating medium shall be directed into the reserve pit. Total Dissolved Solids (TDS) are anticipated to be less than 3000 PPM.
- Sufficient mud inventory will be maintained on location in either tanks or the reserve pit during the drilling of the production hole to handle any adverse conditions that may arise.
- If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite. Enough material shall be maintained on location to allow for the mudweight to be raised to 10.5 lbs/gal should need arise.
- During drilling operations, pit levels and flow from the well shall be monitored by instrumentation to include at least: a pit volume totalizer (PVT), a stroke counter, and a mud-flow indicator.
- A mud-gas separator shall be available on location. Operator does not plan on using a gas detector on the mud return due to the fact that any abnormal pressure is the result of offset water injection.

C. HAZARDOUS MATERIALS AND POLLUTANTS

- Chromate additives **shall NOT** be used in the mud system on Indian lands without prior BLM approval to ensure adequate protection of freshwater aquifers.
- Chemicals subject to reporting under SARA Title III in an amounts equal to or greater than 10,000 pounds annually **shall NOT** be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completion of this well.
- Extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities **shall NOT** be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completion of this well.
- Hazardous substances specifically listed by the EPA as a hazardous waste, as defined in 40 CFR 261 (D), or any substances that through their use would lead to the generation of a hazardous waste, **shall NOT** be used in association with the drilling, testing, or completion of this well.



CONFIDENTIAL
EIGHT POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 31-01
NE NE, SEC 31, T5S, R3W
DUCHESNE COUNTY, UTAH

7. EVALUATION PROGRAM:


Logs:	Triple Combo	TD to base of surface casing (AIT, DSN, CDL) Base of surface casing to surface (GR only)
Cores:	None planned	
DST:	None planned	
Testing:	Operator plans no testing until the completion phase of the well.	

8. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:


- Operator anticipates Bottom Hole Temperatures below 150°F, the maximum temperature for DAP drilling fluids.
- No H₂S has been encountered or is known to exist from previous drilling in the area at this depth.
- Maximum pressure for hydrocarbon bearing zones at native conditions in this area is approximately 1554 PSI (0.25 PSI/ft gradient).
- This well is in the vicinity of active injection wells. Nearby active injection can cause pressures up to a 0.433 PSI/ft gradient (2692 PSI).


CONFIDENTIAL
EIGHT POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 31-01
NE NE, SEC 31, T5S, R3W
DUCHESNE COUNTY, UTAH


TYPICAL 2,000 p.s.i. BLOWOUT PREVENTER

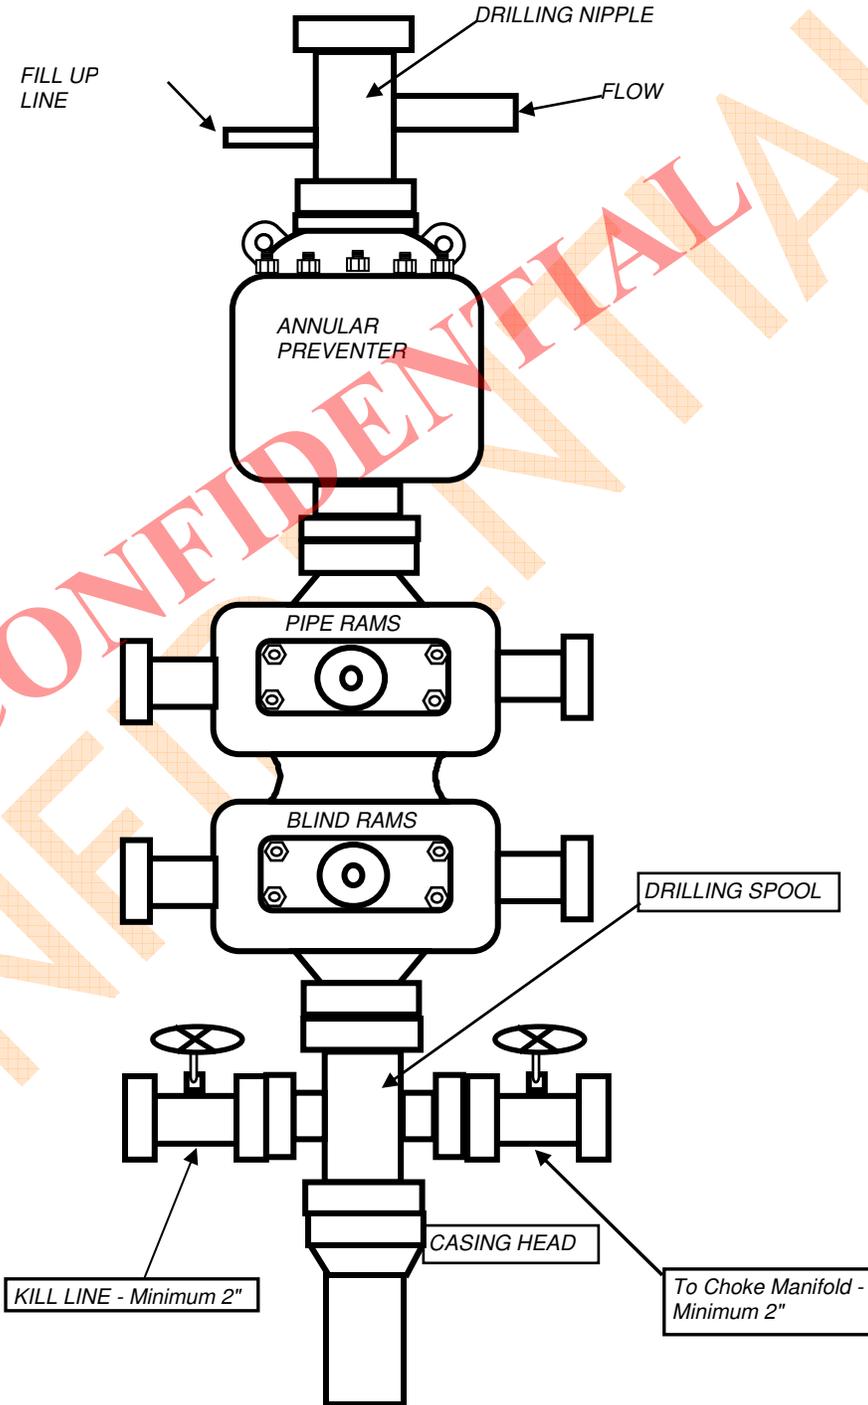

CONFIDENTIAL
EIGHT POINT DRILLING PLAN
PETROGLYPH OPERATING COMPANY, INC
UTE TRIBAL 31-01
NE NE, SEC 31, T5S, R3W
DUCHESNE COUNTY, UTAH
TYPICAL 2,000 p.s.i. CHOKE MANIFOLD

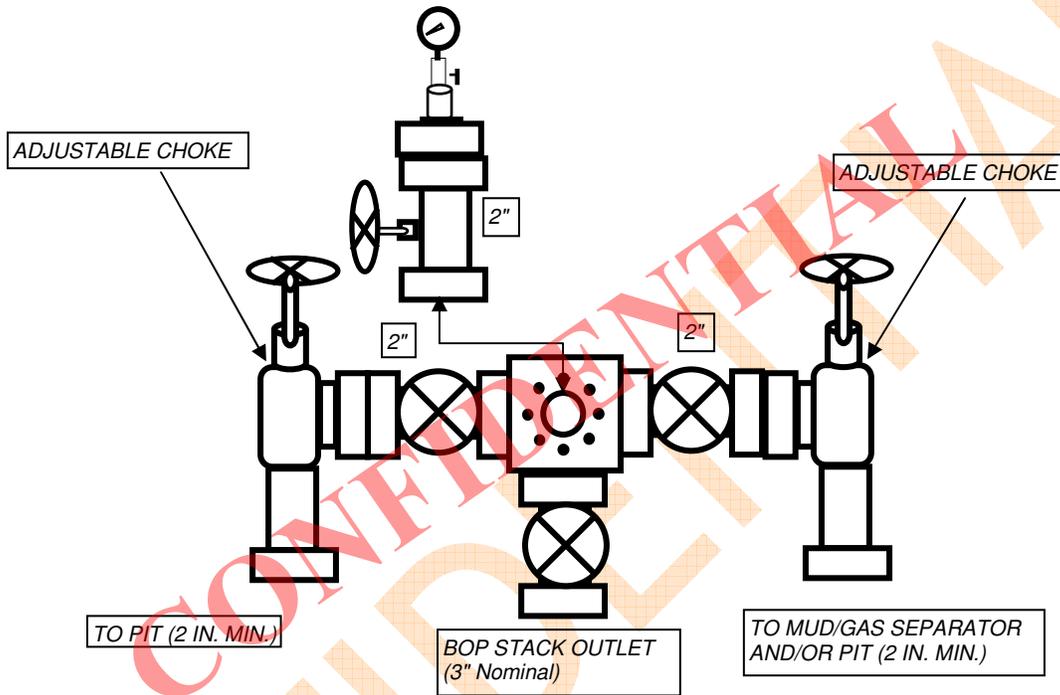

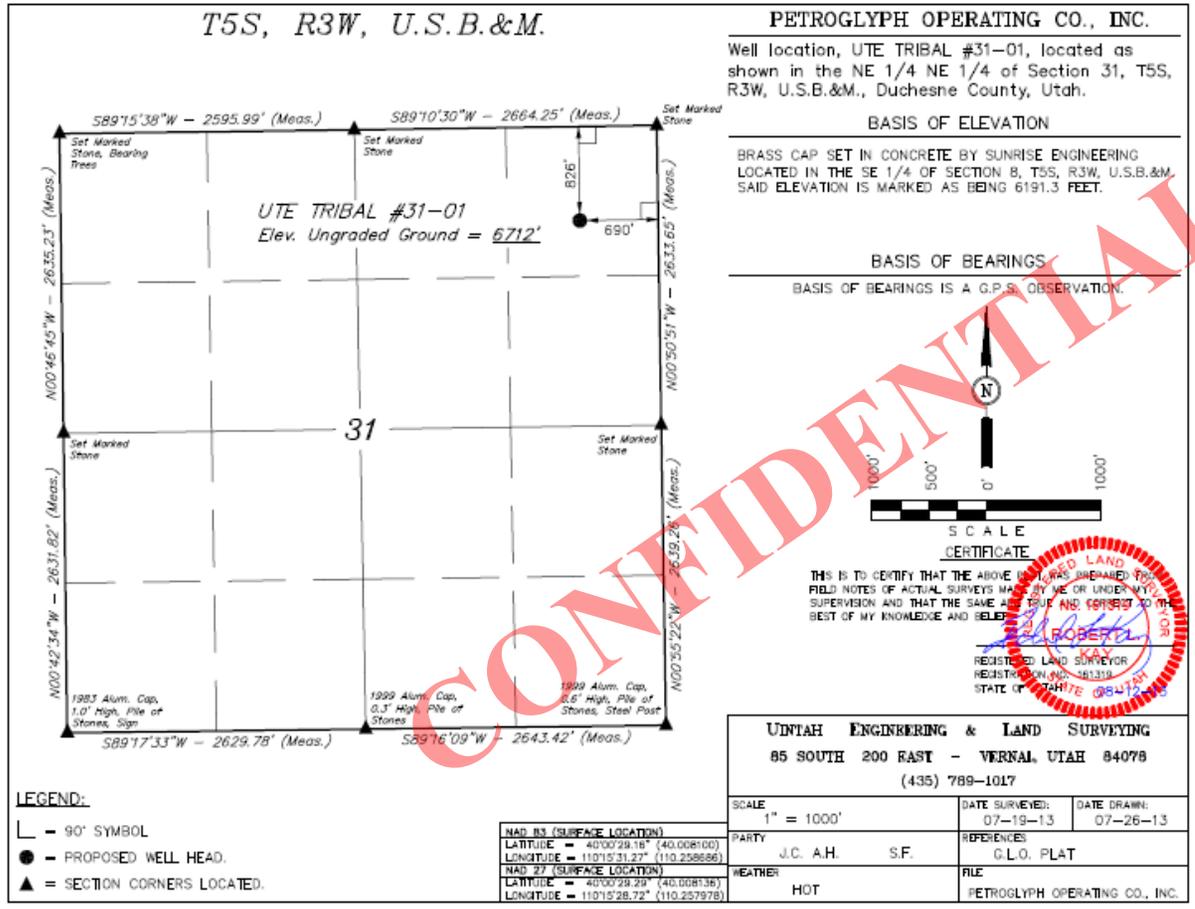

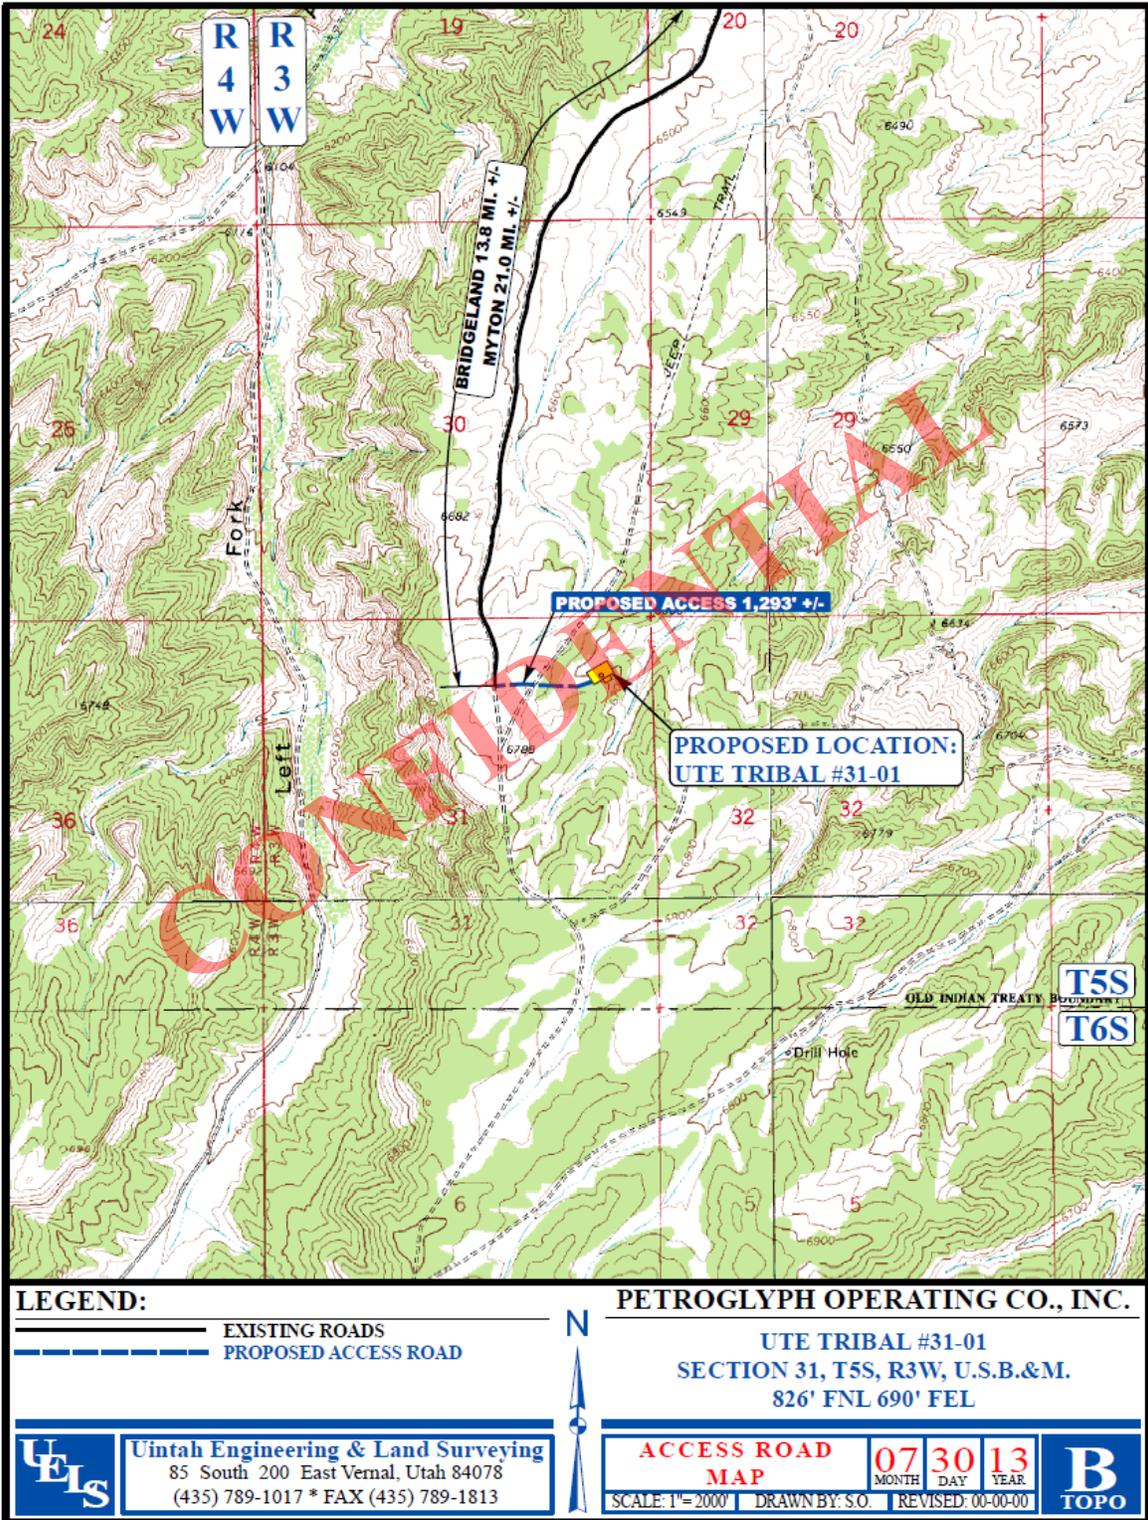

LEGEND:

-  EXISTING ROADS
-  PROPOSED ACCESS ROAD



PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #31-01
SECTION 31, T5S, R3W, U.S.B.&M.
826' FNL 690' FEL



Utah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813

ACCESS ROAD	MAP	07	30	13	B
		MONTH			
SCALE: 1"=2000'		DRAWN BY: S.O.		REVISED: 00-00-00	

Certification


I hereby certify that I, or persons under my direct supervision, have inspected the proposed drillsite and access route; that I am familiar with the conditions that presently exist; that the statements made in the Plan are, to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed by Petroglyph Operating Co., Inc. and its contractors and subcontractors in conformity with this Plan and the terms and conditions under which it is approved.

Please be advised that Petroglyph Operating Co., Inc. is considered to be the operator of the **UTE TRIBAL 31-01 Well, located in the NE/NE of Section 31, T5S, R3W, Duchesne County, Utah; Lease #14-20-H62-3520**; and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond Coverage is provided under Bond #LPM4138335.

Date

Ed Trotter, as Agent for
Petroglyph Operating Co., Inc.

CONFIDENTIAL

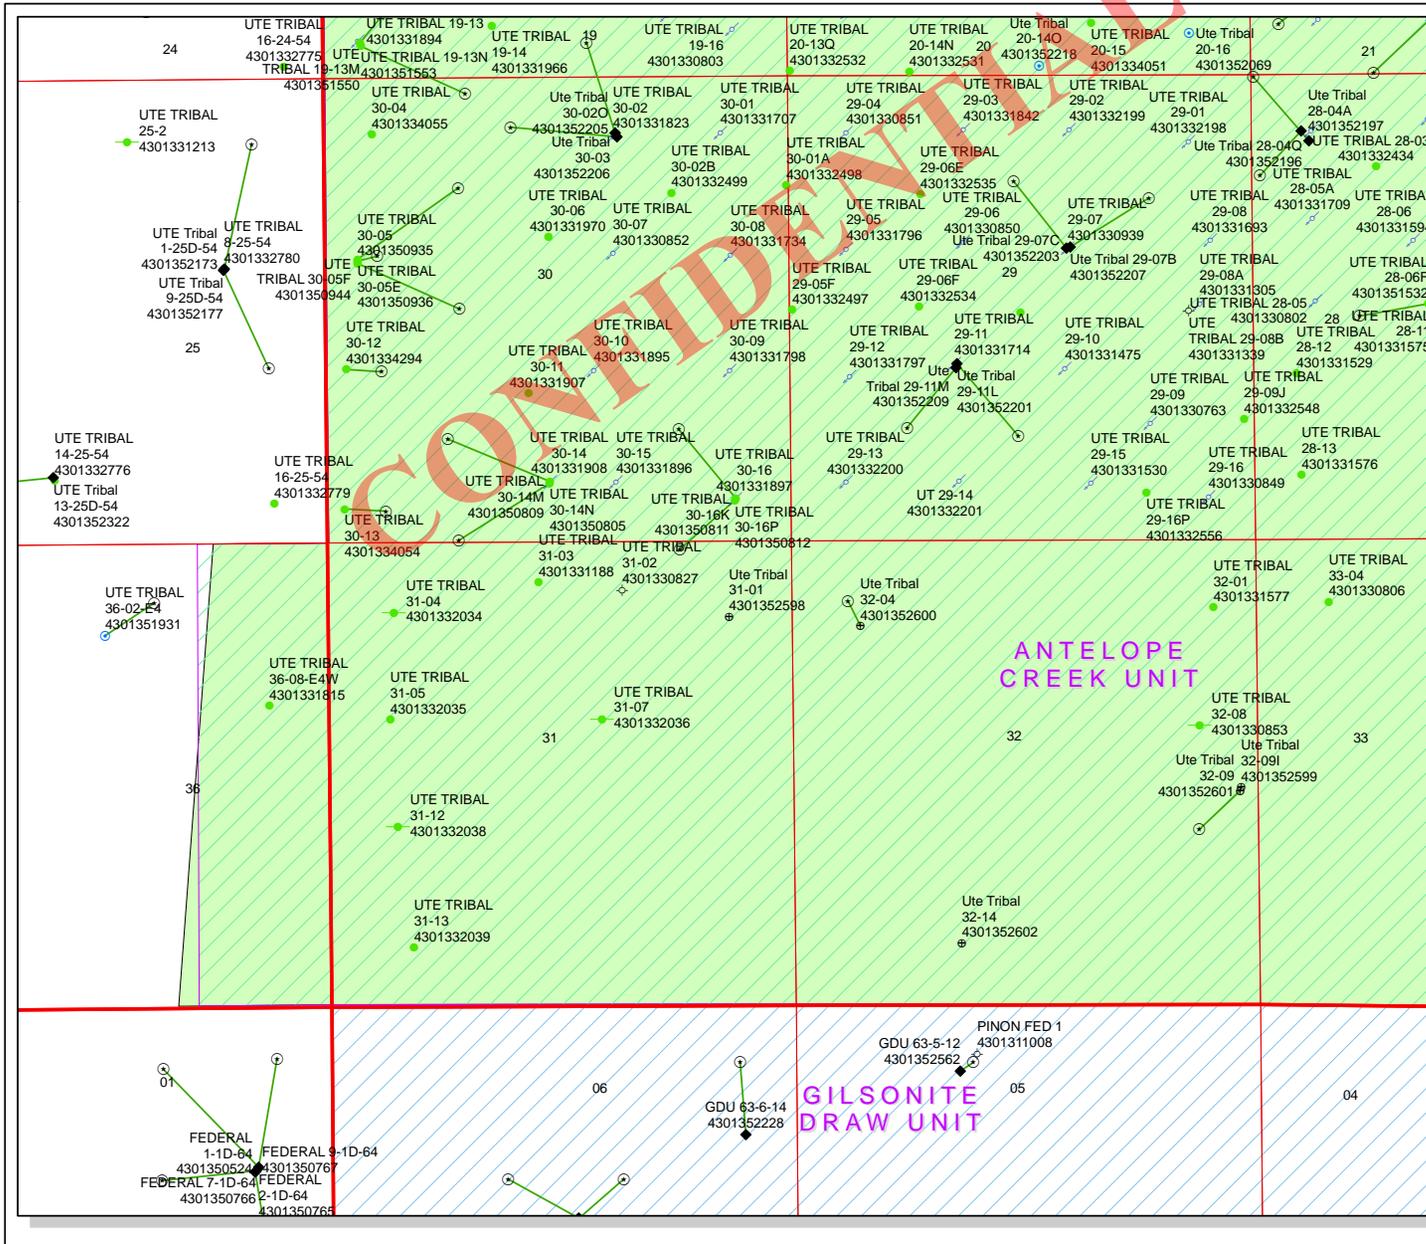

API Number: 4301352598



Well Name: Ute Tribal 31-01

Township: T05.0S Range: R03.0W Section: 31 Meridian: U

Operator: PETROGLYPH OPERATING CO

Map Prepared: 10/30/2013
Map Produced by Diana Mason

Wells Query Status	Units STATUS
APD - Approved Permit	ACTIVE
DRL - Spudded (Drilling Commenced)	EXPLORATORY
GIW - Gas Injection	GAS STORAGE
GS - Gas Storage	NF PP OIL
LOC - New Location	NF SECONDARY
OPS - Operation Suspended	PI OIL
PA - Plugged Abandoned	PP GAS
PGW - Producing Gas Well	PP GEOTHERML
POW - Producing Oil Well	PP OIL
SGW - Shut-in Gas Well	SECONDARY
SOW - Shut-in Oil Well	TERMINATED
TA - Temp. Abandoned	
TW - Test Well	
WDW - Water Disposal	
WW - Water Injection Well	
WSW - Water Supply Well	

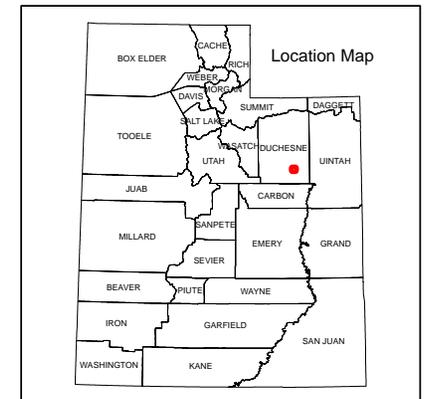

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 10/23/2013

API NO. ASSIGNED: 43013525980000

WELL NAME: Ute Tribal 31-01

OPERATOR: PETROGLYPH OPERATING CO (N3800)

PHONE NUMBER: 435 789-4120

CONTACT: Ed Trotter

PROPOSED LOCATION: NENE 31 050S 030W

Permit Tech Review:

SURFACE: 0826 FNL 0690 FEL

Engineering Review:

BOTTOM: 0826 FNL 0690 FEL

Geology Review:

COUNTY: DUCHESNE

LATITUDE: 40.00802

LONGITUDE: -110.25875

UTM SURF EASTINGS: 563266.00

NORTHINGS: 4428910.00

FIELD NAME: ANTELOPE CREEK

LEASE TYPE: 2 - Indian

LEASE NUMBER: 1420H623520

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 2 - Indian

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: INDIAN - LPM4138336
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 43-8342
- RDCC Review:
- Fee Surface Agreement
- Intent to Commingle

Commingling Approved

LOCATION AND SITING:

- R649-2-3.
- Unit: ANTELOPE CREEK
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
- Board Cause No: Cause 214-2
- Effective Date: 6/9/2000
- Siting: Suspends General Siting
- R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason



GARY R. HERBERT
Governor

SPENCER J. COX
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Ute Tribal 31-01
API Well Number: 43013525980000
Lease Number: 1420H623520
Surface Owner: INDIAN
Approval Date: 11/5/2013

Issued to:

PETROGLYPH OPERATING CO, 960 Broadway Avenue, Ste 500, Boise, ID 83703

Authority:

Pursuant to Utah Code Ann. 40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 214-2. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well - contact Carol Daniels at 801-538-5284

(please leave a voicemail message if not available)

OR

submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website

at <http://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) - due within 5 days of spudding the well
- Monthly Status Report (Form 9) - due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) - due prior to implementation
- Written Notice of Emergency Changes (Form 9) - due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) - due prior to implementation
- Report of Water Encountered (Form 7) - due within 30 days after completion
- Well Completion Report (Form 8) - due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "John Rogers", written in a cursive style.

For John Rogers
Associate Director, Oil & Gas

RECEIVED

FORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

OCT 25 2013

APPLICATION FOR PERMIT TO DRILL OR REENTER

BLM

5. Lease Serial No.
1420H623520

6. If Indian, Allottee or Tribe Name

7. If Unit or CA Agreement, Name and No.
1420H624650

8. Lease Name and Well No.
UTE TRIBAL 31-01

9. API Well No.
43 D13 52598

10. Field and Pool, or Exploratory
ANTELOPE CREEK

1a. Type of Work: DRILL REENTER

CONFIDENTIAL

1b. Type of Well: Oil Well Gas Well Other Single Zone Multiple Zone

2. Name of Operator
PETROGLYPH OPERATING CO., INC. Contact: ED H TROTTER
Call: edtrotter@easilink.com

3a. Address
P.O. BOX 607
ROOSEVELT, UT 84066

3b. Phone No. (include area code)
Ph: 435-789-4120
Fx: 435-789-1420

4. Location of Well (Report location clearly and in accordance with any State requirements. *)

At surface NENE 826FNL 690FEL

At proposed prod. zone NENE 826FNL 690FEL

11. Sec., T., R., M., or Blk. and Survey or Area

Sec 31 T5S R3W Mer UBM

14. Distance in miles and direction from nearest town or post office*
21.24 MILES SOUTHWEST OF MYTON, UTAH

12. County or Parish
DUCHESNE

13. State
UT

15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any)
690

16. No. of Acres in Lease
640.00

17. Spacing Unit dedicated to this well

18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft.
1290

19. Proposed Depth
6217 MD
6217 TVD

20. BLM/BIA Bond No. on file

LPM4138335

21. Elevations (Show whether DF, KB, RT, GL, etc.)
6704 GL

22. Approximate date work will start
12/15/2013

23. Estimated duration
45 DAYS

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- 1. Well plat certified by a registered surveyor.
- 2. A Drilling Plan.
- 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- 5. Operator certification
- 6. Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature (Electronic Submission) Name (Printed/Typed) LESTER FARNSWORTH Ph: 435-722-2531 Date 10/23/2013

Title DISTRICT MANAGER

Approved by (Signature) Name (Printed/Typed) Jerry Kenczka Date APR 30 2014

Title Assistant Field Manager Lands & Mineral Resources Office VERNAL FIELD OFFICE

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

Electronic Submission #224251 verified by the BLM Well Information System
For PETROGLYPH OPERATING CO., INC., sent to the Vernal
Committed to AFMSS for processing by LESLIE BUHLER on 10/31/2013 ()

**NOTICE OF APPROVAL
CONDITIONS OF APPROVAL ATTACHED**

**** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ****

RECEIVED
MAY 12 2014
DIV. OF OIL, GAS & MINING

UDOGM



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Petroglyph Operating Co., Inc.
Well No: Ute Tribal 31-01
API No: 43-013-52598

Location: NENE, Sec. 31, T5S, R3W
Lease No: 14-20-H62-3520
Agreement: Antelope Creek Enhanced

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings to: blm_ut_vn_opreport@blm.gov
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

CONDITIONS OF APPROVAL:

- During the breeding season (February 1- August 31), a site specific survey for active or inactive nests within 0.5-miles of the project area will be completed prior to any ground disturbing activities and the report will be sent to BIA
- If no active or inactive nests are found within the 0.5 miles of the project area Petroglyph May proceed with construction;
- Should an active or inactive nest be found within the project area, Petroglyph will contact the BIA to determine appropriate mitigation measures including the need for a raptor time extension waiver, and will not begin construction until appropriate plan of actions is decided upon by the BIA and Petroglyph; and
- Should a raptor timing extension waiver be required, the BIA will work with the US Fish and Wildlife Service to determine appropriate mitigation measure which may include, but are not limited to the establishment of species-specific spatial buffers and weekly monitoring of inactive nests during construction.
- All areas of disturbance (including surface pipelines) must have appropriate surface use agreements or approvals in place with the proper owner and/or agency before such action is started.
- The conditions of approval, as set forth by those owners and/or agencies, shall be adhered to.

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Gamma Ray Log shall be run from Total Depth to Surface.
- CBL will be run from TD to TOC.
- Cement for the surface casing will be circulated to the surface.
- Cement for long-string shall be circulated 200' above surface casing shoe.

Variance Granted:

Variance for Air-drilling is granted per APD.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**

- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.
- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to BLM_UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs,

core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: 1420H623520
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: UTE
		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
1. TYPE OF WELL Oil Well		8. WELL NAME and NUMBER: Ute Tribal 31-01
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO		9. API NUMBER: 43013525980000
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703		9. FIELD and POOL or WILDCAT: ANTELOPE CREEK
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0826 FNL 0690 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENE Section: 31 Township: 05.0S Range: 03.0W Meridian: U		COUNTY: DUCHESNE
		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input checked="" type="checkbox"/> SPUD REPORT Date of Spud: 8/16/2014	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> CHANGE TUBING	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER	
	OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.		
This well was spud on 8/16/2014 at approximately 10:00 A.M. Using a Bucket Rig provided by Craig's Roustabout Service, Vernal Utah, we set 60' of 16" Conductor. For additional information please contact our staff at 435-722-2531.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY August 18, 2014		
NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 8/18/2014	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: 1420H623520
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: UTE
1. TYPE OF WELL Oil Well		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO		8. WELL NAME and NUMBER: Ute Tribal 31-01
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703		9. API NUMBER: 43013525980000
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0826 FNL 0690 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENE Section: 31 Township: 05.0S Range: 03.0W Meridian: U		9. FIELD and POOL or WILDCAT: ANTELOPE CREEK
		COUNTY: DUCHESNE
		STATE: UTAH

11.

CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input checked="" type="checkbox"/> SPUD REPORT Date of Spud: 8/15/2014	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Please disregard the previously submitted spud notice. This well was spud on 8/15/2014 at approximately 10:00 A.M. Using a Bucket Rig provided by Craig's Roustabout Service, Vernal Utah, we set 60' of 16" Conductor. For additional information please contact our staff at 435-722-2531. The previous spud notice reported the wrong spud date.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
August 18, 2014**

NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 8/18/2014	

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 6

ENTITY ACTION FORM

Operator: Petroglyph Operating Company Operator Account Number: N 3800
Address: P.O. Box 607
city Roosevelt
state UT zip 84066 Phone Number: (435) 722-2531

Well 1

API Number	Well Name		QQ	Sec	Twp	Rng	County
4301352598	Ute Tribal 31-01		NENE	31	5S	3W	Duchesne
Action Code	Current Entity Number	New Entity Number	Spud Date			Entity Assignment Effective Date	
B	99999	12216	8/15/2014			8/21/14	
Comments: Please add well to exiting Ute Tribal 30-15 Tank Battery. <i>GRRV</i> CONFIDENTIAL							

Well 2

API Number	Well Name		QQ	Sec	Twp	Rng	County
4301352629	Ute Tribal 31-06		SWNE	31	5S	3W	Duchesne
Action Code	Current Entity Number	New Entity Number	Spud Date			Entity Assignment Effective Date	
B	99999	12216	8/19/2014			8/21/14	
Comments: Please add well to existing Ute Tribal 30-15 Tank Battery. <i>GRRV</i> CONFIDENTIAL							

Well 3

API Number	Well Name		QQ	Sec	Twp	Rng	County
4301352624	Ute Tribal 29-13Q		SWSW	29	5S	3W	Duchesne
Action Code	Current Entity Number	New Entity Number	Spud Date			Entity Assignment Effective Date	
B	99999	12216	8/20/2014			8/21/14	
Comments: Please add well to existing Ute Tribal 30-15 Tank Battery. <i>GRRV</i> CONFIDENTIAL							

ACTION CODES:

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (Explain in 'comments' section)

RECEIVED

AUG 21 2014

Rodrigo Jurado

Name (Please Print)

[Signature]
Signature

Regulatory Compliance Spc. 8/20/2014

Title Date

CONFIDENTIAL

BLM - Vernal Field Office - Notification Form

Operator Petroglyph Operating Rig Name/# Craig's /Pro Petro
Submitted By Rodrigo Jurado Phone Number 435-722-5302
Well Name/Number Ute Tribal 31-01
Qtr/Qtr NE/NE Section 31 Township 5S Range 3W
Lease Serial Number 14-20-H62-3520
API Number 43-013-52598

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time _____ AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 8/19/2014 7:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks We plan to run +/- 500' of 8-5/8" J-55 Surface Casing at the time indicated. (Sent 8/18/2014 @ 11:00 P.M.)

BLM - Vernal Field Office - Notification Form

Operator Petroglyph Operating Co. Rig Name/# Capstar #334
 Submitted By Geno Rowland Phone Number 970-361-3271
 Well Name/Number Ute Tribal 31-01
 Qtr/Qtr NE/NE Section 31 Township 5S Range 3W
 Lease Serial Number 14-20-H62-3520
 API Number 43-013-52598

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time _____ AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 09/02/2014 19:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks Intensions are to run a 5-1/2" Prod. Casing String to a shoe depth of 6200' MD (KB).

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5.LEASE DESIGNATION AND SERIAL NUMBER: 1420H623520
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: UTE 7.UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: Ute Tribal 31-01
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO	9. API NUMBER: 43013525980000
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703	PHONE NUMBER: 208 685-7685 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0826 FNL 0690 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENE Section: 31 Township: 05.0S Range: 03.0W Meridian: U	9. FIELD and POOL or WILDCAT: ANTELOPE CREEK COUNTY: DUCHESNE STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 10/5/2014 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input checked="" type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Please see attached.

**Accepted by the
Utah Division of
Oil, Gas and Mining**

Date: ~~September 29, 2014~~

By: *Dark Duff*

NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 9/29/2014	

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 9

SUNDRY NOTICES AND REPORTS ON WELLS			5. LEASE DESIGNATION AND SERIAL NUMBER: 1420H623520
Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.			6. IF INDIAN, ALLOTTEE OR TRIBE NAME: Ute Indian Tribe
1. TYPE OF WELL OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER _____			7. UNIT or CA AGREEMENT NAME: 1420H624650
2. NAME OF OPERATOR: Petroglyph Operating Company Inc.			8. WELL NAME and NUMBER: Ute Tribal 31-01
3. ADDRESS OF OPERATOR: P.O. Box 607 CITY Roosevelt STATE UT ZIP 84066		PHONE NUMBER: (435) 722-2531	9. API NUMBER: 4301352598
4. LOCATION OF WELL FOOTAGES AT SURFACE: 826' FNL, 690' FEL COUNTY: Duchesne QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: NENE 31 5S 3W U STATE: UTAH			10. FIELD AND POOL, OR WILDCAT: Antelope Creek

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA			
TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will start: <u>10/5/2014</u> <input type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of work completion: _____	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> DEEPEN <input checked="" type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> PLUG BACK <input type="checkbox"/> PRODUCTION (START/RESUME) <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	<input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> TEMPORARILY ABANDON <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> WATER SHUT-OFF <input type="checkbox"/> OTHER: _____

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On or around 10/5/2014, depending on equipment availability, Petroglyph Operating intends to perforate and fracture treat the following: 4287-90, 4295-4300, 4361-69, 4374-77, 4384-88, 4393-95, 4488-4510, 4514-16, 4652-70, 4871-76, 4980-86, 4990-97, 5036-42, 5192-97, 5205-08, 5217-19, 5230-32, 5235-37, 5243-46, 5261-66, 5272-76, 5303-09, 5405-10, 5420-22, 5430-33, 5456-62, 5528-40, 5550-54, 5657-59, 5686-94, 5718-21, 5740-49 & 5761-64. We will perforate at 4 shot per foot and isolate zones using Halliburton 8K Composite Plugs. We plan complete the following stages:

- 5,657-5,764: 33,600 Gals of fluid containing 60,000#'s of sand,
- 5,405-5,554: 28,000 Gals of fluid containing 50,000#'s of sand,
- 5,192-5,309: 33,600 Gals of fluid containing 60,000#'s of sand,
- 5,036-5,042: 5,600 Gals of fluid containing 10,000#'s of sand,
- 4,871-4,997: 30,800 Gals of fluid containing 55,000#'s of sand,
- 4,652-4,670: 25,200 Gals of fluid containing 45,000#'s of sand,
- 4,488-4,516: 33,600 Gals of fluid containing 60,000#'s of sand,
- 4,361-4,395: 22,400 Gals of fluid containing 40,000#'s of sand,
- 4,287-4,300: 16,800 Gals of fluid containing 30,000#'s of sand.

This plan is tentative and will be adjusted as needed during completion operations. Volumes and amounts of sand are only estimates, actual figures will be reported at a later date. All plugs will be drilled out and the well swabbed if necessary.

NAME (PLEASE PRINT) <u>Rodrigo Jurado</u>	TITLE <u>Regulatory Compliance Specialist</u>
SIGNATURE	DATE <u>9/29/2014</u>

(This space for State use only)

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS		5. LEASE DESIGNATION AND SERIAL NUMBER: 1420H623520
Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: UTE
1. TYPE OF WELL Oil Well		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO		8. WELL NAME and NUMBER: Ute Tribal 31-01
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703		9. API NUMBER: 43013525980000
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0826 FNL 0690 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENE Section: 31 Township: 05.0S Range: 03.0W Meridian: U		9. FIELD and POOL or WILDCAT: ANTELOPE CREEK
		COUNTY: DUCHESNE
		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 10/19/2014	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE TUBING	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. The date of first production for this well was 10-19-2014.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY February 04, 2015		
NAME (PLEASE PRINT)	PHONE NUMBER	TITLE
Rodrigo Jurado	435 722-5302	Regulatory & Compliance Spc
SIGNATURE		DATE
N/A		10/21/2014

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9	
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: 1420H623520	
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: UTE	
1. TYPE OF WELL Oil Well		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK	
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO		8. WELL NAME and NUMBER: Ute Tribal 31-01	
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500 , Boise, ID, 83703		9. API NUMBER: 43013525980000	
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0826 FNL 0690 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENE Section: 31 Township: 05.0S Range: 03.0W Meridian: U		9. FIELD and POOL or WILDCAT: ANTELOPE CREEK	
		COUNTY: DUCHESNE	
		STATE: UTAH	
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA			
TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: <input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 10/20/2014 <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input checked="" type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. Please see attached.			
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY February 23, 2015			
NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc	
SIGNATURE N/A	DATE 2/18/2015		

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 9

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

			5. LEASE DESIGNATION AND SERIAL NUMBER 14-20-H62-3520
			6. IF INDIAN, ALLOTTEE OR TRIBE NAME Ute Indian Tribe
			7. UNIT or CA AGREEMENT NAME: 14-20-H62-4650
1. TYPE OF WELL OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER _____			8. WELL NAME and NUMBER: Ute Tribal 31-01
2. NAME OF OPERATOR: Petroglyph Operating Company Inc.			9. API NUMBER: 4301352598
3. ADDRESS OF OPERATOR: P.O. Box 607		CITY Roosevelt STATE UT ZIP 84066	10. FIELD AND POOL, OR WILDCAT: Antelope Creek
4. LOCATION OF WELL FOOTAGES AT SURFACE: 826' FNL, 690' FEL			COUNTY: Duchesne
QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN NENE 31 5S 3W U			STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will start: _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input checked="" type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLARE
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of work completion: 10/20/2014	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/RESUME)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: _____
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On 9/19/2014 Petroglyph Operating ran GR/CBL and found ETOC @ 65'. On 10/7/2014 we then perforated the following: 4287-90, 4295-4300, 4361-69, 4374-77, 4384-88, 4393-95, 4488-4510, 4514-16, 4652-70, 4871-76, 4980-86, 4990-97, 5036-42, 5192-97, 5205-08, 5217-19, 5230-32, 5235-37, 5243-46, 5261-66, 5272-76, 5271-77, 5303-09, 5302-09, 5405-10, 5420-25, 5430-33, 5456-62, 5528-40, 5550-54, 5657-59, 5686-94, 5718-21, 5740-49 & 5761-64. We isolated and fracture treated the following intervals:

5,657'-5,764': 651 Bbbls of fluid containing 60,000#'s of sand,
 5,405'-5,554': 967 Bbbls of fluid containing 32,000#'s of sand,
 5,192'-5,309': 1578 Bbbls of fluid containing 62,100#'s of sand,
 5,036'-5,042': 394 Bbbls of fluid containing 10,100#'s of sand,
 4,871'-4,997': 607 Bbbls of fluid containing 60,200#'s of sand,
 4,652'-4,670': 505 Bbbls of fluid containing 45,000#'s of sand,
 4,488'-4,670': 505 Bbbls of fluid containing 61,000#'s of sand,
 4,361'-4,395': 505 Bbbls of fluid containing 40,000#'s of sand, 4,287'-4,300': 462 Bbbls of fluid containing 39,560#'s of sand.

Isolation plugs used were Halliburton 8K Composite Plugs, fluid used was Delta 140 18# gelled fluid, sand used was 20/40 Mesh Premium White Sand and guns used were Titan 3-1/8", containing 22.7 gram charges, 0.42" EHD, 23.54" TTP @ 4 SPF @ 120* Phased. All plugs were drilled out and cleaned out to PBTD, 6,127'. The well was swabbed until a good oil cut was see, then ran a pump on 10/20/2014 and put to pump.

NAME (PLEASE PRINT) <u>Rodrigo Jurado</u>	TITLE <u>Regulatory Compliance Specialist</u>
SIGNATURE	DATE <u>2/18/2015</u>

(This space for State use only)

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

AMENDED REPORT FORM 8
(highlight changes)

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. TYPE OF WELL: OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> DRY <input type="checkbox"/> OTHER _____				5. LEASE DESIGNATION AND SERIAL NUMBER: 14-20-H62-3520	
b. TYPE OF WORK: NEW WELL <input checked="" type="checkbox"/> HORIZ. LATS. <input type="checkbox"/> DEEP-EN <input type="checkbox"/> RE-ENTRY <input type="checkbox"/> DIFF. RESVR. <input type="checkbox"/> OTHER _____				6. IF INDIAN, ALLOTTEE OR TRIBE NAME Ute Indian Tribe	
2. NAME OF OPERATOR: Petroglyph Operating Company, Inc.				7. UNIT or CA AGREEMENT NAME 14-20-H62-4650	
3. ADDRESS OF OPERATOR: P.O. Box 607 CITY Roosevelt STATE UT ZIP 84066				8. WELL NAME and NUMBER: Ute Tribal 31-01	
PHONE NUMBER (435) 722-2531				9. API NUMBER: 4301352598	
4. LOCATION OF WELL (FOOTAGES) AT SURFACE: 826' FNL 690' FEL AT TOP PRODUCING INTERVAL REPORTED BELOW: 651' FNL 679' FEL AT TOTAL DEPTH: 670' FNL 705' FEL				10. FIELD AND POOL, OR WILDCAT Antelope Creek	
				11. QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: NENE 31 5S 3W U	
				12. COUNTY Duchesne	
				13. STATE UTAH	

14. DATE SPUDDED: 8/16/2014	15. DATE T.D. REACHED: 9/2/2014	16. DATE COMPLETED: 10/21/2014	ABANDONED <input type="checkbox"/>	READY TO PRODUCE <input checked="" type="checkbox"/>	17. ELEVATIONS (DF, RKB, RT, GL): 6,717' RKB
--------------------------------	------------------------------------	-----------------------------------	------------------------------------	--	---

18. TOTAL DEPTH: MD 6,213 TVD 6,206	19. PLUG BACK T.D.: MD 6,127 TVD 6,120	20. IF MULTIPLE COMPLETIONS, HOW MANY? *	21. DEPTH BRIDGE MD PLUG SET: TVD
--	---	--	--------------------------------------

22. TYPE ELECTRIC AND OTHER MECHANICAL LOGS RUN (Submit copy of each) ACTR, SDDSN, Cement Bond Log, Borehole Volume Plot		23. WAS WELL CORED? NO <input checked="" type="checkbox"/> YES <input type="checkbox"/> (Submit analysis) WAS DST RUN? NO <input checked="" type="checkbox"/> YES <input type="checkbox"/> (Submit report) DIRECTIONAL SURVEY? NO <input type="checkbox"/> YES <input checked="" type="checkbox"/> (Submit copy)	
---	--	---	--

24. CASING AND LINER RECORD (Report all strings set in well)

HOLE SIZE	SIZE/GRADE	WEIGHT (#/ft.)	TOP (MD)	BOTTOM (MD)	STAGE CEMENTER DEPTH	CEMENT TYPE & NO. OF SACKS	SLURRY VOLUME (BBL)	CEMENT TOP **	AMOUNT PULLED
26	16 J-55	75	0	73				0	Conductor
12.25	8.625 J-55	24	0	554		G 360	73	0	
7.875	5.5 J-55	15.5	0	6,210		G 815	261	65'	CBL

25. TUBING RECORD

SIZE	DEPTH SET (MD)	PACKER SET (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)
2.875	5,799							

26. PRODUCING INTERVALS

FORMATION NAME	TOP (MD)	BOTTOM (MD)	TOP (TVD)	BOTTOM (TVD)	INTERVAL (Top/Bot - MD)	SIZE	NO. HOLES	PERFORATION STATUS	
(A) Green River	4,287	5,764	4,280	5,757	4,287 5,764	0.42	744	Open <input checked="" type="checkbox"/>	Squeezed <input type="checkbox"/>
(B)								Open <input type="checkbox"/>	Squeezed <input type="checkbox"/>
(C)								Open <input type="checkbox"/>	Squeezed <input type="checkbox"/>
(D)								Open <input type="checkbox"/>	Squeezed <input type="checkbox"/>

27. PERFORATION RECORD

28. ACID, FRACTURE, TREATMENT, CEMENT SQUEEZE, ETC.

DEPTH INTERVAL	AMOUNT AND TYPE OF MATERIAL
4,287'-5,764'	6,174 Bbls of Delta 140 18# Gelled Fluid Containig 409,960#'s of 20/40 Mesh Sand.

29. ENCLOSED ATTACHMENTS:

<input checked="" type="checkbox"/> ELECTRICAL/MECHANICAL LOGS	<input type="checkbox"/> GEOLOGIC REPORT	<input type="checkbox"/> DST REPORT	<input checked="" type="checkbox"/> DIRECTIONAL SURVEY
<input type="checkbox"/> SUNDRY NOTICE FOR PLUGGING AND CEMENT VERIFICATION	<input type="checkbox"/> CORE ANALYSIS	<input checked="" type="checkbox"/> OTHER: UDOGM Form 7	

30. WELL STATUS:

POW

31. INITIAL PRODUCTION

INTERVAL A (As shown in item #26)

DATE FIRST PRODUCED: 10/19/2014	TEST DATE: 11/15/2014	HOURS TESTED: 24	TEST PRODUCTION RATES: →	OIL – BBL: 86	GAS – MCF: 177	WATER – BBL: 79	PROD. METHOD: Rod Pump
CHOKE SIZE: 32/64	TBG. PRESS. 120	CSG. PRESS. 125	API GRAVITY 39.80	BTU – GAS 1	GAS/OIL RATIO 2,058	24 HR PRODUCTION RATES: →	INTERVAL STATUS: Open

INTERVAL B (As shown in item #26)

DATE FIRST PRODUCED:	TEST DATE:	HOURS TESTED:	TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	INTERVAL STATUS:

INTERVAL C (As shown in item #26)

DATE FIRST PRODUCED:	TEST DATE:	HOURS TESTED:	TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	INTERVAL STATUS:

INTERVAL D (As shown in item #26)

DATE FIRST PRODUCED:	TEST DATE:	HOURS TESTED:	TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	INTERVAL STATUS:

32. DISPOSITION OF GAS (Sold, Used for Fuel, Vented, Etc.)

Used for Fuel

33. SUMMARY OF POROUS ZONES (Include Aquifers):

Show all important zones of porosity and contents thereof. Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

34. FORMATION (Log) MARKERS:

Formation	Top (MD)	Bottom (MD)	Descriptions, Contents, etc.	Name	Top (Measured Depth)
				Mahogany Shale	2,900
				Lower Parachute Creek	3,210
				Garden Gulch	3,579
				Middle Garden Gulch	3,977
				Lower Garden Gulch	4,451
				Douglas Creek	4,598
				Lower Douglas Creek	4,966
				Castle Peak	5,511
				Uteland Butte	5,950
				Wasatch	

35. ADDITIONAL REMARKS (Include plugging procedure)

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records.

NAME (PLEASE PRINT) Rodrigo Jurado

TITLE Regulatory Compliance Specialist

SIGNATURE 

DATE 3/2/2015

This report must be submitted within 30 days of

- completing or plugging a new well
- reentering a previously plugged and abandoned well
- drilling horizontal laterals from an existing well bore
- significantly deepening an existing well bore below the previous bottom-hole depth
- recompleting to a different producing formation
- drilling hydrocarbon exploratory holes, such as core samples and stratigraphic tests

* ITEM 20: Show the number of completions if production is measured separately from two or more formations.

** ITEM 24: Cement Top – Show how reported top(s) of cement were determined (circulated (CIR), calculated (CAL), cement bond log (CBL), temperature survey (TS)).

Send to: Utah Division of Oil, Gas and Mining
1594 West North Temple, Suite 1210
Box 145801
Salt Lake City, Utah 84114-5801

Phone: 801-538-5340
Fax: 801-359-3940

STATE OF UTAH
 DEPARTMENT OF NATURAL RESOURCES
 DIVISION OF OIL, GAS AND MINING

REPORT OF WATER ENCOUNTERED DURING DRILLING

Well name and number: Ute Tribal 31-01

API number: 4301352598

Well Location: QQ NENE Section 31 Township 5S Range 3W County Duchesne

Well operator: Petroglyph Operating Company, Inc.

Address: P.O. Box 607

city Roosevelt state UT zip 84066

Phone: (435) 722-2531

Drilling contractor: Pro Petro

Address: 1422 East 1500 South

city Vernal state UT zip 84078

Phone: (435) 789-1735

Water encountered (attach additional pages as needed):

DEPTH		VOLUME (FLOW RATE OR HEAD)	QUALITY (FRESH OR SALTY)
FROM	TO		
0	545	0	No Water Encountered

Formation tops: 1 _____ 2 _____ 3 _____
 (Top to Bottom) 4 _____ 5 _____ 6 _____
 7 _____ 8 _____ 9 _____
 10 _____ 11 _____ 12 _____

If an analysis has been made of the water encountered, please attach a copy of the report to this form.

I hereby certify that this report is true and complete to the best of my knowledge.

NAME (PLEASE PRINT) Rodrigo Jurado

TITLE Regulatory Compliance Specialist

SIGNATURE 

DATE 8/22/2014



Job Number: UT141437
Company: Petroglyph
Lease/Well: Ute Tribal 31-01
Location: Section 31 T5S, R3W
Rig Name: Capstar 334
RKB: 6717
G.L. or M.S.L.: 6704

State/Country: UT/USA
Declination: 10.98
Grid: True
File name: C:\WINSERVE\UT141437.SVY
Date/Time: 02-Sep-14 / 04:49
Curve Name: Actual

WINSERVE SURVEY CALCULATIONS
Minimum Curvature Method
Vertical Section Plane 10.00
Vertical Section Referenced to Wellhead
Rectangular Coordinates Referenced to Wellhead

<i>Measured Depth FT</i>	<i>Incl Angle Deg</i>	<i>Drift Direction Deg</i>	<i>True Vertical Depth</i>	<i>N-S FT</i>	<i>E-W FT</i>	<i>Vertical Section FT</i>	<i>CLOSURE</i>		<i>Dogleg Severity Deg/100</i>
							<i>Distance FT</i>	<i>Direction Deg</i>	
.00	.00	.00	.00	.00	.00	.00	.00	.00	.00
594.00	.35	158.72	594.00	-1.69	.66	-1.55	1.81	158.72	.06
686.00	.31	121.68	685.99	-2.08	.97	-1.88	2.30	154.98	.23
779.00	2.15	8.65	778.97	-.49	1.45	-.23	1.53	108.70	2.46
Transition from HW to drill pipe									
852.00	2.77	.26	851.91	2.63	1.66	2.88	3.11	32.33	.98
936.00	4.57	18.76	935.73	7.83	2.75	8.18	8.29	19.35	2.54
1021.00	4.66	19.02	1020.46	14.30	4.96	14.94	15.13	19.14	.11
1105.00	4.75	18.32	1104.17	20.82	7.17	21.75	22.02	18.99	.13
1189.00	4.39	20.78	1187.91	27.13	9.40	28.35	28.71	19.11	.49
1274.00	4.79	14.85	1272.64	33.60	11.47	35.08	35.51	18.84	.73
1358.00	4.44	11.64	1356.36	40.18	13.02	41.83	42.24	17.96	.52
1442.00	4.75	6.23	1440.09	46.82	14.05	48.55	48.88	16.71	.63
1527.00	4.75	3.69	1524.80	53.83	14.66	55.56	55.79	15.24	.25
1611.00	4.31	2.85	1608.54	60.45	15.04	62.15	62.30	13.97	.53
1695.00	4.09	357.84	1692.31	66.60	15.09	68.21	68.29	12.76	.51
1779.00	4.79	.30	1776.06	73.10	14.99	74.59	74.62	11.59	.86
1864.00	5.58	2.41	1860.71	80.78	15.18	82.19	82.19	10.65	.96
1948.00	4.26	357.14	1944.40	87.98	15.20	89.28	89.28	9.80	1.66
2032.00	5.63	2.67	2028.09	95.21	15.24	96.41	96.42	9.09	1.73
2117.00	5.58	359.25	2112.68	103.50	15.38	104.60	104.64	8.45	.40
2201.00	4.79	351.86	2196.34	111.06	14.83	111.95	112.05	7.60	1.23
2285.00	6.02	11.16	2279.97	118.85	15.18	119.69	119.82	7.28	2.59
2370.00	4.97	5.09	2364.58	126.90	16.37	127.81	127.95	7.35	1.41
2454.00	3.65	1.31	2448.34	133.19	16.76	134.08	134.24	7.17	1.61
2542.00	2.72	353.31	2536.20	138.07	16.58	138.85	139.06	6.85	1.17

Measured Depth FT	Incl Angle Deg	Drift Direction Deg	True Vertical Depth	N-S FT	E-W FT	Vertical Section FT	C L O S U R E		Dogleg Severity Deg/100
							Distance FT	Direction Deg	
2633.00	2.64	1.18	2627.10	142.31	16.37	142.99	143.25	6.56	.41
2725.00	1.89	355.47	2719.03	145.94	16.29	146.55	146.84	6.37	.85
2816.00	1.76	343.29	2809.99	148.77	15.77	149.25	149.61	6.05	.45
2907.00	2.55	19.81	2900.92	152.02	16.06	152.49	152.86	6.03	1.70
2999.00	2.17	18.80	2992.85	155.59	17.31	156.23	156.55	6.35	.42
3090.00	1.58	14.63	3083.80	158.43	18.18	159.19	159.47	6.55	.67
3181.00	1.45	4.17	3174.77	160.80	18.58	161.58	161.87	6.59	.34
3273.00	1.36	354.37	3266.74	163.04	18.56	163.79	164.10	6.49	.28
3364.00	1.32	357.84	3357.71	165.17	18.42	165.86	166.19	6.36	.10
3455.00	1.10	349.80	3448.69	167.07	18.22	167.70	168.06	6.22	.30
3547.00	1.23	330.51	3540.67	168.80	17.58	169.29	169.72	5.95	.45
3638.00	.66	300.27	3631.66	169.92	16.65	170.23	170.73	5.60	.81
3729.00	.62	282.91	3722.66	170.29	15.71	170.43	171.01	5.27	.22
3821.00	1.19	261.03	3814.64	170.25	14.28	170.15	170.85	4.80	.71
3912.00	1.36	247.27	3905.62	169.69	12.36	169.26	170.14	4.16	.38
4003.00	1.67	328.97	3996.60	170.41	10.68	169.67	170.74	3.58	2.19
4095.00	1.14	20.69	4088.57	172.41	10.31	171.58	172.72	3.42	1.43
4186.00	.97	29.74	4179.56	173.93	11.01	173.20	174.28	3.62	.26
4277.00	.70	.74	4270.55	175.15	11.40	174.47	175.52	3.72	.54
4369.00	.70	284.76	4362.54	175.86	10.86	175.07	176.19	3.53	.94
4460.00	.48	258.22	4453.54	175.92	9.95	174.98	176.20	3.24	.38
4551.00	.88	238.05	4544.53	175.47	8.99	174.37	175.70	2.93	.51
4642.00	1.45	252.37	4635.51	174.76	7.30	173.37	174.91	2.39	.70
4734.00	1.27	219.90	4727.49	173.62	5.53	171.94	173.71	1.83	.85
4825.00	1.76	225.96	4818.46	171.88	3.88	169.94	171.92	1.29	.57
4916.00	1.05	270.35	4909.43	170.91	2.04	168.67	170.92	.68	1.37
5008.00	1.01	285.86	5001.42	171.14	.42	168.61	171.14	.14	.31
5099.00	.92	238.22	5092.41	170.97	-.97	168.20	170.97	359.67	.86
5190.00	1.01	228.33	5183.39	170.05	-2.19	167.09	170.07	359.26	.21
5281.00	1.27	251.45	5274.38	169.20	-3.75	165.98	169.24	358.73	.57
5373.00	2.11	231.85	5366.34	167.83	-6.05	164.23	167.94	357.94	1.10
5464.00	.35	287.09	5457.31	166.87	-7.63	163.01	167.05	357.38	2.12
5555.00	.66	259.45	5548.31	166.86	-8.41	162.86	167.07	357.11	.42
5647.00	.48	229.56	5640.30	166.51	-9.22	162.38	166.77	356.83	.37
5738.00	.79	227.32	5731.30	165.84	-9.98	161.59	166.14	356.56	.34
5829.00	1.23	203.15	5822.29	164.52	-10.82	160.14	164.87	356.24	.66
5921.00	1.45	201.88	5914.26	162.53	-11.64	158.04	162.95	355.90	.24
6012.00	1.19	205.31	6005.24	160.61	-12.48	156.00	161.09	355.56	.30
Final Survey									
6103.00	1.80	206.27	6096.20	158.47	-13.51	153.72	159.05	355.13	.67
Projected to Bit									
6213.00	1.54	206.27	6206.16	155.60	-14.93	150.64	156.31	354.52	.24

