

STATE OF UTAH
 DEPARTMENT OF NATURAL RESOURCES
 DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL

2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>		1. WELL NAME and NUMBER Ute Tribal 11-3-4-1E				
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO		3. FIELD OR WILDCAT WILDCAT				
6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY		5. UNIT or COMMUNITIZATION AGREEMENT NAME				
8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052		7. OPERATOR PHONE 435 646-4825				
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) 20G0005609		9. OPERATOR E-MAIL mcrozier@newfield.com				
11. MINERAL OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input checked="" type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>		12. SURFACE OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input checked="" type="checkbox"/>				
13. NAME OF SURFACE OWNER (if box 12 = 'fee') Deep Creek Investments etal.		14. SURFACE OWNER PHONE (if box 12 = 'fee')				
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee') 2400 Sunnyside Ave ,		16. SURFACE OWNER E-MAIL (if box 12 = 'fee')				
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')		18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>				
19. SLANT VERTICAL <input checked="" type="checkbox"/> DIRECTIONAL <input type="checkbox"/> HORIZONTAL <input type="checkbox"/>						
20. LOCATION OF WELL	FOOTAGES	QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN
LOCATION AT SURFACE	1988 FSL 1986 FWL	NESW	3	4.0 S	1.0 E	U
Top of Uppermost Producing Zone	1988 FSL 1986 FWL	NESW	3	4.0 S	1.0 E	U
At Total Depth	1988 FSL 1986 FWL	NESW	3	4.0 S	1.0 E	U
21. COUNTY UINTAH		22. DISTANCE TO NEAREST LEASE LINE (Feet) 1986		23. NUMBER OF ACRES IN DRILLING UNIT 40		
		25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 1320		26. PROPOSED DEPTH MD: 8035 TVD: 8035		
27. ELEVATION - GROUND LEVEL 5271		28. BOND NUMBER WYB000493		29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 43-7478		

ATTACHMENTS

VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES

<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER	<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN
<input checked="" type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)	<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER
<input type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)	<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP

NAME Mandie Crozier	TITLE Regulatory Tech	PHONE 435 646-4825
SIGNATURE	DATE 04/01/2010	EMAIL mcrozier@newfield.com
API NUMBER ASSIGNED 43047510470000	APPROVAL  Permit Manager	

Proposed Hole, Casing, and Cement

String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Prod	7.875	5.5	0	8035		
Pipe	Grade	Length	Weight			
	Grade J-55 LT&C	8035	15.5			

Proposed Hole, Casing, and Cement

String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Surf	12.25	8.625	0	300		
Pipe	Grade	Length	Weight			
	Grade J-55 ST&C	300	24.0			

11-3-4-1E

MEMORANDUM
of
EASEMENT, RIGHT-OF-WAY
and
SURFACE USE AGREEMENT

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 2nd day of October, 2009 by and between **Deep Creek Investments etal, Lee M. Smith, General Manager** whose address is **2400 Sunnyside Avenue, Salt Lake City, UT 84108**, ("Surface Owner," whether one or more) and **Newfield Production Company**, a Texas corporation ("NEWFIELD"), with offices at 1001 17th Street, Suite 2000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Uintah County, Utah described as follows:

Township 4 South, Range 1 East
Section 2
Section 3 S1/2

Uintah County, Utah

Being 960 acres, more or less and pertaining to the following wells:

- 1-2-4-1E (NENE - Sec. 2), 2-2-4-1E (NWNE - Sec. 2), 3-2-4-1E (NENW - Sec. 2),
- 4-2-4-1E (NWNW - Sec. 2), 5-2-4-1E (SWNW - Sec. 2), 6-2-4-1E (SENE - Sec. 2),
- 7-2-4-1E (SWNE - Sec. 2), 8-2-4-1E (SENE - Sec. 2), 9-2-4-1E (NESE - Sec. 2),
- 10-2-4-1E (NWSE - Sec. 2), 11-2-4-1E (NESW - Sec. 2), 12-2-4-1E (NWSW - Sec. 2),
- 13-2-4-1E (SWSW - Sec. 2), 14-2-4-1E (SESW - Sec. 2), 15-2-4-1E (SWSE - Sec. 2),
- 16-2-4-1E (SESE - Sec. 2), 9-3-4-1E (NESE - Sec. 3), 10-3-4-1E (NWSE - Sec. 3),
- 11-3-4-1E (NESW - Sec. 3), 12-3-4-1E (NWSW - Sec. 3), 13-3-4-1E (SWSW - Sec. 3),
- 14-3-4-1E (SESW - Sec. 3), 15-3-4-1E (SWSE - Sec. 3), 16-3-4-1E (SESE - Sec. 3).

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

1. Compensation for Well; Release of All Claims

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated October 2nd, 2009 as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

2. Grant of Right of Way and Easement

Surface Owner hereby grants, bargains, leases, assigns, and conveys to NEWFIELD an easement and right-of-way for the purpose of construction, using and maintaining access roads, locations for surface equipment and subsurface gathering lines for each well drilled upon the Lands, pipelines, and pipeline interconnections for two years from date of this agreement and so long thereafter as NEWFIELD's oil and gas leases remain in effect.

This Agreement shall be binding upon the respective heirs, executors, administrators, successors, and assigns of the undersigned. This agreement replaces and supersedes any and all prior agreements covering the lands described herein.

These Parties hereto have executed this document effective as of the day first above written.

SURFACE OWNER

NEWFIELD PRODUCTION COMPANY

By: 
Lee M. Smith, General Manager
Deep Creek Investments, etal

By: _____
Daniel W. Shewmake
Vice President - Development


STATE OF UTAH)
)ss
COUNTY OF Salt Lake)

This instrument was acknowledged before me this 2nd day of October, 2009 by Lee M. Smith, Deep Creek Investments, etal, General Manager.

Witness my hand and official seal.

My commission expires 9/8/2013

Tim Eaton
Notary Public



STATE OF COLORADO)
)ss
COUNTY OF DENVER)

This instrument was acknowledged before me this _____, 2009 by Daniel W. Shewmake, as Vice President - Development of Newfield Production Company, a Texas corporation, on behalf of the corporation.

Witness my hand and official seal.

Notary Public

My commission expires _____

NEWFIELD PRODUCTION COMPANY
UTE TRIBAL 11-3-4-1E
NE/SW SECTION 3, T4S, R1E
UINTAH COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0' – 2,845'
Green River	2,845'
Wasatch	7,735'
Proposed TD	8,035'

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil) 2,845' – 7,735'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sampled Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO ₃) (mg/l)
Dissolved Bicarbonate (NaHCO ₃) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO ₄) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: Ute Tribal 11-3-4-1E**

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950 17.53	1,370 14.35	244,000 33.89
Prod casing 5-1/2"	0'	8,035'	15.5	J-55	LTC	4,810 1.88	4,040 1.58	217,000 1.74

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg
 Pore pressure at surface casing shoe = 8.33 ppg
 Pore pressure at prod casing shoe = 8.33 ppg
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: Ute Tribal 11-3-4-1E**

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft ³ /sk)
			ft ³			
Surface casing	300'	Class G w/ 2% CaCl	138 161	30%	15.8	1.17
Prod casing Lead	6,035'	Prem Lite II w/ 10% gel + 3% KCl	417 1359	30%	11.0	3.26
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363 451	30%	14.3	1.24

- * Actual volume pumped will be 15% over the caliper log
- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ±350 feet will be drilled with an air/mist system. The air rig is equipped with a 6 ½" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ±350 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated

bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.

10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the third quarter of 2010, and take approximately seven (7) days from spud to rig release.

2-M SYSTEM

Blowout Prevention Equipment Systems


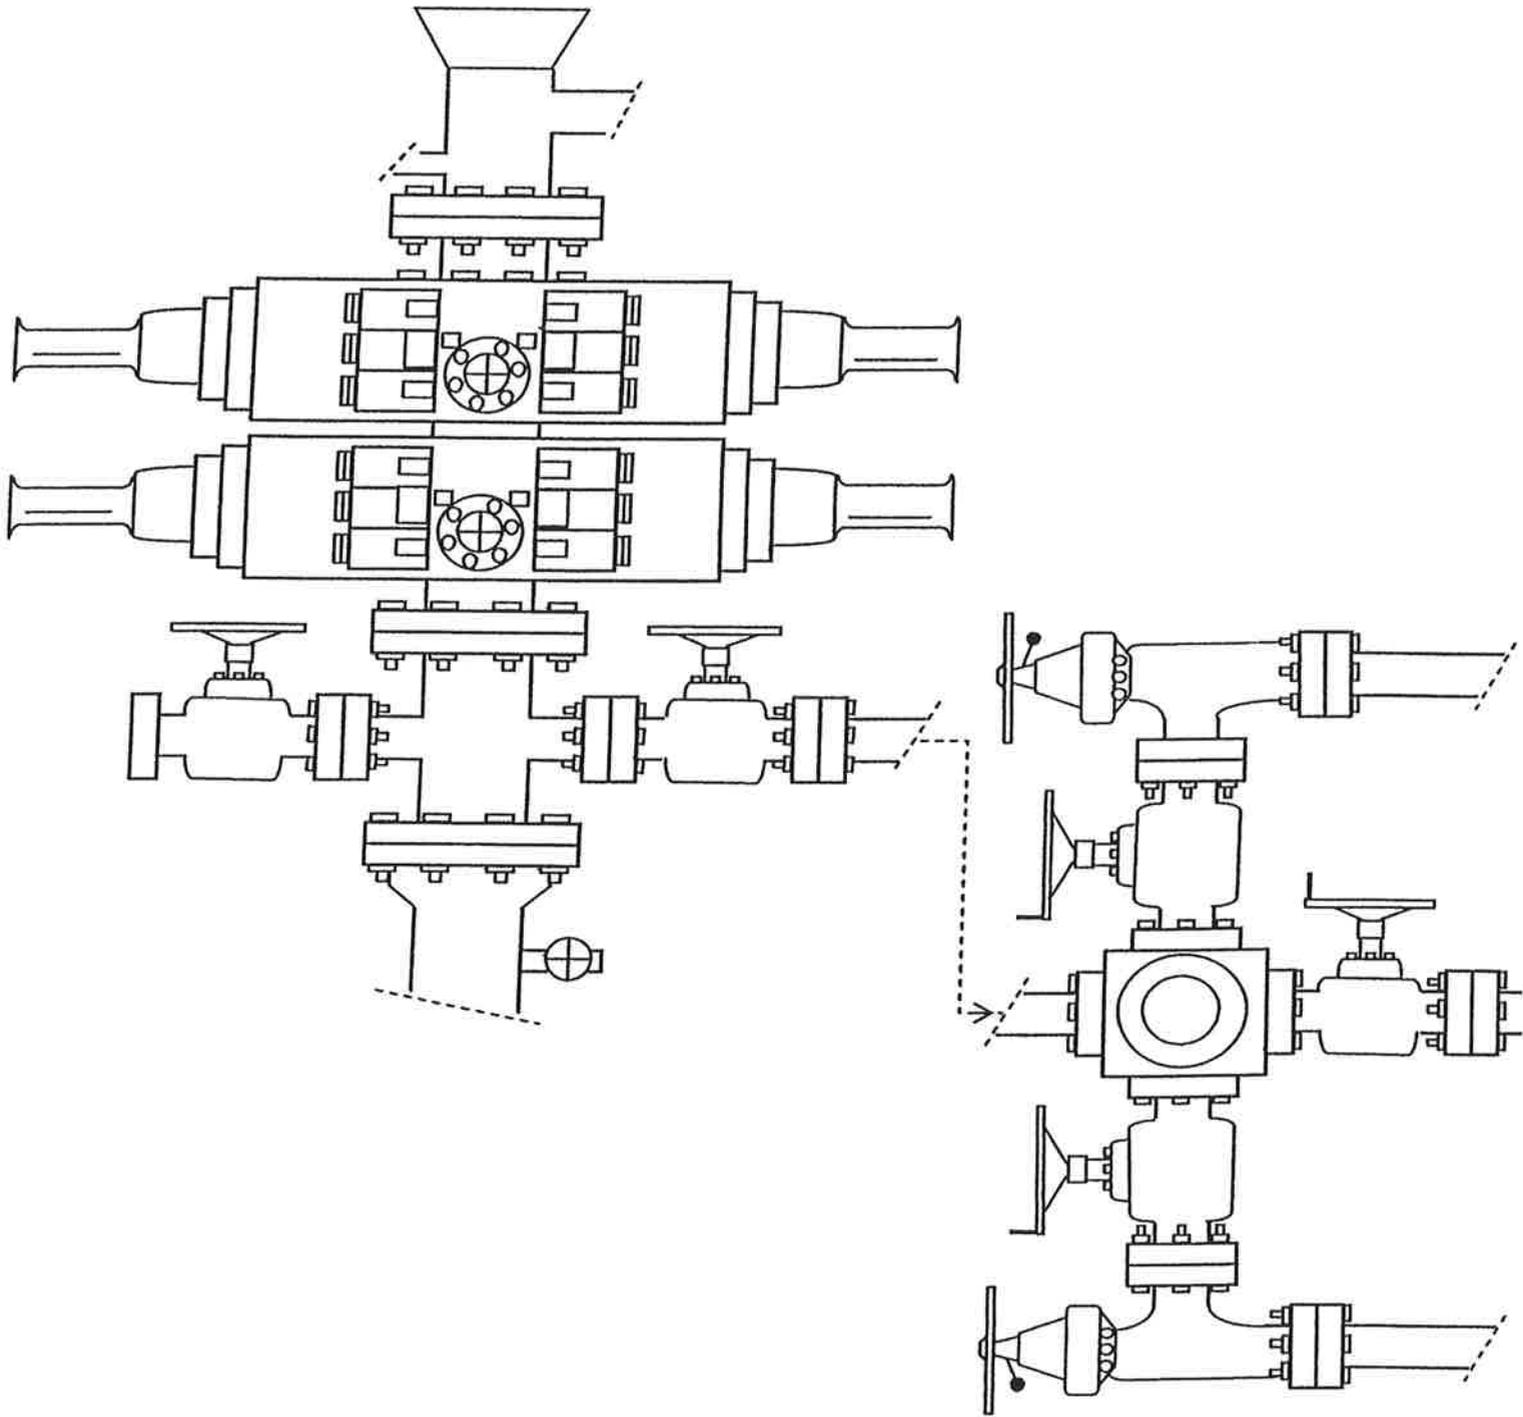


EXHIBIT C



11-3-4-1E
SEC. 3, T4S, R1E, U.S.B.&M.

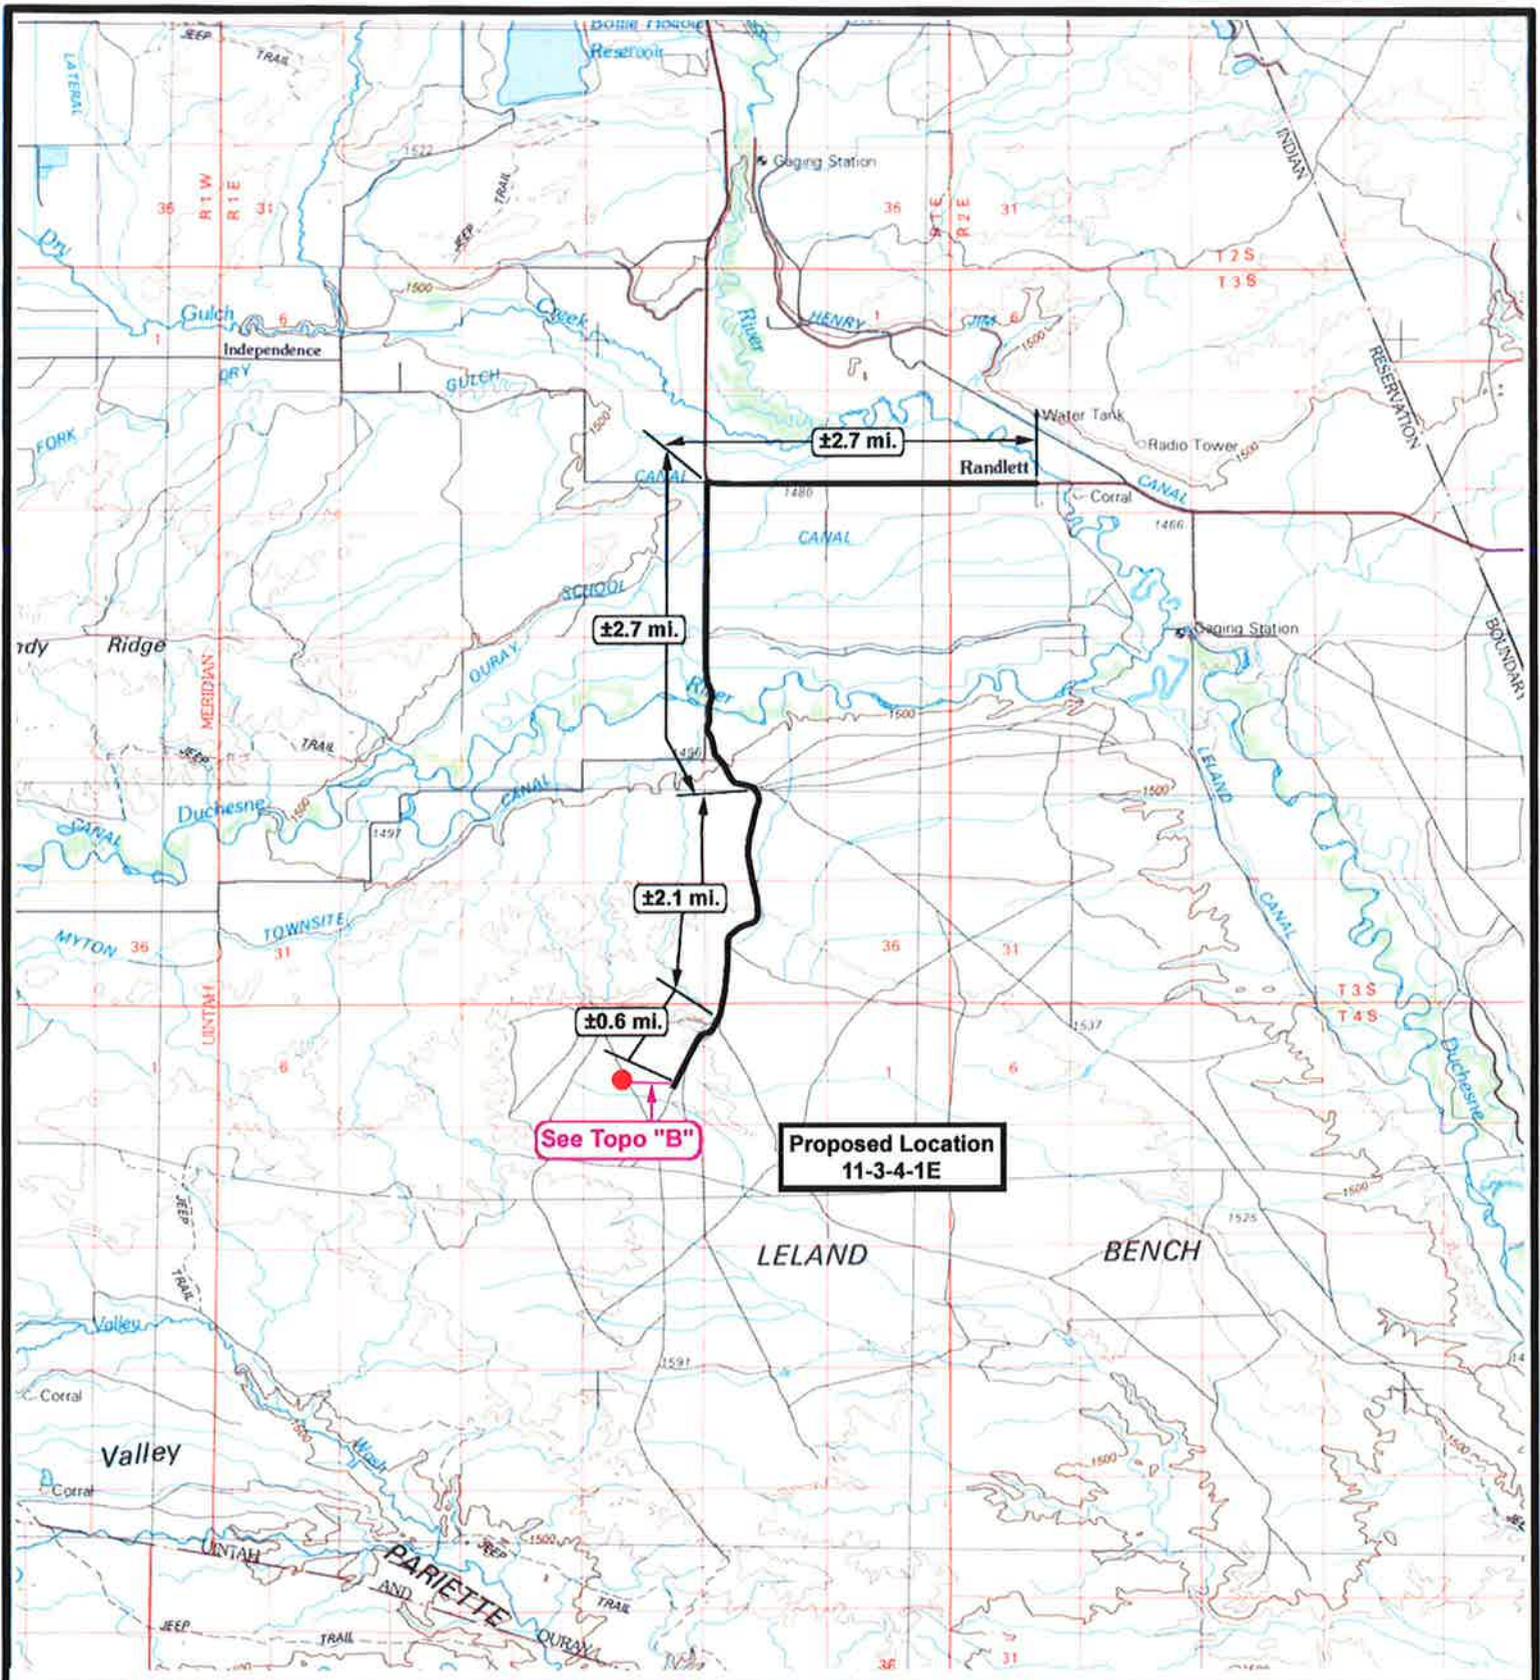


Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: JAS
DATE: 01-14-2010

Legend

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP
"A"

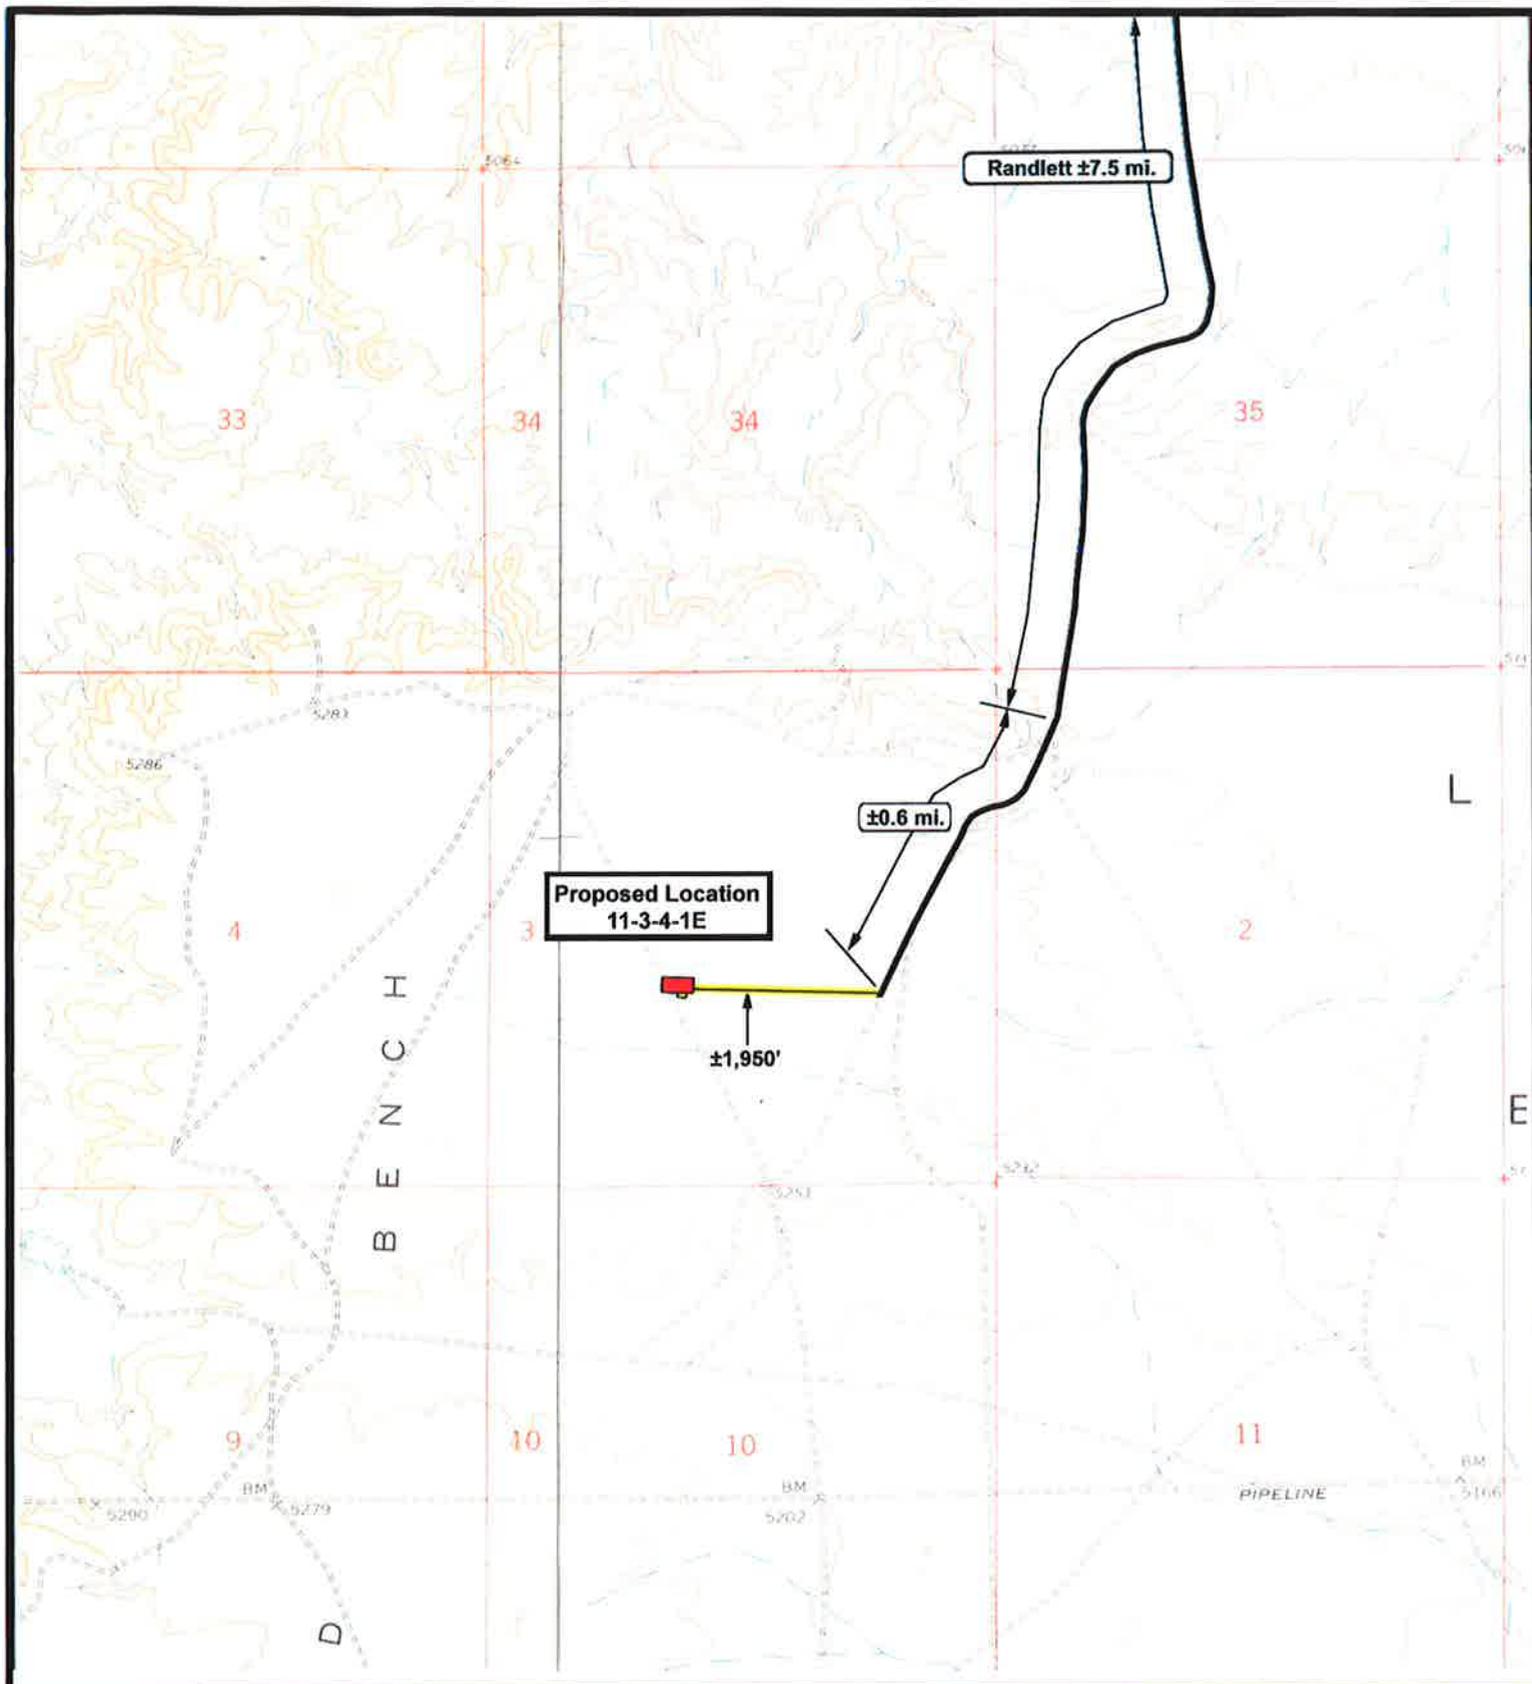

NEWFIELD
Exploration Company

11-3-4-1E
SEC. 3, T4S, R1E, U.S.B.&M.



Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'

DRAWN BY: JAS


DATE: 01-14-2010

Legend

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP

"B"

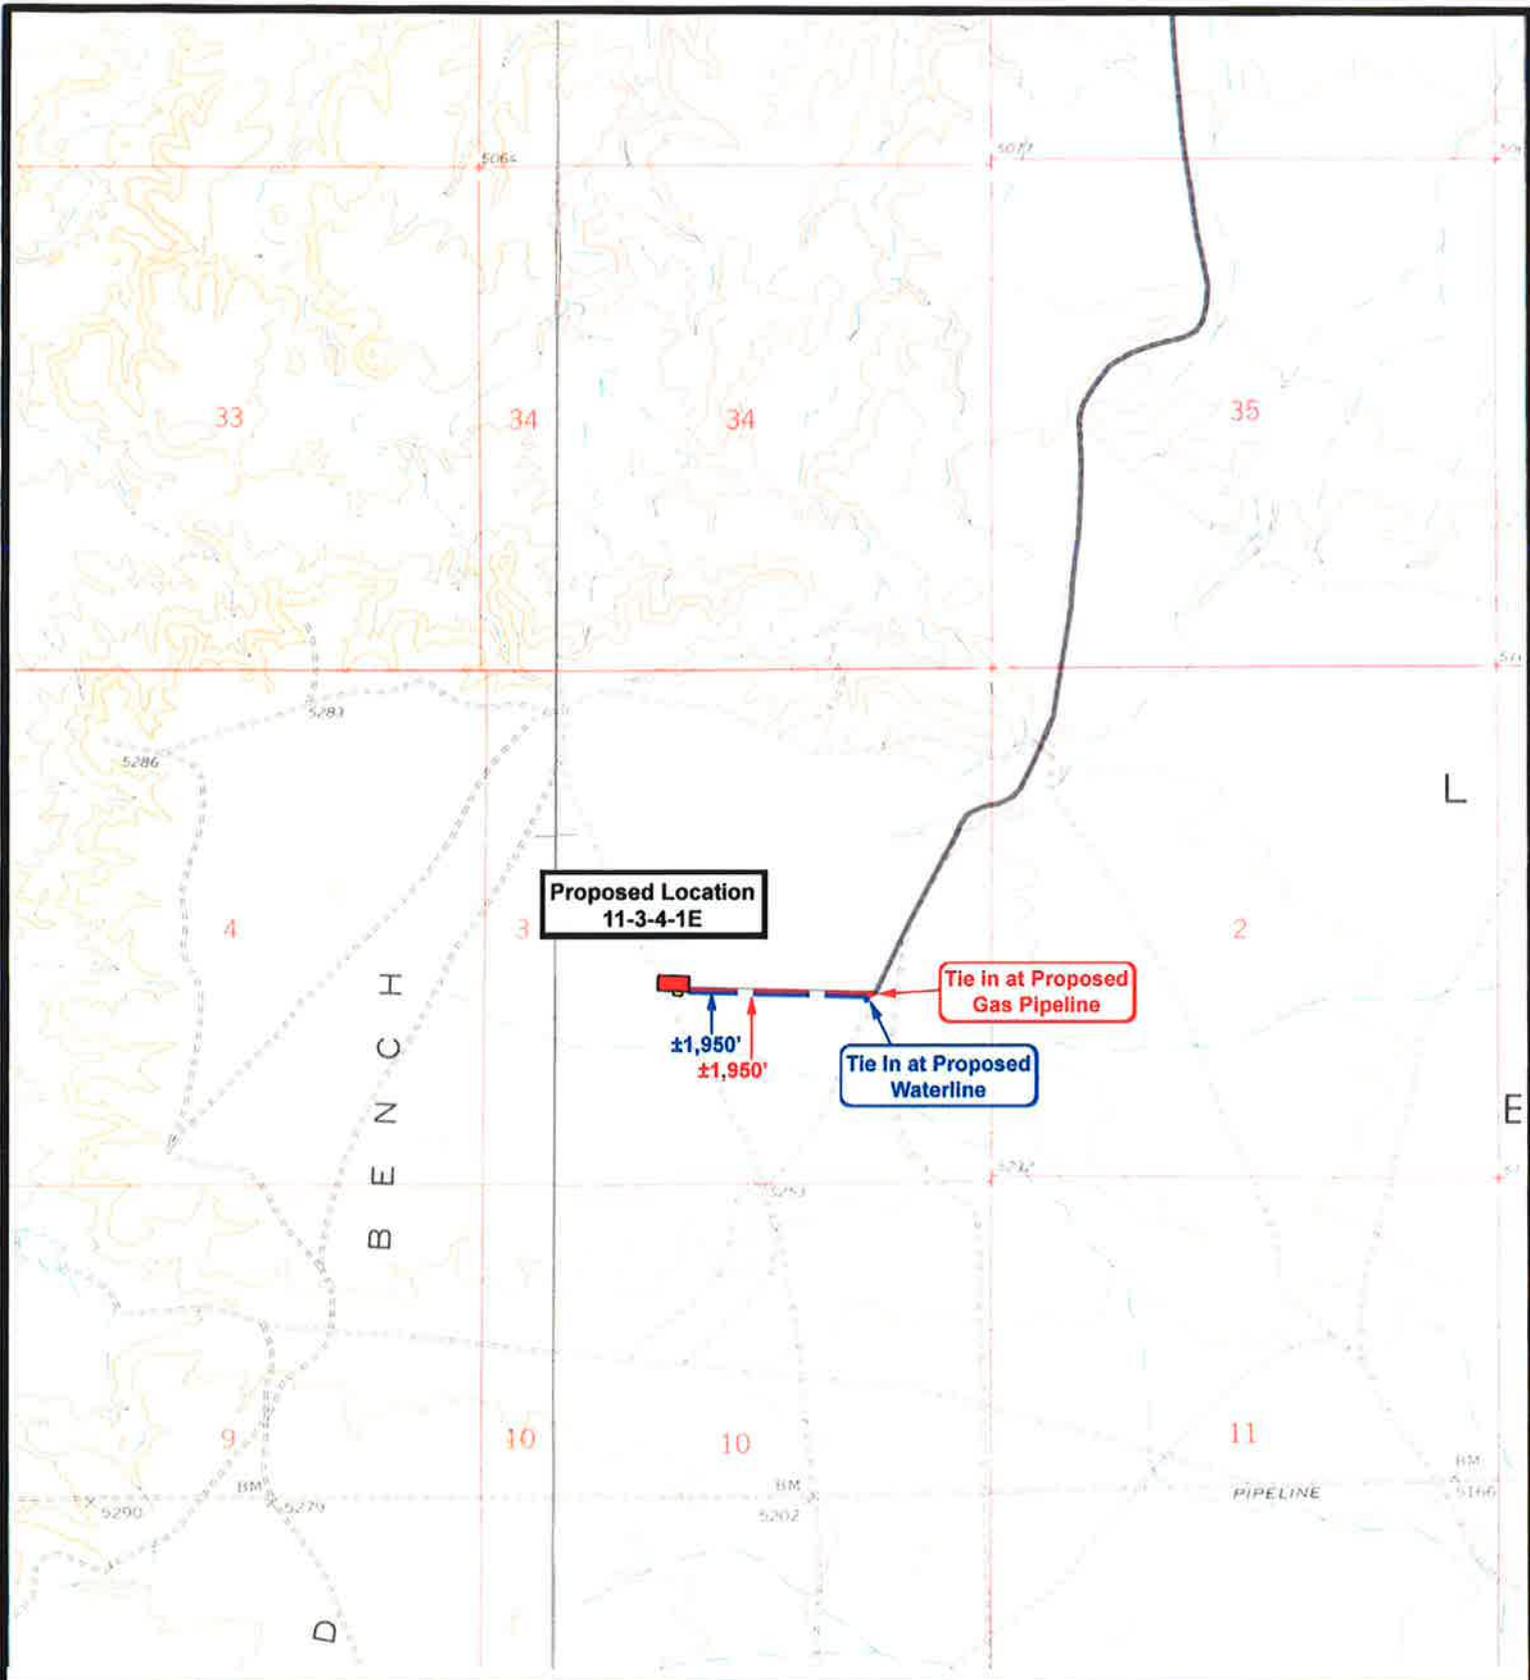

 **NEWFIELD**
Exploration Company

11-3-4-1E
SEC. 3, T4S, R1E, U.S.B.&M.




**Tri-State**
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: JAS
DATE: 01-14-2010

Legend

-  Roads
-  Proposed Gas Line
-  Proposed Water Line

TOPOGRAPHIC MAP
"C"

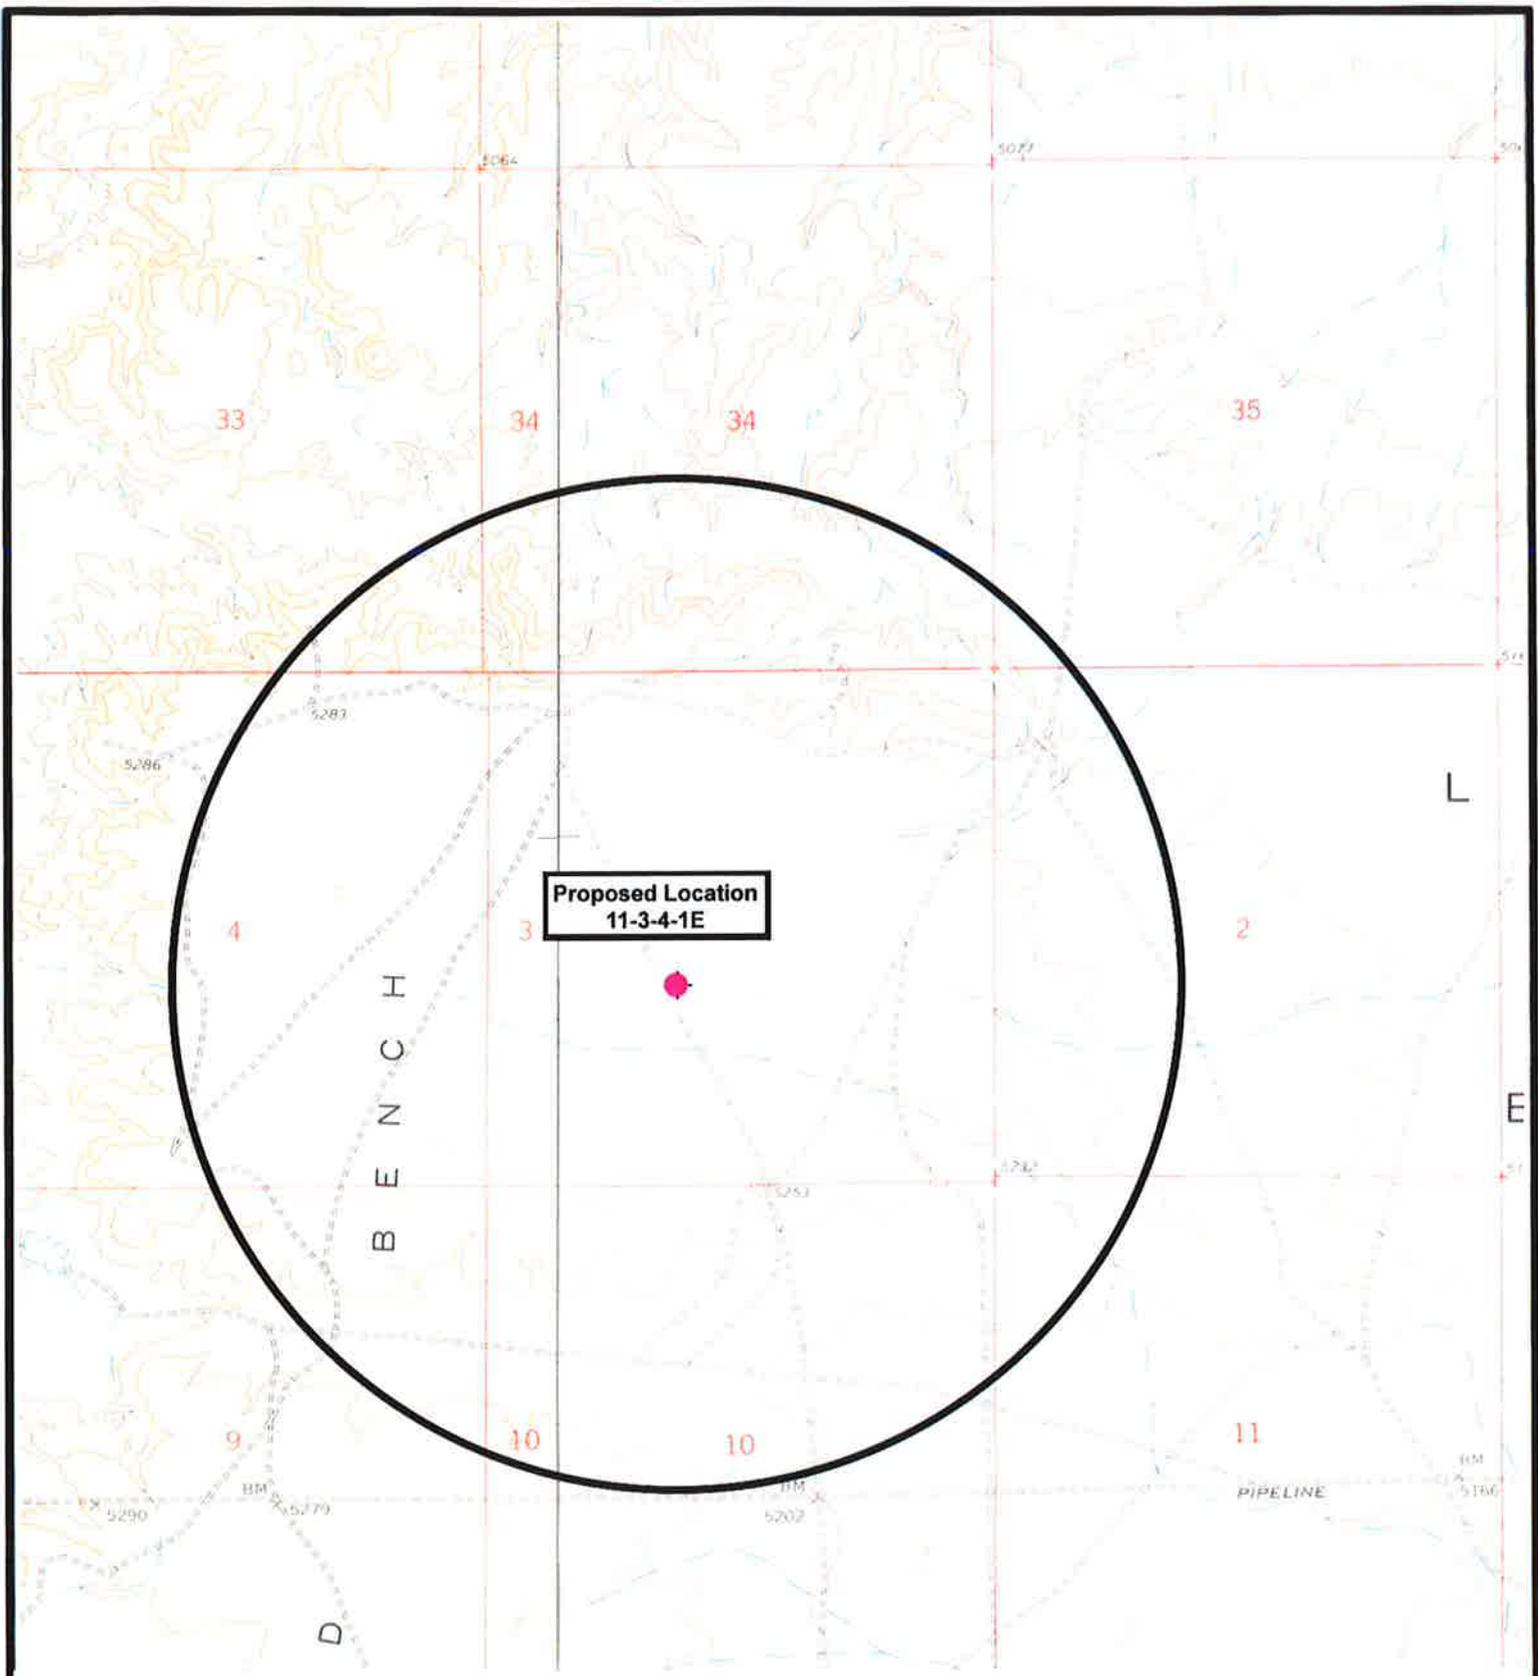

Proposed Location
11-3-4-1E

B
E
N
C
H

PIPELINE



NEWFIELD
Exploration Company

11-3-4-1E
SEC. 3, T4S, R1E, U.S.B.&M.



Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: JAS
DATE: 01-14-2010

Legend

- Location
- One-Mile Radius

Exhibit "B"

**NEWFIELD PRODUCTION COMPANY
UTE TRIBAL 11-3-4-1E
NE/SW SECTION 3, T4S, R1E
UINTAH COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Ute Tribal 11-3-4-1E located in the NE 1/4 SW 1/4 Section 3, T4S, R1E, Uintah County, Utah:

Proceed in a westerly direction out of Randlett, approximately 2.7 miles to it's junction with an existing road to the south; proceed in a southeasterly direction approximately 5.4 miles to it's junction with the beginning of the proposed access road to the west; proceed westerly along the proposed access road approximately 1,950' to the proposed well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

Approximately 1,950' of access road is proposed for the proposed well. See attached Topographic Map "B".

The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District
Water Right : 43-7478

Neil Moon Pond
Water Right: 43-11787

Maurice Harvey Pond
Water Right: 47-1358

Newfield Collector Well
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), State of Utah approved surface disposal facilities, or Federally approved surface disposal facilities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be

reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – Deep Creek Investments.

See attached Memorandum of Surface Use Agreement and Easement ROW.

12. **OTHER ADDITIONAL INFORMATION**

Newfield Production Company requests 1,950' of disturbed area be granted to allow for construction of the planned access road. **Refer to Topographic Map "B"**. A permanent width of 30' and a running surface of 18' is proposed for the planned access road. The construction phase of the planned access road will last approximately (5) days. The planned access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 1,950' of disturbed area be granted for construction of the proposed gas lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a 6" gas gathering line, and a 3" poly fuel gas line, with a permanent width of 30' upon completion of the proposed gas lines. The construction phase of the proposed gas lines will last approximately (5) days. Both proposed lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."**

Newfield Production Company requests 1,950' of disturbed area be granted to allow for construction of the proposed water lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line and 30' wide upon completion of the proposed water lines. Both proposed lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** In the event that the proposed well is converted to a water injection well, a separate injection permit will be applied for through the proper agencies.

- a) Newfield Production Company is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, Newfield is to immediately stop work that might further disturb such materials and contact the Authorized Officer.
- b) Newfield Production will control noxious weeds along rights-of-way for roads, pipelines, well sites or other applicable facilities. On State administered land it is required that a Pesticide Use Proposal shall be submitted and given approval prior to the application of herbicides or other possible hazardous chemicals.
- c) Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on State Lands after the conclusion of drilling operations or at any other time without State authorization. However, if State authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

The Archaeological and Paleontological Report Waivers are attached.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the Ute Tribal 11-3-4-1E, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Ute Tribal 11-3-4-1E, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

The State office as well as the Ute Tribe Energy and Mineral Department shall be notified upon site completion prior to moving on the drilling rig.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

Representative

Name: Tim Eaton
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that Newfield Production Company is considered to be the operator of well #11-3-4-1E, NE/SW Section 3, T4S, R1E, Uintah County, Utah and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.



3/31/10
Date


Mandie Crozier
Regulatory Specialist
Newfield Production Company

NEWFIELD PRODUCTION COMPANY

11-3-4-1E

Section 3, T4S, R1E, U.S.B.&M.

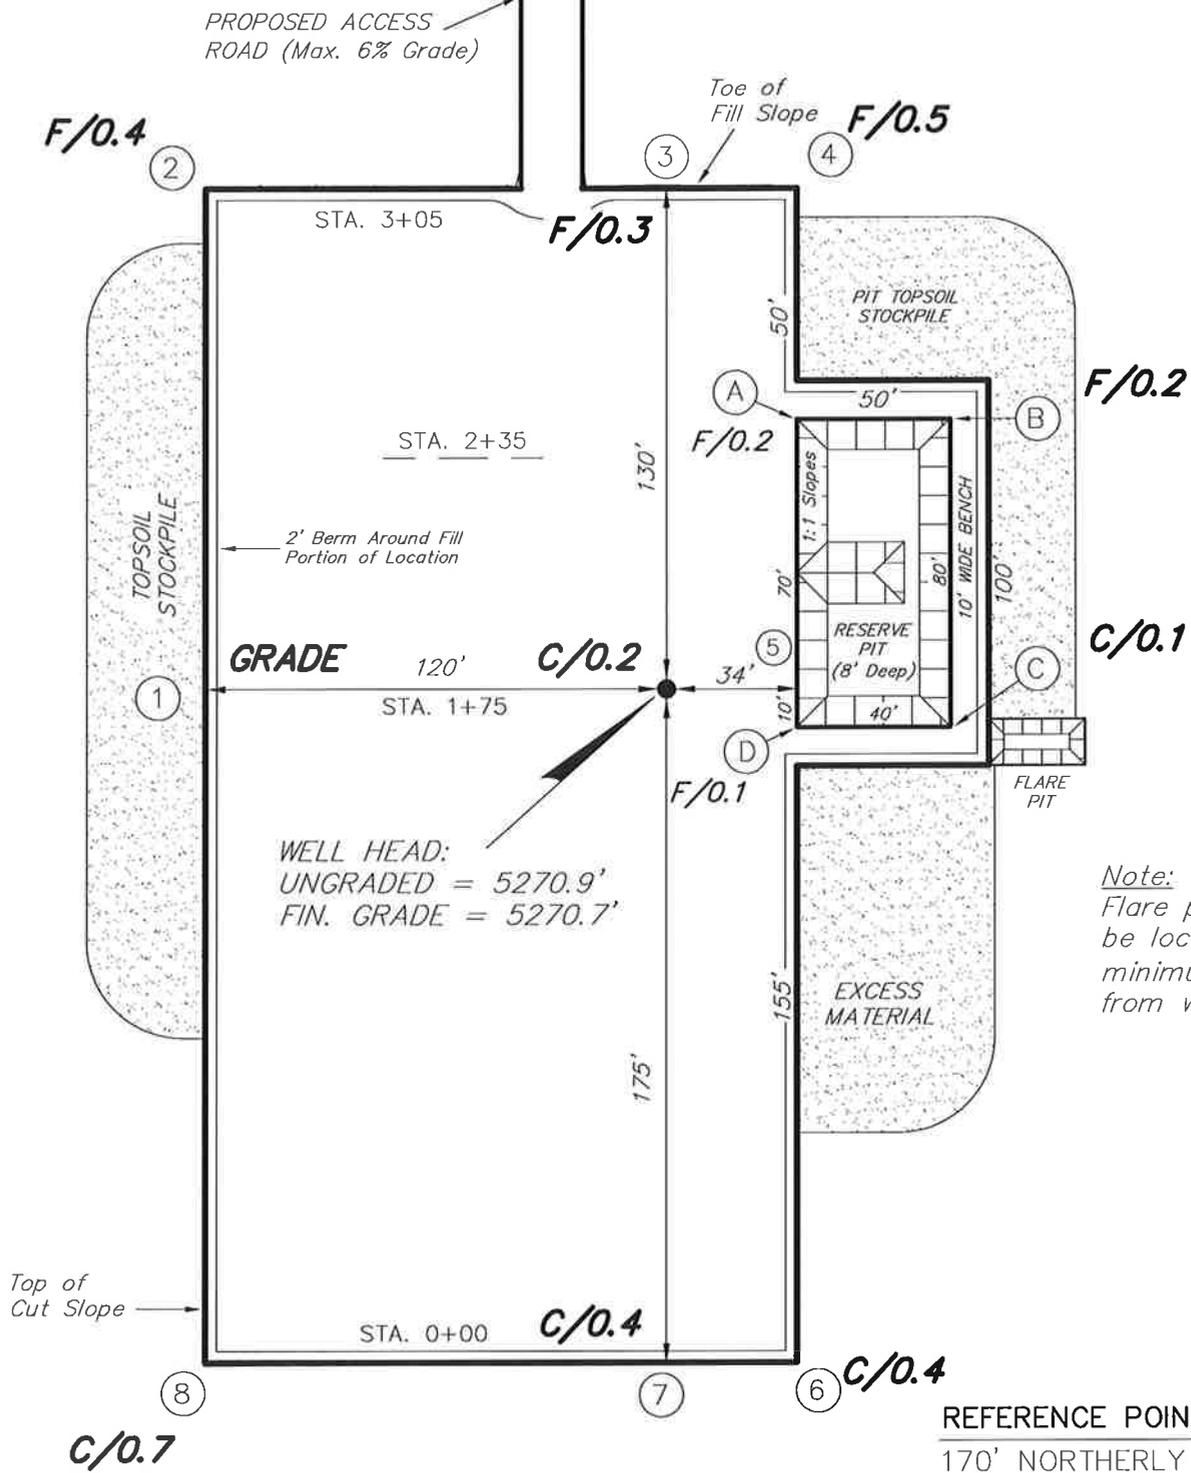

Note:
Flare pit is to be located a minimum of 80' from well head.

REFERENCE POINTS	
170' NORTHERLY	5270.7'
220' NORTHERLY	5271.0'
220' WESTERLY	5271.3'
270' WESTERLY	5271.4'

SURVEYED BY: T.P.	DATE SURVEYED: 01-07-10
DRAWN BY: M.W.	DATE DRAWN: 01-12-10
SCALE: 1" = 50'	REVISED:




Tri State
 Land Surveying, Inc.

(435) 781-2501
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

CROSS SECTIONS

11-3-4-1E

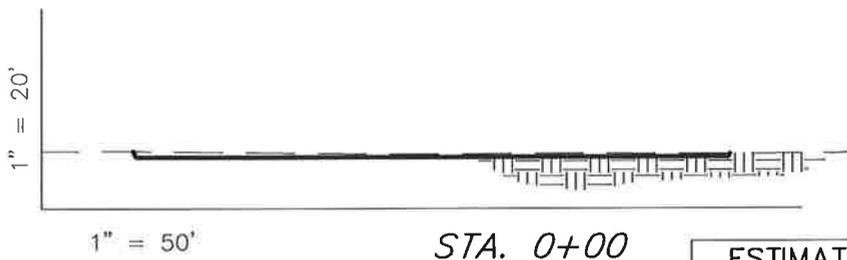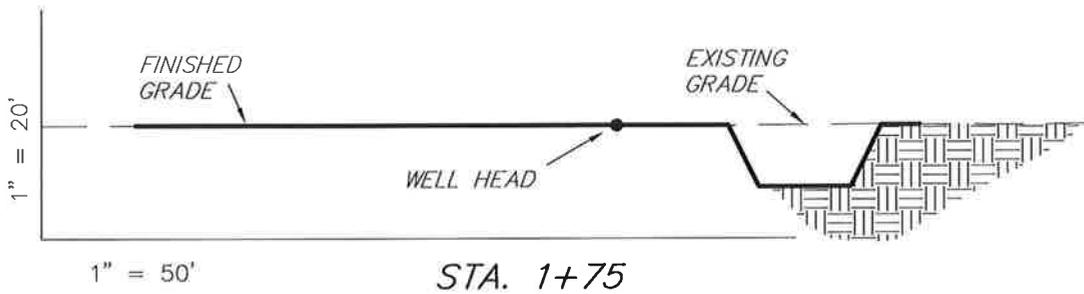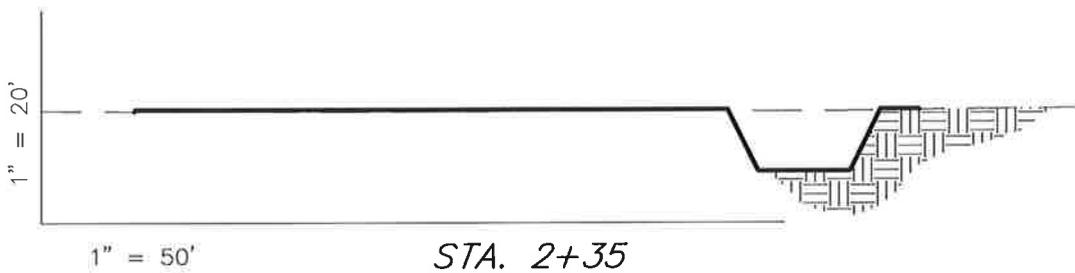

NOTE:
UNLESS OTHERWISE NOTED
CUT SLOPES ARE AT 1:1
FILL SLOPES ARE AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES
(No Shrink or swell adjustments have been used)
(Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	200	190	Topsoil is not included in Pad Cut	10
PIT	640	0		640
TOTALS	840	190	970	650


SURVEYED BY: T.P.	DATE SURVEYED: 01-07-10
DRAWN BY: M.W.	DATE DRAWN: 01-12-10
SCALE: 1" = 50'	REVISED:

Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY

TYPICAL RIG LAYOUT

11-3-4-1E

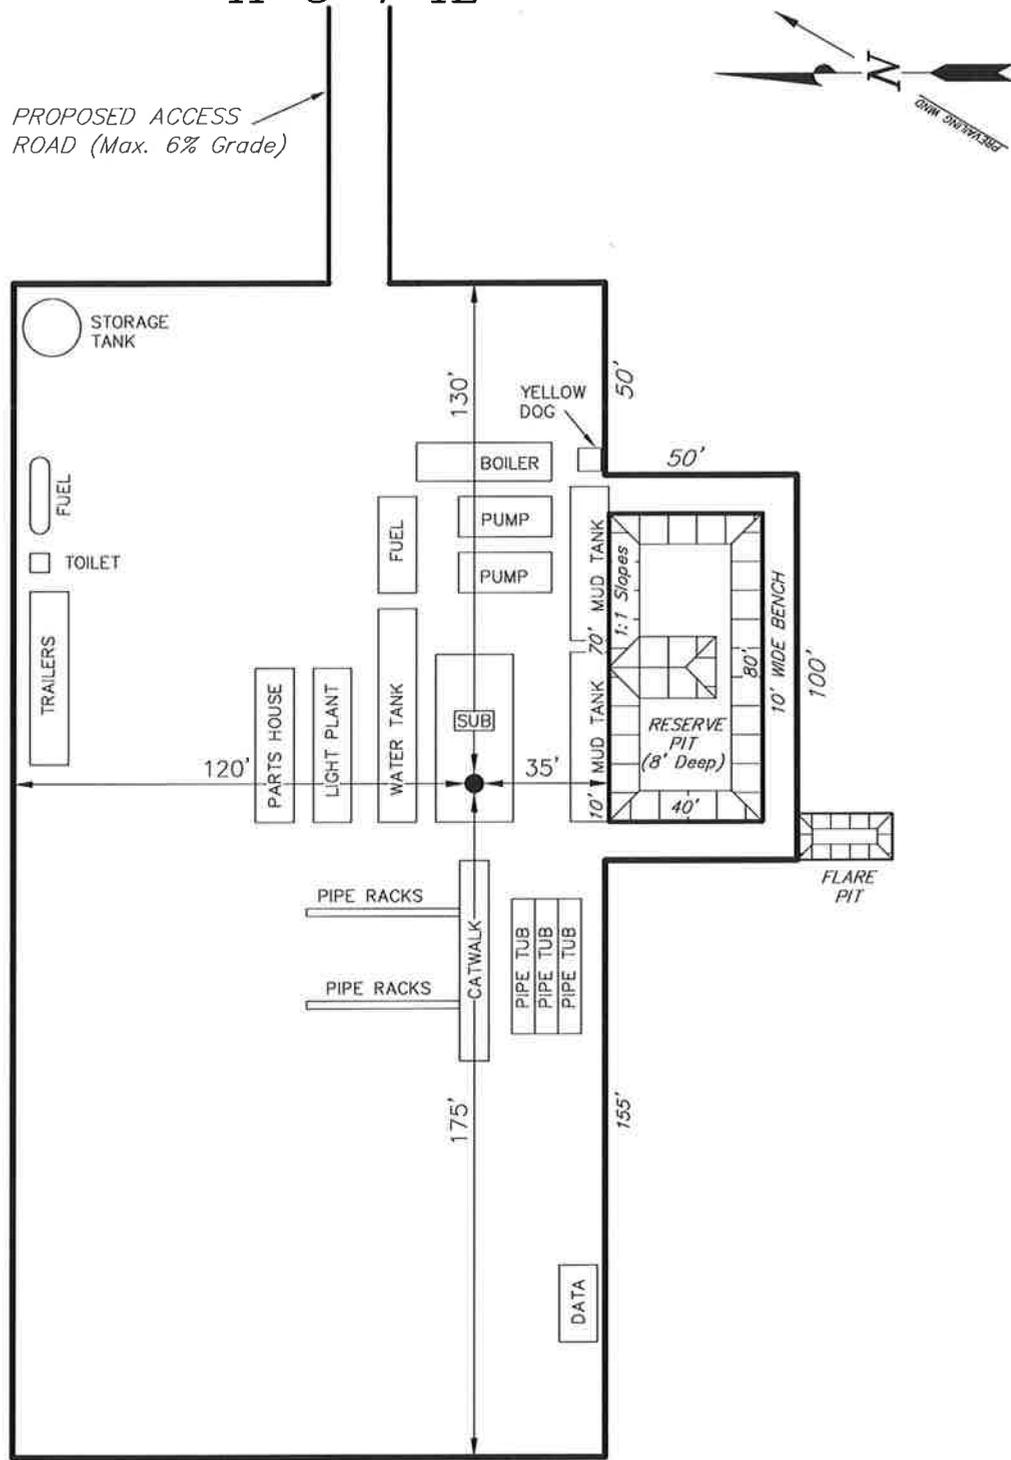

SURVEYED BY: T.P.	DATE SURVEYED: 01-07-10
DRAWN BY: M.W.	DATE DRAWN: 01-12-10
SCALE: 1" = 50'	REVISED:

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

Newfield Production Company Proposed Site Facility Diagram

Ute Tribal 11-3-4-1E

NE/SW Sec. 3, T4S, R1E

Uintah County, Utah

2OG0005609

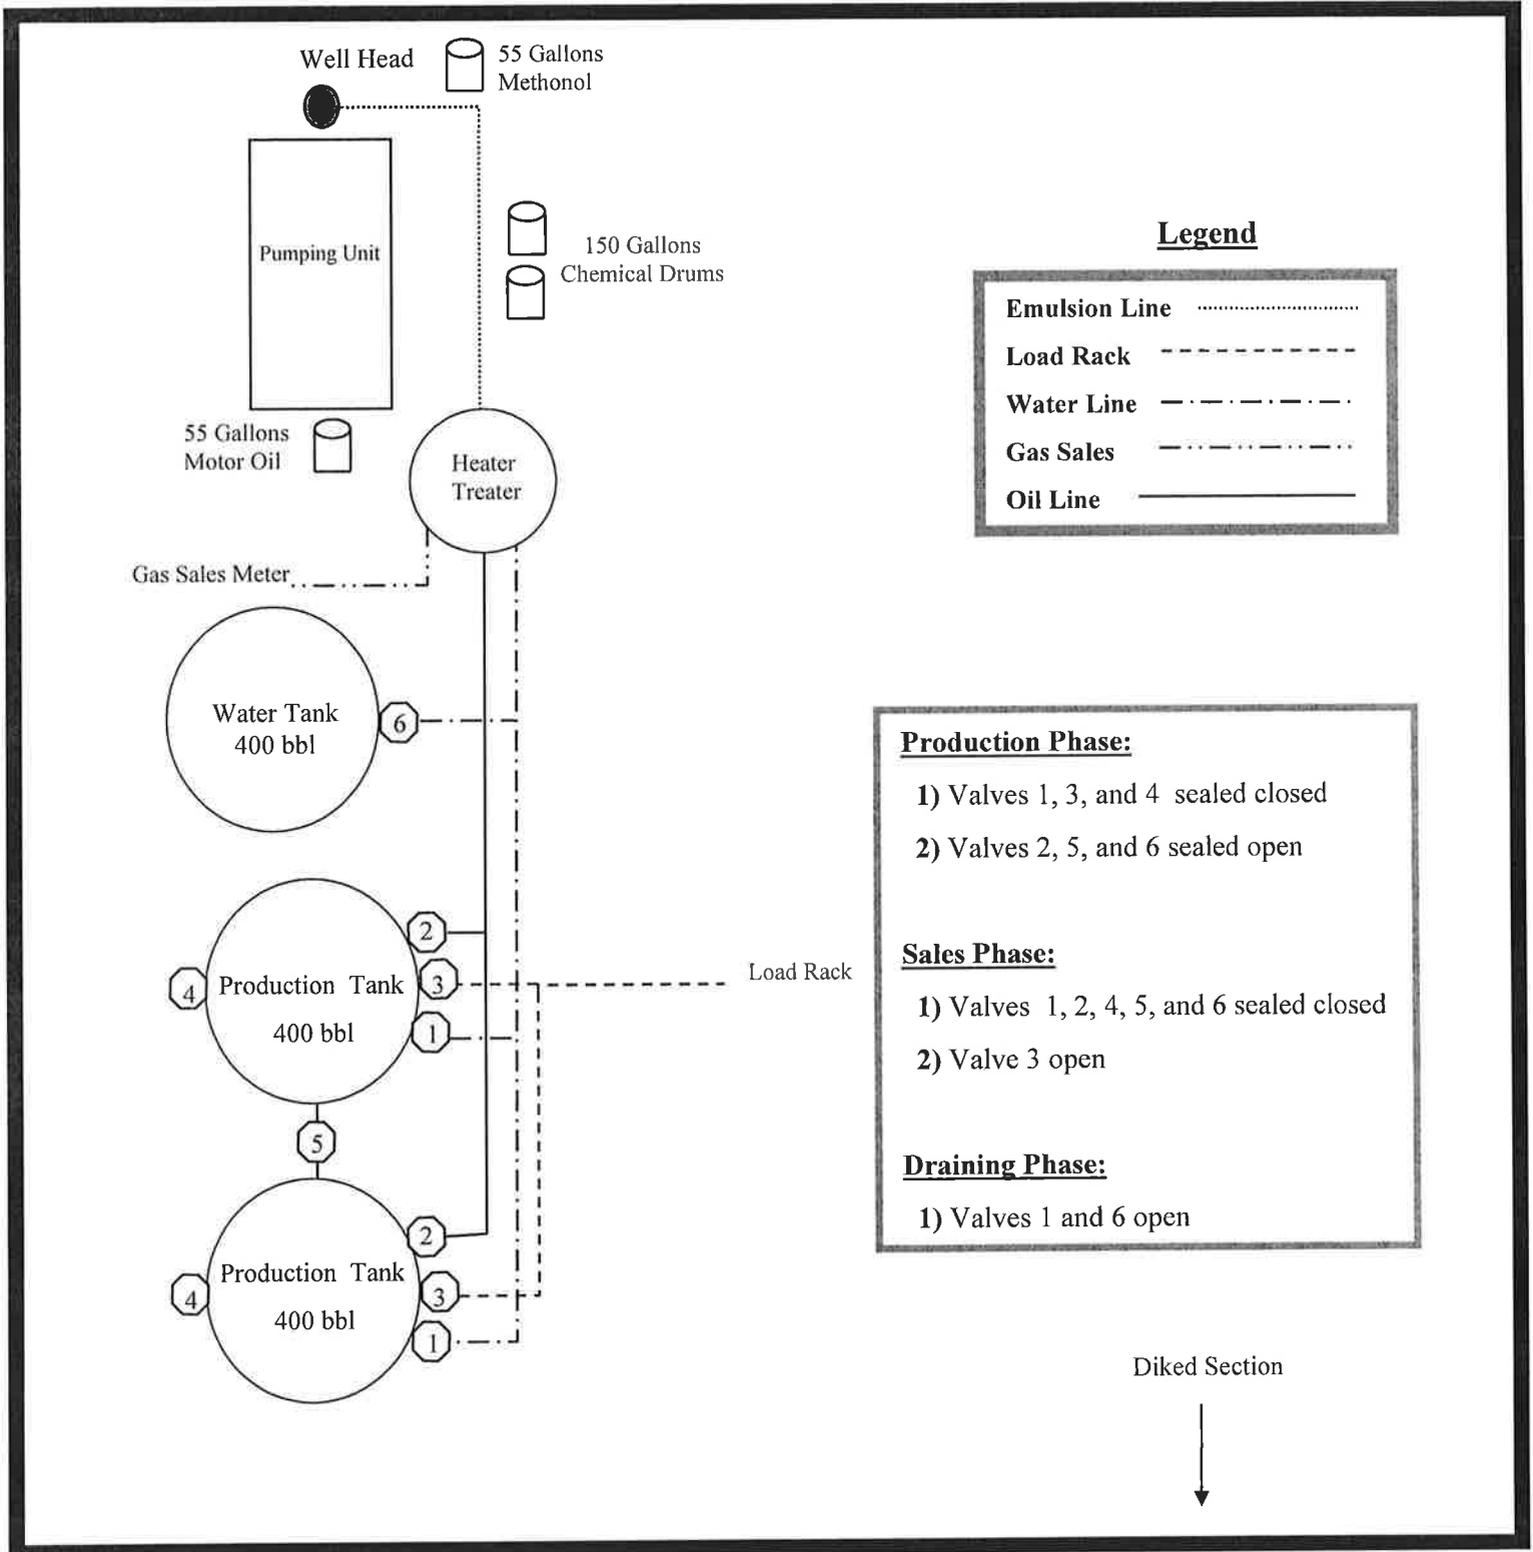


EXHIBIT D

Township 4 South, Range 1 East

Section 2

Section 3 S1/2

Uintah County, Utah


Being 960 acres, more or less and pertaining to the following wells:

1-2-4-1E (NENE – Sec. 2), 2-2-4-1E (NWNE – Sec. 2), 3-2-4-1E (NENW – Sec. 2),
4-2-4-1E (NWNW – Sec. 2), 5-2-4-1E (SWNW – Sec. 2), 6-2-4-1E (SENE – Sec. 2),
7-2-4-1E (SWNE – Sec. 2), 8-2-4-1E (SENE – Sec. 2), 9-2-4-1E (NESE – Sec. 2),
10-2-4-1E (NWSE – Sec. 2), 11-2-4-1E (NESW – Sec. 2), 12-2-4-1E (NWSW – Sec. 2),
13-2-4-1E (SWSW – Sec. 2), 14-2-4-1E (SESW – Sec. 2), 15-2-4-1E (SWSE – Sec. 2),
16-2-4-1E (SESE – Sec. 2), 9-3-4-1E (NESE – Sec. 3), 10-3-4-1E (NWSE – Sec. 3),
11-3-4-1E (NESW – Sec. 3), 12-3-4-1E (NWSW – Sec. 3), 13-3-4-1E (SWSW – Sec. 3),
14-3-4-1E (SESW – Sec. 3), 15-3-4-1E (SWSE – Sec. 3), 16-3-4-1E (SESE – Sec. 3).


ARCHAEOLOGICAL & PALEOTOLOGICAL REPORT WAIVER

For the above referenced location; Deep Creek Investments etal, Lee M. Smith, General Manager the Private Surface Owner whose address is 2400 Sunnyside Avenue, Salt Lake City, UT 84108. (Having a Surface Owner Agreement with Newfield Production Company)

Lee M. Smith, representing this entity does agree to waive the request from the State of Utah and Bureau of Land Management for an Archaeological/Cultural and Paleotological Resource Survey for any wells covered by the Surface Use Agreement dated 10/2/09 between the above said private land owner and Newfield Production. This waiver hereby releases Newfield Production Company from this request.


Lee M. Smith, General Manager Date
Deep Creek Investments, etal



Brad Mecham Date
Newfield Production Company

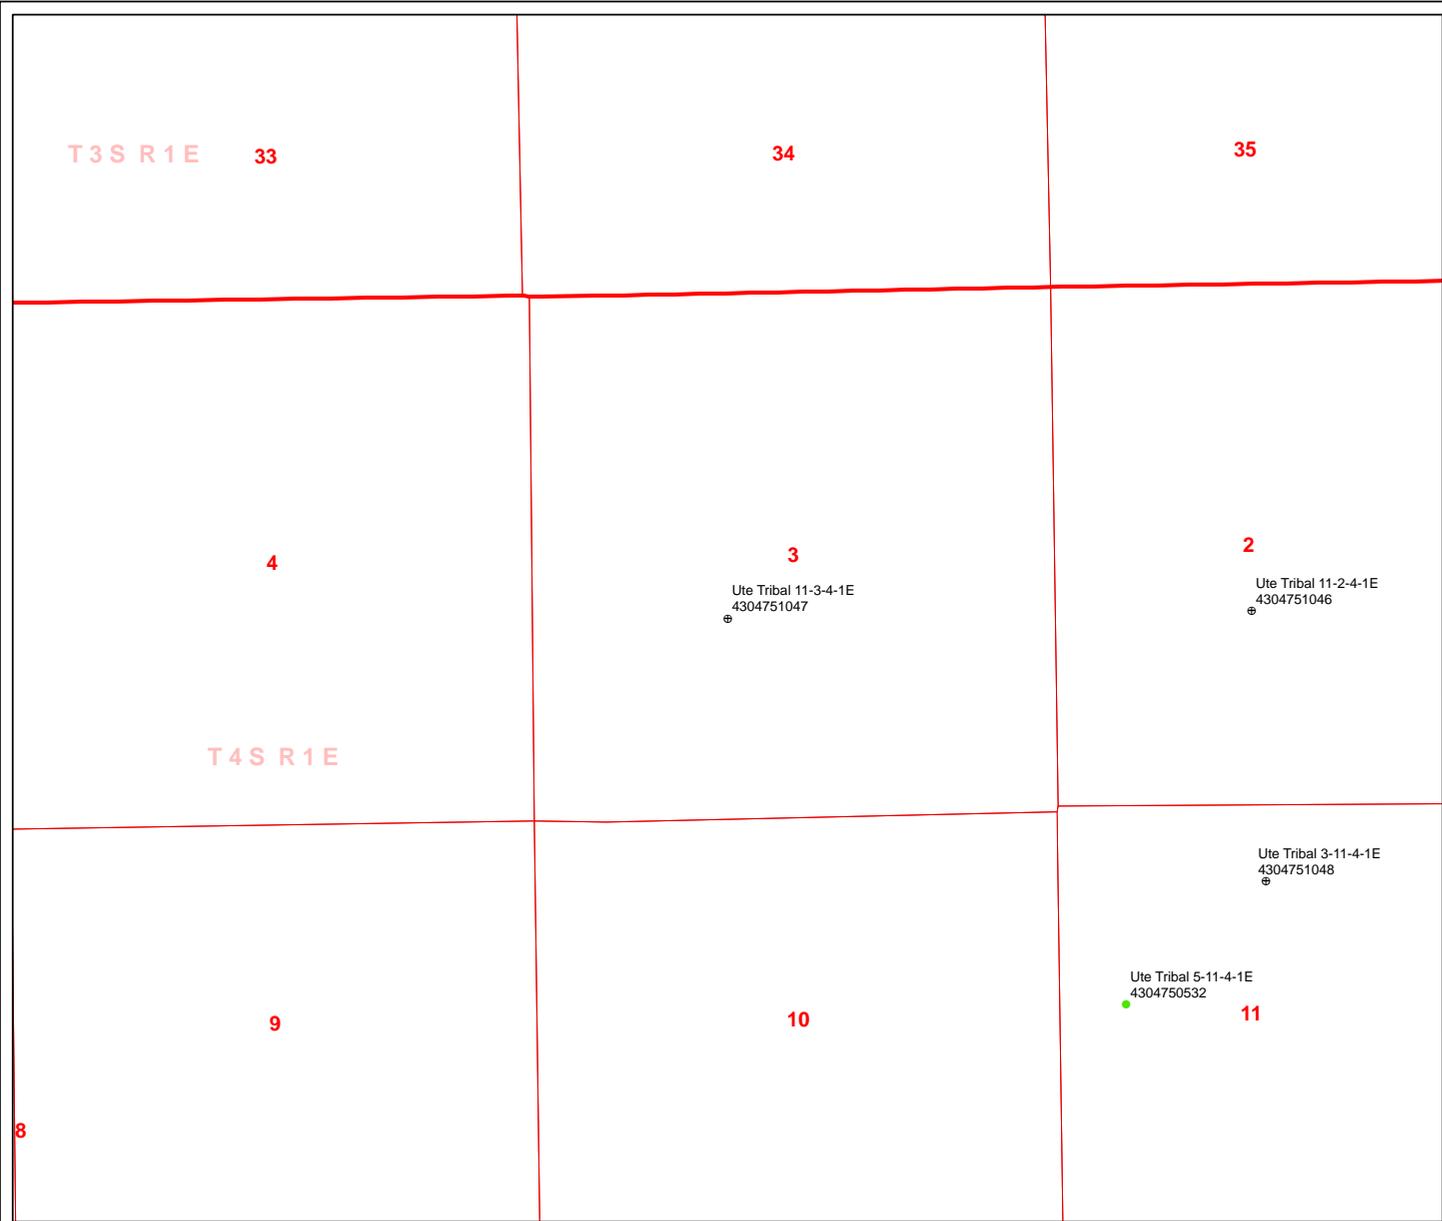

API Number: 4304751047
Well Name: Ute Tribal 11-3-4-1E
Township 04.0 S Range 01.0 E Section 3
Meridian: UBM
 Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
 Map Produced by Diana Mason

- | | |
|---------------|--------------------------------------|
| Units | Wells Query |
| STATUS | ✕ - call other values> |
| ACTIVE | Status |
| EXPLORATORY | ◆ APD - Approved Permit |
| GAS STORAGE | ⊙ DRL - Spudded (Drilling Commenced) |
| NF PP OIL | ⊙ GW - Gas Injection |
| NF SECONDARY | ⊙ GS - Gas Storage |
| PI OIL | ✕ LA - Location Abandoned |
| PP GAS | ⊕ LOC - New Location |
| PP GEOTHERMAL | ⊕ OPS - Operation Suspended |
| PP OIL | ⊕ PA - Plugged Abandoned |
| SECONDARY | ⊕ PGW - Producing Gas Well |
| TERMINATED | ● POW - Producing Oil Well |
| Fields | ⊙ RET - Returned APD |
| Sections | ⊕ SGW - Shut-in Gas Well |
| Township | ⊕ SOW - Shut-in Oil Well |
| | ⊕ TA - Temp. Abandoned |
| | ○ TW - Test Well |
| | ⊕ WDW - Water Disposal |
| | ⊕ WWI - Water Injection Well |
| | ● WSW - Water Supply Well |



ON-SITE PREDRILL EVALUATION

Utah Division of Oil, Gas and Mining

Operator NEWFIELD PRODUCTION COMPANY
Well Name Ute Tribal 11-3-4-1E
API Number 43047510470000 **APD No** 2538 **Field/Unit** WILDCAT
Location: 1/4,1/4 **NESW Sec 3 Tw 4.0S Rng 1.0E 1988 FSL 1986 FWL**
GPS Coord (UTM) 596796 4446210 **Surface Owner** Deep Creek Investments etal.

Participants

Floyd Bartlett (DOGM), Tim Eaton, (Newfield Production Co.), Dustin Gardiner (Tri-State Land Surveying) and Alan Smith (Deep Creek Investments).

Regional/Local Setting & Topography

The general area is on Leland Bench, which is located about 10 miles southwest of Fort Duchesne, Uintah County, Utah. Broad flats with low growing desert shrub type vegetation characterize the area. A few rolling hills and slopes leading to higher flats occur. No springs, seeps or flowing streams are known to occur in the area. The Duchesne River is approximately 6 miles to the east. All lands in the immediate are privately owned. Ute Tribal lands lie to the west and south.

Access to the proposed well site is by State Of Utah or Uintah County roads and existing or proposed oilfield development roads. Distance from Randlett, Utah is approximately 8.1 miles. Approximately 1,950 feet of low standard new road will be constructed to reach the location.

The proposed Ute Tribal 11-3-4-1E oil well is on a broad flat with a very slight slope to the east. No drainages intersect the location.

Surface Use Plan

Current Surface Use

Grazing
 Recreational
 Wildlife Habitat

New Road Miles	Well Pad	Src Const Material	Surface Formation
0.4	Width 204 Length 305	Onsite	UNTA

Ancillary Facilities N

Waste Management Plan Adequate?

Environmental Parameters

Affected Floodplains and/or Wetlands N

Flora / Fauna

Vegetation is a fair desert shrub-forb type. Main plants are horse-brush, broom snakeweed, bud sagebrush, black sagebrush, cheatgrass, curly mesquite grass, prickly pear, globe mallow, squirrel tail, halogeton and annual forbs.

Because of the lack of water and cover the area is not rich in fauna. Antelope, coyotes, prairie dogs and small mammals and rodents occur. Some shrub dependent birds may occur but were not observed. Historically, but not currently, sheep grazed the area.

Soils are a deep sandy loam with little rock.

Soil Type and Characteristics

Soils are a deep sandy loam with little rock.

Erosion Issues N

Sedimentation Issues N

Site Stability Issues N

Drainage Diverson Required? N

Berm Required? Y

Erosion Sedimentation Control Required? N

Paleo Survey Run? N **Paleo Potental Observed?** N **Cultural Survey Run?** N **Cultural Resources?**

Reserve Pit

Site-Specific Factors

Site Ranking

Distance to Groundwater (feet)	>200	0	
Distance to Surface Water (feet)	>1000	0	
Dist. Nearest Municipal Well (ft)	>5280	0	
Distance to Other Wells (feet)	>1320	0	
Native Soil Type	Mod permeability	10	
Fluid Type	Fresh Water	5	
Drill Cuttings	Normal Rock	0	
Annual Precipitation (inches)		0	
Affected Populations			
Presence Nearby Utility Conduits	Not Present	0	
	Final Score	15	2 Sensitivity Level

Characteristics / Requirements

A 40' x 80' x 8' deep reserve pit is planned in a cut on the southeast corner of the location. A liner with a minimum thickness of 16-mils is required. A sub-liner may not be needed because of the lack of rock in the area.

Closed Loop Mud Required? N **Liner Required?** Y **Liner Thickness** 16 **Pit Underlayment Required?** Y

Other Observations / Comments

ATV's were used to access the site. The weather was vvery cold and windy..

Floyd Bartlett
Evaluator

4/6/2010
Date / Time

Application for Permit to Drill Statement of Basis

4/21/2010

Utah Division of Oil, Gas and Mining

Page 1

APD No	API WellNo	Status	Well Type	Surf Owner	CBM
2538	43047510470000	LOCKED	OW	P	No
Operator	NEWFIELD PRODUCTION COMPANY		Surface Owner-APD	Deep Creek Investments etal.	
Well Name	Ute Tribal 11-3-4-1E		Unit		
Field	WILDCAT		Type of Work	DRILL	
Location	NESW 3 4S 1E U 1988 FSL 1986 FWL GPS Coord (UTM) 596186E 4446176N				

Geologic Statement of Basis

The mineral rights for the proposed well are owned by the Ute Tribe. The BLM will be the agency responsible for evaluating and approving the drilling, casing and cement programs.

Brad Hill
APD Evaluator

4/19/2010
Date / Time

Surface Statement of Basis

The general area is on Leland Bench, which is located about 10 miles southwest of Fort Duchesne, Uintah County, Utah. Broad flats with low growing desert shrub type vegetation characterize the area. A few rolling hills and slopes leading to higher flats occur. No springs, seeps or flowing streams are known to occur in the area. The Duchesne River is approximately 6 miles to the east. All lands in the immediate are privately owned. Ute Tribal lands lie to the west and south.

Access to the proposed well site is by State Of Utah or Uintah County roads and existing or proposed oilfield development roads. Distance from Randlett, Utah is approximately 8.1 miles. Approximately 1,950 feet of low standard new road will be constructed to reach the location.

The proposed Ute Tribal 11-3-4-1E oil well is on a broad flat with a very slight slope to the east. No drainages intersect the location. Lee Smith and Alan Smith of Deep Creek Investments privately own the surface. Mr. Lee Smith was contacted by telephone. He referred to Mr. Alan Smith who participated in the pre-site evaluation. A surface use agreement has been completed. The minerals are owned by the United States Government and held in trust for the Ute Indian Tribe. Mr. James Hereford of the BLM, who acts for the Ute Indian Tribe, was invited to the site visit both by telephone and email. He returned an email stating he would not attend but would schedule a separate pre-site with the landowner and Newfield Production once he was furnished the proper information as required by the Federal Onshore Order #1.

The location appears to be a good site for constructing a pad, drilling and operating a well.

Floyd Bartlett
Onsite Evaluator

4/6/2010
Date / Time

Conditions of Approval / Application for Permit to Drill

Category	Condition
Pits	A synthetic liner with a minimum thickness of 16 mils with a felt subliner shall be properly installed and maintained in the reserve pit.
Surface	The well site shall be bermed to prevent fluids from leaving the pad.
Surface	The reserve pit shall be fenced upon completion of drilling operations.

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 4/1/2010

API NO. ASSIGNED: 43047510470000

WELL NAME: Ute Tribal 11-3-4-1E

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: NESW 3 040S 010E

Permit Tech Review:

SURFACE: 1988 FSL 1986 FWL

Engineering Review:

BOTTOM: 1988 FSL 1986 FWL

Geology Review:

COUNTY: Uintah

LATITUDE: 40.16234

LONGITUDE: -109.87053

UTM SURF EASTINGS: 596186.00

NORTHINGS: 4446176.00

FIELD NAME: WILDCAT

LEASE TYPE: 2 - Indian

LEASE NUMBER: 20G0005609

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 4 - Fee

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: FEDERAL - WYB000493
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 43-7478
- RDCC Review: 2010-04-21 00:00:00.0
- Fee Surface Agreement
- Intent to Commingle


Commingle Approved

LOCATION AND SITING:

- R649-2-3.
- Unit:**
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
- Board Cause No:** R649-3-2
- Effective Date:**
- Siting:**
- R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations:
4 - Federal Approval - dmason
5 - Statement of Basis - bhll
21 - RDCC - dmason
23 - Spacing - dmason



State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Ute Tribal 11-3-4-1E
API Well Number: 43047510470000
Lease Number: 2OG0005609
Surface Owner: FEE (PRIVATE)
Approval Date: 5/3/2010

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of R649-3-2. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.

The Application for Permit to Drill has been forwarded to the Resource Development Coordinating Committee for review of this action. The operator will be required to comply with any applicable recommendations resulting from this review. (See attached)

Compliance with the Conditions of Approval/Application for Permit to Drill outlined in the Statement of Basis (copy attached).

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)

OR


submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <https://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:



Gil Hunt
Associate Director, Oil & Gas

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: 20G0005609
---	---

SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME:
--	--

1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: Ute Tribal 11-3-4-1E
------------------------------------	---

2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	9. API NUMBER: 43047510470000
--	---

3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext	9. FIELD and POOL or WILDCAT: WILDCAT
--	--	---

4. LOCATION OF WELL FOOTAGES AT SURFACE: 1988 FSL 1986 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESW Section: 3 Township: 04.0S Range: 01.0E Meridian: U	COUNTY: Uintah STATE: Utah
--	---

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 5/14/2010 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input checked="" type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: Confidential Status

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Newfield is requesting that this well be placed on confidential status.

Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
 May 18, 2010

NAME (PLEASE PRINT) Mandie Crozier	PHONE NUMBER 435 646-4825	TITLE Regulatory Tech
SIGNATURE N/A	DATE 5/14/2010	

BLM - Vernal Field Office - Notification Form

Spud

CONFIDENTIAL

Operator Newfield Exploration

Rig Name/# Ross #26

Submitted By Mitch Benson

Phone Number (435) 823-5885

Name/Numer UTE TRIBAL 11-3-4-1E

Qtr/Qrt NE/SW Section 3 Township 4S Range 1E

Lease Serial Number 2OG0005609

API Number 43-047-51047

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 7/13/2010 9:00:00 AM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate
- Production Casing
- Liner
- Other

Date/Time 7/13/2010 4:00:00 PM

Remarks:

STATE OF UTAH
 DIVISION OF OIL, GAS AND MINING
 ENTITY ACTION FORM -FORM 6

OPERATOR: NEWFIELD PRODUCTION COMPANY
 ADDRESS: RT. 3 BOX 3630
MYTON, UT 84052

OPERATOR ACCT. NO. N2695

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	17703	4304751046	UTE TRIBAL 11-2-4-1E	NESW	2	4S	1E	UINTAH	7/14/2010	7/26/10
WELL 1 COMMENTS: GRRV											
CONFIDENTIAL											
A	99999	17704	4304751047	UTE TRIBAL 11-3-4-1E	NESW	3	4S	1E	UINTAH	7/13/2010	7/26/10
GRRV											
CONFIDENTIAL											
A	99999	17705	4301350297	STEWART 15-20-4-2	SWSE	20	4S	2W	DUCHESNE	7/15/2010	7/26/10
GRRV											
A	99999	17706	4301350300	STEWART 2A-29-4-2	NWNE	29	4S	2W	DUCHESNE	7/13/2010	7/26/10
GRRV											
WELL 5 COMMENTS:											
WELL 5 COMMENTS:											

ACTION CODES (See Instructions on back of form)
 A - new entity for new well (single well only)
 B - well to existing entity (group or unit well)
 C - from one existing entity to another existing entity
 D - well from one existing entity to a new entity
 E - other (explain in comments section)

RECEIVED
JUL 19 2010

151
 Signature _____ Jentri Park
 Production Clerk
 Date 07/19/10

NOTE: Use COMMENT section to explain why each Action Code was selected.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
 NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
 Myton, UT 84052

3b. Phone (include area code)
 435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
 NESW Section 3 T4S R1E

5. Lease Serial No.
 MON BUTTE EDA 20G0005609

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.
 UTE TRIBAL 11-3-4-1E

9. API Well No.
 4304751047

10. Field and Pool, or Exploratory Area
 MYTON-TRIBAL EDA

11. County or Parish, State
 DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA


TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 7/13/2010 MIRU Ross # 26. Spud well @ 12:00 PM. Drill 350' of 12 1/4" hole with air mist. TIH W/ 8 Jt's 8 5/8" J-55 24 # csgn. Set @ 342.77'/KB On 7/20/2010 cement with 180 sks of class "G" w/ 3% CaCL2 + 1/4# sk Cello- Flake Mixed @ 15.8 ppg > 1.17 cf/ sk yeild. Returned 17.5 bbls cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Title
 Drilling Foreman

Signature


Date
 07/22/2010

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____
 Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title _____ Date _____
 Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

RECEIVED

(Instructions on page 2)

JUL 27 2010

DIV. OF OIL, GAS & MINING

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

CONFIDENTIAL

5. LEASE DESIGNATION AND SERIAL NUMBER:
MON BUTTE EDA 20G0005609

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

8. WELL NAME and NUMBER:
UTE TRIBAL 11-3-4-1E

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:
4304751047

3. ADDRESS OF OPERATOR:
Route 3 Box 3630 CITY Myton STATE UT ZIP 84052

PHONE NUMBER
435.646.3721

10. FIELD AND POOL, OR WILDCAT:
MYTON-TRIBAL EDA

4. LOCATION OF WELL:
FOOTAGES AT SURFACE:

COUNTY: DUCHESNE

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NESW, 3, T4S, R1E

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA


TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 08/25/2010	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
The above subject well was completed on 08-25-10, attached is a daily completion status report.

NAME (PLEASE PRINT) Lucy Chavez-Naupoto

TITLE Administrative Assistant

SIGNATURE



DATE 08/30/2010

(This space for State use only)

RECEIVED
SEP 07 2010
DIV. OF OIL, GAS & MINING

Daily Activity Report

Format For Sundry

UTE TRIBAL 11-3-4-1E

6/1/2010 To 10/30/2010

8/11/2010 Day: 1

Completion

Rigless on 8/11/2010 - Run CBL & perforate stage #1. - Install 5m frac head. NU 6" 5K Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head, csg & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 7887' & cement top @ 1050'. Perforate stage #1, BsCarb sds @ (7721'-23', 13'-15', 7662'-64', 54'-56', 44'-47', 31'-34', & 7614'-16') w/ 3 1/8" Port plug guns (11 gram .36" EH 16.82" pen) w/ 3 spf for total of 48 shots. RD H/O truck & The Perforators WLT & mast. Wait on frac crew

Daily Cost: \$0

Cumulative Cost: \$14,012

8/17/2010 Day: 2

Completion

Rigless on 8/17/2010 - Frac well - MIRU The Perforators WLT & crane. RU BJ Services frac equipment. Frac stg #1. Perf & frac stgs #2-7. EWTR 8151 BBLs. RD BJ. RD WLT & crane. RU flowback equipment. Open well to pit for flowback. Flowback well for 13 hrs to recover 2340 BBLs. EWTR 5811 BBLs

Daily Cost: \$0

Cumulative Cost: \$202,001

8/18/2010 Day: 3

Completion

Stone #8 on 8/18/2010 - MIRUSU Stone #8. Set kill plug. TIH w/ tbg for cleanout. - MIRUSU Stone #8. RU The Perforators WLT. Open well. CSG 800 psi. RIH w/ wireline to set kill plug @ 5900'. POOH w/ wireline. RD WLT. Bleed off well. ND Cameron BOP. Break out frac head. MU production. NU Schaffer BOP. RU workfloor. Prep & tally tbg. TIH picking up & drifting tbg. Tag kill plug @ 5900'. RU power swivel. SDFN

Daily Cost: \$0

Cumulative Cost: \$212,901

8/20/2010 Day: 4

Completion

Stone #8 on 8/20/2010 - Drill out plugs - Open well. TBG 1000 psi. CSG 800 psi. Ctch circulation. Drill out kill plug @ 5900'. Circulate well until to relieve pressure. Continue picking up tbg to tag next plug @ 6015'. Drill out plug. Continue picking up tbg to tag next plug @ 6550'. Drill out plug. Continue picking up tbg to tag next plug @ 6755'. Drill out plug. Continue picking up tbg to tag next plug @ 7194'. Drill out plug. Continue picking up tbg to tag next plug @ 7585'. While drilling plug. Lost circulation. Regain circulation. Circulate well clean. SDFN

Daily Cost: \$0

Cumulative Cost: \$218,671

8/23/2010 Day: 5

Completion

Stone #8 on 8/23/2010 - DU CBP. C/O to PBTD. Flow well. Kill well w/ 10# brine. POOH w/ tbg. LD BHA. RIH w/ partial production string. - Csg. @ 700 psi, tbg. @ 600 psi. Bleed off well.

RIH w/ tbg. Tag CBP @ 7575'. DU CBP in 28 min. Cont. RIH w/ tbg. Tag fill @ 7720'. C/O to PBTD @ 7935'. Circulate well clean. Pull up to 7839'. Flow well. Recovered 260 bbls water. Ending oil cut @ approx. 25%. No show of sand. Good show of gas. Kill tbg. w/ 10# brine. RIH w/ tbg. Tag fill @ 7930'. C/O to PBTD @ 7935'. Kill well w/ 175 bbls 10# brine. POOH w/ tbg. LD BHA. RIH w/ 2 7/8" notched collar, 2 jts 2 7/8" tbg., PSN, 1 jt 2 7/8" tbg., 5 1/2" TAC & 152 jts 2 7/8" tbg. SWIFN. 5590 BWTR.

Daily Cost: \$0

Cumulative Cost: \$277,509

8/24/2010 Day: 6

Completion

Stone #8 on 8/24/2010 - Round trip tbg. TAC would not set. Round trip tbg. - Csg. @ 800 psi, tbg. @ 1000 psi. Bleed off well. Kill well w/ 360 bbls 10# brine. ND BOP. TAC would not set. NU BOP. POOH w/ tbg. LD TAC. RIH w/ tbg. SWIFN.

Daily Cost: \$0

Cumulative Cost: \$283,099

8/25/2010 Day: 7

Completion

Stone #8 on 8/25/2010 - Kill well w/ 180 bbls brine. ND BOP. RIH w/ rods. RU pumping unit. Hang off rods. Stroke test to 800 psi. Good pump action. RD. Put well on production @ 5:00 p.m. 122" stroke length, 4 spm. Final Report. 5590 BWTR. - Csg. @ 450 psi, tbg. @ 300 psi. Bleed off well. Kill well w/ 180 bbl 10# brine. ND BOP. Set TAC @ 7692' w/ 18,000 tension. NU wellhead. X-over for rods. Flush tbg. w/ 50 bbls water. RIH w/ Central Hydraulic 2 1/2" x 1 1/2" x 20' x 24' RHAC rod pump, 6- 1 1/2" weight bars, 20- 3/4" guided rods, 165- 3/4" slick rods, 117- 7/8" guided rods, 1- 4', 2' x 7/8" pony subs, 1 1/2" x 30' polished rod. Seat pump. Fill tbg. w/ 2 bbls water. RU pumping unit. Stroke test to 800 psi. Good pump action. RD. Put well on production @ 5:00 p.m. 122" stroke length, 4 spm. Final Report. 5590 BWTR.

Finalized

Daily Cost: \$0

Cumulative Cost: \$328,611

Pertinent Files: Go to File List

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

CONFIDENTIAL

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. Type of Well Oil Well Gas Well Dry Other
 b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Resrv.,
 Other: _____

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

3. Address
1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
(435)646-3721

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

At surface 1988' FSL & 1986' FWL (NE/SW) SEC. 3, T4S, R1E

At top prod. interval reported below

At total depth 7962'

14. Date Spudded
07/13/2010

15. Date T.D. Reached
07/31/2010

16. Date Completed 08/24/2010
 D & A Ready to Prod.

5. Lease Serial No.
EDA 20G0005609

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.

8. Lease Name and Well No.
UTE TRIAL 11-3-4-1E

9. AFI Well No.
43-047-51047

10. Field and Pool or Exploratory
MYTON-TRIBAL EDA

11. Sec., T., R., M., on Block and
Survey or Area
SEC. 3, T4S, R1E

12. County or Parish
UINTAH

13. State
UT

17. Elevations (DF, RKB, RT, GL)*
5271' GL 5283' KB

18. Total Depth: MD 7962'
TVD

19. Plug Back T.D.: MD 7935'
TVD

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each) **MUD LOG**
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	343'		180 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	7957'		340 PRIMLITE		1050'	
NEW						425 50/50 POZ			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 7791'	TA @ 7692'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Green River			7614-7723' BsCarb	.36"	3	48
B) Green River			7438-7545' CPLime	.36"	3	51
C) Green River			7250-7368' CP1 2 3 4	.36"	3	36
D) Green River			6935-7133' BLS LBIKSHL	.36"	3	54

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
7614-7723'	Frac w/ 83789#'s 30/50 sand in 1950 bbls of slick water.
7438-7545'	Frac w/ 63331#'s 30/50 sand in 1487 bbls of slick water.
7250-7368'	Frac w/ 65357#'s 20/40 sand in 410 bbls of Lightning 17 fluid.
6935-7133'	Frac w/ 90559#'s 30/50 sand in 2060 bbls of slick water.

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
8-21-10	9-1-10	24	→	117	43	110			2-1/2" x 1-1/2" x 20' x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
2 7/8"			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

*(See instructions and spaces for additional data on page 2)

RECEIVED
SEP 22 2010

28b. Production - Interval C									
Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

28c. Production - Interval D									
Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD & USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):
 Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers
 GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
				GARDEN GULCH MRK GARDEN GULCH 1	5440' 5638'
				GARDEN GULCH 2 POINT 3	5773' 6104'
				X MRKR Y MRKR	6285' 6326'
				DOUGALS CREEK MRK BI CARBONATE MRK	6485' 6806'
				B LIMESTON MRK CASTLE PEAK	6966' 7208'
				BASAL CARBONATE WASATCH	7570' 7682'


32. Additional remarks (include plugging procedure):

Stage 5: Green River Formation (C & D3) 6621-6686', .36" 3/24 Frac w/ 20012#'s of 20/40 sand in 174 bbls of Lightning 17 fluid
 Stage 6: Green River Formation (DS3) 6462-6472', .36" 3/30 Frac w/ 45633#'s of 20/40 sand in 304 bbls of Lightning 17 fluid
 Stage 7: Green River Formation (GB6) 5946-5955', .36" 3/27 Frac w/ 47300#'s of 20/40 sand in 306 bbls of Lightning 17 fluid

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (I full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Lucy Chavez-Naupoto Title Administrative Assistant
 Signature  Date 09/17/2010

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Daily Activity Report

Format For Sundry

UTE TRIBAL 11-3-4-1E

5/1/2010 To 9/30/2010

UTE TRIBAL 11-3-4-1E

Waiting on Cement

Date: 7/20/2010

Ross #26 at 350. Days Since Spud - @ 15.8ppg and 1.17 yield , returned 17.5 bbls cement to pit, bump plug to 94 psi - Noify BLM, State and Ute tribe of spud, csg and cmt - On 7/13/10 spud @12:00 pm - Drill to 350' Pick up and run 8 jts 8 5/8" surface csg set @ 342.77' KB - On 7/20/10 CMT w/BJ 180 sks of class G cmt + 2% calcium chloride+ .25 # sk cello flake mixed

Daily Cost: \$0

Cumulative Cost: \$48,443

UTE TRIBAL 11-3-4-1E

Rigging down

Date: 7/25/2010

Capstar #329 at 350. 0 Days Since Spud - Prepare to move & repair brakes

Daily Cost: \$0

Cumulative Cost: \$48,793

UTE TRIBAL 11-3-4-1E

Drill 7 7/8" hole with fresh water

Date: 7/27/2010

Capstar #329 at 399. 1 Days Since Spud - collar 32.38, 1x2' hangoff sub, 8 drill collars 241.04'. Tag at 298'. - P/U BHA as follows Smith Mi616 7 7/8" PDC. 6.5 Hunting 7/8 lobe, 4.8 stage, 1.5° motor, Monel drill - Pressure test surface casing, to 1500 psi, for 30 minutes. All tested good. - choke manifold, upper. kelly cock, and safety valve to 2000 psi for 10 minutes. - Drill 7 7/8" hole from 298' to 399' with 20 klbs WOB, 155 total RPM, and 33.67 ft/hr avg ROP. - 24 hr notice sent to BLM and State via email on 7/25/2010 of rig move on 7/26/2010 at 6:00 PM and - BOP test on 7/26/2010. - On 7/26/2010 MIRU set equipment w/ Howcroft trucking. (30 mile move from 15-15-4-3) - Test directional tools. - Accept rig on 7/26/2010 at 20:00. R/U B&C Quicktest. pressure test casing rams, blind rams, annular, - Nipple up BOP

Daily Cost: \$0

Cumulative Cost: \$137,636

UTE TRIBAL 11-3-4-1E

Drill 7 7/8" hole with fresh water

Date: 7/28/2010

Capstar #329 at 4908. 2 Days Since Spud - Wait on directional driller - Drill 7 7/8" hole from 3420' to 4199' with 20 klbs WOB, 155 total RPM, and 222.57 ft/hr avg ROP. - Change out swivel control. - Drill 7 7/8" hole from 2884' to 3420' with 20 klbs WOB, 155 total RPM, and 153.14 ft/hr avg ROP. - Rig service - Drill 7 7/8" hole from 399' to 2884' with 20 klbs WOB, 155 total RPM, and 292.35 ft/hr avg ROP. - Drill 7 7/8" hole from 4199' to 4908' with 20 klbs WOB, 155 total RPM, and 101.29 ft/hr avg ROP.

Daily Cost: \$0

Cumulative Cost: \$159,170

UTE TRIBAL 11-3-4-1E

Drill 7 7/8" hole with salt water

Date: 7/29/2010

Capstar #329 at 6640. 3 Days Since Spud - Run wireline survey at 6481' 1.24°. - Work on Extreme MWD. MWD failure. Bring fluid weight up to a 9.4#/gal to kill well. - Drill 7 7/8" hole from 6511' to 6556' with 20 klbs WOB, 155 total RPM, and 150 ft/hr avg ROP. - were down - Drill 7 7/8" hole from 6556' to 6640' with 20 klbs WOB, 155 total RPM, and 56 ft/hr avg ROP.

- Drill 7 7/8" hole from 6148' to 6511' with 20 klbs WOB, 155 total RPM, and 103.71 ft/hr avg ROP. - Gas to surface. Circulate out through gas buster. Did not shut well in. (6148') - Rig service Function test BOP and Crown-o-matic - Drill 7 7/8" hole from 4908' to 6148' with 20 klbs WOB, 155 total RPM, and 124 ft/hr avg ROP. - Work on Extreme MWD. Tool failed could not get it to work again. Well flowing and kicking while pump

Daily Cost: \$0

Cumulative Cost: \$219,185

UTE TRIBAL 11-3-4-1E

Wait on Completion

Date: 7/30/2010

Capstar #329 at 7962. 5 Days Since Spud - Drill 7 7/8" hole from 6640' to 6874' with 20 klbs WOB, 155 total RPM, and 78 ft/hr avg ROP. - Survey at a depth of 6868'. 2.58° - Drill 7 7/8" hole from 6874' to 7372' with 20 klbs WOB, 155 total RPM, and 124.5 ft/hr avg ROP. - Survey at a depth of 7372'. 2.77° - Drill 7 7/8" hole from 7372' to 7418' with 20 klbs WOB, 155 total RPM, and 92 ft/hr avg ROP. - Rig service. Function test BOP and Crown-o-matic - Drill 7 7/8" hole from 7418' to 7962' (TD) with 20 klbs WOB, 155 total RPM, and 108.8 ft/hr avg ROP. - Circulate - Lay down pipe - Repair swivel motor - Continue to lay down DP and BHA - R/U Halliburton to log well - Log well. Tripple Combo suite. TD to 5000' 30'/hr. - Rig service - Change out hydraulic pump for front swivel motor - R/U and run 188 jts 5 1/2" 15.50# J-55 casing set at 7957'/kb. Tag @ 7945'. Wash down to 7957'. - Circulate - CMT w/BJ Pump 301 sks PL II +3% KCL +5#CSE+0.5#CF+2#KOL+.5SMS+FP+SF mixed @ 11ppg - yield @ 3.54 Then tail of 420 sk 50:50:2+3%KCL+0.5%EC-1+.25# SK CF+.05#SF+.3SMS+FP-6L - Mixed @ 14.4 ppg yeild @ 1.24. At 170bbbls of 189bbbls gone, during displacement, the formation - started to take fluid and we lost 1/2 of the returns. We returned no dyed spacers or cement. - Final displacement pressure was at 2230 psi. - Nipple down and set 5 1/2" slips w/ 147,000# tension. - Drill 7 7/8" hole from 6640' to 6874' with 20 klbs WOB, 155 total RPM, and 78 ft/hr avg ROP. - Survey at a depth of 6868'. 2.58° - Drill 7 7/8" hole from 6874' to 7372' with 20 klbs WOB, 155 total RPM, and 124.5 ft/hr avg ROP. - Survey at a depth of 7372'. 2.77° - Drill 7 7/8" hole from 7372' to 7418' with 20 klbs WOB, 155 total RPM, and 92 ft/hr avg ROP. - Rig service. Function test BOP and Crown-o-matic - Drill 7 7/8" hole from 7418' to 7962' (TD) with 20 klbs WOB, 155 total RPM, and 108.8 ft/hr avg ROP. - Circulate - Lay down pipe - Repair swivel motor - Continue to lay down DP and BHA - R/U Halliburton to log well - Log well. Tripple Combo suite. TD to 5000' 30'/hr. - Rig service - Change out hydraulic pump for front swivel motor - R/U and run 188 jts 5 1/2" 15.50# J-55 casing set at 7957'/kb. Tag @ 7945'. Wash down to 7957'. - Circulate - CMT w/BJ Pump 301 sks PL II +3% KCL +5#CSE+0.5#CF+2#KOL+.5SMS+FP+SF mixed @ 11ppg - yield @ 3.54 Then tail of 420 sk 50:50:2+3%KCL+0.5%EC-1+.25# SK CF+.05#SF+.3SMS+FP-6L - Mixed @ 14.4 ppg yeild @ 1.24. At 170bbbls of 189bbbls gone, during displacement, the formation - started to take fluid and we lost 1/2 of the returns. We returned no dyed spacers or cement. - Final displacement pressure was at 2230 psi. - Nipple down and set 5 1/2" slips w/ 147,000# tension.

Daily Cost: \$0

Cumulative Cost: \$413,380

UTE TRIBAL 11-3-4-1E

Wait on Completion

Date: 7/31/2010

Capstar #329 at 7962. 6 Days Since Spud - Clean mud tanks. Release rig at 10:00 AM 7/31/2010 **Finalized**

Daily Cost: \$0

Cumulative Cost: \$415,810

Pertinent Files: Go to File List
