

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS AND MINING						FORM 3 AMENDED REPORT <input type="checkbox"/>	
APPLICATION FOR PERMIT TO DRILL						1. WELL NAME and NUMBER Ute Tribal 3-10-4-1E	
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT WILDCAT	
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO						5. UNIT or COMMUNITIZATION AGREEMENT NAME	
6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY						7. OPERATOR PHONE 435 646-4825	
8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052						9. OPERATOR E-MAIL mcrozier@newfield.com	
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) 20G0005609			11. MINERAL OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input checked="" type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input checked="" type="checkbox"/>	
13. NAME OF SURFACE OWNER (if box 12 = 'fee') Coleman Brothers LTD						14. SURFACE OWNER PHONE (if box 12 = 'fee')	
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee') Multiple addresses, ,						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')	
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>			19. SLANT VERTICAL <input checked="" type="checkbox"/> DIRECTIONAL <input type="checkbox"/> HORIZONTAL <input type="checkbox"/>	
20. LOCATION OF WELL	FOOTAGES	QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN	
LOCATION AT SURFACE	551 FNL 1828 FWL	NENW	10	4.0 S	1.0 E	U	
Top of Uppermost Producing Zone	551 FNL 1828 FWL	NENW	10	4.0 S	1.0 E	U	
At Total Depth	551 FNL 1828 FWL	NENW	10	4.0 S	1.0 E	U	
21. COUNTY UINTAH			22. DISTANCE TO NEAREST LEASE LINE (Feet) 551			23. NUMBER OF ACRES IN DRILLING UNIT 40	
			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 1320			26. PROPOSED DEPTH MD: 7830 TVD: 7830	
27. ELEVATION - GROUND LEVEL 5264			28. BOND NUMBER RLB0010462			29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 437478	
ATTACHMENTS							
VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES							
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER				<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN			
<input checked="" type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)				<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER			
<input type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)				<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP			
NAME Mandie Crozier			TITLE Regulatory Tech			PHONE 435 646-4825	
SIGNATURE			DATE 09/28/2010			EMAIL mcrozier@newfield.com	
API NUMBER ASSIGNED 43047512900000			APPROVAL			 Permit Manager	

Proposed Hole, Casing, and Cement						
String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Prod	7.875	5.5	0	7830		
Pipe	Grade	Length	Weight			
	Grade J-55 LT&C	7830	15.5			

Proposed Hole, Casing, and Cement						
String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Surf	12.25	8.625	0	300		
Pipe	Grade	Length	Weight			
	Grade J-55 ST&C	300	24.0			

NEWFIELD PRODUCTION COMPANY
UTE TRIBAL 3-10-4-1E
NE/NW SECTION 10, T4S, R1E
UINTAH COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0' -- 2,695'
Green River	2,695'
Wasatch	7,555'
Proposed TD	7,830'

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil) 2,695' – 7,555'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sampled Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO ₃) (mg/l)
Dissolved Bicarbonate (NaHCO ₃) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO ₄) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: Ute Tribal 3-10-4-1E**

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950	1,370	244,000
						17.53	14.35	33.89
Prod casing 5-1/2"	0'	7,830'	15.5	J-55	LTC	4,810	4,040	217,000
						1.93	1.62	1.79

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg
 Pore pressure at surface casing shoe = 8.33 ppg
 Pore pressure at prod casing shoe = 8.33 ppg
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: Ute Tribal 3-10-4-1E**

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft ³ /sk)
			ft ³			
Surface casing	300'	Class G w/ 2% CaCl	138	30%	15.8	1.17
			161			
Prod casing Lead	5,830'	Prem Lite II w/ 10% gel + 3% KCl	403	30%	11.0	3.26
			1313			
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363	30%	14.3	1.24
			451			

- *Actual volume pumped will be 15% over the caliper log
- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
 - Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:
The BOP and related equipment shall meet the minimum requirements of Onshore Oil and Gas Order No. 2 for equipment and testing requirements, procedures, etc., for a **2M** system, and individual components shall be operable as designed. Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ±350 feet will be drilled with an air/mist system. The air rig is equipped with a 6 ½" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ±350 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.



10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the first quarter of 2011, and take approximately seven (7) days from spud to rig release.

T4S, R1E, U.S.B.&M.

NEWFIELD EXPLORATION COMPANY


WELL LOCATION, 3-10-4-1E, LOCATED AS SHOWN IN THE NE 1/4 NW 1/4 OF SECTION 10, T4S, R1E, U.S.B.&M. UTAH COUNTY, UTAH.

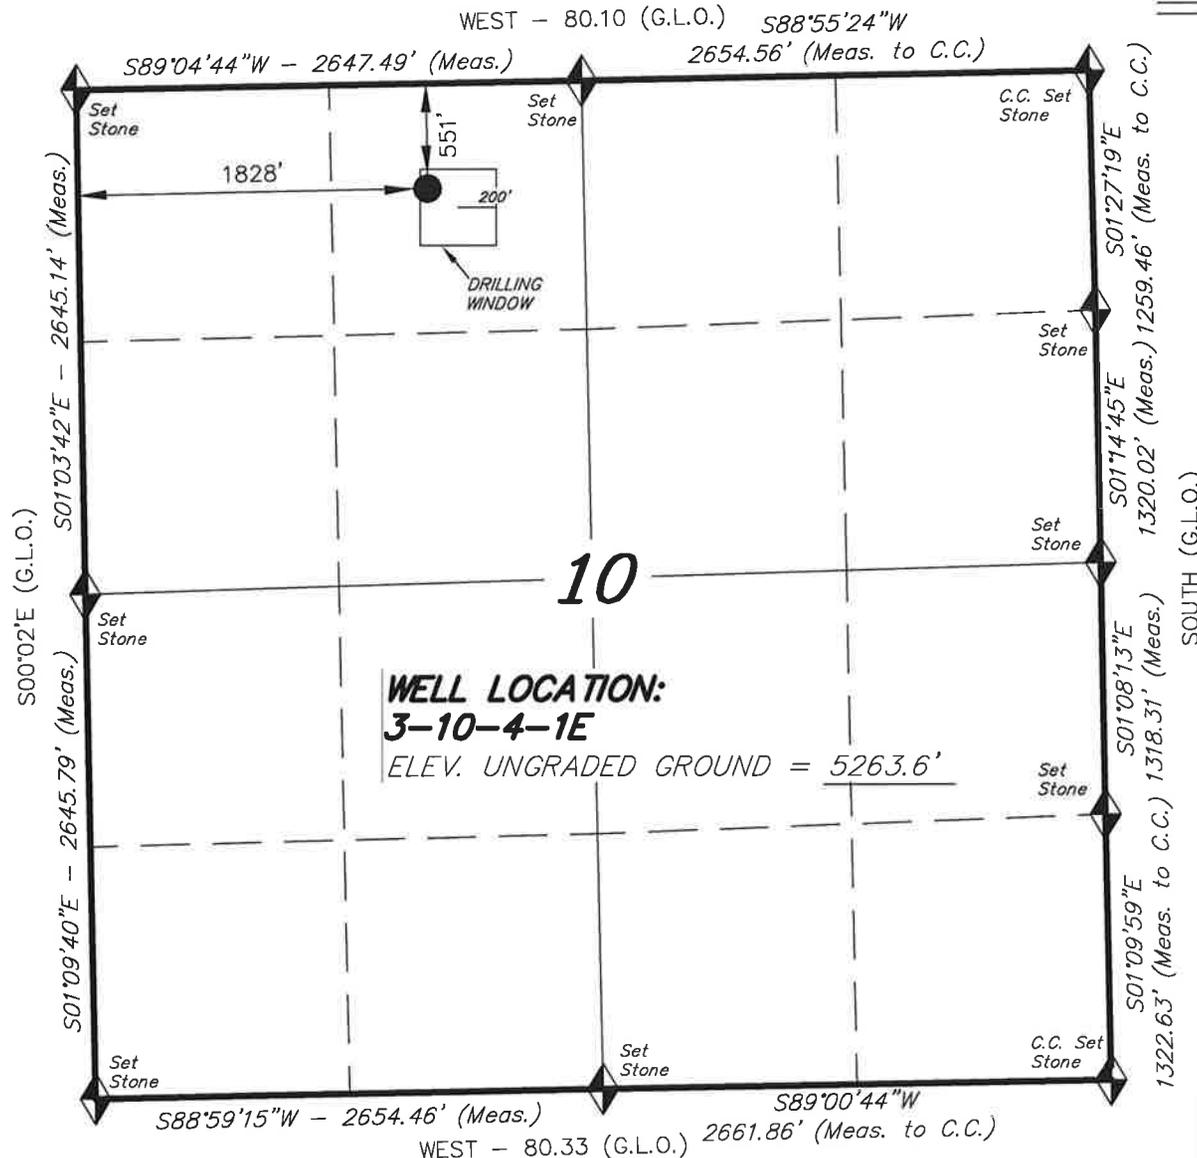

NOTES:

1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.

THIS IS TO CERTIFY THAT THE ABOVE PLOT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF. 189377



◆ = SECTION CORNERS LOCATED


BASIS OF ELEV; Elevations are base on LOCATION: an N.G.S. OPUS Correction. LAT. $40^{\circ}04'09.56''$ LONG. $110^{\circ}00'43.28''$ (Tristate Aluminum Cap) Elev. 5281.57'

3-10-4-1E
(Surface Location) NAD 83
LATITUDE = $40^{\circ}09'19.09''$
LONGITUDE = $109^{\circ}52'18.66''$

TRI STATE LAND SURVEYING & CONSULTING
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

DATE SURVEYED: 09-06-10	SURVEYED BY: D.G.
DATE DRAWN: 09-10-10	DRAWN BY: M.W.
REVISED:	SCALE: 1" = 1000'

Access Road Map

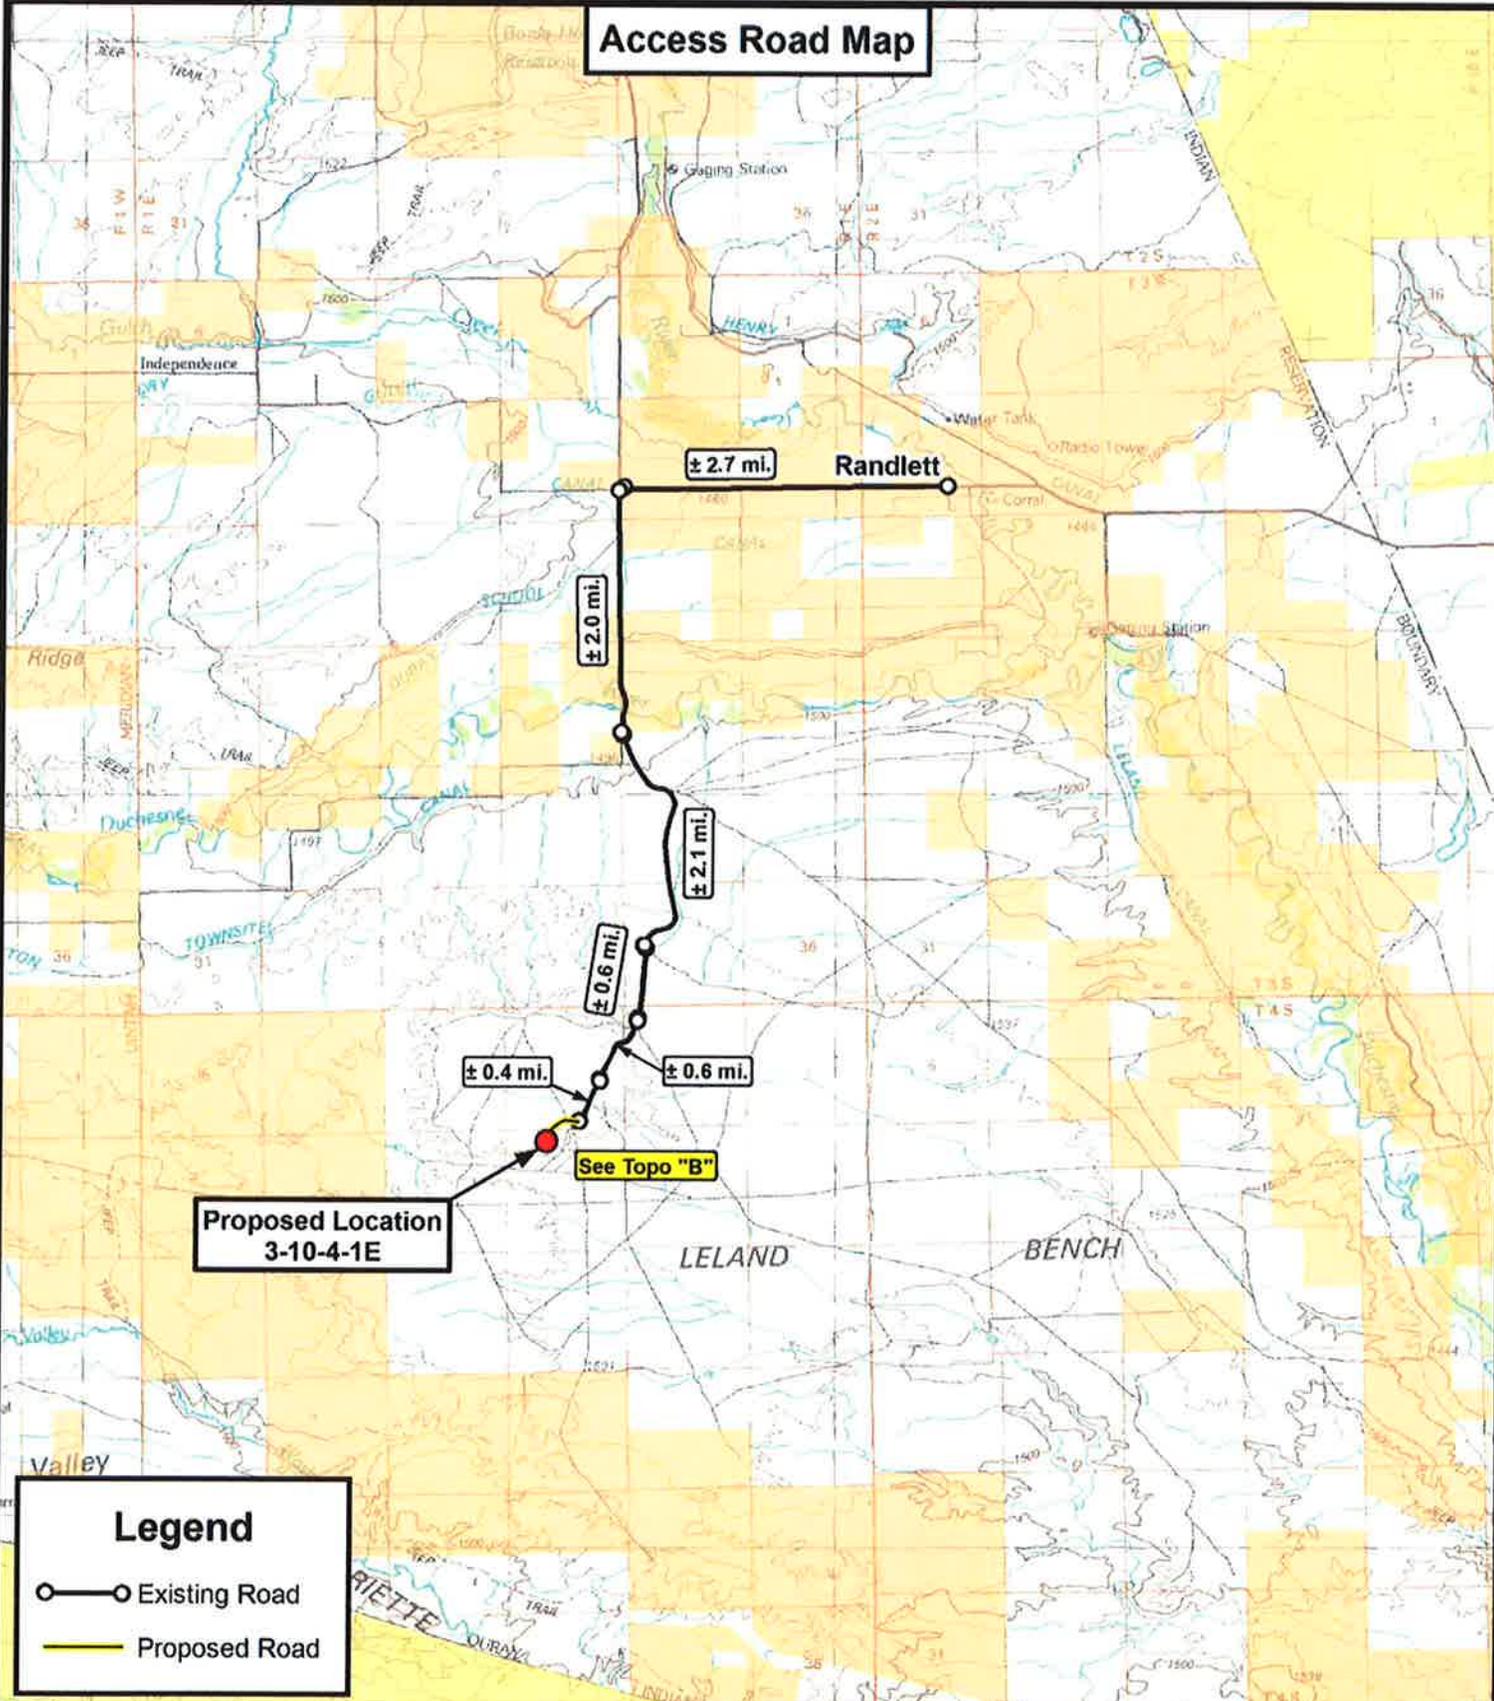

**Proposed Location
3-10-4-1E**

Legend

- Existing Road
- Proposed Road

**Tri State
Land Surveying, Inc.**
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY


**3-10-4-1E
SEC. 10, T4S, R1E, U.S.B.&M.
Uintah County, UT.**

DRAWN BY:	C.H.M.
DATE:	09-13-2010
SCALE:	1:100,000

TOPOGRAPHIC MAP

SHEET
A

Access Road Map

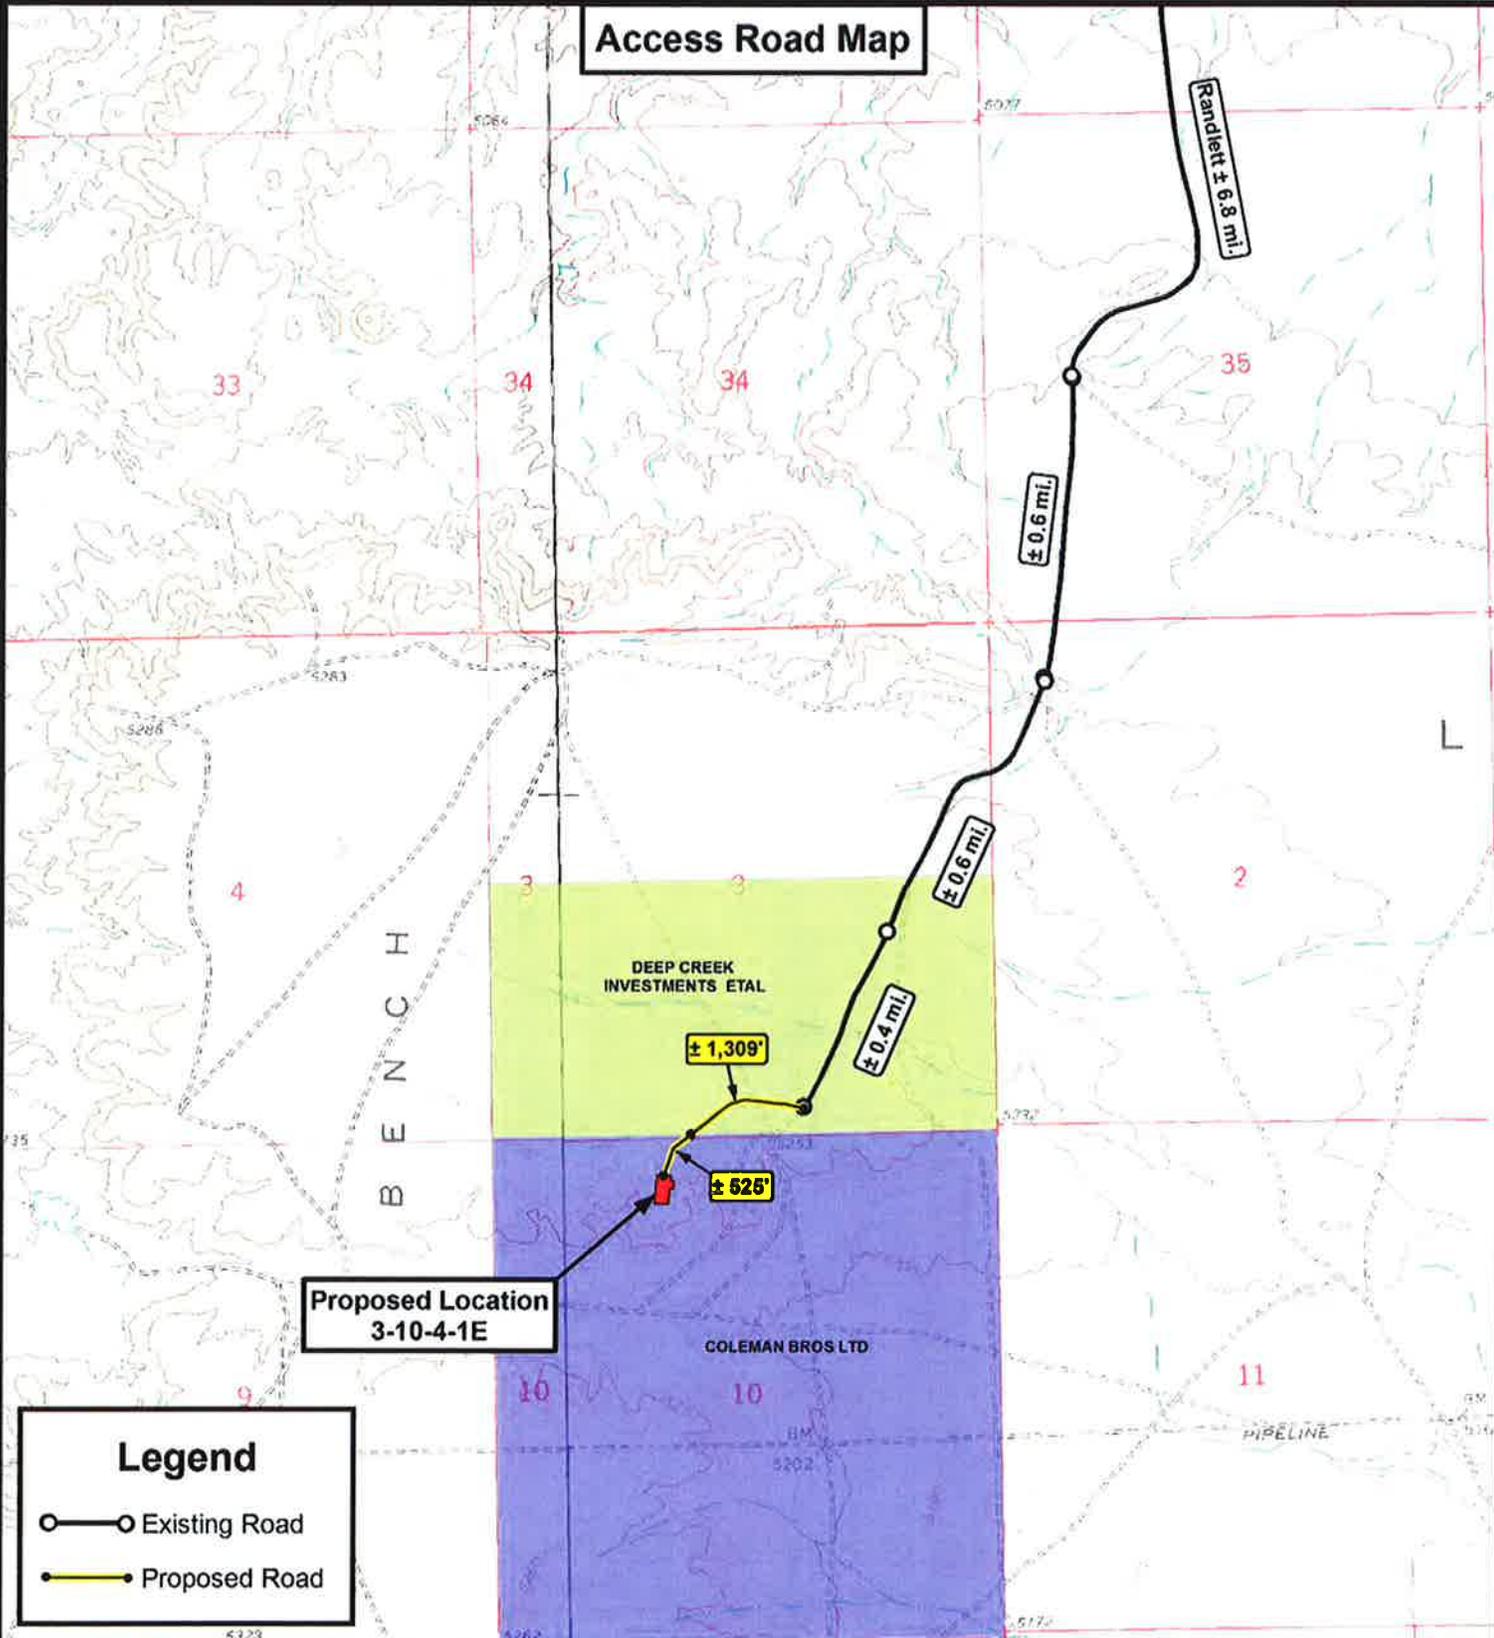

Legend

- Existing Road
- Proposed Road

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



**Tri State
Land Surveying, Inc.**
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY


**3-10-4-1E
SEC. 10, T4S, R1E, U.S.B.&M.
Uintah County, UT.**

DRAWN BY:	C.H.M.
DATE:	09-13-2010
SCALE:	1" = 2,000'

TOPOGRAPHIC MAP

SHEET
B

Proposed Pipeline Map

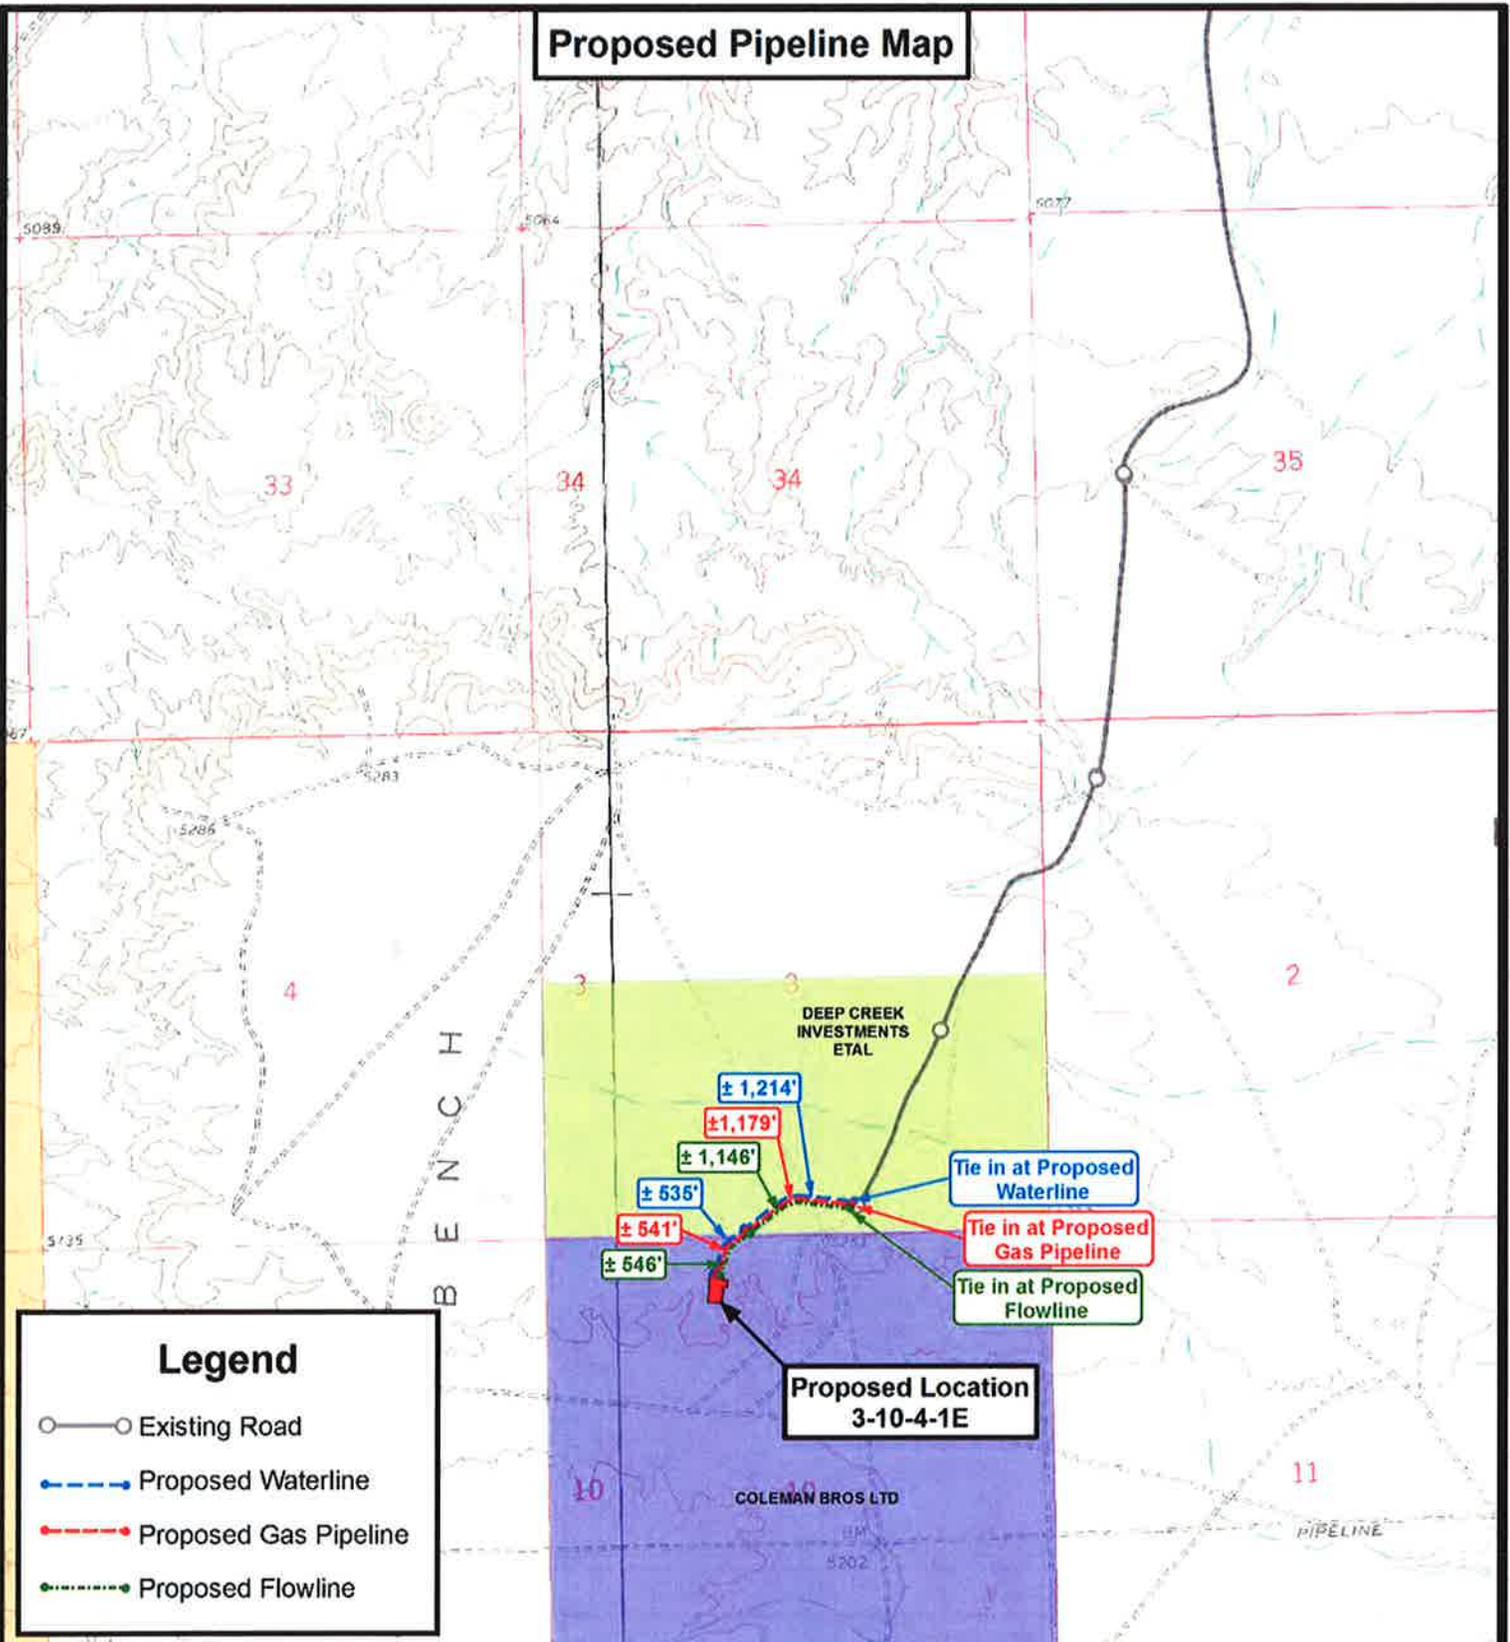

Legend

- Existing Road
- Proposed Waterline
- Proposed Gas Pipeline
- Proposed Flowline

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



Tri State Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

3-10-4-1E
SEC. 10, T4S, R1E, U.S.B.&M.
Uintah County, UT.

DRAWN BY:	C.H.M.
DATE:	09-13-2010
SCALE:	1" = 2,000'

TOPOGRAPHIC MAP

SHEET **C**


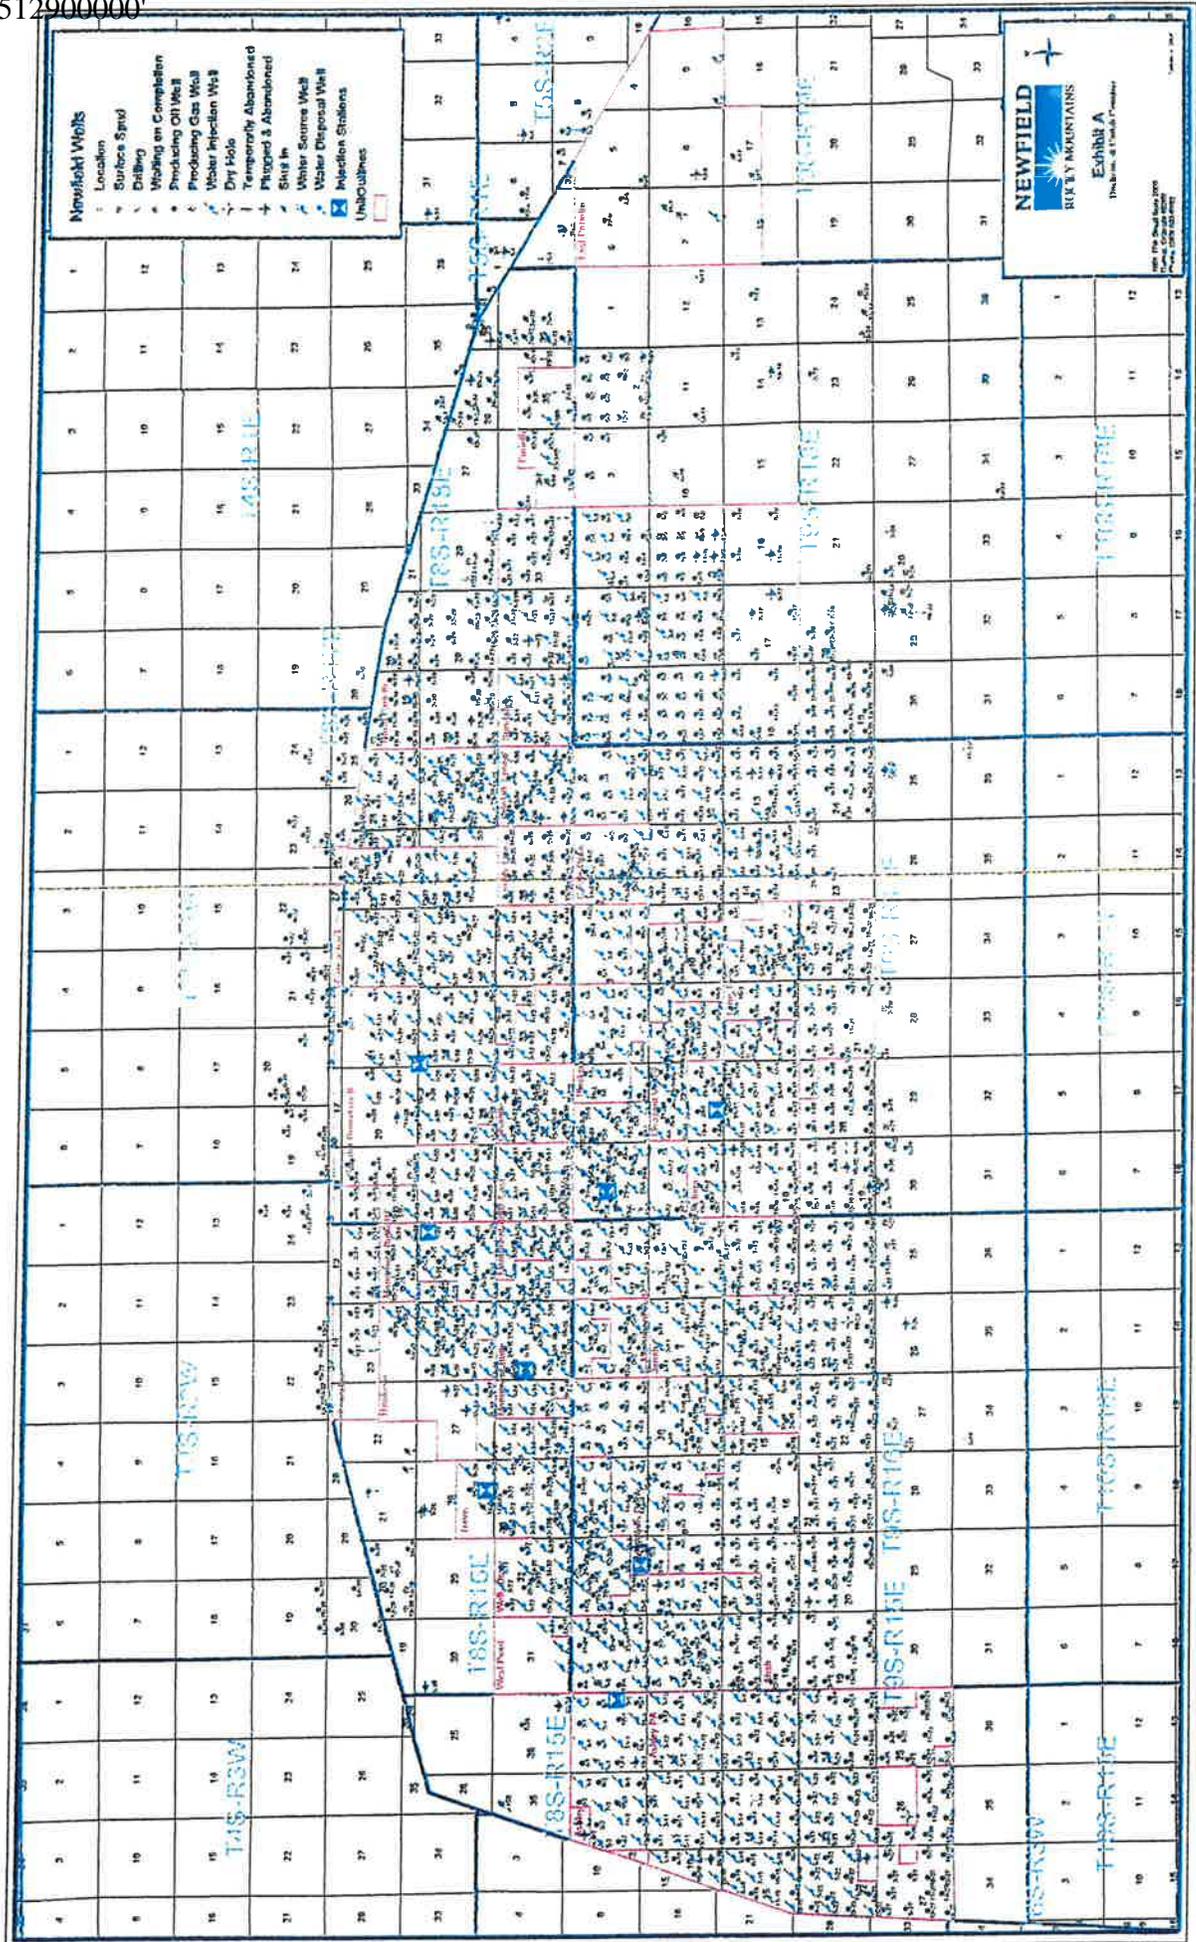


Exhibit "B" Map

**Proposed Location
3-10-4-1E**

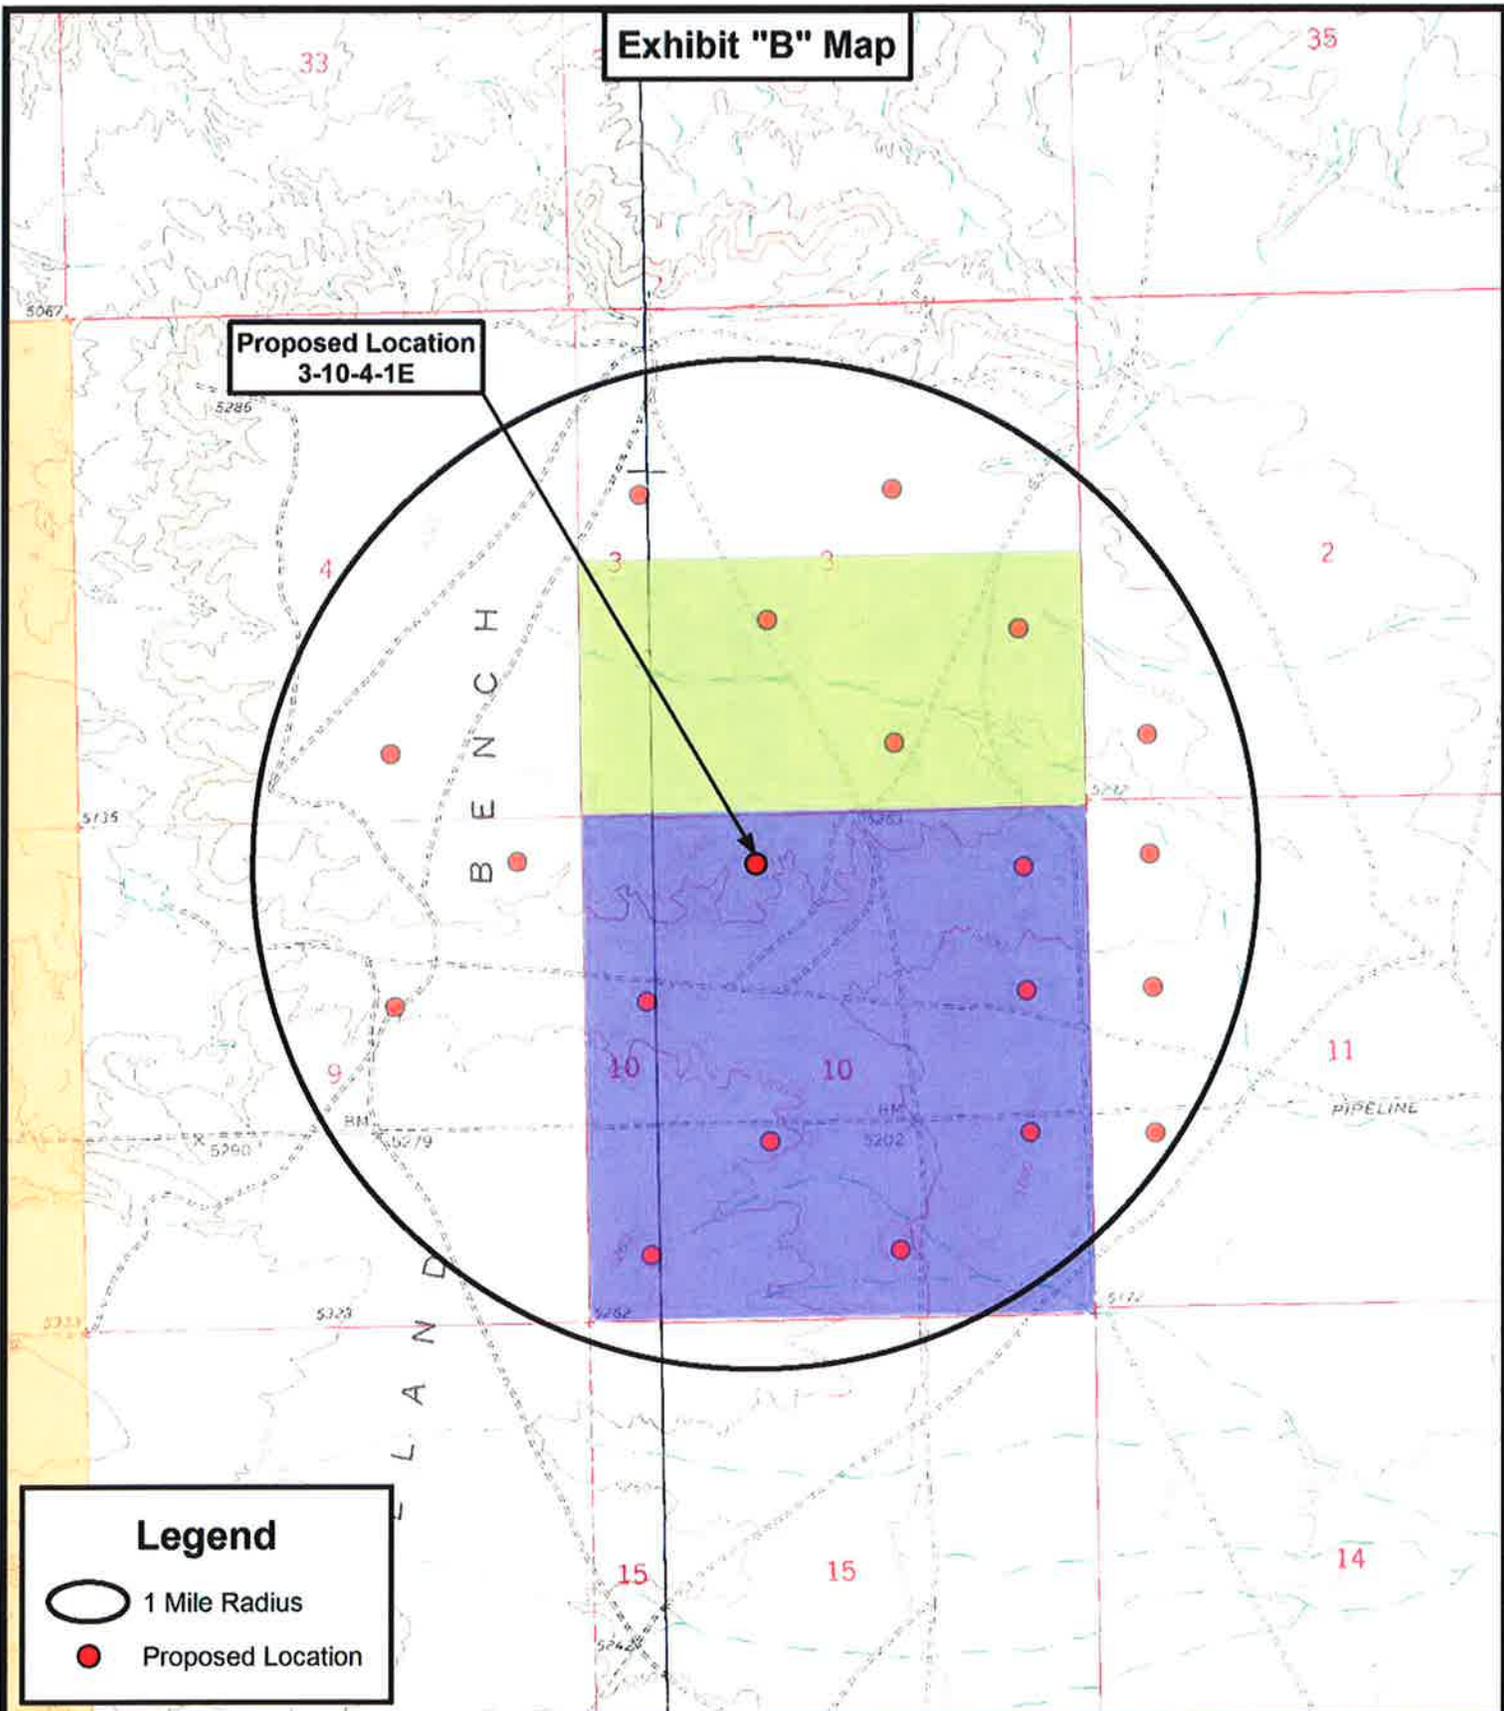

Legend

- 1 Mile Radius
- Proposed Location

Tri State
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

3-10-4-1E
SEC. 10, T4S, R1E, U.S.B.&M.
Uintah County, UT.

DRAWN BY:	C.H.M.
DATE:	09-13-2010
SCALE:	1" = 2,000'

TOPOGRAPHIC MAP

SHEET **D**

3-10-41E

**MEMORANDUM
of
EASEMENT, RIGHT-OF-WAY
and
SURFACE USE AGREEMENT**

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 9th day of June, 2010 by and between **Coleman Brothers LTD; Bonnie Coleman whose address is 148 West Center St, Heber City, UT. 84032**, ("Surface Owner," whether one or more) and Newfield Production Company, a Texas corporation ("NEWFIELD"), with offices at 1001 Seventeenth Street, Suite 2000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Uintah County, Utah described as follows:

Township 4 South, Range 1 East, Uintah Special Base and Meridian

Section 1: All, being 640 acres more or less.
Section 3: N1/2, being 320 acres more or less.
Section 4 All, being 640 acres more or less.
Section 9: All, being 640 acres more or less.
Section 10: All, being 640 acres more or less.
Section 11: S1/2, being 320 acres more or less.
Section 12: S1/2, being 320 acres more or less.
Section 13: All, being 640 acres more or less.
Section 14: All, being 640 acres more or less.
Section 15: S1/2, being 320 acres more or less.
Section 16: All, being 640 acres more or less.
Section 23: N1/2, being 320 acres more or less.
Section 24: All, being 640 acres more or less.

Township 4 South, Range 2 East, Uintah Special Base and Meridian

Section 7: NE1/4; E1/2 NW1/4; LOTS 1 AND 2, being 319 acres more or less.
Section 8: S1/2, being 320 acres more or less.
Section 17: LOTS 6 AND 7; E1/2 SW1/4; SE1/4, being 347 acres more or less.
Section 18: All, being 640 acres more or less
Section 19: All, being 640 acres more or less.
Section 20: All, being 640 acres more or less.
Section 29: All, being 640 acres more or less.
Section 32: N1/2; N1/2S1/2; LOTS 1,2,3, and 4, being 648 acres more or less.
Section 33: All, being 640 acres more or less.

Township 3 South, Range 1 East, Uintah Special Base and Meridian

Section 29: LOTS 1 AND 2, being 79.24 acres more or less.
Section 32: All, being 640 acres more or less.
Section 33: All, being 638 acres more or less.

Uintah County, Utah

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

I. Compensation for Well; Release of All Claims

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated June 9, 2010, as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

**MEMORANDUM
of
EASEMENT, RIGHT-OF-WAY
and
SURFACE USE AGREEMENT**

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 9th day of June, 2010 by and between **Coleman Brothers LTD; Joe Coleman whose address is 393 East Center St, Heber City, UT. 84032**, ("Surface Owner," whether one or more) and Newfield Production Company, a Texas corporation ("NEWFIELD"), with offices at 1001 Seventeenth Street, Suite 2000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Uintah County, Utah described as follows:

Township 4 South, Range 1 East, Uintah Special Base and Meridian

Section 1: All, being 640 acres more or less.
Section 3: N1/2, being 320 acres more or less.
Section 4 All, being 640 acres more or less.
Section 9: All, being 640 acres more or less.
Section 10: All, being 640 acres more or less.
Section 11: S1/2, being 320 acres more or less.
Section 12: S1/2, being 320 acres more or less.
Section 13: All, being 640 acres more or less.
Section 14: All, being 640 acres more or less.
Section 15: S1/2, being 320 acres more or less.
Section 16: All, being 640 acres more or less.
Section 23: N1/2, being 320 acres more or less.
Section 24: All, being 640 acres more or less.

Township 4 South, Range 2 East, Uintah Special Base and Meridian

Section 7: NE1/4; E1/2 NW1/4; LOTS 1 AND 2, being 319 acres more or less.
Section 8: S1/2, being 320 acres more or less.
Section 17: LOTS 6 AND 7; E1/2 SW1/4; SE1/4, being 347 acres more or less.
Section 18: All, being 640 acres more or less
Section 19: All, being 640 acres more or less.
Section 20: All, being 640 acres more or less.
Section 29: All, being 640 acres more or less.
Section 32: N1/2; N1/2S1/2; LOTS 1,2,3, and 4, being 648 acres more or less.
Section 33: All, being 640 acres more or less.

Township 3 South, Range 1 East, Uintah Special Base and Meridian

Section 29: LOTS 1 AND 2, being 79.24 acres more or less.
Section 32: All, being 640 acres more or less.
Section 33: All, being 638 acres more or less.

Uintah County, Utah

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

1. **Compensation for Well; Release of All Claims**

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated June 9, 2010, as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

2. Grant of Right of Way and Easement

Surface Owner hereby grants, bargains, leases, assigns, and conveys to NEWFIELD an easement and right-of-way for the purpose of construction, using and maintaining access roads, locations for surface equipment and subsurface gathering lines for each well drilled upon the Lands, pipelines, and pipeline interconnections for two years from date of this agreement and so long thereafter as NEWFIELD's oil and gas leases remain in effect.

This Agreement shall be binding upon the respective heirs, executors, administrators, successors, and assigns of the undersigned.

These Parties hereto have executed this document effective as of the day first above written.

COLEMAN BROTHERS LTD

NEWFIELD PRODUCTION COMPANY

By: Joe Coleman
Joe Coleman (general partner)
private surface owner

By: _____
Dan Shewmake,
Vice President-Development


STATE OF UTAH)
)ss
COUNTY OF Wasatch)

This instrument was acknowledged before me this 9th day of June, 2010 by **Coleman Bothers LTD, Joe Coleman, (general partner). private surface owner.**

Witness my hand and official seal.

My commission expires 9/8/2013

Tim Eaton
Notary Public



STATE OF COLORADO)
)ss
COUNTY OF Denver)

This instrument was acknowledged before me this _____, 2010 by **Dan Shewmake, Vice President-Development** a Texas corporation, on behalf of the corporation.

Witness my hand and official seal.

Notary Public

My commission expires _____

**MEMORANDUM
of
EASEMENT, RIGHT-OF-WAY
and
SURFACE USE AGREEMENT**

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 5th day of June, 2010 by and between **Coleman Brothers LTD; Mary Jo Coleman Adamson whose address is PO Box 610 Roosevelt, UT. 84066**, ("Surface Owner," whether one or more) and Newfield Production Company, a Texas corporation ("NEWFIELD"), with offices at 1001 Seventeenth Street, Suite 2000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Uintah County, Utah described as follows:

Township 4 South, Range 1 East, Uintah Special Base and Meridian

Section 1: All, being 640 acres more or less.
Section 3: N1/2, being 320 acres more or less.
Section 4 All, being 640 acres more or less.
Section 9: All, being 640 acres more or less.
Section 10: All, being 640 acres more or less.
Section 11: S1/2, being 320 acres more or less.
Section 12: S1/2, being 320 acres more or less.
Section 13: All, being 640 acres more or less.
Section 14: All, being 640 acres more or less.
Section 15: S1/2, being 320 acres more or less.
Section 16: All, being 640 acres more or less.
Section 23: N1/2, being 320 acres more or less.
Section 24: All, being 640 acres more or less.

Township 4 South, Range 2 East, Uintah Special Base and Meridian

Section 7: NE1/4; E1/2 NW1/4; LOTS 1 AND 2, being 319 acres more or less.
Section 8: S1/2, being 320 acres more or less.
Section 17: LOTS 6 AND 7; E1/2 SW1/4; SE1/4, being 347 acres more or less.
Section 18: All, being 640 acres more or less
Section 19: All, being 640 acres more or less.
Section 20: All, being 640 acres more or less.
Section 29: All, being 640 acres more or less.
Section 32: N1/2; N1/2S1/2; LOTS 1,2,3, and 4, being 648 acres more or less.
Section 33: All, being 640 acres more or less.

Township 3 South, Range 1 East, Uintah Special Base and Meridian

Section 29: LOTS 1 AND 2, being 79.24 acres more or less.
Section 32: All, being 640 acres more or less.
Section 33: All, being 638 acres more or less.

Uintah County, Utah

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

1. **Compensation for Well; Release of All Claims**

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated June 5, 2010, as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

2. Grant of Right of Way and Easement

Surface Owner hereby grants, bargains, leases, assigns, and conveys to NEWFIELD an easement and right-of-way for the purpose of construction, using and maintaining access roads, locations for surface equipment and subsurface gathering lines for each well drilled upon the Lands, pipelines, and pipeline interconnections for two years from date of this agreement and so long thereafter as NEWFIELD's oil and gas leases remain in effect.

This Agreement shall be binding upon the respective heirs, executors, administrators, successors, and assigns of the undersigned.

These Parties hereto have executed this document effective as of the day first above written.

COLEMAN BROTHERS LTD

NEWFIELD PRODUCTION COMPANY

By: Mary Jo Coleman Adamson
Mary Jo Coleman Adamson (general partner)
private surface owner

By: _____
Dan Shewmake,
Vice President-Development


STATE OF UTAH)
)ss
COUNTY OF Duchesne)

This instrument was acknowledged before me this 11th day of June, 2010 by **Coleman Bothers LTD, Mary Jo Coleman Adamson, (general partner). private surface owner.**

Witness my hand and official seal.

My commission expires 9/8/2013

[Signature]
Notary Public



STATE OF COLORADO)
)ss
COUNTY OF Denver)

This instrument was acknowledged before me this _____, 2010 by **Dan Shewmake, Vice President-Development** a Texas corporation, on behalf of the corporation.

Witness my hand and official seal.

Notary Public

My commission expires _____

**MEMORANDUM
of
EASEMENT, RIGHT-OF-WAY
and
SURFACE USE AGREEMENT**

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 17th day of June, 2010 by and between **Coleman Brothers LTD; Leila Coleman by whose address is 2390 South Doverway, St George, UT. 84770**, ("Surface Owner," whether one or more) and Newfield Production Company, a Texas corporation ("NEWFIELD"), with offices at 1001 Seventeenth Street, Suite 2000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Uintah County, Utah described as follows:

Township 4 South, Range 1 East, Uintah Special Base and Meridian

Section 1: All, being 640 acres more or less.
Section 3: N1/2, being 320 acres more or less.
Section 4 All, being 640 acres more or less.
Section 9: All, being 640 acres more or less.
Section 10: All, being 640 acres more or less.
Section 11: S1/2, being 320 acres more or less.
Section 12: S1/2, being 320 acres more or less.
Section 13: All, being 640 acres more or less.
Section 14: All, being 640 acres more or less.
Section 15: S1/2, being 320 acres more or less.
Section 16: All, being 640 acres more or less.
Section 23: N1/2, being 320 acres more or less.
Section 24: All, being 640 acres more or less.

Township 4 South, Range 2 East, Uintah Special Base and Meridian

Section 7: NE1/4; E1/2 NW1/4; LOTS 1 AND 2, being 319 acres more or less.
Section 8: S1/2, being 320 acres more or less.
Section 17: LOTS 6 AND 7; E1/2 SW1/4; SE1/4, being 347 acres more or less.
Section 18: All, being 640 acres more or less
Section 19: All, being 640 acres more or less.
Section 20: All, being 640 acres more or less.
Section 29: All, being 640 acres more or less.
Section 32: N1/2; N1/2S1/2; LOTS 1,2,3, and 4, being 648 acres more or less.
Section 33: All, being 640 acres more or less.

Township 3 South, Range 1 East, Uintah Special Base and Meridian

Section 29: LOTS 1 AND 2, being 79.24 acres more or less.
Section 32: All, being 640 acres more or less.
Section 33: All, being 638 acres more or less.

Uintah County, Utah

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

1. **Compensation for Well; Release of All Claims**

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated June 17, 2010, as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

3-10-4-1E
(Access + pipelines)

MEMORANDUM
of
EASEMENT, RIGHT-OF-WAY
and
SURFACE USE AGREEMENT

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 2nd day of October, 2009 by and between **Deep Creek Investments etal, Lee M. Smith, General Manager** whose address is **2400 Sunnyside Avenue, Salt Lake City, UT 84108**, ("Surface Owner," whether one or more) and **Newfield Production Company**, a Texas corporation ("NEWFIELD"), with offices at 1001 17th Street, Suite 2000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Uintah County, Utah described as follows:

Township 4 South, Range 1 East
Section 2
Section 3 S1/2

Uintah County, Utah
Being 960 acres, more or less and pertaining to the following wells:

- 1-2-4-1E (NENE – Sec. 2), 2-2-4-1E (NWNE – Sec. 2), 3-2-4-1E (NENW – Sec. 2),
- 4-2-4-1E (NWNW – Sec. 2), 5-2-4-1E (SWNW – Sec. 2), 6-2-4-1E (SENE – Sec. 2),
- 7-2-4-1E (SWNE – Sec. 2), 8-2-4-1E (SENE – Sec. 2), 9-2-4-1E (NESE – Sec. 2),
- 10-2-4-1E (NWSE – Sec. 2), 11-2-4-1E (NESW – Sec. 2), 12-2-4-1E (NWSW – Sec. 2),
- 13-2-4-1E (SWSW – Sec. 2), 14-2-4-1E (SESW – Sec. 2), 15-2-4-1E (SWSE – Sec. 2),
- 16-2-4-1E (SESE – Sec. 2), 9-3-4-1E (NESE – Sec. 3), 10-3-4-1E (NWSE – Sec. 3),
- 11-3-4-1E (NESW – Sec. 3), 12-3-4-1E (NWSW – Sec. 3), 13-3-4-1E (SWSW – Sec. 3),
- 14-3-4-1E (SESW – Sec. 3), 15-3-4-1E (SWSE – Sec. 3), 16-3-4-1E (SESE – Sec. 3).

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

1. Compensation for Well; Release of All Claims

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated October 2nd, 2009 as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

2. Grant of Right of Way and Easement

Surface Owner hereby grants, bargains, leases, assigns, and conveys to NEWFIELD an easement and right-of-way for the purpose of construction, using and maintaining access roads, locations for surface equipment and subsurface gathering lines for each well drilled upon the Lands, pipelines, and pipeline interconnections for two years from date of this agreement and so long thereafter as NEWFIELD's oil and gas leases remain in effect.

This Agreement shall be binding upon the respective heirs, executors, administrators, successors, and assigns of the undersigned. This agreement replaces and supersedes any and all prior agreements covering the lands described herein.

These Parties hereto have executed this document effective as of the day first above written.

SURFACE OWNER

NEWFIELD PRODUCTION COMPANY

By: 
Lee M. Smith, General Manager
Deep Creek Investments, etal

By: _____
Daniel W. Shewmake
Vice President – Development


STATE OF UTAH)
)ss
COUNTY OF Salt Lake)

This instrument was acknowledged before me this 2nd day of October, 2009 by Lee M. Smith, Deep Creek Investments, etal, General Manager.

Witness my hand and official seal.

My commission expires 9/8/2013

Tim Eaton
Notary Public



STATE OF COLORADO)
)ss
COUNTY OF DENVER)

This instrument was acknowledged before me this _____, 2009 by **Daniel W. Shewmake, as Vice President - Development of Newfield Production Company**, a Texas corporation, on behalf of the corporation.

Witness my hand and official seal.

Notary Public

My commission expires _____

NEWFIELD PRODUCTION COMPANY
UTE TRIBAL 3-10-4-1E
NE/NW SECTION 10, T4S, R1E
UINTAH COUNTY, UTAH

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Ute Tribal 3-10-4-1E located in the NE 1/4 NW 1/4 Section 10, T4S, R1E, Uintah County, Utah:

Proceed in a westerly direction out of Randlett, approximately 2.7 miles to it's junction with an existing road to the south; proceed in a southerly direction approximately 5.7 miles to it's junction with the beginning of the proposed access road to the west; proceed in a southwesterly direction along the proposed access road approximately 1834' to the proposed well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

Approximately 1834' of access road is proposed for the proposed well. See attached **Topographic Map "B"**.

The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District
Water Right : 43-10136

Maurice Harvey Pond
Water Right: 47-1358

Neil Moon Pond
Water Right: 43-11787

Newfield Collector Well
Water Right: 41-1817 (A30414DVA, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), State of Utah approved surface disposal facilities, or Federally approved surface disposal facilities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be

reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – Coleman Brothers LTD(Proposed Location) and Deep Creek Investments etal. (Proposed Access Road and Proposed Pipelines).
See attached Memorandums of Surface Use Agreement and Easement ROW.

12. **OTHER ADDITIONAL INFORMATION**

Newfield Production Company requests 1834' of planned access road to be granted. **Refer to Topographic Map "B"**. Newfield Production Company requests 1720' of surface gas line to be granted. Newfield Production Company requests 1749' of buried water line to be granted .

It is proposed that the disturbed area will be 60' wide to allow for construction of the proposed access road, a 10" or smaller gas gathering line, a 4" poly fuel gas line, a buried 3" steel water injection line and a buried 3" poly water return line. The planned access road will consist of a 18' permanent running surface (9' either side of the centerline) crowned and ditched in order to handle any run-off from any precipitation events that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be turnouts as needed along this road to allow for increases in potential traffic issues. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Both the proposed surface gas and buried water lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** The proposed water pipelines will be buried in a 4-5' deep trench constructed with a trencher or backhoe for the length of the proposal. The equipment will run on the surface and not be flat bladed to minimize surface impacts to precious topsoil in these High Desert environments. If possible, all proposed surface gas pipelines will be installed on the same side of the road as existing gas lines. The construction phase of the planned access road, proposed gas lines and proposed water lines will last approximately (5) days.

In the event that the proposed well is converted to a water injection well, a Sundry Notice 3160-5 form will be applied for through the Bureau of Land Management field office.

- a) Newfield Production Company is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, Newfield is to immediately stop work that might further disturb such materials and contact the Authorized Officer.
- b) Newfield Production will control noxious weeds along rights-of-way for roads, pipelines, well sites or other applicable facilities. On State administered land it is required that a Pesticide Use Proposal shall be submitted and given approval prior to the application of herbicides or other possible hazardous chemicals.
- c) Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on State Lands after the conclusion of drilling operations or at any other time without State authorization. However, if State authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

Surface Flow Line

Newfield requests 1692' of surface flow line be granted. It is proposed that the disturbed area for the surface flowline will be 30' to allow for construction of up to a 14" bundled pipe consisting of 2-2" poly glycol lines and 1-3" production line. **Refer to Topographic Map "C"** for the proposed location of the proposed flow line. Flow lines will be tan and will be constructed using the following procedures:

Clearing and Grading: the proposed flow line will be placed on the surface of the ground. As such no grading or clearing will be needed. The flow line will be centered staked every 200 feet prior to the installation. The flow line will be as close to the access road as possible without interfering with the normal road travel, or road maintenance

Installation for portions along existing roads, lengths of pipe will be laid in the barrow ditch, welded together and moved into place. For lines that go cross-country minimal access will be needed only for maintenance purpose. It is in the best interest of Newfield Exploration to avoid wet and saturated ground that would cause ruts greater than 3 inches in depth. Disturbed areas will be reclaimed with in 120 days of the end of the installation

The Archaeological and Paleontological Reports will be forthcoming.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the Ute Tribal 3-10-4-1E, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Ute Tribal 3-10-4-1E, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

The State office as well as the Ute Tribe Energy and Mineral Department shall be notified upon site completion prior to moving on the drilling rig.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

Representative

Name: Tim Eaton
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that Newfield Production Company is considered to be the operator of well #3-10-4-1E, NE/NW Section 10, T4S, R1E, Uintah County, Utah and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage for this well is covered by the Bureau of Indian Affairs Bond #RLB0010462.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

9/28/10

Date



Mandie Crozier

Regulatory Specialist
Newfield Production Company

2-M SYSTEM

Blowout Prevention Equipment Systems


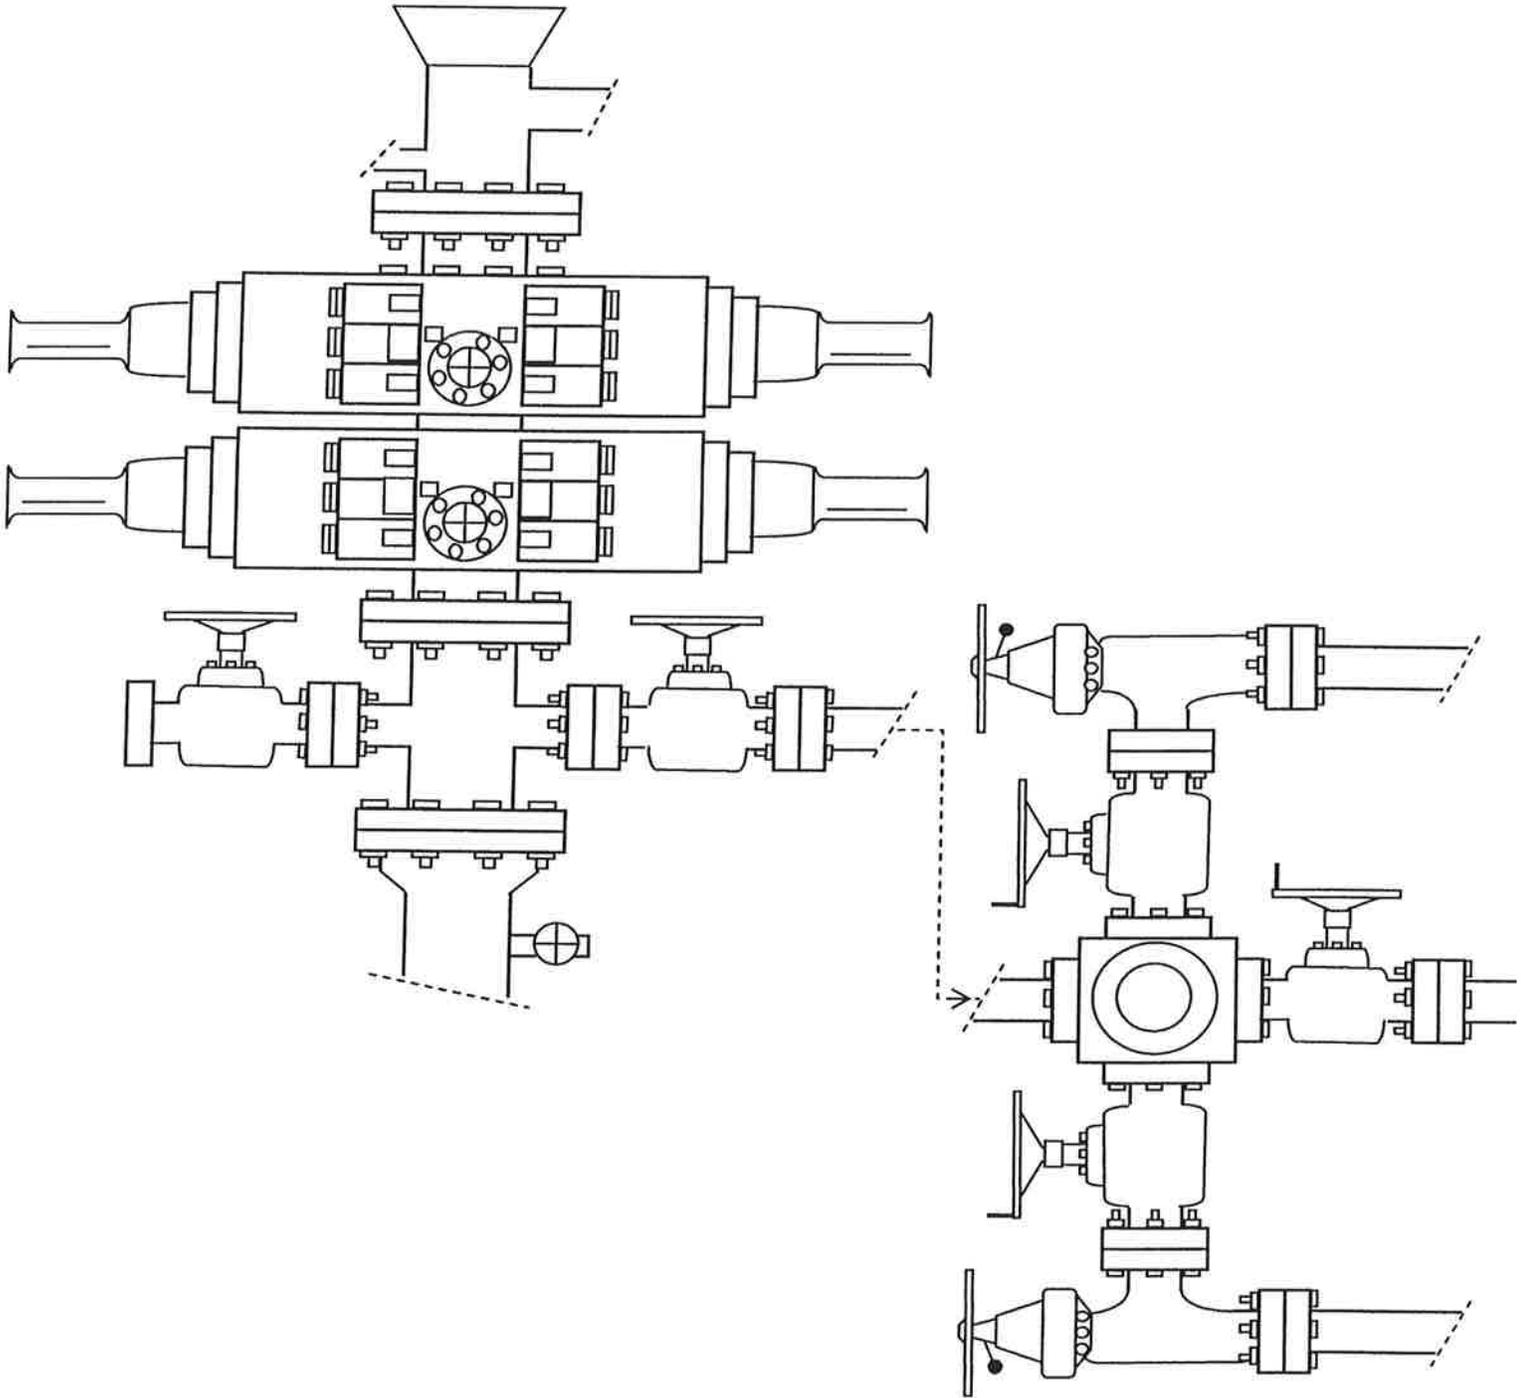


EXHIBIT C

API Number: 4304751290
Well Name: Ute Tribal 3-10-4-1E
Township 04.0 S Range 01.0 E Section 10
Meridian: UBM
Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
 Map Produced by Diana Mason

- | Units | Wells Query |
|-----------------------------|------------------------------------|
| ACTIVE | APD - Approved Permit |
| EXPLORATORY | DRL - Spudded (Drilling Commenced) |
| GAS STORAGE | GIW - Gas Injection |
| NF PP OIL | GS - Gas Storage |
| NF SECONDARY | LA - Location Abandoned |
| PI OIL | LOC - New Location |
| PP GAS | OPS - Operation Suspended |
| PP GEOTHERML | PA - Plugged Abandoned |
| PP OIL | PGW - Producing Gas Well |
| SECONDARY | POW - Producing Oil Well |
| TERMINATED | RET - Returned APD |
| Sections | SGW - Shut-in Gas Well |
| Township | SOW - Shut-in Oil Well |
| Bottom Hole Location - AGRC | TA - Temp. Abandoned |
| | TW - Test Well |
| | WDD - Water Disposal |
| | WW - Water Injection Well |
| | WSW - Water Supply Well |

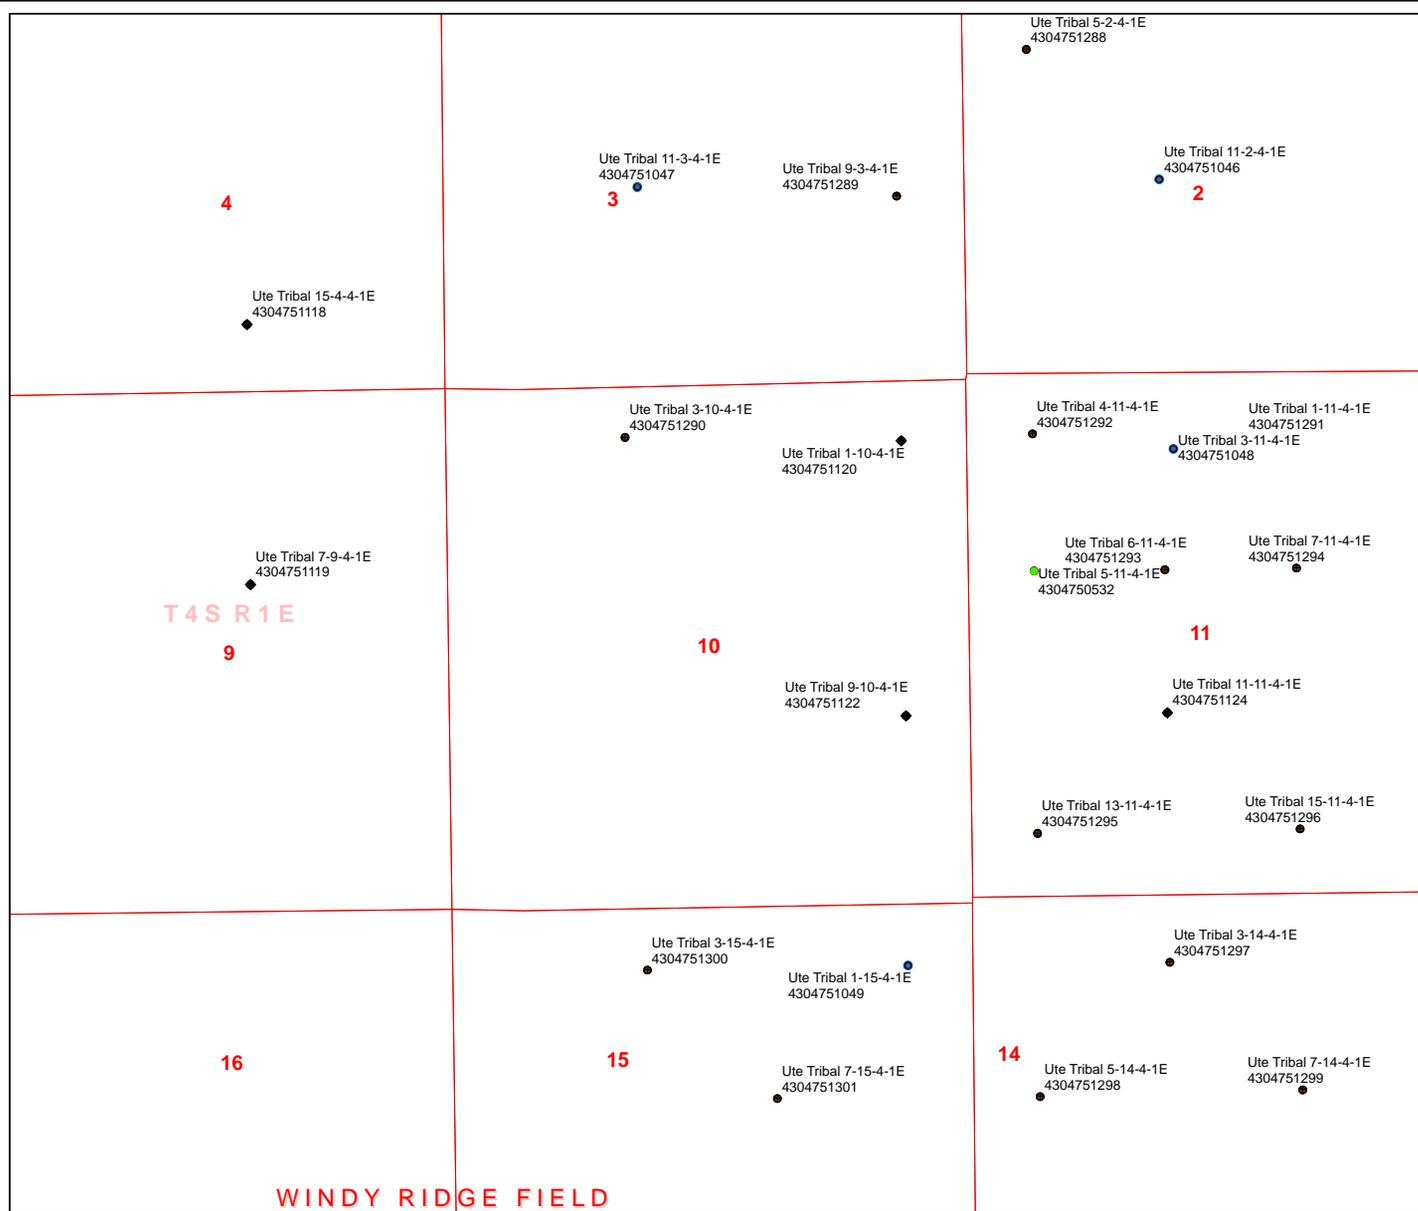



State of Utah

GARY R. HERBERT
Governor

GREG BELL
Lieutenant Governor

Office of the Governor
PUBLIC LANDS POLICY COORDINATION

JOHN HARJA
Director

October 18, 2010

Diana Mason
Petroleum Specialist
Department of Natural Resources
Division of Oil Gas and Mining
1594 West North Temple, Suite 1210
P.O. Box 145801
Salt Lake City, UT 84114-5801

Subject: APD for Newfield Production Co. Ute Tribal 3-10-4-1E well
RDCC Project No. 23222

Dear Ms. Mason:

The State of Utah, through the Public Lands Policy Coordination Office (PLPCO), has reviewed this project. Utah Code (Section 63J-4-601, *et. seq.*) designates PLPCO as the entity responsible to coordinate the review of technical and policy actions that may affect the physical resources of the state, and to facilitate the exchange of information on those actions among federal, state, and local government agencies. As part of this process, PLPCO makes use of the Resource Development Coordinating Committee (RDCC). The RDCC includes representatives from the state agencies that are generally involved or impacted by public lands management.

Division of Air Quality

Because fugitive dust may be generated during soil disturbance the proposed project will be subject to Air Quality rule R307-205-5 for Fugitive Dust. These rules apply to construction activities that disturb an area greater than 1/4 acre in size. A permit, known as an Approval Order, is not required from the Executive Secretary of the Air Quality Board, but steps need to be taken to minimize fugitive dust, such as watering and/or chemical stabilization, providing vegetative or synthetic cover or windbreaks. A copy of the rules can be found at www.rules.utah.gov/publicat/code/r307/r307.htm.

The state encourages the use of Best Management Processes (BMP s) in protecting air quality in Utah. The state recommends the following BMP s as standard operating procedures:

- 1) Emission Standards for Stationary Internal Combustion Engines of 2 g/bhp-hr of NOx for engines less than 300 HP (Tier 3) and 1 g/bhp-hr of NOx for engines over 300 HP (Tier 3).

- 2) No or low bleed controllers for Pneumatic Pumps, Actuators and other Pneumatic devices.
- 3) Green completion or controlled VOC emissions methods with 90% efficiency for Oil or Gas Atmospheric Storage Tanks, VOC Venting controls or flaring, Glycol Dehydration and Amine Units Units, VOC Venting controls or flaring, Well Completion, Re-Completion, Venting, and Planned Blowdown Emissions.

If compressors or pump stations are constructed at the site or if the proponent perceives full production a permit application, known as a Notice of Intent (NOI), should be submitted to the Executive Secretary at the Utah Division of Air Quality at 150 N 1950 West, Salt Lake City, Utah 84116 for review according to R307-401: Permit: Notice of Intent and Approval Order, of the Utah Air Quality Rules. A copy of the rules can be found at www.rules.utah.gov/publicat/code/r307/r307.htm.

The State of Utah appreciates the opportunity to review this proposal and we look forward to working with you on future projects. Please direct any other written questions regarding this correspondence to the Public Lands Policy Coordination Office at the address below, or call Judy Edwards at (801) 537-9023.

Sincerely,

A handwritten signature in black ink, appearing to read 'John Harja', with a stylized flourish at the end.

John Harja
Director

ON-SITE PREDRILL EVALUATION

Utah Division of Oil, Gas and Mining

Operator	NEWFIELD PRODUCTION COMPANY				
Well Name	Ute Tribal 3-10-4-1E				
API Number	43047512900000	APD No	3025	Field/Unit	WILDCAT
Location: 1/4,1/4	NENW	Sec 10	Tw 4.0S	Rng 1.0E	551 FNL 1828 FWL
GPS Coord (UTM)	596144	4445400	Surface Owner	Coleman Brothers LTD	

Participants

See other comments.

Regional/Local Setting & Topography

The general area is on Leland Bench, which is located about 10 miles southwest of Fort Duchesne, Uintah County, Utah. Broad flats with low growing desert shrub type vegetation characterize the area. A few rolling hills and slopes leading to higher flats occur. No springs, seeps or flowing streams are known to occur in the area. The Duchesne River is approximately 7 miles to the east. All lands in the immediate area are privately owned. Solid blocks or scattered Ute Tribal lands surround the area.

Access to the proposed well site is by State of Utah or Uintah County roads and existing or proposed oilfield development roads. Distance from Randlett, Utah is approximately 8.4 miles. Approximately 1,834 feet new road will be constructed to reach this and other nearby locations.

The proposed Ute Tribal 3-10-4-1E oil well is oriented in a north to south direction on a flat area with no apparent slope. Only light excavation will be needed to construct the pad. Maximum cut for the pad is 2.0 feet at Location Corner 3 with a maximum fill of 0.8 feet at Location Corner 6. A steep swale to the east and a swale to the southwest were missed by location the pad in the edge of the normal drilling window. The location appears to be a good site for constructing a pad, drilling and operating a well.

The Coleman Brothers LTD; own the surface.

Surface Use Plan

Current Surface Use

- Grazing
- Recreational
- Wildlfe Habitat

New Road Miles	Well Pad	Src Const Material	Surface Formation
0.4	Width 204 Length 305	Onsite	UNTA

Ancillary Facilities N

Waste Management Plan Adequate?

Environmental Parameters

Affected Floodplains and/or Wetlands N

Flora / Fauna

The vegetation on Leland Bench is a desert shrub/forb type. Similar species are common throughout the area. Principal species are shadscale, bud sage, winter fat, horsebrush, broom snakeweed, Indian ricegrass, needle and thread grass, curly mesquite grass, scarlet globe mallow, matt and Gardiner saltbrush, hordeum jabutum and annual mustards. A few occurrences of cheat grass, rabbit brush, buckwheat and other species occur but are not common. Overall vegetation is fair to good. Impacts from past and current grazing do not exist.

Because of the lack of water and cover the area is not rich in fauna. Species include antelope, coyotes and small mammals and rodents. Some shrub dependent birds may occur but were not observed. Historically, but not currently, sheep and wild horses grazed the area. Light winter cattle grazing currently exists.

Soil Type and Characteristics

Soils are a deep sandy loam with some gravel.

Erosion Issues N

Sedimentation Issues N

Site Stability Issues N

Drainage Diversion Required? N

Berm Required? Y

Erosion Sedimentation Control Required? N

Paleo Survey Run? Y **Paleo Potential Observed?** N **Cultural Survey Run?** Y **Cultural Resources?** N

Reserve Pit

Site-Specific Factors	Site Ranking	
Distance to Groundwater (feet)	100 to 200	5
Distance to Surface Water (feet)	>1000	0
Dist. Nearest Municipal Well (ft)	>5280	0
Distance to Other Wells (feet)	300 to 1320	10
Native Soil Type	Mod permeability	10
Fluid Type	Fresh Water	5
Drill Cuttings	Normal Rock	0
Annual Precipitation (inches)		0
Affected Populations		
Presence Nearby Utility Conduits	Not Present	0
	Final Score	30
		1 Sensitivity Level

Characteristics / Requirements

A 40' x 80' x 8' deep reserve pit is planned mostly in a cut on the northeast corner of the location. A liner with a minimum thickness of 16-mils is required. A sub-liner may not be needed because of the lack of rock in the area.

Closed Loop Mud Required? N **Liner Required?** Y **Liner Thickness** 16 **Pit Underlayment Required?** Y

Other Observations / Comments

Floyd Bartlett (DOGM), Tim Eaton, (Newfield Production Co.), Corie Miller (Tri-State Land Surveying), Christine Cimiluca and Janna Simonsen (BLM), Matt Crazier and Marsha Perry, (Uintah County Planning and Zoning) and Alan Smith Land Owner or representing the Land Owners).

ATV's were used to access the site.

Floyd Bartlett
Evaluator

10/12/2010
Date / Time

Application for Permit to Drill

Statement of Basis

11/2/2010

Utah Division of Oil, Gas and Mining

Page 1

APD No	API WellNo	Status	Well Type	Surf Owner	CBM
3025	43047512900000	LOCKED	OW	P	No
Operator	NEWFIELD PRODUCTION COMPANY		Surface Owner-APD	Coleman Brothers LTD	
Well Name	Ute Tribal 3-10-4-1E		Unit		
Field	WILDCAT		Type of Work	DRILL	
Location	NENW 10 4S 1E U 551 FNL 1828 FWL		GPS Coord (UTM)	596148E	4445402N

Geologic Statement of Basis

The mineral rights for the proposed well are owned by the Ute Tribe. The BLM will be the agency responsible for evaluating and approving the drilling, casing and cement programs.

Brad Hill
APD Evaluator

11/2/2010
Date / Time

Surface Statement of Basis

The general area is on Leland Bench, which is located about 10 miles southwest of Fort Duchesne, Uintah County, Utah. Broad flats with low growing desert shrub type vegetation characterize the area. A few rolling hills and slopes leading to higher flats occur. No springs, seeps or flowing streams are known to occur in the area. The Duchesne River is approximately 7 miles to the east. All lands in the immediate area are privately owned. Solid blocks or scattered Ute Tribal lands surround the area.

Access to the proposed well site is by State of Utah or Uintah County roads and existing or proposed oilfield development roads. Distance from Randlett, Utah is approximately 8.4 miles. Approximately 1,834 feet new road will be constructed to reach this and other nearby locations.

The proposed Ute Tribal 3-10-4-1E oil well is oriented in a north to south direction on a flat area with no apparent slope. Only light excavation will be needed to construct the pad. Maximum cut for the pad is 2.0 feet at Location Corner 3 with a maximum fill of 0.8 feet at Location Corner 6. A steep swale to the east and a swale to the southwest were missed by location the pad in the edge of the normal drilling window. The location appears to be a good site for constructing a pad, drilling and operating a well.

The Coleman Brothers LTD; own the surface. Mrs. Mary Jo Coleman Adamson was contacted by Ms. Christine Cimiluca of the BLM and advised of and invited to the pre-site visit. She did not desire to attend. A surface use agreement has been completed.

The minerals are owned by the United States Government and held in trust for the Ute Indian Tribe. Ms. Christine Cimiluca and Ms. Janna Simonsen of of the BLM, who acts for the Ute Indian Tribe, attended the pre-site evaluation. They had no concerns regarding the location as planned.

Uintah County has recently passed a new ordinance to regulate extraction industries. This ordinance requires a conditional use permit for all oil or gas wells in areas not zoned as industrial. Newfield will be required to obtain a permit for this and other wells on Leland Bench except for a small area which is zoned light industrial.

Floyd Bartlett
Onsite Evaluator

10/12/2010
Date / Time

Conditions of Approval / Application for Permit to Drill

Category	Condition
-----------------	------------------

Application for Permit to Drill Statement of Basis

11/2/2010

Utah Division of Oil, Gas and Mining

Page 2

Pits	A synthetic liner with a minimum thickness of 16 mils with a felt subliner as needed shall be properly installed and maintained in the reserve pit.
Surface	The well site shall be bermed to prevent fluids from leaving the pad.
Surface	The reserve pit shall be fenced upon completion of drilling operations.

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 9/28/2010

API NO. ASSIGNED: 4304751290000

WELL NAME: Ute Tribal 3-10-4-1E

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: NENW 10 040S 010E

Permit Tech Review:

SURFACE: 0551 FNL 1828 FWL

Engineering Review:

BOTTOM: 0551 FNL 1828 FWL

Geology Review:

COUNTY: UINTAH

LATITUDE: 40.15537

LONGITUDE: -109.87109

UTM SURF EASTINGS: 596148.00

NORTHINGS: 4445402.00

FIELD NAME: WILDCAT

LEASE TYPE: 2 - Indian

LEASE NUMBER: 20G0005609

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 4 - Fee

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: INDIAN - RLBO010462
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 437478
- RDCC Review: 2010-11-02 00:00:00.0
- Fee Surface Agreement
- Intent to Commingle

Commingle Approved

LOCATION AND SITING:

- R649-2-3.
- Unit:**
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
- Board Cause No:** R649-3-2
- Effective Date:**
- Siting:**
- R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason
5 - Statement of Basis - bhll
21 - RDCC - dmason
23 - Spacing - dmason



GARY R. HERBERT
Governor

GREGORY S. BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Ute Tribal 3-10-4-1E
API Well Number: 43047512900000
Lease Number: 2OG0005609
Surface Owner: FEE (PRIVATE)
Approval Date: 11/2/2010

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of R649-3-2. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

The Application for Permit to Drill has been forwarded to the Resource Development Coordinating Committee for review of this action. The operator will be required to comply with any applicable recommendations resulting from this review. (See attached)

This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.

Compliance with the Conditions of Approval/Application for Permit to Drill outlined in the Statement of Basis (copy attached).

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)

OR

submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <https://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:



For John Rogers
Associate Director, Oil & Gas

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. 20G0005609
6a. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name UTE
7. Name of Operator Newfield Production Company		7. If Unit or CA Agreement, Name and No. NA
8a. Address Route #3 Box 3630, Myton UT 84052		8. Lease Name and Well No. Ute Tribal 3-10-4-1E
8b. Phone No. (include area code) (435) 646-3721		9. API Well No. 13 047 51290
9. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NE/NW 551' FNL 1828' FWL At proposed prod. zone		10. Field and Pool, or Exploratory Undesignated
10. Distance in miles and direction from nearest town or post office* Approximately 8.7 miles southwest of Randlett, UT		11. Sec., T, R. M. or Blk. and Survey or Area Sec. 10, T4S R1E
11. Distance from proposed* location to nearest property or lease line, ft. Approx. 551' f/lse, NA' f/unit (Also to nearest drig. unit line, if any)	12. No. of acres in lease NA	12. County or Parish Uintah
12. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. NA	13. Proposed Depth 7,830'	13. State UT
13. Elevations (Show whether DF, KDB, RT, GL, etc.) 5264' GL	14. Approximate date work will start* 1st Qtr. 2011	14. Spacing Unit dedicated to this well 40 Acres
15. Attachments		15. BLM/BIA Bond No. on file RLB0010462
16. The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:		16. Estimated duration (7) days from SPUD to rig release

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, must be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification
- Such other site specific information and/or plans as may be required by the BLM.

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 9/28/10
Title Regulatory Specialist		

Approved by (Signature) <i>Jerry Kencosa</i>	Name (Printed/Typed) JERRY KENCOSA	Date FEB 04 2011
Title Assistant Field Manager Lands & Mineral Resources		
Office VERNAL FIELD OFFICE		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

FEB 17 2011

*(Instructions on page 2)

RECEIVED

OCT 01 2010

BLM

NOTICE OF APPROVAL

UDOGM

DIV. OF OIL, GAS & MINING

NOS 9-21-2010

AFMSS# 1DSS0477A

RECEIVED

SEP 30 2010

BLM VERNAL, UTAH

CONDITIONS OF APPROVAL ATTACHED



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company Location: NENW, Sec. 10, T4S R1E
Well No: Ute Tribal 3-10-4-1E Lease No: 2OG0005609
API No: 43-047-51290 Agreement: N/A

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Construction Activity (Notify Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist)	- The Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist shall be notified at least 48 hours in advance of any construction activity. The Ute Tribal office is open Monday through Thursday.
Construction Completion (Notify Ute Tribe Energy & Minerals Dept. and BLM Environmental Scientist)	- Upon completion of the pertinent APD/ROW construction, notify the Ute Tribe Energy & Minerals Dept. for a Tribal Technician to verify the Affidavit of Completion. Notify the BLM Environmental Scientist prior to moving on the drilling rig.
Spud Notice (Notify BLM Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify BLM Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: ut_vn_opreport@blm.gov .
BOP & Related Equipment Tests (Notify BLM Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify BLM Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

- A synthetic liner with a minimum thickness of 16 mils with a felt subliner shall be installed and maintained in the reserve pit.
- Any deviation from submitted APD's and ROW applications the operator will notify the BLM in writing and will receive written authorization of any such change with appropriate authorization.
- All operator employees and/or authorized personnel (sub-contractors) in the field will have approved applicable APD's and ROW permits/authorizations on their person(s) during all phases of construction.
- All vehicular traffic, personnel movement, construction/restoration operations should be confined to the area examined and approved, and to the existing roadways and/or evaluated access routes.
- All permanent surface equipment (meaning on site for six months or longer) will be painted Covert Green to match the surrounding landscape color unless otherwise authorized. This would include all facilities except those required to comply with Occupational Safety and Health Act (OSHA) regulations.
- Reclamation will be completed in accordance with the recontouring and reseeding procedures outlined in the Newfield Exploration Company Castle Peak and Eight Mile Flat Reclamation Plan on file with the Vernal Field Office of the BLM, unless otherwise specified by the private surface owner.

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Newfield Production Co. shall comply with all applicable requirements in the SOP (version: "Ute Tribal Green River Development Program", April 17, 2008). The operator shall also comply with applicable laws and regulations; with lease terms, Onshore Oil and Gas Orders, NTL's; and with other orders and instructions of the authorized officer.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth

(from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and

Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent

Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

Spud
BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross 29 Submitted By
Branden Arnold Phone Number 435-401-0223
Well Name/Number Ute Tribal 3-10-4-1E
Qtr/Qtr NE/NW Section 10 Township 4S Range 1E
Lease Serial Number 2OG0005609
API Number 43-047-51290

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 3/24/2011 10:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 3/24/2011 4:00PM AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks _____

STATE OF UTAH
 DIVISION OF OIL, GAS AND MINING
 ENTITY ACTION FORM -FORM 6

OPERATOR: NEWFIELD PRODUCTION COMPANY
 ADDRESS: RT. 3 BOX 3630
MYTON, UT 84052

OPERATOR ACCT. NO. N2695

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	17983	4301350323	UTE TRIBAL 9-17-4-2W	NESE	17	4S	2W	DUCHESNE	3/21/2011	3/28/11
WELL 1 COMMENTS: <u>GRRV</u>											
A	99999	17989	4304751309	UTE TRIBAL 13-3-4-1E	SWSW	3	4S	1E	UINTAH	3/23/2011	3/28/11
GRRV											
A	99999	17990	4304751290	UTE TRIBAL 3-10-4-1E	NENW	10	4S	1E	UINTAH	3/24/2011	3/28/11
GRRV											

ACTION CODES (See instructions on back of form)
 A - 1 new entity for new well (single well only)
 B - well to existing entity (group or unit well)
 C - from one existing entity to another existing entity
 D - well from one existing entity to a new entity
 E - other (explain in comments section)

RECEIVED
 MAR 23 2011

Signature Jentri Park
 Production Clerk
 03/23/11

NOTE: Use COMMENT section to explain why each Action Code was selected.

DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other		5. Lease Serial No. MON BUTTE EDA 20G0005609
2. Name of Operator NEWFIELD PRODUCTION COMPANY		6. If Indian, Allottee or Tribe Name.
3a. Address Route 3 Box 3630 Myton, UT 84052	3b. Phone (include are code) 435.646.3721	7. If Unit or CA/Agreement, Name and/or
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) 551 FNL 1828 FWL NENW Section 10 T4S R1E		8. Well Name and No. UTE TRIBAL 3-10-4-1E
		9. API Well No. 4304751290
		10. Field and Pool, or Exploratory Area MYTON-TRIBAL EDA
		11. County or Parish, State UINTAH, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____ Spud Notice
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 3/24/11 MIRU Ross #29. Spud well @1:00 PM. Drill 310' of 12 1/4" hole with air mist. TIH W/ 7 Jt's 8 5/8" J-55 24# csgn. Set @ 314.17. On 3/29/11 cement with 160 sks of class "G" w/ 2% CaCL2 + 0.25#/sk Cello- Flake Mixed @ 15.8ppg w/ 1.17ft3/sk yield. Returned 8 barrels cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed) Chevenne Bateman	Title
Signature 	Date 03/30/2011

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by.....	Title	Date
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

RECEIVED

APR 07 2011

STATE OF UTAH
 DEPARTMENT OF NATURAL RESOURCES
 DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
 MON BUTTE EDA 20G0005609

SUNDRY NOTICES AND REPORTS ON WELLS

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

8. WELL NAME and NUMBER:
 UTE TRIBAL 3-10-4-1E

2. NAME OF OPERATOR:
 NEWFIELD PRODUCTION COMPANY

9. API NUMBER:
 4304751290

3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

10. FIELD AND POOL, OR WILDCAT:
 MYTON-TRIBAL EDA

4. LOCATION OF WELL:
 FOOTAGES AT SURFACE: 0551 FNL 1828 FWL COUNTY: UINTAH

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NENW, 10, T4S, R1E STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 05/13/2011	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
 The above subject well was completed on 5/13/2011, attached is a daily completion status report.

NAME (PLEASE PRINT) Jennifer Peatross TITLE Production Technician

SIGNATURE  DATE 05/18/2011

(This space for State use only)

RECEIVED
MAY 23 2011
 DIV. OF OIL, GAS & MINING

Daily Activity Report

Format For Sundry

UTE TRIBAL 3-10-4-1E

3/1/2011 To 7/30/2011

5/3/2011 Day: 1

Completion

Nabors #1608 on 5/3/2011 - MIRUSU. TIH w/ tbg. Drlg DV tool. - MIRUSU. RU BOP's. PU 4-3/4" new rock bit. Tally, drift, pickup new J-55, 6.5#, 8EUE, 2-7/8" tbg to tag fill @ 2571'. RU swivel, pump & tanks. Drlg out plug @ 2577' in 1.5 hours. Pickup & TIH w/ tbg to tag fill @ 7660'. C/O to PBD @ 7663'. TOO H w/ tbg. LD bit & bit sub. RIH w/ 4.825" String mill. 81 jts w/ EOT @ 2555' SIFN.

Daily Cost: \$0

Cumulative Cost: \$61,403

5/9/2011 Day: 2

Completion

Nabors #1608 on 5/9/2011 - TOO H w/ string mill. Test casing to 4500 psi. Run CBL/Perferate 1st stage. - RU swivel, pump & tanks & work mill through DV tool @ 2577'. TOO H w/ tbg. LD mill & x-over sub. RU Hot Oiler & test casing, wellhead w/ valves & BOP's to 4500 psi. RU Perforators LLC WLT w/ lubricator & run CBL under pressure. WLTD was 7668' w/ cmt top @ 240'. RIH w/ 3-1/8" perf guns & perforated wstch sands w/ 3 spf for total of 15 shots. SIFN. -

Daily Cost: \$0

Cumulative Cost: \$72,862

5/10/2011 Day: 3

Completion

Nabors #1608 on 5/10/2011 - Frac well. Flow well back. - Stage #4: RU PSI WLT w/ lubricator. RIH & set plug. Perferate D3 sds w/ 3-1/8" guns for a total of 18 shots. RU BJ Services. Frac w/ 34,979#'s sand. 2024 bbls EWTR. Leave pressure on well. - Stage #6: RU PSI WLT w/ lubricator. RIH & set plug. Perferate GB4 sds w/ 3-1/8" guns for a total of 12 shots. RU BJ Services. Frac w/ 25,476#'s sand. 2803 bbls EWTR. RDE BJ & WLT. Flow well back. Flowed 5 hours & turned to oil. 2200 bbls EWTR. - Stage #5: BJ broke down. RU PSI WLT w/ lubricator. 2- Mis-fires on plug. RIH & set plug. Perferate DS3 sds w/ 3-1/8" guns for a total of 30 shots. RU BJ Services. Frac w/ 49,540#'s sand. 2475 bbls EWTR. Leave pressure on well. - Stage #2: RU PSI WLT w/ lubricator. WLT broke down. RIH & set plug. Perferate CP4/3 sds w/ 3-1/8" guns for a total of 33 shots. RU BJ Services. Frac w/ 80,100#'s sand. 1249 bbls EWTR. Leave pressure on well. - Stage #1: RU BJ Services. Frac Wstch sands w/ 7627#'s sand (cut short due to pressure). 603 bbls EWTR. Leave pressure on well. - Stage #3: RU PSI WLT w/ lubricator. RIH & set plug. Perferate CP1/.5 sds w/ 3-1/8" guns for a total of 33 shots. RU BJ Services. Frac w/ 34,720#'s sand. 1646 bbls EWTR. Leave pressure on well.

Daily Cost: \$0

Cumulative Cost: \$221,485

5/11/2011 Day: 4

Completion

Nabors #1608 on 5/11/2011 - Set kill plug. TIH w/ tbg. Drlg out plugs. - Open well w/ 700 psi on casing. RU Hot Oiler & pump 15 bbls down casing. RU PSI WLT w/ lubricator. RIH w/ solid composite plug & set @ 5775'. RD WLT. RD Cameron BOP's. Instal Schefer BOP's. RU 4-3/4" used Chomp mill & x-over sub. TIH w/ tbg to tag plug @ 5775'. RU swivel, pump & tanks & drlg out plug. Continue TIH w/ tbg drlg out plugs. Last plug drlg out was 7140' (1 remaining).

SIFN.

Daily Cost: \$0**Cumulative Cost:** \$236,096

5/13/2011 Day: 5**Completion**

Nabors #1608 on 5/13/2011 - Circulate well. RIH w/ production. Put well on pump. Final report. - Open well w/ 300 psi on casing. Circulate 160 bbls water. TOOH w/ tbg. LD mill & x-over sub. TIH w/ Bull plug, Collar, 3 jts tbg, 2-7/8" nipple, PBGA, 1 jt tbg, SN, 1 jt tbg, TA new Cntrl Hydrlic w/ 45,000# shear, 231 jts tbg. RD BOP's. Set TA @ 7286' w/ 18,000#'s tension w/ SN 7321' @ & EOT @ 7453'. Pickup up prime pump. TIH w/ 2-1/2" x 1-3/4" x 21' x 24' new Cntrl Hydrlic RHAC pump w/ 225"SL, 1" x 4' stabilizer bar, 6- 1-1/2" weight bars, 20-3/4" guided rods, 145- 3/4" slick rods, 120- 7/8" guided rods 4per, 2',4',6',8' x 7/8" pony rod, 1-1/2" x 30' Polish rod. Space pump. Test tbg & pump to 800 psi w/ unit. RDMOSU. POP @ 9PM w/ 5 spm, 122"SL w/ 2050 bbls EWTR. Final Report. **Finalized**

Daily Cost: \$0**Cumulative Cost:** \$290,440

Pertinent Files: Go to File List

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
20G0005609

6. If Indian, Allottee or Tribe Name
UTE

7. Unit or CA Agreement Name and No.
NA

8. Lease Name and Well No.
UTE TRIBAL 3-10-4-1E

9. AFI Well No.
43-047-51290

10. Field and Pool or Exploratory

11. Sec., T., R., M., on Block and Survey or Area
SEC. 10, T4S, R1E

12. County or Parish
UINTAH

13. State
UT

14. Date Spudded
03/24/2011

15. Date T.D. Reached
04/29/2011

16. Date Completed 05/13/2011
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5264' GL 5276' KB

18. Total Depth: MD 7758'
TVD

19. Plug Back T.D.: MD 7663'
TVD

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	310'		160 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	7709'		270 PRIMLITE		240'	
						550 50/50 POZ			
						310 PRIMLITE			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 7453'	TA @ 7286'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Wasatch	7586'	7619'	7586-7619'	.36"	15	
B) Green River	5824'	7244'	5824-7244'	.34"	126	
C)						
D)						

26. Perforation Record

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Wasatch	7586'	7619'	7586-7619'	.36"	15	
B) Green River	5824'	7244'	5824-7244'	.34"	126	
C)						
D)						

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
5824-7619'	Frac w/ 231806#s 20/40 sand in 1098 bbls of Lightning 17 fluid in 6 stages

RECEIVED
JUN 15 2011
DIV. OF OIL, GAS & MINING

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
5/14/11	5/24/11	24	→	92	19	43			2" x 1-3/4" x 21' x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	PRODUCING
			→						

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD AND USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof. Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS


Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
WASATCH GREEN RIVER	7588'	7619'		GARDEN GULCH MRK	5278'
	5824'	7244'		GARDEN GULCH 1	5483'
				GARDEN GULCH 2	5612'
				POINT 3	5929'
				X MRKR	6121'
				Y MRKR	6162'
				DOUGALS CREEK MRK	6315'
				BI-CARB	6622'
				B LIMESTONE MARK	6800'
				CASTLE PEAK	7066'
				BASAL CARBONATE	7442'
				WASATCH	7554'

32. Additional remarks (include plugging procedure):

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Jennifer Peatross Title Production Technician
 Signature  Date 06/07/2011

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Daily Activity Report

Format For Sundry

UTE TRIBAL 3-10-4-1E**2/1/2011 To 6/30/2011****UTE TRIBAL 3-10-4-1E****Waiting on Cement****Date:** 3/30/2011

Ross #29 at 310. Days Since Spud - On 3/24/11 Ross #29 spud and drilled 310' of 12 1/4" hole, P/U and run 7 jts of 8 5/8" casing set - @ 314.17'KB. On 3/29/11 cement w/BJ w/160 sks of class G+2%kcl+.25#CF mixed @ 15.8ppg and 1.17 - yield. Returned 8bbls to pit, bump plug to 0 psi, BLM and State were notified of spud via email.

Daily Cost: \$0**Cumulative Cost:** \$71,056**UTE TRIBAL 3-10-4-1E****Drilling 7 7/8" hole w/ KCL water****Date:** 4/21/2011

Capstar #328 at 1704. 1 Days Since Spud - Drill out cmt f/ 270-340' - Drill 7 7/8" hole F/340-1704' WOB-10, RPM-60, PP-1775, SPM-122 - Strap BHA M/u cement lines Install flare lines - test BOP's - MIRU Rig up by Hand. - M/U bit directional tools and BHA tih tag cement @ 270'

Daily Cost: \$0**Cumulative Cost:** \$131,434**UTE TRIBAL 3-10-4-1E****Drilling 7 7/8" hole w/ KCL water****Date:** 4/22/2011

Capstar #328 at 4240. 2 Days Since Spud - ROTATE DRILL AND SURVEY F/3968' TO 4108' - ROTATE DRILL F/4108' TO 4240' - ROTATE DRILL AND SURVEY F/1704' TO 2338' WOB 18-25K, 120 SPM, 347 GPM - SAFETY STAND DOWN ON PINCH POINT AND HAND PLACEMENT WITH UBATC HAND AND RIG CREW - ROTATE DRILL AND SURVEY F/2338' TO 3379' WOB 18-25K, 120 SPM, 347 GPM, START LOSING PARTIAL RETURNS - PUMP 20% LCM PILL AND SPOT IN ANULUS, LET SOAK WHILE DOING RIG SERVICE - RIG SERVICE SPR 61 SPM-1450 PSI - ROTATE DRILL AND SURVEY F/3379' TO 3834' WOB 18-25K, 120 SPM, 347 GPM, - CONDITION MUD AND PUMP LCM PILL TO MAINTAIN CIRCULATION - LOST RETURNS, PUMP LCM TO LOST ZONE AND SOAK - HAD TO POOH 5 JTS TO REGAIN MWD TOOL SIGNAL - ROTATE DRILL F/3834' TO 3968'

Daily Cost: \$0**Cumulative Cost:** \$161,237**UTE TRIBAL 3-10-4-1E****Drilling 7 7/8" hole w/ KCL water****Date:** 4/23/2011

Capstar #328 at 5472. 3 Days Since Spud - OPEN WELL AND CIRCULATE OVER SHAKERS AND VENTING OUT GAS THRU BUSTER. REPAIR PLUGGED LINE AND SHUT - ATTEMPTED TO SHUT IN WELL AND CIRCULATE GAS THRU GAS BUSTER, GAS BUSTER RETURN LINE PLUGGED - CIRC AT 61 SPM THRU GAS BUSTER, 15'-20' FLARE. 6421 UNITS OF GAS AT 5327'. - POOH L/D JT AND MONITOR WELL, WELL FLOWING AT 90 BPH RATE, START CONDITIONING MUD WITH ZEO GEL, - ROTATE AND SLIDE DRILL F/5420' TO 5472' LOST FULL RETURNS, 92 BPH LOST RATE. - LOST CIRCULATION, PUMP SWEEPS AND CONDITION MUD TO REGAIN CIRCULATION - ROTATE DRILL AND SLIDE DRILL F/4964' TO 5420' - ROTATE AND SLIDE DRILL FROM 4421' TO 4964' - PUMP LCM SWEEPS TO TRY AND REGAIN CIRCULATION. GOT FULL RETURNS - ROTATE AND SLIDE DRILL F/4240' TO 4421' - HYDRILL AND BEGIN CIRCULATE THRU CHOKE AND BUSTER. CONDITONING MUD TO HELP WITH GAS.

Daily Cost: \$0**Cumulative Cost:** \$183,997

UTE TRIBAL 3-10-4-1E**Circulate & Condition Hole****Date:** 4/24/2011

Capstar #328 at 6095. 4 Days Since Spud - POOH, HOLE STILL FLOWING AFTER 4JTS. CIRC OUT GAS THRU CHOKE, BUILD SMALL DRY JOB - CIRC BU, BUILD DRY JOB, WELL BREATHING, PUMP DRY JOB. - NO PULSE F/ MWD, POOH 9 JTS, NO PULSE, DECISION MADE TO POOH AND C/O MWD - ROTATE AND SLIDE DRILL F/ 5688' TO 6095' - SERVICE RIG - CIRCULATE OUT GAS. - LOSING AT A 110 BBL PER HOUR RATE. BUILD 80 BBL LCM PILL, PUMP AND SPOT FOR 30 MINS. - ROTATE AND SLIDE DRILL F/ 5472' TO 5520' - OPEN WELL AND CIRCULATE AND CONDITION MUD TO 35 VIS AND 8.8 PPG MUD - WELL SHUT IN AND CIRCULATING GAS OUT THRU GAS BUSTER - ROTATE AND SLIDE DRILL F/ 5520' TO 5688'

Daily Cost: \$0**Cumulative Cost:** \$201,455**UTE TRIBAL 3-10-4-1E****Drill 7 7/8" hole with fresh water****Date:** 4/25/2011

Capstar #328 at 6684. 5 Days Since Spud - WELL FLOWING AT 80 BBLS PER HR. WITH 20 FT FLARE, CIRCULATE OUT GAS - POOH WITH DP, WELL FLOWING AGAIN, - CIRCULATE WEIGHTED MUD TO SLOW FLOW RATE - POOH LAYING DOWN SINGLES TO HWDP, 980', FLOW CHECK, WELL FLOW AT 110 BBL PER HR, 20' FLARE - COULD NOT CIRC. GAS OUT. SPOT 9.6 WEIGHTED PILL. WELL STATIC FOR 12 MINS AND STARTED FLOWING - DECISION MAD TO TIH AND TRY TO KILL WELL ON BOTTOM. TIH TO BOTTOM TAKING FLOW RETURNS - WASH LAST 300' TO BOTTOM - ROTATE DRILL F/6186' TO 6231' - FLOW CHECK AND RE-FILL MUD PITS DUE TO LOSSES - CIRCULATE HOLE CLEAN BEFORE WIRELINE SURVEY - WIRELINE TOTCO SURVEY: 3 DEGREES - ROTATE DRILL F/ 6231' TO 6351' - PUMP 40 BBL LCM PILL TO GAIN CIRC RETURNS - ROTATE DRILL F/ 6351' TO 6684' - CIRC HOLE CLEAN AND RUN WIRELINE TOTCO SURVEY: SURVEY 3.25 "BOP DRILL, 1 MIN 5 SEC"

Daily Cost: \$0**Cumulative Cost:** \$223,509**UTE TRIBAL 3-10-4-1E****Circulate & Condition Hole****Date:** 4/26/2011

Capstar #328 at 7776. 6 Days Since Spud - ROTATE DRILL FROM 7318 TO 7776', LOST RETURNS. - SERVICE RIG - ROTATE DRILL F/7182' TO 7318', PUMP LCM 15BBL SWEEPS EVERY CONNECTION - RUN WIRELINE SURVEY. 4 DEG - CIRCULATE BU TO CLEAN HOLE BEFORE RUNNING TOTCO DEVIATION TOOL FOR SURVEY - ROTATE DRILL F/6684' TO 7182', PUMP LCM 15BBL SWEEPS EVERY CONNECTION - PUMP LCM SWEEP

Daily Cost: \$0**Cumulative Cost:** \$253,439**UTE TRIBAL 3-10-4-1E****Logging****Date:** 4/27/2011

Capstar #328 at 7805. 7 Days Since Spud - LOST CIRCULATION, BUILD AND PUMP LCM SWEEP. GOT FULL RETURNS - POOH WITH LOGGING TOOLS - DENISTY TOOL FAILED, POOH AND CHANGE OUT TOOL, RIH ON SECOUND RUN AND HIT BRIDGE AT 4100', - RIH WITH TOOLS, HIT BRIDGE AT 4050', WORKED THRU AND TAGGED BOTTOM AT 7767' LOGGERS DEPTH. - PJSM AND JSA REVIEW WITH CREWS ON RU OF LOG TOOLS, RU LOGGERS - FINISH LAYING DOWM DP AND BHA - POOH L/D DP - BUILD AND SPOT WEIGHTED PILL - FLOW CHECK, WELL FLOWING. DECISION WAS MADE TO SPOT WEIGHTED PILL - POOH L/D DP. TO 4452', - FLOW CHECK WELL. WELL FLOWING AT 25 GPM, SLOWED TO 1.5 GPM, PUMP DRY JOB - CIRCULATE HOLE CLEAN AND BUILD DRY JOB - DEVIATION SURVEY 3 DEG - CIRCULATE BOTTOMS UP - ROTATE FROM 7776' TO 7805' (TD)

Daily Cost: \$0**Cumulative Cost:** \$307,472

UTE TRIBAL 3-10-4-1E**Running casing****Date:** 4/28/2011

Capstar #328 at 7805. 8 Days Since Spud - SET UP PIPE RACKS AND PUMP 20 BBL DRY JOB IN PREPARING TO L/D DP - RIG DOWN LOGGERS - PLACE PIPE RACKS AND LOAD DP TO RUN IN HOLE OPEN ENDED TO RUN LOGS - RIH WITH DRILL PIPE TO 4405' - SERVICE RIG - WAIT ON HALLIBURTON SLIM HOLE LOGGING TOOLS - HALLIBURTON MAKING UP NEW HEAD ON THE WIRELINE REEL - BREAK OFF TOP DRIVE, WELL COMING IN UP DRILL PIPE DUE TO U-TUBING, CIRC BU AND SPOT BALANCE PILL - COUNT DRILL PIPE AND CASING ON LOCATION, MAKE UP GUIDE SHOE AND FLOAT TO SHOE TRACK - CLEAN AND PREP RIG FLOOR TO RIH WOTH CASING - POOH L/D DRILL PIPE FROM 4405' - JSA AND PJSM ON R/D OF LOGGING EQUIP, R/D LOGGERS - RIH WITH SLIM HOLE WIRELINE ASSEMBLY, LOGS TO BOTTOM, LOGGERS DEPTH 7760'

Daily Cost: \$0**Cumulative Cost:** \$366,492

UTE TRIBAL 3-10-4-1E**Rigging down****Date:** 4/29/2011

Capstar #328 at 7805. 9 Days Since Spud - NIPPLE DOWN AND CLEAN PITS. "RIG RELEASE FROM 3-10-4-1E" 04/29/2011 TO UT 13-2-4-1E - RD CEMENTERS, CLEAN LINES AND BEGIN TO CLEAN PITS - PREP RIG FLOOR AND BH CEMENT HEAD IN PLACE. - JSA REVIEW AND PJSM WITH CEMENTERS AND RIG CREW ON CEMENT JOB - PUMP FIRST STAGE OF CEMENT JOB, PUMPED SURE BOND TO PIT, OUR RETURNS F/1ST STAGE, FLOATS HELD - PUMP 2ND STAGE AND DISPL., 50 BBLS CEMENT TO SURFACE, CHECK DV TOOL, TOOL HELD. - RIH CASING, TAG BOTTOM AT 7758'. PU CASING HANGER TO CIRCULATE - CIRCULATE WHILE REMOVING PIPR RACKS AND PIPE HANDLER, BH RU CEMENT EQUIP. LAND CASG. **Finalized**

Daily Cost: \$0**Cumulative Cost:** \$536,449

Pertinent Files: Go to File List

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION				COUNTY	SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG			
E	17990	17990	4304751290	UTE TRIBAL 3-10-4-1E	NENW	10	4S	1E	UINTAH	3/24/2011	5/13/11
WELL 1 COMMENTS: CHANGE TO GR-WS FORMATION											
											6/29/11
E	17996	17996	4304751291	UTE TRIBAL 1-11-4-1E	NENE	11	4S	1E	UINTAH	3/25/2011	5/6/11
CHANGE TO GR-WS FORMATION											
											6/29/11
E	18018	18019 18018	4304751296	UTE TRIBAL 15-11-4-1E	SWSE	11	4S	1E	UINTAH	4/1/2011	5/27/11
CHANGE TO GR-WS FORMATION											
											6/29/11
E	18014	18014	4304751305	UTE TRIBAL 13-2-4-1E	SWSW	2	4S	1E	UINTAH	4/5/2011	5/23/11
CHANGE TO GR-WS FORMATION											
											6/29/11
E	17987	17987	4304751307	UTE TRIBAL 5-3-4-1E	SWNW	3	4S	1E	UINTAH	3/22/2011	5/23/11
CHANGE TO GR-WS FORMATION											
											6/29/11
E	17993	17993	4304751322	UTE TRIBAL 9-11-4-1E	NESE	11	4S	1E	UINTAH	3/31/2011	5/16/11
CHANGE TO GR-WS FORMATION											
											6/29/11

ACTION CODES (See instructions on back of form)
 A - 1 new entity for new well (single well only)
 B - well to existing entity (group or unit well)
 C - from one existing entity to another existing entity
 D - well from one existing entity to a new entity
 E - ther (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.

RECEIVED
 JUN 27 2011

DIV. OF OIL, GAS & MINING

Signature _____ Jentri Park
 Production Clerk _____ 06/23/11

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

Amended

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
14-20-H62-6387

1a. Type of Well Oil Well Gas Well Dry Other
 b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Resvr.,
 Other: _____

6. If Indian, Allottee or Tribe Name
UTE

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

7. Unit or CA Agreement Name and No.
NA

3. Address 1401 17TH ST. SUITE 1000 DENVER, CO 80202
 3a. Phone No. (include area code) (435) 646-3721

8. Lease Name and Well No.
UTE TRIBAL 3-10-4-1E

4. Location of Well (Report location clearly and in accordance with Federal requirements)*
 At surface 551' FNL & 1828' FWL (NE/NW) SEC. 10, T4S, R1E
 At top prod. interval reported below
 At total depth 7758'

9. AFI Well No.
43-047-51290

10. Field and Pool or Exploratory

11. Sec., T., R., M., on Block and Survey or Area
SEC. 10, T4S, R1E

12. County or Parish UINTAH
 13. State UT

14. Date Spudded 03/24/2011
 15. Date T.D. Reached 04/29/2011
 16. Date Completed 05/13/2011
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5264' GL 5276' KB

18. Total Depth: MD 7758' TVD
 19. Plug Back T.D.: MD 7663' TVD
 20. Depth Bridge Plug Set: MD TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
 DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
 Was DST run? No Yes (Submit report)
 Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cement Depth	No. of Sks. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	310'		160 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	7709'		270 PRIMLITE		240'	
						550 50/50 POZ			
						310 PRIMLITE			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 7453'	TA @ 7286'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Wasatch	7586'	7619'	7586-7619'	.36"	15	
B) Green River	5824'	7244'	5824-7244'	.34"	126	
C)						
D)						

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
5824-7619'	Frac w/ 231806#s 20/40 sand in 1098 bbls of Lightning 17 fluid in 6 stages

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
5/14/11	5/24/11	24	→	92	19	43			2" x 1-3/4" x 21' x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

RECEIVED
JUL 07 2011

*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD AND USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
WASATCH GREEN RIVER	7586' 5824'	7619' 7244'		GARDEN GULCH MRK GARDEN GULCH 1	5278' 5483'
				GARDEN GULCH 2 POINT 3	5612' 5929'
				X MRKR Y MRKR	6121' 6162'
				DOUGALS CREEK MRK BI-CARB	6315' 6822'
				B LIMESTONE MARK CASTLE PEAK	6800' 7066'
				BASAL CARBONATE WASATCH	7442' 7554'

32. Additional remarks (include plugging procedure):

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Jennifer Peatross Title Production Technician
 Signature *Jennifer Peatross* Date 07/05/2011

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Daily Activity Report

Format For Sundry

UTE TRIBAL 3-10-4-1E

2/1/2011 To 6/30/2011

UTE TRIBAL 3-10-4-1E

Waiting on Cement

Date: 3/30/2011

Ross #29 at 310. Days Since Spud - On 3/24/11 Ross #29 spud and drilled 310' of 12 1/4" hole, P/U and run 7 jts of 8 5/8" casing set - @ 314.17'KB. On 3/29/11 cement w/BJ w/160 sks of class G+2%kcl+.25#CF mixed @ 15.8ppg and 1.17 - yield. Returned 8bbls to pit, bump plug to 0 psi, BLM and State were notified of spud via email.

Daily Cost: \$0

Cumulative Cost: \$71,056

UTE TRIBAL 3-10-4-1E

Drilling 7 7/8" hole w/ KCL water

Date: 4/21/2011

Capstar #328 at 1704. 1 Days Since Spud - Drill out cmt f/ 270-340' - Drill 7 7/8" hole F/340-1704' WOB-10, RPM-60, PP-1775, SPM-122 - Strap BHA M/u cement lines Install flare lines - test BOP's - MIRU Rig up by Hand. - M/U bit directional tools and BHA tih tag cement @ 270'

Daily Cost: \$0

Cumulative Cost: \$131,434

UTE TRIBAL 3-10-4-1E

Drilling 7 7/8" hole w/ KCL water

Date: 4/22/2011

Capstar #328 at 4240. 2 Days Since Spud - ROTATE DRILL AND SURVEY F/3968' TO 4108' - ROTATE DRILL F/4108' TO 4240' - ROTATE DRILL AND SURVEY F/1704' TO 2338' WOB 18-25K, 120 SPM, 347 GPM - SAFETY STAND DOWN ON PINCH POINT AND HAND PLACEMENT WITH UBATC HAND AND RIG CREW - ROTATE DRILL AND SURVEY F/2338' TO 3379' WOB 18-25K, 120 SPM, 347 GPM, START LOSING PARTIAL RETURNS - PUMP 20% LCM PILL AND SPOT IN ANULUS, LET SOAK WHILE DOING RIG SERVICE - RIG SERVICE SPR 61 SPM-1450 PSI - ROTATE DRILL AND SURVEY F/3379' TO 3834' WOB 18-25K, 120 SPM, 347 GPM, - CONDITION MUD AND PUMP LCM PILL TO MAINTAIN CIRCULATION - LOST RETURNS, PUMP LCM TO LOST ZONE AND SOAK - HAD TO POOH 5 JTS TO REGAIN MWD TOOL SIGNAL - ROTATE DRILL F/3834' TO 3968'

Daily Cost: \$0

Cumulative Cost: \$161,237

UTE TRIBAL 3-10-4-1E

Drilling 7 7/8" hole w/ KCL water

Date: 4/23/2011

Capstar #328 at 5472. 3 Days Since Spud - OPEN WELL AND CIRCULATE OVER SHAKERS AND VENTING OUT GAS THRU BUSTER. REPAIR PLUGGED LINE AND SHUT - ATTEMPTED TO SHUT IN WELL AND CIRCULATE GAS THRU GAS BUSTER, GAS BUSTER RETURN LINE PLUGGED - CIRC AT 61 SPM THRU GAS BUSTER, 15'-20' FLARE. 6421 UNITS OF GAS AT 5327'. - POOH L/D JT AND MONITOR WELL, WELL FLOWING AT 90 BPH RATE, START CONDITIONING MUD WITH ZEO GEL, - ROTATE AND SLIDE DRILL F/5420' TO 5472' LOST FULL RETURNS, 92 BPH LOST RATE. - LOST CIRCULATION, PUMP SWEEPS AND CONDITION MUD TO REGAIN CIRCULATION - ROTATE DRILL AND SLIDE DRILL F/4964' TO 5420' - ROTATE AND SLIDE DRILL FROM 4421' TO 4964' - PUMP LCM SWEEPS TO TRY AND REGAIN CIRCULATION. GOT FULL RETURNS - ROTATE AND SLIDE DRILL F/4240' TO 4421' - HYDRILL AND BEGIN CIRCULATE THRU CHOKE AND BUSTER. CONDITONING MUD TO HELP WITH GAS.

Daily Cost: \$0

Cumulative Cost: \$183,997

UTE TRIBAL 3-10-4-1E**Circulate & Condition Hole****Date:** 4/24/2011

Capstar #328 at 6095. 4 Days Since Spud - POOH, HOLE STILL FLOWING AFTER 4JTS. CIRC OUT GAS THRU CHOKE, BUILD SMALL DRY JOB - CIRC BU, BUILD DRY JOB, WELL BREATHING, PUMP DRY JOB. - NO PULSE F/ MWD, POOH 9 JTS, NO PULSE, DECISION MADE TO POOH AND C/O MWD - ROTATE AND SLIDE DRILL F/ 5688' TO 6095' - SERVICE RIG - CIRCULATE OUT GAS. - LOSING AT A 110 BBL PER HOUR RATE. BUILD 80 BBL LCM PILL, PUMP AND SPOT FOR 30 MINS. - ROTATE AND SLIDE DRILL F/ 5472' TO 5520' - OPEN WELL AND CIRCULATE AND CONDITION MUD TO 35 VIS AND 8.8 PPG MUD - WELL SHUT IN AND CIRCULATING GAS OUT THRU GAS BUSTER - ROTATE AND SLIDE DRILL F/ 5520' TO 5688'

Daily Cost: \$0**Cumulative Cost:** \$201,455

UTE TRIBAL 3-10-4-1E**Drill 7 7/8" hole with fresh water****Date:** 4/25/2011

Capstar #328 at 6684. 5 Days Since Spud - WELL FLOWING AT 80 BBLS PER HR. WITH 20 FT FLARE, CIRCULATE OUT GAS - POOH WITH DP, WELL FLOWING AGAIN, - CIRCULATE WEIGHTED MUD TO SLOW FLOW RATE - POOH LAYING DOWN SINGLES TO HWDP, 980', FLOW CHECK, WELL FLOW AT 110 BBL PER HR, 20' FLARE - COULD NOT CIRC. GAS OUT. SPOT 9.6 WEIGHTED PILL. WELL STATIC FOR 12 MINS AND STARTED FLOWING - DECISION MAD TO TIH AND TRY TO KILL WELL ON BOTTOM. TIH TO BOTTOM TAKING FLOW RETURNS - WASH LAST 300' TO BOTTOM - ROTATE DRILL F/6186' TO 6231' - FLOW CHECK AND RE-FILL MUD PITS DUE TO LOSSES - CIRCULATE HOLE CLEAN BEFORE WIRELINE SURVEY - WIRELINE TOTCO SURVEY: 3 DEGREES - ROTATE DRILL F/ 6231' TO 6351' - PUMP 40 BBL LCM PILL TO GAIN CIRC RETURNS - ROTATE DRILL F/ 6351' TO 6684' - CIRC HOLE CLEAN AND RUN WIRELINE TOTCO SURVEY: SURVEY 3.25 "BOP DRILL, 1 MIN 5 SEC"

Daily Cost: \$0**Cumulative Cost:** \$223,509

UTE TRIBAL 3-10-4-1E**Circulate & Condition Hole****Date:** 4/26/2011

Capstar #328 at 7776. 6 Days Since Spud - ROTATE DRILL FROM 7318 TO 7776', LOST RETURNS. - SERVICE RIG - ROTATE DRILL F/7182' TO 7318', PUMP LCM 15BBL SWEEPS EVERY CONNECTION - RUN WIRELINE SURVEY. 4 DEG - CIRCULATE BU TO CLEAN HOLE BEFORE RUNNING TOTCO DEVIATION TOOL FOR SURVEY - ROTATE DRILL F/6684' TO 7182', PUMP LCM 15BBL SWEEPS EVERY CONNECTION - PUMP LCM SWEEP

Daily Cost: \$0**Cumulative Cost:** \$253,439

UTE TRIBAL 3-10-4-1E**Logging****Date:** 4/27/2011

Capstar #328 at 7805. 7 Days Since Spud - LOST CIRCULATION, BUILD AND PUMP LCM SWEEP. GOT FULL RETURNS - POOH WITH LOGGING TOOLS - DENISTY TOOL FAILED, POOH AND CHANGE OUT TOOL, RIH ON SECOUND RUN AND HIT BRIDGE AT 4100', - RIH WITH TOOLS, HIT BRIDGE AT 4050', WORKED THRU AND TAGGED BOTTOM AT 7767' LOGGERS DEPTH. - PJSM AND JSA REVIEW WITH CREWS ON RU OF LOG TOOLS, RU LOGGERS - FINISH LAYING DOWM DP AND BHA - POOH L/D DP - BUILD AND SPOT WEIGHTED PILL - FLOW CHECK, WELL FLOWING. DECISION WAS MADE TO SPOT WEIGHTED PILL - POOH L/D DP. TO 4452', - FLOW CHECK WELL. WELL FLOWING AT 25 GPM, SLOWED TO 1.5 GPM, PUMP DRY JOB - CIRCULATE HOLE CLEAN AND BUILD DRY JOB - DEVIATION SURVEY 3 DEG - CIRCULATE BOTTOMS UP - ROTATE FROM 7776' TO 7805' (TD)

Daily Cost: \$0**Cumulative Cost:** \$307,472

UTE TRIBAL 3-10-4-1E**Running casing****Date:** 4/28/2011

Capstar #328 at 7805. 8 Days Since Spud - SET UP PIPE RACKS AND PUMP 20 BBL DRY JOB IN PREPARING TO L/D DP - RIG DOWN LOGGERS - PLACE PIPE RACKS AND LOAD DP TO RUN IN HOLE OPEN ENDED TO RUN LOGS - RIH WITH DRILL PIPE TO 4405' - SERVICE RIG - WAIT ON HALLIBURTON SLIM HOLE LOGGING TOOLS - HALLIBURTON MAKING UP NEW HEAD ON THE WIRELINE REEL - BREAK OFF TOP DRIVE, WELL COMING IN UP DRILL PIPE DUE TO U-TUBING, CIRC BU AND SPOT BALANCE PILL - COUNT DRILL PIPE AND CASING ON LOCATION, MAKE UP GUIDE SHOE AND FLOAT TO SHOE TRACK - CLEAN AND PREP RIG FLOOR TO RIH WOTH CASING - POOH L/D DRILL PIPE FROM 4405' - JSA AND PJSM ON R/D OF LOGGING EQUIP, R/D LOGGERS - RIH WITH SLIM HOLE WIRELINE ASSEMBLY, LOGS TO BOTTOM, LOGGERS DEPTH 7760'

Daily Cost: \$0**Cumulative Cost:** \$366,492

UTE TRIBAL 3-10-4-1E**Rigging down****Date:** 4/29/2011

Capstar #328 at 7805. 9 Days Since Spud - NIPPLE DOWN AND CLEAN PITS. "RIG RELEASE FROM 3-10-4-1E" 04/29/2011 TO UT 13-2-4-1E - RD CEMENTERS, CLEAN LINES AND BEGIN TO CLEAN PITS - PREP RIG FLOOR AND BH CEMENT HEAD IN PLACE. - JSA REVIEW AND PJSM WITH CEMENTERS AND RIG CREW ON CEMENT JOB - PUMP FIRST STAGE OF CEMENT JOB, PUMPED SURE BOND TO PIT, OUR RETURNS F/1ST STAGE, FLOATS HELD - PUMP 2ND STAGE AND DISPL., 50 BBLs CEMENT TO SURFACE, CHECK DV TOOL, TOOL HELD. - RIH CASING, TAG BOTTOM AT 7758'. PU CASING HANGER TO CIRCULATE - CIRCULATE WHILE REMOVING PIPR RACKS AND PIPE HANDLER, BH RU CEMENT EQUIP. LAND CASG. **Finalized**

Daily Cost: \$0**Cumulative Cost:** \$536,449

Pertinent Files: Go to File List
