


STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT ☐

APPLICATION FOR PERMIT TO DRILL						1. WELL NAME and NUMBER RW 12A2-28B				
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT RED WASH				
4. TYPE OF WELL Gas Well <input type="checkbox"/> Coalbed Methane Well: NO <input type="checkbox"/>						5. UNIT or COMMUNITIZATION AGREEMENT NAME RED WASH				
6. NAME OF OPERATOR QEP ENERGY COMPANY						7. OPERATOR PHONE 303 308-3068				
8. ADDRESS OF OPERATOR 11002 East 17500 South, Vernal, Ut, 84078						9. OPERATOR E-MAIL debbie.stanberry@questar.com				
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU02025			11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>				
13. NAME OF SURFACE OWNER (if box 12 = 'fee')						14. SURFACE OWNER PHONE (if box 12 = 'fee')				
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')				
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>			19. SLANT VERTICAL <input checked="" type="checkbox"/> DIRECTIONAL <input type="checkbox"/> HORIZONTAL <input type="checkbox"/>				
20. LOCATION OF WELL	FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN			
LOCATION AT SURFACE	2375 FSL 860 FWL		NWSW	28	7.0 S	23.0 E	S			
Top of Uppermost Producing Zone	2375 FSL 860 FWL		NWSW	28	7.0 S	23.0 E	S			
At Total Depth	2375 FSL 860 FWL		NWSW	28	7.0 S	23.0 E	S			
21. COUNTY UINTAH			22. DISTANCE TO NEAREST LEASE LINE (Feet) 860			23. NUMBER OF ACRES IN DRILLING UNIT 10				
			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 926			26. PROPOSED DEPTH MD: 11266 TVD: 11266				
27. ELEVATION - GROUND LEVEL 5601			28. BOND NUMBER ESB000024			29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE A-36125/ 49-2153				
Hole, Casing, and Cement Information										
String	Hole Size	Casing Size	Length	Weight	Grade & Thread	Max Mud Wt.	Cement	Sacks	Yield	Weight
Surf	12.25	9.625	0 - 4915	36.0	N-80 LT&C	0.0	Halliburton Light , Type Unknown	460	3.12	11.0
							Halliburton Premium , Type Unknown	630	1.47	13.5
Prod	7.875	4.5	0 - 11266	11.6	HCP-110 LT&C	10.5	Halliburton Light , Type Unknown	610	3.18	11.0
							Halliburton Premium , Type Unknown	530	1.65	13.5
ATTACHMENTS										
VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES										
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER					<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN					
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)					<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER					
<input type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)					<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP					
NAME Valyn Davis			TITLE Regulatory Affairs Analyst				PHONE 435 781-4369			
SIGNATURE			DATE 09/14/2011				EMAIL Valyn.Davis@qepres.com			
API NUMBER ASSIGNED 43047519380000			APPROVAL  Permit Manager							

RECEIVED: September 20, 2011

QEP Energy Company
RW 12A2-28B
Summarized Drilling Procedure

1. Construct location per plat.
2. MIRU air drilling rig.
3. Pre-set conductor.
4. Nipple up diverter system.
5. Drill 12-1/4" hole to 4,915' with air/mist.
6. RIH with 9-5/8" 36# N-80 casing and cement same per program.
7. RDMO air drilling rig.
8. MIRU conventional drilling rig.
9. NU and test 5M BOPE.
10. Drill out of 9-5/8" shoe and down to 11,266' using conventional mud systems.
11. Log well. Triple or Quad-Combo (GR, NEU/DEN, IND, RES, SON)
12. RIH with 4-1/2" 11.6# HCP-110 casing and cement same per program.
13. Pressure test casing.
14. ND BOP's and NU remainder of wellhead. Set BPV.
15. RDMO.

CONFIDENTIAL

ONSHORE OIL & GAS ORDER NO. 1
QEP ENERGY COMPANY
RW 12A2-28B

DRILLING PROGRAM

ONSHORE OIL & GAS ORDER NO. 1 Approval of Operations on Onshore Federal Oil and Gas Leases

All lease and/or unit operations will be conducted in such a manner that full compliance is made with applicable laws, regulations (43 CFR 3100), Onshore Oil & Gas No. 1, and the approved plan of operations. The operator is fully responsible for the actions of its subcontractors. A copy of these conditions will be furnished the field representative to insure compliance.

1. Formation Tops

The estimated top of important geologic markers are as follows:

<u>Formation</u>	<u>Depth</u>
Uinta	Surface
Green River	3,021'
Mahogany	4,865'
Wasatch	6,361'
Mesaverde	8,741'
Sego	11,166'
TD	11,266'

2. Anticipated Depths of Oil, Gas, Water, and Other Mineral Bearing Zones

The estimated depths at which the top of the anticipated water, oil, gas, or other mineral bearing formations are expected to be encountered as follows:

<u>Substance</u>	<u>Formation</u>	<u>Depth</u>
Oil	Green River	3,021'
Gas	Wasatch	6,361'
Gas	Mesaverde	8,741'
Gas	Sego	11,166'

All fresh water and prospectively valuable minerals encountered during drilling will be recorded by depth and adequately protected. All oil and gas shows will be tested to determine commercial potential.

All water shows and water-bearing sands will be reported to the BLM in Vernal, Utah. Copies of State of Utah form OGC-8-X are acceptable. If flows are detected, samples will be submitted to the BLM along with any water analyses conducted. Fresh water will be obtained from Wonsits Valley water right A36125 (which was filed on May 7, 1964) or Red Wash water right # 49-2153 (which was filed on March 25, 1960). It was

ONSHORE OIL & GAS ORDER NO. 1

QEP ENERGY COMPANY

RW 12A2-28B

determined by the Fish and Wildlife Service that any water right number filed before 1989 is not depleting to the Upper Colorado River System, to supply fresh water for drilling purposes. All water resulting from drilling operations will be disposed of at Red Wash Central Battery Disposal site; SWSE, Section 27, T7S, R23E or Wonsits Valley Disposal Site; SWNW, Section 12, T8S, R21E.

3. Operator's Specification for Pressure Control Equipment

- A. An 11" 5000 psi double ram with blind rams and pipe rams, annular preventer and drilling spool or BOP with 2 side outlets.
- B. All BOP connections subject to pressure shall be flanged, welded or clamped.
- C. Kill line (2" min), 2 choke line valves (3" min), choke line (3" min), 2 kill line valves (2" min) and a check valve, 2 chokes with one remotely controlled from rig floor and a pressure gauge on choke manifold.
- D. Upper and Lower Kelly cock valves with handles and safety valve and subs to fit all drill string connections.
- E. IBOP or float sub available.
- F. Fill up line must be installed above the uppermost preventer.
- G. Ram type preventers and associated equipment shall be tested to approved stack working pressure if isolated by test plug or to 50 percent of internal yield pressure of casing whichever is less. BOP and related equipment shall meet the minimum requirements of Onshore Oil and Gas Order No. 2 for equipment and testing requirements, procedures, etc..., for a 5M system and individual components shall be operable as designed.

4. Casing Design:

Hole Size	Csg. Size	Top (MD)	Bottom (MD)	Wt.	Grade	Thread	Cond.	Expected MW(ppg)
17 1/2"	14"	Sfc	60'	Steel	Conductor	None	Used	N/A
12-1/4"	9-5/8"	Sfc	4,915'	36#	N-80	LTC	New	Air
7 7/8"	4-1/2"	Sfc	11,266'	11.6#	HCP-110	LTC	New	10.5

Casing Strengths:				Collapse	Burst	Tensile (min)
9-5/8"	36#	N-80	LTC	2,370 psi	5,120 psi	820,000 lb.
4 1/2"	11.6#	HCP-110	LTC	8,830 psi	10,710 psi	279,000 lb.

ONSHORE OIL & GAS ORDER NO. 1
QEP ENERGY COMPANY
RW 12A2-28B

Casing Design Factors

*The casing prescribed above meets or exceeds the below listed design factors.

Burst: 1.2
Collapse: 1.2
Tension: 1.6

Maximum anticipated mud weight: 10.5 ppg
Maximum anticipated surface treating pressure: 7,200 psi

5. Cementing Program

9-5/8" Surface Casing:

Lead Slurry: Surface (TOC) – 3,000'. 460 sks (1409 ft³) Halliburton Extendacem, 1 pps Granulite TR 1/4, 0.125 pps Poly-E-Flake, Slurry Weight 11.0 ppg, 3.12 ft³/sk, 50% XS in open hole only.

Tail Slurry: 3,000' – 4,915'. 630 sx (917 ft³) Halliburton Econocem, 0.2% HR-5 Retarder, 1.0 pps Granulite TR 1/4, 0.125 pps Poly-E-Flake, Slurry Weight 13.5 ppg, 1.47 ft³/sk, 50% XS in open hole.

4-1/2" Production Casing*:

Lead Slurry: 3,000' (TOC) – 8,741'. 610 sks (1,927 ft³) Halliburton Extendacem, 1 pps Granulite 1/4, 0.125 pps Poly-E-Flake, Slurry Weight 11.0 lb/gal, 3.18 ft³/sk, 50% excess over gauge in open hole only.

Tail Slurry: 8,741' – 11,266'. 530 sks (866 ft³), Halliburton Expandacem, 0.3% Super CBL (Expander), 0.6% HR-800 (Retarder), 1 pps Granulite TR 1/4, 0.125 pps Poly-E-Flake (LCM). Slurry Weight 13.5 lb/gal, 1.65 ft³/sk, 50% excess over gauge hole.

*Final cement volumes to be calculated from caliper log, if run.

6. Auxiliary Equipment

- A. Kelly Cock – yes
- B. Float at the bit – Yes
- C. Monitoring equipment on the mud system – PVT/Flow Show
- D. Full opening safety valve on the rig floor – Yes

ONSHORE OIL & GAS ORDER NO. 1
QEP ENERGY COMPANY
RW 12A2-28B

- E. Rotating Head – Yes
- F. Request for Variance:

Drilling surface hole with air:

A variance from 43 CFR 3160 Onshore Oil and Gas Order #2, Section III Requirements, subsection E. Special Drilling Operations is requested for the specific operation of drilling and setting surface casing on the subject well with a truck mounted air rig. The variance from the following requirements of Order #2 is requested because surface casing depth for this well is 50' into the Mahogany Bench formation and high pressures are not expected.

1. **Properly lubricated and maintained rotating head** – A diverter system in place of a rotating head. The diverter system forces the air and cutting returns to the reserve pit and is used to drill the surface casing.
2. **Blooi line discharge 100 feet from wellbore and securely anchored** – the blooi line discharge for this operation will be located 50 to 70 feet from the wellhead. This reduced length is necessary due to the smaller location size to minimize surface disturbance.
3. **Automatic igniter or continuous pilot light on blooi line** – a diffuser will be used rather than an automatic pilot/igniter. Water is injected into the compressed air and eliminates the need for a pilot light and the need for dust suppression equipment.
4. **Compressors located in the opposite direction from the blooi line a minimum of 100 feet from the wellbore** – compressors located within 50 feet on the opposite side of the wellbore from the blooi line and is equipped with a 1) emergency kill switch on the driller's console, 2) pressure relief valves on the compressors, 3) spark arrestors on the motors.
5. **Well Kill Fluid** – A suitable amount of water and weighting agents will be available in the reserve pit during air drilling operations to kill the well, if necessary. No overpressured zones are expected in the area.
6. **Deflector on the end of the blooi line** – QEP will mount a deflector unit at the end of the blooi line for the purpose of changing the direction and velocity of the air and cuttings flow into the reserve pit. Changing the velocity and direction of the cuttings and air will preserve the pit liner. In the event the deflector washes out due to erosion caused by the sand blasting effect of the cuttings, there will be no problem because the deflector is mounted on the very end of the blooi. A washed out deflector will be easily replaced.
7. **Flare Pit** – there will be no need of a flare pit during the surface hole air drilling operation because the blooi line is routed directly to the reserve pit. When the big rig arrives for the main drilling after setting surface casing, a flare box will be installed and all flare lines will be routed to the flare box.

ONSHORE OIL & GAS ORDER NO. 1
QEP ENERGY COMPANY
RW 12A2-28B

- G. Drilling below the 9-5/8" casing will be done with water based mud. Maximum anticipated mud weight is 10.5 ppg.
- H. No minimum quantity of weight material will be required to be kept on location.
- I. Gas detector will be used from intermediate casing depth to TD.

7. **Testing, logging and coring program**

- A. Cores – none.
- B. DST – none anticipated
- C. Logging – Mud logging – Intermediate Casing to TD
OH Logs: GR-SP-Induction, Neutron Density.
- D. Formation and Completion Interval:
 - Stimulation will be designed for the particular area of interest as encountered.

8. **Anticipated Abnormal Pressures and Temperatures, Other Potential Hazards**

No abnormal temperatures or pressures are anticipated. Maximum anticipated bottom hole pressure equals approximately 6,151 psi. Maximum anticipated bottom hole temperature is 210° F.

H2S has not been encountered in other wells drilled to similar depths in the general area.

ONSHORE OIL & GAS ORDER NO. 1
QEP ENERGY COMPANY
RW 12A2-28B

5M BOP STACK

Rotating Head

Spacer Spool

5M Annular

5M Double Ram

2" Kill Line


3" Choke Line

2" 5M 2" 5M 2" 5M
Check Manual Manual

3" 5M 3" 5M
Manual HCB

5M x 9 5/8" 5M Casing Head

ONSHORE OIL & GAS ORDER NO. 1
QEP ENERGY COMPANY
RW 12A2-28B

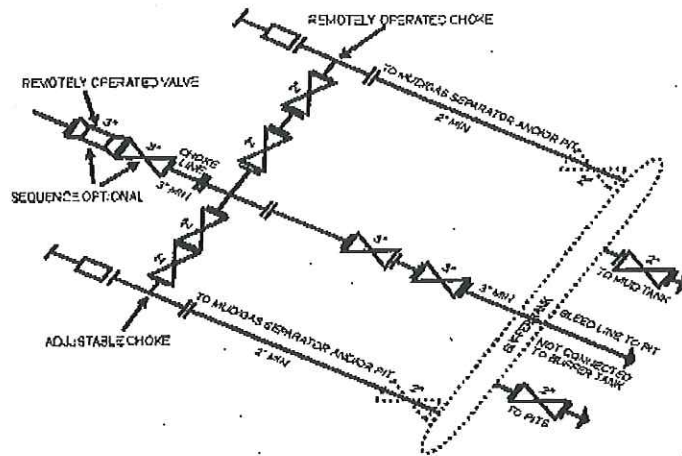

5M CHOKES MANIFOLD EQUIPMENT - CONFIGURATION OF CHOKES MAY VARY

Although not required for any of the choke manifold systems, buffer tanks are sometimes installed downstream of the choke assemblies for the purpose of manifolding the bleed lines together. When buffer tanks are employed, valves must be installed upstream to isolate a failure or malfunction without interrupting flow control. Though not shown on 28L 384, 1084, OR 1534 drawings, it would also be applicable to those situations.
[54 FR 39528, Sept. 27, 1989]

RW 12A2-28B
2,375' FSL & 860' FWL Sec 28 T7S R23E S.L.B.&M.
Uintah County, Utah
KB 5,615'
GL 5,601'

14" Conductor at 60'

Cemented to surface

Top of Production Lead Cement at 3,000'
Top of Surface Tail Cement at 3,000'

12-1/4" Open Hole

9-5/8" 36# N-80 @ 4,915'

7-7/8" Open Hole

Top of Production Tail Cement @ 8,741'

4 1/2" 11.6# HCP-110

11,266'

CONFIDENTIAL

T7S, R23E, S.L.B.&M.

QEP ENERGY COMPANY


Well location, RW #12A2-28B, located as shown in the NW 1/4 SW 1/4 of Section 28, T7S, R23E, S.L.B.&M., Uintah County, Utah.

BASIS OF ELEVATION

BENCH MARK 20EAM LOCATED IN THE SE 1/4 OF SECTION 35, T8S, R21E, S.L.B.&M. TAKEN FROM THE OURAY SE, QUADRANGLE, UTAH, UINTAH COUNTY, 7.5 MINUTE QUAD. (TOPOGRAPHIC MAP) PUBLISHED BY THE UNITED STATES DEPARTMENT OF THE INTERIOR, GEOLOGICAL SURVEY. SAID ELEVATION IS MARKED AS BEING 4697 FEET.

BASIS OF BEARINGS

BASIS OF BEARINGS IS A G.P.S. OBSERVATION.

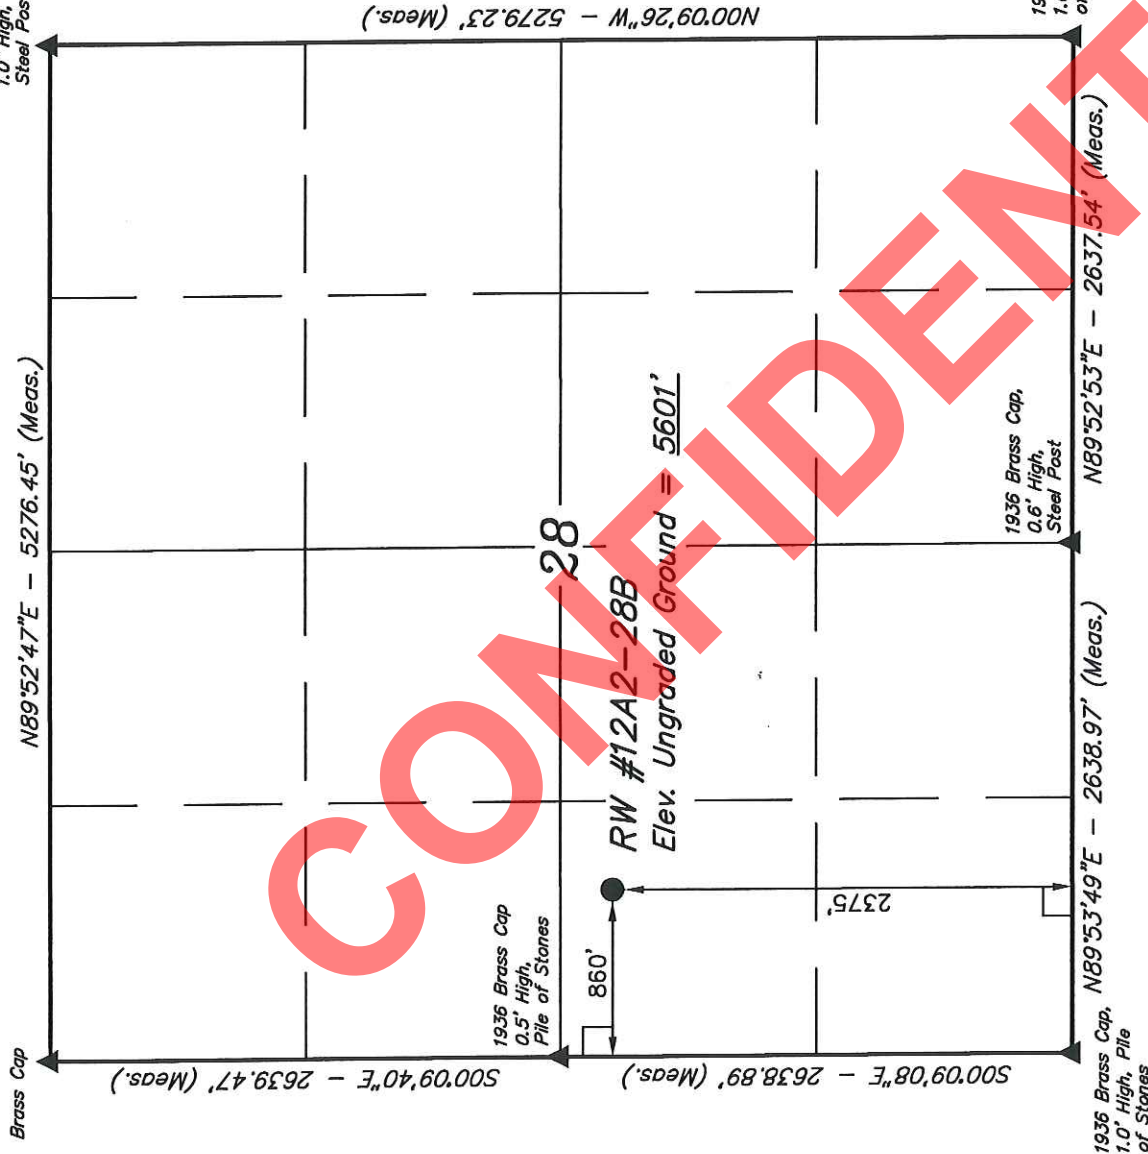

CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

REGISTERED LAND SURVEYOR
REGISTRATION NO. 161319
STATE OF UTAH

08-24-11

UINTAH ENGINEERING & LAND SURVEYING
85 SOUTH 200 EAST - VERNAL, UTAH 84078
(435) 789-1017

SCALE 1" = 1000'	DATE SURVEYED: 08-22-11	DATE DRAWN: 08-23-11
PARTY A.F. B.A. K.O.	REFERENCES G.L.O. PLAT	
WEATHER WARM	FILE	QEP ENERGY COMPANY

LEGEND:

- = 90° SYMBOL
- = PROPOSED WELL HEAD.
- ▲ = SECTION CORNERS LOCATED.

(NAD 83)
LATITUDE = 40°10'47.36" (40.179822)
LONGITUDE = 109°20'18.49" (109.338469)
(NAD 27)
LATITUDE = 40°10'47.49" (40.179858)
LONGITUDE = 109°20'16.04" (109.337789)

QEP ENERGY COMPANY

RW #12A2-28B

LOCATED IN UINTAH COUNTY, UTAH

SECTION 28, T7S, R23E, S.L.B.&M.

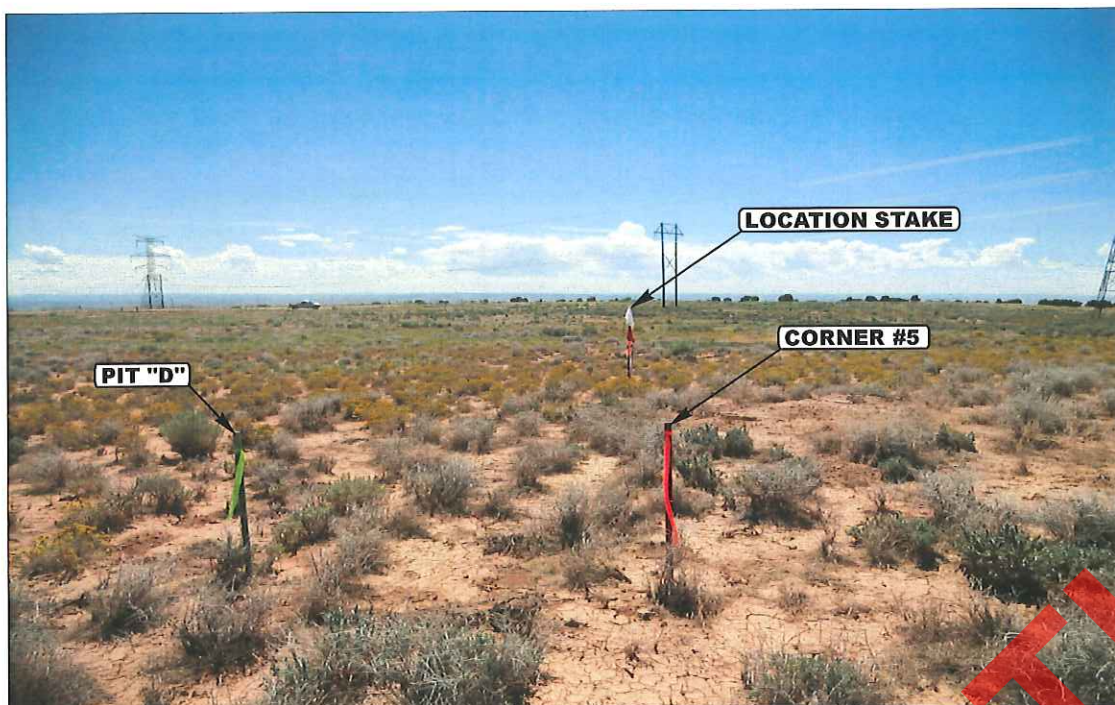


PHOTO: VIEW FROM CORNER #5 TO LOCATION STAKE

CAMERA ANGLE: SOUTHERLY

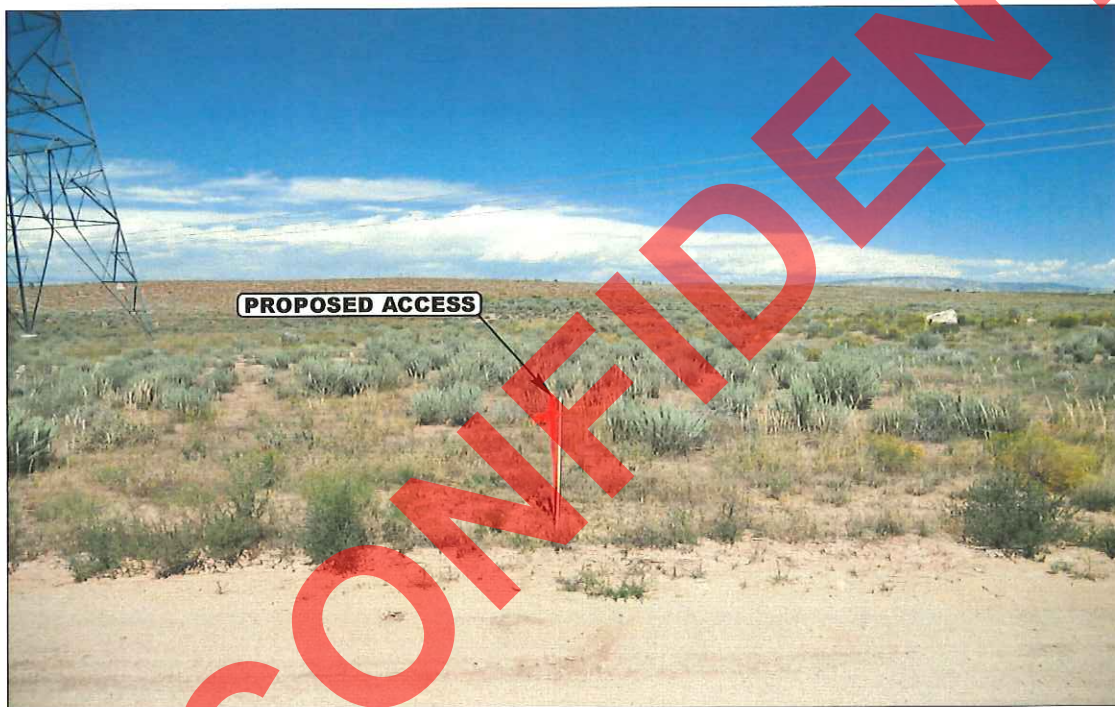


PHOTO: VIEW FROM BEGINNING OF PROPOSED ACCESS

CAMERA ANGLE: NORTHERLY



- Since 1964 -

**U
E
L
S**

Uintah Engineering & Land Surveying

85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813

LOCATION PHOTOS

08 **23** **11**
MONTH DAY YEAR

PHOTO

TAKEN BY: A.F.

DRAWN BY: S.F.

REVISED: 00-00-00

QEP ENERGY COMPANY

LOCATION LAYOUT FOR

RW #12A2-28B

SECTION 28, T7S, R23E, S.L.B.&M.


2375' FSL 860' FWL

FIGURE #1

SCALE: 1" = 50'

DATE: 08-23-11

DRAWN BY: K.O.

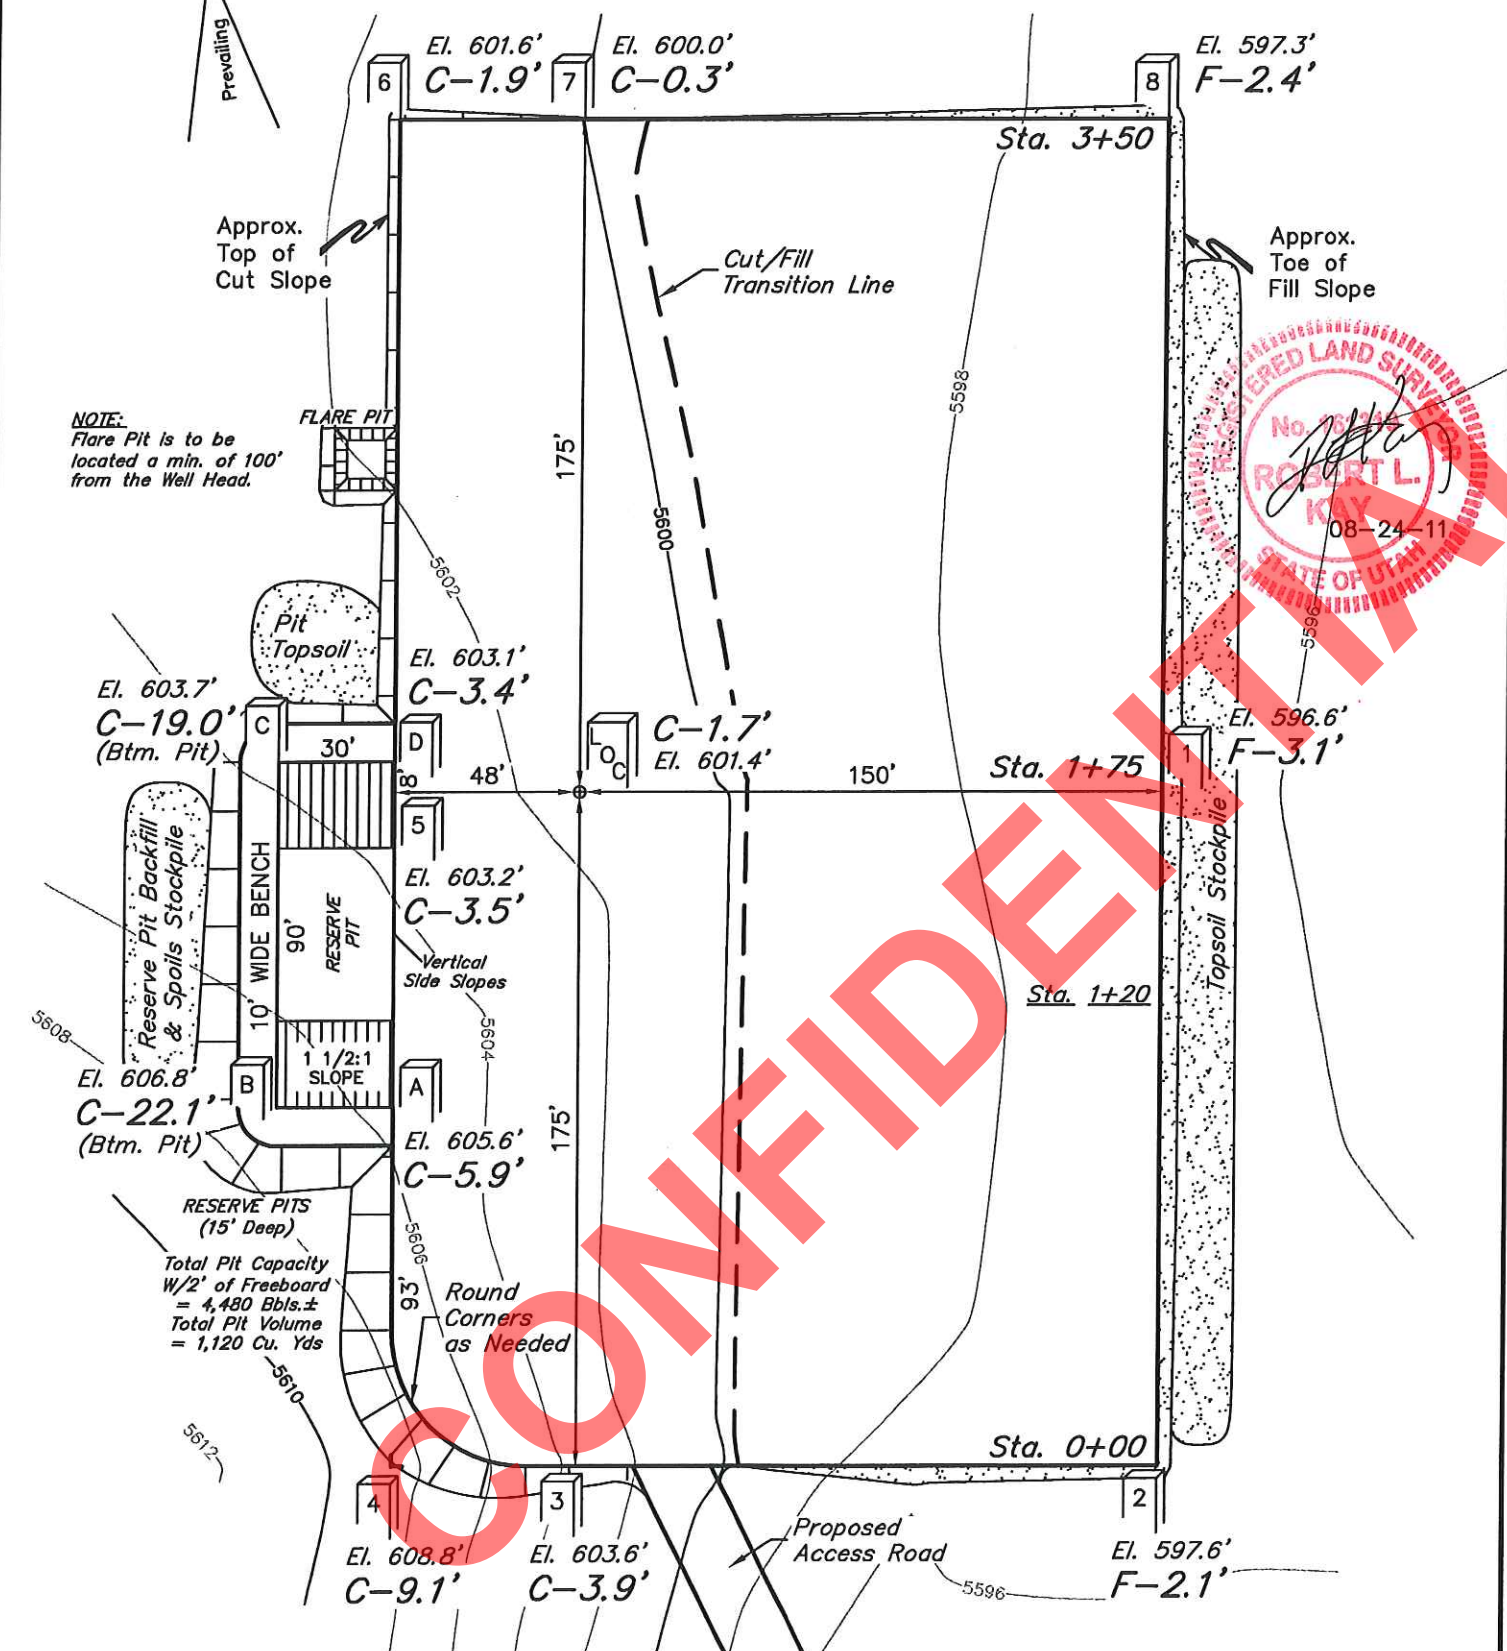

Elev. Ungraded Ground At Loc. Stake = 5601.4'
FINISHED GRADE ELEV. AT LOC. STAKE = 5599.7'

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East * Vernal, Utah 84078 * (435) 789-1017

QEP ENERGY COMPANY

TYPICAL CROSS SECTIONS FOR

RW #12A2-28B






SECTION 28, T7S, R23E, S.L.B.&M.

2375' FSL 860' FWL

FIGURE #2

X-Section
Scale
1" = 50'

DATE: 08-23-11
DRAWN BY: K.O.
REV: 09-12-11



NOTE:

Topsoil should not be
Stripped Below Finished
Grade on Substructure Area.

APPROXIMATE ACREAGES

WELL SITE DISTURBANCE = ± 1.968 ACRES
ACCESS ROAD DISTURBANCE = ± 0.410 ACRES
PIPELINE DISTURBANCE = ± 0.188 ACRES
TOTAL = ± 2.566 ACRES

* NOTE:
FILL QUANTITY INCLUDES
5% FOR COMPACTION

APPROXIMATE YARDAGES

(6") Topsoil Stripping = 1,540 Cu. Yds.
Remaining Location = 3,980 Cu. Yds.
TOTAL CUT = 5,520 CU.YDS.
FILL = 3,420 CU.YDS.

EXCESS MATERIAL = 2,100 Cu. Yds.
Topsoil & Pit Backfill = 2,100 Cu. Yds.
(1/2 Pit Vol.)
EXCESS UNBALANCE = 0 Cu. Yds.
(After Interim Rehabilitation)

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East * Vernal, Utah 84078 * (435) 789-1017

QEP ENERGY COMPANY

TYPICAL RIG LAYOUT FOR

RW #12A2-28B

SECTION 28, T7S, R23E, S.L.B.&M.

2375' FSL 860' FWL

FIGURE #3

SCALE: 1" = 50'


DATE: 08-23-11

DRAWN BY: K.O.



NOTE:
Flare Pit is to be
located a min. of 100'
from the Well Head.

FLARE PIT

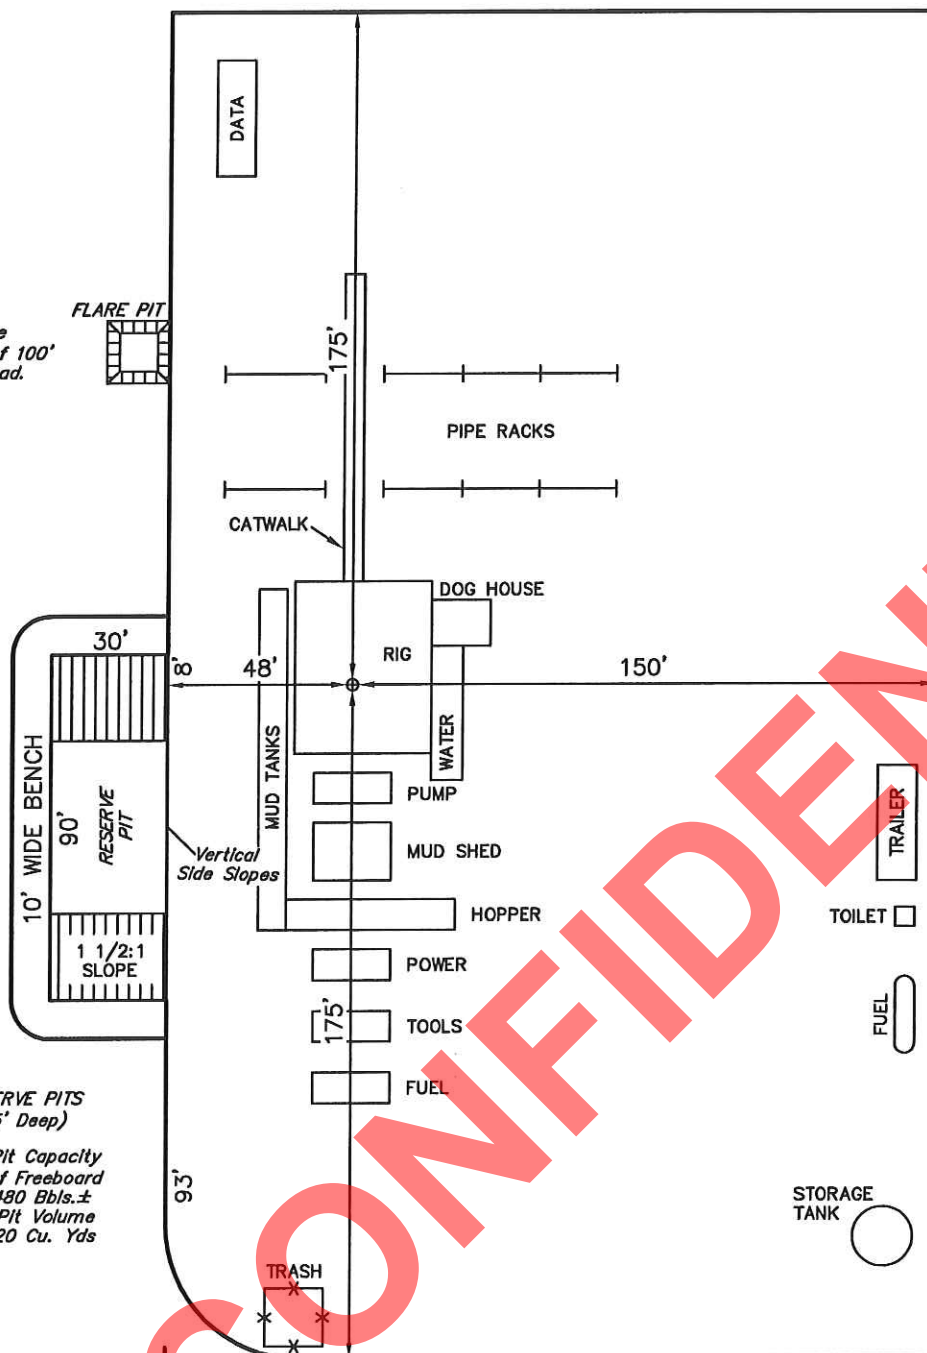

RESERVE PITS
(15' Deep)

Total Pit Capacity
W/2' of Freeboard
= 4,480 Bbls.±
Total Pit Volume
= 1,120 Cu. Yds



QEP ENERGY COMPANY
PRODUCTION FACILITY LAYOUT FOR
RW #12A2-28B
SECTION 28, T7S, R23E, S.L.B.&M.
2375' FSL 860' FWL

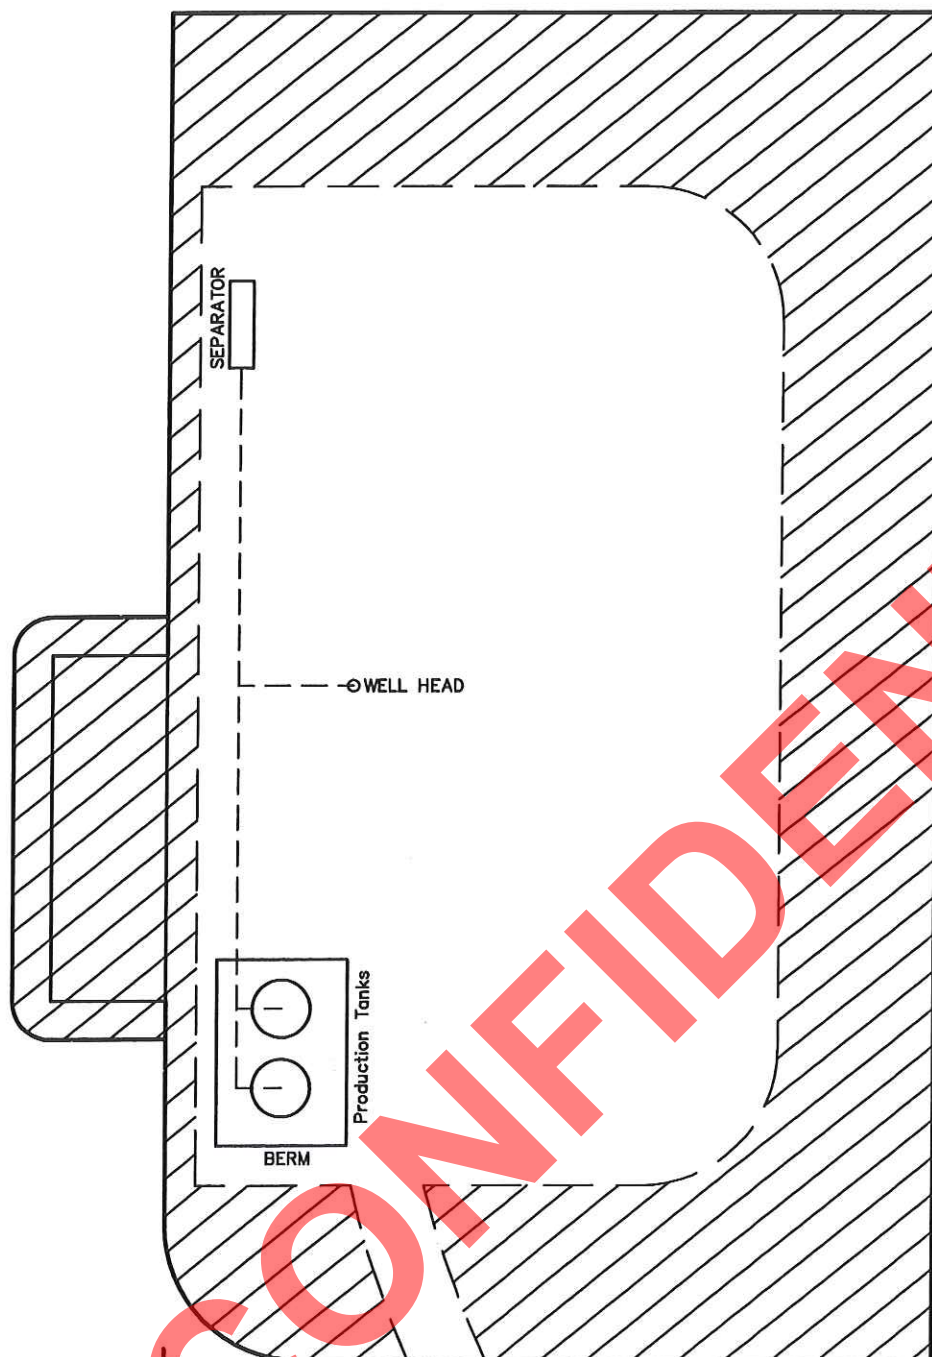


FIGURE #4

SCALE: 1" = 50'

DATE: 08-23-11

DRAWN BY: K.O.



APPROXIMATE ACREAGES
UN-RECLAIMED = ± 0.903 ACRES




RECLAIMED AREA

QEP ENERGY COMPANY
RW #12A2-28B
SECTION 28, T7S, R23E, S.L.B.&M.

PROCEED IN AN EASTERLY, THEN SOUTHERLY DIRECTION FROM VERNAL, UTAH ALONG U.S. HIGHWAY 40 APPROXIMATELY 3.9 MILES TO THE JUNCTION OF STATE HIGHWAY 45; EXIT RIGHT AND PROCEED IN A SOUTHERLY DIRECTION APPROXIMATELY 19.2 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE WEST; TURN RIGHT AND PROCEED IN A WESTERLY DIRECTION APPROXIMATELY 0.3 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE SOUTH; TURN LEFT AND PROCEED IN A SOUTHERLY DIRECTION APPROXIMATELY 0.4 MILES TO THE JUNCTION OF THIS ROAD AND AN EXISTING ROAD TO THE WEST; TURN RIGHT AND PROCEED IN A WESTERLY DIRECTION APPROXIMATELY 0.1 MILES TO THE BEGINNING OF THE PROPOSED ACCESS TO THE NORTH; FOLLOW ROAD FLAGS IN A NORTHERLY, THEN NORTHEASTERLY DIRECTION APPROXIMATELY 596' TO THE PROPOSED LOCATION

TOTAL DISTANCE FROM VERNAL, UTAH TO THE PROPOSED WELL LOCATION IS APPROXIMATELY 24.0 MILES.

CONFIDENTIAL

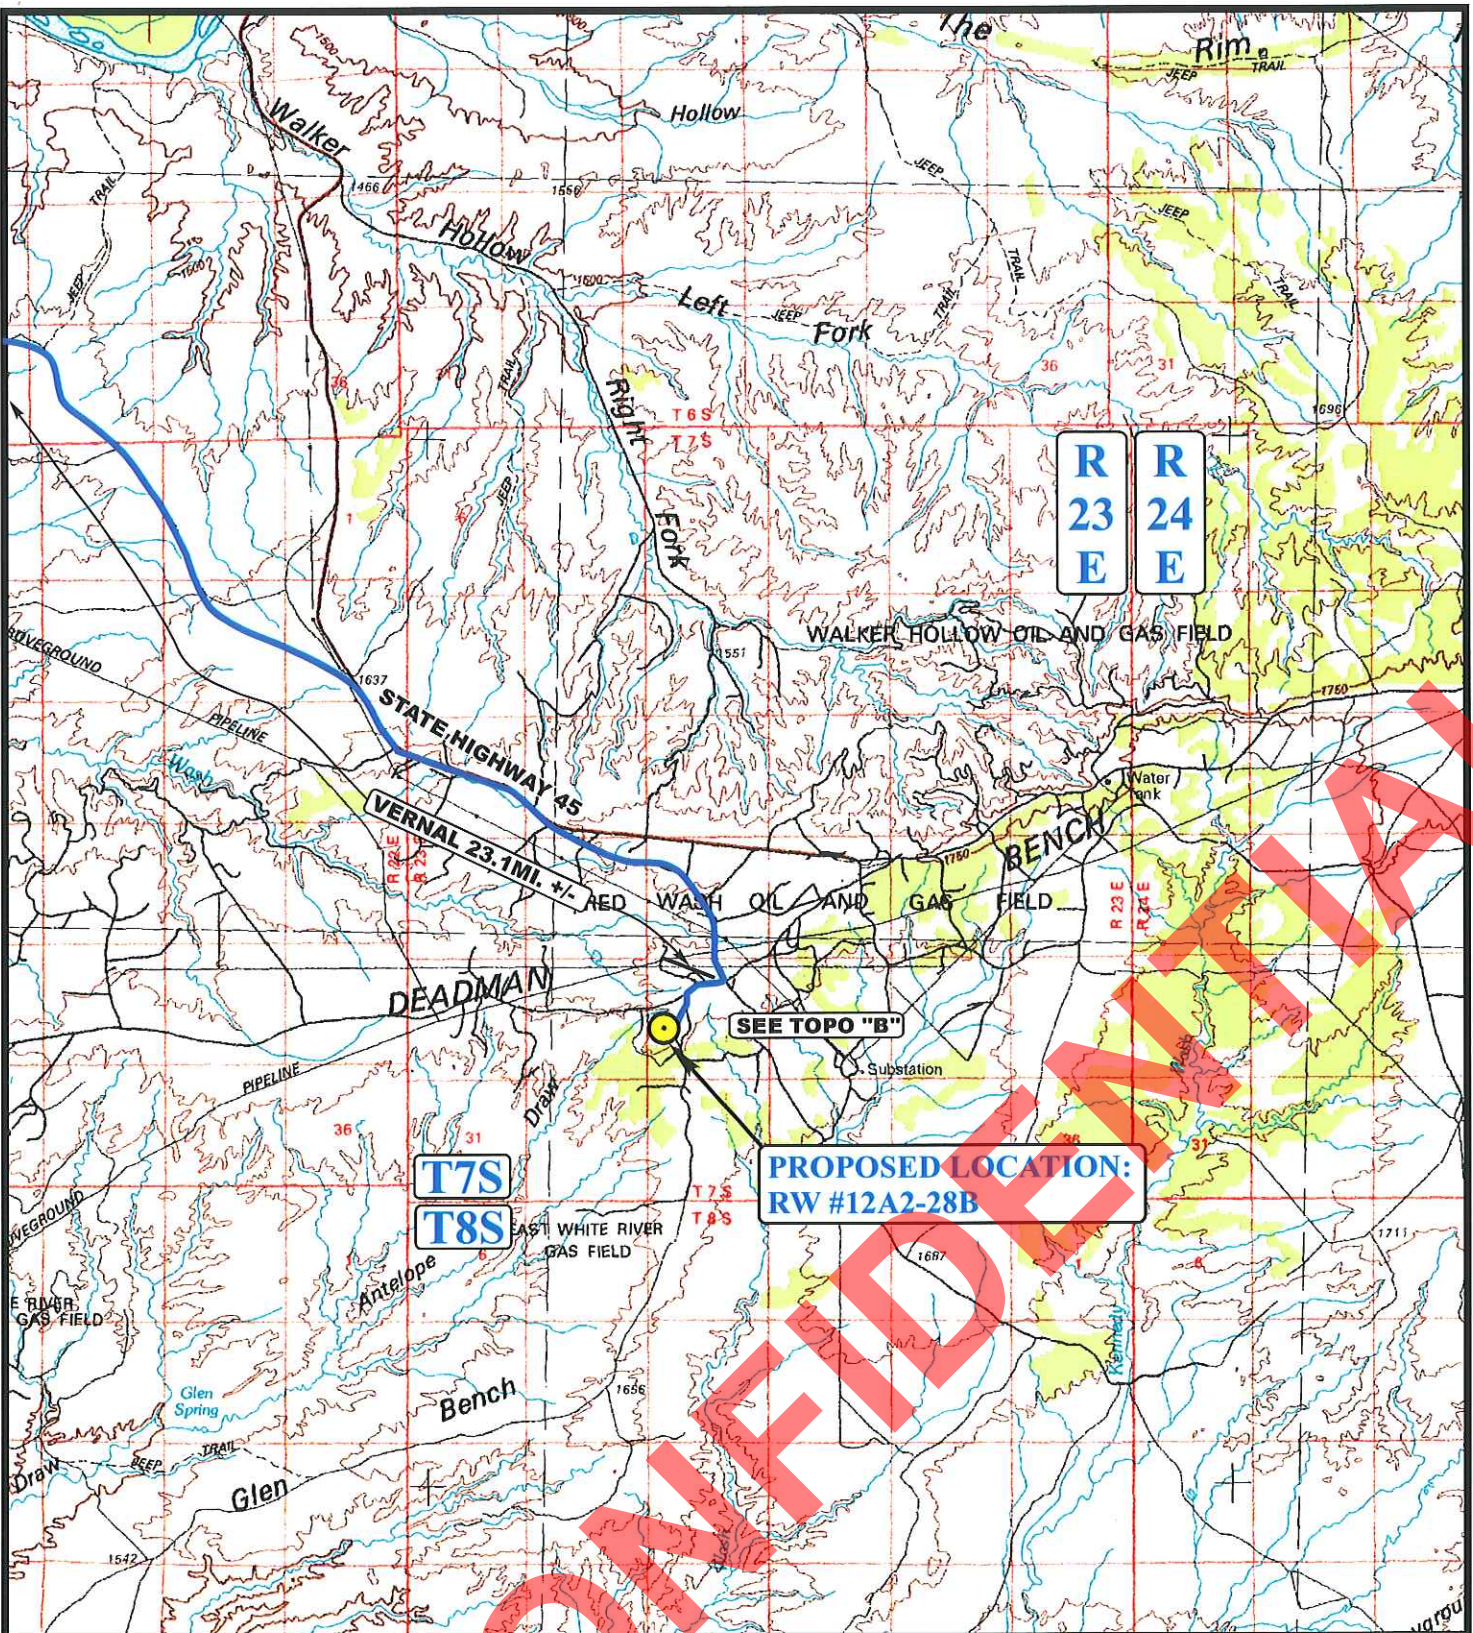

LEGEND:

 **PROPOSED LOCATION**

N

QEP ENERGY COMPANY

RW #12A2-28B

SECTION 28, T7S, R23E, S.L.B.&M.

2375' FSL 860' FWL



Uintah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 (435) 789-1017 * FAX (435) 789-1813

**ACCESS ROAD
 MAP**


08 23 11
 MONTH DAY YEAR

SCALE: 1:100,000

DRAWN BY: S.F.

REVISED: 00-00-00



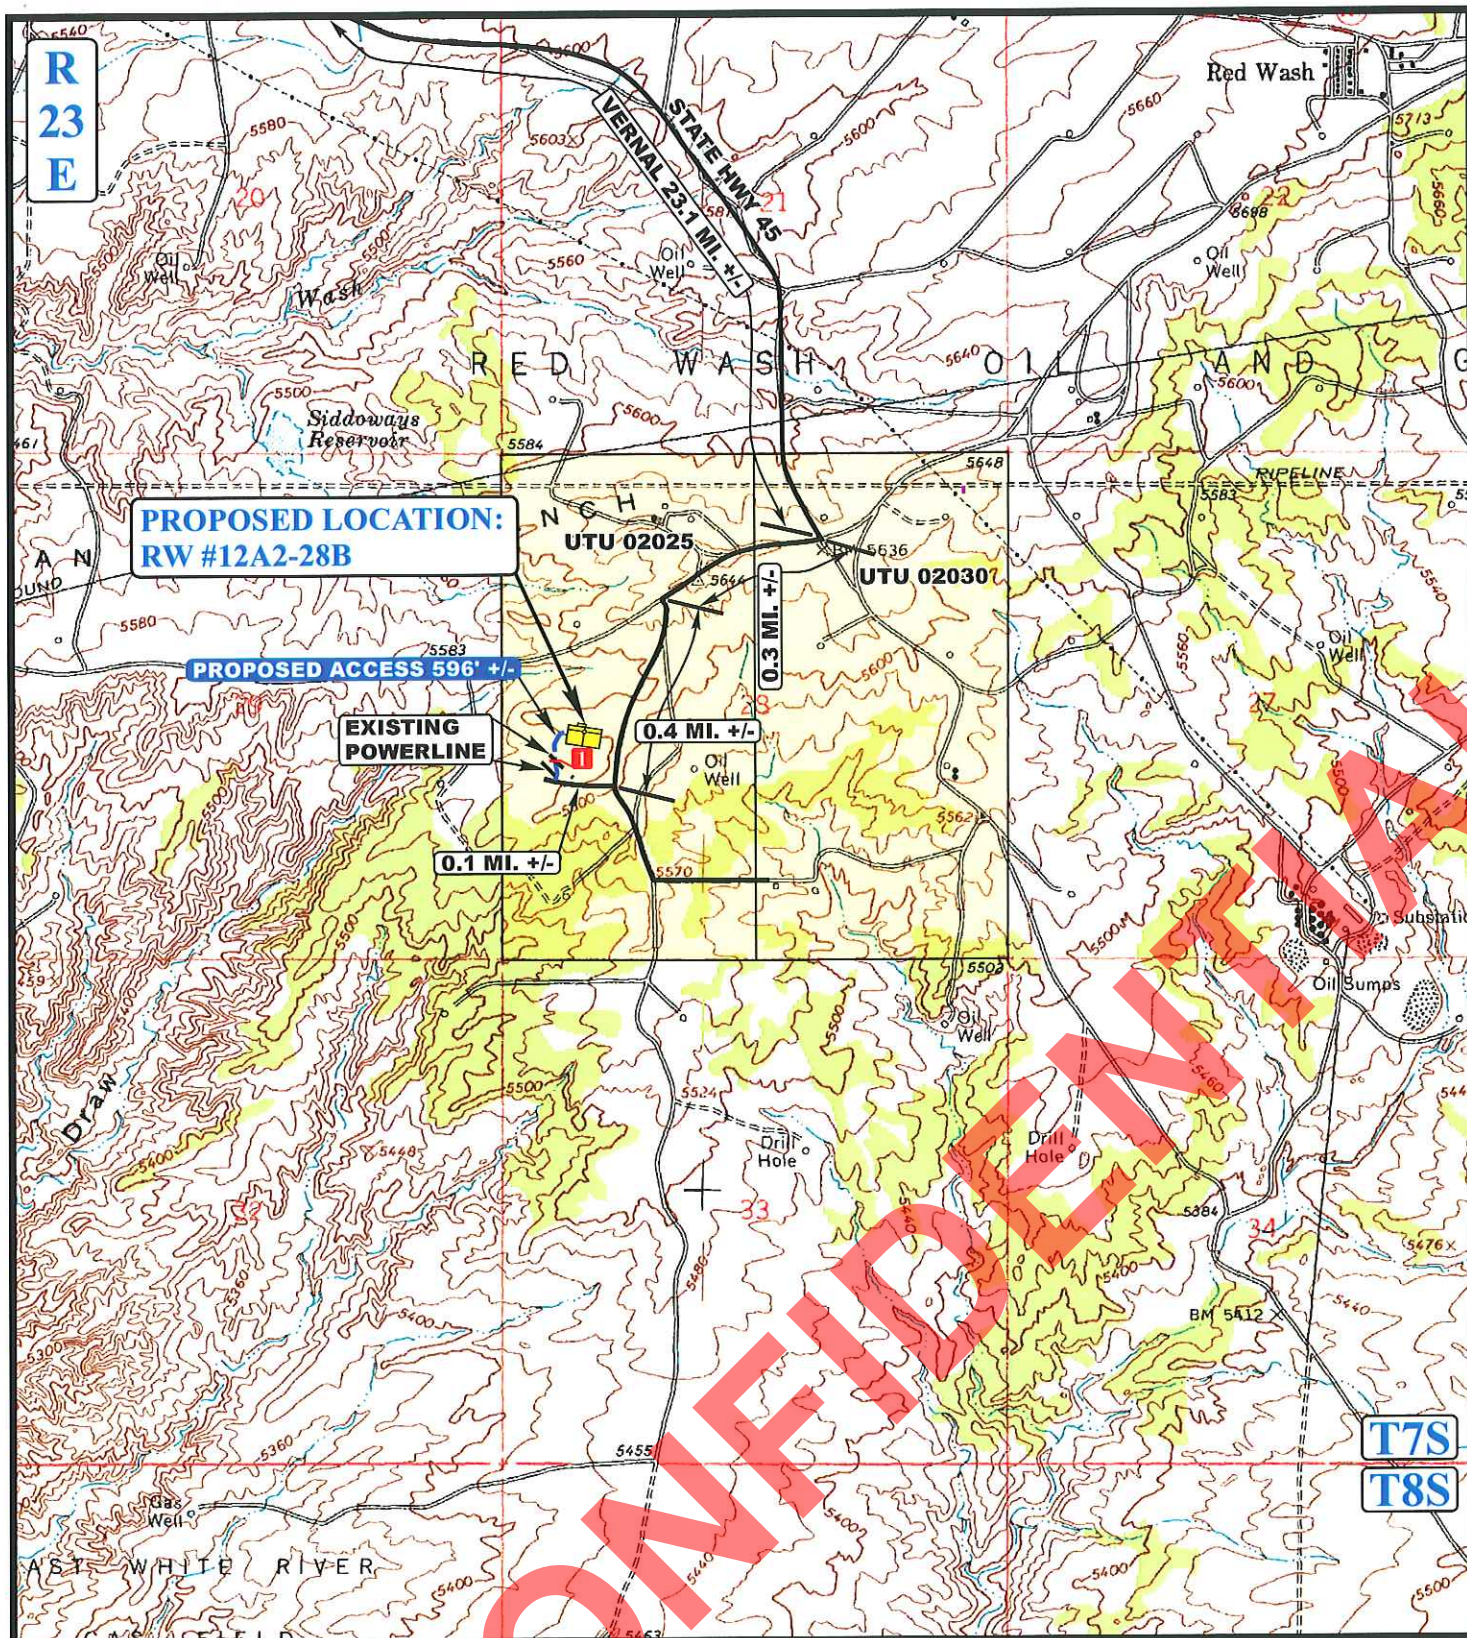

LEGEND:

- EXISTING ROAD
- - - PROPOSED ACCESS ROAD
- - - EXISTING POWER LINE
- I 18" CMP REQUIRED

QEP ENERGY COMPANY

RW #12A2-28B
SECTION 28, T7S, R23E, S.L.B.&M.
2375' FSL 860' FWL



Uintah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 (435) 789-1017 * FAX (435) 789-1813




ACCESS ROAD
MAP

08 23 11
 MONTH DAY YEAR

SCALE: 1" = 2000' DRAWN BY: S.F. REVISED: 00-00-00

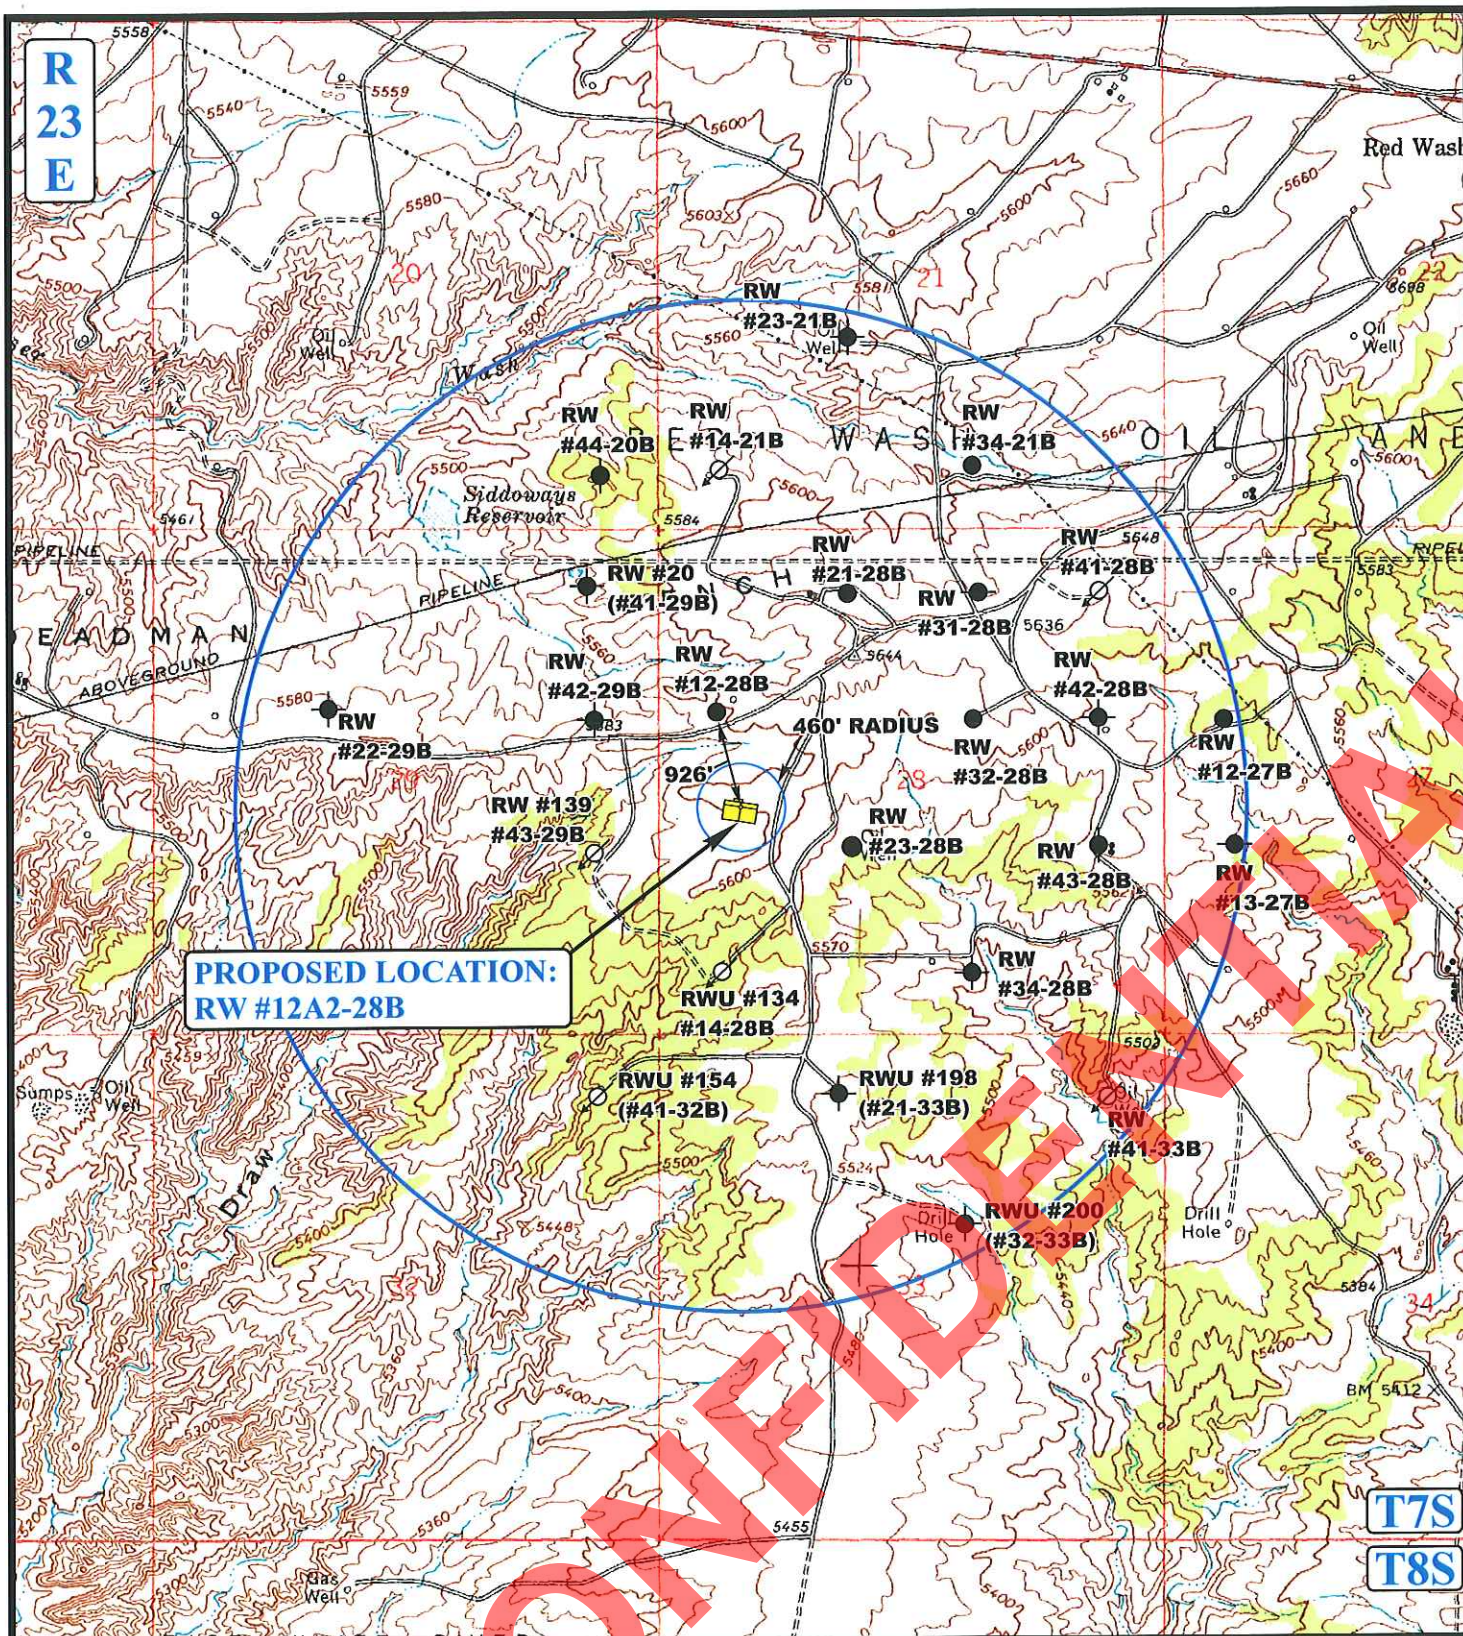

**LEGEND:**

- DISPOSAL WELLS
- PRODUCING WELLS
- SHUT IN WELLS
- ABANDONED WELLS
- TEMPORARILY ABANDONED

QEP ENERGY COMPANY

RW #12A2-28B
SECTION 28, T7S, R23E, S.L.B.&M.
2375' FSL 860' FWL



Uintah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 (435) 789-1017 * FAX (435) 789-1813



TOPOGRAPHIC
MAP


08 23 11
 MONTH DAY YEAR

SCALE: 1" = 2000'

DRAWN BY: S.F.

REVISED: 00-00-00



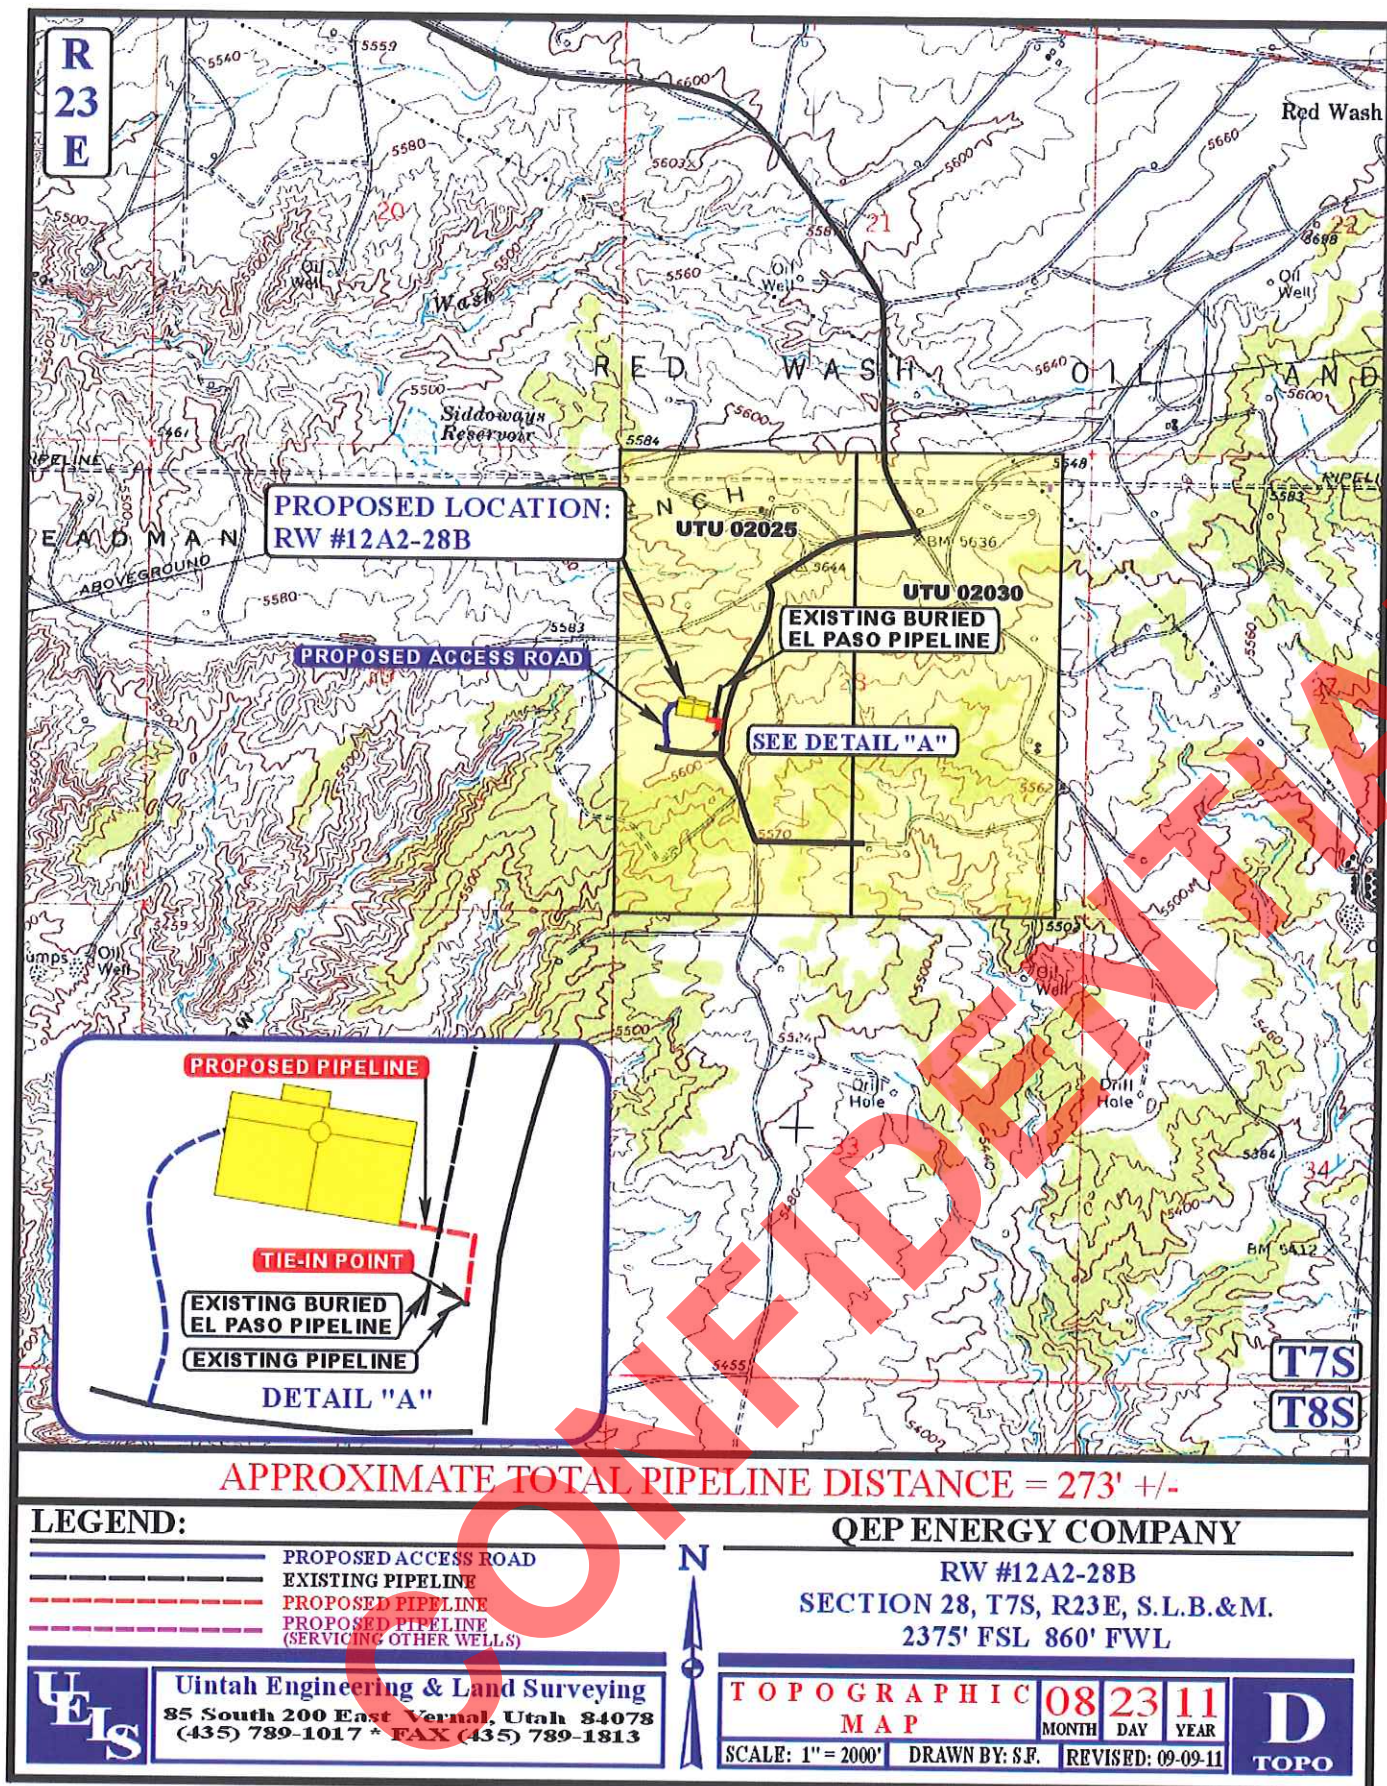

QEP ENERGY COMPANY
REFERENCE MAP: AREA OF VEGETATION
RW #12A2-28B

LOCATED IN UINTAH COUNTY, UTAH
SECTION 28, T7S, R23E, S.L.B.&M.



NOTE:

BEGINNING OF REFERENCE AREA

UTM NORTHING: 14596691.992

UTM EASTING: 2104304.385

(NAD 83) LATITUDE: 40.180219

(NAD 83) LONGITUDE: -109.339225

END OF REFERENCE AREA


UTM NORTHING: 14596733.857

UTM EASTING: 2104108.000

(NAD 83) LATITUDE: 40.180328

(NAD 83) LONGITUDE: -109.339925

PHOTO: VIEW FROM BEGINNING OF REFERENCE AREA

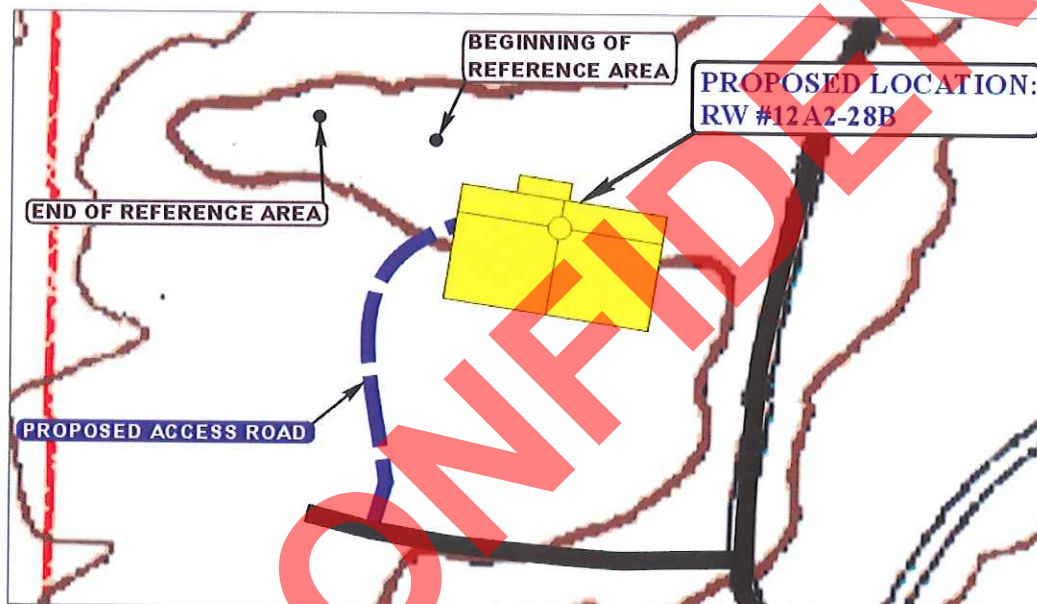

- Since 1964 -

U E L S

Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(435) 789-1017 * FAX (435) 789-1813

SCALE: 1" = 300'

09	09	11	REF.
MONTH	DAY	YEAR	
TAKEN BY: A.F.		DRAWN BY: S.F.	REVISED: 00-00-00

Additional Operator Remarks

QEP Energy Company proposes drill a vertical gas well to a depth of 11,266' to test the Mesa Verde Formation. The 10- and 20-acre Mesa Verde wells being proposed are part of a pilot program that is instrumental in QEP's determination of ultimate well density in the Red Wash field.

If productive, casing will be run and the well completed. If dry, the well will be plugged and abandoned as per BLM and State of Utah requirements.

Please see Onshore Order No. 1.

Please be advised that QEP Energy Company agrees to be responsible under the terms and conditions of the lease for the operations conducted upon the lease lands.

Bond coverage for this well is provided by Bond No.ESB000024. The principal is QEP Energy Company via surety as consent as provided for the 43 CFR 3104.2.

CONFIDENTIAL

**QEP ENERGY COMPANY
RW 12A2-28B
2375' FSL 860' FWL
NWSW, SECTION 28, T7S, R23E
UINTAH COUNTY, UTAH
LEASE # UTU-02025**

**ONSHORE ORDER NO. 1
MULTI – POINT SURFACE USE & OPERATIONS PLAN**

An onsite inspection was conducted for the RW 12A2-28B on September 8, 2011. Weather conditions were sunny at the time of the onsite. In attendance at the inspection were the following individuals:

Kevin Sadlier	Bureau of Land Management
Holly Sadlier	Bureau of Land Management
Stephanie Tomkinson	QEP Energy Company
Ryan Angus	QEP Energy Company
Valyn Davis	QEP Energy Company
Andy Floyd	Uintah Engineering & Land Surveying

1. Existing Roads:

The proposed well site is approximately 24 miles South of Vernal, Utah.

Refer to Topo Maps A and B for location of access roads within a 2 – mile radius.

All existing roads will be maintained and kept in good repair during all phases of operation.

2. Planned Access Roads:

There will be a new access road approximately 596' in length, containing approximately .410 acres. The access road will be crowned and ditched with a running surface of 18 feet and a maximum disturbed width of 30'. Any additional disturbance required due to intersections or sharp curves will be discussed at the on-site and approved by the BLM/VFO AO. Graveling or capping the roadbed will be performed as necessary to provide a well constructed safe road. Should conditions warrant, rock, gravel or culverts will be installed as needed. Surface disturbance and vehicular traffic will be limited to the approved location and access route or, as proposed by the Operator.

Access roads and surface disturbing activities will conform to standards outlined in the BLM and Forest Service publication: Surface Operating Standards for Oil and gas Exploration and Development, Fourth Edition 2006. The road surface and shoulders will be kept in a safe and usable condition and will be maintained in accordance with the original construction standards. All drainage ditches and culverts will be kept clear and free-flowing and will be maintained according to original construction standards. The access road disturbed area will be kept free of trash during operations. All traffic will be confined to the approved road running

surface. Road drainage crossings shall be of the typical dry creek drainage crossing type. Crossings shall be designed so they will not cause excess siltation or accumulation of debris in the drainage nor shall the drainage be blocked by the roadbed. If culverts are needed, the location and size of the culverts will be proposed during the on-site. The operator will clean and maintain approved culverts as needed. Erosion of drainage ditches by runoff water shall be prevented by diverting water off at frequent intervals by means of cutouts. Should mud holes develop, the holes shall be filled in and detours around the holes avoided. When snow is removed from the road during the winter months, the snow should be pushed outside of the borrow ditches, and the turnouts kept clear so that snowmelt will be channeled away from the road.

Refer to Topo Map B for the location of the proposed access road.

3. **Location of Existing Wells Within a 1 – Mile Radius:**

Please refer to Topo Map C.

4. **Location of Existing & Proposed Facilities:**

The following guidelines will apply if the well is productive.

A containment dike will be constructed completely around those production facilities which contain fluids (i.e., production tanks, produced water tanks). These dikes will be constructed of compacted impervious subsoil; hold 110% of the capacity of the largest tank; and, be independent of the back cut. If a Spill Prevention, Control, and Countermeasure (SPCC) Plan is required by the Environmental Protection Agency, the containment dike may be expanded to meet SPCC requirements with approval by the BLM/VFO AO. The specific APD will address additional capacity if such is needed due to environmental concerns. The use of topsoil for the construction of dikes will not be allowed.

All loading lines will be placed inside the berm surrounding the tank batteries.

All permanent (on site six months or longer) above the ground structures constructed or installed, including pumping units, will be painted a color approved by the State.

It was determined on the onsite by the BLM VFO AO that the facilities will be painted Covert Green.

Refer to Topo Map D for the location of the proposed pipeline.

The proposed surface pipeline will be constructed utilizing existing disturbed areas to minimize surface disturbance. No construction activities will be allowed outside of the proposed pipeline.

Prior to construction, the Permittee will develop a plan of installation to minimize surface disturbance. Pipe will be strung along the pipeline route with either a flatbed trailer and rubber tired backhoe or a tracked typed side boom. Where

surface conditions do not allow the pipe to be strung using conventional methods, the Permittee will utilize pull sections to run the fabricated pipe through the area from central staging areas along the pipeline route.

Upon completion of stringing activities the Permittee will fabricate the pipeline on wooden skids adjacent to the centerline of the pipeline route using truck mounted welding machines. All fabricated piping will be lowered off of the wooden skids and placed along the centerline. Upon completion of all activities, the wooden skids will be removed from the pipeline route using a flatbed truck or flatbed truck and trailer.

When the surface terrain prohibits the Permittee from safely installing the pipeline along the pipeline route, grading of the route will be required. Prior to installing the pipeline in these areas a plan will be developed to safely install the pipeline while minimizing grading activities and surface disturbances. Additionally, erosion control Best Management Practices will be installed as needed prior to the start of any grading activities. Surface grading will be limited to what is needed to safely install the pipeline. Track type bulldozers and track type backhoes will be utilized for grading activities.

Upon completion of the pipeline installation, the pipeline route will be restored to the pre-disturbance surface contours.

The proposed pipeline will be a surface 10" or smaller, 273' in length, containing .188 acres.

Road Crossings

Fusion Bond or concrete coated pipe will be used for all road crossings to alleviate future corrosion.

All pipe and fittings used for road crossings will be prefabricated within the proposed pipeline route to minimize the duration of open pipe trench across the roadway. Pipe used for road crossings will be isolated on each end with a flange set and insulation kit and cathodically protected with a magnesium type anode. Adequately sized equipment will be used for minor and major road crossings. Depth of cover for minor roads will be >4' and the depth of cover for major roads will be >6'.

Prior to lowering the pipe in the trench, the Permittee will "Jeep" the pipe to locate and repair any holidays in the pipe coating. Upon lowering the pipe in the trench, 6" of bedding and a minimum of 6" of shading will be installed to protect the pipe using either native soils <1" in diameter or imported sand. Pipe trenches that extend across gravel roads will be backfilled with native soils to within 8" of the driving surface and capped with 3/4" road base. Pipe trenches that extend across asphalt paved roads will be backfilled to 4" of the driving surface with 3/4" road base and capped asphalt material.

5. Location and Type of Water Supply:

Water for drilling purposes would be obtained from Wonsits Valley Water Right # A 36125 (which was filed on May 7, 1964) or Red Wash Water Right # 49-2153

(which was filed on March 25, 1960). It was determined by the Fish and Wildlife Service that any water right number filed before 1989 is not depleting to the Upper Colorado River System.

6. Source of Construction Materials:

Surface and subsoil materials in the immediate area will be utilized.

Any gravel will be obtained from a commercial source.

The use of materials under BLM jurisdiction will conform with 43 CFR 3610.2-3.

7. Methods of Handling Waste Materials:

Drill cuttings will be contained and buried in the reserve pit.

Drilling fluids including salts and chemicals will be contained in the reserve pit. Upon termination of drilling and completion operations, the liquid contents of the reserve pit will be used at the next drill site or will be removed and disposed of at an approved waste disposal facility within 6 months after drilling is terminated. Immediately upon well completion, any hydrocarbons in the pit shall be removed in accordance with 43 CFR 3162.7-1.

Unless specified in the site specific APD, the reserve pit will be constructed on the location and will not be located within natural drainages, where a flood hazard exists or surface runoff will or damage the pit walls. The reserve pit will be constructed so that it will not leak, break, or allow discharge of liquids.

It will be determined at the on-site inspection if a pit liner is necessary, the reserve pit will be lined with a synthetic reinforced liner, a minimum of 20 millimeters thick, with sufficient bedding used to cover any rocks. The liner will overlap the pit walls and be covered with dirt and/or rocks to hold it in place.

No trash or scrap will be disposed of in the pit.

Reserve pit leaks are considered an undesirable event and will be orally reported to the AO.

After first production, produced wastewater will be confined to the approved pit or storage tank for a period not to exceed 90 days.

After the 90 day period, the produced water will be contained in tanks on location and then hauled by truck to one of the following pre-approved disposal sites:

Red Wash Disposal well located in the SESE, Section 28, T7S, R23E,
West End Disposal located in the NESE, Section 28, T7S, R22E.

Produced water, oil, and other byproducts will not be applied to roads or well pads for the control of dust or weeds. The dumping of produced fluids on roads, well sites, or other areas will not be allowed.

Any spills of oil, gas, salt water, or other noxious fluids will be immediately cleaned up and removed to an approved disposal site. The spills will be reported to the AO and other authorities as appropriate.

A chemical porta-toilet will be furnished with the drilling rig. The chemical porta-toilet wastes will be hauled to Ashley Valley Sewer and Water System for disposal.

Garbage, trash, and other waste materials will be collected in a portable, self-contained, fully enclosed trash cage during operations. Trash will not be burned on location. All debris and other waste material not contained in the trash cage will be cleaned up and removed from the location immediately after removal of the drilling rig. All trash and waste material will be hauled to the Uintah County Landfill.

No chemicals subject to reporting under SARA Title III (hazardous materials) in an amount greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of wells. Furthermore, extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will not be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of wells within these areas. Specific APD's shall address any modifications from this policy.

8. **Ancillary Facilities:**

None anticipated.

9. **Well Site Layout: (See Location Layout Diagram)**

The attached Location Layout Diagram describes drill pad cross-sections, cuts and fills and locations of the mud tanks, reserve pit, flare pit, pipe racks, trailer parking, spoil dirt stockpile(s), and surface material stockpile(s).

Please see the attached diagram rig orientation, parking areas, and access roads, as well as the location of the following:

The reserve pit.

The stockpiled topsoil will not be used for facility berms. All brush removed from the well pad during construction will be stockpiled with topsoil.

The flare pit or flare box will be located downwind from the prevailing wind direction.

Any drainage that crosses the well location will be diverted around the location by using ditches, water diversion drains or berms. If deemed necessary at the on-site, erosion drains may be installed to contain sediments that could be produced from access roads and well locations.

A pit liner is required. A felt pit liner will be required if bedrock is encountered.

10. Fencing Requirements:

Any open pits will be fenced during the operations. The fencing will be maintained until such time as the pits are backfilled.

All pits will be fenced according to the following minimum standards:

39 inch net wire will be used with at least one strand of barbed wire on top of the net wire. Barbed wire is not necessary if pipe or some type of reinforcement rod is attached to the top of the entire fence.

The net wire shall be no more than two inches above the ground. The barbed wire shall be three inches over the net wire. Total height of the fence shall be at least 42 inches.

Corner posts shall be cemented and/or braced in such a manner to keep the fence tight at all times.

Standard steel, wood, or pipe posts shall be used between the corner braces. Maximum distance between any 2 fence posts shall be no greater than 16 feet. All wire shall be stretched using a stretching device before it is attached to corner posts.

The reserve pit will be fenced on three (3) sides during drilling operations. The fourth side will be put in place when the rig moves off location. The pit will be fenced and maintained until it is backfilled. If drilling operations does not commence within 3 days, the fourth side of the fence will be installed.

11. Plans for Reclamation of the Surface:

Please refer to QEP Energy Company Uinta Basin Division Reclamation Plan

Site Specific Procedures:

Site Specific Reclamation Summary:

Reclamation will follow Questar Exploration and Production Company, Uinta Basin Division's Reclamation Plan, September 2009 (Questar's Reclamation Plan) and the BLM Green River District Reclamation Guidelines.

All trash and debris will be removed from the disturbed area.

The disturbed area will be backfilled with subsoil.

Topsoil will be spread to an even, appropriate depth and disked if needed.

Water courses and drainages will be restored.

Erosion control devices will be installed where needed.

Seeding will be done in the fall, prior to ground freeze up.

Seed mix will be submitted to a BLM AO for approval prior to seeding.

Monitoring and reporting will be conducted as stated in Questar's Reclamation Plan. A reference site has been established and is included in this application. A sundry notice (Form 3160.5), for the Weed Data Sheet will be filed at a later date.

It was determined and agreed upon that there is 5" inches of top soil.

12. Surface Ownership:

Bureau of Land Management
170 South 500 East
Vernal, Utah 84078
(435) 781-4400

13. Other Information:

A Class III archaeological survey was conducted by Montgomery Archaeology Consultants. A copy of this report was submitted on August 30, 2011, **Moac Report No. 11-249** by Montgomery Archaeology Consultants. Cultural resource clearance was recommended for this location.

A Class III paleontological survey was conducted by Intermountain Paleo Consulting. A copy of this report was submitted on September 2, 2011 **IPC # 11-147** by Stephen D. Sandau. The inspection resulted in the location of no fossil resources. However, if vertebrate fossil(s) are found during construction a paleontologist should be immediately notified. QEP Energy Company will provide Paleo monitor if needed.

Per the onsite on September 8, 2011, the following items were requested/discussed.

Prior to construction the existing unused pipelines on location will be removed.

There is a Burrowing Owl Stipulation from March 1 to August 31. No construction or drilling will commence during this period unless otherwise determined by a wildlife biologist that the site is inactive.

Lessee's or Operator's Representative & Certification:

Valyn Davis
Regulatory Affairs Analyst
QEP Energy Company
11002 East 17500 South
Vernal, UT 84078
(435) 781-4369

Certification: All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws, regulations, Onshore Oil and Gas Orders, the approved Plan of Operations, and any applicable Notice to Lessees.

The Operator will be fully responsible for the actions of its subcontractors. A complete copy of the approved "Application for Permit to Drill" will be furnished to the field representative(s) to ensure compliance and shall be on location during all construction and drilling operations.

QEP Energy Company is considered to be the operator of the subject well.
QEP Energy Company agrees to be responsible under terms and conditions of the lease for the operations conducted upon leased lands.

Bond coverage pursuant to 43 CFR 3104.2 for lease activities is being provided by
Bond No. ESB000024

I hereby certify that I, or persons under my supervision, have inspected the proposed drill site and access route, that I am familiar with the conditions that currently exist; that I have full knowledge of the State and Federal laws applicable to this operations; that the statements made in this plan are, to the best of my knowledge, true and correct; and the work associated with the operations proposed herein will be performed in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.


Valyn Davis

9/14/2011
Date

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office
P.O. Box 45155
Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:
3160
(UT-922)

September 16, 2011

Memorandum

To: Assistant District Manager Minerals, Vernal District
From: Michael Coulthard, Petroleum Engineer
Subject: 2011 Plan of Development Red Wash Unit,
Uintah County, Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2011 within the Red Wash Unit, Uintah County, Utah.

API#	WELL NAME	LOCATION
(Proposed PZ MESA VERDE)		
43-047-15240	RWU 43-13A Sec 13	T07S R22E 1934 FSL 0670 FEL *
43-047-15245	RWU 32-23A Sec 23	T07S R22E 1981 FNL 1982 FEL *
43-047-15279	RWU 32-33A Sec 33	T07S R22E 1976 FNL 1977 FEL *
43-047-16478	RWU 12-27A Sec 27	T07S R22E 2038 FNL 0684 FWL *
43-047-51938	RWU 12A2-28B Sec 28	T07S R23E 2375 FSL 0860 FWL
43-047-51939	RWU 13D2-24A Sec 24	T07S R22E 0347 FSL 0821 FWL
43-047-51940	RWU 14D3-24A Sec 24	T07S R22E 0394 FSL 2320 FWL
43-047-51948	RWU 24-30B Sec 30	T07S R23E 0821 FSL 1441 FWL

* Re-entry of abandoned Green River well.

This office has no objection to permitting the wells at this time.

Michael L. Coulthard

Digitally signed by Michael L. Coulthard
DN: cn=Michael L. Coulthard, o=Bureau of Land Management,
ou=Branch of Minerals, email=Michael_Coulthard@blm.gov,
c=US
Date: 2011.09.16 13:38:14 -06'00'

bcc: File - Red Wash Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:9-16-11

RECEIVED: September 16, 2011

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 9/14/2011**API NO. ASSIGNED:** 43047519380000**WELL NAME:** RW 12A2-28B**OPERATOR:** QEP ENERGY COMPANY (N3700)**PHONE NUMBER:** 435 781-4369**CONTACT:** Valyn Davis**PROPOSED LOCATION:** NSW 28 070S 230E**Permit Tech Review:** ☒**SURFACE:** 2375 FSL 0860 FWL**Engineering Review:** ☐**BOTTOM:** 2375 FSL 0860 FWL**Geology Review:** ☒**COUNTY:** Uintah**LATITUDE:** 40.17985**LONGITUDE:** -109.33779**UTM SURF EASTINGS:** 641520.00**NORTHINGS:** 4448833.00**FIELD NAME:** RED WASH**LEASE TYPE:** 1 - Federal**LEASE NUMBER:** UTU02025**PROPOSED PRODUCING FORMATION(S):** MESA VERDE**SURFACE OWNER:** 1 - Federal**COALBED METHANE:** NO**RECEIVED AND/OR REVIEWED:**

- ☒ **PLAT**
- ☒ **Bond:** FEDERAL - ESB000024
- ☐ **Potash**
- ☐ **Oil Shale 190-5**
- ☐ **Oil Shale 190-3**
- ☐ **Oil Shale 190-13**
- ☒ **Water Permit:** A-36125/ 49-2153
- ☐ **RDCC Review:**
- ☐ **Fee Surface Agreement**
- ☐ **Intent to Commingle**
- Commingle Approved**

LOCATION AND SITING:

- ☐ **R649-2-3.**
- Unit:** RED WASH
- ☐ **R649-3-2. General**
- ☐ **R649-3-3. Exception**
- ☒ **Drilling Unit**
- Board Cause No:** Cause 187-07
- Effective Date:** 9/18/2001
- Siting:** Suspends General Siting
- ☐ **R649-3-11. Directional Drill**

Comments: Presite Completed**Stipulations:** 4 - Federal Approval - dmason**RECEIVED:** September 20, 2011



GARY R. HERBERT
Governor

GREGORY S. BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: RW 12A2-28B
API Well Number: 43047519380000
Lease Number: UTU02025
Surface Owner: FEDERAL
Approval Date: 9/20/2011

Issued to:

QEP ENERGY COMPANY, 11002 East 17500 South, Vernal, Ut 84078

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 187-07. The expected producing formation or pool is the MESA VERDE Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)
- OR
- submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <http://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month

- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "J. Rogers", written over a horizontal line.

For John Rogers
Associate Director, Oil & Gas

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

RECEIVED

SEP 14 2011

FORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010

APPLICATION FOR PERMIT TO DRILL OR REENTER

BLM

CONFIDENTIAL

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU02025
1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other <input type="checkbox"/> Single Zone <input checked="" type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator QEP ENERGY COMPANY		7. If Unit or CA Agreement, Name and No. 892000761X
Contact: VALYN DAVIS E-Mail: Valyn.Davis@qepres.com		8. Lease Name and Well No. RW 12A2-28B
3a. Address 11002 EAST 17500 SOUTH VERNAL, UT 84078	3b. Phone No. (include area code) Ph: 435-781-4369 Fx: 435-781-4395	9. API Well No. 43-047-51938
4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NWSW 2375FSL 860FWL 40.179822 N Lat, 109.338469 W Lon At proposed prod. zone NWSW 2375FSL 860FWL 40.179822 N Lat, 109.338469 W Lon		10. Field and Pool, or Exploratory RED WASH
14. Distance in miles and direction from nearest town or post office* 24		11. Sec., T., R., M., or Blk. and Survey or Area Sec 28 T7S R23E Mer SLB
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 860	16. No. of Acres in Lease 1920.00	12. County or Parish UINTAH
18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 926	19. Proposed Depth 11266 MD 11266 TVD	13. State UT
21. Elevations (Show whether DF, KB, RT, GL, etc.) 5601 GL	22. Approximate date work will start 03/01/2012	17. Spacing Unit dedicated to this well 10.00
		20. BLM/BIA Bond No. on file ESB000024
		23. Estimated duration 30 DAYS

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification
6. Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature (Electronic Submission)	Name (Printed/Typed) VALYN DAVIS Ph: 435-781-4369	Date 09/14/2011
Title REGULATORY AFFAIRS ANALYST		
Approved by (Signature) 	Name (Printed/Typed) Jerry Kenczka	Date DEC 15 2011
Title Assistant Field Manager Lands & Mineral Resources	Office VERNAL FIELD OFFICE	

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Electronic Submission #117509 verified by the BLM Well Information System
For QEP ENERGY COMPANY, sent to the Vernal
Committed to AFMSS for processing by ROBIN R. HANSEN on 09/19/2011 ()

RECEIVED

DEC 21 2011

DIV. OF OIL, GAS & MINING

NOTICE OF APPROVAL

CONDITIONS OF APPROVAL ATTACHED

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **

11SXSD853AE

NOS 8/25/2011



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company:	QEP Energy Company	Location:	NWSW, Sec.28,T7S R23E
Well No:	RW 12A2-28B	Lease No:	UTU-02025
API No:	43-047-51938	Agreement:	Red Wash Unit

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings to: ut_vn_opreport@blm.gov .
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

CONDITIONS OF APPROVAL:

- All vehicles and equipment shall be cleaned either through power-washing, or other approved method, if the vehicles or equipment were brought in from areas outside the Uinta Basin, to prevent weed seed introduction.
- All disturbance areas shall be monitored for noxious weeds annually, for a minimum of three growing seasons following completion of project or until desirable vegetation is established.
- Reclamation will be completed in accordance with the Questar Exploration and Production Company, Uintah Basin Division's Reclamation Plan on file with the Vernal Field Office of the BLM.
- In the event historic or archaeological resources are uncovered during construction, work will stop immediately and the appropriate BLM AO will be notified.
- If paleontologic resources are uncovered during construction activities, the operator shall immediately suspend all operations that will further disturb such resources, and immediately notify the Authorized Officer (AO). The AO will arrange for a determination of significance and, if necessary, recommend a recovery or avoidance plan.
- A Paleontologist acceptable to the BLM will monitor construction activity for surface disturbing activities described in the APD. If paleontologic resources are uncovered during construction activities, the operator shall immediately suspend all operations that will further disturb such resources, and immediately notify the Authorized Officer (AO). The AO will arrange for a determination of significance and, if necessary, recommend a recovery or avoidance plan.

- QEP has agreed not to construct or drill during the following dates, unless otherwise ^{approved} ~~determined~~ by the BLM wildlife biologist. *Authorized Officer*

Well Name	Burrowing Owl March 1 to August 31	Red Tailed Hawk March 1 to August 15	Ferruginous Hawk March 1 to August 1
RW 12A2-28B	Yes	No	No
RW 12C3-25B	No	No	Yes
RW 12D1-25B	No	No	Yes
RW 12D4-25B	No	No	Yes
RW 13D2-24A	Yes	Yes	No
RW 14D3-24A	Yes	Yes	No
RW 23A-28B	No	No	No

- All internal combustion equipment would be kept in good working order.
- Water or other approved dust suppressants would be used at construction sites and along roads, as determined appropriate by the Authorized Officer.
- Open burning of garbage or refuse would not occur at well sites or other facilities.
- Drill rigs would be equipped with Tier II or better diesel engines.
- Low bleed pneumatics would be installed on separator dump valves and other controllers. The use of low bleed pneumatics would result in a lower emission of VOCs.
- During completion, flaring would be limited as much as possible. Production equipment and gathering lines would be installed as soon as possible.
- Well site telemetry would be utilized as feasible for production operations.
- Following well plugging and abandonment, the location, access roads, pipelines, and other facilities shall be reclaimed. All disturbed surfaces shall be reshaped to approximate the original contour; the top soil respread over the surface; and, the surface revegetated. The surface of approved staging areas where construction activities did not occur may require disking or ripping and reseeding.
- The best method to avoid entrainment is to pump from an off-channel location – one that does not connect to the river during high spring flows. An infiltration gallery constructed in a BLM and Service approved location is best.
- If the pump head is located in the river channel where larval fish are known to occur, the following measures apply:
 - do not situate the pump in a low-flow or no-flow area as these habitats tend to concentrate larval fishes;
 - limit the amount of pumping, to the greatest extent possible, during that period of the year when larval fish may be present (April 1 to August 31); and
 - limit the amount of pumping, to the greatest extent possible, during the pre-dawn hours as larval drift studies indicate that this is a period of greatest daily activity.

- Screen all pump intakes with 3/32" mesh material.
- Approach velocities for intake structures will follow the National Marine Fisheries Service's document "Fish Screening Criteria for Anadromous Salmonids". For projects with an in-stream intake that operate in stream reaches where larval fish may be present, the approach velocity will not exceed 0.33 feet per second (ft/s).
- Report any fish impinged on the intake screen to the Service (801.975.3330) and the Utah Division of Wildlife Resources:
Northeastern Region
152 East 100 North, Vernal, UT 84078
Phone: (435) 781-9453

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Gamma ray Log shall be run from Total Depth to Surface.
- CBL will be run from TD to TOC.

Variances Granted:

Air Drilling:

- Properly lubricated and maintained rotating head. Variance granted to use a properly maintained and lubricated diverter bowl in place of a rotating head.
- Blooie line discharge 100' from the well bore. Variance granted for blooie line discharge to be 50' to 70' from the well bore.
- Compressors located in the opposite direction from the blooie line a minimum of 100' from the well bore. Variance granted for truck/trailer mounted air compressors located 50' from the well bore.
- In lieu of mud products on location, operator will fill a 400 bbl tank with water for the kill medium.
- Automatic igniter. Variance granted for igniter, a diffuser will be used instead. Operator will mount a deflector at the end of the blooie line to change direction and reduce the velocity of the cuttings flow to the reserve pit.

Flare pit. Variance granted, there is no need of a flare during the drilling of the surface hole.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.

- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.
- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4.

Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU02025
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: QEP ENERGY COMPANY		7. UNIT or CA AGREEMENT NAME: RED WASH
3. ADDRESS OF OPERATOR: 11002 East 17500 South, Vernal, Ut, 84078		8. WELL NAME and NUMBER: RW 12A2-28B
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2375 FSL 0860 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 28 Township: 07.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047519380000
9. FIELD and POOL or WILDCAT: RED WASH		COUNTY: UINTAH
STATE: UTAH		
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 9/20/2013 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<div style="display: flex; flex-wrap: wrap;"> <div style="width: 33%;"> <input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION </div> <div style="width: 33%;"> <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER </div> <div style="width: 33%;"> <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input checked="" type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/> </div> </div>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. <div style="display: flex; justify-content: space-between;"> <div style="width: 60%;"> QEP ENERGY COMPANY HEREBY REQUESTS A ONE YEAR EXTENSION FOR THE APD ON THE ABOVE CAPTIONED WELL. </div> <div style="width: 35%; text-align: right;"> <p style="color: red; font-weight: bold;">Approved by the Utah Division of Oil, Gas and Mining</p> <p style="color: red; font-weight: bold;">Date: September 27, 2012</p> <p style="color: red; font-weight: bold;">By: </p> </div> </div>		
NAME (PLEASE PRINT) Valyn Davis	PHONE NUMBER 435 781-4369	TITLE Regulatory Affairs Analyst
SIGNATURE N/A		DATE 9/20/2012



The Utah Division of Oil, Gas, and Mining

- State of Utah
- Department of Natural Resources

Electronic Permitting System - Sundry Notices

Request for Permit Extension Validation Well Number 43047519380000

API: 43047519380000

Well Name: RW 12A2-28B

Location: 2375 FSL 0860 FWL QTR NWSW SEC 28 TWNP 070S RNG 230E MER S

Company Permit Issued to: QEP ENERGY COMPANY

Date Original Permit Issued: 9/20/2011

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision. Following is a checklist of some items related to the application, which should be verified.

- If located on private land, has the ownership changed, if so, has the surface agreement been updated? ☒ Yes ☐ No
- Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? ☐ Yes ☒ No
- Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? ☐ Yes ☒ No
- Have there been any changes to the access route including ownership, or rightof- way, which could affect the proposed location? ☐ Yes ☒ No
- Has the approved source of water for drilling changed? ☐ Yes ☒ No
- Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? ☐ Yes ☒ No
- Is bonding still in place, which covers this proposed well? ☒ Yes ☐ No

Signature: Valyn Davis

Date: 9/20/2012

Title: Regulatory Affairs Analyst Representing: QEP ENERGY COMPANY

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9			
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU02025			
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: RED WASH			
2. NAME OF OPERATOR: QEP ENERGY COMPANY		8. WELL NAME and NUMBER: RW 12A2-28B			
3. ADDRESS OF OPERATOR: 11002 East 17500 South , Vernal, Ut, 84078		9. API NUMBER: 43047519380000			
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2375 FSL 0860 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 28 Township: 07.0S Range: 23.0E Meridian: S		9. FIELD and POOL or WILDCAT: RED WASH COUNTY: UINTAH STATE: UTAH			
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA					
TYPE OF SUBMISSION <input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 10/31/2012 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	TYPE OF ACTION <table style="width: 100%; border: none;"> <tr> <td style="width: 33%; vertical-align: top;"> <input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION </td> <td style="width: 33%; vertical-align: top;"> <input checked="" type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER </td> <td style="width: 33%; vertical-align: top;"> <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/> </td> </tr> </table>		<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>
<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>			
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. <div style="display: flex; justify-content: space-between;"> <div style="width: 70%;"> QEP ENERGY COMPANY REQUESTS TO CHANGE THE CASING ON THE ABOVE MENTIONED WELL. QEP ENERGY COMPANY REQUESTS TO ADD AN INTERMEDIATE CASING STRING TO PREVENT THE WIRE LINE FROM BECOMING STUCK DURING LOGGING OPERATIONS. PLEASE SEE ATTACHED. </div> <div style="width: 25%; text-align: right;"> Accepted by the Utah Division of Oil, Gas and Mining Date: October 16, 2012 By: <u><i>Derek Quist</i></u> </div> </div>					
NAME (PLEASE PRINT) Valyn Davis		PHONE NUMBER 435 781-4369			
SIGNATURE N/A		TITLE Regulatory Affairs Analyst DATE 10/15/2012			

QEP ENERGY COMPANY
RW 12A2-28B
43-047-51938

QEP Energy Company requests to change the casing as follows:

We are going to run 7" 26#, N-80 casing as an intermediate string. This casing string will be run from surface to 6,500' MD.

Pipe Info:

Casing Program

Hole Size	Casing Size	Top, MD	Bottom, MD	Weight, lb/ft	Grade	Thread	Condition	MW
8 3/4"	7"	sfc	6,500'	26.0	N-80	LTC	New	8-9 ppg

Strengths:

Casing Strengths:				Collapse	Burst	Tensile (minimum)
7"	26.0 lb.	N-80	LTC	5,410 psi	7,240 psi	519,000 lb.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU02025			
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: RED WASH			
1. TYPE OF WELL Gas Well		8. WELL NAME and NUMBER: RW 12A2-28B			
2. NAME OF OPERATOR: QEP ENERGY COMPANY		9. API NUMBER: 43047519380000			
3. ADDRESS OF OPERATOR: 11002 East 17500 South, Vernal, Ut, 84078		9. FIELD and POOL or WILDCAT: RED WASH			
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2375 FSL 0860 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 28 Township: 07.0S Range: 23.0E Meridian: S		COUNTY: UINTAH STATE: UTAH			
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA					
TYPE OF SUBMISSION <input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 11/12/2012 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	TYPE OF ACTION <table style="width: 100%; border: none;"> <tr> <td style="width: 33%; vertical-align: top;"> <input type="checkbox"/> ACIDIZE <input checked="" type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION </td> <td style="width: 33%; vertical-align: top;"> <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER </td> <td style="width: 33%; vertical-align: top;"> <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/> </td> </tr> </table>		<input type="checkbox"/> ACIDIZE <input checked="" type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>
<input type="checkbox"/> ACIDIZE <input checked="" type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>			
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. QEP ENERGY COMPANY REQUESTS TO CHANGE THE DRILLING PLAN ON THE ABOVE MENTIONED WELL: THE SURFACE HOLE WILL BE DRILLED WITH AIR, AIR/MIST, FOAM OR MUD DEPENDING ON HOLE CONDITIONS. DRILLING BELOW SURFACE CASING WILL BE WITH WATER BASED DRILLING FLUIDS CONSISTING PRIMARILY OF FRESH WATER, BENTONITE, LIGNITE, CAUSTIC, LIME, SODA ASH AND POLYMERS. NO CHROMATES WILL BE USED. IT IS NOT INTENDED TO USE OIL IN THE MUD, HOWEVER, IN THE EVENT IT IS USED, OIL CONCENTRATION WILL BE LESS THAN 4% BY VOLUME. MAXIMUM ANTICIPATED MUD WEIGHT IS 9.5 PPG. QEP ENERGY COMPANY REQUESTS TO SET 90' OF 14" CONDUCTOR PIPE.					
NAME (PLEASE PRINT) Valyn Davis		PHONE NUMBER 435 781-4369			
SIGNATURE N/A		TITLE Regulatory Affairs Analyst DATE 11/7/2012			

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU02025
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: QEP ENERGY COMPANY		7. UNIT or CA AGREEMENT NAME: RED WASH
3. ADDRESS OF OPERATOR: 11002 East 17500 South, Vernal, Ut, 84078		8. WELL NAME and NUMBER: RW 12A2-28B
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2375 FSL 0860 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 28 Township: 07.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047519380000
9. FIELD and POOL or WILDCAT: RED WASH		COUNTY: UINTAH
STATE: UTAH		

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:			
<input checked="" type="checkbox"/> SPUD REPORT Date of Spud: 11/26/2012			
<input type="checkbox"/> DRILLING REPORT Report Date:			

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
 ON 11/26/2012, QEP ENERGY COMPANY SET 90' OF 14" CONDUCTOR PIPE AND CEMENTED IT WITH READY MIX.

Accepted by the
 Utah Division of
 Oil, Gas and Mining
FOR RECORD ONLY
 November 28, 2012

NAME (PLEASE PRINT) Valyn Davis	PHONE NUMBER 435 781-4369	TITLE Regulatory Affairs Analyst
SIGNATURE N/A	DATE 11/26/2012	

BLM - Vernal Field Office - Notification Form

Operator QEP Rig Name/# PETE MARTIN RATHOLE
Submitted By MURRAY BECKER Phone Number 435-828-0315
Well Name/Number RW 12A2-28B
Qtr/Qtr NW/SW Section 28 Township 7 S Range 23 E
Lease Serial Number UTU 02025
API Number 43-047-51938-00-X1

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 11/26/12 08:00 AM ☒
PM ☐

Casing – Please report time casing run starts, not cementing times.

- ☐ Surface Casing
- ☐ Intermediate Casing
- ☐ Production Casing
- ☐ Liner
- ☐ Other

Date/Time _____ AM ☐ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time _____ AM ☐ PM ☐

RECEIVED
NOV 27 2012
DIV. OF OIL, GAS & MINING

Remarks IF NO TROUBLE, THESE TIMES WILL BE CLOSE. DRILL
CONDUCTOR API # 43-047-51938-00-X1 11/26/12 @ 06:00
AM

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 6

ENTITY ACTION FORM

Operator: QEP ENERGY COMPANY Operator Account Number: N 3700
Address: 11002 EAST 17500 SOUTH
city VERNAL
state UT zip 84078 Phone Number: (435) 781-4369

Well 1

API Number	Well Name		QQ	Sec	Twp	Rng	County
4304751938	RW 12A2-28B		NWSW	28	7S	23E	UINTAH
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
B	99999	18478	11/26/2012		11/28/2012		
Comments: <u>WMMFD</u>							

CONFIDENTIAL

Well 2

API Number	Well Name		QQ	Sec	Twp	Rng	County
4304751939	RW 13D2-24A		SWSW	24	7S	22E	UINTAH
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
B	99999	18478	11/26/2012		11/28/2012		
Comments: <u>WMMFD</u>							

CONFIDENTIAL

Well 3

API Number	Well Name		QQ	Sec	Twp	Rng	County
Action Code	Current Entity Number	New Entity Number	Spud Date		Entity Assignment Effective Date		
Comments: <u> </u>							

ACTION CODES:

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new well
- E - Other (Explain in 'comments' section)

RECEIVED
NOV 27 2012

Valyn Davis

Name (Please Print)

Valyn Davis

Signature

Regulatory Affairs Analyst

Title

11/27/2012

Date

CONFIDENTIAL

BLM - Vernal Field Office - Notification Form

Operator QEP Rig Name/# SST RIG 54 Submitted By
MURRAY BECKER Phone Number 435-828-0315

Well Name/Number RW 12A2-28B
Qtr/Qtr NW/SW Section 28 Township 7 S Range 23 E_
Lease Serial Number UTU 02025
API Number 43-047-51938-00-X1

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time _____ AM ☐ PM ☐

Casing – Please report time casing run starts, not cementing times.

- ☐ Surface Casing
- ☐ Intermediate Casing
- ☐ Production Casing
- ☐ Liner
- ☐ Other

Date/Time _____ AM ☐ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time _ ____ AM ☐ PM ☐

RECEIVED

DEC 13 2012

DIV. OF OIL, GAS & MINING

Remarks WILL START TO MOVE RIG TO THE 12A2-28B. API #
43-047-51938-00-X1 AT 10:00 12/13/2012

BLM - Vernal Field Office - Notification Form

Operator QEP Rig Name/# SST RIG 54 Submitted By
MURRAY BECKER Phone Number 435-828-0315

Well Name/Number RW 12A2-28B
Qtr/Qtr NW/SW Section 28 Township 7 S Range 23 E_
Lease Serial Number UTU 02025
API Number 43-047-51938-00-X1

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

☒ Date/Time 12/16/2012 0600 AM
☒ PM ☒

Casing – Please report time casing run starts, not cementing times.

- ☐ Surface Casing
- ☐ Intermediate Casing
- ☐ Production Casing
- ☐ Liner
- ☐ Other

Date/Time _____ AM ☐ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time _____ AM ☐ PM ☐

Remarks IF NO TROUBLE, THESE TIMES WILL BE CLOSE. START
DRILL 12.25 SURFACE HOLE API # 43-047-51938-00-X1
11/26/12 @ 06:00 AM

CONFIDENTIAL

BLM - Vernal Field Office - Notification Form

Operator QEP Rig Name/# SST RIG 54 Submitted By
MURRAY BECKER Phone Number 435-828-0315

Well Name/Number RW 12A2-28B
Qtr/Qtr NW/SW Section 28 Township 7 S Range 23 E
Lease Serial Number UTU 02025
API Number 43-047-51938-00-X1

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time _____ AM ☐ PM ☒

Casing – Please report time casing run starts, not cementing times.

- ☒ Surface Casing
- ☐ Intermediate Casing
- ☐ Production Casing
- ☐ Liner
- ☐ Other

Date/Time 12/19/2012 @ 08:00 _____ AM ☒
PM ☐

BOPE

- ☒ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time 12/20/12 @.3:30 X AM ☐ PM ☐

RECEIVED

DEC 19 2012

DIV. OF OIL, GAS & MINING

Remarks IF NO TROUBLE, THESE TIMES WILL BE CLOSE, IF WE
DON'T HAVE CIRCULATION PROBLEMS.

CONFIDENTIAL

BLM - Vernal Field Office - Notification Form

Operator QEP Rig Name/# SST RIG 54 Submitted By
JIMMY KITTRELL Phone Number 435-828-0315

Well Name/Number RW 12A2-28B
Qtr/Qtr NW/SW Section 28 Township 7 S Range 23 E_
Lease Serial Number UTU 02025
API Number 43-047-51938-00-X1

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time _____ AM ☐ PM ☐

Casing – Please report time casing run starts, not cementing times.

- ☐ Surface Casing
- ☐ Intermediate Casing
- ☒ Production Casing
- ☐ Liner
- ☐ Other

Date/Time 1/05/2013 10:00 AM ☒ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☐ Other

Date/Time _____ AM ☐ PM ☐

RECEIVED
JAN 08 2013
BUREAU OF OIL, GAS & MINING

Remarks IF NO TROUBLE, THESE TIMES WILL BE CLOSE, WE
WILL BE RUNNING 4.5" PRODUCTION, AND CEMENT @ 10:00
ON 1/05/2013.._____

CONFIDENTIAL

BLM - Vernal Field Office - Notification Form

Operator QEP Rig Name/# SST RIG 54 Submitted By
JIMMY KITTRELL Phone Number 435-828-0315

Well Name/Number RW 12A2-28B
Qtr/Qtr NW/SW Section 28 Township 7 S Range 23 E_
Lease Serial Number UTU 02025
API Number 43-047-51938-00-X1

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time _____ AM ☐ PM ☐

Casing – Please report time casing run starts, not cementing times.

- ☐ Surface Casing
- ☐ Intermediate Casing
- ☐ Production Casing
- ☐ Liner
- ☐ Other

RECEIVED

DEC 26 2012

DIV. OF OIL, GAS & MINING

Date/Time _____ AM ☐ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
- ☐ BOPE test at intermediate casing point
- ☐ 30 day BOPE test
- ☒ Other

Date/Time 12/26/12 @19:30 _____ AM ☐ PM ☒

Remarks IF NO TROUBLE, THESE TIMES WILL BE CLOSE, IF WE
DON'T HAVE LOST CIRCULATION PROBLEMS. RE-TEST PIPE
RAMS, HYDRILL & 7" CASING WITH 3.5" DRILL PIPE BOP TEST
WAS DONE ON 12/21/12

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU02025
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: QEP ENERGY COMPANY		7. UNIT or CA AGREEMENT NAME: RED WASH
3. ADDRESS OF OPERATOR: 11002 East 17500 South, Vernal, Ut, 84078		8. WELL NAME and NUMBER: RW 12A2-28B
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2375 FSL 0860 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 28 Township: 07.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047519380000
9. FIELD and POOL or WILDCAT: RED WASH		COUNTY: UINTAH
STATE: UTAH		

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION	OTHER: <input style="width: 100px;" type="text"/>
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 1/31/2013	<input type="checkbox"/> SPUD REPORT Date of Spud:			
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION			

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

THIS WELL COMMENCED PRODUCTION ON JANUARY 31, 2013 @ 10:00 A.M.

**Accepted by the
Utah Division of
Oil, Gas and Mining**

FOR RECORD ONLY

February 13, 2013

NAME (PLEASE PRINT) Valyn Davis	PHONE NUMBER 435 781-4369	TITLE Regulatory Affairs Analyst
SIGNATURE N/A	DATE 2/4/2013	

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

RECEIVED
FEB 28 2013

AMENDED REPORT ☐ FORM 8
(highlight changes)

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. TYPE OF WELL: OIL WELL <input type="checkbox"/> GAS WELL <input checked="" type="checkbox"/> DRY <input type="checkbox"/> OTHER _____				5. LEASE DESIGNATION AND SERIAL NUMBER: UTU02025	
b. TYPE OF WORK: NEW WELL <input checked="" type="checkbox"/> HORIZ. LATS. <input type="checkbox"/> DEEP-EN <input type="checkbox"/> RE-ENTRY <input type="checkbox"/> DIFF. RESVR. <input type="checkbox"/> OTHER _____				6. IF INDIAN, ALLOTTEE OR TRIBE NAME	
2. NAME OF OPERATOR: QEP ENERGY COMPANY				7. UNIT or CA AGREEMENT NAME RED WASH	
3. ADDRESS OF OPERATOR: 11002 E. 17500 S. CITY VERNAL STATE UT ZIP 84078				8. WELL NAME and NUMBER: RW 12A2-28B	
4. LOCATION OF WELL (FOOTAGES) AT SURFACE: NWSW, 2375' FSL, 860' FWL AT TOP PRODUCING INTERVAL REPORTED BELOW: NWSW, 2375' FSL, 860' FWL AT TOTAL DEPTH: NWSW, 2375' FSL, 860' FWL				9. API NUMBER: 4304751938	
14. DATE SPURRED: 11/26/2012				10. FIELD AND POOL, OR WILDCAT RED WASH	
15. DATE T.D. REACHED: 1/4/2013				11. QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: NWSW 28 7S 23E	
16. DATE COMPLETED: 1/28/2013				12. COUNTY UINTAH	
ABANDONED <input type="checkbox"/> READY TO PRODUCE <input checked="" type="checkbox"/>				13. STATE UTAH	
18. TOTAL DEPTH: MD 11,261 TVD 11,254				17. ELEVATIONS (DF, RKB, RT, GL): 5599' GL	
19. PLUG BACK T.D.: MD TVD				21. DEPTH BRIDGE MD PLUG SET: TVD	
20. IF MULTIPLE COMPLETIONS, HOW MANY? *					

22. TYPE ELECTRIC AND OTHER MECHANICAL LOGS RUN (Submit copy of each) TRIPLE COMBO		23. WAS WELL CORED? NO <input checked="" type="checkbox"/> YES <input type="checkbox"/> (Submit analysis) WAS DST RUN? NO <input checked="" type="checkbox"/> YES <input type="checkbox"/> (Submit report) DIRECTIONAL SURVEY? NO <input checked="" type="checkbox"/> YES <input type="checkbox"/> (Submit copy)	
---	--	---	--

24. CASING AND LINER RECORD (Report all strings set in well)

HOLE SIZE	SIZE/GRADE	WEIGHT (#/ft.)	TOP (MD)	BOTTOM (MD)	STAGE CEMENTER DEPTH	CEMENT TYPE & NO. OF SACKS	SLURRY VOLUME (BBL)	CEMENT TOP **	AMOUNT PULLED
12.25	9.625 N-80	40	0	3,912		989	420	652	
8.75	7 N-80	26	0	6,531		495	214		
6.125	4.5 P-11	11.6	0	11,256		700	255		

SIZE	DEPTH SET (MD)	PACKER SET (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)
2.375	7,554							

26. PRODUCING INTERVALS					27. PERFORATION RECORD				
FORMATION NAME	TOP (MD)	BOTTOM (MD)	TOP (TVD)	BOTTOM (TVD)	INTERVAL (Top/Bot - MD)	SIZE	NO. HOLES	PERFORATION STATUS	
(A) MESA VERDE	7,644	11,048			7,644 11,048	.42	203	Open <input type="checkbox"/>	Squeezed <input type="checkbox"/>
(B) WSMVD								Open <input type="checkbox"/>	Squeezed <input type="checkbox"/>
(C)								Open <input type="checkbox"/>	Squeezed <input type="checkbox"/>
(D)								Open <input type="checkbox"/>	Squeezed <input type="checkbox"/>

28. ACID, FRACTURE, TREATMENT, CEMENT SQUEEZE, ETC.

DEPTH INTERVAL	AMOUNT AND TYPE OF MATERIAL
7,644 - 11,048	19,827 BBLs SLICKWATER, 419,871 LBS 30/50 SAND, 120,000 LBS 20/40 SAND

29. ENCLOSED ATTACHMENTS:		30. WELL STATUS:	
<input type="checkbox"/> ELECTRICAL/MECHANICAL LOGS <input type="checkbox"/> SUNDRY NOTICE FOR PLUGGING AND CEMENT VERIFICATION	<input type="checkbox"/> GEOLOGIC REPORT <input type="checkbox"/> CORE ANALYSIS	<input type="checkbox"/> DST REPORT <input type="checkbox"/> DIRECTIONAL SURVEY <input checked="" type="checkbox"/> OTHER: OPS SUMMARY	PGW

31. INITIAL PRODUCTION

INTERVAL A (As shown in item #26)

DATE FIRST PRODUCED: 1/31/2013	TEST DATE: 2/3/2013	HOURS TESTED: 24	TEST PRODUCTION RATES: →	OIL – BBL: 10	GAS – MCF: 1,810	WATER – BBL: 656	PROD. METHOD: FLOWS
CHOKE SIZE: 22/64	TBG. PRESS. 1,473	CSG. PRESS. 2,297	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	INTERVAL STATUS:

INTERVAL B (As shown in item #26)

DATE FIRST PRODUCED:	TEST DATE:	HOURS TESTED:	TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	INTERVAL STATUS:

INTERVAL C (As shown in item #26)

DATE FIRST PRODUCED:	TEST DATE:	HOURS TESTED:	TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	INTERVAL STATUS:

INTERVAL D (As shown in item #26)

DATE FIRST PRODUCED:	TEST DATE:	HOURS TESTED:	TEST PRODUCTION RATES: →	OIL – BBL:	GAS – MCF:	WATER – BBL:	PROD. METHOD:
CHOKE SIZE:	TBG. PRESS.	CSG. PRESS.	API GRAVITY	BTU – GAS	GAS/OIL RATIO	24 HR PRODUCTION RATES: →	INTERVAL STATUS:

32. DISPOSITION OF GAS (Sold, Used for Fuel, Vented, Etc.)

SOLD

33. SUMMARY OF POROUS ZONES (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

34. FORMATION (Log) MARKERS:

Formation	Top (MD)	Bottom (MD)	Descriptions, Contents, etc.	Name	Top (Measured Depth)
				GREEN RIVER	3,025
				BIRDS NEST	3,400
				MAHOGANY	3,812
				WASATCH	6,749
				MESA VERDE	8,656
				SEGO	11,162

35. ADDITIONAL REMARKS (Include plugging procedure)

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records.

NAME (PLEASE PRINT) BENNA MUTH

TITLE REGULATORY ASSISTANT - CONTRACT

SIGNATURE

Benna Muth

DATE 2/25/2013

This report must be submitted within 30 days of

- completing or plugging a new well
- drilling horizontal laterals from an existing well bore
- recompleting to a different producing formation
- reentering a previously plugged and abandoned well
- significantly deepening an existing well bore below the previous bottom-hole depth
- drilling hydrocarbon exploratory holes, such as core samples and stratigraphic tests

* ITEM 20: Show the number of completions if production is measured separately from two or more formations.

** ITEM 24: Cement Top – Show how reported top(s) of cement were determined (circulated (CIR), calculated (CAL), cement bond log (CBL), temperature survey (TS)).

Send to: Utah Division of Oil, Gas and Mining
1594 West North Temple, Suite 1210
Box 145801
Salt Lake City, Utah 84114-5801

Phone: 801-538-5340

Fax: 801-359-3940



QEP Energy Company

Daily Activity and Cost Summary

Well Name: RW 12A2-28B

API 43-047-51938		Surface Legal Location 028007S023E27		Field Name RED WASH		State UTAH		Well Configuration Type Deviated	
Ground Elevation (ft) 5,599.7		Casing Flange Elevation (ft) 5,599.70		Current KB to GL (ft) 10.30		KB to CF (ft) 10.30		Spud Date 12/16/2012 17:00	
Job Category Drilling		Primary Job Type DRILLING		Secondary Job Type DEVELOPMENT		Objective			
Start Date 12/14/2012				Job End Date 1/7/2013					
Purpose									
Summary									
Contractor SST Energy				RIG SST 54		Rig Type TOP DRIVE			
DOL	Start Date	Summary							
1.0	12/14/2012	MOVE RIG, MOVE OUT BACK YARD MUD TANKS, SET OUT PUMPS, SET MATTING BOARDS AND SUB, MUD TANKS, AND BACK YARD IN, SET DWK'S ON RIG FLOOR.							
2.0	12/15/2012	RIG UP SET DERRICK ON RIG FLOOR, SET GEN. HOUSES, RAISE DERRICK, HOOK UP BOILER, FLARE LINES, SET UP RIGHTS, PICK UP TOP DRIVE, FILL MUD TANKS, WORK ON SAFETY ACTION ITEM (WELD ECT) WELD ON RISER ADN FAB FLOW LINE							
3.0	12/16/2012	RIG UP, WELD WORK ON SAFETY ACTION ITEMS, ROUTINE RIG SERVICE, PICK UP DIRECT TOOLS AND TEST, DRILL.							
4.0	12/17/2012	DEIRECT DRILL, SURVEYS, ROUTINE RIG SERVICE AND TOP DRIVE INSPECTION, 2 X SHORT TRIPS,							
5.0	12/18/2012	DIRECT. DRILL, SHORT TRIP, RIG SERVICE, LOSS CIRC							
6.0	12/19/2012	DIRECT DRILL TO TD @ 3,920', LOSS CIRC. SHORT TRIP, CIRC BU, TOO H TO RUN 9.625" SURFACE CASING, RU WEATHERFORD AND RUN CASING, CIRC 1.5 TIME CASING CAP, RU AND CEMENT SURFACE CASING, TOP JOB, WOC.							
7.0	12/20/2012	RUN CASING, CIRC, LOSS CIRC, SET CASING @ 3,912', RU AND CEMENT SURFACE CASING, TOP JOB, WOC, CUT CONDUCTER AND CASING LD LANDING JT, WELD ON WELL HEAD AND TEST TO 1500 PSI							
8.0	12/21/2012	WELD ON WELL HEAD, NIPPLE UP B.O.P. TEST B.O.P. INSTALL WEARBUSHING, CLEAN THAW OUT RIG FLOOR AND MUD TANKS, TIH, DRILL CEMENT EQUIP. TOP RAMS NOT CLOSING TROUBLE SHOOT, TOO H							
9.0	12/22/2012	TRIP OUT, PULL WEARBUSHING AND LOCK DOWN BOLTS, INSTALL WEARBUSHING, TRIP IN, FIT TEST TO 9.6 EMW. ROUTINE RIG SERVICE DIRECT. DRILL,							
10.0	12/23/2012	DIRECT DRILL, ROUTINE RIG SERVICE							
11.0	12/24/2012	DIRECT DRILL TO TD @ 6,540', ROUTINE RIG SERVICE, CIRC TD CONFORMATION SAMPLE SPOT 30 BBL 25% LCM PILL ON BOTTOM, SHORT TRIP, CIRC HOLE CLEAN, TOO H FOR LOGS.							
12.0	12/25/2012	LAY DOWN DIRECT TOOLS, OPEN HOLE LOGS, TIH, CIRC. LAY DOWN D.P.							
13.0	12/26/2012	TEST BOP							
14.0	12/27/2012	TRIP IN PICKING UP 5 1/2" D.P. TAG & DRILL FLOAT COLLAR, SHOE TRACK, FLOAT SHOE & 10' NEW HOLE TO 6550'. FIT TO 11 PPG & DRILL NEW HOLE TO 7164'.							
15.0	12/28/2012	DRILL W/ RIG SERVICE.							
16.0	12/29/2012	DRILL W/ RIG SERVICE.							
17.0	12/30/2012	DRILL W/ RIG SERVICE.							
18.0	12/31/2012	DRILL TO 11186'.							
19.0	1/1/2013	TRIP & LOG							
20.0	1/2/2013	TRIP & LOG.							
21.0	1/3/2013	RAN XPT LOGS.							
22.0	1/4/2013	TRIP IN DRILL TO 11261', SHORT TRIP, & TRIP OUT FOR CSG.							
23.0	1/5/2013	LAY DOWN DRILL PIPE & RUN PRODUCTION CSG.							
24.0	1/6/2013	RAN & CEMENT PRODUCTION CSG.							

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9			
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU02025			
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: RED WASH			
2. NAME OF OPERATOR: QEP ENERGY COMPANY		8. WELL NAME and NUMBER: RW 12A2-28B			
3. ADDRESS OF OPERATOR: 11002 East 17500 South, Vernal, Ut, 84078		9. API NUMBER: 43047519380000			
4. LOCATION OF WELL FOOTAGES AT SURFACE: 2375 FSL 0860 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 28 Township: 07.0S Range: 23.0E Meridian: S		9. FIELD and POOL or WILDCAT: RED WASH			
COUNTY: UINTAH		STATE: UTAH			
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA					
TYPE OF SUBMISSION <input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 1/14/2015 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	TYPE OF ACTION <table style="width: 100%; border: none;"> <tr> <td style="width: 33%; vertical-align: top;"> <input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input checked="" type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION </td> <td style="width: 33%; vertical-align: top;"> <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER </td> <td style="width: 33%; vertical-align: top;"> <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/> </td> </tr> </table>		<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input checked="" type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>
<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input checked="" type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/>			
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. QEP ENERGY COMPANY REQUESTS APPROVAL TO RECOMPLETE THE RW 12A2-28B BY ADDING PERFORATIONS TO THE MESA VERDE FORMATION. SEE ATTACHED PROCEDURES.					
Accepted by the Utah Division of Oil, Gas and Mining Date: January 20, 2015 By:					
NAME (PLEASE PRINT) Benna Muth		PHONE NUMBER 435 781-4320			
SIGNATURE N/A		TITLE Regulatory Assistant			
DATE 1/14/2015					

QEP Energy requests approval to recomplete the RW 12A2-28B by adding perforations to the Mesaverde formation as follows:

1. Set a CFP at 10200'.
2. Stage 1:
 - a. 10151'-10153', 3spf, frac with slick water.
 - b. 10105'-10108', 3spf, frac with slick water.
 - c. 10041'-10044', 3spf, frac with slick water.
 - d. 9977'-9981', 3spf, frac with slick water.
 - e. 9933'-9937', 3spf, frac with slick water.
3. Set a CFP at 9900'.
4. Stage 2:
 - a. 9789'-9795', 3spf, frac with slick water.
 - b. 9710'-9715', 3spf, frac with slick water.
 - c. 9688'-9693', 3spf, frac with slick water.
5. Drill up the top plug and return well to production.
6. Return to drill up the bottom plug and restore existing production after the frac fluid is recovered.
