


STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT ☐

APPLICATION FOR PERMIT TO DRILL						1. WELL NAME and NUMBER BONANZA 1023-5G4DS							
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT NATURAL BUTTES							
4. TYPE OF WELL Gas Well <input type="checkbox"/> Coalbed Methane Well: NO <input type="checkbox"/>						5. UNIT or COMMUNITIZATION AGREEMENT NAME							
6. NAME OF OPERATOR KERR-MCGEE OIL & GAS ONSHORE, L.P.						7. OPERATOR PHONE 720 929-6515							
8. ADDRESS OF OPERATOR P.O. Box 173779, Denver, CO, 80217						9. OPERATOR E-MAIL julie.jacobson@anadarko.com							
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU33433			11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>							
13. NAME OF SURFACE OWNER (if box 12 = 'fee')						14. SURFACE OWNER PHONE (if box 12 = 'fee')							
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')							
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input checked="" type="checkbox"/> (Submit Commingling Application) NO <input type="checkbox"/>			19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/>							
20. LOCATION OF WELL		FOOTAGES		QTR-QTR		SECTION		TOWNSHIP		RANGE		MERIDIAN	
LOCATION AT SURFACE		1625 FSL 1048 FEL		NESE		5		10.0 S		23.0 E		S	
Top of Uppermost Producing Zone		2643 FNL 1424 FEL		SWNE		5		10.0 S		23.0 E		S	
At Total Depth		2643 FNL 1424 FEL		SWNE		5		10.0 S		23.0 E		S	
21. COUNTY UINTAH			22. DISTANCE TO NEAREST LEASE LINE (Feet) 1787			23. NUMBER OF ACRES IN DRILLING UNIT 1923							
			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 424			26. PROPOSED DEPTH MD: 8588 TVD: 8426							
27. ELEVATION - GROUND LEVEL 5297			28. BOND NUMBER WYB000291			29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 43-8496							
Hole, Casing, and Cement Information													
String	Hole Size	Casing Size	Length	Weight	Grade & Thread	Max Mud Wt.	Cement		Sacks	Yield	Weight		
Surf	11	8.625	0 - 2310	28.0	J-55 LT&C	0.2	Type V		180	1.15	15.8		
							Class G		270	1.15	15.8		
Prod	7.875	4.5	0 - 8588	11.6	I-80 LT&C	12.5	Premium Lite High Strength		280	3.38	11.0		
							50/50 Poz		1150	1.31	14.3		
ATTACHMENTS													
VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES													
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER						<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN							
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)						<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER							
<input checked="" type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)						<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP							
NAME Gina Becker				TITLE Regulatory Analyst II				PHONE 720 929-6086					
SIGNATURE				DATE 10/17/2011				EMAIL gina.becker@anadarko.com					
API NUMBER ASSIGNED 43047520580000				APPROVAL  Permit Manager									

RECEIVED: October 26, 2011

Kerr-McGee Oil & Gas Onshore. L.P.**BONANZA 1023-5G4DS**

Surface: 1625 FSL / 1048 FEL NESE
BHL: 2643 FNL / 1424 FEL SWNE

Section 5 T10S R23E

Uintah County, Utah
Mineral Lease: UTU-33433

ONSHORE ORDER NO. 1**DRILLING PROGRAM**

1. & 2. **Estimated Tops of Important Geologic Markers:**
Estimated Depths of Anticipated Water, Oil, Gas, or Mineral Formations:

<u>Formation</u>	<u>Depth</u>	<u>Resource</u>
Uinta	0 - Surface	
Green River	1,253'	
Birds Nest	1,502'	Water
Mahogany	1,860'	Water
Wasatch	4,218'	Gas
Mesaverde	6,258'	Gas
MVU2	7,258'	Gas
MVL1	7,807'	Gas
TVD	8,426'	
TD	8,588'	

3. **Pressure Control Equipment** (Schematic Attached)

Please refer to the attached Drilling Program

4. **Proposed Casing & Cementing Program:**

Please refer to the attached Drilling Program

5. **Drilling Fluids Program:**

Please refer to the attached Drilling Program

6. **Evaluation Program:**

Please refer to the attached Drilling Program

7. Abnormal Conditions:

Maximum anticipated bottom hole pressure calculated at 8426' TVD, approximately equals
 5,393 psi (0.64 psi/ft = actual bottomhole gradient)

Maximum Anticipated Bottom Hole Pressure (MABHP) = Pore Pressure at TD

Maximum anticipated surface pressure equals approximately 3,527 psi (bottom hole pressure
 minus the pressure of a partially evacuated hole calculated at 0.22 psi/foot, per Onshore Order No. 2).

Per Onshore Order No. 2 - Max Anticipated Surf. Press.(MASP) = (Pore Pressure at next csg point-
 (0.22 psi/ft-partial evac gradient x TVD of next csg point))

8. Anticipated Starting Dates:

Drilling is planned to commence immediately upon approval of this application.

9. Variances:

Please refer to the attached Drilling Program.
 Onshore Order #2 – Air Drilling Variance

Kerr-McGee Oil & Gas Onshore LP (KMG) respectfully requests a variance to several requirements associated with air drilling outlined in Onshore Order 2

- Blowout Prevention Equipment (BOPE) requirements;
- Mud program requirements; and
- Special drilling operation (surface equipment placement) requirements associated with air drilling.

This Standard Operating Practices addendum provides supporting information as to why KMG current air drilling practices for constructing the surface casing hole should be granted a variance to Onshore Order 2 air drilling requirements.

The reader should note that the air rig is used only to construct a stable surface casing hole through a historically difficult lost circulation zone. A conventional rotary rig follows the air rig, and is used to drill and construct the majority of the wellbore.

More notable, KMG has used the air rig layout and procedures outlined below to drill the surface casing hole in approximately 675 wells without incident of blow out or loss of life.

Background

In a typical well, KMG utilizes an air rig for drilling the surface casing hole, an interval from the surface to surface casing depths, which varies in depth from 1,700 to 2,800 feet. The air rig drilling operation does not drill through productive or over pressured formations in KMG field, but does penetrate the Uinta and Green River Formations. The purpose of the air drilling operation is to overcome the severe loss circulation zone in the Green River known as the Bird's Nest while creating a stable hole for the surface casing. The surface casing hole is generally drilled to approximately 500 feet below the Bird's Nest.

Before the surface air rig is mobilized, a rathole rig is utilized to set and cement conductor pipe through a competent surface formation. Generally, the conductor is set at 40 feet. In some cases, conductor may be set deeper in areas that the surface formation is not found competent. This rig also drills the rat and mouse holes in preparation for the surface casing and production string drilling operations.

The air rig is then mobilized to drill the surface casing hole by drilling a 12 1/4 inch hole for the first 200 feet, then will drill a 11 inch hole to just above the Bird's Nest interval with an air hammer. The hammer is then tripped and replaced with a 11 inch tri-cone bit. The tri-cone bit is used to drill to the surface casing point, approximately 500 feet below the loss circulation zone (Bird's Nest). The 8-5/8 inch surface casing is then run and cemented in place, thereby isolating the lost circulation zone.

KMG fully appreciates Onshore Order 2 well control and safety requirements associated with a typical air drilling operations. However, the requirements of Onshore Order 2 are excessive with respect to the air rig layout and drilling operation procedures that are currently in practice to drill and control the surface casing hole in KMG Fields.

Variance for BOPE Requirements

The air rig operation utilizes a properly lubricated and maintained air bowl diverter system which diverts the drilling returns to a six-inch blooie line. The air bowl is the only piece of BOPE equipment which is installed during drilling operations and is sufficient to contain the air returns associated with this drilling operation. As was discussed earlier, the drilling of the surface hole does not encounter any over pressured or productive zones, and as a result standard BOPE equipment should not be required. In addition, standard drilling practices do not support the use of BOPE on 40 feet of conductor pipe.

Variance for Mud Material Requirements

Onshore Order 2 also states that sufficient quantities of mud materials shall be maintained or readily accessible for the purpose of assuring adequate well control. Once again, the surface hole drilling operations does not encounter over pressured or productive intervals, and as a result there is not a need to control pressure in the surface hole with a mud system. Instead of mud, the air rigs utilize water from the reserve pit for well control, if necessary. A skid pump which is located near the reserve pit (see attachment) will supply the water to the well bore.

Variance for Special Drilling Operation (surface equipment placement) Requirements

Onshore Order 2 requires specific safety distances or setbacks for the placement of associated standard air drilling equipment, wellbore, and reserve pits. The air rigs used to drill the surface holes are not typical of an air rig used to drill a producing hole in other parts of the US. These are smaller in nature and designed to fit a KMG location. The typical air rig layout for drilling surface hole in the field is attached.

Typically the blooie line discharge point is required to be 100 feet from the well bore. In the case of a KMG well, the reserve pit is only 45 feet from the rig and is used for the drill cuttings. The blooie line, which transports the drill cuttings from the well to the reserve pit, subsequently discharges only 45 feet from the well bore.

Typically the air rig compressors are required to be located in the opposite direction from the blooie line and a minimum of 100 feet from the well bore. At the KMG locations, the air rig compressors are approximately 40 feet from the well bore and approximately 60 feet from the blooie line discharge due to the unique air rig design. The air compressors (see attachment) are located on the rig (1250 cfm) and

on a standby trailer (1170 cfm). A booster sits between the two compressors and boosts the output from 350 psi to 2000 psi. The design does put the booster and standby compressor opposite from the blooie line.

Lastly, Onshore Order 2 addresses the need for an automatic igniter or continuous pilot light on the blooie line. The air rig does not utilize an igniter as the surface hole drilling operation does not encounter productive formations.

Variance for FIT Requirements

KMG also respectfully requests a variance to Onshore Order 2, Section III, Part Bi, for the pressure integrity test (PIT, also known as a formation integrity test (FIT)). This well is not an exploratory well and is being drilled in an area where the formation integrity is well known. Additionally, when an FIT is run with the mud weight as required, the casing shoe frequently breaks down and causes subsequent lost circulation when drilling the entire depth of the well.

Conclusion

The air rig operating procedures and the attached air rig layout have effectively maintained well control while drilling the surface holes in KMG Fields. KMG respectfully requests a variance from Onshore Order 2 with respect to air drilling well control requirements as discussed above.


10. Other Information:

Please refer to the attached Drilling Program.



KERR-McGEE OIL & GAS ONSHORE LP DRILLING PROGRAM

COMPANY NAME	KERR-McGEE OIL & GAS ONSHORE LP					DATE	October 14, 2011		
WELL NAME	BONANZA 1023-5G4DS					TD	8,426'	TVD	8,588' MD
FIELD	Natural Buttes		COUNTY	Uintah	STATE	Utah	FINISHED ELEVATION		5,297'
SURFACE LOCATION	NESE	1625 FSL	1048 FEL	Sec 5	T 10S	R 23E			
	Latitude: 39.975180		Longitude: -109.345065		NAD 83				
BTM HOLE LOCATION	SWNE	2643 FNL	1424 FEL	Sec 5	T 10S	R 23E			
	Latitude: 39.977990		Longitude: -109.346403		NAD 83				
OBJECTIVE ZONE(S)	Wasatch/Mesaverde								
ADDITIONAL INFO	Regulatory Agencies: BLM (Minerals), BLM (Surface), UDOGM Tri-County Health Dept.								

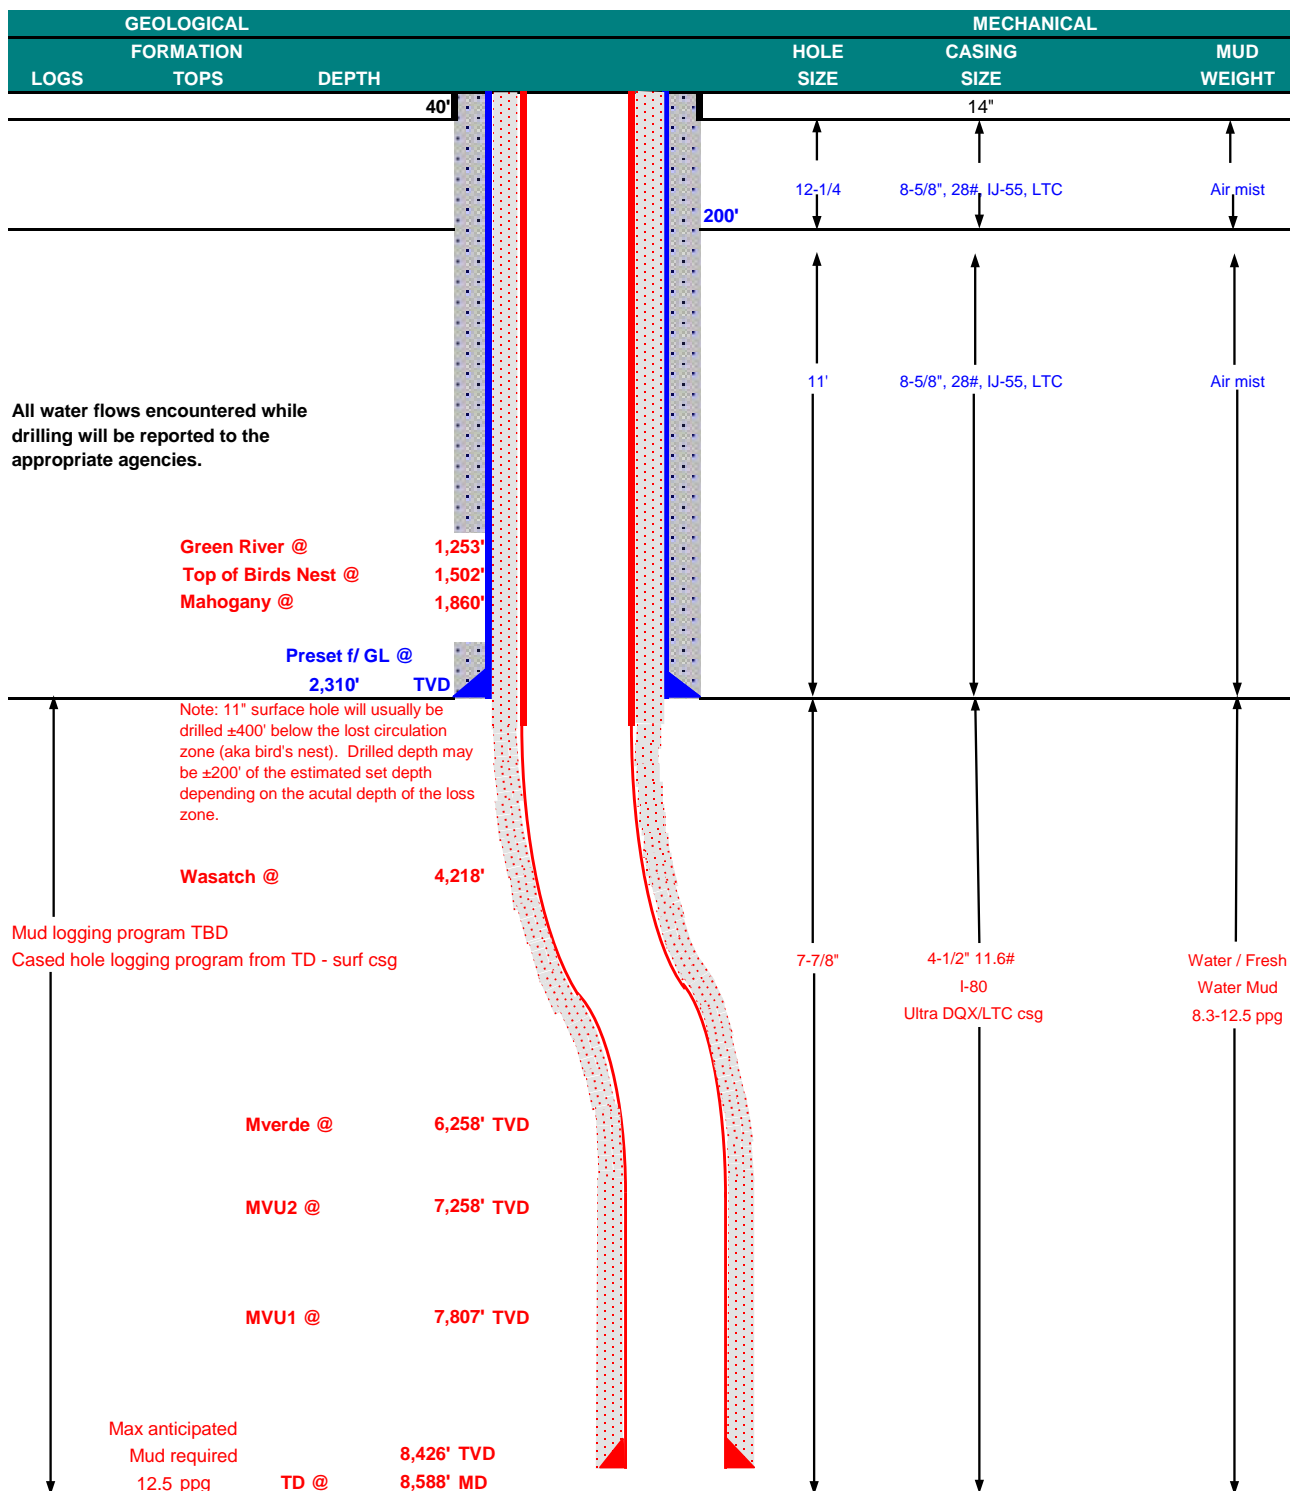



KERR-McGEE OIL & GAS ONSHORE LP

DRILLING PROGRAM

CASING PROGRAM

	SIZE	INTERVAL	WT.	GR.	CPLG.	DESIGN FACTORS			
						BURST	LTC		DQX
							COLLAPSE		TENSION
CONDUCTOR	14"	0-40'							
						3,390	1,880	348,000	N/A
SURFACE	8-5/8"	0 to 2,310	28.00	IJ-55	LTC	2.34	1.74	6.14	N/A
						7,780	6,350	223,000	267,000
PRODUCTION	4-1/2"	0 to 5,000	11.60	I-80	DQX	1.11	1.16		3.31
	4-1/2"	5,000 to 8,588'	11.60	I-80	LTC	1.11	1.16	6.62	

Surface Casing:

(Burst Assumptions: TD = 12.5 ppg)

0.73 psi/ft = frac gradient @ surface shoe

Fracture at surface shoe with 0.1 psi/ft gas gradient above

(Collapse Assumption: Fully Evacuated Casing, Max MW)

(Tension Assumptions: Air Weight of Casing*Buoy.Fact. of water)

Production casing:

(Burst Assumptions: Pressure test with 8.4ppg @ 7000 psi)

0.64 psi/ft = bottomhole gradient

(Collapse Assumption: Fully Evacuated Casing, Max MW)

(Tension Assumptions: Air Weight of Casing*Buoy.Fact. of water)

CEMENT PROGRAM

		FT. OF FILL	DESCRIPTION	SACKS	EXCESS	WEIGHT	YIELD
SURFACE	LEAD	500'	Premium cmt + 2% CaCl	180	60%	15.80	1.15
Option 1			+ 0.25 pps flocele				
	TOP OUT CMT (6 jobs)	1,200'	20 gals sodium silicate + Premium cmt	270	0%	15.80	1.15
			+ 2% CaCl + 0.25 pps flocele				
SURFACE			NOTE: If well will circulate water to surface, option 2 will be utilized				
Option 2	LEAD	1,810'	65/35 Poz + 6% Gel + 10 pps gilsonite	170	35%	11.00	3.82
			+ 0.25 pps Flocele + 3% salt BWOW				
	TAIL	500'	Premium cmt + 2% CaCl	150	35%	15.80	1.15
			+ 0.25 pps flocele				
	TOP OUT CMT	as required	Premium cmt + 2% CaCl	as req.		15.80	1.15
PRODUCTION	LEAD	3,718'	Premium Lite II +0.25 pps	280	20%	11.00	3.38
			celloflake + 5 pps gilsonite + 10% gel				
			+ 0.5% extender				
	TAIL	4,870'	50/50 Poz/G + 10% salt + 2% gel	1,150	35%	14.30	1.31
			+ 0.1% R-3				

*Substitute caliper hole volume plus 0% excess for LEAD if accurate caliper is obtained

*Substitute caliper hole volume plus 10% excess for TAIL if accurate caliper is obtained

FLOAT EQUIPMENT & CENTRALIZERS

SURFACE	Guide shoe, 1 jt, insert float. Centralize first 3 joints with bow spring centralizers. Thread lock guide shoe
PRODUCTION	Float shoe, 1 jt, float collar. No centralizers will be used.

ADDITIONAL INFORMATION

Test casing head to 750 psi after installing. Test surface casing to 1,500 psi prior to drilling out.

BOPE: 11" 5M with one annular and 2 rams. The BOPE will be installed before the production hole is drilled and tested to 5,000 psi (annular to 2,500 psi) prior to drilling out the surface casing shoe. Record on chart recorder and tour sheet. Function test rams on each trip. Maintain safety valve and inside BOP on rig floor at all times. Most rigs have top drives; however, if used, the Kelly is to be equipped with upper and lower kelly valves.

Surveys will be taken at 1,000' minimum intervals.

Most rigs have PVT System for mud monitoring. If no PVT is available, visual monitoring will be utilized.

DRILLING ENGINEER:

Nick Spence / Danny Showers / Chad Loesel


DATE:

DRILLING SUPERINTENDENT:

Kenny Gathings / Lovel Young

DATE:

EXHIBIT A
BONANZA 1023-5G4DS

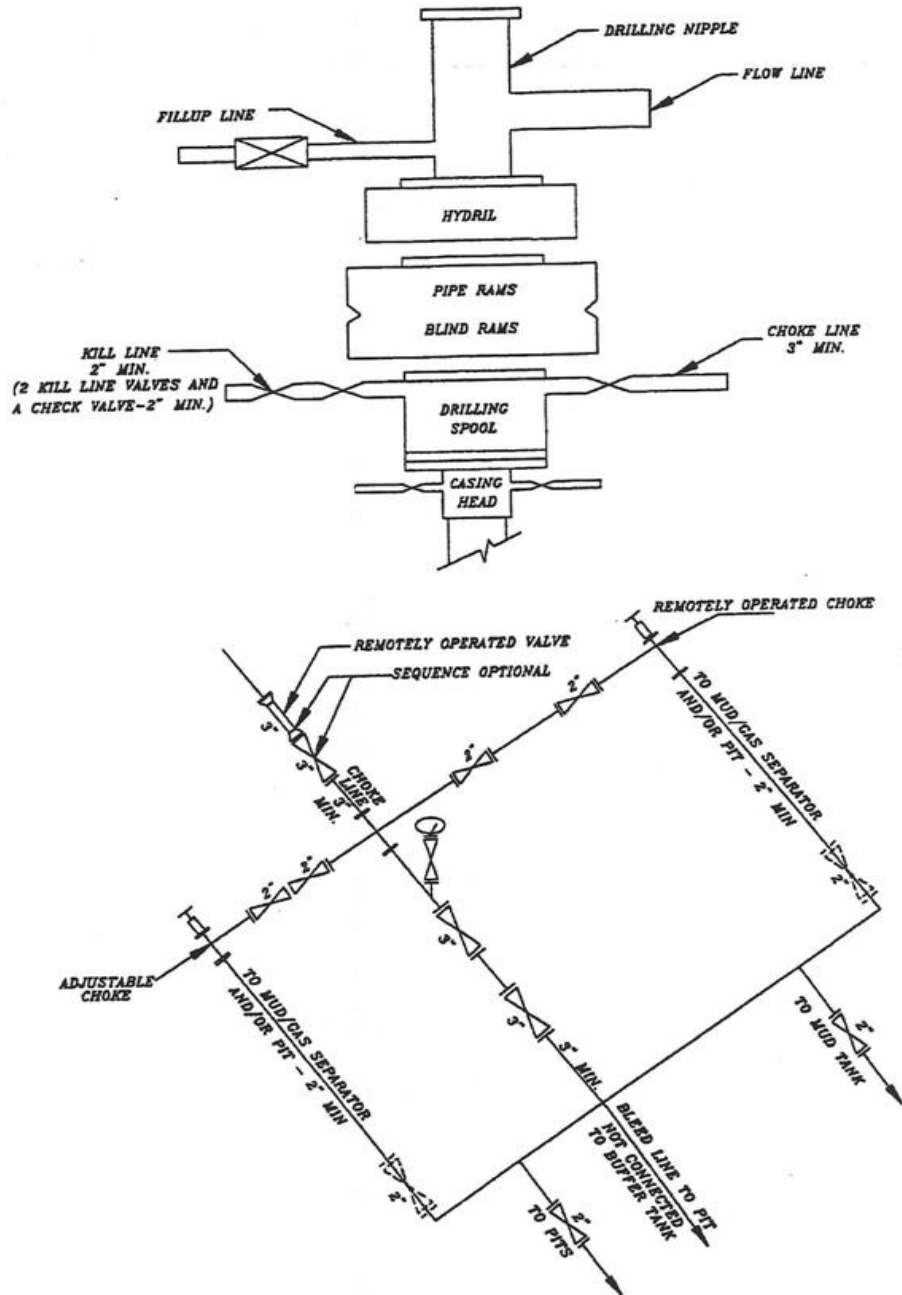


SCHEMATIC DIAGRAM OF 5,000 PSI BOP STACK



-
- A horizontal graphic scale bar with a central zero point. To the left of zero, there are two segments labeled '500'' and one segment labeled '1000''. To the right of zero, there are two segments labeled '500'' and one segment labeled '1000''. The segments are filled with different patterns: diagonal lines for the first 500' on each side, horizontal lines for the next 500' on each side, and a solid grey fill for the final 1000' on each side. The word 'SCALE' is centered below the bar.

SURVEYOR'S CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.


 No.6028691
 JOHN R
 FLAUGH
 STATE OF UTAH
 PROFESSIONAL LAND SURVEYOR
 REGISTRATION No. 6028691
 STATE OF UTAH

WELL PAD: BONANZA 1023-51

**2643' FNL, 1424' FEL (Bottom Hole)
SW $\frac{1}{4}$ NE $\frac{1}{4}$ OF SECTION 5, T10S, R23E,
S.L.B.&M., UTAH COUNTY, UTAH.**



CONSULTING, LLC
371 Coffeen Avenue
Sheridan WY 82801
Phone 307-674-0609
Fax 307-674-0182

TIMBERLINE


(435) 789-1365

ENGINEERING & LAND SURVEYING, INC.
209 NORTH 300 WEST - VERNAL, UTAH 84078

DATE SURVEYED: 03-09-10	SURVEYED BY: M.S.B.	SHEET NO: 2 2 OF 19
DATE DRAWN: 03-10-10	DRAWN BY: E.M.S.	
SCALE: 1" = 1000'	Date Last Revised:	

RELATIVE COORDINATES - From Surface Position to Bottom Hole											
WELL NAME	NORTH	EAST	WELL NAME	NORTH	EAST	WELL NAME	NORTH	EAST	WELL NAME	NORTH	EAST
BONANZA 1023-5J3AS	65.2'	-1043.7'	BONANZA 1023-5G4DS	1023.6'	-376.6'	BONANZA 1023-5I1BS	864.7'	662.6'	BONANZA 1023-5I1CS	509.4'	570.1'
WELL NAME	NORTH	EAST									
BONANZA 1023-5I4BS	68.4'	546.4'									



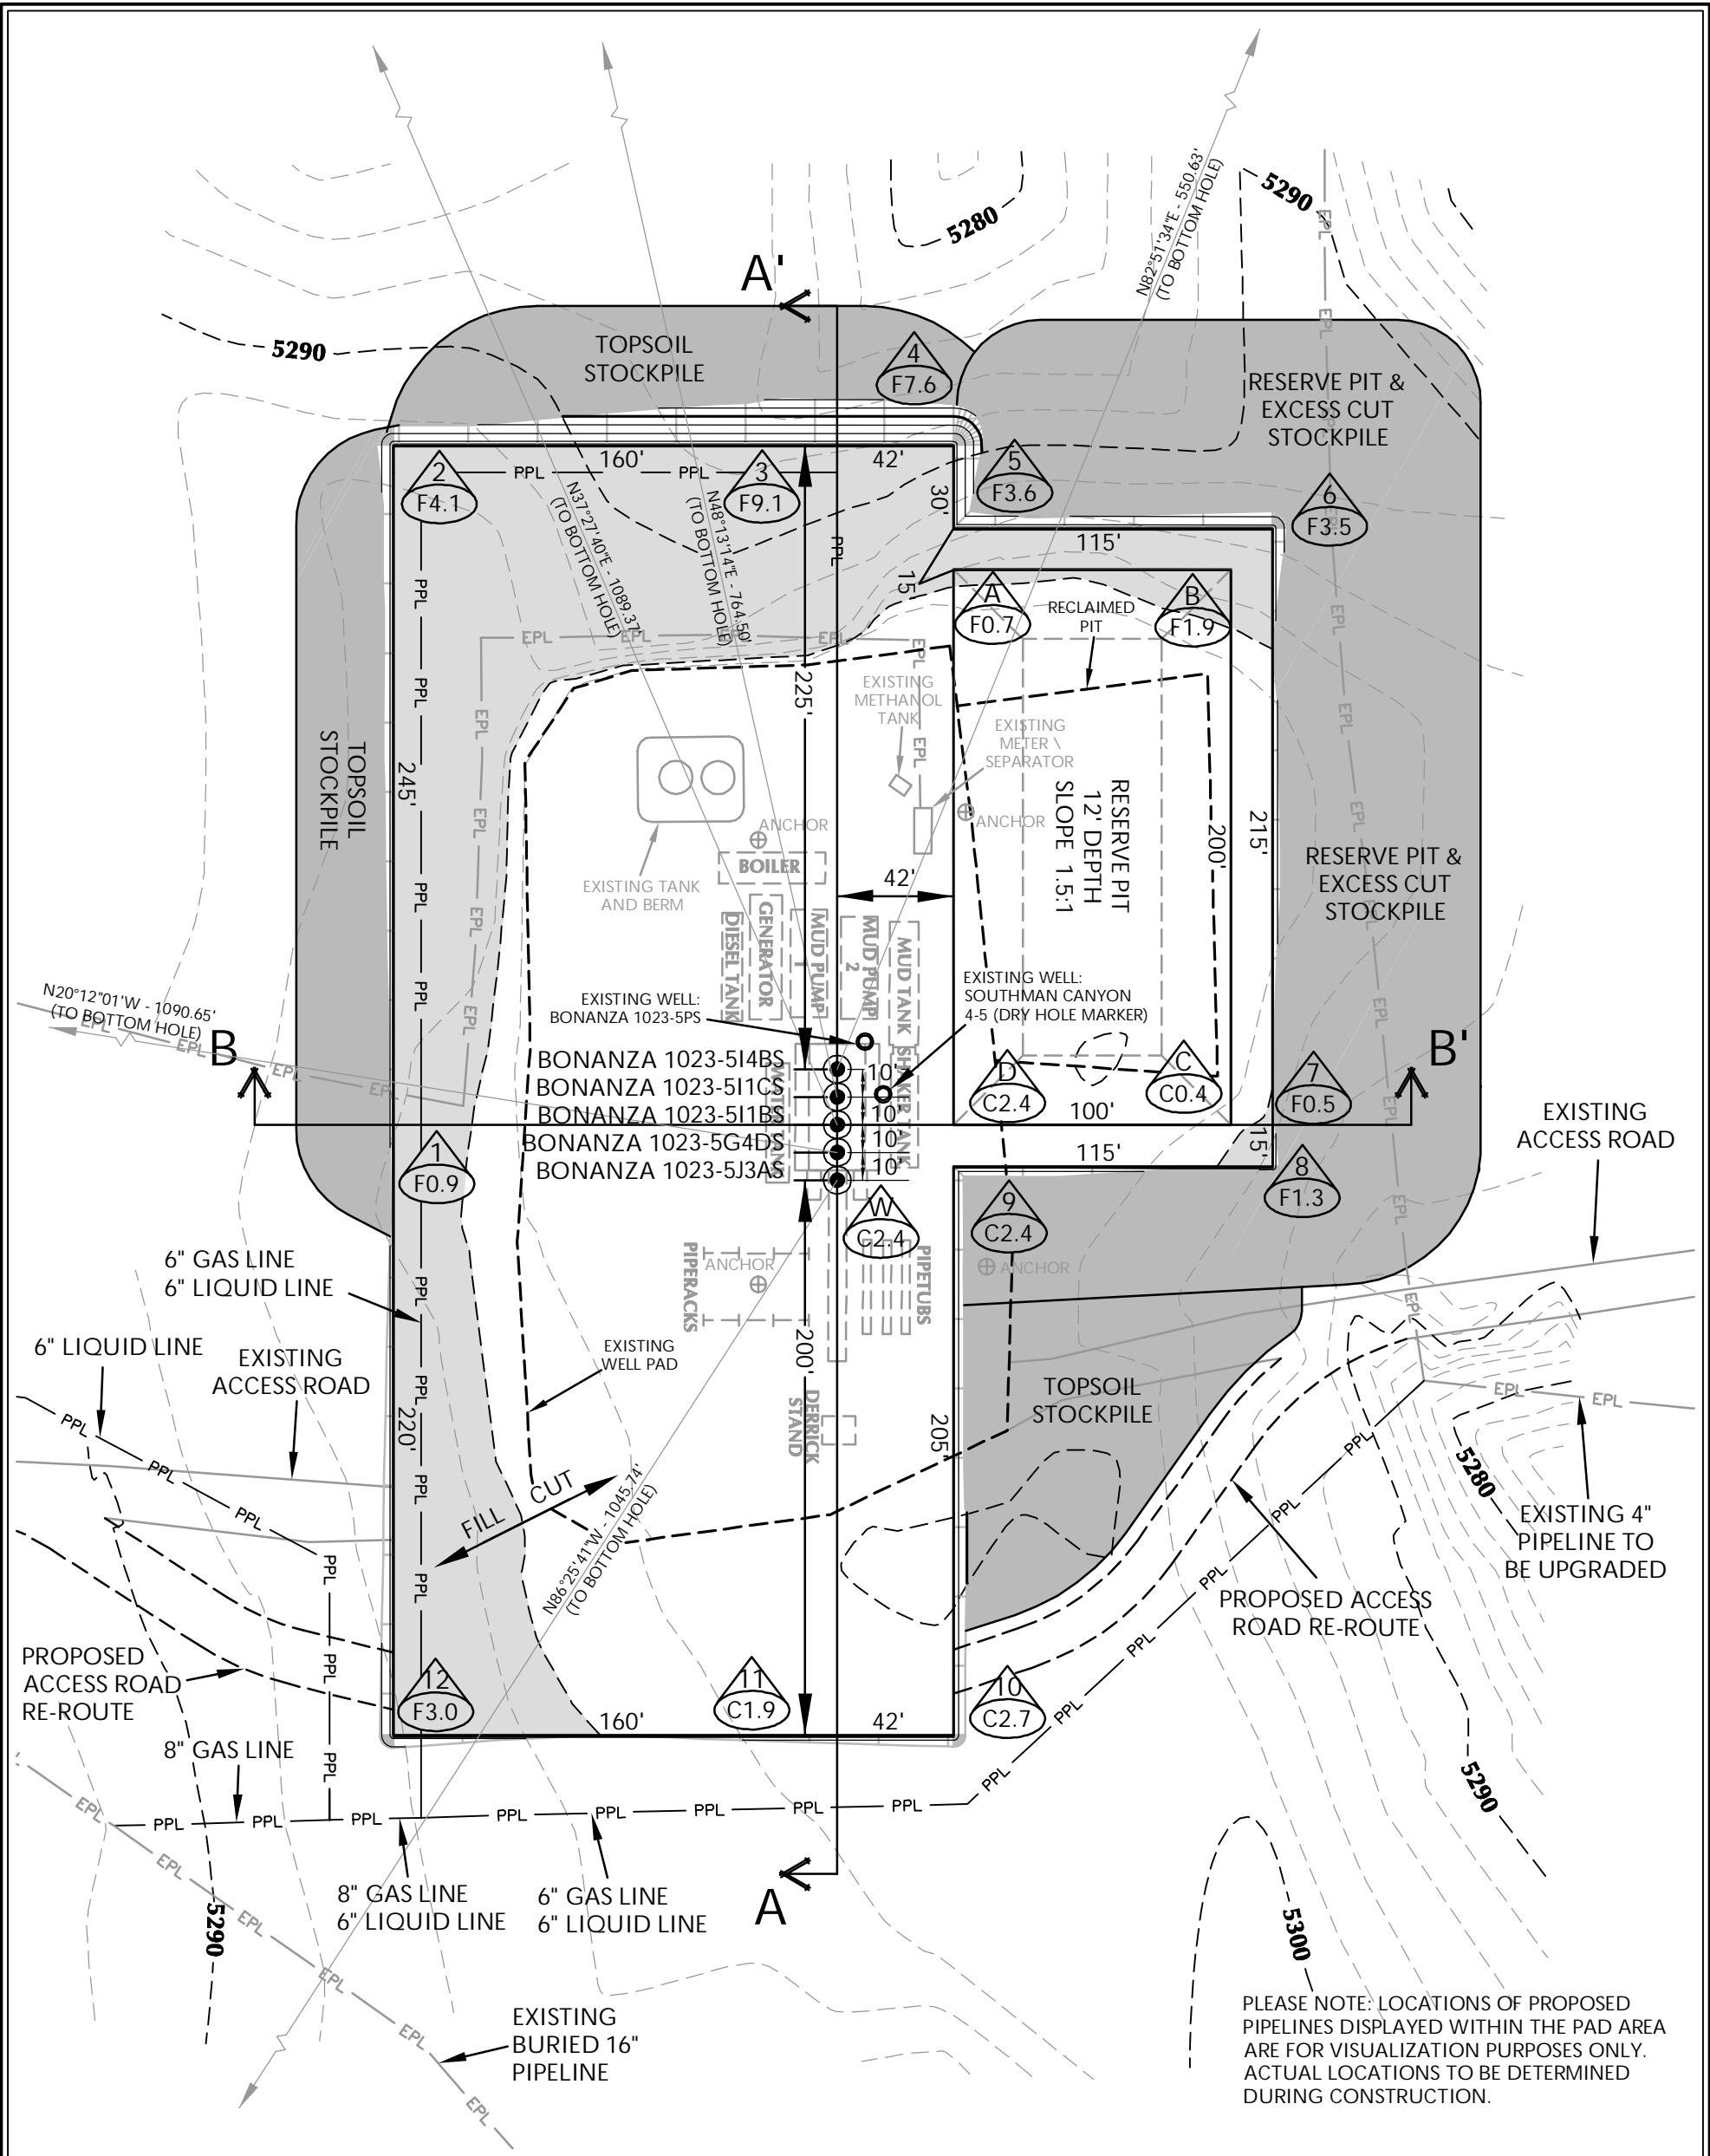

PLEASE NOTE: LOCATIONS OF PROPOSED PIPELINES DISPLAYED WITHIN THE PAD AREA ARE FOR VISUALIZATION PURPOSES ONLY. ACTUAL LOCATIONS TO BE DETERMINED DURING CONSTRUCTION.

WELL PAD - BONANZA 1023-5I DESIGN SUMMARY

EXISTING GRADE @ CENTER OF WELL PAD = 5299.2'
FINISHED GRADE ELEVATION = 5296.8'
CUT SLOPES = 1.5:1
FILL SLOPES = 1.5:1
TOTAL WELL PAD AREA = 2.92 ACRES
TOTAL DAMAGE AREA = 5.89 ACRES
SHRINKAGE FACTOR = 1.10
SWELL FACTOR = 1.00

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street - Denver, Colorado 80202

WELL PAD - BONANZA 1023-5I

WELL PAD - LOCATION LAYOUT
BONANZA 1023-5J3AS,
BONANZA 1023-5G4DS, BONANZA 1023-5I1BS,
BONANZA 1023-5I1CS & BONANZA 1023-5I4BS
LOCATED IN SECTION 5, T10S, R23E,
S.L.B.&M., Uintah County, Utah.



CONSULTING, LLC
371 Coffeen Avenue
Sheridan, WY 82801
Phone 307-674-0609
Fax 307-674-0182

WELL PAD QUANTITIES

TOTAL CUT FOR WELL PAD = 5,476 C.Y.
TOTAL FILL FOR WELL PAD = 5,134 C.Y.
TOPSOIL @ 6" DEPTH = 1,448 C.Y.
EXCESS MATERIAL = 342 C.Y.

RESERVE PIT QUANTITIES

TOTAL CUT FOR RESERVE PIT
+/- 6,680 CY
RESERVE PIT CAPACITY (2' OF FREEBOARD)
+/- 25,330 BARRELS

WELL PAD LEGEND


- EXISTING WELL LOCATION
- PROPOSED WELL LOCATION
- PROPOSED BOTTOM HOLE LOCATION
- EXISTING CONTOURS (2' INTERVAL)
- PROPOSED CONTOURS (2' INTERVAL)
- PPL - PROPOSED PIPELINE
- EPL - EXISTING PIPELINE




HORIZONTAL 0 30 60 1" = 60'
2' CONTOURS

Scale: 1"=60' Date: 3/30/10 SHEET NO: 7
REVISED: SEA 6/25/10 7 OF 17

TIMBERLINE ENGINEERING & LAND SURVEYING, INC.
209 NORTH 300 WEST - VERNAL, UTAH 84078
(435) 789-1365

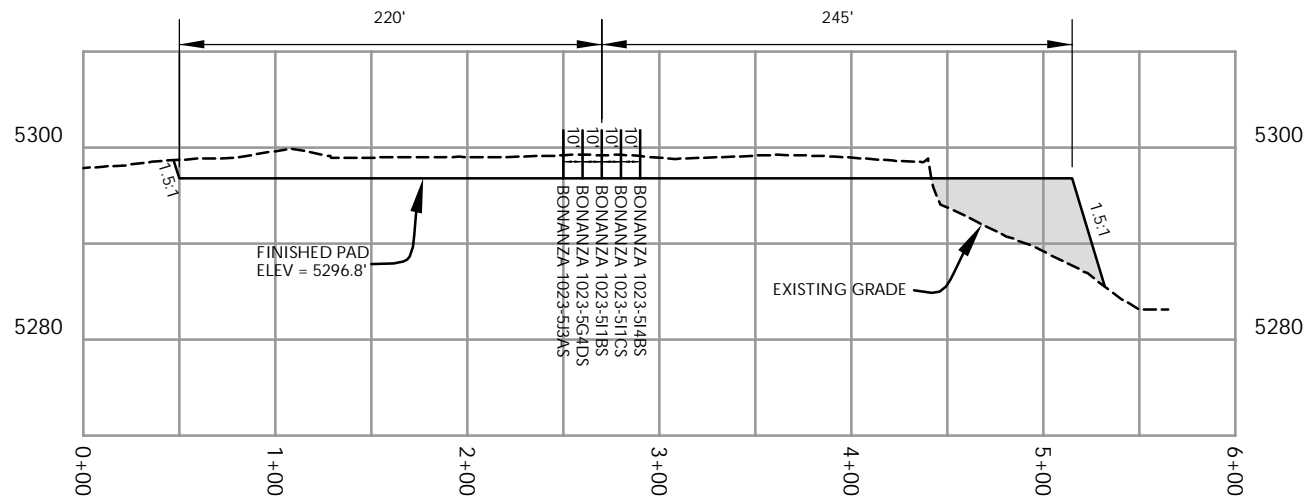

CROSS SECTION A-A'

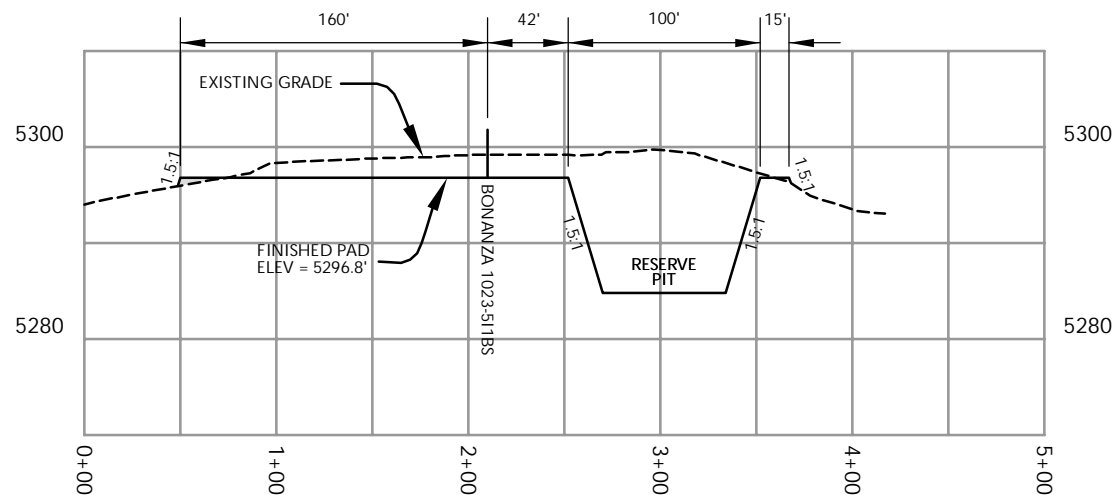

CROSS SECTION B-B'

NOTE: CROSS SECTION B-B' DEPICTS
MAXIMUM RESERVE PIT DEPTH.

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street - Denver, Colorado 80202

WELL PAD - BONANZA 1023-51


WELL PAD - CROSS SECTIONS
BONANZA 1023-5J3AS,
BONANZA 1023-5G4DS, BONANZA 1023-511BS,
BONANZA 1023-511CS & BONANZA 1023-514BS
LOCATED IN SECTION 5, T10S, R23E,
S.L.B.&M., UINTAH COUNTY, UTAH.



CONSULTING, LLC
371 Coffeen Avenue
Sheridan, WY 82801
Phone 307-674-0609
Fax 307-674-0182


TIMBERLINE
ENGINEERING & LAND SURVEYING, INC.
209 NORTH 300 WEST - VERNAL, UTAH 84078

(435) 789-1365



Scale: 1"=100'	Date: 3/30/10	SHEET NO:
REVISED:	SEA 6/25/10	8 8 OF 17

RECEIVED: October 17, 2011

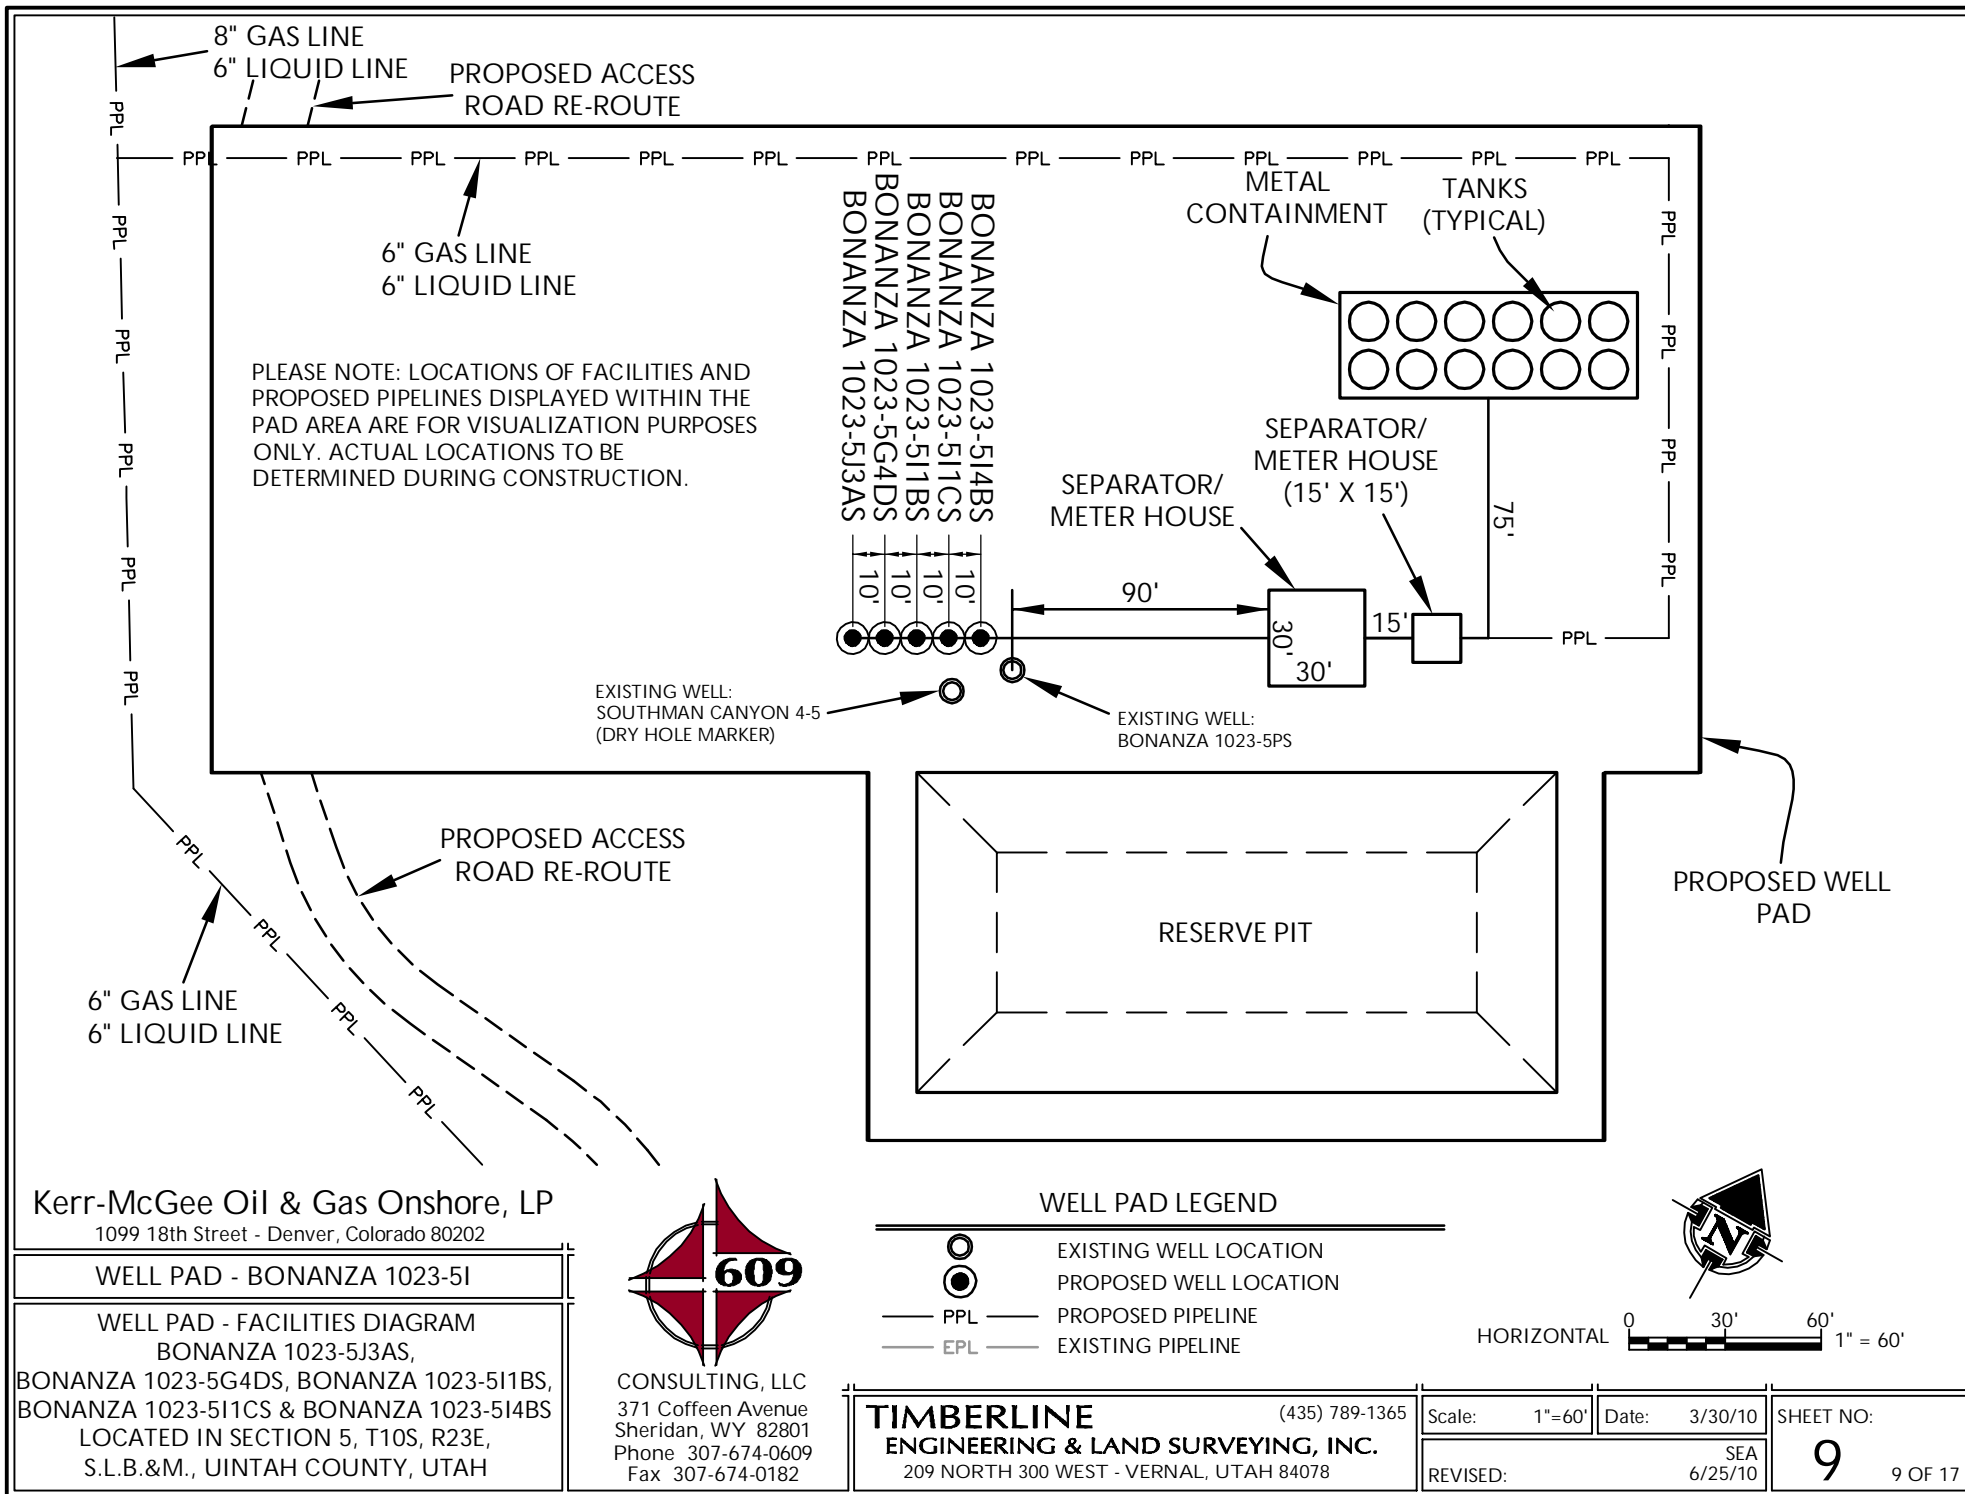

RECEIVED: October 17, 2011

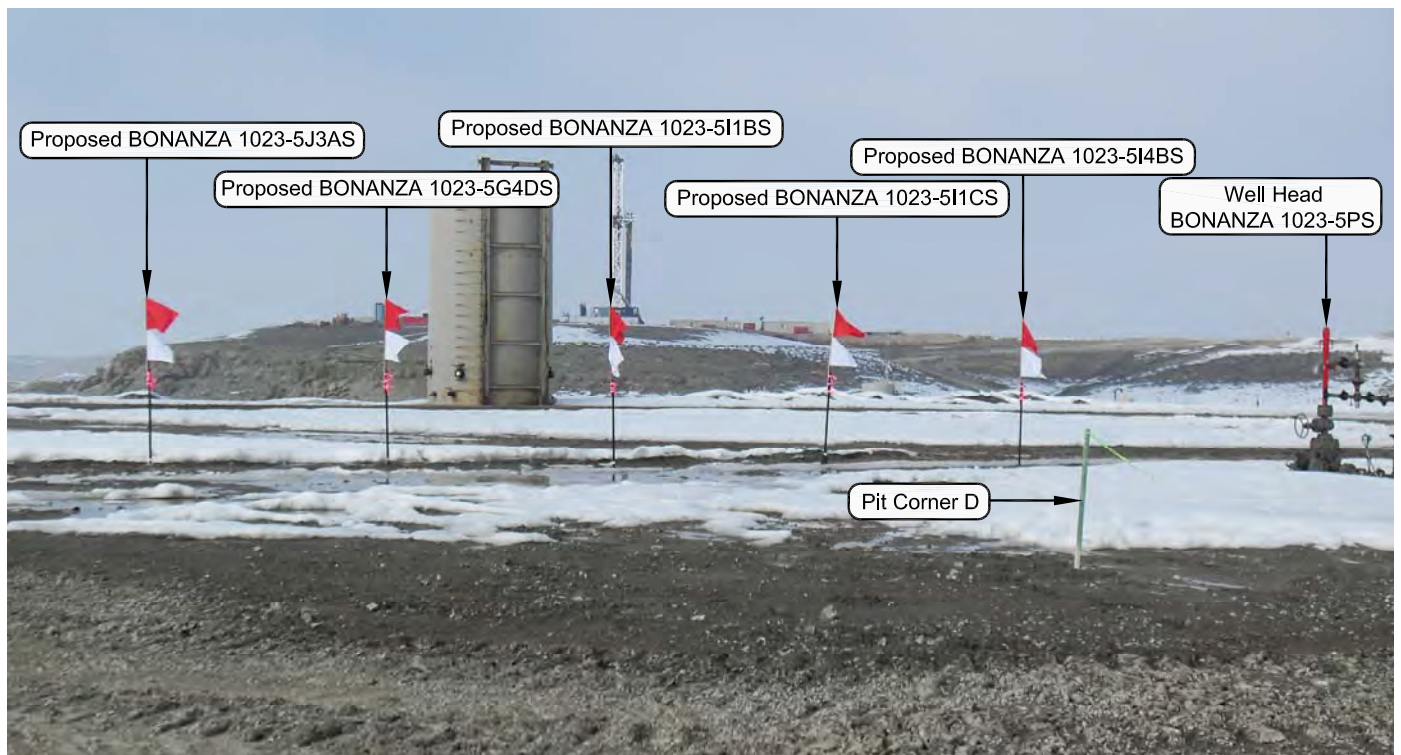


PHOTO VIEW: FROM PIT CORNER D TO LOCATION STAKES

CAMERA ANGLE: NORTHWESTERLY



PHOTO VIEW: FROM BEGINNING OF PROPOSED ROAD

CAMERA ANGLE: SOUTHERLY

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street - Denver, Colorado 80202

WELL PAD - BONANZA 1023-5I

LOCATION PHOTOS
BONANZA 1023-5J3AS, BONANZA 1023-5G4DS,
BONANZA 1023-5I1BS, BONANZA 1023-5I1CS &
BONANZA 1023-5I4BS
LOCATED IN SECTION 5, T10S, R23E,
S.L.B.&M., UTAH COUNTY, UTAH.



CONSULTING, LLC
371 Coffeen Avenue
Sheridan WY 82801
Phone 307-674-0609
Fax 307-674-0182


TIMBERLINE

(435) 789-1365

ENGINEERING & LAND SURVEYING, INC.
209 NORTH 300 WEST - VERNAL, UTAH 84078

DATE PHOTOS TAKEN: 03-09-10	PHOTOS TAKEN BY: M.S.B.	SHEET NO: 10 10 OF 17
DATE DRAWN: 03-10-10	DRAWN BY: E.M.S.	
Date Last Revised:		

RECEIVED: October 17, 2011

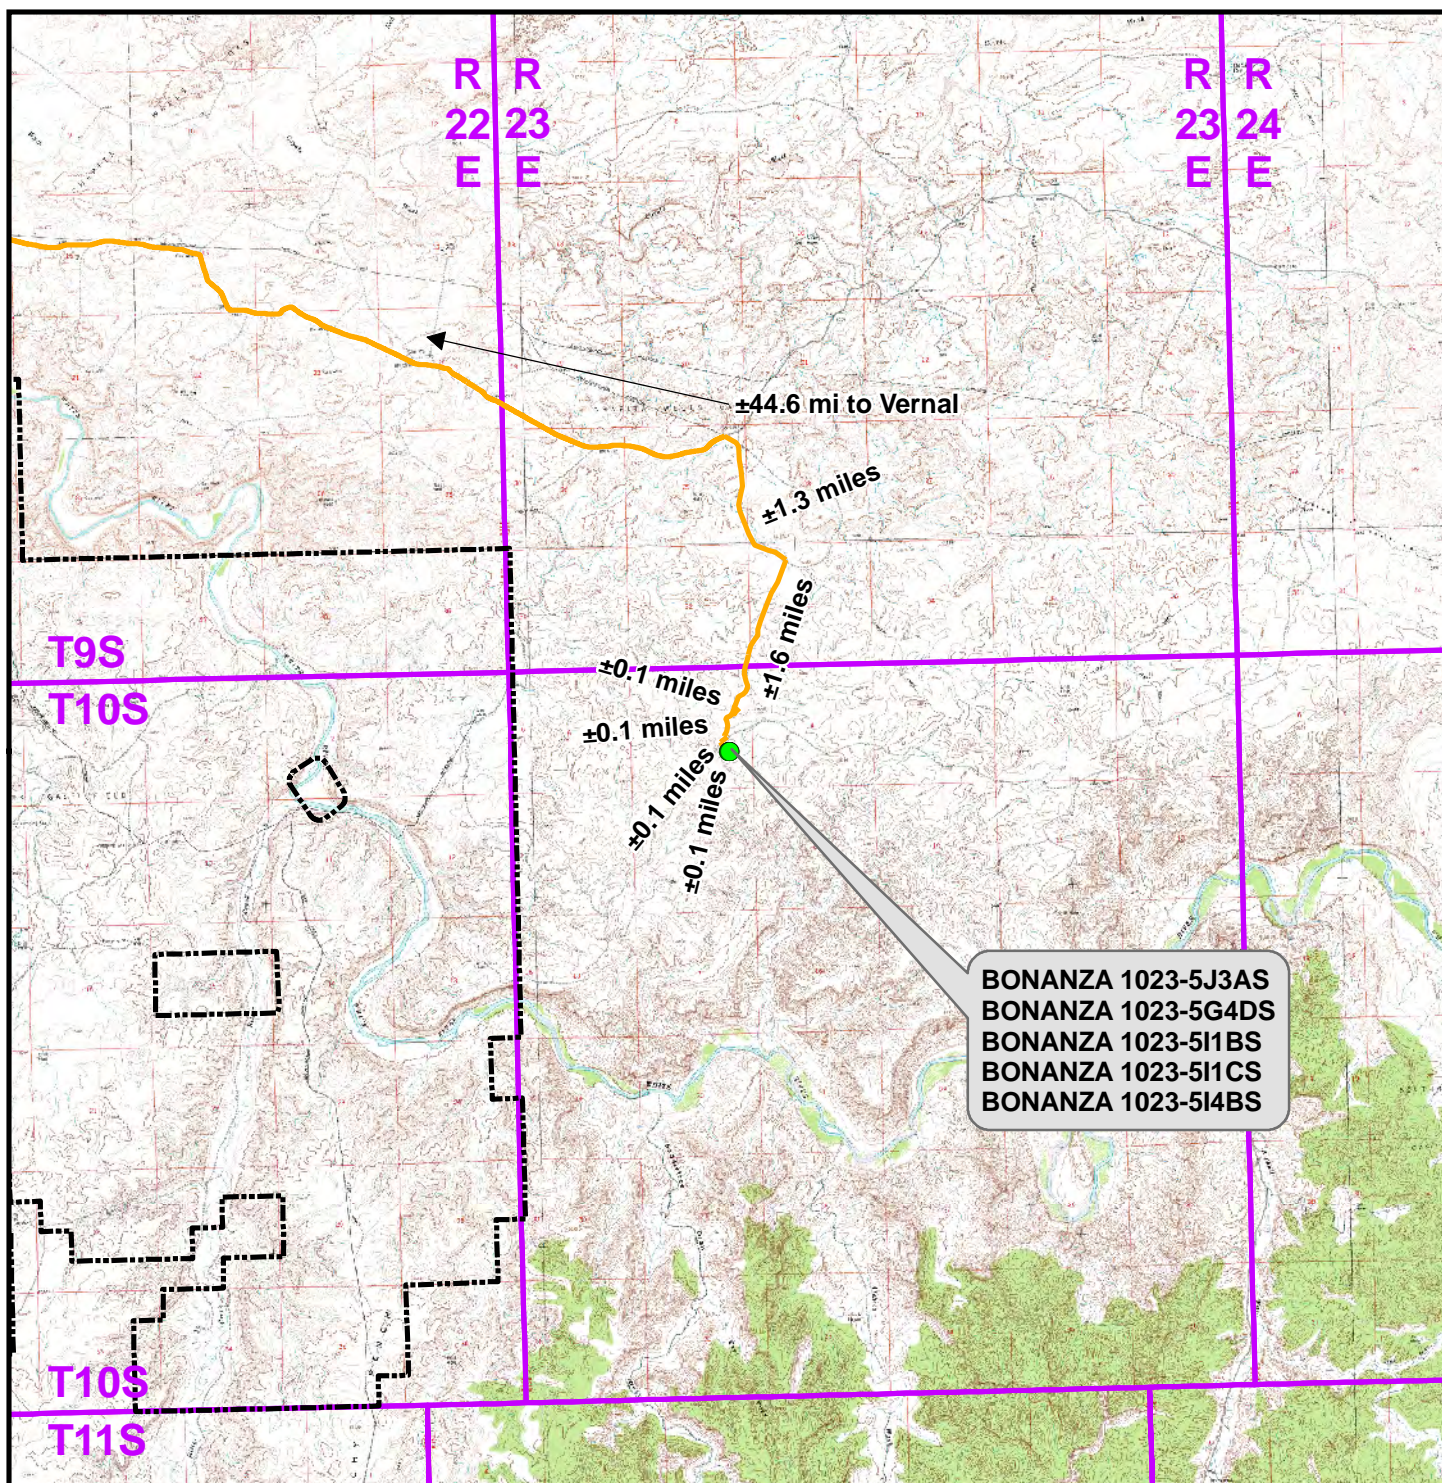

Legend

- Proposed Well Location
- Natural Buttes Unit Boundary
- Access Route - Proposed

Distance From Well Pad - BONANZA 1023-5I To Unit Boundary: ±9,070ft

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street, Denver, Colorado 80202

WELL PAD - BONANZA 1023-5I

TOPO A

BONANZA 1023-5J3AS, BONANZA 1023-5G4DS,
BONANZA 1023-5I1BS, BONANZA 1023-5I1CS &
BONANZA 1023-5I4BS

LOCATED IN SECTION 5, T10S, R23E
S.L.B.&M., UTAH COUNTY, UTAH




Scale: 1:100,000	NAD83 USP Central
Drawn: CPS	Date: 30 Mar 2010
Revised: TL	Date: 25 June 2010

Sheet No:

11 11 of 17

RECEIVED: October 17, 2011

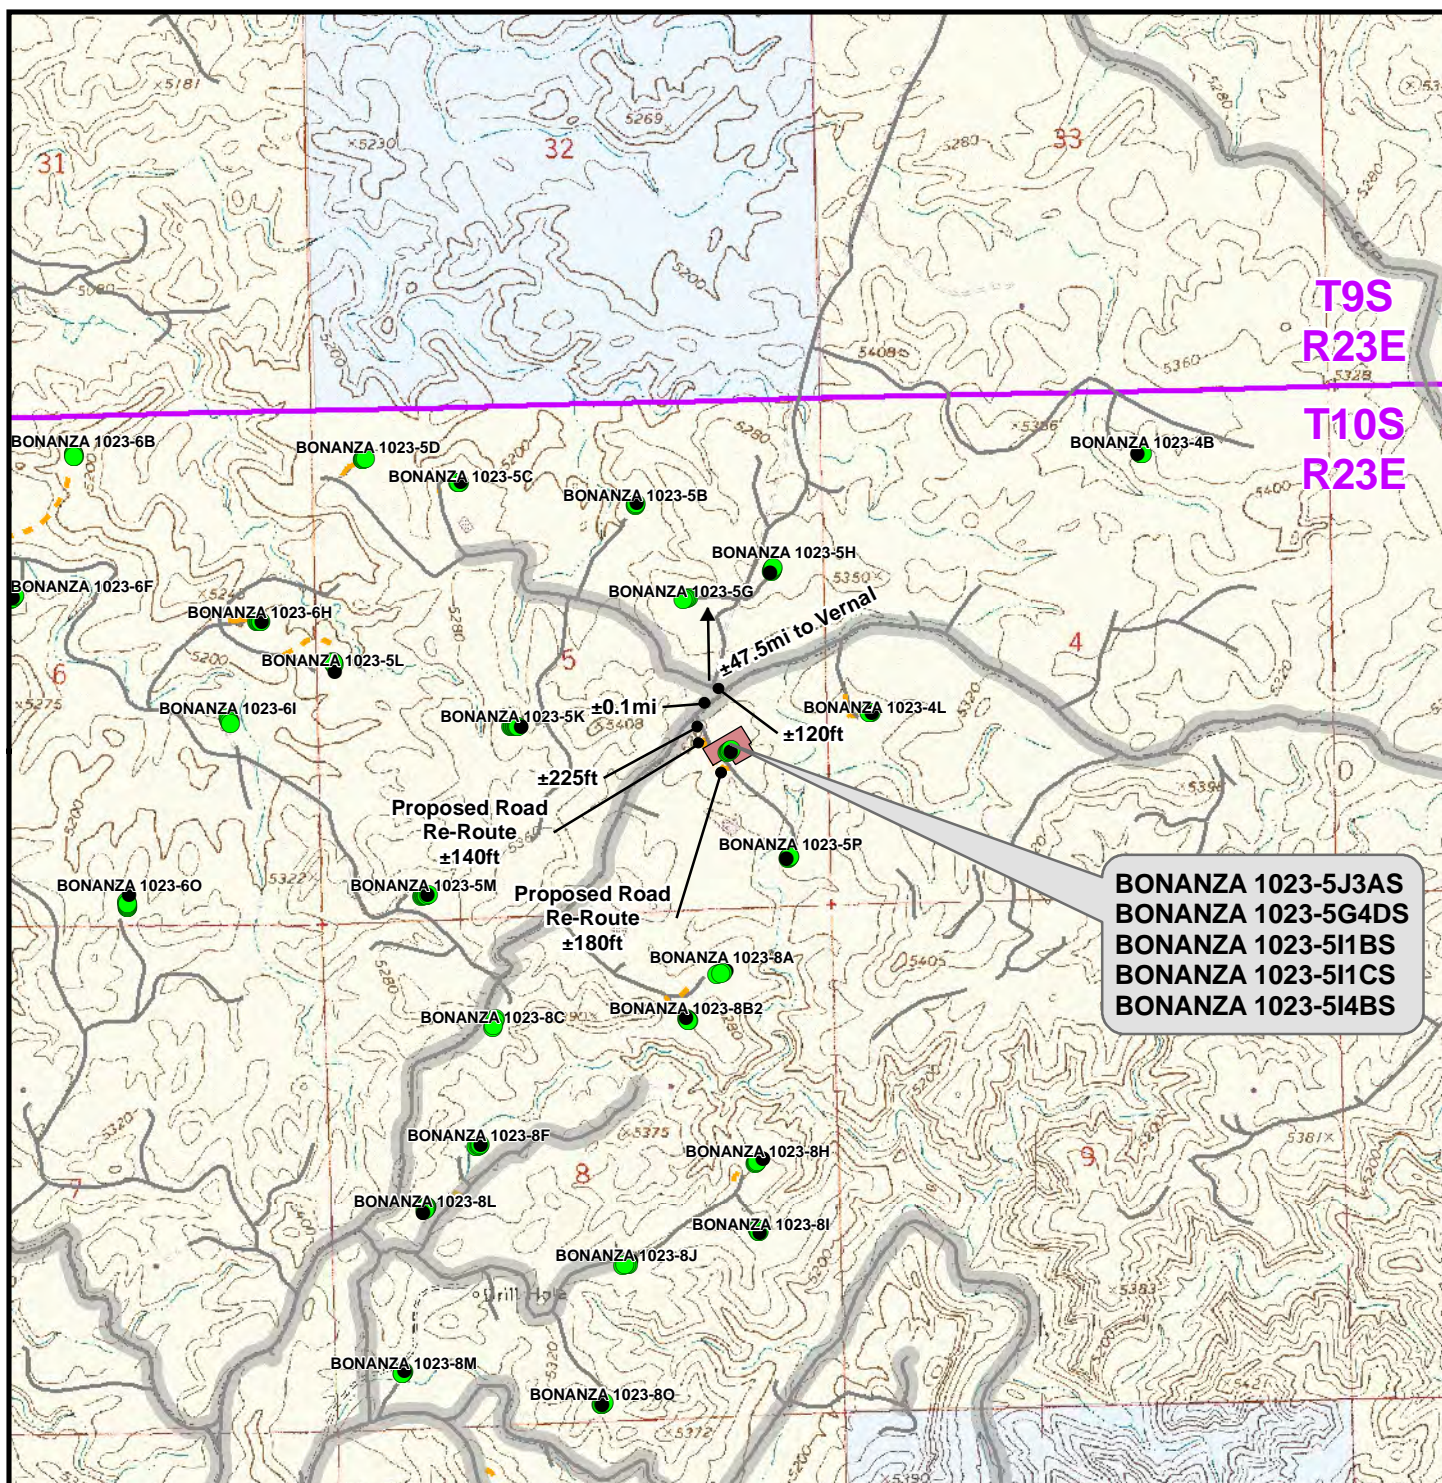

Legend

- | | | | | | |
|-------------------|------------|-----------------------|---------------|-----------------------------|-----------|
| ● Well - Proposed | ■ Well Pad | - - - Road - Proposed | ▬ County Road | ■ Bureau of Land Management | ■ State |
| ● Well - Existing | | ▬ Road - Existing | | ■ Indian Reservation | ■ Private |

Total Proposed Road Re-Route Length: ±320ft

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street, Denver, Colorado 80202

WELL PAD - BONANZA 1023-51

TOPO B

BONANZA 1023-5J3AS, BONANZA 1023-5G4DS,
BONANZA 1023-5I1BS, BONANZA 1023-5I1CS &
BONANZA 1023-5I4BS

LOCATED IN SECTION 5, T10S, R23E
S.L.B.&M., UTAH COUNTY, UTAH




CONSULTING, LLC
371 Coffeen Avenue
Sheridan, WY 82801
Phone (307) 674-0609
Fax (307) 674-0182



Scale: 1" = 2,000ft	NAD83 USP Central	Sheet No:
Drawn: CPS	Date: 30 Mar 2010	12 12 of 17
Revised: TL	Date: 25 June 2010	

RECEIVED: October 17, 2011

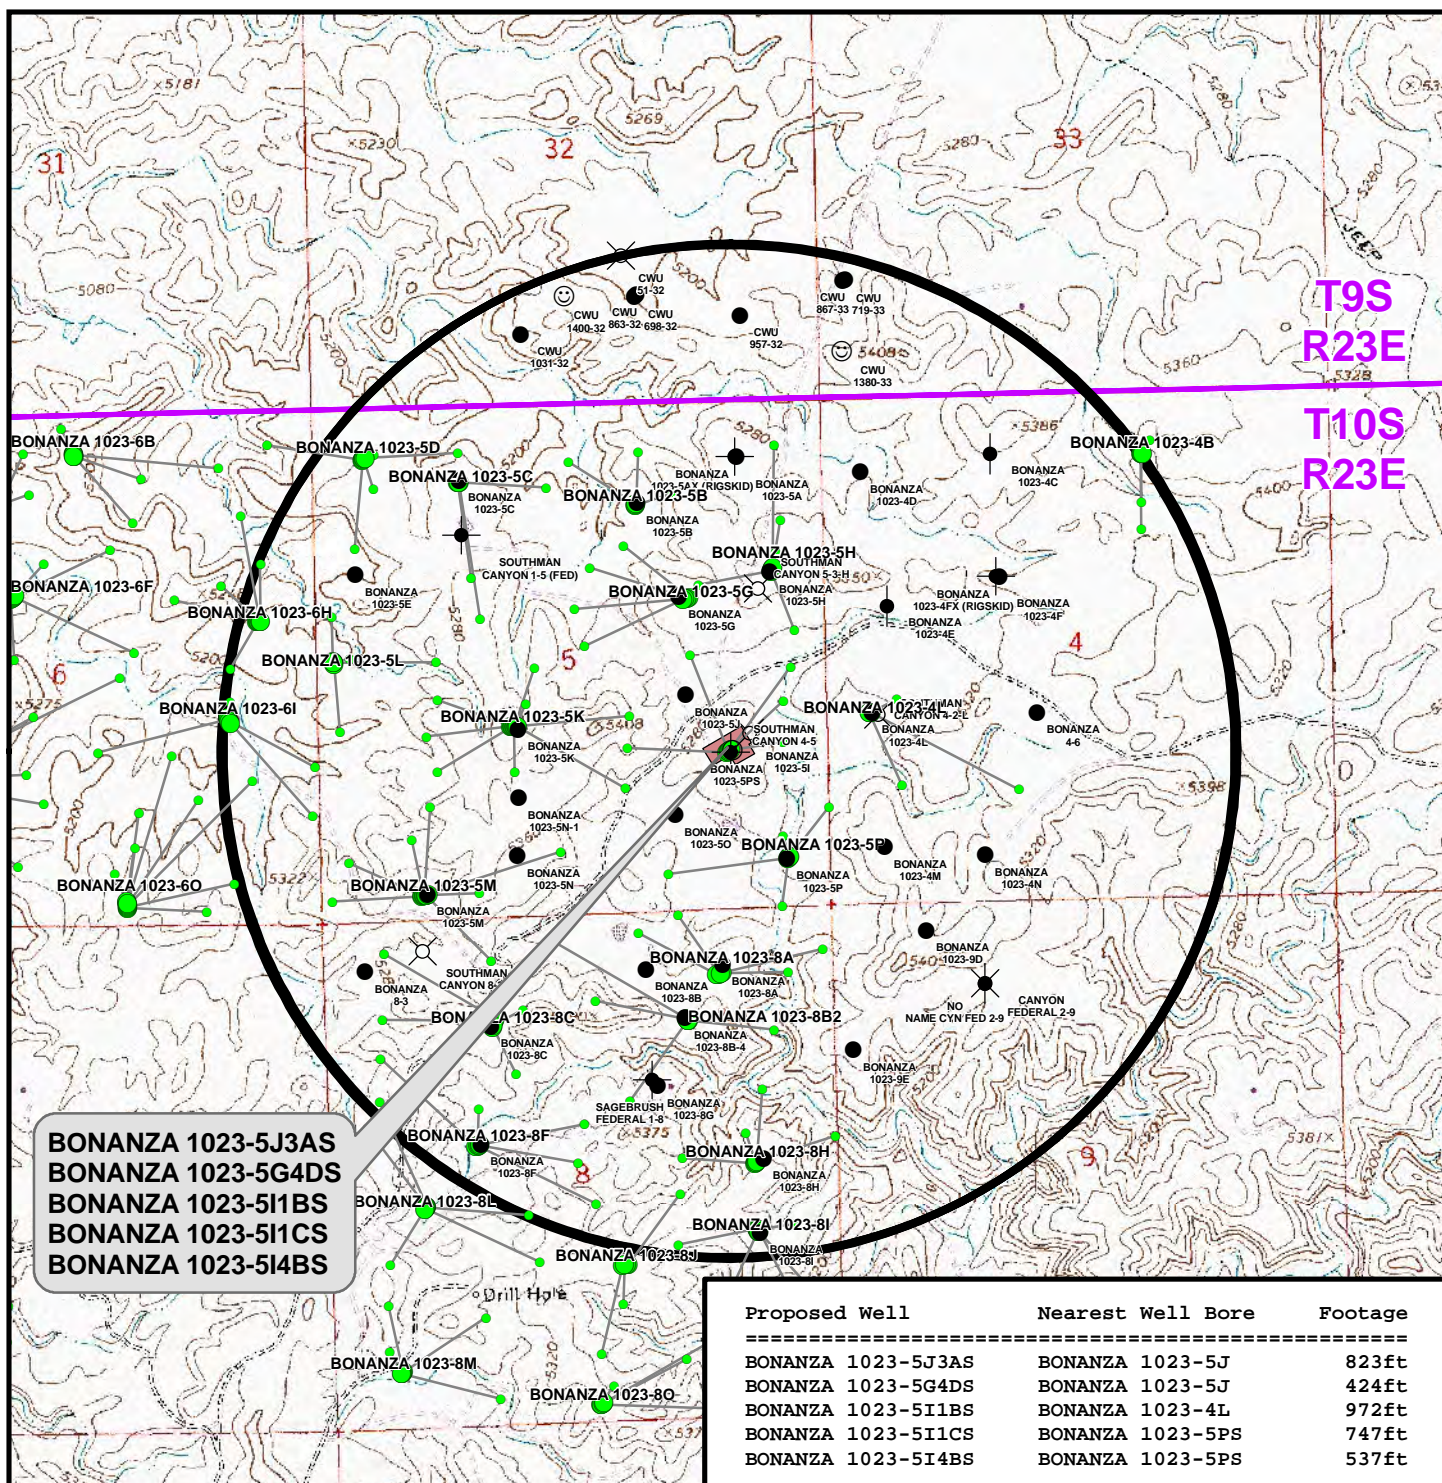**Legend**

- Well - Proposed
- Bottom Hole - Proposed
- Well Path
- Well Pad
- Well - 1 Mile Radius

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street, Denver, Colorado 80202

WELL PAD - BONANZA 1023-5I**TOPO C**

**BONANZA 1023-5J3AS, BONANZA 1023-5G4DS,
BONANZA 1023-5I1BS, BONANZA 1023-5I1CS &
BONANZA 1023-5I4BS**

**LOCATED IN SECTION 5, T10S, R23E
S.L.B.&M., UTAH COUNTY, UTAH**




- Producing
- Temporarily-Abandoned
- Active
- Shut-In
- ☺ Spudded (Drilling commenced; Not yet completed)
- ▲ Approved permit (APD); not yet spudded
- New Permit (Not yet approved or drilled)
- ⊕ Inactive
- ⊗ Drilling Operations Suspended
- ⊗ Plugged and Abandoned
- ⊗ Location Abandoned
- ⊗ Dry hole marker, buried
- ⊗ Returned APD (Unapproved)

Scale: 1" = 2,000ft
NAD83 USP Central
Drawn: CPS
Revised: TL

Sheet No:

13

13 of 17

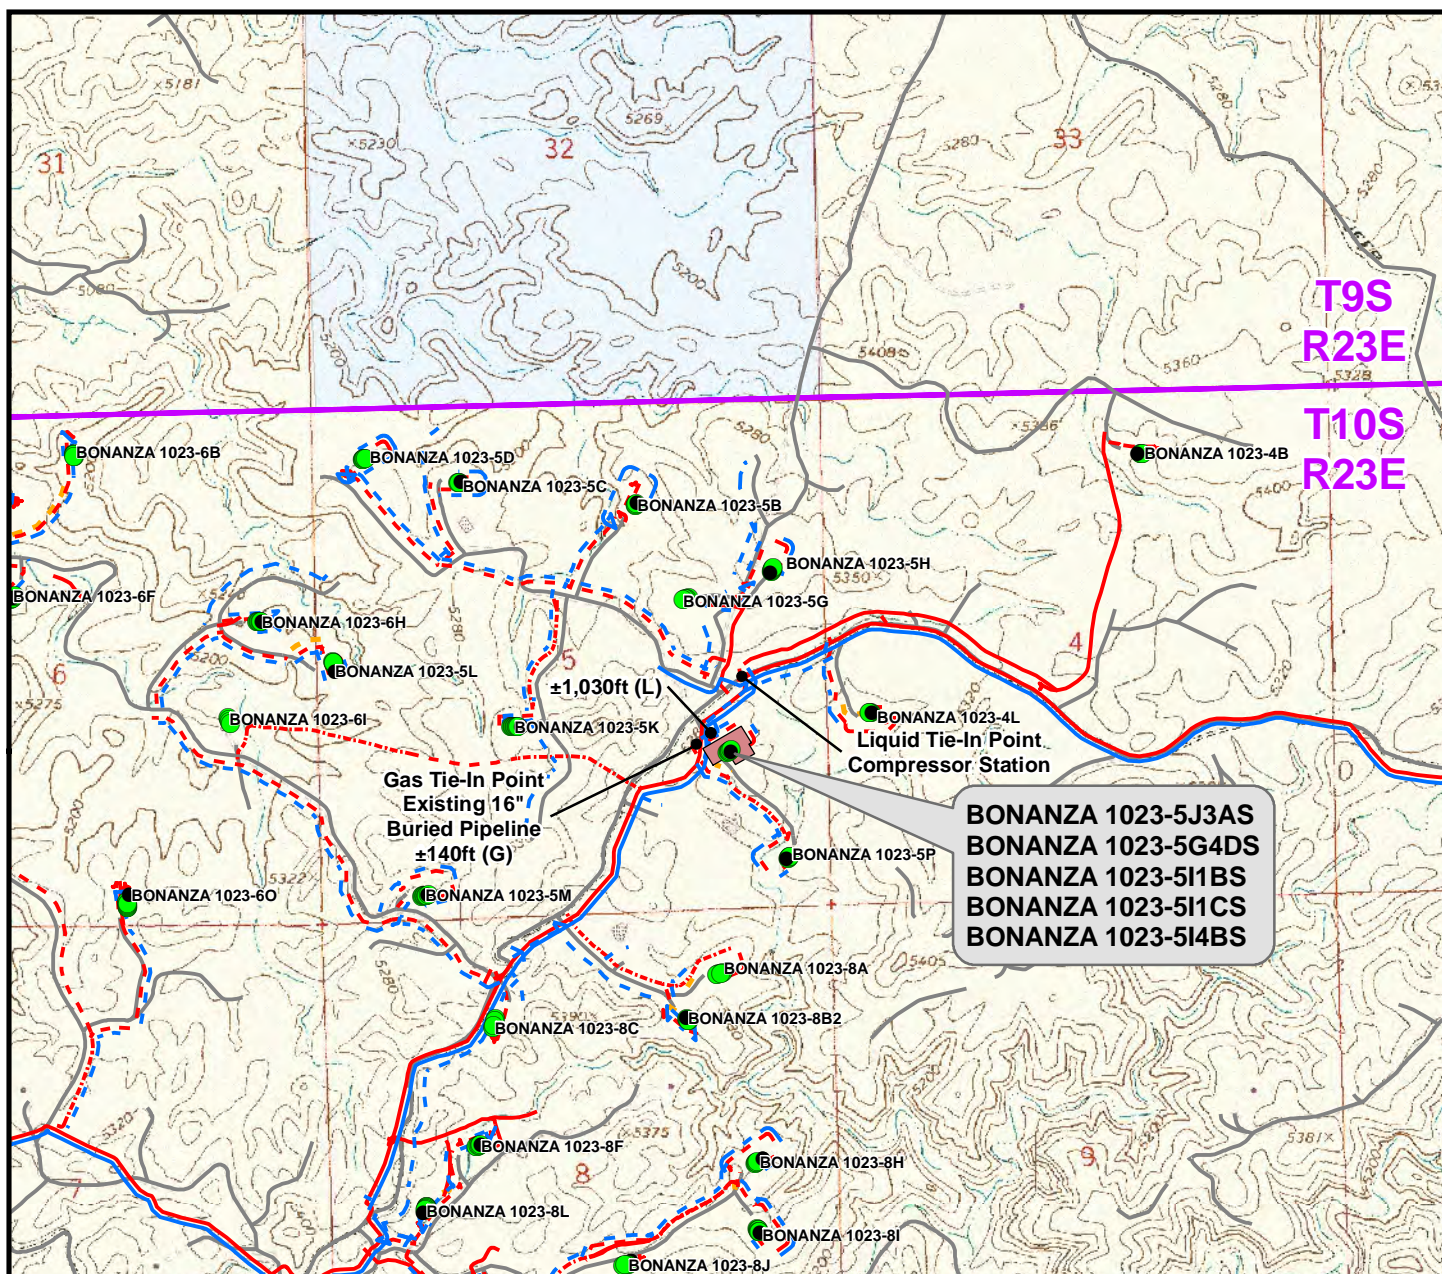

Proposed Liquid Pipeline	Length
Proposed 6" (First Meter House to Edge of Pad)	±680ft
Proposed 6" (Edge of Pad to Compressor Station)	±1,030ft

TOTAL PROPOSED LIQUID PIPELINE = ± 1,710ft

Proposed Gas Pipeline	Length
Proposed 6" (First Meter House to Edge of Pad)	±680ft
Proposed 6" (Edge of Pad to 1023-5P Intersection)	±30ft
Proposed 8" (1023-5P Intersection to Existing 16" Buried Pipeline)	±110ft

TOTAL PROPOSED GAS PIPELINE = ±820ft

Legend

● Well - Proposed	- - - Gas Pipeline - Proposed	- - - Liquid Pipeline - Proposed	- - - Road - Proposed	■ Bureau of Land Management
● Well - Existing	- - - Gas Pipeline - To Be Upgraded	- - - Liquid Pipeline - To Be Upgraded	- - - Road - Existing	■ Indian Reservation
■ Well Pad	- - - Gas Pipeline - Existing	- - - Liquid Pipeline - Existing		■ State
				■ Private

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street, Denver, Colorado 80202

WELL PAD - BONANZA 1023-5I


TOPO D

BONANZA 1023-5J3AS, BONANZA 1023-5G4DS,
BONANZA 1023-5I1BS, BONANZA 1023-5I1CS &
BONANZA 1023-5I4BS
LOCATED IN SECTION 5, T10S, R23E
S.L.B.&M., UTAH COUNTY, UTAH



Scale: 1" = 2,000ft	NAD83 USP Central	Sheet No:
Drawn: CPS	Date: 30 Mar 2010	14 14 of 17
Revised: TL	Date: 25 June 2010	

RECEIVED: October 17, 2011

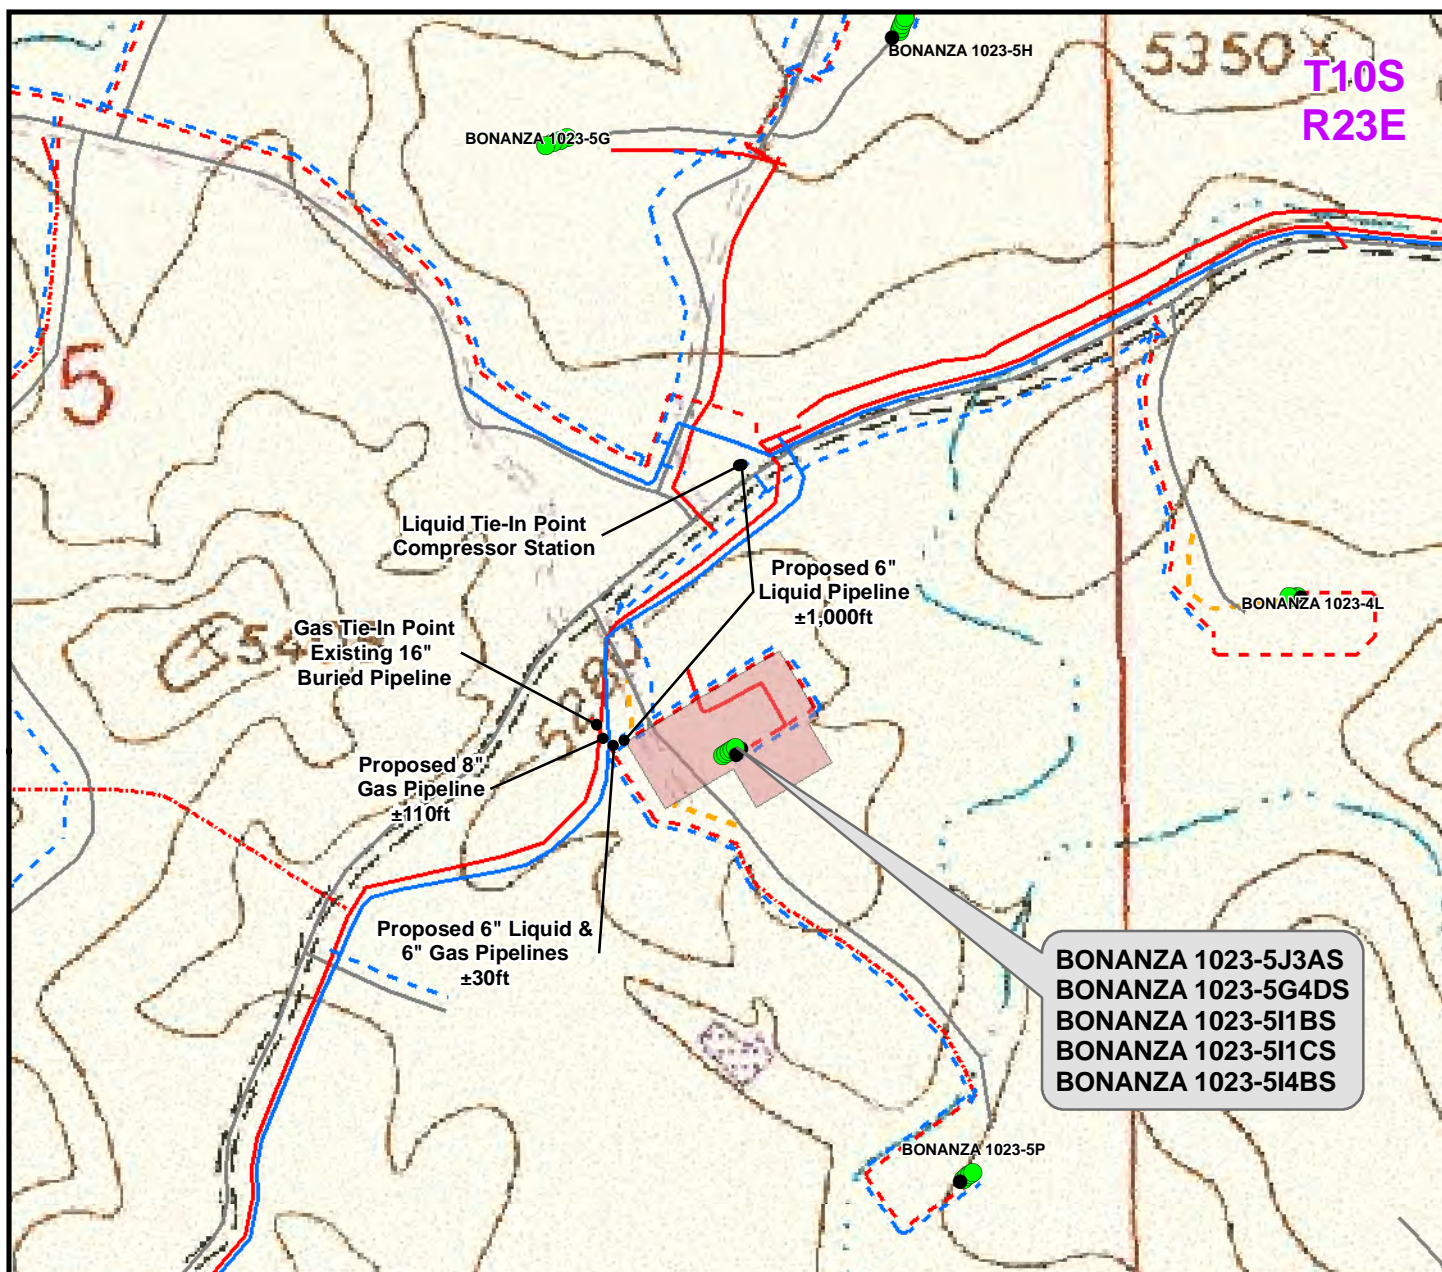

Proposed Liquid Pipeline	Length
Proposed 6" (First Meter House to Edge of Pad)	±680ft
Proposed 6" (Edge of Pad to Compressor Station)	±1,030ft

TOTAL PROPOSED LIQUID PIPELINE = ± 1,710ft

Proposed Gas Pipeline	Length
Proposed 6" (First Meter House to Edge of Pad)	±680ft
Proposed 6" (Edge of Pad to 1023-5P Intersection)	±30ft
Proposed 8" (1023-5P Intersection to Existing 16" Buried Pipeline)	±110ft

TOTAL PROPOSED GAS PIPELINE = ±820ft

Legend

● Well - Proposed	- - - Gas Pipeline - Proposed	- - - Liquid Pipeline - Proposed	- - - Road - Proposed	■ Bureau of Land Management
● Well - Existing	- - - Gas Pipeline - To Be Upgraded	- - - Liquid Pipeline - To Be Upgraded	- - - Road - Existing	■ Indian Reservation
■ Well Pad	- - - Gas Pipeline - Existing	- - - Liquid Pipeline - Existing		■ State
				■ Private

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street, Denver, Colorado 80202


WELL PAD - BONANZA 1023-51

TOPO D (PAD & PIPELINE DETAIL)
BONANZA 1023-5J3AS, BONANZA 1023-5G4DS,
BONANZA 1023-5I1BS, BONANZA 1023-5I1CS &
BONANZA 1023-5I4BS
LOCATED IN SECTION 5, T10S, R23E
S.L.B.&M., UTAH COUNTY, UTAH



Scale: 1" = 500ft	NAD83 USP Central	Sheet No:
Drawn: CPS	Date: 30 Mar 2010	15 15 of 17
Revised: TL	Date: 25 June 2010	

RECEIVED: October 17, 2011

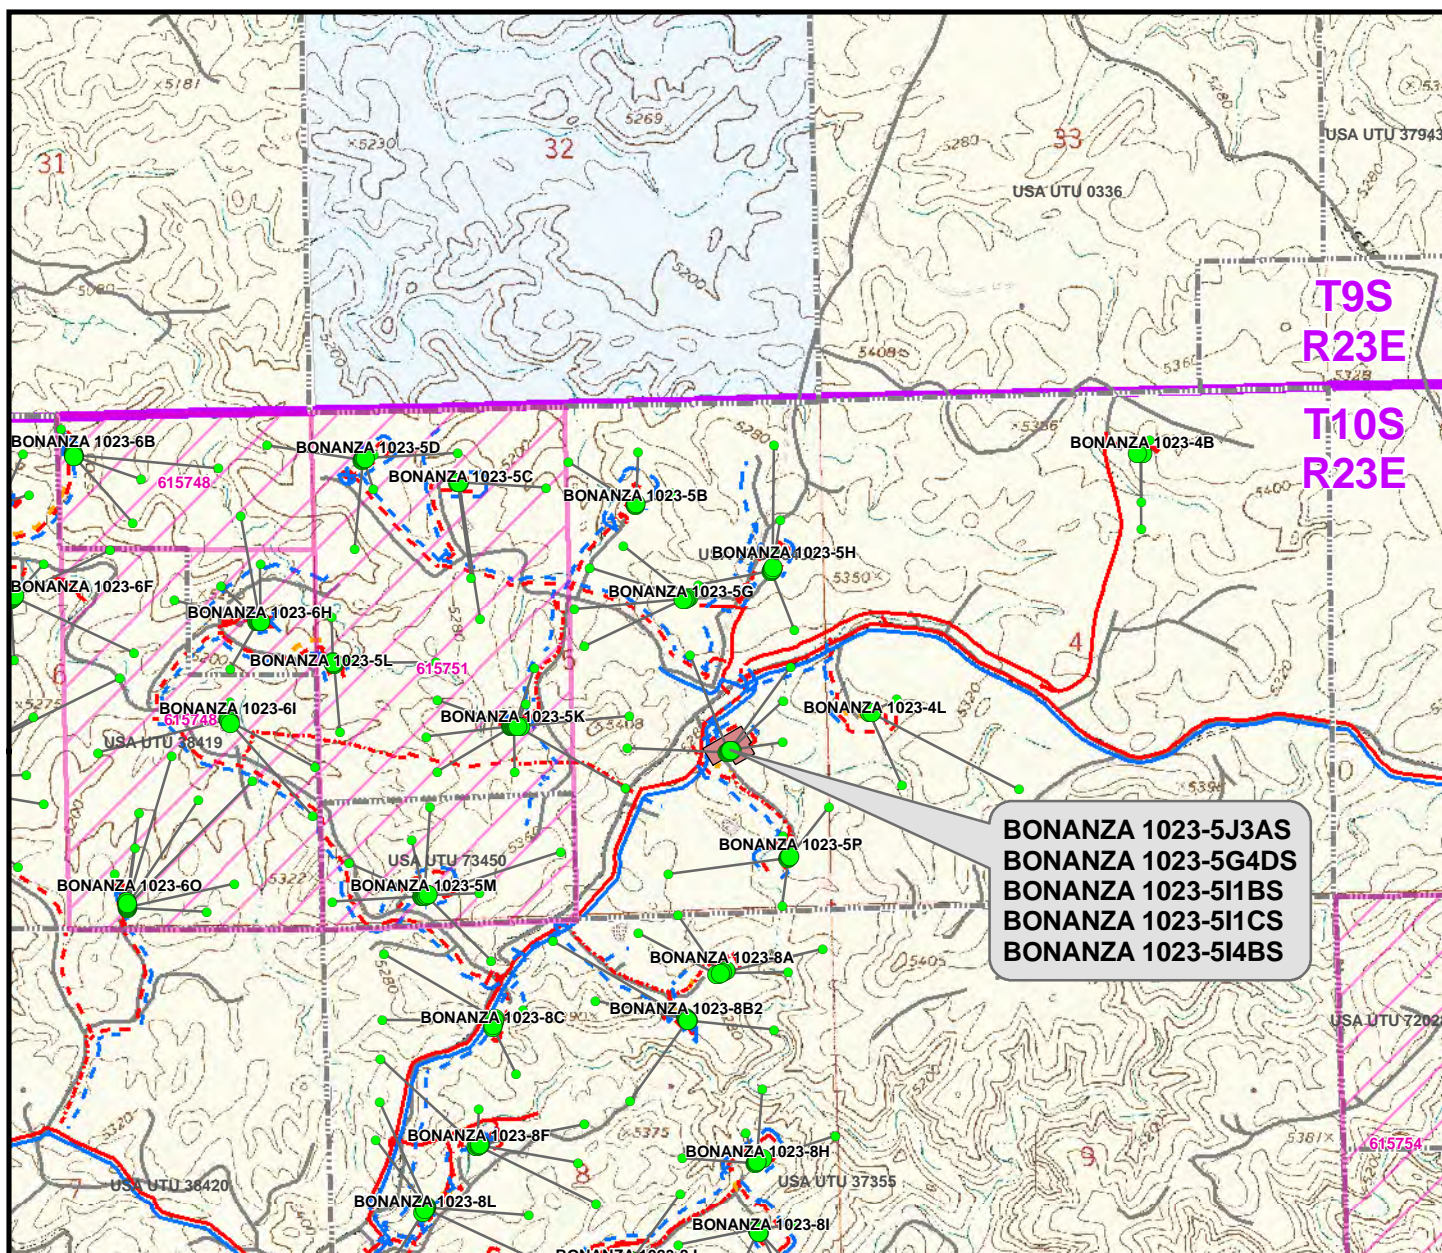

Proposed Well	Distance to Nearest CA Boundary
BONANZA 1023-5J3AS	510ft
BONANZA 1023-5G4DS	1,191ft
BONANZA 1023-5I1BS	2,238ft
BONANZA 1023-5I1CS	2,252ft
BONANZA 1023-5I4BS	2,134ft

Proposed Well	Distance To Nearest Lease Boundary
BONANZA 1023-5J3AS	628ft
BONANZA 1023-5G4DS	1,787ft
BONANZA 1023-5I1BS	2,491ft
BONANZA 1023-5I1CS	2,141ft
BONANZA 1023-5I4BS	1,705ft

Legend

Well - Proposed	Well Pad	Gas Pipeline - Proposed	Liquid Pipeline - Proposed	Road - Proposed	Bureau of Land Management
Bottom Hole - Proposed	CA Agreement	Gas Pipeline - To Be Upgraded	Liquid Pipeline - To Be Upgraded	Road - Existing	Indian Reservation
Well Path	Lease Boundary	Gas Pipeline - Existing	Liquid Pipeline - Existing		State
					Private

Kerr-McGee Oil & Gas Onshore, LP
1099 18th Street, Denver, Colorado 80202

WELL PAD - BONANZA 1023-51

TOPO E
BONANZA 1023-5J3AS, BONANZA 1023-5G4DS,
BONANZA 1023-5I1BS, BONANZA 1023-5I1CS &
BONANZA 1023-5I4BS
LOCATED IN SECTION 5, T10S, R23E
S.L.B.&M., UTAH COUNTY, UTAH



Scale: 1" = 2,000ft	NAD83 USP Central	Sheet No:
Drawn: CPS	Date: 30 Mar 2010	16
Revised: TL	Date: 25 June 2010	16 of 17

RECEIVED: October 17, 2011

**Kerr-McGee Oil & Gas Onshore, LP
WELL PAD – BONANZA 1023-5I
WELLS – BONANZA 1023-5J3AS, BONANZA 1023-5G4DS,
BONANZA 1023-5I1BS, BONANZA 1023-5I1CS &
BONANZA 1023-5I4BS
Section 5, T10S, R23E, S.L.B.&M.**

From the intersection of U.S. Highway 40 and 500 East Street in Vernal, Utah proceed in an easterly then southerly direction along U.S. Highway 40 approximately 3.3 miles to the junction of State Highway 45; exit right and proceed in a southerly direction along State Highway 45 approximately 20.2 miles to the junction of the Glen Bench Road (County B Road 3260). Exit right and proceed in a southwesterly direction along the Glen Bench Road approximately 14.4 miles to the intersection of the Chipeta Wells Road (County B Road 3410) which road intersection is approximately 400 feet northeast of the Mountain Fuel Bridge, at the White River. Exit left and proceed in a southeasterly direction along the Chipeta Wells Road approximately 6.7 miles to a Class D County Road to the right. Exit right and proceed in a southeasterly then southerly direction along the Class D Road approximately 1.3 miles to a second Class D County Road to the right. Exit right and proceed in a southwesterly direction along second Class D Road approximately 1.6 miles to a third Class D County Road to the left. Exit left and proceed in a southeasterly direction along third Class D Road approximately 120 feet to a fourth Class D County Road to the right. Exit right and proceed in a southwesterly direction along fourth Class D Road approximately 0.1 miles to a service road to the left. Exit left and proceed in a southeasterly direction along service road approximately 225 feet to a proposed access road to the right. Exit right and follow the road flags in a southerly direction approximately 140 feet to the proposed well pad.

Total distance from Vernal, Utah to the proposed well location is approximately 47.7 miles in a southerly direction.



ANADARKO PETROLEUM CORP.

UINTAH COUNTY, UTAH (nad 27)

Bonanza 1023-5I

BONANZA 1023-5G4DS

BONANZA 1023-5G4DS

Plan: PLAN #1 4-28-10 RHS

Standard Planning Report

28 April, 2010





Project: UINTAH COUNTY, UTAH (nad 27)
 Site: Bonanza 1023-5I
 Well: BONANZA 1023-5G4DS
 Wellbore: BONANZA 1023-5G4DS
 Section: SECTION 5 T10S R23E
 SHL: 1625 FSL 1048 FEL
 Design: PLAN #1 4-28-10 RHS
 Latitude: 39° 58' 30.770 N
 Longitude: 109° 20' 39.790 W
 GL: 5302.00
 KB: WELL @ 5311.00ft (Original Well Elev)



Weatherford®



Azimuths to True North
 Magnetic North: 11.17°

Magnetic Field
 Strength: 52463.0nT
 Dip Angle: 65.93°
 Date: 4/28/2010
 Model: BGGM2009

LEGEND

— BONANZA 1023-S11BS, BONANZA 1023-S11BS, PLAN #1 4-28-10 RHS V0
 — BONANZA 1023-S11CS, BONANZA 1023-S11CS, PLAN #1 4-28-10 RHS V0
 — BONANZA 1023-S14BS, BONANZA 1023-S14BS, PLAN #1 4-28-10 RHS V0
 — BONANZA 1023-S14CS, BONANZA 1023-S14CS, PLAN #1 4-28-10 RHS V0
 — Bonanza 1023-SPS EXISTING, Bonanza 1023-SPS EXISTING, Bonanza 1023-SPS EXISTING V0
 — Southman Canyon 4-5 EXISTING, Southman Canyon 4-5 EXISTING, Southman Canyon 4-5 EXISTING V0
 — PLAN #1 4-28-10 RHS

FORMATION TOP DETAILS

TVDPath	MDPath	Formation
1253.00	1254.17	GREEN RIVER
4218.00	4333.56	WASATCH
7258.00	7419.88	MESAVERDE

CASING DETAILS

TVD	MD	Name	Size
2010.00	2012.21	8 5/8"	8.62

SECTION DETAILS



MD	Inc	Azi	TVD	+N/-S	+E/-W	DLeg	TFace	VSec	Annotation
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	Start Build 2.00
450.00	3.00	339.87	449.93	3.69	-1.35	2.00	339.87	3.93	Start 1662.35 hold at 450.00 MD
2112.35	3.00	339.87	2110.00	85.37	-31.29	0.00	0.00	90.93	Start DLS 3.00 TFO 0.00
2679.08	20.00	339.87	2663.32	191.08	-70.03	3.00	0.00	203.51	Start 2087.69 hold at 2679.08 MD
4766.78	20.00	339.87	4625.09	861.58	-315.75	0.00	0.00	917.62	Start Drop -2.00
5766.88	0.00	0.00	5605.00	1023.83	-375.21	2.00	180.00	1090.42	Start 2821.00 hold at 5766.88 MD
8587.88	0.00	0.00	8426.00	1023.83	-375.21	0.00	0.00	1090.42	TD at 8587.88

WELLBORE TARGET DETAILS (MAP CO-ORDINATES AND LAT/LONG)

Name	TVD	+N/-S	+E/-W	Latitude	Longitude	Shape
PBHL	8426.00	1023.83	-375.21	39° 58' 40.890 N	109° 20' 44.610 W	Circle (Radius: 25.00)

WELL DETAILS: BONANZA 1023-5G4DS

+N/-S	+E/-W	Northing	Ground Level:	5302.00	Latitude	Longitude	Slot
0.00	0.00	14521325.14	Easting	2104264.12	39° 58' 30.770 N	109° 20' 39.790 W	

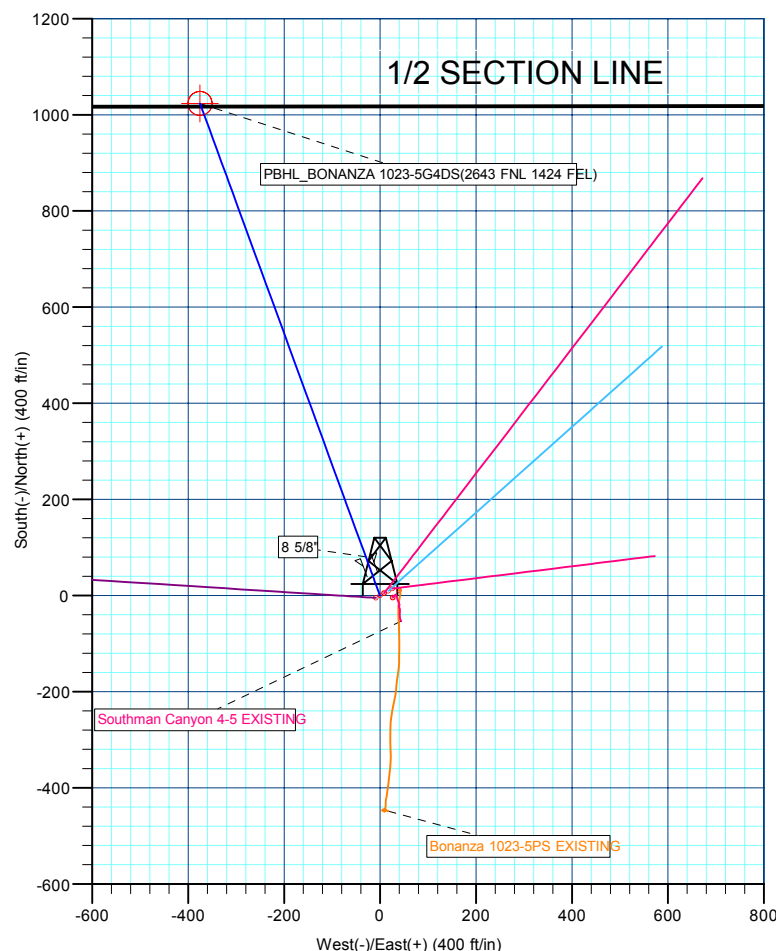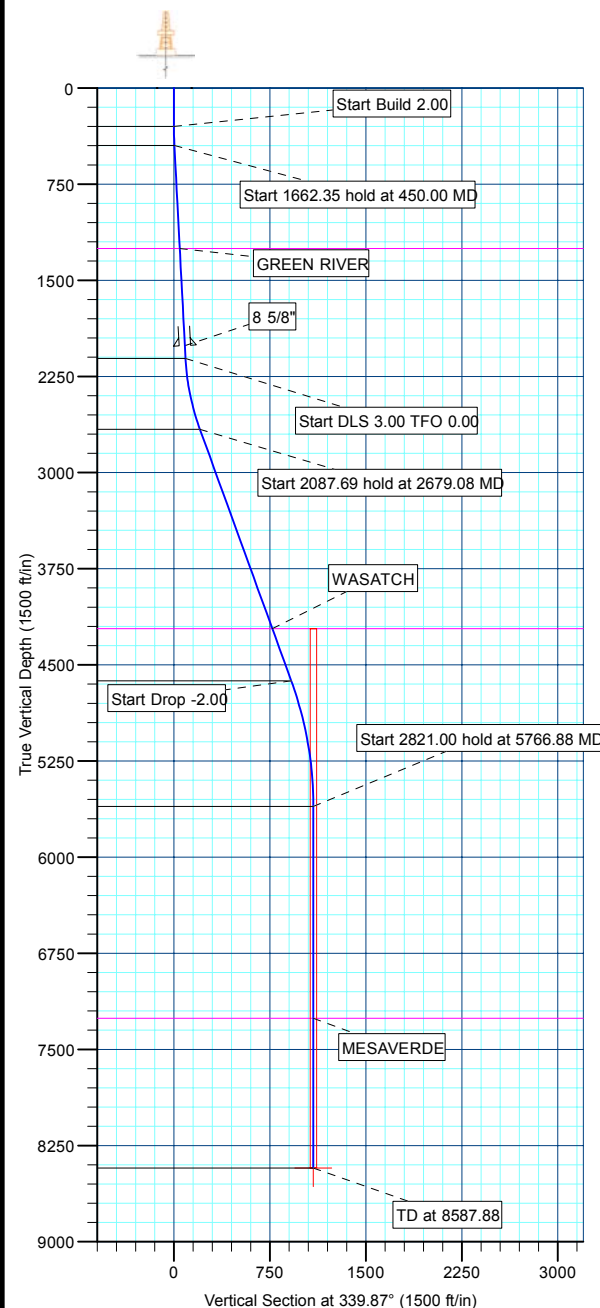

Plan: PLAN #1 4-28-10 RHS (BONANZA 1023-5G4DS/BONANZA 1023-5G4DS)

Created By: Robert H. Scott Date: 9:34, April 28 2010



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Company:	ANADARKO PETROLEUM CORP.	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Project:	UINTAH COUNTY, UTAH (nad 27)	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site:	Bonanza 1023-5I	North Reference:	True
Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Wellbore:	BONANZA 1023-5G4DS		
Design:	PLAN #1 4-28-10 RHS		

Project	UINTAH COUNTY, UTAH (nad 27),		
Map System:	Universal Transverse Mercator (US Survey Fee	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	Zone 12N (114 W to 108 W)		

Site	Bonanza 1023-5I, SECTION 5 T10S R23E			
Site Position:		Northing:	14,521,340.19 ft	Latitude: 39° 58' 30.914 N
From:	Lat/Long	Easting:	2,104,289.90 ft	Longitude: 109° 20' 39.455 W
Position Uncertainty:	0.00 ft	Slot Radius:	in	Grid Convergence: 1.06 °

Well	BONANZA 1023-5G4DS			
Well Position	+N/-S	-14.57 ft	Northing:	14,521,325.14 ft
	+E/-W	-26.06 ft	Easting:	2,104,264.12 ft
Position Uncertainty	0.00 ft	Wellhead Elevation:	ft	Ground Level: 5,302.00 ft

Wellbore	BONANZA 1023-5G4DS				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	BGGM2009	4/28/2010	11.17	65.93	52,463

Design	PLAN #1 4-28-10 RHS			
Audit Notes:				
Version:	Phase:	PLAN	Tie On Depth:	0.00
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)
	0.00	0.00	0.00	339.87

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00	
450.00	3.00	339.87	449.93	3.69	-1.35	2.00	2.00	0.00	339.87	
2,112.35	3.00	339.87	2,110.00	85.37	-31.29	0.00	0.00	0.00	0.00	
2,679.08	20.00	339.87	2,663.32	191.08	-70.03	3.00	3.00	0.00	0.00	
4,766.78	20.00	339.87	4,625.09	861.58	-315.75	0.00	0.00	0.00	0.00	
5,766.88	0.00	0.00	5,605.00	1,023.83	-375.21	2.00	-2.00	0.00	180.00	
8,587.88	0.00	0.00	8,426.00	1,023.83	-375.21	0.00	0.00	0.00	0.00	PBHL_BONANZA 1



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Company:	ANADARKO PETROLEUM CORP.	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Project:	UINTAH COUNTY, UTAH (nad 27)	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site:	Bonanza 1023-5I	North Reference:	True
Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Wellbore:	BONANZA 1023-5G4DS		
Design:	PLAN #1 4-28-10 RHS		

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
Start Build 2.00									
300.00	0.00	0.00	300.00	0.00	0.00	0.00	0.00	0.00	0.00
400.00	2.00	339.87	399.98	1.64	-0.60	1.75	2.00	2.00	0.00
Start 1662.35 hold at 450.00 MD									
450.00	3.00	339.87	449.93	3.69	-1.35	3.93	2.00	2.00	0.00
500.00	3.00	339.87	499.86	6.14	-2.25	6.54	0.00	0.00	0.00
600.00	3.00	339.87	599.73	11.06	-4.05	11.78	0.00	0.00	0.00
700.00	3.00	339.87	699.59	15.97	-5.85	17.01	0.00	0.00	0.00
800.00	3.00	339.87	799.45	20.88	-7.66	22.24	0.00	0.00	0.00
900.00	3.00	339.87	899.31	25.80	-9.46	27.48	0.00	0.00	0.00
1,000.00	3.00	339.87	999.18	30.71	-11.26	32.71	0.00	0.00	0.00
1,100.00	3.00	339.87	1,099.04	35.63	-13.06	37.94	0.00	0.00	0.00
1,200.00	3.00	339.87	1,198.90	40.54	-14.86	43.18	0.00	0.00	0.00
GREEN RIVER									
1,254.17	3.00	339.87	1,253.00	43.20	-15.84	46.01	0.00	0.00	0.00
1,300.00	3.00	339.87	1,298.77	45.45	-16.66	48.41	0.00	0.00	0.00
1,400.00	3.00	339.87	1,398.63	50.37	-18.46	53.65	0.00	0.00	0.00
1,500.00	3.00	339.87	1,498.49	55.28	-20.26	58.88	0.00	0.00	0.00
1,600.00	3.00	339.87	1,598.36	60.20	-22.06	64.11	0.00	0.00	0.00
1,700.00	3.00	339.87	1,698.22	65.11	-23.87	69.35	0.00	0.00	0.00
1,800.00	3.00	339.87	1,798.08	70.02	-25.67	74.58	0.00	0.00	0.00
1,900.00	3.00	339.87	1,897.94	74.94	-27.47	79.81	0.00	0.00	0.00
2,000.00	3.00	339.87	1,997.81	79.85	-29.27	85.05	0.00	0.00	0.00
8 5/8"									
2,012.21	3.00	339.87	2,010.00	80.45	-29.49	85.69	0.00	0.00	0.00
2,100.00	3.00	339.87	2,097.67	84.77	-31.07	90.28	0.00	0.00	0.00
Start DLS 3.00 TFO 0.00									
2,112.35	3.00	339.87	2,110.00	85.37	-31.29	90.93	0.00	0.00	0.00
2,200.00	5.63	339.87	2,197.40	91.56	-33.56	97.52	3.00	3.00	0.00
2,300.00	8.63	339.87	2,296.61	103.22	-37.83	109.93	3.00	3.00	0.00
2,400.00	11.63	339.87	2,395.04	119.73	-43.88	127.52	3.00	3.00	0.00
2,500.00	14.63	339.87	2,492.42	141.05	-51.70	150.23	3.00	3.00	0.00
2,600.00	17.63	339.87	2,588.47	167.13	-61.26	178.01	3.00	3.00	0.00
Start 2087.69 hold at 2679.08 MD									
2,679.08	20.00	339.87	2,663.32	191.08	-70.03	203.51	3.00	3.00	0.00
2,700.00	20.00	339.87	2,682.98	197.80	-72.49	210.67	0.00	0.00	0.00
2,800.00	20.00	339.87	2,776.94	229.92	-84.26	244.87	0.00	0.00	0.00
2,900.00	20.00	339.87	2,870.91	262.03	-96.03	279.08	0.00	0.00	0.00
3,000.00	20.00	339.87	2,964.88	294.15	-107.80	313.28	0.00	0.00	0.00
3,100.00	20.00	339.87	3,058.85	326.27	-119.57	347.49	0.00	0.00	0.00
3,200.00	20.00	339.87	3,152.82	358.38	-131.34	381.69	0.00	0.00	0.00
3,300.00	20.00	339.87	3,246.78	390.50	-143.11	415.90	0.00	0.00	0.00
3,400.00	20.00	339.87	3,340.75	422.62	-154.88	450.10	0.00	0.00	0.00
3,500.00	20.00	339.87	3,434.72	454.73	-166.65	484.31	0.00	0.00	0.00
3,600.00	20.00	339.87	3,528.69	486.85	-178.42	518.52	0.00	0.00	0.00
3,700.00	20.00	339.87	3,622.66	518.97	-190.19	552.72	0.00	0.00	0.00
3,800.00	20.00	339.87	3,716.62	551.08	-201.96	586.93	0.00	0.00	0.00
3,900.00	20.00	339.87	3,810.59	583.20	-213.73	621.13	0.00	0.00	0.00
4,000.00	20.00	339.87	3,904.56	615.32	-225.50	655.34	0.00	0.00	0.00
4,100.00	20.00	339.87	3,998.53	647.43	-237.27	689.54	0.00	0.00	0.00
4,200.00	20.00	339.87	4,092.50	679.55	-249.04	723.75	0.00	0.00	0.00
4,300.00	20.00	339.87	4,186.46	711.67	-260.81	757.95	0.00	0.00	0.00
WASATCH									



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Company:	ANADARKO PETROLEUM CORP.	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Project:	UINTAH COUNTY, UTAH (nad 27)	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site:	Bonanza 1023-5I	North Reference:	True
Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Wellbore:	BONANZA 1023-5G4DS		
Design:	PLAN #1 4-28-10 RHS		

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
4,333.56	20.00	339.87	4,218.00	722.45	-264.76	769.43	0.00	0.00	0.00
4,400.00	20.00	339.87	4,280.43	743.78	-272.58	792.16	0.00	0.00	0.00
4,500.00	20.00	339.87	4,374.40	775.90	-284.35	826.36	0.00	0.00	0.00
4,600.00	20.00	339.87	4,468.37	808.02	-296.12	860.57	0.00	0.00	0.00
4,700.00	20.00	339.87	4,562.34	840.13	-307.89	894.78	0.00	0.00	0.00
Start Drop -2.00									
4,766.78	20.00	339.87	4,625.09	861.58	-315.75	917.62	0.00	0.00	0.00
4,800.00	19.34	339.87	4,656.37	872.08	-319.60	928.80	2.00	-2.00	0.00
4,900.00	17.34	339.87	4,751.29	901.62	-330.42	960.26	2.00	-2.00	0.00
5,000.00	15.34	339.87	4,847.24	928.03	-340.10	988.39	2.00	-2.00	0.00
5,100.00	13.34	339.87	4,944.12	951.28	-348.62	1,013.15	2.00	-2.00	0.00
5,200.00	11.34	339.87	5,041.81	971.34	-355.97	1,034.52	2.00	-2.00	0.00
5,300.00	9.34	339.87	5,140.18	988.19	-362.15	1,052.46	2.00	-2.00	0.00
5,400.00	7.34	339.87	5,239.12	1,001.81	-367.14	1,066.96	2.00	-2.00	0.00
5,500.00	5.34	339.87	5,338.50	1,012.17	-370.94	1,078.00	2.00	-2.00	0.00
5,600.00	3.34	339.87	5,438.21	1,019.27	-373.54	1,085.56	2.00	-2.00	0.00
5,700.00	1.34	339.87	5,538.12	1,023.10	-374.94	1,089.64	2.00	-2.00	0.00
Start 2821.00 hold at 5766.88 MD									
5,766.88	0.00	0.00	5,605.00	1,023.83	-375.21	1,090.42	2.00	-2.00	0.00
5,800.00	0.00	0.00	5,638.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
5,900.00	0.00	0.00	5,738.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,000.00	0.00	0.00	5,838.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,100.00	0.00	0.00	5,938.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,200.00	0.00	0.00	6,038.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,300.00	0.00	0.00	6,138.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,400.00	0.00	0.00	6,238.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,500.00	0.00	0.00	6,338.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,600.00	0.00	0.00	6,438.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,700.00	0.00	0.00	6,538.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,800.00	0.00	0.00	6,638.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
6,900.00	0.00	0.00	6,738.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,000.00	0.00	0.00	6,838.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,100.00	0.00	0.00	6,938.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,200.00	0.00	0.00	7,038.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,300.00	0.00	0.00	7,138.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,400.00	0.00	0.00	7,238.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
MESAVERDE									
7,419.88	0.00	0.00	7,258.00	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,500.00	0.00	0.00	7,338.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,600.00	0.00	0.00	7,438.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,700.00	0.00	0.00	7,538.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,800.00	0.00	0.00	7,638.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
7,900.00	0.00	0.00	7,738.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
8,000.00	0.00	0.00	7,838.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
8,100.00	0.00	0.00	7,938.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
8,200.00	0.00	0.00	8,038.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
8,300.00	0.00	0.00	8,138.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
8,400.00	0.00	0.00	8,238.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
8,500.00	0.00	0.00	8,338.12	1,023.83	-375.21	1,090.42	0.00	0.00	0.00
TD at 8587.88 - PBHL_BONANZA 1023-5G4DS(2643 FNL 1424 FEL)									
8,587.88	0.00	0.00	8,426.00	1,023.83	-375.21	1,090.42	0.00	0.00	0.00



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Company:	ANADARKO PETROLEUM CORP.	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Project:	UINTAH COUNTY, UTAH (nad 27)	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site:	Bonanza 1023-5I	North Reference:	True
Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Wellbore:	BONANZA 1023-5G4DS		
Design:	PLAN #1 4-28-10 RHS		

Design Targets
Target Name

- hit/miss target	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (ft)	Easting (ft)	Latitude	Longitude
- Shape									
PBHL_BONANZA 1023-5I	0.00	0.00	8,426.00	1,023.83	-375.21	14,522,341.83	2,103,869.96	39° 58' 40.890 N	109° 20' 44.610 W
- plan hits target center									
- Circle (radius 25.00)									

Casing Points

Measured Depth (ft)	Vertical Depth (ft)	Name	Casing Diameter (in)	Hole Diameter (in)
2,012.21	2,010.00	8 5/8"	8.62	11.00

Formations

Measured Depth (ft)	Vertical Depth (ft)	Name	Lithology	Dip (°)	Dip Direction (°)
1,254.17	1,253.00	GREEN RIVER			
4,333.56	4,218.00	WASATCH			
7,419.88	7,258.00	MESAVERDE			

Plan Annotations

Measured Depth (ft)	Vertical Depth (ft)	Local Coordinates		Comment
		+N/-S (ft)	+E/-W (ft)	
300.00	300.00	0.00	0.00	Start Build 2.00
450.00	449.93	3.69	-1.35	Start 1662.35 hold at 450.00 MD
2,112.35	2,110.00	85.37	-31.29	Start DLS 3.00 TFO 0.00
2,679.08	2,663.32	191.08	-70.03	Start 2087.69 hold at 2679.08 MD
4,766.78	4,625.09	861.58	-315.75	Start Drop -2.00
5,766.88	5,605.00	1,023.83	-375.21	Start 2821.00 hold at 5766.88 MD
8,587.88	8,426.00	1,023.83	-375.21	TD at 8587.88



ANADARKO PETROLEUM CORP.

UINTAH COUNTY, UTAH (nad 27)

Bonanza 1023-5I

BONANZA 1023-5G4DS

BONANZA 1023-5G4DS

PLAN #1 4-28-10 RHS

Anticollision Report

28 April, 2010



Weatherford®



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Reference	PLAN #1 4-28-10 RHS		
Filter type:	NO GLOBAL FILTER: Using user defined selection & filtering criteria		
Interpolation Method:	Stations	Error Model:	ISCWSA
Depth Range:	0.00 to 20,000.00ft	Scan Method:	Closest Approach 3D
Results Limited by:	Maximum center-center distance of 10,000.00ft	Error Surface:	Elliptical Conic
Warning Levels Evaluated at:	2.00 Sigma		

Survey Tool Program	Date 4/28/2010			
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description
0.00	8,587.88	PLAN #1 4-28-10 RHS (BONANZA 1023-	MWD	MWD - Standard

Summary						
Site Name	Reference Measured Depth (ft)	Offset Measured Depth (ft)	Distance Between Centres (ft)	Distance Between Ellipses (ft)	Separation Factor	Warning
Offset Well - Wellbore - Design						
Bonanza 1023-5I						
BONANZA 1023-5I1BS - BONANZA 1023-5I1BS - PLAN	300.00	300.00	10.07	8.97	9.127	CC, ES
BONANZA 1023-5I1BS - BONANZA 1023-5I1BS - PLAN	400.00	399.65	11.42	9.87	7.371	SF
BONANZA 1023-5I1CS - BONANZA 1023-5I1CS - PLAN	300.00	300.00	19.96	18.86	18.090	CC, ES
BONANZA 1023-5I1CS - BONANZA 1023-5I1CS - PLAN	450.00	448.23	25.15	23.37	14.136	SF
BONANZA 1023-5I4BS - BONANZA 1023-5I4BS - PLAN	300.00	300.00	29.86	28.76	27.193	CC, ES
BONANZA 1023-5I4BS - BONANZA 1023-5I4BS - PLAN	450.00	447.43	35.13	33.36	19.916	SF
BONANZA 1023-5J3AS - BONANZA 1023-5J3AS - PLAN	300.00	300.00	9.89	8.79	8.965	CC, ES
BONANZA 1023-5J3AS - BONANZA 1023-5J3AS - PLAN	400.00	399.67	11.65	10.11	7.552	SF
Bonanza 1023-5PS EXISTING - Bonanza 1023-5PS EXI	0.00	9.00	41.27			
Bonanza 1023-5PS EXISTING - Bonanza 1023-5PS EXI	400.00	408.96	41.56	40.35	34.097	ES
Bonanza 1023-5PS EXISTING - Bonanza 1023-5PS EXI	1,900.00	1,906.28	96.29	88.62	12.562	SF
Southman Canyon 4-5 EXISTING - Southman Canyon 4-	241.84	227.84	26.48	25.62	30.609	CC
Southman Canyon 4-5 EXISTING - Southman Canyon 4-	300.00	285.92	26.57	25.47	24.029	ES
Southman Canyon 4-5 EXISTING - Southman Canyon 4-	2,112.35	2,096.12	104.93	95.40	11.013	SF

Offset Design Bonanza 1023-5I - BONANZA 1023-5I1BS - BONANZA 1023-5I1BS - PLAN #1 4-28-10 RHS												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth	Vertical Depth	Measured Depth	Vertical Depth	Reference	Offset	Highside Toolface	Offset Wellbore Centre		Between Centres	Between Ellipses	Minimum Separation	Separation Factor	Warning
Depth (ft)	Depth (ft)	Depth (ft)	Depth (ft)	(ft)	(ft)	(°)	+N/-S (ft)	+E/-W (ft)	(ft)	(ft)	(ft)		
0.00	0.00	0.00	0.00	0.00	0.00	59.59	5.10	8.69	10.07				
100.00	100.00	100.00	100.00	0.10	0.10	59.59	5.10	8.69	10.07	9.87	0.20	49.248	
200.00	200.00	200.00	200.00	0.33	0.33	59.59	5.10	8.69	10.07	9.42	0.65	15.401	
300.00	300.00	300.00	300.00	0.55	0.55	59.59	5.10	8.69	10.07	8.97	1.10	9.127 CC, ES	
400.00	399.98	399.65	399.63	0.78	0.78	85.02	6.47	9.74	11.42	9.87	1.55	7.371 SF	
450.00	449.93	449.42	449.35	0.90	0.89	90.06	8.19	11.06	13.22	11.44	1.78	7.435	
500.00	499.86	499.35	499.22	1.01	1.00	94.56	10.26	12.65	15.48	13.47	2.01	7.719	
600.00	599.73	599.22	598.95	1.24	1.23	100.45	14.40	15.84	20.19	17.72	2.46	8.196	
700.00	699.59	699.10	698.69	1.47	1.47	104.09	18.55	19.03	25.03	22.10	2.93	8.552	
800.00	799.45	798.97	798.42	1.71	1.70	106.55	22.69	22.21	29.94	26.54	3.39	8.821	
900.00	899.31	898.84	898.16	1.95	1.94	108.31	26.84	25.40	34.89	31.02	3.86	9.030	
1,000.00	999.18	998.71	997.89	2.19	2.18	109.63	30.98	28.58	39.86	35.53	4.33	9.196	
1,100.00	1,099.04	1,098.59	1,097.63	2.43	2.42	110.66	35.12	31.77	44.85	40.04	4.81	9.332	
1,200.00	1,198.90	1,198.46	1,197.37	2.67	2.66	111.48	39.27	34.95	49.85	44.57	5.28	9.443	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
1,300.00	1,298.77	1,298.33	1,297.10	2.91	2.90	112.15	43.41	38.14	54.86	49.11	5.75	9.537	
1,400.00	1,398.63	1,398.20	1,396.84	3.16	3.14	112.71	47.56	41.32	59.88	53.65	6.23	9.617	
1,500.00	1,498.49	1,498.08	1,496.57	3.40	3.38	113.19	51.70	44.51	64.90	58.20	6.70	9.686	
1,600.00	1,598.36	1,597.95	1,596.31	3.64	3.62	113.59	55.84	47.70	69.93	62.75	7.17	9.746	
1,700.00	1,698.22	1,697.82	1,696.04	3.88	3.86	113.94	59.99	50.88	74.95	67.30	7.65	9.798	
1,800.00	1,798.08	1,797.69	1,795.78	4.12	4.11	114.25	64.13	54.07	79.98	71.86	8.12	9.845	
1,900.00	1,897.94	1,897.57	1,895.52	4.36	4.35	114.52	68.28	57.25	85.02	76.42	8.60	9.886	
2,000.00	1,997.81	1,997.44	1,995.25	4.61	4.59	114.76	72.42	60.44	90.05	80.98	9.07	9.924	
2,100.00	2,097.67	2,097.18	2,094.86	4.85	4.83	114.97	76.56	63.62	95.09	85.54	9.55	9.958	
2,112.35	2,110.00	2,109.19	2,106.84	4.88	4.86	114.96	77.12	64.05	95.75	86.14	9.61	9.965	
2,200.00	2,197.40	2,194.20	2,191.55	5.10	5.08	114.68	82.73	68.37	102.48	92.44	10.04	10.210	
2,300.00	2,296.61	2,290.49	2,287.00	5.39	5.36	114.49	92.70	76.02	114.74	104.17	10.57	10.855	
2,400.00	2,395.04	2,385.72	2,380.67	5.72	5.68	114.39	106.29	86.47	131.83	120.68	11.16	11.817	
2,500.00	2,492.42	2,479.59	2,472.05	6.09	6.03	114.29	123.30	99.55	153.64	141.84	11.80	13.016	
2,600.00	2,588.47	2,571.83	2,560.71	6.52	6.43	114.16	143.45	115.04	180.04	167.51	12.53	14.374	
2,679.08	2,663.32	2,643.47	2,628.65	6.91	6.77	114.00	161.44	128.87	204.06	190.91	13.15	15.516	
2,700.00	2,682.98	2,662.41	2,646.47	7.02	6.87	114.12	166.53	132.78	210.83	197.49	13.33	15.814	
2,800.00	2,776.94	2,756.97	2,735.33	7.56	7.37	114.55	192.16	152.48	243.33	229.08	14.24	17.085	
2,900.00	2,870.91	2,851.53	2,824.19	8.13	7.90	114.89	217.80	172.19	275.83	260.65	15.19	18.163	
3,000.00	2,964.88	2,946.08	2,913.05	8.71	8.44	115.15	243.43	191.90	308.35	292.19	16.16	19.079	
3,100.00	3,058.85	3,040.64	3,001.90	9.30	8.99	115.36	269.07	211.60	340.87	323.71	17.16	19.861	
3,200.00	3,152.82	3,135.20	3,090.76	9.91	9.56	115.54	294.71	231.31	373.40	355.21	18.19	20.532	
3,300.00	3,246.78	3,229.76	3,179.62	10.52	10.13	115.68	320.34	251.02	405.92	386.70	19.23	21.112	
3,400.00	3,340.75	3,324.31	3,268.47	11.14	10.72	115.81	345.98	270.72	438.45	418.17	20.28	21.616	
3,500.00	3,434.72	3,418.87	3,357.33	11.77	11.31	115.92	371.61	290.43	470.98	449.63	21.35	22.057	
3,600.00	3,528.69	3,513.43	3,446.19	12.41	11.90	116.01	397.25	310.14	503.51	481.08	22.43	22.445	
3,700.00	3,622.66	3,607.99	3,535.04	13.05	12.50	116.09	422.89	329.84	536.05	512.52	23.52	22.788	
3,800.00	3,716.62	3,702.54	3,623.90	13.70	13.10	116.17	448.52	349.55	568.58	543.96	24.62	23.093	
3,900.00	3,810.59	3,797.10	3,712.76	14.34	13.71	116.23	474.16	369.26	601.11	575.39	25.73	23.365	
4,000.00	3,904.56	3,891.66	3,801.62	15.00	14.32	116.29	499.79	388.96	633.65	606.81	26.84	23.609	
4,100.00	3,998.53	3,986.22	3,890.47	15.65	14.93	116.34	525.43	408.67	666.18	638.23	27.96	23.828	
4,200.00	4,092.50	4,080.77	3,979.33	16.31	15.55	116.39	551.07	428.38	698.72	669.64	29.08	24.027	
4,300.00	4,186.46	4,175.33	4,068.19	16.97	16.17	116.44	576.70	448.08	731.26	701.05	30.21	24.207	
4,400.00	4,280.43	4,269.89	4,157.04	17.63	16.79	116.48	602.34	467.79	763.79	732.45	31.34	24.372	
4,500.00	4,374.40	4,364.45	4,245.90	18.29	17.41	116.51	627.97	487.49	796.33	763.86	32.47	24.522	
4,600.00	4,468.37	4,459.00	4,334.76	18.95	18.03	116.55	653.61	507.20	828.87	795.26	33.61	24.660	
4,700.00	4,562.34	4,553.56	4,423.62	19.62	18.65	116.58	679.25	526.91	861.40	826.65	34.75	24.787	
4,766.78	4,625.09	4,616.70	4,482.95	20.07	19.07	116.60	696.36	540.07	883.13	847.62	35.52	24.866	
4,800.00	4,656.37	4,648.15	4,512.50	20.26	19.28	116.80	704.89	546.62	893.86	857.96	35.90	24.898	
4,900.00	4,751.29	4,743.09	4,601.72	20.76	19.91	117.24	730.63	566.41	925.16	888.17	36.98	25.015	
5,000.00	4,847.24	4,855.87	4,708.40	21.22	20.51	117.51	759.63	588.70	954.10	916.08	38.02	25.096	
5,100.00	4,944.12	4,971.06	4,818.75	21.64	21.05	117.74	785.78	608.80	979.68	940.73	38.95	25.149	
5,200.00	5,041.81	5,087.96	4,932.01	22.01	21.53	117.94	808.71	626.43	1,001.81	962.00	39.81	25.165	
5,300.00	5,140.18	5,206.36	5,047.82	22.34	21.97	118.11	828.18	641.40	1,020.41	979.83	40.57	25.149	
5,400.00	5,239.12	5,326.01	5,165.79	22.63	22.34	118.26	843.98	653.54	1,035.41	994.17	41.24	25.108	
5,500.00	5,338.50	5,446.65	5,285.48	22.87	22.65	118.38	855.95	662.74	1,046.76	1,004.96	41.80	25.041	
5,600.00	5,438.21	5,568.00	5,406.40	23.07	22.90	118.47	863.95	668.89	1,054.42	1,012.15	42.26	24.950	
5,700.00	5,538.12	5,689.78	5,528.07	23.22	23.09	118.54	867.88	671.91	1,058.35	1,015.73	42.61	24.836	
5,766.88	5,605.00	5,766.71	5,605.00	23.29	23.18	98.45	868.32	672.25	1,058.94	1,016.15	42.79	24.749	
5,800.00	5,638.12	5,799.83	5,638.12	23.33	23.21	98.45	868.32	672.25	1,058.94	1,016.08	42.86	24.705	
5,900.00	5,738.12	5,899.83	5,738.12	23.44	23.32	98.45	868.32	672.25	1,058.94	1,015.84	43.10	24.567	
6,000.00	5,838.12	5,999.83	5,838.12	23.55	23.44	98.45	868.32	672.25	1,058.94	1,015.59	43.35	24.429	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
6,100.00	5,938.12	6,099.83	5,938.12	23.67	23.55	98.45	868.32	672.25	1,058.94	1,015.35	43.59	24.291	
6,200.00	6,038.12	6,199.83	6,038.12	23.79	23.67	98.45	868.32	672.25	1,058.94	1,015.10	43.84	24.152	
6,300.00	6,138.12	6,299.83	6,138.12	23.90	23.79	98.45	868.32	672.25	1,058.94	1,014.84	44.10	24.013	
6,400.00	6,238.12	6,399.83	6,238.12	24.02	23.91	98.45	868.32	672.25	1,058.94	1,014.59	44.35	23.875	
6,500.00	6,338.12	6,499.83	6,338.12	24.15	24.03	98.45	868.32	672.25	1,058.94	1,014.33	44.61	23.736	
6,600.00	6,438.12	6,599.83	6,438.12	24.27	24.15	98.45	868.32	672.25	1,058.94	1,014.06	44.88	23.597	
6,700.00	6,538.12	6,699.83	6,538.12	24.39	24.28	98.45	868.32	672.25	1,058.94	1,013.80	45.14	23.458	
6,800.00	6,638.12	6,799.83	6,638.12	24.52	24.41	98.45	868.32	672.25	1,058.94	1,013.53	45.41	23.319	
6,900.00	6,738.12	6,899.83	6,738.12	24.65	24.53	98.45	868.32	672.25	1,058.94	1,013.26	45.68	23.181	
7,000.00	6,838.12	6,999.83	6,838.12	24.78	24.66	98.45	868.32	672.25	1,058.94	1,012.98	45.96	23.043	
7,100.00	6,938.12	7,099.83	6,938.12	24.91	24.79	98.45	868.32	672.25	1,058.94	1,012.71	46.23	22.905	
7,200.00	7,038.12	7,199.83	7,038.12	25.04	24.92	98.45	868.32	672.25	1,058.94	1,012.43	46.51	22.767	
7,300.00	7,138.12	7,299.83	7,138.12	25.17	25.06	98.45	868.32	672.25	1,058.94	1,012.15	46.79	22.630	
7,400.00	7,238.12	7,399.83	7,238.12	25.31	25.19	98.45	868.32	672.25	1,058.94	1,011.86	47.08	22.493	
7,500.00	7,338.12	7,499.83	7,338.12	25.44	25.33	98.45	868.32	672.25	1,058.94	1,011.57	47.37	22.356	
7,600.00	7,438.12	7,599.83	7,438.12	25.58	25.46	98.45	868.32	672.25	1,058.94	1,011.28	47.66	22.220	
7,700.00	7,538.12	7,699.83	7,538.12	25.72	25.60	98.45	868.32	672.25	1,058.94	1,010.99	47.95	22.085	
7,800.00	7,638.12	7,799.83	7,638.12	25.86	25.74	98.45	868.32	672.25	1,058.94	1,010.70	48.24	21.950	
7,900.00	7,738.12	7,899.83	7,738.12	26.00	25.88	98.45	868.32	672.25	1,058.94	1,010.40	48.54	21.816	
8,000.00	7,838.12	7,999.83	7,838.12	26.14	26.02	98.45	868.32	672.25	1,058.94	1,010.10	48.84	21.682	
8,100.00	7,938.12	8,099.83	7,938.12	26.28	26.17	98.45	868.32	672.25	1,058.94	1,009.80	49.14	21.549	
8,200.00	8,038.12	8,199.83	8,038.12	26.43	26.31	98.45	868.32	672.25	1,058.94	1,009.49	49.45	21.416	
8,300.00	8,138.12	8,299.83	8,138.12	26.57	26.46	98.45	868.32	672.25	1,058.94	1,009.19	49.75	21.285	
8,400.00	8,238.12	8,399.83	8,238.12	26.72	26.60	98.45	868.32	672.25	1,058.94	1,008.88	50.06	21.154	
8,500.00	8,338.12	8,499.83	8,338.12	26.86	26.75	98.45	868.32	672.25	1,058.94	1,008.57	50.37	21.023	
8,527.84	8,365.96	8,527.67	8,365.96	26.91	26.79	98.45	868.32	672.25	1,058.94	1,008.48	50.46	20.987	
8,587.88	8,426.00	8,542.71	8,381.00	26.99	26.81	98.45	868.32	672.25	1,059.90	1,009.32	50.57	20.957	



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design Bonanza 1023-5I - BONANZA 1023-5I1CS - BONANZA 1023-5I1CS - PLAN #1 4-28-10 RHS												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
0.00	0.00	0.00	0.00	0.00	0.00	60.49	9.83	17.37	19.96				
100.00	100.00	100.00	100.00	0.10	0.10	60.49	9.83	17.37	19.96	19.76	0.20	97.607	
200.00	200.00	200.00	200.00	0.33	0.33	60.49	9.83	17.37	19.96	19.31	0.65	30.523	
300.00	300.00	300.00	300.00	0.55	0.55	60.49	9.83	17.37	19.96	18.86	1.10	18.090 CC, ES	
400.00	399.98	398.91	398.87	0.78	0.77	83.57	11.54	19.29	22.24	20.69	1.55	14.359	
450.00	449.93	448.23	448.08	0.90	0.89	86.49	13.66	21.67	25.15	23.37	1.78	14.136 SF	
500.00	499.86	497.38	497.03	1.01	1.01	88.81	16.61	24.98	29.31	27.30	2.01	14.571	
600.00	599.73	594.99	593.82	1.24	1.27	89.79	24.96	34.35	41.27	38.77	2.49	16.564	
700.00	699.59	691.27	688.54	1.47	1.59	88.48	36.41	47.19	57.91	54.93	2.98	19.406	
800.00	799.45	785.75	780.53	1.71	1.98	86.58	50.71	63.24	79.21	75.72	3.49	22.715	
900.00	899.31	878.05	869.27	1.95	2.44	84.73	67.59	82.18	105.11	101.11	4.00	26.295	
1,000.00	999.18	967.92	954.39	2.19	2.95	83.10	86.75	103.68	135.49	130.98	4.51	30.017	
1,100.00	1,099.04	1,062.42	1,043.19	2.43	3.55	81.82	108.25	127.81	168.04	163.00	5.03	33.393	
1,200.00	1,198.90	1,156.92	1,131.99	2.67	4.16	80.95	129.75	151.93	200.64	195.09	5.54	36.197	
1,300.00	1,298.77	1,251.42	1,220.80	2.91	4.79	80.33	151.25	176.06	233.26	227.20	6.06	38.493	
1,400.00	1,398.63	1,345.92	1,309.60	3.16	5.42	79.86	172.75	200.18	265.91	259.33	6.58	40.397	
1,500.00	1,498.49	1,440.42	1,398.40	3.40	6.06	79.49	194.25	224.31	298.57	291.46	7.11	41.999	
1,600.00	1,598.36	1,534.92	1,487.21	3.64	6.69	79.19	215.75	248.43	331.24	323.60	7.64	43.365	
1,700.00	1,698.22	1,629.42	1,576.01	3.88	7.34	78.95	237.25	272.56	363.92	355.74	8.17	44.540	
1,800.00	1,798.08	1,723.92	1,664.81	4.12	7.98	78.75	258.75	296.68	396.60	387.89	8.70	45.562	
1,900.00	1,897.94	1,818.42	1,753.62	4.36	8.62	78.57	280.25	320.81	429.28	420.04	9.24	46.458	
2,000.00	1,997.81	1,912.92	1,842.42	4.61	9.27	78.43	301.75	344.93	461.97	452.19	9.78	47.249	
2,100.00	2,097.67	2,007.43	1,931.23	4.85	9.91	78.30	323.26	369.06	494.66	484.34	10.32	47.952	
2,112.35	2,110.00	2,019.09	1,942.19	4.88	9.99	78.28	325.91	372.04	498.69	488.31	10.38	48.033	
2,200.00	2,197.40	2,102.05	2,020.15	5.10	10.56	77.53	344.78	393.22	526.95	516.10	10.86	48.543	
2,300.00	2,296.61	2,196.85	2,109.23	5.39	11.21	77.22	366.35	417.42	558.22	546.77	11.45	48.763	
2,400.00	2,395.04	2,292.42	2,199.04	5.72	11.86	77.40	388.09	441.81	588.50	576.40	12.10	48.636	
2,500.00	2,492.42	2,407.99	2,308.38	6.09	12.47	78.38	413.00	469.76	616.23	603.38	12.85	47.948	
2,600.00	2,588.47	2,524.53	2,419.90	6.52	13.03	79.96	435.50	495.00	640.20	626.51	13.69	46.764	
2,679.08	2,663.32	2,616.80	2,509.00	6.91	13.45	81.60	451.43	512.88	656.79	642.37	14.43	45.526	
2,700.00	2,682.98	2,641.19	2,532.66	7.02	13.55	82.20	455.36	517.29	660.89	646.25	14.63	45.158	
2,800.00	2,776.94	2,758.30	2,646.86	7.56	14.01	85.04	472.59	536.63	679.21	663.55	15.66	43.372	
2,900.00	2,870.91	2,876.02	2,762.52	8.13	14.42	87.84	487.17	552.99	695.46	678.74	16.72	41.598	
3,000.00	2,964.88	2,994.04	2,879.19	8.71	14.78	90.64	499.00	566.26	709.70	691.90	17.80	39.879	
3,100.00	3,058.85	3,112.07	2,996.43	9.30	15.07	93.46	508.02	576.38	722.00	703.13	18.88	38.249	
3,200.00	3,152.82	3,229.79	3,113.77	9.91	15.30	96.32	514.22	583.33	732.51	712.57	19.95	36.724	
3,300.00	3,246.78	3,346.90	3,230.77	10.52	15.48	99.23	517.59	587.12	741.38	720.39	20.99	35.314	
3,400.00	3,340.75	3,456.89	3,340.75	11.14	15.60	102.04	518.30	587.91	748.93	726.94	21.99	34.057	
3,500.00	3,434.72	3,550.86	3,434.72	11.77	15.69	104.43	518.30	587.91	757.23	734.32	22.91	33.050	
3,600.00	3,528.69	3,644.83	3,528.69	12.41	15.78	106.77	518.30	587.91	766.98	743.16	23.81	32.207	
3,700.00	3,622.66	3,738.80	3,622.66	13.05	15.87	109.05	518.30	587.91	778.10	753.41	24.69	31.512	
3,800.00	3,716.62	3,832.76	3,716.62	13.70	15.97	111.27	518.30	587.91	790.55	765.01	25.54	30.949	
3,900.00	3,810.59	3,926.73	3,810.59	14.34	16.07	113.43	518.30	587.91	804.27	777.90	26.37	30.502	
4,000.00	3,904.56	4,020.70	3,904.56	15.00	16.17	115.52	518.30	587.91	819.18	792.01	27.16	30.158	
4,100.00	3,998.53	4,114.67	3,998.53	15.65	16.28	117.53	518.30	587.91	835.23	807.30	27.93	29.906	
4,200.00	4,092.50	4,208.64	4,092.50	16.31	16.38	119.48	518.30	587.91	852.34	823.68	28.67	29.734	
4,300.00	4,186.46	4,302.60	4,186.46	16.97	16.49	121.36	518.30	587.91	870.47	841.10	29.37	29.634	
4,400.00	4,280.43	4,396.57	4,280.43	17.63	16.60	123.16	518.30	587.91	889.54	859.49	30.06	29.597	
4,500.00	4,374.40	4,490.54	4,374.40	18.29	16.71	124.89	518.30	587.91	909.51	878.79	30.71	29.614	
4,600.00	4,468.37	4,584.51	4,468.37	18.95	16.83	126.55	518.30	587.91	930.30	898.95	31.34	29.681	
4,700.00	4,562.34	4,678.48	4,562.34	19.62	16.94	128.15	518.30	587.91	951.86	919.91	31.95	29.790	
4,766.78	4,625.09	4,741.22	4,625.09	20.07	17.02	129.17	518.30	587.91	966.67	934.32	32.35	29.883	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design Bonanza 1023-5I - BONANZA 1023-5I1CS - BONANZA 1023-5I1CS - PLAN #1 4-28-10 RHS												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
4,800.00	4,656.37	4,772.51	4,656.37	20.26	17.06	129.78	518.30	587.91	974.03	941.47	32.56	29.918	
4,900.00	4,751.29	4,867.43	4,751.29	20.76	17.18	131.46	518.30	587.91	995.12	962.01	33.11	30.054	
5,000.00	4,847.24	4,963.38	4,847.24	21.22	17.30	132.91	518.30	587.91	1,014.44	980.81	33.63	30.167	
5,100.00	4,944.12	5,060.26	4,944.12	21.64	17.43	134.16	518.30	587.91	1,031.78	997.67	34.11	30.251	
5,200.00	5,041.81	5,157.95	5,041.81	22.01	17.56	135.20	518.30	587.91	1,046.98	1,012.43	34.55	30.303	
5,300.00	5,140.18	5,256.32	5,140.18	22.34	17.69	136.06	518.30	587.91	1,059.91	1,024.95	34.96	30.319	
5,400.00	5,239.12	5,355.26	5,239.12	22.63	17.83	136.74	518.30	587.91	1,070.47	1,035.13	35.33	30.296	
5,500.00	5,338.50	5,454.64	5,338.50	22.87	17.96	137.25	518.30	587.91	1,078.56	1,042.89	35.67	30.234	
5,600.00	5,438.21	5,554.35	5,438.21	23.07	18.10	137.60	518.30	587.91	1,084.14	1,048.16	35.98	30.131	
5,700.00	5,538.12	5,654.26	5,538.12	23.22	18.24	137.79	518.30	587.91	1,087.16	1,050.90	36.26	29.985	
5,766.88	5,605.00	5,721.14	5,605.00	23.29	18.34	117.69	518.30	587.91	1,087.74	1,051.31	36.42	29.864	
5,800.00	5,638.12	5,754.26	5,638.12	23.33	18.39	117.69	518.30	587.91	1,087.74	1,051.22	36.51	29.789	
5,900.00	5,738.12	5,854.26	5,738.12	23.44	18.53	117.69	518.30	587.91	1,087.74	1,050.94	36.80	29.558	
6,000.00	5,838.12	5,954.26	5,838.12	23.55	18.68	117.69	518.30	587.91	1,087.74	1,050.65	37.09	29.327	
6,100.00	5,938.12	6,054.26	5,938.12	23.67	18.83	117.69	518.30	587.91	1,087.74	1,050.35	37.38	29.098	
6,200.00	6,038.12	6,154.26	6,038.12	23.79	18.98	117.69	518.30	587.91	1,087.74	1,050.06	37.68	28.870	
6,300.00	6,138.12	6,254.26	6,138.12	23.90	19.13	117.69	518.30	587.91	1,087.74	1,049.76	37.98	28.643	
6,400.00	6,238.12	6,354.26	6,238.12	24.02	19.28	117.69	518.30	587.91	1,087.74	1,049.46	38.28	28.417	
6,500.00	6,338.12	6,454.26	6,338.12	24.15	19.43	117.69	518.30	587.91	1,087.74	1,049.15	38.58	28.193	
6,600.00	6,438.12	6,554.26	6,438.12	24.27	19.59	117.69	518.30	587.91	1,087.74	1,048.85	38.89	27.970	
6,700.00	6,538.12	6,654.26	6,538.12	24.39	19.74	117.69	518.30	587.91	1,087.74	1,048.54	39.20	27.749	
6,800.00	6,638.12	6,754.26	6,638.12	24.52	19.90	117.69	518.30	587.91	1,087.74	1,048.22	39.51	27.530	
6,900.00	6,738.12	6,854.26	6,738.12	24.65	20.06	117.69	518.30	587.91	1,087.74	1,047.91	39.83	27.312	
7,000.00	6,838.12	6,954.26	6,838.12	24.78	20.22	117.69	518.30	587.91	1,087.74	1,047.59	40.14	27.096	
7,100.00	6,938.12	7,054.26	6,938.12	24.91	20.38	117.69	518.30	587.91	1,087.74	1,047.27	40.46	26.881	
7,200.00	7,038.12	7,154.26	7,038.12	25.04	20.54	117.69	518.30	587.91	1,087.74	1,046.95	40.79	26.669	
7,300.00	7,138.12	7,254.26	7,138.12	25.17	20.71	117.69	518.30	587.91	1,087.74	1,046.62	41.11	26.458	
7,400.00	7,238.12	7,354.26	7,238.12	25.31	20.87	117.69	518.30	587.91	1,087.74	1,046.30	41.44	26.249	
7,500.00	7,338.12	7,454.26	7,338.12	25.44	21.04	117.69	518.30	587.91	1,087.74	1,045.97	41.77	26.042	
7,600.00	7,438.12	7,554.26	7,438.12	25.58	21.21	117.69	518.30	587.91	1,087.74	1,045.64	42.10	25.837	
7,700.00	7,538.12	7,654.26	7,538.12	25.72	21.37	117.69	518.30	587.91	1,087.74	1,045.30	42.43	25.633	
7,800.00	7,638.12	7,754.26	7,638.12	25.86	21.54	117.69	518.30	587.91	1,087.74	1,044.97	42.77	25.432	
7,900.00	7,738.12	7,854.26	7,738.12	26.00	21.71	117.69	518.30	587.91	1,087.74	1,044.63	43.11	25.232	
8,000.00	7,838.12	7,954.26	7,838.12	26.14	21.89	117.69	518.30	587.91	1,087.74	1,044.29	43.45	25.035	
8,100.00	7,938.12	8,054.26	7,938.12	26.28	22.06	117.69	518.30	587.91	1,087.74	1,043.94	43.79	24.839	
8,200.00	8,038.12	8,154.26	8,038.12	26.43	22.23	117.69	518.30	587.91	1,087.74	1,043.60	44.13	24.646	
8,300.00	8,138.12	8,254.26	8,138.12	26.57	22.40	117.69	518.30	587.91	1,087.74	1,043.25	44.48	24.454	
8,400.00	8,238.12	8,354.26	8,238.12	26.72	22.58	117.69	518.30	587.91	1,087.74	1,042.91	44.83	24.264	
8,500.00	8,338.12	8,454.26	8,338.12	26.86	22.75	117.69	518.30	587.91	1,087.74	1,042.56	45.18	24.077	
8,507.10	8,345.22	8,461.36	8,345.22	26.87	22.77	117.69	518.30	587.91	1,087.74	1,042.53	45.20	24.063	
8,587.88	8,426.00	8,486.14	8,370.00	26.99	22.81	117.69	518.30	587.91	1,089.18	1,043.79	45.39	23.998	



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design Bonanza 1023-5I - BONANZA 1023-5I4BS - BONANZA 1023-5I4BS - PLAN #1 4-28-10 RHS												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
0.00	0.00	0.00	0.00	0.00	0.00	60.79	14.57	26.06	29.86				
100.00	100.00	100.00	100.00	0.10	0.10	60.79	14.57	26.06	29.86	29.66	0.20	150.097	
200.00	200.00	200.00	200.00	0.33	0.32	60.79	14.57	26.06	29.86	29.21	0.65	46.044	
300.00	300.00	300.00	300.00	0.55	0.55	60.79	14.57	26.06	29.86	28.76	1.10	27.193 CC, ES	
400.00	399.98	398.45	398.40	0.78	0.76	85.62	14.88	28.58	32.08	30.55	1.54	20.880	
450.00	449.93	447.43	447.28	0.90	0.87	90.59	15.27	31.71	35.13	33.36	1.76	19.916 SF	
500.00	499.86	496.17	495.82	1.01	0.99	95.66	15.81	36.05	39.71	37.72	1.99	19.918	
600.00	599.73	592.73	591.58	1.24	1.25	102.83	17.32	48.28	53.33	50.87	2.47	21.626	
700.00	699.59	687.69	685.03	1.47	1.57	106.75	19.39	64.98	72.39	69.45	2.95	24.575	
800.00	799.45	780.64	775.58	1.71	1.96	108.71	21.97	85.76	96.43	93.00	3.43	28.100	
900.00	899.31	874.22	865.79	1.95	2.42	109.68	25.03	110.48	124.53	120.60	3.93	31.703	
1,000.00	999.18	970.02	957.99	2.19	2.92	110.28	28.23	136.27	153.19	148.78	4.41	34.764	
1,100.00	1,099.04	1,065.82	1,050.20	2.43	3.44	110.69	31.43	162.06	181.86	176.96	4.89	37.173	
1,200.00	1,198.90	1,161.61	1,142.40	2.67	3.96	110.99	34.63	187.86	210.53	205.14	5.38	39.099	
1,300.00	1,298.77	1,257.41	1,234.60	2.91	4.50	111.22	37.83	213.65	239.21	233.32	5.88	40.665	
1,400.00	1,398.63	1,353.20	1,326.80	3.16	5.03	111.40	41.03	239.45	267.89	261.50	6.38	41.964	
1,500.00	1,498.49	1,449.00	1,419.01	3.40	5.57	111.54	44.22	265.24	296.57	289.68	6.89	43.056	
1,600.00	1,598.36	1,544.80	1,511.21	3.64	6.11	111.66	47.42	291.03	325.25	317.86	7.39	43.983	
1,700.00	1,698.22	1,640.59	1,603.41	3.88	6.65	111.76	50.62	316.83	353.94	346.03	7.90	44.781	
1,800.00	1,798.08	1,736.39	1,695.61	4.12	7.19	111.85	53.82	342.62	382.62	374.21	8.41	45.474	
1,900.00	1,897.94	1,832.18	1,787.82	4.36	7.74	111.92	57.02	368.42	411.31	402.38	8.93	46.081	
2,000.00	1,997.81	1,927.98	1,880.02	4.61	8.28	111.98	60.21	394.21	439.99	430.56	9.44	46.617	
2,100.00	2,097.67	2,023.78	1,972.22	4.85	8.83	112.04	63.41	420.00	468.68	458.73	9.95	47.093	
2,112.35	2,110.00	2,035.60	1,983.60	4.88	8.89	112.05	63.81	423.19	472.22	462.21	10.02	47.148	
2,200.00	2,197.40	2,119.32	2,064.18	5.10	9.37	111.56	66.60	445.73	498.09	487.64	10.45	47.679	
2,300.00	2,296.61	2,228.50	2,169.60	5.39	9.90	111.61	70.10	473.92	528.32	517.34	10.98	48.117	
2,400.00	2,395.04	2,341.90	2,280.01	5.72	10.34	112.30	73.27	499.53	557.40	545.87	11.53	48.337	
2,500.00	2,492.42	2,455.85	2,391.80	6.09	10.74	113.52	75.99	521.44	585.53	573.41	12.11	48.333	
2,600.00	2,588.47	2,569.90	2,504.39	6.52	11.09	115.21	78.23	539.48	613.08	600.35	12.73	48.162	
2,679.08	2,663.32	2,659.85	2,593.58	6.91	11.33	116.81	79.65	550.96	634.76	621.52	13.24	47.956	
2,700.00	2,682.98	2,683.62	2,617.20	7.02	11.39	117.42	79.97	553.59	640.46	627.07	13.39	47.823	
2,800.00	2,776.94	2,798.14	2,731.25	7.56	11.64	120.25	81.25	563.86	666.52	652.38	14.14	47.127	
2,900.00	2,870.91	2,913.93	2,846.86	8.13	11.83	123.00	82.03	570.21	690.55	675.66	14.89	46.371	
3,000.00	2,964.88	3,030.71	2,963.61	8.71	11.98	125.69	82.32	572.50	712.52	696.90	15.63	45.595	
3,100.00	3,058.85	3,125.95	3,058.85	9.30	12.09	127.80	82.32	572.51	733.82	717.50	16.31	44.985	
3,200.00	3,152.82	3,219.91	3,152.82	9.91	12.20	129.78	82.32	572.51	756.05	739.06	16.99	44.500	
3,300.00	3,246.78	3,313.88	3,246.78	10.52	12.31	131.65	82.32	572.51	779.16	761.50	17.66	44.130	
3,400.00	3,340.75	3,407.85	3,340.75	11.14	12.42	133.42	82.32	572.51	803.06	784.75	18.31	43.858	
3,500.00	3,434.72	3,501.82	3,434.72	11.77	12.54	135.09	82.32	572.51	827.68	808.73	18.95	43.673	
3,600.00	3,528.69	3,595.79	3,528.69	12.41	12.66	136.66	82.32	572.51	852.96	833.38	19.58	43.562	
3,700.00	3,622.66	3,689.75	3,622.66	13.05	12.78	138.15	82.32	572.51	878.85	858.65	20.20	43.516	
3,800.00	3,716.62	3,783.72	3,716.62	13.70	12.90	139.56	82.32	572.51	905.29	884.49	20.80	43.524	
3,900.00	3,810.59	3,877.69	3,810.59	14.34	13.03	140.89	82.32	572.51	932.23	910.84	21.39	43.579	
4,000.00	3,904.56	3,971.66	3,904.56	15.00	13.16	142.15	82.32	572.51	959.64	937.66	21.97	43.673	
4,100.00	3,998.53	4,065.63	3,998.53	15.65	13.29	143.34	82.32	572.51	987.47	964.92	22.54	43.800	
4,200.00	4,092.50	4,159.59	4,092.50	16.31	13.42	144.47	82.32	572.51	1,015.69	992.58	23.11	43.956	
4,300.00	4,186.46	4,253.56	4,186.46	16.97	13.56	145.54	82.32	572.51	1,044.27	1,020.61	23.66	44.135	
4,400.00	4,280.43	4,347.53	4,280.43	17.63	13.69	146.56	82.32	572.51	1,073.18	1,048.97	24.21	44.333	
4,500.00	4,374.40	4,441.50	4,374.40	18.29	13.83	147.52	82.32	572.51	1,102.39	1,077.64	24.75	44.546	
4,600.00	4,468.37	4,535.47	4,468.37	18.95	13.97	148.44	82.32	572.51	1,131.88	1,106.60	25.28	44.773	
4,700.00	4,562.34	4,629.43	4,562.34	19.62	14.11	149.31	82.32	572.51	1,161.63	1,135.82	25.81	45.010	
4,766.78	4,625.09	4,692.18	4,625.09	20.07	14.21	149.86	82.32	572.51	1,181.63	1,155.47	26.16	45.173	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design Bonanza 1023-5I - BONANZA 1023-5I4BS - BONANZA 1023-5I4BS - PLAN #1 4-28-10 RHS												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
4,800.00	4,656.37	4,723.47	4,656.37	20.26	14.26	150.23	82.32	572.51	1,191.46	1,165.09	26.37	45.189	
4,900.00	4,751.29	4,818.38	4,751.29	20.76	14.40	151.24	82.32	572.51	1,219.24	1,192.29	26.94	45.254	
5,000.00	4,847.24	4,914.34	4,847.24	21.22	14.55	152.10	82.32	572.51	1,244.22	1,216.73	27.49	45.261	
5,100.00	4,944.12	5,011.22	4,944.12	21.64	14.71	152.83	82.32	572.51	1,266.32	1,238.31	28.01	45.213	
5,200.00	5,041.81	5,108.91	5,041.81	22.01	14.86	153.43	82.32	572.51	1,285.47	1,256.98	28.49	45.115	
5,300.00	5,140.18	5,207.28	5,140.18	22.34	15.02	153.93	82.32	572.51	1,301.61	1,272.66	28.94	44.968	
5,400.00	5,239.12	5,306.22	5,239.12	22.63	15.18	154.32	82.32	572.51	1,314.68	1,285.32	29.36	44.775	
5,500.00	5,338.50	5,405.60	5,338.50	22.87	15.35	154.61	82.32	572.51	1,324.65	1,294.91	29.74	44.535	
5,600.00	5,438.21	5,505.31	5,438.21	23.07	15.51	154.81	82.32	572.51	1,331.49	1,301.40	30.09	44.250	
5,700.00	5,538.12	5,605.22	5,538.12	23.22	15.68	154.92	82.32	572.51	1,335.19	1,304.79	30.40	43.921	
5,766.88	5,605.00	5,672.10	5,605.00	23.29	15.79	134.81	82.32	572.51	1,335.89	1,305.31	30.59	43.675	
5,800.00	5,638.12	5,705.22	5,638.12	23.33	15.85	134.81	82.32	572.51	1,335.89	1,305.20	30.70	43.519	
5,900.00	5,738.12	5,805.22	5,738.12	23.44	16.02	134.81	82.32	572.51	1,335.89	1,304.86	31.04	43.039	
6,000.00	5,838.12	5,905.22	5,838.12	23.55	16.19	134.81	82.32	572.51	1,335.89	1,304.51	31.38	42.565	
6,100.00	5,938.12	6,005.22	5,938.12	23.67	16.36	134.81	82.32	572.51	1,335.89	1,304.16	31.73	42.098	
6,200.00	6,038.12	6,105.22	6,038.12	23.79	16.54	134.81	82.32	572.51	1,335.89	1,303.81	32.08	41.638	
6,300.00	6,138.12	6,205.22	6,138.12	23.90	16.71	134.81	82.32	572.51	1,335.89	1,303.46	32.44	41.185	
6,400.00	6,238.12	6,305.22	6,238.12	24.02	16.89	134.81	82.32	572.51	1,335.89	1,303.10	32.79	40.739	
6,500.00	6,338.12	6,405.22	6,338.12	24.15	17.07	134.81	82.32	572.51	1,335.89	1,302.75	33.15	40.299	
6,600.00	6,438.12	6,505.22	6,438.12	24.27	17.25	134.81	82.32	572.51	1,335.89	1,302.39	33.51	39.867	
6,700.00	6,538.12	6,605.22	6,538.12	24.39	17.43	134.81	82.32	572.51	1,335.89	1,302.02	33.87	39.441	
6,800.00	6,638.12	6,705.22	6,638.12	24.52	17.61	134.81	82.32	572.51	1,335.89	1,301.66	34.23	39.022	
6,900.00	6,738.12	6,805.22	6,738.12	24.65	17.79	134.81	82.32	572.51	1,335.89	1,301.29	34.60	38.609	
7,000.00	6,838.12	6,905.22	6,838.12	24.78	17.97	134.81	82.32	572.51	1,335.89	1,300.93	34.97	38.203	
7,100.00	6,938.12	7,005.22	6,938.12	24.91	18.16	134.81	82.32	572.51	1,335.89	1,300.56	35.34	37.803	
7,200.00	7,038.12	7,105.22	7,038.12	25.04	18.34	134.81	82.32	572.51	1,335.89	1,300.19	35.71	37.410	
7,300.00	7,138.12	7,205.22	7,138.12	25.17	18.53	134.81	82.32	572.51	1,335.89	1,299.81	36.08	37.023	
7,400.00	7,238.12	7,305.22	7,238.12	25.31	18.71	134.81	82.32	572.51	1,335.89	1,299.44	36.46	36.642	
7,500.00	7,338.12	7,405.22	7,338.12	25.44	18.90	134.81	82.32	572.51	1,335.89	1,299.06	36.83	36.267	
7,600.00	7,438.12	7,505.22	7,438.12	25.58	19.09	134.81	82.32	572.51	1,335.89	1,298.68	37.21	35.899	
7,700.00	7,538.12	7,605.22	7,538.12	25.72	19.28	134.81	82.32	572.51	1,335.89	1,298.30	37.59	35.536	
7,800.00	7,638.12	7,705.22	7,638.12	25.86	19.47	134.81	82.32	572.51	1,335.89	1,297.92	37.97	35.179	
7,900.00	7,738.12	7,805.22	7,738.12	26.00	19.66	134.81	82.32	572.51	1,335.89	1,297.54	38.36	34.828	
8,000.00	7,838.12	7,905.22	7,838.12	26.14	19.85	134.81	82.32	572.51	1,335.89	1,297.15	38.74	34.483	
8,100.00	7,938.12	8,005.22	7,938.12	26.28	20.04	134.81	82.32	572.51	1,335.89	1,296.77	39.13	34.143	
8,200.00	8,038.12	8,105.22	8,038.12	26.43	20.23	134.81	82.32	572.51	1,335.89	1,296.38	39.51	33.809	
8,300.00	8,138.12	8,205.22	8,138.12	26.57	20.43	134.81	82.32	572.51	1,335.89	1,295.99	39.90	33.480	
8,400.00	8,238.12	8,305.22	8,238.12	26.72	20.62	134.81	82.32	572.51	1,335.89	1,295.60	40.29	33.156	
8,500.00	8,338.12	8,405.22	8,338.12	26.86	20.81	134.81	82.32	572.51	1,335.89	1,295.21	40.68	32.838	
8,587.88	8,426.00	8,424.10	8,357.00	26.99	20.85	134.81	82.32	572.51	1,337.68	1,296.79	40.89	32.717	



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design Bonanza 1023-5I - BONANZA 1023-5J3AS - BONANZA 1023-5J3AS - PLAN #1 4-28-10 RHS												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
0.00	0.00	0.00	0.00	0.00	0.00	-118.59	-4.73	-8.69	9.89				
100.00	100.00	100.00	100.00	0.10	0.10	-118.59	-4.73	-8.69	9.89	9.69	0.20	48.371	
200.00	200.00	200.00	200.00	0.33	0.33	-118.59	-4.73	-8.69	9.89	9.24	0.65	15.126	
300.00	300.00	300.00	300.00	0.55	0.55	-118.59	-4.73	-8.69	9.89	8.79	1.10	8.965 CC, ES	
400.00	399.98	399.67	399.65	0.78	0.77	-102.35	-4.62	-10.42	11.65	10.11	1.54	7.552 SF	
450.00	449.93	449.44	449.37	0.90	0.88	-105.79	-4.49	-12.58	13.90	12.13	1.77	7.867	
500.00	499.86	499.36	499.22	1.01	0.98	-108.72	-4.32	-15.18	16.65	14.66	1.99	8.364	
600.00	599.73	599.19	598.92	1.24	1.21	-112.37	-3.99	-20.40	22.23	19.79	2.44	9.098	
700.00	699.59	699.03	698.62	1.47	1.44	-114.56	-3.66	-25.61	27.87	24.96	2.90	9.595	
800.00	799.45	798.87	798.32	1.71	1.68	-116.01	-3.33	-30.83	33.53	30.16	3.37	9.951	
900.00	899.31	898.70	898.02	1.95	1.92	-117.03	-2.99	-36.04	39.21	35.37	3.84	10.216	
1,000.00	999.18	998.54	997.72	2.19	2.16	-117.80	-2.66	-41.26	44.90	40.59	4.31	10.422	
1,100.00	1,099.04	1,098.38	1,097.42	2.43	2.40	-118.40	-2.33	-46.47	50.59	45.81	4.78	10.585	
1,200.00	1,198.90	1,198.21	1,197.12	2.67	2.64	-118.87	-2.00	-51.68	56.29	51.04	5.25	10.717	
1,300.00	1,298.77	1,298.05	1,296.82	2.91	2.89	-119.26	-1.67	-56.90	62.00	56.27	5.73	10.827	
1,400.00	1,398.63	1,397.89	1,396.52	3.16	3.13	-119.58	-1.34	-62.11	67.70	61.50	6.20	10.920	
1,500.00	1,498.49	1,497.72	1,496.22	3.40	3.37	-119.85	-1.00	-67.33	73.41	66.73	6.67	10.999	
1,600.00	1,598.36	1,597.56	1,595.92	3.64	3.62	-120.09	-0.67	-72.54	79.11	71.97	7.15	11.067	
1,700.00	1,698.22	1,697.40	1,695.62	3.88	3.86	-120.29	-0.34	-77.76	84.82	77.20	7.62	11.126	
1,800.00	1,798.08	1,797.23	1,795.32	4.12	4.11	-120.46	-0.01	-82.97	90.53	82.43	8.10	11.178	
1,900.00	1,897.94	1,897.07	1,895.02	4.36	4.35	-120.62	0.32	-88.19	96.24	87.67	8.57	11.224	
2,000.00	1,997.81	1,996.91	1,994.72	4.61	4.59	-120.76	0.65	-93.40	101.95	92.90	9.05	11.265	
2,100.00	2,097.67	2,096.74	2,094.42	4.85	4.84	-120.88	0.99	-98.62	107.67	98.14	9.53	11.302	
2,112.35	2,110.00	2,108.85	2,106.51	4.88	4.87	-120.89	1.03	-99.26	108.38	98.79	9.59	11.307	
2,200.00	2,197.40	2,193.34	2,190.73	5.10	5.09	-120.75	1.44	-105.82	115.70	105.69	10.01	11.560	
2,300.00	2,296.61	2,288.89	2,285.53	5.39	5.37	-120.61	2.20	-117.71	129.26	118.72	10.53	12.271	
2,400.00	2,395.04	2,383.16	2,378.35	5.72	5.69	-120.46	3.24	-134.06	148.26	137.15	11.11	13.349	
2,500.00	2,492.42	2,475.75	2,468.63	6.09	6.05	-120.27	4.54	-154.55	172.57	160.84	11.73	14.706	
2,600.00	2,588.47	2,566.34	2,555.89	6.52	6.46	-120.00	6.08	-178.80	202.03	189.60	12.43	16.259	
2,679.08	2,663.32	2,636.37	2,622.50	6.91	6.80	-119.72	7.45	-200.37	228.85	215.83	13.02	17.571	
2,700.00	2,682.98	2,654.65	2,639.76	7.02	6.90	-119.82	7.84	-206.40	236.40	223.20	13.20	17.909	
2,800.00	2,776.94	2,746.70	2,726.27	7.56	7.42	-120.06	9.83	-237.76	273.07	258.98	14.09	19.382	
2,900.00	2,870.91	2,839.72	2,813.68	8.13	7.97	-120.23	11.85	-269.51	309.78	294.76	15.02	20.631	
3,000.00	2,964.88	2,932.73	2,901.08	8.71	8.54	-120.36	13.87	-301.26	346.49	330.52	15.97	21.691	
3,100.00	3,058.85	3,025.75	2,988.49	9.30	9.12	-120.47	15.88	-333.01	383.20	366.24	16.96	22.597	
3,200.00	3,152.82	3,118.76	3,075.89	9.91	9.71	-120.57	17.90	-364.76	419.91	401.95	17.96	23.375	
3,300.00	3,246.78	3,211.78	3,163.30	10.52	10.32	-120.64	19.92	-396.50	456.63	437.64	18.99	24.047	
3,400.00	3,340.75	3,304.79	3,250.71	11.14	10.93	-120.71	21.94	-428.25	493.34	473.31	20.03	24.632	
3,500.00	3,434.72	3,397.81	3,338.11	11.77	11.55	-120.76	23.95	-460.00	530.05	508.97	21.08	25.143	
3,600.00	3,528.69	3,490.82	3,425.52	12.41	12.18	-120.81	25.97	-491.75	566.77	544.62	22.15	25.591	
3,700.00	3,622.66	3,583.84	3,512.92	13.05	12.81	-120.85	27.99	-523.50	603.48	580.26	23.22	25.988	
3,800.00	3,716.62	3,676.85	3,600.33	13.70	13.45	-120.89	30.01	-555.25	640.20	615.89	24.30	26.341	
3,900.00	3,810.59	3,769.87	3,687.74	14.34	14.09	-120.93	32.03	-586.99	676.91	651.52	25.40	26.655	
4,000.00	3,904.56	3,862.88	3,775.14	15.00	14.74	-120.96	34.04	-618.74	713.63	687.14	26.49	26.937	
4,100.00	3,998.53	3,955.90	3,862.55	15.65	15.38	-120.98	36.06	-650.49	750.35	722.75	27.59	27.192	
4,200.00	4,092.50	4,048.91	3,949.95	16.31	16.03	-121.01	38.08	-682.24	787.06	758.36	28.70	27.421	
4,300.00	4,186.46	4,141.93	4,037.36	16.97	16.68	-121.03	40.10	-713.99	823.78	793.96	29.81	27.630	
4,400.00	4,280.43	4,234.94	4,124.77	17.63	17.34	-121.05	42.11	-745.74	860.49	829.56	30.93	27.820	
4,500.00	4,374.40	4,327.96	4,212.17	18.29	17.99	-121.07	44.13	-777.49	897.21	865.16	32.05	27.993	
4,600.00	4,468.37	4,420.98	4,299.58	18.95	18.65	-121.09	46.15	-809.23	933.93	900.75	33.17	28.152	
4,700.00	4,562.34	4,513.99	4,386.99	19.62	19.31	-121.10	48.17	-840.98	970.64	936.34	34.30	28.298	
4,766.78	4,625.09	4,576.10	4,445.35	20.07	19.75	-121.11	49.51	-862.18	995.16	960.11	35.05	28.390	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design Bonanza 1023-5I - BONANZA 1023-5J3AS - BONANZA 1023-5J3AS - PLAN #1 4-28-10 RHS												Offset Site Error:	0.00 ft
Survey Program: 0-MWD												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
4,800.00	4,656.37	4,607.04	4,474.43	20.26	19.97	-121.33	50.19	-872.74	1,007.27	971.82	35.44	28.419	
4,900.00	4,751.29	4,718.11	4,579.28	20.76	20.65	-121.87	52.51	-909.29	1,041.95	1,005.39	36.56	28.499	
5,000.00	4,847.24	4,836.30	4,692.30	21.22	21.22	-122.36	54.70	-943.77	1,072.91	1,035.34	37.57	28.561	
5,100.00	4,944.12	4,956.80	4,808.89	21.64	21.74	-122.79	56.63	-974.09	1,099.96	1,061.47	38.49	28.579	
5,200.00	5,041.81	5,079.32	4,928.65	22.01	22.19	-123.19	58.27	-999.89	1,123.00	1,083.69	39.32	28.562	
5,300.00	5,140.18	5,203.54	5,051.07	22.34	22.58	-123.56	59.60	-1,020.80	1,141.95	1,101.90	40.05	28.514	
5,400.00	5,239.12	5,329.10	5,175.63	22.63	22.90	-123.90	60.59	-1,036.53	1,156.72	1,116.05	40.66	28.446	
5,500.00	5,338.50	5,455.61	5,301.71	22.87	23.14	-124.21	61.25	-1,046.86	1,167.25	1,126.08	41.17	28.351	
5,600.00	5,438.21	5,582.69	5,428.68	23.07	23.32	-124.51	61.55	-1,051.63	1,173.51	1,131.94	41.57	28.229	
5,700.00	5,538.12	5,692.13	5,538.12	23.22	23.43	-124.72	61.58	-1,051.98	1,175.97	1,134.11	41.86	28.094	
5,766.88	5,605.00	5,759.01	5,605.00	23.29	23.51	-144.88	61.58	-1,051.98	1,176.41	1,134.40	42.02	27.999	
5,800.00	5,638.12	5,792.12	5,638.12	23.33	23.54	-144.88	61.58	-1,051.98	1,176.41	1,134.32	42.09	27.947	
5,900.00	5,738.12	5,892.12	5,738.12	23.44	23.65	-144.88	61.58	-1,051.98	1,176.41	1,134.07	42.34	27.783	
6,000.00	5,838.12	5,992.12	5,838.12	23.55	23.77	-144.88	61.58	-1,051.98	1,176.41	1,133.82	42.59	27.619	
6,100.00	5,938.12	6,092.12	5,938.12	23.67	23.88	-144.88	61.58	-1,051.98	1,176.41	1,133.56	42.85	27.454	
6,200.00	6,038.12	6,192.12	6,038.12	23.79	23.99	-144.88	61.58	-1,051.98	1,176.41	1,133.31	43.11	27.290	
6,300.00	6,138.12	6,292.12	6,138.12	23.90	24.11	-144.88	61.58	-1,051.98	1,176.41	1,133.04	43.37	27.125	
6,400.00	6,238.12	6,392.12	6,238.12	24.02	24.23	-144.88	61.58	-1,051.98	1,176.41	1,132.78	43.63	26.961	
6,500.00	6,338.12	6,492.12	6,338.12	24.15	24.35	-144.88	61.58	-1,051.98	1,176.41	1,132.51	43.90	26.797	
6,600.00	6,438.12	6,592.12	6,438.12	24.27	24.47	-144.88	61.58	-1,051.98	1,176.41	1,132.24	44.17	26.633	
6,700.00	6,538.12	6,692.12	6,538.12	24.39	24.60	-144.88	61.58	-1,051.98	1,176.41	1,131.97	44.44	26.469	
6,800.00	6,638.12	6,792.12	6,638.12	24.52	24.72	-144.88	61.58	-1,051.98	1,176.41	1,131.69	44.72	26.306	
6,900.00	6,738.12	6,892.12	6,738.12	24.65	24.85	-144.88	61.58	-1,051.98	1,176.41	1,131.41	45.00	26.143	
7,000.00	6,838.12	6,992.12	6,838.12	24.78	24.97	-144.88	61.58	-1,051.98	1,176.41	1,131.13	45.28	25.980	
7,100.00	6,938.12	7,092.12	6,938.12	24.91	25.10	-144.88	61.58	-1,051.98	1,176.41	1,130.85	45.57	25.818	
7,200.00	7,038.12	7,192.12	7,038.12	25.04	25.23	-144.88	61.58	-1,051.98	1,176.41	1,130.56	45.85	25.656	
7,300.00	7,138.12	7,292.12	7,138.12	25.17	25.36	-144.88	61.58	-1,051.98	1,176.41	1,130.27	46.14	25.495	
7,400.00	7,238.12	7,392.12	7,238.12	25.31	25.50	-144.88	61.58	-1,051.98	1,176.41	1,129.98	46.43	25.335	
7,500.00	7,338.12	7,492.12	7,338.12	25.44	25.63	-144.88	61.58	-1,051.98	1,176.41	1,129.69	46.73	25.175	
7,600.00	7,438.12	7,592.12	7,438.12	25.58	25.76	-144.88	61.58	-1,051.98	1,176.41	1,129.39	47.03	25.016	
7,700.00	7,538.12	7,692.12	7,538.12	25.72	25.90	-144.88	61.58	-1,051.98	1,176.41	1,129.09	47.33	24.858	
7,800.00	7,638.12	7,792.12	7,638.12	25.86	26.04	-144.88	61.58	-1,051.98	1,176.41	1,128.79	47.63	24.700	
7,900.00	7,738.12	7,892.12	7,738.12	26.00	26.18	-144.88	61.58	-1,051.98	1,176.41	1,128.48	47.93	24.544	
8,000.00	7,838.12	7,992.12	7,838.12	26.14	26.32	-144.88	61.58	-1,051.98	1,176.41	1,128.18	48.24	24.388	
8,100.00	7,938.12	8,092.12	7,938.12	26.28	26.46	-144.88	61.58	-1,051.98	1,176.41	1,127.87	48.55	24.233	
8,200.00	8,038.12	8,192.12	8,038.12	26.43	26.60	-144.88	61.58	-1,051.98	1,176.41	1,127.56	48.86	24.079	
8,300.00	8,138.12	8,292.12	8,138.12	26.57	26.74	-144.88	61.58	-1,051.98	1,176.41	1,127.24	49.17	23.925	
8,400.00	8,238.12	8,392.12	8,238.12	26.72	26.89	-144.88	61.58	-1,051.98	1,176.41	1,126.93	49.49	23.773	
8,500.00	8,338.12	8,492.12	8,338.12	26.86	27.03	-144.88	61.58	-1,051.98	1,176.41	1,126.61	49.80	23.622	
8,553.04	8,391.15	8,545.16	8,391.15	26.94	27.11	-144.88	61.58	-1,051.98	1,176.41	1,126.44	49.97	23.542	
8,587.88	8,426.00	8,566.01	8,412.00	26.99	27.14	-144.88	61.58	-1,051.98	1,176.50	1,126.44	50.06	23.501	



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design													Offset Site Error:	0.00 ft
Survey Program: 514-MWD													Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning	
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor		
0.00	0.00	9.00	9.00	0.00	0.01	74.65	10.93	39.79	41.27					
100.00	100.00	108.99	108.99	0.10	0.12	74.62	10.95	39.80	41.27	41.05	0.22	187.253		
200.00	200.00	208.99	208.99	0.33	0.23	74.55	11.00	39.81	41.30	40.75	0.55	74.603		
300.00	300.00	308.98	308.98	0.55	0.34	74.44	11.09	39.82	41.34	40.45	0.89	46.618		
400.00	399.98	408.96	408.96	0.78	0.44	96.82	11.21	39.85	41.56	40.35	1.22	34.097 ES		
450.00	449.93	458.91	458.91	0.90	0.50	99.68	11.28	39.86	41.91	40.52	1.39	30.229		
500.00	499.86	508.84	508.84	1.01	0.55	103.06	11.36	39.88	42.45	40.90	1.56	27.295		
600.00	599.73	608.69	608.69	1.24	0.76	109.50	11.52	39.94	44.00	42.00	1.99	22.053		
700.00	699.59	708.53	708.53	1.47	0.97	115.46	11.66	40.06	46.12	43.68	2.44	18.893		
800.00	799.45	808.36	808.36	1.71	1.19	120.85	11.78	40.24	48.75	45.87	2.89	16.891		
900.00	899.31	908.19	908.19	1.95	1.40	125.66	11.88	40.48	51.84	48.51	3.33	15.564		
1,000.00	999.18	1,008.02	1,008.02	2.19	1.61	129.91	11.96	40.78	55.31	51.54	3.77	14.655		
1,100.00	1,099.04	1,107.82	1,107.82	2.43	1.82	133.65	11.99	41.14	59.13	54.92	4.21	14.034		
1,200.00	1,198.90	1,207.59	1,207.59	2.67	2.03	136.98	11.90	41.58	63.29	58.64	4.65	13.611		
1,300.00	1,298.77	1,307.35	1,307.34	2.91	2.24	139.95	11.70	42.11	67.77	62.69	5.09	13.325		
1,400.00	1,398.63	1,407.21	1,407.20	3.16	2.45	142.61	11.38	42.67	72.51	67.00	5.52	13.139		
1,500.00	1,498.49	1,507.22	1,507.21	3.40	2.65	145.09	10.99	42.99	77.22	71.27	5.95	12.985		
1,600.00	1,598.36	1,607.24	1,607.23	3.64	2.85	147.45	10.54	42.97	81.83	75.45	6.37	12.837		
1,700.00	1,698.22	1,707.21	1,707.20	3.88	3.05	149.73	10.03	42.64	86.35	79.55	6.80	12.696		
1,800.00	1,798.08	1,806.77	1,806.76	4.12	3.26	151.82	9.39	42.33	91.11	83.88	7.23	12.598		
1,900.00	1,897.94	1,906.28	1,906.27	4.36	3.46	153.71	8.52	42.24	96.29	88.62	7.66	12.562 SF		
2,000.00	1,997.81	2,005.80	2,005.77	4.61	3.67	155.55	7.23	42.19	101.89	93.79	8.10	12.579		
2,100.00	2,097.67	2,104.99	2,104.95	4.85	3.88	157.04	5.93	42.57	107.89	99.36	8.54	12.640		
2,112.35	2,110.00	2,117.17	2,117.13	4.88	3.91	157.24	5.69	42.61	108.69	100.10	8.59	12.654		
2,200.00	2,197.40	2,202.56	2,202.47	5.10	4.09	159.28	2.99	42.59	116.88	107.92	8.96	13.048		
2,300.00	2,296.61	2,298.20	2,297.84	5.39	4.30	163.49	-4.04	41.01	133.35	123.99	9.36	14.247		
2,400.00	2,395.04	2,391.74	2,390.96	5.72	4.51	167.49	-12.80	39.51	157.13	147.38	9.75	16.123		
2,500.00	2,492.42	2,479.91	2,478.43	6.09	4.73	170.87	-23.72	38.43	189.21	179.11	10.11	18.723		
2,600.00	2,588.47	2,564.15	2,561.58	6.52	4.95	173.55	-37.20	38.27	230.10	219.66	10.44	22.035		
2,679.08	2,663.32	2,631.69	2,628.09	6.91	5.13	175.18	-48.95	38.75	267.22	256.52	10.70	24.985		
2,700.00	2,682.98	2,649.82	2,645.94	7.02	5.18	175.58	-52.16	38.94	277.52	266.73	10.79	25.729		
2,800.00	2,776.94	2,735.43	2,730.17	7.56	5.42	177.17	-67.40	39.60	326.88	315.66	11.22	29.132		
2,900.00	2,870.91	2,819.94	2,813.18	8.13	5.66	178.46	-83.26	39.81	377.00	365.33	11.67	32.315		
3,000.00	2,964.88	2,908.02	2,899.72	8.71	5.92	179.47	-99.65	40.18	427.17	415.05	12.12	35.246		
3,100.00	3,058.85	2,998.03	2,988.22	9.30	6.17	-179.67	-116.05	40.00	476.91	464.34	12.58	37.912		
3,200.00	3,152.82	3,087.97	3,076.80	9.91	6.44	-179.01	-131.63	39.78	525.95	512.90	13.05	40.312		
3,300.00	3,246.78	3,173.79	3,161.32	10.52	6.71	-178.46	-146.50	39.36	574.97	561.45	13.52	42.538		
3,400.00	3,340.75	3,258.31	3,244.40	11.14	6.98	-177.83	-161.94	37.50	624.35	610.36	13.99	44.618		
3,500.00	3,434.72	3,345.43	3,329.96	11.77	7.27	-177.23	-178.18	35.14	673.98	659.49	14.49	46.528		
3,600.00	3,528.69	3,439.24	3,422.28	12.41	7.58	-176.77	-194.75	33.50	723.05	708.06	14.99	48.232		
3,700.00	3,622.66	3,528.07	3,509.73	13.05	7.87	-176.36	-210.18	31.34	771.75	756.26	15.49	49.832		
3,800.00	3,716.62	3,626.91	3,607.14	13.70	8.18	-175.90	-226.62	28.08	819.62	803.61	16.01	51.197		
3,900.00	3,810.59	3,710.00	3,689.11	14.34	8.44	-175.58	-239.95	25.47	867.07	850.57	16.50	52.542		
4,000.00	3,904.56	3,794.18	3,772.12	15.00	8.73	-175.31	-253.75	23.23	914.96	897.95	17.01	53.794		
4,100.00	3,998.53	3,863.65	3,840.52	15.65	8.97	-175.14	-265.86	21.98	963.95	946.47	17.49	55.130		
4,200.00	4,092.50	3,944.58	3,919.99	16.31	9.26	-174.99	-281.11	21.55	1,014.42	996.43	17.99	56.402		
4,300.00	4,186.46	4,040.82	4,014.65	16.97	9.59	-174.87	-298.51	21.39	1,064.33	1,045.82	18.51	57.494		
4,400.00	4,280.43	4,118.50	4,091.14	17.63	9.85	-174.82	-312.07	21.78	1,113.92	1,094.92	19.00	58.632		
4,500.00	4,374.40	4,185.00	4,156.33	18.29	10.09	-174.77	-325.13	22.30	1,165.28	1,145.81	19.47	59.858		
4,600.00	4,468.37	4,264.59	4,234.16	18.95	10.40	-174.66	-341.79	22.38	1,217.64	1,197.67	19.97	60.975		
4,700.00	4,562.34	4,368.08	4,335.45	19.62	10.78	-174.46	-362.95	20.74	1,269.27	1,248.75	20.52	61.847		
4,766.78	4,625.09	4,434.79	4,400.86	20.07	11.02	-174.32	-375.94	19.16	1,303.08	1,282.19	20.89	62.382		

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	0.00 ft
Survey Program: 514-MWD												Offset Well Error:	0.00 ft
Reference	Offset	Semi Major Axis		Distance									
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
4,800.00	4,656.37	4,468.09	4,433.55	20.26	11.14	-174.30	-382.23	18.47	1,319.59	1,298.48	21.11	62.505	
4,900.00	4,751.29	4,616.13	4,579.59	20.76	11.63	-174.20	-406.23	15.50	1,364.84	1,343.00	21.84	62.485	
5,000.00	4,847.24	4,746.49	4,708.84	21.22	12.02	-174.15	-422.92	12.89	1,404.06	1,381.56	22.50	62.389	
5,100.00	4,944.12	4,910.95	4,872.79	21.64	12.43	-174.20	-435.52	11.59	1,435.07	1,411.87	23.19	61.881	
5,200.00	5,041.81	5,053.32	5,015.01	22.01	12.73	-174.29	-441.78	10.94	1,460.42	1,436.63	23.79	61.383	
5,300.00	5,140.18	5,148.83	5,110.46	22.34	12.92	-174.34	-444.72	10.09	1,480.98	1,456.71	24.26	61.039	
5,400.00	5,239.12	5,277.30	5,238.92	22.63	13.15	-174.40	-446.45	9.48	1,496.45	1,471.69	24.76	60.438	
5,500.00	5,338.50	5,374.69	5,336.31	22.87	13.32	-174.44	-447.25	9.10	1,508.13	1,482.97	25.16	59.947	
5,600.00	5,438.21	5,484.06	5,445.68	23.07	13.51	-174.47	-447.98	8.73	1,516.23	1,490.69	25.54	59.362	
5,700.00	5,538.12	5,582.83	5,544.45	23.22	13.68	-174.48	-448.02	8.52	1,520.28	1,494.41	25.87	58.776	
5,766.88	5,605.00	5,644.12	5,605.73	23.29	13.79	165.38	-448.19	8.72	1,521.29	1,495.24	26.05	58.395	
5,800.00	5,638.12	5,674.26	5,635.88	23.33	13.84	165.38	-448.36	8.81	1,521.50	1,495.33	26.17	58.146	
5,900.00	5,738.12	5,801.31	5,762.92	23.44	14.06	165.40	-448.65	8.30	1,521.69	1,495.09	26.60	57.204	
6,000.00	5,838.12	5,892.00	5,853.60	23.55	14.21	165.41	-447.83	7.98	1,520.74	1,493.78	26.96	56.399	
6,039.36	5,877.48	5,924.88	5,886.48	23.60	14.27	165.40	-447.62	8.20	1,520.58	1,493.48	27.10	56.105	
6,100.00	5,938.12	5,967.79	5,929.38	23.67	14.35	165.38	-447.78	8.59	1,520.94	1,493.64	27.30	55.712	
6,200.00	6,038.12	6,076.13	6,037.71	23.79	14.54	165.35	-448.81	9.79	1,522.16	1,494.46	27.70	54.951	
6,300.00	6,138.12	6,188.81	6,150.39	23.90	14.74	165.34	-448.95	10.15	1,522.37	1,494.26	28.11	54.161	
6,400.00	6,238.12	6,301.38	6,262.95	24.02	14.93	165.35	-448.25	9.60	1,521.63	1,493.11	28.52	53.355	
6,500.00	6,338.12	6,398.79	6,360.36	24.15	15.09	165.35	-447.29	9.27	1,520.60	1,491.69	28.90	52.610	
6,600.00	6,438.12	6,490.59	6,452.16	24.27	15.25	165.34	-446.68	9.53	1,520.02	1,490.74	29.28	51.917	
6,678.67	6,516.78	6,564.21	6,525.78	24.37	15.38	165.34	-446.54	9.56	1,519.88	1,490.30	29.57	51.391	
6,700.00	6,538.12	6,583.50	6,545.07	24.39	15.42	165.34	-446.56	9.54	1,519.89	1,490.24	29.65	51.254	
6,800.00	6,638.12	6,674.34	6,635.91	24.52	15.58	165.34	-446.97	9.57	1,520.34	1,490.31	30.03	50.629	
6,900.00	6,738.12	6,780.86	6,742.42	24.65	15.78	165.33	-447.81	9.98	1,521.23	1,490.79	30.44	49.976	
7,000.00	6,838.12	6,895.83	6,857.38	24.78	15.99	165.39	-447.49	8.31	1,520.52	1,489.65	30.87	49.259	
7,100.00	6,938.12	6,990.34	6,951.88	24.91	16.16	165.43	-447.37	7.23	1,520.11	1,488.85	31.26	48.631	
7,200.00	7,038.12	7,088.19	7,049.72	25.04	16.34	165.47	-447.38	6.18	1,519.85	1,488.19	31.66	48.011	
7,300.00	7,138.12	7,194.51	7,156.04	25.17	16.54	165.52	-447.43	4.85	1,519.59	1,487.52	32.07	47.384	
7,400.00	7,238.12	7,306.35	7,267.88	25.31	16.73	165.51	-446.33	4.75	1,518.61	1,486.12	32.49	46.738	
7,500.00	7,338.12	7,392.58	7,354.09	25.44	16.89	165.49	-445.35	5.10	1,517.63	1,484.77	32.86	46.182	
7,600.00	7,438.12	7,486.12	7,447.63	25.58	17.06	165.46	-444.98	5.88	1,517.45	1,484.20	33.25	45.640	
7,615.27	7,453.39	7,500.78	7,462.29	25.60	17.08	165.45	-444.95	6.01	1,517.45	1,484.14	33.31	45.558	
7,700.00	7,538.12	7,584.97	7,546.48	25.72	17.24	165.41	-444.71	7.02	1,517.47	1,483.82	33.65	45.101	
7,800.00	7,638.12	7,684.11	7,645.60	25.86	17.43	165.35	-444.34	8.70	1,517.54	1,483.49	34.04	44.575	
7,900.00	7,738.12	7,784.66	7,746.14	26.00	17.61	165.29	-444.07	10.08	1,517.63	1,483.18	34.44	44.060	
8,000.00	7,838.12	7,875.18	7,836.66	26.14	17.78	165.26	-444.19	10.90	1,517.99	1,483.16	34.83	43.588	
8,100.00	7,938.12	7,962.37	7,923.84	26.28	17.95	165.24	-444.93	11.86	1,519.09	1,483.88	35.20	43.150	
8,200.00	8,038.12	8,057.27	8,018.72	26.43	18.14	165.20	-446.33	13.09	1,520.85	1,485.25	35.60	42.719	
8,300.00	8,138.12	8,170.00	8,131.43	26.57	18.36	165.16	-447.70	14.65	1,522.38	1,486.35	36.03	42.251	
8,400.00	8,238.12	8,270.13	8,231.55	26.72	18.55	165.12	-448.41	16.01	1,523.42	1,486.98	36.44	41.811	
8,500.00	8,338.12	8,359.00	8,320.41	26.86	18.72	165.07	-448.69	17.46	1,524.21	1,487.40	36.82	41.399	
8,587.88	8,426.00	8,359.00	8,320.41	26.99	18.72	165.07	-448.69	17.46	1,528.28	1,491.28	37.00	41.308	



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design												Offset Site Error:	0.00 ft
Survey Program: 100-NS-GYRO-MS												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						Warning
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	
0.00	0.00	0.00	0.00	0.00	0.00	98.56	-4.01	26.62	30.34				
100.00	100.00	86.08	86.08	0.10	0.11	98.34	-3.89	26.51	26.80	26.58	0.22	123.726	
200.00	200.00	186.05	186.05	0.33	0.36	97.65	-3.53	26.29	26.53	25.84	0.68	38.877	
241.84	241.84	227.84	227.84	0.42	0.44	97.31	-3.37	26.27	26.48	25.62	0.87	30.609 CC	
300.00	300.00	285.92	285.92	0.55	0.55	96.95	-3.21	26.38	26.57	25.47	1.11	24.029 ES	
400.00	399.98	386.01	386.00	0.78	0.76	119.72	-2.97	26.60	27.59	26.05	1.54	17.935	
450.00	449.93	435.99	435.99	0.90	0.89	123.10	-2.76	26.56	28.64	26.87	1.77	16.142	
500.00	499.86	485.93	485.93	1.01	1.02	126.90	-2.54	26.51	30.04	28.03	2.02	14.887	
600.00	599.73	585.74	585.74	1.24	1.28	133.70	-2.27	26.45	33.29	30.78	2.51	13.271	
700.00	699.59	685.51	685.51	1.47	1.51	139.34	-2.20	26.59	37.19	34.22	2.96	12.546	
800.00	799.45	785.38	785.38	1.71	1.71	143.55	-2.00	26.97	41.51	38.11	3.40	12.211	
900.00	899.31	885.31	885.30	1.95	1.95	147.12	-1.85	27.20	45.92	42.06	3.86	11.888	
1,000.00	999.18	985.20	985.19	2.19	2.20	150.16	-1.72	27.30	50.39	46.04	4.34	11.600	
1,100.00	1,099.04	1,084.77	1,084.76	2.43	2.42	152.35	-1.48	27.78	55.18	50.39	4.79	11.520	
1,200.00	1,198.90	1,184.54	1,184.53	2.67	2.61	154.07	-1.44	28.64	60.45	55.25	5.20	11.616	
1,300.00	1,298.77	1,284.39	1,284.38	2.91	2.80	155.53	-1.42	29.51	65.80	60.17	5.62	11.700	
1,400.00	1,398.63	1,384.74	1,384.72	3.16	3.03	156.71	-1.12	30.23	70.87	64.79	6.08	11.658	
1,500.00	1,498.49	1,484.68	1,484.66	3.40	3.28	157.77	-0.50	30.56	75.46	68.90	6.56	11.499	
1,600.00	1,598.36	1,584.51	1,584.49	3.64	3.54	158.90	-0.09	30.72	80.13	73.08	7.05	11.366	
1,700.00	1,698.22	1,684.53	1,684.51	3.88	3.81	159.69	0.55	31.10	84.79	77.25	7.54	11.246	
1,800.00	1,798.08	1,784.06	1,784.04	4.12	4.06	160.25	1.30	31.70	89.52	81.50	8.02	11.164	
1,900.00	1,897.94	1,883.95	1,883.92	4.36	4.31	161.06	1.52	32.09	94.54	86.05	8.49	11.131	
2,000.00	1,997.81	1,983.95	1,983.92	4.61	4.56	161.79	1.82	32.39	99.46	90.48	8.98	11.078	
2,100.00	2,097.67	2,083.79	2,083.76	4.85	4.83	162.46	2.16	32.65	104.33	94.86	9.47	11.019	
2,112.35	2,110.00	2,096.12	2,096.08	4.88	4.86	162.54	2.20	32.69	104.93	95.40	9.53	11.013 SF	
2,200.00	2,197.40	2,183.45	2,183.41	5.10	5.08	163.38	2.37	32.84	111.20	101.27	9.93	11.199	
2,300.00	2,296.61	2,282.21	2,282.18	5.39	5.24	164.94	2.25	32.91	123.29	113.00	10.28	11.989	
2,400.00	2,395.04	2,380.47	2,380.43	5.72	5.33	166.70	1.87	33.09	140.77	130.24	10.53	13.365	
2,500.00	2,492.42	2,477.76	2,477.72	6.09	5.40	168.42	1.48	33.26	163.40	152.65	10.75	15.200	
2,600.00	2,588.47	2,573.10	2,573.06	6.52	5.49	169.93	1.02	33.52	191.25	180.29	10.97	17.442	
2,679.08	2,663.32	2,647.52	2,647.48	6.91	5.58	170.94	0.55	33.94	217.06	205.92	11.14	19.487	
2,700.00	2,682.98	2,667.11	2,667.07	7.02	5.61	171.22	0.42	34.05	224.31	213.09	11.22	19.993	
2,800.00	2,776.94	2,760.40	2,760.35	7.56	5.72	172.37	-0.31	34.45	259.05	247.46	11.59	22.355	
2,900.00	2,870.91	2,852.71	2,852.66	8.13	5.81	173.34	-1.50	34.53	294.13	282.18	11.95	24.613	
3,000.00	2,964.88	2,944.62	2,944.55	8.71	5.91	174.03	-2.94	35.15	329.76	317.43	12.33	26.750	
3,100.00	3,058.85	3,037.70	3,037.61	9.30	6.03	174.64	-4.79	35.69	365.73	353.01	12.72	28.751	
3,200.00	3,152.82	3,132.63	3,132.53	9.91	6.14	175.16	-6.46	36.09	401.48	388.36	13.12	30.603	
3,300.00	3,246.78	3,227.05	3,226.94	10.52	6.27	175.58	-7.77	36.37	436.88	423.36	13.53	32.301	
3,400.00	3,340.75	3,319.53	3,319.41	11.14	6.40	175.93	-9.08	36.73	472.36	458.42	13.95	33.868	
3,500.00	3,434.72	3,412.00	3,411.86	11.77	6.54	176.21	-10.53	37.25	508.06	493.68	14.37	35.344	
3,600.00	3,528.69	3,505.37	3,505.22	12.41	6.70	176.45	-12.02	37.89	543.83	529.00	14.83	36.677	
3,700.00	3,622.66	3,598.75	3,598.59	13.05	6.86	176.65	-13.47	38.63	579.61	564.33	15.28	37.930	
3,800.00	3,716.62	3,693.34	3,693.17	13.70	7.04	176.82	-14.84	39.36	615.30	599.55	15.75	39.066	
3,900.00	3,810.59	3,788.09	3,787.91	14.34	7.22	176.99	-16.08	39.93	650.81	634.59	16.22	40.121	
4,000.00	3,904.56	3,881.98	3,881.79	15.00	7.38	177.15	-17.23	40.33	686.19	669.51	16.69	41.123	
4,100.00	3,998.53	3,975.75	3,975.55	15.65	7.55	177.31	-18.42	40.55	721.55	704.39	17.15	42.069	
4,200.00	4,092.50	4,071.97	4,071.76	16.31	7.70	177.46	-19.56	40.59	756.76	739.16	17.60	42.986	
4,300.00	4,186.46	4,169.34	4,169.13	16.97	7.85	177.60	-20.29	40.49	791.55	773.50	18.06	43.840	
4,400.00	4,280.43	4,264.07	4,263.86	17.63	8.00	177.73	-20.68	40.32	826.02	807.52	18.51	44.631	
4,500.00	4,374.40	4,357.46	4,357.24	18.29	8.14	177.83	-21.06	40.22	860.53	841.57	18.96	45.385	
4,600.00	4,468.37	4,451.62	4,451.41	18.95	8.29	177.93	-21.46	40.16	895.06	875.64	19.42	46.100	
4,700.00	4,562.34	4,546.52	4,546.31	19.62	8.44	178.03	-21.81	40.00	929.50	909.63	19.87	46.775	

CC - Min centre to center distance or convergent point, SF - min separation factor, ES - min ellipse separation



Weatherford International Ltd.

Anticollision Report



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Offset Design Bonanza 1023-5I - Southman Canyon 4-5 EXISTING - Southman Canyon 4-5 EXISTING - Southman Canyon 4-5 EXISTING												Offset Site Error:	0.00 ft
Survey Program: 100-NS-GYRO-MS												Offset Well Error:	0.00 ft
Reference		Offset		Semi Major Axis			Distance						
Measured Depth (ft)	Vertical Depth (ft)	Measured Depth (ft)	Vertical Depth (ft)	Reference (ft)	Offset (ft)	Highside Toolface (°)	Offset Wellbore Centre +N/-S (ft)	+E/-W (ft)	Between Centres (ft)	Between Ellipses (ft)	Minimum Separation (ft)	Separation Factor	Warning
4,766.78	4,625.09	4,610.08	4,609.86	20.07	8.54	178.09	-22.01	39.81	952.45	932.27	20.17	47.212	
4,800.00	4,656.37	4,642.18	4,641.96	20.26	8.57	178.13	-22.08	39.71	963.65	943.30	20.35	47.345	
4,900.00	4,751.29	4,739.69	4,739.48	20.76	8.69	178.23	-22.11	39.39	995.01	974.16	20.85	47.716	
5,000.00	4,847.24	4,835.87	4,835.65	21.22	8.82	178.31	-21.92	39.08	1,022.84	1,001.50	21.33	47.947	
5,100.00	4,944.12	4,928.82	4,928.60	21.64	8.97	178.37	-21.92	38.96	1,047.54	1,025.75	21.80	48.055	
5,200.00	5,041.81	5,023.37	5,023.15	22.01	9.13	178.41	-22.22	39.05	1,069.22	1,046.97	22.25	48.064	
5,300.00	5,140.18	5,121.69	5,121.48	22.34	9.34	178.45	-22.63	39.18	1,087.58	1,064.88	22.70	47.904	
5,400.00	5,239.12	5,220.62	5,220.40	22.63	9.55	178.48	-23.05	39.28	1,102.51	1,079.38	23.13	47.667	
5,500.00	5,338.50	5,320.07	5,319.85	22.87	9.77	178.50	-23.43	39.45	1,113.96	1,090.43	23.53	47.348	
5,600.00	5,438.21	5,419.81	5,419.59	23.07	9.99	178.51	-23.77	39.70	1,121.93	1,098.04	23.89	46.962	
5,700.00	5,538.12	5,519.55	5,519.33	23.22	10.22	178.51	-24.13	39.95	1,126.43	1,102.21	24.22	46.506	
5,766.88	5,605.00	5,586.32	5,586.10	23.29	10.38	158.39	-24.39	40.07	1,127.50	1,103.07	24.42	46.168	
5,800.00	5,638.12	5,619.43	5,619.20	23.33	10.45	158.39	-24.52	40.12	1,127.64	1,103.09	24.55	45.928	
5,900.00	5,738.12	5,719.45	5,719.23	23.44	10.68	158.39	-24.93	40.26	1,128.07	1,103.11	24.96	45.191	
6,000.00	5,838.12	5,818.56	5,818.34	23.55	10.90	158.39	-25.36	40.37	1,128.51	1,103.14	25.37	44.478	
6,100.00	5,938.12	5,913.86	5,913.64	23.67	11.12	158.39	-26.00	40.61	1,129.23	1,103.46	25.78	43.805	
6,200.00	6,038.12	6,009.48	6,009.25	23.79	11.34	158.39	-26.98	41.08	1,130.37	1,104.18	26.19	43.167	
6,300.00	6,138.12	6,108.18	6,107.93	23.90	11.56	158.40	-28.30	41.43	1,131.74	1,105.15	26.60	42.553	
6,400.00	6,238.12	6,206.92	6,206.66	24.02	11.78	158.43	-29.90	41.39	1,133.23	1,106.22	27.01	41.961	
6,500.00	6,338.12	6,306.41	6,306.14	24.15	12.00	158.47	-31.62	41.25	1,134.79	1,107.38	27.41	41.394	
6,600.00	6,438.12	6,405.81	6,405.53	24.27	12.21	158.50	-33.36	41.21	1,136.40	1,108.57	27.82	40.843	
6,700.00	6,538.12	6,503.71	6,503.41	24.39	12.43	158.54	-35.18	41.19	1,138.12	1,109.89	28.24	40.308	
6,800.00	6,638.12	6,601.67	6,601.35	24.52	12.65	158.58	-37.22	41.13	1,140.04	1,111.39	28.65	39.794	
6,900.00	6,738.12	6,703.93	6,703.58	24.65	12.89	158.62	-39.33	41.06	1,141.93	1,112.86	29.07	39.276	
7,000.00	6,838.12	6,805.87	6,805.51	24.78	13.12	158.65	-41.21	41.01	1,143.63	1,114.13	29.50	38.765	
7,100.00	6,938.12	6,902.80	6,902.42	24.91	13.35	158.68	-43.00	41.12	1,145.39	1,115.47	29.92	38.276	
7,200.00	7,038.12	7,000.00	6,999.60	25.04	13.57	158.70	-44.97	41.48	1,147.42	1,117.07	30.35	37.807	
7,300.00	7,138.12	7,099.81	7,099.38	25.17	13.81	158.72	-47.09	41.96	1,149.58	1,118.79	30.79	37.339	
7,400.00	7,238.12	7,199.90	7,199.45	25.31	14.06	158.74	-49.24	42.38	1,151.72	1,120.50	31.23	36.882	
7,500.00	7,338.12	7,300.06	7,299.59	25.44	14.30	158.74	-51.29	43.00	1,153.86	1,122.19	31.67	36.433	
7,600.00	7,438.12	7,400.00	7,399.51	25.58	14.55	158.73	-53.15	44.05	1,155.98	1,123.86	32.11	35.996	
7,700.00	7,538.12	7,400.00	7,399.51	25.72	14.55	158.73	-53.15	44.05	1,162.41	1,130.10	32.31	35.972	
7,800.00	7,638.12	7,400.00	7,399.51	25.86	14.55	158.73	-53.15	44.05	1,177.34	1,144.82	32.51	36.209	
7,900.00	7,738.12	7,400.00	7,399.51	26.00	14.55	158.73	-53.15	44.05	1,200.44	1,167.72	32.72	36.693	
8,000.00	7,838.12	7,400.00	7,399.51	26.14	14.55	158.73	-53.15	44.05	1,231.25	1,198.33	32.92	37.404	
8,100.00	7,938.12	7,400.00	7,399.51	26.28	14.55	158.73	-53.15	44.05	1,269.21	1,236.09	33.12	38.322	
8,200.00	8,038.12	7,400.00	7,399.51	26.43	14.55	158.73	-53.15	44.05	1,313.70	1,280.38	33.32	39.424	
8,300.00	8,138.12	7,400.00	7,399.51	26.57	14.55	158.73	-53.15	44.05	1,364.09	1,330.56	33.53	40.687	
8,400.00	8,238.12	7,400.00	7,399.51	26.72	14.55	158.73	-53.15	44.05	1,419.74	1,386.01	33.73	42.092	
8,500.00	8,338.12	7,400.00	7,399.51	26.86	14.55	158.73	-53.15	44.05	1,480.06	1,446.13	33.93	43.616	
8,587.88	8,426.00	7,400.00	7,399.51	26.99	14.55	158.73	-53.15	44.05	1,536.50	1,502.38	34.11	45.040	

Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Reference Depths are relative to WELL @ 5311.00ft (Original Well Elev) Coordinates are relative to: BONANZA 1023-5G4DS

Offset Depths are relative to Offset Datum

Coordinate System is Universal Transverse Mercator (US Survey Feet), Zone 12N

Central Meridian is 111° 0' 0.000 W °

Grid Convergence at Surface is: 1.06°



Company:	ANADARKO PETROLEUM CORP.	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UINTAH COUNTY, UTAH (nad 27)	TVD Reference:	WELL @ 5311.00ft (Original Well Elev)
Reference Site:	Bonanza 1023-5I	MD Reference:	WELL @ 5311.00ft (Original Well Elev)
Site Error:	0.00ft	North Reference:	True
Reference Well:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Well Error:	0.00ft	Output errors are at	2.00 sigma
Reference Wellbore	BONANZA 1023-5G4DS	Database:	EDM 2003.21 Single User Db
Reference Design:	PLAN #1 4-28-10 RHS	Offset TVD Reference:	Offset Datum

Reference Depths are relative to WELL @ 5311.00ft (Original Well Elev) Coordinates are relative to: BONANZA 1023-5G4DS


Offset Depths are relative to Offset Datum

Coordinate System is Universal Transverse Mercator (US Survey Feet), Zone 12N

Central Meridian is 111° 0' 0.000 W °

Grid Convergence at Surface is: 1.06°

Separation Factor Plot

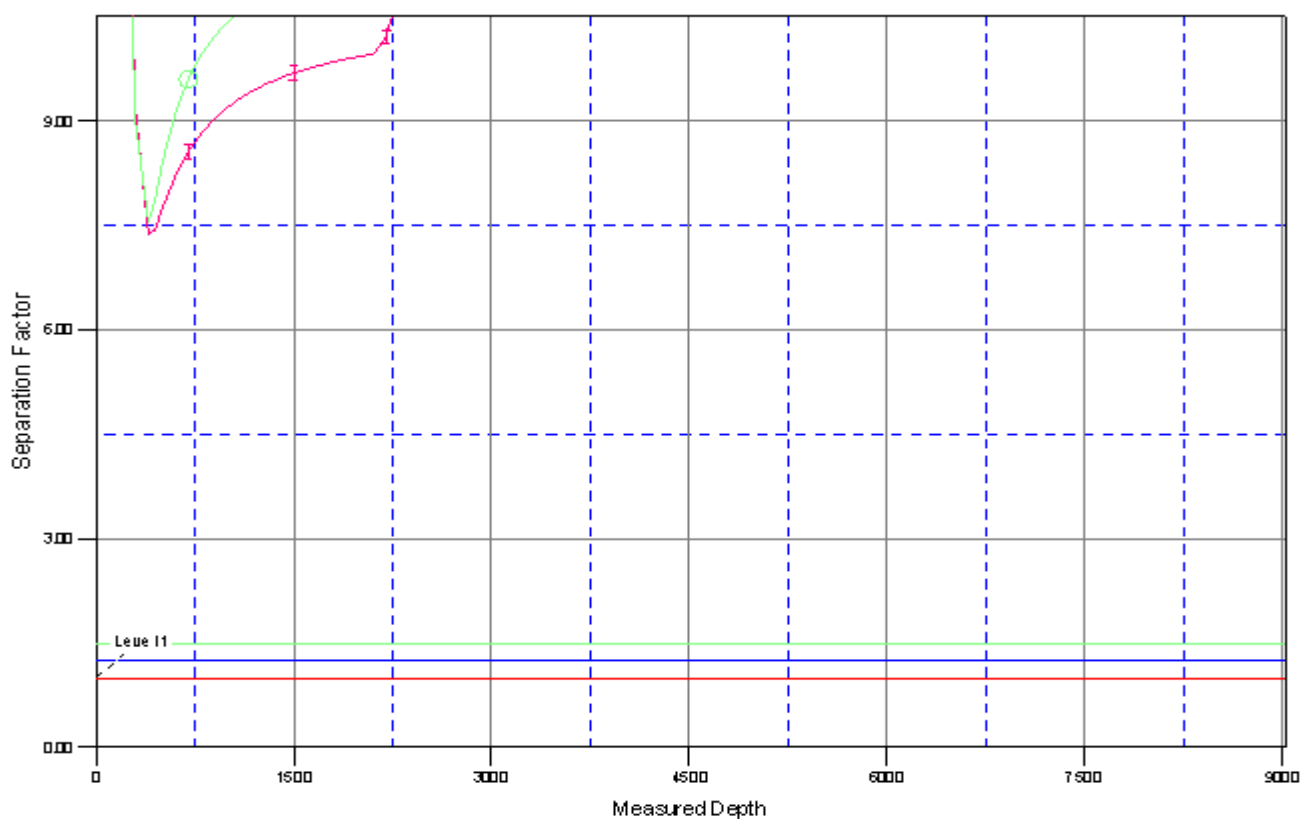

LEGEND

1 RHS \0
0 RHS \0

◆ BONANZA1023-5HBS, BONANZA1023-5HBS, PLAN#1 4-28-10 RHS \0
● BONANZA1023-5BAS, BONANZA1023-5BAS, PLAN#1 4-28-10 RHS \0

✱ Bonanza 1023-6PS EXISTING,
■ Southman Canyon 45 EXISTING

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
 Bonanza 1023-5I4BS/ 1023-5J3AS
 Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
 Surface Use Plan of Operations
 1 of 13

Kerr-McGee Oil & Gas Onshore. L.P.

Bonanza 1023-5I Pad

<u>API #</u>	<u>BONANZA 1023-5G4DS</u>		
	Surface: 1625 FSL / 1048 FEL	NESE	Lot
	BHL: 2643 FNL / 1424 FEL	SWNE	Lot
<u>API #</u>	<u>BONANZA 1023-5I1BS</u>		
	Surface: 1629 FSL / 1039 FEL	NESE	Lot
	BHL: 2491 FSL / 376 FEL	NESE	Lot
<u>API #</u>	<u>BONANZA 1023-5I1CS</u>		
	Surface: 1634 FSL / 1030 FEL	NESE	Lot
	BHL: 2141 FSL / 460 FEL	NESE	Lot
<u>API #</u>	<u>BONANZA 1023-5I4BS</u>		
	Surface: 1639 FSL / 1021 FEL	NESE	Lot
	BHL: 1705 FSL / 475 FEL	NESE	Lot
<u>API #</u>	<u>BONANZA 1023-5J3AS</u>		
	Surface: 1620 FSL / 1056 FEL	NESE	Lot
	BHL: 1690 FSL / 2100 FEL	NWSE	Lot

This Surface Use Plan of Operations (SUPO) or 13-point plan provides site-specific information for the above-referenced wells.

In accordance with Utah Oil & Gas Conservation Rule R649-3-11 pertaining to Directional Drilling, these wells will be directionally drilled. Refer to Topo Map A for directions to the location and Topo Maps A and B for location of access roads within a 2-mile radius.

An on-site meeting was held on May 18, 2010. Present were:

- David Gordon, NRS; Kevin Sadiler, NRS; Ryan Angus, PET Engineer; Steve Strong, Reclamation; Dan Emmett, Wildlife Biologist - BLM;
- John Slaugh, Mitch Batty, Brian Venn, Jacob Dunham, Jake Edmunds, B.J. Reenders - 609 & Timberline Engineering & Land Surveying, Inc.
- Danielle Piernot and Kathy Schneebeck Dulnoan, Regulatory; Brad Burman, Completions; Clay Einerson, Construction; Grizz Oleen, Environmental; Charles Chase, Reclamation; Lovell Young, Drilling, Roger Parry and Ramey Hoopes, Construction

A. Existing Roads:

Existing roads consist of county and improved/unimproved access roads (two-tracks). In accordance with Onshore Order #1, Kerr-McGee will, in accordance with BMPs, improve or maintain existing roads in a condition that is the same as or better than before operations began. New or reconstructed proposed access roads are discussed in Section B.

The existing roads will be maintained in a safe and usable condition. Maintenance for existing roads will continue until final abandonment and reclamation of well pads and/or other facilities, as applicable. Road maintenance will include, but is not limited to, blading, ditching, and/or culvert installation and cleanout. To ensure safe operating conditions, gravel surfacing will be performed where excessive rutting or erosion may occur. Dust control will be performed as necessary to ensure safe operating conditions.

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
Bonanza 1023-5I4BS/ 1023-5J3AS
Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
Surface Use Plan of Operations
2 of 13

Roads, gathering lines and electrical distribution lines will occupy common disturbance corridors where possible. Where available, roadways will be used as the staging area and working space for installation of gathering lines. All disturbances located in the same corridor will overlap each other to the maximum extent possible, while maintaining safe and sound construction and installation practices. Unless otherwise approved or requested in site specific documents, in no case will the maximum disturbance widths of the access road and utility corridors exceed the widths specified in Part D of this document.

All access roads leading to the pad are existing and on lease; therefore do not require a ROW.

** Please refer to Topo B

±225' (0.1 miles) – Section 5 T10S R23E (NE/4 SE/4) – On-lease UTU33433, from the proposed road re-route at the 1023-5I intersection to tie-in to the the county road intersection.

B. New or Reconstructed Access Roads:

All new or reconstructed roads will be located, designed, and maintained to meet the standards of the BLM. BMPs. Described in the BLM's Surface Operating Standards for Oil and Gas Exploration and Development, 4th Edition (Gold Book) (USDI and USDA, 2007) and/or BLM Manual Section 9113 (1985) will be considered in consultation with the BLM in the design, construction, improvement and maintenance of all new or reconstructed roads. If a new road would cross a water of the United States, Kerr-McGee will adhere to the requirements of applicable Nationwide Permits of the Department of Army Corps of Engineers.

Each new well pad or pad expansion may require construction of a new access road and/or de-commissioning of an older road. Plans, routes, and distances for new roads and road improvements are provided in design packages, exhibits and maps for a project. Project-specific maps are submitted to depict the locations of existing, proposed, and/or decommissioned and include the locations for supporting structures, including, but not limited to, culverts, bridges, low water crossings, range infrastructure, and haul routes, as per OSO 1. Designs for cuts and fills, including spoils source and storage areas, are provided with the road designs, as necessary.

Where safety objectives can be met. As applicable, Kerr-McGee may use unimproved and/or two-track roads for lease operations, to lessen total disturbance.

Road designs will be based on the road safety requirements, traffic characteristics, environmental conditions, and the vehicles the road is intended to carry. Generally, newly constructed unpaved lease roads will be crowned and ditched with the running surfaces of the roads approximately 12-18 feet wide and a total road corridor width not to exceed 45 feet, except where noted in the road design for a specific project. Maximum grade will generally not exceed 8%. Borrow ditches will be back sloped 3:1 or less. Construction BMPs will be employed to control onsite and offsite erosion.

Where topography would direct storm water runoff to an access road or well pad, drainage ditches or other common drainage control facilities, such as V- or wing-ditches, will be constructed to divert surface water runoff. Drainage features, including culverts, will be constructed or installed prior to commencing other operations, including drilling or facilities placement. Riprap will be placed at the inlet and outlet at the culvert(s), as necessary.

Prior to construction, new access road(s) will be staked according to the requirements of OSO 1. Construction activity will not be conducted using frozen or saturated materials or during periods when significant watershed damage (e.g. rutting, extensive sheet soil erosion, formation of rills/gullies, etc.) is likely to occur. Vegetative debris will not be placed in or under fill embankments.

New road maintenance will include, but is not limited to, blading, ditching, culvert installation and cleanout, gravel surfacing where excessive rutting or erosion may occur and dust control, as necessary to ensure safe operating

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
 Bonanza 1023-5I4BS/ 1023-5J3AS
 Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
 Surface Use Plan of Operations
 3 of 13

conditions. All vehicular traffic, personnel movement, construction/restoration operations will be confined to the approved area and to existing roadways and/or access routes.

Snow removal will be conducted on an as-needed basis to accommodate safe travel. Snow removal will occur as necessary throughout the year, as will necessary drainage ditch construction. Removed snow may be stored on permitted well pads to reduce hauling distances and/or at the aerial extent of approved disturbance boundaries to facilitate snow removal for the remainder of the season.

If a county road crossing or encroachment permit is needed, it will be obtained prior to construction.

±320' (0.06 miles) – Section 5 T10S R23E (SE/4 SE/4) – On-lease UTU33433, from existing road traveling Northwest to re-route around the Bonanza 1023-5I pad to tie-in to the existing county road intersection.

** Please refer to Topo B

C. Location of Existing Wells:

A) Refer to Topo Map C.

D. Location of Existing and/or Proposed Facilities:

This pad will expand the existing pad for the Bonanza 1023-5PS, which is a producing gas well, and the Southman Canyon 4-5, which is a plugged and abandoned well according to the Utah Division of Oil, Gas and Mining (UDOGM) records on May 25, 2011. Gathering (pipeline) infrastructure will be utilized to collect and transport gas and fluids from the wells which are owned and operated by Kerr McGee Oil and Gas Onshore LP (Kerr-McGee).

Should the well(s) prove productive, production facilities will be installed on the disturbed portion of each well pad. A berm will be constructed completely around production components (typically excluding dehy's and/or separators) that contain fluids (i.e. production tanks, produced liquids tanks). The berms will generally be constructed of compacted subsoil or corrugated metal, and will hold the capacity of the largest tank and have sufficient freeboard to accommodate a 25 year rainfall event. This includes pumping units. Aboveground structures constructed or installed onsite for 6 months or longer, will be painted a flat, non-reflective, earth-tone color chosen at the onsite in coordination with the BLM (typically Shadow Gray). A production facility layout is provided as part of a project-specific APD, ROW or NOS submission.

GAS GATHERING

Please refer to Exhibit B and Topo D- Pad and Pipeline Detail.

The gas gathering pipeline material: Steel line pipe. Surface = Bare pipe. Buried = Coated with fusion bonded epoxy coating (or equivalent). The total gas gathering pipeline distance from the meter to the tie in point is ±820' and the individual segments are broken up as follows:

The following segments are "onlease", no ROW needed.

- ±680' (0.1 miles) – Section 5 T10S R23E (NE/4 SE/4) – On-lease UTU33433, BLM surface, New 6" buried gas gathering pipeline from the first meter house to the edge of the pad. Please refer to Topo D2 - Pad and Pipeline Detail.
- ±30' (0.01 miles) – Section 5 T10S R23E (NE/4 SE/4) – On-lease UTU33433, BLM surface, New 6" buried gas gathering pipeline from the edge of the pad to tie-in to the proposed 8" gas gathering pipeline at the 1023-5P intersection. Please refer to Topo D and Exhibit A, Line 10

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
 Bonanza 1023-5I4BS/ 1023-5J3AS
 Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
 Surface Use Plan of Operations
 4 of 13

±110' (0.02 miles) – Section 5 T10S R23E (NE/4 SE/4) – On-lease UTU33433, BLM surface, New 8" buried gas gathering pipeline from the 1023-5P intersection to the existing 16" buried pipeline. Please refer to Exhibit A, Line 9. This pipeline will be used concurrently with the Bonanza 1023-5P Pad.

LIQUID GATHERING

The total liquid gathering pipeline distance from the separator to the tie in point is ±1,710' and the individual segments are broken up as follows:

The following segments are "onlease", no ROW needed.

- ±680' (0.1 miles) – Section 5 T10S R23E (NE/4 SE/4) – On-lease UTU33433, BLM surface, New 6" buried liquid gathering pipeline from the first meter house to the edge of the pad. Please refer to Topo D2 - Pad and Pipeline Detail.
- ±30' (0.01 miles) – Section 5 T10S R23E (NE/4 SE/4) – On-lease UTU33433, BLM surface, New 6" buried liquid gathering pipeline from the edge of the pad to tie-in to the proposed 6" liquid gathering pipeline at the 1023-5P intersection. Please refer to Topo D and Exhibit B, Line 11.
- ±1,000' (0.2 miles) – Section 5 T10S R23E (NE/4 SE/4) – Lease UTU33433, BLM surface, New 6" buried liquid gathering pipeline from the proposed 6" buried liquid at the 1023-5I intersection to the tie-in at the compressor station. Please refer to Exhibit B, Line 10. This pipeline will be used concurrently with the Bonanza 1023-5P Pad.

Pipeline Gathering Construction

Gathering (pipeline) infrastructure will be utilized to collect and transport gas and fluids from the wells which are owned and operated by Kerr McGee. Gas gathering pipeline(s), gas lift, or liquids pipelines may be constructed to lie on the surface or be buried. Where the pipeline is adjacent to the road or well pad, the road and/or well pad will be utilized for construction activities and staging. The area of disturbance during construction from the edge of road or well pad will typically be 30' in width. Where pipelines run cross country, the width of disturbance will typically be 45 ft for buried lines and 30 ft for surface lines. In addition, Kerr-McGee requests for a permanent 30' disturbance width that will be maintained for the portion adjacent to the road. The need for the 30' permanent disturbance width is for maintenance and repairs. Cross country permanent disturbance width also are required to be 30ft.

Above-ground installation will generally not require clearing of vegetation or blading of the surface, except where safety considerations necessitate earthwork. In some surface pipeline installation instances pipe cannot be constructed where it will lay. In these cases where an above-ground pipeline is constructed parallel and adjacent to a road, it will be welded/fused on the road and then lifted from the road to the pipeline route. In other cases where a pipeline route is not parallel and adjacent to a road (cross-country between sites), it will be welded/fused in place at a well pad, access road, or designated work area and pulled between connection locations with a suitable piece of equipment.

Buried pipelines will generally be installed parallel and adjacent to existing and/or newly constructed roads and within the permitted disturbance corridor. Buried pipelines may vary from 2 inches (typically fuel gas lines) to 24 inches (typically transportation lines) in diameter, but 6 to 16 inches is typical for a buried gas line. The diameter of liquids pipelines may vary from 2 inches to 12 inches, but 6 inches is the typical diameter. Gas lift lines may vary from 2 to 12 inches in diameter, but 6-inch diameter pipes are generally used for gas lift. If two or more pipelines are present (gas gathering, gas lift, and fluids), they will share a common trench where possible.

Typically, to install a buried pipeline, topsoil will be removed, windrowed and placed on the non-working side of the route for later reclamation. Because working room is limited, the spoil may be spread out across the working side and construction will take place on the spoil. The working side of the corridor will be used for pipe stringing, bending, welding and equipment travel. Small areas on the working side displaying ruts or uneven ground will be groomed to facilitate the safe passage of equipment. After the pipelines are installed, spoil will be placed back into the trench, and the topsoil will be redistributed over the disturbed corridor prior to final reclamation. Typical depth of the trench will be 6 feet, but depths may vary

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
Bonanza 1023-5I4BS/ 1023-5J3AS
Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
Surface Use Plan of Operations
5 of 13

according to site-specific conditions (presence of bedrock, etc.). The proposed trench width for the pipeline would range from 18-48 inches.

The pipeline will be welded along the proposed route and lowered into place. Trenching equipment will cut through the soil or into the bedrock and create good backfill, eliminating the need to remove large rocks. The proposed buried pipeline will be visually and radiographically inspected and the entire pipeline will be pneumatically or hydrostatically tested before being placed into service. Routine vehicle traffic will be prevented from using pipeline routes as travel ways by posting signs at the route's intersection with an access road.

The liquid gathering lines will be made of polyethylene or a composite polyethylene/steel or polyethylene/fiberglass that is not subject to internal or external pipe corrosion. The content of the produced fluids to be transferred by the liquid gathering system will be approximately 92% produced water and 8% condensate. Trunk line valve connections for the water gathering system will be below ground but accessible from the surface in order to prevent freezing during winter time.

If pipelines or roads encounter a drainage that could be subject to flooding or surface water during extreme precipitation events, Kerr-McGee will apply all applicable Army Corps mandates as well as the BLM's Hydraulic Considerations for Pipeline Crossings of Stream Channels (BLM Technical Note 423, April 2007). In addition, all stream and drainage crossings will be evaluated to determine the need for stream alteration permits from the State of Utah Division of Water Rights and if necessary, required permits will be secured. Similarly, where a road or pipeline crossing exists the pipe will be butt welded and buried to a depth between 24 and 48 inches or more. Dirt roads will be cut and restored to a condition equivalent to the existing condition. All Uintah County road encroachment and crossing permits, where applicable, will be obtained prior to crossing construction. In no case will pressure testing of pipelines result in discharge of liquids to the surface.

Pipeline signs will be installed along the route to indicate the pipeline proximity, ownership, and to provide emergency contact phone numbers. Above ground valves and lateral T's will be installed at various locations for production integrity and safety purposes.

Upon completion of the proposed buried pipeline, the entire area of disturbance will be reclaimed to the standards proposed in the Green River District Reclamation Guidelines. Please refer to section J for more details regarding final reclamation.

When no longer deemed necessary by the operator, Kerr-McGee or its successor will consult with the BLM, Vernal Field Office before terminating of the use of the pipeline(s).

The Anadarko Completions Transportation System (ACTS) information:

Please refer to Exhibit C for ACTs Lines

Kerr-McGee will use either a closed loop drilling system that will require one pit and one storage area to be constructed on the drilling pad or a traditional drilling operation with one pit. The storage area will be used to contain only the de-watered drill cuttings and will be lined and reclaimed according to traditional pit closure standards. The pit will be constructed to allow for completion operations. The completion operations pit is lined and will be used for the wells drilled on the pad or used as part of our Anadarko Completions Transportation (ACTS) system which is discussed in more detail below. Using the closed loop drilling system will allow Kerr-McGee to decrease the amount of disturbance/footprint on location compared to a single large drilling/completion pit.

If Kerr-McGee does not use a closed loop system, it will construct a drilling reserve pit to contain drill cuttings and for use in completion operations. Depending on the location of the pit, its relation to future drilling locations, the reserve/completion pit will be utilized for the completion of the wells on that pad and/or be used as part of our ACTS system.

Kerr-McGee will use ACTS to optimize the completion processes for multiple pads across the project area which may include up to a section of development. ACTS will facilitate management of frac fluids by utilizing existing reserve pits and temporary, surface-laid aluminum liquids transfer lines between frac locations. The pit will be refurbished as follows

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
Bonanza 1023-5I4BS/ 1023-5J3AS
Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
Surface Use Plan of Operations
6 of 13

when a traditional drill pit is used: mix and pile up drill cuttings with dry dirt, bury the original liner in the pit, walk bottom of pit with cat. Kerr-McGee will reline the pit with a 30 mil liner and double felt padding. The refurbished pit will be the same size or smaller as specified in the originally approved ROW/APD. The pit refurb will be done in a normal procedure and there will be no modification to the pit.

All four sides of the completions pit will be fenced in according to standard pit fencing procedures. Netting will be installed over all pits.

The collected hydrocarbons will be treated and sold at approved sales facilities. A loading rack with drip containment will also be installed where water trucks would unload and load to prevent damage caused from pulling hoses in and out of the pit .

ACTS will require temporarily laying multiple 6" aluminum water transfer lines on the surface between either existing or refurbished reserve pits. Please see the attached ACTS exhibit C for placement of the proposed temporary lines. The temporary aluminum transfer lines will be utilized to transport frac fluid being injected and/or recovered during the completion process and will be laid adjacent to existing access roads or pipeline corridors. Upon completion of the frac operation, the liquids transfer lines will be flushed with fresh water and purged with compressed air. The contents of the transfer lines will be flushed into a water truck for delivery to another ACTS location or a reserve pit.

The volume of frac fluid transported through a water transfer line will vary, but volume is projected to be approximately 1.75 bbls per 50-foot joint. Although the maximum working pressure is 125 psig, the liquids transfer lines will be operated at a pressure of approximately 30 to 40 psig. Kerr-McGee requests to keep the netted pit open for one year from first production of the first produced well on the pad. During this time the surrounding well location completion fluids may be recycled in this pit and utilized for other frac jobs in the area. After one year Kerr-McGee will backfill the pit and reclaim. If the pit is not needed for an entire year it will be backfilled and reclaimed earlier. Kerr-McGee understands that due to the temporary nature of this system, BLM considers this a casual use situation; therefore, no permanent ROW or temporary use plan will need to be issued by the BLM.

E. Location and Types of Water Supply:

Water for drilling and completion operations will be obtained from the following sources:

Permit # 49-2307	JD Field Services	Green River- Section 15, T2N, R22E
Permit # 49-2321	R.N. Industries	White River- Section 2, T10S, R24E
Permit # 49-2319	R.N. Industries	White River- Various Sources
Permit # 49-2320	R.N. Industries	Green River- Section 33, T8S, R23E

Water will be hauled to location over the roads marked on Maps A and B.

No water well is to be drilled on this lease.

F. Construction Materials:

Construction operations will typically be completed with native materials found on location. Construction materials that must be imported to the site (mineral material aggregate, soils or materials suitable for fill/surfacing) will be obtained from a nearby permitted source (described in site-specific documents). No construction materials will be removed from federal lands without prior approval from the BLM. A source location other than an on-location construction site will be designated either via a map or narrative within the project specific materials provided to the BLM.

G. Methods for Handling Waste:

All wastes subject to regulation will be handled in compliance with applicable laws to minimize the potential for leaks or spills to the environment. Kerr-McGee also maintains a Spill Control and Countermeasure Plan, which includes notification requirements, including the BLM, for all reportable spills of oil, produced liquids, and hazardous materials.

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
Bonanza 1023-5I4BS/ 1023-5J3AS
Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
Surface Use Plan of Operations
7 of 13

Any accidental release, such as a leak or spill in excess of the reportable quantity, as established by 40 CFR Part 117.3, will be reported as per the requirements of CERCLA, Section 102 B. If a release involves petroleum hydrocarbons or produced liquids, Kerr-McGee will comply with the notification requirements of NTL-3A. Drill cuttings and/or drilling fluids will be contained in the reserve/frac pit whether a closed loop system is used or not. Cuttings will be buried in pit(s) upon closure. Unless specifically approved by the BLM, no oil or other oil-based drilling additives, chromium/metals-based, or saline muds will be used during drilling. Only fresh water (as specified above), biodegradable polymer soap, bentonite clay, and/or non-toxic additives will be used in the mud system.

Pits will be constructed to minimize the accumulation of surface precipitation runoff into the pit (via appropriate placement of subsoil storage areas and/or construction of berms, ditches, etc). Should unexpected liquid petroleum hydrocarbons (crude oil or condensate) be encountered during drilling, completions or well testing, liquid petroleum hydrocarbons will either be contained in test tanks on the well site or evacuated by vacuum trucks and transported to an approved disposal/sales facility. Should petroleum hydrocarbons unexpectedly be released into a pit, they will be removed as soon as practical but in no case will they remain longer than 72 hours unless an alternate is approved by the BLM. Should timely removal not be feasible, the pit will be netted as soon as practical. Similarly, hydrocarbon removal will take place prior to the closure of the pit, unless authorization is provided for disposal via alternate pit closure methods (e.g. solidification).

The reserve and/or fracture stimulation pit will be lined with an impermeable liner. The liner will be a synthetic material 30 mil or thicker. The bottom and side walls of the pit will be void of any sharp rocks that could puncture the liner. The liner will be installed over smooth fill subgrade that is free of pockets, loose rocks, or other materials (i.e. sand, sifted dirt, bentonite, straw, etc.) that could damage the liner. After evaporation and when dry, the reserve pit liners will be cut off, ripped and/or folded back (as safety considerations allow) as near to the mud surface as possible and buried on location or hauled to a landfill prior to backfilling the pit with a minimum of five feet of soil material.

Where necessary and if conditions (freeboard, etc.) allow, produced liquids from newly completed wells may be temporarily disposed of into pits for a period not to exceed 90 days as per Onshore Order Number 7 (OSO 7). Subsequently, permanent approved produced water disposal methods will be employed in accordance with OSO 7 and/or as described in a Water Management Plan (WMP). Otherwise, fluids disposal locations and associated haul routes, for ROW consideration, are typically depicted on Topo A of individual projects. Revisions to the water source or method of transportation will be subject to written approval from the BLM.

Any additional pits necessary for subsequent operations, such as temporary flare or workover pits, will be contained within the originally approved well pad and disturbance boundaries. Such temporary pits will be backfilled and reclaimed within 180 days of completion of work at a well location.

Pits containing drilling cuttings, mud, and/or completions fluids will be allowed to dry. Any free fluids remaining after one year from reaching total depth, date of completion, and/or determination of inactivity will be removed (as weather conditions allow) to an approved site and the pit reclaimed. Installation and operation of any sprinklers, pumps, and equipment will ensure that water spray or mist does not drift.

No garbage or non-exempt substances as defined by Resource Conservation and Recovery Act (RCRA) subtitle C will be placed in the reserve pit. All refuse (trash and other solid waste including cans, paper, cable, etc.) generated during construction, drilling, completion, and well testing activities will be contained in an enclosed receptacle, removed from the drill locations promptly, and transported to an approved disposal facility. Immediately after removal of the drilling rig, all debris and other waste materials not contained within trash receptacles will be collected and removed from the well location.

For the protection of livestock and wildlife, all open pits (excluding flare pits) will be fenced to prevent wildlife or livestock entry. Total height of pit fencing will be at least 42 inches and corner posts will be cemented and/or braced in such a manner as to keep the fence tight at all times. Standard steel, wood, or pipe posts shall be used between the corner braces. Maximum distance between any 2 fence posts shall be no greater than 16 feet. Siphons, catchments, and absorbent pads

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
Bonanza 1023-5I4BS/ 1023-5J3AS
Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
Surface Use Plan of Operations
8 of 13

will be installed to keep hydrocarbons produced by the drilling rig or other equipment on location from entering the reserve pit. Hydrocarbons, contaminated pads, and/or soils will be disposed of in accordance with state and federal requirements.

Portable, self-contained chemical toilets and/or sewage processing facilities will be provided for human waste disposal. Upon completion of operations, or as required, the toilet holding tanks will be pumped and the contents disposed of in an approved sewage disposal facility. All applicable regulations pertaining to disposal of human and solid waste will be observed.

Materials Management

Hazardous materials above reportable quantities will not be produced by drilling or completing proposed wells or constructing the pipelines/facilities. The term "hazardous materials" as used here means: (1) any substance, pollutant, or containment listed as hazardous under the Comprehensive Environmental Response, Compensation, and Liability Act (CERCLA) of 1980, as amended 42 U.S.C. 9601 et seq., and the regulations issued under CERCLA; and (2) any hazardous waste as defined in RCRA of 1976, as amended. In addition, no extremely hazardous substance, as defined in 40 CFR 355, in threshold planning quantities, would be used, produced, stored, transported, or disposed of while producing any well.

Hazardous materials may be contained in some grease or lubricants, solvents, acids, paint, and herbicides, among others as defined above. Kerr-McGee maintains a file, per 29 CFR 1910.1200 (g) containing current Material Safety Data Sheets (MSDS) for all chemicals, compounds, and/or substances that are used during the course of construction, drilling, completion, and production operations for this project. The transport, use, storage and handling of hazardous materials will follow procedures specified by federal and state regulations. Transportation of hazardous materials to the well location is regulated by the Department of Transportation (DOT) under 49 CFR, Parts 171-180. DOT regulations pertain to the packing, container handling, labeling, vehicle placarding, and other safety aspects.

Potentially hazardous materials used in the development or operation of wells will be kept in limited quantities on well sites and at the production facilities for short periods of time. Chemicals meeting the criteria for being an acutely hazardous material/substance or meet the quantities criteria per BLM Instruction Memorandum No. 93-344 will not be used.

Chemicals subject to reporting under Title III of the Superfund Amendments and Reauthorization Act (SARA) in quantities of 10,000 pounds or more may be produced and/or stored at production facilities (crude oil/condensate, produced water). They may also be kept in limited quantities on drilling sites (barite, diesel fuel, cement, cottonseed hulls etc.) for short periods of time during drilling or completion activities.

Fluids disposal and pipeline/haul routes are depicted on Topo Map A.

Any produced water separated from recoverable condensate from the proposed well will be contained in a water tank and will then be transported by pipeline and/or truck to one of the pre-approved disposal sites:

RNI in Sec. 5 T9S R22E
NBU #159 in Sec. 35 T9S R21E
Ace Oilfield in Sec. 2 T6S R20E
MC&MC in Sec. 12 T6S R19E
Pipeline Facility in Sec. 36 T9S R20E
Goat Pasture Evaporation Pond in SW/4 Sec. 16 T10S R22E
Bonanza Evaporation Pond in Sec. 2 T10S R23E

Or to one of the following Kerr-McGee active Salt Water Disposal (SWD) wells:

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
Bonanza 1023-5I4BS/ 1023-5J3AS
Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
Surface Use Plan of Operations
9 of 13

NBU 159 SWD in Sec. 35 T9S R21E
CIGE 112D SWD in Sec. 19 T9S R21E
CIGE 114 SWD in Sec. 34 T9S R21E
NBU 921-34K SWD in Sec. 34 T9S R21E
NBU 921-33F SWD in Sec. 34 T9S R21E

H. Ancillary Facilities:

No additional ancillary facilities are planned for this location.

I. Well Site Layout:

The location, orientation and aerial extent of each drill pad, reserve/completion/flare pit (for closed loop or non-closed loop operations), access road ingress/egress points, drilling rig, dikes/ditches, existing wells/infrastructure, proposed cuts and fills, and topsoil and spoil material stockpile locations are depicted on the exhibits for each project, where applicable. Site-specific conditions may require slight deviation in actual equipment depending on whether a closed loop system is used. Surface distance may be less if using closed loop. But in either case, the area of disturbance will not exceed the maximum disturbance outlined in the attached exhibits.

For the protection of livestock and wildlife, all open pits and cellars will be fenced to prevent wildlife or livestock entry. Total height of pit fencing will be at least 42 inches and corner posts will be cemented and/or braced in such a manner as to keep the fence tight at all times. Standard steel, wood, or pipe posts shall be used between the corner braces. Maximum distance between any 2 fence posts shall be no greater than 16 feet.

Each well will utilize either a centralized tank battery, centralized fluids management system, or have tanks installed on its pad. Production/ Produced Liquid tanks will be constructed, maintained, and operated to prevent unauthorized surface or subsurface discharges of liquids and to prevent livestock or wildlife entry. The tanks will be kept reasonably free from surface accumulations of liquid hydrocarbons. The tanks are not to be used for disposal of liquids from additional sources without prior approval of BLM.

J. Plans for Surface Reclamation:

The surface reclamation will be undertaken in two phases: interim and final. Interim reclamation is conducted following well completion and extends through the period of production. Interim reclamation is for the area of the well pad that is not required for production activities. Final reclamation is conducted following well plugging/conversion and/or facility abandonment processes.

Reclamation activities in both phases may include but is not limited to the re-contouring or re-configuration of topographic surfaces, restoration of drainage systems, segregation of spoils materials, minimizing surface disturbance, re-evaluating backfill requirements, pit closure, topsoil redistribution, soil treatments, seeding and weed control.

Interim Reclamation

Interim reclamation may include pit evaporation, fluid removal, pit solidification, re-contouring, ripping, spreading top soil, seeding, and/or weed control. Interim reclamation will be performed in accordance with OSO 1, or written notification will be provided to the BLM for approval. Where feasible, drilling locations, reserve pits, or access routes not utilized for production operations will be re-contoured to a natural appearance.

Interim re-contouring involves bringing all construction material from cuts and fills back onto the well pad and site and reestablishing the natural contours where desirable and practical. Fill and stockpiled spoils no longer necessary to the operation will be spread on the cut slopes and covered with stockpiled topsoil. All stockpiled top soils will be used for

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
Bonanza 1023-5I4BS/ 1023-5J3AS
Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
Surface Use Plan of Operations
10 of 13

interim reclamation where practical to maintain soil viability. Where possible, the land surface will be left “rough” after re-contouring to ensure that the maximum surface area will be available to support the reestablishment of vegetative cover.

A reserve pit, upon being allowed to dry, will be backfilled and compacted with cover materials that are void of any topsoil, vegetation, large stones, rocks or foreign objects. Soils that are moisture laden, saturated, or partially/completely frozen will not be used for backfill or cover. The pit area will be mounded to allow for settling and to promote positive surface drainage away from the pit. Disposal of pit fluids and linings is discussed in Section G.

Final Reclamation

Final reclamation will be performed for unproductive wells and after the end of the life of a productive well. As soon as practical after the conclusion of drilling and testing operations, unproductive drill holes will be plugged and abandoned (P&A). Site and road reclamation will commence following plugging. In no case will reclamation at non-producing locations be initiated later than six (6) months from the date a well is plugged. A joint inspection of the disturbed area to be reclaimed may be requested by Kerr-McGee. The primary purpose of this inspection will be to review the existing conditions, or agree upon a revised final reclamation and abandonment plan. The BLM will be notified prior to commencement of reclamation operations. A Notice of Intent to Abandon will be filed for final recommendations regarding surface reclamation.

After plugging, all wellhead equipment that is no longer needed will be removed, and the well site will be reclaimed. Final contouring will blend with and follow as closely as practical the natural terrain and contours of the original site and surrounding areas. After re-contouring the site to the approximate contour that existed prior to pad construction, final grading will be conducted over the entire surface of the well site and access road. The area will be ripped to a depth of 18 to 24 inches on 18 to 24-inch centers, where practical. The surface soil material will be pitted with small depressions to form longitudinal depressions 12 to 18 inches deep, where practical. The entire area will be uniformly covered with the depressions constructed perpendicular to the natural flow of water.

Reclamation of roads will be performed at the discretion of the BLM. All unnecessary surface equipment and structures (e.g. cattle guards) and water control structures (e.g. culverts, drainage pipes) not needed to facilitate successful reclamation will be removed during final reclamation. Roads that will be reclaimed will be ripped to a depth of 18 inches where practical, re-contoured to approximate the original contour of the ground and seeded in accordance with the seeding specifications of the BLM.

Upon successfully completing reclamation of a P&A location, a Final Abandonment Notice will be submitted to the BLM.

Measures Common to Interim and Final Reclamation

Soil preparation will be conducted using a disk for areas in need of more soil preparation following site preparation. This will provide primary soil tillage to a depth no greater than 6 inches. Prior to reseeding, compacted areas will be scarified by ripping or chiseling to loosen compacted soils, promote water infiltration, and improve soil aeration and root penetration.

Seeding will occur year-round as conditions allow and will typically be accomplished through the use of a no-till rangeland style seed drill with a “picker box” in order to seed “fluffy” seed. Where drill seeding is not the preferred method, seed will be broadcast and then raked into the ground at double the rate of drill seeding. Seed mixes appropriate to the native plant community as determined and specified for each project location based on the site specific soils will be used for re-vegetation. The seed mixes will be selected from a list provided by or approved by the BLM, or a specific seed mix will be proposed by Kerr-McGee to the BLM and used after its approval. The selected specific seed mix for each well location and road segment will be utilized while performing interim and final reclamation for each project. All seed will be certified and tags will be maintained by Kerr-McGee. Every effort will be made to obtain “cheat grass free seed”.

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
 Bonanza 1023-5I4BS/ 1023-5J3AS
 Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
 Surface Use Plan of Operations
 11 of 13

Seed Mix to be used for Well Site, Access Road, and Pipeline (as applicable):

Bonanza Area Mix	Pure Live Seed lbs/acre
Crested Wheat (Hycrest)	2
Bottlebrush Squirreltail	1
Western Wheatgrass	1
Indian Ricegrass	1
Fourwing Saltbush	2
Shadscale	2
Forage Kochia	0.25
Rocky Mountain Bee	0.5
Total	9.75

Additional soil amendments and/or stabilization may be required on sites with poor soils and/or excessive erosion potential. Where severe erosion can become a problem and/or the use of machinery is not practical, seed will be hand broadcast and raked with twice the specified amount of seed. Slopes will be stabilized using materials specifically designed to prevent erosion on steep slopes and hold seed in place so vegetation can become permanently established. These materials will include, but are not limited to: erosion control blankets, hydro-mulch, and/or bonded fiber matrix at a rate to achieve a minimum of 80 percent soil coverage. Soil amendments such as "Sustain" (an organic fertilizer that will be applied at the rate 1,800 – 2,100 lbs/acre with seed) may also be dry broadcast or applied with hydro-seeding equipment.

Weed Control

All weed management will be done in accordance with the Vernal BLM Surface Disturbance Weed Policy. Noxious weeds will be controlled, as applicable, on project areas. Monitoring and management of noxious and/or invasive weeds of concern will be completed annually until the project is deemed successfully reclaimed by the surface management agency and/or owner according to the Anadarko Integrated Weed Management Plan. Noxious weed infestations will be mapped using a GPS unit and submitted to the BLM with information required in the Vernal BLM Surface Disturbance Weed Policy. If herbicide is to be applied it will be done according to an approved Pesticide Use Permit (PUP), inclusive of applicable locations. All pesticide applications will be recorded using a Pesticide Application Record (PAR) and will be submitted along with a Pesticide Use Report (PUR) annually prior to Dec. 31.

Monitoring

Monitoring of reclaimed project areas will be completed annually during the growing season and actions to ensure reclamation success will be taken as needed. During the first two growing seasons an ocular methodology will be used to determine the success of the reclamation activities. During the 3rd growing season a 200 point line intercept (quantitative) methodology will be used to obtain basal cover. The goal is to have the reclaimed area reach 30% basal cover when compared to the reference site. If after three growing seasons the area has not reached 30% basal cover, additional reclamation activities may be necessary. Monitoring will continue until the reclaimed area reaches 75% basal cover of desirable vegetation when compared to the reference site. (Green River District Reclamation Guidelines)

All monitoring reports will be submitted electronically to the Vernal BLM in the form of a geo-database no later than March 1st of the calendar year following the data collection.

K. Surface/Mineral Ownership:

United States of America
 Bureau of Land Management
 170 South 500 East
 Vernal, UT 84078
 (435)781-4400

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
 Bonanza 1023-5I4BS/ 1023-5J3AS
 Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
 Surface Use Plan of Operations
 12 of 13

L. Other Information:

Onsite Specifics:

- Facilities: Will be painted Shadow Grey
- Top Soil: Need to save 6" topsoil

Cultural and Paleontological Resources

All personnel are strictly prohibited from collecting artifacts, any paleontological specimens or fossils, and from disturbing any significant cultural resources in the area. If artifacts, fossils, or any culturally sensitive materials are exposed or identified in the area of construction, all construction operations that would affect the newly discovered resource will cease, and Kerr-McGee will provide immediate notification to the BLM.

Resource Reports:

A Class I literature survey was completed on April 23, 2010 by Montgomery Archaeological Consultants, Inc (MOAC). For additional details please refer to report MOAC 10-056.

A paleontological reconnaissance survey was completed on May 13, 2010 by SWCA Environmental Consultants. For additional details please refer to report UT10-14314-13.

Biological field survey was completed on April 21, 2010 by Grasslands Consulting, Inc (GCI). For additional details please refer to report GCI-205.

Proposed Action Annual Emissions Tables:

Table 1: Proposed Action Annual Emissions (tons/year) ¹			
Pollutant	Development	Production	Total
NO _x	3.8	0.12	3.92
CO	2.2	0.11	2.31
VOC	0.1	4.9	5
SO ₂	0.005	0.0043	0.0093
PM ₁₀	1.7	0.11	1.81
PM _{2.5}	0.4	0.025	0.425
Benzene	2.2E-03	0.044	0.046
Toluene	1.6E-03	0.103	0.105
Ethylbenzene	3.4E-04	0.005	0.005
Xylene	1.1E-03	0.076	0.077
n-Hexane	1.7E-04	0.145	0.145
Formaldehyde	1.3E-02	8.64E-05	1.31E-02

¹ Emissions include 1 producing well and associated operations traffic during the year in which the project is developed

Table 2: Proposed Action versus 2012 WRAP Phase III Emissions Inventory Comparison			
Species	Proposed Action Production Emissions (ton/yr)	2012 Uintah Basin Emission Inventory ^a (ton/yr)	Percentage of Proposed Action to WRAP Phase III
NO _x	19.6	16,547	0.12%
VOC	25	127,495	0.02%

^a http://www.wrapair.org/forums/ogwg/PhaseIII_Inventory.html

Uintah Basin Data

10/12/2011

RECEIVED: October 17, 2011

Bonanza 1023-5G4DS/ 1023-5I1BS/ 1023-5I1CS
Bonanza 1023-5I4BS/ 1023-5J3AS
Kerr-McGee Oil Gas Onshore, L.P.

Bonanza 1023-5I Pad
Surface Use Plan of Operations
13 of 13

M. Lessee's or Operators' Representative & Certification:

Gina T. Becker
Regulatory Analyst II
Kerr-McGee Oil & Gas Onshore LP
PO Box 173779
Denver, CO 80217-3779
(720) 929-6086

Tommy Thompson
General Manager, Drilling
Kerr-McGee Oil & Gas Onshore LP
PO Box 173779
Denver, CO 80217-3779
(720) 929-6724

Certification: All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws, regulations, Onshore Oil and Gas Orders, the approved Plan of Operations, and any applicable Notice to Lessees.

The Operator will be fully responsible for the actions of its subcontractors. A complete copy of the approved "Application for Permit to Drill" will be furnished to the field representative(s) to ensure compliance and shall be on location during all construction and drilling operations.

Kerr-McGee Oil & Gas Onshore LP is considered to be the operator of the subject well. Kerr-McGee Oil & Gas Onshore LP agrees to be responsible under terms and conditions of the lease for the operations conducted upon leased lands.

Bond coverage pursuant to 43 CFR 3104 for lease activities is being provided by Bureau of Land Management Nationwide Bond WYB000291.

I hereby certify that I, or persons under my supervision, have inspected the proposed drill site and access route, that I am familiar with the conditions that currently exist; that I have full knowledge of the State and Federal laws applicable to this operation; that the statements made in this plan are, to the best of my knowledge, true and correct; and the work associated with the operations proposed herein will be performed in conformity with this APD package and the terms and conditions under which it is approved. I also certify that I, or the company I represent, am responsible for operations conducted under this application. These statements are subject to the provisions of 18 U.S.C. 1001 for the filing of false statements.





Gina T. Becker

October 12, 2011

Date

Map Produced by Diana Mason

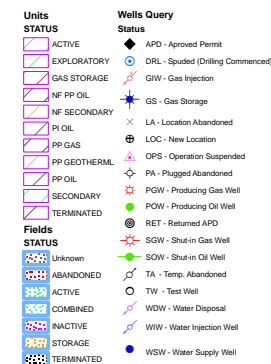

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 10/17/2011**API NO. ASSIGNED:** 43047520580000**WELL NAME:** BONANZA 1023-5G4DS**OPERATOR:** KERR-MCGEE OIL & GAS ONSHORE, L.P. (N2995)**PHONE NUMBER:** 720 929-6086**CONTACT:** Gina Becker**PROPOSED LOCATION:** NESE 05 100S 230E**Permit Tech Review:** ☒**SURFACE:** 1625 FSL 1048 FEL**Engineering Review:** ☒**BOTTOM:** 2643 FNL 1424 FEL**Geology Review:** ☒**COUNTY:** UINTAH**LATITUDE:** 39.97516**LONGITUDE:** -109.34509**UTM SURF EASTINGS:** 641317.00**NORTHINGS:** 4426312.00**FIELD NAME:** NATURAL BUTTES**LEASE TYPE:** 1 - Federal**LEASE NUMBER:** UTU33433**PROPOSED PRODUCING FORMATION(S):** WASATCH-MESA VERDE**SURFACE OWNER:** 1 - Federal**COALBED METHANE:** NO**RECEIVED AND/OR REVIEWED:**☒ **PLAT**☒ **Bond:** FEDERAL - WYB000291☐ **Potash**☐ **Oil Shale 190-5**☐ **Oil Shale 190-3**☐ **Oil Shale 190-13**☒ **Water Permit:** 43-8496☐ **RDCC Review:**☐ **Fee Surface Agreement**☒ **Intent to Commingle****Commingle Approved****LOCATION AND SITING:**☐ **R649-2-3.****Unit:**☐ **R649-3-2. General**☐ **R649-3-3. Exception**☒ **Drilling Unit****Board Cause No:** Cause 179-14**Effective Date:** 6/12/2008**Siting:** 460' Fr Ext Drl Unit Boundary☒ **R649-3-11. Directional Drill****Comments:** Presite Completed**Stipulations:**
3 - Commingle - ddoucet
4 - Federal Approval - dmason
15 - Directional - dmason**RECEIVED: October 26, 2011**



GARY R. HERBERT
Governor

GREGORY S. BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: BONANZA 1023-5G4DS

API Well Number: 43047520580000

Lease Number: UTU33433

Surface Owner: FEDERAL

Approval Date: 10/26/2011

Issued to:

KERR-MCGEE OIL & GAS ONSHORE, L.P., P.O. Box 173779, Denver, CO 80217

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 179-14. The expected producing formation or pool is the WASATCH-MESA VERDE Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

Commingling:

In accordance with Board Cause No. 179-14, commingling of the production from the Wasatch formation and the Mesaverde formation in this well is allowed.

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)
OR

submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <http://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "John Rogers", written over a horizontal line.

For John Rogers
Associate Director, Oil & Gas

UDOGMUNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT**RECEIVED**

JUL 22 2011

FORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010**BLM**
APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU33433
1b. Type of Well: <input type="checkbox"/> Oil Well <input checked="" type="checkbox"/> Gas Well <input type="checkbox"/> Other <input type="checkbox"/> Single Zone <input checked="" type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator KERR-MCGEE OIL & GAS ONSHORE Contact: GINA T BECKER Email: GINA.BECKER@ANADARKO.COM		7. If Unit or CA Agreement, Name and No.
3a. Address P.O. BOX 173779 DENVER, CO 80202-3779	3b. Phone No. (include area code) Ph: 720-929-6086 Fx: 720-929-7086	8. Lease Name and Well No. BONANZA 1023-5G4DS
4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NESE 1625FSL 1048FEL 39.975180 N Lat, 109.345065 W Lon At proposed prod. zone SWNE 2643FNL 1424FEL 39.977990 N Lat, 109.346403 W Lon		9. API Well No. 43-047 52058
14. Distance in miles and direction from nearest town or post office* APPROXIMATELY 48 MILES SOUTHEAST OF VERNAL, UTAH		10. Field and Pool, or Exploratory BONANZA
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 1424	16. No. of Acres in Lease 1923.00	11. Sec., T., R., M., or Blk. and Survey or Area Sec 5 T10S R23E Mer SLB
17. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 1787	18. Proposed Depth 8588 MD 8426 TVD	12. County or Parish UINTAH
21. Elevations (Show whether DF, KB, RT, GL, etc.) 5299 GL	22. Approximate date work will start 12/31/2011	13. State UT
23. Estimated duration 60-90 DAYS		17. Spacing Unit dedicated to this well

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- | | |
|---|--|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature (Electronic Submission)	Name (Printed/Typed) GINA T BECKER Ph: 720-929-6086	Date 07/05/2011
Title REGULATORY ANALYST II		
Approved by (Signature) 	Name (Printed/Typed) Jerry Kenczka	Date MAR 02 20
Title Assistant Field Manager Lands & Mineral Resources	Office VERNAL FIELD OFFICE	

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

CONDITIONS OF APPROVAL ATTACHED

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

Electronic Submission #112239 verified by the BLM Well Information System
For KERR-MCGEE OIL & GAS ONSHORE, sent to the Vernal**NOTICE OF APPROVAL
RECEIVED**

MAR 14 2012

DIV. OF OIL, GAS & MINING

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company:	Kerr McGee Oil & Gas Onshore, LP	Location:	NESE, Sec. 5, T10S, R23E (S) SWNE, Sec. 5, T10S, R23E (B)
Well No:	Bonanza 1023-5G4DS	Lease No:	UTU-33433
API No:	43-047-52058	Agreement:	N/A

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings to: ut_vn_opreport@blm.gov .
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

SITE SPECIFIC COAs

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horse power must not emit more than 2 grams of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower-hour.
- All new and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gram of NO_x per horsepower-hour.
- Construction or drilling is not allowed for the Bonanza 1023-5M and Bonanza 1023-5P pads from January 1 – August 31 to minimize impacts during golden eagle nesting.
- If it is anticipated that construction or drilling will occur during the given timing restriction, a BLM or qualified biologist shall be notified to conduct surveys for raptors. Depending upon the results of the surveys, permission to proceed may or may not be granted by the Authorized Officer.
- All reclamation will comply with the Green River Reclamation Guidelines
- All vehicles and equipment shall be cleaned either through power-washing, or other approved method, if the vehicles or equipment were previously operated outside the Uinta Basin, to prevent weed seed introduction.
- All disturbance areas shall be monitored for noxious weeds annually, for a minimum of three growing seasons following completion of project or until desirable vegetation is established
- Noxious and invasive weeds will be controlled throughout the area of project disturbance.

- Noxious weeds will be inventoried and reported to BLM in the annual reclamation report. Where an integrated pest management program is applicable, coordination has been undertaken with the state and local management program (if existing). A copy of the pest management plan will be submitted for each project.
- A pesticide use permit (PUP) will be obtained for the project, if applicable.
- A permitted paleontologist is to be present to monitor construction at well pads 1023-5C, 5D, 5K, 5L, 5M and 5P during all surface disturbing activities: examples include the following building of the well pad, access road, and pipelines.
- The best method to avoid entrainment is to pump from an off-channel location – one that does not connect to the river during high spring flows. An infiltration gallery constructed in a BLM and Service approved location is best.
- If the pump head is located in the river channel where larval fish are known to occur, the following measures apply:
 - a. do not situate the pump in a low-flow or no-flow area as these habitats tend to concentrate larval fishes;
 - b. limit the amount of pumping, to the greatest extent possible, during that period of the year when larval fish may be present (April 1 to August 31); and
 - c. limit the amount of pumping, to the greatest extent possible, during the pre-dawn hours as larval drift studies indicate that this is a period of greatest daily activity.
- Screen all pump intakes with 3/32" mesh material.
- Approach velocities for intake structures will follow the National Marine Fisheries Service's document "Fish Screening Criteria for Anadromous Salmonids". For projects with an in-stream intake that operate in stream reaches where larval fish may be present, the approach velocity will not exceed 0.33 feet per second (ft/s).
- Report any fish impinged on the intake screen to the Service (801.975.3330) and the Utah Division of Wildlife Resources:
 - Northeastern Region
 - 152 East 100 North, Vernal, UT 84078
 - Phone: (435) 781-9453
- Discovery Stipulation: Re-initiation of section 7 consultation with the USFWS will be sought immediately if any loss of plants or occupied habitat for Pariette cactus or Uinta Basin hookless cactus is anticipated as a result of project activities.

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DRILLING PLAN COA's:

- A copy of Kerr McGee's Standard Operating Practices (SOP version: dated 7/17/08 and approved 7/28/08) shall be on location.
- Surface casing cement shall be brought to surface.
- Production casing cement shall be brought 200' up and into the surface casing.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned.
- Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.

- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.
- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (1/4, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

BLM - Vernal Field Office - Notification Form

Operator KERR-McGEE OIL & GAS Rig Name/# BUCKET RIG
Submitted By J. Scharnowske Phone Number 720.929.6304
Well Name/Number BONANZA 1023-5G4DS
Qtr/Qtr NESE Section 5 Township 10S Range 23E
Lease Serial Number UTU33433
API Number 4304752058

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 05/21/2012 09:00 HRS AM ☐ PM ☐

Casing – Please report time casing run starts, not cementing times.

- ☒ Surface Casing
☐ Intermediate Casing
☐ Production Casing
☐ Liner
☐ Other

Date/Time 06/08/2012 08:00 HRS AM ☐ PM ☐

BOPE

- ☐ Initial BOPE test at surface casing point
☐ BOPE test at intermediate casing point
☐ 30 day BOPE test
☐ Other

RECEIVED

MAY 18 2012

DIV. OF OIL, GAS & MINING

Date/Time _____ AM ☐ PM ☐

Remarks ESTIMATED DATE AND TIME. PLEASE CONTACT KENNY GATHINGS AT

435.828.0986 OR LOVEL YOUNG AT 435.781.7051

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU33433
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: KERR-MCGEE OIL & GAS ONSHORE, L.P.		7. UNIT or CA AGREEMENT NAME:
3. ADDRESS OF OPERATOR: P.O. Box 173779 1099 18th Street, Suite 600, Denver, CO, 80217 3779		8. WELL NAME and NUMBER: BONANZA 1023-5G4DS
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1625 FSL 1048 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESE Section: 05 Township: 10.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047520580000
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		9. FIELD and POOL or WILDCAT: NATURAL BUTTES
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 5/16/2012 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<div style="display: flex; flex-wrap: wrap;"> <div style="width: 33%;"> <input type="checkbox"/> ACIDIZE <input checked="" type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION </div> <div style="width: 33%;"> <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER </div> <div style="width: 33%;"> <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/> </div> </div>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. THE OPERATOR REQUESTS APPROVAL FOR A FIT WAIVER, A CLOSED LOOP DRILLING OPTION, AND A PRODUCTION CASING CHANGE. ALL OTHER ASPECTS OF THE PREVIOUSLY APPROVED DRILLING PLAN WILL NOT CHANGE. PLEASE SEE THE ATTACHMENT. THANK YOU.		
Accepted by the Utah Division of Oil, Gas and Mining Date: May 24, 2012 By:		
NAME (PLEASE PRINT) Cara Mahler		PHONE NUMBER 720 929-6029
SIGNATURE N/A		TITLE Regulatory Analyst I
DATE 5/16/2012		

Kerr-McGee Oil & Gas Onshore. L.P.**BONANZA 1023-5G4DS**

Surface: 1625 FSL / 1048 FEL NESE
BHL: 2643 FNL / 1424 FEL SWNE

Section 5 T10S R23E

Uintah County, Utah
Mineral Lease: UTU-33433

ONSHORE ORDER NO. 1**DRILLING PROGRAM**

1. & 2. **Estimated Tops of Important Geologic Markers:**
Estimated Depths of Anticipated Water, Oil, Gas, or Mineral Formations:

<u>Formation</u>	<u>Depth</u>	<u>Resource</u>
Uinta	0 - Surface	
Green River	1,253'	
Birds Nest	1,502'	Water
Mahogany	1,860'	Water
Wasatch	4,218'	Gas
Mesaverde	6,258'	Gas
Sego	8,426'	Gas
TVD	8,426'	
TD	8,588'	

3. **Pressure Control Equipment** (Schematic Attached)

Please refer to the attached Drilling Program

4. **Proposed Casing & Cementing Program:**

Please refer to the attached Drilling Program

5. **Drilling Fluids Program:**

Please refer to the attached Drilling Program

6. **Evaluation Program:**

Please refer to the attached Drilling Program

7. Abnormal Conditions:

Maximum anticipated bottom hole pressure calculated at 8426' TVD, approximately equals
5,393 psi (0.64 psi/ft = actual bottomhole gradient)

Maximum Anticipated Bottom Hole Pressure (MABHP) = Pore Pressure at TD

Maximum anticipated surface pressure equals approximately 3,527 psi (bottom hole pressure
minus the pressure of a partially evacuated hole calculated at 0.22 psi/foot, per Onshore Order No. 2).

Per Onshore Order No. 2 - Max Anticipated Surf. Press.(MASP) = (Pore Pressure at next csg point-

(0.22 psi/ft-partial evac gradient x TVD of next csg point))

8. Anticipated Starting Dates:

Drilling is planned to commence immediately upon approval of this application.

9. Variances:

Please refer to the attached Drilling Program.

Onshore Order #2 – Air Drilling Variance

Kerr-McGee Oil & Gas Onshore LP (KMG) respectfully requests a variance to several requirements associated with air drilling outlined in Onshore Order 2

- Blowout Prevention Equipment (BOPE) requirements;
- Mud program requirements; and
- Special drilling operation (surface equipment placement) requirements associated with air drilling.

This Standard Operating Practices addendum provides supporting information as to why KMG current air drilling practices for constructing the surface casing hole should be granted a variance to Onshore Order 2 air drilling requirements.

The reader should note that the air rig is used only to construct a stable surface casing hole through a historically difficult lost circulation zone. A conventional rotary rig follows the air rig, and is used to drill and construct the majority of the wellbore.

More notable, KMG has used the air rig layout and procedures outlined below to drill the surface casing hole in approximately 675 wells without incident of blow out or loss of life.

Background

In a typical well, KMG utilizes an air rig for drilling the surface casing hole, an interval from the surface to surface casing depths, which varies in depth from 1,700 to 2,800 feet. The air rig drilling operation does not drill through productive or over pressured formations in KMG field, but does penetrate the Uinta and Green River Formations. The purpose of the air drilling operation is to overcome the severe loss circulation zone in the Green River known as the Bird's Nest while creating a stable hole for the surface casing. The surface casing hole is generally drilled to approximately 500 feet below the Bird's Nest.

Before the surface air rig is mobilized, a rathole rig is utilized to set and cement conductor pipe through a competent surface formation. Generally, the conductor is set at 40 feet. In some cases, conductor may be set deeper in areas that the surface formation is not found competent. This rig also drills the rat and mouse holes in preparation for the surface casing and production string drilling operations.

The air rig is then mobilized to drill the surface casing hole by drilling a 12 1/4 inch hole for the first 200 feet, then will drill a 11 inch hole to just above the Bird's Nest interval with an air hammer. The hammer is then tripped and replaced with a 11 inch tri-cone bit. The tri-cone bit is used to drill to the surface casing point, approximately 500 feet below the loss circulation zone (Bird's Nest). The 8-5/8 inch surface casing is then run and cemented in place, thereby isolating the lost circulation zone.

KMG fully appreciates Onshore Order 2 well control and safety requirements associated with a typical air drilling operations. However, the requirements of Onshore Order 2 are excessive with respect to the air rig layout and drilling operation procedures that are currently in practice to drill and control the surface casing hole in KMG Fields.

Variance for BOPE Requirements

The air rig operation utilizes a properly lubricated and maintained air bowl diverter system which diverts the drilling returns to a six-inch blooie line. The air bowl is the only piece of BOPE equipment which is installed during drilling operations and is sufficient to contain the air returns associated with this drilling operation. As was discussed earlier, the drilling of the surface hole does not encounter any over pressured or productive zones, and as a result standard BOPE equipment should not be required. In addition, standard drilling practices do not support the use of BOPE on 40 feet of conductor pipe.

Variance for Mud Material Requirements

Onshore Order 2 also states that sufficient quantities of mud materials shall be maintained or readily accessible for the purpose of assuring adequate well control. Once again, the surface hole drilling operations does not encounter over pressured or productive intervals, and as a result there is not a need to control pressure in the surface hole with a mud system. Instead of mud, the air rigs utilize water from the reserve pit for well control, if necessary. A skid pump which is located near the reserve pit (see attachment) will supply the water to the well bore.

Variance for Special Drilling Operation (surface equipment placement) Requirements

Onshore Order 2 requires specific safety distances or setbacks for the placement of associated standard air drilling equipment, wellbore, and reserve pits. The air rigs used to drill the surface holes are not typical of an air rig used to drill a producing hole in other parts of the US. These are smaller in nature and designed to fit a KMG location. The typical air rig layout for drilling surface hole in the field is attached.

Typically the blooie line discharge point is required to be 100 feet from the well bore. In the case of a KMG well, the reserve pit is only 45 feet from the rig and is used for the drill cuttings. The blooie line, which transports the drill cuttings from the well to the reserve pit, subsequently discharges only 45 feet from the well bore.

Typically the air rig compressors are required to be located in the opposite direction from the blooie line and a minimum of 100 feet from the well bore. At the KMG locations, the air rig compressors are approximately 40 feet from the well bore and approximately 60 feet from the blooie line discharge due to the unique air rig design. The air compressors (see attachment) are located on the rig (1250 cfm) and

on a standby trailer (1170 cfm). A booster sits between the two compressors and boosts the output from 350 psi to 2000 psi. The design does put the booster and standby compressor opposite from the blooie line.

Lastly, Onshore Order 2 addresses the need for an automatic igniter or continuous pilot light on the blooie line. The air rig does not utilize an igniter as the surface hole drilling operation does not encounter productive formations.

Variance for FIT Requirements

KMG also respectfully requests a variance to Onshore Order 2, Section III, Part Bi, for the pressure integrity test (PIT, also known as a formation integrity test (FIT)). This well is not an exploratory well and is being drilled in an area where the formation integrity is well known. Additionally, when an FIT is run with the mud weight as required, the casing shoe frequently breaks down and causes subsequent lost circulation when drilling the entire depth of the well.

Conclusion

The air rig operating procedures and the attached air rig layout have effectively maintained well control while drilling the surface holes in KMG Fields. KMG respectfully requests a variance from Onshore Order 2 with respect to air drilling well control requirements as discussed above.

10. Other Information:


Please refer to the attached Drilling Program.

BONANZA 1023-5G4DS

Drilling Program
5 of 7

KERR-McGEE OIL & GAS ONSHORE LP DRILLING PROGRAM

COMPANY NAME	KERR-McGEE OIL & GAS ONSHORE LP					DATE	May 16, 2012		
WELL NAME	BONANZA 1023-5G4DS					TD	8,426'	TVD	8,588' MD
FIELD	Natural Buttes		COUNTY	Uintah	STATE	Utah	FINISHED ELEVATION		5296.8
SURFACE LOCATION	NESE	1625 FSL	1048 FEL	Sec 5	T 10S	R 23E			
BTM HOLE LOCATION	Latitude:	39.975180	Longitude:	-109.345065			NAD 83		
	SWNE	2643 FNL	1424 FEL	Sec 5	T 10S	R 23E			
OBJECTIVE ZONE(S)	Latitude:	39.977990	Longitude:	-109.346403			NAD 83		
	Wasatch/Mesaverde								
ADDITIONAL INFO	Regulatory Agencies: BLM (Minerals), BLMM (Surface), UDOGM Tri-County Health Dept.								

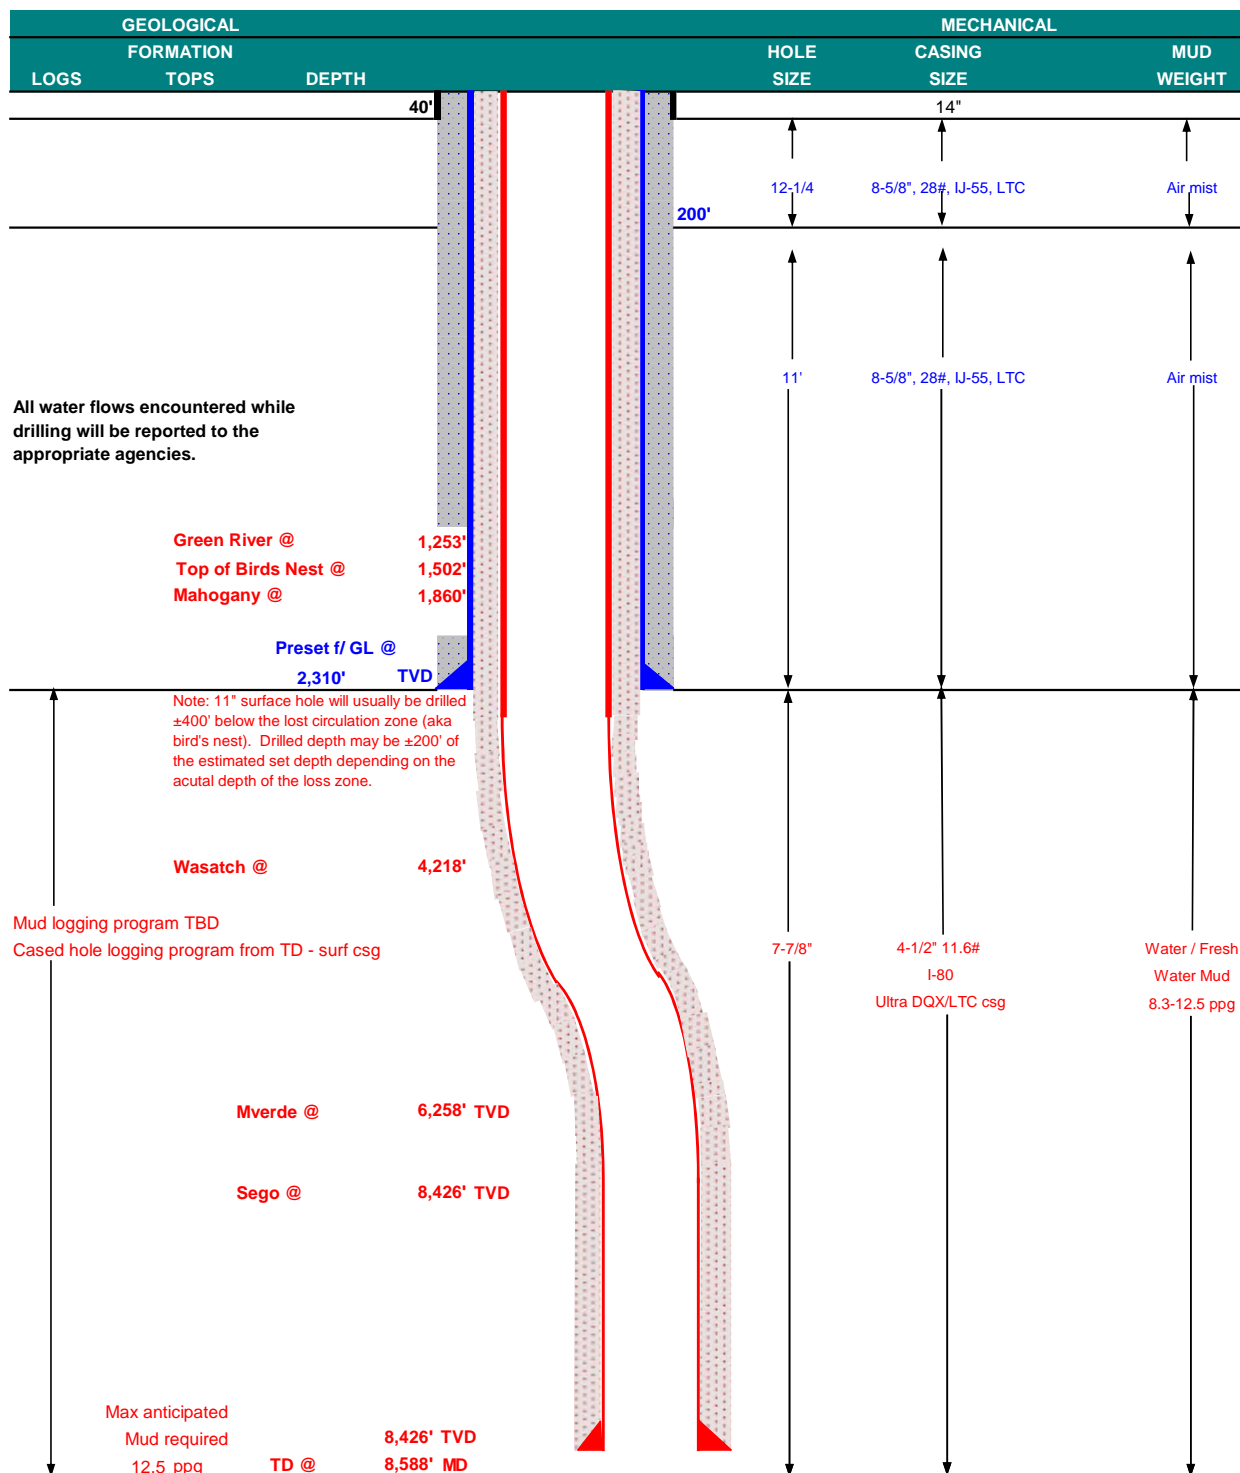

RECEIVED: May. 16, 2012

BONANZA 1023-5G4DS

Drilling Program
6 of 7

KERR-McGEE OIL & GAS ONSHORE LP

DRILLING PROGRAM

CASING PROGRAM

	SIZE	INTERVAL	WT.	GR.	CPLG.	DESIGN FACTORS		
						BURST	LTC	DQX
CONDUCTOR	14"	0-40'				3,390	1,880	348,000
SURFACE	8-5/8"	0 to 2,310	28.00	IJ-55	LTC	2.34	1.74	6.14
						7,780	6,350	223,000
PRODUCTION	4-1/2"	0 to 5,000	11.60	I-80	DQX	1.11	1.16	3.31
						7,780	6,350	223,000
	4-1/2"	5,000 to 8,588'	11.60	I-80	LTC	1.11	1.16	6.62

Surface Casing:

(Burst Assumptions: TD = 12.5 ppg) 0.73 psi/ft = frac gradient @ surface shoe

Fracture at surface shoe with 0.1 psi/ft gas gradient above

(Collapse Assumption: Fully Evacuated Casing, Max MW)

(Tension Assumptions: Air Weight of Casing*Buoy.Fact. of water)

Production casing:

(Burst Assumptions: Pressure test with 8.4ppg @ 7000 psi) 0.64 psi/ft = bottomhole gradient

(Collapse Assumption: Fully Evacuated Casing, Max MW)

(Tension Assumptions: Air Weight of Casing*Buoy.Fact. of water)

CEMENT PROGRAM

		FT. OF FILL	DESCRIPTION	SACKS	EXCESS	WEIGHT	YIELD
SURFACE Option 1	LEAD	500'	Premium cmt + 2% CaCl + 0.25 pps flocele	180	60%	15.80	1.15
	TOP OUT CMT (6 jobs)	1,200'	20 gals sodium silicate + Premium cmt + 2% CaCl + 0.25 pps flocele	270	0%	15.80	1.15
NOTE: If well will circulate water to surface, option 2 will be utilized							
SURFACE Option 2	LEAD	1,810'	65/35 Poz + 6% Gel + 10 pps gilsonite + 0.25 pps Flocele + 3% salt BWOW	170	35%	11.00	3.82
	TAIL	500'	Premium cmt + 2% CaCl + 0.25 pps flocele	150	35%	15.80	1.15
	TOP OUT CMT	as required	Premium cmt + 2% CaCl	as req.		15.80	1.15
PRODUCTION	LEAD	3,718'	Premium Lite II +0.25 pps celloflake + 5 pps gilsonite + 10% gel + 0.5% extender	290	35%	12.00	3.38
	TAIL	4,870'	50/50 Poz/G + 10% salt + 2% gel + 0.1% R-3	1,150	35%	14.30	1.31

*Substitute caliper hole volume plus 0% excess for LEAD if accurate caliper is obtained

*Substitute caliper hole volume plus 10% excess for TAIL if accurate caliper is obtained

FLOAT EQUIPMENT & CENTRALIZERS

SURFACE	Guide shoe, 1 jt, insert float. Centralize first 3 joints with bow spring centralizers. Thread lock guide shoe
PRODUCTION	Float shoe, 1 jt, float collar. 15 centralizers for a Mesaverde and 20 for a Blackhawk well. 1 centralizer on the first 3 joints and one every third joint thereafter.

ADDITIONAL INFORMATION

Test casing head to 750 psi after installing. Test surface casing to 1,500 psi prior to drilling out.

BOPE: 11" 5M with one annular and 2 rams. The BOPE will be installed before the production hole is drilled and tested to 5,000 psi (annular to 2,500 psi) prior to drilling out the surface casing shoe. Record on chart recorder and tour sheet. Function test rams on each trip. Maintain safety valve and inside BOP on rig floor at all times. Most rigs have top drives; however, if used, the Kelly is to be equipped with upper and lower kelly valves.

Surveys will be taken at 1,000' minimum intervals.

Most rigs have PVT System for mud monitoring. If no PVT is available, visual monitoring will be utilized.

DRILLING ENGINEER:

Nick Spence / Danny Showers / Chad Loesel

DATE:


DRILLING SUPERINTENDENT:

Kenny Gathings / Lovel Young

DATE:

RECEIVED: May. 16, 2012

EXHIBIT A
BONANZA 1023-5G4DS

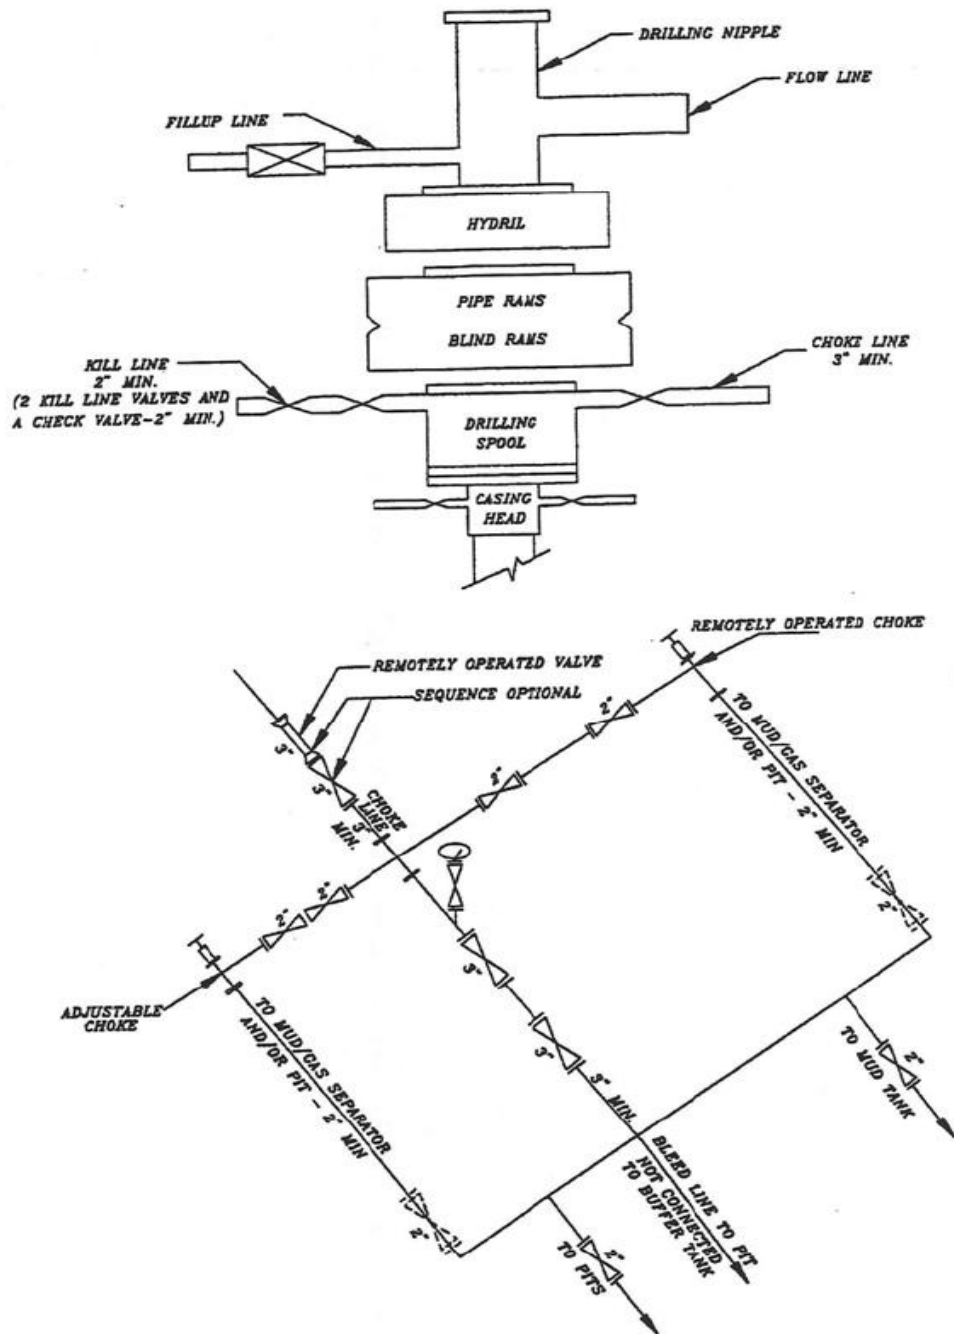

SCHEMATIC DIAGRAM OF 5,000 PSI BOP STACK

Requested Drilling Options:

Kerr-McGee will use either a closed loop drilling system that will require one pit and one cuttings storage area to be constructed on the drilling pad or a traditional drilling operation with one pit used for drilling and completion operations. The cuttings storage area will be used to contain only the de-watered drill cuttings and will be lined and bermed to prevent any liquid runoff. The drill cuttings will be buried in the completion pit once completion operations are completed according to traditional pit closure standards. The pit will be constructed to allow for completion operations. The completion operations pit will be lined with a synthetic material 20 mil or thicker and will be used for the completing of the wells on the pad or used as part of our Aandarko Completions Transportation System (ACTS). Using the closed loop drilling system will allow Kerr-McGee to decrease the amount of disturbance/footprint on location compared to a single large drilling/completions pit.

If Kerr-McGee does not use a closed loop drilling system, it will construct a traditional drilling/completions pit to contain drill cuttings and for use in completion operations. The pit will be lined with a synthetic material 20 mil or thicker. The drill cuttings will be buried in the pit using traditional pit closure standards.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU33433
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: KERR-MCGEE OIL & GAS ONSHORE, L.P.		7. UNIT or CA AGREEMENT NAME:
3. ADDRESS OF OPERATOR: P.O. Box 173779 1099 18th Street, Suite 600, Denver, CO, 80217 3779		8. WELL NAME and NUMBER: BONANZA 1023-5G4DS
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1625 FSL 1048 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESE Section: 05 Township: 10.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047520580000
PHONE NUMBER: 720 929-6514		9. FIELD and POOL or WILDCAT: NATURAL BUTTES
COUNTY: UINTAH		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input checked="" type="checkbox"/> SPUD REPORT Date of Spud: 5/21/2012	<input type="checkbox"/> CASING REPAIR	
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> CHANGE WELL NAME	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. MIRU TRIPPLE A BUCKET RIG. DRILLED 20" CONDUCTOR HOLE TO 40'. RAN 14" 36.7# SCHEDULE 10 PIPE. CMT W/28 SX READY MIX. SPUD WELL ON 05/21/2012 AT 1600 HRS.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY May 24, 2012		
NAME (PLEASE PRINT) Sheila Wopsock	PHONE NUMBER 435 781-7024	TITLE Regulatory Analyst
SIGNATURE N/A	DATE 5/24/2012	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9																									
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU33433																									
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:																									
2. NAME OF OPERATOR: KERR-MCGEE OIL & GAS ONSHORE, L.P.		7. UNIT or CA AGREEMENT NAME: PONDEROSA																									
3. ADDRESS OF OPERATOR: P.O. Box 173779 1099 18th Street, Suite 600, Denver, CO, 80217 3779		8. WELL NAME and NUMBER: BONANZA 1023-5G4DS																									
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1625 FSL 1048 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESE Section: 05 Township: 10.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047520580000																									
10. FIELD and POOL or WILDCAT: NATURAL BUTTES		9. FIELD and POOL or WILDCAT: NATURAL BUTTES																									
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		COUNTY: UINTAH																									
<table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th style="width: 20%;">TYPE OF SUBMISSION</th> <th colspan="4">TYPE OF ACTION</th> </tr> </thead> <tbody> <tr> <td style="vertical-align: top;"> <input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: </td> <td style="vertical-align: top;"> <input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION </td> <td style="vertical-align: top;"> <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER </td> <td style="vertical-align: top;"> <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION </td> <td style="vertical-align: top;"> OTHER: <input style="width: 100px;" type="text"/> </td> </tr> <tr> <td style="vertical-align: top;"> <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: </td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td style="vertical-align: top;"> <input type="checkbox"/> SPUD REPORT Date of Spud: </td> <td></td> <td></td> <td></td> <td></td> </tr> <tr> <td style="vertical-align: top;"> <input checked="" type="checkbox"/> DRILLING REPORT Report Date: 6/2/2012 </td> <td></td> <td></td> <td></td> <td></td> </tr> </tbody> </table>			TYPE OF SUBMISSION	TYPE OF ACTION				<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION	OTHER: <input style="width: 100px;" type="text"/>	<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:					<input type="checkbox"/> SPUD REPORT Date of Spud:					<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 6/2/2012				
TYPE OF SUBMISSION	TYPE OF ACTION																										
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER	<input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION	OTHER: <input style="width: 100px;" type="text"/>																							
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:																											
<input type="checkbox"/> SPUD REPORT Date of Spud:																											
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 6/2/2012																											
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. MIRU AIR RIG ON 5/31/2012. DRILLED SURFACE HOLE TO 2460'. RAN SURFACE CASING AND CEMENTED. WELL IS WAITING ON ROTARY RIG. DETAILS OF CEMENT JOB WILL BE INCLUDED WITH WELL COMPLETION REPORT.																											
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY June 07, 2012																											
NAME (PLEASE PRINT) Cara Mahler		PHONE NUMBER 720 929-6029																									
SIGNATURE N/A		TITLE Regulatory Analyst I																									
DATE 6/4/2012																											

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 6

ENTITY ACTION FORM

Operator: KERR MCGEE OIL & GAS ONSHORE LP Operator Account Number: N 2995
Address: 1368 SOUTH 1200 EAST
city VERNAL
state UT zip 84078 Phone Number: (435) 781-7024

Well 1

API Number	Well Name		QQ	Sec	Twp	Rng	County
4304752058	BONANZA 1023-5G4DS		NESE	5	10S	23E	UINTAH
Action Code	Current Entity Number	New Entity Number	Spud Date			Entity Assignment Effective Date	
B	99999	18519	5/21/2012			5/30/2012	
Comments: MIRU TRIPPLE A BUCKET RIG. Add to Ponderosa SPUD WELL ON 05/21/2012 AT 1600 HRS. wsmvd BHL: Sune							

Well 2

API Number	Well Name		QQ	Sec	Twp	Rng	County
4304752062	BONANZA 1023-5J3AS		NESE	5	10S	23E	UINTAH
Action Code	Current Entity Number	New Entity Number	Spud Date			Entity Assignment Effective Date	
B	99999	18519	5/22/2012			5/30/2012	
Comments: MIRU TRIPPLE A BUCKET RIG. Ponderosa Unit SPUD WELL ON 05/22/2012 AT 0800 HRS. wsmvd BHL: nuse							

Well 3

API Number	Well Name		QQ	Sec	Twp	Rng	County
Action Code	Current Entity Number	New Entity Number	Spud Date			Entity Assignment Effective Date	
Comments:							

ACTION CODES:

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (Explain in 'comments' section)

SHEILA WOPSOCK

Name (Please Print)

Signature

REGULATORY ANALYST

5/24/2012

Title

RECEIVED Date

MAY 29 2012

Div. of Oil, Gas & Mining

State of Utah - Notification Form

Operator KERR MCGEE OIL AND GAS Rig Name/# XTREME 12
Submitted By DALTON KING Phone Number 435- 828-0985
Well Name/Number BONANZA 1023-5G4DS
Qtr/Qtr NE/SE Section 5 Township 10S Range 23E
Lease Serial Number UTU-33433
API Number 43-047-52058

Casing – Time casing run starts, not cementing times.

- ☐ Production Casing
☐ Other

Date/Time _____ AM ☐ PM ☐

BOPE

- ☒ Initial BOPE test at surface casing point
☐ Other

RECEIVED

JUN 20 2012

DIV. OF OIL, GAS & MINING

Date/Time 6/20/2012 03:00 AM ☒ PM ☐

Rig Move

Location To: BONANZA 1023-5G4DS

Date/Time 6/20/2012 01:00 AM ☒ PM ☐

Remarks TIME IS ESTIMATED

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU33433
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: KERR-MCGEE OIL & GAS ONSHORE, L.P.		7. UNIT or CA AGREEMENT NAME: PONDEROSA
3. ADDRESS OF OPERATOR: P.O. Box 173779 1099 18th Street, Suite 600, Denver, CO, 80217 3779		8. WELL NAME and NUMBER: BONANZA 1023-5G4DS
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1625 FSL 1048 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESE Section: 05 Township: 10.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047520580000
PHONE NUMBER: 720 929-6514		9. FIELD and POOL or WILDCAT: NATURAL BUTTES
COUNTY: UINTAH		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 6/26/2012	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> CHANGE WELL NAME	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. MIRU ROTARY RIG. FINISHED DRILLING FROM 2460' TO 8625' ON 6/23/2012. RAN 4-1/2" 11.6# I-80 PRODUCTION CASING. CEMENTED PRODUCTION CASING. RELEASED XTREME 12 RIG ON 6/26/2012 @ 11:30 HRS. DETAILS OF CEMENT JOB WILL BE INCLUDED WITH THE WELL COMPLETION REPORT. WELL IS WAITING ON FINAL COMPLETION ACTIVITIES.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY July 03, 2012		
NAME (PLEASE PRINT) Cara Mahler	PHONE NUMBER 720 929-6029	TITLE Regulatory Analyst I
SIGNATURE N/A	DATE 6/29/2012	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU33433
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: KERR-MCGEE OIL & GAS ONSHORE, L.P.		7. UNIT or CA AGREEMENT NAME: PONDEROSA
3. ADDRESS OF OPERATOR: P.O. Box 173779 1099 18th Street, Suite 600, Denver, CO, 80217 3779		8. WELL NAME and NUMBER: BONANZA 1023-5G4DS
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1625 FSL 1048 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESE Section: 05 Township: 10.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047520580000
PHONE NUMBER: 720 929-6514		9. FIELD and POOL or WILDCAT: NATURAL BUTTES
COUNTY: UINTAH		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 8/2/2012	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE TUBING	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER	
	OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. No activity for the month of July 2012. Well TD at 8,625'.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY August 02, 2012		
NAME (PLEASE PRINT) Cara Mahler	PHONE NUMBER 720 929-6029	TITLE Regulatory Analyst I
SIGNATURE N/A	DATE 8/2/2012	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU33433
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: KERR-MCGEE OIL & GAS ONSHORE, L.P.		7. UNIT or CA AGREEMENT NAME: PONDEROSA
3. ADDRESS OF OPERATOR: P.O. Box 173779 1099 18th Street, Suite 600, Denver, CO, 80217 3779		8. WELL NAME and NUMBER: BONANZA 1023-5G4DS
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1625 FSL 1048 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESE Section: 05 Township: 10.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047520580000
PHONE NUMBER: 720 929-6514		9. FIELD and POOL or WILDCAT: NATURAL BUTTES
COUNTY: UINTAH		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 9/4/2012	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE TUBING	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. No Activity for the month of August 2012. Well TD at 8,625		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY September 05, 2012		
NAME (PLEASE PRINT) Lindsey Frazier	PHONE NUMBER 720 929-6857	TITLE Regulatory Analyst II
SIGNATURE N/A	DATE 9/4/2012	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU33433
1. TYPE OF WELL Gas Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: KERR-MCGEE OIL & GAS ONSHORE, L.P.		7. UNIT or CA AGREEMENT NAME: PONDEROSA
3. ADDRESS OF OPERATOR: P.O. Box 173779 1099 18th Street, Suite 600, Denver, CO, 80217 3779		8. WELL NAME and NUMBER: BONANZA 1023-5G4DS
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1625 FSL 1048 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESE Section: 05 Township: 10.0S Range: 23.0E Meridian: S		9. API NUMBER: 43047520580000
5. FIELD and POOL or WILDCAT: NATURAL BUTTES		9. FIELD and POOL or WILDCAT: NATURAL BUTTES
COUNTY: UINTAH		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 9/19/2012	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE TUBING	
	<input type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. The subject well was placed on production on 09/19/2012. The Chronological Well History will be submitted with the well completion Report.		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY September 20, 2012		
NAME (PLEASE PRINT) Lindsey Frazier	PHONE NUMBER 720 929-6857	TITLE Regulatory Analyst II
SIGNATURE N/A	DATE 9/20/2012	

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
UTU33433

1a. Type of Well ☐ Oil Well ☒ Gas Well ☐ Dry ☐ Other
b. Type of Completion ☒ New Well ☐ Work Over ☐ Deepen ☐ Plug Back ☐ Diff. Resvr.
Other _____

6. If Indian, Allottee or Tribe Name

7. Unit or CA Agreement Name and No.
UTU88209A

2. Name of Operator
KERR MCGEE OIL & GAS ONSHORE, Contact: JAIME L. SCHARNOWSKE
Mail: JAIME.SCHARNOWSKE@ANADARKO.COM

8. Lease Name and Well No.
BONANZA 1023-5G4DS

3. Address PO BOX 173779
DENVER, CO 80217

3a. Phone No. (include area code)
Ph: 720-929-6304

9. API Well No.
43-047-52058

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

At surface NESE 1625FSL 1048FEL 39.975179 N Lat, 109.345064 W Lon

At top prod interval reported below SWNE 2627FNL 1432FEL

At total depth SWNE 2665FNL 1413FEL BHL by HSM

10. Field and Pool, or Exploratory
NATURAL BUTTES

11. Sec., T., R., M., or Block and Survey
or Area Sec 5 T10S R23E Mer SLB

12. County or Parish
UINTAH

13. State
UT

14. Date Spudded
05/21/2012

15. Date T.D. Reached
06/23/2012

16. Date Completed
☐ D & A ☒ Ready to Prod.
09/19/2012

17. Elevations (DF, KB, RT, GL)*
5297 GL

18. Total Depth: MD 8625
TVD 8461

19. Plug Back T.D.: MD 8564
TVD 8400

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
CBL/GR/CCL/TEMP-BHV-DSN/SD/ACTR

22. Was well cored? ☒ No ☐ Yes (Submit analysis)
Was DST run? ☒ No ☐ Yes (Submit analysis)
Directional Survey? ☐ No ☒ Yes (Submit analysis)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
20.000	14.000 STL	36.7	0	40		28			
11.000	8.625 IJ-55	28.0	0	2448		1125		0	
7.875	4.500 I-80	11.6	0	8611		1320		1780	

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2.375	8002							

25. Producing Intervals

26. Perforation Record

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) WASATCH	5835	6328	5835 TO 6328	0.360	48	OPEN
B) MESAVERDE	7004	8539	7004 TO 8539	0.360	168	OPEN
C)						
D)						

27. Acid, Fracture, Treatment, Cement Squeeze, Etc.

Depth Interval	Amount and Type of Material
5835 TO 8539	PUMP 10,189 BBLs SLICK H2O & 220,300 LBS 30/50 OTTAWA SAND

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
09/19/2012	09/24/2012	24	→	0.0	1601.0	0.0			FLows FROM WELL
Choke Size	Tbg. Press. Flwg.	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	
20/64	SI 1140	1807.0	→	0	1601	0		PGW	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg.	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	
	SI		→						

(See Instructions and spaces for additional data on reverse side)

ELECTRONIC SUBMISSION #153900 VERIFIED BY THE BLM WELL INFORMATION SYSTEM

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **

RECEIVED

OCT 16 2012

DIV. OF OIL, GAS & MINING

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	
			→						

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas:Oil Ratio	Well Status	
			→						

29. Disposition of Gas(Sold, used for fuel, vented, etc.)
SOLD

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top Meas. Depth
				GREEN RIVER BIRD'S NEST MAHOGANY WASATCH MESAVERDE	1167 1355 1896 4395 6393

32. Additional remarks (include plugging procedure):

The first 210' of the surface hole was drilled with a 12 ?? bit. The remainder of surface hole was drilled with an 11? bit. DQX csg was run from surface to 5001 ft; LTC csg was run from 5,001 ft to 8,611 ft. Attached is the chronological well history, perforation report & final survey.

33. Circle enclosed attachments:

- | | | | |
|---|--------------------|---------------|-----------------------|
| 1. Electrical/Mechanical Logs (1 full set req'd.) | 2. Geologic Report | 3. DST Report | 4. Directional Survey |
| 5. Sundry Notice for plugging and cement verification | 6. Core Analysis | 7. Other: | |

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions):

Electronic Submission #153900 Verified by the BLM Well Information System.
For KERR MCGEE OIL & GAS ONSHORE,L, sent to the Vernal

Name (please print) JAIME L. SCHARNOWSKETitle REGULATORY ANALYSTSignature (Electronic Submission)Date 10/08/2012

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

**** ORIGINAL ** ORIGINAL ** ORIGINAL ** ORIGINAL ** ORIGINAL ** ORIGINAL ** ORIGINAL ****

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
5/31/2012	9:30 - 10:30	1.00	DRLSUR	13	A	P		WAIT ON CEMENT
	10:30 - 11:30	1.00	DRLSUR	02	C	P		SPUD 05/31/2012 10:30 hrs. DRILL 12.25" HOLE 44'-210' (166', 110'/PER HOUR). 12.25 in. BIT ON 55 th RUN. WEIGHT ON BIT 5-15 K. STROKES PER MINUTE 120 GALLONS PER MINUTE 491. PRESSURE ON/OFF (BOTTOM) 800/600. ROTARY RPM 55, MOTOR RPM 83, TOTAL RPM 138. UP/DOWN/ ROTATE 20/20/20 K. DRAG 0 K.
	11:30 - 15:00	3.50	DRLSUR	06	A	P		CIRCULATE CLOSED LOOP SYSTEM WITH 8.5# WATER. DRILL DOWN TO 210' WITH 6" DRILL COLLARS. CIRC 15 MINUTES AND, TRIP OUT TO CHANGE ASSEMBLY. PRE JOB SAFETY MEETING, LAY DOWN 6" DRILL COLLARS, BREAK 12 1/4" BIT. MAKE UP Q506F 11" BIT (1 TH RUN) (SN 7024523) PICK UP 8" DIRECTIONAL ASSEMBLY. INSTALL EM TOOL. TRIP IN HOLE.
	15:00 - 16:00	1.00	DRLSUR	06	A	X		GOT ON BOTTOM KICKED PUMPS IN WELLS COMMUNICATED TRIPPED OUT OF HOLE WAITED ON CEMENT TO ARRIVE
	16:00 - 17:30	1.50	DRLSUR	21	D	X		WAIT ON READY MIX TRUCK AND PRO PETRO CEMENTERS
	17:30 - 18:00	0.50	DRLSUR	12	F	X		PUT 4 YRDS CEMENT DOWN WELL 3/5 CEMENT TO SURFACE FELL 90'
	18:00 - 18:30	0.50	DRLSUR	12	F	X		MIX AND PUMP (125 SX) 22.4 BBLs OF SAME TAIL CEMENT W/ 4% CALC. DOWN BACKSIDE CEMENT TO SURFACE
	18:30 - 22:30	4.00	DRLSUR	13	A	X		WAIT ON CEMENT
	22:30 - 0:00	1.50	DRLSUR	02	C	P		DRILL 11" SURFACE HOLE 210'- 430' (220' AT 146 FT HR) WEIGHT ON BIT 15-25 K. STROKES PER MINUTE 120 GALLONS PER MINUTE 491. PRESSURE ON/OFF(BOTTOM) 1090/880. ROTARY RPM 55, MOTOR RPM 83, TOTAL RPM 138. UP/DOWN/ ROTATE 47/40/43 K. DRAG 7 K.
								SLIDING 15'-20 PER 90'OF ROTATION GETTING 1.8 DEGREE BUILD RATES
								CIRCULATE CLOSED LOOP SYSTEM WITH 8.6# WATER. RUNNING VOLUME OVER BOTH SHAKERS 200 API SCREENS ON SHAKERS NO HOLE ISSUES.

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
6/1/2012	0:00 - 0:00	24.00	DRLSUR	02	C	P		<p>DRILL 11" SURFACE HOLE 430' - 2460' T.D. (2030' AT 84 FT HR)</p> <p>WEIGHT ON BIT 15-25 K.</p> <p>STROKES PER MINUTE 120 GALLONS PER MINUTE 491.</p> <p>PRESSURE ON/OFF(BOTTOM) 1090/880.</p> <p>ROTARY RPM 55, MOTOR RPM 83, TOTAL RPM 138.</p> <p>UP/DOWN/ ROTATE 96/76/73 K. DRAG 20 K.</p> <p>SLIDING 15'-20 PER 90'OF ROTATION GETTING 1.8 DEGREE BUILD RATES LANDED 3.5' HIGH 3.5' RIGHT OF LINE SLIDING 802' 32%</p> <p>LAST SURVEY 19.7 DEG 336.79 AZI</p> <p>CIRCULATE CLOSED LOOP SYSTEM WITH 8.6# WATER.</p> <p>RUNNING VOLUME OVER BOTH SHAKERS</p> <p>200 API SCREENS ON SHAKERS</p> <p>NO HOLE ISSUES.</p>
6/2/2012	0:00 - 1:30	1.50	DRLSUR	05	C	P		<p>CIRCULATE AND CONDITION MUD PRIOR TO LDDS</p> <p>TOOH LAYING DOWN DRILL STRING BREAK DOWN MWD TOOLS DIRECTIONAL TOOLS MUD MOTOR AND BIT</p> <p>RIG UP AND RUN 55 JOINTS 8.625" J55 28#</p> <p>SURFACE CASING SHOE AT 2436' BAFFLE AT 2393' NO PROBLEMS RUN 200' OF 1" PIPE DOWN BACK SIDE LAY RIG OVER</p> <p>PRESSURE TEST LINES TO 2000 PSI. PUMP 135 BBLS OF WATER AHEAD. CATCH PSI. PUMP 20 BBLS OF 8.3# GEL WATER AHEAD. MIX AND PUMP (300 SX) 61.4 BBLS OF 15.8# 1.15 YD 5 GAL/SK PREMIUM CEMENT W/ 2% CALC. DROP PLUG ON FLY. DISPLACE W/ 143 BBLS OF H2O. NO CIRC THROUGH OUT. FINAL LIFT OF 210 PSI AT 4 BBL/MIN. BUMP PLUG WITH 500 PSI FOR 5 MIN. FLOAT HELD. MIX AND PUMP (200 SX) 41.7 BBLS OF SAME TAIL CEMENT W/ 4% CALC. DOWN BACKSIDE, NO CEMENT TO SURFACE. SHUT DOWN AND CLEAN TRUCK. WAIT 1.5 HOURS MIX AND PUMP (200 SX) 41.4 BBLS OF SAME TAIL CEMENT W/ 4% CALC. DOWN BACKSIDE NO CEMENT TO SURFACE. NO CEMENT TO SURFACE. SHUT DOWN AND CLEAN TRUCK. WAIT 1.5 HOURS MIX AND PUMP (200 SX) 41.4 BBLS OF SAME TAIL CEMENT W/ 4% CALC. DOWN BACKSIDE NO CEMENT TO SURFACE. NO CEMENT TO SURFACE. SHUT DOWN AND CLEAN TRUCK. WAIT 1.5 HOURS MIX AND PUMP (225 SX) 45.4 BBLS OF SAME TAIL CEMENT W/ 4% CALC. DOWN BACKSIDE NO CEMENT TO SURFACE. NO CEMENT TO SURFACE. SHUT DOWN AND CLEAN TRUCK. CEMENT TO SURFACE WAIT ON CEMENT RELEASE RIG @ 18:00</p>
	1:30 - 6:00	4.50	DRLSUR	06	A	P		
	6:00 - 9:30	3.50	DRLSUR	12	C	P		
	9:30 - 16:00	6.50	DRLSUR	12	E	P		
	16:00 - 18:00	2.00	DRLSUR	21	E	P		

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/O/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
6/20/2012	13:00 - 14:00	1.00	MIRU	01	C	P		SKID THE RIG TO THE BONANZA 1023-5G4DS. CENTER THE RIG
	14:00 - 15:00	1.00	MIRU	14	A	P		NIPPLE UP THE BOP , FLOW LINE, AND CHOKE
	15:00 - 19:00	4.00	PRPSPD	15	A	P		HOLD SAFETY MEETING. TEST TOP DRIVE VALVE, I-BOP VALVE, FLOOR VALVE, DART VALVE, PIPE AND BLIND RAMS, INSIDE AND OUTSIDE KILL LINE VALVES INSIDE OUTSIDE CHOKE LINE VALVE, HCR VALVE, CHOKE LINE, CHOKE MANIFOLD VALVES AND CHOKES TO 5000 PSI FOR 10 MINUTES AND 250 PSI FOR 5 MINUTES. TEST ANNULAR TO 2500 PSI FOR 10 MIN AND 250 PSI FOR 5 MINUTES. TESTING CASING TO 1500 PSI FOR 30 MINUTES.
	19:00 - 19:30	0.50	PRPSPD	14	B	P		INSTALL THE WEAR BUSHING
	19:30 - 21:30	2.00	PRPSPD	06	A	P		PICKED UP / SCRIBED THE BHA AND PICKED UP THE HEAVY WEIGHT DRILL PIPE
	21:30 - 22:30	1.00	MAINT	09	A	P		CUT AND SLIPPED 71' OF DRILLING LINE
	22:30 - 23:00	0.50	PRPSPD	14	B	P		REPLACED AND INSTALLED THE ROTATING HEAD RUBBER
	23:00 - 0:00	1.00	PRPSPD	06	A	P		CONTINUED TO PPICK UP DRILL PIPE AND TRIP IN THE HOLE
	0:00 - 0:30	0.50	PRPSPD	06	A	P		FINISHED PICKING UP DRILL PIPE. TAGGED CEMENT @ 2350'
	0:30 - 1:00	0.50	DRLPRC	02	F	P		DRILLED THE CEMENT AND FLOAT EQUIPMENT . 40 RPM
6/21/2012	1:00 - 15:00	14.00	DRLPRC	02	D	P		10-12K WEIGHT ON BIT DRILL SLIDE 2471'- 3974' (1503' @ 107.4'/HR) WEIGHT ON BIT 19-23K. AVERAGE WEIGHT ON BIT 21K. ROTARY RPM 60. MUD MOTOR RPM 83. STROKES PER MINUTE 115 GALLONS PER MINUTE 517. ON/OFF PSI 1780/1440 DIFF 340. TORQUE HIGH/LOW 8900/7400. OFF BOTTOM TORQUE 5020 STRING WEIGHT UP/DOWN/ROT 120/88/98. DRAG 22K. BIT POSITION . 4 5' LOW 8' LEFT OF THE LINE SLIDE 386' AT 82.6'/HR. SLIDE 37% ROTATE 63%. RUNNING 2 CENTRIFUGES AND DE WATERING.(WT 8.4 VIS 26.) USED 75 BBLS DRILL WATER FOR HOLE VOLUME. LOST 40 BBLS DRILL WATER INTO FORMATION. (LOSING 5 BBLS HR) USED 100 BBL. OF FRESH WATER PUMP 5% LCM SWEEPS TO HELP WITH LOSSES. (ADD 50 BBLS OF 32 VIS DRILL WATER TO PITS FOR SWEEPS) ADDING POLYMER TO SYSTEM HELP STABALIZE SHALES. NO FLARE.
	15:00 - 15:30	0.50	MAINT	07	A	P		RIG SERVICE

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	15:30 - 0:00	8.50	DRLPRC	02	D	P		DRILL SLIDE 3974' - 5109 (1135' @ 133.5'/HR) WEIGHT ON BIT 19-23K. AVERAGE WEIGHT ON BIT 21K. ROTARY RPM 60. MUD MOTOR RPM 83. STROKES PER MINUTE 115 GALLONS PER MINUTE 517. ON/OFF PSI 1800/1600 DIFF 200. TORQUE HIGH/LOW 9200/8300. OFF BOTTOM TORQUE 6300 STRING WEIGHT UP/DOWN/ROT 140/80/105. DRAG 35K. BIT POSITION 5013' 6'N 7' W OF CENTER SLIDE 26' AT 78.8'/HR. SLIDE 2.32% ROTATE 96.33%. RUNNING 2 CENTRIFUGES AND DE WATERING.(WT 8.4 VIS 26.) USED 70 BBLS DRILL WATER FOR HOLE VOLUME. LOST 130 BBLS DRILL WATER INTO THE FORMATION (LOSING 15 BBLS HR) USED 0 BBL. OF FRESH WATER. PUMP 5% LCM SWEEPS TO HELP WITH LOSSES. (ADD 50 BBLS OF 32 VIS DRILL WATER TO PITS FOR SWEEPS) ADDING POLYMER TO SYSTEM HELP STABALIZE SHALES. NO FLARE.
6/22/2012	0:00 - 5:00	5.00	DRLPRC	02	D	P		DRILL SLIDE 5109' - 5835' (724' @ 144.8'/HR) WEIGHT ON BIT 19-23K. AVERAGE WEIGHT ON BIT 21K. ROTARY RPM 60. MUD MOTOR RPM 83. STROKES PER MINUTE 115 GALLONS PER MINUTE 517. ON/OFF PSI 1800/1600 DIFF 200. TORQUE HIGH/LOW 9200/8300. OFF BOTTOM TORQUE 6300 STRING WEIGHT UP/DOWN/ROT 140/80/105. DRAG 35K. BIT POSITION 16' N, 9' W OF CENTER SLIDE 0' AT ' /HR. SLIDE 0% ROTATE 100%. RUNNING 2 CENTRIFUGES AND DE WATERING.(WT 8.4 VIS 26.) USED 200 BBLS DRILL WATER FOR HOLE VOLUME. LOST 150 BBLS DRILL WATER INTO THE FORMATION (LOSING 20 BBLS HR) LOST 50 BBL. @ 5750' USED 0 BBL. OF FRESH WATER. PUMP 5% LCM SWEEPS TO HELP WITH LOSSES. (ADD 50 BBLS OF 32 VIS DRILL WATER TO PITS FOR SWEEPS) ADDING POLYMER TO SYSTEM HELP STABALIZE SHALES. NO FLARE.

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	5:00 - 5:30	0.50	MAINT	07	A	P		SERVICED TOP DRIVE, INSPECT BRAKES, EMERGENCY STOP 1 SECOND REACTION TIME.
	5:30 - 17:30	12.00	DRLPRC	02	D	P		DRILL SLIDE 5835'-7151' (1310' @ 109'/HR) WEIGHT ON BIT 20-25K. AVERAGE WEIGHT ON BIT 23K. ROTARY RPM 60. MUD MOTOR RPM 83. STROKES PER MINUTE 115 GALLONS PER MINUTE 517. ON/OFF PSI 2346/1929 DIFF 417. TORQUE HIGH/LOW 12139/10470. OFF BOTTOM TORQUE 9249 STRING WEIGHT UP/DOWN/ROT 160/100/130. DRAG 30K. CURRENT BIT POSITION 13' NORTH, 11' WEST OF CENTER SLIDE 36' AT 80'/HR. SLIDE 5% ROTATE 95%. RUNNING 2 CENTRIFUGES AND DE WATERING.(WT 8.4 VIS 26.) USED 71 BBLS DRILL WATER FOR HOLE VOLUME. LOST 150 BBLS DRILL WATER INTO THE FORMATION (LOSING 12 BBLS HR) USED 150 BBL. OF FRESH WATER. PUMP 5% LCM SWEEPS TO HELP WITH LOSSES. (ADD 50 BBLS OF 32 VIS DRILL WATER TO PITS FOR SWEEPS) ADDING POLYMER TO SYSTEM HELP STABALIZE SHALES. NO FLARE.
	17:30 - 18:00	0.50	DRLPRC	07	A	P		RIG SERVICE. SERVICE TOP DRIVE. CHECK GENERATORS. SERVICE CROWN. CHECK BRAKE ADJUSTMENT AND TEST EMERGENCY STOP.

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	18:00 - 0:00	6.00	DRLPRC	02	D	P		<p>DRILL SLIDE 7151'-7674' (523' @ 87'/HR) WEIGHT ON BIT 20-25K. AVERAGE WEIGHT ON BIT 23K. ROTARY RPM 60. MUD MOTOR RPM 83. STROKES PER MINUTE 115 GALLONS PER MINUTE 517. ON/OFF PSI 2346/1929 DIFF 417. TORQUE HIGH/LOW 12139/10470. OFF BOTTOM TORQUE 9249 STRING WEIGHT UP/DOWN/ROT 160/100/130. DRAG 30K. CURRENT BIT POSITION 5' SOUTH, 2' EAST OF CENTER SLIDE 55' AT 75'/HR. SLIDE 8% ROTATE 93%. RUNNING 2 CENTRIFUGES AND DE WATERING.(WT 8.4 VIS 26.) USED 28 BBLS DRILL WATER FOR HOLE VOLUME. LOST 60 BBLS DRILL WATER INTO THE FORMATION (LOSING 10 BBLS HR) USED 100 BBL. OF FRESH WATER. PUMP 5% LCM SWEEPS TO HELP WITH LOSSES. (ADD 50 BBLS OF 32 VIS DRILL WATER TO PITS FOR SWEEPS) ADDING POLYMER TO SYSTEM HELP STABALIZE SHALES. NO FLARE.</p> <p>LIGHT MUD UP AT 7500' WENT CONVENTIONAL WITH BOTH CENTRAFUGES BEGIN ADDING CHEMICALS TO DRILL WATER TO ALLOW FOR GELS TO YIELD ADD GELL FOR 32 VIS</p>

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
6/23/2012	0:00 - 5:30	5.50	DRLPRC	02	D	P		<p>DRILL SLIDE 7674'-8396' (722' @ 131'/HR) WEIGHT ON BIT 20-25K. AVERAGE WEIGHT ON BIT 23K. ROTARY RPM 60. MUD MOTOR RPM 83. STROKES PER MINUTE 115 GALLONS PER MINUTE 517. ON/OFF PSI 2520/2020 DIFF 500. TORQUE HIGH/LOW 13019/10470. OFF BOTTOM TORQUE 9249 STRING WEIGHT UP/DOWN/ROT 180/120/145. DRAG 35K. CURRENT BIT POSITION 18' SOUTH, 9' EAST OF CENTER SLIDE 0' AT 0'/HR. SLIDE 0% ROTATE 100%. ROTATE TO TD. RUNNING 2 CENTRIFUGES CONVENTIONAL.(WT 8.5 VIS 28.) USED 39 BBLS DRILL WATER FOR HOLE VOLUME. LOST 60 BBLS DRILL WATER INTO THE FORMATION (LOSING 10.5 BBLS HR) USED 100 BBL. OF FRESH WATER. PUMP 5% LCM SWEEPS TO HELP WITH LOSSES. (ADD 50 BBLS OF 32 VIS DRILL WATER TO PITS FOR SWEEPS) ADDING POLYMER TO SYSTEM HELP STABALIZE SHALES. NO FLARE. SERVICED TOP DRIVE, INSPECT BRAKES, EMERGANCY STOP 1 SECOND REACTION TIME.</p>
	5:30 - 6:00	0.50	DRLPRC	07	A	P		

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	6:00 - 9:00	3.00	DRLPRC	02	D	P		<p>DRILL SLIDE 8396'-8625' (229' @ 76'/HR) TD@ 06/23/2012 09:00</p> <p>WEIGHT ON BIT 20-25K. AVERAGE WEIGHT ON BIT 23K.</p> <p>ROTARY RPM 60. MUD MOTOR RPM 83.</p> <p>STROKES PER MINUTE 115 GALLONS PER MINUTE 517.</p> <p>ON/OFF PSI 2520/2020 DIFF 500.</p> <p>TORQUE HIGH/LOW 13019/10470. OFF BOTTOM TORQUE 9249</p> <p>STRING WEIGHT UP/DOWN/ROT 180/120/145. DRAG 35K.</p> <p>CURRENT BIT POSITION 21' SOUTH, 11' EAST OF CENTER</p> <p>SLIDE 0' AT 0'/HR.</p> <p>SLIDE 0% ROTATE 100%. ROTATE TO TD.</p> <p>RUNNING 2 CENTRIFUGES CONVENTIONAL.(WT 8.5 VIS 28.)</p> <p>USED 12 BBLS DRILL WATER FOR HOLE VOLUME.</p> <p>LOST 30 BBLS DRILL WATER INTO THE FORMATION (LOSING 10 BBLS HR)</p> <p>USED 50 BBL. OF FRESH WATER.</p> <p>PUMP 5% LCM SWEEPS TO HELP WITH LOSSES.</p> <p>(ADD 50 BBLS OF 32 VIS DRILL WATER TO PITS FOR SWEEPS)</p> <p>ADDING POLYMER TO SYSTEM HELP STABILIZE SHALES.</p> <p>NO FLARE.</p> <p>MUD UP @ 8400' TRANSFERED 800 BBLS OF 11.4# 38 VIS MUD INTO MUD TANKS MIXING 15-20 BAGS OF SAWDUST TO HELP WITH LOSSES,</p> <p>DISPLACED 700 BBLS OF DRILL WATER INTO TWO 400 UPRIGHT'S,</p> <p>ENDED UP WITH 10.4# 34 VIS MUD IN AND 10.1# 31VIS MUD OUT</p>
	9:00 - 9:30	0.50	MAINT	07	A	P		<p>RIG SERVICE. SERVICE TOP DRIVE. CHECK GENERATORS. SERVICE CROWN. CHECK BRAKE ADJUSTMENT AND TEST EMERGENCY STOP.</p>
	9:30 - 12:00	2.50	EVALPR	05	B	P		<p>EVEN MUD TO 11.4# 45 VIS FOR WIPER TRIP.</p> <p>HOLE SEEPING 10 BBLS HR. PUMP 5 SX SWEEPS OF LCM EVERY 30 MIN.</p> <p>ADDED 40 BBLS OF 9# MUD INTO PILL TANK AND MIXED 13# PILL FOR DRY JOB AND HOLD.</p>
	12:00 - 18:00	6.00	EVALPR	06	E	P		<p>NO FLOW ON FLOW CHECK.</p> <p>PUMP AND ROTATE OUT OF HOLE TO 4500'. 60K PULL OVER FROM 4500'.</p> <p>HOLE TIGHT AND STICKEY FROM 8625' TO 4500'.</p> <p>PUMP DRY JOB @ 4500'.</p>
	18:00 - 19:30	1.50	EVALPR	06	E	P		<p>WIPER TRIP TO SHOE. NO TIGHT HOLE FROM 4000'-2436'. HOLE TOOK EXTRA 20 BBLS OF MUD TO FILLON TRIP OUT. NO FLOW ON FLOW CHECK.</p>

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	19:30 - 23:00	3.50	EVALPR	06	E	P		TRIP IN HOLE TO 6850'. REAM THROUGH BRIDGES 4000', 4637', 4817', 5100', 5212', 5608', 6316', 6407', 6522', 6707', 6850'. GOOD HOLE DISPLACEMENT ON TRIP IN. TOOK 30 BBLs MUD WHILE REAMING BRIDGES, PUMP LCM SWEEP WHILE REAMING.
	23:00 - 0:00	1.00	EVALPR	05	B	P		LOST PARTIAL RETURNS @ 6850', SWEEP HOLE WITH TWO LCM SWEEP'S TO CONTROL SEEPAGE. PULLED OUT OF TIGHT HOLE TO 6700' (LOSS 100 BBLs MUD, THEN MUD STARTED HOLDING) CONTINUE TO SWEEP HOLE WITH LCM TO CONTAIN LOSSES AND TO CLEAN HOLE. MUD IN 11.4 VIS 40. MUD OUT 11.4 VIS 40.
6/24/2012	0:00 - 4:00	4.00	EVALPR	06	E	P		TRIP BACK TO BOTTOM OF HOLE. GOOD DISPLACEMENT ON TRIP IN. FILL PIPE @ 5000'. HIT A BRIDGE @ 6850' WASHED AND REAMED ALL THE WAY BACK TO BOTTOM FORM 6850'-8625' 20' OF FILL ON BOTTOM, HAD A 10' FLAIR FOR 30 MINUTES BOTTOMS UP (3,567 SCF).
	4:00 - 6:00	2.00	EVALPR	05	B	P		CIRCULATE AND CONDITION MUD. CIRCULATE BOTTOMS UP. RETURNS CLEAN COMING OVER SHAKERS. MUD WT IN 11.1 VIS 42 MUD WT OUT 11.0 VIS 39. WORK PIPE UP AND DOWN EVERY 5 MINUTES WHILE CIRCULATING. NO LOSSES. PUMPED LCM SWEEP AROUND TO CLEAN HOLE. BUILD 40 BBL 13# DRY JOB AND HOLD. NO FLAIR
	6:00 - 15:30	9.50	EVALPR	06	E	X		TRIP OUT OF HOLE TO SHOE. PUMP AND ROTATE FOR 4000', PUMP 30 BBLs OF 13# DRY JOB. HOLE PULLING TIGHT @ 6150', 6000'. HOLE TAKING PROPER FLUID ON TRIP. NO FLOW ON FLOW CHECKS.
	15:30 - 20:00	4.50	EVALPR	06	E	X		TRIP BACK TO BOTTOM OF HOLE. GOOD DISPLACEMENT ON TRIP IN. FILL PIPE @ 4000'. HIT BRIDGES @ 4000', 5100', 5218', 5308', 6600', 6944', ON TRIP IN
	20:00 - 20:30	0.50	EVALPR	07	A	P		RIG SERVICE. SERVICE TOP DRIVE. CHECK GENERATORS. CHECK BRAKE ADJUSTMENT AND TEST EMERGENCY STOP.
	20:30 - 23:30	3.00	EVALPR	08	A	Z		***FAILURE: RIG EQUIPMENT - (COMMUNICATION SYSTEM/BRAKE HANDLE) 20:30 CURRENT DEPTH OF DRILL STRING 6944', HOLE DEPTH 8625'
	23:30 - 0:00	0.50	EVALPR	06	E	X		BLEW A FUSE IN THE DRILLERS CONSOLE RESULTING IN A RIG COMMUNICATION FAILURE, RESTORED RIG COMMUNICATION SYSTEM TO LATEST VERSION, REPLACED BRAKE HANDLE/JOY STICK. TRIP BACK TO BOTTOM OF HOLE. GOOD DISPLACEMENT ON TRIP IN. FILL PIPE @ 4000'. HIT BRIDGES @ 6992', WASHED AND REAMED FROM 8544' TO 8625', ON TRIP IN

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
6/25/2012	0:00 - 1:00	1.00	EVALPR	06	E	P		TRIP BACK TO BOTTOM OF HOLE. GOOD DISPLACEMENT ON TRIP IN. FILL PIPE @ 5000'. HIT A BRIDGE @ 6850' WASHED AND REAMED ALL THE WAY BACK TO BOTTOM FORM 6850'-8625' 20' OF FILL ON BOTTOM, HAD A 10' FLAIR FOR 30 MINUTES BOTTOMS UP (3,567 SCF).
	1:00 - 3:00	2.00	EVALPR	05	B	P		CIRCULATE AND CONDITION MUD. CIRCULATE BOTTOMS UP. RETURNS CLEAN COMING OVER SHAKERS. MUD WT IN 11.1 VIS 42 MUD WT OUT 11.0 VIS 39. WORK PIPE UP AND DOWN EVERY 5 MINUTES WHILE CIRCULATING. NO LOSSES. PUMPED LCM SWEEP AROUND TO CLEAN HOLE. BUILD 40 BBL 13# DRY JOB AND HOLD. NO FLAIR TRIP OUT OF HOLE FOR LOGGS.
	3:00 - 13:00	10.00	EVALPR	06	D	P		PUMP AND ROTATE FOR 4000', PUMP 30 BBLs OF 13# DRY JOB. HOLE PULLING TIGHT @ 6150', 6000'. HOLE TAKING PROPER FLUID ON TRIP. NO FLOW ON FLOW CHECKS.
	13:00 - 16:00	3.00	EVALPR	11	D	P		PULL ROTATING RUBBER, LAY DOWN HEAVY WEIGHT DRILL PIPE, LAY DOWN DIRECTIONAL TOOL'S, BREAK BIT LAY DOWN MOTOR. ***FAILURE: LOGS BRIDGED OFF
	16:00 - 19:00	3.00	CSGPRO	12	A	P		HOLD SAFETY MEETING WITH HALLIBURTON LOGGERS. RIG UP LOGGERS AND RUN IN HOLE WITH TRIPLE COMBO LOGGING TOOLS. LOG UP FROM 3915'-2536'. PULL OUT AND LAY DOWN TOOLS. RIG DOWN HALLIBURTON. PULL WEAR BUSHING. HOLD SAFETY MEETING WITH KIMZEY CASING AND TSI HAND. REMOVE DRILL PIPE ELEVATORS. RIG UP CASING ELEVATORS. RIG UP INTERGRATED CASING TONGES.

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	19:00 - 0:00	5.00	CSGPRO	12	C	P		<p>(INSPECT FLOAT EQUIPMENT)</p> <p>MAKE UP 4.5" K-55 LTC WEATHERFORD FLOAT SHOE ON SHOE JOINT WITH THREAD LOCK. MAKE UP 4.5" K-55 FLOAT COLLAR W/ THREAD LOCK ON TOP OF SHOE JOINT.</p> <p>RUN CENTRALIZERS ON FIRST 3 JOINTS AND EVERY THIRD JOINT FOR TOTAL OF 15 CENTRALIZERS.</p> <p>BREAK CIRCULATION @ 2400'. NO PROBLEMS WITH FLOAT SHOE OR COLLAR.</p> <p>RUN A TOTAL OF 82 JOINTS OF 4.5" 11.6# I-80 LTC CASING (3654.31'). MAKE UP DQX CROSS OVER JOINT AND RIG UP TORQUE TURN. PERFORM DUMP TEST.</p> <p>RUN A TOTAL 25 JOINTS OF 4.5" 11.6# I-80 DQX CSG WITH TORQUE TURN (1077.5'). (TSI HAND WITNESSED CASING JOB.</p> <p>FILLED CASING AND CIRCULATED AT 2400' AND 4500'. GOOD CIRCULATION WITH NO LOSSES WAS ESTABLISHED.</p> <p>1 BAD JOINT LT&C CHANGED OUT FOR DQX JOINT IN STOCK PILE.</p> <p>TOTAL OF 82 JTS OF 4.5" 11.6# I-80 LTC (3654.31')</p> <p>TOTAL 25 JTS OF 4.5" 11.6# I-80 DQX CSING (1077.5')</p>

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
6/26/2012	0:00 - 6:00	6.00	CSGPRO	12	C	P		<p>(INSPECT FLOAT EQUIPMENT)</p> <p>MAKE UP 4.5" K-55 LTC WEATHERFORD FLOAT SHOE ON SHOE JOINT WITH THREAD LOCK. MAKE UP 4.5" K-55 FLOAT COLLAR W/ THREAD LOCK ON TOP OF SHOE JOINT.</p> <p>RUN CENTRALIZERS ON FIRST 3 JOINTS AND EVERY THIRD JOINT FOR TOTAL OF 15 CENTRALIZERS.</p> <p>BREAK CIRCULATION @ 2400'. NO PROBLEMS WITH FLOAT SHOE OR COLLAR.</p> <p>RUN A TOTAL OF 81 JOINTS OF 4.5" 11.6# I-80 LTC CASING (3610.01'). MAKE UP DQX CROSS OVER JOINT AND RIG UP TORQUE TURN. PERFORM DUMP TEST. RUN A TOTAL 115 JOINTS OF 4.5" 11.6# I-80 DQX CSG WITH TORQUE TURN (5003.83'). (TSI HAND WITNESSED CASING JOB, BILLY BRUBAKER).</p> <p>FILLED CASING AND CIRCULATED AT 2400' AND 5500'. GOOD CIRCULATION WITH NO LOSSES WAS ESTABLISHED.</p> <p>WASHED THROUGH BRIDGE @ 5443', AND 5938', WASH DOWN LAST JOINT AND LANDING JOINT. 10' FILL ON BOTTOM.</p> <p>LANDED CASING ON CAMERON SLOTTED MANDREL WITH LANDING JOINT.</p> <p>1 BAD JOINT OF LT&C CHANGED OUT FOR DQX IN STOCK PILE.</p> <p>5 BAD JOINT DQX CHANGED OUT FOR DQX JOINT IN STOCK PILE.</p> <p>TOTAL OF 81 JTS OF 4.5" 11.6# I-80 LTC (3610.01')</p> <p>TOTAL 115 JTS OF 4.5" 11.6# I-80 DQX CSG (5003.83')</p> <p>LAND FLOAT SHOE @ 8611.30' KB</p> <p>LAND TOP OF FLOAT COLLAR @ 8564.07' KB.</p> <p>LAND TOP OF MESA MARKER JT @ 6420.58 KB.</p> <p>LAND TOP DQX TO LTC CROSS OVER JOINT @ 4982.83' KB.</p> <p>CIRCULATE DOWN CASING WITH RIG. GOOD CIRCULATION WITH NO LOSSES @ 363 GALLONS PER MINUTE. NO FLARE ON BOTTOMS UP. MUD WT 11.5 VIS 42. RIG DOWN KIMZEY CASING.</p>
	6:00 - 7:30	1.50	CSGPRO	05	D	P		

US ROCKIES REGION

Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: PROPETRO 12/12, XTC 12/12

Event: DRILLING

Start Date: 5/16/2012

End Date: 6/26/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	7:30 - 10:30	3.00	CSGPRO	12	E	P		<p>RIG UP CEMENT HEAD WITH WEATHERFORD TOP PLUG INSTALLED. PRESSURE TEST LINES TO 5000 PSI.</p> <p>PUMP 25 BBLS OF FRESH WATER. PUMP 192 BBLS (415 SX) OF 12.0# 2.26 YIELD 12.48 GAL/SK OF LEAD CEMENT. PUMP 211 BBLS (905SX) OF 14.3# 1.31 YIELD 5.91 GAL/SK POZ 50/50 TAIL CEMENT. SHUT DOWN AND FLUSH LINES. DROP TOP PLUG DISPLACE WITH 132.5 BBLS OF FRESH WATER TREATED WITH CLAYFIX AND MAGNACIDE. FULL RETURNS THROUGH OUT JOB.NO CEMENT OR SPACER TO SURFACE</p> <p>LIFT PSI OF 2136 @ 3 BBLS MINUTE. BUMP PLUG 2823 PSI. . PRESSURE HELD 5 MINUTES. FLOAT HELD. FLOW BACK 1.5 BBLS. ESTIMATED TOP OF CEMENT FOR LEAD 660'. ESTIMATED TOP OF CEMENT FOR TAIL 3500'. STORED 790 BBLS OF 11.5# MUD.</p> <p>RIG DOWN CEMENTERS. FLUSH STACK WITH FRESH WATER.</p>
	10:30 - 11:30	1.00	RDMO	14	A	P		<p>UNSCREW LANDING JT. RUN IN WITH PACK OFF. TURN IN LANDING DOGS. UNSCREW FROM PACK OFF. LAYDOWN LANDING JT. UNDO FLOW LINE. NIPPLE DOWN BOPE. UNDO CHOKE LINE. PICK UP STACK. AND COVER WELL. RELEASE RIG 6/26/2012 11:30.</p>

1 General

1.1 Customer Information

Company	US ROCKIES REGION
Representative	
Address	

1.2 Well/Wellbore Information

Well	BONANZA 1023-5G4DS GREEN	Wellbore No.	OH
Well Name	BONANZA 1023-5G4DS	Wellbore Name	BONANZA 1023-5G4DS
Report No.	1	Report Date	9/5/2012
Project	UTAH-UINTAH	Site	BONANZA 1023-5I PAD
Rig Name/No.		Event	COMPLETION
Start Date	9/5/2012	End Date	9/18/2012
Spud Date	5/31/2012	Active Datum	RKB @5,312.00usft (above Mean Sea Level)
UWI	NE/SE/O/10/S/23/E/5/O/0/26/PM/S/1625/E/O/1048/O/O		

1.3 General

Contractor		Job Method		Supervisor	
Perforated Assembly		Conveyed Method			

1.4 Initial Conditions

Fluid Type		Fluid Density		Gross Interval	5,835.0 (usft)-8,539.0 (usft)	Start Date/Time	5/15/2012 12:00AM
Surface Press		Estimate Res Press		No. of Intervals	48	End Date/Time	5/30/2012 12:00AM
TVD Fluid Top		Fluid Head		Total Shots	216	Net Perforation Interval	58.00 (usft)
Hydrostatic Press		Press Difference		Avg Shot Density	3.72 (shot/ft)	Final Surface Pressure	
Balance Cond	NEUTRAL					Final Press Date	

1.5 Summary

2 Intervals

2.1 Perforated Interval

Date	Formation/ Reservoir	CCL@ (usft)	CCL-T S (usft)	MD Top (usft)	MD Base (usft)	Shot Density (shot/ft)	Misfires/ Add. Shot	Diamete r (in)	Carr Type /Stage No	Carr Size (in)	Phasing (°)	Charge Desc /Charge Manufacturer	Charge Weight (gram)	Reason	Misrun
5/15/2012 12:00AM	WASATCH/			5,835.0	5,836.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	

2.1 Perforated Interval (Continued)

Date	Formation/ Reservoir	CCL@ (usft)	CCL-T S (usft)	MD Top (usft)	MD Base (usft)	Shot Density (shot/ft)	Misfires/ Add. Shot	Diamete r (in)	Carr Type /Stage No	Carr Size (in)	Phasing (°)	Charge Desc /Charge Manufacturer	Charge Weight (gram)	Reason	Misrun
5/15/2012 12:00AM	WASATCH/			5,854.0	5,856.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	WASATCH/			5,999.0	6,001.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	WASATCH/			6,040.0	6,041.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	WASATCH/			6,143.0	6,144.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	WASATCH/			6,219.0	6,221.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	WASATCH/			6,253.0	6,255.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	WASATCH/			6,327.0	6,328.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,004.0	7,006.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,075.0	7,076.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,112.0	7,113.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,147.0	7,149.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,205.0	7,206.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,230.0	7,231.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,271.0	7,272.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,310.0	7,312.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,333.0	7,334.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,383.0	7,384.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,425.0	7,426.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,467.0	7,468.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,479.0	7,480.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,501.0	7,503.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	

2.1 Perforated Interval (Continued)

Date	Formation/ Reservoir	CCL@ (usft)	CCL-T S (usft)	MD Top (usft)	MD Base (usft)	Shot Density (shot/ft)	Misfires/ Add. Shot	Diamete r (in)	Carr Type /Stage No	Carr Size (in)	Phasing (°)	Charge Desc /Charge Manufacturer	Charge Weight (gram)	Reason	Misrun
5/15/2012 12:00AM	MESAVERDE/			7,566.0	7,567.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,626.0	7,627.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,651.0	7,652.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,669.0	7,670.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,678.0	7,679.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,705.0	7,706.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,716.0	7,718.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,782.0	7,783.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,811.0	7,812.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,824.0	7,825.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/15/2012 12:00AM	MESAVERDE/			7,863.0	7,864.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/16/2012 12:00AM	MESAVERDE/			7,910.0	7,911.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/17/2012 12:00AM	MESAVERDE/			7,931.0	7,932.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/18/2012 12:00AM	MESAVERDE/			7,978.0	7,980.0	3.00		0.360	EXP/	3.375	120.00		23.00	PRODUCTIO N	
5/19/2012 12:00AM	MESAVERDE/			8,029.0	8,030.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/20/2012 12:00AM	MESAVERDE/			8,043.0	8,044.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/21/2012 12:00AM	MESAVERDE/			8,073.0	8,074.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/22/2012 12:00AM	MESAVERDE/			8,099.0	8,100.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/23/2012 12:00AM	MESAVERDE/			8,121.0	8,122.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/24/2012 12:00AM	MESAVERDE/			8,197.0	8,198.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/25/2012 12:00AM	MESAVERDE/			8,283.0	8,284.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	

2.1 Perforated Interval (Continued)

Date	Formation/ Reservoir	CCL@ (usft)	CCL-T S (usft)	MD Top (usft)	MD Base (usft)	Shot Density (shot/ft)	Misfires/ Add. Shot	Diamete r (in)	Carr Type /Stage No	Carr Size (in)	Phasing (°)	Charge Desc /Charge Manufacturer	Charge Weight (gram)	Reason	Misrun
5/26/2012 12:00AM	MESAVERDE/			8,300.0	8,301.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/27/2012 12:00AM	MESAVERDE/			8,319.0	8,320.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/28/2012 12:00AM	MESAVERDE/			8,327.0	8,328.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/29/2012 12:00AM	MESAVERDE/			8,422.0	8,423.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	
5/30/2012 12:00AM	MESAVERDE/			8,538.0	8,539.0	4.00		0.360	EXP/	3.375	90.00		23.00	PRODUCTIO N	

3 Plots

3.1 Wellbore Schematic

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: GWS 1/1

Event: COMPLETION

Start Date: 9/5/2012

End Date: 9/18/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
5/31/2012	-							
6/1/2012	-							
9/5/2012	9:00 - 10:30	1.50	FRAC	33	C	P		FILL SURFACE CSG. MIRU B&C QUICK TEST. PSI TEST T/ 1000 PSI. HELD FOR 15 MIN LOST 10 PSI. PSI TEST T/ 3500 PSI. HELD FOR 15 MIN LOST 25 PSI. 1ST PSI TEST T/ 7000 PSI. HELD FOR 30 MIN LOST 82 PSI. NO COMMUNICATION OR MIGRATION WITH SURFACE CSG BLEED OFF PSI. MOVE T/ NEXT WELL. SWFW
9/7/2012	7:00 - 7:15	0.25	COMP	48		P		HELD SAFETY MEETING: SAFETY SIGNS
	7:15 - 10:00	2.75	COMP	37		P		PERF STG 1)PU 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH PERF AS PER PERF DESIGN. POOH. SWFW

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: GWS 1/1

Event: COMPLETION

Start Date: 9/5/2012

End Date: 9/18/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
9/11/2012	8:00 - 18:00	10.00	COMP	36	B	P		<p>FRAC STG 1)WHP 1,325 PSI, BRK 3,406 PSI @ 4.8 BPM. ISIP 2,588 PSI, FG .74. CALC HOLES OPEN @ 50.1 BPM @ 3,800 PSI = 100% HOLES OPEN. (24/24 HOLES OPEN) ISIP 2,251 PSI, FG .70, NPI -337 PSI. MP 5,507 PSI, MR 51.1 BPM, AP 3,947 PSI, AR 49.5 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PERF STG 2)PU 4 1/2 8K HAL CBP & 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH SET CBP @ 8228' P/U PERF AS PER PERF DESIGN. POOH. X-OVER FOR FRAC CREW</p> <p>FRAC STG 2)WHP 1,021 PSI, BRK 5,010 PSI @ 4.6 BPM. ISIP 3,986 PSI, FG .92. CALC HOLES OPEN @ 50.7 BPM @ 4,397 PSI = 100% HOLES OPEN. (24/24 HOLES OPEN) ISIP 2,419 PSI, FG .73, NPI -1,567 PSI. MP 4,419 PSI, MR 50.8 BPM, AP 4,286 PSI, AR 50.7 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PERF STG 3)PU 4 1/2 8K HAL CBP & 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH SET CBP @ 8,010' P/U PERF AS PER PERF DESIGN. POOH. X-OVER FOR FRAC CREW</p> <p>FRAC STG 3)WHP 1,896 PSI, BRK 5,051 PSI @ 4.8 BPM. ISIP 3,051 PSI, FG .82. CALC HOLES OPEN @ 50.1 BPM @ 4,510 PSI = 100% HOLES OPEN. (24/24 HOLES OPEN) ISIP 2,470 PSI, FG .75, NPI -581 PSI. MP 4,583 PSI, MR 50.2 BPM, AP 4,371 PSI, AR 50.1 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PERF STG 4)PU 4 1/2 8K HAL CBP & 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH SET CBP @ 7,748' P/U PERF AS PER PERF DESIGN. POOH. X-OVER FOR FRAC CREW SWIFN.</p>

US ROCKIES REGION

Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: GWS 1/1

Event: COMPLETION

Start Date: 9/5/2012

End Date: 9/18/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
9/12/2012	7:00 - 18:00	11.00	COMP	36	B	P		<p>FRAC STG 4)WHP 366 PSI, BRK 2724 PSI @ 4.9 BPM. ISIP 1747 PSI, FG .66. CALC HOLES OPEN @ 54.7 BPM @ 3725 PSI = 100% HOLES OPEN. (24/24 HOLES OPEN) ISIP 1635 PSI, FG .65, NPI -112 PSI. MP 4449 PSI, MR 54.9 BPM, AP 3712 PSI, AR 54.2 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PERF STG 5)PU 4 1/2 8K HAL CBP & 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH SET CBP @ 7533' P/U PERF AS PER DESIGN. POOH, XO T/ FRAC.</p> <p>FRAC STG 5)WHP 1400 PSI, BRK 3736 PSI @ 5.0 BPM. ISIP 2089 PSI, FG .71. CALC HOLES OPEN @ 55.1 BPM @ 3464 PSI = 100% HOLES OPEN. (24/24 HOLES OPEN) ISIP 1609 PSI, FG .65, NPI -480 PSI. MP 3589 PSI, MR 55.3 BPM, AP 3439 PSI, AR 55.2 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PERF STG 6)PU 4 1/2 8K HAL CBP & 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH SET CBP @ 7364' P/U PERF AS PER DESIGN. POOH, XO T/ FRAC.</p> <p>FRAC STG 6)WHP 632 PSI, BRK 1846 PSI @ 4.7 BPM. ISIP 1190 PSI, FG .60. CALC HOLES OPEN @ 55 BPM @ 3020 PSI = 100% HOLES OPEN. (24/24 HOLES OPEN) ISIP 1589 PSI, FG .65, NPI 399 PSI. MP 3228 PSI, MR 55.2 BPM, AP 3178 PSI, AR 55 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PERF STG 7)PU 4 1/2 8K HAL CBP & 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH SET CBP @ 7179' P/U PERF AS PER DESIGN. POOH, SWFN. HSM. HIGH PSI LINES.</p>
9/13/2012	6:45 - 7:00	0.25	COMP	48		P		

US ROCKIES REGION

Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: GWS 1/1

Event: COMPLETION

Start Date: 9/5/2012

End Date: 9/18/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	7:00 - 18:00	11.00	COMP	36	B	P		<p>FRAC STG 7)WHP 105 PSI, BRK 2319 PSI @ 4.7 BPM. ISIP 1248 PSI, FG .61. CALC HOLES OPEN @ 54.5 BPM @ 3650 PSI = 100% HOLES OPEN. (24/24 HOLES OPEN) ISIP 1725 PSI, FG .68, NPI 477 PSI. MP 4053 PSI, MR 54.6 BPM, AP 3878 PSI, AR 54.5 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PERF STG 8)PU 4 1/2 8K HAL CBP & 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH SET CBP @ 6358' P/U PERF AS PER DESIGN. POOH, XO T/ FRAC.</p> <p>FRAC STG 8)WHP 105 PSI, BRK 1960 PSI @ 4.9 BPM. ISIP 1104 PSI, FG .61. CALC HOLES OPEN @ 54.7 BPM @ 3940 PSI = 88% HOLES OPEN. (21/24 HOLES OPEN) ISIP 2026 PSI, FG .76, NPI 922 PSI. MP 4182 PSI, MR 54.8 BPM, AP 3903 PSI, AR 50.5 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PERF STG 9)PU 4 1/2 8K HAL CBP & 3 1/8 EXP GUN, 23 GM, .36 HOLE SIZE. 90 DEG PHASING. RIH SET CBP @ 6071' P/U PERF AS PER DESIGN. POOH, XO T/ FRAC.</p> <p>FRAC STG 9)WHP 1032 PSI, BRK 1323 PSI @ 5.0 BPM. ISIP 1108 PSI, FG .62. CALC HOLES OPEN @ 55 BPM @ 3142 PSI = 100% HOLES OPEN. (24/24 HOLES OPEN) ISIP 1467 PSI, FG .68, NPI 359 PSI. MP 3186 PSI, MR 55 BPM, AP 3141 PSI, AR 54.9 BPM PUMPED 30/50 OTTAWA SAND IN THIS STAGE X-OVER FOR W L</p> <p>PU 4 1/2 8K HAL CBP. RIH SET KILL PLUG @ 5785'. POOH, SWI. DONE FRACING THIS WELL.</p> <p>TOTAL SAND = 220,300 LBS TOTAL CLFL = 10,189 BBL HSM, SLIPS, TRIPS & FALLS, PU TBG, D/O PLUGS</p>
9/18/2012	7:00 - 7:15	0.25	DRLOUT	48		P		

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: GWS 1/1

Event: COMPLETION

Start Date: 9/5/2012

End Date: 9/18/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
	7:15 - 18:00	10.75	DRLOUT	31	I	P		<p>(MIRU 9/17/12), SPOT TBG TRAILER, PU BHA, TALLY & PU TBG, RU P/S, FILL TBG & BREAK CIRC, P/T BOP TO 3,000 PSI, SURFACE CSG VALVE OPEN & LOCKED, D/O PLUGS.</p> <p>C/O 20' SAND, TAG 1ST PLUG @ 5,785' DRL PLUG IN 12 MIN. 0 PSI INCREASE WELL WENT ON VACUMN RIH, CSG PRESS 0 PSI. ((NO FLOW W/O PUMP))</p> <p>C/O 30' SAND, TAG 2ND PLUG @ 6,071' DRL PLUG IN 10 MIN. 0 PSI INCREASE WELL WENT ON VACUMN RIH, CSG PRESS 0 PSI. ((NO FLOW W/O PUMP))</p> <p>C/O 25' SAND, TAG 3RD PLUG @ 6,358' DRL PLUG IN 12 MIN. 400 PSI INCREASE RIH, CSG PRESS 150 PSI.</p> <p>C/O 20' SAND, TAG 4TH PLUG @ 7,179' DRL PLUG IN 13 MIN. 500 PSI INCREASE RIH, CSG PRESS 250 PSI.</p> <p>C/O 25' SAND, TAG 5TH PLUG @ 7,364' DRL PLUG IN 12 MIN. 400 PSI INCREASE RIH, CSG PRESS 200 PSI.</p> <p>C/O 30' SAND, TAG 6TH PLUG @ 7,533' DRL PLUG IN 11 MIN. 300 PSI INCREASE RIH, CSG PRESS 300 PSI.</p> <p>C/O 45' SAND, TAG 7TH PLUG @ 7,748' DRL PLUG IN 14 MIN. 300 PSI INCREASE RIH, CSG PRESS 450 PSI.</p> <p>C/O 25' SAND, TAG 8TH PLUG @ 8,010' DRL PLUG IN 12 MIN. 400 PSI INCREASE RIH, CSG PRESS 300 PSI.</p> <p>C/O 25' SAND, TAG 9TH PLUG @ 8,228' DRL PLUG IN 10 MIN. 400 PSI INCREASE RIH, CSG PRESS 400 PSI.</p> <p>PBTD @ 8,564', BTM PERF @ 8,539', RIH TAGGED @ 8,545', C/O TO PBTD @ 8,564', 25' PAST BTM PERF W/ 270 JTS 2 3/8" L-80 TBG, LD 18 JTS, PU & STRIP IN TBG HANGER & LAND TBG W/ 252 JTS 2 3/8" L-80, EOT 8,001.71'.</p> <p>RD POWER SWIVEL, FLOOR & TBG EQUIP, ND BOPS, NU WH, DROP BALL TO SHEAR OFF BIT W/ 2,400 PSI, LET BIT FALL FOR 20 MIN. P/T FLOW LINE FROM WH TO HAL 9000 TO 3,000 PSI W/ RIG PUMP, NO VISIBLE LEAKS.</p> <p>TURN OVER TO DELSCO FLOW BACK CREW, WILL</p>

US ROCKIES REGION
Operation Summary Report

Well: BONANZA 1023-5G4DS GREEN

Spud Date: 5/31/2012

Project: UTAH-UINTAH

Site: BONANZA 1023-5I PAD

Rig Name No: GWS 1/1

Event: COMPLETION

Start Date: 9/5/2012

End Date: 9/18/2012

Active Datum: RKB @5,312.00usft (above Mean Sea Level)

UWI: NE/SE/0/10/S/23/E/5/0/0/26/PM/S/1625/E/0/1048/0/0

Date	Time Start-End	Duration (hr)	Phase	Code	Sub Code	P/U	MD From (usft)	Operation
								RD & MOVE IN AM, SDFN.
								KB= 15'
								4 1/16" CAMERON HANGER = .83' TBG
								DELIVERED 283 JTS
								252 JTS 2 3/8" L-80 = 7,983.68'
								TBG USED 252 JTS
								POBS= 2.20'
								TBG RETURNED 31 JTS
								EOT @ 8,001.71'
								TWTR= 10,189 BBLS
								TWR= 3,000 BBLS
								TWLTR= 7,189 BBLS
								WELL TURNED TO SALES @ 1730 HR ON
								9/18/2012, 1200 MCFD, 1680 BWPD, FCP 1525#, FTP
								1500# , 20/64" CK.
	18:00 - 18:00	0.00	DRLOUT	50				

Project: UTAH - UTM (feet), NAD27, Zone 12N
Site: UINTAH_BONANZA 1023-5I PAD
Well: BONANZA 1023-5G4DS
Wellbore: BONANZA 1023-5G4DS
Section:
SHL:
Design: BONANZA 1023-5G4DS (wp01)
Latitude: 39.975214
Longitude: -109.344386
GL: 5297.00
KB: 5297' GL + 15' GL @ 5312.00ft

FORMATION TOP DETAILS		
TVDPath	MDPath	Formation
4203.00	4378.56	WASATCH
4803.00	4978.68	top of cylinder
6246.00	6421.71	MESAVERDE
8432.00	8607.74	SEGO

WELL DETAILS: BONANZA 1023-5G4DS						
+N/-S	+E/-W	Northing	Ground Level: Easting	5297.00 Latitude	Longitude	Slot
0.00	0.00	14521325.14	2104264.12	39.975214	-109.344386	



CASING DETAILS			
TVD	MD	Name	Size
2353.42	2443.52	8-5/8	8-5/8



Azimuths to True North
Magnetic North: 10.88°
Magnetic Field
Strength: 52237.4nT
Dip Angle: 65.85°
Date: 6/5/2012
Model: IGRF2010

DESIGN TARGET DETAILS									
Name	TVD	+N/-S	+E/-W	Northing	Easting	Latitude	Longitude	Shape	
DRILLERS TARGET (BONANZA 1023-5G4DS)	4385.60	1043.83	-385.21	14522361.64	2103859.59	39.978080	-109.345761	Circle (Radius: 15.00)	
INTERCEPT (BONANZA 1023-5G4DS)	4803.00	1042.01	-384.30	14522359.83	2103860.54	39.978075	-109.345757	Point	
BONANZA 1023-5G4DS BHL	8432.00	1023.83	-375.21	14522341.83	2103869.96	39.978025	-109.345725	Circle (Radius: 25.00)	

SECTION DETAILS								
MD	Inc	Azi	TVD	+N/-S	+E/-W	Dleg	TFace	VSect
2406.00	19.70	336.79	2318.10	517.17	-188.74	0.00	0.00	550.54
2601.54	19.70	339.71	2502.19	578.38	-213.16	0.50	91.45	616.40
3576.34	19.70	339.71	3419.95	886.58	-327.08	0.00	0.00	944.98
4561.28	0.00	0.00	4385.60	1043.83	-385.21	2.00	180.00	1112.64
4668.22	0.32	153.43	4492.54	1043.56	-385.08	0.30	153.43	1112.34
8607.74	0.32	153.43	8432.00	1023.83	-375.21	0.00	0.00	1090.42

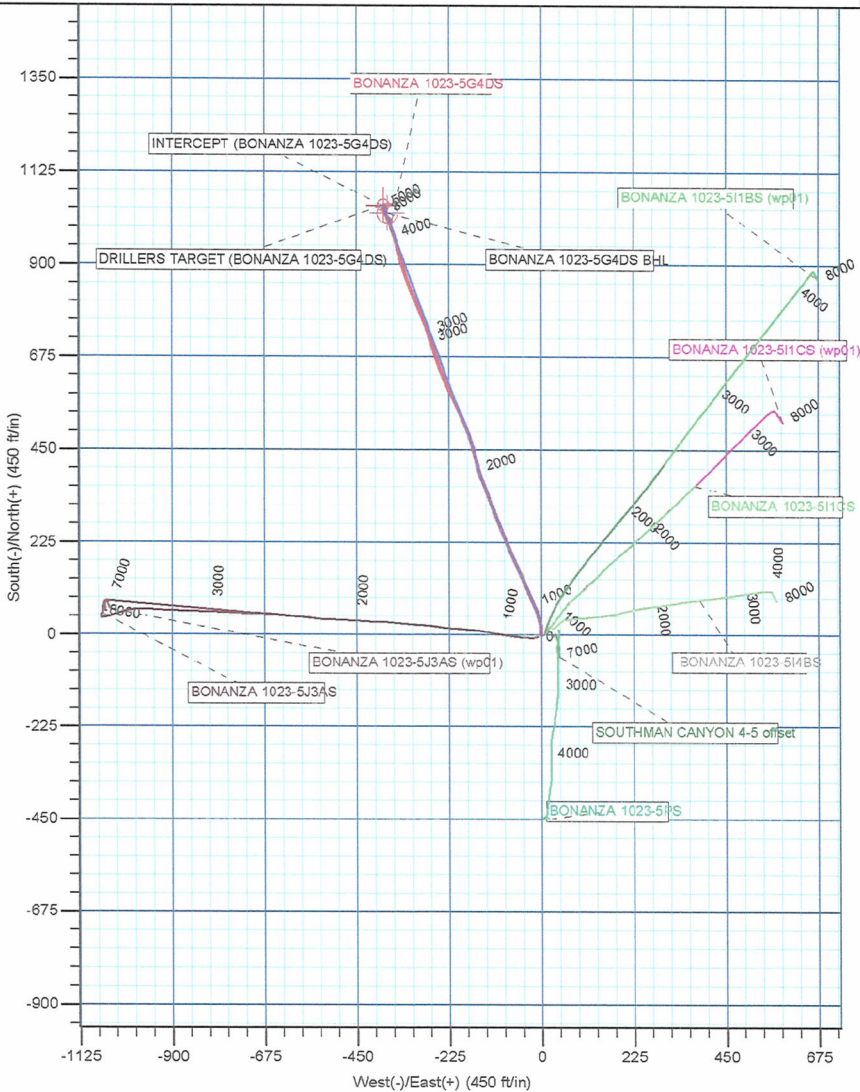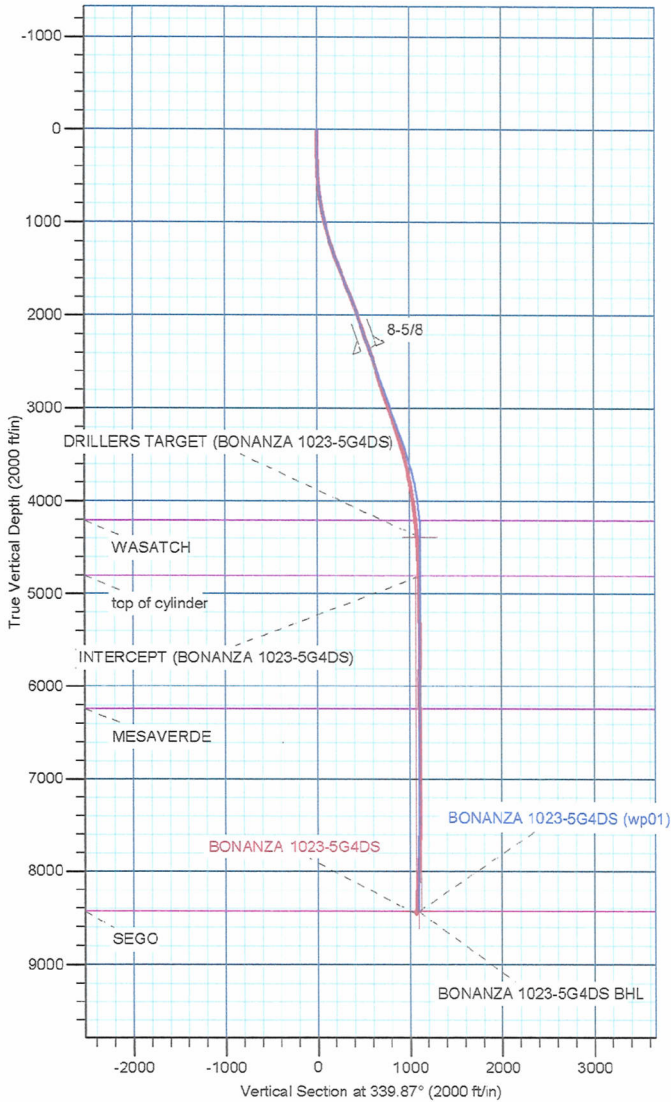

US ROCKIES REGION PLANNING

UTAH - UTM (feet), NAD27, Zone 12N

UINTAH_BONANZA 1023-5I PAD

BONANZA 1023-5G4DS

BONANZA 1023-5G4DS

Design: BONANZA 1023-5G4DS

Standard Survey Report

10 July, 2012

Anadarko Petroleum Corp

Survey Report

Company:	US ROCKIES REGION PLANNING	Local Co-ordinate Reference:	Well BONANZA 1023-5G4DS
Project:	UTAH - UTM (feet), NAD27, Zone 12N	TVD Reference:	5297' GL + 15' GL @ 5312.00ft
Site:	UINTAH_BONANZA 1023-5I PAD	MD Reference:	5297' GL + 15' GL @ 5312.00ft
Well:	BONANZA 1023-5G4DS	North Reference:	True
Wellbore:	BONANZA 1023-5G4DS	Survey Calculation Method:	Minimum Curvature
Design:	BONANZA 1023-5G4DS	Database:	edmp

Project	UTAH - UTM (feet), NAD27, Zone 12N		
Map System:	Universal Transverse Mercator (US Survey Feet)	System Datum:	Mean Sea Level
Geo Datum:	NAD 1927 (NADCON CONUS)		
Map Zone:	Zone 12N (114 W to 108 W)		

Site	UINTAH_BONANZA 1023-5I PAD				
Site Position:		Northing:	14,521,340.20 usft	Latitude:	39.975254
From:	Lat/Long	Easting:	2,104,289.90 usft	Longitude:	-109.344293
Position Uncertainty:	0.00 ft	Slot Radius:	13-3/16 "	Grid Convergence:	1.06 °

Well	BONANZA 1023-5G4DS					
Well Position	+N/-S	0.00 ft	Northing:	14,521,325.15 usft	Latitude:	39.975214
	+E/-W	0.00 ft	Easting:	2,104,264.11 usft	Longitude:	-109.344386
Position Uncertainty		0.00 ft	Wellhead Elevation:	ft	Ground Level:	5,297.00 ft

Wellbore	BONANZA 1023-5G4DS				
Magnetics	Model Name	Sample Date	Declination	Dip Angle	Field Strength
	IGRF2010	6/5/2012	(°)	(°)	(nT)
			10.88	65.85	52,237

Design	BONANZA 1023-5G4DS				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	11.00
Vertical Section:	Depth From (TVD)	+N/-S	+E/-W	Direction	
	(ft)	(ft)	(ft)	(°)	
	0.00	0.00	0.00	340.00	

Survey Program	Date	7/10/2012		
From	To	Survey (Wellbore)	Tool Name	Description
(ft)	(ft)			
184.00	2,406.00	Survey #1 (BONANZA 1023-5G4DS)	MWD	MWD - STANDARD
2,472.00	8,625.00	Survey #2 (BONANZA 1023-5G4DS)	MWD	MWD - STANDARD

Survey										
Measured	Inclination	Azimuth	Vertical	+N/-S	+E/-W	Vertical	Dogleg	Build	Turn	
Depth	(°)	(°)	Depth	(ft)	(ft)	Section	Rate	Rate	Rate	
(ft)			(ft)			(ft)	(°/100usft)	(°/100usft)	(°/100usft)	
11.00	0.00	0.00	11.00	0.00	0.00	0.00	0.00	0.00	0.00	
184.00	0.26	227.89	184.00	-0.26	-0.29	-0.15	0.15	0.15	0.00	
269.00	0.53	350.06	269.00	-0.01	-0.50	0.17	0.83	0.32	143.73	
352.00	1.58	351.64	351.98	1.50	-0.73	1.67	1.27	1.27	1.90	
442.00	2.90	355.15	441.91	5.00	-1.11	5.08	1.47	1.47	3.90	
532.00	4.84	356.30	531.70	11.06	-1.55	10.92	2.16	2.16	1.28	
622.00	6.33	358.49	621.27	19.81	-1.92	19.27	1.67	1.66	2.43	
712.00	7.29	348.14	710.64	30.36	-3.23	29.63	1.73	1.07	-11.50	
802.00	9.15	340.65	799.71	42.70	-6.77	42.44	2.38	2.07	-8.32	
892.00	11.19	337.15	888.30	57.50	-12.53	58.32	2.37	2.27	-3.89	

Anadarko Petroleum Corp

Survey Report

Company: US ROCKIES REGION PLANNING
Project: UTAH - UTM (feet), NAD27, Zone 12N
Site: UINTAH_BONANZA 1023-5I PAD
Well: BONANZA 1023-5G4DS
Wellbore: BONANZA 1023-5G4DS
Design: BONANZA 1023-5G4DS

Local Co-ordinate Reference: Well BONANZA 1023-5G4DS
TVD Reference: 5297' GL + 15' GL @ 5312.00ft
MD Reference: 5297' GL + 15' GL @ 5312.00ft
North Reference: True
Survey Calculation Method: Minimum Curvature
Database: edmp

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
982.00	13.23	336.85	976.26	75.02	-19.97	77.32	2.27	2.27	-0.33
1,072.00	15.30	337.22	1,063.48	95.44	-28.62	99.47	2.30	2.30	0.41
1,162.00	17.06	337.58	1,149.91	118.59	-38.25	124.52	1.96	1.96	0.40
1,252.00	18.55	336.35	1,235.60	143.91	-49.03	152.00	1.71	1.66	-1.37
1,342.00	20.18	335.48	1,320.50	171.15	-61.22	181.77	1.84	1.81	-0.97
1,432.00	21.63	336.26	1,404.57	200.46	-74.34	213.80	1.64	1.61	0.87
1,522.00	20.93	337.31	1,488.44	230.47	-87.22	246.41	0.89	-0.78	1.17
1,612.00	19.96	336.43	1,572.77	259.39	-99.56	277.80	1.13	-1.08	-0.98
1,702.00	21.54	340.04	1,656.93	289.00	-111.35	309.65	2.26	1.76	4.01
1,792.00	22.95	339.51	1,740.23	320.97	-123.13	343.72	1.58	1.57	-0.59
1,882.00	21.02	338.02	1,823.68	352.37	-135.31	377.40	2.23	-2.14	-1.66
1,972.00	18.99	340.14	1,908.25	381.12	-146.33	408.18	2.39	-2.26	2.36
2,062.00	18.03	344.61	1,993.60	408.32	-155.00	436.71	1.90	-1.07	4.97
2,152.00	19.07	346.85	2,078.92	436.07	-162.05	465.19	1.40	1.16	2.49
2,242.00	19.79	343.29	2,163.80	464.98	-169.77	495.00	1.54	0.80	-3.96
2,332.00	19.87	339.69	2,248.46	493.92	-179.46	525.51	1.36	0.09	-4.00
2,406.00	19.70	336.79	2,318.10	517.17	-188.74	550.54	1.35	-0.23	-3.92
FIRST MWD SURVEY									
2,472.00	19.71	335.25	2,380.23	537.50	-197.79	572.74	0.79	0.02	-2.33
2,562.00	18.54	332.85	2,465.27	564.02	-210.67	602.06	1.57	-1.30	-2.67
2,653.00	17.73	333.90	2,551.74	589.34	-223.37	630.19	0.96	-0.89	1.15
2,744.00	16.44	335.80	2,638.73	613.53	-234.74	656.81	1.54	-1.42	2.09
2,835.00	16.38	339.30	2,726.02	637.28	-244.56	682.49	1.09	-0.07	3.85
2,926.00	18.25	341.30	2,812.90	662.78	-253.66	709.57	2.16	2.05	2.20
3,016.00	18.81	341.67	2,898.23	689.90	-262.74	738.16	0.64	0.62	0.41
3,107.00	20.31	344.55	2,983.98	719.05	-271.56	768.57	1.96	1.65	3.16
3,198.00	18.88	338.92	3,069.71	748.02	-281.07	799.04	2.60	-1.57	-6.19
3,289.00	18.31	336.30	3,155.96	774.84	-292.11	828.02	1.11	-0.63	-2.88
3,379.00	17.94	337.42	3,241.50	800.59	-303.11	855.98	0.56	-0.41	1.24
3,470.00	17.19	337.67	3,328.25	825.97	-313.61	883.41	0.83	-0.82	0.27
3,561.00	17.06	340.05	3,415.22	850.95	-323.27	910.20	0.78	-0.14	2.62
3,652.00	15.81	341.17	3,502.50	875.23	-331.82	935.94	1.42	-1.37	1.23
3,742.00	12.75	342.05	3,589.71	896.29	-338.84	958.13	3.41	-3.40	0.98
3,833.00	11.94	342.80	3,678.61	914.84	-344.72	977.57	0.91	-0.89	0.82
3,924.00	11.25	347.17	3,767.75	932.48	-349.48	995.78	1.23	-0.76	4.80
4,015.00	9.88	345.55	3,857.21	948.70	-353.40	1,012.36	1.54	-1.51	-1.78
4,105.00	10.13	344.42	3,945.84	963.80	-357.45	1,027.93	0.35	0.28	-1.26
4,196.00	9.13	341.67	4,035.55	978.36	-361.87	1,043.13	1.21	-1.10	-3.02
4,287.00	6.44	339.05	4,125.71	989.99	-365.97	1,055.45	2.98	-2.96	-2.88
4,378.00	5.19	337.55	4,216.24	998.56	-369.36	1,064.67	1.38	-1.37	-1.65
4,468.00	4.38	336.67	4,305.92	1,005.47	-372.28	1,072.16	0.90	-0.90	-0.98
4,559.00	3.63	334.55	4,396.70	1,011.27	-374.89	1,078.50	0.84	-0.82	-2.33
4,650.00	2.88	334.55	4,487.55	1,015.93	-377.11	1,083.64	0.82	-0.82	0.00

Anadarko Petroleum Corp

Survey Report

Company: US ROCKIES REGION PLANNING
Project: UTAH - UTM (feet), NAD27, Zone 12N
Site: UINTAH_BONANZA 1023-5I PAD
Well: BONANZA 1023-5G4DS
Wellbore: BONANZA 1023-5G4DS
Design: BONANZA 1023-5G4DS

Local Co-ordinate Reference: Well BONANZA 1023-5G4DS
TVD Reference: 5297' GL + 15' GL @ 5312.00ft
MD Reference: 5297' GL + 15' GL @ 5312.00ft
North Reference: True
Survey Calculation Method: Minimum Curvature
Database: edmp

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
4,741.00	2.63	333.55	4,578.45	1,019.87	-379.02	1,087.99	0.28	-0.27	-1.10
4,832.00	2.31	338.17	4,669.36	1,023.44	-380.64	1,091.90	0.41	-0.35	5.08
4,922.00	1.88	342.42	4,759.30	1,026.53	-381.76	1,095.19	0.51	-0.48	4.72
5,013.00	1.75	341.05	4,850.26	1,029.27	-382.66	1,098.07	0.15	-0.14	-1.51
5,104.00	1.25	340.80	4,941.22	1,031.52	-383.44	1,100.45	0.55	-0.55	-0.27
5,195.00	1.25	350.42	5,032.20	1,033.43	-383.93	1,102.42	0.23	0.00	10.57
5,286.00	1.19	343.05	5,123.18	1,035.32	-384.37	1,104.34	0.18	-0.07	-8.10
5,376.00	0.94	343.42	5,213.17	1,036.92	-384.85	1,106.01	0.28	-0.28	0.41
5,467.00	0.63	343.05	5,304.16	1,038.11	-385.21	1,107.26	0.34	-0.34	-0.41
5,558.00	0.44	351.30	5,395.15	1,038.93	-385.41	1,108.10	0.22	-0.21	9.07
5,649.00	0.31	68.30	5,486.15	1,039.37	-385.23	1,108.45	0.53	-0.14	84.62
5,740.00	0.50	130.17	5,577.15	1,039.21	-384.70	1,108.11	0.49	0.21	67.99
5,831.00	0.94	136.67	5,668.14	1,038.41	-383.89	1,107.08	0.49	0.48	7.14
5,921.00	1.06	125.67	5,758.13	1,037.38	-382.70	1,105.72	0.25	0.13	-12.22
6,012.00	1.38	126.80	5,849.11	1,036.24	-381.14	1,104.10	0.35	0.35	1.24
6,103.00	0.94	113.42	5,940.09	1,035.28	-379.58	1,102.67	0.56	-0.48	-14.70
6,194.00	1.06	113.30	6,031.08	1,034.65	-378.12	1,101.58	0.13	0.13	-0.13
6,284.00	0.44	38.30	6,121.07	1,034.60	-377.14	1,101.19	1.15	-0.69	-83.33
6,375.00	0.94	12.05	6,212.06	1,035.60	-376.77	1,102.01	0.64	0.55	-28.85
6,466.00	1.63	330.92	6,303.04	1,037.46	-377.24	1,103.92	1.22	0.76	-45.20
6,557.00	1.31	320.57	6,394.01	1,039.40	-378.53	1,106.18	0.46	-0.35	-11.37
6,647.00	0.81	323.92	6,484.00	1,040.71	-379.56	1,107.76	0.56	-0.56	3.72
6,738.00	0.50	326.80	6,574.99	1,041.56	-380.16	1,108.77	0.34	-0.34	3.16
6,829.00	0.31	285.67	6,665.99	1,041.96	-380.61	1,109.30	0.37	-0.21	-45.20
6,920.00	0.75	193.05	6,756.98	1,041.44	-380.98	1,108.94	0.91	0.48	-101.78
7,011.00	0.69	270.67	6,847.98	1,040.87	-381.67	1,108.63	0.99	-0.07	85.30
7,101.00	0.50	283.05	6,937.97	1,040.96	-382.59	1,109.04	0.25	-0.21	13.76
7,192.00	0.38	232.17	7,028.97	1,040.87	-383.22	1,109.16	0.43	-0.13	-55.91
7,283.00	0.50	206.67	7,119.97	1,040.33	-383.63	1,108.80	0.25	0.13	-28.02
7,374.00	0.50	195.42	7,210.97	1,039.59	-383.92	1,108.20	0.11	0.00	-12.36
7,465.00	0.81	170.42	7,301.96	1,038.57	-383.91	1,107.25	0.46	0.34	-27.47
7,555.00	0.81	214.80	7,391.95	1,037.42	-384.17	1,106.25	0.68	0.00	49.31
7,646.00	1.00	260.55	7,482.94	1,036.77	-385.32	1,106.03	0.80	0.21	50.27
7,737.00	1.00	236.55	7,573.93	1,036.20	-386.77	1,105.99	0.46	0.00	-26.37
7,828.00	1.25	182.05	7,664.91	1,034.77	-387.47	1,104.89	1.16	0.27	-59.89
7,918.00	1.88	146.17	7,754.88	1,032.56	-386.68	1,102.54	1.26	0.70	-39.87
8,009.00	2.44	143.92	7,845.82	1,029.75	-384.71	1,099.23	0.62	0.62	-2.47
8,100.00	2.56	145.67	7,936.73	1,026.51	-382.42	1,095.40	0.16	0.13	1.92
8,191.00	2.88	149.05	8,027.63	1,022.87	-380.10	1,091.19	0.39	0.35	3.71
8,281.00	3.19	147.17	8,117.50	1,018.83	-377.58	1,086.53	0.36	0.34	-2.09
8,372.00	3.44	146.42	8,208.35	1,014.43	-374.70	1,081.40	0.28	0.27	-0.82
8,463.00	3.56	139.42	8,299.18	1,010.01	-371.35	1,076.10	0.49	0.13	-7.69
8,575.00	3.56	140.39	8,410.96	1,004.69	-366.87	1,069.57	0.05	0.00	0.87

LAST MWD SURVEY

Anadarko Petroleum Corp

Survey Report

Company: US ROCKIES REGION PLANNING
Project: UTAH - UTM (feet), NAD27, Zone 12N
Site: UINTAH_BONANZA 1023-5I PAD
Well: BONANZA 1023-5G4DS
Wellbore: BONANZA 1023-5G4DS
Design: BONANZA 1023-5G4DS

Local Co-ordinate Reference: Well BONANZA 1023-5G4DS
TVD Reference: 5297' GL + 15' GL @ 5312.00ft
MD Reference: 5297' GL + 15' GL @ 5312.00ft
North Reference: True
Survey Calculation Method: Minimum Curvature
Database: edmp

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100usft)	Build Rate (°/100usft)	Turn Rate (°/100usft)
8,625.00	3.56	140.39	8,460.87	1,002.29	-364.89	1,066.65	0.00	0.00	0.00
PROJECTION TO TD									

Checked By: _____ Approved By: _____ Date: _____
