

| STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS AND MINING | | | | | | FORM 3 AMENDED REPORT | | | | |
|--|------------------|-------------|--|--------------------------------|--|--|-----------------------------|-------|-------|--------|
| APPLICATION FOR PERMIT TO DRILL | | | | | | 1. WELL NAME and NUMBER GMBU P-32-8-18 | | | | |
| 2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/> | | | | | | 3. FIELD OR WILDCAT MONUMENT BUTTE | | | | |
| 4. TYPE OF WELL Oil Well Coalbed Methane Well: NO | | | | | | 5. UNIT or COMMUNITIZATION AGREEMENT NAME GMBU (GRRV) | | | | |
| 6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY | | | | | | 7. OPERATOR PHONE 435 646-4825 | | | | |
| 8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052 | | | | | | 9. OPERATOR E-MAIL mcrozier@newfield.com | | | | |
| 10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU-74404 | | | 11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/> | | | 12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/> | | | | |
| 13. NAME OF SURFACE OWNER (if box 12 = 'fee') | | | | | | 14. SURFACE OWNER PHONE (if box 12 = 'fee') | | | | |
| 15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee') | | | | | | 16. SURFACE OWNER E-MAIL (if box 12 = 'fee') | | | | |
| 17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN') | | | 18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/> | | | 19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/> | | | | |
| 20. LOCATION OF WELL | FOOTAGES | | QTR-QTR | SECTION | TOWNSHIP | RANGE | MERIDIAN | | | |
| LOCATION AT SURFACE | 2163 FSL 736 FEL | | NESE | 31 | 8.0 S | 18.0 E | S | | | |
| Top of Uppermost Producing Zone | 1687 FSL 281 FEL | | NESE | 31 | 8.0 S | 18.0 E | S | | | |
| At Total Depth | 1235 FSL 119 FWL | | SWSW | 32 | 8.0 S | 18.0 E | S | | | |
| 21. COUNTY UINTAH | | | 22. DISTANCE TO NEAREST LEASE LINE (Feet) 119 | | 23. NUMBER OF ACRES IN DRILLING UNIT 20 | | | | | |
| | | | 25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 861 | | 26. PROPOSED DEPTH MD: 6518 TVD: 6375 | | | | | |
| 27. ELEVATION - GROUND LEVEL 4981 | | | 28. BOND NUMBER WYB000493 | | 29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 437478 | | | | | |
| Hole, Casing, and Cement Information | | | | | | | | | | |
| String | Hole Size | Casing Size | Length | Weight | Grade & Thread | Max Mud Wt. | Cement | Sacks | Yield | Weight |
| SURF | 12.25 | 8.625 | 0 - 300 | 24.0 | J-55 ST&C | 8.3 | Class G | 138 | 1.17 | 15.8 |
| PROD | 7.875 | 5.5 | 0 - 6518 | 15.5 | J-55 LT&C | 8.3 | Premium Lite High Strength | 312 | 3.26 | 11.0 |
| | | | | | | | 50/50 Poz | 363 | 1.24 | 14.3 |
| ATTACHMENTS | | | | | | | | | | |
| VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES | | | | | | | | | | |
| <input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER | | | | | <input checked="" type="checkbox"/> COMPLETE DRILLING PLAN | | | | | |
| <input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE) | | | | | <input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER | | | | | |
| <input checked="" type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED) | | | | | <input checked="" type="checkbox"/> TOPOGRAPHICAL MAP | | | | | |
| NAME Mandie Crozier | | | | TITLE Regulatory Tech | | | PHONE 435 646-4825 | | | |
| SIGNATURE | | | | DATE 04/30/2012 | | | EMAIL mcrozier@newfield.com | | | |
| API NUMBER ASSIGNED 43047525940000 | | | | APPROVAL Permit Manager | | | | | | |

NEWFIELD PRODUCTION COMPANY
GMBU P-32-8-18
AT SURFACE: NE/SE SECTION 31, T8S R18E
UINTAH COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

| | |
|--------------------|--------------|
| Uinta | 0' – 1580' |
| Green River | 1580' |
| Wasatch | 6225' |
| Proposed TD | 6518' |

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil) 1580' – 6225'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

| | |
|--|---|
| Location & Sampled Interval | Date Sampled |
| Flow Rate | Temperature |
| Hardness | pH |
| Water Classification (State of Utah) | Dissolved Calcium (Ca) (mg/l) |
| Dissolved Iron (Fe) (ug/l) | Dissolved Sodium (Na) (mg/l) |
| Dissolved Magnesium (Mg) (mg/l) | Dissolved Carbonate (CO ₃) (mg/l) |
| Dissolved Bicarbonate (NaHCO ₃) (mg/l) | Dissolved Chloride (Cl) (mg/l) |
| Dissolved Sulfate (SO ₄) (mg/l) | Dissolved Total Solids (TDS) (mg/l) |

4. **PROPOSED CASING PROGRAM**

a. Casing Design: GMBU P-32-8-18

| Size | Interval | | Weight | Grade | Coupling | Design Factors | | |
|--------------------------|----------|--------|--------|-------|----------|----------------|----------------|------------------|
| | Top | Bottom | | | | Burst | Collapse | Tension |
| Surface casing 8-5/8" | 0' | 300' | 24.0 | J-55 | STC | 2,950 17.53 | 1,370 14.35 | 244,000 33.89 |
| Prod casing 5-1/2" | 0' | 6,518' | 15.5 | J-55 | LTC | 4,810 2.32 | 4,040 1.95 | 217,000 2.15 |

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg
 Pore pressure at surface casing shoe = 8.33 ppg
 Pore pressure at prod casing shoe = 8.33 ppg
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. Cementing Design: GMBU O-32-8-18

| Job | Fill | Description | Sacks | OH Excess* | Weight (ppg) | Yield (ft ³ /sk) |
|---------------------|--------|-------------------------------------|-----------------|---------------|-----------------|--------------------------------|
| | | | ft ³ | | | |
| Surface casing | 300' | Class G w/ 2% CaCl | 138 161 | 30% | 15.8 | 1.17 |
| Prod casing Lead | 4,518' | Prem Lite II w/ 10% gel + 3% KCl | 312 1018 | 30% | 11.0 | 3.26 |
| Prod casing Tail | 2,000' | 50/50 Poz w/ 2% gel + 3% KCl | 363 451 | 30% | 14.3 | 1.24 |

*Actual volume pumped will be 15% over the caliper log

- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ± 300 feet will be drilled with an air/mist system. The air rig is equipped with a 6 1/2" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ± 300 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.


9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated


bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.

10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the third quarter of 2012, and take approximately seven (7) days from spud to rig release.

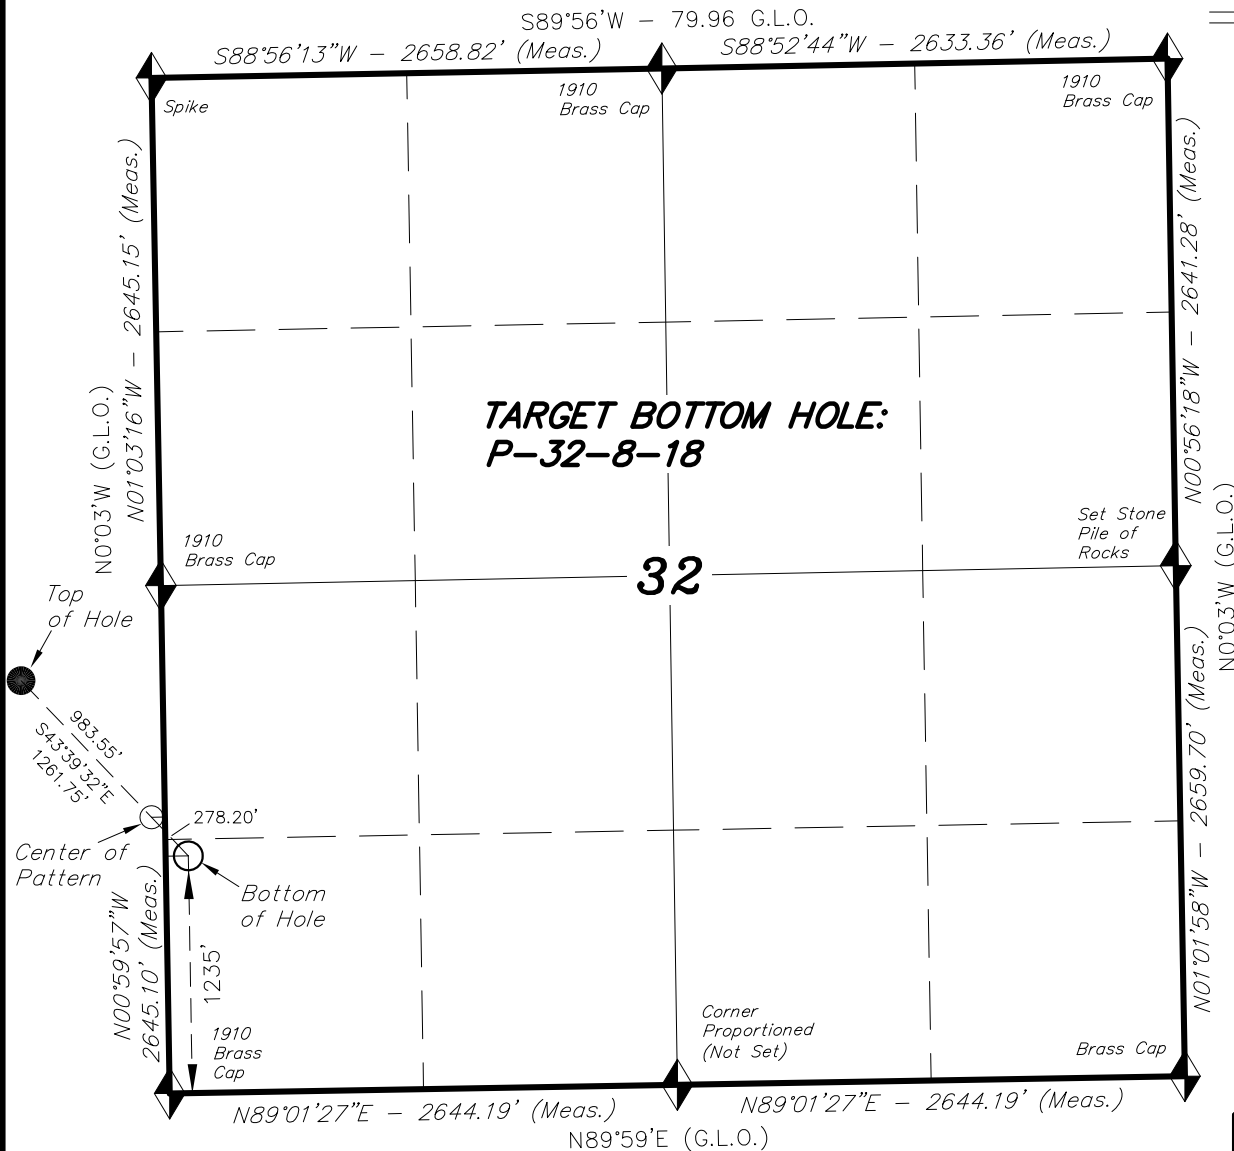T8S, R18E, S.L.B.&M.**NEWFIELD EXPLORATION COMPANY**


TARGET BOTTOM HOLE, P-32-8-18,
LOCATED AS SHOWN IN THE SW 1/4
SW 1/4 OF SECTION 32, T8S, R18E,
S.L.B.&M. UTAH COUNTY, UTAH.

**NOTES:**

1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.
4. The Bottom of Hole footages are 1235' FSL & 119' FWL.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
MADE BY ME OR UNDER MY SUPERVISION AND THAT
THE SAME ARE TRUE AND CORRECT TO THE BEST
OF MY KNOWLEDGE AND BELIEF.



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are based on
an N.G.S. OPUS Correction. LOCATION:
LAT. 40°04'09.56" LONG. 110°00'43.28"
(Tristate Aluminum Cap) Elev. 5281.57'


TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

| | | |
|----------------------------|-------------------|----------|
| DATE SURVEYED: 08-16-11 | SURVEYED BY: S.H. | VERSION: |
| DATE DRAWN: 08-22-11 | DRAWN BY: M.W. | V1 |
| REVISED: | SCALE: 1" = 1000' | |

RECEIVED: April 30, 2012

Access Road Map

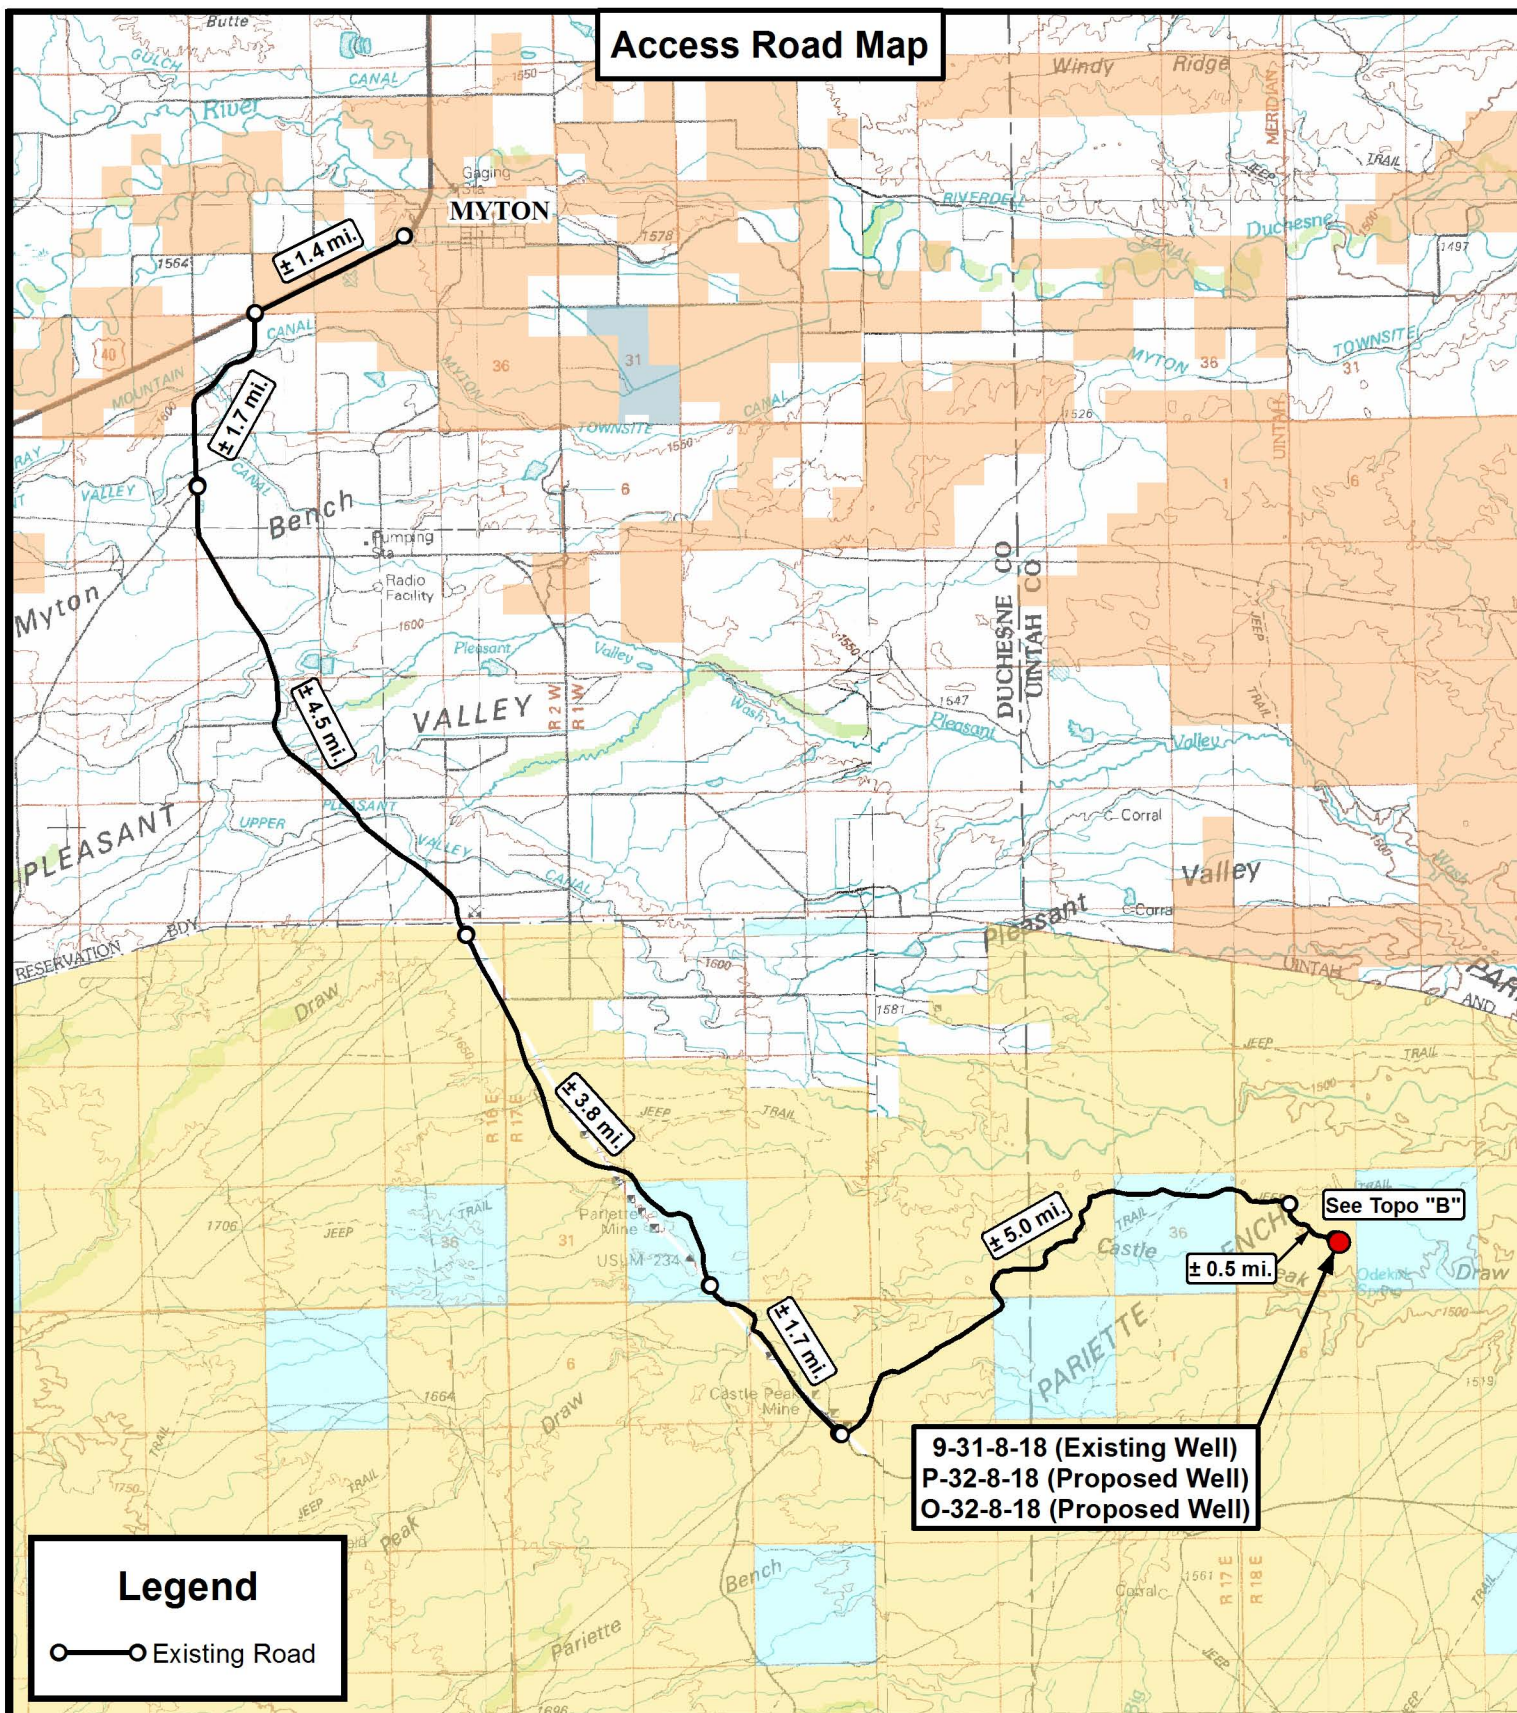

Tri State
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

9-31-8-18 (Existing Well)
 P-32-8-18 (Proposed Well)
 O-32-8-18 (Proposed Well)
 SEC. 31, T8S, R18E, S.L.B.&M. Uintah County, UT.


| | | | |
|-----------|------------|----------|----------|
| DRAWN BY: | D.C.R. | REVISED: | VERSION: |
| DATE: | 08-29-2011 | | V1 |
| SCALE: | 1:100,000 | | |

TOPOGRAPHIC MAP

SHEET

A

Access Road Map

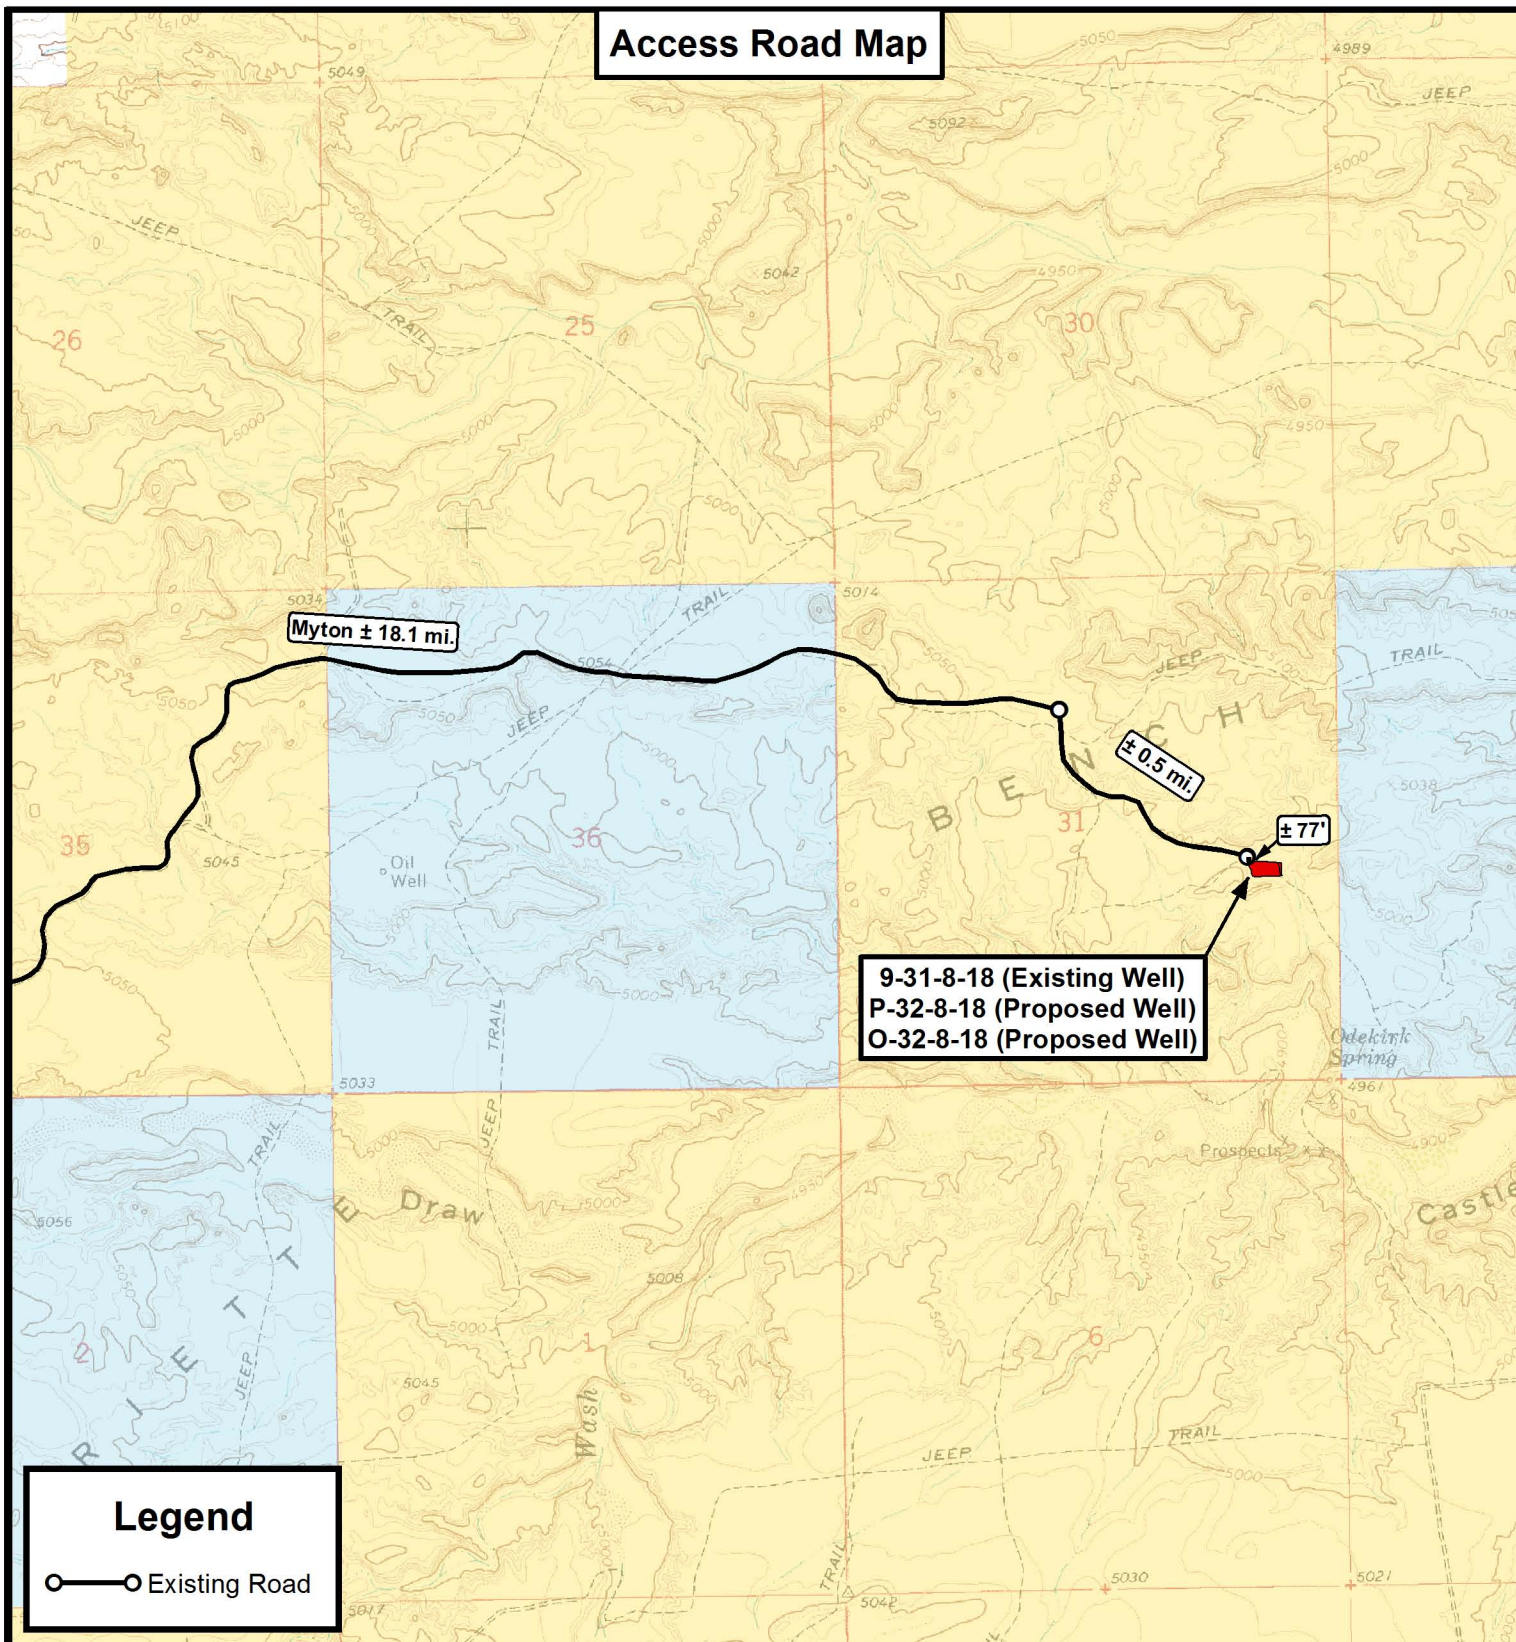

Legend

Existing Road

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



**Tri State
Land Surveying, Inc.**

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518

**NEWFIELD EXPLORATION COMPANY**

9-31-8-18 (Existing Well)
P-32-8-18 (Proposed Well)
O-32-8-18 (Proposed Well)

SEC. 31, T8S, R18E, S.L.B.&M. Uintah County, UT.


| | | | |
|-----------|-------------|----------|-----------|
| DRAWN BY: | D.C.R. | REVISED: | VERSION: |
| DATE: | 08-29-2011 | | V1 |
| SCALE: | 1" = 2,000' | | |

TOPOGRAPHIC MAP

SHEET

B

Proposed Pipeline Map

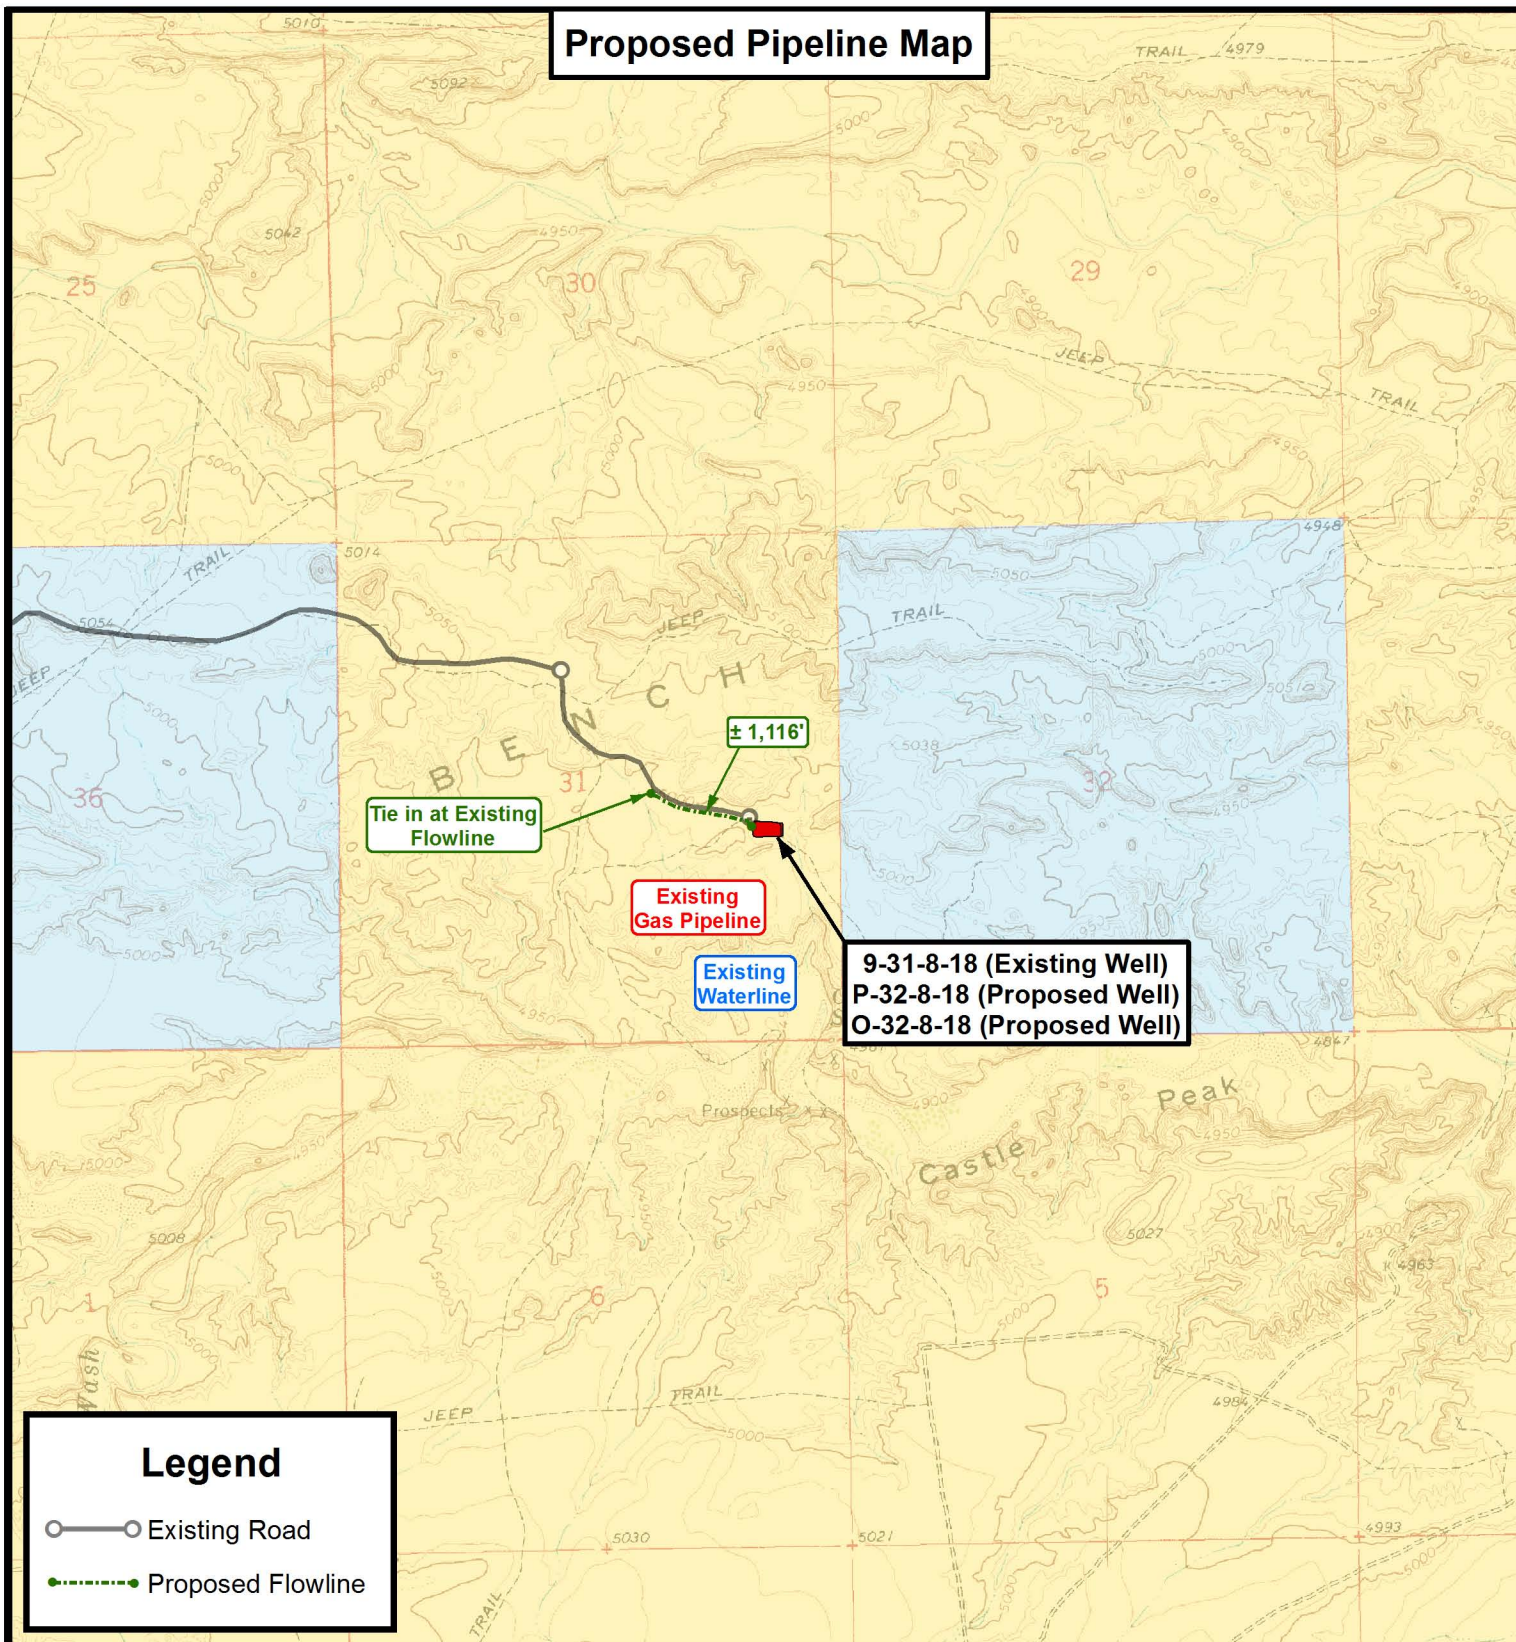

Legend

- Existing Road
- Proposed Flowline

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.

Tri State
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

9-31-8-18 (Existing Well)
P-32-8-18 (Proposed Well)
O-32-8-18 (Proposed Well)
SEC. 31, T8S, R18E, S.L.B.&M. Uintah County, UT.

| | | | |
|-----------|-------------|----------|----------|
| DRAWN BY: | D.C.R. | REVISED: | VERSION: |
| DATE: | 08-29-2011 | | V1 |
| SCALE: | 1" = 2,000' | | |


TOPOGRAPHIC MAP

SHEET

C

Exhibit "B" Map

9-31-8-18 (Existing Well)
P-32-8-18 (Proposed Well)
O-32-8-18 (Proposed Well)

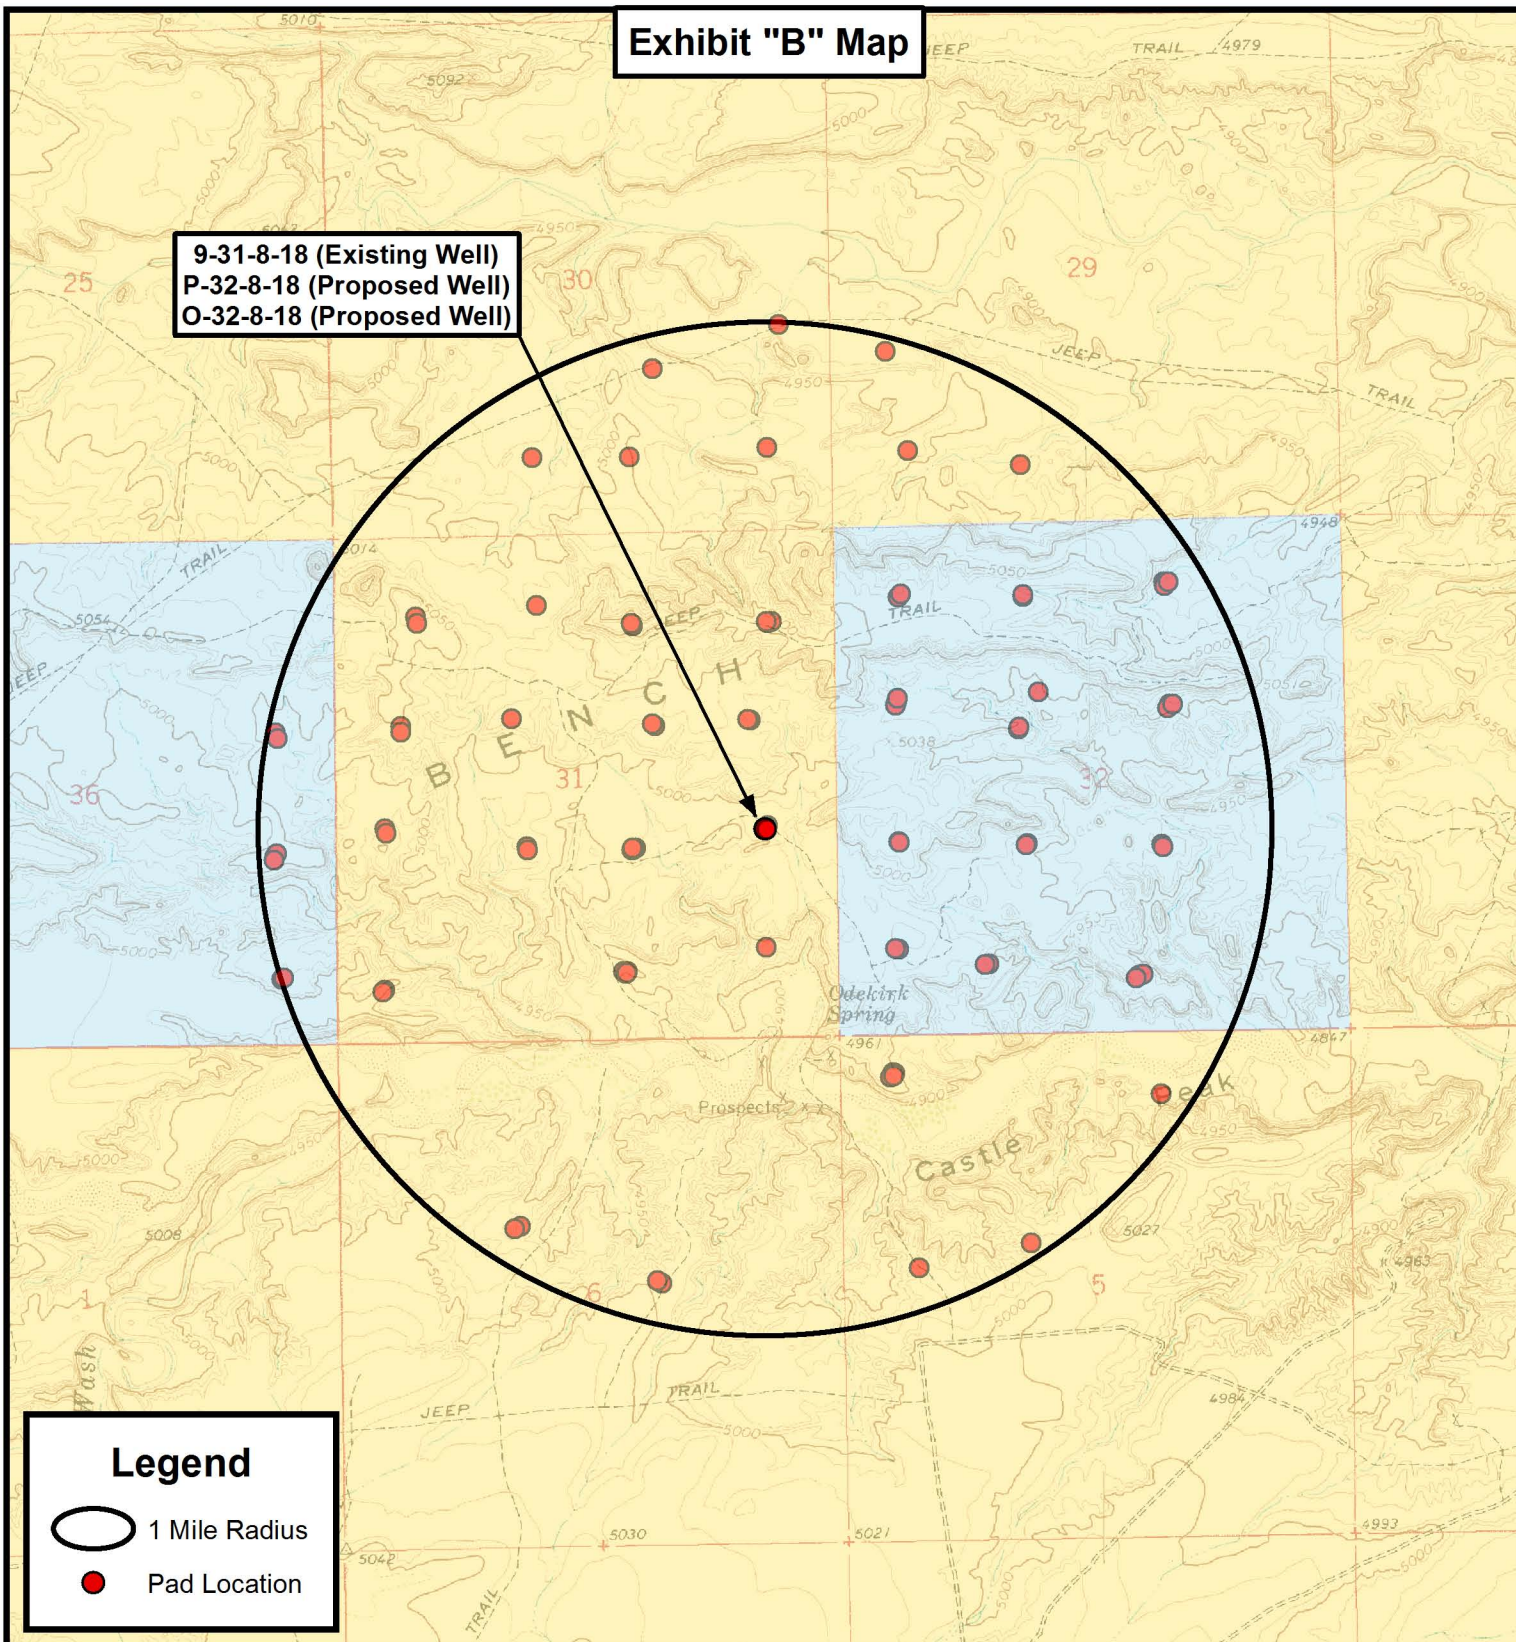**Legend**

-  1 Mile Radius
-  Pad Location

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.

Tri State
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518

**NEWFIELD EXPLORATION COMPANY**

9-31-8-18 (Existing Well)
P-32-8-18 (Proposed Well)
O-32-8-18 (Proposed Well)
SEC. 31, T8S, R18E, S.L.B.&M. Uintah County, UT.

| | | | |
|-----------|-------------|----------|----------|
| DRAWN BY: | D.C.R. | REVISED: | VERSION: |
| DATE: | 08-29-2011 | | V1 |
| SCALE: | 1" = 2,000' | | |

TOPOGRAPHIC MAP

SHEET

D



NEWFIELD EXPLORATION

**USGS Myton SW (UT)
SECTION 31 T8S, R18E
P-32-8-18**

Wellbore #1

Plan: Design #1

Standard Planning Report

16 August, 2011





PayZone Directional Services, LLC.

Planning Report



| | | | |
|------------------|----------------------------|-------------------------------------|-------------------------------------|
| Database: | EDM 2003.21 Single User Db | Local Co-ordinate Reference: | Well P-32-8-18 |
| Company: | NEWFIELD EXPLORATION | TVD Reference: | P-32-8-18 @ 4993.0ft (Newfield Rig) |
| Project: | USGS Myton SW (UT) | MD Reference: | P-32-8-18 @ 4993.0ft (Newfield Rig) |
| Site: | SECTION 31 T8S, R18E | North Reference: | True |
| Well: | P-32-8-18 | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | Design #1 | | |

| | | | |
|--------------------|--|----------------------|----------------|
| Project | USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA | | |
| Map System: | US State Plane 1983 | System Datum: | Mean Sea Level |
| Geo Datum: | North American Datum 1983 | | |
| Map Zone: | Utah Central Zone | | |

| | | | | |
|------------------------------|----------------------|---------------------|-----------------|-------------------------------------|
| Site | SECTION 31 T8S, R18E | | | |
| Site Position: | | Northing: | 7,201,349.38 ft | Latitude: 40° 4' 44.300 N |
| From: | Lat/Long | Easting: | 2,079,946.45 ft | Longitude: 109° 55' 44.860 W |
| Position Uncertainty: | 0.0 ft | Slot Radius: | " | Grid Convergence: 1.01 ° |

| | | | | |
|-----------------------------|---|-------------|----------------------------|-----------------|
| Well | P-32-8-18, SHL LAT: 40 04 23.19 LONG: -109 55 46.03 | | | |
| Well Position | +N/-S | -2,136.0 ft | Northing: | 7,199,212.14 ft |
| | +E/-W | -90.9 ft | Easting: | 2,079,893.03 ft |
| Position Uncertainty | | 0.0 ft | Wellhead Elevation: | 4,993.0 ft |
| | | | Ground Level: | 4,981.0 ft |

| | | | | | |
|------------------|-------------------|--------------------|------------------------|----------------------|----------------------------|
| Wellbore | Wellbore #1 | | | | |
| Magnetics | Model Name | Sample Date | Declination (°) | Dip Angle (°) | Field Strength (nT) |
| | IGRF2010 | 2011/08/16 | 11.24 | 65.84 | 52,292 |

| | | | | |
|--------------------------|------------------------------|-------------------|----------------------|----------------------|
| Design | Design #1 | | | |
| Audit Notes: | | | | |
| Version: | Phase: | PROTOTYPE | Tie On Depth: | 0.0 |
| Vertical Section: | Depth From (TVD) (ft) | +N/-S (ft) | +E/-W (ft) | Direction (°) |
| | 5,200.0 | 0.0 | 0.0 | 136.34 |

| Plan Sections | | | | | | | | | | |
|----------------------|-----------------|-------------|---------------------|------------|------------|-----------------------|----------------------|---------------------|---------|---------------|
| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) | TFO (°) | Target |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 | 0.00 | |
| 1,488.1 | 13.32 | 136.34 | 1,480.1 | -74.3 | 70.9 | 1.50 | 1.50 | 0.00 | 136.34 | |
| 5,310.8 | 13.32 | 136.34 | 5,200.0 | -711.5 | 679.0 | 0.00 | 0.00 | 0.00 | 0.00 | P-32-8-18 TGT |
| 6,518.3 | 13.32 | 136.34 | 6,375.0 | -912.8 | 871.1 | 0.00 | 0.00 | 0.00 | 0.00 | |



| | | | |
|------------------|----------------------------|-------------------------------------|-------------------------------------|
| Database: | EDM 2003.21 Single User Db | Local Co-ordinate Reference: | Well P-32-8-18 |
| Company: | NEWFIELD EXPLORATION | TVD Reference: | P-32-8-18 @ 4993.0ft (Newfield Rig) |
| Project: | USGS Myton SW (UT) | MD Reference: | P-32-8-18 @ 4993.0ft (Newfield Rig) |
| Site: | SECTION 31 T8S, R18E | North Reference: | True |
| Well: | P-32-8-18 | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | Design #1 | | |

| Planned Survey | | | | | | | | | |
|---------------------|-----------------|-------------|---------------------|------------|------------|-----------------------|-----------------------|----------------------|---------------------|
| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Vertical Section (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
| 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 100.0 | 0.00 | 0.00 | 100.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 200.0 | 0.00 | 0.00 | 200.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 300.0 | 0.00 | 0.00 | 300.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 400.0 | 0.00 | 0.00 | 400.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 500.0 | 0.00 | 0.00 | 500.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| 700.0 | 1.50 | 136.34 | 700.0 | -0.9 | 0.9 | 1.3 | 1.50 | 1.50 | 0.00 |
| 800.0 | 3.00 | 136.34 | 799.9 | -3.8 | 3.6 | 5.2 | 1.50 | 1.50 | 0.00 |
| 900.0 | 4.50 | 136.34 | 899.7 | -8.5 | 8.1 | 11.8 | 1.50 | 1.50 | 0.00 |
| 1,000.0 | 6.00 | 136.34 | 999.3 | -15.1 | 14.4 | 20.9 | 1.50 | 1.50 | 0.00 |
| 1,100.0 | 7.50 | 136.34 | 1,098.6 | -23.6 | 22.6 | 32.7 | 1.50 | 1.50 | 0.00 |
| 1,200.0 | 9.00 | 136.34 | 1,197.5 | -34.0 | 32.5 | 47.0 | 1.50 | 1.50 | 0.00 |
| 1,300.0 | 10.50 | 136.34 | 1,296.1 | -46.3 | 44.2 | 64.0 | 1.50 | 1.50 | 0.00 |
| 1,400.0 | 12.00 | 136.34 | 1,394.2 | -60.4 | 57.6 | 83.5 | 1.50 | 1.50 | 0.00 |
| 1,488.1 | 13.32 | 136.34 | 1,480.1 | -74.3 | 70.9 | 102.8 | 1.50 | 1.50 | 0.00 |
| 1,500.0 | 13.32 | 136.34 | 1,491.7 | -76.3 | 72.8 | 105.5 | 0.00 | 0.00 | 0.00 |
| 1,600.0 | 13.32 | 136.34 | 1,589.0 | -93.0 | 88.8 | 128.6 | 0.00 | 0.00 | 0.00 |
| 1,700.0 | 13.32 | 136.34 | 1,686.3 | -109.7 | 104.7 | 151.6 | 0.00 | 0.00 | 0.00 |
| 1,800.0 | 13.32 | 136.34 | 1,783.6 | -126.3 | 120.6 | 174.6 | 0.00 | 0.00 | 0.00 |
| 1,900.0 | 13.32 | 136.34 | 1,880.9 | -143.0 | 136.5 | 197.7 | 0.00 | 0.00 | 0.00 |
| 2,000.0 | 13.32 | 136.34 | 1,978.2 | -159.7 | 152.4 | 220.7 | 0.00 | 0.00 | 0.00 |
| 2,100.0 | 13.32 | 136.34 | 2,075.6 | -176.4 | 168.3 | 243.8 | 0.00 | 0.00 | 0.00 |
| 2,200.0 | 13.32 | 136.34 | 2,172.9 | -193.0 | 184.2 | 266.8 | 0.00 | 0.00 | 0.00 |
| 2,300.0 | 13.32 | 136.34 | 2,270.2 | -209.7 | 200.1 | 289.8 | 0.00 | 0.00 | 0.00 |
| 2,400.0 | 13.32 | 136.34 | 2,367.5 | -226.4 | 216.0 | 312.9 | 0.00 | 0.00 | 0.00 |
| 2,500.0 | 13.32 | 136.34 | 2,464.8 | -243.0 | 231.9 | 335.9 | 0.00 | 0.00 | 0.00 |
| 2,600.0 | 13.32 | 136.34 | 2,562.1 | -259.7 | 247.8 | 359.0 | 0.00 | 0.00 | 0.00 |
| 2,700.0 | 13.32 | 136.34 | 2,659.4 | -276.4 | 263.7 | 382.0 | 0.00 | 0.00 | 0.00 |
| 2,800.0 | 13.32 | 136.34 | 2,756.7 | -293.0 | 279.6 | 405.0 | 0.00 | 0.00 | 0.00 |
| 2,900.0 | 13.32 | 136.34 | 2,854.0 | -309.7 | 295.5 | 428.1 | 0.00 | 0.00 | 0.00 |
| 3,000.0 | 13.32 | 136.34 | 2,951.3 | -326.4 | 311.4 | 451.1 | 0.00 | 0.00 | 0.00 |
| 3,100.0 | 13.32 | 136.34 | 3,048.7 | -343.0 | 327.4 | 474.2 | 0.00 | 0.00 | 0.00 |
| 3,200.0 | 13.32 | 136.34 | 3,146.0 | -359.7 | 343.3 | 497.2 | 0.00 | 0.00 | 0.00 |
| 3,300.0 | 13.32 | 136.34 | 3,243.3 | -376.4 | 359.2 | 520.2 | 0.00 | 0.00 | 0.00 |
| 3,400.0 | 13.32 | 136.34 | 3,340.6 | -393.0 | 375.1 | 543.3 | 0.00 | 0.00 | 0.00 |
| 3,500.0 | 13.32 | 136.34 | 3,437.9 | -409.7 | 391.0 | 566.3 | 0.00 | 0.00 | 0.00 |
| 3,600.0 | 13.32 | 136.34 | 3,535.2 | -426.4 | 406.9 | 589.4 | 0.00 | 0.00 | 0.00 |
| 3,700.0 | 13.32 | 136.34 | 3,632.5 | -443.0 | 422.8 | 612.4 | 0.00 | 0.00 | 0.00 |
| 3,800.0 | 13.32 | 136.34 | 3,729.8 | -459.7 | 438.7 | 635.4 | 0.00 | 0.00 | 0.00 |
| 3,900.0 | 13.32 | 136.34 | 3,827.1 | -476.4 | 454.6 | 658.5 | 0.00 | 0.00 | 0.00 |
| 4,000.0 | 13.32 | 136.34 | 3,924.4 | -493.1 | 470.5 | 681.5 | 0.00 | 0.00 | 0.00 |
| 4,100.0 | 13.32 | 136.34 | 4,021.7 | -509.7 | 486.4 | 704.6 | 0.00 | 0.00 | 0.00 |
| 4,200.0 | 13.32 | 136.34 | 4,119.1 | -526.4 | 502.3 | 727.6 | 0.00 | 0.00 | 0.00 |
| 4,300.0 | 13.32 | 136.34 | 4,216.4 | -543.1 | 518.2 | 750.7 | 0.00 | 0.00 | 0.00 |
| 4,400.0 | 13.32 | 136.34 | 4,313.7 | -559.7 | 534.1 | 773.7 | 0.00 | 0.00 | 0.00 |
| 4,500.0 | 13.32 | 136.34 | 4,411.0 | -576.4 | 550.0 | 796.7 | 0.00 | 0.00 | 0.00 |
| 4,600.0 | 13.32 | 136.34 | 4,508.3 | -593.1 | 566.0 | 819.8 | 0.00 | 0.00 | 0.00 |
| 4,700.0 | 13.32 | 136.34 | 4,605.6 | -609.7 | 581.9 | 842.8 | 0.00 | 0.00 | 0.00 |
| 4,800.0 | 13.32 | 136.34 | 4,702.9 | -626.4 | 597.8 | 865.9 | 0.00 | 0.00 | 0.00 |
| 4,900.0 | 13.32 | 136.34 | 4,800.2 | -643.1 | 613.7 | 888.9 | 0.00 | 0.00 | 0.00 |
| 5,000.0 | 13.32 | 136.34 | 4,897.5 | -659.7 | 629.6 | 911.9 | 0.00 | 0.00 | 0.00 |
| 5,100.0 | 13.32 | 136.34 | 4,994.8 | -676.4 | 645.5 | 935.0 | 0.00 | 0.00 | 0.00 |
| 5,200.0 | 13.32 | 136.34 | 5,092.2 | -693.1 | 661.4 | 958.0 | 0.00 | 0.00 | 0.00 |



PayZone Directional Services, LLC.

Planning Report




| | | | |
|------------------|----------------------------|-------------------------------------|-------------------------------------|
| Database: | EDM 2003.21 Single User Db | Local Co-ordinate Reference: | Well P-32-8-18 |
| Company: | NEWFIELD EXPLORATION | TVD Reference: | P-32-8-18 @ 4993.0ft (Newfield Rig) |
| Project: | USGS Myton SW (UT) | MD Reference: | P-32-8-18 @ 4993.0ft (Newfield Rig) |
| Site: | SECTION 31 T8S, R18E | North Reference: | True |
| Well: | P-32-8-18 | Survey Calculation Method: | Minimum Curvature |
| Wellbore: | Wellbore #1 | | |
| Design: | Design #1 | | |

| Planned Survey | | | | | | | | | |
|---------------------|-----------------|-------------|---------------------|------------|------------|-----------------------|-----------------------|----------------------|---------------------|
| Measured Depth (ft) | Inclination (°) | Azimuth (°) | Vertical Depth (ft) | +N/-S (ft) | +E/-W (ft) | Vertical Section (ft) | Dogleg Rate (°/100ft) | Build Rate (°/100ft) | Turn Rate (°/100ft) |
| 5,300.0 | 13.32 | 136.34 | 5,189.5 | -709.7 | 677.3 | 981.1 | 0.00 | 0.00 | 0.00 |
| 5,310.8 | 13.32 | 136.34 | 5,200.0 | -711.5 | 679.0 | 983.5 | 0.00 | 0.00 | 0.00 |
| 5,400.0 | 13.32 | 136.34 | 5,286.8 | -726.4 | 693.2 | 1,004.1 | 0.00 | 0.00 | 0.00 |
| 5,500.0 | 13.32 | 136.34 | 5,384.1 | -743.1 | 709.1 | 1,027.1 | 0.00 | 0.00 | 0.00 |
| 5,600.0 | 13.32 | 136.34 | 5,481.4 | -759.7 | 725.0 | 1,050.2 | 0.00 | 0.00 | 0.00 |
| 5,700.0 | 13.32 | 136.34 | 5,578.7 | -776.4 | 740.9 | 1,073.2 | 0.00 | 0.00 | 0.00 |
| 5,800.0 | 13.32 | 136.34 | 5,676.0 | -793.1 | 756.8 | 1,096.3 | 0.00 | 0.00 | 0.00 |
| 5,900.0 | 13.32 | 136.34 | 5,773.3 | -809.8 | 772.7 | 1,119.3 | 0.00 | 0.00 | 0.00 |
| 6,000.0 | 13.32 | 136.34 | 5,870.6 | -826.4 | 788.6 | 1,142.3 | 0.00 | 0.00 | 0.00 |
| 6,100.0 | 13.32 | 136.34 | 5,967.9 | -843.1 | 804.6 | 1,165.4 | 0.00 | 0.00 | 0.00 |
| 6,200.0 | 13.32 | 136.34 | 6,065.2 | -859.8 | 820.5 | 1,188.4 | 0.00 | 0.00 | 0.00 |
| 6,300.0 | 13.32 | 136.34 | 6,162.6 | -876.4 | 836.4 | 1,211.5 | 0.00 | 0.00 | 0.00 |
| 6,400.0 | 13.32 | 136.34 | 6,259.9 | -893.1 | 852.3 | 1,234.5 | 0.00 | 0.00 | 0.00 |
| 6,500.0 | 13.32 | 136.34 | 6,357.2 | -909.8 | 868.2 | 1,257.5 | 0.00 | 0.00 | 0.00 |
| 6,518.3 | 13.32 | 136.34 | 6,375.0 | -912.8 | 871.1 | 1,261.8 | 0.00 | 0.00 | 0.00 |

API Well Number: 43047525940000





Project: USGS Myton SW (UT)
 Site: SECTION 31 T8S, R18E
 Well: P-32-8-18
 Wellbore: Wellbore #1
 Design: Design #1



Azimuths to True North
 Magnetic North: 11.24°

Magnetic Field
 Strength: 52291.9snT
 Dip Angle: 65.84°
 Date: 2011/08/16
 Model: IGRF2010

KOP @ 600'
 DOGLEG RATE 1.5 DEG/100
 TARGET RADIUS IS 75'

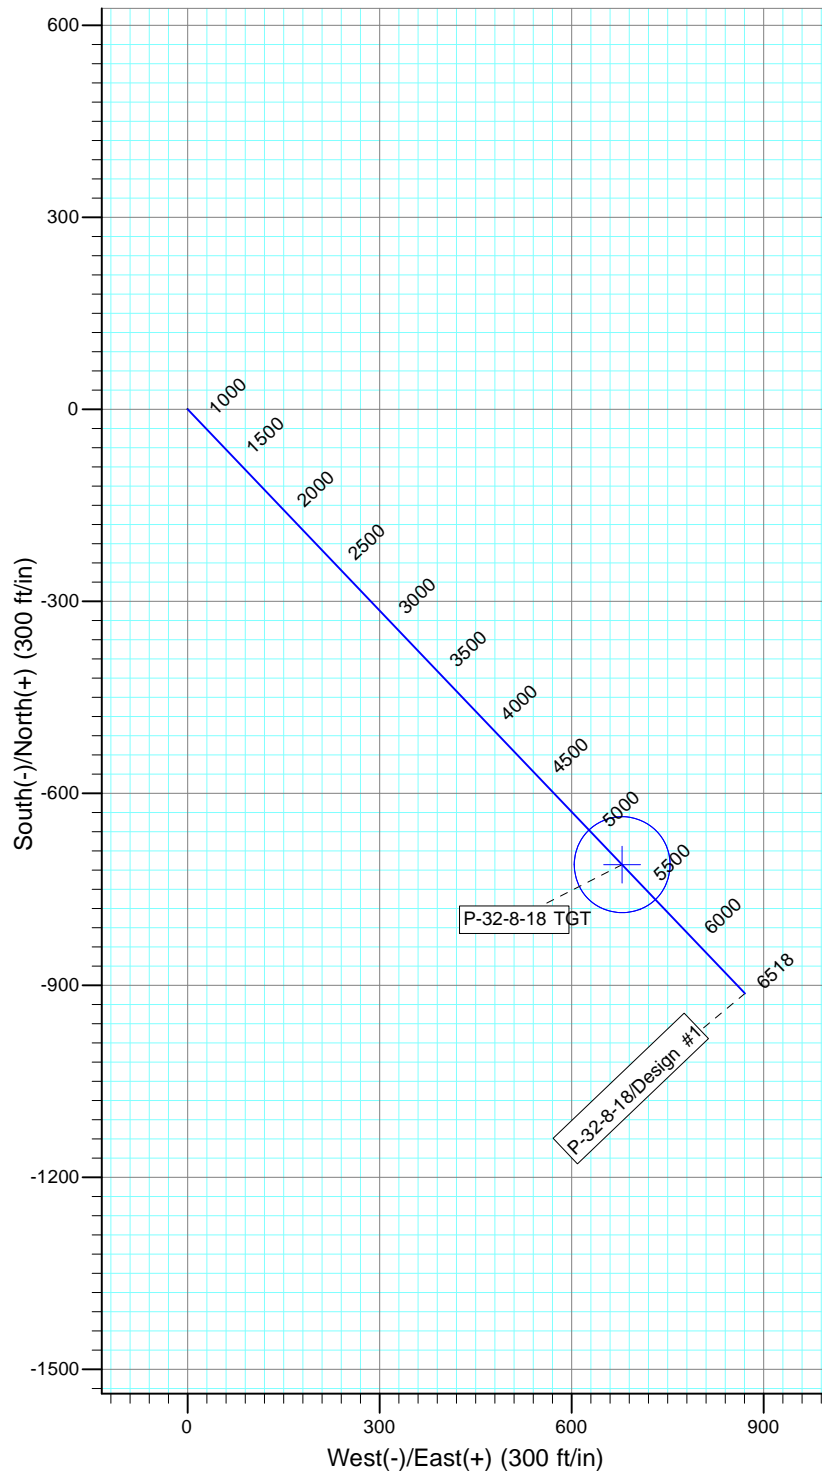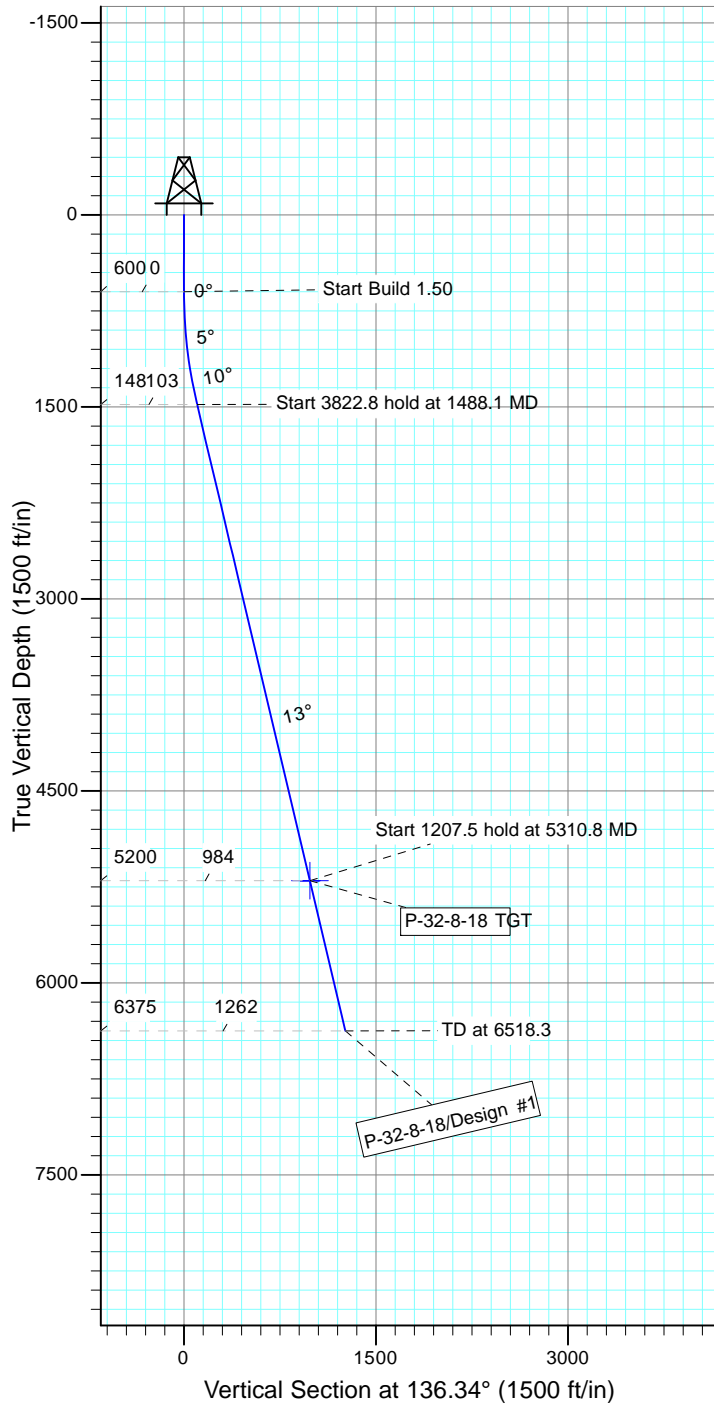

WELLBORE TARGET DETAILS

| Name | TVD | +N/-S | +E/-W | Shape |
|---------------|--------|--------|-------|-----------------------|
| P-32-8-18 TGT | 5200.0 | -711.5 | 679.0 | Circle (Radius: 75.0) |

SECTION DETAILS

| Sec | MD | Inc | Azi | TVD | +N/-S | +E/-W | DLeg | TFace | VSec | Target |
|-----|--------|-------|--------|--------|--------|-------|------|--------|--------|---------------|
| 1 | 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.0 | |
| 2 | 600.0 | 0.00 | 0.00 | 600.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.0 | |
| 3 | 1488.1 | 13.32 | 136.34 | 1480.1 | -74.3 | 70.9 | 1.50 | 136.34 | 102.8 | |
| 4 | 5310.8 | 13.32 | 136.34 | 5200.0 | -711.5 | 679.0 | 0.00 | 0.00 | 983.5 | P-32-8-18 TGT |
| 5 | 6518.3 | 13.32 | 136.34 | 6375.0 | -912.8 | 871.1 | 0.00 | 0.00 | 1261.8 | |



**NEWFIELD PRODUCTION COMPANY
GMBU P-32-8-18
AT SURFACE: NE/SE SECTION 31, T8S R18E
UINTAH COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site GMBU P-32-8-18 located in the NE 1/4 SE 1/4 Section 31, T8S R18E, Uintah County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 – 1.4 miles \pm to the junction of this highway and UT State Hwy 53; proceed in a southeasterly direction – 11.7 miles \pm to it's junction with an existing road to the northeast; ; proceed in a northeasterly direction – 5.0 miles \pm to it's junction with an existing road to the southeast; proceed in a southeasterly direction – 0.5 miles \pm to it's junction with the beginning of the access road to the existing 9-31-8-18 well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

There is no proposed access road for this location. The proposed well will be drilled directionaly off of the existing 9-31-8-18 well pad. See attached **Topographic Map "B"**.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District
Water Right : 43-10136

Maurice Harvey Pond
Water Right: 47-1358

Neil Moon Pond
Water Right: 43-11787

Newfield Collector Well
Water Right: 47-1817 (A30414DVA, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

- b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – Bureau of Land Management.

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. State of Utah Antiquities Project Permit # U-01-MQ-0787b 12/7/01, prepared by

Montgomery Archaeological Consultants. Paleontological Resource Survey prepared by, Wade Miller, 3/1/02. See attached report cover pages, Exhibit "D".

Surface Flow Line

Newfield requests 1,116' of surface flow line be granted. The Surface Flow Line will consist of up to a 14" bundled pipe consisting of 2-2" poly glycol lines and 1-3" production line. For all new wells, Newfield. **Refer to Topographic Map "C"** for the proposed location of the proposed flow line. Flow lines will be tan and will be constructed using the following procedures:

Clearing and Grading: No clearing or grading of the ROW will be required. The centerline of the proposed route will be staked prior to installation. Flow lines shall be placed as close to existing roads as possible without interfering with normal road travel or road maintenance activities. Due to the proximity of existing facilities, no temporary use or construction/storage areas are anticipated. If necessary, temporary use or construction/storage areas will be identified on a topographic map included in the approved permit.

Installation: The proposed flow lines will be installed 4-6" above the ground. For portions along existing two-track and primary access roads, lengths of pipe will be strung out in the borrow ditch, welded together, and rolled or dragged into place with heavy equipment. For pipelines that are installed cross-country (not along existing or proposed roads), travel along the lines will be infrequent and for maintenance needs only. No installation activities will be performed during periods when the soil is too wet to adequately support installation equipment. If such equipment creates ruts in excess of three (3) inches deep, the soil will be deemed too wet to adequately support the equipment.

Termination and Final Reclamation: After abandonment of the associated production facilities, the flow lines will be cut and removed, and any incidental surface disturbance reclaimed. Reclamation procedures will follow those outlined in the Castle Peak and Eight Mile Flat Reclamation and Weed Management Plan.

Water Disposal

After first production, if the production water meets quality guidelines, it will be transported to the Ashley, Monument Butte, Jonah, South Wells Draw and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project. Water not meeting quality criteria, will be disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), Federally approved surface disposal facilities or at a State of Utah approved surface disposal facilities.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Details of the On-Site Inspection

The proposed GMBU P-32-8-18 was on-sited on 1/13/12. The following were present; Tim Eaton (Newfield Production), Janna Simonsen (Bureau of Land Management), Aaron Roe (Bureau of Land Management), Suzanne Grayson (Bureau of Land Management), and Jessie Brunson (USFWS).

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the GMBU P-32-8-18, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the GMBU P-32-8-18, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

Representative

Name: Corie Miller

Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052

Telephone: (435) 646-3721

Certification


Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #P-32-8-18, Section 31, Township 8S, Range 18E: Lease UTU-74404 Uintah County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

4/25/12
Date

Mandie Crozier
Regulatory Analyst
Newfield Production Company

Typical 2M BOP stack configuration

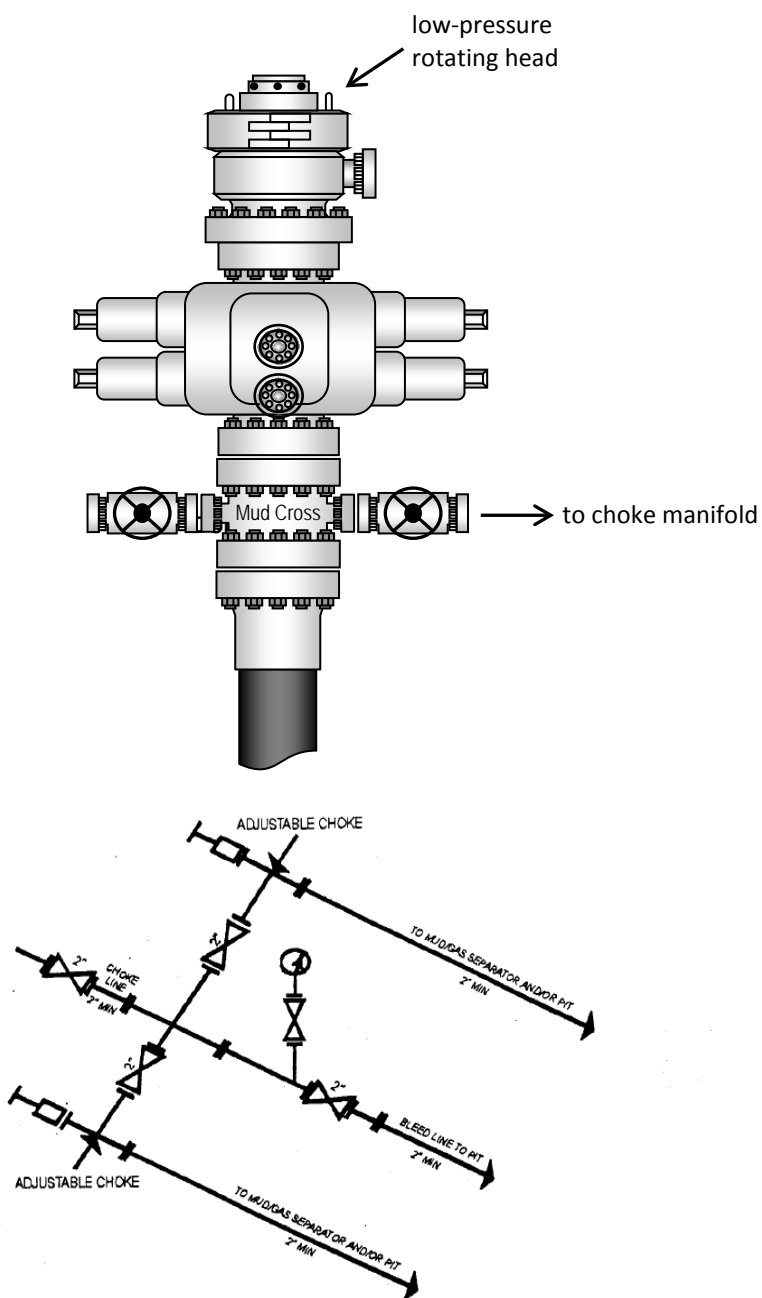

2M CHOKE MANIFOLD EQUIPMENT - CONFIGURATION OF CHOKES MAY VARY

NEWFIELD EXPLORATION COMPANY

WELL PAD INTERFERENCE PLAT

9-31-8-18 (Existing Well)

P-32-8-18 (Proposed Well)

O-32-8-18 (Proposed Well)

Pad Location: NESE Section 31, T8S, R18E, S.L.B.&M.



TOP HOLE FOOTAGES


P-32-8-18 (PROPOSED)
2163' FSL & 736' FEL

O-32-8-18 (PROPOSED)
2178' FSL & 722' FEL

CENTER OF PATTERN FOOTAGES

P-32-8-18 (PROPOSED)
1440' FSL & 70' FEL

O-32-8-18 (PROPOSED)
2615' FNL & 60' FEL

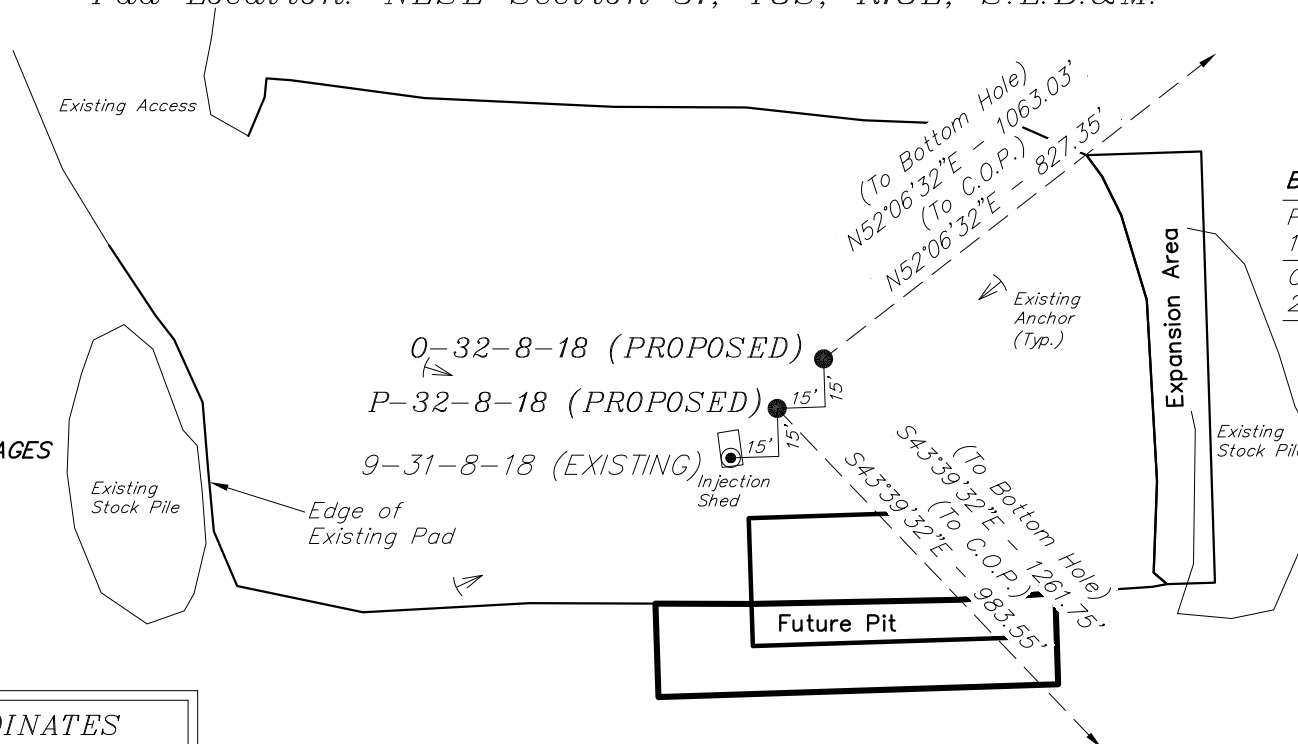

BOTTOM HOLE FOOTAGES

P-32-8-18 (PROPOSED)
1235' FSL & 119' FWL

O-32-8-18 (PROPOSED)
2474' FNL & 129' FWL

RELATIVE COORDINATES From Top Hole to C.O.P.

| WELL | NORTH | EAST |
|-----------|-------|------|
| P-32-8-18 | -712' | 679' |
| O-32-8-18 | 508' | 653' |

RELATIVE COORDINATES From Top Hole to Bottom Hole


| WELL | NORTH | EAST |
|-----------|-------|------|
| P-32-8-18 | -913' | 871' |
| O-32-8-18 | 653' | 839' |

LATITUDE & LONGITUDE Surface position of Wells (NAD 83)

| WELL | LATITUDE | LONGITUDE |
|-----------|----------------|-----------------|
| 9-31-8-18 | 40° 04' 23.04" | 109° 55' 46.22" |
| P-32-8-18 | 40° 04' 23.19" | 109° 55' 46.03" |
| O-32-8-18 | 40° 04' 23.34" | 109° 55' 45.84" |

| | | |
|-------------------|-------------------------|----------|
| SURVEYED BY: S.H. | DATE SURVEYED: 08-16-11 | VERSION: |
| DRAWN BY: M.W. | DATE DRAWN: 08-22-11 | V1 |
| SCALE: 1" = 60' | REVISED: | |





Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

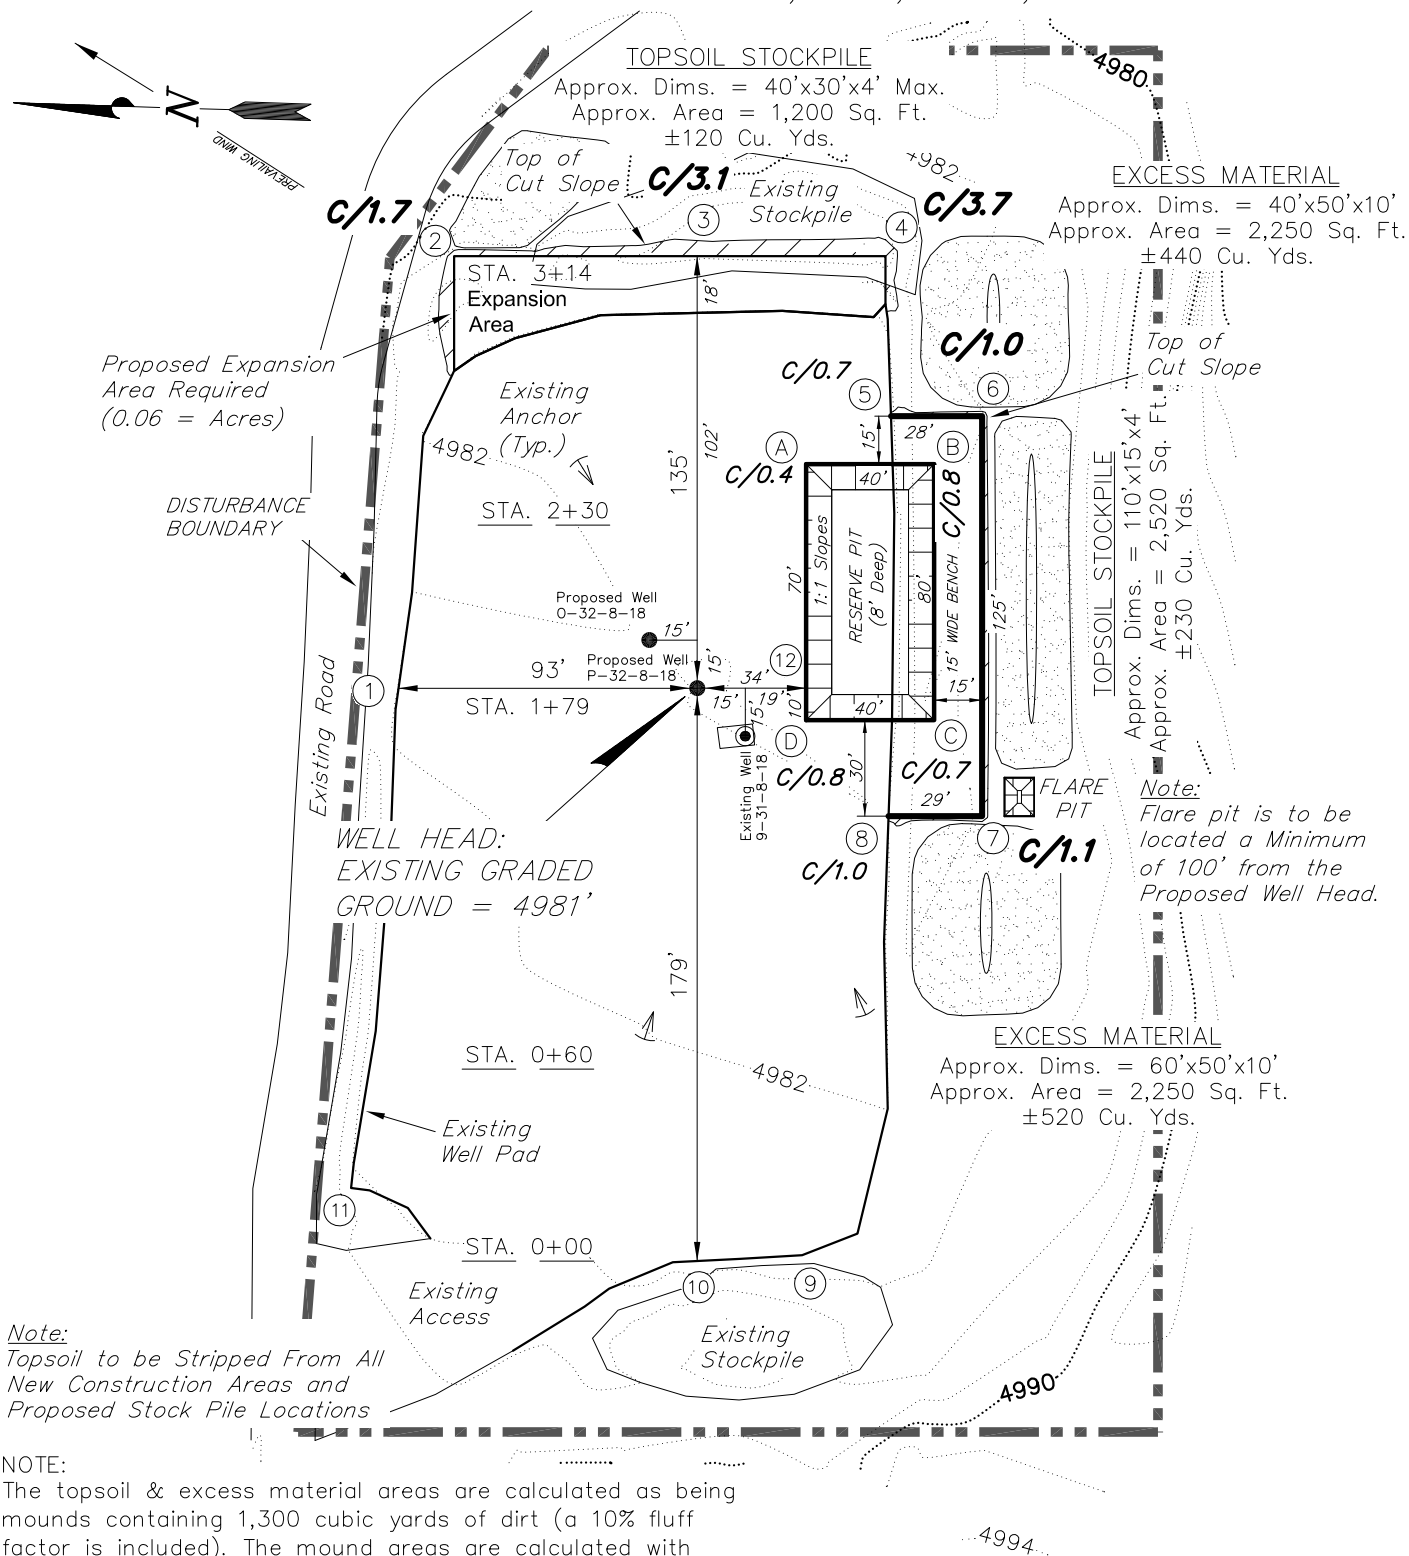NEWFIELD EXPLORATION COMPANY**LOCATION LAYOUT****9-31-8-18 (Existing Well)****P-32-8-18 (Proposed Well)****0-32-8-18 (Proposed Well)****Pad Location: NESE Section 31, T8S, R18E, S.L.B.&M.**

| | | |
|-------------------|-------------------------|----------|
| SURVEYED BY: S.H. | DATE SURVEYED: 08-16-11 | VERSION: |
| DRAWN BY: M.W. | DATE DRAWN: 08-22-11 | V1 |
| SCALE: 1" = 60' | REVISED: | |

Tri State
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078
(435) 781-2501

RECEIVED: April 30, 2012

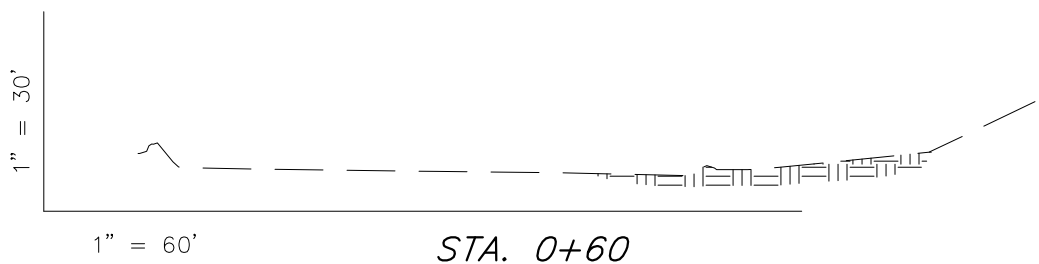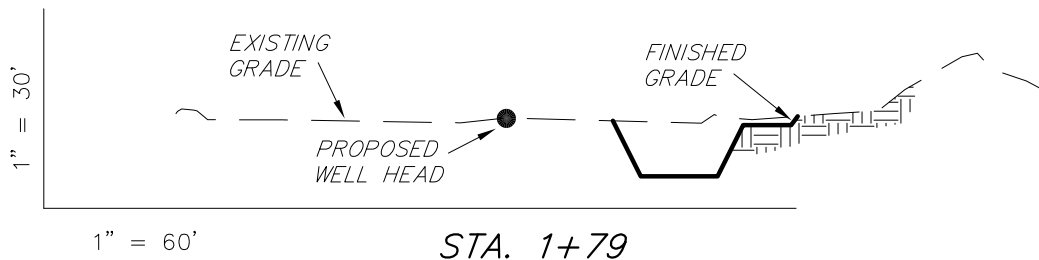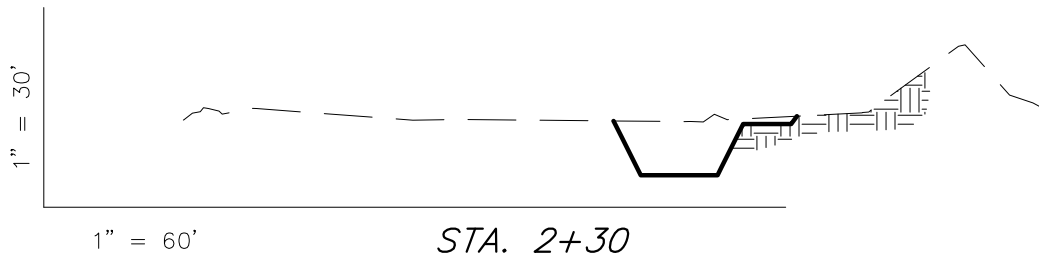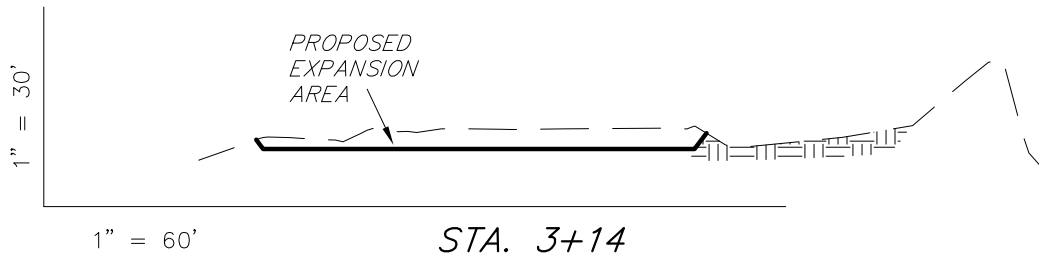NEWFIELD EXPLORATION COMPANY***CROSS SECTIONS******9-31-8-18 (Existing Well)******P-32-8-18 (Proposed Well)******O-32-8-18 (Proposed Well)******Pad Location: NESE Section 31, T8S, R18E, S.L.B.&M.***

NOTE:
UNLESS OTHERWISE
NOTED ALL CUT/FILL
SLOPES ARE AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES
(No Shrink or swell adjustments have been used)
(Expressed in Cubic Yards)

| ITEM | CUT | FILL | 6" TOPSOIL | EXCESS |
|--------|-----|------|--|--------|
| PAD | 180 | 0 | Topsoil is not included in Pad Cut | 180 |
| PIT | 690 | 0 | | 690 |
| TOTALS | 870 | 0 | 320 | 870 |

| | | |
|-------------------|-------------------------|----------|
| SURVEYED BY: S.H. | DATE SURVEYED: 08-16-11 | VERSION: |
| DRAWN BY: M.W. | DATE DRAWN: 08-22-11 | V1 |
| SCALE: 1" = 60' | REVISED: | |

Tri State
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078
(435) 781-2501

RECEIVED: April 30, 2012

VIA ELECTRONIC DELIVERY



May 3, 2012

State of Utah, Division of Oil, Gas and Mining
ATTN: Diana Mason
P.O. Box 145801
Salt Lake City, UT 84114-5801

RE: Directional Drilling
GMBU P-32-8-18
Greater Monument Butte (Green River) Unit

Surface Hole: T8S-R18E Section 31: NESE (UTU-74404)
2163' FNL 736' FEL

At Target: T8S-R18E Section 32: SWSW (ML-22058)
1235' FSL 119' FWL

Uintah County, Utah

Dear Ms. Mason:

Pursuant to the filing by Newfield Production Company (NPC) of an Application for Permit to Drill the above referenced well dated 5/1/2012, a copy of which is attached, and in accordance with Oil and Gas Conservation Rule R649-3-11, NPC hereby submits this letter as notice of our intention to directionally drill this well.

The surface hole and target locations of this well are both within the boundaries of the Greater Monument Butte Unit (UTU-87538X), of which Newfield certifies that it is the operator. Further, Newfield certifies that all lands within 460 feet of the entire directional well bore are within the Greater Monument Butte Unit.

NPC is permitting this well as a directional well in order to mitigate surface disturbance by utilizing pre-existing roads and pipelines.

NPC hereby requests our application for permit to drill be granted pursuant to R649-3-11. If you have any questions or require further information, please contact the undersigned at 303-383-4121 or by email at lburget@newfield.com. Your consideration in this matter is greatly appreciated.

Sincerely,
Newfield Production Company

A handwritten signature in blue ink that reads "Leslie Burget".

Leslie Burget
Land Associate

Form 3160-3
(August 2007)UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENTFORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010

APPLICATION FOR PERMIT TO DRILL OR REENTER

| | | |
|--|---|--|
| 1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER | | 5. Lease Serial No. UTU74404 |
| 1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone | | 6. If Indian, Allottee or Tribe Name |
| 2. Name of Operator NEWFIELD PRODUCTION COMPANY | | 7. If Unit or CA Agreement, Name and No. GREATER MONUMENT |
| Contact: MANDIE CROZIER Email: mcrozier@newfield.com | | 8. Lease Name and Well No. GMBU P-32-8-18 |
| 3a. Address ROUTE #3 BOX 3630 MYTON, UT 84052 | 3b. Phone No. (include area code) Ph: 435-646-4825 Fx: 435-646-3031 | 9. API Well No. |
| 4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NESE 2163FSL 736FEL At proposed prod. zone SWSW 1235FSL 119FWL | | 10. Field and Pool, or Exploratory MONUMENT BUTTE |
| 11. Sec., T., R., M., or Blk. and Survey or Area Sec 31 T8S R18E Mer SLB | | |
| 14. Distance in miles and direction from nearest town or post office* 18.6 MILES SOUTHEAST OF MYTON, UT | | 12. County or Parish UINTAH |
| 13. State UT | | |
| 15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 119' | 16. No. of Acres in Lease 277.52 | 17. Spacing Unit dedicated to this well 20.00 |
| 18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 861' | 19. Proposed Depth 6518 MD 6375 TVD | 20. BLM/BIA Bond No. on file WYB000493 |
| 21. Elevations (Show whether DF, KB, RT, GL, etc.) 4981 GL | 22. Approximate date work will start 07/31/2012 | 23. Estimated duration 7 DAYS |

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- | | |
|---|--|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

| | | |
|--|---|--------------------|
| 25. Signature (Electronic Submission) | Name (Printed/Typed) MANDIE CROZIER Ph: 435-646-4825 | Date 05/01/2012 |
| Title REGULATORY ANALYST | | |
| Approved by (Signature) | Name (Printed/Typed) | Date |
| Title | Office | |

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

Electronic Submission #136993 verified by the BLM Well Information System
For NEWFIELD PRODUCTION COMPANY, sent to the Vernal

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **

API Well Number: 43047525940000


Additional Operator Remarks:

SURFACE LEASE: UTU-74404
BOTTOM HOLE LEASE: ML-22058

T8S, R18E, S.L.B.&M.

NEWFIELD EXPLORATION COMPANY

WELL LOCATION, P-32-8-18, LOCATED AS SHOWN IN THE NE 1/4 SE 1/4 OF SECTION 31, T8S, R18E, S.L.B.&M. UINTAH COUNTY, UTAH.

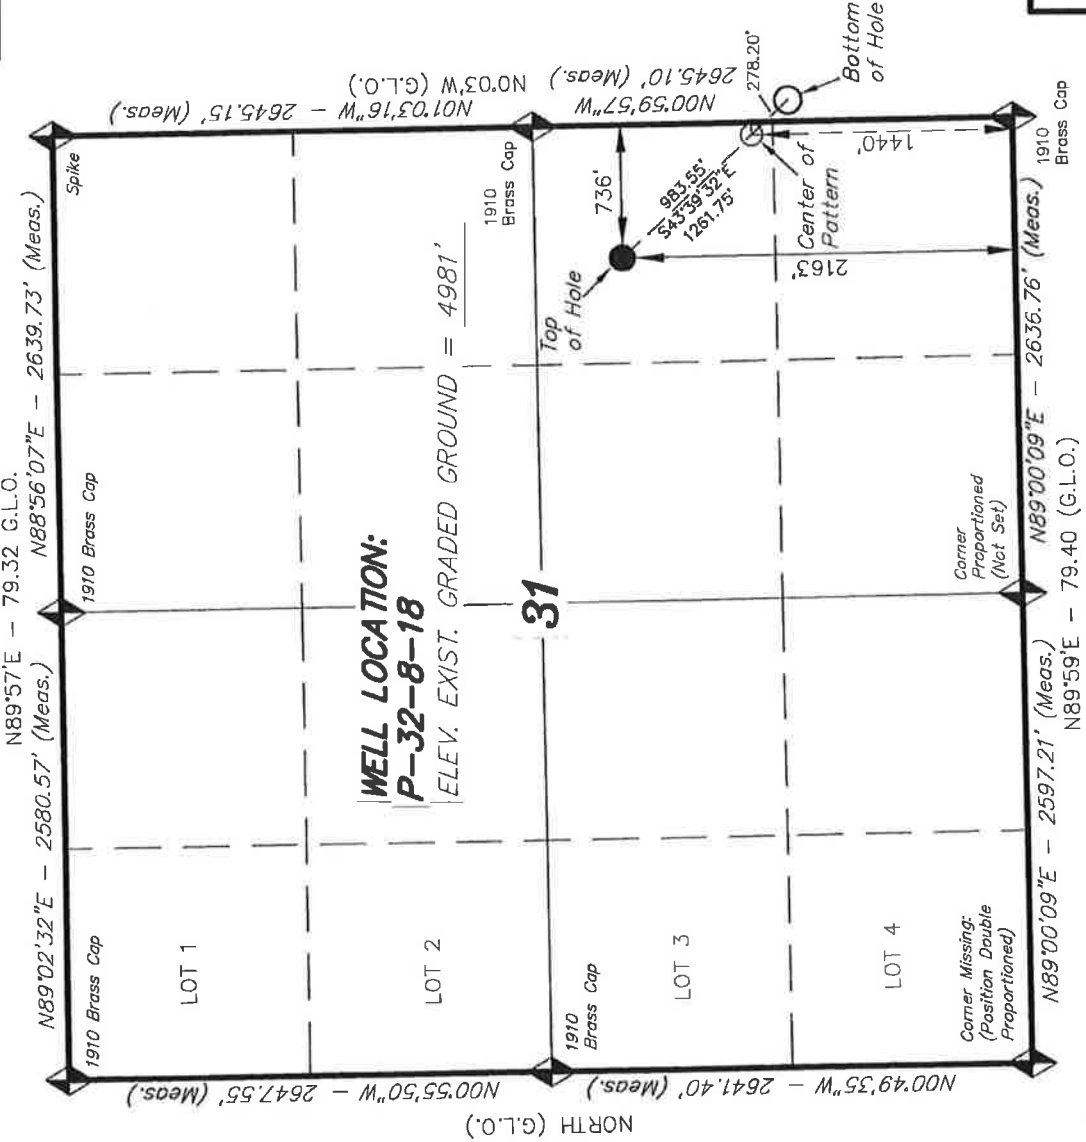


WELL LOCATION:
P-32-8-18
ELEV. EXIST. GRADED GROUND = 4981'

SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are based on an N.G.S. OPUS Correction. LOCATION: LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'

P-32-8-18
(Surface Location) NAD 83
LATITUDE = 40° 04' 23.19"
LONGITUDE = 109° 55' 46.03"



- NOTES:
1. Well footages are measured at right angles to the Section Lines.
 2. Bearings are based on Global Positioning Satellite observations.
 3. The Center of Pattern footages are 1440' FSL & 70' FEL.

THIS IS TO CERTIFY THAT THE ABOVE SURVEY WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

STACY W.
11-11-11
REGISTERED LAND SURVEYOR
REGISTRATION NO. 65189377
STATE OF UTAH



TRI STATE LAND SURVEYING & CONSULTING
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

| | | |
|----------------------------|-------------------|----------|
| DATE SURVEYED: 08-16-11 | SURVEYED BY: S.H. | VERSION: |
| DATE DRAWN: 08-22-11 | DRAWN BY: M.W. | V1 |
| REVISED: | SCALE: 1" = 1000' | |

T8S, R18E, S.L.B.&M.

NEWFIELD EXPLORATION COMPANY

TARGET BOTTOM HOLE, P-32-8-18,
LOCATED AS SHOWN IN THE SW 1/4
SW 1/4 OF SECTION 32, T8S, R18E,
S.L.B.&M. UTAH COUNTY, UTAH.

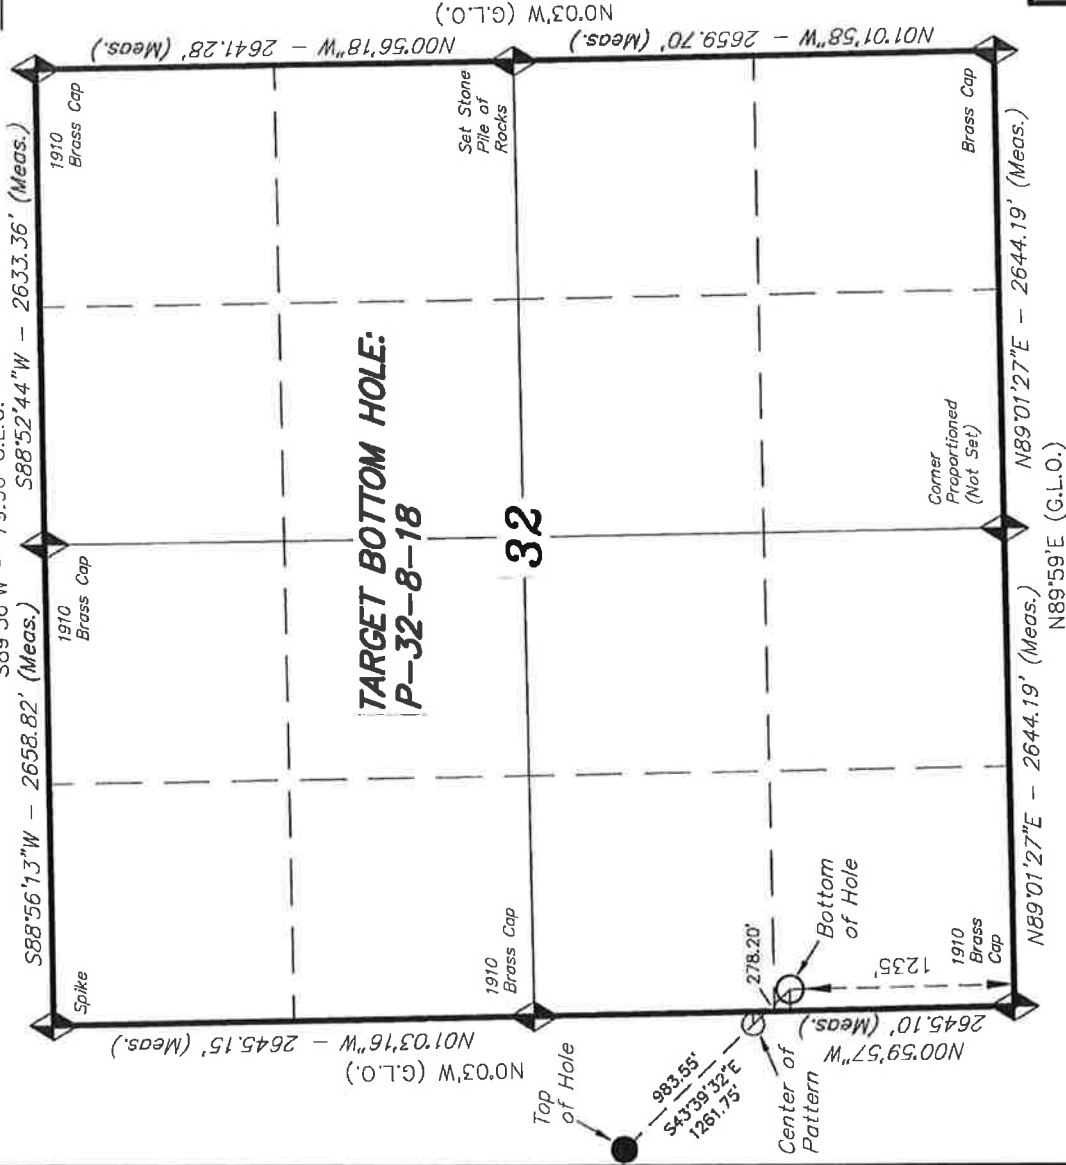

NOTES:

1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.
4. The Bottom of Hole footages are 1235' FSL & 119' FWL.

THIS IS TO CERTIFY THAT THE ABOVE PERT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.


11-11-11
STACY W.
REGISTERED LAND SURVEYOR
STATE OF UTAH

TRI STATE LAND SURVEYING & CONSULTING
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

| | | |
|----------------------------|-------------------|----------|
| DATE SURVEYED: 08-16-11 | SURVEYED BY: S.H. | VERSION: |
| DATE DRAWN: 08-22-11 | DRAWN BY: M.W. | V1 |
| REVISED: | SCALE: 1" = 1000' | |

◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are based on an N.G.S. OPUS Correction. LOCATION: LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'

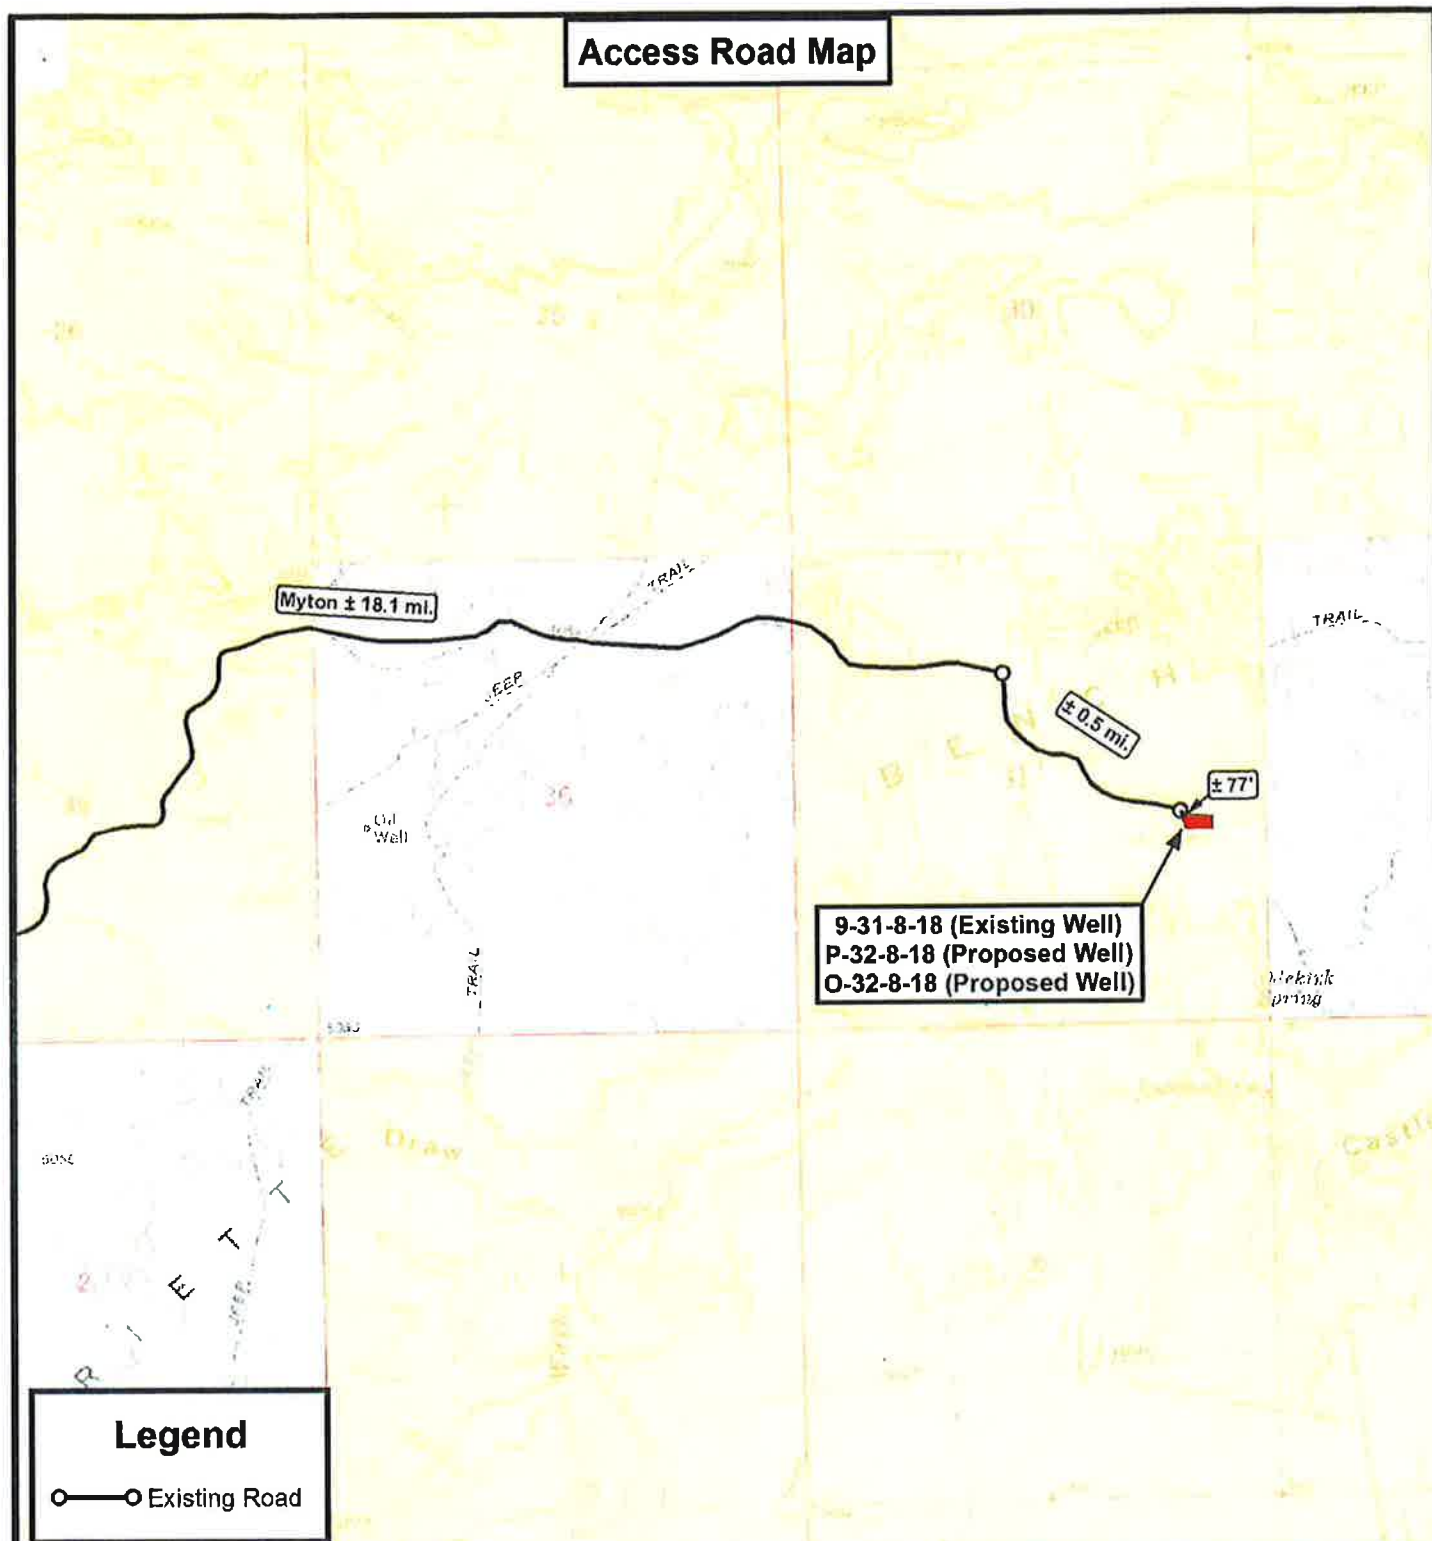

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



Tri State
Land Surveying, Inc.

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

9-31-8-18 (Existing Well)
P-32-8-18 (Proposed Well)
O-32-8-18 (Proposed Well)
SEC. 31, T9S, R18E, S.L.B.&M. Uintah County, UT.

| | | | |
|-----------|-------------|----------|-----------|
| DRAWN BY: | D.C.R. | REVISED: | VERSION: |
| DATE: | 08-29-2011 | | V1 |
| SCALE: | 1" = 2,000' | | |

TOPOGRAPHIC MAP

SHEET

B

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office
P.O. Box 45155
Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:
3160
(UT-922)

May 8, 2012

Memorandum

To: Assistant District Manager Minerals, Vernal District
From: Michael Coulthard, Petroleum Engineer
Subject: 2012 Plan of Development Greater Monument
Butte Unit, Duchesne and Uintah Counties,
Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2012 within the Greater Monument Butte Unit, Duchesne and Uintah Counties, Utah.

| API # | WELL NAME | LOCATION |
|---------------------------|--|------------------------------------|
| (Proposed PZ GREEN RIVER) | | |
| 43-047-52547 | GMBU V-26-8-17 | Sec 35 T08S R17E 0596 FNL 1880 FEL |
| | BHL Sec 26 T08S R17E 0100 FSL 1172 FEL | |
| 43-047-52592 | GMBU O-31-8-18 | Sec 36 T08S R17E 1975 FSL 0613 FEL |
| | BHL Sec 31 T08S R18E 2548 FNL 0112 FWL | |
| 43-047-52593 | GMBU F-31-8-18 | Sec 36 T08S R17E 0667 FNL 0629 FEL |
| | BHL Sec 31 T08S R18E 1496 FNL 0273 FWL | |
| 43-047-52594 | GMBU P-32-8-18 | Sec 31 T08S R18E 2163 FSL 0736 FEL |
| | BHL Sec 32 T08S R18E 1235 FSL 0119 FWL | |
| 43-047-52595 | GMBU O-32-8-18 | Sec 31 T08S R18E 2178 FSL 0722 FEL |
| | BHL Sec 32 T08S R18E 2474 FNL 0129 FWL | |
| 43-047-52596 | GMBU F-32-8-18 | Sec 31 T08S R18E 0982 FNL 0644 FEL |
| | BHL Sec 32 T08S R18E 1552 FNL 0145 FWL | |
| 43-047-52597 | GMBU P-31-8-18 | Sec 36 T08S R17E 1958 FSL 0626 FEL |
| | BHL Sec 31 T08S R18E 1037 FSL 0209 FWL | |
| 43-047-52598 | GMBU I-31-8-18 | Sec 31 T08S R18E 0989 FNL 0664 FEL |
| | BHL Sec 31 T08S R18E 1646 FNL 1507 FEL | |
| 43-047-52599 | GMBU S-31-8-18 | Sec 31 T08S R18E 1960 FSL 2123 FEL |
| | BHL Sec 31 T08S R18E 1174 FSL 1320 FEL | |

RECEIVED: May 08, 2012

| API # | WELL NAME | LOCATION |
|---------------------------|----------------|------------------------------------|
| (Proposed PZ GREEN RIVER) | | |
| 43-013-51394 | GMBU T-34-8-17 | Sec 35 T08S R17E 0689 FSL 0848 FWL |
| | BHL | Sec 34 T08S R17E 1363 FSL 0169 FEL |
| 43-013-51395 | GMBU O-35-8-17 | Sec 34 T08S R17E 1877 FNL 0742 FEL |
| | BHL | Sec 35 T08S R17E 2309 FSL 0186 FWL |
| 43-047-52600 | GMBU Y-25-8-17 | Sec 35 T08S R17E 0671 FNL 0645 FEL |
| | BHL | Sec 25 T08S R17E 0211 FSL 0228 FWL |
| 43-047-52602 | GMBU Y-30-8-18 | Sec 36 T08S R17E 0662 FNL 0133 FEL |
| | BHL | Sec 30 T08S R18E 0029 FSL 0317 FWL |

This office has no objection to permitting the wells at this time.


Michael L. Coulthard

Digitally signed by Michael L. Coulthard
DN: cn=Michael L. Coulthard, o=Bureau of Land Management,
ou=Branch of Minerals, email=Michael_Coulthard@blm.gov,
c=US
Date: 2012.05.08 14:49:49 -06'00'

bcc: File - Greater Monument Butte Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:5-8-12

RECEIVED: May 08, 2012

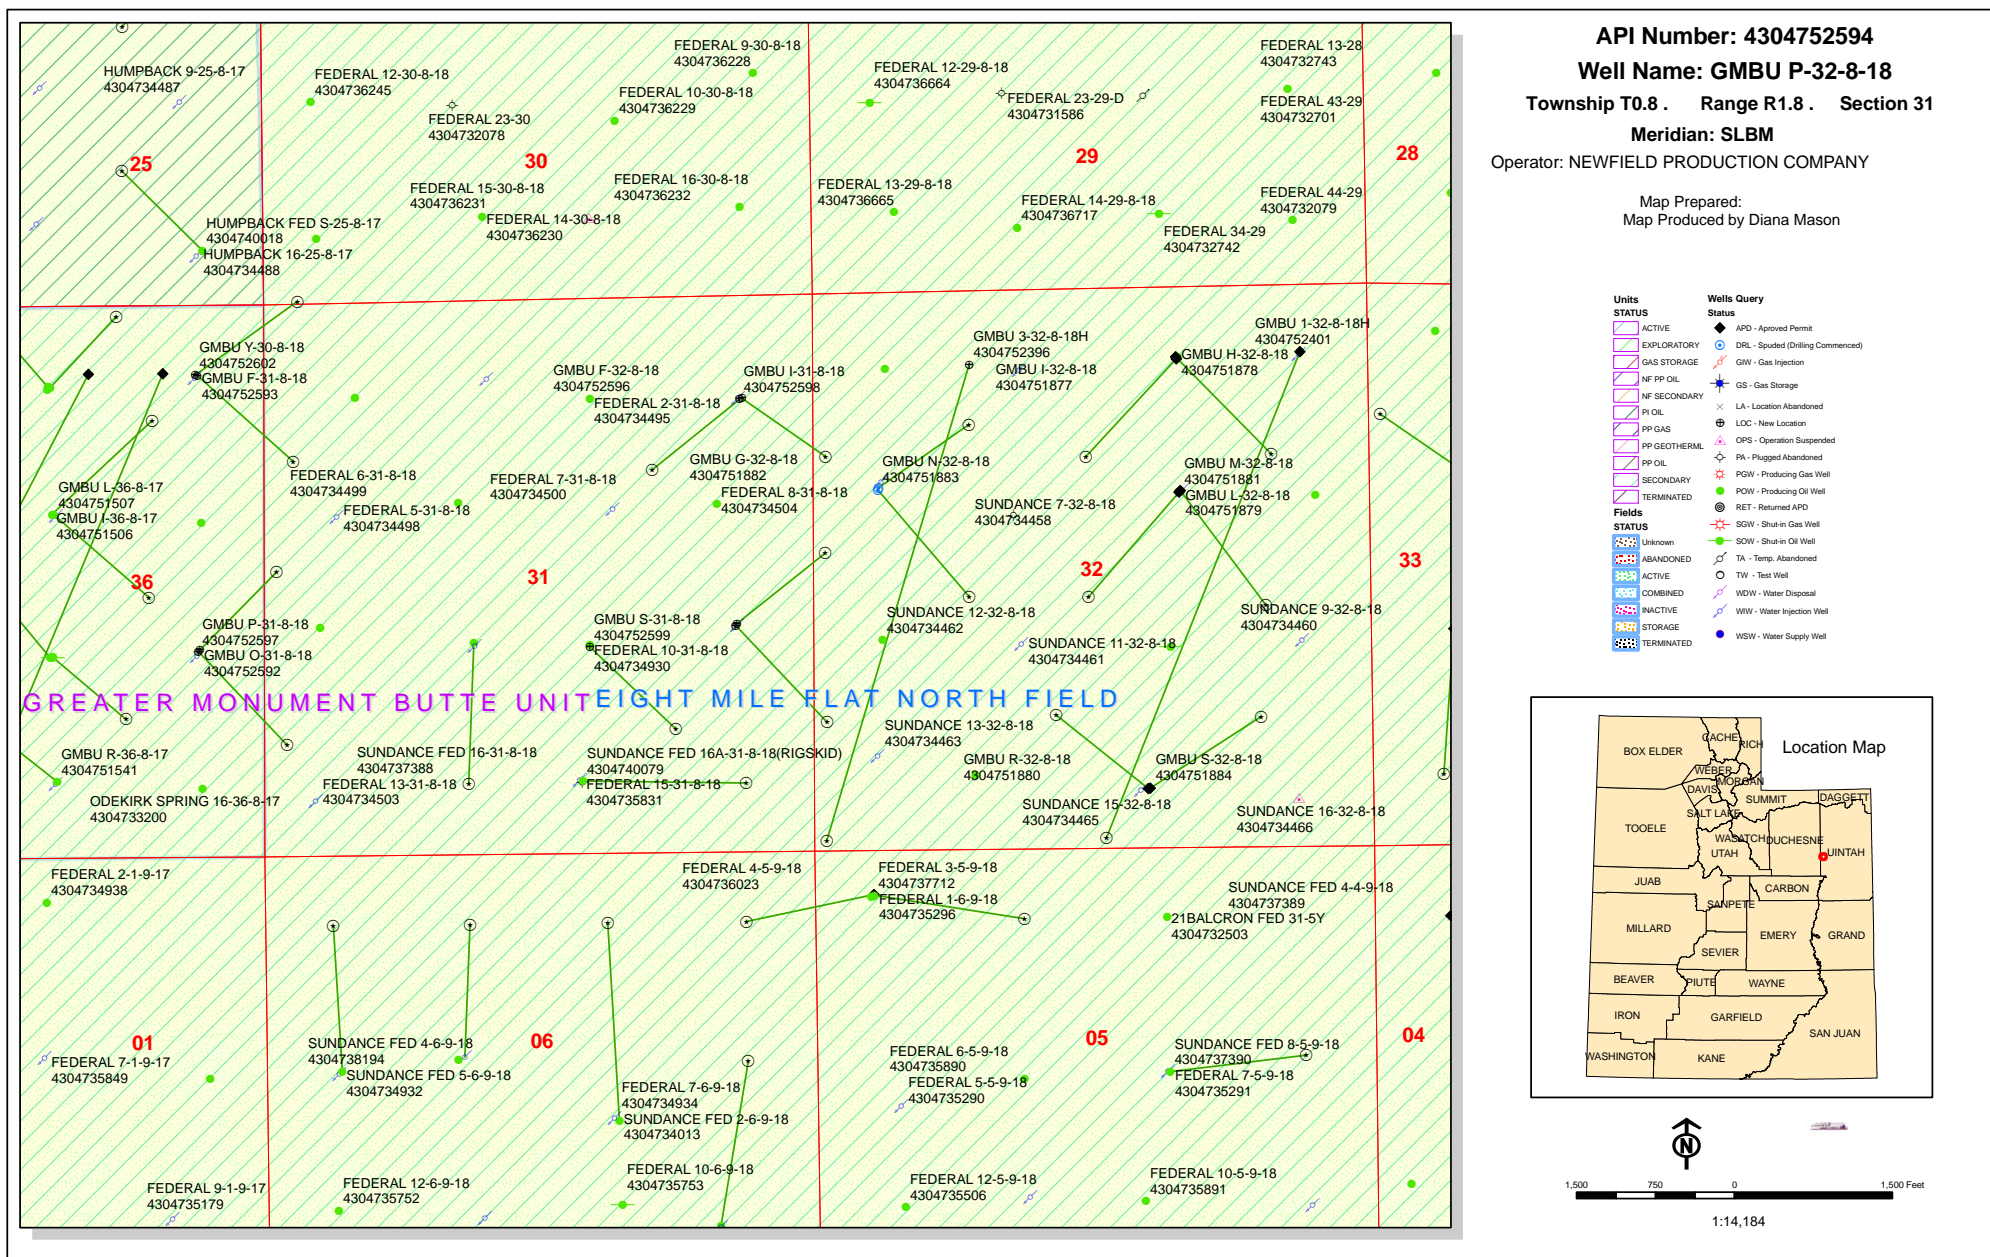

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 4/30/2012

API NO. ASSIGNED: 43047525940000

WELL NAME: GMBU P-32-8-18

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: NESE 31 080S 180E

Permit Tech Review: ☒

SURFACE: 2163 FSL 0736 FEL

Engineering Review: ☐

BOTTOM: 1235 FSL 0119 FWL

Geology Review: ☒

COUNTY: UINTAH

LATITUDE: 40.07304

LONGITUDE: -109.92949

UTM SURF EASTINGS: 591282.00

NORTHINGS: 4436413.00

FIELD NAME: MONUMENT BUTTE

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-74404

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 1 - Federal

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- ☒ PLAT
- ☒ Bond: FEDERAL - WYB000493
- ☐ Potash
- ☐ Oil Shale 190-5
- ☐ Oil Shale 190-3
- ☐ Oil Shale 190-13
- ☒ Water Permit: 437478
- ☐ RDCC Review:
- ☐ Fee Surface Agreement
- ☐ Intent to Commingle

Commingling Approved

LOCATION AND SITING:

- ☐ R649-2-3.
- Unit: GMBU (GRRV)
- ☐ R649-3-2. General
- ☐ R649-3-3. Exception
- ☒ Drilling Unit
- Board Cause No: Cause 213-11
- Effective Date: 11/30/2009
- Siting: Suspends General Siting
- ☒ R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason
15 - Directional - dmason
27 - Other - bhill

RECEIVED: May 17, 2012



GARY R. HERBERT
Governor

GREGORY S. BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: GMBU P-32-8-18
API Well Number: 43047525940000
Lease Number: UTU-74404
Surface Owner: FEDERAL
Approval Date: 5/17/2012

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. 40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 213-11. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Production casing cement shall be brought up to or above the top of the unitized interval for the Greater Monument Butte Unit (Cause No. 213-11).

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well - contact Carol Daniels at 801-538-5284

(please leave a voicemail message if not available)

OR

submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website
at <http://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) - due within 5 days of spudding the well
- Monthly Status Report (Form 9) - due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) - due prior to implementation
- Written Notice of Emergency Changes (Form 9) - due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) - due prior to implementation
- Report of Water Encountered (Form 7) - due within 30 days after completion
- Well Completion Report (Form 8) - due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "John Rogers", written over a horizontal line.

For John Rogers
Associate Director, Oil & Gas

RECEIVED
UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
MAY 08 2012FORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010


APPLICATION FOR PERMIT TO DRILL OR REENTER

| | | |
|--|--|---|
| 1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER | | 5. Lease Serial No. UTU74404 |
| 1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone | | 6. If Indian, Allottee or Tribe Name |
| 2. Name of Operator NEWFIELD PRODUCTION COMPANY Contact: MANDIE CROZIER Email: mcrozier@newfield.com | | 7. If Unit or CA Agreement, Name and No. GREATER MONUMENT |
| 3a. Address ROUTE #3 BOX 3630 MYTON, UT 84052 | | 8. Lease Name and Well No. GMBU P-32-8-18 |
| 3b. Phone No. (include area code) Ph: 435-646-4825 Fx: 435-646-3031 | | 9. API Well No. 43-047-52594 |
| 4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NESE 2163FSL 736FEL At proposed prod. zone SWSW 1235FSL 119FWL Sec. 32 | | 10. Field and Pool, or Exploratory MONUMENT BUTTE |
| 14. Distance in miles and direction from nearest town or post office* 18.6 MILES SOUTHEAST OF MYTON, UT | | 11. Sec., T., R., M., or Blk. and Survey or Area Sec 31 T8S R18E Mer SLB |
| 15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 119' | 16. No. of Acres in Lease 277.52 | 12. County or Parish UINTAH |
| 18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 861' | 19. Proposed Depth 6518 MD 6375 TVD | 13. State UT |
| 21. Elevations (Show whether DF, KB, RT, GL, etc.) 4981 GL | 22. Approximate date work will start 07/31/2012 | 17. Spacing Unit dedicated to this well 20.00 |
| | | 20. BLM/BIA Bond No. on file WYB000493 |
| | | 23. Estimated duration 7 DAYS |

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification
- Such other site specific information and/or plans as may be required by the authorized officer.

| | | |
|--|---|---------------------|
| 25. Signature (Electronic Submission) | Name (Printed/Typed) MANDIE CROZIER Ph: 435-646-4825 | Date 05/01/2012 |
| Title REGULATORY ANALYST | | |
| Approved by (Signature)  | Name (Printed/Typed) Jerry Kenczka | Date NOV 16 2012 |
| Title Assistant Field Manager Lands & Mineral Resources | Office VERNAL FIELD OFFICE | |

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

Electronic Submission #136993 verified by the BLM Well Information System
For NEWFIELD PRODUCTION COMPANY, sent to the Vernal
Committed to AFMSS for processing by LESLIE ROBINSON on 05/14/2012 ()

UDOGM

NOTICE OF APPROVAL

CONDITIONS OF APPROVAL ATTACHED

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company
Well No: GMBU P-32-8-18
API No: 43-047-52594

Location: NESE Sec. 31, T8S, R18E
Lease No: UTU-74404
Agreement: GREATER MONUMENT BUTTE

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

| | |
|---|---|
| Location Construction (Notify Environmental Scientist) | - Forty-Eight (48) hours prior to construction of location and access roads. |
| Location Completion (Notify Environmental Scientist) | - Prior to moving on the drilling rig. |
| Spud Notice (Notify Petroleum Engineer) | - Twenty-Four (24) hours prior to spudding the well. |
| Casing String & Cementing (Notify Supv. Petroleum Tech.) | - Twenty-Four (24) hours prior to running casing and cementing all casing strings to: blm ut vn opreport@blm.gov |
| BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.) | - Twenty-Four (24) hours prior to initiating pressure tests. |
| First Production Notice (Notify Petroleum Engineer) | - Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days. |

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

•
Monitoring and Reporting

- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) that designates the proposed site-specific monitoring and reference sites chosen for the location. A description of the proposed sites shall be included, as well as a map showing the locations of the proposed sites.
- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) 3 growing seasons after reclamation efforts have occurred evaluating the status of the reclaimed areas in order to determine whether the BLM standards set forth in the Green River District Reclamation Guidelines have been met (30% or greater basal cover).
- Prior to beginning new surface disturbance, the operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) providing the results of the noxious weed inventory described in the Green River District Reclamation Guidelines (2011). If weeds are found the report shall include 1) A GPS location recorded in North American Datum 1983; 2) species; 3) canopy cover or number of plants; 4) and size of infestation (estimate square feet or acres. Information shall be also documented in the reclamation report.

CONDITIONS OF APPROVAL

Wildlife

In accordance with the Record of Decision for the Castle Peak and Eightmile Flat Oil and Gas Expansion Project, Newfield Rocky Mountains Inc., the following COA's are required:

- WFM-1 On level or gently sloping ground (5 percent slope or less) Newfield will elevate surface pipelines (4 inches or greater in diameter) a minimum of 6 inches above the ground to allow passage of small animals beneath the pipe. This ground clearance will be achieved by placing the pipeline on blocks at intervals of 150 to 200 feet.

- WFM-4 Newfield will install noise reduction devices on all pump jacks to reduce intermittent noise to 45 dBA at 660 feet from the source.

COA's derived from mitigating measures in the EA:

- Newfield will contract a qualified biologist to conduct a breeding bird survey within 330 feet (100 meters) from proposed surface disturbance activities associated with wellfield development (e.g. well pads, roads, pipelines, power lines, and ancillary facilities) that would occur during the breeding season from April 1 through July 31. If an active nest for important migratory bird species (USFWS Bird of Conservation Concern, Partners in Flight Priority Bird Species, Utah Sensitive Species) is documented during the survey, Newfield will coordinate with to determine if any additional protection measures will be required. Alternatively, prior to surface disturbance activities within that year, Newfield will clear vegetation within the year of surface disturbance activities outside of the breeding season (April 1 through July 31).

If construction and drilling is anticipated during any of the following wildlife seasonal spatial restrictions, a BLM biologist or a qualified consulting firm biologist must conduct applicable surveys using an accepted protocol prior to any ground disturbing activities.

- The proposed project is within ½ mile of a golden eagle nest. If construction or drilling is proposed from January 1-August 31 then a nest survey will be conducted by a qualified biologist. If the nest is found to be inactive, then permission to proceed may be granted by the BLM Authorized Officer. If the nest is determined to be active, then the timing restriction will remain in effect.

For protection of T&E Fish if drawing water from the Green River

- For areas of fresh water collection, an infiltration gallery will be constructed in a Service approved location. An infiltration gallery is basically a pit or trench dug within the floodplain to a depth below the water table. Water is drawn from the pit rather than from the river directly. If this is not possible, limit pumping within the river to off-channel locations that do not connect to the river during high spring flows.
- If water cannot be drawn using the measures above and the pump head will be located in the river channel where larval fish are known to occur, the following measures apply:
 - Avoid pumping from low-flow or no-flow areas as these habitats tend to concentrate larval fish
 - Avoid pumping to the greatest extent possible, during that period of the year when larval fish may be present (see previous bullet); and
 - Avoid pumping, to the greatest extent possible, during the midnight hours (10:00 p.m. to 2:00 a.m.) as larval drift studies indicate that this is a period of greatest daily activity. Dusk is the preferred pumping time, as larval drift abundance is lowest during this time.
 - Screen all pump intakes with 3/32-inch mesh material.
 -
- Report any fish impinged on the intake screen to the FWS office (801.975.3330) and the:
Utah Division of Wildlife Resources
Northeastern Region
152 East 100 North
Vernal, UT 84078
(435) 781-9453

Air Quality

- All internal combustion equipment will be kept in good working order.
- Water or other approved dust suppressants will be used at construction sites and along roads, as determined appropriate by the Authorized Officer. Dust suppressant such as magnesium chloride or fresh water may be used, as needed, during the drilling phase.
- Open burning of garbage or refuse will not occur at well sites or other facilities.
- Drill rigs will be equipped with Tier II or better diesel engines.
- Low bleed pneumatics will be installed on separator dump valves and other controllers.
- During completion, no venting will occur, and flaring will be limited as much as possible. Production equipment and gathering lines will be installed as soon as possible.
- Telemetry will be installed to remotely monitor and control production.
- Signs will be installed on the access road, reducing speed to 25 MPH, during the drilling phase.
- When feasible, two or more rigs (including drilling and completion rigs) will not be run simultaneously within 200 meters of each other. If two or more rigs must be run simultaneously within 200 meters of each other, then effective public health buffer zones out to 200 meters (m) from the nearest emission source will be implemented. Examples of an effective public health protection buffer zone include the demarcation of a public access exclusion zone by signage at intervals of every 250 feet that is visible from a distance of 125 feet during daylight hours, and a physical buffer such as active surveillance to ensure the property is not accessible by the public during drilling operations. Alternatively, the proponent may demonstrate compliance with the 1-hour NO₂ National Ambient Air Quality Standards (NAAQS) with appropriate and accepted near-field modeling. As part of this demonstration, the proponent may propose alternative mitigation that could include but is not limited to natural gas-fired drill rigs, installation of NO_x controls, time/use restrictions, and/or drill rig spacing.
- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 grams of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower-hour.
- All new and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 grams of NO_x per horsepower-hour.
- Green completions would be used for all well completion activities where technically feasible.
- Employ enhanced VOC emission controls with 95% control efficiency on production equipment having a potential to emit greater than 5 tons per year.

Threatened, Endangered and Candidate Plant Species

Reinitiation of Section 7 consultation with the USFWS will be sought immediately if any loss of plants or occupied habitat for Pariette cactus or Uinta Basin hookless cactus is anticipated as a result of project activities.

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Newfield Production Co. shall adhere to all referenced requirements in the SOP (version: "Greater Monument Butte Green River Development Program", Feb 16, 2012). The operator shall also comply with applicable laws and regulations; with lease terms Onshore Oil and Gas Orders, NTL's; and with other orders and instructions of the, authorized officer.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB

or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to BLM_UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid,

and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Pro Petro 8
Submitted By Branden Arnold Phone Number 435-401-0223
Well Name/Number GMBU P-32-8-18
Qtr/Qtr NE/SE Section 31 Township 8S Range 18E
Lease Serial Number UTU74404
API Number 43-047-52594

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 3/24/13 8:00 AM ☒ PM ☐

Casing – Please report time casing run starts, not cementing times.

- ☒ Surface Casing
☐ Intermediate Casing
☐ Production Casing
☐ Liner
☐ Other

Date/Time 3/24/13 3:00 AM ☐ PM ☒

BOPE

- ☐ Initial BOPE test at surface casing point
☐ BOPE test at intermediate casing point
☐ 30 day BOPE test
☐ Other

RECEIVED

MAR 28 2013

DIV OF OIL, GAS & MINING

Date/Time _____ AM ☐ PM ☐

Remarks _____

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include area code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Section 31 T8S R18E 2163 FSL 0736 FEL

5. Lease Serial No.

USA UTU-74404

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

GMBU

8. Well Name and No.

GMBU P-32-8-18

9. API Well No.

4304752594

10. Field and Pool, or Exploratory Area

GREATER MB UNIT

11. County or Parish, State

UINTAH, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

| TYPE OF SUBMISSION | TYPE OF ACTION | | | | |
|---|--|---|--|---|--|
| <input type="checkbox"/> Notice of Intent | <input type="checkbox"/> Acidize | <input type="checkbox"/> Deepen | <input type="checkbox"/> Production (Start/Resume) | <input type="checkbox"/> Water Shut-Off | |
| <input checked="" type="checkbox"/> Subsequent Report | <input type="checkbox"/> Alter Casing | <input type="checkbox"/> Fracture Treat | <input type="checkbox"/> Reclamation | <input type="checkbox"/> Well Integrity | |
| <input type="checkbox"/> Final Abandonment | <input type="checkbox"/> Casing Repair | <input type="checkbox"/> New Construction | <input type="checkbox"/> Recomplete | <input checked="" type="checkbox"/> Other | |
| | <input type="checkbox"/> Change Plans | <input type="checkbox"/> Plug & Abandon | <input type="checkbox"/> Temporarily Abandon | Spud Notice | |
| | <input type="checkbox"/> Convert to Injector | <input type="checkbox"/> Plug Back | <input type="checkbox"/> Water Disposal | | |

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 3/24/13 MIRU ProPetro #8. Spud well @8:00 AM. Drill 324' of 12 1/4" hole with air mist. TIH W/ 7 Jt's 8 5/8" J-55 24# csgn. Set @ 324.88. On 3/26/13 cement with 175 sks of class "G" w/ 2% CaCL2 + 0.25#/sk Cello- Flake Mixed @ 15.8ppg w/ 1.17ft3/sk yield. Returned 7 barrels cement to pit. WOC.

RECEIVED

APR 02 2013

DIV. OF OIL, GAS & MINING

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Title

Branden Arnold

Signature

Date

03/28/2013

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

Casing / Liner Detail

Well GMBU P-32-8-18

Prospect GMBU

Foreman

Run Date:

String Type Conductor, 14", 36.75#, H-40, W (Welded)

- Detail From Top To Bottom -

| Depth | Length | JTS | Description | OD | ID |
|-------|--------|-----|---------------|--------|--------|
| 40.00 | | | 10' KB | | |
| 10.00 | 30.00 | | 14" Conductor | 14.000 | 13.500 |
| 40.00 | | | - | | |

Cement Detail

Cement Company:

| Slurry | # of Sacks | Weight (ppg) | Yield | Volume (ft³) | Description - Slurry Class and Additives |
|--------|------------|--------------|-------|--------------|--|
|--------|------------|--------------|-------|--------------|--|

| | |
|---------------------------------|---|
| Stab-In-Job? | |
| BHT: | 0 |
| Initial Circulation Pressure: | |
| Initial Circulation Rate: | |
| Final Circulation Pressure: | |
| Final Circulation Rate: | |
| Displacement Fluid: | |
| Displacement Rate: | |
| Displacement Volume: | |
| Mud Returns: | |
| Centralizer Type And Placement: | |

| | |
|-------------------------------|--|
| Cement To Surface? | |
| Est. Top of Cement: | |
| Plugs Bumped? | |
| Pressure Plugs Bumped: | |
| Floats Holding? | |
| Casing Stuck On / Off Bottom? | |
| Casing Reciprocated? | |
| Casing Rotated? | |
| CIP: | |
| Casing Wt Prior To Cement: | |
| Casing Weight Set On Slips: | |

Casing / Liner Detail

Well GMBU P-32-8-18
Prospect GMBU
Foreman
Run Date:
String Type Surface, 8.625", 24#, J-55, STC (Generic)

- Detail From Top To Bottom -

| Depth | Length | JTS | Description | OD | ID |
|--------|--------|-----|-----------------------|-------|----|
| 322.88 | | | 10' KB | | |
| 10.00 | 1.42 | | Wellhead | | |
| 11.42 | 266.27 | 6 | 8 5/8" Surface Casing | 8.625 | |
| 277.69 | 44.22 | 1 | Shoe Joint | 8.625 | |
| 321.91 | 0.97 | | Guide Shoe | 8.625 | |
| 322.88 | | | - | | |

Cement Detail

Cement Company: Other

| Slurry | # of Sacks | Weight (ppg) | Yield | Volume (ft ³) | Description - Slurry Class and Additives |
|----------|------------|--------------|-------|---------------------------|--|
| Slurry 1 | 175 | 15.8 | 1.17 | 204.75 | Class G + 2% CaCl + .25# CF |

| | |
|--|-------|
| Stab-In-Job? | No |
| BHT: | 0 |
| Initial Circulation Pressure: | |
| Initial Circulation Rate: | |
| Final Circulation Pressure: | |
| Final Circulation Rate: | |
| Displacement Fluid: | Water |
| Displacement Rate: | |
| Displacement Volume: | |
| Mud Returns: | |
| Centralizer Type And Placement: | |
| Middle of first, top of second and third for a total of three. | |

| | |
|-------------------------------|------|
| Cement To Surface? | Yes |
| Est. Top of Cement: | 0 |
| Plugs Bumped? | Yes |
| Pressure Plugs Bumped: | 400 |
| Floats Holding? | No |
| Casing Stuck On / Off Bottom? | No |
| Casing Reciprocated? | No |
| Casing Rotated? | No |
| CIP: | 9:45 |
| Casing Wt Prior To Cement: | |
| Casing Weight Set On Slips: | |

| | | |
|--|--|---|
| STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING | | FORM 9 |
| SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals. | | 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-74404 |
| 1. TYPE OF WELL Oil Well | | 6. IF INDIAN, ALLOTTEE OR TRIBE NAME: |
| 2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY | | 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV) |
| 3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052 | | 8. WELL NAME and NUMBER: GMBU P-32-8-18 |
| 4. LOCATION OF WELL FOOTAGES AT SURFACE: 2163 FSL 0736 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NESE Section: 31 Township: 08.0S Range: 18.0E Meridian: S | | 9. API NUMBER: 43047525940000 |
| PHONE NUMBER: 435 646-4825 Ext | | 9. FIELD and POOL or WILDCAT: MONUMENT BUTTE |
| COUNTY: UINTAH | | STATE: UTAH |
| 11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA | | |
| TYPE OF SUBMISSION | TYPE OF ACTION | |
| <input type="checkbox"/> NOTICE OF INTENT Approximate date work will start: | <input type="checkbox"/> ACIDIZE | |
| <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: | <input type="checkbox"/> ALTER CASING | |
| <input type="checkbox"/> SPUD REPORT Date of Spud: | <input type="checkbox"/> CASING REPAIR | |
| <input checked="" type="checkbox"/> DRILLING REPORT Report Date: 4/29/2013 | <input type="checkbox"/> CHANGE TO PREVIOUS PLANS | |
| | <input type="checkbox"/> CHANGE TUBING | |
| | <input type="checkbox"/> CHANGE WELL STATUS | |
| | <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS | |
| | <input type="checkbox"/> CONVERT WELL TYPE | |
| | <input type="checkbox"/> DEEPEN | |
| | <input type="checkbox"/> FRACTURE TREAT | |
| | <input type="checkbox"/> NEW CONSTRUCTION | |
| | <input type="checkbox"/> OPERATOR CHANGE | |
| | <input type="checkbox"/> PLUG AND ABANDON | |
| | <input type="checkbox"/> PLUG BACK | |
| | <input checked="" type="checkbox"/> PRODUCTION START OR RESUME | |
| | <input type="checkbox"/> RECLAMATION OF WELL SITE | |
| | <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION | |
| | <input type="checkbox"/> REPERFORATE CURRENT FORMATION | |
| | <input type="checkbox"/> SIDETRACK TO REPAIR WELL | |
| | <input type="checkbox"/> TEMPORARY ABANDON | |
| | <input type="checkbox"/> TUBING REPAIR | |
| | <input type="checkbox"/> VENT OR FLARE | |
| | <input type="checkbox"/> WATER DISPOSAL | |
| | <input type="checkbox"/> WATER SHUTOFF | |
| | <input type="checkbox"/> SI TA STATUS EXTENSION | |
| | <input type="checkbox"/> WILDCAT WELL DETERMINATION | |
| | <input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/> | |
| 12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. The above well was placed on production on 04/29/2013 at 15:15 hours. | | |
| Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY May 10, 2013 | | |
| NAME (PLEASE PRINT) Jennifer Peatross | PHONE NUMBER 435 646-4885 | TITLE Production Technician |
| SIGNATURE N/A | DATE 5/9/2013 | |

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT **PBTVD 6199'**

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. Type of Well ☒ Oil Well ☐ Gas Well ☐ Dry ☐ Other
b. Type of Completion: ☒ New Well ☐ Work Over ☐ Deepen ☐ Plug Back ☐ Diff. Resvr.,
Other: _____

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

3. Address
1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
(435) 646-3721

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

At surface 2163' FSL & 736' FEL (NE/SE) SEC. 31, T8S, R18E (UTU-74404)

At top prod. interval reported below 1583' FSL & 170' FEL (NE/SE) SEC. 31, T8S, R18E (UTU-74404)

At total depth 1270' FSL & 99' FWL (SW/SW) SEC. 32, T8S, R18E (ML-22058)

14. Date Spudded
03/24/2013

15. Date T.D. Reached
04/02/2013

16. Date Completed 04/29/2013
☐ D & A ☒ Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
4981' GL 4991' KB

18. Total Depth: MD 6390'
TVD 6234'

19. Plug Back T.D.: MD 6335'
TVD

20. Depth Bridge Plug Set: MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)

DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? ☒ No ☐ Yes (Submit analysis)
Was DST run? ☒ No ☐ Yes (Submit report)
Directional Survey? ☐ No ☒ Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

| Hole Size | Size/Grade | Wt. (#/ft.) | Top (MD) | Bottom (MD) | Stage Cementer Depth | No. of Sks. & Type of Cement | Slurry Vol. (BBL) | Cement Top* | Amount Pulled |
|-----------|-------------|-------------|----------|-------------|----------------------|------------------------------|-------------------|-------------|---------------|
| 12-1/4" | 8-5/8" J-55 | 24# | 0 | 323' | | 175 CLASS G | | | |
| 7-7/8" | 5-1/2" J-55 | 15.5# | 0 | 6381' | | 480 50/50 POZ | | 70' | |
| | | | | | | 251 PREMLITE | | | |
| | | | | | | | | | |
| | | | | | | | | | |
| | | | | | | | | | |
| | | | | | | | | | |

24. Tubing Record

| Size | Depth Set (MD) | Packer Depth (MD) | Size | Depth Set (MD) | Packer Depth (MD) | Size | Depth Set (MD) | Packer Depth (MD) |
|--------|----------------|-------------------|------|----------------|-------------------|------|----------------|-------------------|
| 2-7/8" | EOT@ 6124' | TA @ 6025' | | | | | | |

25. Producing Intervals

| Formation | Top | Bottom | Perforated Interval | Size | No. Holes | Perf. Status |
|----------------|----------|----------|---------------------|-------|-----------|--------------|
| A) Green River | 4498' MD | 6044' MD | 4498-6044' MD | 0.34" | 66 | |
| B) | | | | | | |
| C) | | | | | | |
| D) | | | | | | |

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

| Depth Interval | Amount and Type of Material |
|----------------|--|
| 4498-6044' MD | Frac w/ 239569#s 20/40 white sand in 2190 bbls of Lightning 17 fluid, in 4 stages. |
| | |
| | |

28. Production - Interval A

| Date First Produced | Test Date | Hours Tested | Test Production | Oil BBL | Gas MCF | Water BBL | Oil Gravity Corr. API | Gas Gravity | Production Method |
|---------------------|----------------------|--------------|-----------------|---------|---------|-----------|-----------------------|-------------|---------------------------------|
| 4/29/13 | 5/8/13 | 24 | → | 25 | 46 | 0 | | | 2-1/2" x 1-3/4" x 24' RHAC Pump |
| Choke Size | Tbg. Press. Flwg. SI | Csg. Press. | 24 Hr. Rate → | Oil BBL | Gas MCF | Water BBL | Gas/Oil Ratio | Well Status | |
| | | | | | | | | PRODUCING | |

28a. Production - Interval B

| Date First Produced | Test Date | Hours Tested | Test Production | Oil BBL | Gas MCF | Water BBL | Oil Gravity Corr. API | Gas Gravity | Production Method |
|---------------------|----------------------|--------------|-----------------|---------|---------|-----------|-----------------------|-------------|-------------------|
| | | | → | | | | | | |
| Choke Size | Tbg. Press. Flwg. SI | Csg. Press. | 24 Hr. Rate → | Oil BBL | Gas MCF | Water BBL | Gas/Oil Ratio | Well Status | |
| | | | | | | | | | |

*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

| Date First Produced | Test Date | Hours Tested | Test Production → | Oil BBL | Gas MCF | Water BBL | Oil Gravity Corr. API | Gas Gravity | Production Method |
|---------------------|-------------------------|--------------|----------------------|---------|---------|-----------|--------------------------|-------------|-------------------|
| Choke Size | Tbg. Press. Flwg. SI | Csg. Press. | 24 Hr. Rate → | Oil BBL | Gas MCF | Water BBL | Gas/Oil Ratio | Well Status | |

28c. Production - Interval D

| Date First Produced | Test Date | Hours Tested | Test Production → | Oil BBL | Gas MCF | Water BBL | Oil Gravity Corr. API | Gas Gravity | Production Method |
|---------------------|-------------------------|--------------|----------------------|---------|---------|-----------|--------------------------|-------------|-------------------|
| Choke Size | Tbg. Press. Flwg. SI | Csg. Press. | 24 Hr. Rate → | Oil BBL | Gas MCF | Water BBL | Gas/Oil Ratio | Well Status | |

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD AND USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS


| Formation | Top | Bottom | Descriptions, Contents, etc. | Name | Top |
|-----------|-----|--------|------------------------------|---------------------------------------|----------------|
| | | | | | Meas. Depth |
| | | | | GARDEN GULCH MRK GARDEN GULCH 1 | 4003' 4178' |
| | | | | GARDEN GULCH 2 POINT 3 | 4297' 4573' |
| | | | | X MRKR Y MRKR | 4797' 4834' |
| | | | | DOUGLAS CREEK MRK BI CARBONATE MRK | 4969' 5207' |
| | | | | B LIMESTONE MRK CASTLE PEAK | 5417' 5793' |
| | | | | BASAL CARBONATE WASATCH | 6207' 6329' |

32. Additional remarks (include plugging procedure):

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- ☐ Electrical/Mechanical Logs (1 full set req'd.)
 ☐ Geologic Report
 ☐ DST Report
 ☒ Directional Survey
☐ Sundry Notice for plugging and cement verification
 ☐ Core Analysis
 ☒ Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Jennifer Peatross Title Production Technician
 Signature  Date 05/30/2013

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 3)

(Form 3160-4, page 2)



NEWFIELD EXPLORATION

USGS Myton SW (UT)

SECTION 31 T8S, R18E

P-32-8-18

Wellbore #1

Design: Actual

End of Well Report

15 April, 2013





Payzone Directional

End of Well Report



| | | | |
|-----------|----------------------|------------------------------|-----------------------------------|
| Company: | NEWFIELD EXPLORATION | Local Co-ordinate Reference: | Well P-32-8-18 |
| Project: | USGS Myton SW (UT) | TVD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Site: | SECTION 31 T8S, R18E | MD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Well: | P-32-8-18 | North Reference: | True |
| Wellbore: | Wellbore #1 | Survey Calculation Method: | Minimum Curvature |
| Design: | Actual | Database: | EDM 2003.21 Single User Db |

| | | | |
|-------------|--|---------------|----------------|
| Project: | USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA | System Datum: | Mean Sea Level |
| Map System: | US State Plane 1983 | | |
| Geo Datum: | North American Datum 1983 | | |
| Map Zone: | Utah Central Zone | | |

| | | | |
|-----------------------|----------------------|-------------------|-------------------|
| Site | SECTION 31 T8S, R18E | | |
| Site Position: | | Northing: | 7,201,349.38 ft |
| From: | Lat/Long | Easting: | 2,079,946.45 ft |
| Position Uncertainty: | 0.0 ft | Slot Radius: | " |
| | | Latitude: | 40° 4' 44.300 N |
| | | Longitude: | 109° 55' 44.860 W |
| | | Grid Convergence: | 1.01 ° |

| | | | |
|----------------------|---|---------------------|-------------------|
| Well | P-32-8-18, SHL LAT: 40 04 23.19 LONG: -109 55 46.03 | | |
| Well Position | +N/S 0.0 ft | Northing: | 7,199,212.13 ft |
| | +E/W 0.0 ft | Easting: | 2,079,893.03 ft |
| Position Uncertainty | 0.0 ft | Wellhead Elevation: | 4,991.0 ft |
| | | Latitude: | 40° 4' 23.190 N |
| | | Longitude: | 109° 55' 46.030 W |
| | | Ground Level: | 4,981.0 ft |

| | | | |
|-----------|-------------|-------------|-----------------|
| Wellbore | Wellbore #1 | | |
| Magnetics | Model Name | Sample Date | Declination (°) |
| | IGRF2010 | 8/16/2011 | 11.24 |
| | | | 65.84 |
| | | | 52.292 |

| | | | |
|-------------------|------------------|---------------|-----------|
| Design | Actual | | |
| Audit Notes: | | | |
| Version: | 1.0 | Phase: | ACTUAL |
| Vertical Section: | | Tie On Depth: | 0.0 |
| | Depth From (TVD) | +N-S (ft) | +E/W (ft) |
| | 0.0 | 0.0 | 0.0 |
| | | Direction (°) | 136.34 |

| | | | | |
|----------------|---------|-------------------------|-----------|----------------|
| Survey Program | Date | 4/15/2013 | | |
| From (ft) | To (ft) | Survey (Wellbore) | Tool Name | Description |
| 377.0 | 6,371.2 | Survey #1 (Wellbore #1) | MWD | MWD - Standard |



Payzone Directional
End of Well Report



| | | | |
|-----------|----------------------|------------------------------|-----------------------------------|
| Company: | NEWFIELD EXPLORATION | Local Co-ordinate Reference: | Well P-32-8-18 |
| Project: | USGS Myton SW (UT) | TVD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Site: | SECTION 31 T8S, R18E | MD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Well: | P-32-8-18 | North Reference: | True |
| Wellbore: | Wellbore #1 | Survey Calculation Method: | Minimum Curvature |
| Design: | Actual | Database: | EDM 2003.21 Single User Db |

| Survey | MD (ft) | Inc (°) | Azi (azimuth) (°) | TVD (ft) | V. Sec (ft) | N/S (ft) | EW (ft) | Dleg (°/100ft) | Build (°/100ft) | Turn (°/100ft) |
|--------|------------|------------|----------------------|-------------|----------------|-------------|------------|-------------------|--------------------|-------------------|
| | 0.0 | 0.00 | 0.00 | 0.0 | 0.0 | 0.0 | 0.0 | 0.00 | 0.00 | 0.00 |
| | 377.0 | 0.48 | 107.70 | 377.0 | 1.4 | -0.5 | 1.5 | 0.13 | 0.13 | 0.00 |
| | 407.0 | 0.40 | 113.60 | 407.0 | 1.6 | -0.6 | 1.7 | 0.31 | -0.27 | 19.67 |
| | 438.0 | 0.60 | 102.30 | 438.0 | 1.8 | -0.6 | 2.0 | 0.72 | 0.65 | -36.45 |
| | 468.0 | 0.80 | 116.90 | 468.0 | 2.2 | -0.8 | 2.3 | 0.94 | 0.67 | 55.33 |
| | 499.0 | 1.10 | 104.40 | 499.0 | 2.6 | -1.0 | 2.8 | 1.23 | 0.97 | -46.77 |
| | 529.0 | 1.50 | 101.80 | 529.0 | 3.2 | -1.1 | 3.5 | 1.35 | 1.33 | -8.67 |
| | 560.0 | 1.80 | 103.80 | 560.0 | 3.9 | -1.3 | 4.3 | 0.99 | 0.97 | 6.45 |
| | 590.0 | 2.10 | 106.90 | 589.9 | 4.8 | -1.6 | 5.3 | 1.06 | 1.00 | 10.33 |
| | 621.0 | 2.20 | 108.10 | 620.9 | 5.8 | -1.9 | 6.4 | 0.35 | 0.32 | 3.87 |
| | 652.0 | 2.70 | 105.20 | 651.9 | 7.0 | -2.3 | 7.7 | 1.66 | 1.61 | -9.35 |
| | 682.0 | 2.80 | 100.40 | 681.9 | 8.2 | -2.6 | 9.1 | 0.84 | 0.33 | -16.00 |
| | 713.0 | 3.00 | 102.30 | 712.8 | 9.5 | -2.9 | 10.6 | 0.72 | 0.65 | 6.13 |
| | 743.0 | 3.70 | 103.50 | 742.8 | 10.9 | -3.3 | 12.3 | 2.34 | 2.33 | 4.00 |
| | 773.0 | 4.40 | 103.00 | 772.7 | 12.7 | -3.8 | 14.4 | 2.34 | 2.33 | -1.67 |
| | 804.0 | 4.90 | 102.80 | 803.6 | 14.8 | -4.4 | 16.8 | 1.61 | 1.61 | -0.65 |
| | 834.0 | 5.10 | 104.50 | 833.5 | 17.0 | -5.0 | 19.4 | 0.83 | 0.67 | 5.67 |
| | 865.0 | 5.30 | 107.10 | 864.4 | 19.4 | -5.8 | 22.1 | 1.00 | 0.65 | 8.39 |
| | 896.0 | 5.80 | 111.60 | 895.2 | 22.1 | -6.7 | 24.9 | 2.14 | 1.61 | 14.52 |
| | 926.0 | 6.10 | 113.70 | 925.0 | 24.9 | -7.9 | 27.8 | 1.24 | 1.00 | 7.00 |
| | 956.0 | 6.20 | 115.40 | 954.9 | 27.9 | -9.3 | 30.7 | 0.69 | 0.33 | 5.67 |
| | 987.0 | 6.50 | 117.60 | 985.7 | 31.1 | -10.8 | 33.8 | 1.25 | 0.97 | 7.10 |
| | 1,017.0 | 6.80 | 122.00 | 1,015.5 | 34.5 | -12.5 | 36.8 | 1.97 | 1.00 | 14.67 |
| | 1,061.0 | 7.30 | 126.20 | 1,059.2 | 39.7 | -15.6 | 41.3 | 1.63 | 1.14 | 9.55 |
| | 1,105.0 | 7.70 | 131.50 | 1,102.8 | 45.4 | -19.2 | 45.7 | 1.82 | 0.91 | 12.05 |
| | 1,149.0 | 8.70 | 134.30 | 1,146.3 | 51.7 | -23.5 | 50.3 | 2.45 | 2.27 | 6.36 |
| | 1,192.0 | 9.50 | 135.20 | 1,188.8 | 58.5 | -28.2 | 55.1 | 1.89 | 1.86 | 2.09 |



Payzone Directional
End of Well Report



| | | | |
|-----------|----------------------|------------------------------|-----------------------------------|
| Company: | NEWFIELD EXPLORATION | Local Co-ordinate Reference: | Well P-32-8-18 |
| Project: | USGS Myton SW (UT) | TVD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Site: | SECTION 31 T8S, R18E | MD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Well: | P-32-8-18 | North Reference: | True |
| Wellbore: | Wellbore #1 | Survey Calculation Method: | Minimum Curvature |
| Design: | Actual | Database: | EDM 2003.21 Single User Db |

| Survey | MD (ft) | Inc (°) | Azi (azimuth) (°) | TVD (ft) | V. Sec (ft) | N/S (ft) | EW (ft) | DLeg (°/100ft) | Build (°/100ft) | Turn (°/100ft) |
|--------|------------|------------|----------------------|-------------|----------------|-------------|------------|-------------------|--------------------|-------------------|
| | 1,236.0 | 10.60 | 136.70 | 1,232.1 | 66.2 | -33.8 | 60.5 | 2.57 | 2.50 | 3.41 |
| | 1,280.0 | 11.10 | 137.40 | 1,275.3 | 74.5 | -39.8 | 66.1 | 1.18 | 1.14 | 1.59 |
| | 1,324.0 | 11.70 | 138.50 | 1,318.5 | 83.1 | -46.3 | 71.9 | 1.45 | 1.36 | 2.50 |
| | 1,368.0 | 12.30 | 139.70 | 1,361.5 | 92.3 | -53.2 | 77.9 | 1.48 | 1.36 | 2.73 |
| | 1,411.0 | 13.00 | 139.70 | 1,403.4 | 101.7 | -60.4 | 84.0 | 1.63 | 1.63 | 0.00 |
| | 1,455.0 | 13.80 | 140.60 | 1,446.2 | 111.9 | -68.2 | 90.5 | 1.88 | 1.82 | 2.05 |
| | 1,499.0 | 14.50 | 139.80 | 1,488.9 | 122.6 | -76.5 | 97.4 | 1.65 | 1.59 | -1.82 |
| | 1,543.0 | 14.80 | 139.30 | 1,531.5 | 133.7 | -84.9 | 104.6 | 0.74 | 0.68 | -1.14 |
| | 1,587.0 | 15.10 | 138.40 | 1,574.0 | 145.0 | -93.5 | 112.1 | 0.86 | 0.68 | -2.05 |
| | 1,631.0 | 15.00 | 138.20 | 1,616.5 | 156.5 | -102.0 | 119.7 | 0.26 | -0.23 | -0.45 |
| | 1,675.0 | 15.10 | 137.60 | 1,659.0 | 167.9 | -110.5 | 127.4 | 0.42 | 0.23 | -1.36 |
| | 1,718.0 | 14.80 | 136.40 | 1,700.5 | 179.0 | -118.6 | 134.9 | 1.00 | -0.70 | -2.79 |
| | 1,762.0 | 14.70 | 136.10 | 1,743.1 | 190.2 | -126.7 | 142.7 | 0.29 | -0.23 | -0.68 |
| | 1,806.0 | 14.60 | 135.80 | 1,785.6 | 201.3 | -134.7 | 150.4 | 0.29 | -0.23 | -0.68 |
| | 1,850.0 | 14.30 | 134.40 | 1,828.2 | 212.3 | -142.5 | 158.2 | 1.05 | -0.68 | -3.18 |
| | 1,893.0 | 13.80 | 132.10 | 1,870.0 | 222.7 | -149.6 | 165.8 | 1.74 | -1.16 | -5.35 |
| | 1,937.0 | 13.40 | 130.10 | 1,912.7 | 233.0 | -156.4 | 173.6 | 1.40 | -0.91 | -4.55 |
| | 1,981.0 | 12.80 | 129.80 | 1,955.6 | 242.9 | -162.8 | 181.2 | 1.37 | -1.36 | -0.68 |
| | 2,025.0 | 13.20 | 132.40 | 1,998.5 | 252.8 | -169.3 | 188.7 | 1.61 | 0.91 | 5.91 |
| | 2,069.0 | 13.10 | 135.20 | 2,041.3 | 262.8 | -176.3 | 195.9 | 1.47 | -0.23 | 6.36 |
| | 2,113.0 | 13.20 | 136.40 | 2,084.1 | 272.8 | -183.5 | 202.9 | 0.66 | 0.23 | 2.73 |
| | 2,156.0 | 13.40 | 136.70 | 2,126.0 | 282.7 | -190.6 | 209.7 | 0.49 | 0.47 | 0.70 |
| | 2,200.0 | 13.20 | 136.00 | 2,168.8 | 292.8 | -198.0 | 216.7 | 0.58 | -0.45 | -1.59 |
| | 2,244.0 | 13.30 | 138.30 | 2,211.6 | 302.9 | -205.3 | 223.5 | 1.22 | 0.23 | 5.23 |
| | 2,288.0 | 13.40 | 138.90 | 2,254.5 | 313.0 | -213.0 | 230.2 | 0.39 | 0.23 | 1.36 |
| | 2,331.0 | 13.60 | 138.00 | 2,296.3 | 323.1 | -220.5 | 236.9 | 0.67 | 0.47 | -2.09 |
| | 2,375.0 | 13.80 | 139.30 | 2,339.0 | 333.5 | -228.3 | 243.8 | 0.83 | 0.45 | 2.95 |



Payzone Directional

End of Well Report



| | | | |
|-----------|----------------------|------------------------------|-----------------------------------|
| Company: | NEWFIELD EXPLORATION | Local Co-ordinate Reference: | Well P-32-8-18 |
| Project: | USGS Mylon SW (UT) | TVD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Site: | SECTION 31 T8S, R18E | MD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Well: | P-32-8-18 | North Reference: | True |
| Wellbore: | Wellbore #1 | Survey Calculation Method: | Minimum Curvature |
| Design: | Actual | Database: | EDM 2003.21 Single User Db |

| Survey | MD (ft) | Inc (°) | Azi (azimuth) (°) | TVD (ft) | V. Sec (ft) | N/S (ft) | EW (ft) | Dleg (°/100ft) | Build (°/100ft) | Turn (°/100ft) |
|--------|------------|------------|----------------------|-------------|----------------|-------------|------------|-------------------|--------------------|-------------------|
| | 2,419.0 | 14.00 | 140.00 | 2,381.7 | 344.0 | -236.4 | 250.6 | 0.59 | 0.45 | 1.59 |
| | 2,463.0 | 14.20 | 140.40 | 2,424.4 | 354.7 | -244.6 | 257.5 | 0.51 | 0.45 | 0.91 |
| | 2,507.0 | 14.30 | 140.00 | 2,467.0 | 365.5 | -252.9 | 264.4 | 0.32 | 0.23 | -0.91 |
| | 2,550.0 | 13.90 | 138.70 | 2,508.8 | 376.0 | -260.9 | 271.2 | 1.19 | -0.93 | -3.02 |
| | 2,594.0 | 13.20 | 137.30 | 2,551.5 | 386.3 | -268.5 | 278.1 | 1.76 | -1.59 | -3.18 |
| | 2,638.0 | 12.70 | 136.80 | 2,594.4 | 396.1 | -275.7 | 284.8 | 1.16 | -1.14 | -1.14 |
| | 2,682.0 | 12.80 | 136.70 | 2,637.3 | 405.9 | -282.8 | 291.5 | 0.23 | 0.23 | -0.23 |
| | 2,726.0 | 12.90 | 136.10 | 2,680.2 | 415.6 | -290.0 | 298.1 | 0.74 | 0.23 | 3.18 |
| | 2,769.0 | 13.20 | 137.80 | 2,722.1 | 425.3 | -297.2 | 304.6 | 0.72 | 0.70 | -0.70 |
| | 2,813.0 | 13.50 | 137.70 | 2,764.9 | 435.5 | -304.8 | 311.5 | 0.68 | 0.68 | -0.23 |
| | 2,857.0 | 13.80 | 137.60 | 2,807.7 | 445.9 | -312.4 | 318.5 | 0.68 | 0.68 | -0.23 |
| | 2,901.0 | 13.90 | 137.40 | 2,850.4 | 456.4 | -320.2 | 325.6 | 0.25 | 0.23 | -0.45 |
| | 2,945.0 | 13.20 | 136.80 | 2,893.2 | 466.7 | -327.7 | 332.6 | 1.62 | -1.59 | -1.36 |
| | 2,989.0 | 12.10 | 134.80 | 2,936.1 | 476.3 | -334.7 | 339.3 | 2.69 | -2.50 | -4.55 |
| | 3,032.0 | 11.70 | 133.60 | 2,978.2 | 485.2 | -340.8 | 345.7 | 1.09 | -0.93 | -2.79 |
| | 3,076.0 | 11.60 | 134.10 | 3,021.3 | 494.1 | -347.0 | 352.1 | 0.32 | -0.23 | 1.14 |
| | 3,120.0 | 11.30 | 133.00 | 3,064.4 | 502.8 | -353.0 | 358.4 | 0.84 | -0.68 | -2.50 |
| | 3,164.0 | 11.50 | 134.20 | 3,107.5 | 511.5 | -359.0 | 364.7 | 0.71 | 0.45 | 2.73 |
| | 3,208.0 | 12.10 | 135.20 | 3,150.6 | 520.5 | -365.3 | 371.1 | 1.44 | 1.36 | 2.27 |
| | 3,251.0 | 12.70 | 135.90 | 3,192.6 | 529.7 | -371.9 | 377.5 | 1.44 | 1.40 | 1.63 |
| | 3,295.0 | 13.40 | 138.70 | 3,235.5 | 539.7 | -379.2 | 384.3 | 2.14 | 1.59 | 6.36 |
| | 3,339.0 | 13.40 | 139.20 | 3,278.3 | 549.8 | -386.9 | 391.0 | 0.26 | 0.00 | 1.14 |
| | 3,383.0 | 13.00 | 138.20 | 3,321.1 | 559.9 | -394.5 | 397.6 | 1.05 | -0.91 | -2.27 |
| | 3,427.0 | 13.20 | 137.70 | 3,364.0 | 569.8 | -401.9 | 404.3 | 0.52 | 0.45 | -1.14 |
| | 3,470.0 | 13.50 | 139.50 | 3,405.8 | 579.8 | -409.3 | 410.8 | 1.19 | 0.70 | 4.19 |
| | 3,514.0 | 14.00 | 140.00 | 3,448.5 | 590.2 | -417.3 | 417.6 | 1.17 | 1.14 | 1.14 |
| | 3,558.0 | 13.90 | 139.60 | 3,491.2 | 600.8 | -425.4 | 424.4 | 0.32 | -0.23 | -0.91 |



Payzone Directional End of Well Report



| | | | |
|-----------|----------------------|------------------------------|-----------------------------------|
| Company: | NEWFIELD EXPLORATION | Local Co-ordinate Reference: | Well P-32-8-18 |
| Project: | USGS Myton SW (UT) | TVD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Site: | SECTION 31 T8S, R18E | MD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Well: | P-32-8-18 | North Reference: | True |
| Wellbore: | Wellbore #1 | Survey Calculation Method: | Minimum Curvature |
| Design: | Actual | Database: | EDM 2003.21 Single User Db |

| Survey | MD (ft) | Inc (°) | Azi (azimuth) (°) | TVD (ft) | V. Sec (ft) | N/S (ft) | EW (ft) | Dleg (°/100ft) | Build (°/100ft) | Turn (°/100ft) |
|--------|------------|------------|----------------------|-------------|----------------|-------------|------------|-------------------|--------------------|-------------------|
| | 3,602.0 | 13.40 | 138.30 | 3,534.0 | 611.2 | -433.2 | 431.3 | 1.33 | -1.14 | -2.95 |
| | 3,646.0 | 12.90 | 137.30 | 3,576.8 | 621.2 | -440.7 | 438.0 | 1.25 | -1.14 | -2.27 |
| | 3,689.0 | 13.10 | 136.70 | 3,618.7 | 630.8 | -447.7 | 444.6 | 0.56 | 0.47 | -1.40 |
| | 3,733.0 | 13.60 | 137.60 | 3,661.5 | 641.0 | -455.2 | 451.5 | 1.23 | 1.14 | 2.05 |
| | 3,777.0 | 13.40 | 139.30 | 3,704.3 | 651.3 | -462.9 | 458.3 | 1.01 | -0.45 | 3.86 |
| | 3,821.0 | 13.40 | 137.80 | 3,747.1 | 661.5 | -470.5 | 465.1 | 0.79 | 0.00 | -3.41 |
| | 3,865.0 | 13.40 | 136.70 | 3,789.9 | 671.6 | -478.0 | 472.0 | 0.58 | 0.00 | -2.50 |
| | 3,909.0 | 13.10 | 136.00 | 3,832.8 | 681.7 | -485.3 | 478.9 | 0.77 | -0.66 | -1.59 |
| | 3,952.0 | 12.70 | 136.50 | 3,874.7 | 691.3 | -492.2 | 485.6 | 0.97 | -0.93 | 1.16 |
| | 3,996.0 | 12.70 | 134.60 | 3,917.6 | 701.0 | -499.1 | 492.4 | 0.95 | 0.00 | -4.32 |
| | 4,040.0 | 12.70 | 132.40 | 3,960.5 | 710.7 | -505.8 | 499.4 | 1.10 | 0.00 | -5.00 |
| | 4,084.0 | 12.70 | 133.10 | 4,003.5 | 720.3 | -512.4 | 506.5 | 0.35 | 0.00 | 1.59 |
| | 4,128.0 | 13.10 | 134.60 | 4,046.3 | 730.1 | -519.2 | 513.6 | 1.19 | 0.91 | 3.41 |
| | 4,172.0 | 13.20 | 136.10 | 4,089.2 | 740.1 | -526.3 | 520.6 | 0.81 | 0.23 | 3.41 |
| | 4,216.0 | 13.50 | 138.00 | 4,132.0 | 750.3 | -533.7 | 527.5 | 1.21 | 0.68 | 4.32 |
| | 4,259.0 | 13.70 | 139.10 | 4,173.8 | 760.4 | -541.3 | 534.2 | 0.76 | 0.47 | 2.56 |
| | 4,303.0 | 13.50 | 141.50 | 4,216.6 | 770.7 | -549.3 | 540.8 | 1.36 | -0.45 | 5.45 |
| | 4,347.0 | 13.40 | 142.00 | 4,259.4 | 780.9 | -557.3 | 547.1 | 0.35 | -0.23 | 1.14 |
| | 4,391.0 | 13.30 | 140.60 | 4,302.2 | 791.0 | -565.2 | 553.5 | 0.77 | -0.23 | -3.18 |
| | 4,435.0 | 12.90 | 139.90 | 4,345.0 | 801.0 | -572.9 | 559.9 | 0.98 | -0.91 | -1.59 |
| | 4,479.0 | 13.00 | 139.60 | 4,387.9 | 810.8 | -580.4 | 566.2 | 0.27 | 0.23 | -0.68 |
| | 4,522.0 | 13.30 | 138.70 | 4,429.8 | 820.6 | -587.8 | 572.6 | 0.84 | 0.70 | -2.09 |
| | 4,566.0 | 13.20 | 139.00 | 4,472.6 | 830.7 | -595.4 | 579.3 | 0.28 | -0.23 | 0.68 |
| | 4,610.0 | 12.70 | 137.20 | 4,515.5 | 840.5 | -602.7 | 585.9 | 1.46 | -1.14 | -4.09 |
| | 4,654.0 | 12.00 | 136.20 | 4,558.5 | 849.9 | -609.6 | 592.3 | 1.66 | -1.59 | -2.27 |
| | 4,698.0 | 12.30 | 137.50 | 4,601.5 | 859.2 | -616.4 | 598.6 | 0.92 | 0.68 | 2.95 |
| | 4,741.0 | 12.80 | 138.70 | 4,643.4 | 868.5 | -623.3 | 604.9 | 1.31 | 1.16 | 2.79 |



Payzone Directional
End of Well Report



| | | | |
|-----------|----------------------|------------------------------|-----------------------------------|
| Company: | NEWFIELD EXPLORATION | Local Co-ordinate Reference: | Well P-32-8-18 |
| Project: | USGS Wytton SW (UT) | TVD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Site: | SECTION 31 T8S, R18E | MD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Well: | P-32-8-18 | North Reference: | True |
| Wellbore: | Wellbore #1 | Survey Calculation Method: | Minimum Curvature |
| Design: | Actual | Database: | EDM 2003.21 Single User Db |

| Survey | MD (ft) | Inc (°) | Azi (azimuth) (°) | TVD (ft) | V. Sec (ft) | N/S | EW (ft) | DLeg (°/100ft) | Build (°/100ft) | Turn (°/100ft) |
|---------------|------------|------------|----------------------|-------------|----------------|--------|------------|-------------------|--------------------|-------------------|
| | 4,785.0 | 13.10 | 139.10 | 4,686.3 | 878.4 | -630.7 | 611.4 | 0.71 | 0.68 | 0.91 |
| | 4,829.0 | 13.00 | 139.60 | 4,729.2 | 888.3 | -638.3 | 617.8 | 0.34 | -0.23 | 1.14 |
| | 4,873.0 | 13.20 | 138.70 | 4,772.0 | 898.3 | -645.8 | 624.4 | 0.65 | 0.45 | -2.05 |
| | 4,917.0 | 13.20 | 138.50 | 4,814.9 | 908.3 | -653.4 | 631.0 | 0.10 | 0.00 | -0.45 |
| | 4,960.0 | 13.10 | 140.20 | 4,856.8 | 918.1 | -660.8 | 637.4 | 0.93 | -0.23 | 3.95 |
| | 5,004.0 | 13.20 | 141.60 | 4,899.6 | 928.0 | -668.5 | 643.7 | 0.76 | 0.23 | 3.18 |
| | 5,048.0 | 13.40 | 141.80 | 4,942.4 | 938.1 | -676.5 | 650.0 | 0.47 | 0.45 | 0.45 |
| | 5,092.0 | 13.30 | 141.10 | 4,985.2 | 948.2 | -684.4 | 656.3 | 0.43 | -0.23 | -1.59 |
| | 5,136.0 | 13.00 | 140.60 | 5,028.1 | 958.2 | -692.2 | 662.6 | 0.73 | -0.68 | -1.14 |
| | 5,180.0 | 12.40 | 141.30 | 5,071.0 | 967.9 | -699.7 | 668.7 | 1.41 | -1.36 | 1.59 |
| | 5,223.0 | 12.00 | 137.10 | 5,113.0 | 976.9 | -706.6 | 674.6 | 2.26 | -0.93 | -9.77 |
| | 5,267.0 | 12.10 | 138.70 | 5,156.1 | 986.1 | -713.4 | 680.8 | 0.79 | 0.23 | 3.64 |
| | 5,309.4 | 12.58 | 138.80 | 5,197.5 | 995.2 | -720.2 | 686.8 | 1.14 | 1.14 | 0.23 |
| P-32-8-18 TGT | | | | | | | | | | |
| | 5,311.0 | 12.60 | 138.80 | 5,199.0 | 995.5 | -720.5 | 687.0 | 1.14 | 1.14 | 0.22 |
| | 5,355.0 | 13.00 | 137.50 | 5,242.0 | 1,005.3 | -727.7 | 693.5 | 1.12 | 0.91 | -2.95 |
| | 5,399.0 | 12.70 | 136.10 | 5,284.9 | 1,015.0 | -734.9 | 700.2 | 0.98 | -0.68 | -3.18 |
| | 5,442.0 | 12.00 | 137.40 | 5,326.9 | 1,024.2 | -741.6 | 706.5 | 1.75 | -1.63 | 3.02 |
| | 5,486.0 | 11.80 | 138.90 | 5,369.9 | 1,033.3 | -748.3 | 712.6 | 0.84 | -0.45 | 3.41 |
| | 5,530.0 | 12.00 | 138.90 | 5,413.0 | 1,042.4 | -755.2 | 718.5 | 0.45 | 0.45 | 0.00 |
| | 5,574.0 | 12.40 | 136.80 | 5,456.0 | 1,051.7 | -762.1 | 724.8 | 1.36 | 0.91 | -4.77 |
| | 5,618.0 | 12.90 | 138.40 | 5,498.9 | 1,061.3 | -769.2 | 731.3 | 1.39 | 1.14 | 3.64 |
| | 5,661.0 | 12.10 | 139.30 | 5,540.9 | 1,070.6 | -776.2 | 737.4 | 1.91 | -1.86 | 2.09 |
| | 5,705.0 | 12.10 | 141.30 | 5,583.9 | 1,079.8 | -783.3 | 743.3 | 0.95 | 0.00 | 4.55 |
| | 5,749.0 | 12.70 | 141.00 | 5,626.9 | 1,089.2 | -790.6 | 749.2 | 1.37 | 1.36 | -0.68 |
| | 5,793.0 | 13.10 | 142.30 | 5,669.8 | 1,099.0 | -798.3 | 755.3 | 1.12 | 0.91 | 2.95 |
| | 5,837.0 | 13.30 | 143.20 | 5,712.6 | 1,109.0 | -806.3 | 761.4 | 0.85 | 0.45 | 2.05 |



Payzone Directional

End of Well Report




| | | | |
|-----------|----------------------|------------------------------|-----------------------------------|
| Company: | NEWFIELD EXPLORATION | Local Co-ordinate Reference: | Well P-32-8-18 |
| Project: | USGS Mylon SW (UT) | TVD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Site: | SECTION 31 T8S, R18E | MD Reference: | P-32-8-18 @ 4991.0ft (NDSI SS #2) |
| Well: | P-32-8-18 | North Reference: | True |
| Wellbore: | Wellbore #1 | Survey Calculation Method: | Minimum Curvature |
| Design: | Actual | Database: | EDM 2003.21 Single User Db |

| Survey | MD (ft) | Inc (°) | Azi (azimuth) (°) | TVD (ft) | V. Sec (ft) | N/S (ft) | EW (ft) | DLeg (°/100ft) | Build (°/100ft) | Turn (°/100ft) |
|--------|------------|------------|----------------------|-------------|----------------|-------------|------------|-------------------|--------------------|-------------------|
| | 5,880.0 | 13.80 | 143.30 | 5,754.4 | 1,119.0 | -814.4 | 767.4 | 1.16 | 1.16 | 0.23 |
| | 5,924.0 | 14.10 | 141.10 | 5,797.1 | 1,129.5 | -822.8 | 773.9 | 1.38 | 0.68 | -5.00 |
| | 5,968.0 | 14.00 | 138.50 | 5,839.8 | 1,140.2 | -830.9 | 780.8 | 1.45 | -0.23 | -5.91 |
| | 6,012.0 | 13.70 | 137.70 | 5,882.5 | 1,150.7 | -838.8 | 787.8 | 0.81 | -0.68 | -1.82 |
| | 6,056.0 | 13.80 | 137.60 | 5,925.3 | 1,161.2 | -846.5 | 794.9 | 0.23 | 0.23 | -0.23 |
| | 6,099.0 | 13.30 | 137.70 | 5,967.1 | 1,171.2 | -854.0 | 801.7 | 1.16 | -1.16 | 0.23 |
| | 6,143.0 | 12.40 | 138.10 | 6,010.0 | 1,181.0 | -861.2 | 808.2 | 2.06 | -2.05 | 0.91 |
| | 6,187.0 | 11.50 | 138.70 | 6,053.0 | 1,190.1 | -868.0 | 814.3 | 2.06 | -2.05 | 1.36 |
| | 6,231.0 | 10.80 | 140.40 | 6,096.2 | 1,198.6 | -874.5 | 819.8 | 1.76 | -1.59 | 3.86 |
| | 6,275.0 | 10.10 | 141.00 | 6,139.4 | 1,206.6 | -880.7 | 824.9 | 1.61 | -1.59 | 1.36 |
| | 6,319.0 | 9.50 | 140.60 | 6,182.8 | 1,214.0 | -886.5 | 829.6 | 1.37 | -1.36 | -0.91 |
| | 6,371.2 | 8.80 | 140.10 | 6,234.3 | 1,222.3 | -892.9 | 834.9 | 1.35 | -1.34 | -0.96 |

Checked By: _____ Approved By: _____ Date: _____





Project: USGS Myton SW (UT)
 Site: SECTION 31 T8S, R18E
 Well: P-32-8-18
 Wellbore: Wellbore #1
 Design: Actual



Azimuths to True North
 Magnetic North: 11.24°
 Magnetic Field
 Strength: 52291.9nT
 Dip Angle: 65.84°
 Date: 8/16/2011
 Model: IGRF2010

API Well Number: 43047525940000

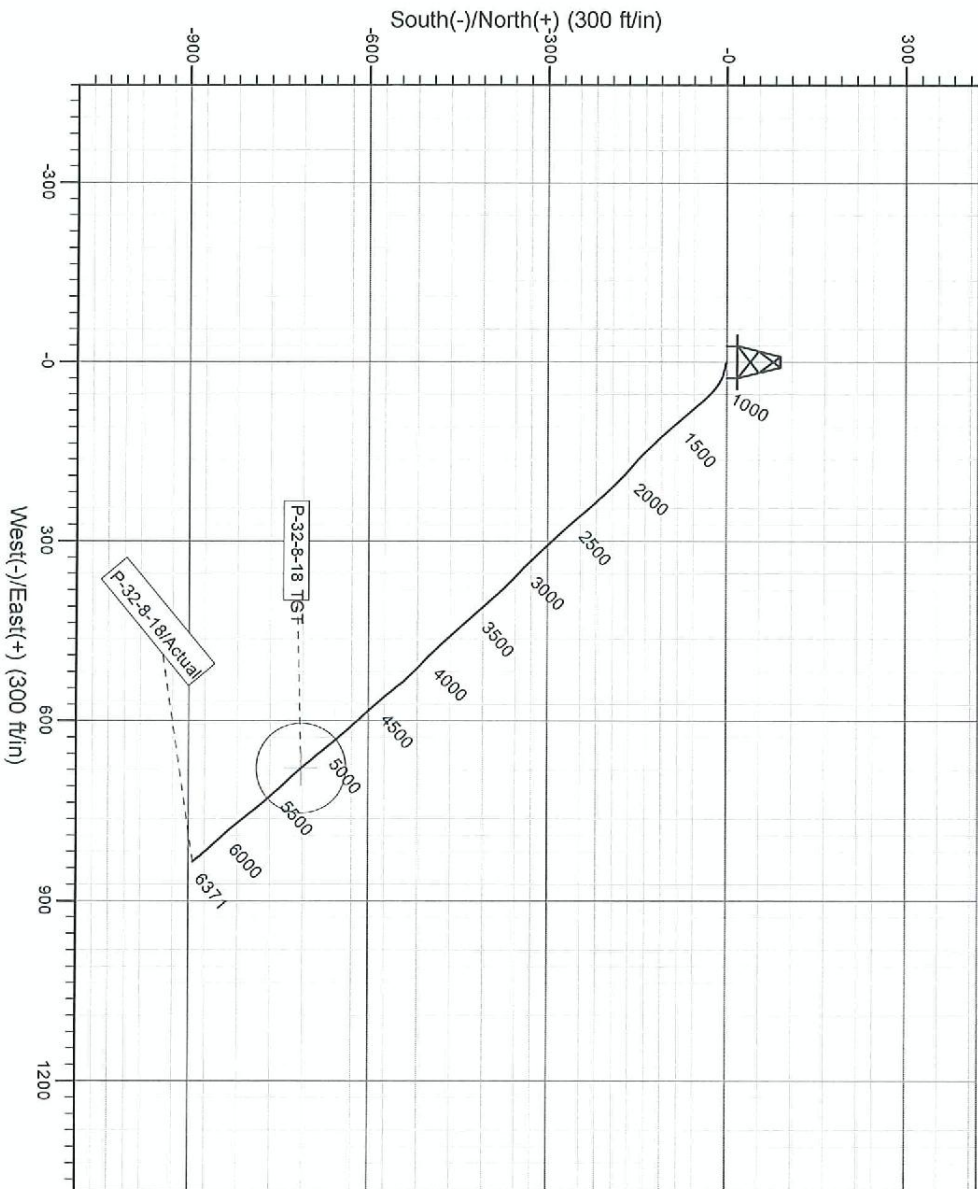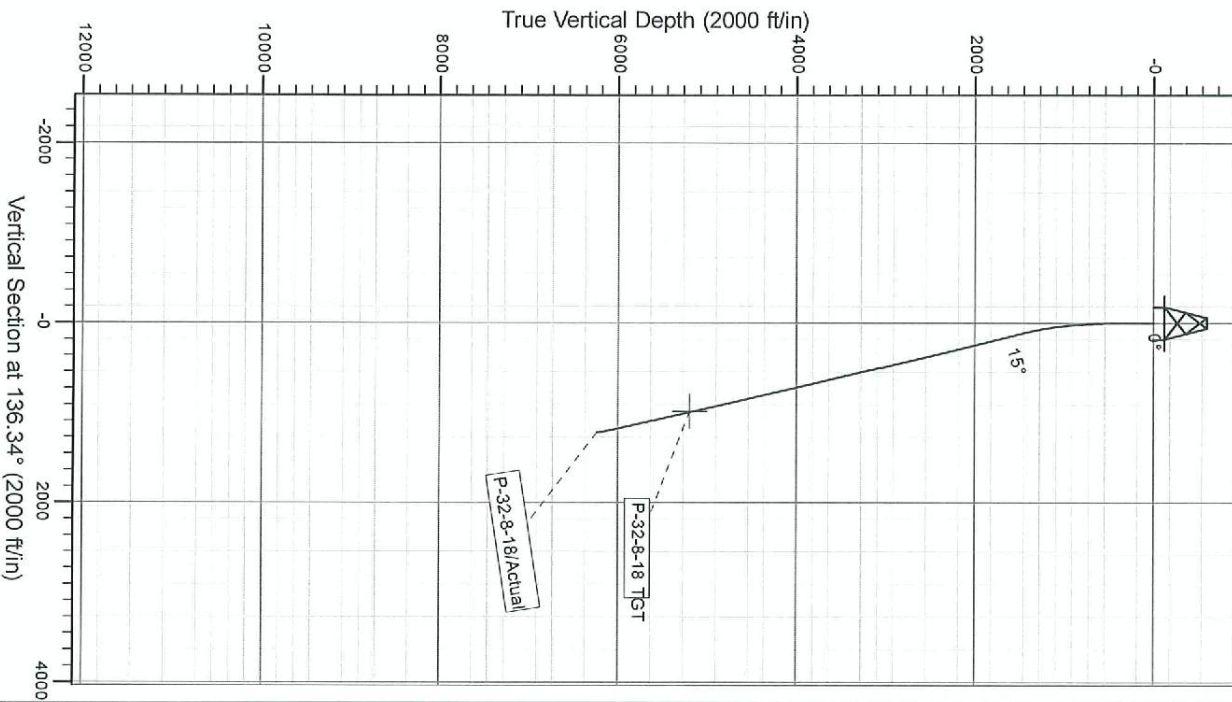

Design: Actual (P-32-8-18Wellbore #1)

Created By: *David Wells* Date: 12:28, April 15 2013

THIS SURVEY IS CORRECT TO THE BEST OF
 MY KNOWLEDGE AND IS SUPPORTED
 BY ACTUAL FIELD DATA

Daily Activity Report**Format For Sundry****GMBU P-32-8-18****2/1/2013 To 6/30/2013****4/17/2013 Day: 1****Completion**

Rigless on 4/17/2013 - CBL/psi test/perforate stg1 - RU S&S test trailer. Load & test csg to 4300# against bottom of BOP for 30min-good test. Test frac valve & csg valves-good tests. - RIH w/3 1/8" slick guns (16g, 0.34 EH, 21.00 pen). Perforate stg 1 @ CP4 6042-44', 6033-35', CP2 5914-15', 5907-09'. RD wireline. - MIRU Perforators wireline. RIH w/CBL tools. Run log from 6309' to surface under 0 psi. Estimated cement top @70'. SJ @3942-54'.

Daily Cost: \$0**Cumulative Cost:** \$19,291**4/18/2013 Day: 2****Completion**

Rigless on 4/18/2013 - Frac stg 1 & 2. Screenout stg2. Flowback well, RIH w/wight bar. Attempt to plug/perf. - Stage #2, LODC sands. 1270 psi on well. Frac LODC sds w/ 35,430#s of 20/40 White sand in 202 bbls Lightning 17 fluid. Broke @ 2793 psi @ 3.6 BPM. Treated w/ ave pressure of 2198 psi @ ave rate of 18.3 BPM. Pumped 504 gals of 15% HCL in flush for Stage #3. Screenout 30 bbls short of full flush leaving approximately 5300# sand in pipe, 349? of fill. Immediately flowback well. - Stage #1, CP4 & CP2 sands. 65 psi on well. Frac CP4 & CP2 sds w/ 50,431#s of 20/40 White sand in 288 bbls Lightning 17 fluid. Broke @ 1988 psi @ 3.3 BPM. ISIP 1515 psi, FG=.69, 1 min SIP 1373 psi, 4 min SIP 1188 psi. Treated w/ ave pressure of 2698 psi @ ave rate of 38.9 BPM. Pumped 504 gals of 15% HCL in flush for Stage #2. ISDP 1560 psi. FG=.69, 5 min SIP 1413 psi, 10 min SIP 1356 psi, 15 min SIP 1329 psi. Leave pressure on well. RU Perforators WLT, crane & lubricator. Pressure test lubricator to 4000 psi w/BakerHughes blender. RIH w/ Weatherford 5-1/2" 5K total composite flow through frac plug, perf guns. Set plug @ 5640'. Perforate LODC @ 5562-63?, 5555-56?, 5548-49' w/ 3 1/8" slick guns (16g, 0.34 EH, 21.00 pen) w/ 3 spf for total of 21 shots. 529 total BWTR - PSI test frac iron to 5300#, test pump kick-outs-good tests - Safety meeting - MIRU Baker Hughes frac fleet. - Flowback well. Return approx 150bbls. Returned acid but no sand. - RIH w/weight bar in attempt to gauge sand depth. Able to get weight bar to 5480' without seeing sand. POOH w/weight bar, RIH w/plug and perf guns. Tag sand (?) @ 5340'. - Tools came free, able to pull out of hole at desired speed. Tool string is completely intact. Visible damage to plug base. SWIFN - Able to slowly (max of 3 fmin) pull out of hole.

Daily Cost: \$0**Cumulative Cost:** \$30,612**4/19/2013 Day: 3****Completion**

Rigless on 4/19/2013 - Attempt sand @ 5100'pt to flush, unsuccessful. RIH w/wireline, tag sand @ 5100' - Frac 3 stages on O-32-8-18. - RU frac iron to P-32. Safety meeting & psi test frac iron to 4600#-good test.k - Attempt to flush, pumped 2.6bbls before pressuring out. - RIH w/weight bar to gauge sand depth, Tag sand @ 5100'. 540' of fill on top of plug @ 5640. POOH w/wireline. Call engineer for guidance.

Daily Cost: \$0**Cumulative Cost:** \$38,783**4/23/2013 Day: 5****Completion**

WWS #3 on 4/23/2013 - Perforate stg 3, frac stg 3-4 off rig. Flowback well - RU Perforators wireline. RIH w/Weatherford 5-1/2" 5K total composite flow through frac plug, perf guns. Set plug @ 5400'. Perforate B1 @ 5324-27', 5307-09? w/ 3 1/8" slick guns (16g, 0.34 EH, 21.00 pen) w/ 3 spf for total of 215 shots. POOH w/wireline. - Crew travel & safety mtg - Crew travel & safety mtg - LOAM from S-31-8-18 to P-32-8-18. MIRU, wait on 5K spool. ND manual frac valve, NU 5K spool & BOPs, Offload tbg, RU B&C Quick Test - LOAM from S-31-8-18 to P-32-8-18. MIRU, wait on 5K spool. ND manual frac valve, NU 5K spool & BOPs, Offload tbg, RU B&C Quick Test - PSI test BOPs-good tests - PSI test BOPs-good tests - Tally, PU & TIH w/NC, PSN & 164 jts. Tag fill @ 5109' - Tally, PU & TIH w/NC, PSN & 164 jts. Tag fill @ 5109' - Pull 6 stand & make up circ stand. C/O 346' of fill to 5455'. Circ well clean. - Pull 6 stand & make up circ stand. C/O 346' of fill to 5455'. Circ well clean. - TOO H w/tbg, LD NC & PSN, remove unneeded equipment form location to make room for frac crew. - Flowback well. Recovered approx. 600bbls-no visual oil. - Flowback well. Recovered approx. 600bbls-no visual oil. - Stage #4, GB6 & GB4 sands. 940 psi on well. Frac B1 sds w/ 104,436#s of 20/40 White sand in 557 bbls Lightning 17 fluid. Broke @ 2702 psi @ 2.3 BPM. Treated w/ ave pressure of 2123 psi @ ave rate of 44 BPM. ISDP 1840 psi. FG=.84, 5 min SIP 1748 psi, 10 min SIP 1643 psi, 15 min SIP 1534 psi. 769 total BWTR - Stage #4, GB6 & GB4 sands. 940 psi on well. Frac B1 sds w/ 104,436#s of 20/40 White sand in 557 bbls Lightning 17 fluid. Broke @ 2702 psi @ 2.3 BPM. Treated w/ ave pressure of 2123 psi @ ave rate of 44 BPM. ISDP 1840 psi. FG=.84, 5 min SIP 1748 psi, 10 min SIP 1643 psi, 15 min SIP 1534 psi. 769 total BWTR - Stage #3, B1 sands. 107 psi on well. Frac B1 sds w/ 49,273#s of 20/40 White sand in 292 bbls Lightning 17 fluid. Broke @ 3551 psi @ 2.5 BPM. Treated w/ ave pressure of 2243 psi @ ave rate of 28 BPM. Pumped 504 gals of 15% HCL in flush for Stage #4. ISDP 1322 psi. FG=.68, 5 min SIP 1202 psi, 10 min SIP 1152 psi, 15 min SIP 1122 psi. Leave pressure on well. RU Perforators WLT, crane & lubricator. Pressure test lubricator to 4000 psi w/BakerHughes blender. RIH w/ Weatherford 5-1/2" 5K total composite flow through frac plug, perf guns. Set plug @ 4640'. Perforate GB6 & GB4 @ 4562-64?, 4554-56?, 4506-08?, 4498-99? w/ 3 1/8" slick guns (16g, 0.34 EH, 21.00 pen) w/ 3 spf for total of 21 shots. 502 total BWTR - Stage #3, B1 sands. 107 psi on well. Frac B1 sds w/ 49,273#s of 20/40 White sand in 292 bbls Lightning 17 fluid. Broke @ 3551 psi @ 2.5 BPM. Treated w/ ave pressure of 2243 psi @ ave rate of 28 BPM. Pumped 504 gals of 15% HCL in flush for Stage #4. ISDP 1322 psi. FG=.68, 5 min SIP 1202 psi, 10 min SIP 1152 psi, 15 min SIP 1122 psi. Leave pressure on well. RU Perforators WLT, crane & lubricator. Pressure test lubricator to 4000 psi w/BakerHughes blender. RIH w/ Weatherford 5-1/2" 5K total composite flow through frac plug, perf guns. Set plug @ 4640'. Perforate GB6 & GB4 @ 4562-64?, 4554-56?, 4506-08?, 4498-99? w/ 3 1/8" slick guns (16g, 0.34 EH, 21.00 pen) w/ 3 spf for total of 21 shots. 502 total BWTR - PSI test frac iron to 5300#-good test. Test pump kick-outs-good - PSI test frac iron to 5300#-good test. Test pump kick-outs-good - Safety meeting - Safety meeting - MIRU Baker Hughes frac fleet. - MIRU Baker Hughes frac fleet. - RU Perforators wireline. RIH w/Weatherford 5-1/2" 5K total composite flow through frac plug, perf guns. Set plug @ 5400'. Perforate B1 @ 5324-27', 5307-09? w/ 3 1/8" slick guns (16g, 0.34 EH, 21.00 pen) w/ 3 spf for total of 215 shots. POOH w/wireline. - RU S&S testers. PSI test frac valve-good test - RU S&S testers. PSI test frac valve-good test - ND pipe rams/NU frac valve. - ND pipe rams/NU frac valve. - Crew travel - Crew travel - RD floor & tbg equip. SWIFN - RD floor & tbg equip. SWIFN - TOO H w/tbg, LD NC & PSN, remove unneeded equipment form location to make room for frac crew.

Daily Cost: \$0

Cumulative Cost: \$139,640

4/25/2013 Day: 6

Completion

WWS #3 on 4/25/2013 - Drill out plugs, C/O 460' of fill. Circ well clean, begin TOO H w/tbg - Tag plug @ 4640', RU Graco pwr swvl, drill out plug (18min). Cont. TIH w/tbg, tag fill @ 5218'. C/O 182' of fill to plug @ 5400'. Circ well celan, drill out plug (27min). Cont. PU & TIH, tag fill @ 5450'. C/O 190' of fill to plug @ 5640'. Circ well clean, drill out plug (29min). Cont PU & TIH, tag fill @ 6246', C/O 89' of fill to PB @ 6335'. - Crew travel - TOO H w/108 jts.

SWIFN - w/well dead, RD wireline (no KP set), ND manual frac valve, NU BOPs. RU pressure tester & test BOP connection-good test - PU & TIH w/used 4 3/4" chomp bit & tbg - Circ well clean, Rack out drill equip. LD extra tbg. - Crw travel & safety mtg

Daily Cost: \$0

Cumulative Cost: \$150,114

4/26/2013 Day: 7

Completion

WWS #3 on 4/26/2013 - RT tbg, RIH w/production string, hang horse head, ready to PWOP when surface equipment is ready. - Crew travel & safety mtg - Crew travel ** FINAL REPORT - PU & TIH w/rods as follows: 30-7/8" 8per rods, 137-3/4" 4per, 73-7/8" 4per, 1-8', 1-5', 1-2'x7/8" pony rods, 1-1 1/2"x30' polish rod. Seat pump, RU pumping unit. Fill tbg w/2bbbs. Stroke pump w/unit to 800psi-good pump action. RDMO. Unable to PWOP, waiting on surface equip. - prep rods, PU & prime John Crane 2 1/2"x1 3/4" RHACx24' pump - W/well dead, cont. POOH w/tbg. LD chomp bit, PU & TIH w/BHA & tbg as follows: NC, 2 jts, PSN, 1 jt, TAC, 192 jts. ND BOPs, set TAC w/18000# tension. Land tbg w/tbg hanger. NU B1 adapter flange w/TAC @ 6025.44, PSN @ 6059.65, EOT @ 6123.52, x-over to rod equip. **Finalized**

Daily Cost: \$0

Cumulative Cost: \$232,739

Pertinent Files: Go to File List
