



May 31, 2006


State of Utah  
Division of Oil, Gas & Mining  
Attn: Diana Whitney  
1594 West North Temple - Suite 1210  
P.O. Box 145801  
Salt Lake City, Utah 84114-5801

RE: Applications for Permit to Drill: Federal 1-19-9-17, 2-19-9-17, 3-19-9-17, 5-19-9-17, 6-19-9-17, 7-19-9-17, 8-19-9-17, 10-19-9-17, 11-19-9-17, 12-19-9-17, 13-19-9-17, 14-19-9-17, 15-19-9-17, and 16-19-9-17.

Dear Diana:

Enclosed find APD's on the above referenced wells. The proposed 3-19-9-17 and 7-19-9-17 locations are Exception Locations. Our Land Department will send you the required Exception Location Letters. If you have any questions, feel free to give either Shon Mckinnon or myself a call.

Sincerely,

  
Mandie Crozier  
Regulatory Specialist

mc  
enclosures

RECEIVED  
MAY 31 2006  
DIV. OF OIL, GAS & MINING

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**APPLICATION FOR PERMIT TO DRILL OR REENTER**


5. Lease Serial No. <b>UTU-77369</b>
6. If Indian, Allottee or Tribe Name <b>N/A</b>
7. If Unit or CA Agreement, Name and No. <b>N/A</b>
8. Lease Name and Well No. <b>Federal 3-19-9-17</b>
9. API Well No. <b>43-013-33190</b>

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER	
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone	
2. Name of Operator <b>Newfield Production Company</b>	
3a. Address <b>Route #3 Box 3630, Myton UT 84052</b>	3b. Phone No. (include area code) <b>(435) 646-3721</b>
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface <b>NE/NW 454' FNL 1851' FWL 580982 X 40.022392</b> At proposed prod. zone <b>443046-14 -110.051004</b>	
10. Field and Pool, or Exploratory <b>Monument Butte</b>	
11. Sec., T., R., M., or Blk. and Survey or Area <b>NE/NW Sec. 19, T9S R17E</b>	
14. Distance in miles and direction from nearest town or post office* <b>Approximatley 16.9 miles south of Myton, Utah</b>	12. County or Parish <b>Duchesne</b>
	13. State <b>UT</b>
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) <b>Approx. 454' f/lse, NA' f/unit</b>	16. No. of Acres in lease <b>1189.60</b>
	17. Spacing Unit dedicated to this well <b>40 Acres</b>
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. <b>Approx. 1372'</b>	19. Proposed Depth <b>5864'</b>
	20. BLM/BIA Bond No. on file <b>UTB000192</b>
21. Elevations (Show whether DF, KDB, RT, GL, etc.) <b>5527' GL</b>	22. Approximate date work will start* <b>4th Quarter 2006</b>
	23. Estimated duration <b>Approximately seven (7) days from spud to rig release.</b>

**24. Attachments**

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- |   |  |
|---|--|
| 1. Well plat certified by a registered surveyor.  | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).    |
| 2. A Drilling Plan.   | 5. Operator certification.   |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature 	Name (Printed/Typed) <b>Mandie Crozier</b>	Date <b>5/31/06</b>
Title <b>Regulatory Specialist</b>		
Approved by (Signature) 	Name (Printed/Typed) <b>BRADLEY G. HILL</b>	Date <b>06-29-06</b>
Title <b>ENVIRONMENTAL MANAGER</b>	Off.	

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

\*(Instructions on reverse)

RECEIVED

MAY 31 2006

Federal Approval of Oil  
Activities Mandatory



DIV. OF OIL, GAS & MINING

# T9S, R17E, S.L.B.&M.

N89°51'E - 78.66 (G.L.O.)

## NEWFIELD PRODUCTION COMPANY

WELL LOCATION, S. PLEASANT VALLEY  
3-19-9-17, LOCATED AS SHOWN IN THE  
NE 1/4 NW 1/4 OF SECTION 19,  
T9S, R17E, S.L.B.&M. DUCHESNE COUNTY, UTAH.

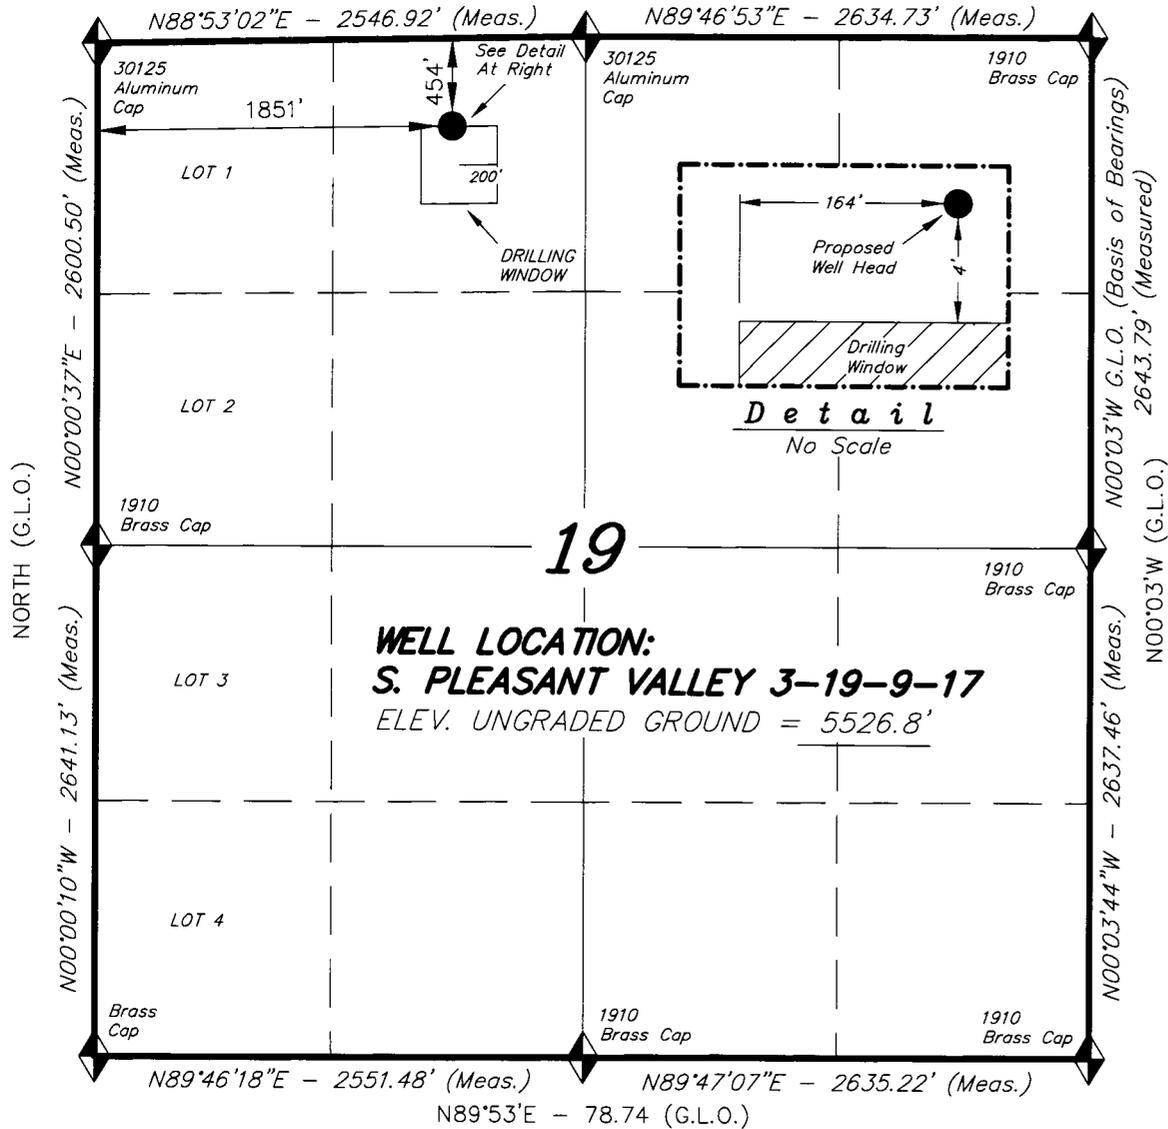

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS  
PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS  
MADE BY ME OR UNDER MY SUPERVISION AND THAT  
THE SAME ARE TRUE AND CORRECT TO THE BEST OF  
MY KNOWLEDGE AND BELIEF. No. 189377

**REGISTERED LAND SURVEYOR**  
STACY W. STEWART  
REGISTERED LAND SURVEYOR  
REGISTRATION No. 189377  
STATE OF UTAH

◆ = SECTION CORNERS LOCATED

BASIS OF ELEV;  
U.S.G.S. 7-1/2 min QUAD (MYTON SE)

**S. PLEASANT VALLEY 3-19-9-17**  
**(Surface Location) NAD 83**  
LATITUDE = 40° 01' 20.47"  
LONGITUDE = 110° 03' 06.25"


### TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078  
(435) 781-2501

DATE SURVEYED: 04-21-06	SURVEYED BY: D.P.
DATE DRAWN: 04-25-06	DRAWN BY: F.T.M.
REVISED:	SCALE: 1" = 1000'

# T9S, R17E, S.L.B.&M.



N89°51'E - 78.66 (G.L.O.)

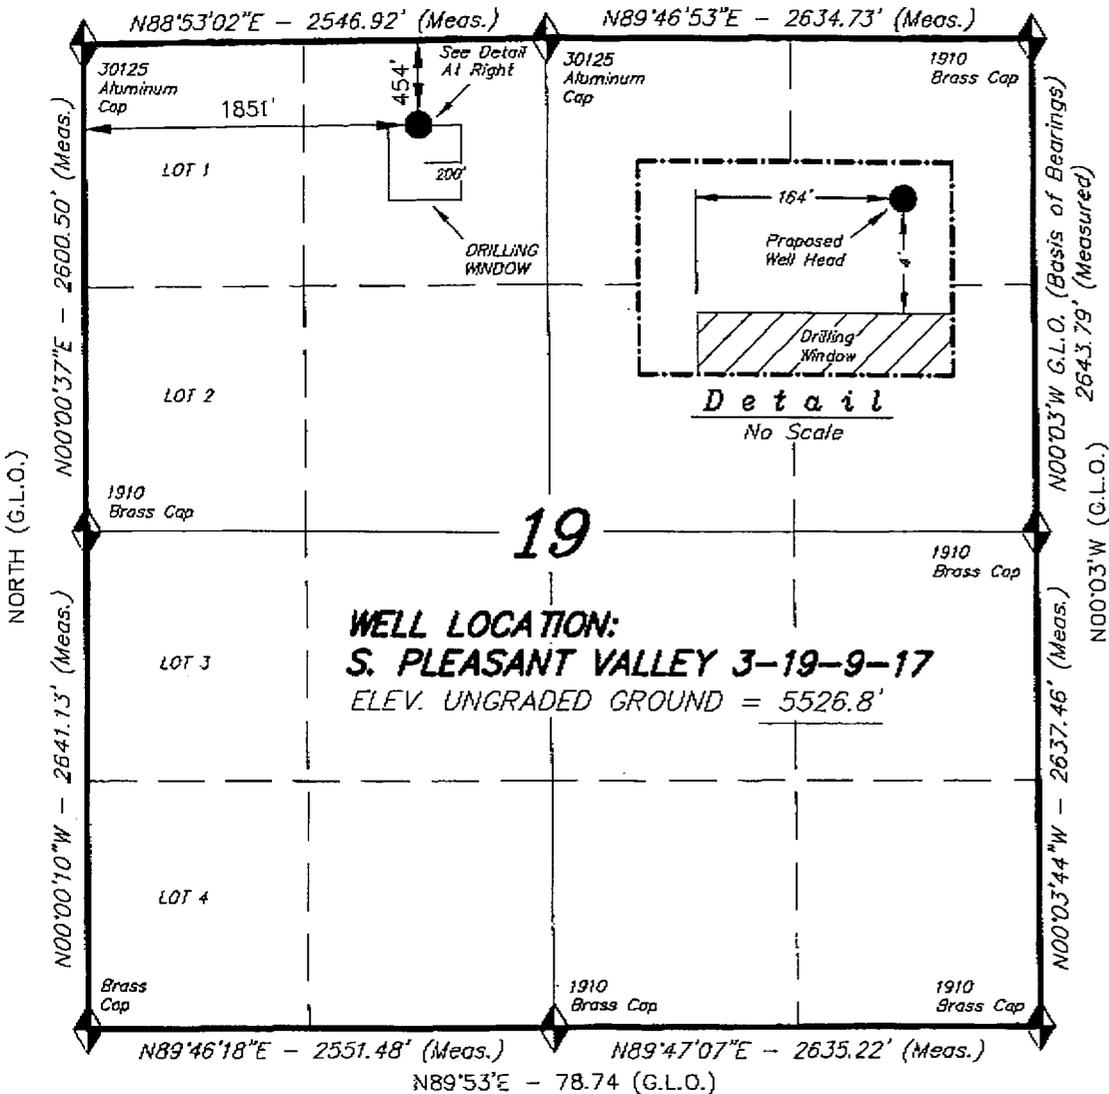


**WELL LOCATION:**  
**S. PLEASANT VALLEY 3-19-9-17**  
 ELEV. UNGRADED GROUND = 5526.8'

## NEWFIELD PRODUCTION COMPANY

WELL LOCATION, S. PLEASANT VALLEY  
 3-19-9-17, LOCATED AS SHOWN IN THE  
 NE 1/4 NW 1/4 OF SECTION 19, T9S,  
 R17E, S.L.B.&M. DUCHESNE COUNTY, UTAH.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS  
 PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS  
 MADE BY ME OR UNDER MY SUPERVISION AND THAT  
 THE SAME ARE TRUE AND CORRECT TO THE BEST OF  
 MY KNOWLEDGE AND BELIEF. No.189377



### TRI STATE LAND SURVEYING & CONSULTING


180 NORTH VERNAL AVE. - VERNAL, UTAH 84078  
 (435) 781-2501

DATE SURVEYED: 04-21-06	SURVEYED BY: D.P.
DATE DRAWN: 04-25-06	DRAWN BY: F.T.M.
REVISED:	SCALE: 1" = 1000'

◆ = SECTION CORNERS LOCATED

BASIS OF ELEV;  
 U.S.G.S. 7-1/2 min QUAD (MYTON SE)

S. PLEASANT VALLEY 3-19-9-17  
 (Surface Location) NAD 83  
 LATITUDE = 40° 01' 20.47"  
 LONGITUDE = 110° 03' 06.25"

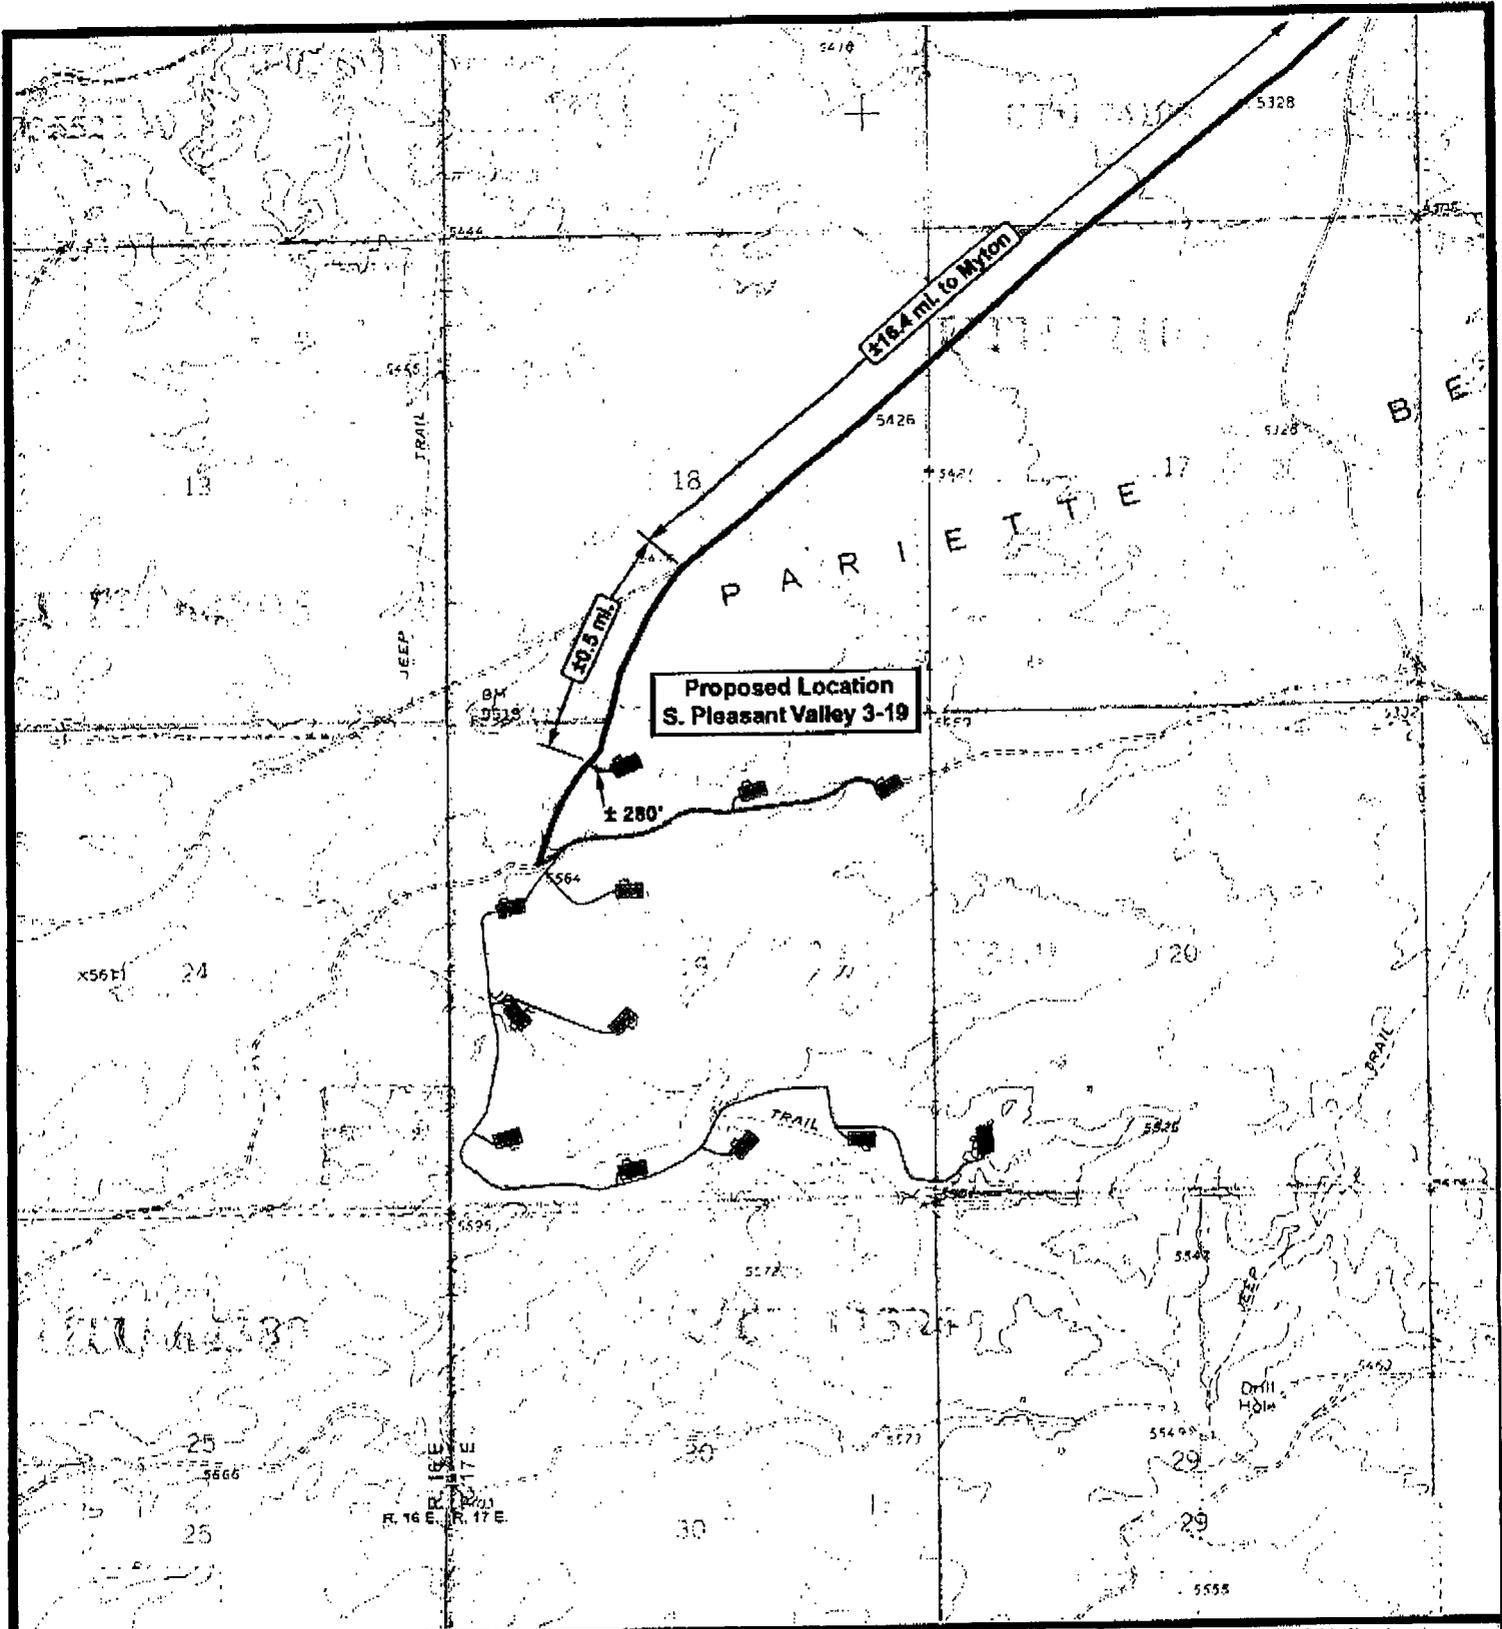

Fawcett  
Exploration Company

**S. Pleasant Valley 3-19-9-17  
SEC. 19, T9S, R17E, S.L.B.&M.**



*Tri-State*  
*Land Surveying Inc.*  
(435) 781-2501  
180 North Vernal Ave., Vernal, Utah 84078

SCALE: 1" = 2,000'

DRAWN BY: mw

DATE: 05-08-2006

**Legend**

-  Existing Road
-  Proposed Access
-  Existing Two-Track

TOPOGRAPHIC MAP

**"B"**

**NEWFIELD PRODUCTION COMPANY  
FEDERAL #3-19-9-17  
NE/NW SECTION 19, T9S, R17E  
DUCHESNE COUNTY, UTAH**

**ONSHORE ORDER NO. 1**

**DRILLING PROGRAM**

**1. GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

**2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0' – 2564'
Green River	2564'
Wasatch	5864'

**3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation 2564' -- 5864' - Oil

**4. PROPOSED CASING PROGRAM**

Please refer to the Monument Butte Field Standard Operation Procedure (SOP).

**5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

Please refer to the Monument Butte Field SOP. See Exhibit "C".

**6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

Please refer to the Monument Butte Field SOP.

**7. AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Please refer to the Monument Butte Field SOP.

**8. TESTING, LOGGING AND CORING PROGRAMS:**

Please refer to the Monument Butte Field SOP.

**9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered.

**10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

Please refer to the Monument Butte Field SOP.

**NEWFIELD PRODUCTION COMPANY  
FEDERAL #3-19-9-17  
NE/NW SECTION 19, T9S, R17E  
DUCHESNE COUNTY, UTAH**

**ONSHORE ORDER NO. 1**

**MULTI-POINT SURFACE USE & OPERATIONS PLAN**

**1. EXISTING ROADS**

See attached Topographic Map "A"

To reach Newfield Production Company well location site Federal #3-19-9-17 located in the NE 1/4 NW 1/4 Section 19, T9S, R17E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.6 miles ± to the junction of this highway and UT State Hwy 53; proceed southeasterly along Hwy 53 – 11.7 miles ± to it's junction with an existing dirt road to the southwest; proceed southwesterly – 3.6 miles ± to it's junction with the beginning of the proposed access road; proceed southeasterly along the proposed access road – 280' ± to the proposed well location.

**2. PLANNED ACCESS ROAD**

See Topographic Map "B" for the location of the proposed access road.

**3. LOCATION OF EXISTING WELLS**

Refer to Exhibit "B".

**4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES**

All permanent surface equipment will be painted Carlsbad Canyon.  
Please refer to the Monument Butte Field Standard Operating Procedure (SOP).

**5. LOCATION AND TYPE OF WATER SUPPLY**

Please refer to the Monument Butte Field SOP. See Exhibit "A".

**6. SOURCE OF CONSTRUCTION MATERIALS**

Please refer to the Monument Butte Field SOP.

**7. METHODS FOR HANDLING WASTE DISPOSAL**

Please refer to the Monument Butte Field SOP.

**8. ANCILLARY FACILITIES**

Please refer to the Monument Butte Field SOP.

9. **WELL SITE LAYOUT**

See attached Location Layout Diagram.

10. **PLANS FOR RESTORATION OF SURFACE**

Please refer to the Monument Butte Field SOP.

11. **SURFACE OWNERSHIP** - Bureau Of Land Management (Proposed location and access roads leading to).

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. MOAC Report #04-206, 6/15/05. Paleontological Resource Survey prepared by. Wade E. Miller, 4/26/06. See attached report cover pages, Exhibit "D".

For the Federal #3-19-9-17 Newfield Production Company requests 280' of disturbed area be granted in Lease UTU-77369 to allow for construction of the proposed access road. **Refer to Topographic Map "B"**. The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests 6470' of disturbed area be granted in Lease UTU-77369 to allow for construction of the proposed gas lines. It is proposed that the disturbed area will be 50' wide to allow for construction of a 6" gas gathering line, and a 3" poly fuel gas line. Both lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Newfield Production Company requests 7290' of disturbed area be granted in Lease UTU-77369 to allow for construction of the proposed water lines. It is proposed that the disturbed area will be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

**Exceptional Spacing**

According to Rule R649-3-2, which governs the location of wells in the State of Utah, Newfield Production is required to request administrative approval for a location exception from all non-unitized lease interest owners within a 460-foot radius of the new proposed location. Our Land Department in Denver has been notified of this exception location and will submit the required Exception Location Letter to all affected lease interest owners.

**Water Disposal**

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

**Threatened, Endangered, And Other Sensitive Species**

**Mountain Plover:** If new construction or surface disturbing activities are scheduled to occur between May 1 and June 15, detailed surveys of the area within 0.5 mile of the proposed location and within 300 feet of proposed access routes must be conducted to detect the presence of mountain plovers. All surveys must be conducted in accordance with the survey protocols outlined in the most recent USFWS Survey Protocol. Surveys must be completed prior to initiating new construction or surface disturbing activities. No new construction or surface disturbing activities will be allowed between March 15 and August 15 within a 0.5 mile radius of any documented mountain plover nest site.

**Reserve Pit Liner**

A 12 mil liner with felt is required. Please refer to the Monument Butte Field SOP.

**Location and Reserve Pit Reclamation**

Please refer to the Monument Butte Field SOP.

The following seed mixture will be used on the topsoil stockpile, to the recontoured surface of the reserve pit, and for final reclamation: (All poundages are in pure live seed)

Western Wheatgrass	<i>Pascopyrum Smithii</i>	6 lbs/acre
Galletta Grass	<i>Hilaria Jamesii</i>	6 lbs/acre

**Details of the On-Site Inspection**

The proposed Federal #3-19-9-17 was on-sited on 4/27/06. The following were present; Shon Mckinnon (Newfeild Production), Chris Carusona (Bureau of Land Management), and Brandon McDonald (Bureau of Landmanagement). Weather conditions were clear and ground cover was 100% open.

**13. LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION**

Representative

Name: Shon Mckinnon  
Address: Route #3 Box 3630  
Myton, UT 84052  
Telephone: (435) 646-3721

Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #3-19-9-17 NE/NW Section 19, Township 9S, Range 17E; Lease UTU-77369 Duchesne County, Utah; and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by US Specialty Insurance #B001832.

I hereby certify that the proposed drillsite and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and

subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

5/31/06

Date





Mandie Crozier  
Regulatory Specialist  
Newfield Production Company

# NEWFIELD PRODUCTION COMPANY

S. PLEASANT VALLEY 3-19-9-17

Section 19, T9S, R17E, S.L.B.&M.

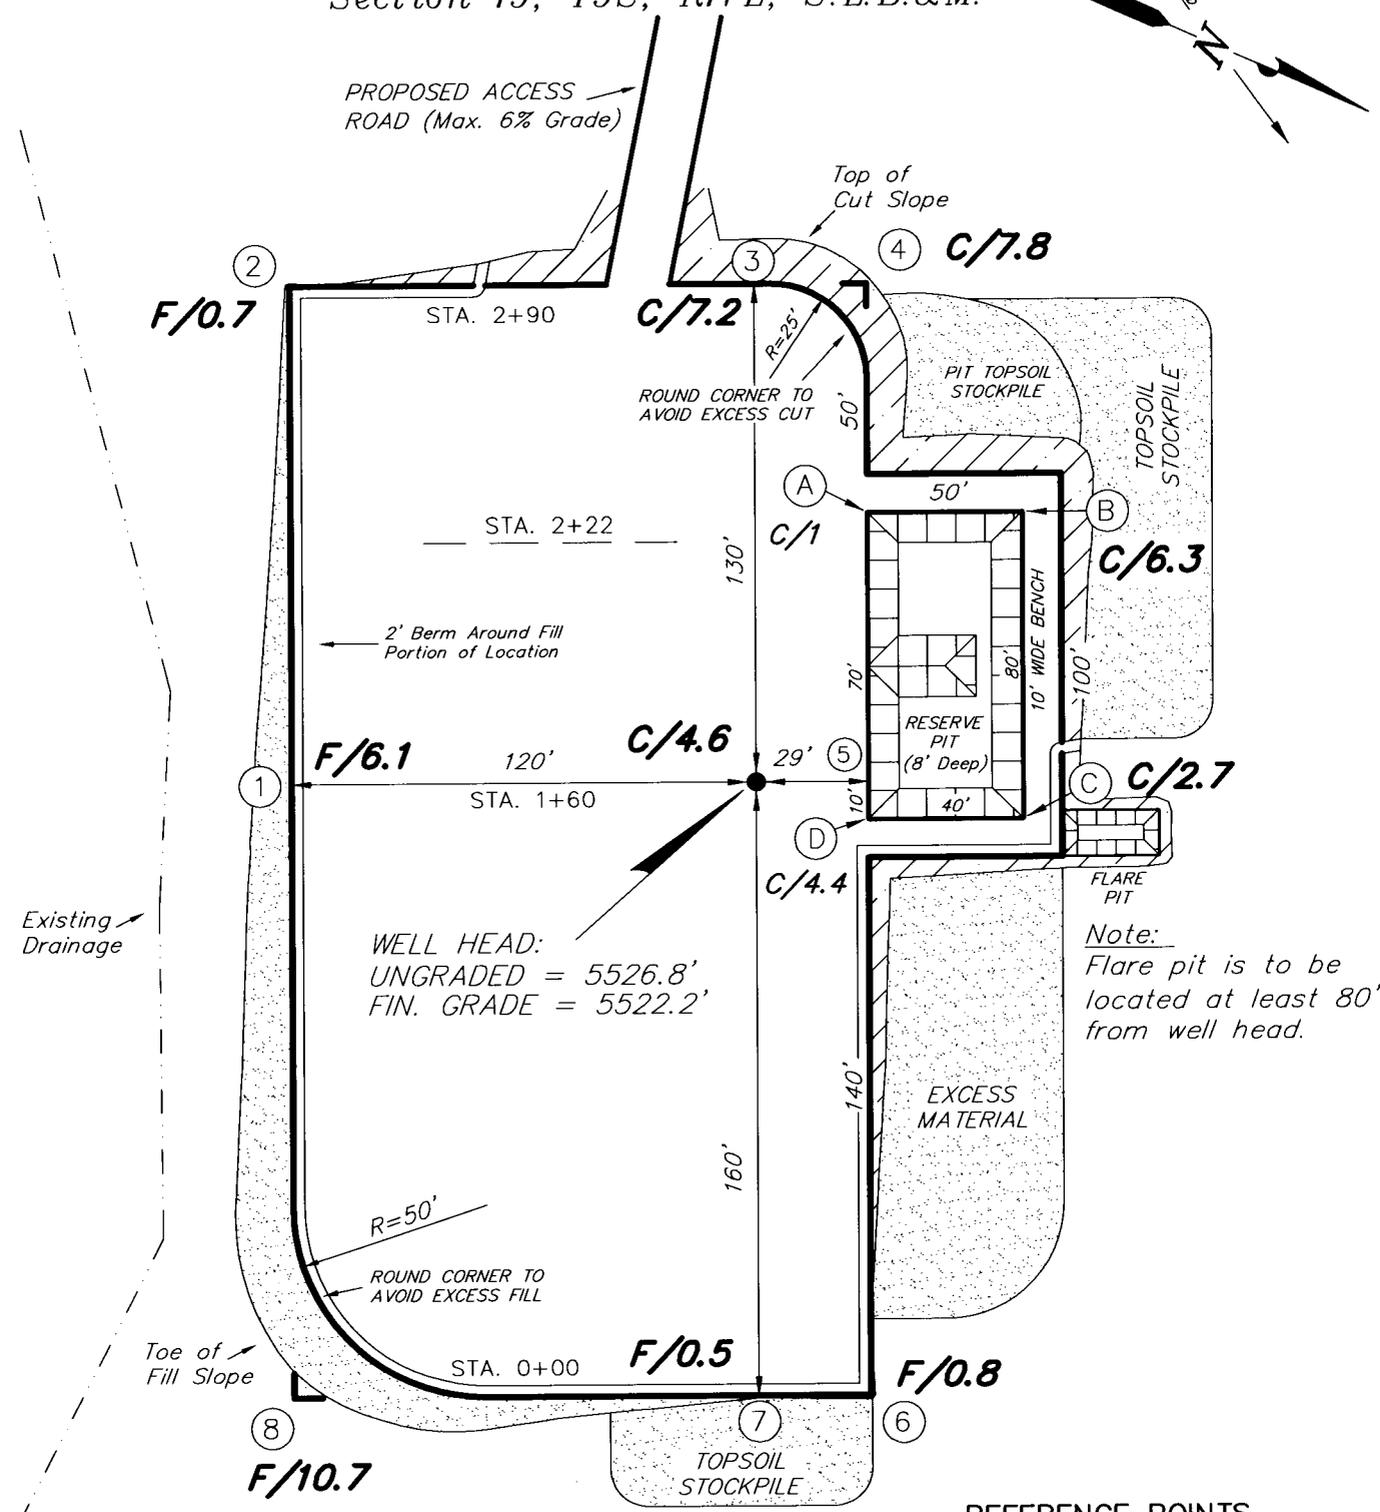

Note:  
Flare pit is to be located at least 80' from well head.

REFERENCE POINTS

210' NORTHEAST	= 5520.3'
260' NORTHEAST	= 5519.7'
170' SOUTHEAST	= 5516.3'
220' SOUTHEAST	= 5523.8'





SURVEYED BY: D.P.	SCALE: 1" = 50'
DRAWN BY: F.T.M.	DATE: 04-26-06

**Tri State** (435) 781-2501  
 Land Surveying, Inc.  
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

# NEW FIELD PRODUCTION COMPANY

## CROSS SECTIONS

### S. PLEASANT VALLEY 3-19-9-17

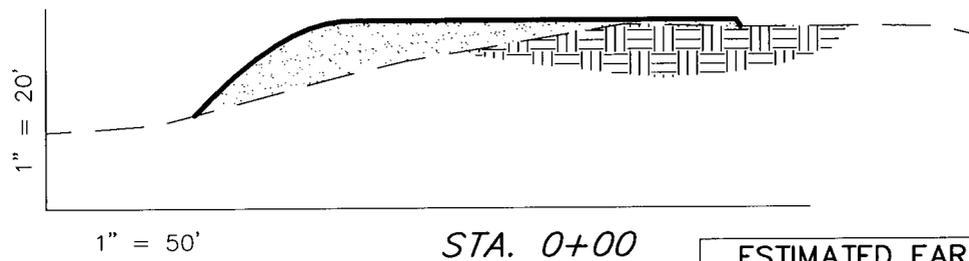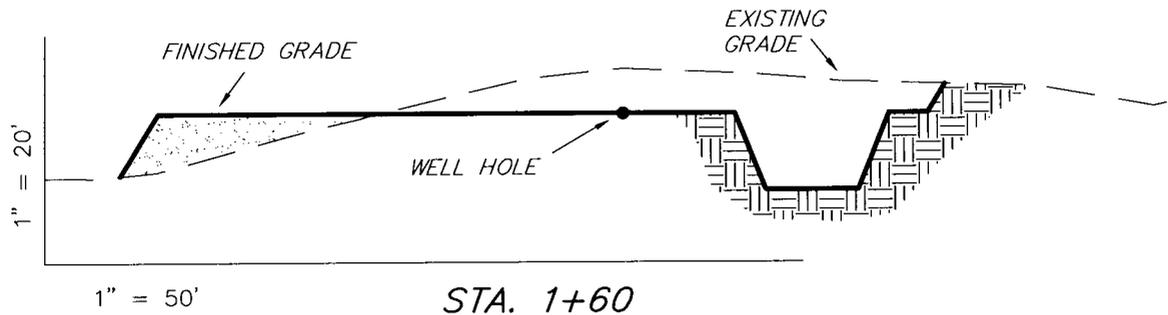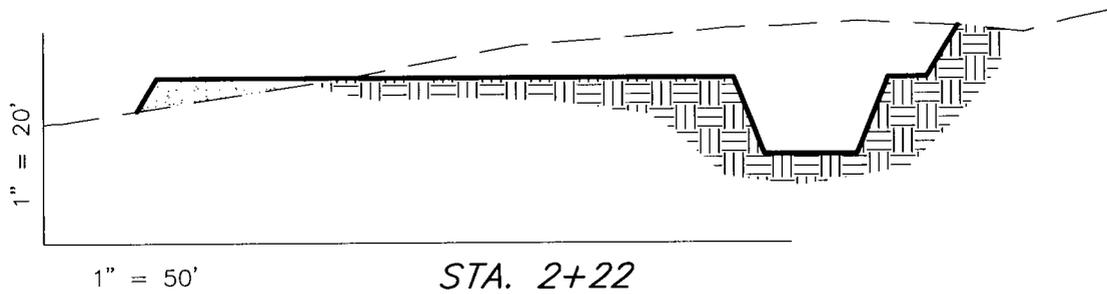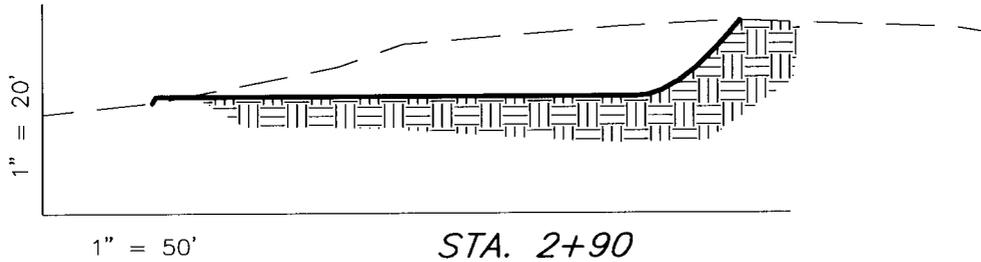

NOTE:  
UNLESS OTHERWISE NOTED  
ALL CUT/FILL SLOPES ARE  
AT 1.5:1

#### ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	3,220	3,220	Topsail is not included in Pad Cut	0
PIT	640	0		640
TOTALS	3,860	3,220	1,010	640

SURVEYED BY: D.P.


SCALE: 1" = 50'

DRAWN BY: F.T.M.


DATE: 04-26-06

**Tri State** (435) 781-2501  
Land Surveying, Inc.  
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

**NEWFIELD PRODUCTION COMPANY**  
**TYPICAL RIG LAYOUT**  
**S. PLEASANT VALLEY 3-19-9-17**

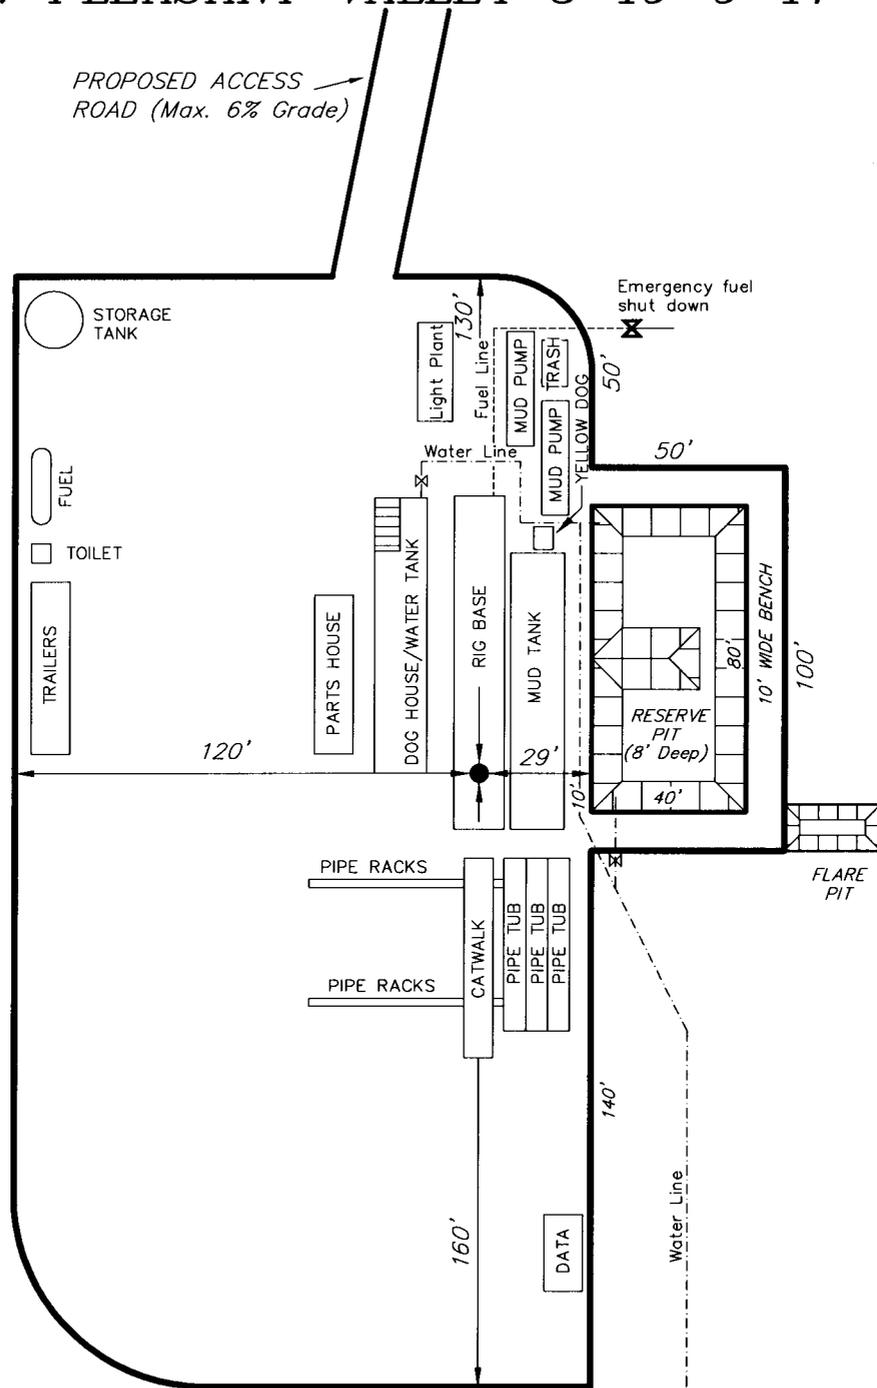

SURVEYED BY: D.P.	SCALE: 1" = 50'	 (435) 781-2501 180 NORTH VERNAL AVE. VERNAL, UTAH 84078
DRAWN BY: F.T.M.	DATE: 04-26-06	

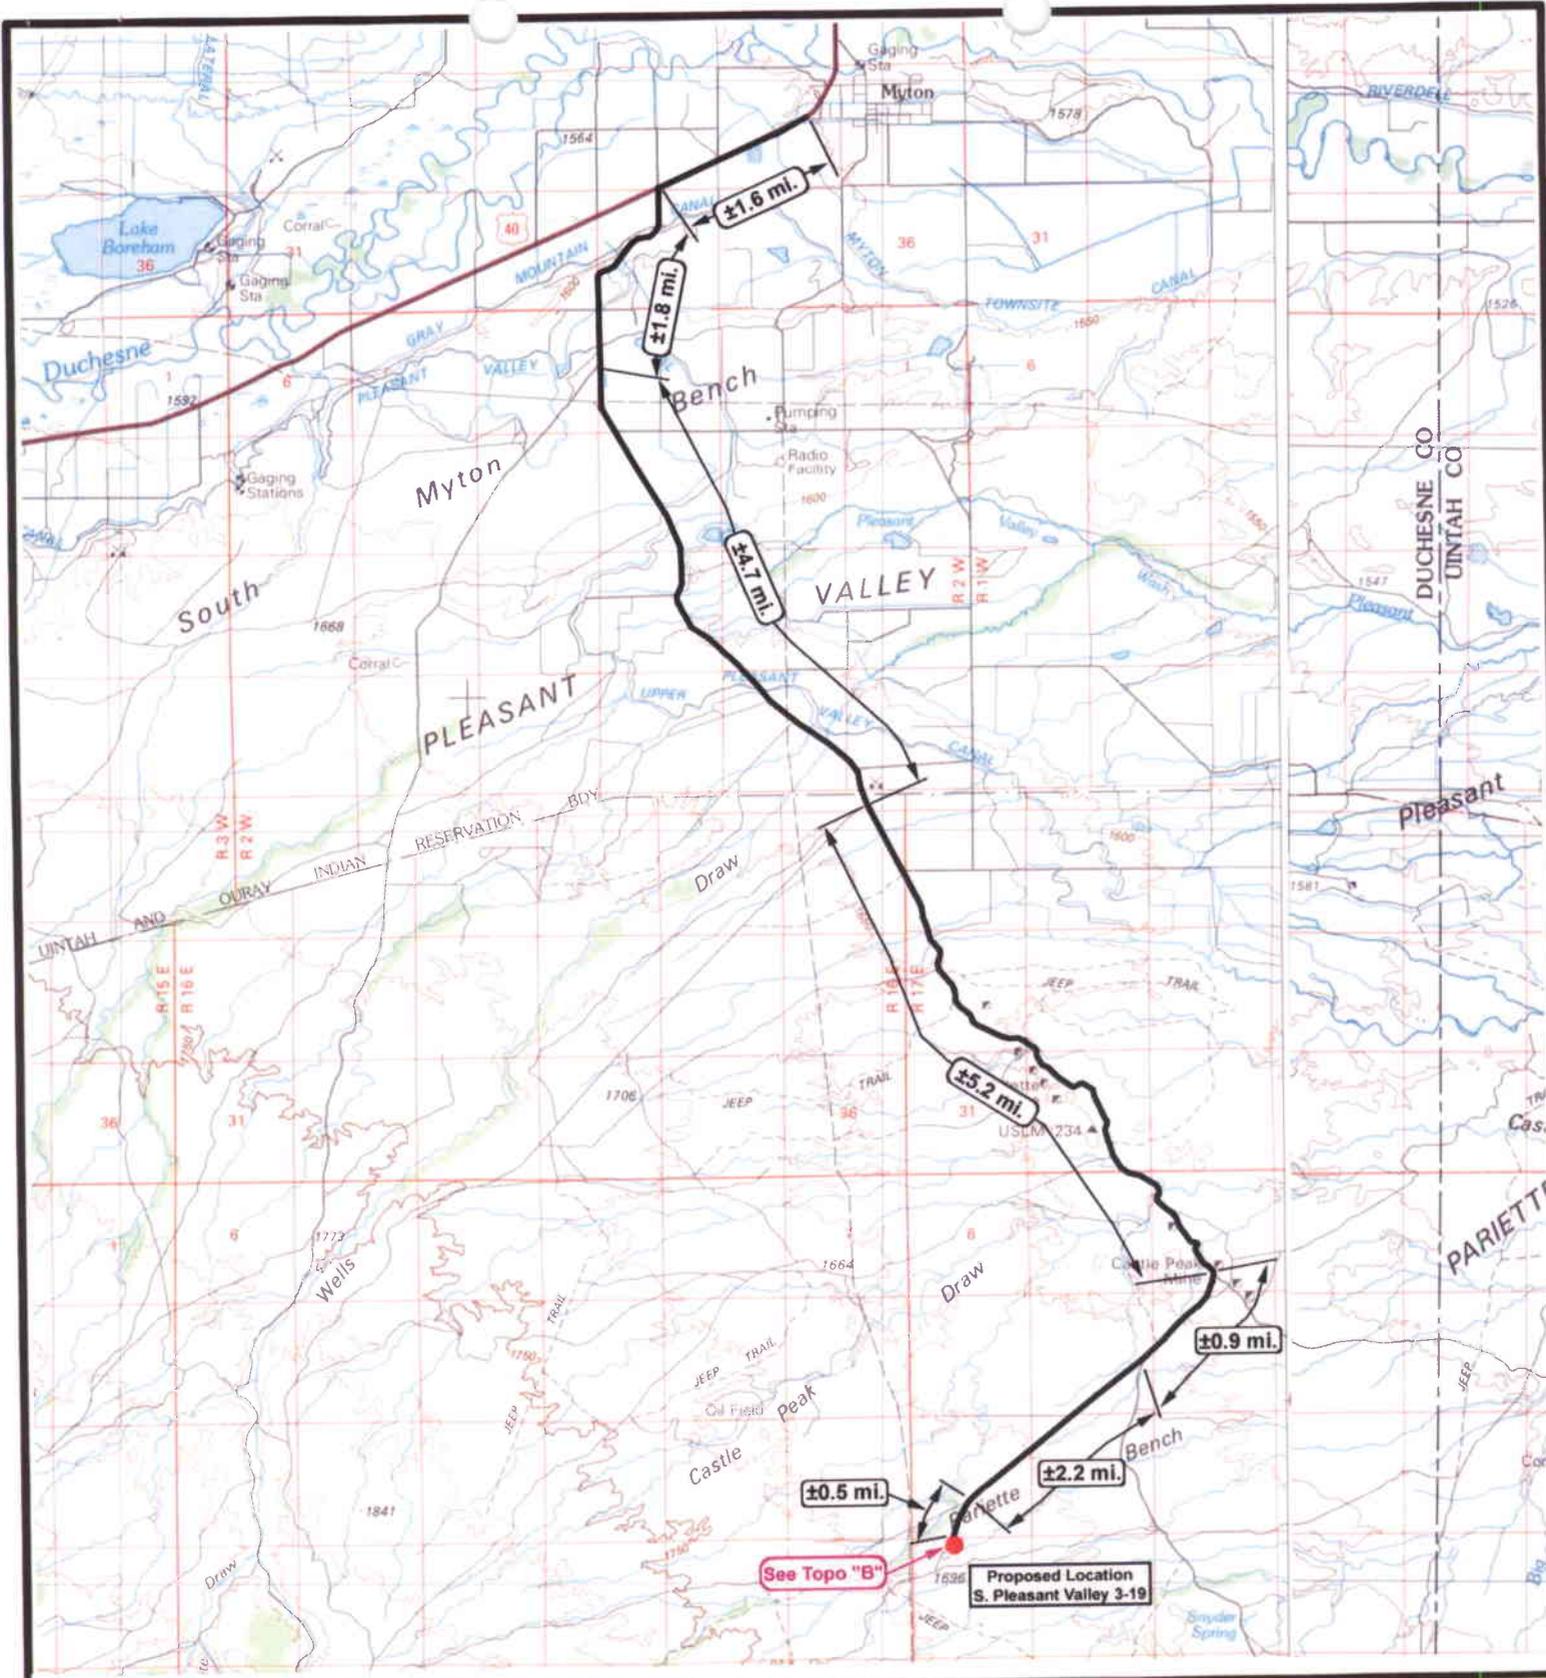

**NEWFIELD**  
Exploration Company

**S. Pleasant Valley 3-19-9-17**  
**SEC. 19, T9S, R17E, S.L.B.&M.**




*Tri-State*  
Land Surveying Inc.  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1 = 100,000  
DRAWN BY: mw  
DATE: 05-08-2006

**Legend**

- Existing Road
- Proposed Access

**TOPOGRAPHIC MAP**  
**"A"**

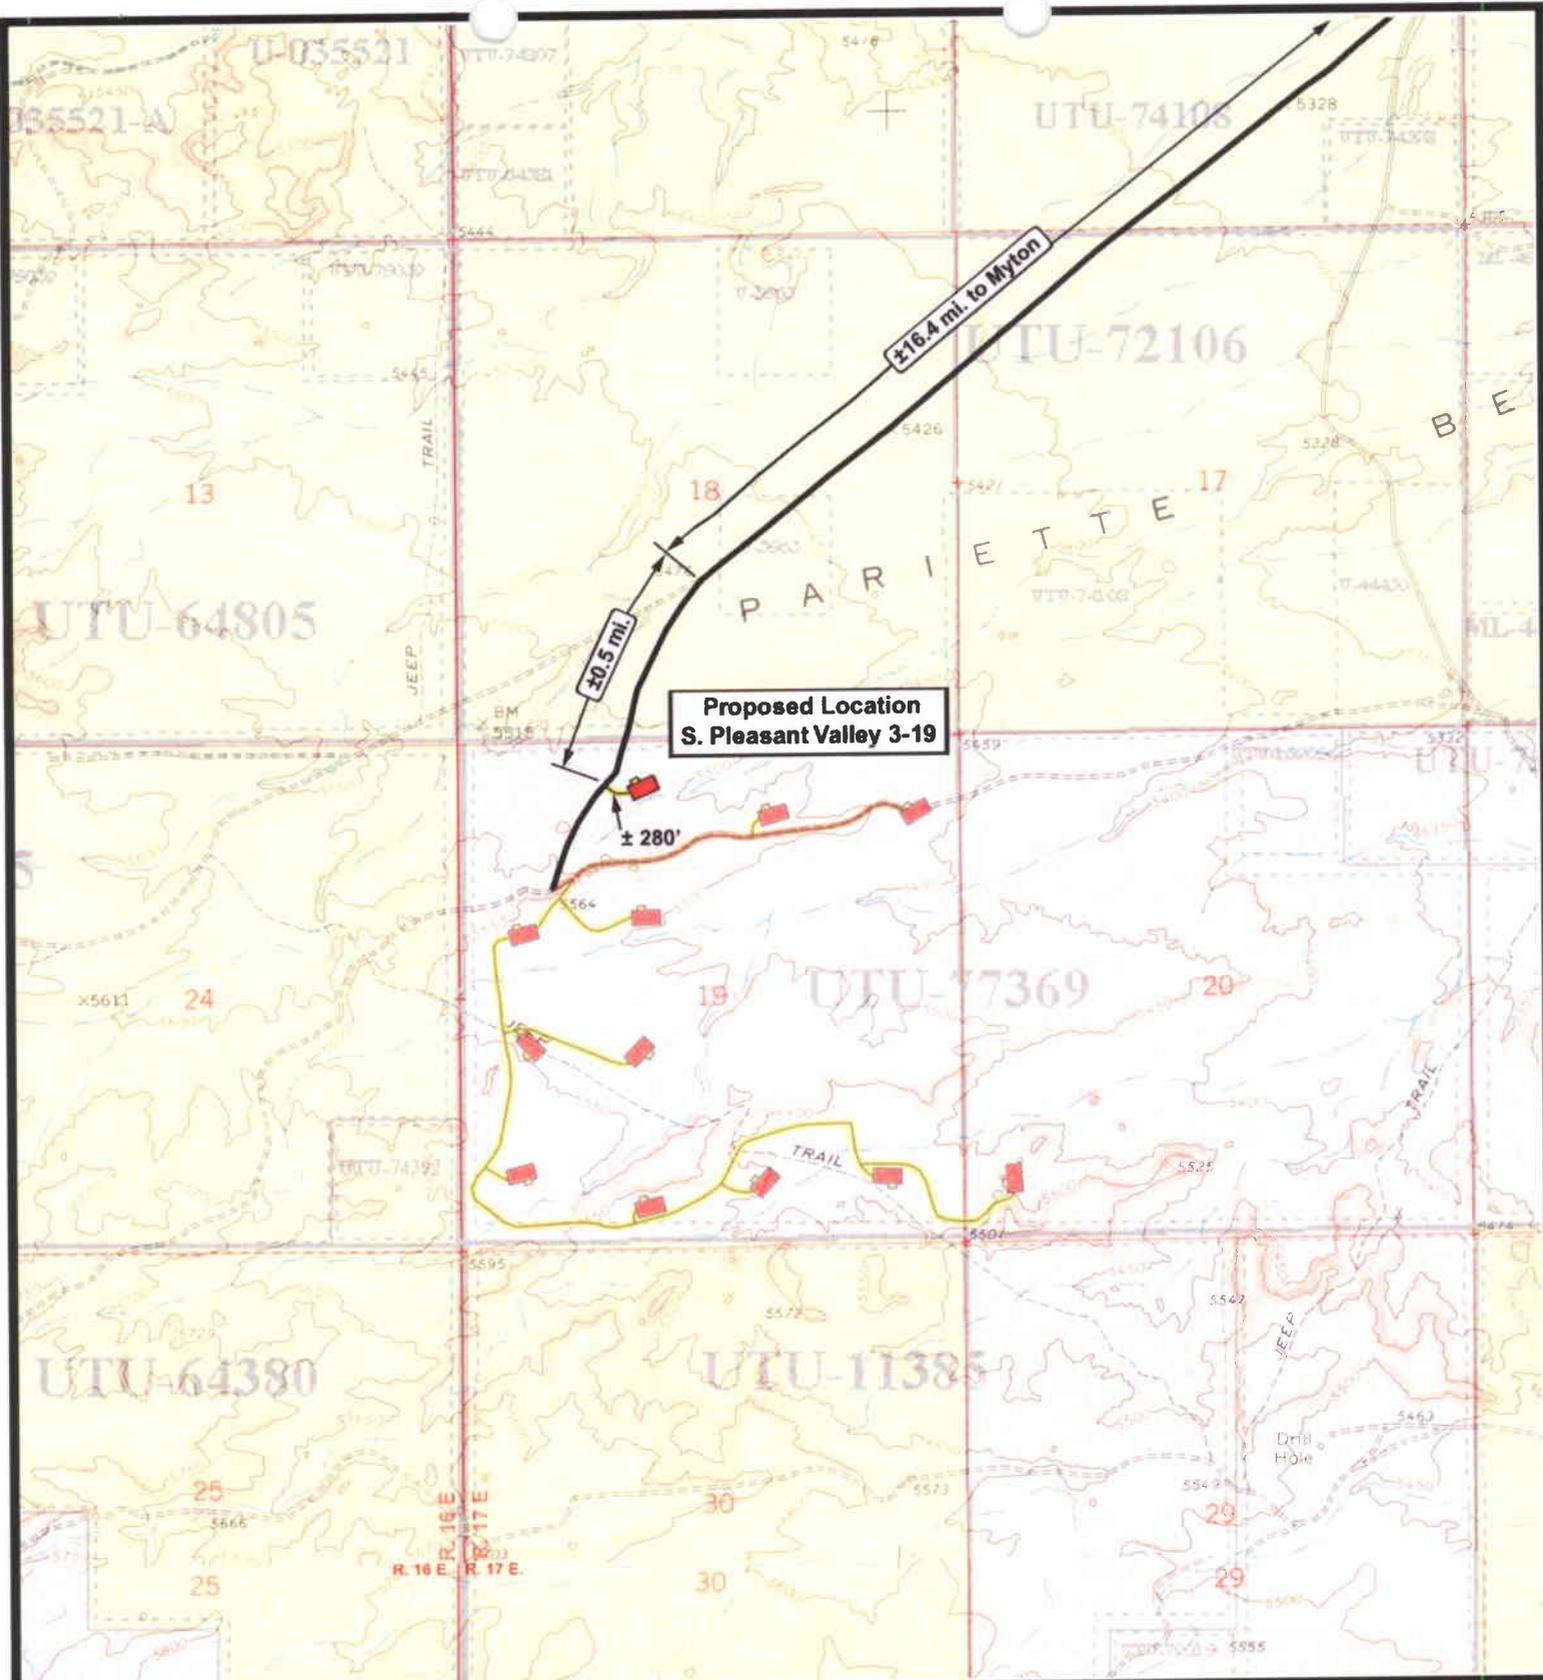

**Proposed Location  
S. Pleasant Valley 3-19**



**NEWFIELD**  
Exploration Company

**S. Pleasant Valley 3-19-9-17  
SEC. 19, T9S, R17E, S.L.B.&M.**





*Tri-State*  
Land Surveying Inc.  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'  
DRAWN BY: mw  
DATE: 05-08-2006

**Legend**

-  Existing Road
-  Proposed Access
-  Existing Two-Track

TOPOGRAPHIC MAP  
**"B"**

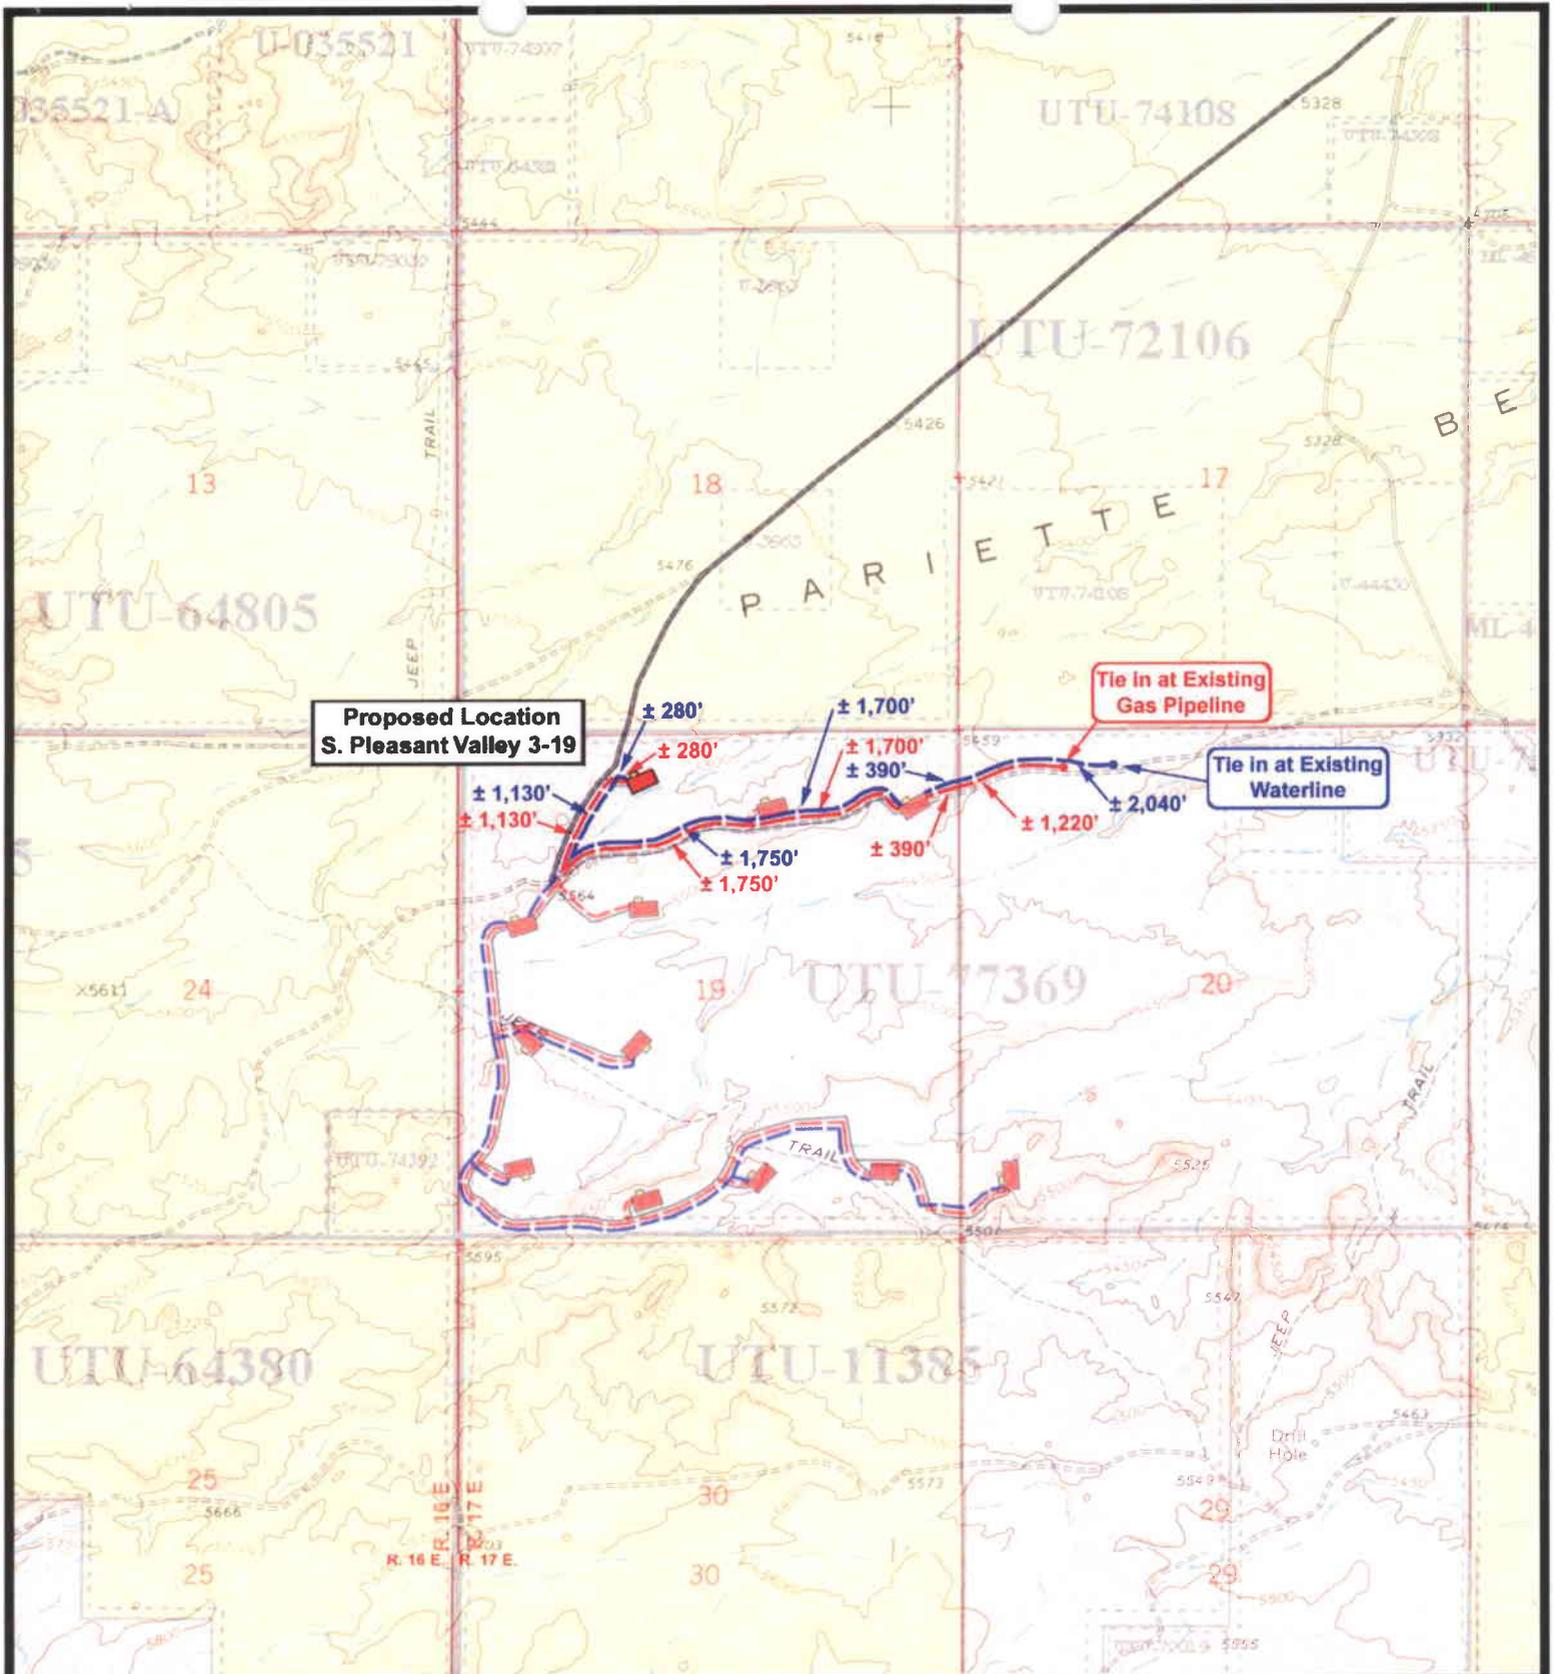

**Proposed Location  
S. Pleasant Valley 3-19**

**Tie in at Existing  
Gas Pipeline**

**Tie in at Existing  
Waterline**

**NEWFIELD**  
Exploration Company

**S. Pleasant Valley 3-19-9-17  
SEC. 19, T9S, R17E, S.L.B.&M.**




*Tri-State  
Land Surveying Inc.*  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2,000'  
DRAWN BY: mw  
DATE: 05-08-2006

**Legend**

- Roads
- Proposed Gas Line
- Proposed Water Line

TOPOGRAPHIC MAP  
**"C"**

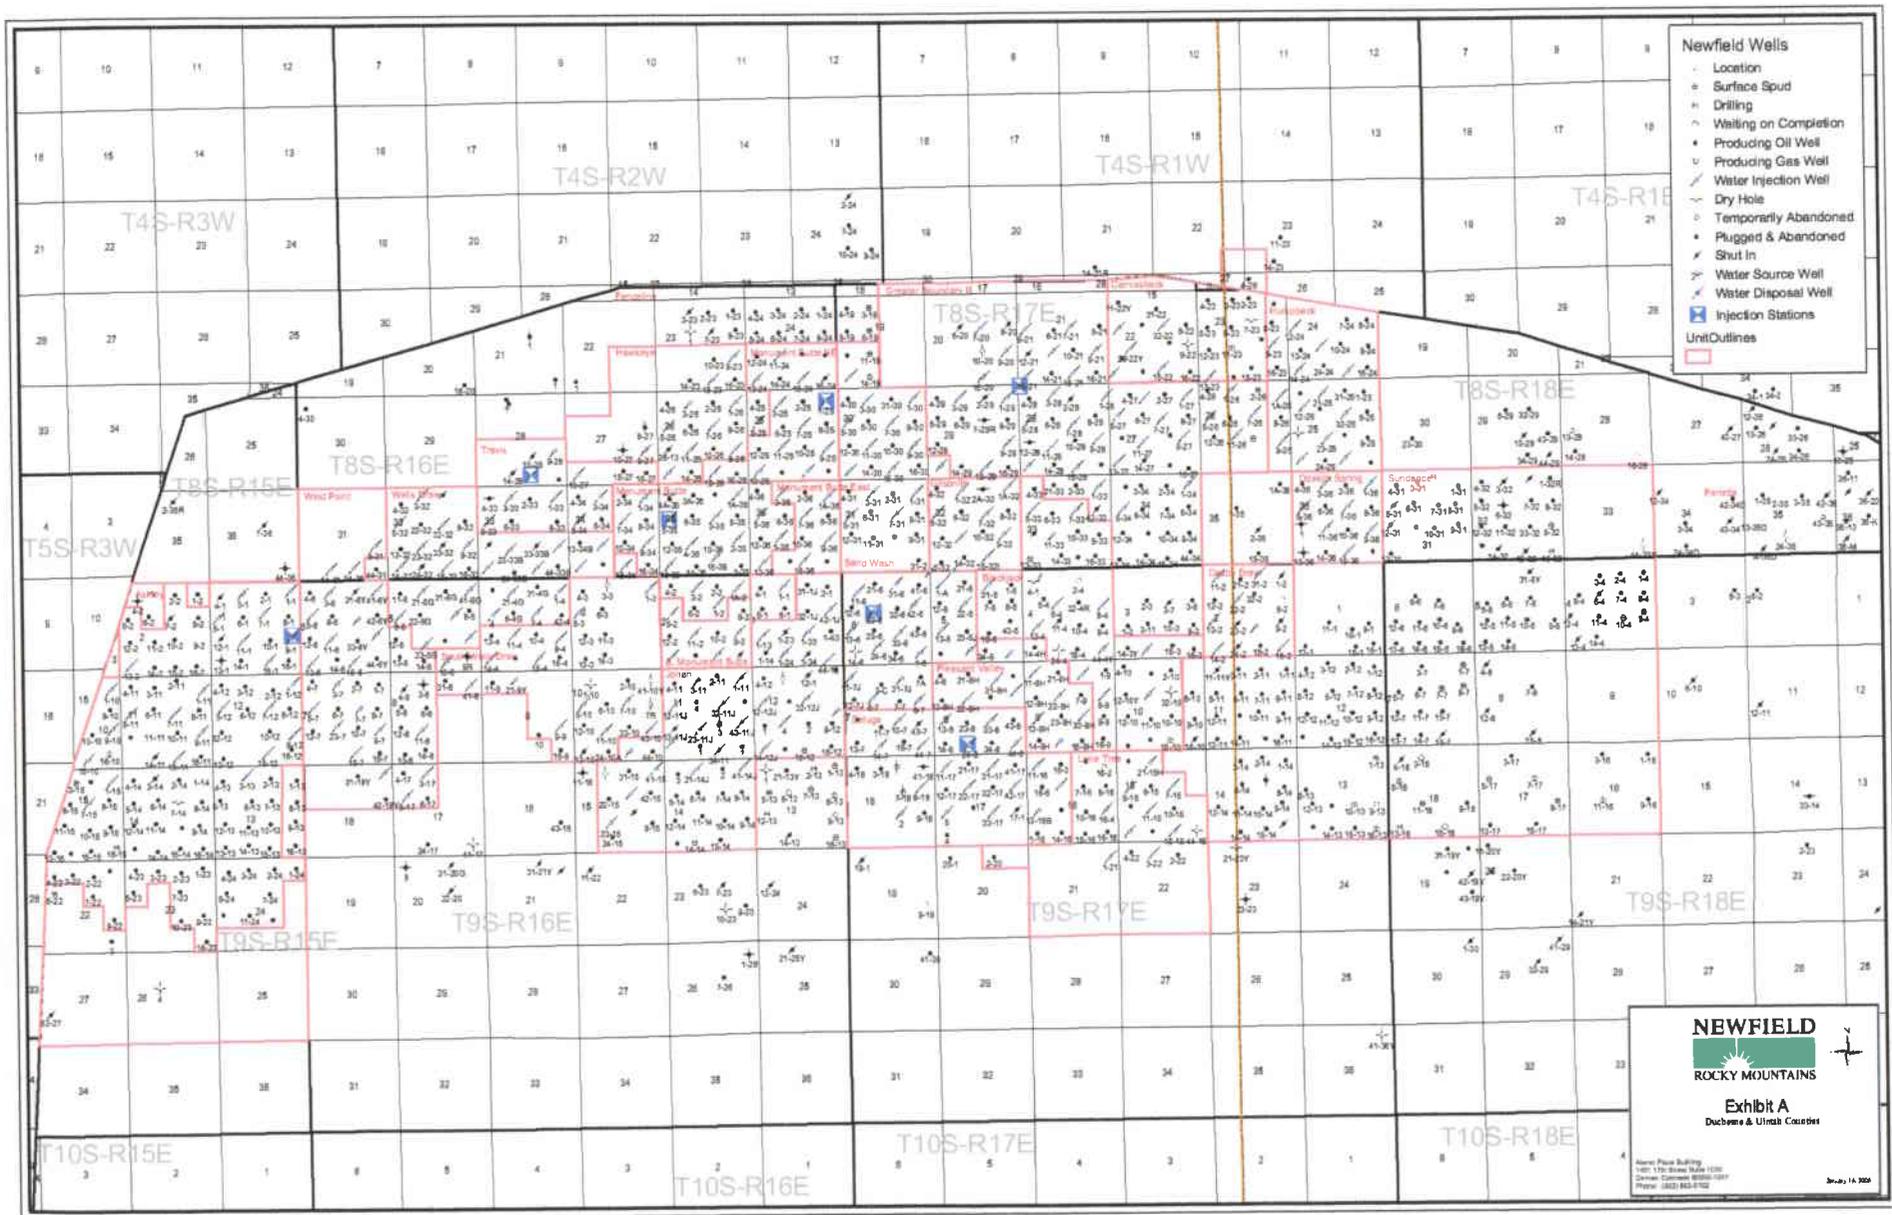

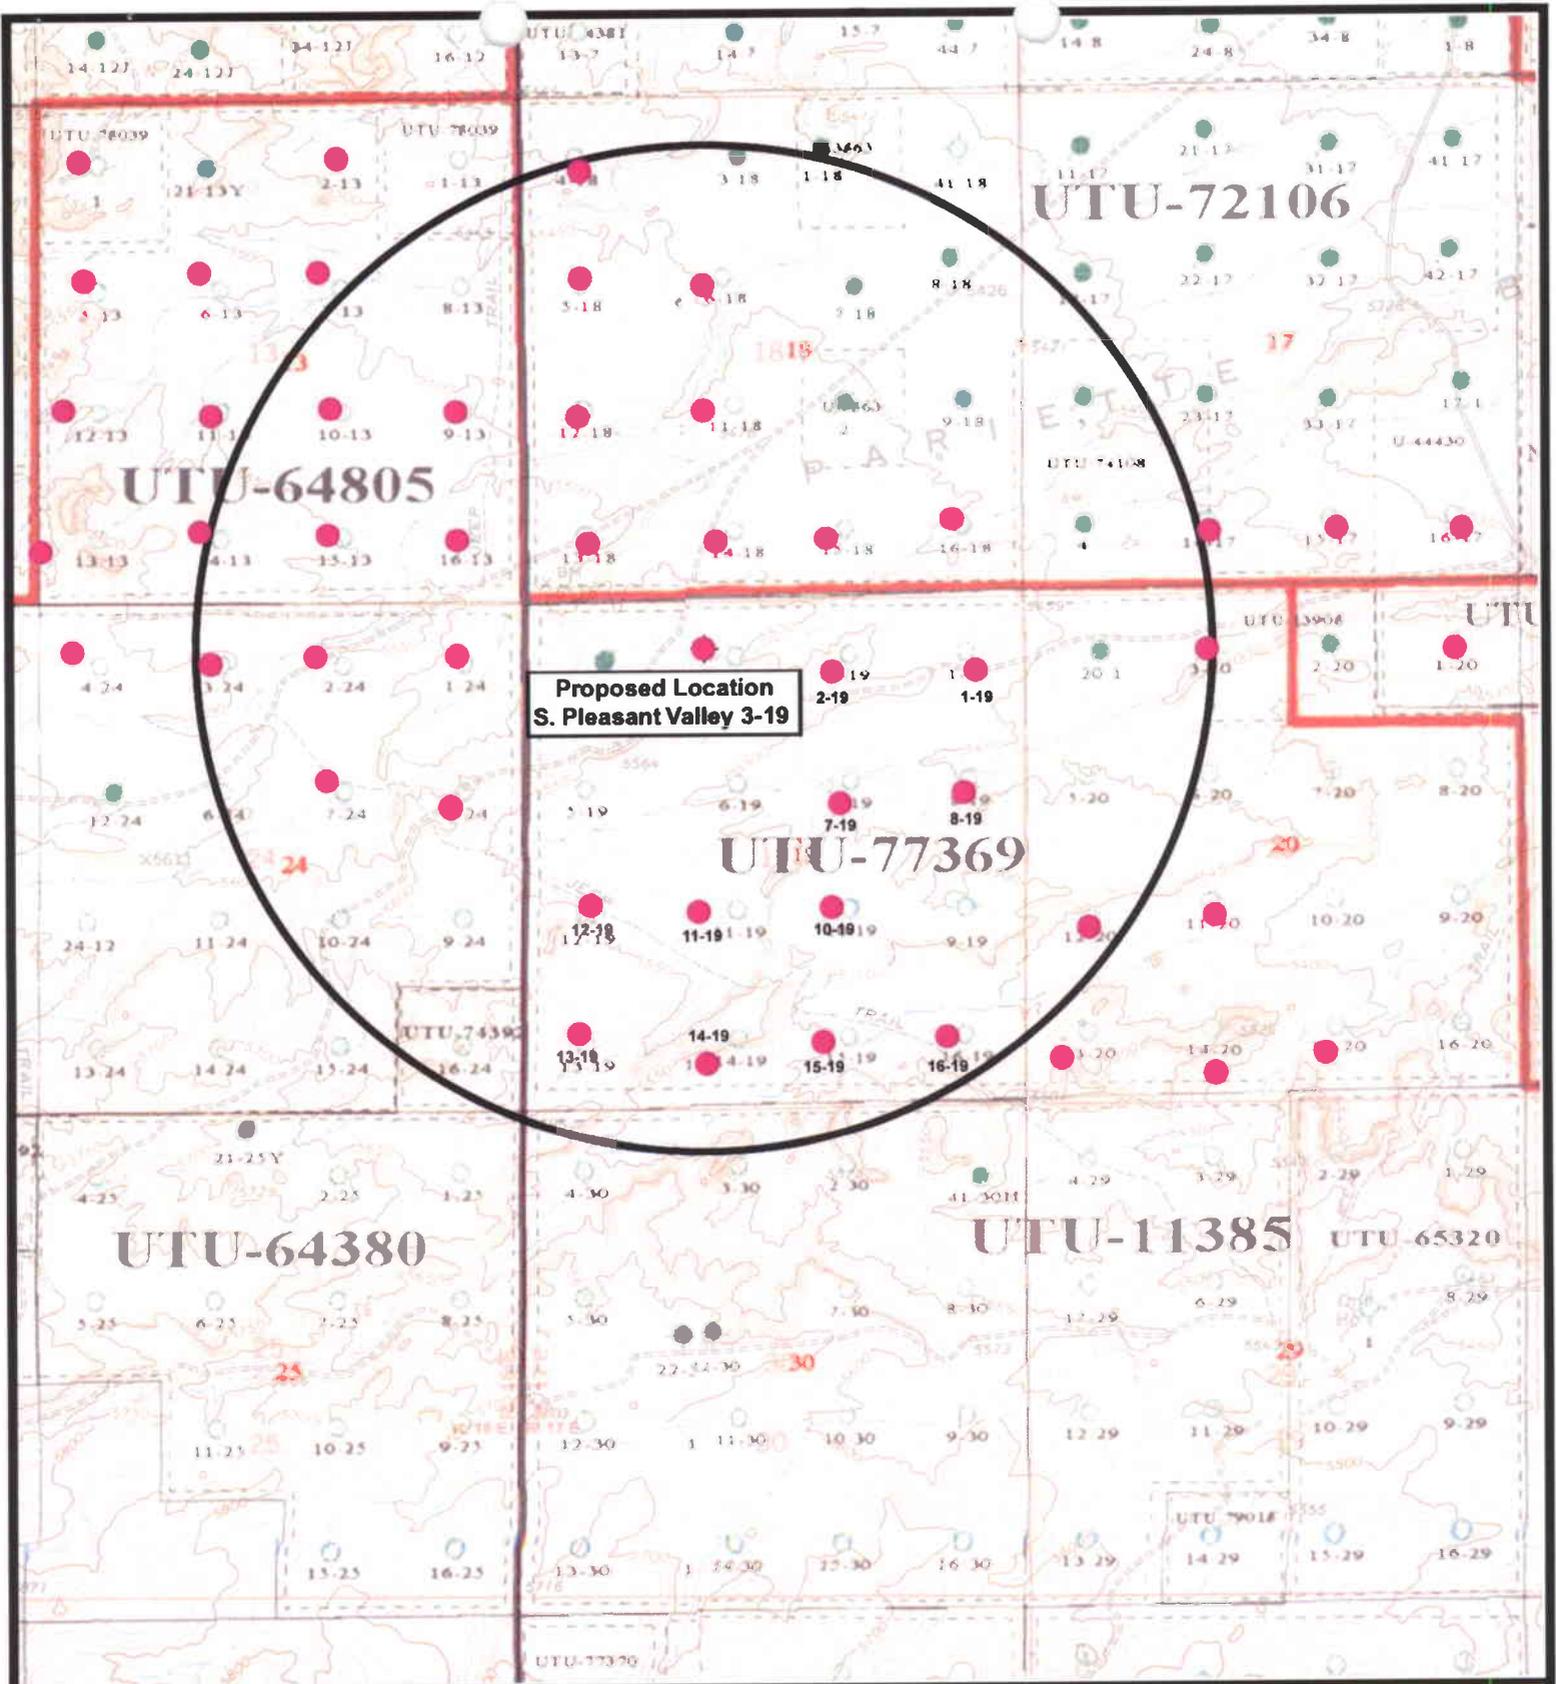

**Proposed Location  
S. Pleasant Valley 3-19**

**UTU-64380**

**UTU-77369**

**UTU-11385**

**UTU-65320**

**S. Pleasant Valley 3-19-9-17  
SEC. 19, T9S, R17E, S.L.B.&M.**



**NEWFIELD**  
Exploration Company



*Tri-State*  
*Land Surveying Inc.*  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

**SCALE: 1" = 2,000'**  
**DRAWN BY: mw**  
**DATE: 05-04-2006**

**Legend**

- Location
- One-Mile Radius

**Exhibit "B"**

# 2-M SYSTEM

Blowout Prevention Equipment Systems

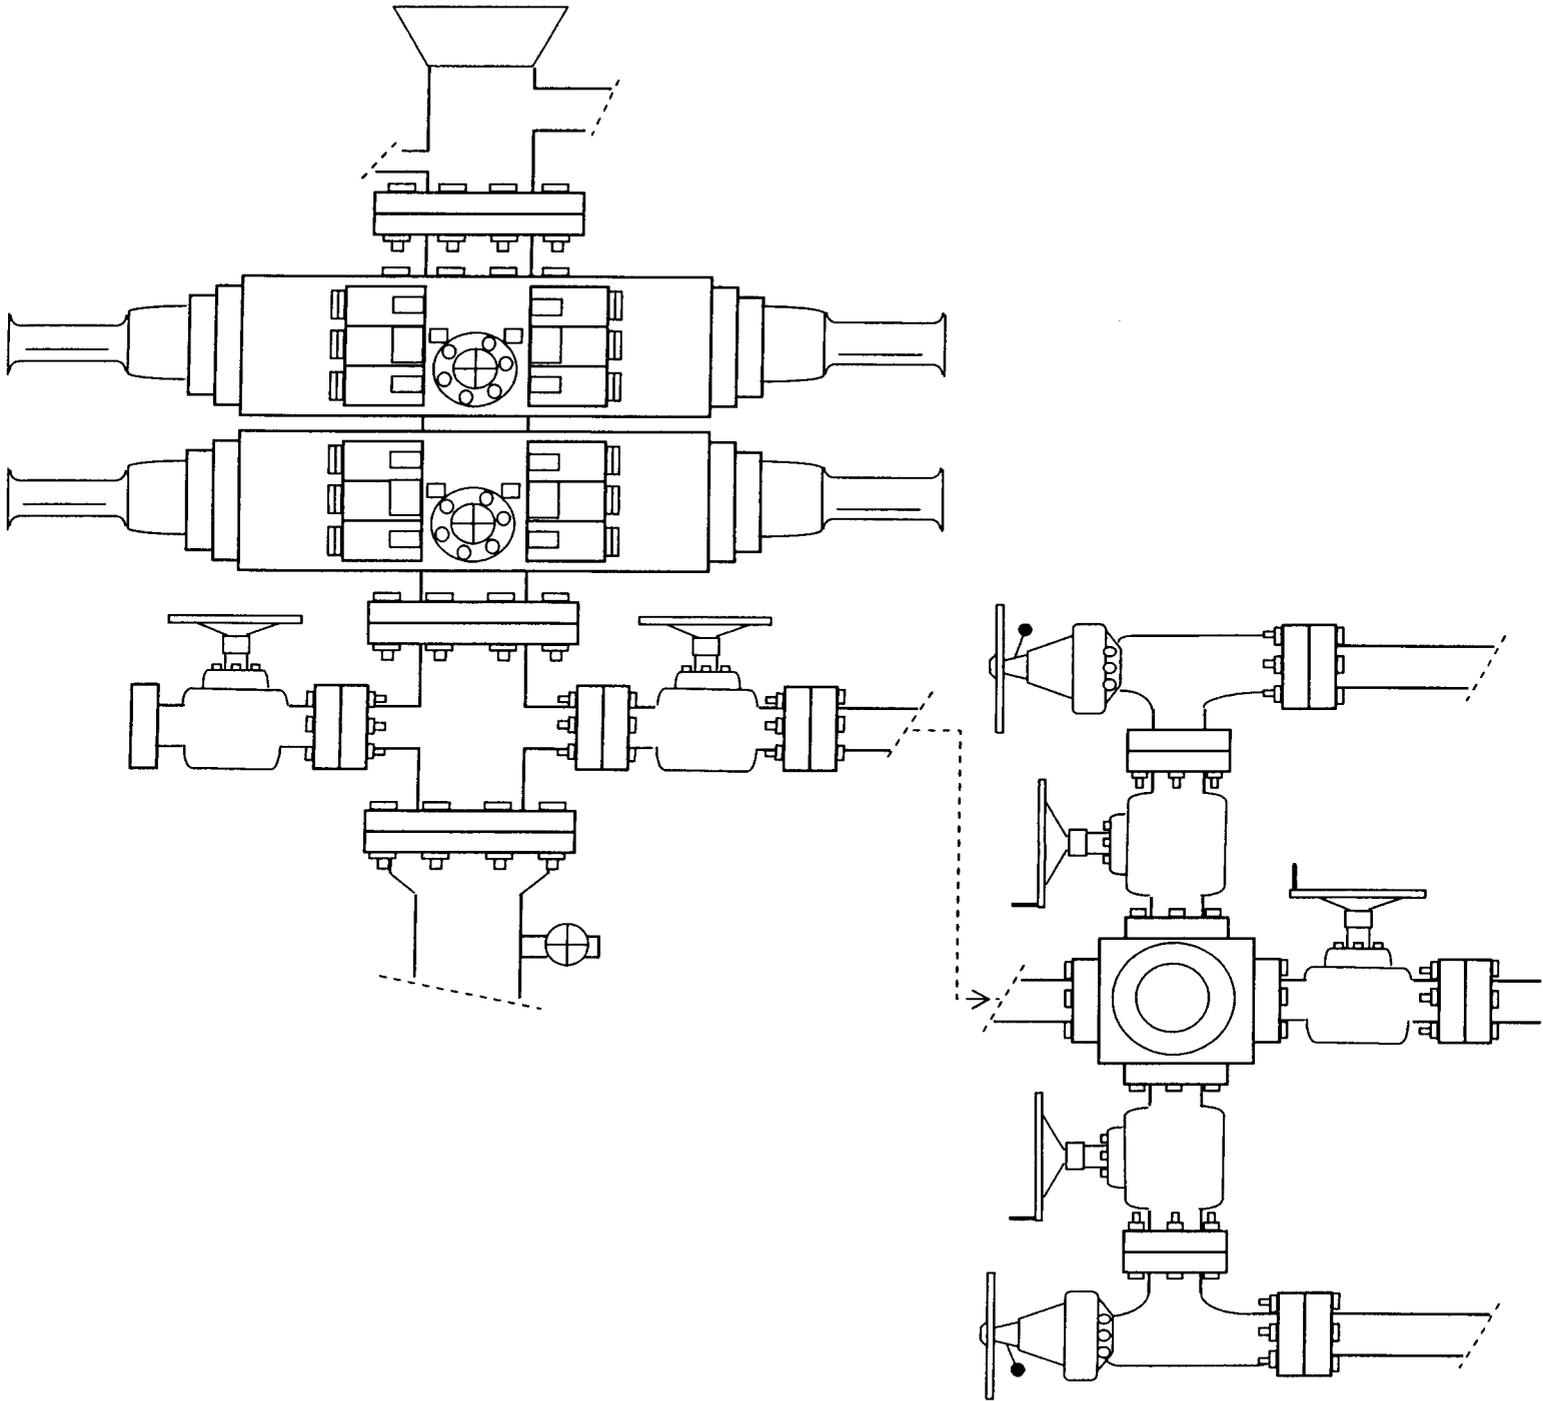


EXHIBIT C

Exhibit "D"

Page 1 of 2

CULTURAL RESOURCE INVENTORY OF  
NEWFIELD EXPLORATION'S BLOCK PARCELS  
IN T9S, R17E, SEC. 19, 20, 21 & 22  
DUCHESNE COUNTY, UTAH

Katie Simon

Prepared For:

Bureau of Land Management  
Vernal Field Office

Prepared Under Contract With:

Newfield Exploration Company  
Route 3 Box 3630  
Myton, Utah 84052

Prepared By:

Montgomery Archaeological Consultants  
P.O. Box 147  
Moab, Utah 84532

MOAC Report No. 04-206

June 15, 2005

United States Department of Interior (FLPMA)  
Permit No. 05-UT-60122

State of Utah Antiquities Project (Survey)  
Permit No. U-05-MQ-0516b

**NEWFIELD PRODUCTION COMPANY**

**PALEONTOLOGICAL SURVEY OF PROPOSED  
PRODUCTION DEVELOPMENT AREAS,  
DUCHESNE AND UINTAH COUNTIES, UTAH**

NE 1/4, NW 1/4, Section 33, T 9 S, R 18 E; Section 19, T 9 S, R 17 E [entire section excluding the NW 1/4, NW 1/4]; Section 27, T 9 S, R 16 E [entire section excluding the NW 1/4, NW 1/4], Section 28, T 9 S, R 16 E [entire section]; Section 29, T 9 S, R 16 E [entire section]; Section 30, T 9 S, R 16 E [entire section].

**REPORT OF SURVEY**

Prepared for:

**Newfield Production Company**

Prepared by:

**Wade E. Miller  
Consulting Paleontologist  
April 26, 2006**


# Newfield Production Company Proposed Site Facility Diagram

Federal 3-19-9-17

NE/NW Sec. 19, T9S, 17E

Duchesne County, Utah

UTU-77369

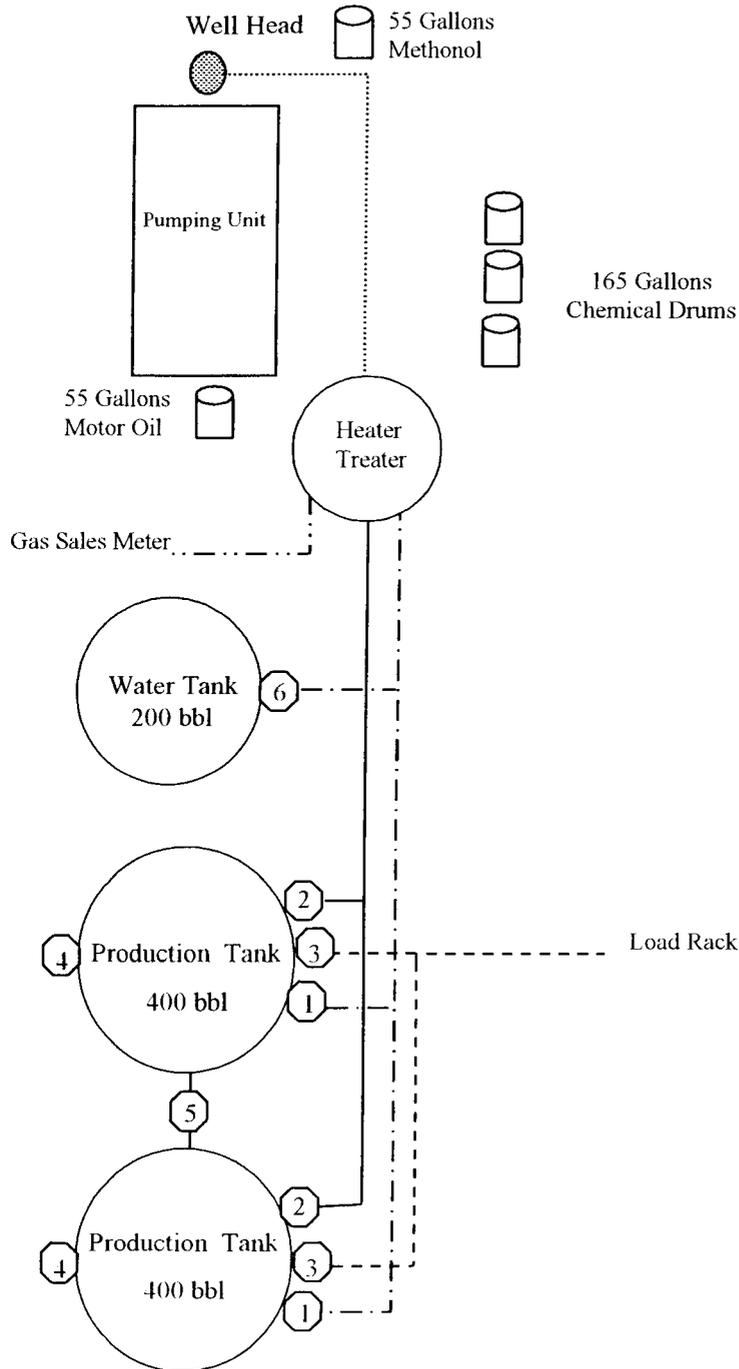

## Legend

<b>Emulsion Line</b>	.....
<b>Load Rack</b>	- - - - -
<b>Water Line</b>	- · - · -
<b>Gas Sales</b>	- · - - -
<b>Oil Line</b>	—————

### Production Phase:

- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open

### Sales Phase:

- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

### Draining Phase:

- 1) Valves 1 and 6 open

Diked Section



**WORKSHEET  
APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 05/31/2006

API NO. ASSIGNED: 43-013-33190

WELL NAME: FEDERAL 3-19-9-17

OPERATOR: NEWFIELD PRODUCTION ( N2695 )

CONTACT: MANDIE CROZIER

PHONE NUMBER: 435-646-3721

PROPOSED LOCATION:

NENW 19 090S 170E  
 SURFACE: 0454 FNL 1851 FWL  
 BOTTOM: 0454 FNL 1851 FWL  
 COUNTY: DUCHESNE  
 LATITUDE: 40.02239 LONGITUDE: -110.0510  
 UTM SURF EASTINGS: 580982 NORTHINGS: 4430464  
 FIELD NAME: MONUMENT BUTTE ( 105 )

INSPECT LOCATN BY: / /		
Tech Review	Initials	Date
Engineering		
Geology		
Surface		

LEASE TYPE: 1 - Federal  
 LEASE NUMBER: UTU-77369  
 SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: GRRV  
 COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:

- Plat
- Bond: Fed[1] Ind[] Sta[] Fee[]  
(No. UTB000192 )
- Potash (Y/N)
- Oil Shale 190-5 (B) or 190-3 or 190-13
- Water Permit  
(No. MUNICIPAL )
- RDCC Review (Y/N)  
(Date: \_\_\_\_\_ )
- Fee Surf Agreement (Y/N)
- Intent to Commingle (Y/N)

LOCATION AND SITING:

- R649-2-3.
- Unit: \_\_\_\_\_
- R649-3-2. General  
Siting: 460 From Qtr/Qtr & 920' Between Wells
- R649-3-3. Exception
- Drilling Unit  
Board Cause No: \_\_\_\_\_  
Eff Date: \_\_\_\_\_  
Siting: \_\_\_\_\_
- R649-3-11. Directional Drill

COMMENTS: See Separate File

STIPULATIONS: 1- Federal Approval  
2- Spacing Strip



**MONUMENT BUTTE FIELD**

OPERATOR: NEWFIELD PROD CO (N2695)

SEC: 19 T. 9S R. 17E

FIELD: MONUMENT BUTTE (105)

COUNTY: DUCHESNE

SPACING: R649-3-3 / EXCEPTION LOCATION

- Field Status**
- ABANDONED
  - ACTIVE
  - COMBINED
  - INACTIVE
  - PROPOSED
  - STORAGE
  - TERMINATED

- Unit Status**
- EXPLORATORY
  - GAS STORAGE
  - NF PP OIL
  - NF SECONDARY
  - PENDING
  - PI OIL
  - PP GAS
  - PP GEOTHERML
  - PP OIL
  - SECONDARY
  - TERMINATED

- Wells Status**
- GAS INJECTION
  - GAS STORAGE
  - LOCATION ABANDONED
  - NEW LOCATION
  - PLUGGED & ABANDONED
  - PRODUCING GAS
  - PRODUCING OIL
  - SHUT-IN GAS
  - SHUT-IN OIL
  - TEMP. ABANDONED
  - TEST WELL
  - WATER INJECTION
  - WATER SUPPLY
  - WATER DISPOSAL
  - DRILLING



PREPARED BY: DIANA WHITNEY  
DATE: 6-JUNE-2006



June 21, 2006

Utah Division of Oil, Gas & Mining  
P.O. Box 145801  
Attn: Diana Whitney  
Salt Lake City, Utah 84114-5801

Re: Exception Location: Federal  
3-19-9-17; UTU-77369  
Duchesne Cty., Utah

Dear Ms. Whitney:

Pursuant to Rule R649-3-3 of the Oil & Gas Rules and Regulations of the State of Utah, Newfield Production Company, Inc. hereby requests an exception location for the drilling of the captioned well. Rule R649-3-2 requires a well to be located in the center of a forty (40) acre quarter-quarter section, or a substantially equivalent lot or tract, with a tolerance of two hundred (200) feet in any direction from the center.

The location referenced above is an exception location under Rule 649-3-2, being 4' north of the drilling window tolerance for the NENW of Sec 19-T9S-R17E. The attached plat depicts the proposed drillsite location and illustrates the deviation from the drilling window, in accordance with Rule R649-3-2. This location has been selected to avoid extreme terrain.

Please note the proposed location is staked on Federal lease UTU-77369. The drillsite lease and all surrounding acreage within a four hundred sixty foot (460') radius of the proposed location is owned by Newfield Production Company.

If you have any questions or need additional information please contact me at (303) 382-4479. Thank you for your assistance in this matter.

Sincerely,

A handwritten signature in black ink that reads "Rhonda Deimer". The signature is written in a cursive, flowing style.

Rhonda Deimer  
Land Associate

RECEIVED  
JUN 26 2006

DIV. OF OIL, GAS & MINING



**State of Utah**

**Department of  
Natural Resources**

MICHAEL R. STYLER  
*Executive Director*

**Division of  
Oil, Gas & Mining**

JOHN R BAZA  
*Division Director*

JON M. HUNTSMAN, JR.  
*Governor*

GARY R. HERBERT  
*Lieutenant Governor*

June 29, 2006

Newfield Production Company  
Route #3 Box 3630  
Myton, Utah 84052

Re: Federal 3-19-9-17 Well, 454' FNL, 1851' FWL, NE NW, Sec. 19, T. 9 South,  
R. 17 East, Duchesne County, Utah


Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

Appropriate information has been submitted to DOGM and administrative approval of the requested exception location is hereby granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-33190.

Sincerely,



for Gil Hunt  
Associate Director

mf  
Enclosures

cc: Duchesne County Assessor  
Bureau of Land Management, Vernal District Office

**Operator:** Newfield Production Company

**Well Name & Number** Federal 3-19-9-17

**API Number:** 43-013-33190

**Lease:** UTU-77369

**Location:** NE NW                      **Sec.** 19                      **T.** 9 South                      **R.** 17 East

### **Conditions of Approval**

#### **1. General**

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

#### **2. Notification Requirements**

Notify the Division within 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dan Jarvis at (801) 538-5338

#### **3. Reporting Requirements**

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

#### **4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.**

#### **5. This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.**

**RECEIVED**

**JUN 01 2006**

FORM APPROVED  
OMB No. 1004-0136  
Expires January 31, 2004

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**APPLICATION FOR PERMIT TO DRILL OR REENTER**

5. Lease Serial No.	UTU-77369
6. If Indian, Allottee or Tribe Name	N/A
7. If Unit or CA Agreement, Name and No.	N/A
8. Lease Name and Well No.	Federal 3-19-9-17
9. API Well No.	43-013-33190
10. Field and Pool, or Exploratory Monument Butte	
11. Sec., T., R., M., or Blk. and Survey or Area	NE/NW Sec. 19, T9S R17E
12. County or Parish	Duchesne
13. State	UT

1a. Type of Work:  DRILL  REENTER

1b. Type of Well:  Oil Well  Gas Well  Other  Single Zone  Multiple Zone

2. Name of Operator  
Newfield Production Company

3a. Address  
Route #3 Box 3630, Myton UT 84052

3b. Phone No. (include area code)  
(435) 646-3721

4. Location of Well (Report location clearly and in accordance with any State requirements. \*)  
At surface NE/NW 454' FNL 1851' FWL  
At proposed prod. zone

14. Distance in miles and direction from nearest town or post office\*  
Approximatley 16.9 miles south of Myton, Utah

15. Distance from proposed\* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 454' f/lse, NA' f/unit

16. No. of Acres in lease  
1189.60

17. Spacing Unit dedicated to this well  
40 Acres

18. Distance from proposed location\* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1372'

19. Proposed Depth  
5864'

20. BLM/BIA Bond No. on file  
UTB000192

21. Elevations (Show whether DF, KDB, RT, GL, etc.)  
5527' GL


22. Approximate date work will start\*  
4th Quarter 2006

23. Estimated duration  
Approximately seven (7) days from opud to rig release.

**24. Attachments**

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature  Name (Printed/Typed) Mandie Crozier Date 5/31/06

Title Regulatory Specialist

Approved by (Signature)  Name (Printed/Typed) Terry Kenceks Date 2-15-2007

Title Assistant Field Manager Office VERNAL FIELD OFFICE  
Lands & Mineral Resources

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

**CONDITIONS OF APPROVAL ATTACHED**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

\*(Instructions on reverse)

**RECEIVED**

**FEB 26 2007**

**NOTICE OF APPROVAL**

DIV. OF OIL, GAS & MINING

No NDS

**UDOGM** CXS0090A



UNITED STATES DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
VERNAL FIELD OFFICE  
170 South 500 East VERNAL, UT 84078 (435) 781-4400



**CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL**

**Company:** Newfield Production Company      **Location:** NENW, Sec 19, T9S, R17E  
**Well No:** Federal 3-19-9-17      **Lease No:** UTU-77369  
**API No:** 43-013-33190      **Agreement:** N/A

Petroleum Engineer:	Matt Baker	Office: 435-781-4490	Cell: 435-828-4470
Petroleum Engineer:	Michael Lee	Office: 435-781-4432	Cell: 435-828-7875
Petroleum Engineer:	Jim Ashley	Office: 435-781-4470	Cell: 435-828-7874
Petroleum Engineer:	Ryan Angus	Office: 435-781-4430	
Supervisory Petroleum Technician:	Jamie Sparger	Office: 435-781-4502	Cell: 435-828-3913
Environmental Scientist:	Paul Buhler	Office: 435-781-4475	Cell: 435-828-4029
Environmental Scientist:	Karl Wright	Office: 435-781-4484	
Natural Resource Specialist:	Holly Villa	Office: 435-781-4404	
Natural Resource Specialist:	Melissa Hawk	Office: 435-781-4476	
Natural Resource Specialist:	Chuck Macdonald	Office: 435-781-4441	
Natural Resource Specialist:	Darren Williams	Office: 435-781-4447	
Natural Resource Specialist:	Verlyn Pindell	Office: 435-781-3402	
<b>After Hours Contact Number:</b>	<b>435-781-4513</b>	<b>Fax:</b> 435-781-4410	

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR  
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a one-year period. An additional year extension may be applied for by sundry notice prior to expiration.**

**NOTIFICATION REQUIREMENTS**

- Location Construction (Notify Chuck Macdonald) - Forty-Eight (48) hours prior to construction of location and access roads.
- Location Completion (Notify Chuck Macdonald) - Prior to moving on the drilling rig.
- Spud Notice (Notify Petroleum Engineer) - Twenty-Four (24) hours prior to spudding the well.
- Casing String & Cementing (Notify Jamie Sparger) - Twenty-Four (24) hours prior to running casing and cementing all casing strings.
- BOP & Related Equipment Tests (Notify Jamie Sparger) - Twenty-Four (24) hours prior to initiating pressure tests.
- First Production Notice (Notify Petroleum Engineer) - Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM  
CONDITIONS OF APPROVAL (COAs)***

**LEASE STIPULATIONS AND NOTICES**

- Adhere to Executive Order 5327 of April 15, 1930, stipulations for lands in oil shale withdrawal.
- Lands in this lease have been identified as containing Mountain Plover habitat. Modifications to the Surface Use Plan of Operations may be required in order to protect the Mountain Plover habitat from surface disturbing activities in accordance with Section 6 of the lease term, Endangered Species Act, and 43 CFR 3101.1-2.
- Timing Limitations (for construction and drilling) – **May 15 through June 15** – in order to protect Mountain Plover nesting season

**CONDITIONS OF APPROVAL**

- This well is being approved in accordance with Washington Instruction Memorandum 2005-247 and Section 390 (Category 3) of the Energy Policy Act which establishes statutory categorical exclusions (CX) under the National Environmental Policy Act (NEPA). Category 3 states that an oil or gas well can be drilled within a developed field for which an approved land use plan or any environmental document prepared pursuant to NEPA analyzed drilling as a reasonably foreseeable activity, so long as such plan or document was approved within five (5) years prior to the date of spudding the well. This well is covered under the *Final Environmental Impact Statement and Record of Decision Castle Peak and Eightmile Flat Oil and Gas Exploration Project Newfield Rocky Mountains Inc.*, signed August 24, 2005. If the well has not been spudded by August 24, 2010, a new environmental document will have to be prepared prior to the approval of the APD.
- All applicable local, state, and/or federal laws, regulations, and/or statutes will be complied with.
- Right of way (ROW) will not be required:
- All traffic related to this action will be restricted to approved routes. Cross-country vehicle travel will not be allowed.
- No vehicle travel, construction or routine maintenance activities shall be performed during periods when the soil is too wet to adequately support vehicles and/or construction equipment. If such equipment creates ruts in excess of three inches deep, the soil shall be deemed too wet to adequately support construction equipment.
- The access road will be crowned and ditched. Flat-bladed roads are not allowed.
- If additional erosion occurs during the life of this project, more culverts, low water crossings, berms, wing ditches or etc. will be needed to control the erosion.

- Low-water crossings will be appropriately constructed to avoid sedimentation of drainage ways and other water resources.
- Pipelines will be buried at all major drainage crossings.
- Prevent fill and stock piles from entering drainages.
- The reserve pit will be lined with a 12 ml or greater liner and felt prior to spudding.
- The liner is to be cut 5 feet below ground surface or at the level of the cuttings, whichever is deeper, and the excess liner material is to be disposed of at an authorized disposal site.
- When the reserve pit contains fluids or toxic substances, the operator must ensure animals do not ingest or become entrapped in pit fluids.
- If paleontologic or cultural materials are uncovered during construction, the operator shall immediately stop work that might further disturb or move such materials and contact the Authorized Officer (AO) within 48 hours. A determination will be made by the AO as to necessary mitigation for the discovered paleontologic/cultural material.
- If Uinta Basin hookless cactus or other special status plants are found, construction will cease and the AO will be notified to determine the appropriate mitigation.
- The following seed mix (PLS formula) will be used for interim reclamation:

Western Wheatgrass ( <i>Pascopyrum smithii</i> )	6 lbs/acre
Galleta Grass ( <i>Hilaria jamesii</i> )	6 lbs/acre

  - Rates are set for drill seeding; double the rate if broadcasting.
  - Reseeding may be required if initial seeding is not successful.
- The operator will be responsible for treatment and control of invasive and noxious weeds.
- The topsoil from the reserve pit shall be stripped and piled separately near the reserve pit. When the reserve pit is closed, it shall be recontoured and the topsoil respread, and the area shall be seeded in the same manner as the location topsoil.
- Once the location is plugged and abandoned, it shall be recontoured to natural topology, topsoil shall be respread, and the entire location shall be seeded with a seed mix recommended by the AO (preferably of native origin). Seed application will follow all guidelines in the interim seed mix bullet statement above. If reclamation seeding should take place using the broadcast method, the seed at a minimum will be walked into the soil with a dozer immediately after the seeding is completed.
- The authorized officer may prohibit surface disturbing activities during severe winter conditions to minimize watershed damage. This limitation does not apply to operation and maintenance of producing wells.

- The authorized officer may prohibit surface disturbing activities during wet or muddy conditions to minimize watershed damage. This limitation does not apply to operation and maintenance of producing wells.
- All well facilities not regulated by OSHA will be painted Carlsbad Canyon.
- All boulders with a length or diameter greater than 3 feet, that are found showing at the surface, will be stockpiled for use during final reclamation.
- Notify the Authorized Officer 48 hours prior to surface disturbing activities.
- Operator shall notify any active gilsonite mining operation within 2 miles of the location 48 hours prior to any blasting during construction for this well.

### ***DOWNHOLE CONDITIONS OF APPROVAL***

**All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to.** The following items are emphasized:

#### **SITE SPECIFIC DOWNHOLE CONDITIONS OF APPROVAL**

1. None.

#### **DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS**

1. There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well. Any changes in operation must have prior approval from the BLM, Vernal Field Office Petroleum Engineers.
2. The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
3. **Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.**
4. Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.

All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.

BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.

Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.

No aggressive/fresh hard-banded drill pipe shall be used within casing.

Cement baskets shall not be run on surface casing.

5. The lessee/operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled and analyzed (a copy of the analyses to be submitted to the BLM Field Office in Vernal, Utah).
6. All oil and gas shows shall be adequately tested for commercial possibilities, reported, and protected.

7. The lessee/operator must report encounters of all non oil and gas mineral resources (such as gilsonite, tar sands, oil shale, etc.) to the Vernal Field Office in writing within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.
8. No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM, Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM, Vernal Field Office shall be obtained and notification given before resumption of operations.
9. Chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.

Any change in the program shall be approved by the BLM, Vernal Field Office. "Sundry Notices and Reports on Wells" (Form BLM 3160-5) shall be filed for all changes of plans and other operations in accordance with 43 CFR 3162.3-2.

Emergency approval may be obtained orally, but such approval does not waive the written report requirement. Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan pursuant to Onshore Oil & Gas Order No. 1 of 43 CFR 3164.1 and prior approval by the BLM, Vernal Field Office.

In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.

10. Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.

**Please submit an electronic copy of all other logs run on this well in LAS format to UT\_VN\_Wellogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**

11. All off-lease storage, off-lease measurement, or commingling on-lease or off-lease shall have prior written approval from the BLM, Vernal Field Office.

All measurement points shall be identified as point of sales or allocation for royalty determination prior to the installation of facilities.

12. Oil and gas meters shall be calibrated in place prior to any deliveries. The Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM, Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement.
13. A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM, Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
14. This APD is approved subject to the requirement that, should the well be successfully completed for production, the BLM, Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
  - a. Operator name, address, and telephone number.
  - b. Well name and number.
  - c. Well location ( $\frac{1}{4}$ , Sec., Twn, Rng, and P.M.).
  - d. Date well was placed in a producing status (date of first production for which royalty will be paid).
  - e. The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
  - f. The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.

- g. Unit agreement and / or participating area name and number, if applicable.
  - h. Communitization agreement number, if applicable.
15. Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from Field Office Petroleum Engineers.
  16. All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production
  17. Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
  18. Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

FORM APPROVED  
Budget Bureau No. 1004-0135  
Expires: March 31, 1993

**SUNDRY NOTICES AND REPORTS ON WELLS**

Do not use this form for proposals to drill or to deepen or reentry a different reservoir.  
Use "APPLICATION FOR PERMIT -" for such proposals

5. Lease Designation and Serial No.  
**UTU-77369**

6. If Indian, Allottee or Tribe Name  
**NA**

7. If Unit or CA, Agreement Designation  
**N/A**

8. Well Name and No.  
**FEDERAL 3-19-9-17**

9. API Well No.  
**43-013-33190**

10. Field and Pool, or Exploratory Area  
**MONUMENT BUTTE**

11. County or Parish, State  
**DUCHESNE COUNTY, UT.**

**SUBMIT IN TRIPLICATE**

1. Type of Well  
 Oil Well     Gas Well     Other

2. Name of Operator  
**NEWFIELD PRODUCTION COMPANY**

3. Address and Telephone No.  
**Rt. 3 Box 3630, Myton Utah, 84052 435-646-3721**

4. Location of Well (Footage, Sec., T., R., m., or Survey Description)  
**454 FNL 1851 FWL NE/NW Section 19, T9S R17E**

12. CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION

- Notice of Intent
- Subsequent Report
- Final Abandonment Notice

TYPE OF ACTION

- Abandonment
- Recompletion
- Plugging Back
- Casing Repair
- Altering Casing
- Other **Permit Extension**
- Change of Plans
- New Construction
- Non-Routine Fracturing
- Water Shut-Off
- Conversion to Injection
- Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)\*

Newfield Production Company requests to extend the Permit to Drill this well for one year. The original approval date was 6/29/06 (expiration 6/29/07).

Approved by the  
Utah Division of  
Oil, Gas and Mining

RECEIVED  
MAY 30 2007

Date: 05-30-07  
By: [Signature]

DIV. OF OIL, GAS & MINING

3:31 PM

14. I hereby certify that the foregoing is true and correct  
Signed Mandie Crozier Title Regulatory Specialist Date 5/29/2007  
Mandie Crozier

CC: UTAH DOGM

(This space for Federal or State office use)

Approved by \_\_\_\_\_ Title \_\_\_\_\_ Date \_\_\_\_\_

Conditions of approval, if any:

CC: Utah DOGM

**Application for Permit to Drill  
Request for Permit Extension  
Validation**

(this form should accompany the Sundry Notice requesting permit extension)

**API:** 43-013-33190  
**Well Name:** Federal 3-19-9-17  
**Location:** NE/NW Section 19,T9S R17E  
**Company Permit Issued to:** Newfield Production Company  
**Date Original Permit Issued:** 6/29/2006

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision.

Following is a checklist of some items related to the application, which should be verified.

If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes  No

Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes  No

Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes  No

Have there been any changes to the access route including ownership, or right-of-way, which could affect the proposed location? Yes  No

Has the approved source of water for drilling changed? Yes  No

Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes  No

Is bonding still in place, which covers this proposed well? Yes  No

  
Signature

5/29/2007

Date

**Title:** Regulatory Specialist

**Representing:** Newfield Production Company

# DIVISION OF OIL, GAS AND MINING

## **SPUDDING INFORMATION**

Name of Company: NEWFIELD PRODUCTION COMPANY

Well Name: FEDERAL 3-19-9-17

Api No: 43-013-33190 Lease Type: FEDERAL

Section 19 Township 09S Range 17E County DUCHESNE

Drilling Contractor NDSI RIG # NS#1

### **SPUDDED:**

Date 08/30/07

Time 8:00 AM

How DRY

**Drilling will Commence:** \_\_\_\_\_

Reported by DELL RAY

Telephone # (45) 828-6110

Date 08/30/07 Signed CHD

STATE OF UTAH  
 DIVISION OF OIL, GAS AND MINING  
 ENTITY ACTION FORM -FORM 6

OPERATOR: NEWFIELD PRODUCTION COMPANY  
 ADDRESS: RT. 3 BOX 3698  
MYTON, UT 84062

OPERATOR ACCT. NO. N2895

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	16360	4301333190	FEDERAL 3-19-9-17	NENW	19	9S	17E	DUCHESNE	8/30/2007	9/25/07
WELL 1 COMMENTS: <i>GRRV</i>											
A	99999	16361	4304734943	FEDERAL 3-14-9-18	NENW	14	9S	18E	UINTAH	8/31/2007	9/25/07
<i>MNCS</i>											
A	99999	16362	4301333192	FEDERAL 6-19-9-17	SEnw	19	9S	17E	DUCHESNE	9/5/2007	9/25/07
<i>GRRV</i>											
A	99999	16363	4301333191	FEDERAL 5-19-9-17	SWNW	19	9S	17E	DUCHESNE	9/4/2007	9/25/07
<i>GRRV</i>											
ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	QQ	SC	TP	RG	COUNTY	SPUD DATE	EFFECTIVE DATE
WELL 5 COMMENTS:											
ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	QQ	SC	TP	RG	COUNTY	SPUD DATE	EFFECTIVE DATE
WELL 5 COMMENTS:											

ACTION CODES (See instructions on back of form)

- A - New entity for new well (plug in well only)
- B - well to existing entity (group or unit well)
- C - from one existing entity to another existing entity
- D - well from one existing entity to a new entity
- E - Error (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.

RECEIVED  
 SEP 06 2007

DIV. OF OIL, GAS & MINING

*Jenri Park*  
 Signature Jenri Park  
 Production Clerk  
 Date 09/06/07

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**SUNDRY NOTICES AND REPORTS ON WELLS**  
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.



1. Type of Well  
 Oil Well    Gas Well    Other

2. Name of Operator  
 NEWFIELD PRODUCTION COMPANY

3a. Address    Route 3 Box 3630  
                   Myton, UT 84052

3b. Phone    (include are code)  
                   435.646.3721

4. Location of Well    (Footage, Sec., T., R., M., or Survey Description)  
 454 FNL 1851 FWL  
 NENW Section 19 T9S R17E

5. Lease Serial No.  
 USA UTU-77369

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.  
 FEDERAL 3-19-9-17

9. API Well No.  
 4301333190

10. Field and Pool, or Exploratory Area  
 MONUMENT BUTTE

11. County or Parish, State  
 DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 8/30/2007 MIRU NDSI NS # 1.Spud well @ 8:00 AM. Drill 320' of 12 1/4" hole with air mist. TIH W/ 7 Jt's 8 5/8" J-55 24 # csgn. Set @ 324.33'/ KB On 9/1/2007 cement with 160 sks of class "G" w/ 2% CaCL2 + 1/4# sk Cello- Flake Mixed @ 15.8 ppg > 1.17 cf/ sk yeild. Returned 6 bbls cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed) Troy Zufelt	Title Drilling Supervisor
Signature 	Date 09/02/2007



Approved by _____	Title _____	Date _____
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office _____	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction.

(Instructions on reverse)

**RECEIVED**  
**SEP 06 2007**  
 DIV. OF OIL, GAS & MINING

**NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT**

8 5/8 CASING SET AT 324.33

LAST CASING 8 5/8" set @ 324.33  
 DATUM 12' KB  
 DATUM TO CUT OFF CASING \_\_\_\_\_  
 DATUM TO BRADENHEAD FLANGE \_\_\_\_\_  
 TD DRILLER 320' LOGGER \_\_\_\_\_  
 HOLE SIZE 12 1/4

OPERATOR Newfield Production Company  
 WELL Federal 3-19-9-17  
 FIELD/PROSPECT Monument Butte  
 CONTRACTOR & RIG # NDSI NS # 1

**LOG OF CASING STRING:**

PIECES	OD	ITEM - MAKE - DESCRIPTION	WT / FT	GRD	THREAD	CONDT	LENGTH
		Shoe Joint 44.18'					
		WHI - 92 csg head			8rd	A	0.95
7	8 5/8"	Maverick ST&C csg	24#	J-55	8rd	A	312.48
		<b>GUIDE</b> shoe			8rd	A	0.9
CASING INVENTORY BAL.		FEET	JTS	TOTAL LENGTH OF STRING			314.33
TOTAL LENGTH OF STRING		314.33	7	LESS CUT OFF PIECE			2
LESS NON CSG. ITEMS		1.85		PLUS DATUM TO T/CUT OFF CSG			12
PLUS FULL JTS. LEFT OUT		0		CASING SET DEPTH			<b>324.33</b>
TOTAL		312.48	7	} COMPARE			
TOTAL CSG. DEL. (W/O THRDS)		312.48	7				
TIMING		1ST STAGE					
BEGIN RUN CSG.	Spud	8/30/2007	8:00 AM	GOOD CIRC THRU JOB <u>YES</u>			
CSG. IN HOLE		8/31/2007	2:30 PM	Bbls CMT CIRC TO SURFACE <u>6</u>			
BEGIN CIRC		9/1/2007	7:31 AM	RECIPROCATED PIPE FOR <u>N/A</u>			
BEGIN PUMP CMT		9/1/2007	7:50 AM				
BEGIN DSPL. CMT		9/1/2007	8:04 AM	BUMPED PLUG TO <u>122</u> PSI			
PLUG DOWN		9/1/2007	8:15 AM				
CEMENT USED		CEMENT COMPANY- <b>B. J.</b>					
STAGE	# SX	CEMENT TYPE & ADDITIVES					
1	160	Class "G" w/ 2% CaCL2 + 1/4#/sk Cello-Flake mixed @ 15.8 ppg 1.17 cf/sk yield					
CENTRALIZER & SCRATCHER PLACEMENT		SHOW MAKE & SPACING					
Centralizers - Middle first, top second & third for 3							

COMPANY REPRESENTATIVE Troy Zufelt DATE 9/1/2007

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**SUNDRY NOTICES AND REPORTS ON WELLS**  
Do not use this form for proposals to drill or to re-enter an  
abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.

USA UTU-77369

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.  
FEDERAL 3-19-9-17

9. API Well No.  
4301333190

10. Field and Pool, or Exploratory Area  
MONUMENT BUTTE

11. County or Parish, State  
DUCHESNE, UT

**SUBMIT IN TRIPLICATE - Other Instructions on reverse side**

1. Type of Well  
 Oil Well  Gas Well  Other

2. Name of Operator  
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630  
Myton, UT 84052

3b. Phone (include area code)  
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)  
454 FNL 1851 FWL  
NENW Section 19 T9S R17E

**12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to	<input type="checkbox"/> Plug Back	<input checked="" type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

Formation water is produced to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

**Accepted by the  
Utah Division of  
Oil, Gas and Mining  
FOR RECORD ONLY**

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Mandie Crozier

Title  
Regulatory Specialist

Signature *Mandie Crozier*

Date  
10/18/2007

**THIS SPACE FOR FEDERAL OR STATE OFFICE USE**

Approved by \_\_\_\_\_  
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title \_\_\_\_\_ Date \_\_\_\_\_  
Office \_\_\_\_\_

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

**RECEIVED**  
**OCT 24 2007**  
DIV. OF OIL, GAS & MINING

**STATE OF UTAH**  
DEPARTMENT OF NATURAL RESOURCES  
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:  
USA UTU-77369

**SUNDRY NOTICES AND REPORTS ON WELLS**

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

7. UNIT or CA AGREEMENT NAME:

1. TYPE OF WELL: OIL WELL  GAS WELL  OTHER

8. WELL NAME and NUMBER:  
FEDERAL 3-19-9-17

2. NAME OF OPERATOR:  
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:  
4301333190

3. ADDRESS OF OPERATOR:  
Route 3 Box 3630 CITY Myton STATE UT ZIP 84052

PHONE NUMBER  
435.646.3721

10. FIELD AND POOL, OR WILDCAT:  
MONUMENT BUTTE

4. LOCATION OF WELL:  
FOOTAGES AT SURFACE: 454 FNL 1851 FWL

COUNTY: DUCHESNE

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NENW, 19, T9S, R17E

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA


TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate)  Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only)  Date of Work Completion: 10/30/2007	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was completed on 10/15/07, attached is a daily completion status report.

NAME (PLEASE PRINT) Jentri Park

TITLE Production Clerk

SIGNATURE 

DATE 10/30/2007

(This space for State use only)

**RECEIVED**

**NOV 09 2007**

**DIV. OF OIL, GAS & MINING**

**Daily Activity Report**

Format For Sundry

**FEDERAL 3-19-9-17****8/1/2007 To 12/30/2007****10/5/2007 Day: 1****Completion**

Rigless on 10/4/2007 - Instal 5K frac head. NU 6" 5K Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head, csg & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 5665' & cement top @ 113'. Perforate stage #1, CP5 sds @ 5570-85' w/ 3-1/8" Slick Guns (19 gram, .49" HE, 120°) w/ 4 spf for total of 48 shots. 136 bbls EWTR. SIFN.

**10/11/2007 Day: 2****Completion**

Rigless on 10/10/2007 - Stage #1 CP5 sds. RU BJ Services. 190 psi on well. Frac CP5 sds w/ 35,225#'s of 20/40 sand in 436 bbls of Lightning 17 fluid. Broke @ 3003 psi. Treated w/ ave pressure of 1942 psi w/ ave rate of 24.8 BPM. ISIP 2019 psi. Leave pressure on well. 572 BWTR. Stage #2 CP.5 & CP1 sds. RU The Perforators, llc WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 5', 6' perf guns. Set plug @ 5440'. Perforate CP.5 & CP1 sds @ 5292-98' & 5332-37' w/ 3-1/8" Slick Guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 44 shots. RU BJ Services. 1625 psi on well. Frac CP.5 & CP1 sds w/ 25,321#'s of 20/40 sand in 352 bbls of Lightning 17 fluid. Broke @ 2300 psi. Treated w/ ave pressure of 2390 psi w/ ave rate of 19.9 BPM. ISIP 2054 psi. Leave pressure on well. 924 BWTR. Stage #3 D1 sds. RU The Perforators, llc WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 6' perf gun. Set plug @ 4570'. Perforate D1 sds @ 4472-78' w/ 3-1/8" Slick Guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 24 shots. RU BJ Services. 1745 psi on well. Frac D1 sds w/ 15,151#'s of 20/40 sand in 254 bbls of Lightning 17 fluid. Broke @ 2850 psi. Treated w/ ave pressure of 2012 psi w/ ave rate of 24.8 BPM. ISIP 1759 psi. Leave pressure on well. 1178 BWTR. Stage #4 PB 7 sds. RU The Perforators, llc WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 7' perf gun. Set plug @ 4200'. Perforate PB7 sds @ 4105-12' w/ 3-1/8" Slick Guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 28 shots. RU BJ Services. 1485 psi on well. Frac PB7 sds w/ 25,019#'s of 20/40 sand in 335 bbls of Lightning 17 fluid. Broke @ 3960 psi. Treated w/ ave pressure of 2423 psi w/ ave rate of 24.8 BPM. ISIP 3008 psi. Leave pressure on well. 1513 BWTR. Stage #5 GB6 sds. RU The Perforators, llc WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 10' perf gun. Set plug @ 4050'. Perforate GB6 sds @ 3980-90' w/ 3-1/8" Slick Guns (19 gram, .49" HE, 120°, 21.92" pen, EXP-3319-331 Titan) w/ 4 spf for total of 40 shots. RU BJ Services. 1460 psi on well. Frac GB6 sds w/ 41,613#'s of 20/40 sand in 410 bbls of Lightning 17 fluid. Broke @ 3047 psi. Treated w/ ave pressure of 1648 psi w/ ave rate of 24.8 BPM. ISIP 1770 psi. Open well to pit for immediate flowback @ 1 bpm. Well flowed for 3.5 hrs. & died. Recovered 230 bbls. SWIFN.

**10/12/2007 Day: 3****Completion**

Rigless on 10/11/2007 - MIRU Western #2. Bleed off well. ND Cameron BOP & 5m frac head. NU 3m production head & Schafer BOP. RIH w/ 4 3/4" chomp bit, bit sub & 2 7/8" tbg. from pipe racks (tallying & drifting). Tag @ 4033'. RU powerswivel & pump. C/O to CBP @ 4050'. DU CBP in 29 min. Cont. RIH w/ tbg. Tag @ 4073'. C/O to CBP @ 4200'. DU CBP in 42 min. Circulate well clean. SWIFN.

---

**10/15/2007 Day: 4****Completion**

Rigless on 10/14/2007 - Bleed off well. RIH w/ tbg. Tag CBP @ 4570'. DU CBP in 24 min. Cont. RIH w/ tbg. Tag @ 5425'. C/O to CBP @ 5440'. DU CBP in 22 min. Cont. RIH w/ tbg. Tag @ 5575'. C/O to PBTD @ 5704'. Circulate well clean. Pull up to 5641'. RU swab. SFL @ surface. Made 18 runs. Recovered 156 bbls. Trace of oil. No show of sand. EFL @ 2300'. RD swab. SWIFN.

---

**10/16/2007 Day: 5****Completion**

Western #2 on 10/15/2007 - Bleed off well. RIH w/ tbg. Tag @ 5700'. C/O to PBTD @ 5704'. Circulate well clean. POOH w/ tbg. LD BHA. RIH w/ 2 7/8" notched collar, 2 jts 2 7/8" tbg., PSN, 1 jt 2 7/8" tbg., 5 1/2" TAC, 179 jts 2 7/8" tbg. ND BOP. Set TAC @ 5523' w/ 16,000# tension. NU wellhead. X-over for rods. Flush tbg. w/ 60 bbls water. RIH w/ CDI 2 1/2" x 1 1/2" x 16' x 19.5' RHAC pump, 5- 1 1/2" weight bars, 20- 3/4" guided rods, 95- 3/4" slick rods, 101- 3/4" guided rods, 1- 8', 2- 6', 1- 2' x 3/4" pony subs, 1 1/2" x 26' polished rod. Seat pump. RU pumping unit. Hang off rods. Stroke test to 800 psi. Adjust tag. RD. Put well on production @ 5:30 p.m. 5 spm, 102" stroke length. Final Report.

---

**Pertinent Files: Go to File List**

**SUBMIT IN DUPLICATE\***  
(See other instructions on reverse side)

FORM APPROVED

OMB NO. 1004-0137

Expires: February 28, 1995

**UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT**

5. LEASE DESIGNATION AND SERIAL NO.

UTU-77369

**WELL COMPLETION OR RECOMPLETION REPORT AND LOG\***

6. IF INDIAN, ALLOTTEE OR TRIBE NAME

NA

1a. TYPE OF WORK

OIL WELL  GAS WELL  DRY  Other \_\_\_\_\_

7. UNIT AGREEMENT NAME

Federal

1b. TYPE OF WELL

NEW WELL  WORK OVER  DEEPEN  PLUG BACK  DIFF RESVR.  Other \_\_\_\_\_

8. FARM OR LEASE NAME, WELL NO.

Federal 3-19-9-17

2. NAME OF OPERATOR

Newfield Exploration Company

9. WELL NO.

43-013-33190

3. ADDRESS AND TELEPHONE NO.

1401 17th St. Suite 1000 Denver, CO 80202

10. FIELD AND POOL OR WILDCAT

Monument Butte

4. LOCATION OF WELL (Report locations clearly and in accordance with any State requirements.\*)

At Surface 454' FNL & 1851' FWL (NE/NW) Sec. 19, T9S, R17E

11. SEC., T., R., M., OR BLOCK AND SURVEY OR AREA

Sec. 19, T9S, R17E

At top prod. Interval reported below

At total depth

14. API NO. 43-013-33190 DATE ISSUED 06/29/07

12. COUNTY OR PARISH

Duchesne

13. STATE

UT

15. DATE SPUDDED

08/30/07

16. DATE T.D. REACHED

09/24/07

17. DATE COMPL. (Ready to prod.)

10/15/07

18. ELEVATIONS (DF, RKB, RT, GR, ETC.)\*

5527' GL

5539' KB

19. ELEV. CASINGHEAD

20. TOTAL DEPTH, MD & TVD

5750'

21. PLUG BACK T.D., MD & TVD

5704'

22. IF MULTIPLE COMPL., HOW MANY\*

23. INTERVALS DRILLED BY

----->

ROTARY TOOLS

X

CABLE TOOLS

24. PRODUCING INTERVAL(S), OF THIS COMPLETION--TOP, BOTTOM, NAME (MD AND TVD)\*

Green River 3980'-5582'

25. WAS DIRECTIONAL SURVEY MADE

No

26. TYPE ELECTRIC AND OTHER LOGS RUN

Dual Induction Guard, SP, Compensated Density, Compensated Neutron, GR, Caliper, Cement Bond Log

27. WAS WELL CORED

No

23. CASING RECORD (Report all strings set in well)

CASING SIZE/GRADE	WEIGHT, LB./FT.	DEPTH SET (MD)	HOLE SIZE	TOP OF CEMENT, CEMENTING RECORD	AMOUNT PULLED
8-5/8" - J-55	24#	324'	12-1/4"	To surface with 160 sx Class "G" cmt	
5-1/2" - J-55	15.5#	5757'	7-7/8"	300 sx Premlite II and 450 sx 50/50 Poz	

29. LINER RECORD

SIZE	TOP (MD)	BOTTOM (MD)	SACKS CEMENT*	SCREEN (MD)	SIZE	DEPTH SET (MD)	PACKER SET (MD)
					2-7/8"	EOT @ 5619'	TA @ 5523'

31. PERFORATION RECORD (Interval, size and number)

INTERVAL	SIZE	SPF/NUMBER	DEPTH INTERVAL (MD)	AMOUNT AND KIND OF MATERIAL USED
(CP5) 5570'-5582'	.49"	4/48	5570'-5582'	Frac w/ 35,225# 20/40 sand in 436 bbls fluid
(CP.5 & CP1) 5292'-98', 5332'-37'	.49"	4/44	5292'-5337'	Frac w/ 25,321# 20/40 sand in 352 bbls fluid
(D1) 4472'-4478'	.49"	4/24	4472'-4478'	Frac w/ 15,151# 20/40 sand in 254 bbls fluid
(PB7) 4105'-4112'	.49"	4/28	4105'-4112'	Frac w/ 25,019# 20/40 sand in 335 bbls fluid
(GB6) 3980'-3990'	.49"	4/40	3980'-3990'	Frac w/ 41,613# 20/40 sand in 410 bbls fluid

33.\* PRODUCTION

DATE FIRST PRODUCTION	PRODUCTION METHOD (Flowing, gas lift, pumping--size and type of pump)	WELL STATUS (Producing or shut-in)					
10/15/07	2-1/2" x 1-1/2" x 19.5' RHAC SM Plunger Pump	PRODUCING					
DATE OF TEST	HOURS TESTED	CHOKE SIZE	PROD'N. FOR TEST PERIOD	OIL--BBL.	GAS--MCF.	WATER--BBL.	GAS-OIL RATIO
10 day ave			----->	34	8	56	235
FLOW, TUBING PRESS.	CASING PRESSURE	CALCULATED 24-HOUR RATE	OIL-BBL.	GAS--MCF.	WATER--BBL.	OIL GRAVITY-API (CORR.)	
		----->					

34. DISPOSITION OF GAS (Sold, used for fuel, vented, etc.)

Sold & Used for Fuel

35. LIST OF ATTACHMENTS

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records

SIGNED

*[Signature]*  
Jentri Park

TITLE

Production Clerk

DATE

11/7/2007

\*(See Instructions and Spaces for Additional Data on Reverse Side)

**RECEIVED**  
NOV 09 2007

DIV. OF OIL, GAS & MINING

37. SUMMARY OF POROUS ZONES: (Show all important zones of porosity and contents thereof, cored intervals, and all drill-stem, tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures, and recoveries);

38. GEOLOGIC MARKERS

FORMATION	TOP	BOTTOM	DESCRIPTION, CONTENTS, ETC.	NAME	TOP	
					MEAS. DEPTH	TRUE VERT. DEPTH
			<b>Well Name Federal 3-19-9-17</b>	Garden Gulch Mkr	3448'	
				Garden Gulch 1	3652'	
				Garden Gulch 2	3762'	
				Point 3 Mkr	4005'	
				X Mkr	4273'	
				Y-Mkr	4306'	
				Douglas Creek Mkr	4430'	
				BiCarbonate Mkr	4663'	
				B Limestone Mkr	4770'	
				Castle Peak	5258'	
				Basal Carbonate	5700'	
				Total Depth (LOGGERS)	5740'	

<b>STATE OF UTAH</b> DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
<b>SUNDRY NOTICES AND REPORTS ON WELLS</b>  Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		<b>5. LEASE DESIGNATION AND SERIAL NUMBER:</b> UTU-77369
		<b>6. IF INDIAN, ALLOTTEE OR TRIBE NAME:</b>
<b>1. TYPE OF WELL</b> Oil Well		<b>7. UNIT or CA AGREEMENT NAME:</b> GMBU (GRRV)
<b>2. NAME OF OPERATOR:</b> NEWFIELD PRODUCTION COMPANY		<b>8. WELL NAME and NUMBER:</b> FEDERAL 3-19-9-17
<b>3. ADDRESS OF OPERATOR:</b> Rt 3 Box 3630 , Myton, UT, 84052		<b>9. API NUMBER:</b> 43013331900000
<b>PHONE NUMBER:</b> 435 646-4825 Ext		<b>9. FIELD and POOL or WILDCAT:</b> MONUMENT BUTTE
<b>4. LOCATION OF WELL</b> <b>FOOTAGES AT SURFACE:</b> 0454 FNL 1851 FWL <b>QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN:</b> Qtr/Qtr: NENW Section: 19 Township: 09.0S Range: 17.0E Meridian: S		<b>COUNTY:</b> DUCHESNE
		<b>STATE:</b> UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 3/26/2013	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input checked="" type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input checked="" type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The subject well has been converted from a producing oil well to an injection well on 03/26/2013. Initial MIT on the above listed well. On 03/26/2013 the casing was pressured up to 1275 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tubing pressure was 50 psig during the test. There was not an EPA representative available to witness the test. EPA# UT22197-09903

**Accepted by the  
Utah Division of  
Oil, Gas and Mining  
FOR RECORD ONLY  
April 10, 2013**

<b>NAME (PLEASE PRINT)</b> Lucy Chavez-Naupoto	<b>PHONE NUMBER</b> 435 646-4874	<b>TITLE</b> Water Services Technician
<b>SIGNATURE</b> N/A	<b>DATE</b> 4/3/2013	

## Mechanical Integrity Test Casing or Annulus Pressure Mechanical Integrity Test

U.S. Environmental Protection Agency  
Underground Injection Control Program  
999 18<sup>th</sup> Street, Suite 500 Denver, CO 80202-2466

EPA Witness: \_\_\_\_\_ Date: 3/26/2013  
 Test conducted by: Cody Marx  
 Others present: \_\_\_\_\_

-09903

Well Name: <u>Federal 319-9-17</u>	Type: ER SWD	Status: AC TA UC
Field: <u>Monument Butte</u>		
Location: <u>NE/NW</u> Sec: <u>19</u> T <u>9</u> N/S R <u>17</u> E/W County: <u>Duchesne</u> State: <u>Ut.</u>		
Operator: <u>Cody Marx</u>		
Last MIT: <u>1/1</u>	Maximum Allowable Pressure: _____	PSIG

Is this a regularly scheduled test?     Yes     No  
 Initial test for permit?                 Yes     No  
 Test after well rework?                 Yes     No  
 Well injecting during test?             Yes     No    If Yes, rate: \_\_\_\_\_ bpd

Pre-test casing/tubing annulus pressure: 1275 psig

MIT DATA TABLE	Test #1	Test #2	Test #3
<b>TUBING PRESSURE</b>			
Initial Pressure	<u>50</u> psig	psig	psig
End of test pressure	<u>50</u> psig	psig	psig
<b>CASING / TUBING ANNULUS PRESSURE</b>			
0 minutes	<u>1275</u> psig	psig	psig
5 minutes	<u>1275</u> psig	psig	psig
10 minutes	<u>1275</u> psig	psig	psig
15 minutes	<u>1275</u> psig	psig	psig
20 minutes	<u>1275</u> psig	psig	psig
25 minutes	<u>1275</u> psig	psig	psig
30 minutes	<u>1275</u> psig	psig	psig
_____ minutes	psig	psig	psig
_____ minutes	psig	psig	psig
<b>RESULT</b>	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail

Does the annulus pressure build back after the test?     Yes     No

### MECHANICAL INTEGRITY PRESSURE TEST

Additional comments for mechanical integrity pressure test, such as volume of fluid added to annulus and bled back at end of test, reason for failing test (casing head leak, tubing leak, other), etc.:

Signature of Witness: \_\_\_\_\_



## Daily Activity Report

Format For Sundry

**FEDERAL 3-19-9-17**

**1/1/2013 To 5/30/2013**

**3/21/2013 Day: 1**

**Conversion**

WWS #7 on 3/21/2013 - MIRUSU, Pooh w/ rods & tbg. - MIRUSU, pump 60 bbls htd wtr. Dwn csg unseat rod pump & flush w/ 30 bbls L/D rod string & RHAC pump stoping to flush w/ 30 bbls 1 more time. Change over to tbg. Equip. rls TAC Pooh breaking & Doping OOH, SWIFN

**Daily Cost:** \$0

**Cumulative Cost:** \$10,500

---

**3/25/2013 Day: 2**

**Conversion**

WWS #7 on 3/25/2013 - Perf C-Sand f/ 4608-26' w/ 3 spf & 120 deg. Phasing, P/U RIH w/ 56-1/2 Pkr & RBP break dwn perms - 0# SIP, R/U Extreme W/L RIH w/ 3-1/8 perf gun @ 120 deg. Phasing perf C-Sand f/ 4608-26' Pooh R/D same P/U RIH w/ 5-1/2 HD Pkr & TS Rbp, followed by 148 jts. 2-7/8 N-80 frac string set RBP @ 4654' & pkr @ 4560' R/U Advantage H/O fill tbg. w/ 17 bbls break dwn zone w/ 3800# @ 1 bpm inject 10 bbls @ 2300 and 1 bpm ISIP 1900# FG.-.85 RLS pkr SWIFN

**Daily Cost:** \$0

**Cumulative Cost:** \$18,100

---

**3/27/2013 Day: 3**

**Conversion**

WWS #7 on 3/27/2013 - Frac C-sand w/ 22,769# 20/40 white Pooh w/ tools start back in hole w/ injection BHA - R/U Baker Hughes, frac C-Sand w/ 22,769# 20/40 white w/ 17# gelled system, open to flow back on #20 choke @ 3 bpm adjusting choke as needed recovered 150 bbls rls pkr reverse circ. Clean RIH rls RBP & Pooh w/ tools L/d work string, P/U start in hole w/ AS1X pkr & injection EOT @ 1500' SWIFN - Cont. in hole w/ tbg. & BHA pump 20 bbls dwn tbg. Drop S/V test tbg. To 3000# test for 1 hr. (good) r/u sandline RIH ret. S/V, N/D BOP pump PKR fluid set AS1X w/ 15k tension N/U injestion wellhead test ann. To 1500# for 1 hr.(good) RDSUMOL EOT @ 3941' - Cont. in hole w/ tbg. & BHA pump 20 bbls dwn tbg. Drop S/V test tbg. To 3000# test for 1 hr. (good) r/u sandline RIH ret. S/V, N/D BOP pump PKR fluid set AS1X w/ 15k tension N/U injestion wellhead test ann. To 1500# for 1 hr.(good) RDSUMOL EOT @ 3941' - R/U Baker Hughes, frac C-Sand w/ 22,769# 20/40 white w/ 17# gelled system, open to flow back on #20 choke @ 3 bpm adjusting choke as needed recovered 150 bbls rls pkr reverse circ. Clean RIH rls RBP & Pooh w/ tools L/d work string, P/U start in hole w/ AS1X pkr & injection EOT @ 1500' SWIFN

**Daily Cost:** \$0

**Cumulative Cost:** \$79,200

---

**4/2/2013 Day: 5**

**Conversion**

Rigless on 4/2/2013 - Conduct initial MIT - Initial MIT on the above listed well. On 03/26/2013 the casing was pressured up to 1275 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tubing pressure was 50 psig during the test. There was not an EPA representative available to witness the test. EPA# UT22197-09903

**Finalized**

**Daily Cost:** \$0

**Cumulative Cost:** \$114,334

---

**Pertinent Files: [Go to File List](#)**

<b>STATE OF UTAH</b> DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		<b>FORM 9</b>
<b>SUNDRY NOTICES AND REPORTS ON WELLS</b>  Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		<b>5. LEASE DESIGNATION AND SERIAL NUMBER:</b> UTU-77369
<b>1. TYPE OF WELL</b> Water Injection Well		<b>6. IF INDIAN, ALLOTTEE OR TRIBE NAME:</b>  <b>7. UNIT or CA AGREEMENT NAME:</b> GMBU (GRRV)
<b>2. NAME OF OPERATOR:</b> NEWFIELD PRODUCTION COMPANY		<b>8. WELL NAME and NUMBER:</b> FEDERAL 3-19-9-17
<b>3. ADDRESS OF OPERATOR:</b> Rt 3 Box 3630 , Myton, UT, 84052		<b>9. API NUMBER:</b> 43013331900000
<b>4. LOCATION OF WELL</b> <b>FOOTAGES AT SURFACE:</b> 0454 FNL 1851 FWL <b>QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN:</b> Qtr/Qtr: NENW Section: 19 Township: 09.0S Range: 17.0E Meridian: S		<b>PHONE NUMBER:</b> 435 646-4825 Ext
<b>9. FIELD and POOL or WILDCAT:</b> MONUMENT BUTTE		<b>9. FIELD and POOL or WILDCAT:</b> MONUMENT BUTTE
<b>COUNTY:</b> DUCHESNE		<b>STATE:</b> UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
<b>TYPE OF SUBMISSION</b>	<b>TYPE OF ACTION</b>	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 4/11/2013	<input type="checkbox"/> ALTER CASING	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CASING REPAIR	
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	
	<input type="checkbox"/> CHANGE TUBING	
	<input checked="" type="checkbox"/> CHANGE WELL STATUS	
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	
	<input checked="" type="checkbox"/> CONVERT WELL TYPE	
	<input type="checkbox"/> DEEPEN	
	<input type="checkbox"/> FRACTURE TREAT	
	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	
	<input type="checkbox"/> PLUG AND ABANDON	
	<input type="checkbox"/> PLUG BACK	
	<input type="checkbox"/> PRODUCTION START OR RESUME	
	<input type="checkbox"/> RECLAMATION OF WELL SITE	
	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	
	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	
	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	
	<input type="checkbox"/> VENT OR FLARE	
	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	
	<input type="checkbox"/> SI TA STATUS EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	
	<input type="checkbox"/> OTHER: <input style="width: 100px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. <p style="text-align: center;">The above reference well was put on injection at 10:00 AM on 04/11/2013. EPA # UT22197-09903</p> <div style="text-align: right; padding-right: 50px;"> <p><b>Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY April 19, 2013</b></p> </div>		
<b>NAME (PLEASE PRINT)</b> Lucy Chavez-Naupoto	<b>PHONE NUMBER</b> 435 646-4874	<b>TITLE</b> Water Services Technician
<b>SIGNATURE</b> N/A	<b>DATE</b> 4/19/2013	

Spud Date: 08.30.07  
 Put on Production: 10.15.07  
 GI: 5527' KB: 5539'

# FEDERAL 3-19-9-17

## Injection Wellbore Diagram

### SURFACE CASING

CSG SIZE: 8-5/8"  
 GRADE: J-55  
 WEIGHT: 24#  
 LENGTH: 7 jts. (312.48')  
 DEPTH LANDED: 324.33' KB  
 HOLE SIZE: 12-1/4"  
 CEMENT DATA: 160 sxs Class "G" cement, est 6 bbls cement to surf.

### PRODUCTION CASING

CSG SIZE: 5-1/2"  
 GRADE: J-55  
 WEIGHT: 15.5#  
 LENGTH: 144 jts. (5743.28')  
 DEPTH LANDED: 5756.53' KB  
 HOLE SIZE: 7-7/8"  
 CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50-50 POZ.  
 CEMENT TOP: 113'

### TUBING

SIZE/GRADE/WT.: 2-7/8" J-55 6.5#  
 NO. OF JOINTS: 127 jts (3913.1')  
 SEATING NIPPLE: 2-7/8" (1.10')  
 SN LANDED AT: 3925.1' KB  
 ON-OFF TOOL AT: 3926.2'  
 ARROW #1 PACKER CE AT: 3932'  
 XO 2-3/8 x 2-7/8 J-55 AT: 3935'  
 TBG PUP 2-3/8 J-55 AT: 3935.5'  
 X/N NIPPLE AT: 3939.6'  
 TOTAL STRING LENGTH: EOT @ 3941.2'

### FRAC. JOB

10/10/07 5570-5582' Frac CFS sands as follows:  
 35225# 20-40 sand in 436 bbls Lightning 17 frac fluid. Treated @ avg press of 1942 psi w/avg rate of 24.8 BPM. ISIP 2019 psi. Calc flush: 5755 gal. Actual flush: 5061 gal.

10/10/07 5292-5337' Frac C.P.S & CPI sands as follows:  
 25321# 20-40 sand in 352 bbls Lightning 17 frac fluid. Treated @ avg press of 2390 psi w/avg rate of 19.9 BPM. ISIP 2054 psi. Calc flush: 5290 gal. Actual flush: 4704 gal.

10/10/07 4472-4478' Frac DI sands as follows:  
 15151# 20-40 sand in 254 bbls Lightning 17 frac fluid. Treated @ avg press of 2012 psi w/avg rate of 24.8 BPM. ISIP 1759 psi. Calc flush: 4470 gal. Actual flush: 3885 gal.

10/10/07 4105-4112' Frac PB7 sands as follows:  
 25019# 20-40 sand in 335 bbls Lightning 17 frac fluid. Treated @ avg press of 2423 psi w/avg rate of 24.8 BPM. ISIP 3008 psi. Calc flush: 4103 gal. Actual flush: 3608 gal.


10/10/07 3980-3990' Frac GB6 sands as follows:  
 41613# 20-40 sand in 410 bbls Lightning 17 frac fluid. Treated @ avg press of 1648 psi w/avg rate of 24.8 BPM. ISIP 1770 psi. Calc flush: 3980 gal. Actual flush: 3898 gal.

6/16/08 HIT. Rod & tubing updated.

03/25/13 4608-4624' Frac C sands as follows: 22769# 20-40 sand in 222 bbls Lightning 17 frac fluid.

03/26/13 Convert to Injection Well

03/26/13 Conversion MITT Finalized - update (by detail)

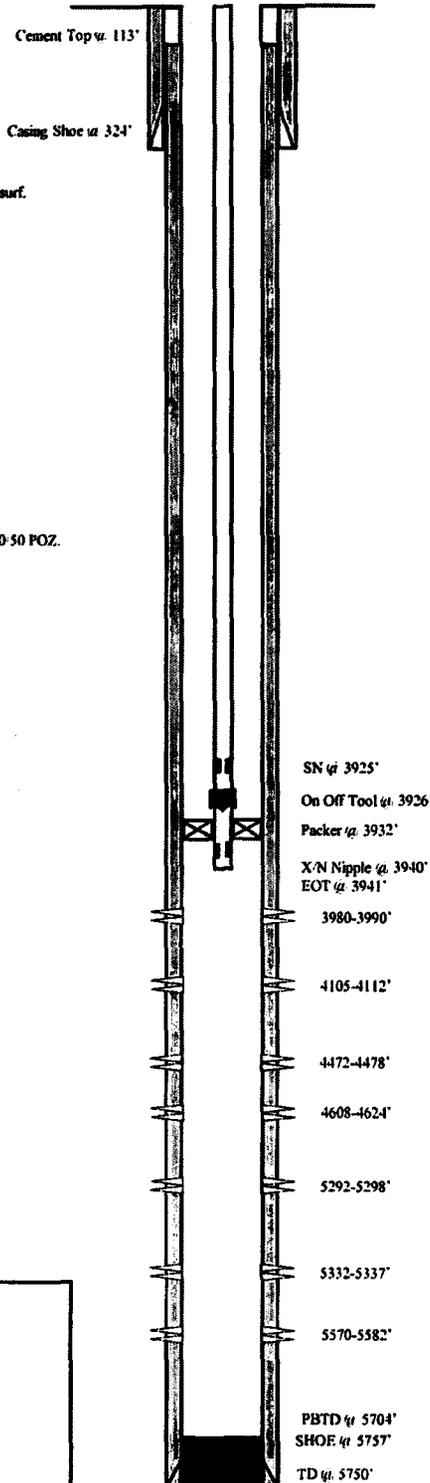

### PERFORATION RECORD

10/10/07	5570-5582'	4 JSPF	48 holes
10/10/07	5332-5337'	4 JSPF	20 holes
10/10/07	5292-5298'	4 JSPF	24 holes
10/10/07	4472-4478'	4 JSPF	24 holes
10/10/07	4105-4112'	4 JSPF	28 holes
10/10/07	3980-3990'	4 JSPF	40 holes
03/22/13	4608-4624'	3 JSPF	48holes

**NEWFIELD**

**FEDERAL 3-19-9-17**  
 454' FNL & 1851' FWL  
 NE/NW Section 19-T9S-R17E  
 Duchesne Co, Utah  
 API #43-013-33190; Lease # UTU-77369

Spud Date: 08/30/07  
 Put on Production: 10/15/07  
 GL: 5527' KB: 5539'

# FEDERAL 3-19-9-17

## Injection Wellbore Diagram

### SURFACE CASING


CSG SIZE: 8-5/8"  
 GRADE: J-55  
 WEIGHT: 24#  
 LENGTH: 7 jts. (312.48')  
 DEPTH LANDED: 324.33' KB  
 HOLE SIZE: 12-1/4"  
 CEMENT DATA: 160 sxs Class "G" cmt. est 6 bbls cmt to surf.

### PRODUCTION CASING

CSG SIZE: 5-1/2"  
 GRADE: J-55  
 WEIGHT: 15.5#  
 LENGTH: 144 jts. (5743.28')  
 DEPTH LANDED: 5756.53' KB  
 HOLE SIZE: 7-7/8"  
 CEMENT DATA: 300 sxs Prem. Lite II mixed & 450 sxs 50/50 POZ  
 CEMENT TOP: 113'

### TUBING

SIZE GRADE WT.: 2-7/8" J-55 6.5#  
 NO. OF JOINTS: 127 jts. (3913.1')  
 SEATING NIPPLE: 2-7/8" (1.10')  
 SN LANDED AT: 3925.1' KB  
 ON/OFF TOOL AT: 3926.2'  
 ARROW #1 PACKER CE AT: 3932'  
 XO 2-3/8" x 2-7/8" J-55 AT: 3935'  
 TBG PUP 2-3/8" J-55 AT: 3935.5'  
 X N NIPPLE AT: 3939.6'  
 TOTAL STRING LENGTH: EOT @ 3941.2'

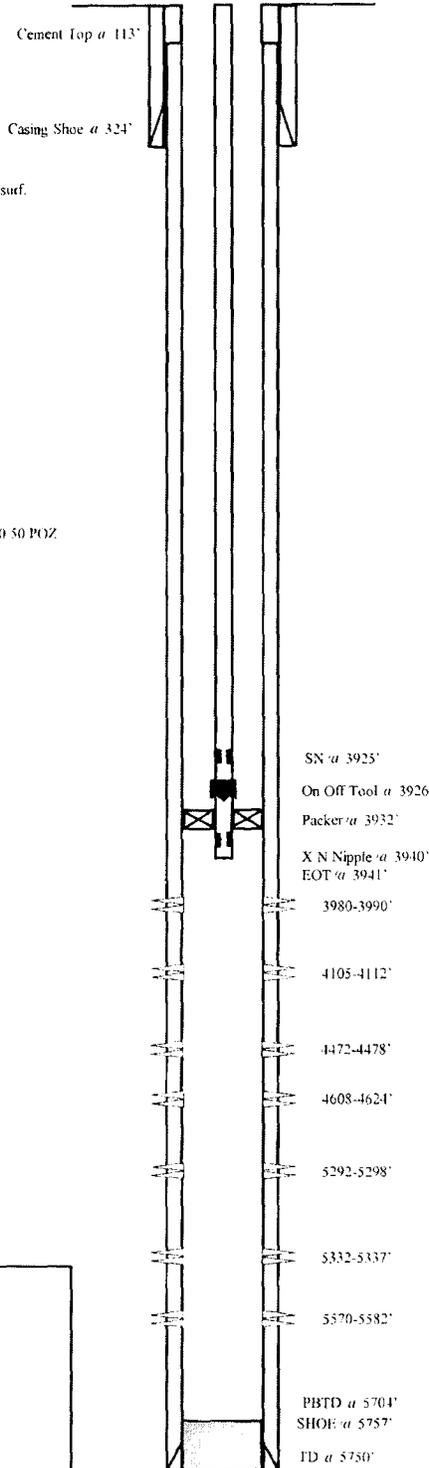

### FRAC JOB

10/10/07 5570-5582' **Frac CP5 sands as follows:**  
 35225# 20/40 sand in 436 bbls Lightning 17 frac fluid. Treated @ avg press of 1942 psi w avg rate of 24.8 BPM. ISIP 2019 psi. Calc flush: 5755 gal. Actual flush: 5061 gal.

10/10/07 5292-5337' **Frac CP.5 & CPI sands as follows:**  
 25321# 20/40 sand in 352 bbls Lightning 17 frac fluid. Treated @ avg press of 2390 psi w avg rate of 19.9 BPM. ISIP 2054 psi. Calc flush: 5290 gal. Actual flush: 4704 gal.

10/10/07 4472-4478' **Frac DI sands as follows:**  
 15151# 20/40 sand in 254 bbls Lightning 17 frac fluid. Treated @ avg press of 2012 psi w avg rate of 24.8 BPM. ISIP 1759 psi. Calc flush: 4470 gal. Actual flush: 3885 gal.

10/10/07 4105-4112' **Frac PB7 sands as follows:**  
 25019# 20/40 sand in 335 bbls Lightning 17 frac fluid. Treated @ avg press of 2423 psi w avg rate of 24.8 BPM. ISIP 3008 psi. Calc flush: 4103 gal. Actual flush: 3608 gal.

10/10/07 3980-3990' **Frac GB6 sands as follows:**  
 41613# 20/40 sand in 410 bbls Lightning 17 frac fluid. Treated @ avg press of 1648 psi w avg rate of 24.8 BPM. ISIP 1770 psi. Calc flush: 3980 gal. Actual flush: 3893 gal.

6/16/08 **HIT. Rod & tubing updated.**

03/25/13 **4608-4624' Frac C sands as follows:** 22769# 20/40 sand in 222 bbls Lightning 17 frac fluid.

03/26/13 **Convert to Injection Well**

03/26/13 **Conversion MIT Finalized - update tbg detail**

### PERFORATION RECORD

10/10/07	5570-5582'	4 JSPP	48 holes
10/10/07	5332-5337'	4 JSPP	20 holes
10/10/07	5292-5298'	4 JSPP	24 holes
10/10/07	4472-4478'	4 JSPP	24 holes
10/10/07	4105-4112'	4 JSPP	28 holes
10/10/07	3980-3990'	4 JSPP	40 holes
03/22/13	4608-4624'	3 JSPP	48 holes

**NEWFIELD**

**FEDERAL 3-19-9-17**  
 454' FNL & 1851' FWL  
 NE NW Section 19-19S-R17E  
 Duchesne Co, Utah  
 API #43-013-33190; Lease # UTU-77369
