

STATE OF UTAH
 DIVISION OF OIL, GAS AND MINING

| | |
|--|--|
| | 5. LEASE DESIGNATION AND SERIAL NO. 20G0005609 |
| APPLICATION FOR PERMIT TO DRILL, DEEPEN | 6. IF INDIAN, ALLOTTEE OR TRIBE NAME UTE |

| | |
|--|--------------------------------------|
| 1a. TYPE OF WORK DRILL <input type="checkbox"/> DEEPEN <input checked="" type="checkbox"/> RE-ENTER <input type="checkbox"/> | 7. UNIT AGREEMENT NAME N/A |
| 1b. TYPE OF WELL OIL <input checked="" type="checkbox"/> GAS <input type="checkbox"/> OTHER <input type="checkbox"/> SINGLE ZONE <input type="checkbox"/> MULTIPLE ZONE <input checked="" type="checkbox"/> | 8. FARM OR LEASE NAME |

| | |
|---|--|
| 2. NAME OF OPERATOR Newfield Production Company | 9. WELL NO. UTE TRIBAL 15-19-4-2 |
|---|--|

| | |
|---|---|
| 3. ADDRESS AND TELEPHONE NUMBER: Route #3 Box 3630, Myton, UT 84052 Phone: (435) 646-3721 | 10. FIELD AND POOL OR WILDCAT <i>South Myton Bench</i> |
|---|---|

| | |
|--|--|
| 4. LOCATION OF WELL (FOOTAGE) At Surface SW/SE 572480X 579' FSL 2106' FEL 40.11489 At proposed Producing Zone 44406454 -110.14949 | 11. QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: SW/SE Sec. 19, T4S, R2W |
|--|--|

| | | |
|---|-------------------------------|------------------------|
| 14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE* Approximately 12.3 miles southwest of Myton, UT | 12. County Duchesne | 13. STATE UT |
|---|-------------------------------|------------------------|

| | | |
|---|--|---|
| 15. DISTANCE FROM PROPOSED* LOCATION TO NEAREST PROPERTY OR LEASE LINE, FT. (Also to nearest drlg. unit line, if any) Approx. 534' f/lse line and NA' f/unit line | 16. NO. OF ACRES IN LEASE NA | 17. NO. OF ACRES ASSIGNED TO THIS WELL 40 |
|---|--|---|

| | | |
|---|------------------------------------|--|
| 18. DISTANCE FROM PROPOSED LOCATION* TO NEAREST WELL, DRILLING, COMPLETED, OR APPLIED FOR ON THIS LEASE, FT. NA | 19. PROPOSED DEPTH 6800' | 20. ROTARY OR CABLE TOOLS Rotary |
|---|------------------------------------|--|

| | |
|---|--|
| 21. ELEVATIONS (Show whether DF, RT, GR, etc.) 5498' GL | 22. APPROX. DATE WORK WILL START* 3rd Quarter 2007 |
|---|--|

23. PROPOSED CASING AND CEMENTING PROGRAM

| SIZE OF HOLE | SIZE OF CASING | WEIGHT/FOOT | SETTING DEPTH | QUANTITY OF CEMENT |
|-------------------------|----------------|--------------|---------------|--|
| 12 1/4 | 8 5/8 | 24# | 290' | 155 sx +/- 10% |
| 7 7/8 | 5 1/2 | 15.5# | TD | 275 sx lead followed by 450 sx tail |
| See Detail Below | | | | |

DESCRIBE PROPOSED PROGRAM: If proposal is to deepen, give date on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

***The actual cement volumes will be calculated off of the open hole logs, plus 15% excess:**

SURFACE PIPE - 155 sx Class G Cement +/I 10%, w/ 2% CaCl2 & 1/4#/sk Cello-flake
 Weight: 15.8 PPG YIELD: 1.17 Cu Ft/sk H2O Req: 5 gal/sk

LONG STRING - Lead: Premium Lite II Cement + 3lbs/sk BA-90 + 3% KCl + .25 lbs/sk Cello Flake + 2 lbs/sk Kol Seal + 10% Bentonite + .5% Sodium Metasilicate
 Weight: 11.0 PPG YIELD: 3.43 Cu Ft/sk H2O Req: 21.04 gal/sk

Tail: 50-50 Poz-Class G Cement + 3% KCl + .25 lbs/sk Cello Flake + 2% Bentonite + .3% Sodium Metasilicate
 Weight: 14.2 PPG YIELD: 1.59 Cu Ft/sk H2O Req: 7.88 gal/sk

| | | |
|--|-------------------------------------|------------------------|
| 24. Name & Signature <i>Mandie Crozier</i> Mandie Crozier | Title: Regulatory Specialist | Date: 5/11/2007 |
|--|-------------------------------------|------------------------|

(This space for State use only)



API Number Assigned: 43-013-33462 APPROVAL: _____

RECEIVED
MAY 16 2007
 DIV. OF OIL, GAS & MINING

T4S, R2W, U.S.B.&M.
 EAST - 80.06 (G.L.O.)

NEWFIELD PRODUCTION COMPANY

WELL LOCATION, UTE TRIBAL 15-19-4-2,
 LOCATED AS SHOWN IN THE SW 1/4 SE
 1/4 OF SECTION 19, T4S, R2W, U.S.B.&M.
 DUCHESNE COUNTY, UTAH.

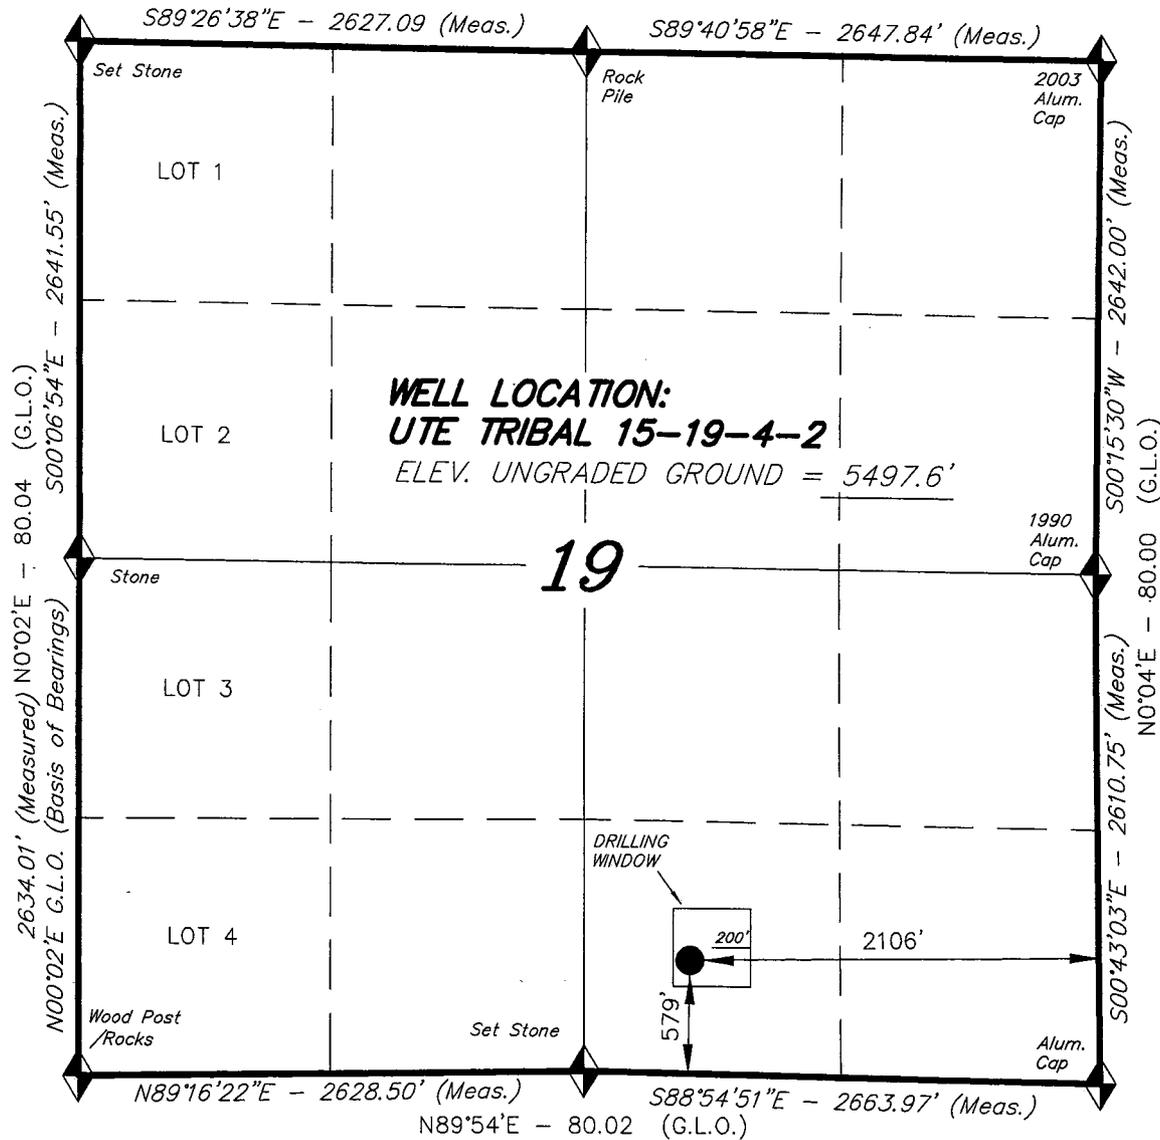

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
 PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
 MADE BY ME OR UNDER MY SUPERVISION AND THAT
 THE SAME ARE TRUE AND CORRECT TO THE BEST OF
 MY KNOWLEDGE AND BELIEF. No. 189377

Stacy W. Stewart
STACY W. STEWART
 REGISTERED LAND SURVEYOR
 REGISTRATION No. 189377
 STATE OF UTAH

◆ = SECTION CORNERS LOCATED

BASIS OF ELEV;
 U.S.G.S. 7-1/2 min QUAD (MYTON SW)

UTE TRIBAL 15-19-4-2
 (Surface Location) NAD 83
 LATITUDE = 40° 06' 53.64"
 LONGITUDE = 110° 09' 00.58"

TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
 (435) 781-2501

| | |
|----------------------------|-------------------|
| DATE SURVEYED: 03-08-07 | SURVEYED BY: C.M. |
| DATE DRAWN: 03-27-07 | DRAWN BY: T.C.J. |
| REVISED: | SCALE: 1" = 1000' |

NEWFIELD PRODUCTION COMPANY
UTE TRIBAL #15-19-4-2
SW/SE SECTION 19, T4S, R2W
DUCHESNE COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

| | |
|-------------|-----------|
| Uinta | 0 – 1600' |
| Green River | 1600' |
| Wasatch | 6800' |

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation 1600' – 6800' – Oil

4. **PROPOSED CASING PROGRAM:**

Surface Casing: 8-5/8" J-55 24# w/ST&C collars; set at 290' (New)
Production Casing: 5-1/2" J-55, 15.5# w/LT&C collars; set at TD (New or used, inspected).

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

A fresh water/polymer system will be utilized to drill the well. If necessary, to control formation fluids, the system will be weighted with the addition of bentonite gel, and if conditions warrant, barite. This fresh water system typically will contain Total Dissolved Solids (TDS) of less than 3000 PPM. Neither potassium chloride nor chromates will be utilized in the fluid system. The anticipated mud weight is 8.4 ppg and weighted as necessary for gas control.

AIR DRILLING

In the event that the proposed location is to be "Air Drilled", Newfield requests a variance to regulations requiring a straight run blooie line. Newfield proposes that the flowline will contain two (2) 90-degree turns. Newfield also requests a variance to regulations requiring an automatic igniter or continuous pilot light on the blooie line. Newfield requests authorization to ignite as needed, and the flowline at 80'.

Newfield Production Company requests that the spark arrest, exhaust, or water cooled exhaust be waived under the Special Drilling Operations of Onshore Order #2.

MUD PROGRAM

Surface – 3200’
3200’ – TD’

MUD TYPE

fresh water system
fresh water system

From surface to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCL substitute additive. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite. No chromate additives will be used in the mud system.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 290’ +/-, and a Compensated Neutron-Formation Density Log from TD to 3500’ +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered; or that any other abnormal hazards such as H₂S will be encountered in this area.

10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the third quarter of 2007, and take approximately seven (7) days from spud to rig release.

NEWFIELD PRODUCTION COMPANY
UTE TRIBAL #15-19-4-2
SW/SE SECTION 19, T4S, R2W
DUCHESNE COUNTY, UTAH

THIRTEEN POINT SURFACE PROGRAM

1. EXISTING ROADS

See attached **Topographic Map "A"**

To reach Newfield Production Company well location site Ute Tribal 15-19-4-2 located in the SW¼ SE¼ Section 19, T4S, R2W, S.L.B. & M., Duchesne County, Utah:

Proceed in a southwesterly direction out of Myton, Utah along Highway 40 approximately 1.9 miles to the junction of this highway and Utah State Highway 53; proceed southwesterly along Utah State Highway 53 approximately 1.7 miles to its junction with an existing road to the southwest; proceed southwesterly approximately 4.6 miles to its junction with an existing road to the west; proceed southwesterly approximately 2.2 miles to its junction with an existing road to the northeast; proceed northeasterly approximately 1.1 miles to its junction with the beginning of the proposed access road to the northeast; proceed northeasterly along the proposed access road approximately 4,650' to the propose well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

Approximately 4,650' of access road is proposed. See attached **Topographic Map "B"**.

The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%.

There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to **EXHIBIT B**.

4. **LOCATION OF EXISTING AND/OR PROPOSED FACILITIES**

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck for drilling purposes from the following water sources:

Johnson Water District
Water Right: 43-10136

Neil Moon Pond
Water Right: 43-11787

Maurice Harvey Pond
Water Right: 47-1358

Newfield Collector Well
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

8. **ANCILLARY FACILITIES:**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT:**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) **Producing Location**

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) **Dry Hole Abandoned Location**

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP:** Moon Land and Livestock LTD Partnership, Duchesne, Utah. See attached Surface Use Agreement.

12. **OTHER ADDITIONAL INFORMATION:**

- a) Newfield Production Company is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, Newfield is to immediately stop work that might further disturb such materials and contact the Authorized Officer.
- b) Newfield Production will control noxious weeds along rights-of-way for roads, pipelines, well sites or other applicable facilities. On State administered land it is required that a Pesticide Use Proposal shall be submitted and given approval prior to the application of herbicides or other possible hazardous chemicals.
- c) Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on State Lands after the conclusion of drilling operations or at any other time without State authorization. However, if State authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

The Archaeological Report Waiver for this location is attached.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the Ute Tribal 15-19-4-2, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Ute

Tribal 15-19-4-2 Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

The State office as well as the Ute Tribe Energy and Mineral Department shall be notified upon site completion prior to moving on the drilling rig.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

Representative

Name: Kim Kettle
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721


Certification

Please be advised that Newfield Production Company is considered to be the operator of well #15-19-4-2, SW/SE Section 19, T4S, R2W, Duchesne County, Utah and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by US Specialty Insurance #B002792.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

5/11/07

Date


Mandie Crozier
Regulatory Specialist
Newfield Production Company

MEMORANDUM
of
EASEMENT, RIGHT-OF-WAY
and
SURFACE USE AGREEMENT

This Easement, Right-of-Way and Surface Use Agreement ("Agreement") is entered into this 2nd day of May, 2007 by and between **Moon Land & Livestock LTD Partnership whose address is HC 64 Box 167 Duchesne, Utah 84021** ("Surface Owner," whether one or more) and Newfield Production Company, a Texas corporation ("NEWFIELD"), with offices at 1401 17th Street, Suite #1000, Denver, Colorado 80202, covering certain lands, (the "Lands") situated in Duchesne County, Utah described as follows:

Township 4 South, Range 2 West
SWSE Section 19

Duchesne County, Utah

being, 40 acres more or less,

and associated roads and pipeline routes beginning at each wellsite and traversing the lands as shall be agreed upon prior to the construction of same.

For and in consideration of the sum of ten dollars (\$10.00), and other valuable consideration, the receipt and sufficiency of which are hereby acknowledged, the undersigned hereby agree to the terms and provisions set forth as follows:

1. Compensation for Well: Release of All Claims

NEWFIELD shall pay to Surface Owner the sum as set forth in and according to the terms of that certain Letter Agreement for Easement, Right-of Way and Surface Use by and between Surface Owner and NEWFIELD, dated May 02, 2007, as full payment and satisfaction for any and all detriment, depreciation, injury or damage of any nature to the Lands or growing crops thereon that may occur as a result of NEWFIELD's drilling or completion operations or its continuing activities for the production or transportation of oil, gas, or other hydrocarbons or products associated with the foregoing including, but not limited to, surface use, access, pipelines, gathering lines, pipeline interconnections, and any and all other reasonable or customary uses of land related to said operations or activities.

2. Grant of Right of Way and Easement


Surface Owner hereby grants, bargains, leases, assigns, and conveys to NEWFIELD an easement and right-of-way for the purpose of construction, using and maintaining access roads, locations for surface equipment and subsurface gathering lines for each well drilled upon the Lands, pipelines, and pipeline interconnections for two years from date of this agreement and so long thereafter as NEWFIELD's oil and gas leases remain in effect.

This Agreement shall be binding upon the respective heirs, executors, administrators, successors, and assigns of the undersigned.

These Parties hereto have executed this document effective as of the day first above written.

MOON LAND & LIVESTOCK LTD PARTNERSHIP

NEWFIELD PRODUCTION COMPANY

By: 

Russell Moon, Surface Owner

By: _____
Gary D. Packer, President

STATE OF UTAH)
)ss
COUNTY OF _____)

This instrument was acknowledged before me this _____ day of _____, 2007 by **Russell Moon, on behalf of Moon Land & Livestock LTD Partnership.**

Witness my hand and official seal.

Notary Public

My commission expires _____

STATE OF COLORADO)
)ss
COUNTY OF Denver)

This instrument was acknowledged before me this _____, 2007 by **Gary D. Packer, as President of Newfield Production Company, a Texas corporation, on behalf of the corporation.**

Witness my hand and official seal.

Notary Public

My commission expires _____


EXHIBIT D

Ute Tribe 15-19-4-2
SWSE Sec. 19, T4S, R2W

CULTURAL REPORT WAIVER

For the above referenced location; Moon Land & Livestock LTD Partnership, Russell Moon, the Private Surface Owner. (Having a Surface Owner Agreement with Newfield Production Company)

Russell Moon, representing this entity does agree to waive the request from the State of Utah and Bureau of Land Management for an Archaeological/Cultural Survey. This waiver hereby releases Newfield Production Company from this request.


Russell Moon Date
Private Surface Owner


Brad Meham Date
Newfield Production Company


NEW WELD PRODUCTION COMPANY

UTE TRIBAL 15-19-4-2
Section 19, T4S, R2W, U.S.B.&M.



Keep Material out of Existing Drainage

PROPOSED ACCESS ROAD (Max. 6% Grade)

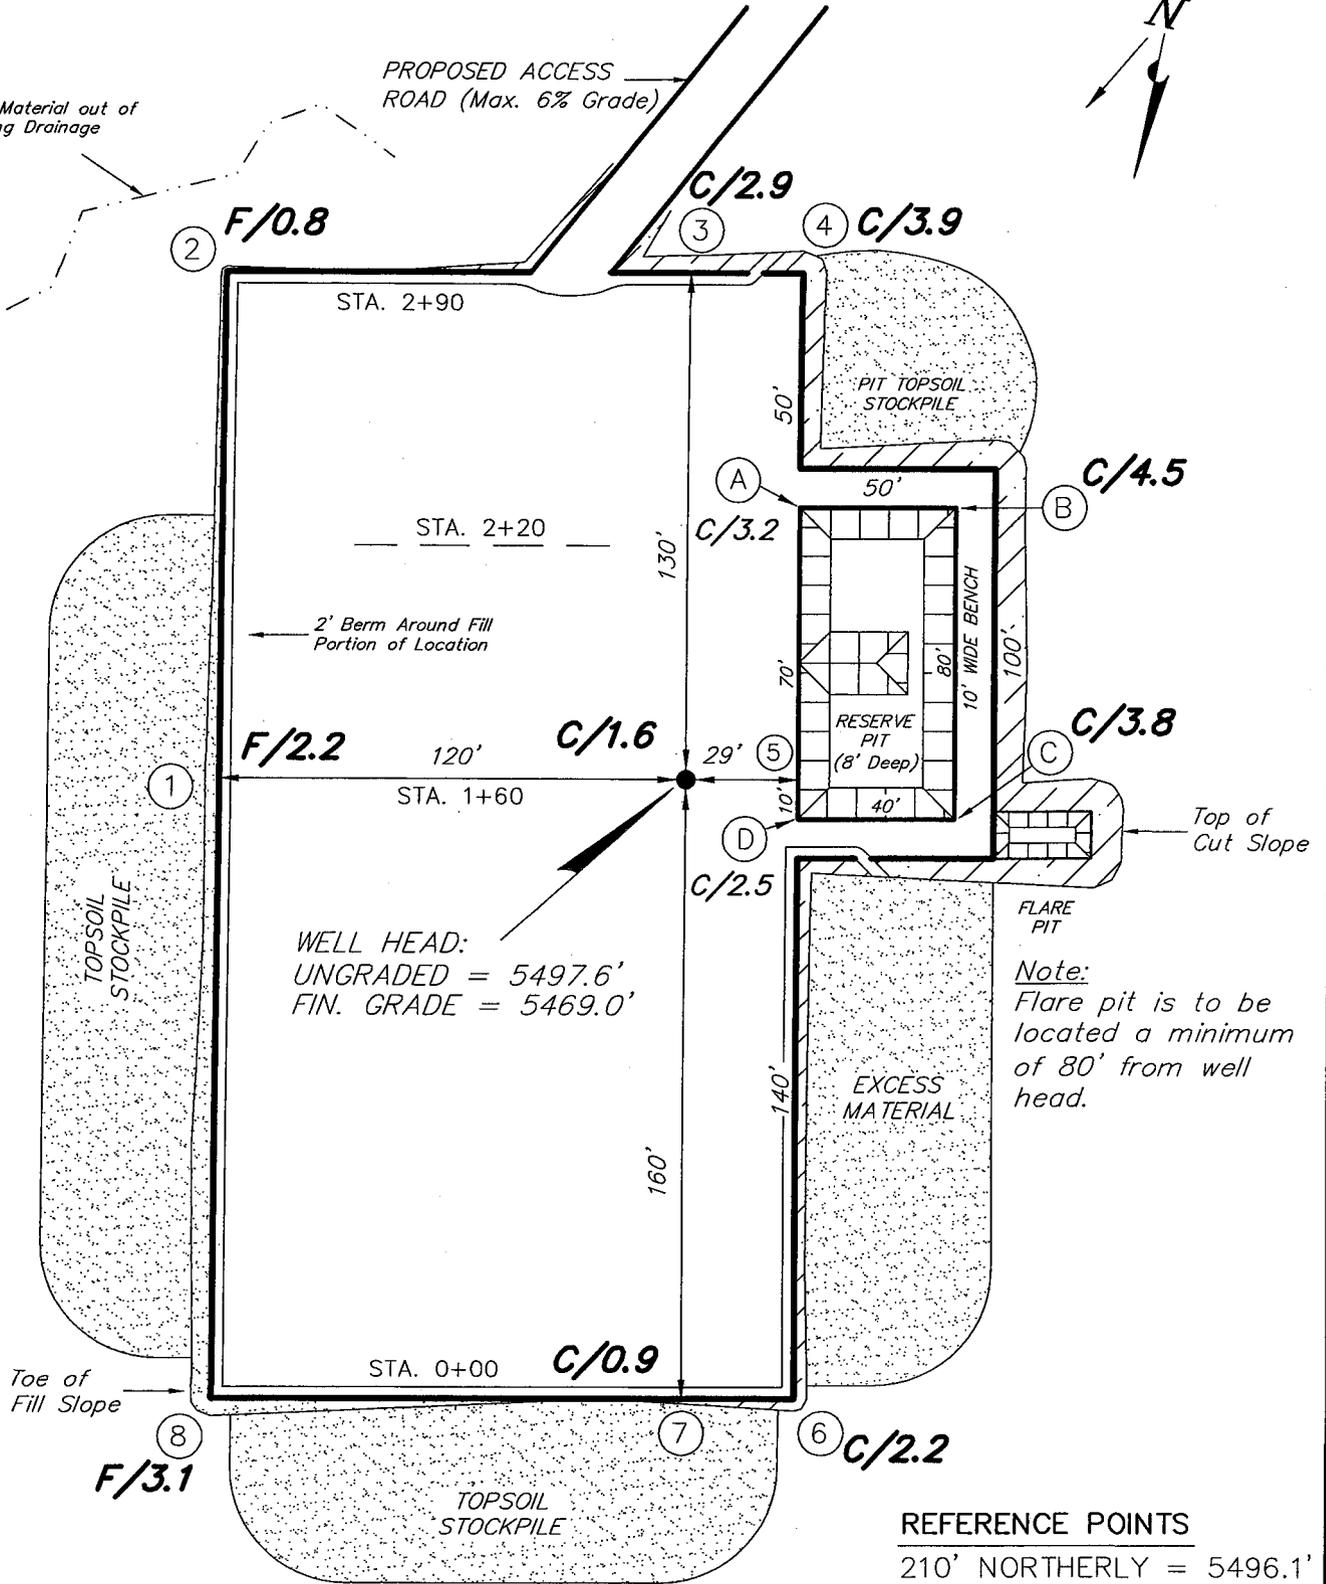

WELL HEAD:
UNGRADED = 5497.6'
FIN. GRADE = 5469.0'

Note:
Flare pit is to be located a minimum of 80' from well head.

REFERENCE POINTS





| | |
|----------------|-----------|
| 210' NORTHERLY | = 5496.1' |
| 260' NORTHERLY | = 5497.3' |
| 170' EASTERLY | = 5491.9' |
| 220' EASTERLY | = 5490.6' |

| | | |
|-------------------|-----------------|--|
| SURVEYED BY: C.M. | SCALE: 1" = 50' | <p>Tri State Land Surveying, Inc. 180 NORTH VERNAL AVE. VERNAL, UTAH 84078</p> |
| DRAWN BY: T.C.J. | DATE: 03-27-07 | |

NEWFIELD PRODUCTION COMPANY

CROSS SECTIONS

UTE TRIBAL 15-19-4-2

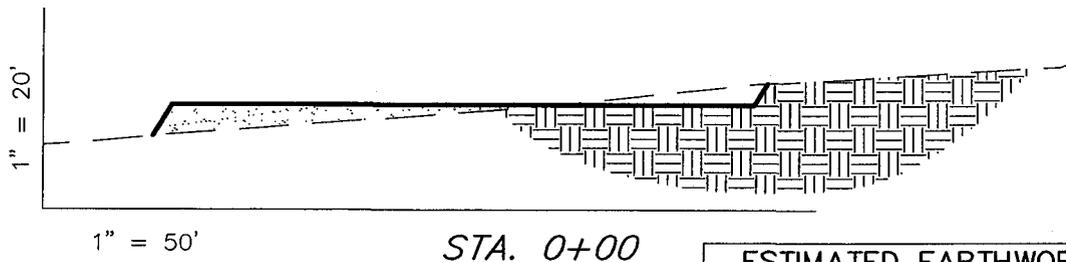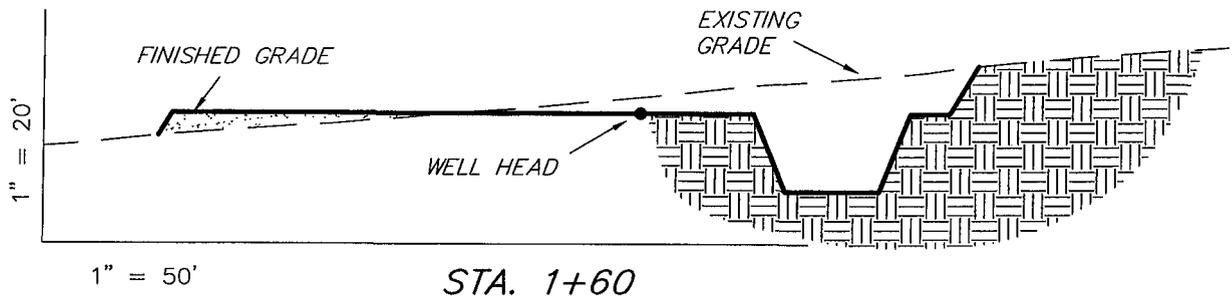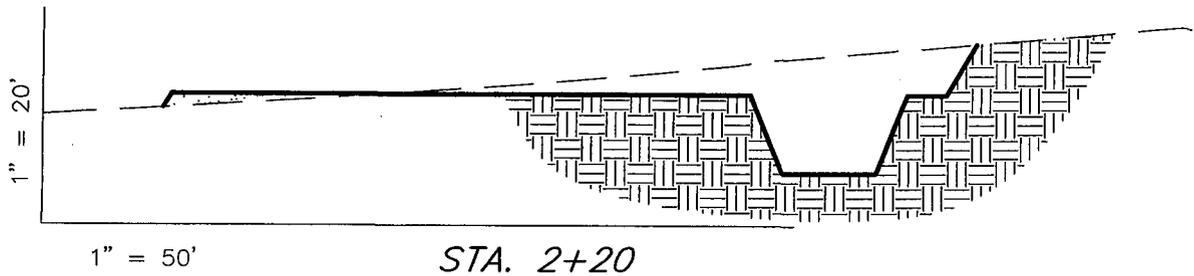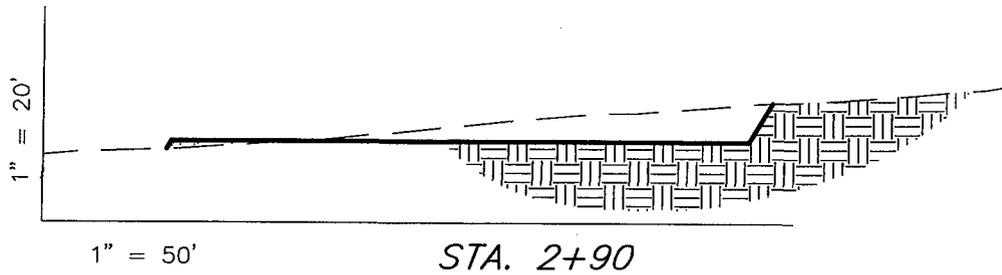

| ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards) | | | | |
|---|-------|-------|--|--------|
| ITEM | CUT | FILL | 6" TOPSOIL | EXCESS |
| PAD | 1,560 | 1,560 | Topsoil is not included in Pad Cut | 0 |
| PIT | 640 | 0 | | 640 |
| TOTALS | 2,200 | 1,560 | 980 | 640 |

NOTE:
UNLESS OTHERWISE NOTED
ALL CUT/FILL SLOPES ARE
AT 1.5:1

SURVEYED BY: C.M.

SCALE: 1" = 50'


DRAWN BY: T.C.J.

DATE: 03-27-07

Tri State
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078
 (435) 781-2501

NEWFIELD PRODUCTION COMPANY

TYPICAL RIG LAYOUT UTE TRIBAL 15-19-4-2

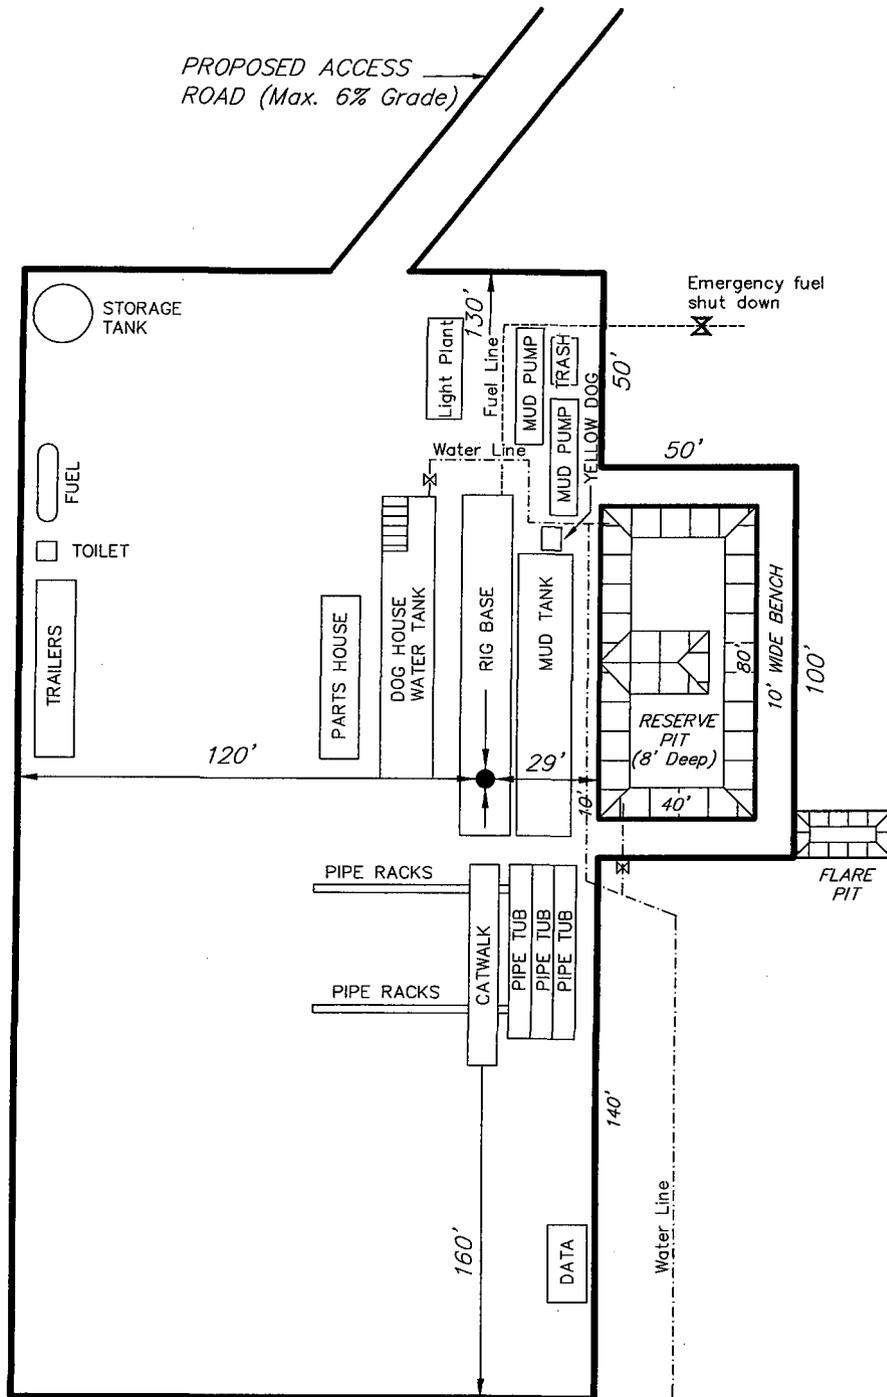


SURVEYED BY: C.M.

SCALE: 1" = 50'

DRAWN BY: T.C.J.

DATE: 03-27-07

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

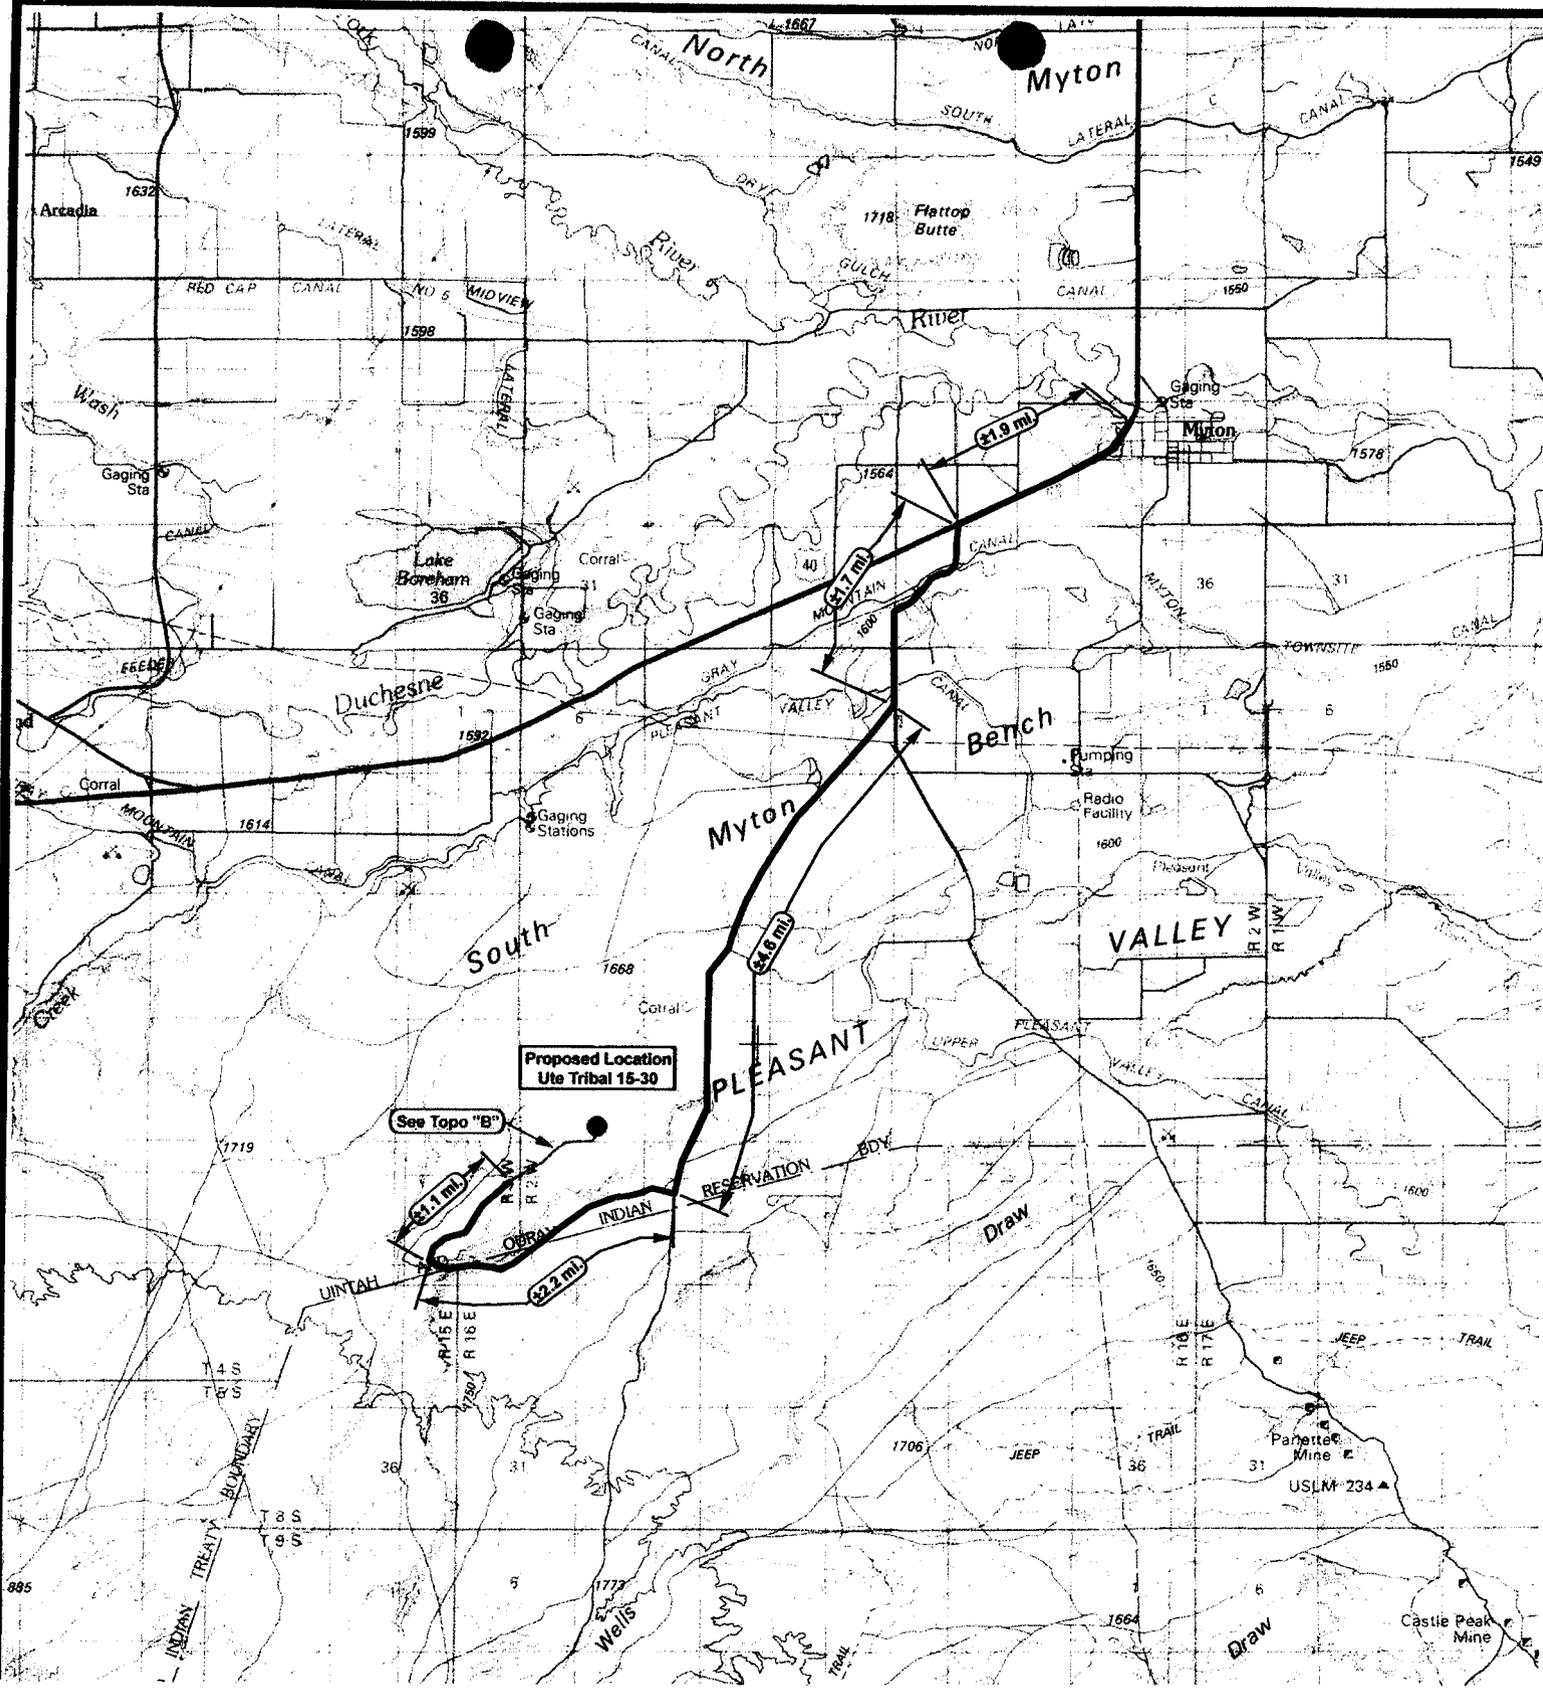

**Proposed Location
Ute Tribal 15-30**

See Topo "B"

1.1 ml

2.2 ml

4.8 ml

11.9 ml



NEWFIELD
Exploration Company

**Ute Tribal 15-19-4-2
SEC. 19, T4S, R2W, U.S.B.&M.**




Tri-State
Land Surveying Inc.
(435) 781-2501
38 West 100 North Vernal, Utah 84078

SCALE: 1" = 100,000
DRAWN BY: mw
DATE: 03-29-2007

Legend
Existing Road
Proposed Access

TOPOGRAPHIC MAP

"A"

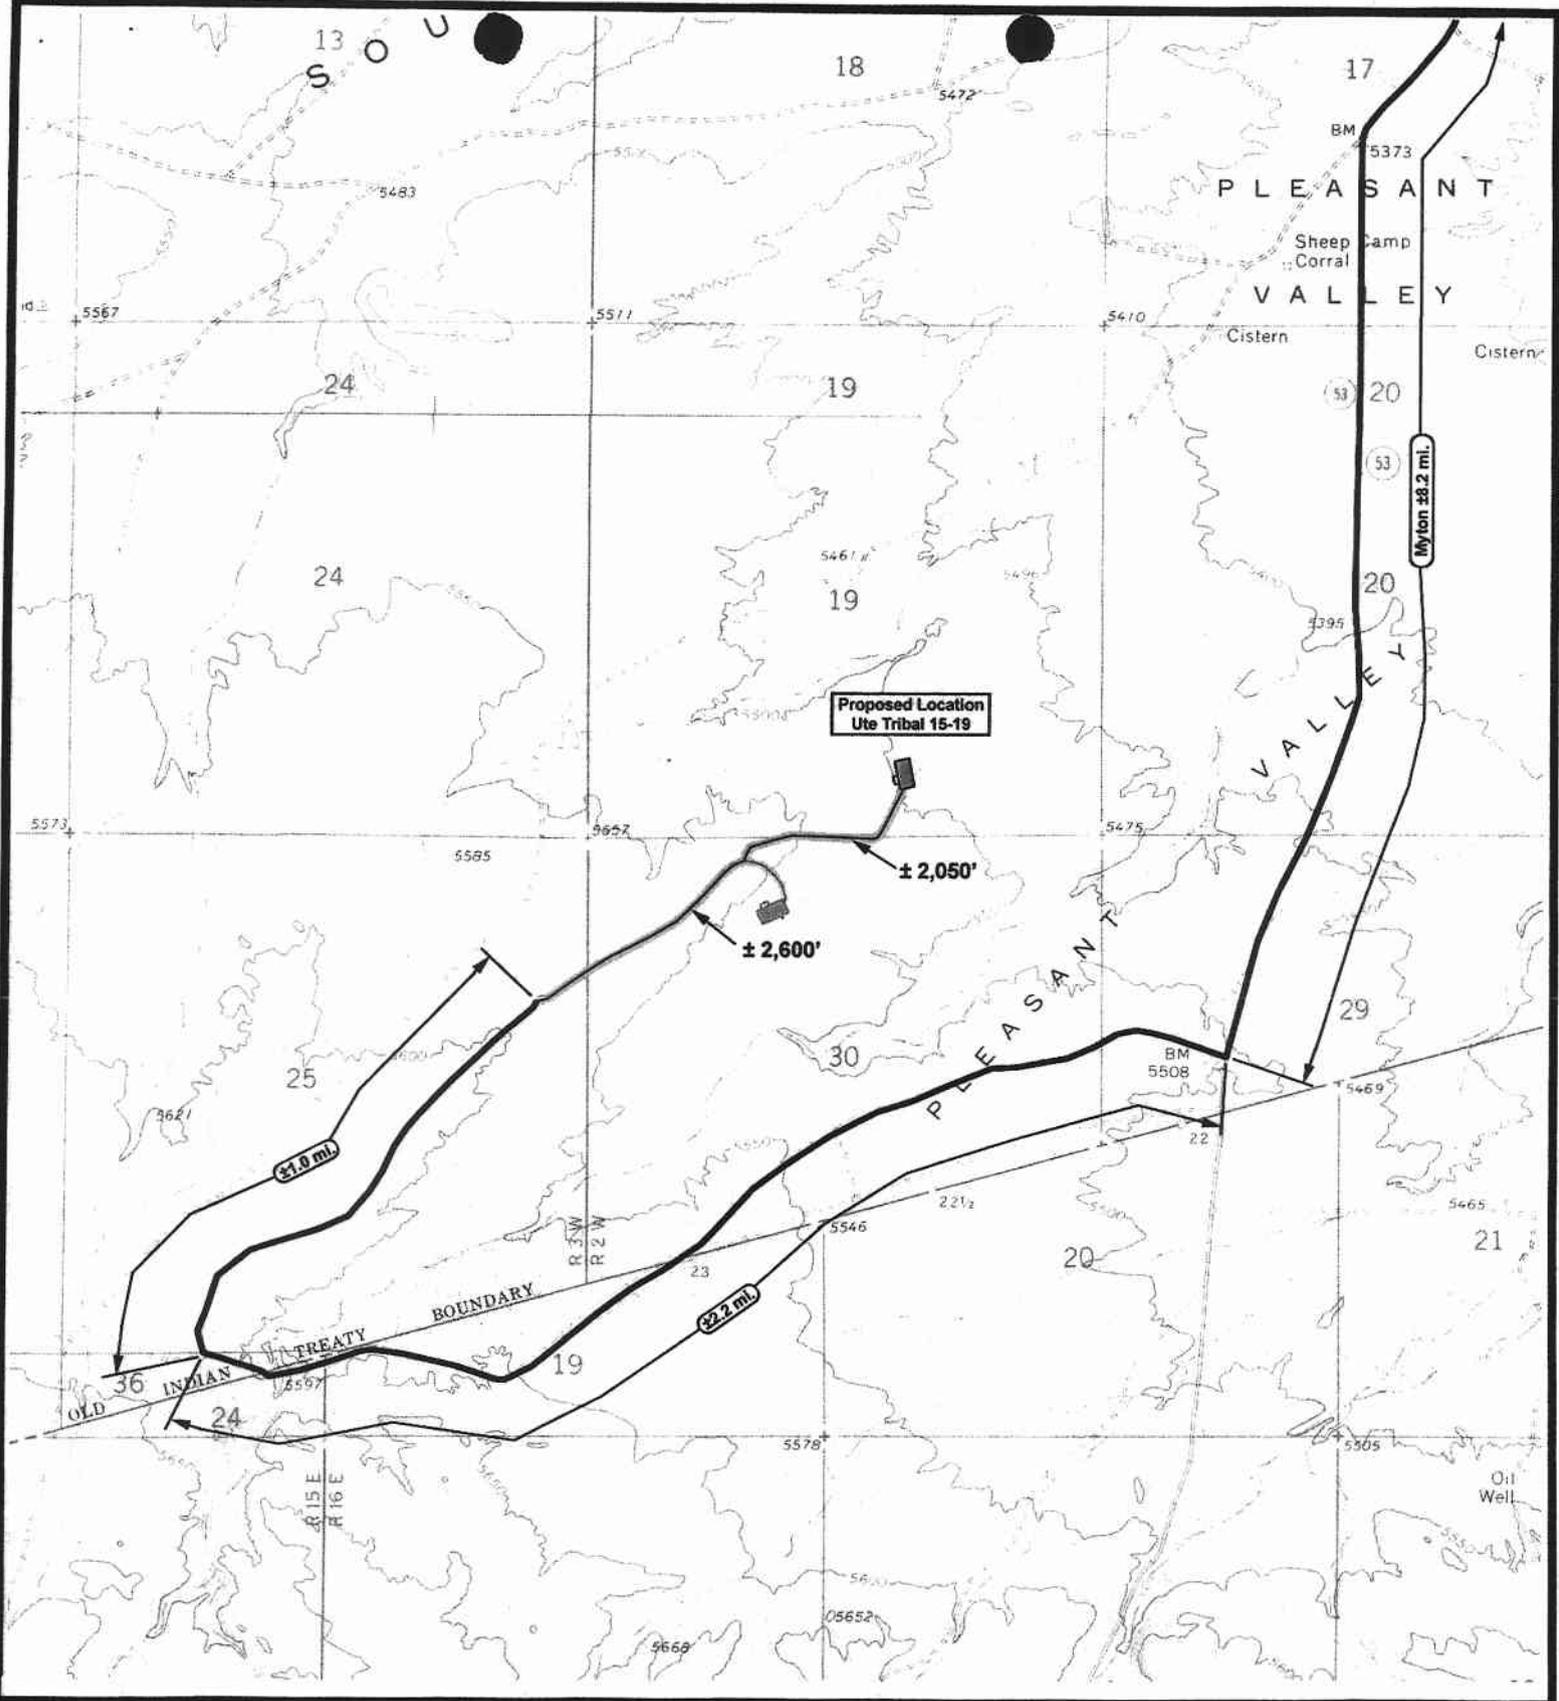

NEWFIELD
Exploration Company

Ute Tribal 15-19-4-2
SEC. 19, T4S, R2W, U.S.B.&M.

Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2000'
DRAWN BY: mw
DATE: 03-29-2007

Legend

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP

"B"

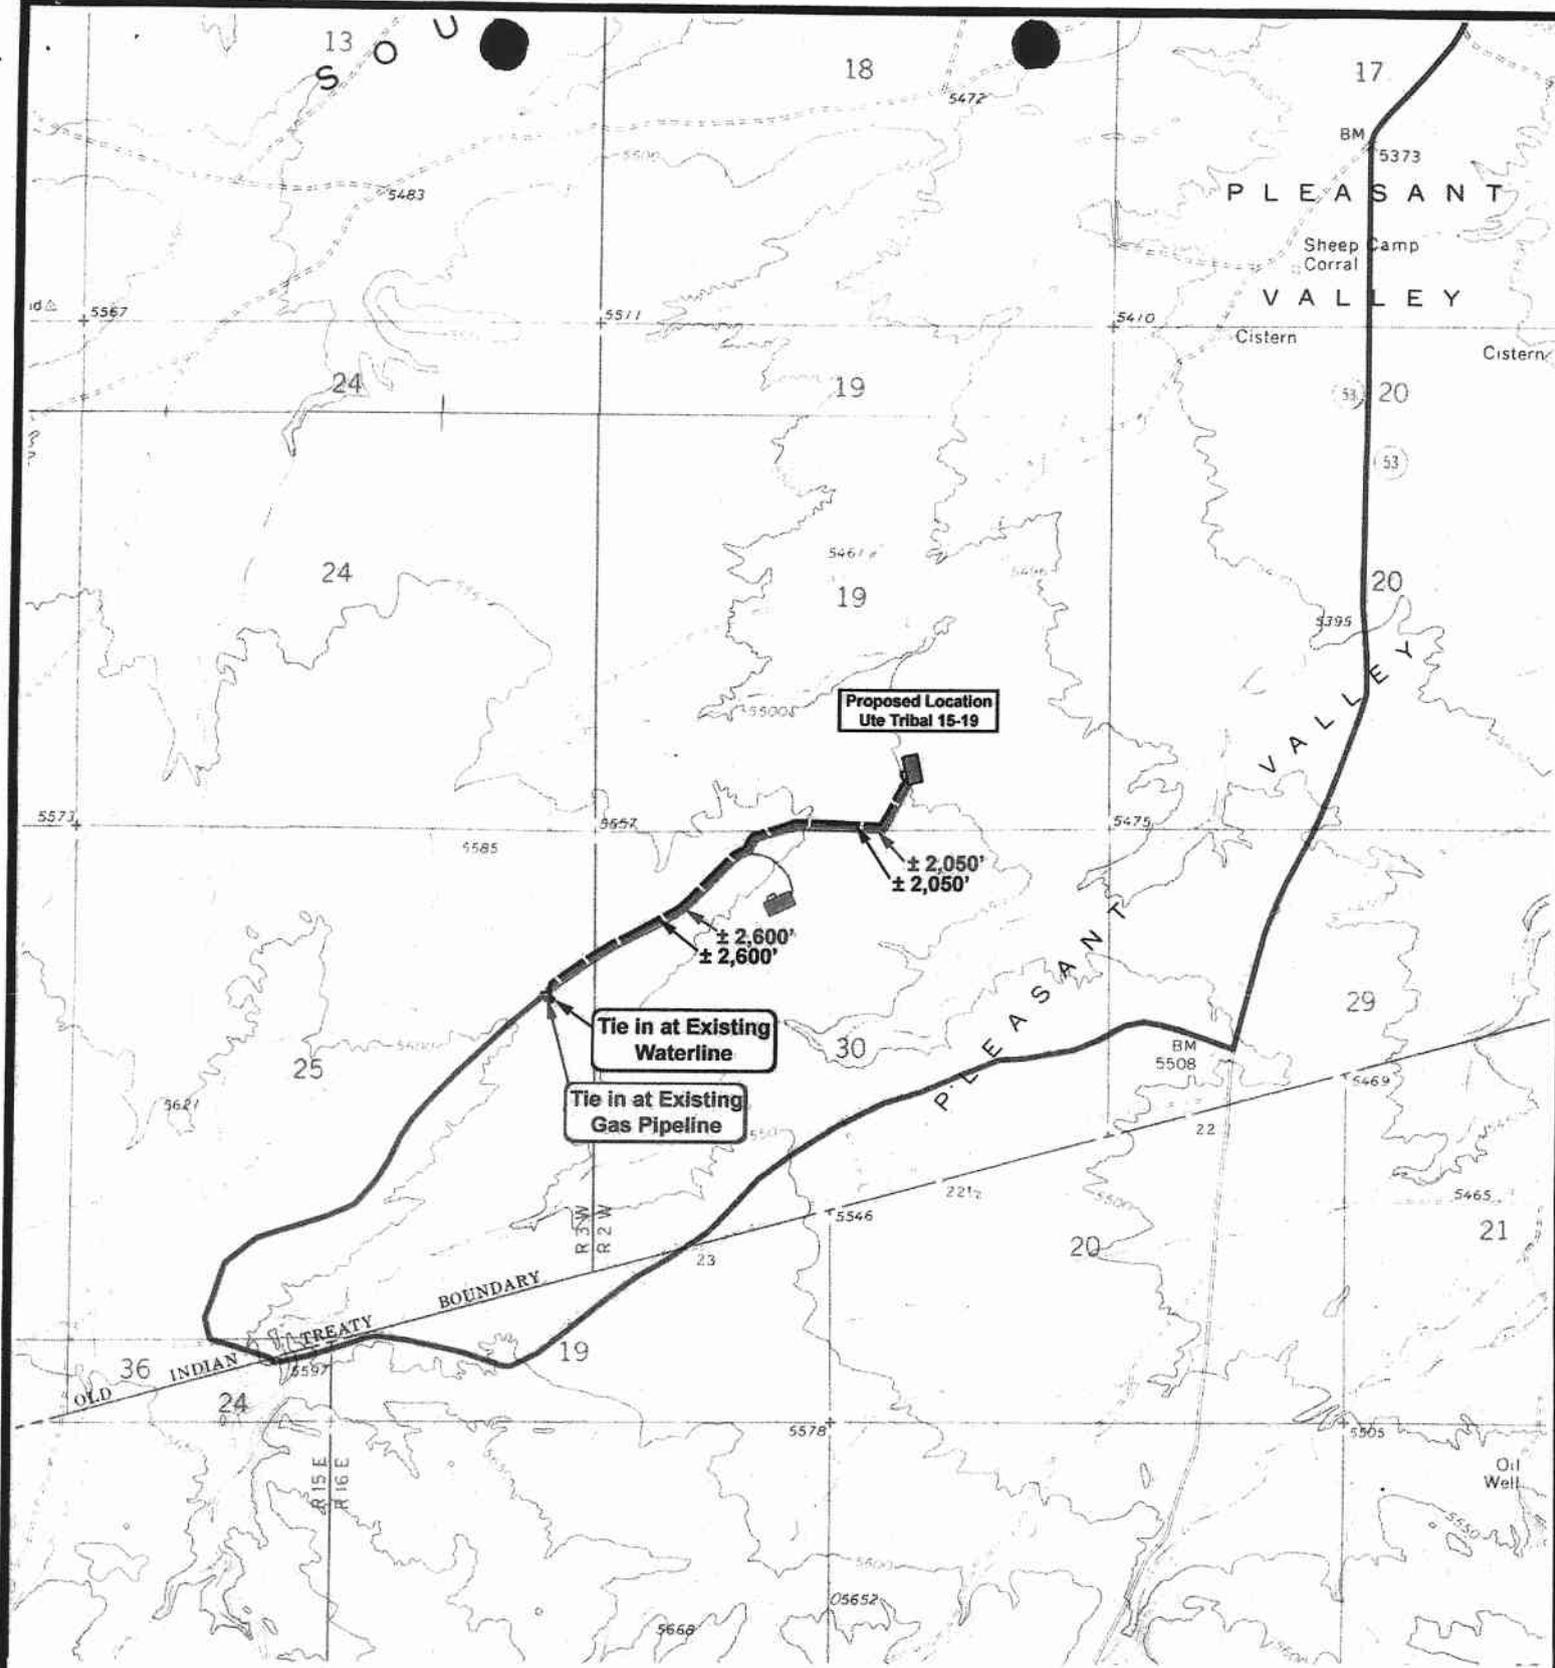

NEWFIELD
Exploration Company

Ute Tribal 15-19-4-2
SEC. 19, T4S, R2W, U.S.B.&M.



Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078


SCALE: 1" = 2000'
DRAWN BY: mw
DATE: 03-29-2007

Legend

- Roads
- Proposed Gas Line
- Proposed Water Line

TOPOGRAPHIC MAP

"C"

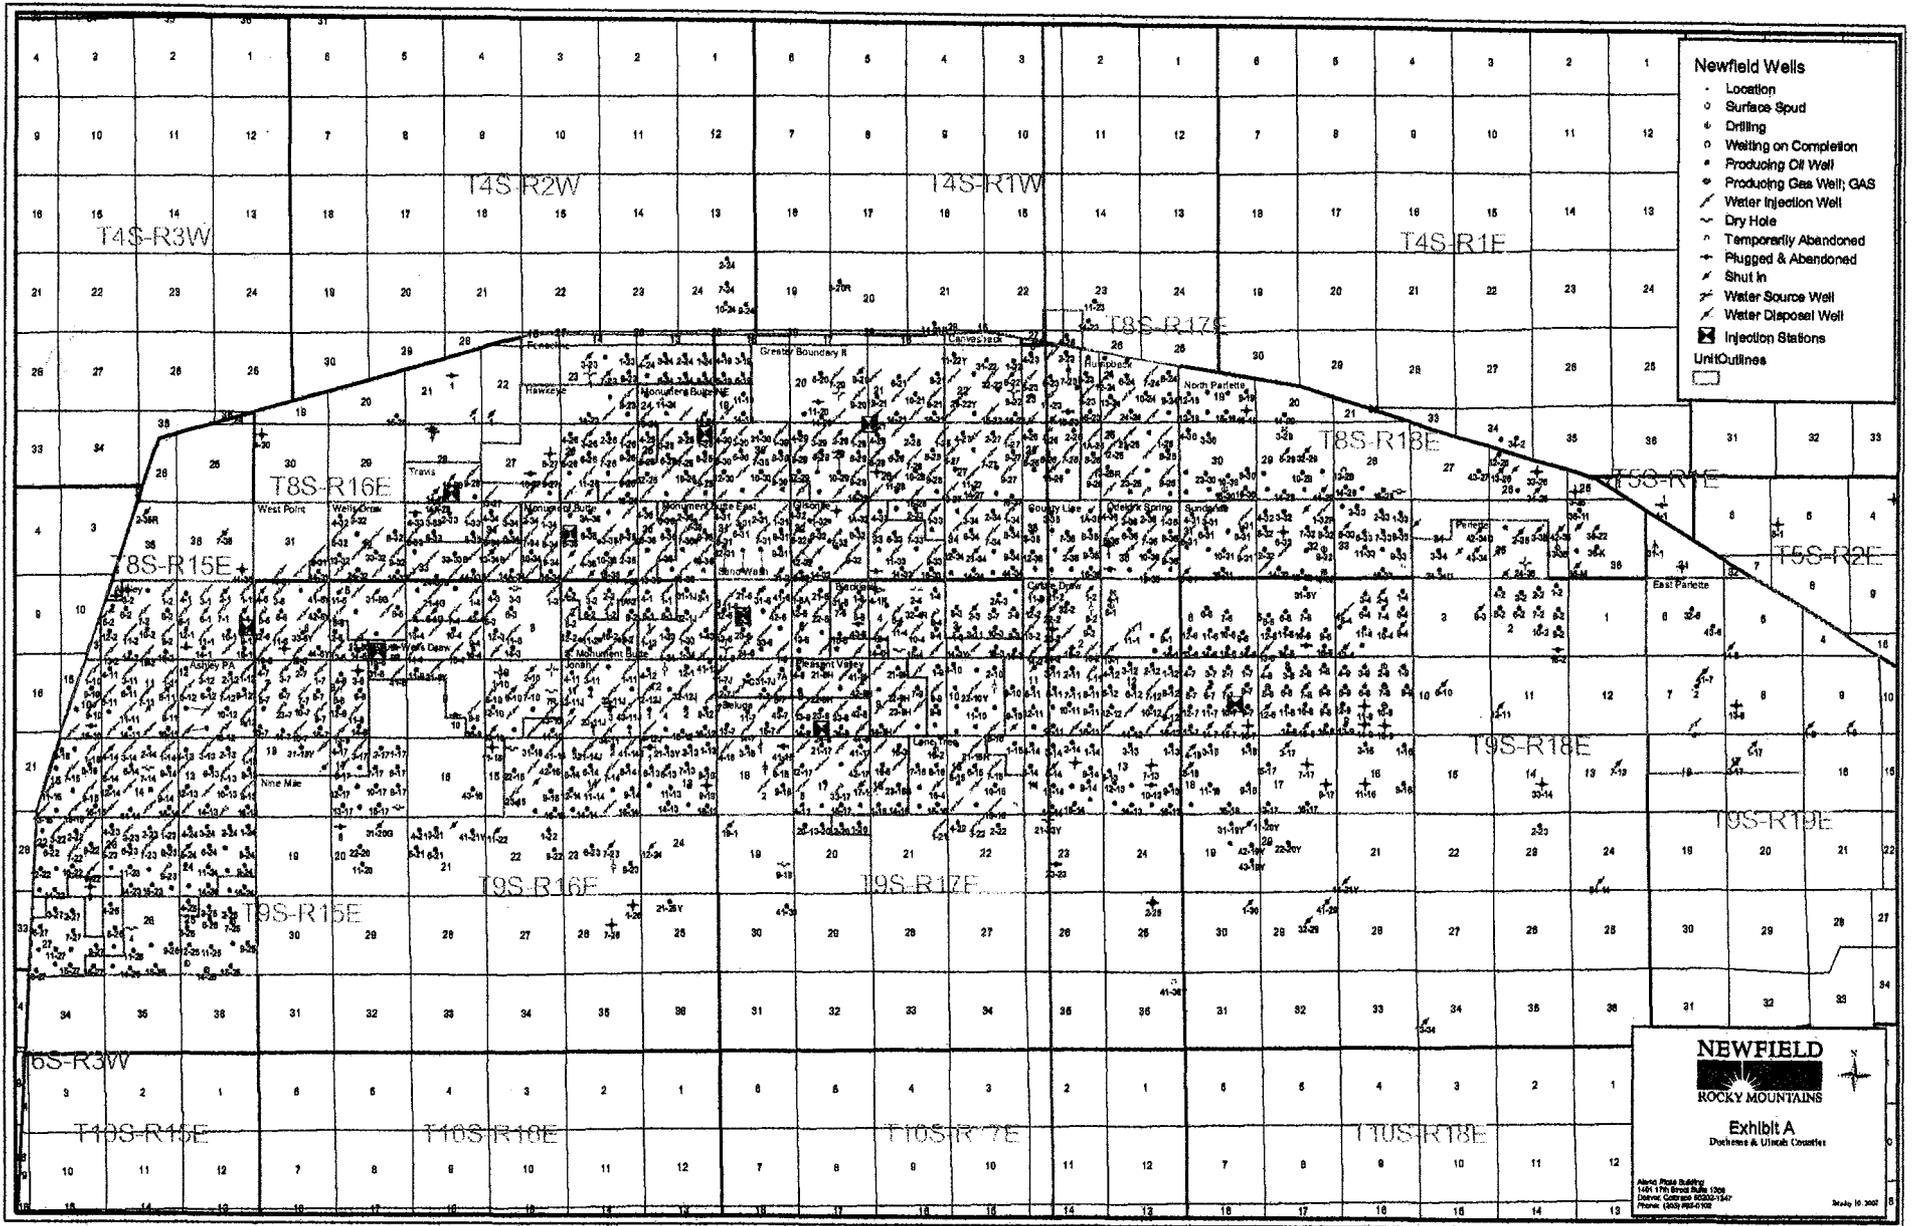


- Newfield Wells**
- Location
 - Surface Spud
 - ⊕ Drilling
 - Waiting on Completion
 - Producing Oil Well
 - Producing Gas Well, GAS
 - Water Injection Well
 - Dry Hole
 - Temporarily Abandoned
 - Plugged & Abandoned
 - Shut In
 - Water Source Well
 - Water Disposal Well
 - ⊠ Injection Stations
 - Unit Outlines

NEWFIELD
ROCKY MOUNTAINS

Exhibit A
 Discoveries & Ultimate Reserves

Maple Ridge Building
 1001 17th Street Suite 1700
 Denver, Colorado 80202-1747
 Phone: (303) 733-1100

May 10, 2007

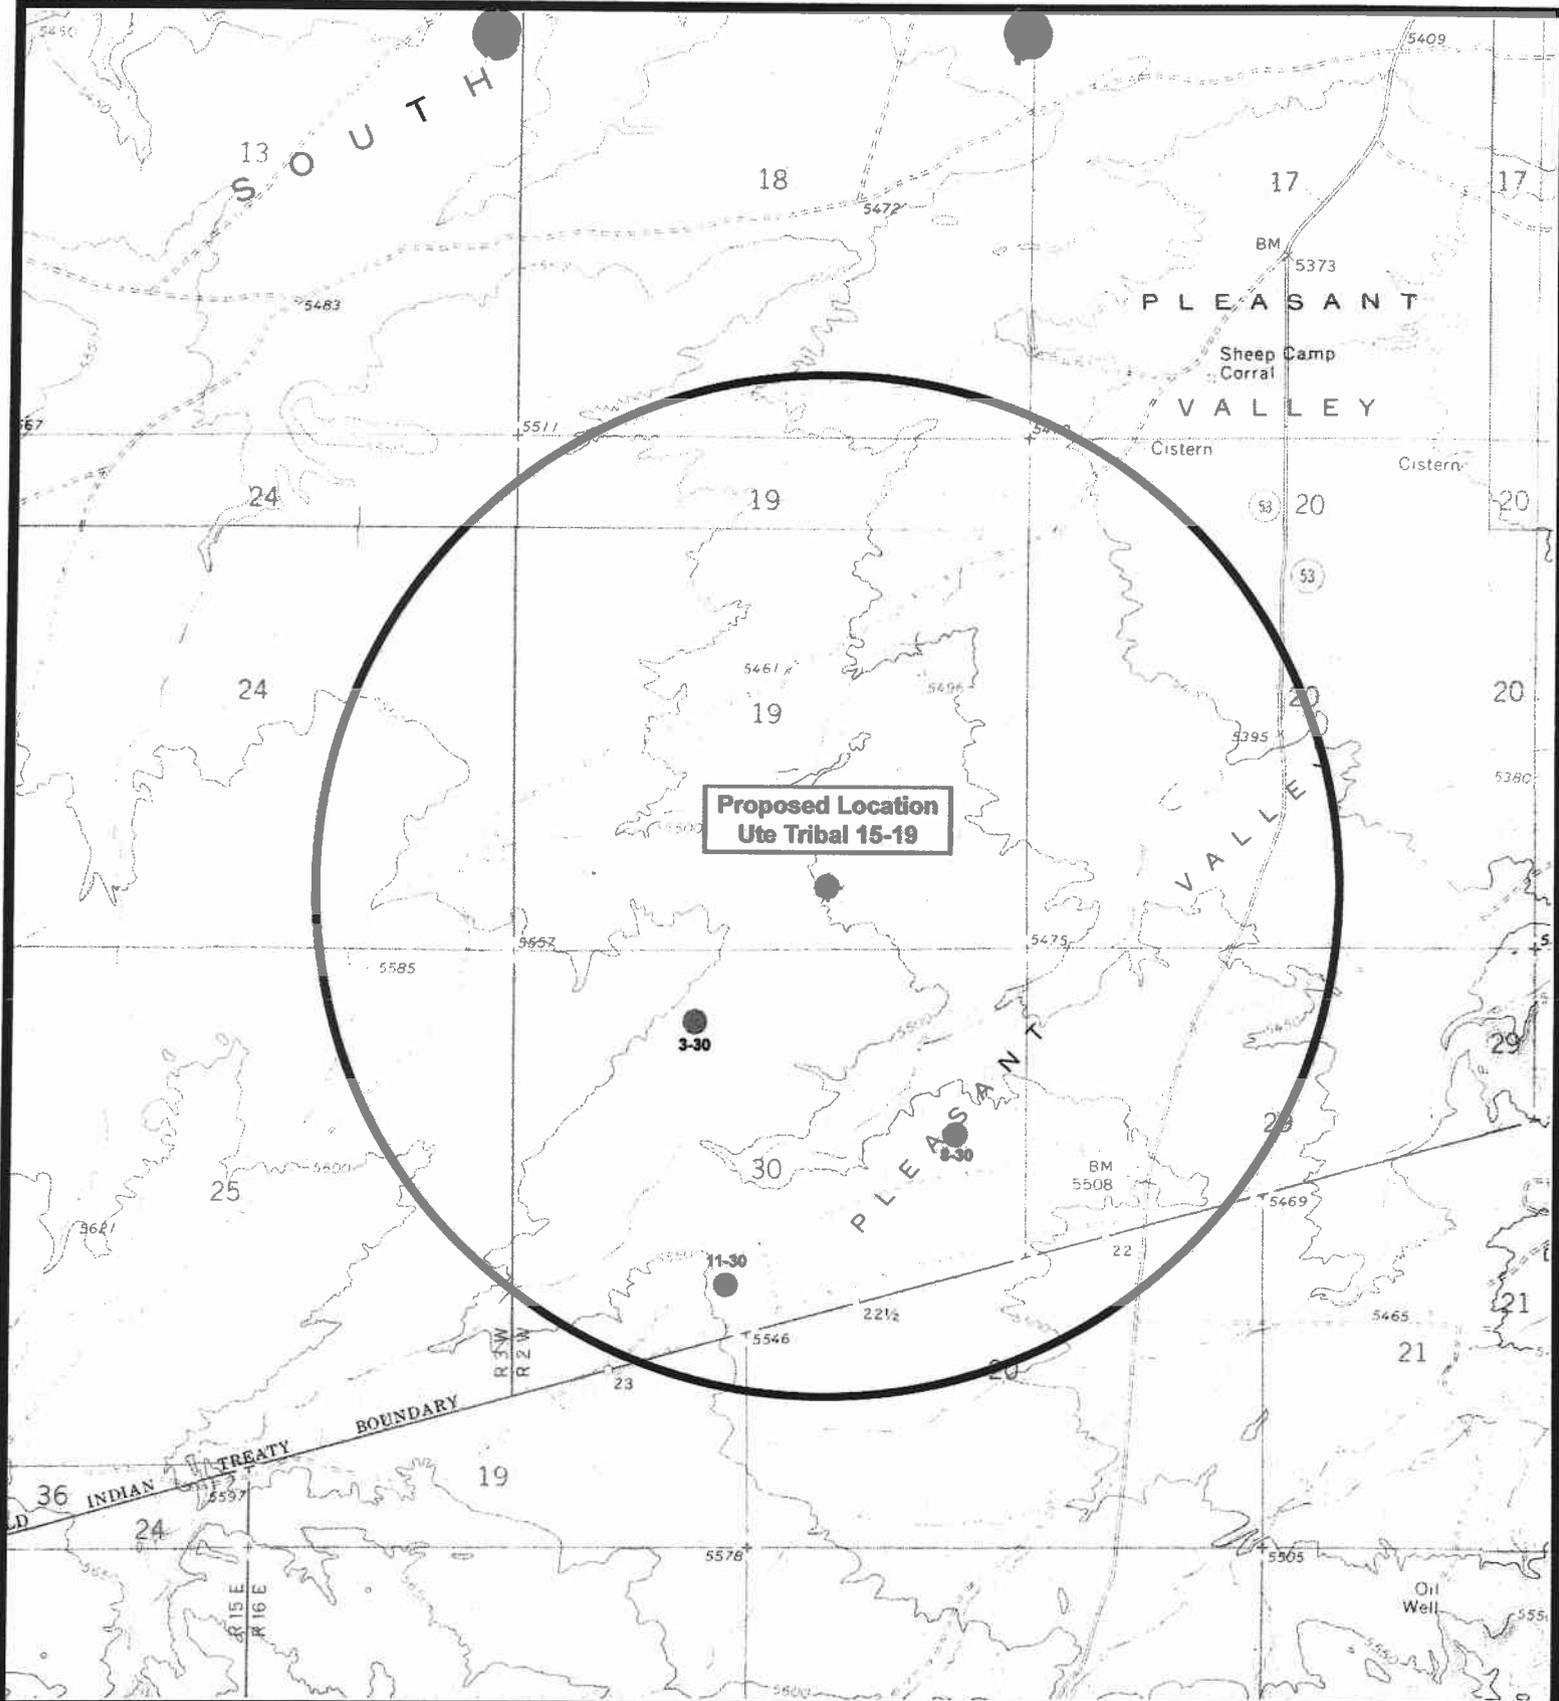

**Proposed Location
Ute Tribal 15-19**



NEWFIELD
Exploration Company

Ute Tribal 15-19-4-2
SEC. 19, T4S, R2W, U.S.B.&M.




Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'

DRAWN BY: mw

DATE: 03-29-2007

Legend

- Location
- One-Mile Radius

Exhibit "B"

2-M SYSTEM

Blowout Prevention Equipment Systems

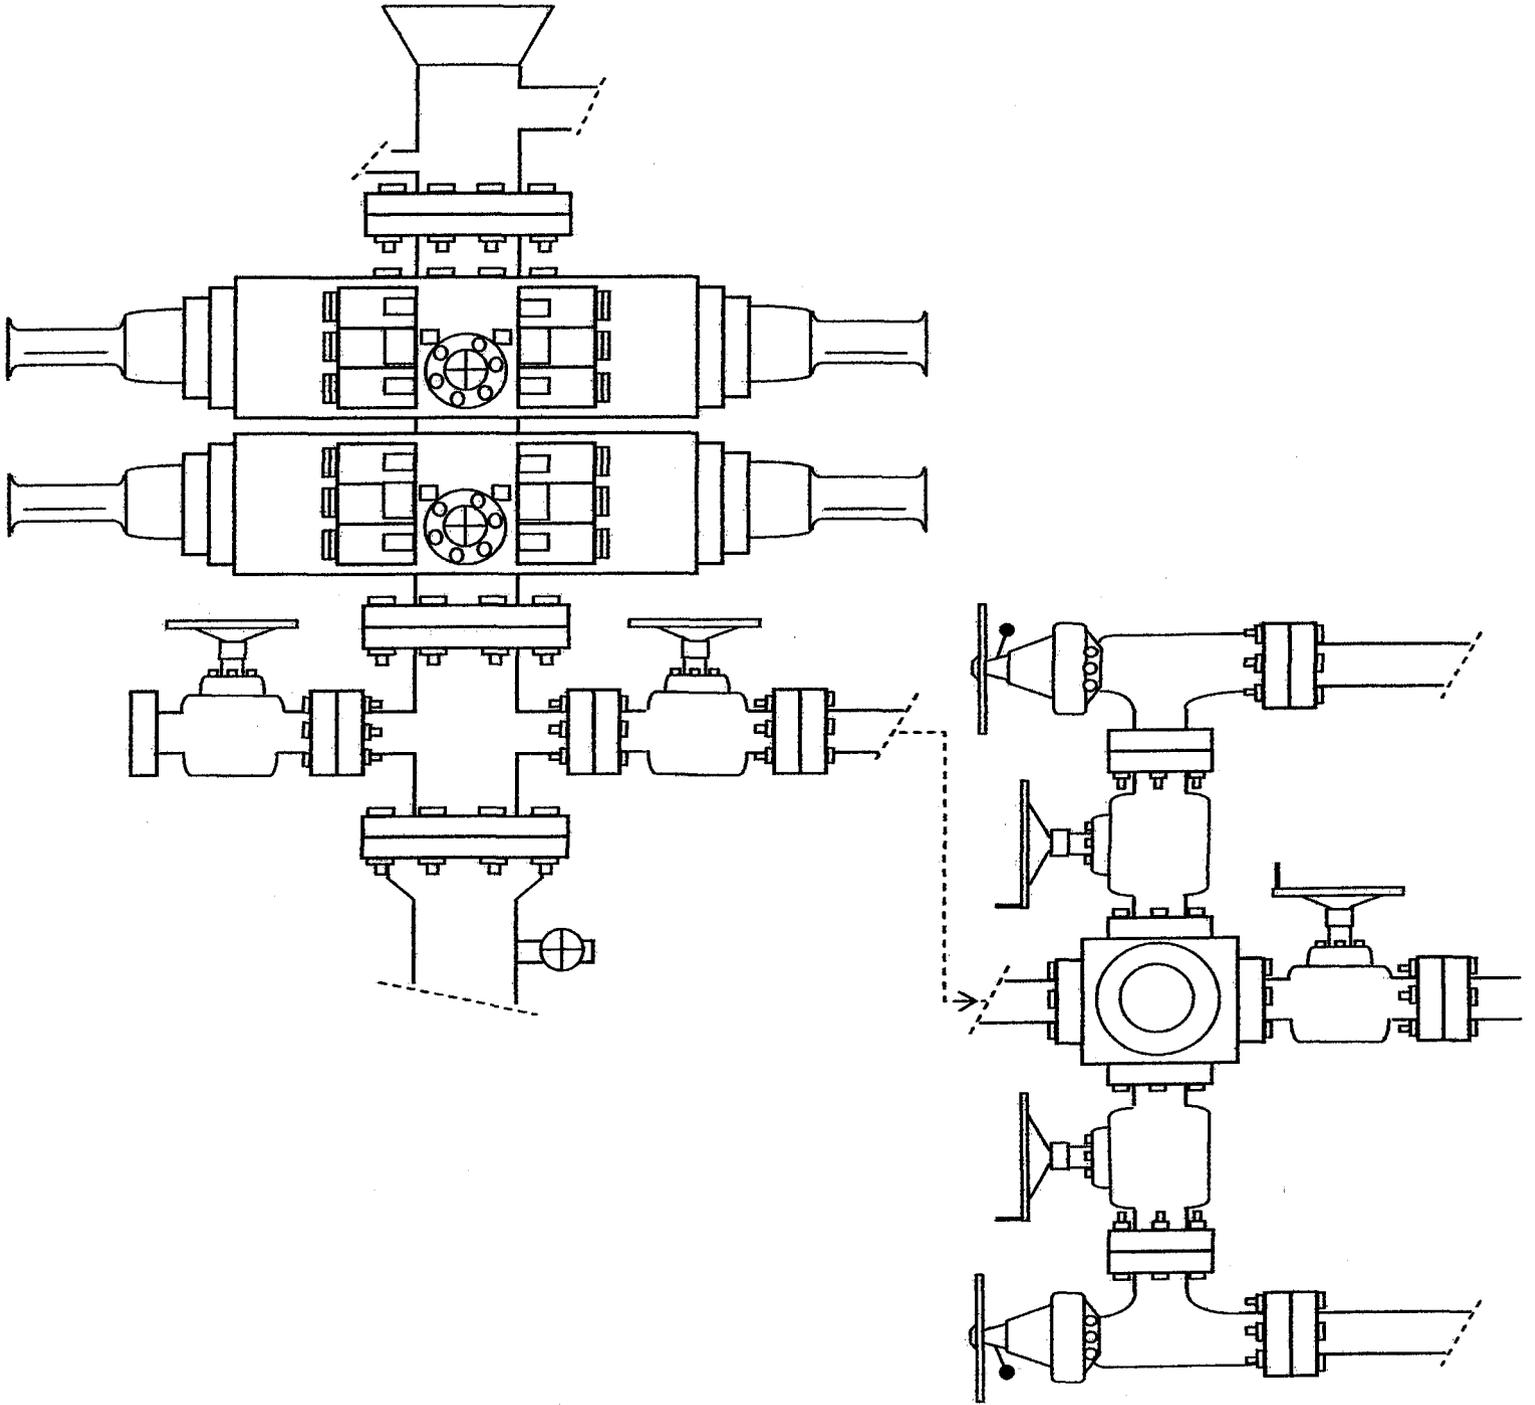


EXHIBIT C

Form 3160-3
(September 2001)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0136
Expires January 31, 2004

| | |
|--|--|
| 5. Lease Serial No. 20G0005609 | |
| 6. If Indian, Allottee or Tribe Name Ute | |
| 7. If Unit or CA Agreement, Name and No. N/A | |
| 8. Lease Name and Well No. Ute Tribal 15-19-4-2 | |
| 9. API Well No. 43-01333662 | |
| 1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER | 10. Field and Pool, or Exploratory Monument Butte |
| 1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone | 11. Sec., T., R., M., or Blk. and Survey or Area SW/SE Sec. 19, T4S R2W |
| 2. Name of Operator Newfield Production Company | 12. County or Parish Duchesne |
| 3a. Address Route #3 Box 3630, Myton UT 84052 | 13. State UT |
| 3b. Phone No. (include area code) (435) 646-3721 | 14. Distance in miles and direction from nearest town or post office* Approximatley 12.3 miles southwest of Myton, Utah |
| 4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface SW/SE 579' FSL 2106' FEL At proposed prod. zone | 15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 534' ft/ase, NA' ft/unit NA |
| 16. No. of Acres in lease NA | 17. Spacing Unit dedicated to this well 40 Acres |
| 18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. NA | 19. Proposed Depth 6800' |
| 20. BLM/BIA Bond No. on file B002792 | 21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5498' GL |
| 22. Approximate date work will start* 3rd Quarter 2007 | 23. Estimated duration Approximately seven (7) days from spud to rig release. |

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be required by the authorized officer.

| | | |
|--|--|-----------------|
| 25. Signature <i>Mandie Crozier</i> | Name (Printed/Typed) Mandie Crozier | Date 5/11/07 |
| Title Regulatory Specialist | | |
| Approved by (Signature) | Name (Printed/Typed) | Date |
| Title | Office | |

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on reverse)

Approved by the
Utah Division of
Oil, Gas and Mining

Federal Approval of this
Action is Necessary

Date: 0-01-07
By: [Signature]

NEWFIELD PRODUCTION COMPANY
UTE TRIBAL #15-19-4-2
SW/SE SECTION 19, T4S, R2W
DUCHESNE COUNTY, UTAH

ONSHORE ORDER NO. 1

DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

| | |
|-------------|-------------|
| Uinta | 0' - 1,600' |
| Green River | 1,600' |
| TD | 6,800' |

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation (Oil) 1,600' - 6,800'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

| | |
|--|---|
| Location & Sampled Interval | Date Sampled |
| Flow Rate | Temperature |
| Hardness | pH |
| Water Classification (State of Utah) | Dissolved Calcium (Ca) (mg/l) |
| Dissolved Iron (Fe) (ug/l) | Dissolved Sodium (Na) (mg/l) |
| Dissolved Magnesium (Mg) (mg/l) | Dissolved Carbonate (CO ₃) (mg/l) |
| Dissolved Bicarbonate (NaHCO ₃) (mg/l) | Dissolved Chloride (Cl) (mg/l) |
| Dissolved Sulfate (SO ₄) (mg/l) | Dissolved Total Solids (TDS) (mg/l) |

Ten Point Well Program &
Thirteen Point Well Program
Page 2 of 12

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: Ute Tribal 15-19-4-2**

| Surface casing 8-5/8" | 0' | 300' | 24.0 | J-55 | STC | 2,950 | 1,370 | 244,000 |
|--------------------------|----|--------|------|------|-----|-------|-------|---------|
| | | | | | | 17.53 | 14.35 | 33.89 |
| Prod casing 5-1/2" | 0' | 6,800' | 15.5 | J-55 | LTC | 4,810 | 4,040 | 217,000 |
| | | | | | | 2.22 | 1.87 | 2.06 |

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

| | |
|--|--------------|
| Frac gradient at surface casing shoe = | 13.0 ppg |
| Pore pressure at surface casing shoe = | 8.33 ppg |
| Pore pressure at prod casing shoe = | 8.33 ppg |
| Gas gradient = | 0.115 psi/ft |

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: Ute Tribal 15-19-4-2**

| Surface casing | 300' | Class G w/ 2% CaCl | 138 161 | 30% | 15.8 | 1.17 |
|---------------------|--------|-------------------------------------|-------------|-----|------|------|
| Prod casing Lead | 4,800' | Prem Lite II w/ 10% gel + 3% KCl | 332 1081 | 30% | 11.0 | 3.26 |
| Prod casing Tail | 2,000' | 50/50 Poz w/ 2% gel + 3% KCl | 363 451 | 30% | 14.3 | 1.24 |

- *Actual volume pumped will be 15% over the caliper log
- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
 - Compressive strength of tail cement: 2500 psi @ 24 hours

Waiting On Cement: A minimum of four (4) hours shall elapse prior to attempting any pressure testing of the BOP equipment which would subject the surface casing cement to pressure, and a minimum of six (6) hours shall elapse before drilling out of the wiper plug, cement, or shoe is begun. WOC time shall be recorded in the Driller's Log. Compressive Strength shall be a minimum of 500 psi prior to drilling out.

The Vernal BLM Office shall be notified, with sufficient lead time, in order to have a BLM representative on location while running all casing strings and cementing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if

Ten Point Well Program &
Thirteen Point Well Program
Page 3 of 12

the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

The production casing cementing program shall be conducted as approved to protect and/or isolate all usable water zones, potentially productive zones, lost circulation zones, abnormally pressured zones, and any prospectively valuable deposits of minerals.

As a minimum, usable water zones shall be isolated and/or protected by having a cement top for the production casing at least 200 feet above the base of the usable water. If gilsonite is encountered while drilling, it shall be isolated and/or protected via the cementing program.

Top plugs shall be used to reduce contamination of cement by displacement fluid. A bottom plug or other acceptable technique, such as a suitable preflush fluid, inner string cement method, etc., shall be utilized to help isolate the cement from contamination by the mud being displaced ahead of the cement slurry.

All casing strings below the conductor shall be pressure tested to 0.22 psi per foot of casing string length or to 1500 psi, whichever is greater, but not to exceed 70% of the minimum internal yield. If pressure declines more than 10% in 30 minutes, corrective action shall be taken.

A Form 3160-5, "Sundry Notices and Reports on Wells" shall be filed with the Vernal Office Manager within 30 days after the work is completed. This report must include the following information:

Setting of each string of casing showing the size, grade, weight of casing set, depth, amounts and type of cement used, whether cement circulated or the top of the cement behind the casing, depth of the cementing tools used, casing test method and results, and the date of the work done. Spud date will be shown on the first reports submitted.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The Company's Class 2M minimum specifications for pressure control equipment for a standard Monument Butte development well are as follows:

A 2000 psi WP hydraulic BOP stack consisting of two ram preventers (double or two singles) and either an annular preventer or a rotating head. If no annular preventer is used, ram blocks will be changed to match the outside diameter of casing and the stack will be retested prior to running any casing string.

Connections - All components on the stack and choke and kill lines shall have either flanged, studded, clamp hub or equivalent proprietary connections except control line outlets and pressure gauges.

Choke Manifold - The minimum equipment requirements are shown in Exhibit C. The choke manifold shall be located at least 5 feet from the BOP stack, outside the substructure.

Pressure Monitoring - A means of monitoring the inlet pressure of the choke manifold shall be provided. The capability to isolate this outlet shall be provided.

Drillstring Control Devices - An upper and lower kelly valve, drillstring safety valve including correct closing handle, and an inside BOP shall be provided. The safety valve and inside BOP shall have connections or crossovers to fit all tubulars with OD to allow adequate clearance for running in the hole. All drillstring valves shall be rated to the required BOP WP.

Ten Point Well Program &
Thirteen Point Well Program
Page 4 of 12

The BOP and related equipment shall meet the minimum requirements of Onshore Oil and Gas Order No. 2 for equipment and testing requirements, procedures, etc., for a 2M system, and individual components shall be operable as designed.

Function test of the BOP equipment shall be made daily. All required BOP tests and/or drills shall be recorded in the Driller's report.

Chart recorders will be used for all pressure tests. Test charts, with individual test results identified, shall be maintained on location while drilling and shall be made available to BLM representatives upon request.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ± 3200 feet will be drilled with either fresh water or an air/mist system, depending on the drilling contractor's preference. From about 3200 feet, or in the case of the air/mist system when hole conditions dictate, to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite.

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

a. **Logging Program:**

(the log types run may change at the discretion of the geologist)

FDC/CNL/GR/DLL: TD - 3,200'

CBL: A cement bond log will be run from TD to the cement top of the production casing. A field copy will be submitted to the Vernal BLM Office.

b. **Cores:** As deemed necessary.

c. **Drill Stem Tests:** No DSTs are planned in the Green River.

Drill stem tests, if they are run, will adhere to the following requirements: Initial opening of the drill stem test tools shall be restricted to daylight hours unless specific approval to start

Ten Point Well Program &
Thirteen Point Well Program
Page 5 of 12

during other hours is obtained from the Authorized Officer (AO). However, DSTs may be allowed to continue at night if the test was initiated during daylight hours and the rate of flow is stabilized and if adequate lighting is available (i.e., lighting which is adequate for visibility and vapor-proof for safe operations). Packers can be released but tripping shall not begin before daylight, unless prior approval is obtained from the AO. Closed chamber DSTs may be performed day or night.

Some means of reverse circulation shall be provided in case of flow to the surface showing evidence of hydrocarbons.

Separation equipment required for the anticipated recovery shall be properly installed before a test starts.

If a DST is performed, all engines within 100 feet of the wellbore that are required to be operational during the test shall have spark arresters or water-cooled exhausts.

Please refer to the Monument Butte Field Standard Operation Procedure (SOP).

9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.

10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:

a. Drilling Activity

| | |
|--------------------------------|---|
| Anticipated Commencement Date: | Upon approval of the site specific APD. |
| Drilling Days: | Approximately 7 days. |
| Completion Days: | Approximately 10 - 14 days. |

b. Notification of Operations

The Vernal BLM office will be notified at least 24 hours prior to the commencement of spudding the well (to be followed with a Sundry Notice, Form 3160-5), of initiating pressure tests of the blowout preventer and related equipment, and running casing and cementing of all casing strings. Notification will be made during regular work hours (7:45 a.m.-4:30 p.m., Monday - Friday except holidays).

Immediate Report: Spills, blowouts, fires, leaks, accidents, or any other unusual occurrences shall be promptly reported in accordance with the appropriate regulations, Onshore Orders, or BLM policy.

No location will be constructed or moved, no well will be plugged, and no drilling or workover equipment will be removed from a well to be placed in suspended status without prior approval from the AO. If operations are to be suspended, prior approval of the AO will be obtained and notification given to the BLM before resumption of operations.

Daily drilling and completion reports shall be submitted to the Vernal BLM Office on a weekly basis.

Ten Point Well Program &
Thirteen Point Well Program
Page 6 of 12

Whether the well is completed as a dry hole or a producer, the "Well Completion and Recompletion Report and Log" (Form 3160-4) will be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3164. One copy of all logs, core descriptions, core analyses, well test data, geologic summaries, sample description, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations will be filed with Form 3160-4. Samples (cuttings, fluids, and/or gases) will be submitted when requested by the Authorized Officer (AO).

A completion rig will be used for completion operations after the wells are stimulated to run the production tubing. All conditions of this approved plan will be applicable during all operations conducted with the completion rig.

Operator shall report production data to the MMS pursuant to 30 CFR 216.5 using form MMS/3160. In accordance with Onshore Oil and Gas Order No. 1, a well will be reported on form 3160-6, "Monthly Report of Operations," starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report will be filed with the Vernal BLM Office.

The date on which production is commenced or resumed will be construed for oil wells as the date on which liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated, or the date on which liquid hydrocarbons are first produced into a permanent storage facility, whichever occurs first; and for gas wells, as the date on which associated liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated, or the date on which gas is measured through permanent metering facilities, whichever occurs first.

Should the well be successfully completed for production, the AO will be notified when the well is placed in a producing status. Such notification will be sent by written communication not later than 5 days following the date when the well is placed on production.

Pursuant to Onshore Order No. 7, with the approval of the AO, produced water may be temporarily disposed of into unlined pits for a period of up to 90 days. During this period, an application for approval of the permanent disposal method must be submitted to the AO.

Pursuant to NTL-4A, lessees or operators are authorized to vent/flare gas during the initial well evaluation tests, not to exceed 30 days or the production of 50 MMCF of gas, whichever occurs first. An application must be filed with the AO and approval received for any venting/flaring of gas beyond the initial 30 days or authorized test period.

A schematic facilities diagram, as required by 43 CFR 3162.7-5(b.9.d), shall be submitted to the Vernal BLM Office within 60 days of installation or first production, whichever occurs first. All site security regulations, as specified in Onshore Oil & Gas Order No. 3, shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with 43 CFR 3162.7-5(b.4).

Well abandonment operations shall not be commenced without the prior approval of the AO. In the case of newly drilled dry holes or failures, and in emergency situations, oral approval will be obtained from the AO. A "Subsequent Report of Abandonment", Form 3160-5, will be filed with the Authorized Officer within 30 days following completion of the well for abandonment. This report will indicate placement of the plugs and current status of the surface restoration. Final Abandonment will not be approved until the surface reclamation work required by the approved APD or approved abandonment notice has been completed to the satisfaction of the AO, or the appropriate surface managing agency.

Ten Point Well Program &
Thirteen Point Well Program
Page 7 of 12

Pursuant to Onshore Oil and Gas Order No. 1, lessees and operators have the responsibility to see that their exploration, development, production, and construction operations are conducted in a manner which conforms with applicable Federal laws and regulations and with the State and local laws, to the extent to which they are applicable, to operations on Federal or Indian lands.

Ten Point Well Program &
Thirteen Point Well Program
Page 8 of 12

NEWFIELD PRODUCTION COMPANY
UTE TRIBAL #15-19-4-2
SW/SE SECTION 19, T4S, R2W
DUCHESNE COUNTY, UTAH

THIRTEEN POINT SURFACE PROGRAM

1. EXISTING ROADS

See attached **Topographic Map "A"**

To reach Newfield Production Company well location site Ute Tribal 15-19-4-2 located in the SW¼ SE¼ Section 19, T4S, R2W, S.L.B. & M., Duchesne County, Utah:

Proceed in a southwesterly direction out of Myton, Utah along Highway 40 approximately 1.9 miles to the junction of this highway and Utah State Highway 53; proceed southwesterly along Utah State Highway 53 approximately 1.7 miles to its junction with an existing road to the southwest; proceed southwesterly approximately 4.6 miles to its junction with an existing road to the west; proceed southwesterly approximately 2.2 miles to its junction with an existing road to the northeast; proceed northeasterly approximately 1.1 miles to its junction with the beginning of the proposed access road to the northeast; proceed northeasterly along the proposed access road approximately 4,650' to the proposed well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

Approximately 4,650' of access road is proposed. See attached **Topographic Map "B"**.

The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%.

There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to **EXHIBIT B**.

Ten Point Well Program &
Thirteen Point Well Program
Page 9 of 12

4. **LOCATION OF EXISTING AND/OR PROPOSED FACILITIES**

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck for drilling purposes from the following water sources:

Johnson Water District
Water Right: 43-10136

Neil Moon Pond
Water Right: 43-11787

Maurice Harvey Pond
Water Right: 47-1358

Newfield Collector Well
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Ten Point Well Program &
Thirteen Point Well Program
Page 10 of 12

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

8. **ANCILLARY FACILITIES:**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT:**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) **Producing Location**

Ten Point Well Program &
Thirteen Point Well Program
Page 11 of 13

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

b) **Dry Hole Abandoned Location**

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP:** Moon Land and Livestock LTD Partnership, Duchesne, Utah. See attached Surface Use Agreement.

12. **OTHER ADDITIONAL INFORMATION:**

Newfield Production Company requests 4650' of disturbed area be granted for construction of the proposed gas lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a 6" gas gathering line, and a 3" poly fuel gas line, with a permanent width of 30' upon completion of the proposed gas lines. The construction phase of the proposed gas lines will last approximately (5) days. Both lines will tie in to the existing pipeline infrastructure. Refer to Topographic Map "C."

Newfield Production Company requests 4650' of disturbed area be granted for construction of the proposed water lines. It is proposed that the disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line, with a permanent width of 30' upon completion of the proposed water return line. The construction phase of the proposed water lines will last approximately (5) days. Refer to Topographic Map "C."

The Easement ROW for construction of the proposed gas and water pipelines in Sec. 25, T4S R3W will be forthcoming.

- a) Newfield Production Company is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, Newfield is to immediately stop work that might further disturb such materials and contact the Authorized Officer.
- b) Newfield Production will control noxious weeds along rights-of-way for roads, pipelines, well sites or other applicable facilities. On State administered land it is required that a Pesticide Use Proposal shall be submitted and given approval prior to the application of herbicides or other possible hazardous chemicals.
- c) Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on State Lands after the conclusion of drilling operations or at any other time without State authorization. However, if State authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

Ten Point Well Program &
Thirteen Point Well Program
Page 12 of 13

The Archaeological Report Waiver for this location is attached.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the Ute Tribal 15-19-4-2, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Ute Tribal 15-19-4-2 Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

The State office as well as the Ute Tribe Energy and Mineral Department shall be notified upon site completion prior to moving on the drilling rig.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

Representative

Name: Kim Kettle
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that Newfield Production Company is considered to be the operator of well #15-19-4-2, SW/SE Section 19, T4S, R2W, Duchesne County, Utah and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by US Specialty Insurance #B002792.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

5/11/07

Ten Point Well Program &
Thirteen Point Well Program
Page 13 of 13


Date


Mandie Crozier
Regulatory Specialist
Newfield Production Company

NEW ELD PRODUCTION COMPANY

UTE TRIBAL 15-19-4-2

Section 19, T4S, R2W, U.S.B.&M.




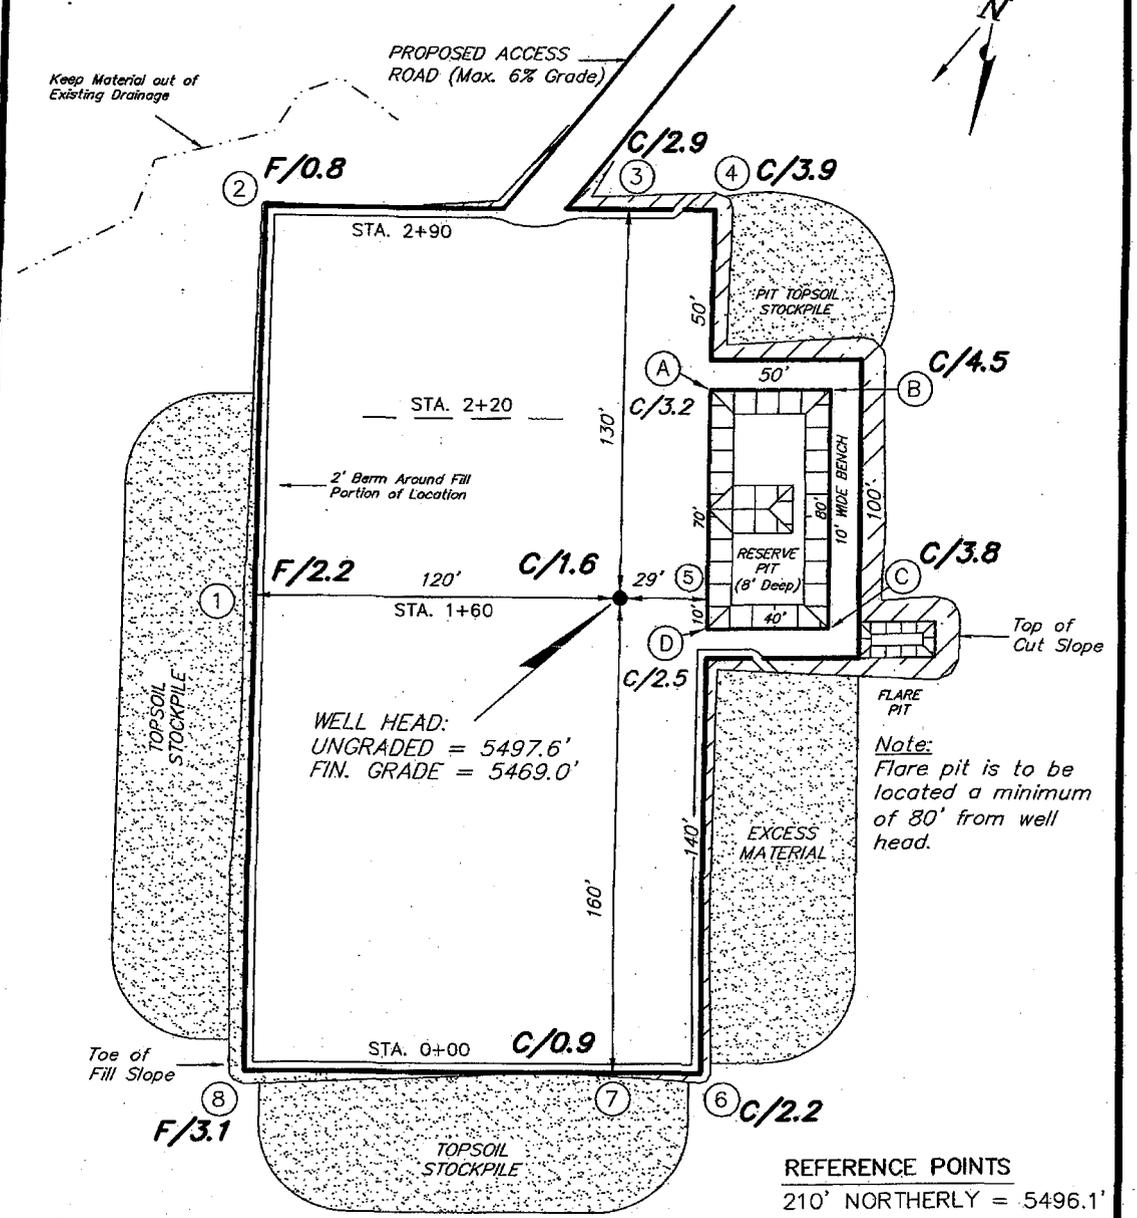


REFERENCE POINTS
 210' NORTHERLY = 5496.1'
 260' NORTHERLY = 5497.3'
 170' EASTERLY = 5491.9'
 220' EASTERLY = 5490.6'

| | |
|-------------------|-----------------|
| SURVEYED BY: C.M. | SCALE: 1" = 50' |
| DRAWN BY: T.C.J. | DATE: 03-27-07 |

Tri State Land Surveying, Inc. (435) 781-2501
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NE FIELD PRODUCTION COMPANY
CROSS SECTIONS
UTE TRIBAL 15-19-4-2



NOTE:
 UNLESS OTHERWISE NOTED
 ALL CUT/FILL SLOPES ARE
 AT 1.5:1

| ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards) | | | | |
|---|-------|-------|--|--------|
| ITEM | CUT | FILL | 6" TOPSOIL | EXCESS |
| PAD | 1,560 | 1,560 | Topsail is not included in Pad Cut | 0 |
| PIT | 640 | 0 | | 640 |
| TOTALS | 2,200 | 1,560 | 980 | 640 |

SURVEYED BY: C.M.

SCALE: 1" = 50'


DRAWN BY: T.C.J.

DATE: 03-27-07


Tri State (435) 781-2501
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEW FELD PRODUCTION COMPANY TYPICAL RIG LAYOUT UTE TRIBAL 15-19-4-2


PROPOSED ACCESS ROAD (Max. 6% Grade)

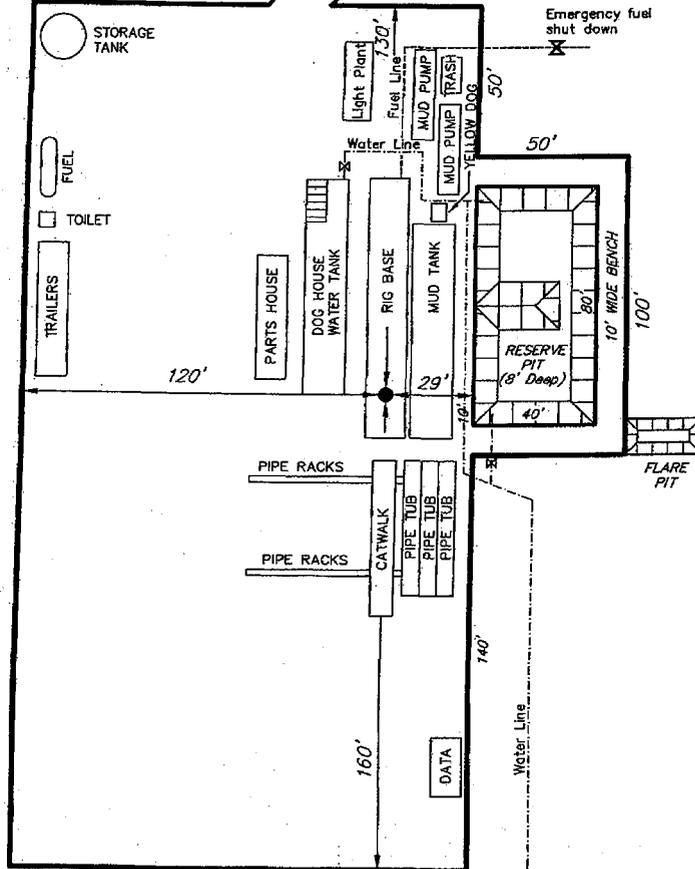

| | | |
|-------------------|-----------------|---|
| SURVEYED BY: C.M. | SCALE: 1" = 50' | Tri State Land Surveying, Inc. 180 NORTH VERNAL AVE. VERNAL, UTAH 84078 (435) 781-2501 |
| DRAWN BY: T.C.J. | DATE: 03-27-07 | |

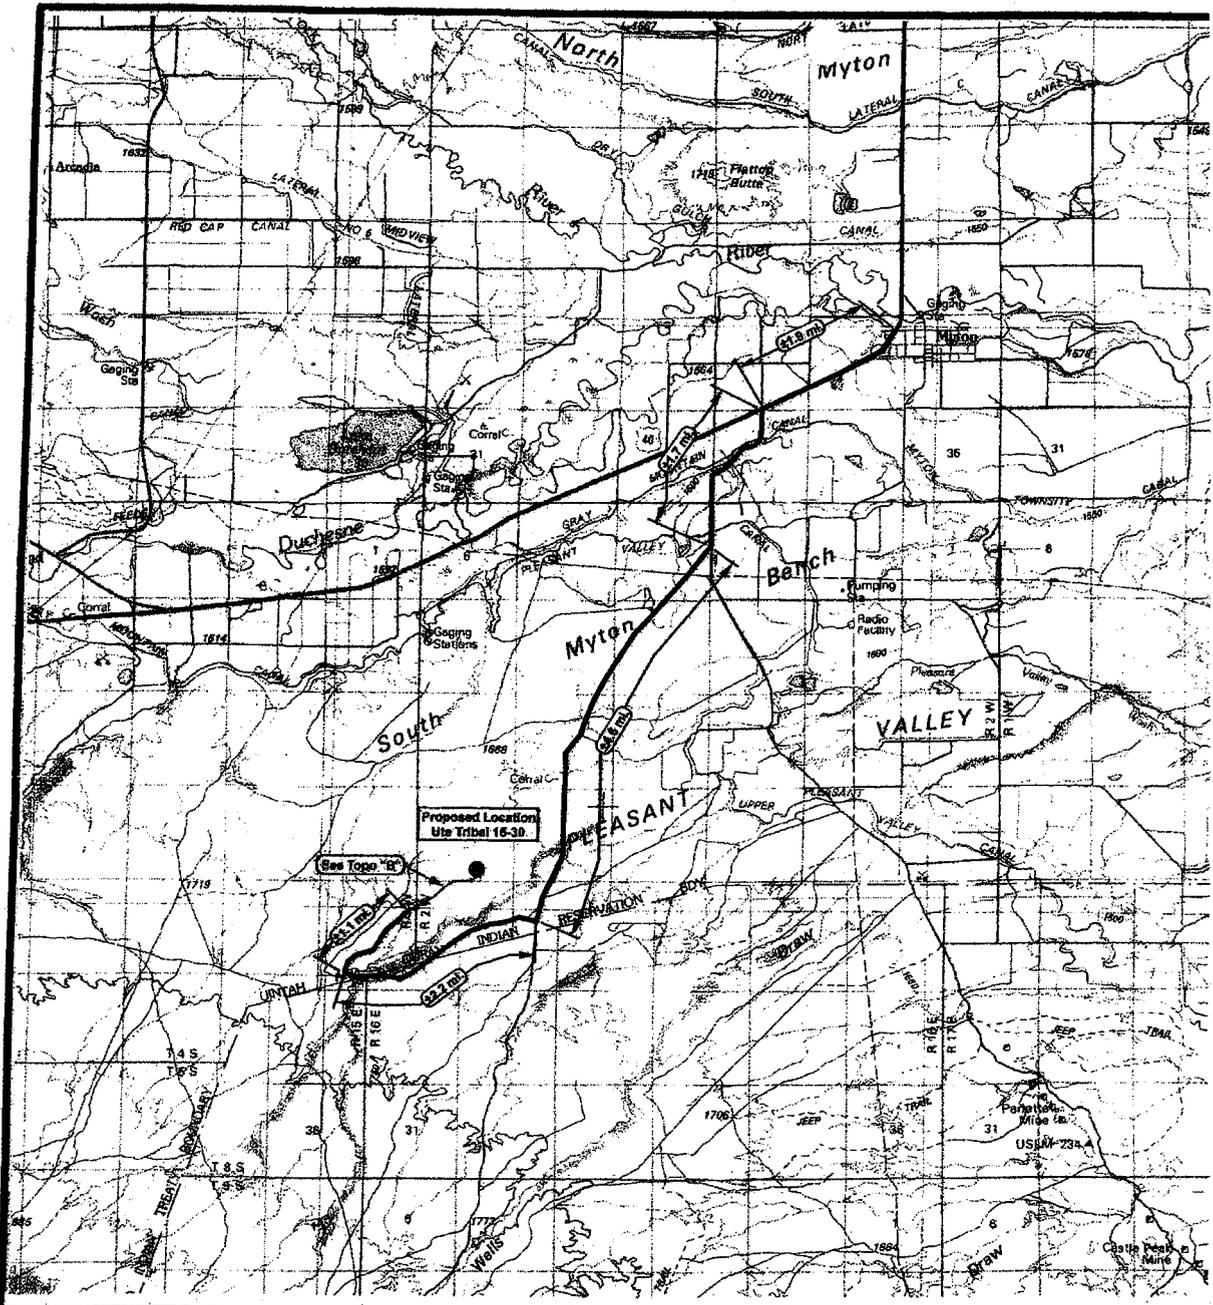



PLANNED
 Exploration Company
Ute Tribal 15-19-4-2
SEC. 19, T4S, R2W, U.S.B.&M.





Tri-State
Land Surveying Inc.
 (435) 781-2501
 38 West 100 North Verml, Utah 84078
 SCALE: 1" = 100.000
 DRAWN BY: DMW
 DATE: 03-29-2007


Existing Road
 Proposed Access
 TOPOGRAPHIC MAP
"A"

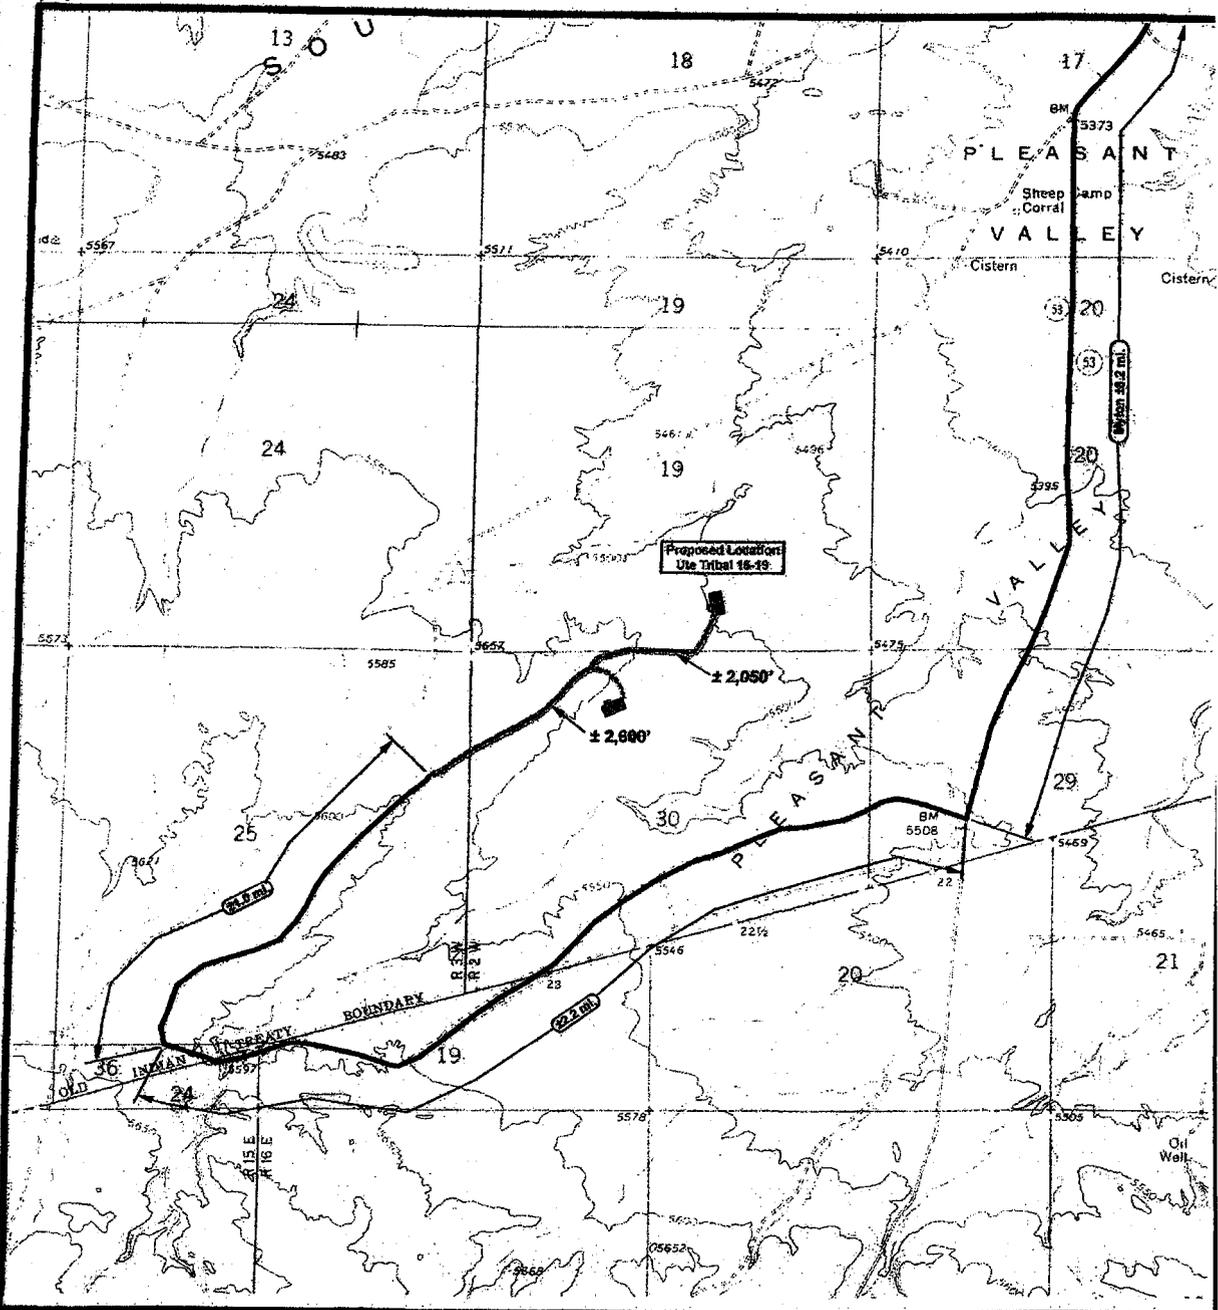


| | | | |
|--|--|--|--|
| <p>BUREAU OF LAND MANAGEMENT U.S. DEPARTMENT OF THE INTERIOR</p> | | <p>Tri-State Land Surveying Inc. (435) 781-2501 100 North Vernal Ave., Vernal, Utah 84078</p> | <p> Existing Road Proposed Access</p> |
| <p>Ute Tribal 15-19-4-2 SEC. 19, T4S, R2W, U.S.B.&M.</p> | | <p>SCALE: 1" = 2000' DRAWN BY: mw DATE: 03-29-2007</p> | <p>TOPOGRAPHIC MAP "B"</p> |

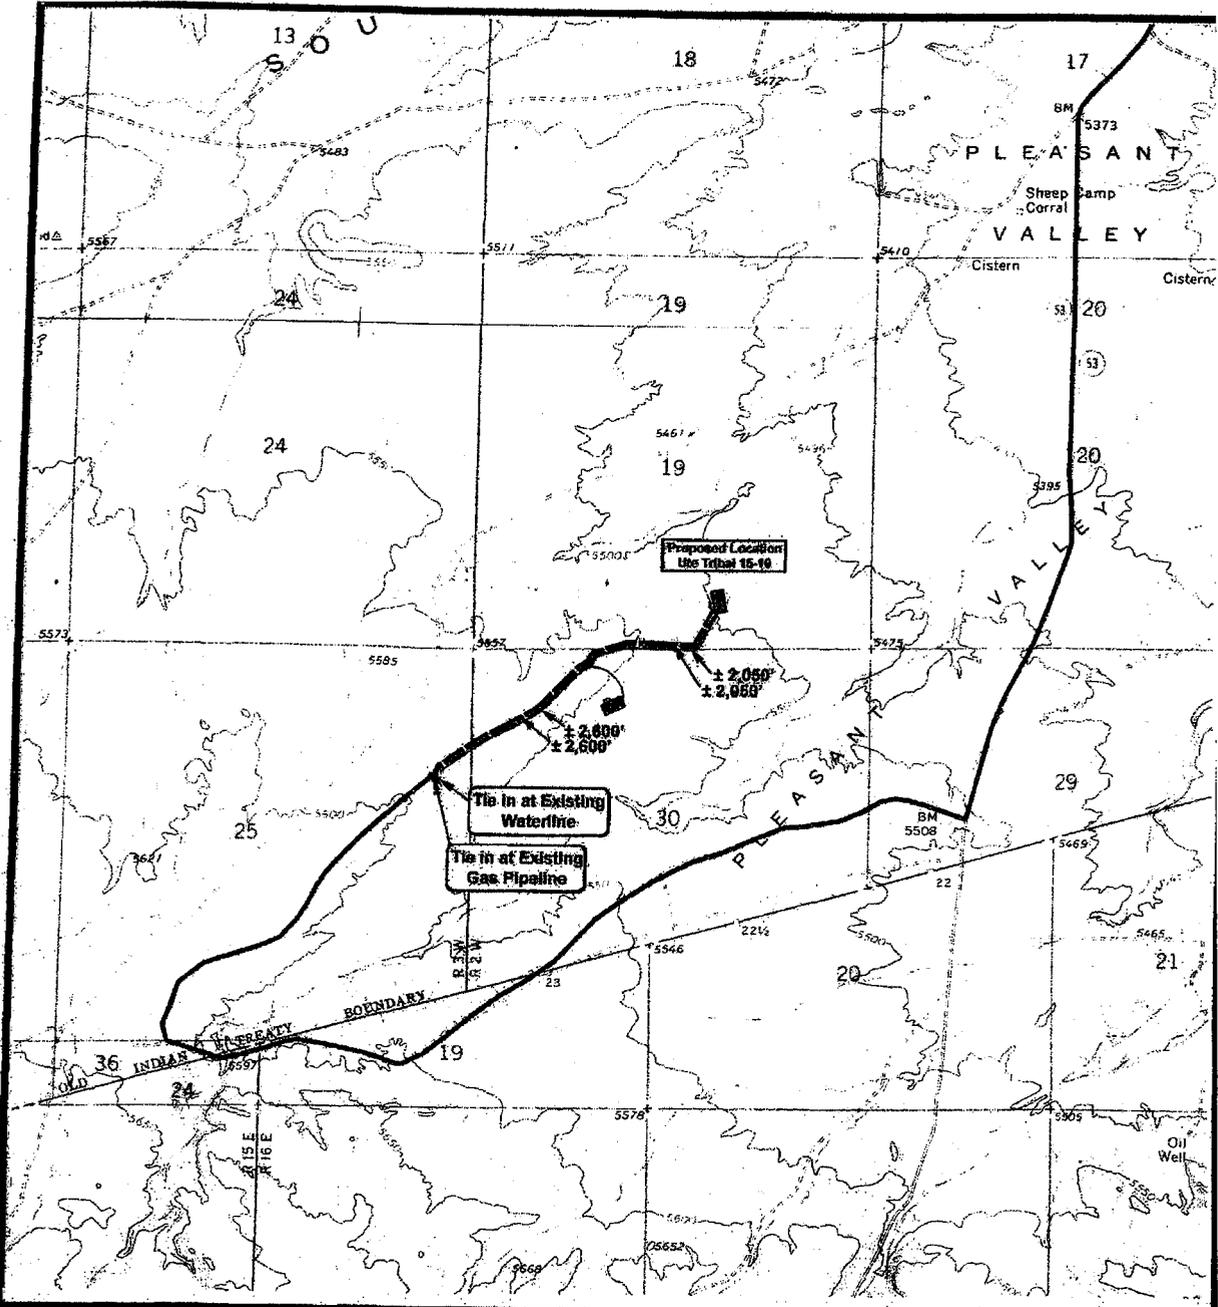

| | | | | | | | | | |
|--|---|---|---|--|-------|--|-------------------|--|---------------------|
|  <p>UNAPPORTIONED EQUILIBRIUM COMPANY</p> |  | <p>Tri-State Land Surveying Inc. (435) 781-2501 180 North Vermont Ave., Vernal, Utah 84078</p> <p>SCALE: 1" = 2000' DRAWN BY: ipw DATE: 03-29-2007</p> | <p>TOPOGRAPHIC MAP</p> <p>"C"</p> <table border="1"> <tr><td></td><td>Roads</td></tr> <tr><td></td><td>Proposed Gas Line</td></tr> <tr><td></td><td>Proposed Water Line</td></tr> </table> | | Roads | | Proposed Gas Line | | Proposed Water Line |
| | Roads | | | | | | | | |
| | Proposed Gas Line | | | | | | | | |
| | Proposed Water Line | | | | | | | | |
| <p>Ute Tribal 15-19-4-2 SEC. 19, T4S, R2W, U.S.B.&M.</p> | | | | | | | | | |

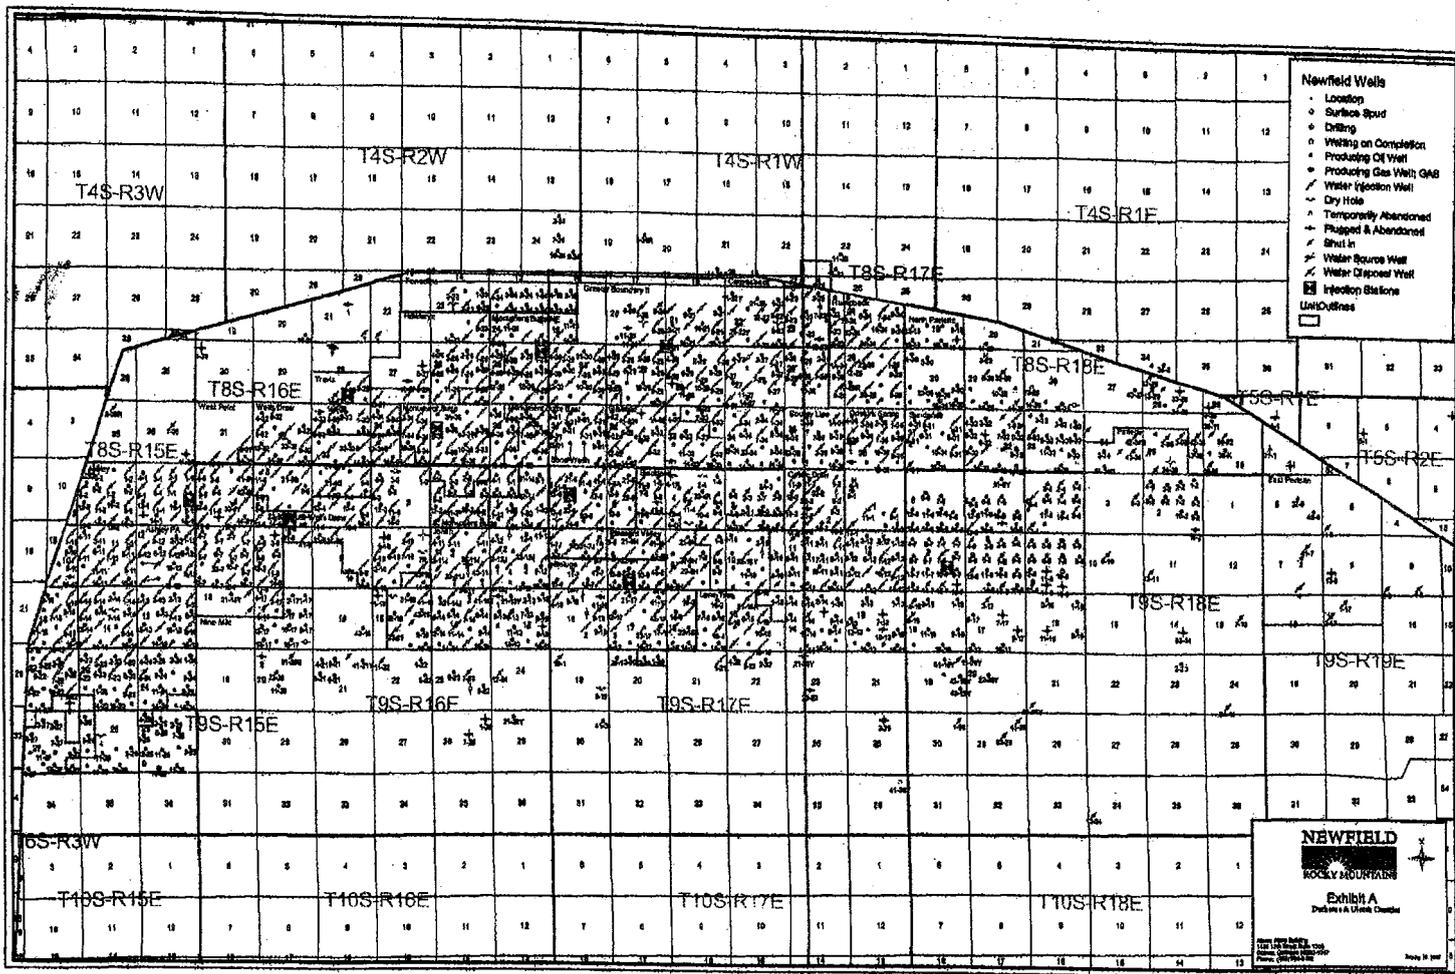

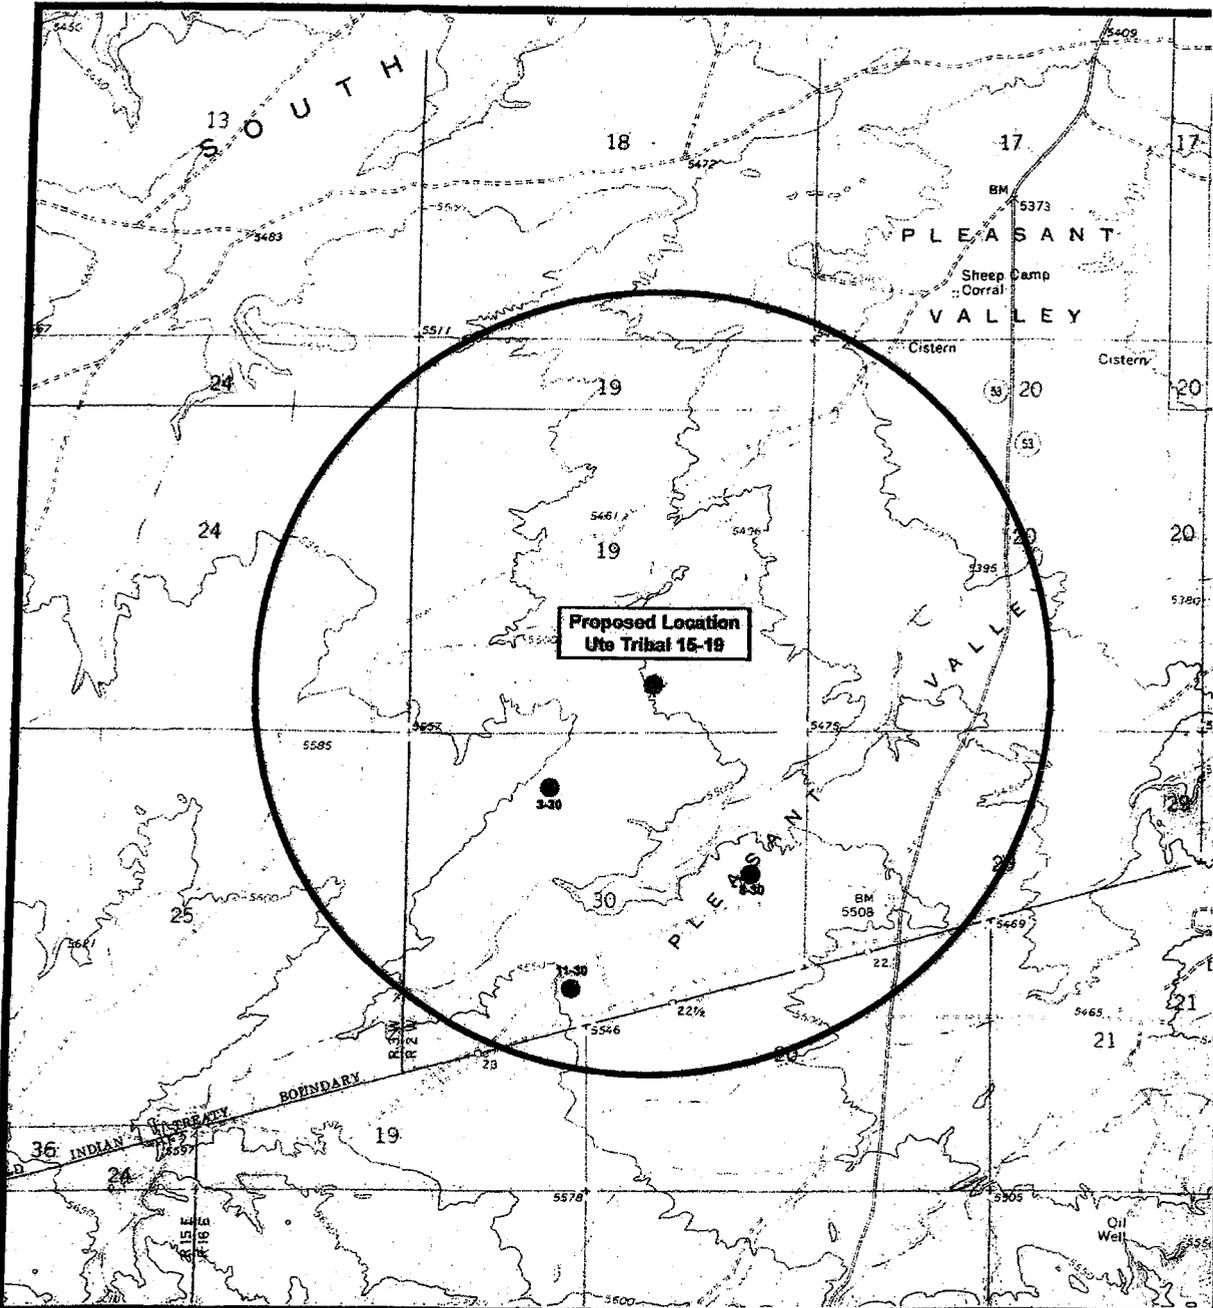

**Environmental
Exploration Company**

**Ute Tribal 15-19-4-2
SEC. 19, T4S, R2W, U.S.B.&M.**



**Tri-State
Land Surveying Inc.**
(436) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: JHW
DATE: 03-29-2007

- Location
- One-Mile Radius

Exhibit "B"

2-M SYSTEM Blowout Prevention Equipment Systems

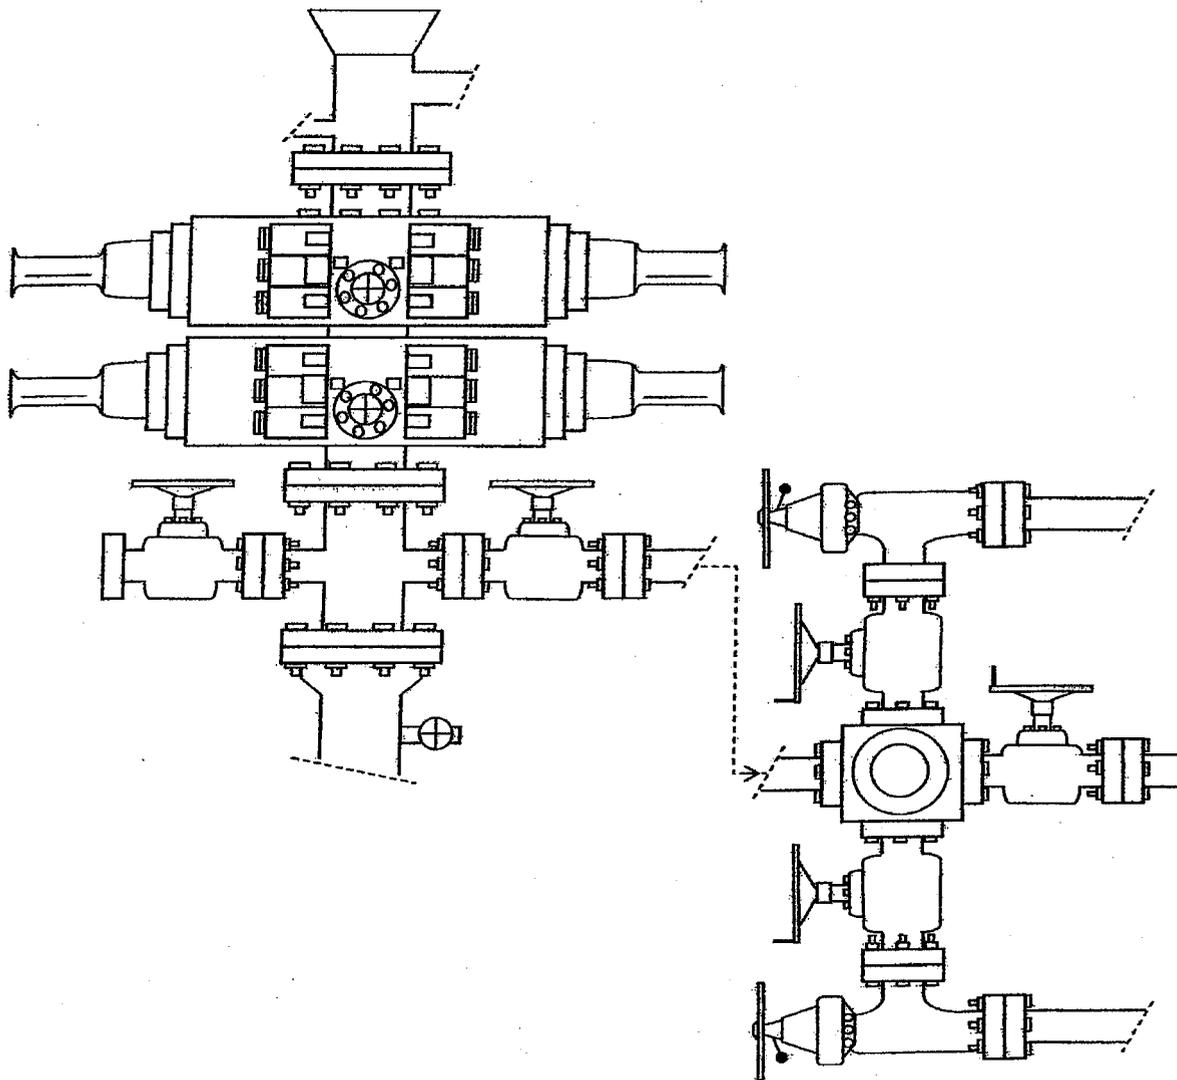


EXHIBIT C

**WORKSHEET
APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 05/16/2007

API NO. ASSIGNED: 43-013-33662

WELL NAME: UTE TRIBAL 15-19-4-2
 OPERATOR: NEWFIELD PRODUCTION (N2695)
 CONTACT: MANDIE CROZIER

PHONE NUMBER: 435-646-3721

PROPOSED LOCATION:

SWSE 19 040S 020W
 SURFACE: 0579 FSL 2106 FEL
 BOTTOM: 0579 FSL 2106 FEL
 COUNTY: DUCHESNE
 LATITUDE: 40.11489 LONGITUDE: -110.1495
 UTM SURF EASTINGS: 572480 NORTHINGS: 4440645
 FIELD NAME: SOUTH MYTON BENCH (117)

| INSPECT LOCATN BY: / / | | |
|------------------------|----------|------|
| Tech Review | Initials | Date |
| Engineering | | |
| Geology | | |
| Surface | | |

LEASE TYPE: 2 - Indian
 LEASE NUMBER: 20G0005609
 SURFACE OWNER: 4 - Fee

PROPOSED FORMATION: GRRV
 COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:


- Plat
- Bond: Fed[] Ind[2] Sta[] Fee[]
(No. B002792)
- Potash (Y/N)
- Oil Shale 190-5 (B) or 190-3 or 190-13
- Water Permit
(No. 43-10136)
- RDCC Review (Y/N)
(Date: _____)
- Fee Surf Agreement (Y/N)
- Intent to Commingle (Y/N)

LOCATION AND SITING:

- ___ R649-2-3.
- Unit: _____
- R649-3-2. General
Siting: 460 From Qtr/Qtr & 920' Between Wells
- ___ R649-3-3. Exception
- ___ Drilling Unit
Board Cause No: _____
Eff Date: _____
Siting: _____
- ___ R649-3-11. Directional Drill

COMMENTS: Needs Permit (09-14-07)

STIPULATIONS: 1- Federal Approval
2- Spacing WSP
3- STATEMENT OF BASIS

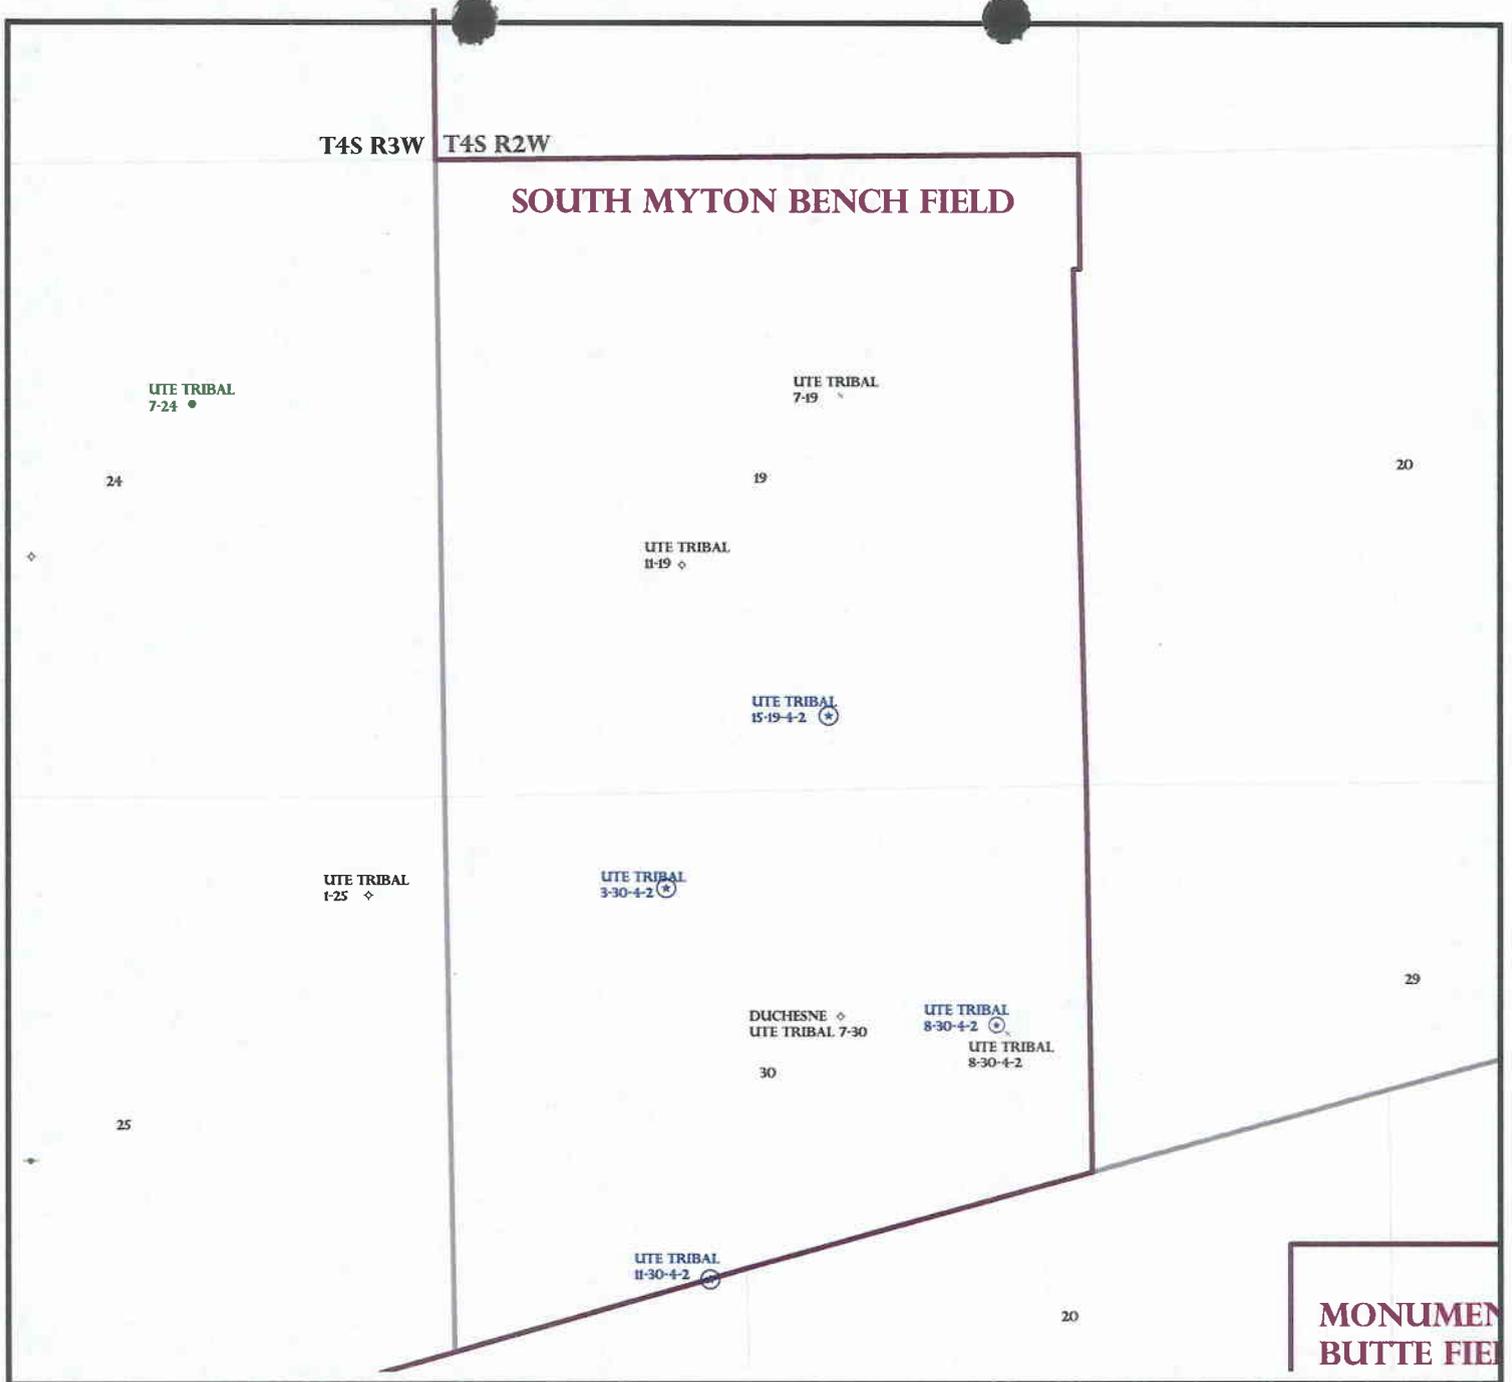

**MONUMEN
BUTTE FIELD**

OPERATOR: NEWFIELD PROD CO (N2695)

SEC: 19,30 T.4S R. 2W

FIELD: S. MYTON BENCH (117)

COUNTY: DUCHESNE

SPACING: R649-3-2 / GENERAL SITING

Field Status


- ABANDONED
- ACTIVE
- COMBINED
- INACTIVE
- PROPOSED
- STORAGE
- TERMINATED

Unit Status

- EXPLORATORY
- GAS STORAGE
- NF PP OIL
- NF SECONDARY
- PENDING
- PI OIL
- PP GAS
- PP GEOTHERML
- PP OIL
- SECONDARY
- TERMINATED

Wells Status

- ✂ GAS INJECTION
- ✂ GAS STORAGE
- ✂ LOCATION ABANDONED
- ✂ NEW LOCATION
- ✂ PLUGGED & ABANDONED
- ✂ PRODUCING GAS
- ✂ PRODUCING OIL
- ✂ SHUT-IN GAS
- ✂ SHUT-IN OIL
- ✂ TEMP. ABANDONED
- ✂ TEST WELL
- ✂ WATER INJECTION
- ✂ WATER SUPPLY
- ✂ WATER DISPOSAL
- ✂ DRILLING



Utah Oil Gas and Mining



PREPARED BY: DIANA MASON
DATE: 16-MAY-2007

Application for Permit to Drill

Statement of Basis

10/1/2007

Utah Division of Oil, Gas and Mining

Page 1

| APD No | API WellNo | Status | Well Type | Surf Ownr | CBM |
|------------------|---|--------------------------|-----------|-----------|-----|
| 426 | 43-013-33662-00-00 | | OW | P | No |
| Operator | NEWFIELD PRODUCTION COMPANY | Surface Owner-APD | | | |
| Well Name | UTE TRIBAL 15-19-4-2 | Unit | | | |
| Field | SOUTH MYTON BENCH | Type of Work | | | |
| Location | SWSE 19 4S 2W U 579 FSL 2106 FEL GPS Coord (UTM) 572480E 4440645N | | | | |

Geologic Statement of Basis

The Ute Tribe owns the mineral rights for the proposed well. The BLM will be the agency responsible for evaluating and approving the drilling, casing and cement programs.

Brad Hill
APD Evaluator

10/1/2007
Date / Time

Surface Statement of Basis

The general area is approximately 12.0 road miles southwest of Myton, UT in a sub-drainage of Pleasant Valley Wash which drains into the Pariette Draw drainage of Duchesne County. Both of these draws contain perennial streams somewhat consisting of irrigation runoff and seepage. Pariette Draw runs into the Green River approximately 6 miles downstream from Ouray, Utah and about 14 miles downstream from the location. Broad flats with those in lower Pleasant Valley frequently used for agriculture characterize the area. Flats are intersected by drainages with gentle to moderate side slopes.

The proposed Ute Tribal 15-19-4-2 oil well location is in upper non-irrigated portion of Pleasant Valley. It is on a very gentle slope leading to the southeast from a rolling rise to the northwest. Very minor swales exist in the area, non of which will require a diversion around the pad. The location was moved to the west prior to staking to avoid a drainage. Access is by State and County and planned oil field development roads. Two thousand and fifty feet of new road across Moons private land will be required to reach the location.

Russell Moon owns the surface of the location. Mr. Moon was contacted by telephone on September 10, 2007 and said he would not attend the pre-site visit. A signed surface use agreement and a cultural resource survey waiver exist. The minerals are owned by the United States Government and held in trust for the Ute Indian Tribe. Charles MacDonald of the BLM represented the Ute Indian Tribe. Mr. Macdonald had no concerns regarding the proposed location.

The location appears to be a suitable site for drilling and operating a well.

Floyd Bartlett
Onsite Evaluator

9/14/2007
Date / Time

Conditions of Approval / Application for Permit to Drill

| Category | Condition |
|----------|---|
| Pits | A synthetic liner with a minimum thickness of 16 mils with a felt subliner shall be properly installed and maintained in the reserve pit. |

ON-SITE PREDRILL EVALUATION

Utah Division of Oil, Gas and Mining

Operator NEWFIELD PRODUCTION COMPANY
Well Name UTE TRIBAL 15-19-4-2
API Number 43-013-33662-0 **APD No** 426 **Field/Unit** SOUTH MYTON BENCH
Location: 1/4,1/4 SWSE **Sec** 19 **Tw** 4S **Rng** 2W 579 FSL 2106 FEL
GPS Coord (UTM) 572484 4440653 **Surface Owner**

Participants

Floyd Bartlett (DOGM), Kim Swasey (Newfield), Charles Macdonald (BLM).

Regional/Local Setting & Topography

The proposed location is approximately 12.0 road miles southwest of Myton, UT in a sub-drainage of Pleasant Valley Wash which drains into the Pariette Draw drainage of Duchesne County. Both of these draws contain perennial streams somewhat consisting of irrigation runoff and seepage. Pariette Draw runs into the Green River approximately 6 miles downstream from Ouray, Utah and about 14 miles downstream from the location. Broad flats with those in lower Pleasant Valley frequently used for agriculture characterize the area. Flats are intersected by drainages with gentle to moderate side slopes.

The proposed Ute Tribal 15-19-4-2 oil well location is in upper non-irrigated portion of Pleasant Valley. It is on a very gentle slope leading to the southeast from a rolling rise to the northwest. Very minor swales exist in the area, non of which will require a diversion around the pad. The location was moved to the west prior to staking to avoid a drainage. Access is by State and County and planned oil field development roads. Two thousand and fifty feet of new road across Moons private land will be required to reach the location.

Surface Use Plan

Current Surface Use

Grazing
Wildlife Habitat

New Road

| Miles | Well Pad | Src Const Material | Surface Formation |
|--------------|------------------------------------|---------------------------|--------------------------|
| 0.4 | Width 199 Length 290 | Onsite | UNTA |

Ancillary Facilities N

Waste Management Plan Adequate? Y

Environmental Parameters

Affected Floodplains and/or Wetland N

Flora / Fauna

Deseret shrub type consisting of horsebrush, cheatgrass, halogeton, Indian ricegrass, globe mallow, shadscale, agrosis, curly mesquite, rabbit brush and spring annuals.

Cattle, antelope, prairie dogs, small mammals and birds.

Soil Type and Characteristics

Deep sandy clay loam.

Erosion Issues N

Sedimentation Issues N

Site Stability Issues N

Drainage Diversion Required N

Berm Required? N

Erosion Sedimentation Control Required? N

Paleo Survey Run? N Paleo Potential Observed? N Cultural Survey Run? N Cultural Resources?

Reserve Pit

| Site-Specific Factors | | Site Ranking |
|--|------------------|----------------------------|
| Distance to Groundwater (feet) | >200 | 0 |
| Distance to Surface Water (feet) | >1000 | 0 |
| Dist. Nearest Municipal Well (ft) | >5280 | 0 |
| Distance to Other Wells (feet) | 300 to 1320 | 10 |
| Native Soil Type | Mod permeability | 10 |
| Fluid Type | Fresh Water | 5 |
| Drill Cuttings | Normal Rock | 0 |
| Annual Precipitation (inches) | <10 | 0 |
| Affected Populations | <10 | 0 |
| Presence Nearby Utility Conduits | Not Present | 0 |
| Final Score | | 25 |
| | | 1 Sensitivity Level |

Characteristics / Requirements

40' x 80' x 8' deep located in an area of cut on the southwest side of the location. A pit liner is required. Newfield commonly uses a 16 mil liner.

Closed Loop Mud Required? N Liner Required? Y Liner Thickness 16 Pit Underlayment Required? Y

Other Observations / Comments

Floyd Bartlett
Evaluator

9/14/2007
Date / Time

From: "Mandie Crozier" <mcrozier@newfield.com>
To: "Diana Mason" <dianawhitney@utah.gov>
Date: 6/8/2007 10:14 AM
Subject: RE: Newfield Tribal APD's
Attachments: 8-30-4-2_001.tif; 11-30-4-2_001.tif; 15-19-4-2_001.tif; 3-30-4-2_001.tif; 8-25-4-1_001.tif; 6-25-4-1_001.tif; 6-30-4-1_001.tif; 13-22-4-2_001.tif; 16-22-4-2_001.tif; 12-29-4-1_001.tif; 16-29-4-1_001.tif; 13-19-4-1_001.tif; 6-22-4-1_001.tif; 8-21-4-1_001.tif; 10-21-4-1_001.tif

Here are 15 of the 17 that have previously been submitted. We had to amend the 10 point drilling plan on all of them and then I had to add some narrative in the 13 point surface use plan for the proposed pipelines. Let me know if you have any questions or need anything else.

Mandie Crozier
 Newfield Production
 (435)646-4825

-----Original Message-----

From: Diana Mason [mailto:dianawhitney@utah.gov]
 Sent: Friday, June 08, 2007 8:32 AM
 To: Mandie Crozier
 Subject: RE: Newfield Tribal APD's

43013-33662

Yes

>>> "Mandie Crozier" <mcrozier@newfield.com> 6/8/2007 8:03 AM >>>
 Can I just scan them in and e-mail them to you?

Mandie Crozier
 Newfield Production
 (435)646-4825

-----Original Message-----

From: Diana Mason [mailto:dianawhitney@utah.gov]
 Sent: Friday, June 08, 2007 7:45 AM
 To: Mandie Crozier
 Subject: Re: Newfield Tribal APD's

Yes, will you send them into us to. Thanks

>>> "Mandie Crozier" <mcrozier@newfield.com> 6/7/2007 1:40 PM >>>
 I have had to amend the 10 point plan for all of the Tribal Permits. The BLM has requested that we have a more detailed casing and cement design. I was not sure if you guys needed a copy of those amendment or not. All of the depths have stayed the same.

Mandie Crozier
 Newfield Production
 Phone: (435)646-4825
 Fax: (435) 646-3031



JON M. HUNTSMAN, JR.
Governor

GARY R. HERBERT
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil Gas and Mining

JOHN R. BAZA
Division Director

October 1, 2007

Newfield Production Company
Rt. #3, Box 3630
Myton, UT 84052

Re: Ute Tribal 15-19-4-2 Well, 579' FSL, 2106' FEL, SW SE, Sec. 19, T. 4 South, R. 2 West,
Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-33662.

Sincerely,

Gil Hunt
Associate Director

pab
Enclosures

cc: Duchesne County Assessor
UTE INDIAN TRIBE



Operator: Newfield Production Company
Well Name & Number Ute Tribal 15-19-4-2
API Number: 43-013-33662
Lease: 2OG0005609

Location: SW SE Sec. 19 T. 4 South R. 2 West

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

2. Notification Requirements

Notify the division within 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dustin Doucet at (801) 538-5281 (801) 733-0983 home


3. Reporting Requirements

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.

5. Compliance with the Conditions of Approval/Application for Permit to Drill outlined in the Statement of Basis. (Copy Attached)

6. This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.



UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0136
Expires January 31, 2004

APPLICATION FOR PERMIT TO DRILL OR REENTER

| | | |
|--|--|--|
| 1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER | | 5. Lease Serial No. 20G0005609 |
| 1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone | | 6. If Indian, Allottee or Tribe Name Ute |
| 2. Name of Operator Newfield Production Company | | 7. If Unit or CA Agreement, Name and No. N/A |
| 3a. Address Route #3 Box 3630, Myton UT 84052 | 3b. Phone No. (include area code) (435) 646-3721 | 8. Lease Name and Well No. Ute Tribal 15-19-4-2 |
| 4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface SWSE 579' FSL 2106' FEL At proposed prod. zone | | 9. API Well No. 43-013-33662 |
| 14. Distance in miles and direction from nearest town or post office* Approximatley 12.3 miles southwest of Myton, Utah | | 10. Field and Pool, or Exploratory Monument Butte |
| 15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 534' f/lse, NA' f/unit | 16. No. of Acres in lease NA | 11. Sec., T., R., M., or Blk. and Survey or Area SW/SE Sec. 19, T4S R2W |
| 17. Spacing Unit dedicated to this well 40 Acres | 18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. NA | 12. County or Parish Duchesne |
| 19. Proposed Depth 6800' | 20. BLM/BIA Bond No. on file B002792 | 13. State UT |
| 21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5498' GL | 22. Approximate date work will start* 3rd Quarter 2007 | 23. Estimated duration Approximately seven (7) days from spud to rig release. |

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be required by the authorized officer.

| | | |
|--|--|-----------------|
| 25. Signature <i>Mandie Crozier</i> | Name (Printed/Typed) Mandie Crozier | Date 5/11/07 |
|--|--|-----------------|

| | | |
|---|--|--------------------|
| Title Regulatory Specialist | Name (Printed/Typed) <i>James Newells</i> | Date 11-13-2007 |
| Approved by (Signature) <i>[Signature]</i> | Office VERNAL FIELD OFFICE | |
| Title Assistant Field Manager Lands & Mineral Resources | | |

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on reverse)

CONDITIONS OF APPROVAL ATTACHED

NOTICE OF APPROVAL

RECEIVED

NOV 19 2007

DIV. OF OIL, GAS & MINING



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East VERNAL, UT 84078 (435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company **Location:** SWSE, Sec 19, T4S, R2W
Well No: Ute Tribal 15-19-4-2 **Lease No:** 2OG0005609
API No: 43-047-33662 **Agreement:** N/A

| Title | Name | Office Phone Number | Cell Phone Number |
|-----------------------------------|-----------------|---------------------|-------------------|
| Petroleum Engineer: | Matt Baker | (435) 781-4490 | (435) 828-4470 |
| Petroleum Engineer: | Michael Lee | (435) 781-4432 | (435) 828-7875 |
| Petroleum Engineer: | James Ashley | (435) 781-4470 | (435) 828-7874 |
| Petroleum Engineer: | Ryan Angus | (435) 781-4430 | (435) 828-7368 |
| Supervisory Petroleum Technician: | Jamie Sparger | (435) 781-4502 | (435) 828-3913 |
| NRS/Enviro Scientist: | Paul Buhler | (435) 781-4475 | (435) 828-4029 |
| NRS/Enviro Scientist: | Karl Wright | (435) 781-4484 | (435) 828-7381 |
| NRS/Enviro Scientist: | Holly Villa | (435) 781-4404 | |
| NRS/Enviro Scientist: | | (435) 781-4476 | |
| NRS/Enviro Scientist: | Chuck MacDonald | (435) 781-4441 | (435) 828-7481 |
| NRS/Enviro Scientist: | Jannice Cutler | (435) 781-3400 | (435) 828-3544 |
| NRS/Enviro Scientist: | Michael Cutler | (435) 781-3401 | (435) 828-3546 |
| NRS/Enviro Scientist: | Anna Figueroa | (435) 781-3407 | (435) 828-3548 |
| NRS/Enviro Scientist: | Verlyn Pindell | (435) 781-3402 | (435) 828-3547 |
| NRS/Enviro Scientist: | Darren Williams | (435) 781-4447 | |
| NRS/Enviro Scientist: | Nathan Packer | (435) 781-3405 | (435) 828-3545 |

Fax: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

- | | |
|---|---|
| Construction Activity | - The Ute Tribe Energy & Minerals Dept. shall be notified in writing 48 hours in advance of any construction activity. The Ute Tribal office is open Monday through Thursday. |
| Construction Completion | - Upon completion of the pertinent APD/ROW construction, notify the Ute Tribe Energy & Minerals Dept. for a Tribal Technician to verify the Affidavit of Completion. |
| Spud Notice (Notify Petroleum Engineer) | - Twenty-Four (24) hours prior to spudding the well. |
| Casing String & Cementing (Notify Supv. Petroleum Tech.) | - Twenty-Four (24) hours prior to running casing and cementing all casing strings. |
| BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.) | - Twenty-Four (24) hours prior to initiating pressure tests. |
| First Production Notice (Notify Petroleum Engineer) | - Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days. |

SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)

- All areas of disturbance (including surface pipelines) must have appropriate surface use agreements or approvals in place with the proper owner and/or agency before such action is started.

DOWNHOLE CONDITIONS OF APPROVAL

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

SITE SPECIFIC DOWNHOLE CONDITIONS OF APPROVAL

- Production Casing cement top shall be a minimum of 200 feet above the surface casing shoe.
- Logging: Run gamma ray and electric logs from TD to surface casing.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person

making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- Chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be

filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

DIVISION OF OIL, GAS AND MINING

SPUDDING INFORMATION

Name of Company: NEWFIELD PRODUCTION COMPANY

Well Name: UTE TRIBAL 15-19-4-2

Api No: 43-013-33662 Lease Type: IND – FEE SURF

Section 19 Township 04S Range 02W County DUCHESNE

Drilling Contractor NDSI RIG # NS#1

SPUDDED:

Date 02/08/08

Time 3:00 PM

How DRY

Drilling will Commence: _____

Reported by BRANDON HALL

Telephone # (435) 828-6110

Date 02/11/08 Signed CHD

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE. Other Instructions on reverse side

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
 NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
 Myton, UT 84052

3b. Phone (include area code)
 435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
 SWSE Section 19 T4S R2W

5. Lease Serial No.
 FEE

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.
 UTE TRIBAL 15-19-4-2

9. API Well No.
 43013-33622

10. Field and Pool, or Exploratory Area
 MONUMENT BUTE

11. County or Parish, State
 DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

| TYPE OF SUBMISSION | TYPE OF ACTION | | | |
|---|--|---|---|--|
| <input type="checkbox"/> Notice of Intent | <input type="checkbox"/> Acidize | <input type="checkbox"/> Deepen | <input type="checkbox"/> Production(Start/Resume) | <input type="checkbox"/> Water Shut-Off |
| <input checked="" type="checkbox"/> Subsequent Report | <input type="checkbox"/> Alter Casing | <input type="checkbox"/> Fracture Treat | <input type="checkbox"/> Reclamation | <input type="checkbox"/> Well Integrity |
| <input type="checkbox"/> Final Abandonment | <input type="checkbox"/> Casing Repair | <input type="checkbox"/> New Construction | <input type="checkbox"/> Recomplete | <input checked="" type="checkbox"/> Other _____ Spud Notice |
| | <input type="checkbox"/> Change Plans | <input type="checkbox"/> Plug & Abandon | <input type="checkbox"/> Temporarily Abandon | |
| | <input type="checkbox"/> Convert to | <input type="checkbox"/> Plug Back | <input type="checkbox"/> Water Disposal | |

13--Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 2/8/08 MIRU NDSI NS#1. Spud well @ 3:00pm. Drill 320' of 12 1/4" hole with air mist. TIH W/ 7 Jt's 8 5/8" J-55 24 # csgn. Set @ 324 33' KB On 2/10/08/cement with 160 sks of class "G" w/ 3% CaCL2 + 1/4# sk Cello- Flake Mixed @ 15.8 ppg > 1.17 cf/ sk yield. Returned 4 bbis cement to pit. WOC.

I hereby certify that the foregoing is true and correct (Printed/ Typed)
 Don Bastian
 Signature: *Don Bastian*

Title
 Drilling Foreman

Date
 02/11/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED
FEB 12 2008
 DIV. OF OIL, GAS & MINING

NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

_____ **8 5/8** _____ CASING SET AT _____ **324.33** _____

LAST CASING 8 5/8" SET AT 324.33'
 DATUM 12' KB
 DATUM TO CUT OFF CASING _____
 DATUM TO BRADENHEAD FLANGE _____
 TD DRILLER 320' LOGGER _____
 HOLE SIZE 12 1/4

OPERATOR NewField Production Company
 WELL Ute Tribal 15-19-4-2W
 FIELD/PROSPECT Monument Butte
 CONTRACTOR & RIG # NDSI NS #1

LOG OF CASING STRING:

| PIECES | OD | ITEM - MAKE - DESCRIPTION | WT / FT | GRD | THREAD | CONDT | LENGTH |
|---|--------|---|---------------------|------------------|--|-------|---------------|
| | | Shoe Joint 44.68' | | | | | |
| | | WHI - 92 csg head | | | 8rd | A | 0.95 |
| 7 | 8 5/8" | Maverick ST&C csg | 24# | J-55 | 8rd | A | 312.48 |
| | | GUIDE shoe | | | 8rd | A | 0.9 |
| CASING INVENTORY BAL. | | | FEET | JTS | TOTAL LENGTH OF STRING | | 314.33 |
| TOTAL LENGTH OF STRING | | | 314.33 | 7 | LESS CUT OFF PIECE | | 2 |
| LESS NON CSG ITEMS | | | 1.85 | | PLUS DATUM TO T/CUT OFF CSG | | 12 |
| PLUS FULL JTS. LEFT OUT | | | 0 | | CASING SET DEPTH | | 324.33 |
| TOTAL | | | 312.48 | 7 | } COMPARE | | |
| TOTAL CSG. DEL. (W/O THRDS) | | | 312.48 | 7 | | | |
| TIMING | | | 1ST STAGE | | | | |
| BEGIN RUN CSG. | | | Spud 3:00 PM | 2/8/2008 | GOOD CIRC THRU JOB <u>Yes</u> | | |
| CSG. IN HOLE | | | 3:30 PM | 2/9/2008 | Bbls CMT CIRC TO SURFACE <u>4</u> | | |
| BEGIN CIRC | | | 3:24 PM | 2/10/2008 | RECIPROCATED PIPE FOR _____ THRU _____ FT STROKE | | |
| BEGIN PUMP CMT | | | 3:34 PM | 2/10/2008 | N/A | | |
| BEGIN DSPL. CMT | | | 3:50 PM | 2/10/2008 | BUMPED PLUG TO <u>101</u> PSI | | |
| PLUG DOWN | | | 4:00 PM | 2/10/2008 | | | |
| CEMENT USED | | CEMENT COMPANY- B. J. | | | | | |
| STAGE | # SX | CEMENT TYPE & ADDITIVES | | | | | |
| | 160 | Class "G" w/ 2% CaCL2 + 1/4#/sk Cello-Flake mixed @ 15.8 ppg 1.17 cf/sk yield | | | | | |
| CENTRALIZER & SCRATCHER PLACEMENT | | | SHOW MAKE & SPACING | | | | |
| Centralizers - Middle first, top second & third for 3 | | | | | | | |

COMPANY REPRESENTATIVE Don Bastian DATE 2/10/2008

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM -FORM 6

OPERATOR: NEWFIELD PRODUCTION COMPANY
ADDRESS: RT. 9 BOX 3630
MYTON, UT 84062

OPERATOR ACCT. NO. N2695

| ACTION CODE | CURRENT ENTITY NO. | NEW ENTITY NO. | API NUMBER | WELL NAME | WELL LOCATION | | | | SPUD DATE | EFFECTIVE DATE | |
|--|--------------------|----------------|------------|-----------------------|---------------|----|----|-----|-----------|----------------|---------|
| | | | | | QQ | SC | TP | RG | | | COUNTY |
| A | 99999 | 16691 | 4304733661 | Ute Tribal 11-30-4-2W | NESW | 30 | 4S | 2W | Duchesne | 2/7/2008 | 2/15/08 |
| WELL 1 COMMENTS: <i>GRRV 4301333661</i> | | | | | | | | | | | |
| A | 99999 | 16692 | 4304733662 | Ute Tribal 15-19-4-2W | NESW | 19 | 4S | 2W | Duchesne | 2/8/2008 | 2/15/08 |
| WELL 2 COMMENTS: <i>GRRV 4301333662 9WSE</i> | | | | | | | | | | | |
| A | 99999 | 16693 | 4301333119 | Federal 8-20-9-17 | SENE | 20 | 9S | 17E | Duchesne | 2/4/2008 | 2/15/08 |
| WELL 3 COMMENTS: <i>GRRV 43-013-33227</i> | | | | | | | | | | | |
| A | 99999 | 16694 | 4301333179 | Federal 12-23-9-16 | NWSW | 23 | 9S | 16E | Duchesne | 2/5/2008 | 2/15/08 |
| WELL 4 COMMENTS: <i>GRRV</i> | | | | | | | | | | | |
| | | | | | | | | | | | |
| WELL 5 COMMENTS: | | | | | | | | | | | |
| | | | | | | | | | | | |
| WELL 6 COMMENTS: | | | | | | | | | | | |

- ACTION CODES (See instructions on back of form)
- A - 1 new entity for new well (single well only)
 - B - well to existing entity (group or unit well)
 - C - from one existing entity to another existing entity
 - D - well from one existing entity to a new entity
 - E - other (explain in comments section)

RECEIVED
FEB 12 2008

Tammi Lee
Signature
Tammi Lee
Production Clerk
Date 02/12/08

NOTE: Use COMMENT section to explain why each Action Code was selected.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No
FEE

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.
UTE TRIBAL 15-19-4-2

9. API Well No.
4301333662

10. Field and Pool, or Exploratory Area
MONUMENT BUTTE

11. County or Parish, State
DUCHESNE, UT

SUBMIT IN TRIPlicate. Other Instructions on reverse side

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address: (Route) 3 Box 3630
Myton, UT 84052

3b. Phone (include area code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
SWSE Section 19 T4S R2W

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

| TYPE OF SUBMISSION | TYPE OF ACTION | | |
|---|--|---|---|
| <input type="checkbox"/> Notice of Intent | <input type="checkbox"/> Acidize | <input type="checkbox"/> Deepen | <input type="checkbox"/> Production(Start/Resume) |
| <input checked="" type="checkbox"/> Subsequent Report | <input type="checkbox"/> Alter Casing | <input type="checkbox"/> Fracture Treat | <input type="checkbox"/> Reclamation |
| <input type="checkbox"/> Final Abandonment | <input type="checkbox"/> Casing Repair | <input type="checkbox"/> New Construction | <input type="checkbox"/> Recomplete |
| | <input type="checkbox"/> Change Plans | <input type="checkbox"/> Plug & Abandon | <input type="checkbox"/> Temporarily Abandon |
| | <input type="checkbox"/> Convert to | <input type="checkbox"/> Plug Back | <input type="checkbox"/> Water Disposal |
| | | | <input type="checkbox"/> Water Shut-Off |
| | | | <input type="checkbox"/> Well Integrity |
| | | | <input checked="" type="checkbox"/> Other _____ |
| | | | Weekly Status Report _____ |

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final reclamation.

On 2/15/08, MIRU Patterson #155. Set all equipment. Pressure test Kelly, TIW, Choke manifold, & Bop's to 2,000 psi. Test 8.625 csgn to 1,500 psi. Vernal BLM field, & Roosevelt DOGM office was notified of test. PU BHA and tag cement @ 280'. Drill out cement & shoe. Drill a 7.875 hole with fresh water to a depth of 6750'. Lay down drill string & BHA. Open hole log w/ Dig/SP/GR log's TD to surface. PU & TIH with Guide shoe, shoe jt, float collar, 157 jt's of 5.5 J-55, 15.5# csgn. Set @ 6757.94' / KB. Cement with 325 sks cement mixed @ 11.0 ppg & 3.43 yld. The 450 sks cement mixed @ 14.4 ppg & 1.24 yld. Returned 26 bbls of cement to reserve pit. Nipple down Bop's. Drop slips @ 98,000 #'s tension. Release rig @ 11:30 pm

I hereby certify that the foregoing is true and correct (Printed/Typed)
Don Bastian

Signature: *Don Bastian*

Title: Drilling Foreman

Date: 02/21/2008

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____ Title _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office _____

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED

FEB 22 2008

DIV. OF OIL, GAS & MINING

NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

5 1/2" CASING SET AT 6757.94

Flt cllr @ 6700.28

LAST CASING 8 5/8" Set @ 324.33
 DATUM 12' KB
 DATUM TO CUT OFF CASING 12'
 DATUM TO BRADENHEAD FLANGE _____
 TD DRILLER 6750' TD loggers 6760'
 HOLE SIZE 7 7/8"

OPERATOR Newfield Production Company
 WELL Ute Tribal 15-19-4-2 W
 FIELD/PROSPECT Monument Butte
 CONTRACTOR & RIG # Patterson # 155

| LOG OF CASING STRING: | | | | | | | |
|---|--------|---|---------------------|-----------------------------|--------|-------|----------------|
| PIECES | OD | ITEM - MAKE - DESCRIPTION | WT / FT | GRD | THREAD | CONDT | LENGTH |
| | | Landing Jt | | | | | |
| | | Short jt 6.88' @ 4723.49' | | | | | |
| 157 | 5 1/2" | ETC LT & C casing | 15.5# | J-55 | 8rd | A | 6729.71 |
| | | | | | | | 0.6 |
| 1 | 5 1/2" | ETC LT&C csg | 15.5# | J-55 | 8rd | A | 43.38 |
| | | GUIDE shoe | | | 8rd | A | 0.65 |
| CASING INVENTORY BAL. | | FEET | JTS | TOTAL LENGTH OF STRING | | | 6774.34 |
| TOTAL LENGTH OF STRING | | 6788.34 | 158 | LESS CUT OFF PIECE | | | 16.4 |
| LESS NON CSG. ITEMS | | 15.25 | | PLUS DATUM TO T/CUT OFF CSG | | | |
| PLUS FULL JTS. LEFT OUT | | 169.37 | 5 | CASING SET DEPTH | | | 6757.94 |
| TOTAL | | 6942.46 | 163 | } COMPARE | | | |
| TOTAL CSG. DEL. (W/O THRDS) | | 6942.46 | 163 | | | | |
| TIMING | | 1ST STAGE | 2nd STAGE | | | | |
| BEGIN RUN CSG. | | 6:00 AM | 2/20/2008 | GOOD CIRC THRU JOB | | | Yes |
| CSG. IN HOLE | | 2:30 AM | 2/20/2008 | Bbls CMT CIRC to surface | | | 26 |
| BEGIN CIRC. | | 2:50 PM | 2/20/2008 | RECIPROCATED PIPE FOR | | | THRUSTROKE |
| BEGIN PUMP CMT | | 4:29 PM | 2/20/2008 | DID BACK PRES. VALVE HOLD ? | | | Yes |
| BEGIN DSPL CMT | | 5:30 PM | 2/20/2008 | BUMPED PLUG TO | | | 2481 PSI |
| PLUG DOWN | | 5:50 PM | 2/20/2008 | | | | |
| CEMENT USED | | CEMENT COMPANY- B. J. | | | | | |
| STAGE | #SX | CEMENT TYPE & ADDITIVES | | | | | |
| 1 | 325 | Premlite II w/ + 3 % KCL, 5#s /sk CSE + 2# sk/kolseal +.5SMS+FP+SF | | | | | |
| | | mixed @ 11.0 ppg W / 3.49 cf/sk yield | | | | | |
| 2 | 450 | 50/50:2 W/ 2% Gel + 3% KCL, .5%EC1, 1/4# skC.F.2%SF+.3% SMS+FP-6L mixed @14.4 ppgW/ 1.24YLD | | | | | |
| CENTRALIZER & SCRATCHER PLACEMENT | | | SHOW MAKE & SPACING | | | | |
| Centralizers - Middle first, top second & third. Then every third collar for a total of 20. | | | | | | | |

COMPANY REPRESENTATIVE Don Bastian DATE 2/20/2008

BEGIN DSPL
 PLUG DOWN
 CEMENT LOG
 MARK

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other instructions on reverse side

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
 NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
 Myton, UT 84052

3b. Phone (include area code)
 435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
 SWSE Section 19 T4S R2W

5. Lease Serial No.
 FEE

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.
 UTE TRIBAL 15-19-4-2

9. API Well No.
 4301333662

10. Field and Pool, or Exploratory Area
 MONUMENT BUTTE

11. County or Parish, State
 DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

| TYPE OF SUBMISSION | TYPE OF ACTION | | | |
|---|--|---|---|---|
| <input type="checkbox"/> Notice of Intent | <input type="checkbox"/> Acidize | <input type="checkbox"/> Deepen | <input type="checkbox"/> Production(Start/Resume) | <input type="checkbox"/> Water Shut-Off |
| <input checked="" type="checkbox"/> Subsequent Report | <input type="checkbox"/> Alter Casing | <input type="checkbox"/> Fracture Treat | <input type="checkbox"/> Reclamation | <input type="checkbox"/> Well Integrity |
| <input type="checkbox"/> Final Abandonment | <input type="checkbox"/> Casing Repair | <input type="checkbox"/> New Construction | <input type="checkbox"/> Recomplete | <input checked="" type="checkbox"/> Other _____ |
| | <input type="checkbox"/> Change Plans | <input type="checkbox"/> Plug & Abandon | <input type="checkbox"/> Temporarily Abandon | Weekly Status Report |
| | <input type="checkbox"/> Convert to | <input type="checkbox"/> Plug Back | <input type="checkbox"/> Water Disposal | |

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

The above mentioned well went on production 3/20/08. See attached daily activity report.

| | |
|---|---------------------------|
| I hereby certify that the foregoing is true and correct (Printed/ Typed) Tammi Lee | Title Production Clerk |
| Signature | Date 03/24/2008 |

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

| | | |
|---|--------|------|
| Approved by | Title | Date |
| Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon. | Office | |

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED

MAR 26 2008

DIV. OF OIL, GAS & MINING

Daily Activity Report

Format For Sundry

UTE TRIBAL 15-19-4-2

1/1/2008 To 5/30/2008

3/8/2008 Day: 1**Completion**

Rigless on 3/7/2008 - Install 5m frac head. NU 6" 5K Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head, csg & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 6679' & cement top @ 230'. Perforate stage #1, CP2 sds @ 6357-64' & CP1 sds @ 6280-90' w/ 3-1/8" Slick Guns (19 gram, .49"EH, 120°) w/ 4 spf for total of 52 shots. 160 BWTR. SWIFN.

3/16/2008 Day: 2**Completion**

Rigless on 3/15/2008 - Stage #1 CP1 & CP2 sds. RU BJ Services. 108 psi on well. Frac CP1 & CP2 sds w/ 24,676#'s of 20/40 sand in 377 bbls of Lightning 17 fluid. Broke @ 2841 psi. Treated w/ ave pressure of 2637 psi w/ ave rate of 23.0 BPM. ISIP 2557 psi. Leave pressure on well. 537 BWTR. Stage #2 LODC sds. RU Lone Wolf, llc WLT, crane & Lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 24' perf gun. Set plug @ 6090'. Perforate LODC sds @ 5970-94' w/ 3-1/8" Slick Guns (.369"EH, 22.7 gram, 90°) w/ 4 spf for total of 96 shots. RU BJ Services. 2183 psi on well. Frac LODC sds w/ 109,924#'s of 20/40 sand in 837 bbls of Lightning 17 fluid. Broke @ 3981 psi. Treated w/ ave pressure of 2469 psi w/ ave rate of 23.1 BPM. ISIP 2799 psi. Leave pressure on well. 1374 BWTR. Stage #3 A1 sds. RU Lone Wolf, llc WLT, crane & Lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 18' perf gun. Set plug @ 5870'. Perforate A1 sds @ 5770-88' w/ 3-1/8" Slick Guns (.369"EH, 22.7 gram, 90°) w/ 4 spf for total of 72 shots. RU BJ Services. 2096 psi on well. Frac A1 sds w/ 95,349#'s of 20/40 sand in 747 bbls of Lightning 17 fluid. Broke @ 3970 psi. Treated w/ ave pressure of 2257 psi w/ ave rate of 23.2 BPM. ISIP 2656 psi. Leave pressure on well. 2121 BWTR. stage #4 D3 sds. RU Lone Wolf, llc WLT, crane & Lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 6' perf gun. Set plug @ 5520'. Perforate D3 sds @ 5410-16' w/ 3-1/8" Slick Guns (.369"EH, 22.7 gram, 90°) w/ 4 spf for total of 24 shots. RU BJ Services. 1263 psi on well. Frac D3 sds w/ 24,601#'s of 20/40 sand in 383 bbls of Lightning 17 fluid. Broke @ 4161 psi. Treated w/ ave pressure of 2210 psi w/ ave rate of 23.2 BPM. ISIP 2656 psi. Leave pressure on well. 2504 BWTR. Stage #5 D1 sds. RU Lone Wolf, llc WLT, crane & Lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 15' perf gun. Set plug @ 5350'. Perforate D1 sds @ 5307-22' w/ 3-1/8" Slick Guns (.369"EH, 22.7 gram, 90°) w/ 4 spf for total of 60 shots. RU BJ Services. 1608 psi on well. Perfs would not break. Dump bail acid on perfs. RU BJ Services. 1324 psi on well. Frac D3 sds w/ 100,224#'s of 20/40 sand in 757 bbls of Lightning 17 fluid. Broke @ 3615 psi. Treated w/ ave pressure of 2317 psi w/ ave rate of 23.1 BPM. ISIP 2545 psi. Leave pressure on well. 3261 BWTR. Stage #6 GB4 & GB6 sds. RU Lone Wolf, llc WLT, crane & Lubricator. RIH w/ Weatherford 5-1/2" 6K composite flow through frac plug & 6', 9' perf guNS. Set plug @ 4960'. Perforate GB4 sds @ 4804-10' & GB6 sds @ 4853-62' w/ 3-1/8" Slick Guns (.369"EH, 22.7 gram, 90°) w/ 4 spf for total of 60 shots. RU BJ Services. 2161 psi on well. Frac GB4 & GB6 sds w/ 67,221#'s of 20/40 sand in 534 bbls of Lightning 17 fluid. Broke @ 3369 psi. Treated w/ ave pressure of 2756 psi w/ ave rate of 23.1 BPM. ISIP 2840 psi. Open well to pit for immediate flowback @ approx. 1 bpm. Well flowed for 8 hrs. & died. Recovered 450 bbls water.

3/18/2008 Day: 3**Completion**

Western #1 on 3/17/2008 - MIRU Western #1. Bleed off well. ND Cameron BOP & 5m frac head. NU 3m production head & Schafer BOP. RIH w/ 4 3/4" chomp bit, bit sub & 78 jts new 2 7/8" tbg. from pipe rack (drifting & tallying). SWIFN.

3/19/2008 Day: 4**Completion**

Western #1 on 3/18/2008 - Bleed off well. RIH w/ tbg. Tag @ 4877'. RU powerswivel & pump. C/O to CBP @ 4960'. DU CBP in 10 min. Cont. RIH w/ tbg. Tag CBP @ 5350'. DU CBP in 20 min.

Cont. RIH w/ tbg. Tag CBP @ 5520'. DU CBP in 19 min. Cont. RIH w/ tbg. Tag fill @ 5782'. C/O to CBP @ 5870'. DU CBP in 25 min. Cont. RIH w/ tbg. Tag fill @ 6070'. C/O to CBP @ 6090'. DU CBP in 24 min. Cont. RIH w/ tbg. Tag @ 6573'. C/O to PBSD @ 6713'. Circulate well clean. Pull up to 6633'. SWIFN.

3/20/2008 Day: 5

Completion

Western #1 on 3/19/2008 - Open well to pit. Well flowed for 2.5 hrs. Recovered 170 bbls. RU pump to tbg. Pump 30 bbls water down tbg. RIH w/ tbg. Tag PBSD @ 6713'. Circulate well w/ 200 bbls brine water. POOH w/ tbg. LD BHA. RIH w/ 2 7/8" notched collar, 2 jts 2 7/8" tbg., PSN, 1 jt 2 7/8" tbg., 5 1/2" TAC, 201 jts 2 7/8" tbg. ND BOP. Set TAC @ 6324' w/ 16,000# tension. NU wellhead. X-over for rods. Flush tbg. w/ 60 bbls water. RIH w/ CDI 2 1/2" x 1 1/2" x 14' x 18' RHAC pump, 6- 1 1/2" weight bars, 20- 3/4" guided rods, 89- 3/4" slick rods. SWIFN.

3/21/2008 Day: 6

Completion

Western #1 on 3/20/2008 - Cont. RIH w/ rods. Seat pump. Fill tbg. w/ 5 bbls water. Stroke test to 800 psi. RU pumping unit. Hang off rods. Adjust tag. RD. PWOP @ 2:00 p.m. 86" stroke length, 5 spm. Final Report.

Pertinent Files: Go to File List

(See other instructions on reverse side)

OMB NO. 1004-0137

Expires: February 28, 1995

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

WELL COMPLETION OR RECOMPLETION REPORT AND LOG*

1a. TYPE OF WORK

OIL WELL GAS WELL DRY Other _____

1b. TYPE OF WELL

NEW WELL WORK OVER DEEPEN PLUG BACK DIFF RESVR. Other _____

2. NAME OF OPERATOR

Newfield Exploration Company

3. ADDRESS AND TELEPHONE NO.

1401 17th St. Suite 1000 Denver, CO 80202

4. LOCATION OF WELL (Report locations clearly and in accordance with any State requirements.*)

At Surface 579' FSL & 2106' FEL (SW/SE) Sec. 19, T4S, R2W

At top prod. Interval reported below

At total depth

14. API NO. 43-013-33662 DATE ISSUED 10/01/07

12. COUNTY OR PARISH Duchesne 13. STATE UT

15. DATE SPUNDED 02/08/08 16. DATE T.D. REACHED 02/19/08 17. DATE COMPL. (Ready to prod.) 03/20/08 18. ELEVATIONS (DF, RKB, RT, GR, ETC.)* 5498' GL 5510' KB 19. ELEV. CASINGHEAD

20. TOTAL DEPTH, MD & TVD 6750' 21. PLUG BACK T.D., MD & TVD 6713' 22. IF MULTIPLE COMPL., HOW MANY* 23. INTERVALS DRILLED BY -----> ROTARY TOOLS X CABLE TOOLS

24. PRODUCING INTERVAL(S), OF THIS COMPLETION--TOP, BOTTOM, NAME (MD AND TVD)* Green River 4804'-6364' 25. WAS DIRECTIONAL SURVEY MADE No

26. TYPE ELECTRIC AND OTHER LOGS RUN Dual Induction Guard, SP, Compensated Density, Compensated Neutron, GR, Caliper, Cement Bond Log 27. WAS WELL CORED No

CASING RECORD (Report all strings set in well)

| CASING SIZE/GRADE | WEIGHT, LB./FT. | DEPTH SET (MD) | HOLE SIZE | TOP OF CEMENT, CEMENTING RECORD | AMOUNT PULLED |
|-------------------|-----------------|----------------|-----------|---|---------------|
| 8-5/8" - J-55 | 24# | 324' | 12-1/4" | To surface with 160 sx Class "G" cmt | |
| 5-1/2" - J-55 | 15.5# | 6758' | 7-7/8" | 325 sx Premlite II and 450 sx 50/50 Poz | |

29. LINER RECORD 30. TUBING RECORD

| SIZE | TOP (MD) | BOTTOM (MD) | SACKS CEMENT* | SCREEN (MD) | SIZE | DEPTH SET (MD) | PACKER SET (MD) |
|------|----------|-------------|---------------|-------------|--------|----------------|-----------------|
| | | | | | 2-7/8" | EOT @ | TA @ |
| | | | | | | 6423' | 6324' |

31. PERFORATION RECORD (Interval, size and number) 32. ACID, SHOT, FRACTURE, CEMENT SQUEEZE, ETC.

| INTERVAL | SIZE | SPF/NUMBER | DEPTH INTERVAL (MD) | AMOUNT AND KIND OF MATERIAL USED |
|------------------------------------|-------|------------|---------------------|---|
| (CP2 & 1) 6357'-6364', 6280'-6290' | .49" | 4/68 | 6280'-6364' | Frac w/ 24,676# 20/40 sand in 377 bbls fluid |
| (LODC) 5970'-5994' | .369" | 4/96 | 5970'-5994' | Frac w/ 109,924# 20/40 sand in 837 bbls fluid |
| (A1) 5770'-5788' | .369" | 4/72 | 5770'-5788' | Frac w/ 95,349# 20/40 sand in 747 bbls fluid |
| (D3) 5410'-5416' | .369" | 4/24 | 5410'-5416' | Frac w/ 24,601# 20/40 sand in 383 bbls fluid |
| (D1) 5307'-5322' | .369" | 4/60 | 5307'-5322' | Frac w/ 100,244# 20/40 sand in 757 bbls fluid |
| (GB4 & 6) 4804'-4810', 4853'-4862' | .369" | 4/60 | 4804'-4862' | Frac w/ 67,221# 20/40 sand in 534 bbls fluid |

33.* PRODUCTION

| DATE FIRST PRODUCTION | PRODUCTION METHOD (Flowing, gas lift, pumping--size and type of pump) | WELL STATUS (Producing or shut-in) | | | | | |
|-----------------------|---|------------------------------------|-------------------------|-----------|-------------|-------------------------|---------------|
| 03/21/08 | 2-1/2" x 1-3/4" x 16' x 20' RHAC SM Plunger Pump | PRODUCING | | | | | |
| DATE OF TEST | HOURS TESTED | CHOKE SIZE | PROD'N. FOR TEST PERIOD | OIL--BBL. | GAS--MCF. | WATER--BBL. | GAS-OIL RATIO |
| 10 day ave | | | -----> | 706 | 245 | 131 | 347 |
| FLOW. TUBING PRESS. | CASING PRESSURE | CALCULATED 24-HOUR RATE | OIL-BBL. | GAS--MCF. | WATER--BBL. | OIL GRAVITY-API (CORR.) | |
| | | -----> | | RECEIVED | | | |

34. DISPOSITION OF GAS (Sold, used for fuel, vented, etc.) Sold & Used for Fuel TEST WITNESSED BY MAY 02 2008

35. LIST OF ATTACHMENTS

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records
SIGNED Jentri Park TITLE Production Technician DATE 4/24/2008

37. SUMMARY OF POROUS ZONES: (Show all important zones of porosity and contents thereof; cored intervals, and all drill-stem, tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures, and recoveries);

| FORMATION | TOP | BOTTOM | DESCRIPTION, CONTENTS, ETC. | GEOLOGIC MARKERS | |
|-----------|-----|--------|------------------------------------|------------------|------------------|
| | | | | MEAS. DEPTH | TRUE VERT. DEPTH |
| | | | Well Name Ute Tribal 15-19-4-2W | 4234' | |
| | | | | 4463' | |
| | | | | 4589' | |
| | | | | 4885' | |
| | | | | 5131' | |
| | | | | 5160' | |
| | | | | 5272' | |
| | | | | 5536' | |
| | | | | 5676' | |
| | | | | 6236' | |
| | | | | 6640' | |
| | | | | 6760' | |

NEWFIELD



Well Name: Ute Tribal 15-19-4-2
 LOCATION: S19, T4S, R2W
 COUNTY/STATE: Duchesne
 API: 43-013-33662

Spud Date: 2-8-08
 TD: 6750'
 CSG: 2-20-08
 POP: 3-20-08

| DATE | HRS | Oil (bbls) | Water (bbls) | Recovered Water (bbls) | Gas (mcf) | Casing Pressure (psi) | SPM | Comments |
|-----------|-----|-------------|--------------|------------------------|-------------|-----------------------|-------|--|
| 3/20/2008 | | | | 3205 | | | | POP @ 2:00 P.M. w/ 86" SL @ 5 SPM. 3205 Total water to recover. |
| 3/21/2008 | 17 | 80 | 110 | 3095 | 13 | 50 | 5 | tubing 50 |
| 3/22/2008 | 24 | 35 | 215 | 2880 | 40 | 300 | 5 | tubing 65 |
| 3/23/2008 | 24 | 112 | 110 | 2770 | 110 | 500 | 5 | tubing 400 |
| 3/24/2008 | 12 | 362 | 410 | 2360 | 171 | 900 | 5 | tubing 200. Clutched - oil sales. Transferred 60 bbls from T2 to T3. |
| 3/25/2008 | 7 | 618 | 178 | 2182 | 82 | 900 | 0 | tubing 200, flowing. |
| 3/26/2008 | 18 | 921 | 163 | 2019 | 267 | 500 | 5 | tubing 150 |
| 3/27/2008 | 24 | 1054 | 164 | 1855 | 399 | 350 | 5 | tubing 100 |
| 3/28/2008 | 20 | 874 | 131 | 1724 | 253 | 1400 | 5 | Down - water tank full |
| 3/29/2008 | 21 | 919 | 91 | 1633 | 251 | 500 | 5 | Tubing 200, Down - water haul. |
| 3/30/2008 | 24 | 762 | 90 | 1543 | 321 | 1000 | 4 1/2 | TUBING 400 |
| 3/31/2008 | 24 | 608 | 45 | 1498 | 167 | 1100 | 5 | Tubing 300 |
| 4/1/2008 | 24 | 548 | 64 | 1434 | 241 | 600 | 5 | |
| 4/2/2008 | 24 | 393 | 16 | 1418 | 296 | 1000 | 5 | TUBING 250 |
| 4/3/2008 | | | | 1418 | | | | |
| 4/4/2008 | | | | 1418 | | | | |
| 4/5/2008 | | | | 1418 | | | | |
| 4/6/2008 | | | | 1418 | | | | |
| 4/7/2008 | | | | 1418 | | | | |
| 4/8/2008 | | | | 1418 | | | | |
| 4/9/2008 | | | | 1418 | | | | |
| 4/10/2008 | | | | 1418 | | | | |
| 4/11/2008 | | | | 1418 | | | | |
| 4/12/2008 | | | | 1418 | | | | |
| 4/13/2008 | | | | 1418 | | | | |
| 4/14/2008 | | | | 1418 | | | | |
| 4/15/2008 | | | | 1418 | | | | |
| 4/16/2008 | | | | 1418 | | | | |
| 4/17/2008 | | | | 1418 | | | | |
| 4/18/2008 | | | | 1418 | | | | |
| 4/19/2008 | | | | 1418 | | | | |
| 4/20/2008 | | | | 1418 | | | | |
| | | 7286 | 1787 | | 2611 | | | |

| | |
|---|---|
| STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING | FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: 2OG0005609 |
|---|---|

| | |
|--|---|
| SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals. | 6. IF INDIAN, ALLOTTEE OR TRIBE NAME: UTE 7. UNIT or CA AGREEMENT NAME: |
|--|---|

| | |
|-----------------------------|--|
| 1. TYPE OF WELL Oil Well | 8. WELL NAME and NUMBER: UTE TRIBAL 15-19-4-2 |
|-----------------------------|--|

| | |
|---|----------------------------------|
| 2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY | 9. API NUMBER: 43013336620000 |
|---|----------------------------------|

| | | |
|---|-----------------------------------|--|
| 3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052 | PHONE NUMBER: 435 646-4825 Ext | 9. FIELD and POOL or WILDCAT: SOUTH MYTON BENCH |
|---|-----------------------------------|--|

| | |
|--|---|
| 4. LOCATION OF WELL FOOTAGES AT SURFACE: 0579 FSL 2106 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SWSE Section: 19 Township: 04.0S Range: 02.0W Meridian: U | COUNTY: DUCHESNE STATE: UTAH |
|--|---|

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

| TYPE OF SUBMISSION | TYPE OF ACTION | | |
|--|--|---|---|
| <input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 12/18/2013 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date: | <input type="checkbox"/> ACIDIZE <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> DEEPEN <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PRODUCTION START OR RESUME <input checked="" type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> WILDCAT WELL DETERMINATION | <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> OTHER | <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> PLUG BACK <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> APD EXTENSION OTHER: <input style="width: 100px;" type="text"/> |

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
 Newfield proposes to perforate and fracture stimulate from 5560-5569 with in the current production formation (Green River).

Approved by the Utah Division of Oil, Gas and Mining

Date: January 14, 2014

By: *Derek Quist*

| | | |
|---------------------------------------|------------------------------|--------------------------|
| NAME (PLEASE PRINT) Mandie Crozier | PHONE NUMBER 435 646-4825 | TITLE Regulatory Tech |
| SIGNATURE N/A | | DATE 12/18/2013 |
