

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL						1. WELL NAME and NUMBER Greater Monument Butte W-31-8-17		
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT MONUMENT BUTTE		
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO						5. UNIT or COMMUNITIZATION AGREEMENT NAME GMBU (GRRV)		
6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY						7. OPERATOR PHONE 435 646-4825		
8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052						9. OPERATOR E-MAIL mcrozier@newfield.com		
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU-020252A			11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>		
13. NAME OF SURFACE OWNER (if box 12 = 'fee')						14. SURFACE OWNER PHONE (if box 12 = 'fee')		
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')		
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>			19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/>		
20. LOCATION OF WELL		FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN
LOCATION AT SURFACE		673 FNL 1973 FWL		NENW	6	9.0 S	17.0 E	S
Top of Uppermost Producing Zone		103 FNL 2464 FWL		NENW	6	9.0 S	17.0 E	S
At Total Depth		124 FSL 2492 FEL		SWSE	31	8.0 S	17.0 E	S
21. COUNTY DUCHESNE			22. DISTANCE TO NEAREST LEASE LINE (Feet) 124			23. NUMBER OF ACRES IN DRILLING UNIT 20		
			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 1630			26. PROPOSED DEPTH MD: 6110 TVD: 6110		
27. ELEVATION - GROUND LEVEL 5304			28. BOND NUMBER WYB000493			29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 437478		
ATTACHMENTS								
VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES								
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER				<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN				
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)				<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER				
<input checked="" type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)				<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP				
NAME Mandie Crozier			TITLE Regulatory Tech			PHONE 435 646-4825		
SIGNATURE			DATE 01/13/2011			EMAIL mcrozier@newfield.com		
API NUMBER ASSIGNED 43013505840000			APPROVAL			 Permit Manager		

Proposed Hole, Casing, and Cement

String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Prod	7.875	5.5	0	6110		
Pipe	Grade	Length	Weight			
	Grade J-55 LT&C	6110	15.5			

Proposed Hole, Casing, and Cement						
String	Hole Size	Casing Size	Top (MD)	Bottom (MD)		
Surf	12.25	8.625	0	300		
Pipe	Grade	Length	Weight			
	Grade J-55 ST&C	300	24.0			

NEWFIELD PRODUCTION COMPANY
GREATER MONUMENT BUTTE W-31-8-17
AT SURFACE: NE/NW (LOT #3) SECTION 6, T9S, R17E
DUCHESNE COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta	0' – 1535'
Green River	1535'
Wasatch	6170'
Proposed TD	6110'

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation (Oil) 1535' – 6170'

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sampled Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO ₃) (mg/l)
Dissolved Bicarbonate (NaHCO ₃) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO ₄) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: Greater Monument Butte W-31-8-17**

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950 17.53	1,370 14.35	244,000 33.89
Prod casing 5-1/2"	0'	6,110'	15.5	J-55	LTC	4,810 2.47	4,040 2.08	217,000 2.29

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe = 13.0 ppg
 Pore pressure at surface casing shoe = 8.33 ppg
 Pore pressure at prod casing shoe = 8.33 ppg
 Gas gradient = 0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: Greater Monument Butte W-31-8-17**

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft ³ /sk)
			ft ³			
Surface casing	300'	Class G w/ 2% CaCl	138	30%	15.8	1.17
			161			
Prod casing Lead	4,110'	Prem Lite II w/ 10% gel + 3% KCl	284	30%	11.0	3.26
			926			
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363	30%	14.3	1.24
			451			

- *Actual volume pumped will be 15% over the caliper log
- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours
- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ±350 feet will be drilled with an air/mist system. The air rig is equipped with a 6 ½" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ±350 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.



10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the second quarter of 2011, and take approximately seven (7) days from spud to rig release.

R17E, S.L.B.&M.

NEWFIELD EXPLORATION COMPANY


WELL LOCATION, W-31-8-17, LOCATED AS SHOWN IN THE NE 1/4 NW 1/4 (LOT 3) OF SECTION 6, T9S, R17E, S.L.B.&M. DUCHESNE COUNTY, UTAH.

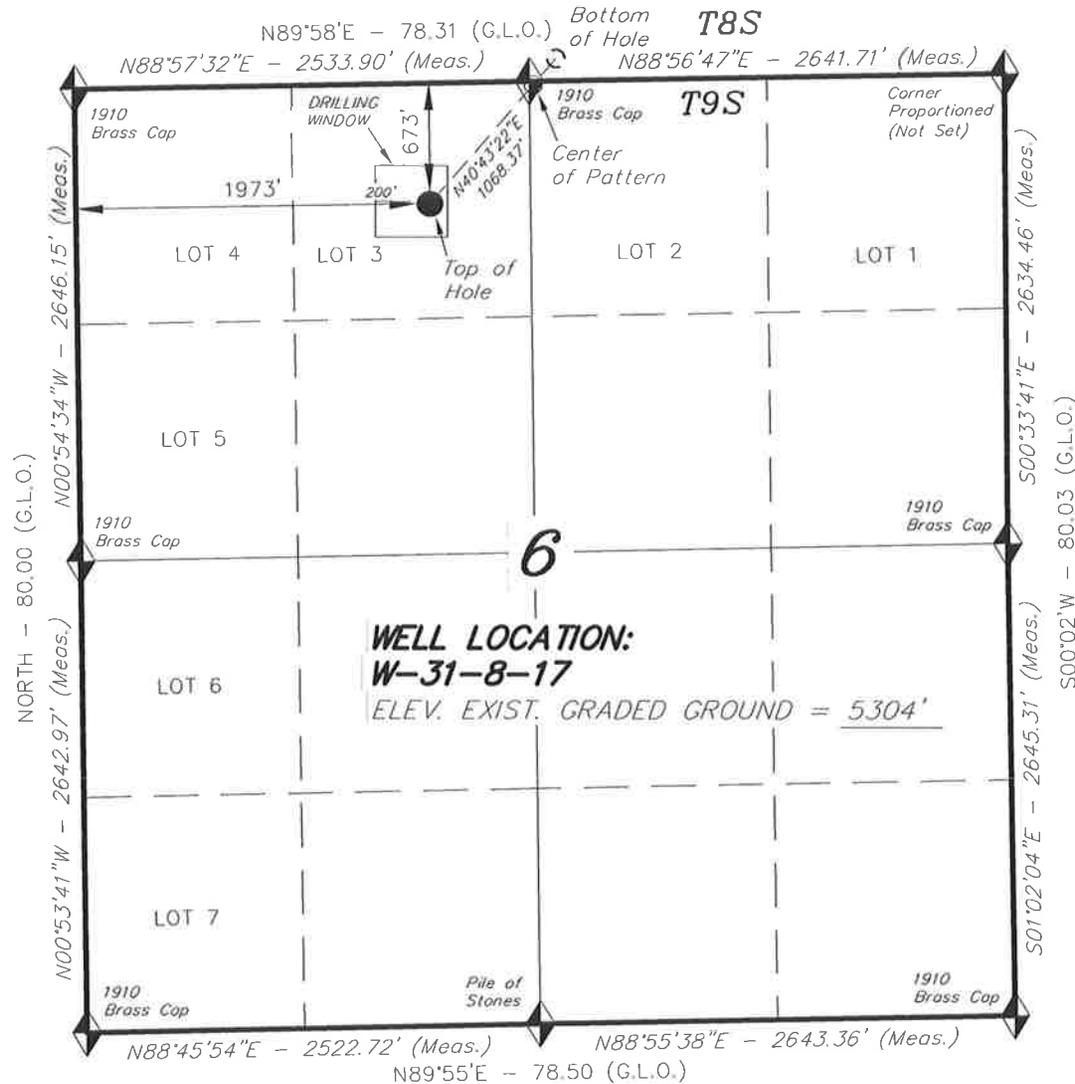

Note:
 1. The center of pattern footages are 20' FNL & 2620' FEL.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD AND ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are base on LOCATION: an N.G.S. OPUS Correction. LAT. 40°04'09.56" LONG. 110°00'43.28" (Tristate Aluminum Cap) Elev. 5281.57'



W-31-8-17
 (Surface Location) NAD 83
 LATITUDE = 40° 03' 54.97"
 LONGITUDE = 110° 03' 04.66"

TRI STATE LAND SURVEYING & CONSULTING 180 NORTH VERNAL AVE. - VERNAL, UTAH 84078 (435) 781-2501	
DATE SURVEYED: 07-14-10	SURVEYED BY: D.G.
DATE DRAWN: 07-22-10	DRAWN BY: M.W.
REVISED: 01-11-11 F.T.M.	SCALE: 1" = 1000'

R17E, S.L.B.&M.

NEWFIELD EXPLORATION COMPANY

TARGET BOTTOM HOLE, W-31-8-17,
 LOCATED AS SHOWN IN THE SW 1/4
 SE 1/4 OF SECTION 31, T8S, R17E,
 S.L.B.&M. DUCHESNE COUNTY, UTAH.

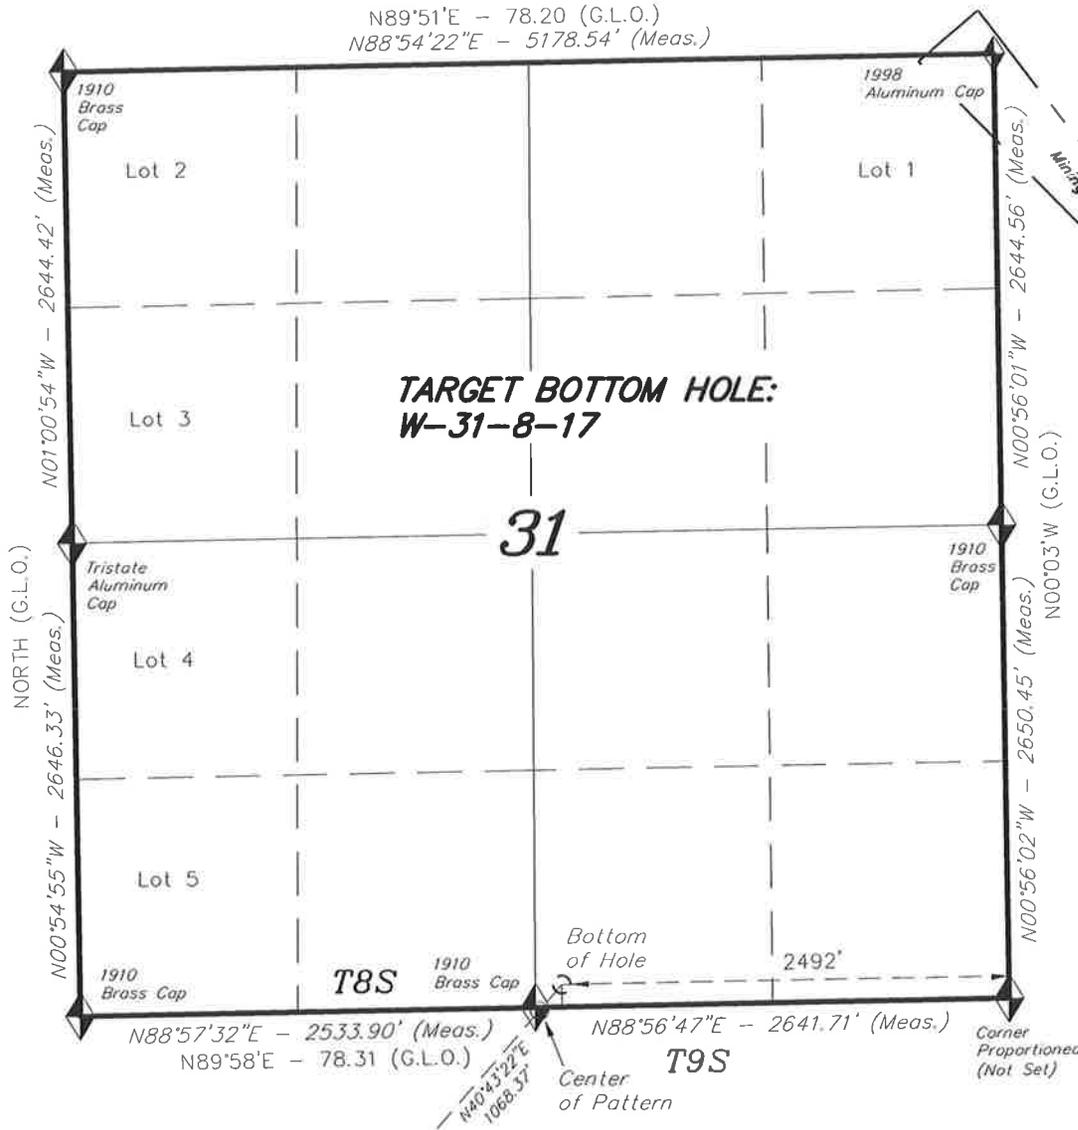


Note:

1. The bottom of hole footages are 124' FSL & 2492' FEL.


BASIS OF ELEV; Elevations are base on
 LOCATION: an N.G.S. OPUS Correction.
 LAT. $40^{\circ}04'09.56''$ LONG. $110^{\circ}00'43.28''$
 (Tristate Aluminum Cap) Elev. 5281.57'

THIS IS TO CERTIFY THAT THE ABOVE PLAN WAS
 PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
 MADE BY ME OR UNDER MY SUPERVISION AND THAT
 THE SAME ARE TRUE AND CORRECT TO THE BEST
 OF MY KNOWLEDGE AND BELIEF.



TRI STATE LAND SURVEYING & CONSULTING	
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078 (435) 781-2501	
DATE SURVEYED: 07-14-10	SURVEYED BY: D.G.
DATE DRAWN: 07-22-10	DRAWN BY: M.W.
REVISED: 01-11-11 F.T.M.	SCALE: 1" = 1000'

◆ = SECTION CORNERS LOCATED

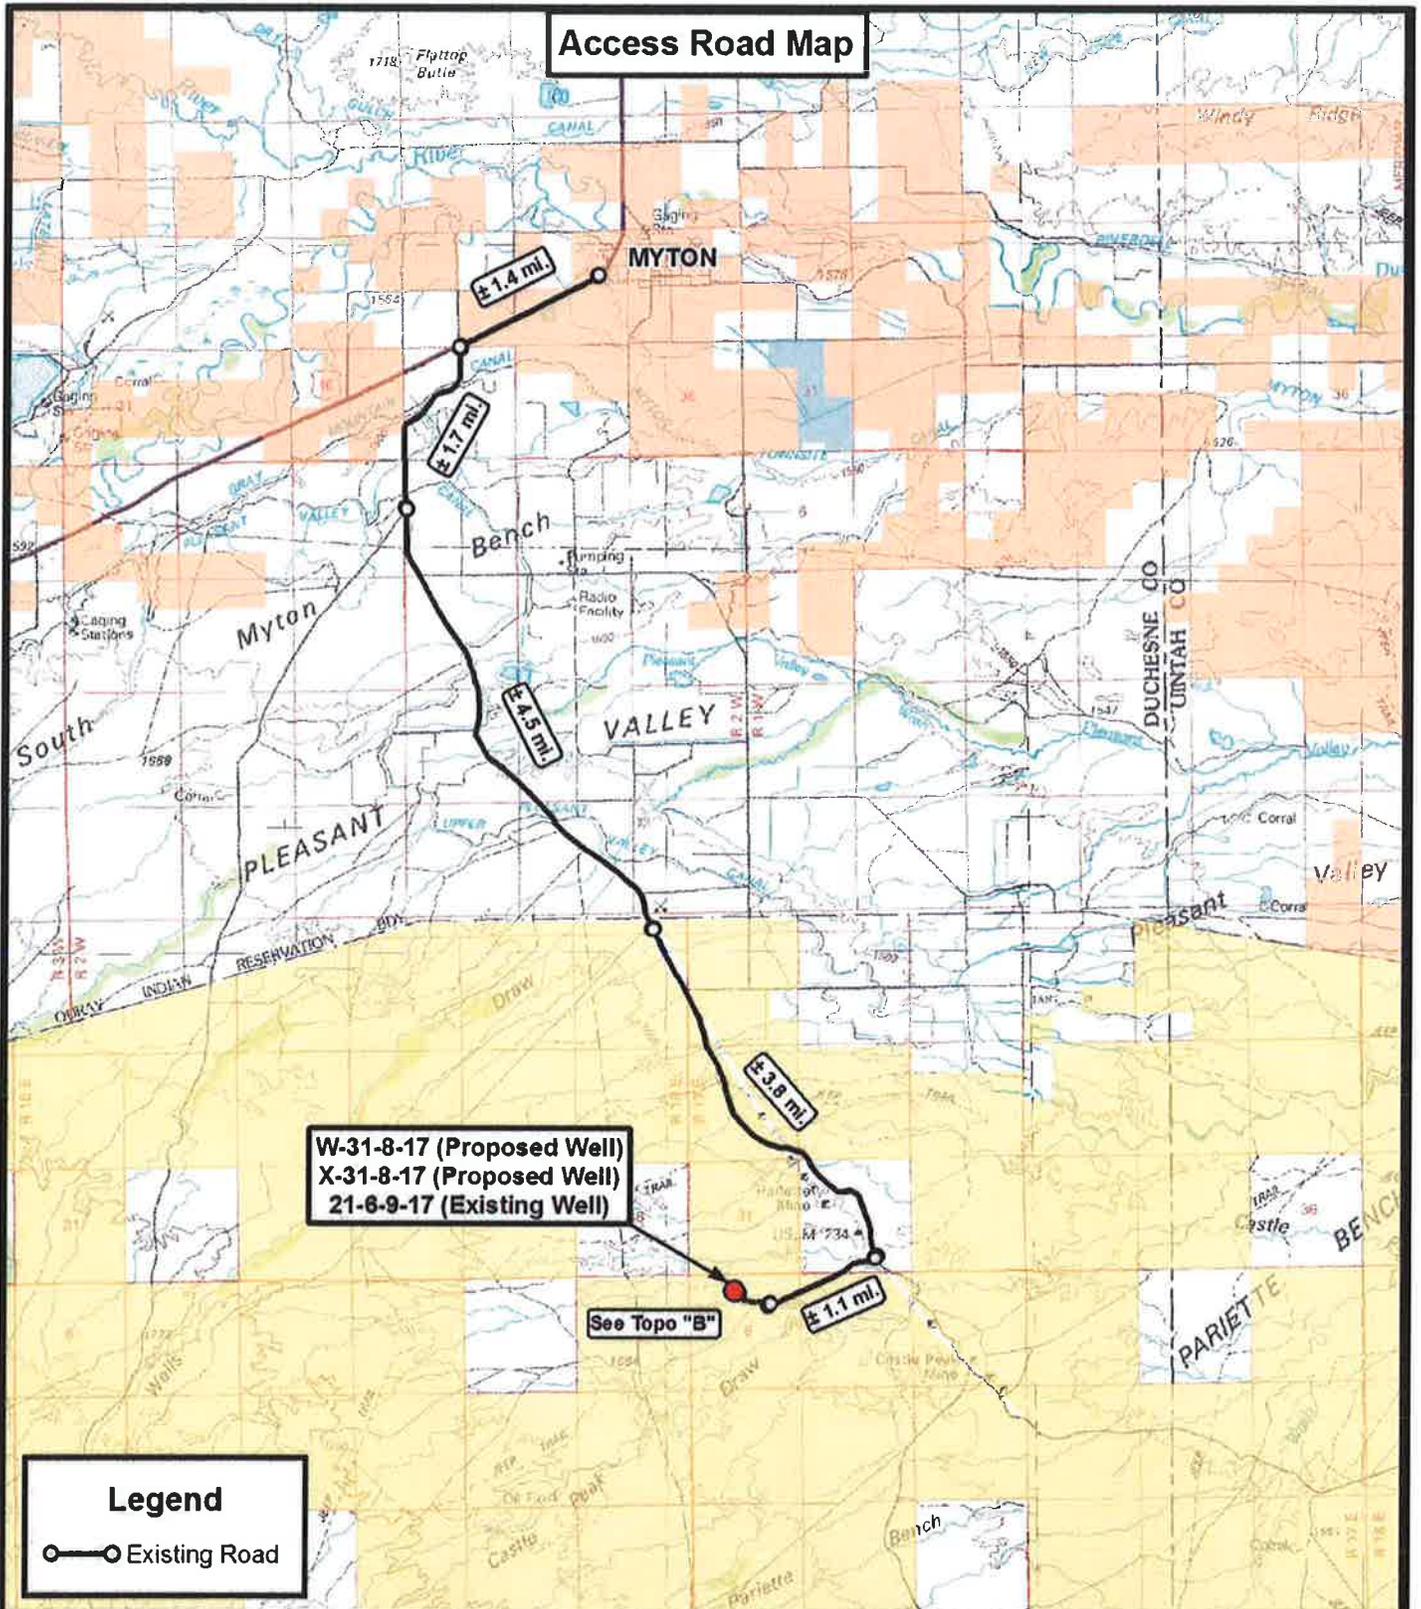

Access Road Map

W-31-8-17 (Proposed Well)
 X-31-8-17 (Proposed Well)
 21-6-9-17 (Existing Well)

See Topo "B"

Legend

—○— Existing Road

Tri State Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518




NEWFIELD EXPLORATION COMPANY

W-31-8-17 (Proposed Well)
 X-31-8-17 (Proposed Well)
 21-6-9-17 (Existing Well)
 SEC. 6, T9S, R17E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	C.H.M.	REVISED:	01-11-2011
DATE:	07-20-2010		
SCALE:	1:100,000		

TOPOGRAPHIC MAP

SHEET
A

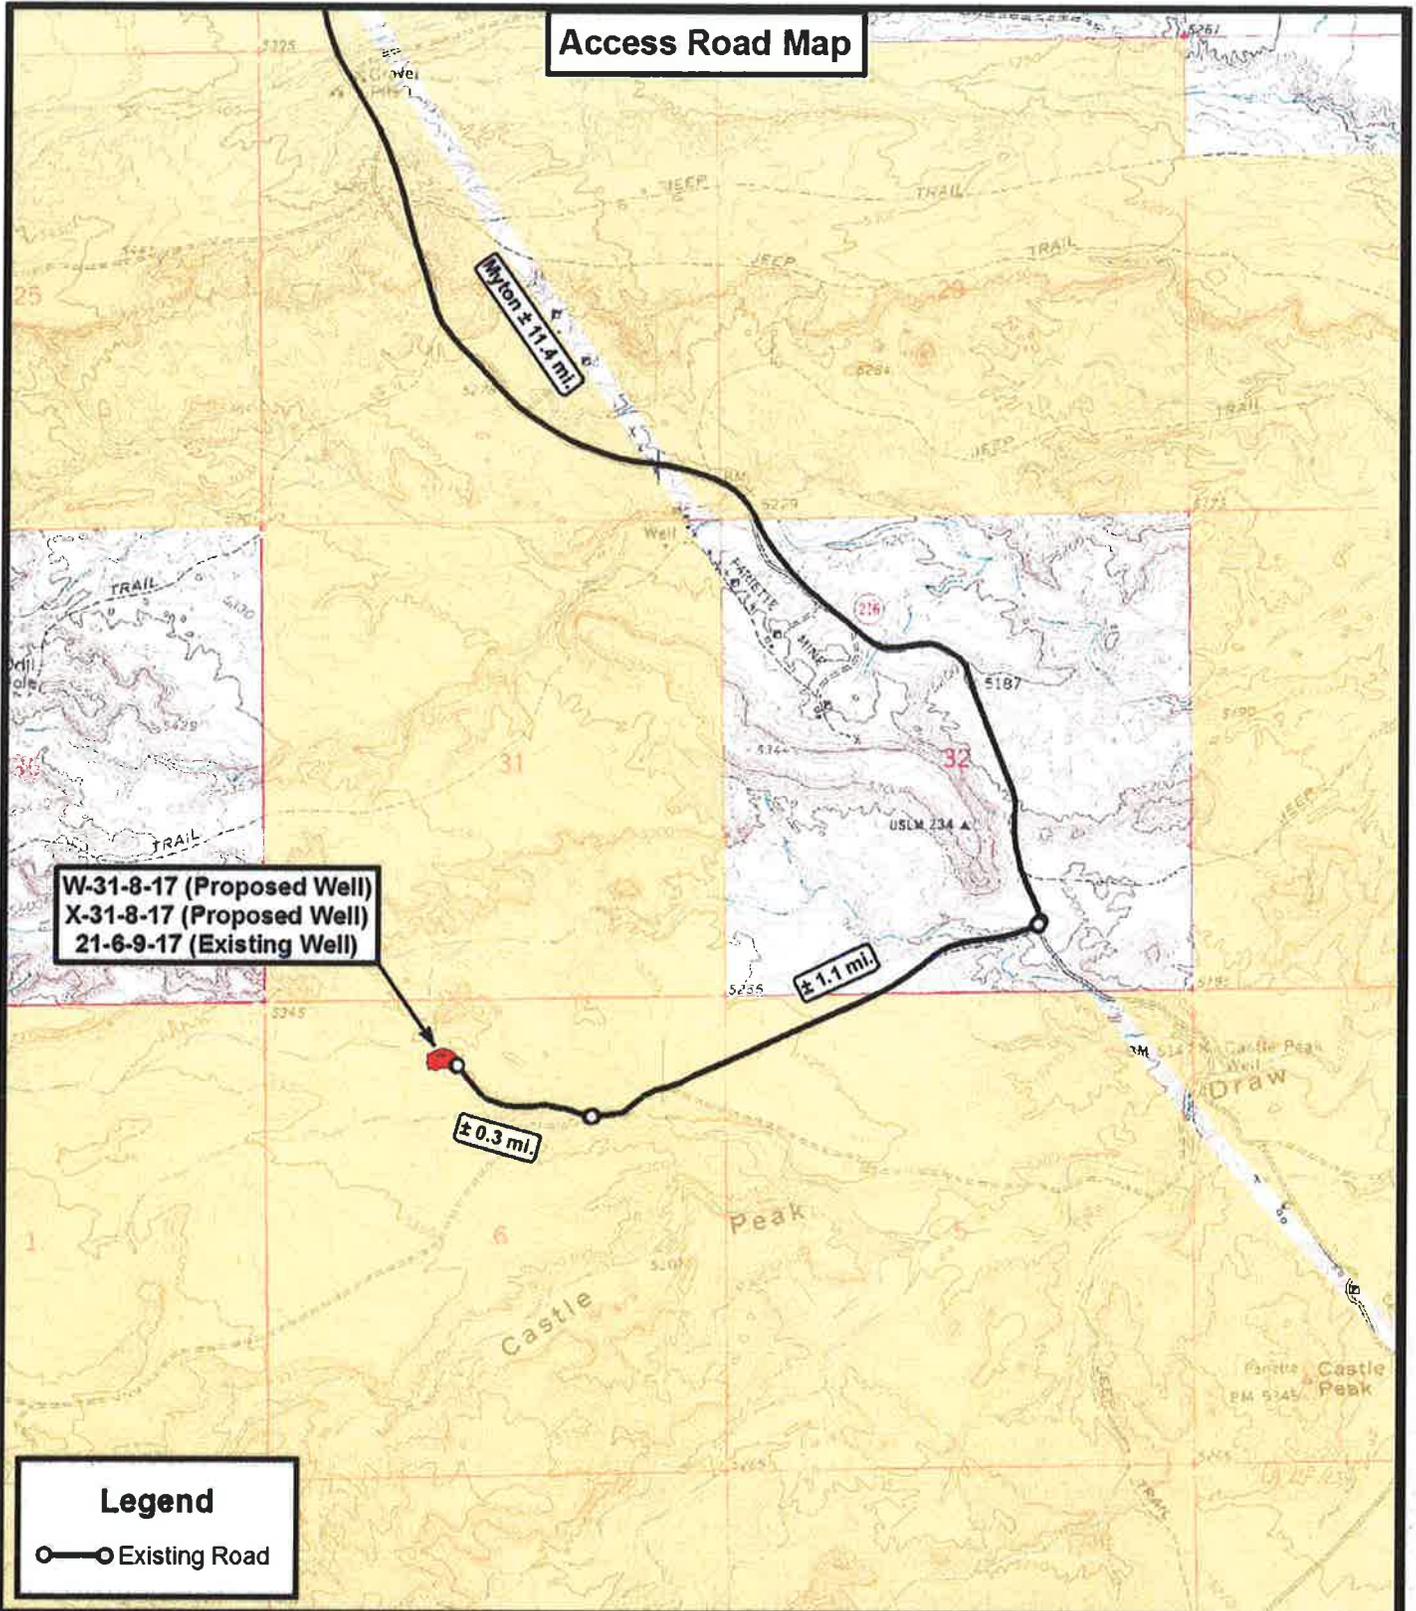

Legend

○—○ Existing Road

Tri State
Land Surveying, Inc.
 100 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY


W-31-8-17 (Proposed Well)
 X-31-8-17 (Proposed Well)
 21-6-9-17 (Existing Well)
 SEC. 6, T9S, R17E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	C.H.M.	REVISED:	01-11-2011
DATE:	07-20-2010		
SCALE:	1" = 2,000'		

TOPOGRAPHIC MAP

SHEET
B

Proposed Pipeline Map

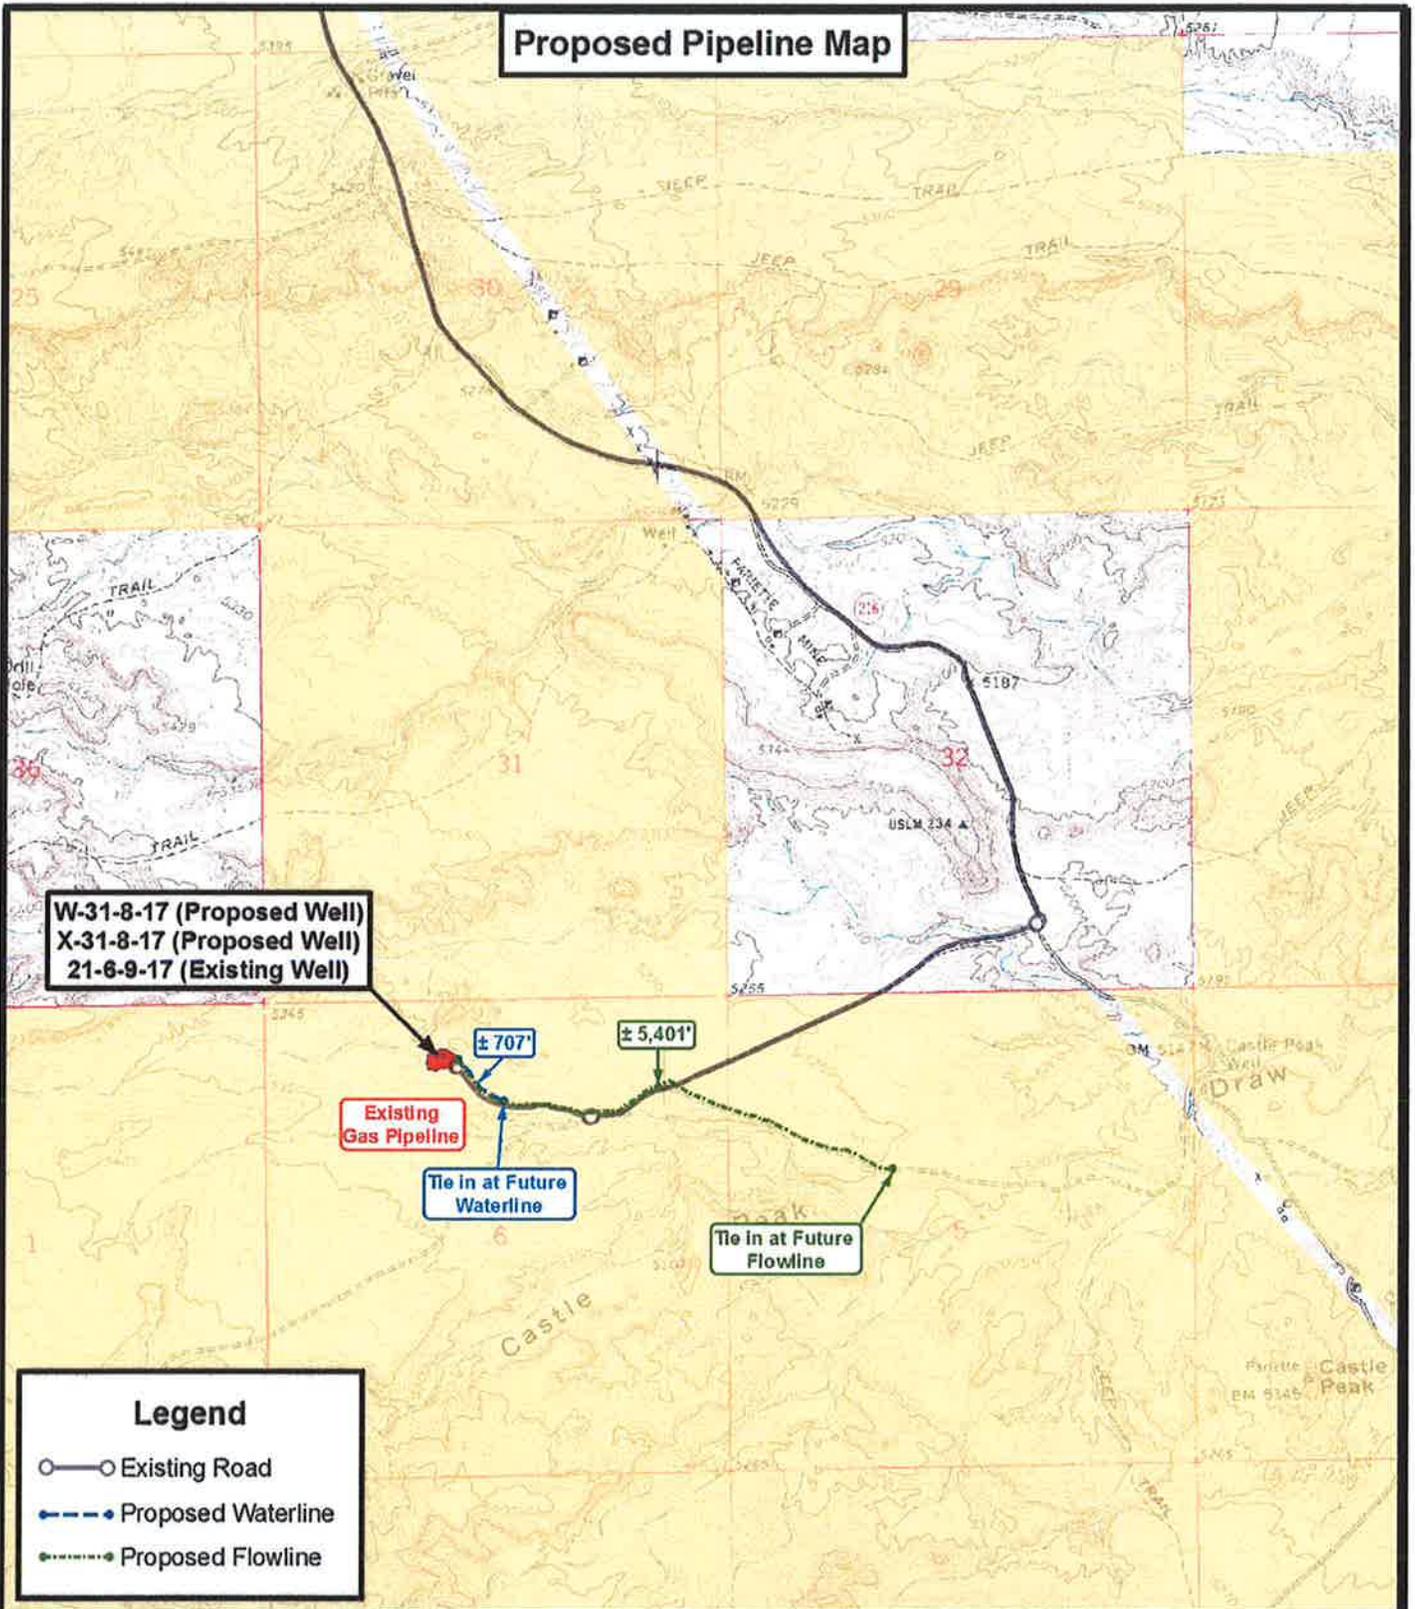

W-31-8-17 (Proposed Well)
X-31-8-17 (Proposed Well)
21-6-9-17 (Existing Well)

Existing Gas Pipeline

Tie in at Future Waterline

Tie in at Future Flowline

Legend

- Existing Road
- Proposed Waterline
- Proposed Flowline

Tri State Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078
 P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

W-31-8-17 (Proposed Well)
X-31-8-17 (Proposed Well)
21-6-9-17 (Existing Well)
SEC. 8, T9S, R17E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	C.H.M.	REVISED:	08-06-2010
DATE:	07-20-2010	REVISED:	01-11-2011
SCALE:	1" = 2,000'		

TOPOGRAPHIC MAP

SHEET
C


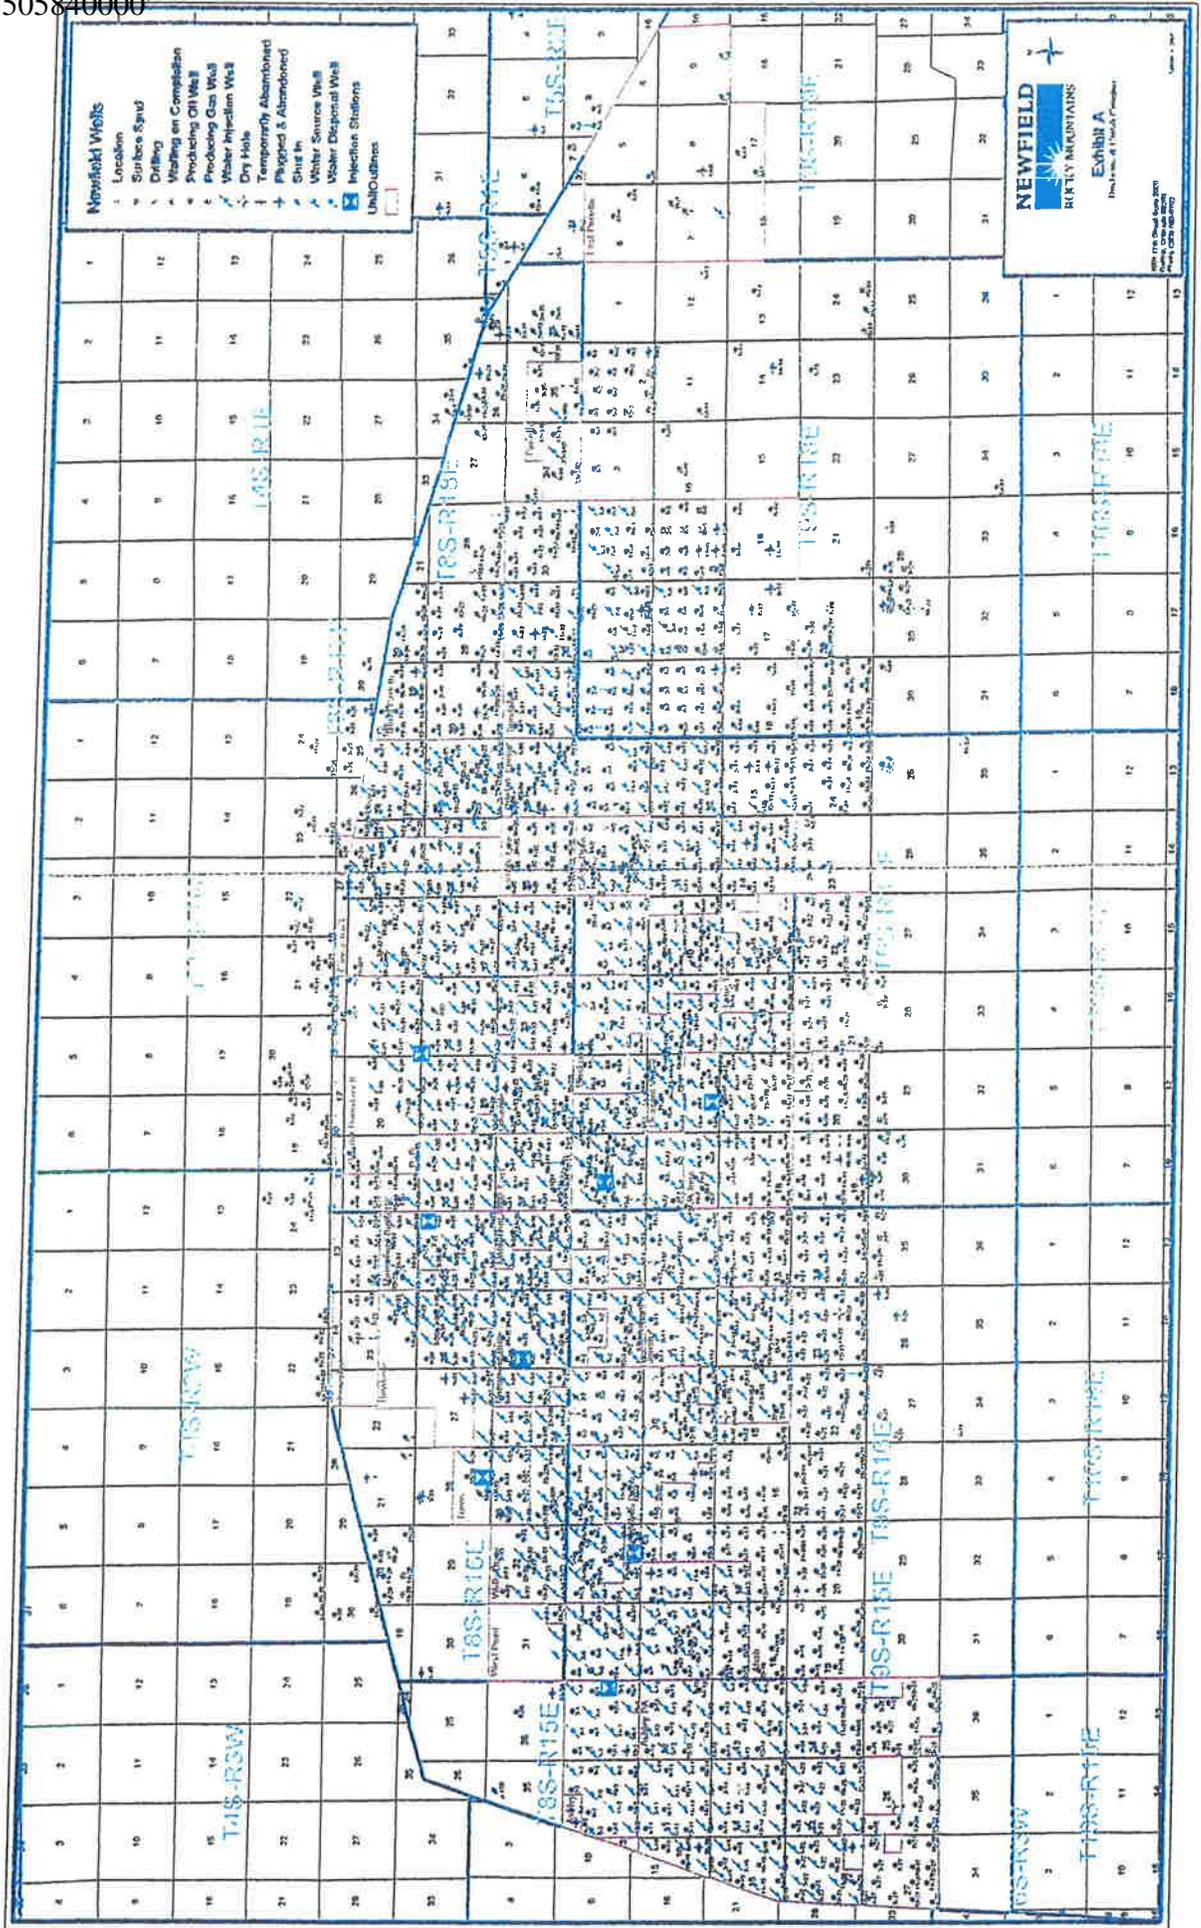


Exhibit "B" Map

**W-31-8-17 (Proposed Well)
X-31-8-17 (Proposed Well)
21-6-9-17 (Existing Well)**

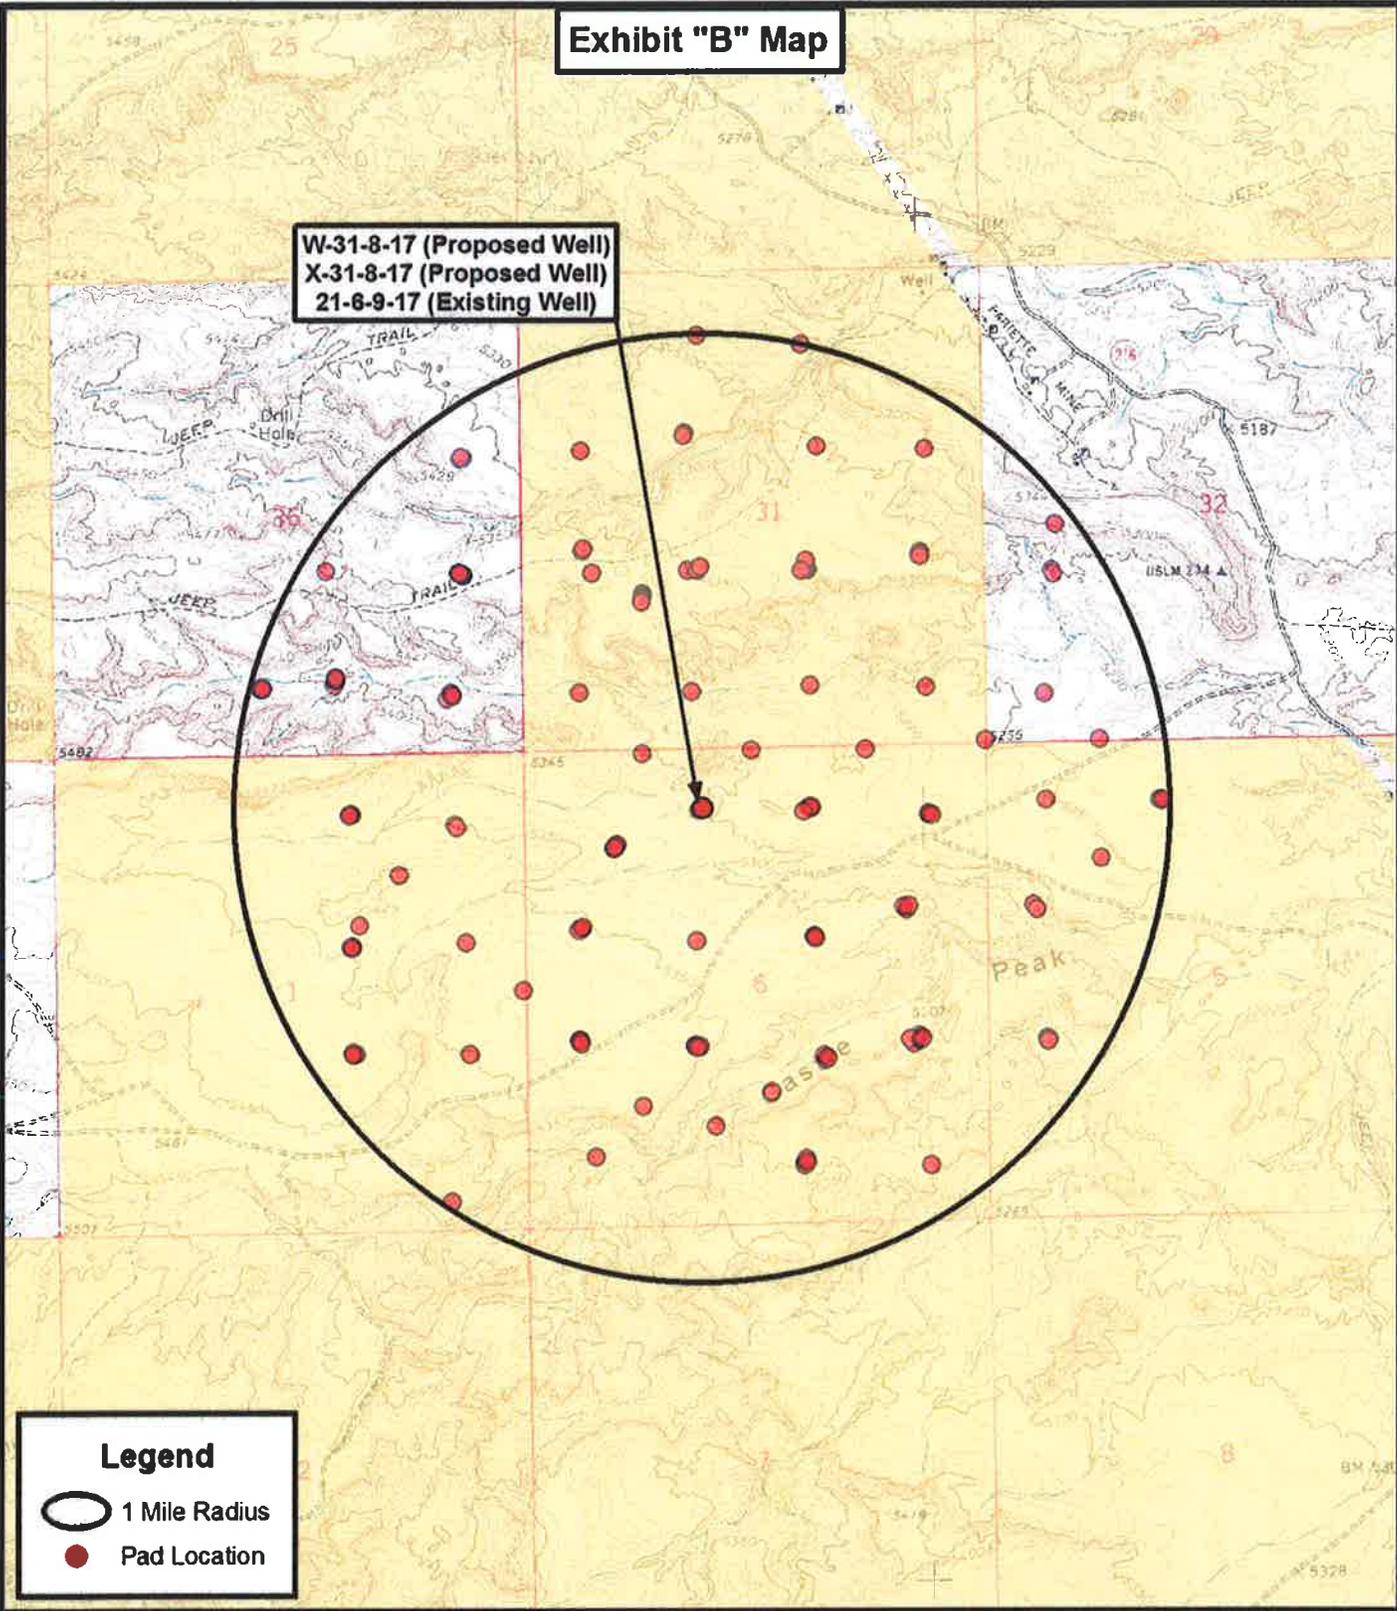

Legend

-  1 Mile Radius
-  Pad Location



**Tri State
Land Surveying, Inc.**
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

**W-31-8-17 (Proposed Well)
X-31-8-17 (Proposed Well)
21-6-9-17 (Existing Well)
SEC. 6, T9S, R17E, S.L.B.&M. Duchesne County, UT.**

DRAWN BY:	C.H.M.	REVISED:	08-09-2010
DATE:	07-20-2010	REVISED:	01-11-2011
SCALE:	1" = 2,000'		

TOPOGRAPHIC MAP

SHEET
D

NEWFIELD



NEWFIELD EXPLORATION

**USGS Myton SW (UT)
SECTION 6 T9S, R17E
W-31-8-17**

Wellbore #1

Plan: Design #1

Standard Planning Report

11 January, 2011



PayZone Directional Services, LLC.

Planning Report



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well W-31-8-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	W-31-8-17 @ 5316.0ft (NEWFIELD)
Project:	USGS Myton SW (UT)	MD Reference:	W-31-8-17 @ 5316.0ft (NEWFIELD)
Site:	SECTION 6 T9S, R17E	North Reference:	True
Well:	W-31-8-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Project	USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Utah Central Zone		

Site	SECTION 6 T9S, R17E				
Site Position:		Northing:	7,195,000.00 ft	Latitude:	40° 3' 47.061 N
From:	Lat/Long	Easting:	2,047,000.00 ft	Longitude:	110° 2' 50.009 W
Position Uncertainty:	0.0 ft	Slot Radius:	"	Grid Convergence:	0.93 °

Well	W-31-8-17, SHL LAT: 40° 03' 54.97" LONG: 110° 03' 04.66"					
Well Position	+N/-S	800.2 ft	Northing:	7,195,781.68 ft	Latitude:	40° 3' 54.970 N
	+E/-W	-1,139.0 ft	Easting:	2,045,848.19 ft	Longitude:	110° 3' 4.660 W
Position Uncertainty		0.0 ft	Wellhead Elevation:	5,316.0 ft	Ground Level:	5,304.0 ft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010	2010/07/29	11.42	65.84	52,372

Design	Design #1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)
	0.0	0.0	0.0	40.72

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.00	0.00	0.00	0.00	
1,404.7	12.07	40.72	1,398.7	64.0	55.1	1.50	1.50	0.00	40.72	
5,189.6	12.07	40.72	5,100.0	663.9	571.4	0.00	0.00	0.00	0.00	W-31-8-17 TGT1
6,110.0	12.07	40.72	6,000.0	809.7	697.0	0.00	0.00	0.00	0.00	



PayZone Directional Services, LLC.

Planning Report



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well W-31-8-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	W-31-8-17 @ 5316.0ft (NEWFIELD)
Project:	USGS Myton SW (UT)	MD Reference:	W-31-8-17 @ 5316.0ft (NEWFIELD)
Site:	SECTION 6 T9S, R17E	North Reference:	True
Well:	W-31-8-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N-S (ft)	+E-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	1.50	40.72	700.0	1.0	0.9	1.3	1.50	1.50	0.00
800.0	3.00	40.72	799.9	4.0	3.4	5.2	1.50	1.50	0.00
900.0	4.50	40.72	899.7	8.9	7.7	11.8	1.50	1.50	0.00
1,000.0	6.00	40.72	999.3	15.9	13.7	20.9	1.50	1.50	0.00
1,100.0	7.50	40.72	1,098.6	24.8	21.3	32.7	1.50	1.50	0.00
1,200.0	9.00	40.72	1,197.5	35.6	30.7	47.0	1.50	1.50	0.00
1,300.0	10.50	40.72	1,296.1	48.5	41.7	64.0	1.50	1.50	0.00
1,404.7	12.07	40.72	1,398.7	64.0	55.1	84.4	1.50	1.50	0.00
1,500.0	12.07	40.72	1,492.0	79.1	68.1	104.4	0.00	0.00	0.00
1,600.0	12.07	40.72	1,589.7	95.0	81.7	125.3	0.00	0.00	0.00
1,700.0	12.07	40.72	1,687.5	110.8	95.4	146.2	0.00	0.00	0.00
1,800.0	12.07	40.72	1,785.3	126.7	109.0	167.1	0.00	0.00	0.00
1,900.0	12.07	40.72	1,883.1	142.5	122.7	188.0	0.00	0.00	0.00
2,000.0	12.07	40.72	1,980.9	158.4	136.3	208.9	0.00	0.00	0.00
2,100.0	12.07	40.72	2,078.7	174.2	149.9	229.8	0.00	0.00	0.00
2,200.0	12.07	40.72	2,176.5	190.1	163.6	250.8	0.00	0.00	0.00
2,300.0	12.07	40.72	2,274.3	205.9	177.2	271.7	0.00	0.00	0.00
2,400.0	12.07	40.72	2,372.1	221.7	190.9	292.6	0.00	0.00	0.00
2,500.0	12.07	40.72	2,469.8	237.6	204.5	313.5	0.00	0.00	0.00
2,600.0	12.07	40.72	2,567.6	253.4	218.1	334.4	0.00	0.00	0.00
2,700.0	12.07	40.72	2,665.4	269.3	231.8	355.3	0.00	0.00	0.00
2,800.0	12.07	40.72	2,763.2	285.1	245.4	376.2	0.00	0.00	0.00
2,900.0	12.07	40.72	2,861.0	301.0	259.1	397.1	0.00	0.00	0.00
3,000.0	12.07	40.72	2,958.8	316.8	272.7	418.0	0.00	0.00	0.00
3,100.0	12.07	40.72	3,056.6	332.7	286.4	439.0	0.00	0.00	0.00
3,200.0	12.07	40.72	3,154.4	348.5	300.0	459.9	0.00	0.00	0.00
3,300.0	12.07	40.72	3,252.2	364.4	313.6	480.8	0.00	0.00	0.00
3,400.0	12.07	40.72	3,349.9	380.2	327.3	501.7	0.00	0.00	0.00
3,500.0	12.07	40.72	3,447.7	396.1	340.9	522.6	0.00	0.00	0.00
3,600.0	12.07	40.72	3,545.5	411.9	354.6	543.5	0.00	0.00	0.00
3,700.0	12.07	40.72	3,643.3	427.8	368.2	564.4	0.00	0.00	0.00
3,800.0	12.07	40.72	3,741.1	443.6	381.8	585.3	0.00	0.00	0.00
3,900.0	12.07	40.72	3,838.9	459.5	395.5	606.2	0.00	0.00	0.00
4,000.0	12.07	40.72	3,936.7	475.3	409.1	627.2	0.00	0.00	0.00
4,100.0	12.07	40.72	4,034.5	491.2	422.8	648.1	0.00	0.00	0.00
4,200.0	12.07	40.72	4,132.3	507.0	436.4	669.0	0.00	0.00	0.00
4,300.0	12.07	40.72	4,230.1	522.9	450.1	689.9	0.00	0.00	0.00
4,400.0	12.07	40.72	4,327.8	538.7	463.7	710.8	0.00	0.00	0.00
4,500.0	12.07	40.72	4,425.6	554.6	477.3	731.7	0.00	0.00	0.00
4,600.0	12.07	40.72	4,523.4	570.4	491.0	752.6	0.00	0.00	0.00
4,700.0	12.07	40.72	4,621.2	586.3	504.6	773.5	0.00	0.00	0.00
4,800.0	12.07	40.72	4,719.0	602.1	518.3	794.4	0.00	0.00	0.00
4,900.0	12.07	40.72	4,816.8	618.0	531.9	815.4	0.00	0.00	0.00
5,000.0	12.07	40.72	4,914.6	633.8	545.5	836.3	0.00	0.00	0.00
5,100.0	12.07	40.72	5,012.4	649.7	559.2	857.2	0.00	0.00	0.00
5,189.6	12.07	40.72	5,100.0	663.9	571.4	875.9	0.00	0.00	0.00

W-31-8-17 TGT1



PayZone Directional Services, LLC.
Planning Report



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well W-31-8-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	W-31-8-17 @ 5316.0ft (NEWFIELD)
Project:	USGS Myton SW (UT)	MD Reference:	W-31-8-17 @ 5316.0ft (NEWFIELD)
Site:	SECTION 6 T9S, R17E	North Reference:	True
Well:	W-31-8-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
5,200.0	12.07	40.72	5,110.2	665.5	572.8	878.1	0.00	0.00	0.00	
5,300.0	12.07	40.72	5,207.9	681.4	586.5	899.0	0.00	0.00	0.00	
5,400.0	12.07	40.72	5,305.7	697.2	600.1	919.9	0.00	0.00	0.00	
5,500.0	12.07	40.72	5,403.5	713.1	613.8	940.8	0.00	0.00	0.00	
5,600.0	12.07	40.72	5,501.3	728.9	627.4	961.7	0.00	0.00	0.00	
5,700.0	12.07	40.72	5,599.1	744.8	641.0	982.6	0.00	0.00	0.00	
5,800.0	12.07	40.72	5,696.9	760.6	654.7	1,003.6	0.00	0.00	0.00	
5,900.0	12.07	40.72	5,794.7	776.5	668.3	1,024.5	0.00	0.00	0.00	
6,000.0	12.07	40.72	5,892.5	792.3	682.0	1,045.4	0.00	0.00	0.00	
6,110.0	12.07	40.72	6,000.0	809.7	697.0	1,068.4	0.00	0.00	0.00	

Targets										
Target Name	Dip Angle (°)	Dip Dir. (°)	TVD (ft)	+N/-S (ft)	+E/-W (ft)	Northing (ft)	Easting (ft)	Latitude	Longitude	
W-31-8-17 TGT1 - hit/miss target - Shape - Circle (radius 75.0)	0.00	0.00	5,100.0	663.9	571.4	7,196,454.71	2,046,408.77	40° 4' 1.531 N	110° 2' 57.310 W	





Project: USGS Myton SW (UT)
 Site: SECTION 6 T9S, R17E
 Well: W-31-8-17
 Wellbore: Wellbore #1
 Design: Design #1



Azimuths to True North
 Magnetic North: 11.42°

Magnetic Field
 Strength: 52371.6snT
 Dip Angle: 65.84°
 Date: 2010/07/29
 Model: IGRF2010

KOP @ 600'
 DOGLEG RATE 1.5 DEG/100'
 TARGET RADIUS IS 75'

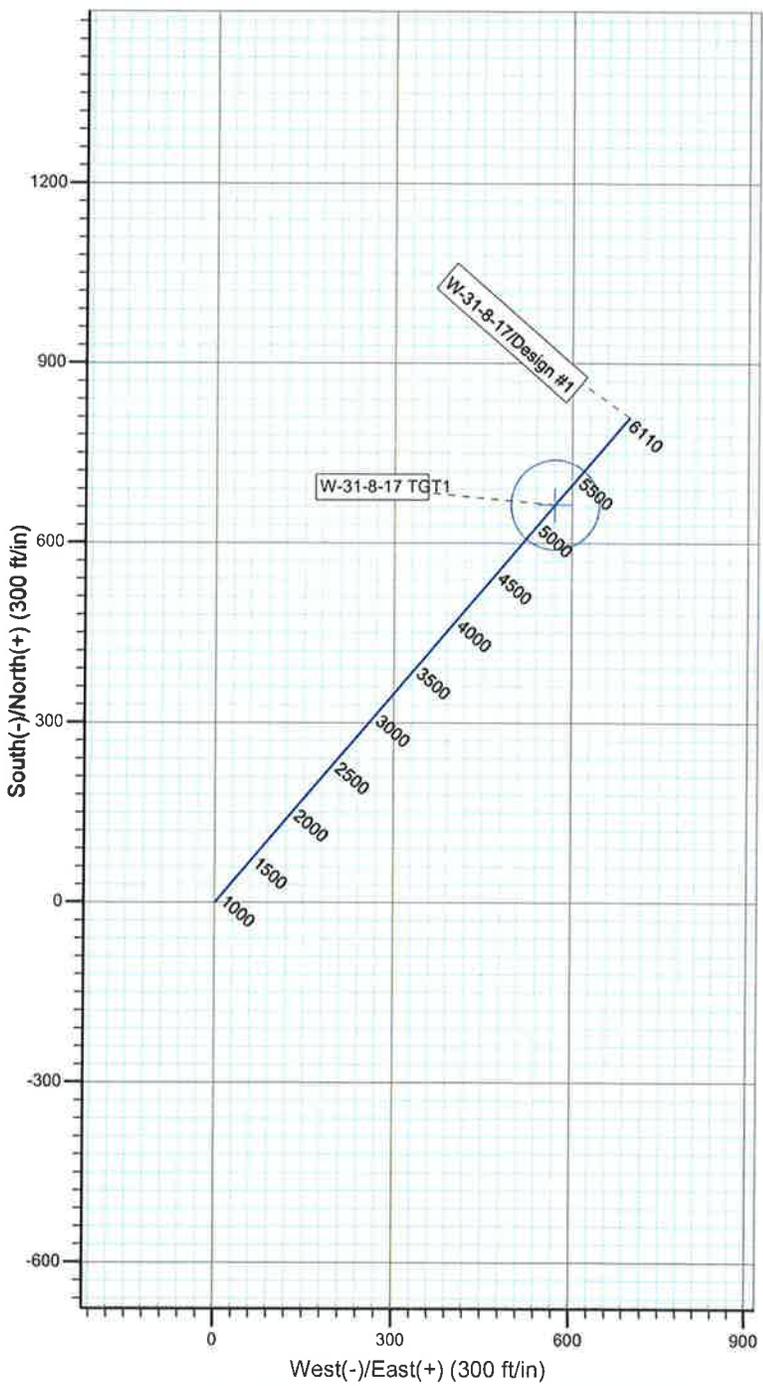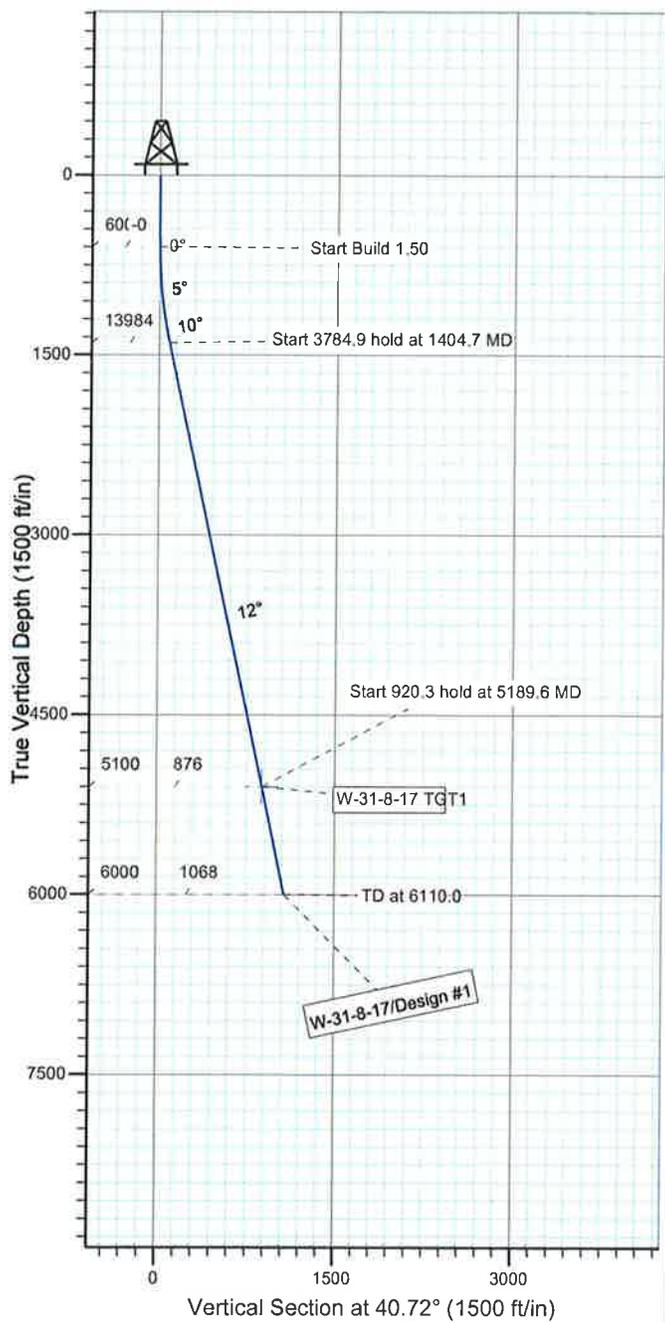

WELLBORE TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Shape
W-31-8-17 TGT1	5100.0	663.9	571.4	Circle (Radius: 75.0)

SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	DLeg	TFace	VSec	Target
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2	600.0	0.00	0.00	600.0	0.0	0.0	0.00	0.00	0.0	
3	1404.7	12.07	40.72	1398.7	64.0	55.1	1.50	40.72	84.4	
4	5189.6	12.07	40.72	5100.0	663.9	571.4	0.00	0.00	875.9	W-31-8-17 TGT1
5	6110.0	12.07	40.72	6000.0	809.7	697.0	0.00	0.00	1068.4	



**NEWFIELD PRODUCTION COMPANY
GREATER MONUMENT BUTTE W-31-8-17
AT SURFACE: NE/NW (LOT #3) SECTION 6, T9S, R17E
DUCHESNE COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Greater Monument Butte W-31-8-17 located in the NE 1/4 NW 1/4 Section 6, T9S, R17E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 – 1.4 miles \pm to the junction of this highway and UT State Hwy 53; proceed southeasterly – 10.0 miles \pm to it's junction with an existing road to the southwest; proceed in a southwesterly direction - 1.1 miles \pm to it's junction with an existing road to the northwest; proceed in a northwesterly direction – 0.3 miles \pm to the existing 21-6-9-17 well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

There is no proposed access road for this location. The proposed well will be drilled directionaly off of the existing 21-6-9-17 well pad. See attached **Topographic Map "B"**.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District
Water Right : 43-10136

Maurice Harvey Pond
Water Right: 47-1358

Neil Moon Pond
Water Right: 43-11787

Newfield Collector Well
Water Right: 47-1817 (A30414DVA, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

- b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – Bureau of Land Management.

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey will be forthcoming. The Paleontological Resource Survey for this area is attached. Paleontological Resource Survey prepared by, Wade E. Miller, 9/17/10. See attached report cover page, Exhibit "D".

Newfield Production Company requests 707' of buried water line to be granted in Lease UTU-020252A.

It is proposed that the disturbed area will be 60' wide to allow for construction of the proposed access road, a 10" or smaller gas gathering line, a 4" poly fuel gas line, a buried 10" steel water injection line, a buried 3" poly water return line, and a and a 14" surface flow line. The planned access road will consist of a 20' permanent running surface (10' either side of the centerline) crowned and ditched in order to handle any run-off from any precipitation events that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be turnouts as needed along this road to allow for increases in potential traffic issues. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Both the proposed surface gas and buried water lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** The proposed water pipelines will be buried in a 4-5' deep trench constructed with a trencher or backhoe for the length of the proposal. The equipment will run on the surface and not be flat bladed to minimize surface impacts to precious topsoil in these High Desert environments. If possible, all proposed surface gas pipelines will be installed on the same side of the road as existing gas lines. The construction phase of the planned access road, proposed gas lines and proposed water lines will last approximately (5) days.

In the event that the proposed well is converted to a water injection well, a Sundry Notice 3160-5 form will be applied for through the Bureau of Land Management field office.

Surface Flow Line

Newfield requests 5,401' of surface flow line be granted. The Surface Flow Line will consist of up to a 14" bundled pipe consisting of 2-2" poly glycol lines and 1-3" production line. For all new wells, Newfield. **Refer to Topographic Map "D"** for the proposed location of the proposed flow line. Flow lines will be tan and will be constructed using the following procedures:

Clearing and Grading: No clearing or grading of the ROW will be required. The centerline of the proposed route will be staked prior to installation. Flow lines shall be placed as close to existing roads as possible without interfering with normal road travel or road maintenance activities. Due to the proximity of existing facilities, no temporary use or construction/storage areas are anticipated. If necessary, temporary use or construction/storage areas will be identified on a topographic map included in the approved permit.

Installation: The proposed flow lines will be installed 4-6" above the ground. For portions along existing two-track and primary access roads, lengths of pipe will be strung out in the borrow ditch, welded together, and rolled or dragged into place with heavy equipment. For pipelines that are installed cross-country (not along existing or proposed roads), travel along the lines will be infrequent and for maintenance needs only. No installation activities will be performed during periods when the soil is too wet to adequately support installation equipment. If such equipment creates ruts in excess of three (3) inches deep, the soil will be deemed too wet to adequately support the equipment.

Water Disposal

After first production, if the production water meets quality guidelines, it will be transported to the Ashley, Monument Butte, Jonah, South Wells Draw and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project. Water not meeting quality criteria, will be disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), Federally approved surface disposal facilities or at a State of Utah approved surface disposal facilities.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Details of the On-Site Inspection

The proposed Greater Monument Butte W-31-8-17 was on-sited on 12/13/10. The following were present; Tim Eaton (Newfield Production and Janna Simonsen (Bureau of Land Management).

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the Greater Monument Butte W-31-8-17, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the Greater Monument Butte W-31-8-17, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**

Representative

Name: Tim Eaton
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #W-31-8-17, Section 6, Township 9S, Range 17E: Lease UTU-020252A Duchesne County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

1/12/11
Date


Mandie Crozier
Regulatory Specialist
Newfield Production Company

2-M SYSTEM

Blowout Prevention Equipment Systems

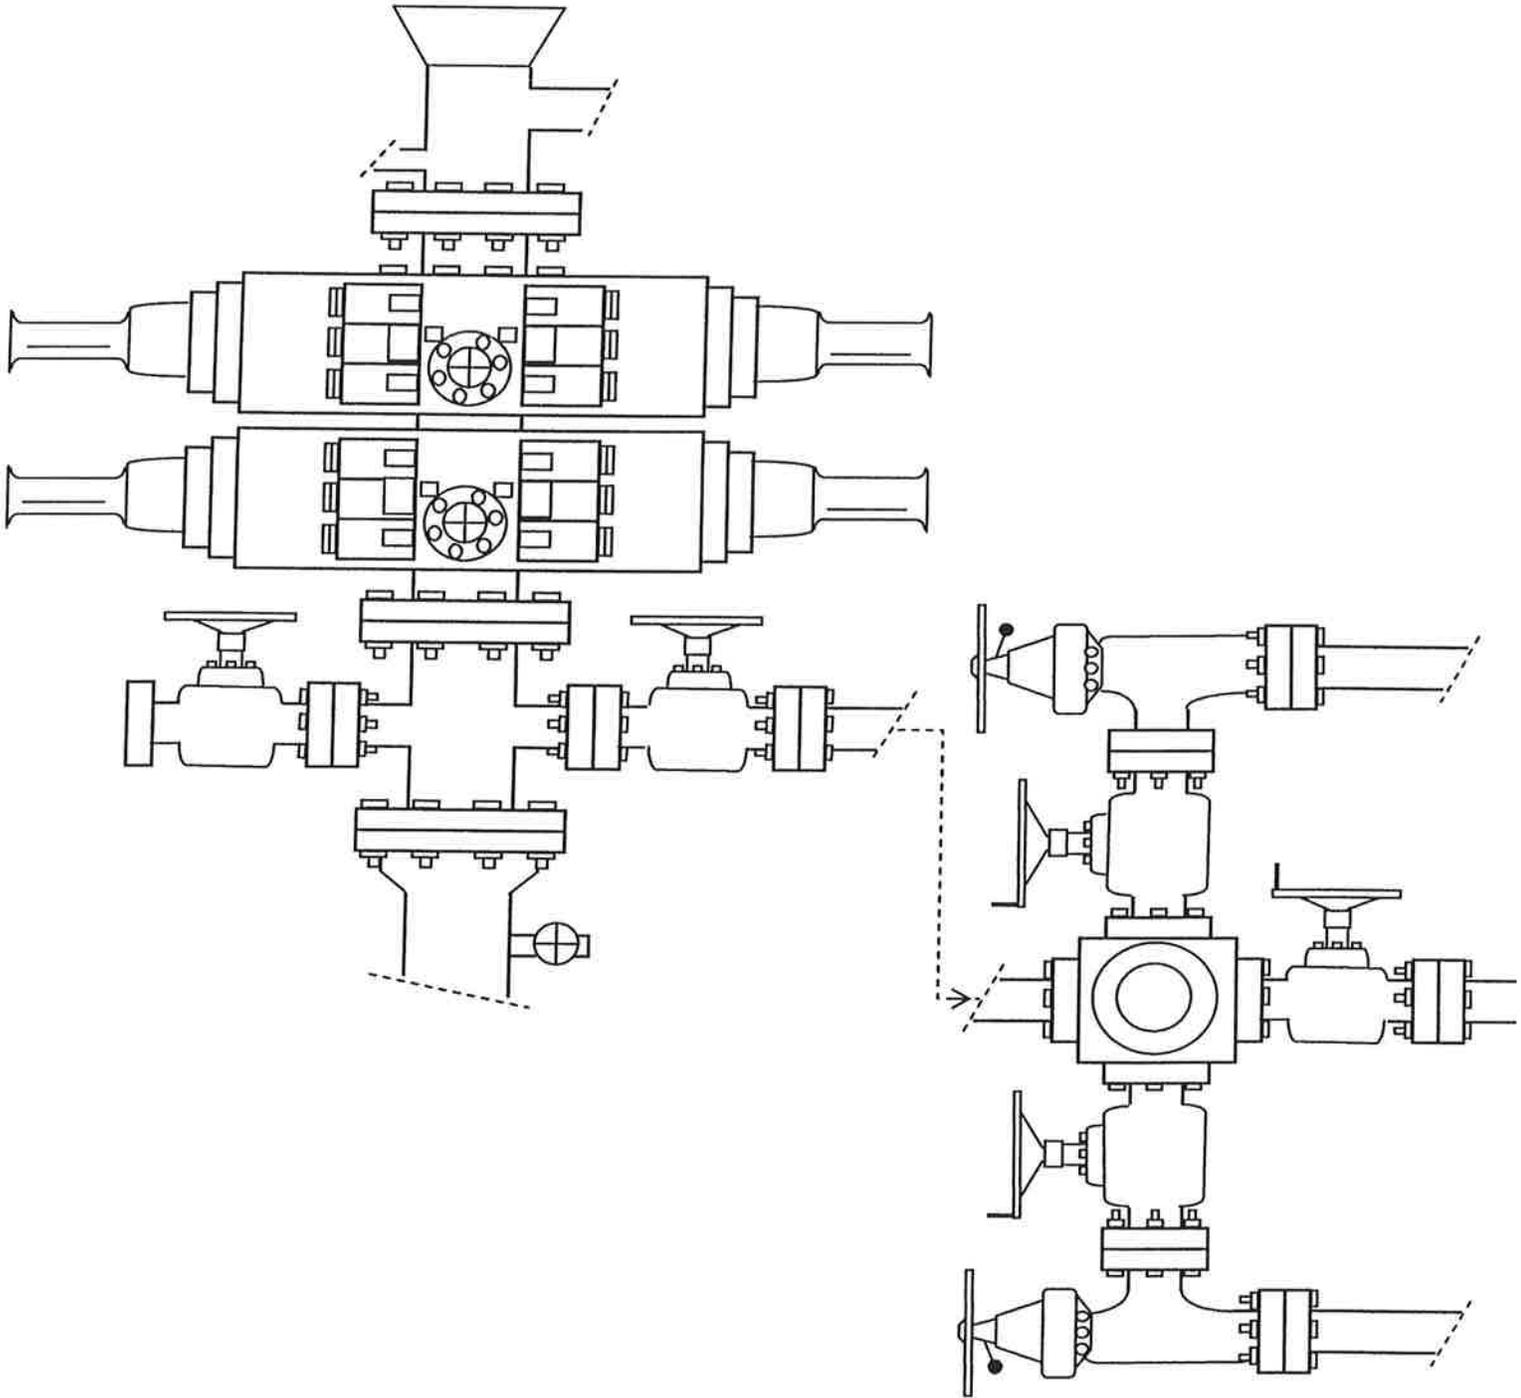


EXHIBIT C



VIA ELECTRONIC DELIVERY

January 13, 2011

State of Utah, Division of Oil, Gas and Mining
ATTN: Diana Mason
P.O. Box 145801
Salt Lake City, UT 84114-5801

RE: Directional Drilling
Greater Monument Butte W-31-8-17
Greater Monument Butte (Green River) Unit

Surface Hole: T9S-R17E Section 6: NENW (Lot #3) (UTU-020252A)
673' FNL 1973' FWL

At Target: T8S-R17E Section 31: SWSE (UTU-74869)
124' FSL 2492' FEL

Duchesne County, Utah

Dear Ms. Mason:

Pursuant to the filing by Newfield Production Company (NPC) of an Application for Permit to Drill the above referenced well dated 1/12/11, a copy of which is attached, and in accordance with Oil and Gas Conservation Rule R649-3-11, NPC hereby submits this letter as notice of our intention to directionally drill this well.

The surface hole and target locations of this well are both within the boundaries of the Greater Monument Butte Unit (UTU-87538X), of which Newfield certifies that it is the operator. Further, Newfield certifies that all lands within 460 feet of the entire directional well bore are within the Greater Monument Butte Unit.

NPC is permitting this well as a directional well in order to mitigate surface disturbance by utilizing pre-existing roads and pipelines.

NPC hereby requests our application for permit to drill be granted pursuant to R649-3-11. If you have any questions or require further information, please contact the undersigned at 303-383-4197 or by email at sgillespie@newfield.com. Your consideration in this matter is greatly appreciated.

Sincerely,
Newfield Production Company

A handwritten signature in blue ink, appearing to read "Shane Gillespie".

Shane Gillespie
Land Associate

Form 3160-3
(August 2007)

FORM APPROVED
OMB No. 1004-0137
Expires July 31, 2010

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT


APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		7. If Unit or CA Agreement, Name and No. Greater Monument Butte
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		8. Lease Name and Well No. Greater Monument Butte W-31-8-17
2. Name of Operator Newfield Production Company		9. API Well No.
3a. Address Route #3 Box 3630, Myton UT 84052	3b. Phone No. (include area code) (435) 646-3721	10. Field and Pool, or Exploratory Monument Butte
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NE/NW (LOT #3) 673' FNL 1973' FWL Sec. 6, T9S R17E (UTU-020252A) At proposed prod. zone SW/SE 124' FSL 2492' FEL Sec. 31, T8S R17E (UTU-74869)		11. Sec., T. R. M. or Blk. and Survey or Area Sec. 6, T9S R17E
14. Distance in miles and direction from nearest town or post office* Approximately 12.8 miles south of Myton, UT		12. County or Parish Duchesne
		13. State UT
15. Distance from proposed* location to nearest property or lease line, ft. Approx. 124' f/lse, NA f/unit (Also to nearest drig. unit line, if any)	16. No. of acres in lease 640.00	17. Spacing Unit dedicated to this well 20 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1630'	19. Proposed Depth 6,110'	20. BLM/BIA Bond No. on file WYB000493
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5304' GL	22. Approximate date work will start* 2nd Qtr - 2011	23. Estimated duration (7) days from SPUD to rig release

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- | | |
|--|---|
| 1. Well plat certified by a registered surveyor. | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above). |
| 2. A Drilling Plan. | 5. Operator certification |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the BLM. |

25. Signature 	Name (Printed Typed) Mandie Crozier	Date 1/12/11
--	--	-----------------

Title Regulatory Specialist		
--------------------------------	--	--

Approved by (Signature)	Name (Printed Typed)	Date
-------------------------	----------------------	------

Title	Office
-------	--------

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)



*(Instructions on page 2)

R17E, S.L.B.&M.

NEWFIELD EXPLORATION COMPANY

N89°51'E - 78.20 (G.L.O.)
N88°54'22"E - 5178.54' (Meas.)

TARGET BOTTOM HOLE, W-31-8-17,
LOCATED AS SHOWN IN THE SW 1/4
SE 1/4 OF SECTION 31, T8S, R17E,
S.L.B.&M. DUCHESNE COUNTY, UTAH.



Note:
1. The bottom of hole footages are
124' FSL & 2492' FEL.

**TARGET BOTTOM HOLE:
W-31-8-17**

BASIS OF ELEV: Elevations are base on
LOCATION: an N.G.S. OPUS Correction.
LAT. 40°04'09.56" LONG. 110°00'43.28"
(Tristate Aluminum Cap) Elev. 5281.57'


THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS
PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS
MADE BY ME OR UNDER MY SUPERVISION AND THAT
THE SAME ARE TRUE AND CORRECT TO THE BEST
OF MY KNOWLEDGE AND BELIEF, 1893777



TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
(435) 781-2501

DATE SURVEYED: 07-14-10	SURVEYED BY: D.G.
DATE DRAWN: 07-22-10	DRAWN BY: M.W.
REVISED: 01-11-11 F.T.M.	SCALE: 1" = 1000'


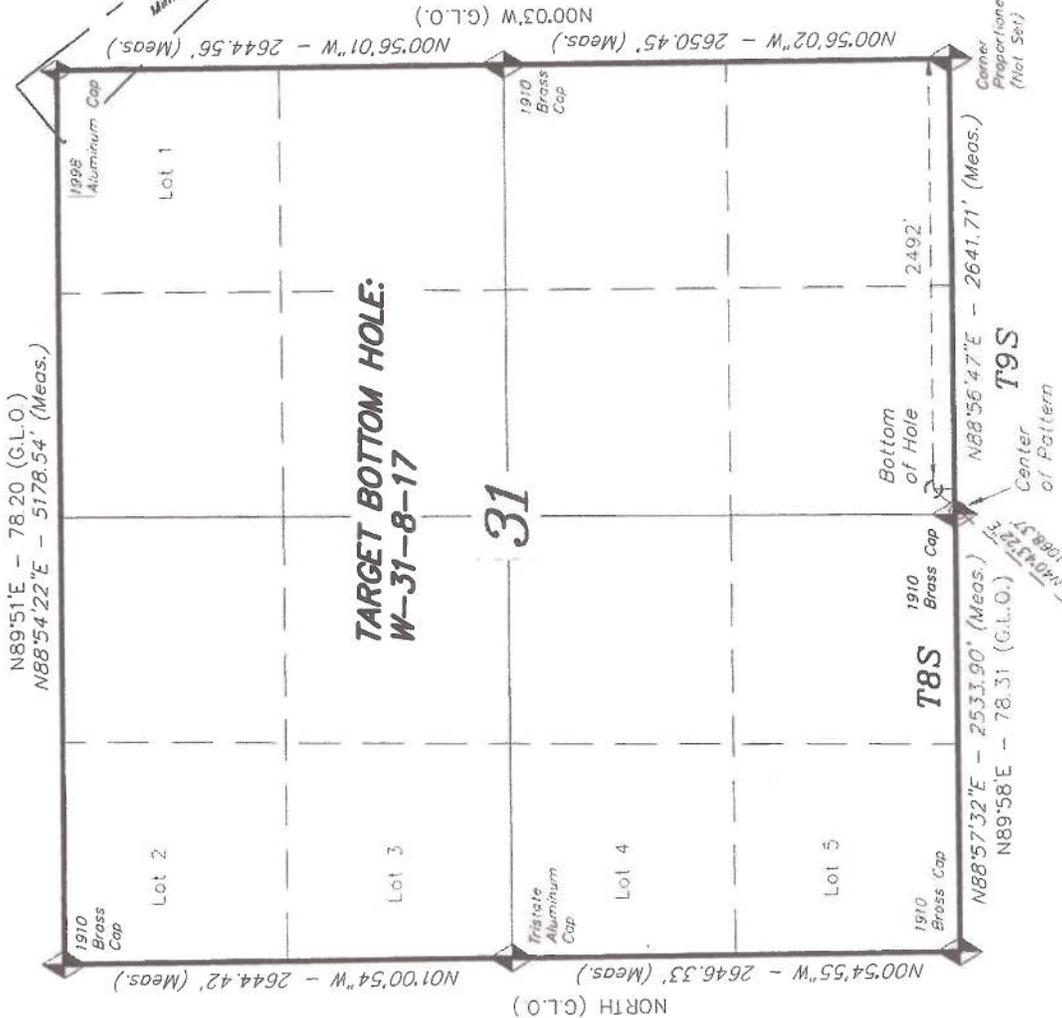


◆ = SECTION CORNERS LOCATED

API Number: 4301350584
Well Name: Greater Monument Butte W-31-8-17
Township 09.0 S Range 17.0 E Section 06
Meridian: SLBM
Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
 Map Produced by Diana Mason

Units STATUS	Wells Query Status
ACTIVE	APD - Approved Permit
EXPLORATORY	DRL - Spudded (Drilling Commenced)
GAS STORAGE	GIW - Gas Injection
NF PP OIL	GS - Gas Storage
NF SECONDARY	LA - Location Abandoned
PI OIL	LOC - New Location
PP GAS	OPS - Operation Suspended
PP GEOTHERMAL	PA - Plugged Abandoned
PP OIL	PGW - Producing Gas Well
SECONDARY	POW - Producing Oil Well
TERMINATED	RET - Returned APD
Fields STATUS	SGW - Shut-in Gas Well
Unknown	SOW - Shut-in Oil Well
ABANDONED	TA - Temp. Abandoned
ACTIVE	TW - Test Well
COMBINED	WDW - Water Disposal
INACTIVE	WIW - Water Injection Well
STORAGE	WSW - Water Supply Well
TERMINATED	
Sections	
Township	

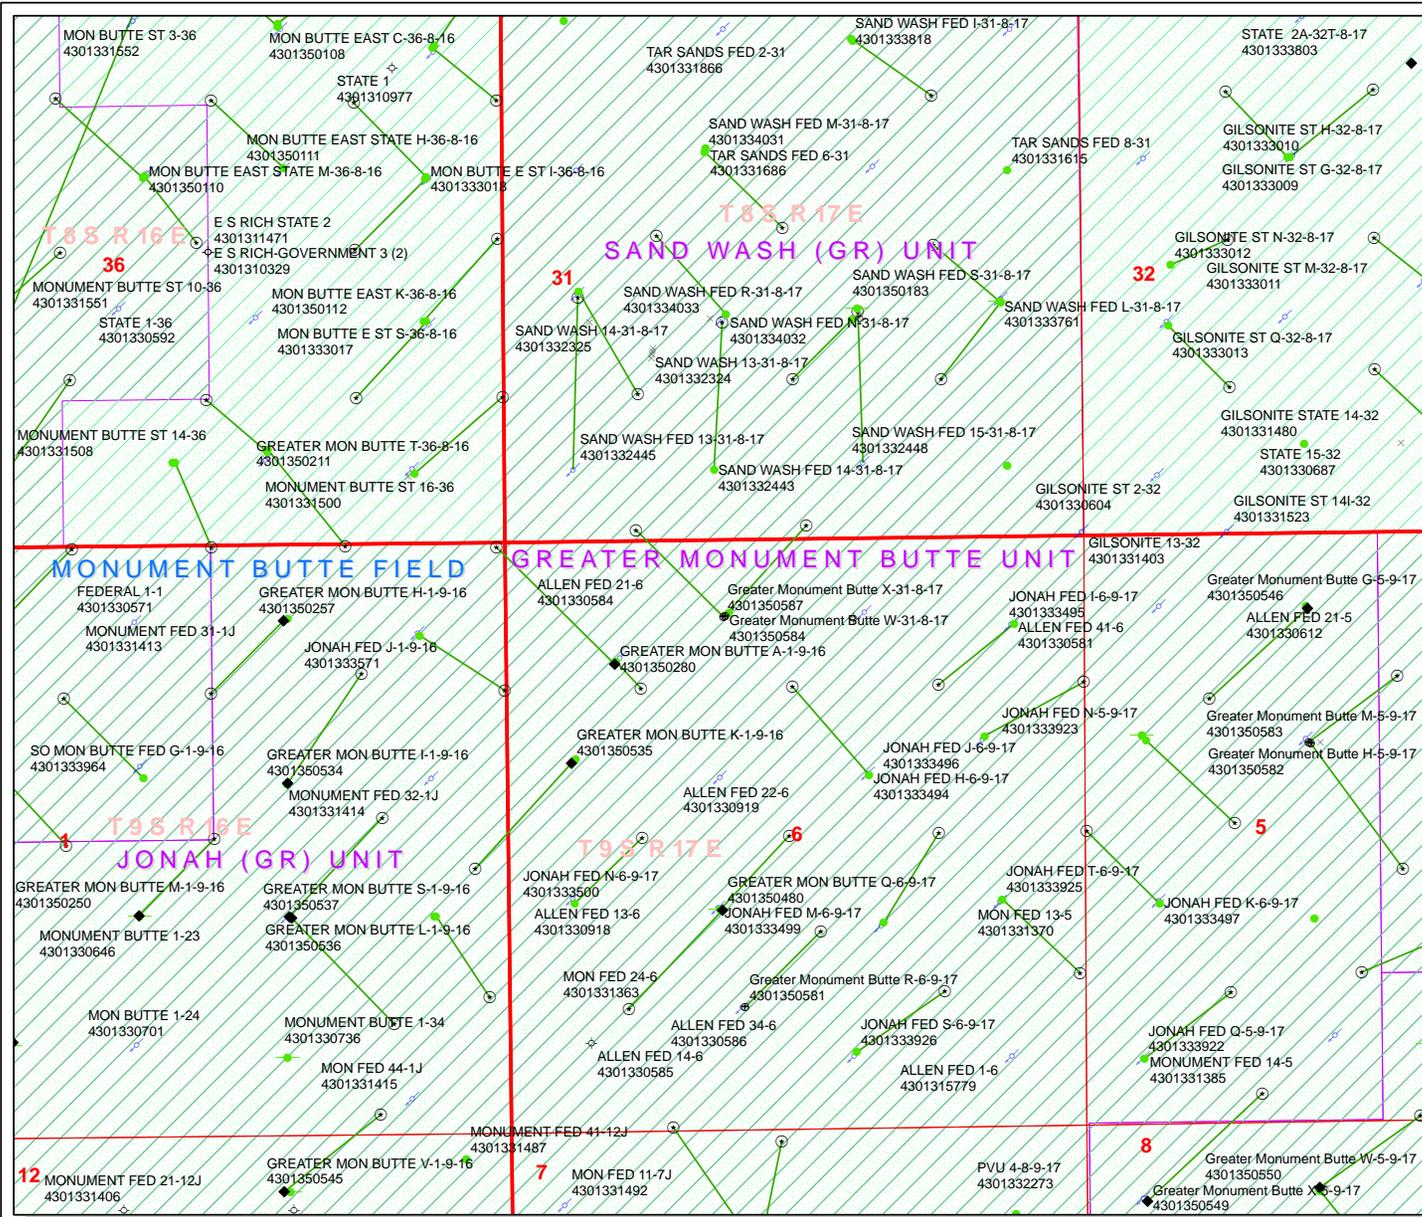

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office

P.O. Box 45155

Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:

3160

(UT-922)

January 19, 2011

Memorandum

To: Assistant District Manager Minerals, Vernal District

From: Michael Coulthard, Petroleum Engineer

Subject: 2011 Plan of Development Greater Monument
Butte Unit, Duchesne and Uintah Counties,
Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2011 within the Greater Monument Butte Unit, Duchesne and Uintah Counties, Utah.

API#	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-50582	GMBU H-5-9-17	Sec 05 T09S R17E 1874 FNL 2011 FWL BHL Sec 05 T09S R17E 1292 FNL 2461 FEL
43-013-50583	GMBU M-5-9-17	Sec 05 T09S R17E 1887 FNL 2025 FWL BHL Sec 05 T09S R17E 2263 FSL 2418 FEL
43-013-50584	GMBU W-31-8-17	Sec 06 T09S R17E 0673 FNL 1973 FWL BHL Sec 31 T08S R17E 0124 FSL 2492 FEL
43-013-50585	GMBU S-7-9-17	Sec 07 T09S R17E 0854 FSL 1726 FEL BHL Sec 07 T09S R17E 1492 FSL 1204 FEL
43-013-50586	GMBU N-8-9-17	Sec 08 T09S R17E 2099 FNL 0566 FWL BHL Sec 08 T09S R17E 2375 FSL 1723 FWL
43-013-50587	GMBU X-31-8-17	Sec 06 T09S R17E 0687 FNL 1957 FWL BHL Sec 31 T08S R17E 0103 FSL 1179 FWL

This office has no objection to permitting the wells at this time.

Michael L. Coulthard

Digitally signed by Michael L. Coulthard
DN: cn=Michael L. Coulthard, o=Bureau of Land Management, ou=Branch of Minerals,
email=Michael_Coulthard@blm.gov, c=US
Date: 2011.01.19 09:17:19 -0700

bcc: File - Greater Monument Butte Unit
Division of Oil Gas and Mining
Central Files
Agr. Sec. Chron
Fluid Chron

MCoulthard:mc:1-19-11

WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 1/13/2011

API NO. ASSIGNED: 43013505840000

WELL NAME: Greater Monument Butte W-31-8-17

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: NENW 06 090S 170E

Permit Tech Review:

SURFACE: 0673 FNL 1973 FWL

Engineering Review:

BOTTOM: 0124 FSL 2492 FEL

Geology Review:

COUNTY: DUCHESNE

LATITUDE: 40.06529

LONGITUDE: -110.05058

UTM SURF EASTINGS: 580968.00

NORTHINGS: 4435226.00

FIELD NAME: MONUMENT BUTTE

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-020252A

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 1 - Federal

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: FEDERAL - WYB000493
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 437478
- RDCC Review:
- Fee Surface Agreement
- Intent to Commingle

Commingle Approved

LOCATION AND SITING:

- R649-2-3.
Unit: GMBU (GRRV)
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
Board Cause No: Cause 213-11
Effective Date: 11/30/2009
Siting: Suspends General Siting
- R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason
15 - Directional - dmason
27 - Other - bhill



GARY R. HERBERT
Governor

GREGORY S. BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: Greater Monument Butte W-31-8-17
API Well Number: 43013505840000
Lease Number: UTU-020252A
Surface Owner: FEDERAL
Approval Date: 1/19/2011

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. §40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 213-11. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Production casing cement shall be brought up to or above the top of the unitized interval for the Greater Monument Butte Unit (Cause No. 213-11).

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well – contact Carol Daniels at 801-538-5284 (please leave a voicemail message if not available)
OR
submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website at <https://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) – due within 5 days of spudding the well
- Monthly Status Report (Form 9) – due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) – due prior to implementation
- Written Notice of Emergency Changes (Form 9) – due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) – due prior to implementation
- Report of Water Encountered (Form 7) – due within 30 days after completion
- Well Completion Report (Form 8) – due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "John Rogers", written in a cursive style.

For John Rogers
Associate Director, Oil & Gas

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

5a. Type of work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU-020252A
5b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name NA
2. Name of Operator Newfield Production Company		7. If Unit or CA Agreement, Name and No. Greater Monument Butte
3a. Address Route #3 Box 3630, Myton UT 84052		8. Lease Name and Well No. Greater Monument Butte W-31-8-17
3b. Phone No. (include area code) (435) 646-3721		9. API Well No. 43 013 50584
4. Location of Well (Report location clearly and in accordance with any State requirements.)* At surface NE/NW (LOT #3) 673' FNL 1973' FWL Sec. 6, T9S R17E (UTU-020252A) At proposed prod. zone SW/SE 124' FSL 2492' FEL Sec. 31, T8S R17E (UTU-74869)		10. Field and Pool, or Exploratory Monument Butte
14. Distance in miles and direction from nearest town or post office* Approximately 12.8 miles south of Myton, UT		11. Sec., T. R. M. or Blk. and Survey or Area Sec. 6, T9S R17E
15. Distance from proposed* location to nearest property or lease line, ft. Approx. 124' f/lse, NA f/unit (Also to nearest drig. unit line, if any)	16. No. of acres in lease 640.00	12. County or Parish Duchesne
17. Spacing Unit dedicated to this well 20 Acres	18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1630'	13. State UT
19. Proposed Depth 6,110'	20. BLM/BIA Bond No. on file WYB000493	
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5304' GL	22. Approximate date work will start* 2nd Qtr. 2011	23. Estimated duration (7) days from SPUD to rig release

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, must be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO must be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification
- Such other site specific information and/or plans as may be required by the BLM.

25. Signature <i>Mandie Crozier</i>	Name (Printed/Typed) Mandie Crozier	Date 1/12/11
Title Regulatory Specialist		

Approved by (Signature) <i>Jerry Kenczka</i>	Name (Printed/Typed) Jerry Kenczka	Date DEC 13 2011
Title Assistant Field Manager Lands & Mineral Resources		
Office VERNAL FIELD OFFICE		

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

CONDITIONS OF APPROVAL ATTACHED

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

(Continued on page 2)

DEC 19 2011

*(Instructions on page 2)

NOTICE OF APPROVAL

NOS ^{APD} posted 4/14/2011

UDOGM

AFMSS# 11RRH2064A

DIV. OF OIL, GAS & MINING

RECEIVED

JAN 14 2011

BLM VERNAL, UTAH

NO NOS



**UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE**

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company
Well No: GMBU W-31-8-17
API No: 43-047-50584

013

Location: NENW, Sec. 6, T9S, R17E
Lease No: UTU-020252A
Agreement:

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	- Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	- Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: blm ut vn opreport@blm.gov
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

**SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.
- After cessation of drilling and completion operations, any visible or measurable layer of oil must be removed from the surface of the reserve pit and the pit kept free of oil.
- Pits must be free of oil and other liquid and solid wastes prior to filling. Pit liners must not be breached (cut) or filled (squeezed) while still containing fluids. The pit liner must be removed to the solids level or treated to prevent its reemergence to the surface or its interference with long-term successful revegetation.

If construction and drilling is anticipated during any of the following wildlife seasonal or spatial restrictions, a qualified consulting firm biologist must be contacted 2 weeks prior in order to conduct applicable surveys using an accepted protocol prior to any ground disturbing activities.

- Three raptor nest surveys must be conducted during the nesting season within ½ mile of the project area(s). It is recommended that these surveys be spaced 3 weeks apart, so nesting status and reproductive success can be verified and documented.
- No surface occupancy or use is allowed within ½ mile of golden eagle nests from January 1 through August 31. If during the surveys known nests/habitat is found to be inactive, an exemption may be requested in writing, survey results reviewed and approved by ~~a~~ BLM ~~minerals biologist~~ *the Authorized Officer* before granting the exemption.
- Mountain plover surveys will be conducted to protocol by a professional Environmental Consulting Firm biologist prior to any ground disturbing activities. Reports from survey results must be reviewed by a BLM minerals biologist prior to proceeding with the proposed project. A seasonal restriction for all ground disturbing activities in mountain plover habitat from May 1-June 15 is required.
- No surface occupancy or use is allowed within 1/2 mile of red-tailed hawk nests from March 1 to August 15. If during the surveys known nests/habitat is found to be inactive, an exemption may be requested in writing, survey results reviewed and approved by ~~a~~ BLM ~~minerals biologist~~ *the Authorized Officer* before granting the exemption.
- Install hospital mufflers where possible to reduce noise impacts to wildlife.

Reclamation

- Reclamation will be completed in accordance with the Newfield Exploration Company Castle Peak and Eight Mile Flat Reclamation Plan on file with the Vernal Field Office of the BLM.
- The reclamation seed mix will incorporate low growing grasses, instead of crested wheatgrass, which negatively impacts mountain plover habitat.
- Appropriate erosion control and revegetation measures will be employed. In areas with unstable soils where seeding alone may not adequately control erosion, grading will be used to minimize slopes and water bars will be installed on disturbed slopes. Erosion control efforts will be monitored by Newfield and, if necessary, modifications will be made to control erosion.

Monitoring and Reporting

- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) that designates the proposed site-specific monitoring and reference sites chosen for the location. A description of the proposed sites shall be included, as well as a map showing the locations of the proposed sites.
- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) 3 growing seasons after reclamation efforts have occurred evaluating the status of the reclaimed areas in order to determine whether the BLM standards set forth in the Green River District Reclamation Guidelines have been met (30% or greater basal cover).

**DOWNHOLE PROGRAM
CONDITIONS OF APPROVAL (COAs)**

SITE SPECIFIC DOWNHOLE COAs:

- Newfield Production Co. shall comply with all applicable requirements in the SOP (version: "Greater Monument Butte Green River Development Program", June 24, 2008). The operator shall comply with applicable laws and regulations; with lease terms, Onshore Oil and Gas Orders, NTL's; and with other orders and instructions of the authorized officer.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB

or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to BLM_UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location ($\frac{1}{4}$ $\frac{1}{4}$, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid,

and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross 29 Submitted By
Branden Arnold Phone Number 435-401-0223
Well Name/Number GMB W-31-8-17
Qtr/Qtr NE/NW Section 6 Township 9S Range 17E
Lease Serial Number UTU-020252A
API Number 43-013-50584

Spud Notice – Spud is the initial spudding of the well, not drilling out below a casing string.

Date/Time 1/10/12 9:00 AM PM

Casing – Please report time casing run starts, not cementing times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 1/10/12 3:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks _____

CONFIDENTIAL

FORM 3160-5
(August 2007)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include area code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
069 0673 FNL 1973 FWL
Section 34 T8S R17E

5. Lease Serial No.

USA UTU-020252-A

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

GMBU

8. Well Name and No.

GRTR MON BUTTE W-31-8-17

9. API Well No.

4301350584

10. Field and Pool, or Exploratory Area

GREATER MB UNIT

11. County or Parish, State

DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recomplate in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 1/10/12 MIRU Ross #29. Spud well @9:00 AM. Drill 320' of 12 1/4" hole with air mist. TIH W/ 8 Jt's 8 5/8" J-55 24# csgn. Set @ 341.42 KB. On 1/11/12 cement with 160 sks of class "G" w/ 2% CaCL2 + 0.25#/sk Cello- Flake Mixed @ 15.8ppg w/ 1.17ft3/sk yield. Returned 1 barrels cement to pit. WOC.

RECEIVED

JAN 24 2012

DIV. OF OIL, GAS & MINING

I hereby certify that the foregoing is true and correct (Printed/ Typed) Branden Arnold	Title
Signature <i>Branden Arnold</i>	Date 01/19/2012

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____	Title	Date
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

Casing / Liner Detail

Well: GMBU W-31-8-17
 Prospect: Monument Butte
 Foreman: _____
 Run Date: 1/10/2012
 String Type: Conductor, 14", 36.7#, H-40, W (Welded)

- Detail From Top To Bottom -

Depth	Length	JTS	Description	OD	ID
10.00	20.00	1	14" CONDUCTOR	14.000	

Cement Detail

Cement Company:					
Slurry	# of Sacks	Weight (ppg)	Yield	Volume (ft³)	Description - Slurry Class and Additives
Stab-In-Job?			Cement To Surface?		
BHT:			Est. Top of Cement:		
Initial Circulation Pressure:			Plugs Bumped?		
Initial Circulation Rate:			Pressure Plugs Bumped:		
Final Circulation Pressure:			Floats Holding?		
Final Circulation Rate:			Casing Stuck On / Off Bottom?		
Displacement Fluid:			Casing Reciprocated?		
Displacement Rate:			Casing Rotated?		
Displacement Volume:			CIP:		
Mud Returns:			Casing Wt Prior To Cement:		
Centralizer Type And Placement:			Casing Weight Set On Slips:		

Casing / Liner Detail

Well GMBU W-31-8-17
 Prospect Monument Butte
 Foreman _____
 Run Date: 1/10/2012
 String Type Surface, 8.625", 24#, J-55, STC (Generic)

- Detail From Top To Bottom -

Depth	Length	JTS	Description	OD	ID
10.00	288.85	7	8 5/8 surface casing	8.620	
298.85	1.42		Wellhead		
300.27	-2.00		Cutoff		
298.27	42.25	1	Shoe JT.	8.620	
340.52	0.90		Guide Shoe		
341.42			Total KB		

Cement Detail

Cement Company:					
Slurry	# of Sacks	Weight (ppg)	Yield	Volume (ft³)	Description - Slurry Class and Additives
Slurry 1	160	15.8	1.17	187.2	G*+2%CaCl Mixed@ 15.8ppg W/1.17
Stab-In-Job?			Cement To Surface?		
BHT:			0	Est. Top of Cement:	
Initial Circulation Pressure:				Plugs Bumped?	
Initial Circulation Rate:				Pressure Plugs Bumped:	
Final Circulation Pressure:				112	
Final Circulation Rate:				Floats Holding?	
Displacement Fluid:			Water	Casing Stuck On / Off Bottom?	
Displacement Rate:				Casing Reciprocated?	
Displacement Volume:			18.4	Casing Rotated?	
Mud Returns:				CIP:	
Centralizer Type And Placement:				11:10	
Middle of first, top of second and third for a total of three.					
Casing Wt Prior To Cement:			Casing Weight Set On Slips:		

STATE OF UTAH
 DIVISION OF OIL, GAS AND MINING
 ENTITY ACTION FORM -FORM 6

OPERATOR: **NEWFIELD PRODUCTION COMPANY**
 ADDRESS: **RT. 3 BOX 3630**
MYTON, UT 84052

OPERATOR ACCT. NO. **N2695**

ACTION CODE	CURRENT ENTITY NO	NEW ENTITY NO	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4301350497	GMBU R-17-9-17	SWSE	17	9S	17E	DUCHESNE	12/30/2011	1/31/12
WELL 1 COMMENTS: GRRV BHL: NESW											
B	99999	17400	4301350498	GMBU S-17-9-17	NESE	17	9S	17E	DUCHESNE	12/30/2011	1/31/12
GRRV BHL: NESE											
B	99999	17400	4301350582	GMBU H-5-9-17	SENW	5	9S	17E	DUCHESNE	1/6/2012	1/31/12
GRRV BHL: NWNE											
B	99999	17400	4301350583	GMBU M-5-9-17	NWSE	5	9S	17E	DUCHESNE	1/6/2012	1/31/12
GRRV BHL: NWSE											
B	99999	17400	4301350584	GMBU W-31-8-17	SWSE	34	8S	17E	DUCHESNE	1/10/2012	1/31/12
GRRV BHL: S 31 T 8S SWSE											
B	99999	17400	4301350587	GMBU X-31-8-17	SWSW	34	8S	17E	DUCHESNE	1/10/2012	1/31/12
GRRV BHL: S:31 T:8S SWSW											

ACTION CODES (See instructions on back of form)


- A - 1 new entity for new well (single well only)
- B - well to existing entity (group or unit well)
- C - from one existing entity to another existing entity
- D - well from one existing entity to a new entity
- E - other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected

RECEIVED

JAN 19 2012

DIV. OF OIL, GAS & MINING


 Signature
 Production Clerk

Jentri Park

01/19/12

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-020252A
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Oil Well		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		8. WELL NAME and NUMBER: GREATER MON BUTTE W-31-8-17
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052		9. API NUMBER: 43013505840000
PHONE NUMBER: 435 646-4825 Ext		9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0673 FNL 1973 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENW Section: 06 Township: 09.0S Range: 17.0E Meridian: S		COUNTY: DUCHESNE
		STATE: UTAH

11.

CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 2/27/2012	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above well was placed on production on 02/27/2012 at 16:00 hours.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
June 08, 2012**

NAME (PLEASE PRINT) Jennifer Peatross	PHONE NUMBER 435 646-4885	TITLE Production Technician
SIGNATURE N/A	DATE 6/8/2012	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9 5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-020252A
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	6. IF INDIAN, ALLOTTEE OR TRIBE NAME: 7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
1. TYPE OF WELL Oil Well	8. WELL NAME and NUMBER: GREATER MON BUTTE W-31-8-17
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	9. API NUMBER: 43013505840000
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0673 FNL 1973 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENW Section: 06 Township: 09.0S Range: 17.0E Meridian: S	9. FIELD and POOL or WILDCAT: MONUMENT BUTTE COUNTY: DUCHESNE STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 2/27/2012	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above well was placed on production on 02/27/2012 at 16:00 hours.

RECEIVED

JUN 21 2012

DIV. OF OIL, GAS & MINING

NAME (PLEASE PRINT) Jennifer Peatross	PHONE NUMBER 435 646-4885	TITLE Production Technician
SIGNATURE N/A	DATE 6/8/2012	

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB NO. 1004-0137
Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

5. Lease Serial No.
UTU-020252A

1a. Type of Well Oil Well Gas Well Dry Other
b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Reserv.,
Other: _____

6. If Indian, Allottee or Tribe Name
NA

7. Unit or CA Agreement Name and No.
GMBU (GRRV)

2. Name of Operator
NEWFIELD EXPLORATION COMPANY

8. Lease Name and Well No.
GMBU W-31-8-17

3. Address
1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
(435) 646-3721

9. AFI Well No.
43-013-50584

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

10. Field and Pool or Exploratory
MONUMENT BUTTE

11. Sec., T., R., M., on Block and
Survey or Area
SEC. 6, T9S, R17E

At surface 673' FNL & 1973' FWL (NE/NW) SEC. 6, T9S, R17E (UTU-020252A)

At top prod. interval reported below 123' FNL & 2458' FWL (NE/NW) SEC. 6, T9S, R17E (UTU-020252A)

At total depth 179' FSL & ~~2566'~~ ^{2458'} FEL (SW/SE) SEC. 31, T8S, R17E (UTU-74869) *Bill by OHSM*

12. County or Parish
DUCHESNE

13. State
UT

14. Date Spudded
01/10/2012

15. Date T.D. Reached
02/04/2012

16. Date Completed 03/12/2012
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
5304' GL 5314' KB

18. Total Depth: MD 6299'
TVD 6180'

19. Plug Back T.D.: MD 6250'
TVD 6131'

20. Depth Bridge Plug Set:
MD
TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND.

22. Was well cored? No Yes (Submit analysis)
Was DST run? No Yes (Submit report)
Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sks. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	341'		160 CLASS "G"			
7-7/8"	5-1/2" J-55	15.5#	0	6292'		275 PRIMLITE 450 50/50 POZ		238'	

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 5569'	TA @ 5470'						

25. Producing Intervals

26. Perforation Record

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Green River	5444'	5486'	5444-5486'	.34"	21	
B)						
C)						
D)						

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
5444-5486'	Frac w/ 244731# 20/40 white sand and 1921 bbls Lightning 17 fluid, in 1 stages.

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
2/26/12	3/22/12	24	→	94	70	9			2-1/2" x 1-3/4" x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

RECEIVED

JUL 02 2012

*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production →	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate →	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD AND USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS

Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
GREEN RIVER	5444'	5486'		GARDEN GULCH MARKER	3833'
				GARDEN GULCH 1	4038'
				GARDEN GULCH 2	4158'
				POINT 3 MARKER	4431'
				X MRKR	4683'
				Y MRKR	4719'
				DOUGLAS CREEK MRKR	4849'
				BI-CARBONATE	5097'
				B LIMESTONE	5221'
				CASTLE PEAK	5726'
				BASAL CARBONATE	6158'
				WASATCH	6282'


32. Additional remarks (include plugging procedure):

The above well was placed on production on 2/27/2012, but was shut in while adjacent well was completed. The pumping unit was activated on 3/12/2012 and test data was taken ten days following, on 3/22/2012.

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other:

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Jennifer Peatross Title Production Technician
 Signature  Date 04/09/2012

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

NEWFIELD



NEWFIELD EXPLORATION

**USGS Myton SW (UT)
SECTION 6 T9S, R17E
W-31-8-17**

Wellbore #1

Design: Actual

Standard Survey Report

18 February, 2012





Payzone Directional Survey Report



Company: NEWFIELD EXPLORATION
Project: USGS Myton SW (UT)
Site: SECTION 6 T9S, R17E
Well: W-31-8-17
Wellbore: Wellbore #1
Design: Actual

Local Co-ordinate Reference: Well W-31-8-17
TVD Reference: W-31-8-17 @ 5316.0ft (NDSI SS #2)
MD Reference: W-31-8-17 @ 5316.0ft (NDSI SS #2)
North Reference: True
Survey Calculation Method: Minimum Curvature
Database: EDM 2003.21 Single User Db

Project:	USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Utah Central Zone		

Site:	SECTION 6 T9S, R17E				
Site Position:		Northing:	7,195,000.00 ft	Latitude:	40° 3' 47.061 N
From:	Lat/Long	Easting:	2,047,000.00 ft	Longitude:	110° 2' 50.009 W
Position Uncertainty:	0.0 ft	Slot Radius:	"	Grid Convergence:	0.93 °

Well:	W-31-8-17, SHL LAT: 40° 03' 54.97" LONG: 110° 03' 04.66"					
Well Position	+N/-S	0.0 ft	Northing:	7,195,781.67 ft	Latitude:	40° 3' 54.970 N
	+E/-W	0.0 ft	Easting:	2,045,848.19 ft	Longitude:	110° 3' 4.660 W
Position Uncertainty		0.0 ft	Wellhead Elevation:	5,316.0 ft	Ground Level:	5,304.0 ft

Wellbore:	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination	Dip Angle	Field Strength
	IGRF2010	7/29/2010	(°)	(°)	(nT)
			11.42	65.84	52,372

Design:	Actual				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:		Depth From (TVD)	+N/-S	+E/-W	Direction
		(ft)	(ft)	(ft)	(°)
		0.0	0.0	0.0	40.22

Survey Program	Date 2/18/2012				
From	To	Survey (Wellbore)	Tool Name	Description	
(ft)	(ft)				
351.0	6,299.0	Survey #1 (Wellbore #1)	MWD	MWD - Standard	

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
351.0	1.22	120.40	351.0	-1.9	3.2	0.6	0.35	0.35	0.00
382.0	1.30	104.40	382.0	-2.1	3.8	0.8	1.16	0.26	-51.61
413.0	1.40	103.70	413.0	-2.3	4.6	1.2	0.33	0.32	-2.26
443.0	1.80	113.90	442.9	-2.6	5.3	1.5	1.63	1.33	34.00
473.0	2.10	115.50	472.9	-3.0	6.3	1.7	1.02	1.00	5.33
504.0	2.40	105.00	503.9	-3.4	7.4	2.2	1.64	0.97	-33.87
535.0	2.60	101.40	534.9	-3.7	8.7	2.8	0.82	0.65	-11.61
565.0	2.90	103.10	564.8	-4.1	10.1	3.4	1.04	1.00	5.67
596.0	3.20	99.30	595.8	-4.4	11.8	4.2	1.17	0.97	-12.26
626.0	3.70	104.70	625.7	-4.8	13.5	5.1	1.99	1.67	18.00
654.0	3.60	101.30	653.7	-5.2	15.2	5.9	0.85	-0.36	-12.14
687.0	4.00	97.00	686.6	-5.5	17.4	7.0	1.49	1.21	-13.03

**Payzone Directional
Survey Report**



Company:	NEWFIELD EXPLORATION	Local Co-ordinate Reference:	Well W-31-8-17
Project:	USGS Myton SW (UT)	TVD Reference:	W-31-8-17 @ 5316.0ft (NDSI SS #2)
Site:	SECTION 6 T9S, R17E	MD Reference:	W-31-8-17 @ 5316.0ft (NDSI SS #2)
Well:	W-31-8-17	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Actual	Database:	EDM 2003.21 Single User Db

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
718.0	4.50	93.30	717.5	-5.7	19.7	8.4	1.84	1.61	-11.94
748.0	4.80	89.90	747.4	-5.8	22.1	9.9	1.36	1.00	-11.33
779.0	5.00	85.20	778.3	-5.6	24.8	11.7	1.45	0.65	-15.16
809.0	5.50	85.00	808.2	-5.4	27.5	13.6	1.67	1.67	-0.67
840.0	6.00	86.90	839.0	-5.2	30.6	15.8	1.73	1.61	6.13
884.0	6.70	82.70	882.8	-4.7	35.4	19.3	1.91	1.59	-9.55
928.0	6.90	76.20	926.5	-3.8	40.6	23.3	1.81	0.45	-14.77
972.0	7.10	72.50	970.1	-2.3	45.7	27.7	1.12	0.45	-8.41
1,015.0	6.90	70.00	1,012.8	-0.7	50.7	32.2	0.85	-0.47	-5.81
1,059.0	7.30	65.00	1,056.5	1.4	55.7	37.0	1.67	0.91	-11.36
1,103.0	7.30	57.80	1,100.1	4.1	60.6	42.3	2.08	0.00	-16.36
1,147.0	7.50	52.40	1,143.7	7.3	65.2	47.7	1.64	0.45	-12.27
1,191.0	7.50	47.20	1,187.4	11.0	69.6	53.4	1.54	0.00	-11.82
1,234.0	7.34	41.61	1,230.0	15.0	73.5	58.9	1.72	-0.37	-13.00
1,278.0	6.72	34.49	1,273.7	19.2	76.8	64.3	2.43	-1.41	-16.18
1,322.0	7.34	35.77	1,317.4	23.6	79.9	69.6	1.45	1.41	2.91
1,366.0	7.87	33.88	1,361.0	28.4	83.2	75.4	1.33	1.20	-4.30
1,410.0	7.82	38.97	1,404.6	33.2	86.8	81.4	1.58	-0.11	11.57
1,453.0	8.30	43.00	1,447.1	37.8	90.8	87.5	1.72	1.12	9.37
1,497.0	8.88	41.90	1,490.6	42.6	95.2	94.0	1.37	1.32	-2.50
1,541.0	9.20	45.50	1,534.1	47.6	100.0	100.9	1.48	0.73	8.18
1,585.0	9.80	42.80	1,577.5	52.8	105.0	108.1	1.35	0.91	-6.14
1,629.0	9.50	45.10	1,620.9	58.0	110.0	115.4	0.90	-0.23	5.23
1,673.0	9.50	43.63	1,664.3	63.2	115.1	122.6	0.55	0.00	-3.34
1,716.0	9.50	45.20	1,706.7	68.3	120.1	129.7	0.60	0.00	3.65
1,760.0	9.90	46.40	1,750.1	73.5	125.4	137.1	1.02	0.91	2.73
1,804.0	10.02	43.63	1,793.4	78.8	130.8	144.6	1.12	0.27	-6.30
1,848.0	10.02	40.16	1,836.7	84.5	135.9	152.3	1.37	0.00	-7.89
1,892.0	10.30	40.56	1,880.0	90.5	140.9	160.1	0.66	0.64	0.91
1,936.0	10.60	42.31	1,923.3	96.4	146.2	168.0	0.99	0.68	3.98
1,979.0	11.70	44.30	1,965.5	102.5	151.9	176.3	2.71	2.56	4.63
2,023.0	11.90	42.00	2,008.6	109.0	158.1	185.3	1.16	0.45	-5.23
2,067.0	11.70	37.10	2,051.6	116.0	163.8	194.3	2.32	-0.45	-11.14
2,111.0	12.35	31.85	2,094.7	123.5	169.0	203.4	2.89	1.48	-11.93
2,155.0	13.23	30.80	2,137.6	131.9	174.0	213.0	2.07	2.00	-2.39
2,198.0	14.37	31.59	2,179.3	140.6	179.3	223.2	2.69	2.65	1.84
2,242.0	15.60	32.40	2,221.8	150.3	185.4	234.4	2.84	2.80	1.84
2,286.0	16.30	32.83	2,264.2	160.5	191.9	246.4	1.61	1.59	0.98
2,330.0	16.61	34.00	2,306.4	170.9	198.7	258.8	1.03	0.70	2.66
2,374.0	17.40	34.84	2,348.4	181.5	206.0	271.6	1.88	1.80	1.91
2,417.0	17.53	35.55	2,389.4	192.0	213.5	284.5	0.58	0.30	1.65
2,461.0	16.66	33.70	2,431.5	202.7	220.8	297.3	2.33	-1.98	-4.20
2,505.0	16.39	32.90	2,473.7	213.1	227.7	309.7	0.80	-0.61	-1.82
2,549.0	16.35	34.05	2,515.9	223.5	234.5	322.1	0.74	-0.09	2.61
2,593.0	15.60	33.39	2,558.2	233.5	241.2	334.1	1.75	-1.70	-1.50
2,636.0	14.70	32.12	2,599.7	243.0	247.3	345.2	2.23	-2.09	-2.95
2,680.0	13.60	32.43	2,642.4	252.1	253.1	355.9	2.51	-2.50	0.70
2,724.0	12.44	32.21	2,685.2	260.4	258.4	365.7	2.64	-2.64	-0.50
2,768.0	12.50	33.40	2,728.2	268.4	263.5	375.1	0.60	0.14	2.70
2,812.0	13.00	37.20	2,771.1	276.4	269.1	384.8	2.22	1.14	8.64
2,855.0	13.70	38.00	2,813.0	284.2	275.2	394.7	1.68	1.63	1.86
2,899.0	13.70	39.50	2,855.7	292.3	281.7	405.1	0.81	0.00	3.41
2,943.0	13.90	40.00	2,898.4	300.4	288.4	415.6	0.53	0.45	1.14
2,987.0	13.50	39.70	2,941.2	308.4	295.1	426.1	0.92	-0.91	-0.68



Payzone Directional Survey Report



Company: NEWFIELD EXPLORATION
 Project: USGS Myton SW (UT)
 Site: SECTION 6 T9S, R17E
 Well: W-31-8-17
 Wellbore: Wellbore #1
 Design: Actual

Local Co-ordinate Reference: Well W-31-8-17
 TVD Reference: W-31-8-17 @ 5316.0ft (NDSI SS #2)
 MD Reference: W-31-8-17 @ 5316.0ft (NDSI SS #2)
 North Reference: True
 Survey Calculation Method: Minimum Curvature
 Database: EDM 2003.21 Single User Db

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N-S (ft)	+E-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	
3,031.0	12.30	38.30	2,984.1	316.0	301.3	435.9	2.82	-2.73	-3.18	
3,074.0	11.30	40.60	3,026.2	322.8	306.9	444.7	2.57	-2.33	5.35	
3,118.0	11.60	42.80	3,069.3	329.4	312.7	453.4	1.20	0.68	5.00	
3,162.0	12.00	41.10	3,112.4	336.0	318.7	462.4	1.20	0.91	-3.86	
3,206.0	10.70	41.10	3,155.5	342.6	324.4	471.0	2.95	-2.95	0.00	
3,249.0	9.80	36.70	3,197.8	348.5	329.2	478.7	2.77	-2.09	-10.23	
3,293.0	10.60	36.20	3,241.1	354.8	333.8	486.5	1.83	1.82	-1.14	
3,337.0	11.10	41.90	3,284.3	361.2	339.0	494.7	2.69	1.14	12.95	
3,381.0	11.70	43.70	3,327.5	367.6	345.0	503.4	1.59	1.36	4.09	
3,425.0	11.50	42.30	3,370.6	374.0	351.0	512.3	0.78	-0.45	-3.18	
3,469.0	11.80	40.50	3,413.7	380.7	356.9	521.1	1.07	0.68	-4.09	
3,512.0	12.60	39.80	3,455.7	387.7	362.7	530.2	1.89	1.86	-1.63	
3,556.0	13.20	39.60	3,498.6	395.2	369.0	540.0	1.37	1.36	-0.45	
3,600.0	13.30	39.60	3,541.4	403.0	375.4	550.1	0.23	0.23	0.00	
3,644.0	13.30	41.70	3,584.2	410.7	382.0	560.3	1.10	0.00	4.77	
3,688.0	13.20	39.70	3,627.0	418.3	388.6	570.3	1.07	-0.23	-4.55	
3,732.0	12.80	38.60	3,669.9	426.0	394.8	580.2	1.07	-0.91	-2.50	
3,775.0	12.50	37.20	3,711.9	433.4	400.6	589.6	1.00	-0.70	-3.26	
3,819.0	12.90	36.50	3,754.8	441.2	406.4	599.3	0.97	0.91	-1.59	
3,863.0	12.90	38.20	3,797.7	449.0	412.4	609.1	0.86	0.00	3.86	
3,907.0	12.92	36.95	3,840.6	456.8	418.4	618.9	0.64	0.05	-2.84	
3,950.0	12.88	37.13	3,882.5	464.4	424.2	628.5	0.13	-0.09	0.42	
3,994.0	13.32	36.51	3,925.3	472.4	430.1	638.5	1.05	1.00	-1.41	
4,038.0	13.50	35.10	3,968.1	480.7	436.1	648.6	0.85	0.41	-3.20	
4,082.0	13.10	35.28	4,011.0	488.9	441.9	658.7	0.91	-0.91	0.41	
4,125.0	12.92	38.18	4,052.9	496.7	447.7	668.4	1.57	-0.42	6.74	
4,169.0	12.79	35.81	4,095.8	504.5	453.6	678.2	1.23	-0.30	-5.39	
4,213.0	13.01	37.44	4,138.7	512.4	459.5	688.0	0.97	0.50	3.70	
4,257.0	12.61	33.35	4,181.6	520.3	465.1	697.7	2.25	-0.91	-9.30	
4,301.0	11.63	34.00	4,224.6	528.0	470.3	706.8	2.25	-2.23	1.48	
4,345.0	11.69	35.55	4,267.7	535.3	475.3	715.7	0.72	0.14	3.52	
4,388.0	11.82	34.59	4,309.8	542.5	480.4	724.4	0.55	0.30	-2.23	
4,432.0	11.87	33.22	4,352.8	550.0	485.4	733.4	0.65	0.11	-3.11	
4,476.0	11.51	32.56	4,395.9	557.5	490.2	742.2	0.87	-0.82	-1.50	
4,520.0	11.25	34.32	4,439.1	564.7	495.0	750.9	0.99	-0.59	4.00	
4,564.0	11.69	36.47	4,482.2	571.9	500.1	759.6	1.39	1.00	4.89	
4,607.0	12.17	35.81	4,524.2	579.0	505.3	768.4	1.16	1.12	-1.53	
4,651.0	12.35	39.76	4,567.2	586.4	511.1	777.8	1.95	0.41	8.98	
4,695.0	11.95	40.07	4,610.3	593.5	517.0	787.0	0.92	-0.91	0.70	
4,739.0	11.73	41.17	4,653.3	600.4	522.9	796.1	0.72	-0.50	2.50	
4,783.0	11.65	43.81	4,696.4	607.0	528.9	805.0	1.23	-0.18	6.00	
4,826.0	11.65	44.51	4,738.5	613.2	534.9	813.6	0.33	0.00	1.63	
4,870.0	11.80	42.40	4,781.6	619.7	541.1	822.6	1.03	0.34	-4.80	
4,914.0	12.00	43.50	4,824.7	626.3	547.3	831.6	0.69	0.45	2.50	
4,958.0	12.50	41.70	4,867.7	633.2	553.6	840.9	1.43	1.14	-4.09	
5,002.0	12.90	41.50	4,910.6	640.4	560.0	850.6	0.91	0.91	-0.45	
5,045.0	13.30	40.90	4,952.5	647.8	566.4	860.4	0.98	0.93	-1.40	
5,089.0	13.00	42.20	4,995.3	655.2	573.1	870.4	0.96	-0.68	2.95	
5,133.0	12.30	43.40	5,038.2	662.3	579.6	880.0	1.70	-1.59	2.73	
5,177.0	12.80	41.80	5,081.2	669.4	586.1	889.5	1.38	1.14	-3.64	
5,192.3	12.76	41.21	5,096.1	671.9	588.3	892.9	0.88	-0.24	-3.84	
W-31-8-17 TGT1										
5,221.0	12.70	40.10	5,124.1	676.7	592.4	899.3	0.88	-0.22	-3.87	
5,264.0	12.00	38.70	5,166.1	683.8	598.3	908.4	1.77	-1.63	-3.26	



Payzone Directional Survey Report



Company: NEWFIELD EXPLORATION
Project: USGS Myton SW (UT)
Site: SECTION 6 T9S, R17E
Well: W-31-8-17
Wellbore: Wellbore #1
Design: Actual

Local Co-ordinate Reference: Well W-31-8-17
TVD Reference: W-31-8-17 @ 5316.0ft (NDSI SS #2)
MD Reference: W-31-8-17 @ 5316.0ft (NDSI SS #2)
North Reference: True
Survey Calculation Method: Minimum Curvature
Database: EDM 2003.21 Single User Db

Survey

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
5,308.0	11.80	38.80	5,209.2	690.9	604.0	917.5	0.46	-0.45	0.23
5,352.0	12.70	36.40	5,252.2	698.3	609.7	926.8	2.35	2.05	-5.45
5,396.0	13.00	35.20	5,295.1	706.2	615.4	936.6	0.91	0.68	-2.73
5,440.0	13.00	35.80	5,337.9	714.3	621.1	946.5	0.31	0.00	1.36
5,483.0	14.30	36.20	5,379.7	722.5	627.1	956.6	3.03	3.02	0.93
5,538.0	14.40	36.90	5,433.0	733.4	635.2	970.2	0.36	0.18	1.27
5,572.0	13.90	37.60	5,466.0	740.0	640.2	978.5	1.55	-1.47	2.06
5,616.0	13.40	38.30	5,508.7	748.2	646.6	988.9	1.20	-1.14	1.59
5,660.0	13.05	36.03	5,551.6	756.2	652.7	998.9	1.42	-0.80	-5.16
5,704.0	11.91	37.22	5,594.5	763.9	658.4	1,008.4	2.66	-2.59	2.70
5,747.0	10.50	34.75	5,636.7	770.6	663.3	1,016.7	3.46	-3.28	-5.74
5,791.0	9.93	35.19	5,680.0	777.0	667.8	1,024.5	1.31	-1.30	1.00
5,835.0	9.80	31.33	5,723.3	783.3	671.9	1,032.0	1.53	-0.30	-8.77
5,879.0	9.98	30.67	5,766.7	789.8	675.8	1,039.4	0.48	0.41	-1.50
5,923.0	10.80	33.79	5,810.0	796.5	680.0	1,047.3	2.26	1.86	7.09
5,967.0	10.77	35.24	5,853.2	803.3	684.7	1,055.5	0.62	-0.07	3.30
6,010.0	10.63	38.67	5,895.4	809.7	689.5	1,063.5	1.52	-0.33	7.98
6,054.0	10.17	39.81	5,938.7	815.8	694.5	1,071.4	1.15	-1.05	2.59
6,098.0	11.00	37.74	5,982.0	822.1	699.6	1,079.5	2.07	1.89	-4.70
6,142.0	11.25	35.50	6,025.2	828.9	704.6	1,087.9	1.13	0.57	-5.09
6,185.0	11.16	33.13	6,067.3	835.8	709.3	1,096.3	1.09	-0.21	-5.51
6,229.0	10.11	34.05	6,110.6	842.6	713.8	1,104.3	2.42	-2.39	2.09
6,245.0	9.98	34.97	6,126.3	844.9	715.4	1,107.1	1.29	-0.81	5.75
6,299.0	9.00	35.50	6,179.6	852.2	720.5	1,116.0	1.82	-1.81	0.98

Checked By: _____ Approved By: _____ Date: _____






Project: USGS Myton SW (UT)
 Site: SECTION 6 T9S, R17E
 Well: W-31-8-17
 Wellbore: Wellbore #1
 Design: Actual



Azimuths to True North
 Magnetic North: 11.42°

Magnetic Field
 Strength: 52371.6snT
 Dip Angle: 65.84°
 Date: 7/29/2010
 Model: IGRF2010

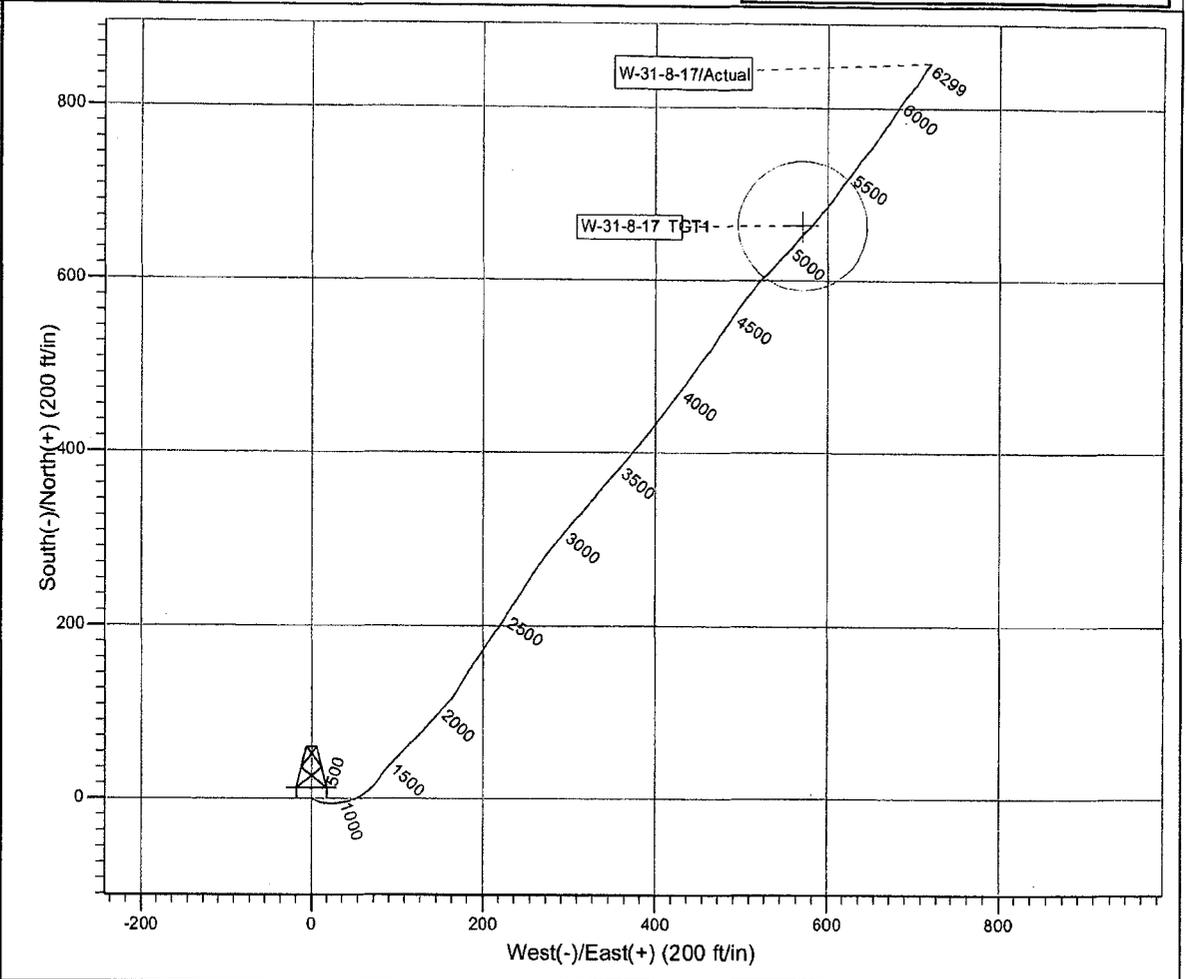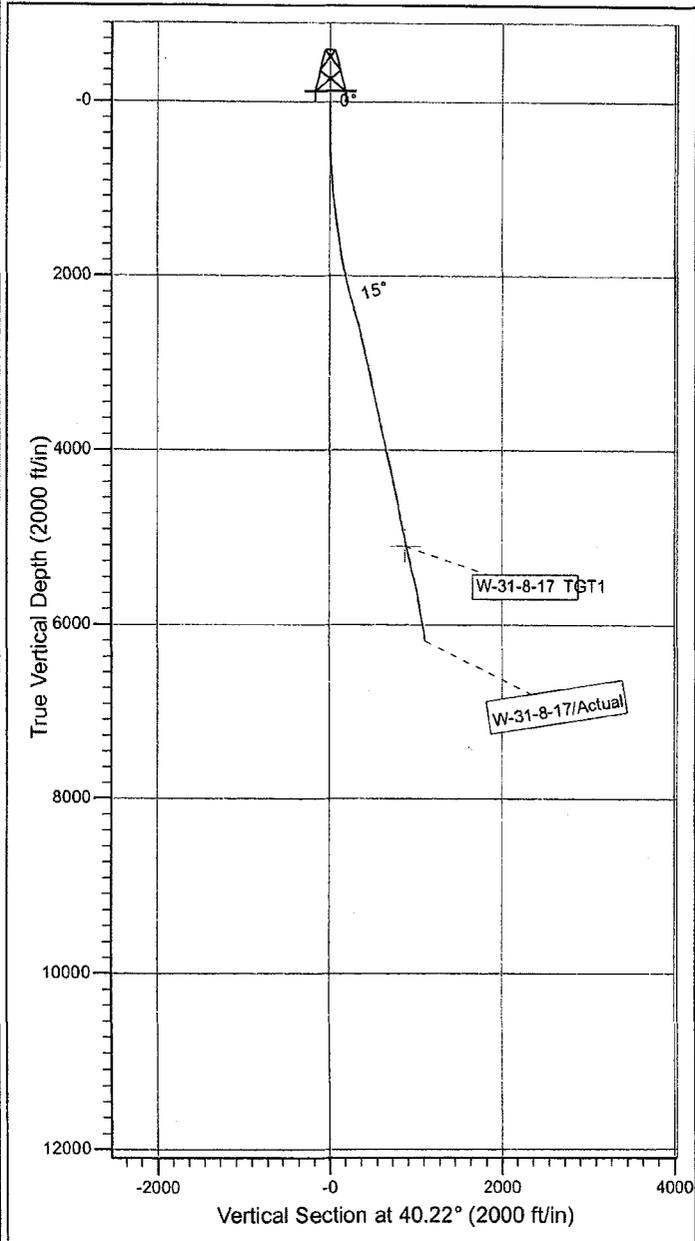

Design: Actual (W-31-8-17/Wellbore #1)

Created By: Sarah Welt Date: 15:00, February 18 2012

THIS SURVEY IS CORRECT TO THE BEST OF
 MY KNOWLEDGE AND IS SUPPORTED
 BY ACTUAL FIELD DATA

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-020252A
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Oil Well		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		8. WELL NAME and NUMBER: GREATER MON BUTTE W-31-8-17
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052		9. API NUMBER: 43013505840000
PHONE NUMBER: 435 646-4825 Ext		9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0673 FNL 1973 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENW Section: 06 Township: 09.0S Range: 17.0E Meridian: S		COUNTY: DUCHESNE
		STATE: UTAH

11.

CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 5/10/2013	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> OTHER	OTHER: <input type="text" value="Recompletion"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above well was recompleted and placed back on production. See attached Daily Activity Report.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
August 28, 2013**

NAME (PLEASE PRINT) Mandie Crozier	PHONE NUMBER 435 646-4825	TITLE Regulatory Tech
SIGNATURE N/A	DATE 7/24/2013	

Daily Activity Report

Format For Sundry

GMBU W-31-8-17

3/1/2013 To 5/30/2013

4/23/2013 Day: 1

Recompletion

Nabors #1450 on 4/23/2013 - MIRUSU, TOO H w/ rods & pump, Unset Tac, NU & test frac valve & BOPs - DROP LINES, R.D. WRAP LINES & DO PRE -TRIP INSPECT, LOAD TRAILERS - Travel time / JSP MEETING - N.U. BOP'S - SPOT IN, WAIT FOR DEADMEN TO BE TESTED & 1 TO BE INSTALLED, RUSU, STRETCH LINES - FLUSH CSG w/ 60 BW 7% KCL, R/D HORSEHEAD, UNSEAT POLISH ROD, L.D. 3 - RODS, FLUSH TBG w/ 40 BW 7% KCL @ 250 DEG, SOFT SEAT PUMP, FILL w/ 10 BW 7% KCL, PT TBG TO 3000#, GOOD - N.U. FLOW TEE, L.D. POLISH ROD & PONIES, POOH w/ 75 -7/8" 4per, 136 -3/4" 4per, L.D. 5 -WT BARS w/ STABILIZERS, L.D. PUMP - N.D. WELLHEAD & FLOWLINE, STRIP OFF HANGER, UNSET TAC, STRIP ON HANGER, LAND IN WH w/ BPV IN PLACE - N.U. BLIND RAMS, MAN FRAC VALVE, DOUBLE PIPE RAMS w/ WASHINGTON HEAD, TIGHTEN BOLTS - R.U. B&C QUICK TEST & TEST FRAC VALVE, BLIND RAMS, DOUBLE PIPE RAMS & GATE VALVES HIGH & LOW, R.U. PUMP & HARDLINE - CREW TRAVEL - MOVE FROM THE CLF 1 -35 -8-17 TO W-31-8-17 (6 Miles)

Daily Cost: \$10,989

Cumulative Cost: \$10,989

4/24/2013 Day: 2

Recompletion

Nabors #1450 on 4/24/2013 - TIH & TAG FILL @ 6161', CLEAN OUT TO PBTD @ 6250', 89' FILL, LOST 300 BBLS WATER, TOO H SCANNING TBG, (170-YELLOW BAND & 4-BLUE BAND), RU PERFORATORS WIRELINE & PERF CP-5 & PB-10 FORMATIONS - BLEED WELL, ON VACUUM, PREP & TALLY TBG, M.U. & RIH w/ 20 -JNTS 2 7/8" J -55 TBG, TAG FILL @ 6161' - CIRC 250 BBLS 7% KCL TO CATCH CIRC, CLEAN OUT SAND TO PBTD @ 6250', 89' FILL, CIRC SAND OUT, LOST 300 BW - TOO H & STAND BACK 22 -JNTS THAT WE PICKED UP, R.U. TBG SCANNER (PRS) TOO H w/ 170 -YELLOW 2 7/8" J -55 JNTS TBG, 4 -BLUE JNTS TBG, L.D. T/A, 1 -JNT, S/N, 2 -JNTS TBG & N.C. - R.U. PERFORATORS WIRELINE, MU & RIH & W/ 3 1/8" DISPOSABLE SLICK GUNS (16g, 0.34 EH, 21.00 pen), PERFORATE CP-5 @ 6133'-34', 6106'-07', 6079'-80' & PB-10 @ 4609'-11' & 4602'-03', POOH & RD WIRELINE, SWI - R.U. TBG P.U. LINE, SPOT TBG TRAILER IN, PREP & TALLY 1st ROW, TRANSFER OIL FROM FLAT TANK TO PRODUCTION TANKS, SWI, S.D.F.N. - CREW TRAVEL - Travel time / JSP MEETING - USING A TBG SWIVEL

Daily Cost: \$16,555

Cumulative Cost: \$27,544

4/25/2013 Day: 3

Recompletion

Nabors #1450 on 4/25/2013 - PU WFT 5 1/2" plug & pkr, PU N-80 tbg, Break down PB-10 & CP-5 formations, Could not get middle CP-5 to break down (6106'-07'), Set tools for 1st frac - Crew Travel - Crew Travel & Safety Meeting - MU WFT 5 1/2" HD pkr & TS bridge plug, PU 147-jts 2 7/8" N-80 tbg, Set RBP @ 4620', LD 1-jt & set PKR @ 4596', RU BMW Hot oil truck, Fill tbg w/ 18 bbls 7% KCL, Break down PB-10 formation (4602'-03', 4609'-11') w/ 3 bbls 7% KCL @ 2,900 psi, ISIP 1,000 psi, Fill csg w/ 49 bbls 7% KCL, Release PKR, PU 1-jt tbg, Latch on & release RBP - Continue PU 2 7/8" N-80 tbg, PU ttl of 193-jts 2 7/8" N-80- tbg, Set RBP @ 6089', LD 2-jts & set PKR @ 6026', RU BMW Hot oil truck, Fill tbg w/ 8 bbls 7% KCL, Break down CP-5 formation (6079'-80') w/ 3 bbls 7% KCL @ 3,900 psi, ISIP 1,900 psi, Fill csg w/ 22 bbls 7% KCL, Release PKR, PU 2-jt tbg, Latch on & release RBP - PU 1-jt tbg (194-jts in), Set RBP @ 6120', LD 1-jt tbg & PU 12' tbg subs, Set PKR @ 6087', RU BMW Hot oil truck, Fill tbg

w/ 3 bbls 7% KCL, Try to break down CP-5 formation (6106'-6107'), Press up to 4,800 psi several times & could not get to break, Fill csg w/ 8 bbls 7% KCL, Release PKR, LD tbg subs, PU 1-jt tbg, Latch on & release RBP - PU 2 jts tbg (196-jts in), Set RBP @ 6175', POOH w/ 2-jts & PU 10' tbg sub, Set PKR @ 6116', RU BMW Hot oil truck, Break down CP-5 formation (6133'-34") w/ 3 bbls 7% KCL @ 2,200 psi, ISIP 1,600 psi. - Release PKR, POOH w/ 4-jts tbg, Stab washington rubber & MU wash stand, MU frac valve w/ 6' tbg sub, Set PKR 5960', EOT @ 5970', SWI

Daily Cost: \$8,766

Cumulative Cost: \$36,310

4/26/2013 Day: 4

Recompletion

Nabors #1450 on 4/26/2013 - RU Baker Hughes & frac CP-5 formation, Flow back well recover 770 bbls, Release & move tools, RU Baker Hughes & frac PB-10 formation, Flow back well recover 210 bbls, SWI - Crew Travel - Open well to tank w/ adjustable choke @ approx. 3 bpm, Recover 210 bbls, Show of oil, SWI, - Finish RU Baker Hughes frac equipment w/ pop off on csg set @ 1500 psi. - (Stg #1) Hold pre-job safety meeting, Press test lines to 6000 psi, Open well w/ 0 psi, Load tbg w/ 7 bbls 7% KCL, Break down CP-5 formation @ 3770 psi w/ 8 bbls 7% KCL @ 2.1 bpm, Pump 6 bbls 15% HCL Pump 95.2 bbls to get acid on perfs & find x-link, Pump 15 bbls 7% KCL pad to load screws, Pump 730.2 bbls 7% KCL 1-2# sand (ramped), Pump 553.4 bbls 7% KCL 2-4# sand (ramped), Pumped 37.1 bbls 7% KCL slick water flush, Max psi 4578, Avg psi 4119, Max rate 14.8, Avg rate 13.8, ISIP 2278, F.G. .81, Pumped 110,123# sand in formation, Pumped total of 1431 bbls, (Pumped 116 bbls 7% KCL down csg to monitor during job), Wait on 5,10 & 15-min (5-min 1789, 10-min 1740, 15-min 1726) (Tried to increase rate but could not due to pumps kicking out) - Open well to tank w/ adjustable choke @ approx. 3 bpm, Recover 770 bbls, No sign of oil. - RU pump to csg & apply 500 psi, Release PKR & reverse tbg clean, TIH w/ 6-jts tbg, Tag sand @ 6145', Circulate sand off plug reverse clean, Release RBP, TOOH w/ 49-jts tbg, Set RBP @ 4639', TOOH w/ 2-jts tbg, MU frac valve & 6' tbg sub, Set PKR @ 4569', EOT @ 4579', RU pump to csg & apply 500 psi to monitor during job. - (Stg #1) Hold pre-job safety meeting, Press test lines to 6000 psi, Open well w/ 40 psi, Break down PB-10 formation @ 4330 psi w/ 1.3 bbls 7% KCL @ 1.5 bpm, Pump 6 bbls 15% HCL Pump 73 bbls to get acid on perfs & find x-link, Pump 15 bbls 7% KCL pad to load screws, Pump 222.2 bbls 7% KCL 1-2# sand (ramped), Pump 198.4 bbls 7% KCL 2-4# sand (ramped), Pumped 27.6 bbls 7% KCL slick water flush, Max psi 4722, Avg psi 4279, Max rate 19.1, Avg rate 18.8, ISIP 2224, F.G. .93, Pumped 32,819# sand in formation, Pumped total of 536 bbls, Wait on 5,10 & 15-min (5-min 2028, 10-min 1950, 15-min 1900)

Daily Cost: \$107,410

Cumulative Cost: \$143,720

4/27/2013 Day: 5

Recompletion

Nabors #1450 on 4/27/2013 - Release tools, LD N-80 tbg, TIH w/ production tbg, Set TAC & land tbg, NU wellhead - CREW TRAVEL HOME - M/U & RIH W/ PRODUCTION AS FOLLOWS: 2 7/8" N/C, 1-JT 2 7/8" J-55 TBG, 2 7/8" S/N, 2-JTS 2 7/8" J-55 TBG, 5 1/2" B2-C TAC, RIH W/ 193 JTS - RIH W/ REMAINING N-80 TBG FROM DERRICK - L/D REMAINING WORKSTRING - - LAY DOWN WORKSTRING - L/D PLUG AND PACKER - SITP 250 PSI - BLEED TBG OFF - PRESSURE CSG UP TO 200 PSI - RELEASE PACKER - CIRCULATE DOWN CSG W/ 30 BBLS - P/U 1 JT - RIH W/ WASH STAND - CIRCULATE DOWN TO PLUG - LATCH ONTO PLUG - CIRCULATE WELL W/ 50 BBLS - RELEASE PLUG - WATCH WELL FOR FLOW FOR 10 MINUTES - CREW TRAVEL AND JSP MEETING - SET TAC FROM FLOOR - LAND TBG ON HANGER - R/D WORKFLOOR - N/D DOUBLE GATE PIPE RAMS - N/D FRAC VALVE - N/D SINGLE GATE BLIND RAMS - UNLAND TBG - REMOVE SUB FROM BELOW HANGER - RELAND TBG IN 18000#'S TENSION - N/U WELLHEAD - CHANGE OVER FOR RODS - SWIFW

Daily Cost: \$7,037
Cumulative Cost: \$150,757

4/30/2013 Day: 6

Recompletion

Nabors #1450 on 4/30/2013 - TIH w/ pump & rods, Space out & seat pump, RU unit, PWOP @ 15:00 - M.U. TEST & RIH w/ PUMP #NFJ342 (2 1/2" x 1 3/4" x 24' RHAC w/ 4' SM GROOVED PLUNGER), 5 - 1 1/2" WT BARS w/ STABILIZERS, 20 - 3/4" 4per (New) 136 - 3/4" 4per (OLD) 50 - 7/8" 4per (Old) TONGS BROKE DOWN - TONGS BROKE DOWN, FIX TONGS - FLUSHED CSG w/ 60 BW @ 250 DEG WHILE RIGGING UP, BRAKES ON UNIT WOULD NOT HOLD, HAD TO BRIDAL HORSE HEAD TO REMOVE, UNSEAT PUMP, L.D. POLISH ROD, POOH w/ 3 - 7/8" 4per, FLUSH TBG w/ 40 BW @ 250 DEG, SOFT SEAT PUMP, FILL w/ BW, PT TBG TO 3000# - S.I.R.U.S.U. STRETCH LINES - Travel time / JSP MEETING - RIH w/ RODS - DROP LINES R.D. WRAP LINES - FILL TBG w/ 19 BW, ST w/ RIG TO 800#, GOOD, UNIT WOULDN'T ROLL, BRIDAL HEAD, HANG HEAD, ADJUST TAG, ROLL UNIT, GOOD PUMP ACTION, PWOP @ 15:00 - CONT RIH w/ 25 - 7/8" GUIDED 4per (OLD) 8 - 7/8" GUIDED 4 per (New) 1 1/2" x 30' POLISHED ROD, SPACE OUT, SEAT PUMP - FIXED ROD BASKET LIGHT **Finalized**

Daily Cost: \$63,700
Cumulative Cost: \$214,457

Pertinent Files: Go to File List
