

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 3

AMENDED REPORT

APPLICATION FOR PERMIT TO DRILL						1. WELL NAME and NUMBER GMBU T-5-9-17				
2. TYPE OF WORK DRILL NEW WELL <input checked="" type="checkbox"/> REENTER P&A WELL <input type="checkbox"/> DEEPEN WELL <input type="checkbox"/>						3. FIELD OR WILDCAT MONUMENT BUTTE				
4. TYPE OF WELL Oil Well Coalbed Methane Well: NO						5. UNIT or COMMUNITIZATION AGREEMENT NAME GMBU (GRRV)				
6. NAME OF OPERATOR NEWFIELD PRODUCTION COMPANY						7. OPERATOR PHONE 435 646-4825				
8. ADDRESS OF OPERATOR Rt 3 Box 3630 , Myton, UT, 84052						9. OPERATOR E-MAIL mcrozier@newfield.com				
10. MINERAL LEASE NUMBER (FEDERAL, INDIAN, OR STATE) UTU-75038			11. MINERAL OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>			12. SURFACE OWNERSHIP FEDERAL <input checked="" type="checkbox"/> INDIAN <input type="checkbox"/> STATE <input type="checkbox"/> FEE <input type="checkbox"/>				
13. NAME OF SURFACE OWNER (if box 12 = 'fee')						14. SURFACE OWNER PHONE (if box 12 = 'fee')				
15. ADDRESS OF SURFACE OWNER (if box 12 = 'fee')						16. SURFACE OWNER E-MAIL (if box 12 = 'fee')				
17. INDIAN ALLOTTEE OR TRIBE NAME (if box 12 = 'INDIAN')			18. INTEND TO COMMINGLE PRODUCTION FROM MULTIPLE FORMATIONS YES <input type="checkbox"/> (Submit Commingling Application) NO <input checked="" type="checkbox"/>			19. SLANT VERTICAL <input type="checkbox"/> DIRECTIONAL <input checked="" type="checkbox"/> HORIZONTAL <input type="checkbox"/>				
20. LOCATION OF WELL		FOOTAGES		QTR-QTR	SECTION	TOWNSHIP	RANGE	MERIDIAN		
LOCATION AT SURFACE		1936 FSL 500 FWL		NWSW	4	9.0 S	17.0 E	S		
Top of Uppermost Producing Zone		1576 FSL 95 FWL		NWSW	4	9.0 S	17.0 E	S		
At Total Depth		1282 FSL 261 FEL		SESE	5	9.0 S	17.0 E	S		
21. COUNTY DUCHESNE			22. DISTANCE TO NEAREST LEASE LINE (Feet) 38			23. NUMBER OF ACRES IN DRILLING UNIT 20				
27. ELEVATION - GROUND LEVEL 5224			25. DISTANCE TO NEAREST WELL IN SAME POOL (Applied For Drilling or Completed) 1191			26. PROPOSED DEPTH MD: 6024 TVD: 5925				
28. BOND NUMBER WYB000493			29. SOURCE OF DRILLING WATER / WATER RIGHTS APPROVAL NUMBER IF APPLICABLE 437478							
Hole, Casing, and Cement Information										
String	Hole Size	Casing Size	Length	Weight	Grade & Thread	Max Mud Wt.	Cement	Sacks	Yield	Weight
SURF	12.25	8.625	0 - 300	24.0	J-55 ST&C	8.3	Class G	138	1.17	15.8
PROD	7.875	5.5	0 - 6024	15.5	J-55 LT&C	8.3	Premium Lite High Strength	278	3.26	11.0
							50/50 Poz	363	1.24	14.3
ATTACHMENTS										
VERIFY THE FOLLOWING ARE ATTACHED IN ACCORDANCE WITH THE UTAH OIL AND GAS CONSERVATION GENERAL RULES										
<input checked="" type="checkbox"/> WELL PLAT OR MAP PREPARED BY LICENSED SURVEYOR OR ENGINEER					<input checked="" type="checkbox"/> COMPLETE DRILLING PLAN					
<input type="checkbox"/> AFFIDAVIT OF STATUS OF SURFACE OWNER AGREEMENT (IF FEE SURFACE)					<input type="checkbox"/> FORM 5. IF OPERATOR IS OTHER THAN THE LEASE OWNER					
<input checked="" type="checkbox"/> DIRECTIONAL SURVEY PLAN (IF DIRECTIONALLY OR HORIZONTALLY DRILLED)					<input checked="" type="checkbox"/> TOPOGRAPHICAL MAP					
NAME Mandie Crozier				TITLE Regulatory Tech			PHONE 435 646-4825			
SIGNATURE				DATE 06/05/2012			EMAIL mcrozier@newfield.com			
API NUMBER ASSIGNED 43013514800000				APPROVAL  Permit Manager						

NEWFIELD PRODUCTION COMPANY
 GMBU T-5-9-17
 AT SURFACE: NW/SW SECTION 4, T9S R17E
 DUCHESNE COUNTY, UTAH

TEN POINT DRILLING PROGRAM

1. **GEOLOGIC SURFACE FORMATION:**

Uinta formation of Upper Eocene Age

2. **ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:**

Uinta	0' – 1425'
Green River	1425'
Wasatch	6135'
Proposed TD	6024'

3. **ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:**

Green River Formation (Oil)	1425' – 6135'
-----------------------------	---------------

Fresh water may be encountered in the Uinta Formation, but would not be expected below about 350'. All water shows and water bearing geologic units shall be reported to the geologic and engineering staff of the Vernal Office prior to running the next string of casing or before plugging orders are requested. All water shows must be reported within one (1) business day after being encountered.

All usable (<10,000 PPM TDS) water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling will be recorded by depth and adequately protected. This information shall be reported to the Vernal Office.

Detected water flows shall be sampled, analyzed, and reported to the geologic & engineering staff of the Vernal Office. The office may request additional water samples for further analysis. Usage of the State of Utah form *Report of Water Encountered* is acceptable, but not required.

The following information is requested for water shows and samples where applicable:

Location & Sampled Interval	Date Sampled
Flow Rate	Temperature
Hardness	pH
Water Classification (State of Utah)	Dissolved Calcium (Ca) (mg/l)
Dissolved Iron (Fe) (ug/l)	Dissolved Sodium (Na) (mg/l)
Dissolved Magnesium (Mg) (mg/l)	Dissolved Carbonate (CO ₃) (mg/l)
Dissolved Bicarbonate (NaHCO ₃) (mg/l)	Dissolved Chloride (Cl) (mg/l)
Dissolved Sulfate (SO ₄) (mg/l)	Dissolved Total Solids (TDS) (mg/l)

4. **PROPOSED CASING PROGRAM**

a. **Casing Design: GMBU T-5-9-17**

Size	Interval		Weight	Grade	Coupling	Design Factors		
	Top	Bottom				Burst	Collapse	Tension
Surface casing 8-5/8"	0'	300'	24.0	J-55	STC	2,950 17.53	1,370 14.35	244,000 33.89
Prod casing 5-1/2"	0'	6,024'	15.5	J-55	LTC	4,810 2.51	4,040 2.11	217,000 2.32

Assumptions:

- 1) Surface casing max anticipated surface press (MASP) = Frac gradient – gas gradient
- 2) Prod casing MASP (production mode) = Pore pressure – gas gradient
- 3) All collapse calculations assume fully evacuated casing w/ gas gradient
- 4) All tension calculations assume air weight

Frac gradient at surface casing shoe =	13.0 ppg
Pore pressure at surface casing shoe =	8.33 ppg
Pore pressure at prod casing shoe =	8.33 ppg
Gas gradient =	0.115 psi/ft

All casing shall be new or, if used, inspected and tested. Used casing shall meet or exceed API standards for new casing.

All casing strings shall have a minimum of 1 (one) centralizer on each of the bottom three (3) joints.

b. **Cementing Design: GMBU T-5-9-17**

Job	Fill	Description	Sacks	OH Excess*	Weight (ppg)	Yield (ft ³ /sk)
			ft ³			
Surface casing	300'	Class G w/ 2% CaCl	138	30%	15.8	1.17
			161			
Prod casing Lead	4,024'	Prem Lite II w/ 10% gel + 3% KCl	278	30%	11.0	3.26
			906			
Prod casing Tail	2,000'	50/50 Poz w/ 2% gel + 3% KCl	363	30%	14.3	1.24
			451			

*Actual volume pumped will be 15% over the caliper log

- Compressive strength of lead cement: 1800 psi @ 24 hours, 2250 psi @ 72 hours

- Compressive strength of tail cement: 2500 psi @ 24 hours

Hole Sizes: A 12-1/4" hole will be drilled for the 8-5/8" surface casing. A 7-7/8" hole will be drilled for the 5-1/2" production casing.

The 8-5/8" surface casing shall in all cases be cemented back to surface. In the event that during the primary surface cementing operation the cement does not circulate to surface, or if the cement level should fall back more than 8 feet from surface, then a remedial surface cementing operation shall be performed to insure adequate isolation and stabilization of the surface casing.

5. **MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:**

The operator's minimum specifications for pressure control equipment are as follows:

An 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOP's will be check daily.

Refer to **Exhibit C** for a diagram of BOP equipment that will be used on this well.

6. **TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:**

From surface to ± 300 feet will be drilled with an air/mist system. The air rig is equipped with a 6 1/2" blooie line that is straight run and securely anchored. The blooie line is used with a discharge less than 100 ft from the wellbore in order to minimize the well pad size. The blooie line is not equipped with an automatic igniter or continuous pilot light and the compressor is located less than 100 ft from the well bore due to the low possibility of combustion with the air dust mixture. The trailer mounted compressor (capacity of 2000 CFM) has a safety shut-off valve which is located 15 feet from the air rig. A truck with 70 bbls of water is on stand by to be used as kill fluid, if necessary. From about ± 300 feet to TD, a fresh water system will be utilized. Clay inhibition and hole stability will be achieved with a KCl substitute additive. This additive will be identified in the APD and reviewed to determine if the reserve pit shall be lined. This fresh water system will typically contain Total Dissolved Solids (TDS) of less than 3000 PPM. Anticipated mud weight is 8.4 lbs/gal. If necessary to control formation fluids or pressure, the system will be weighted with the addition of bentonite gel, and if pressure conditions warrant, with barite

No chromate additives will be used in the mud system on Federal and/or Indian lands without prior BLM approval to ensure adequate protection of fresh aquifers.

No chemicals subject to reporting under SARA Title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling, testing, or completing of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling, testing, or completing of this well.

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

Newfield Production will **visually** monitor pit levels and flow from the well during drilling operations.

7. **AUXILIARY SAFETY EQUIPMENT TO BE USED:**

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. **TESTING, LOGGING AND CORING PROGRAMS:**

The logging program will consist of a Dual Induction, Gamma Ray and Caliper log from TD to base of surface casing @ 300' +/-, and a Compensated Neutron-Formation Density Log from TD to 3500' +/- . A cement bond log will be run from PBTD to cement top. No drill stem testing or coring is planned for this well.

9. **ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:**

No abnormal temperatures or pressures are anticipated. No hydrogen sulfide has been encountered or is known to exist from previous drilling in the area at this depth. Maximum anticipated

bottomhole pressure will approximately equal total depth in feet multiplied by a 0.433 psi/foot gradient.



10. **ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:**

It is anticipated that the drilling operations will commence the third quarter of 2012, and take approximately seven (7) days from spud to rig release.

T9S, R17E, S.L.B.&M.

NEWFIELD EXPLORATION COMPANY


WELL LOCATION, T-5-9-17, LOCATED AS SHOWN IN THE NW 1/4 SW 1/4 OF SECTION 4, T9S, R17E, S.L.B.&M. DUCHESNE COUNTY, UTAH.

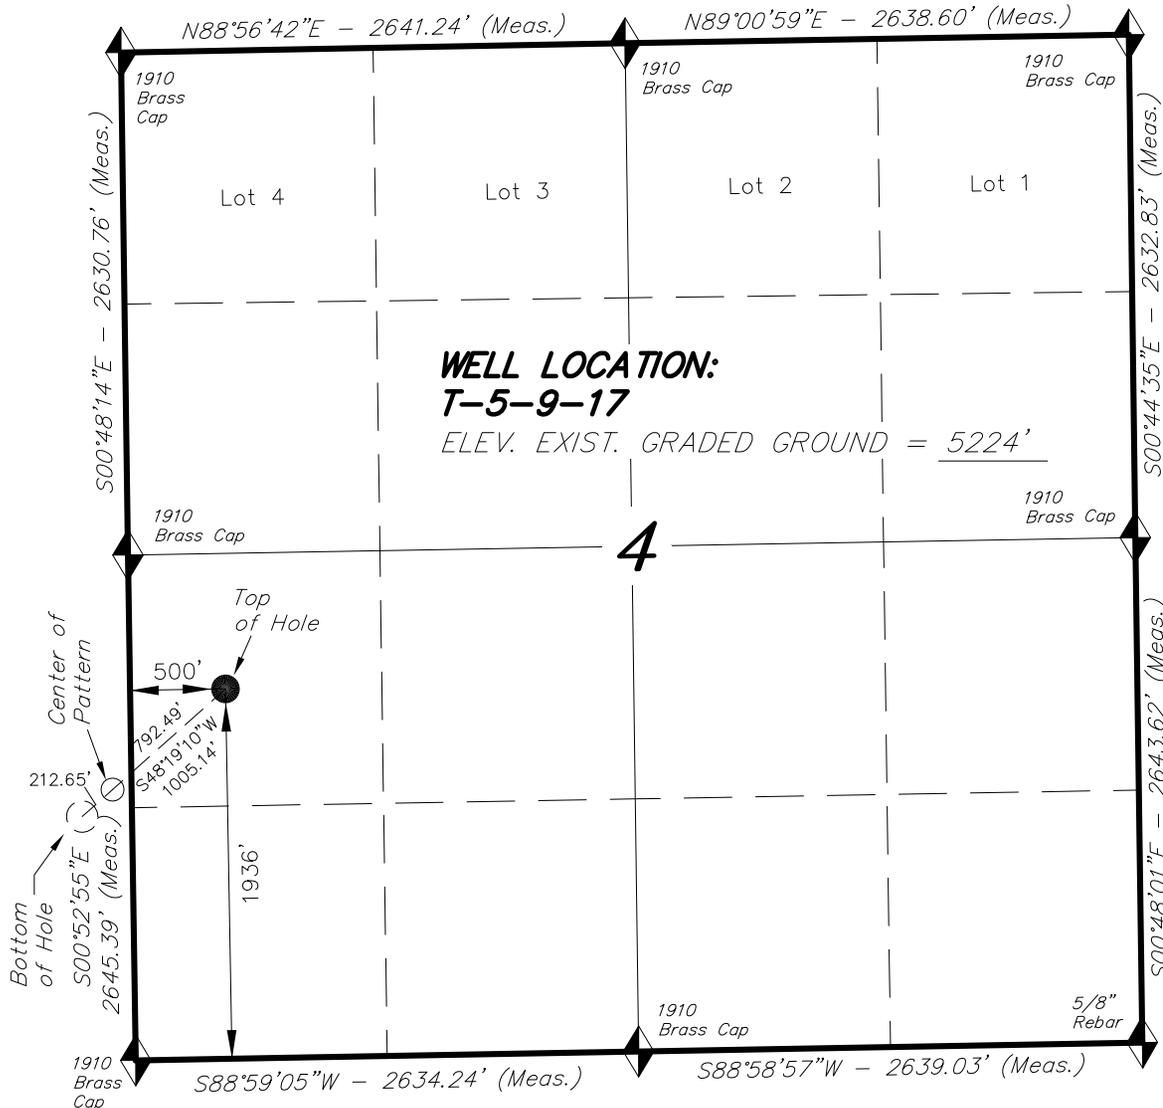

NOTES:

1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.



◆ = SECTION CORNERS LOCATED

BASIS OF ELEV; Elevations are based on an N.G.S. OPUS Correction. LOCATION: LAT. $40^{\circ}04'09.56''$ LONG. $110^{\circ}00'43.28''$ (Tristate Aluminum Cap) Elev. 5281.57'

T-5-9-17
 (Surface Location) NAD 83
 LATITUDE = $40^{\circ}03'28.82''$
 LONGITUDE = $110^{\circ}01'09.20''$


TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
 (435) 781-2501


DATE SURVEYED: 01-28-12	SURVEYED BY: S.H.	VERSION:
DATE DRAWN: 05-01-12	DRAWN BY: F.T.M.	V3
REVISED: 05-14-12 F.T.M.	SCALE: 1" = 1000'	

T9S, R17E, S.L.B.&M.

NEWFIELD EXPLORATION COMPANY

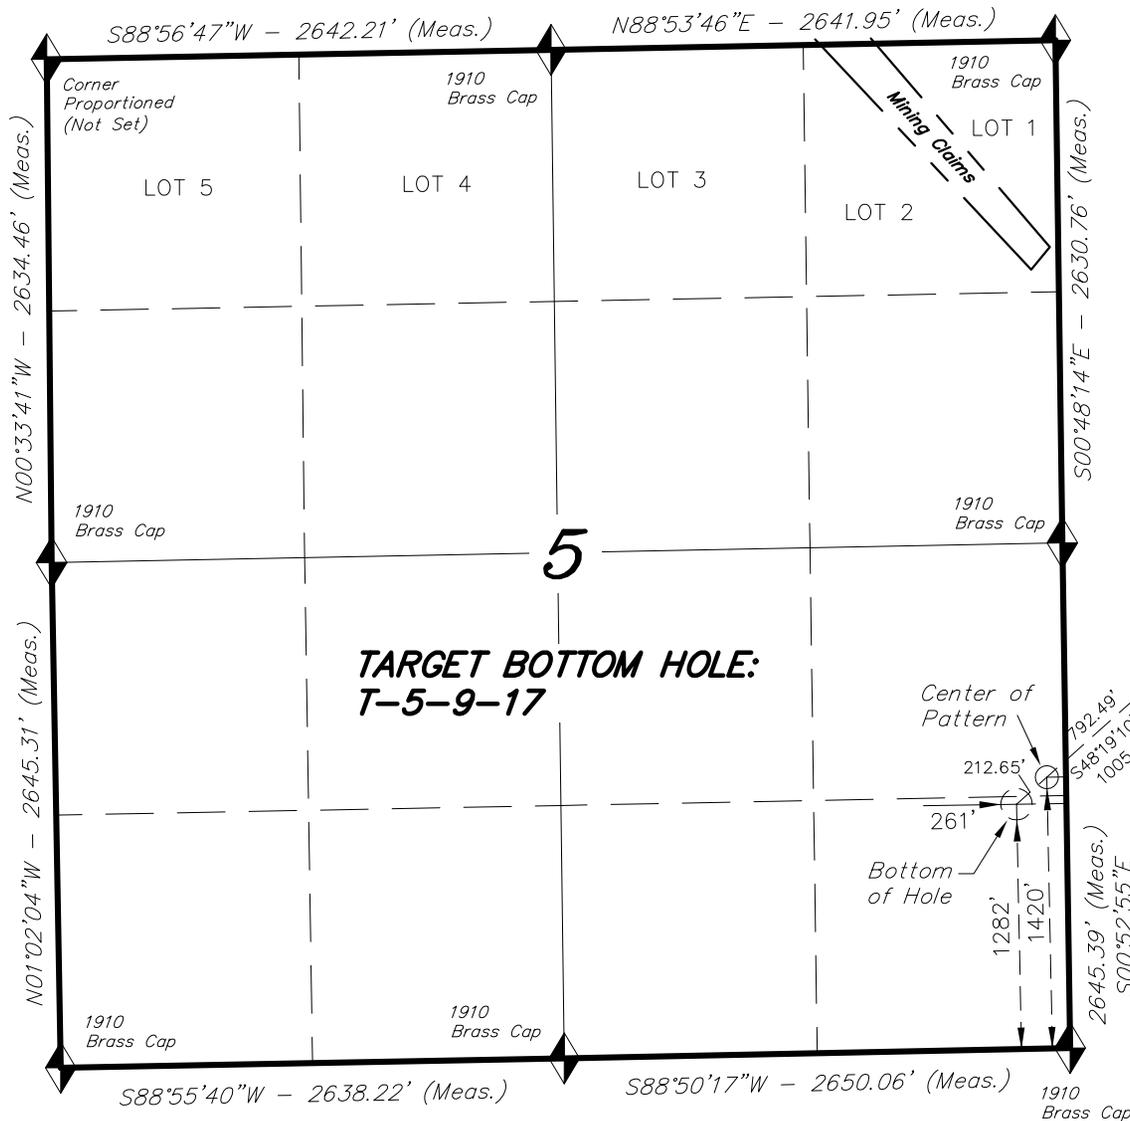

TARGET BOTTOM HOLE, T-5-9-17, LOCATED AS SHOWN IN THE SE 1/4 SE 1/4 OF SECTION 5, T9S, R17E, S.L.B.&M. DUCHESNE COUNTY, UTAH.



NOTES:

1. Well footages are measured at right angles to the Section Lines.
2. Bearings are based on Global Positioning Satellite observations.
3. The Center of Pattern footages are 1420' FSL & 100' FEL.

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.



BASIS OF ELEV; Elevations are based on an N.G.S. OPUS Correction. LOCATION: LAT. $40^{\circ}04'09.56''$ LONG. $110^{\circ}00'43.28''$ (Tristate Aluminum Cap) Elev. 5281.57'


◆ = SECTION CORNERS LOCATED

TRI STATE LAND SURVEYING & CONSULTING

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078
 (435) 781-2501

DATE SURVEYED: 07-06-11	SURVEYED BY: S.H.	VERSION:
DATE DRAWN: 05-01-12	DRAWN BY: F.T.M.	V3
REVISED: 05-14-12 F.T.M.	SCALE: 1" = 1000'	

Access Road Map

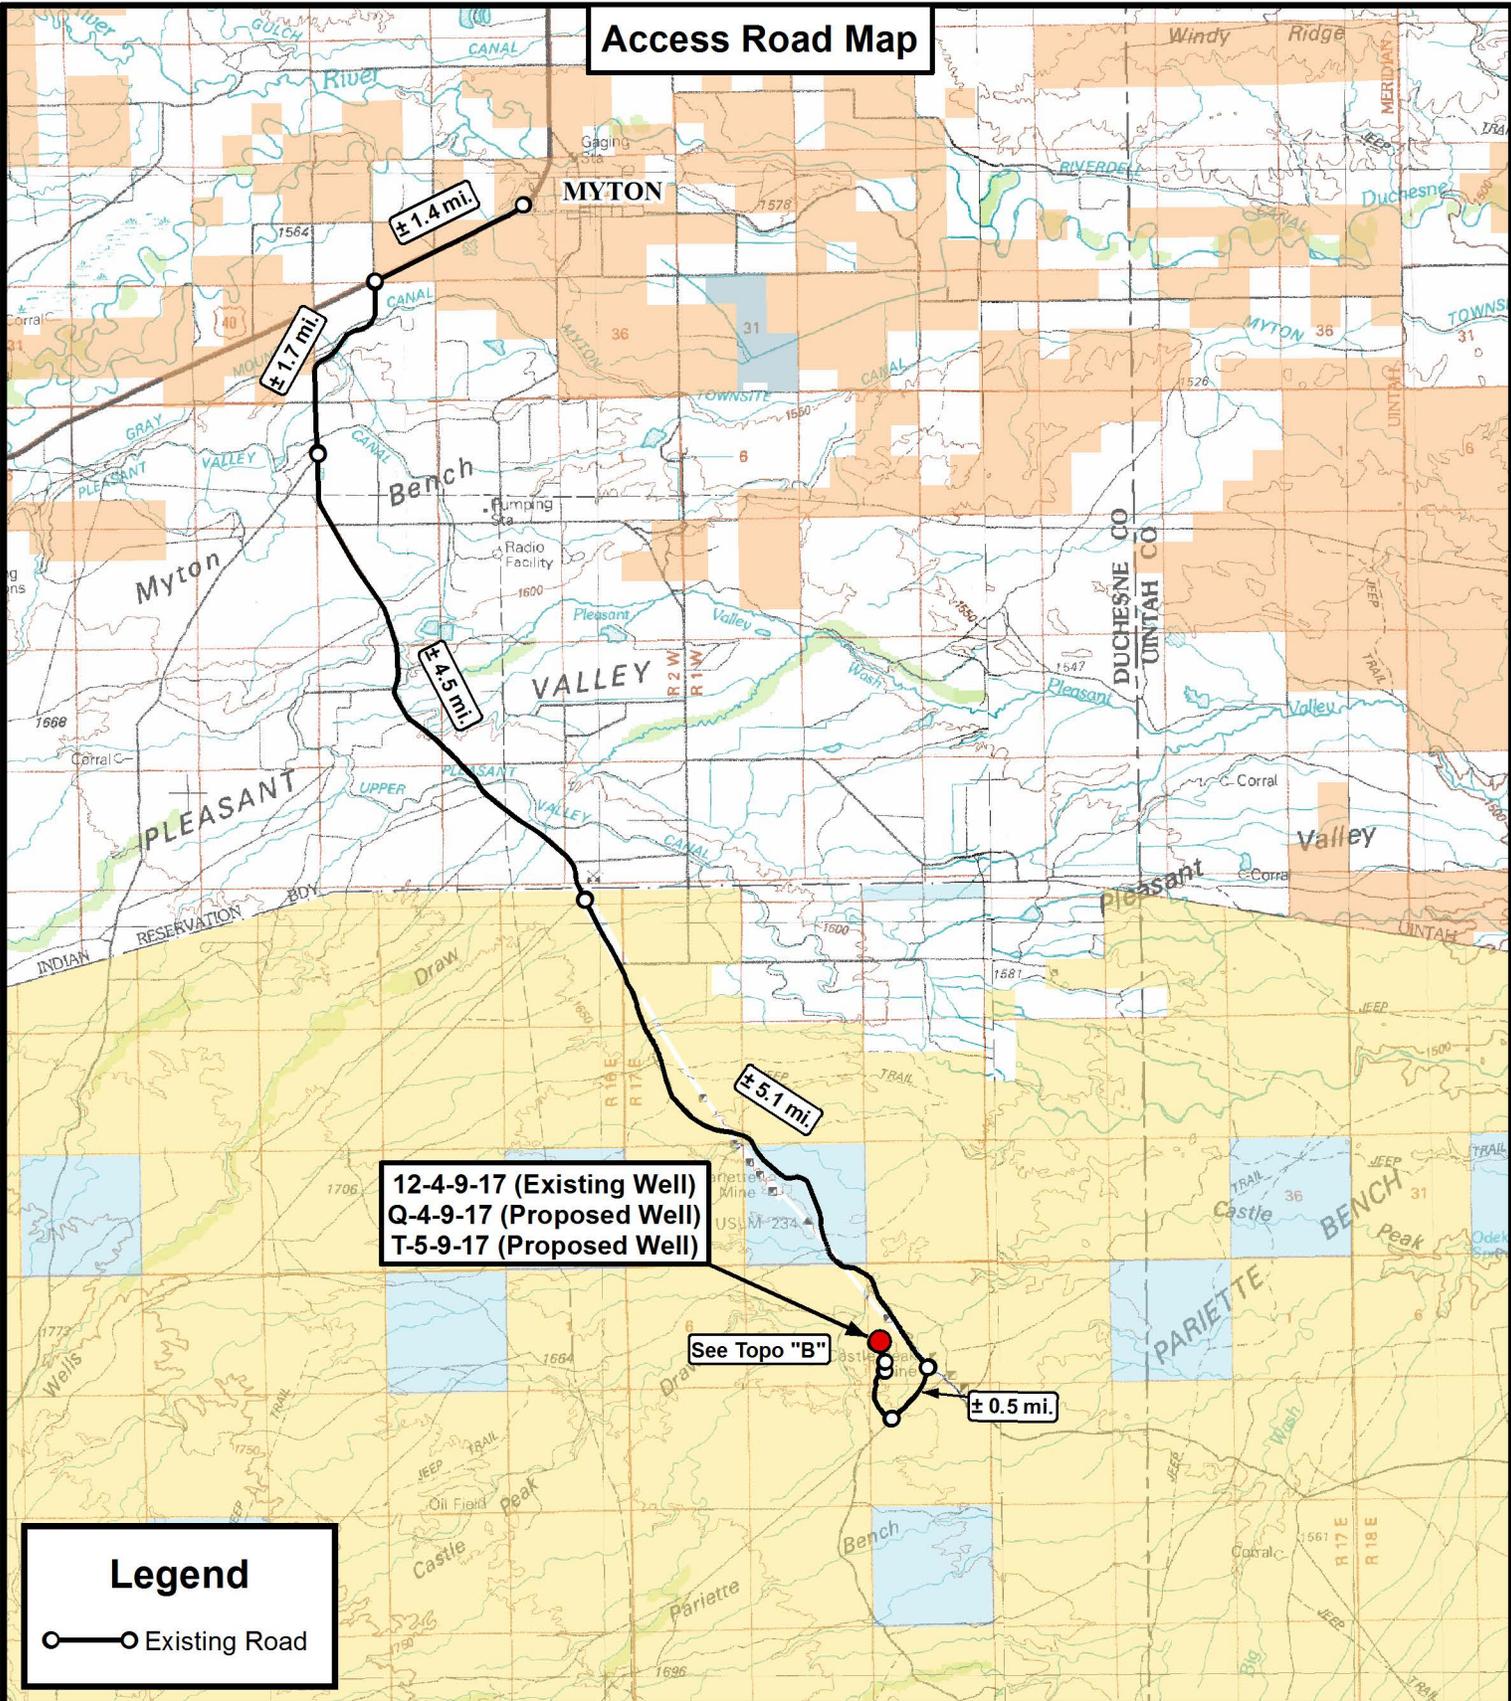

12-4-9-17 (Existing Well)
 Q-4-9-17 (Proposed Well)
 T-5-9-17 (Proposed Well)

See Topo "B"

Legend

○—○ Existing Road



**Tri State
 Land Surveying, Inc.**
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

12-4-9-17 (Existing Well)
 Q-4-9-17 (Proposed Well)
 T-5-9-17 (Proposed Well)
 SEC. 4, T9S, R17E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	A.P.C.	REVISED:	05-14-12 D.C.R.	VERSION:
DATE:	05-01-2012			V3
SCALE:	1:100,000			

TOPOGRAPHIC MAP

SHEET **A**

Proposed Pipeline Map

12-4-9-17 (Existing Well)
 Q-4-9-17 (Proposed Well)
 T-5-9-17 (Proposed Well)

Existing Waterline

Flowline Previously Proposed

± 2,119'

± 1,874'

Tie in at Existing Gas Pipeline

Legend

- Existing Road
- Proposed Gas Pipeline

Total Pipeline Distances	
Proposed Gas Pipeline	± 3,993'

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



Tri State Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

12-4-9-17 (Existing Well)
 Q-4-9-17 (Proposed Well)
 T-5-9-17 (Proposed Well)

SEC. 4, T9S, R17E, S.L.B.&M. Duchesne County, UT.


DRAWN BY:	D.C.R.	REVISED:	05-14-12 D.C.R.	VERSION:	
DATE:	02-03-2012			V3	
SCALE:	1" = 2,000'				

TOPOGRAPHIC MAP

SHEET **C**

Exhibit "B" Map

12-4-9-17 (Existing Well)
 Q-4-9-17 (Proposed Well)
 T-5-9-17 (Proposed Well)

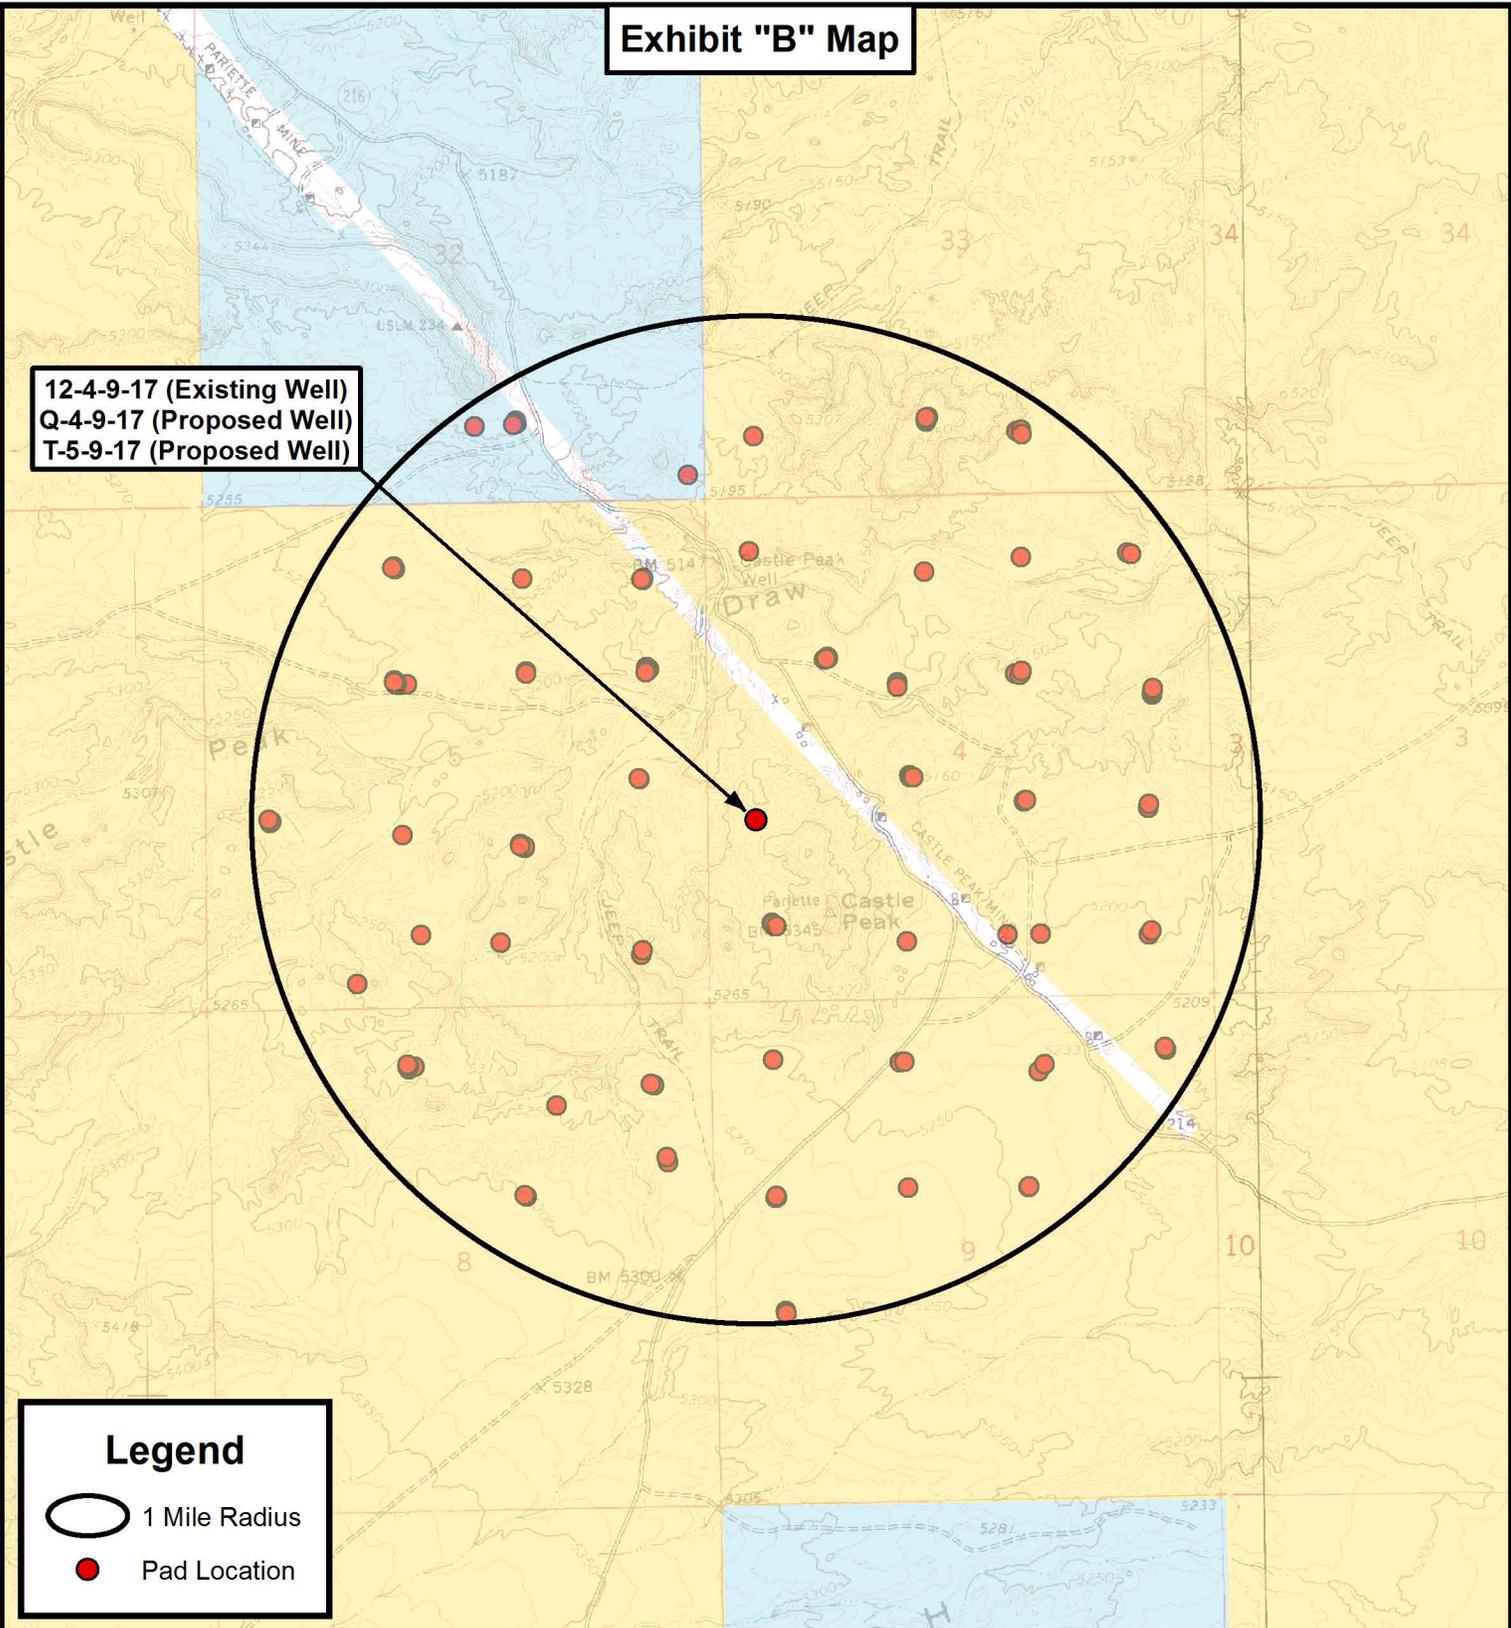

Legend

-  1 Mile Radius
-  Pad Location

THE PARCEL INFORMATION SHOWN HAS NOT BEEN SURVEYED BY TRI-STATE LAND SURVEYING, INC. - TRI-STATE DOES NOT WARRANTY PROPERTY PARCEL DATA OR ANY ASSOCIATED INFORMATION. A PROPERTY SURVEY IS REQUIRED TO DETERMINE THE ACTUAL LOCATION OF PROPERTY LINES AND SHOW ACCURATE DISTANCES ACROSS PARCELS.



**Tri State
Land Surveying, Inc.**
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

P: (435) 781-2501
 F: (435) 781-2518



NEWFIELD EXPLORATION COMPANY

12-4-9-17 (Existing Well)
 Q-4-9-17 (Proposed Well)
 T-5-9-17 (Proposed Well)

SEC. 4, T9S, R17E, S.L.B.&M. Duchesne County, UT.

DRAWN BY:	A.P.C.	REVISED:	05-14-12 D.C.R.	VERSION:
DATE:	05-01-2012			V3
SCALE:	1" = 2,000'			

TOPOGRAPHIC MAP

SHEET **D**



NEWFIELD EXPLORATION

**USGS Myton SW (UT)
SECTION 4 T9S R17E
T-5-9-17**

Wellbore #1

Plan: Design #1

Standard Planning Report

30 April, 2012





Payzone Directional
Planning Report



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well T-5-9-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	T-5-9-17 @ 5237.0ft (Original Well Elev)
Project:	USGS Myton SW (UT)	MD Reference:	T-5-9-17 @ 5237.0ft (Original Well Elev)
Site:	SECTION 4 T9S R17E	North Reference:	True
Well:	T-5-9-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Project	USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Utah Central Zone		

Site	SECTION 4 T9S R17E				
Site Position:		Northing:	7,194,100.00 ft	Latitude:	40° 3' 36.542 N
From:	Lat/Long	Easting:	2,057,000.00 ft	Longitude:	110° 0' 41.593 W
Position Uncertainty:	0.0 ft	Slot Radius:	"	Grid Convergence:	0.95 °

Well	T-5-9-17, SHL LAT: 40 03 28.42 LONG: -110 01 09.36					
Well Position	+N/-S	-821.9 ft	Northing:	7,193,242.46 ft	Latitude:	40° 3' 28.420 N
	+E/-W	-2,158.8 ft	Easting:	2,054,855.07 ft	Longitude:	110° 1' 9.360 W
Position Uncertainty		0.0 ft	Wellhead Elevation:	5,237.0 ft	Ground Level:	5,225.0 ft

Wellbore	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010	4/30/2012	11.19	65.79	52,199

Design	Design #1			
Audit Notes:				
Version:	Phase:	PROTOTYPE	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (ft)	+N/-S (ft)	+E/-W (ft)	Direction (°)
	0.0	0.0	0.0	228.32

Plan Sections										
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)	TFO (°)	Target
0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.00	0.00	
600.0	0.00	0.00	600.0	0.0	0.0	0.00	0.00	0.00	0.00	
1,366.6	11.50	228.32	1,361.5	-51.0	-57.3	1.50	1.50	0.00	228.32	
4,957.2	11.50	228.32	4,880.0	-527.0	-591.9	0.00	0.00	0.00	0.00	T-5-9-17 TGT
6,023.6	11.50	228.32	5,925.0	-668.4	-750.7	0.00	0.00	0.00	0.00	



Payzone Directional
Planning Report



Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well T-5-9-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	T-5-9-17 @ 5237.0ft (Original Well Elev)
Project:	USGS Myton SW (UT)	MD Reference:	T-5-9-17 @ 5237.0ft (Original Well Elev)
Site:	SECTION 4 T9S R17E	North Reference:	True
Well:	T-5-9-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
100.0	0.00	0.00	100.0	0.0	0.0	0.0	0.00	0.00	0.00
200.0	0.00	0.00	200.0	0.0	0.0	0.0	0.00	0.00	0.00
300.0	0.00	0.00	300.0	0.0	0.0	0.0	0.00	0.00	0.00
400.0	0.00	0.00	400.0	0.0	0.0	0.0	0.00	0.00	0.00
500.0	0.00	0.00	500.0	0.0	0.0	0.0	0.00	0.00	0.00
600.0	0.00	0.00	600.0	0.0	0.0	0.0	0.00	0.00	0.00
700.0	1.50	228.32	700.0	-0.9	-1.0	1.3	1.50	1.50	0.00
800.0	3.00	228.32	799.9	-3.5	-3.9	5.2	1.50	1.50	0.00
900.0	4.50	228.32	899.7	-7.8	-8.8	11.8	1.50	1.50	0.00
1,000.0	6.00	228.32	999.3	-13.9	-15.6	20.9	1.50	1.50	0.00
1,100.0	7.50	228.32	1,098.6	-21.7	-24.4	32.7	1.50	1.50	0.00
1,200.0	9.00	228.32	1,197.5	-31.3	-35.1	47.0	1.50	1.50	0.00
1,300.0	10.50	228.32	1,296.1	-42.5	-47.8	64.0	1.50	1.50	0.00
1,366.6	11.50	228.32	1,361.5	-51.0	-57.3	76.7	1.50	1.50	0.00
1,400.0	11.50	228.32	1,394.2	-55.4	-62.2	83.3	0.00	0.00	0.00
1,500.0	11.50	228.32	1,492.2	-68.7	-77.1	103.3	0.00	0.00	0.00
1,600.0	11.50	228.32	1,590.2	-81.9	-92.0	123.2	0.00	0.00	0.00
1,700.0	11.50	228.32	1,688.2	-95.2	-106.9	143.1	0.00	0.00	0.00
1,800.0	11.50	228.32	1,786.2	-108.4	-121.8	163.1	0.00	0.00	0.00
1,900.0	11.50	228.32	1,884.2	-121.7	-136.7	183.0	0.00	0.00	0.00
2,000.0	11.50	228.32	1,982.1	-135.0	-151.6	202.9	0.00	0.00	0.00
2,100.0	11.50	228.32	2,080.1	-148.2	-166.5	222.9	0.00	0.00	0.00
2,200.0	11.50	228.32	2,178.1	-161.5	-181.4	242.8	0.00	0.00	0.00
2,300.0	11.50	228.32	2,276.1	-174.7	-196.2	262.8	0.00	0.00	0.00
2,400.0	11.50	228.32	2,374.1	-188.0	-211.1	282.7	0.00	0.00	0.00
2,500.0	11.50	228.32	2,472.1	-201.2	-226.0	302.6	0.00	0.00	0.00
2,600.0	11.50	228.32	2,570.1	-214.5	-240.9	322.6	0.00	0.00	0.00
2,700.0	11.50	228.32	2,668.1	-227.7	-255.8	342.5	0.00	0.00	0.00
2,800.0	11.50	228.32	2,766.1	-241.0	-270.7	362.4	0.00	0.00	0.00
2,900.0	11.50	228.32	2,864.1	-254.3	-285.6	382.4	0.00	0.00	0.00
3,000.0	11.50	228.32	2,962.1	-267.5	-300.5	402.3	0.00	0.00	0.00
3,100.0	11.50	228.32	3,060.1	-280.8	-315.4	422.2	0.00	0.00	0.00
3,200.0	11.50	228.32	3,158.1	-294.0	-330.2	442.2	0.00	0.00	0.00
3,300.0	11.50	228.32	3,256.1	-307.3	-345.1	462.1	0.00	0.00	0.00
3,400.0	11.50	228.32	3,354.0	-320.5	-360.0	482.0	0.00	0.00	0.00
3,500.0	11.50	228.32	3,452.0	-333.8	-374.9	502.0	0.00	0.00	0.00
3,600.0	11.50	228.32	3,550.0	-347.1	-389.8	521.9	0.00	0.00	0.00
3,700.0	11.50	228.32	3,648.0	-360.3	-404.7	541.9	0.00	0.00	0.00
3,800.0	11.50	228.32	3,746.0	-373.6	-419.6	561.8	0.00	0.00	0.00
3,900.0	11.50	228.32	3,844.0	-386.8	-434.5	581.7	0.00	0.00	0.00
4,000.0	11.50	228.32	3,942.0	-400.1	-449.4	601.7	0.00	0.00	0.00
4,100.0	11.50	228.32	4,040.0	-413.3	-464.3	621.6	0.00	0.00	0.00
4,200.0	11.50	228.32	4,138.0	-426.6	-479.1	641.5	0.00	0.00	0.00
4,300.0	11.50	228.32	4,236.0	-439.9	-494.0	661.5	0.00	0.00	0.00
4,400.0	11.50	228.32	4,334.0	-453.1	-508.9	681.4	0.00	0.00	0.00
4,500.0	11.50	228.32	4,432.0	-466.4	-523.8	701.3	0.00	0.00	0.00
4,600.0	11.50	228.32	4,530.0	-479.6	-538.7	721.3	0.00	0.00	0.00
4,700.0	11.50	228.32	4,628.0	-492.9	-553.6	741.2	0.00	0.00	0.00
4,800.0	11.50	228.32	4,725.9	-506.1	-568.5	761.1	0.00	0.00	0.00
4,900.0	11.50	228.32	4,823.9	-519.4	-583.4	781.1	0.00	0.00	0.00
4,957.2	11.50	228.32	4,880.0	-527.0	-591.9	792.5	0.00	0.00	0.00
5,000.0	11.50	228.32	4,921.9	-532.7	-598.3	801.0	0.00	0.00	0.00
5,100.0	11.50	228.32	5,019.9	-545.9	-613.1	821.0	0.00	0.00	0.00



Payzone Directional Planning Report




Database:	EDM 2003.21 Single User Db	Local Co-ordinate Reference:	Well T-5-9-17
Company:	NEWFIELD EXPLORATION	TVD Reference:	T-5-9-17 @ 5237.0ft (Original Well Elev)
Project:	USGS Myton SW (UT)	MD Reference:	T-5-9-17 @ 5237.0ft (Original Well Elev)
Site:	SECTION 4 T9S R17E	North Reference:	True
Well:	T-5-9-17	Survey Calculation Method:	Minimum Curvature
Wellbore:	Wellbore #1		
Design:	Design #1		

Planned Survey									
Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
5,200.0	11.50	228.32	5,117.9	-559.2	-628.0	840.9	0.00	0.00	0.00
5,300.0	11.50	228.32	5,215.9	-572.4	-642.9	860.8	0.00	0.00	0.00
5,400.0	11.50	228.32	5,313.9	-585.7	-657.8	880.8	0.00	0.00	0.00
5,500.0	11.50	228.32	5,411.9	-598.9	-672.7	900.7	0.00	0.00	0.00
5,600.0	11.50	228.32	5,509.9	-612.2	-687.6	920.6	0.00	0.00	0.00
5,700.0	11.50	228.32	5,607.9	-625.5	-702.5	940.6	0.00	0.00	0.00
5,800.0	11.50	228.32	5,705.9	-638.7	-717.4	960.5	0.00	0.00	0.00
5,900.0	11.50	228.32	5,803.9	-652.0	-732.3	980.4	0.00	0.00	0.00
6,000.0	11.50	228.32	5,901.9	-665.2	-747.2	1,000.4	0.00	0.00	0.00
6,023.6	11.50	228.32	5,925.0	-668.4	-750.7	1,005.1	0.00	0.00	0.00





Project: USGS Myton SW (UT)
 Site: SECTION 4 T9S R17E
 Well: T-5-9-17
 Wellbore: Wellbore #1
 Design: Design #1



Azimuths to True North
 Magnetic North: 11.19°

Magnetic Field
 Strength: 52199.2snT
 Dip Angle: 65.79°
 Date: 4/30/2012
 Model: IGRF2010

KOP @ 600'
 DOGLEG RATE 1.5 DEG/100
 TARGET RADIUS IS 75'

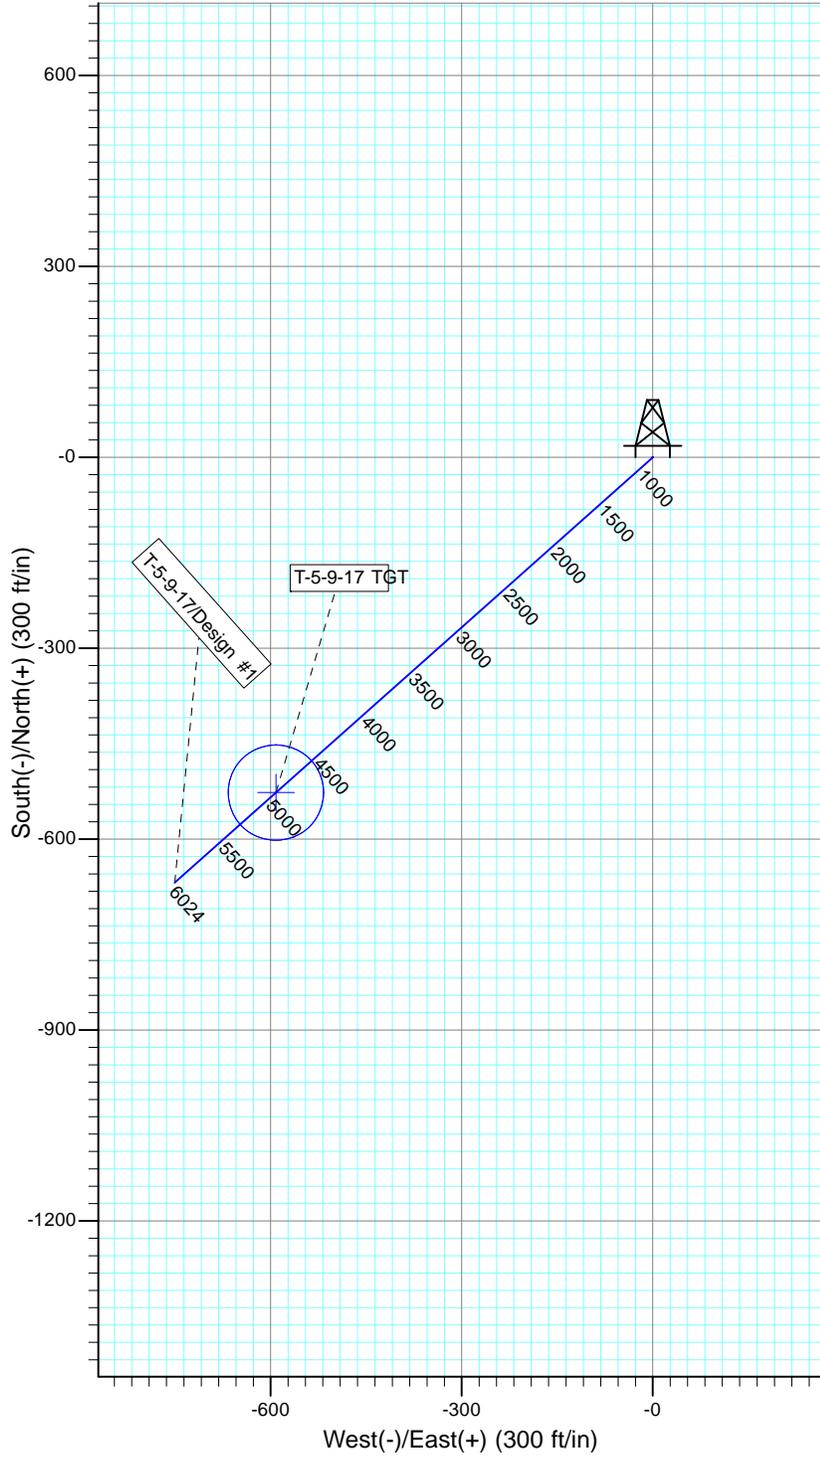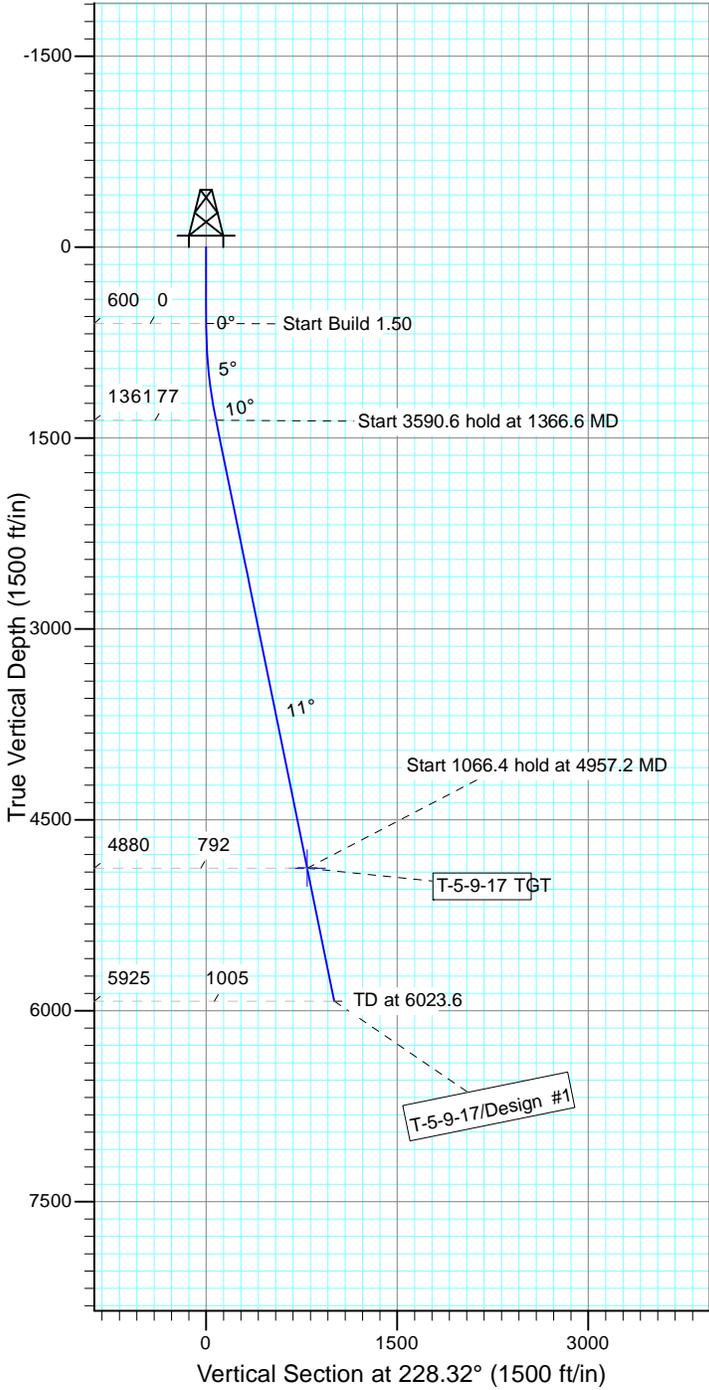

WELLBORE TARGET DETAILS

Name	TVD	+N/-S	+E/-W	Shape
T-5-9-17 TGT	4880.0	-527.0	-591.9	Circle (Radius: 75.0)

SECTION DETAILS

Sec	MD	Inc	Azi	TVD	+N/-S	+E/-W	DLeg	TFace	VSec	Target
1	0.0	0.00	0.00	0.0	0.0	0.0	0.00	0.00	0.0	
2	600.0	0.00	0.00	600.0	0.0	0.0	0.00	0.00	0.0	
3	1366.6	11.50	228.32	1361.5	-51.0	-57.3	1.50	228.32	76.7	
4	4957.2	11.50	228.32	4880.0	-527.0	-591.9	0.00	0.00	792.5	T-5-9-17 TGT
5	6023.6	11.50	228.32	5925.0	-668.4	-750.7	0.00	0.00	1005.1	



**NEWFIELD PRODUCTION COMPANY
GMBU T-5-9-17
AT SURFACE: NW/SW SECTION 4, T9S R17E
DUCHESNE COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site GMBU T-5-9-17 located in the NW 1/4 SW 1/4 Section 4, T9S R17E, Duchesne County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 – 1.4 miles \pm to the junction of this highway and UT State Hwy 53; proceed in a southeasterly direction – 11.3 miles \pm to it's junction with an existing road to the southwest; proceed in a southwesterly direction – 0.5 miles \pm to it's junction with an existing road road to the northwest; proceed in a northwesterly direction 0.7 miles \pm to the existing 12-4-9-17 well location.

The aforementioned dirt oil field service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads for access during the drilling, completion and production phase will be maintained at the standards required by the State of Utah, or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal. Any necessary fill material for repair will be purchase and hauled from private sources.

2. PLANNED ACCESS ROAD

There is no proposed access road for this location. The proposed well will be drilled directionally off of the existing 12-4-9-17 well pad. See attached **Topographic Map "B"**.

There will be **no** culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will be no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery, the well pad will be surrounded by a dike of sufficient capacity to contain at minimum 110% of the largest tank volume within the facility battery.

Tank batteries will be built to State specifications.

All permanent (on site for six (6) months or longer) structures, constructed or installed (including pumping units), will be painted a flat, non-reflective, earth tone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities will be painted within six months of installation.

5. **LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck from nearest water source as determined by a Newfield representative for the purpose of drilling the above mentioned well. The available water sources are as follows:

Johnson Water District
Water Right : 43-10136

Maurice Harvey Pond
Water Right: 47-1358

Neil Moon Pond
Water Right: 43-11787

Newfield Collector Well
Water Right: 47-1817 (A30414DVA, contracted with the Duchesne County Conservancy District).

There will be no water well drilled at this site.

6. **SOURCE OF CONSTRUCTION MATERIALS**

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road.

A mineral material application is not required for this location.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

A small reserve pit (90' x 40' x 8' deep, or less) will be constructed from native soil and clay materials. The reserve pit will receive the processed drill cutting (wet sand, shale & rock) removed from the wellbore. Any drilling fluids, which do accumulate in the pit as a result of shale-shaker carryover, cleaning of the sand trap, etc., will be promptly reclaimed. All drilling fluids will be fresh water based, typically containing Total Dissolved Solids of less than 3000 PPM. No potassium chloride, chromates, trash, debris, nor any other substance deemed hazardous will be placed in this pit. Therefore, it is proposed that no synthetic liner be required in the reserve pit. However, if upon constructing the pit there is insufficient fine clay and silt present, a liner will be used for the purpose of reducing water loss through percolation.

Newfield requests approval that a flare pit not be constructed or utilized on this location.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

8. **ANCILLARY FACILITIES**

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. **WELL SITE LAYOUT**

See attached Location Layout Sheet.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- a) A 39-inch net wire shall be used with at least one strand of barbed wire on top of the net.
- b) The net wire shall be no more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be centered and/or braced in such a manner to keep tight at all times
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

Existing fences to be crossed by the access road will be braced and tied off before cutting so as to prevent slacking in the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BLM specifications.

10. **PLANS FOR RESTORATION OF SURFACE:**

- a) Producing Location

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximated natural contours. Weather permitting, the reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons removed.

- b) Dry Hole Abandoned Location

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the State of Utah will attach the appropriate surface rehabilitation conditions of approval.

11. **SURFACE OWNERSHIP** – State of Utah.

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. State of Utah Antiquities Project Permit # U-11-MQ-0698b 8/29/11, prepared by

Montgomery Archaeological Consultants. Paleontological Resource Survey prepared by, SWCA, 8/24/11. See attached report cover pages, Exhibit "D".

Newfield Production Company requests 3,993' of surface gas line be granted. **Refer to Topographic Map "B"**.

Water Disposal

After first production, if the production water meets quality guidelines, it will be transported to the Ashley, Monument Butte, Jonah, South Wells Draw and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project. Water not meeting quality criteria, will be disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E), Federally approved surface disposal facilities or at a State of Utah approved surface disposal facilities.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations, Onshore Oil and Gas Orders, the approved plan of operations and any applicable Notice to Lessees. A copy of these conditions will be furnished to the field representative to ensure compliance.

Details of the On-Site Inspection

The proposed GMBU T-5-9-17 was on-sited on 5/24/12. The following were present; Corie Miller (Newfield Production), Janna Simonsen (Bureau of Land Management) and Dave Gordon (Bureau of Land Management).

Hazardous Material Declaration

Newfield Production Company guarantees that during the drilling and completion of the GMBU T-5-9-17, Newfield will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986. Newfield also guarantees that during the drilling and completion of the GMBU T-5-9-17, Newfield will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Newfield Production Company or a contractor employed by Newfield Production shall contact the State office at (801) 722-3417, 48 hours prior to construction activities.

13. **LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION:**
Representative

Name: Corie Miller
Address: Newfield Production Company
Route 3, Box 3630
Myton, UT 84052
Telephone: (435) 646-3721

Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #T-5-9-17, Section 4, Township 9S, Range 17E: Lease UTU-75038 Duchesne County, Utah: and is

responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by, Federal Bond #WYB000493.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of the 18 U.S.C. 1001 for the filing of a false statement.

6/4/12

Date

Mandie Crozier
Regulatory Analyst
Newfield Production Company

Typical 2M BOP stack configuration



2M CHOKE MANIFOLD EQUIPMENT - CONFIGURATION OF CHOKES MAY VARY

NEWFIELD EXPLORATION COMPANY

WELL PAD INTERFERENCE PLAT

12-4-9-17 (Existing Well)

Q-4-9-17 (Proposed Well)

T-5-9-17 (Proposed Well)

Pad Location: NWSW Section 4, T9S, R17E, S.L.B.&M.




TOP HOLE FOOTAGES

T-5-9-17 (PROPOSED)
1936' FSL & 500' FWL

CENTER OF PATTERN FOOTAGES

T-5-9-17 (PROPOSED)
1420' FSL & 100' FEL

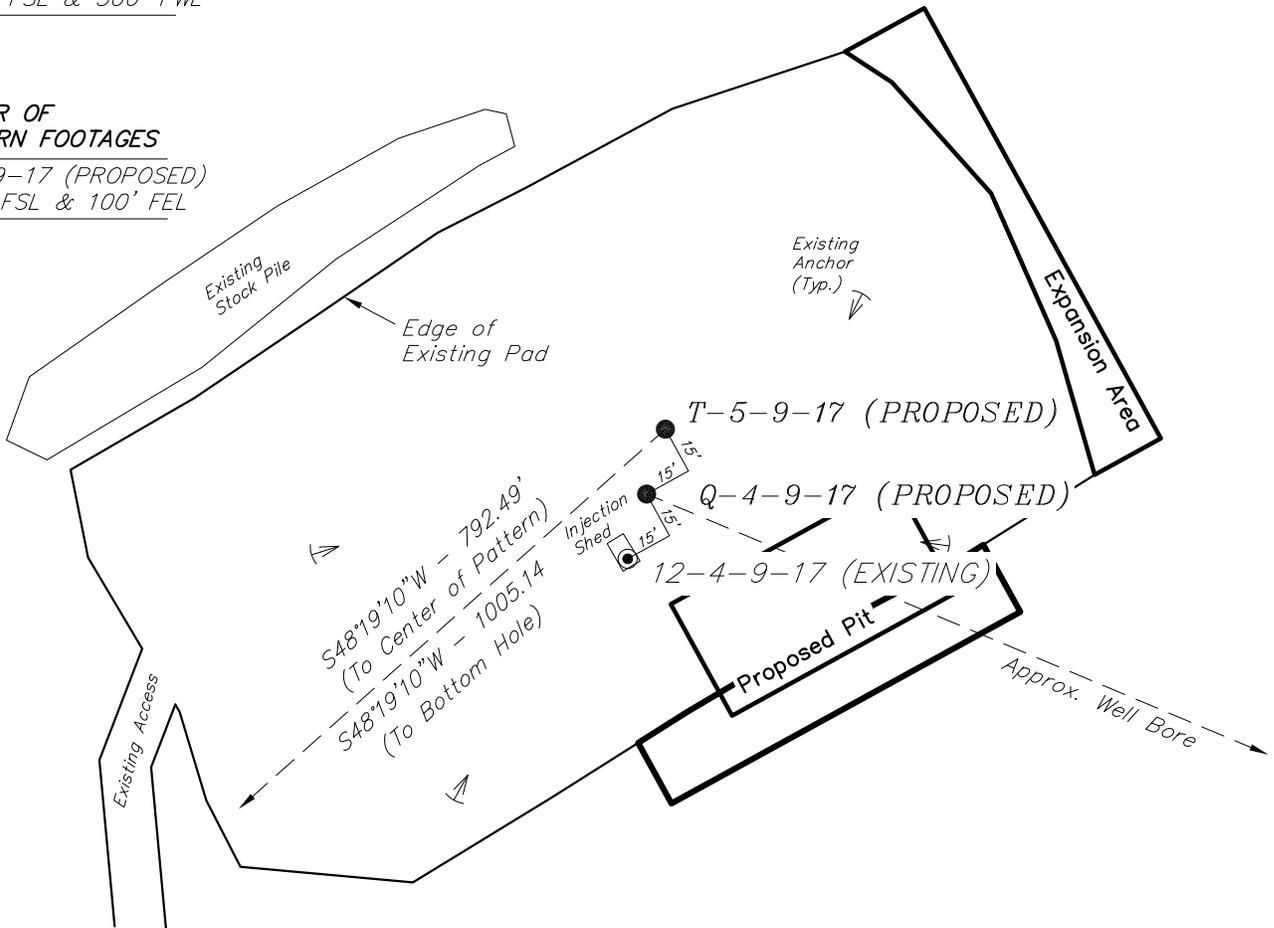

Note:

Bearings are based on GPS Observations.

**RELATIVE COORDINATES
From Top Hole to C.O.P.**

WELL	NORTH	EAST
T-5-9-17	-527'	-592'

**RELATIVE COORDINATES
From Top Hole to Bottom Hole**

WELL	NORTH	EAST
T-5-9-17	-668'	-751'

BOTTOM HOLE FOOTAGES

T-5-9-17 (PROPOSED)
1282' FSL & 261' FEL

**LATITUDE & LONGITUDE
Surface position of Wells (NAD 83)**

WELL	LATITUDE	LONGITUDE
12-4-9-17	40° 03' 28.42"	110° 01' 09.36"
Q-4-9-17	40° 03' 28.62"	110° 01' 09.28"
T-5-9-17	40° 03' 28.82"	110° 01' 09.20"

SURVEYED BY: S.H.	DATE SURVEYED: 07-06-11	VERSION: V3
DRAWN BY: F.T.M.	DATE DRAWN: 05-01-12	
SCALE: 1" = 60'	REVISED: F.T.M. 05-14-12	

Tri State (435) 781-2501
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD EXPLORATION COMPANY



LOCATION LAYOUT

12-4-9-17 (Existing Well)

Q-4-9-17 (Proposed Well)

T-5-9-17 (Proposed Well)

Pad Location: NWSW Section 4, T9S, R17E, S.L.B.&M.

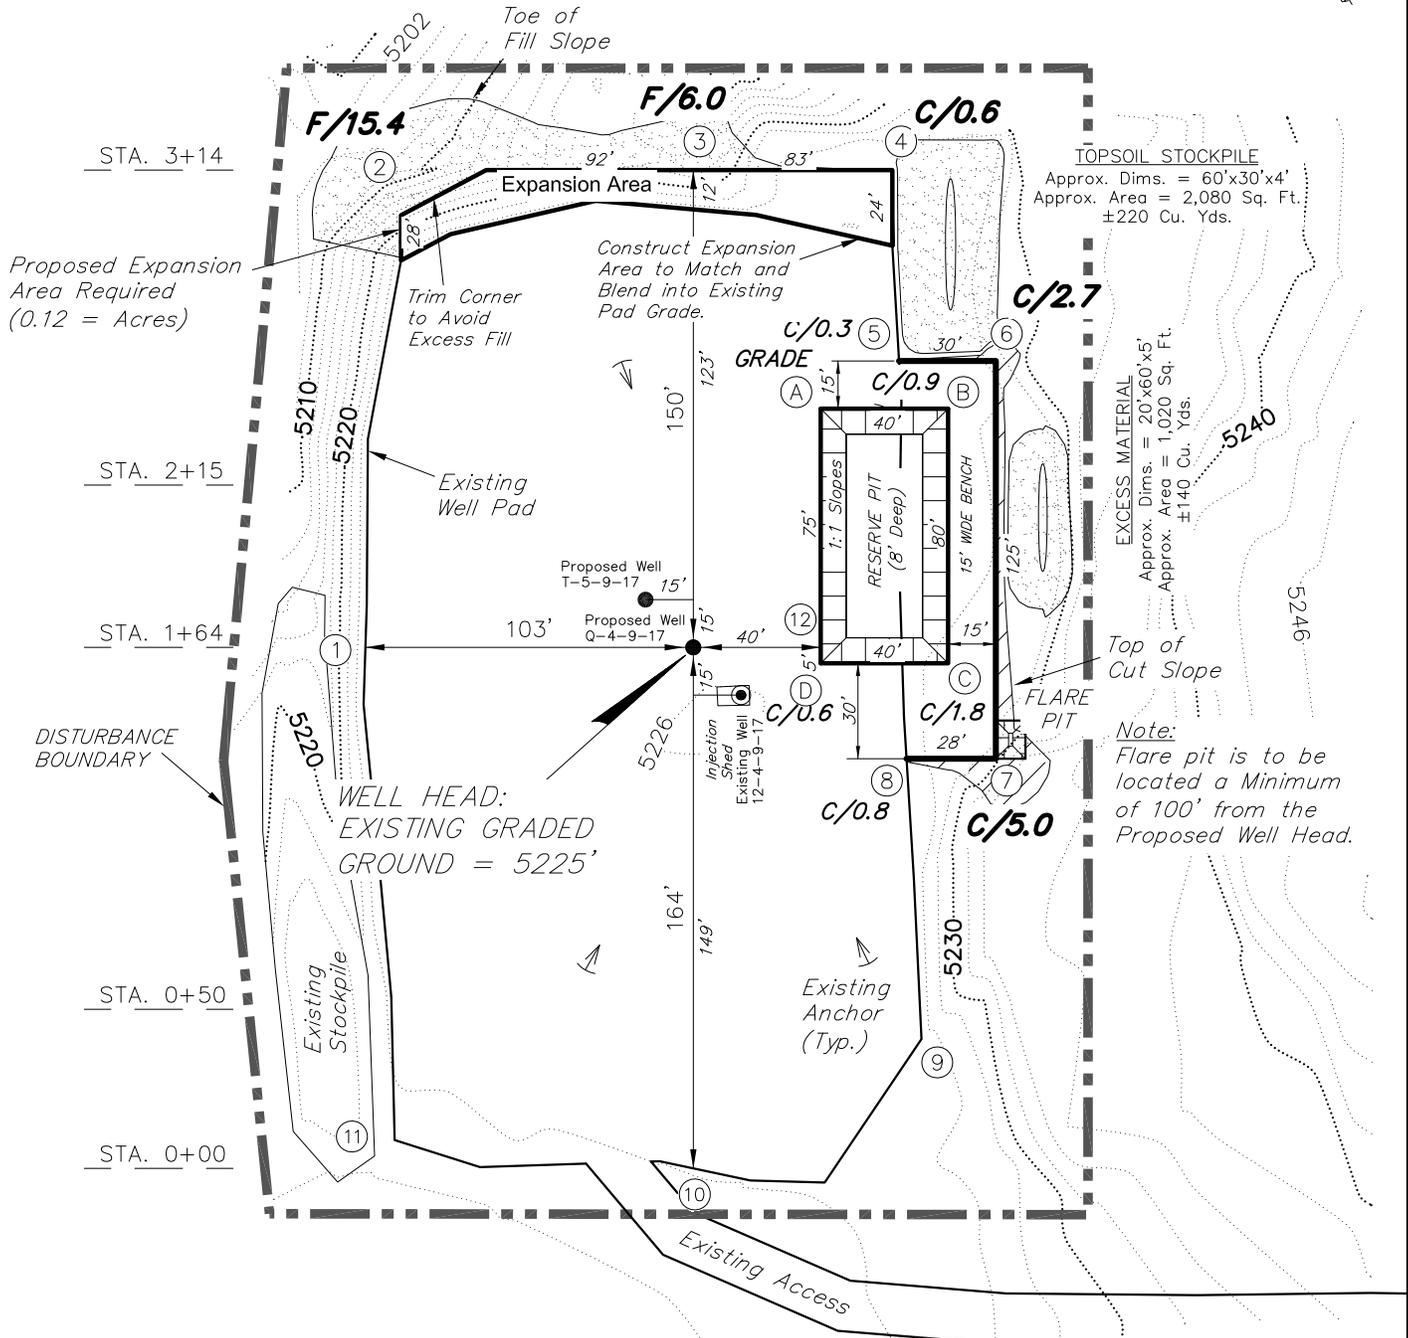

NOTE:
The topsoil & excess material areas are calculated as being mounds containing 360 cubic yards of dirt (a 10% fluff factor is included). The mound areas are calculated with push slopes of 1.5:1 & fall slopes of 1.5:1.

Note:
Topsoil to be Stripped From All New Construction Areas and Proposed Stock Pile Locations

SURVEYED BY: S.H.	DATE SURVEYED: 07-06-11	VERSION:
DRAWN BY: M.W.	DATE DRAWN: 02-01-12	V3
SCALE: 1" = 60'	REVISED: F.T.M. 05-14-12	

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD EXPLORATION COMPANY





CROSS SECTIONS

12-4-9-17 (Existing Well)

Q-4-9-17 (Proposed Well)

T-5-9-17 (Proposed Well)

Pad Location: NWSW Section 4, T9S, R17E, S.L.B.&M.

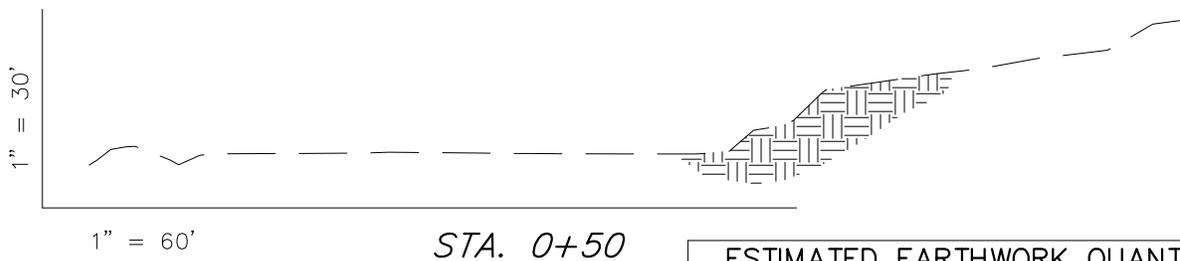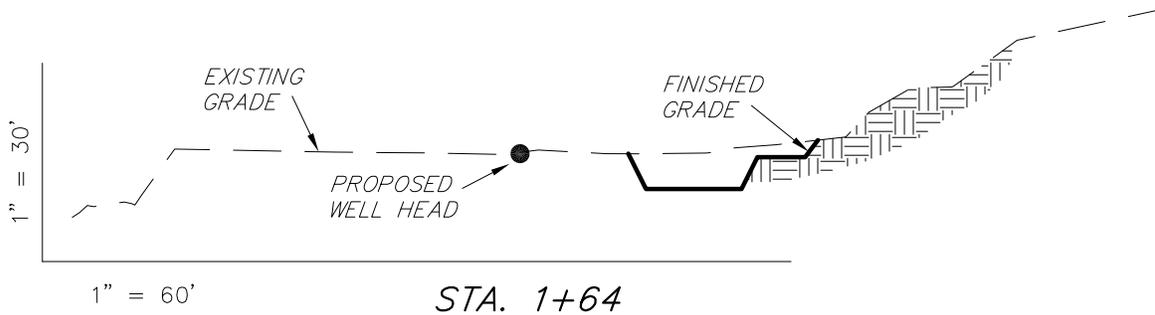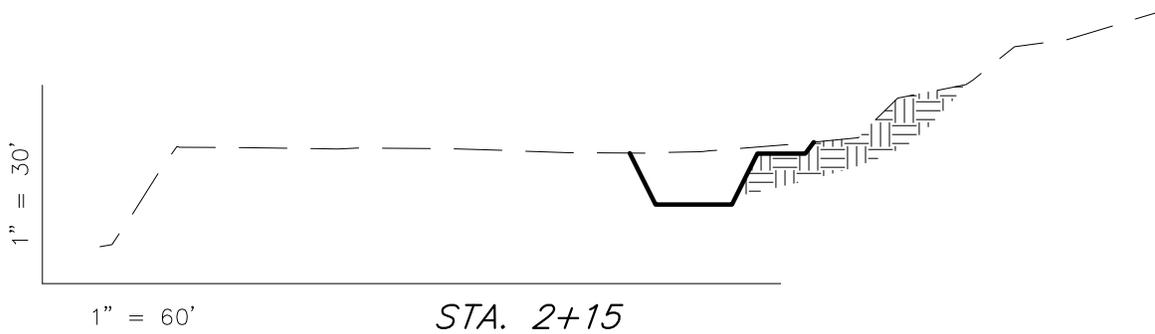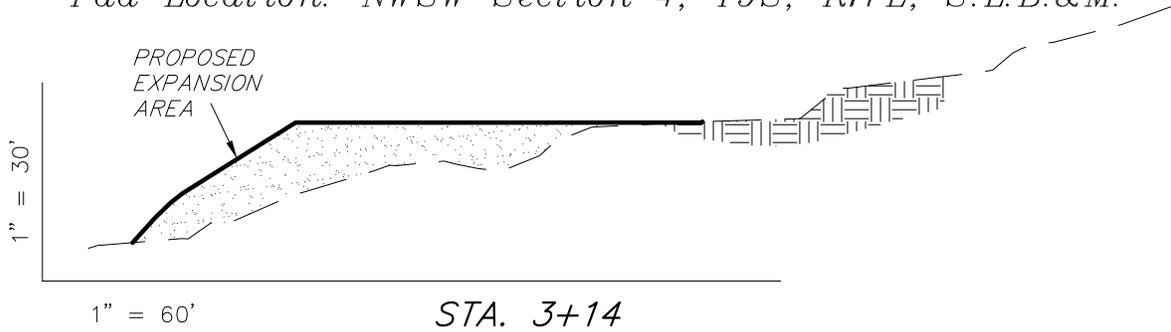

ESTIMATED EARTHWORK QUANTITIES
(No Shrink or swell adjustments have been used)
(Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	150	710	Topsoil is not included in Pad Cut	-560
PIT	690	0		690
TOTALS	840	710	200	130

NOTE:
UNLESS OTHERWISE
NOTED ALL CUT/FILL
SLOPES ARE AT 1.5:1

SURVEYED BY: S.H.	DATE SURVEYED: 07-06-11	VERSION:
DRAWN BY: M.W.	DATE DRAWN: 02-01-12	V3
SCALE: 1" = 60'	REVISED: F.T.M. 05-14-12	

Tri State

Land Surveying, Inc.

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

(435) 781-2501

NEWFIELD EXPLORATION COMPANY



TYPICAL RIG LAYOUT

12-4-9-17 (Existing Well)

Q-4-9-17 (Proposed Well)

T-5-9-17 (Proposed Well)

Pad Location: NWSW Section 4, T9S, R17E, S.L.B.&M.

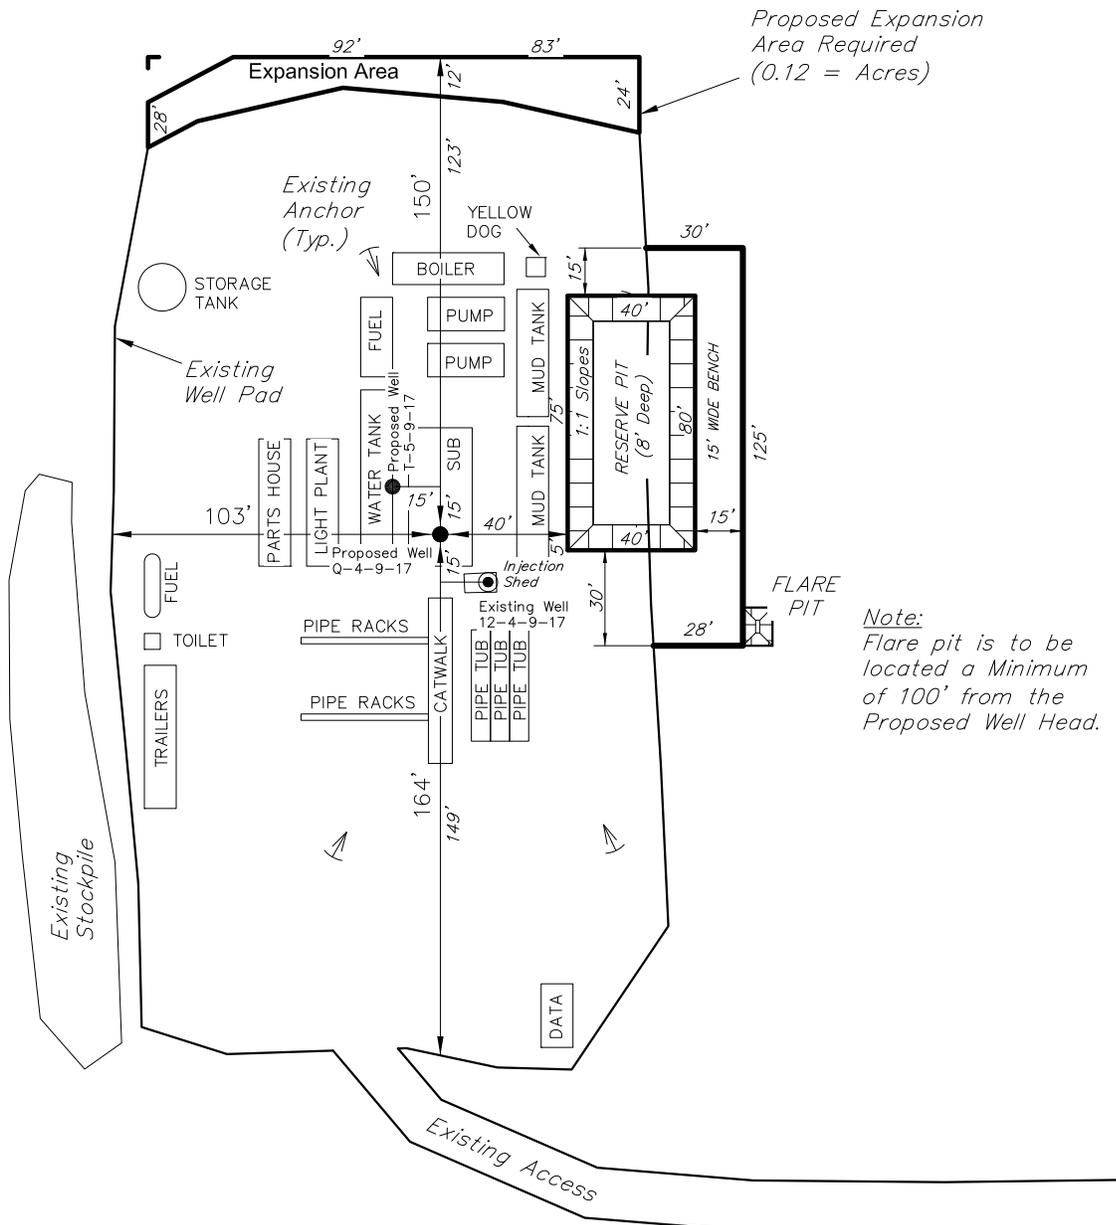

SURVEYED BY: S.H.	DATE SURVEYED: 07-06-11	VERSION:
DRAWN BY: M.W.	DATE DRAWN: 02-01-12	V3
SCALE: 1" = 60'	REVISED: F.T.M. 05-14-12	

Tri State (435) 781-2501
 Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078

United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office

P.O. Box 45155

Salt Lake City, Utah 84145-0155

IN REPLY REFER TO:**3160****(UT-922)**

June 11, 2012

Memorandum

To: Assistant District Manager Minerals, Vernal District

From: Michael Coulthard, Petroleum Engineer

Subject: 2012 Plan of Development Greater Monument
Butte Unit, Duchesne and Uintah Counties,
Utah.

Pursuant to email between Diana Whitney, Division of Oil, Gas and Mining, and Mickey Coulthard, Utah State Office, Bureau of Land Management, the following wells are planned for calendar year 2012 within the Greater Monument Butte Unit, Duchesne and Uintah Counties, Utah.

API #	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-51461	GMBU R-29-8-17	Sec 29 T08S R17E 0676 FSL 1990 FWL BHL Sec 29 T08S R17E 1679 FSL 2467 FEL
43-013-51467	GMBU H-9-9-17	Sec 09 T09S R17E 0725 FNL 1875 FEL BHL Sec 09 T09S R17E 1509 FNL 2495 FWL
43-013-51468	GMBU E-10-9-17	Sec 04 T09S R17E 0675 FSL 0647 FEL BHL Sec 10 T09S R17E 0075 FNL 0156 FWL
43-013-51469	GMBU Q-3-9-17	Sec 03 T09S R17E 1946 FSL 0796 FWL BHL Sec 03 T09S R17E 1079 FSL 1581 FWL
43-013-51470	GMBU P-3-9-17	Sec 04 T09S R17E 0690 FSL 0631 FEL BHL Sec 03 T09S R17E 1386 FSL 0186 FWL
43-013-51471	GMBU O-7-9-17	Sec 12 T09S R16E 2560 FNL 0320 FEL BHL Sec 07 T09S R17E 1703 FSL 0089 FWL
43-013-51472	GMBU I-9-9-17	Sec 09 T09S R17E 0746 FNL 1874 FEL BHL Sec 09 T09S R17E 1552 FNL 1081 FEL
43-013-51473	GMBU P-7-9-17	Sec 12 T09S R16E 1930 FSL 0740 FEL BHL Sec 07 T09S R17E 1085 FSL 0230 FWL

RECEIVED: June 12, 2012

API #	WELL NAME	LOCATION
(Proposed PZ GREEN RIVER)		
43-013-51474	GMBU R-3-9-17	Sec 03 T09S R17E 0577 FSL 1858 FWL
		BHL Sec 03 T09S R17E 1445 FSL 2479 FEL
43-013-51475	GMBU K-4-9-17	Sec 03 T09S R17E 1888 FNL 0749 FWL
		BHL Sec 04 T09S R17E 2396 FSL 0032 FEL
43-013-51476	GMBU S-9-9-17	Sec 09 T09S R17E 0783 FSL 0722 FEL
		BHL Sec 09 T09S R17E 1445 FSL 1487 FEL
43-013-51477	GMBU C-9-9-17	Sec 04 T09S R17E 0669 FSL 1839 FEL
		BHL Sec 09 T09S R17E 0191 FNL 2460 FWL
43-013-51478	GMBU D-10-9-17	Sec 03 T09S R17E 0585 FSL 1839 FWL
		BHL Sec 10 T09S R17E 0288 FNL 1243 FWL
43-013-51480	GMBU T-5-9-17	Sec 04 T09S R17E 1936 FSL 0500 FWL
		BHL Sec 05 T09S R17E 1282 FSL 0261 FEL
43-013-51481	GMBU F-7-9-17	Sec 12 T09S R16E 2555 FNL 0370 FEL
		BHL Sec 07 T09S R17E 0955 FNL 0126 FWL

This office has no objection to permitting the wells at this time.

Michael L. Coulthard


Digitally signed by Michael L. Coulthard
 DN: cn=Michael L. Coulthard, o=Bureau of Land Management,
 ou=Branch of Minerals, email=Michael_Coulthard@blm.gov, c=US
 Date: 2012.06.11 10:34:31 -06'00'

bcc: File - Greater Monument Butte Unit
 Division of Oil Gas and Mining
 Central Files
 Agr. Sec. Chron
 Fluid Chron


MCoulthard:mc:6-11-12

API Number: 4301351480
Well Name: GMBU T-5-9-17
 Township T09. Range R1.7. Section 04
 Meridian: SLBM
 Operator: NEWFIELD PRODUCTION COMPANY

Map Prepared:
 Map Produced by Diana Mason

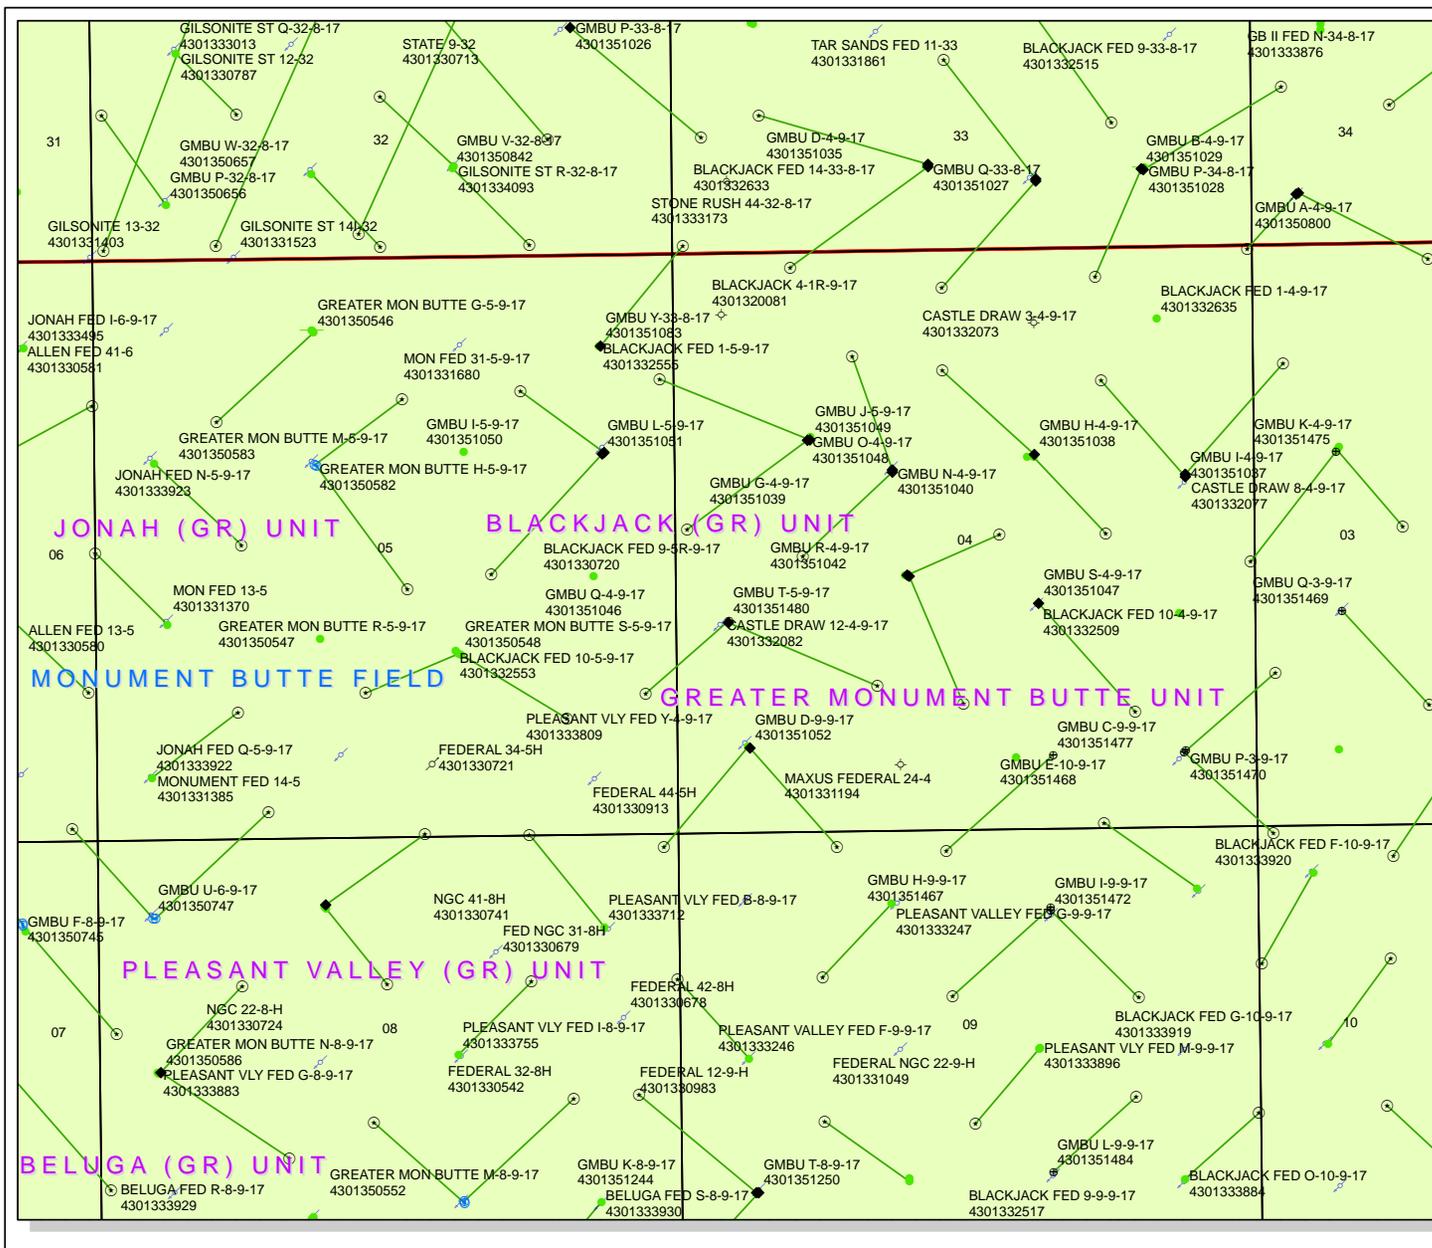

Units STATUS	Wells Query Status
ACTIVE	APD - Approved Permit
EXPLORATORY	DRIL - Spudded (Drilling Commenced)
GAS STORAGE	GIW - Gas Injection
NF PP OIL	GS - Gas Storage
NF SECONDARY	LOC - New Location
PI OIL	OPS - Operation Suspended
PP GAS	PA - Plugged Abandoned
PP GEOTHERML	PGW - Producing Gas Well
PP OIL	SGW - Shut-in Gas Well
SECONDARY	POW - Producing Oil Well
TERMINATED	SGW - Shut-in Oil Well
Unknown	TA - Temp. Abandoned
ABANDONED	TW - Test Well
ACTIVE	WDW - Water Disposal
COMBINED	WW - Water Injection Well
INACTIVE	WSW - Water Supply Well
STORAGE	
TERMINATED	



WORKSHEET APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 6/5/2012

API NO. ASSIGNED: 43013514800000

WELL NAME: GMBU T-5-9-17

OPERATOR: NEWFIELD PRODUCTION COMPANY (N2695)

PHONE NUMBER: 435 646-4825

CONTACT: Mandie Crozier

PROPOSED LOCATION: NWSW 04 090S 170E

Permit Tech Review:

SURFACE: 1936 FSL 0500 FWL

Engineering Review:

BOTTOM: 1282 FSL 0261 FEL

Geology Review:

COUNTY: DUCHESNE

LATITUDE: 40.05797

LONGITUDE: -110.01921

UTM SURF EASTINGS: 583650.00

NORTHINGS: 4434653.00

FIELD NAME: MONUMENT BUTTE

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-75038

PROPOSED PRODUCING FORMATION(S): GREEN RIVER

SURFACE OWNER: 1 - Federal

COALBED METHANE: NO

RECEIVED AND/OR REVIEWED:

- PLAT
- Bond: FEDERAL - WYB000493
- Potash
- Oil Shale 190-5
- Oil Shale 190-3
- Oil Shale 190-13
- Water Permit: 437478
- RDCC Review:
- Fee Surface Agreement
- Intent to Commingle

Commingle Approved

LOCATION AND SITING:

- R649-2-3.
- Unit: GMBU (GRRV)
- R649-3-2. General
- R649-3-3. Exception
- Drilling Unit
- Board Cause No: Cause 213-11
- Effective Date: 11/30/2009
- Siting: Suspends General Siting
- R649-3-11. Directional Drill

Comments: Presite Completed

Stipulations: 4 - Federal Approval - dmason
15 - Directional - dmason
27 - Other - bhll



GARY R. HERBERT
Governor

GREGORY S. BELL
Lieutenant Governor

State of Utah

DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER
Executive Director

Division of Oil, Gas and Mining

JOHN R. BAZA
Division Director

Permit To Drill

Well Name: GMBU T-5-9-17
API Well Number: 43013514800000
Lease Number: UTU-75038
Surface Owner: FEDERAL
Approval Date: 6/18/2012

Issued to:

NEWFIELD PRODUCTION COMPANY , Rt 3 Box 3630 , Myton, UT 84052

Authority:

Pursuant to Utah Code Ann. 40-6-1 et seq., and Utah Administrative Code R649-3-1 et seq., the Utah Division of Oil, Gas and Mining issues conditions of approval, and permit to drill the listed well. This permit is issued in accordance with the requirements of Cause 213-11. The expected producing formation or pool is the GREEN RIVER Formation(s), completion into any other zones will require filing a Sundry Notice (Form 9). Completion and commingling of more than one pool will require approval in accordance with R649-3-22.

Duration:

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date

General:

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

Conditions of Approval:

State approval of this well does not supercede the required federal approval, which must be obtained prior to drilling.

In accordance with Utah Admin. R.649-3-11, Directional Drilling, the operator shall submit a complete angular deviation and directional survey report to the Division within 30 days following completion of the well.

Production casing cement shall be brought up to or above the top of the unitized interval for the Greater Monument Butte Unit (Cause No. 213-11).

Notification Requirements:

The operator is required to notify the Division of Oil, Gas and Mining of the following actions during drilling of this well:

- Within 24 hours following the spudding of the well - contact Carol Daniels at 801-538-5284

(please leave a voicemail message if not available)

OR

submit an electronic sundry notice (pre-registration required) via the Utah Oil & Gas website
at <http://oilgas.ogm.utah.gov>

Reporting Requirements:

All reports, forms and submittals as required by the Utah Oil and Gas Conservation General Rules will be promptly filed with the Division of Oil, Gas and Mining, including but not limited to:

- Entity Action Form (Form 6) - due within 5 days of spudding the well
- Monthly Status Report (Form 9) - due by 5th day of the following calendar month
- Requests to Change Plans (Form 9) - due prior to implementation
- Written Notice of Emergency Changes (Form 9) - due within 5 days
- Notice of Operations Suspension or Resumption (Form 9) - due prior to implementation
- Report of Water Encountered (Form 7) - due within 30 days after completion
- Well Completion Report (Form 8) - due within 30 days after completion or plugging

Approved By:

A handwritten signature in black ink, appearing to read "John Rogers", written over a horizontal line.

For John Rogers
Associate Director, Oil & Gas

RECEIVED

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0136
Expires July 31, 2010

JUN 11 2012

APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU75038
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name
2. Name of Operator NEWFIELD PRODUCTION COMPANY Contact: MANDIE CROZIER Email: mcrozier@newfield.com		7. If Unit or CA Agreement, Name and No. GREATER MONUMENT
3a. Address ROUTE #3 BOX 3630 MYTON, UT 84052		8. Lease Name and Well No. GMBU T-5-9-17
3b. Phone No. (include area code) Ph: 435-646-4825 Fx: 435-646-3031		9. API Well No. 43-013-51480
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NWSW 1936FSL 500FWL At proposed prod. zone SESE 1282FSL 261FEL		10. Field and Pool, or Exploratory MONUMENT BUTTE
14. Distance in miles and direction from nearest town or post office* 13.9	11. Sec., T., R., M., or Blk. and Survey or Area Sec 4 T9S R17E Mer SLB	12. County or Parish DUCHESNE
15. Distance from proposed location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) 38'	13. State UT	17. Spacing Unit dedicated to this well 20.00
16. No. of Acres in Lease 535.31	18. Distance from proposed location to nearest well, drilling, completed, applied for, on this lease, ft. 1191'	20. BLM/BIA Bond No. on file WYB000493
19. Proposed Depth 6024 MD 5925 TVD	21. Elevations (Show whether DF, KB, RT, GL, etc.) 5224 GL	23. Estimated duration 7 DAYS
22. Approximate date work will start 09/30/2012	24. Attachments	

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No. 1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification
- Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature (Electronic Submission)	Name (Printed/Typed) MANDIE CROZIER Ph: 435-646-4825	Date 06/05/2012
Title REGULATORY ANALYST		
Approved by (Signature) 	Name (Printed/Typed) Jerry Kenczka	Date NOV 16 2012
Title Assistant Field Manager Lands & Mineral Resources		
Office VERNAL FIELD OFFICE		

Application approval does not warrant or certify the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

Additional Operator Remarks (see next page)

NOTICE OF APPROVAL

Electronic Submission #139740 verified by [redacted] Well Information System
For NEWFIELD PRODUCTION COMPANY sent to the Vernal Field Office
Committed to AFMSS for processing by [redacted] BINSON on 06/11/2012

UDOGM

POSTED
FROM
TO

** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED ** OPERATOR-SUBMITTED **

12UBR0701AE NO NUG APD Posted 6/11/12.



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL

Company: Newfield Production Company
Well No: GMBU T-5-9-17
API No: 43-013-51480

Location: SWNW, Sec. 4, T9S, R17E
Lease No: UTU-75038
Agreement: GREATER MONUMENT BUTTE

OFFICE NUMBER: (435) 781-4400

OFFICE FAX NUMBER: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

NOTIFICATION REQUIREMENTS

Location Construction (Notify Environmental Scientist)	- Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	- Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	- Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to running casing and cementing all casing strings to: blm_ut_vn_opreport@blm.gov
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	- Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	- Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

SURFACE USE PROGRAM CONDITIONS OF APPROVAL (COAs)

- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 gms of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower.
- All and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 gms of NO_x per horsepower-hour.
- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

Monitoring and Reporting

- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) that designates the proposed site-specific monitoring and reference sites chosen for the location. A description of the proposed sites shall be included, as well as a map showing the locations of the proposed sites.
- The operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) 3 growing seasons after reclamation efforts have occurred evaluating the status of the reclaimed areas in order to determine whether the BLM standards set forth in the Green River District Reclamation Guidelines have been met (30% or greater basal cover).
- Prior to beginning new surface disturbance, the operator shall submit a Sundry Notice (Form 3160-5) to the BLM Authorized Officer (AO) providing the results of the noxious weed inventory described in the Green River District Reclamation Guidelines (2011). If weeds are found the report shall include 1) A GPS location recorded in North American Datum 1983; 2) species; 3) canopy cover or number of plants; 4) and size of infestation (estimate square feet or acres. Information shall be also documented in the reclamation report.

CONDITIONS OF APPROVAL

Wildlife

In accordance with the Record of Decision for the Castle Peak and Eightmile Flat Oil and Gas Expansion Project, Newfield Rocky Mountains Inc., the following COA's are required:

- WFM-1 On level or gently sloping ground (5 percent slope or less) Newfield will elevate surface pipelines (4 inches or greater in diameter) a minimum of 6 inches above the ground to allow passage of small animals beneath the pipe. This ground clearance will be achieved by placing the pipeline on blocks at intervals of 150 to 200 feet.
- WFM-4 Newfield will install noise reduction devices on all pump jacks to reduce intermittent noise to 45 dBA at 660 feet from the source.

COA's derived from mitigating measures in the EA:

- Newfield will contract a qualified biologist to conduct a breeding bird survey within 330 feet (100 meters) from proposed surface disturbance activities associated with wellfield development (e.g. well pads, roads, pipelines, power lines, and ancillary facilities) that will occur during the breeding season from April 1 through July 31. If an active nest for important migratory bird species (USFWS Bird of Conservation Concern, Partners in Flight Priority Bird Species, Utah Sensitive Species) is documented during the survey, Newfield will coordinate with to determine if any additional protection measures will be required. Alternatively, prior to surface disturbance activities within that year, Newfield will clear vegetation within the year of surface disturbance activities outside of the breeding season (April 1 through July 31).

If construction and drilling is anticipated during any of the following wildlife seasonal spatial restrictions, a BLM biologist or a qualified consulting firm biologist must conduct applicable surveys using an accepted protocol prior to any ground disturbing activities.

- The proposed project is within ½ mile of a golden eagle nest. If construction or drilling is proposed from January 1-August 31 then a nest survey will be conducted by a qualified biologist. If the nest is found to be inactive, then permission to proceed may be granted by the BLM Authorized Officer. If the nest is determined to be active, then the timing restriction will remain in effect.

For protection of T&E Fish if drawing water from the Green River

- For areas of fresh water collection, an infiltration gallery will be constructed in a Service approved location. An infiltration gallery is basically a pit or trench dug within the floodplain to a depth below the water table. Water is drawn from the pit rather than from the river directly. If this is not possible, limit pumping within the river to off-channel locations that do not connect to the river during high spring flows.
- If water cannot be drawn using the measures above and the pump head will be located in the river channel where larval fish are known to occur, the following measures apply:
 - Avoid pumping from low-flow or no-flow areas as these habitats tend to concentrate larval fish
 - Avoid pumping to the greatest extent possible, during that period of the year when larval fish may be present (see previous bullet); and
 - Avoid pumping, to the greatest extent possible, during the midnight hours (10:00 p.m. to 2:00 a.m.) as larval drift studies indicate that this is a period of greatest daily activity. Dusk is the preferred pumping time, as larval drift abundance is lowest during this time.
 - Screen all pump intakes with 3/32-inch mesh material.
- Report any fish impinged on the intake screen to the FWS office (801.975.3330) and the:
Utah Division of Wildlife Resources
Northeastern Region
152 East 100 North
Vernal, UT 84078
(435) 781-9453

Air Quality

- All internal combustion equipment will be kept in good working order.
- Water or other approved dust suppressants will be used at construction sites and along roads, as determined appropriate by the Authorized Officer. Dust suppressant such as magnesium chloride or fresh water may be used, as needed, during the drilling phase.
- Open burning of garbage or refuse will not occur at well sites or other facilities.
- Drill rigs will be equipped with Tier II or better diesel engines.
- Low bleed pneumatics will be installed on separator dump valves and other controllers.
- During completion, no venting will occur, and flaring will be limited as much as possible. Production equipment and gathering lines will be installed as soon as possible.
- Telemetry will be installed to remotely monitor and control production.
- Signs will be installed on the access road, reducing speed to 25 MPH, during the drilling phase.
- When feasible, two or more rigs (including drilling and completion rigs) will not be run simultaneously within 200 meters of each other. If two or more rigs must be run simultaneously within 200 meters of each other, then effective public health buffer zones out to 200 meters (m) from the nearest emission source will be implemented. Examples of an effective public health protection buffer zone include the demarcation of a public access exclusion zone by signage at intervals of every 250 feet that is visible from a distance of 125 feet during daylight hours, and a physical buffer such as active surveillance to ensure the property is not accessible by the public during drilling operations. Alternatively, the proponent may demonstrate compliance with the 1-hour NO₂ National Ambient Air Quality Standards (NAAQS) with appropriate and accepted near-field modeling. As part of this demonstration, the proponent may propose alternative mitigation that could include but is not limited to natural gas-fired drill rigs, installation of NO_x controls, time/use restrictions, and/or drill rig spacing.
- All new and replacement internal combustion gas field engines of less than or equal to 300 design-rated horsepower must not emit more than 2 grams of NO_x per horsepower-hour. This requirement does not apply to gas field engines of less than or equal to 40 design-rated horsepower-hour.
- All new and replacement internal combustion gas field engines of greater than 300 design rated horsepower must not emit more than 1.0 grams of NO_x per horsepower-hour.
- Green completions will be used for all well completion activities where technically feasible.
- Employ enhanced VOC emission controls with 95% control efficiency on production equipment having a potential to emit greater than 5 tons per year.

Threatened, Endangered and Candidate Plant Species

Reinitiation of Section 7 consultation with the USFWS will be sought immediately if any loss of plants or occupied habitat for Pariette cactus or Uinta Basin hookless cactus is anticipated as a result of project activities.

DOWNHOLE PROGRAM

CONDITIONS OF APPROVAL (COAs)

SITE SPECIFIC DOWNHOLE COAs:

- Newfield Production Co. shall adhere to all referenced requirements in the SOP (version: "Greater Monument Butte Green River Development Program", Feb 16, 2012). The operator shall also comply with applicable laws and regulations; with lease terms Onshore Oil and Gas Orders, NTL's; and with other orders and instructions of the, authorized officer.

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.
- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB

or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.

- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to BLM_UT_VN_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

OPERATING REQUIREMENT REMINDERS:

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- For information regarding production reporting, contact the Office of Natural Resources Revenue (ONRR) at www.ONRR.gov.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - Operator name, address, and telephone number.
 - Well name and number.
 - Well location ($\frac{1}{4}$ / $\frac{1}{4}$, Sec., Twn, Rng, and P.M.).
 - Date well was placed in a producing status (date of first production for which royalty will be paid).
 - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - Unit agreement and/or participating area name and number, if applicable.
 - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.
- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid,

and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.

- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

BLM - Vernal Field Office - Notification Form

Operator Newfield Exploration Rig Name/# Ross 26 Submitted By
Branden Arnold Phone Number 435-401-0223
Well Name/Number GMBU T-5-9-17
Qtr/Qtr NW/SW Section 4 Township 9S Range 17E
Lease Serial Number UTU-75038
API Number 43-013-51480

Spud Notice – Spud is the initial spudding of the well, not drilling
out below a casing string.

Date/Time 1/4/13 8:00 AM PM

Casing – Please report time casing run starts, not cementing
times.

- Surface Casing
- Intermediate Casing
- Production Casing
- Liner
- Other

Date/Time 1/4/13 3:00 AM PM

BOPE

- Initial BOPE test at surface casing point
- BOPE test at intermediate casing point
- 30 day BOPE test
- Other

Date/Time _____ AM PM

Remarks _____

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM -FORM 6

OPERATOR: **NEWFIELD PRODUCTION COMPANY**
ADDRESS: **RT. 3 BOX 3630**
MYTON, UT 84052

OPERATOR ACCT. NO. **N2695**

ACTION CODE	CURRENT ENTITY NO	NEW ENTITY NO	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4301351361	GMBU B-27-8-17	SWSE	22	8S	17E	DUCHESNE	12/28/2012	1-14-13

WELL 1 COMMENTS:

GRRV BHL: nene S27

ACTION CODE	CURRENT ENTITY NO	NEW ENTITY NO	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4301351362	GMBU C-27-8-17	SWSE	22	8S	17E	DUCHESNE	12/29/2012	1-14-13

GRRV BHL: nenuw S27

ACTION CODE	CURRENT ENTITY NO	NEW ENTITY NO	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4301351476	GMBU S-9-9-17	SESE	9	9S	17E	DUCHESNE	12/22/2012	1-14-13

GRRV BHL: nuse

ACTION CODE	CURRENT ENTITY NO	NEW ENTITY NO	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4301351484	GMBU L-9-9-17	NWSE	9	9S	17E	DUCHESNE	12/27/2012	1-14-13

GRRV BHL: sene

ACTION CODE	CURRENT ENTITY NO	NEW ENTITY NO	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4301351480	GMBU T-5-9-17	NWSW	4	9S	17E	DUCHESNE	1/4/2013	1-14-13

GRRV BHL: sese S5

ACTION CODE	CURRENT ENTITY NO	NEW ENTITY NO	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
B	99999	17400	4301351046	GMBU Q-4-9-17	NWSW	4	9S	17E	DUCHESNE	1/3/2013	1-14-13

GRRV BHL: sese

ACTION CODE	CURRENT ENTITY NO	NEW ENTITY NO	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
											1-14-13

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (explain in comments section)

RECEIVED

JAN 14 2013

Div. of Oil, Gas & Mining

Tabitha Timothy
Signature

Tabitha Timothy

Production Clerk

01/08/13

NOTE: Use COMMENT section to explain why each Action Code was selected.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED
OMB No. 1004-0137
Expires: July 31, 2010

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone (include are code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

Section 4 T9S R17E

5. Lease Serial No.

USA UTU-75038

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

GMBU

8. Well Name and No.

GMBU T-5-9-17

9. API Well No.

4301351480

10. Field and Pool, or Exploratory Area

GREATER MB UNIT

11. County or Parish, State

DUCHESNE, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplate horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recomplate in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 1/4/13 MIRU Ross #26. Spud well @12:00 PM. Drill 330' of 12 1/4" hole with air mist. TIH W/ 7 Jt's 8 5/8" J-55 24# csgn. Set @ 320.30. On 1/8/13 cement with 160 sks of class "G" w/ 2% CaCL2 + 0.25#/sk Cello- Flake Mixed @ 15.8ppg w/ 1.17ft3/sk yield. Returned 4 barrels cement to pit. WOC.

RECEIVED

JAN 16 2013

DIV. OF OIL, GAS & MINING

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Branden Arnold

Signature

Branden Arnold

Title

Date

01/08/2013

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

Casing / Liner Detail

Well: GMBU T-5-9-17
Prospect: Monument Butte
Foreman:
Run Date:
String Type: Surface, 8.625", 24#, J-55, STC (Generic)

- Detail From Top To Bottom -

Depth	Length	JTS	Description	OD	ID
320.30			10' KB		
10.00	264.85	6	8 5/8 Casing	8.625	
274.85	44.55	1	Shoe Joint	8.625	
319.40	0.90	1	Guide Shoe		
320.30			-		

Cement Detail

Cement Company: BJ

Slurry	# of Sacks	Weight (ppg)	Yield	Volume (ft ³)	Description - Slurry Class and Additives
Slurry 1	160	15.8	1.17	187.2	Class G+2%kcl+.25#CF

ab-In-Job?	No
IFT:	0
Initial Circulation Pressure:	
Initial Circulation Rate:	
Final Circulation Pressure:	
Final Circulation Rate:	
Displacement Fluid:	Water
Displacement Rate:	
Displacement Volume:	17
Fluid Returns:	
Centralizer Type And Placement:	

Cement To Surface?	Yes
Est. Top of Cement:	0
Plugs Bumped?	Yes
Pressure Plugs Bumped:	400
Floats Holding?	No
Casing Stuck On / Off Bottom?	No
Casing Reciprocated?	No
Casing Rotated?	No
CIP:	11:21
Casing Wt Prior To Cement:	
Casing Weight Set On Slips:	

middle of first, top of second and third for a total of three.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS	
Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	
1. TYPE OF WELL Oil Well	5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-75038
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
PHONE NUMBER: 435 646-4825 Ext	8. WELL NAME and NUMBER: GMBU T-5-9-17
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1936 FSL 0500 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NWSW Section: 04 Township: 09.0S Range: 17.0E Meridian: S	9. API NUMBER: 43013514800000
	9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
	COUNTY: DUCHESNE
	STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion:	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input checked="" type="checkbox"/> DRILLING REPORT Report Date: 3/5/2013	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input checked="" type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above well was placed on production on 03/05/2013 at 12:00 hours.

Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
 March 27, 2013

NAME (PLEASE PRINT) Jennifer Peatross	PHONE NUMBER 435 646-4885	TITLE Production Technician
SIGNATURE N/A	DATE 3/27/2013	

UNITED STATES
 DEPARTMENT OF THE INTERIOR
 BUREAU OF LAND MANAGEMENT

FORM APPROVED
 OMB NO. 1004-0137
 Expires: July 31, 2010

WELL COMPLETION OR RECOMPLETION REPORT AND LOG

1a. Type of Well Oil Well Gas Well Dry Other
 b. Type of Completion: New Well Work Over Deepen Plug Back Diff. Resrv.,
 Other: _____

5. Lease Serial No.
 UTU-75038

2. Name of Operator
 NEWFIELD EXPLORATION COMPANY

6. If Indian, Allottee or Tribe Name

3. Address
 1401 17TH ST. SUITE 1000 DENVER, CO 80202

3a. Phone No. (include area code)
 (435) 646-3721

7. Unit or CA Agreement Name and No.
 GMBU (GRRV)

4. Location of Well (Report location clearly and in accordance with Federal requirements)*

At surface 1936' FSL & 500' FWL (NW/SW) SEC. 4, T9S, R17E (UTU-75038)
 At top prod. interval reported below 1503' FSL & 11' FWL (NW/SW) SEC. 4, T9S, R17E (UTU-75038)
 At total depth 1236' FSL & 275' FEL (SE/SE) SEC. 5, T9S, R17E (UTU-72108)

8. Lease Name and Well No.
 GMBU T-5-9-17

9. API Well No.
 43-013-51480

10. Field and Pool or Exploratory
 MONUMENT BUTTE

11. Sec., T., R., M., on Block and
 Survey or Area SEC. 4, T9S, R17E

12. County or Parish
 DUCHENSE

13. State
 UT

14. Date Spudded
 01/04/2013

15. Date T.D. Reached
 02/07/2013

16. Date Completed 03/05/2013
 D & A Ready to Prod.

17. Elevations (DF, RKB, RT, GL)*
 5224' GL 5234' KB

18. Total Depth: MD 6220'
 TVD 6117'

19. Plug Back T.D.: MD 6162'
 TVD

20. Depth Bridge Plug Set: MD
 TVD

21. Type Electric & Other Mechanical Logs Run (Submit copy of each)
 DUAL IND GRD, SP, COMP. DENSITY, COMP. NEUTRON, GR, CALIPER, CMT BOND

22. Was well cored? No Yes (Submit analysis)
 Was DST run? No Yes (Submit report)
 Directional Survey? No Yes (Submit copy)

23. Casing and Liner Record (Report all strings set in well)

Hole Size	Size/Grade	Wt. (#/ft.)	Top (MD)	Bottom (MD)	Stage Cementer Depth	No. of Sk. & Type of Cement	Slurry Vol. (BBL)	Cement Top*	Amount Pulled
12-1/4"	8-5/8" J-55	24#	0	320'		160 CLASS G			
7-7/8"	5-1/2" J-55	15.5#	0	6208'		425 BONDCEM		552'	
						250 ECONCEM			

24. Tubing Record

Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)	Size	Depth Set (MD)	Packer Depth (MD)
2-7/8"	EOT@ 5949'	TA @ 5851'						

25. Producing Intervals

Formation	Top	Bottom	Perforated Interval	Size	No. Holes	Perf. Status
A) Green River	4183' MD	5892' MD	4183-5892' MD	0.34"	90	
B)						
C)						
D)						

27. Acid, Fracture, Treatment, Cement Squeeze, etc.

Depth Interval	Amount and Type of Material
4183-5892' MD	Frac w/ 356700#s 20/40 white sand in 2485 bbls of Lightning 17 fluid, in 4 stages.

28. Production - Interval A

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
3/5/13	3/15/13	24	→	65	112	58			2-1/2" x 1-3/4" x 20' x 21' x 24' RHAC Pump
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→					PRODUCING	

28a. Production - Interval B

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

*(See instructions and spaces for additional data on page 2)

28b. Production - Interval C

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

28c. Production - Interval D

Date First Produced	Test Date	Hours Tested	Test Production	Oil BBL	Gas MCF	Water BBL	Oil Gravity Corr. API	Gas Gravity	Production Method
			→						
Choke Size	Tbg. Press. Flwg. SI	Csg. Press.	24 Hr. Rate	Oil BBL	Gas MCF	Water BBL	Gas/Oil Ratio	Well Status	
			→						

29. Disposition of Gas (Solid, used for fuel, vented, etc.)

SOLD AND USED FOR FUEL

30. Summary of Porous Zones (Include Aquifers):

Show all important zones of porosity and contents thereof: Cored intervals and all drill-stem tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures and recoveries.

31. Formation (Log) Markers

GEOLOGICAL MARKERS


Formation	Top	Bottom	Descriptions, Contents, etc.	Name	Top
					Meas. Depth
				GARDEN GULCH MRK GARDEN GULCH 1	3735' 3915'
				GARDEN GULCH 2 POINT 3	4033'
				X MRKR Y MRKR	4544' 4579'
				DOUGLAS CREEK MRK BI CARBONATE MRK	4710' 4941'
				B LIMESTONE MRK CASTLE PEAK	5065' 5569'
				BASAL CARBONATE WASATCH	6002' 6124'

32. Additional remarks (include plugging procedure):

33. Indicate which items have been attached by placing a check in the appropriate boxes:

- Electrical/Mechanical Logs (1 full set req'd.)
 Geologic Report
 DST Report
 Directional Survey
 Sundry Notice for plugging and cement verification
 Core Analysis
 Other: Drilling Daily Activity

34. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records (see attached instructions)*

Name (please print) Jennifer Peatross Title Production Technician
 Signature  Date 04/03/2013

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.



NEWFIELD EXPLORATION

USGS Myton SW (UT)

SECTION 4 T9S R17E

T-5-9-17

Wellbore #1

Design: Actual

Standard Survey Report

14 February, 2013



Payzone Directional
Survey Report



Company:	NEWFIELD EXPLORATION	Local Co-ordinate Reference:	Well T-5-9-17
Project:	USGS Myton SW (UT)	TVD Reference:	T-5-9-17 @ 5237.0ft (NDSI SS #2)
Site:	SECTION 4 T9S R17E	MD Reference:	T-5-9-17 @ 5237.0ft (NDSI SS #2)
Well:	T-5-9-17	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Actual	Database:	EDM 2003.21 Single User Db

Project:	USGS Myton SW (UT), DUCHESNE COUNTY, UT, USA		
Map System:	US State Plane 1983	System Datum:	Mean Sea Level
Geo Datum:	North American Datum 1983		
Map Zone:	Utah Central Zone		

Site:	SECTION 4 T9S R17E				
Site Position:	Northing:	7,194,100.00 ft	Latitude:	40° 3' 36.542 N	
From:	Lat/Long	Easting:	2,057,000.00 ft	Longitude:	110° 0' 41.593 W
Position Uncertainty:	0.0 ft	Slot Radius:	"	Grid Convergence:	0.95 °

Well:	T-5-9-17, SHL LAT: 40 03 28.82 LONG: -110 01 09.20					
Well Position	+N-S	0.0 ft	Northing:	7,193,283.14 ft	Latitude:	40° 3' 28.820 N
	+E-W	0.0 ft	Easting:	2,054,866.84 ft	Longitude:	110° 1' 9.200 W
Position Uncertainty	0.0 ft	Wellhead Elevation:	5,237.0 ft	Ground Level:	5,225.0 ft	

Wellbore:	Wellbore #1				
Magnetics	Model Name	Sample Date	Declination (°)	Dip Angle (°)	Field Strength (nT)
	IGRF2010	4/30/2012	11.19	65.79	52,199

Design:	Actual				
Audit Notes:					
Version:	1.0	Phase:	ACTUAL	Tie On Depth:	0.0
Vertical Section:	Depth From (TVD) (ft)	+N-S (ft)	+E-W (ft)	Direction (°)	
	0.0	0.0	0.0	227.90	

Survey Program	Date: 2/14/2013				
From (ft)	To (ft)	Survey (Wellbore)	Tool Name	Description	
345.0	6,220.0	Survey #1 (Wellbore #1)	MWD	MWD - Standard	

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N-S (ft)	+E-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
0.0	0.00	0.00	0.0	0.0	0.0	0.0	0.00	0.00	0.00
345.0	0.20	288.10	345.0	0.2	-0.6	0.3	0.06	0.06	0.00
376.0	0.30	277.00	376.0	0.2	-0.7	0.4	0.36	0.32	-35.81
406.0	0.30	268.00	406.0	0.2	-0.9	0.5	0.16	0.00	-30.00
437.0	0.50	261.90	437.0	0.2	-1.1	0.7	0.66	0.65	-19.68
467.0	0.50	276.60	467.0	0.2	-1.3	0.9	0.43	0.00	49.00
498.0	0.40	262.70	498.0	0.2	-1.6	1.0	0.48	-0.32	-44.84
528.0	0.40	273.10	528.0	0.2	-1.8	1.2	0.24	0.00	34.67
559.0	0.30	267.00	559.0	0.2	-2.0	1.3	0.34	-0.32	-19.68
590.0	0.30	194.40	590.0	0.1	-2.1	1.5	1.15	0.00	-234.19
620.0	0.40	218.50	620.0	0.0	-2.2	1.6	0.59	0.33	80.33
651.0	0.50	260.80	651.0	-0.2	-2.4	1.9	1.09	0.32	136.45
681.0	0.90	297.50	681.0	-0.1	-2.7	2.0	1.94	1.33	122.33



Company:	NEWFIELD EXPLORATION	Local Co-ordinate Reference:	Well T-5-9-17
Project:	USGS Mylon SW (UT)	TVD Reference:	T-5-9-17 @ 5237.0ft (NDSI SS #2)
Site:	SECTION 4 T9S R17E	MD Reference:	T-5-9-17 @ 5237.0ft (NDSI SS #2)
Well:	T-5-9-17	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Actual	Database:	EDM 2003.21 Single User Db

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/S (ft)	+E/W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
712.0	1.40	287.10	712.0	0.2	-3.3	2.3	1.74	1.61	-33.55
743.0	1.90	271.20	743.0	0.3	-4.2	2.9	2.17	1.61	-51.29
773.0	2.50	260.60	772.9	0.2	-5.3	3.8	2.41	2.00	-35.33
804.0	2.90	249.00	803.9	-0.2	-6.7	5.1	2.18	1.29	-37.42
834.0	3.30	237.40	833.9	-0.9	-8.1	6.7	2.47	1.33	-38.67
864.0	4.00	233.30	863.8	-2.0	-9.7	8.6	2.49	2.33	-13.67
895.0	4.70	238.70	894.7	-3.3	-11.6	10.9	2.61	2.26	17.42
925.0	5.40	242.50	924.6	-4.6	-14.0	13.5	2.58	2.33	12.67
955.0	6.20	244.50	954.5	-6.0	-16.7	16.4	2.75	2.67	6.67
986.0	6.90	243.10	985.2	-7.5	-19.8	19.8	2.32	2.26	-4.52
1,017.0	7.50	240.90	1,016.0	-9.4	-23.3	23.5	2.13	1.94	-7.10
1,060.0	8.20	235.40	1,058.6	-12.5	-28.2	29.3	2.39	1.63	-12.79
1,104.0	8.70	231.10	1,102.1	-16.4	-33.4	35.8	1.83	1.14	-9.77
1,148.0	9.10	229.40	1,145.6	-20.7	-38.6	42.6	1.09	0.91	-3.86
1,192.0	9.50	226.60	1,189.0	-25.5	-43.9	49.7	1.37	0.91	-6.36
1,235.0	9.60	227.60	1,231.4	-30.3	-49.2	56.8	0.45	0.23	2.33
1,279.0	10.00	228.90	1,274.8	-35.3	-54.7	64.3	1.04	0.91	2.95
1,323.0	10.60	230.00	1,318.1	-40.4	-60.7	72.2	1.43	1.36	2.50
1,367.0	11.10	228.10	1,361.3	-45.8	-67.0	80.4	1.40	1.14	-4.32
1,411.0	11.60	224.80	1,404.4	-51.8	-73.2	89.1	1.86	1.14	-7.50
1,454.0	11.80	223.50	1,446.5	-58.1	-79.3	97.8	0.77	0.47	-3.02
1,498.0	11.60	223.60	1,489.6	-64.5	-85.5	106.7	0.46	-0.45	0.23
1,542.0	11.90	224.50	1,532.7	-71.0	-91.7	115.6	0.80	0.68	2.05
1,586.0	11.70	223.30	1,575.8	-77.5	-97.9	124.6	0.72	-0.45	-2.73
1,630.0	11.10	221.10	1,618.9	-83.9	-103.8	133.2	1.68	-1.36	-5.00
1,673.0	10.90	220.70	1,661.1	-90.1	-109.1	141.4	0.50	-0.47	-0.93
1,717.0	11.10	223.50	1,704.3	-96.3	-114.8	149.7	1.30	0.45	6.36
1,761.0	11.40	225.70	1,747.5	-102.4	-120.8	158.3	1.19	0.68	5.00
1,805.0	12.00	227.20	1,790.5	-108.6	-127.3	167.2	1.53	1.36	3.41
1,849.0	12.50	228.60	1,833.5	-114.8	-134.2	176.6	1.32	1.14	3.18
1,892.0	12.40	230.60	1,875.5	-120.8	-141.3	185.8	1.03	-0.23	4.65
1,936.0	12.20	231.80	1,918.5	-126.7	-148.6	195.2	0.74	-0.45	2.73
1,980.0	12.40	230.20	1,961.5	-132.6	-155.8	204.5	0.90	0.45	-3.64
2,024.0	12.20	224.00	2,004.5	-139.0	-162.7	213.9	3.03	-0.45	-14.09
2,068.0	11.90	220.40	2,047.5	-145.8	-168.9	223.0	1.84	-0.68	-8.18
2,111.0	12.00	222.50	2,089.6	-152.5	-174.8	231.9	1.04	0.23	4.88
2,155.0	12.70	224.10	2,132.6	-159.3	-181.2	241.3	1.77	1.59	3.64
2,199.0	12.50	227.30	2,175.5	-166.0	-188.1	250.9	1.65	-0.45	7.27
2,243.0	12.00	230.00	2,218.5	-172.2	-195.1	260.2	1.73	-1.14	6.14
2,287.0	11.70	233.30	2,261.6	-177.8	-202.2	269.2	1.68	-0.68	7.50
2,331.0	12.00	233.40	2,304.6	-183.2	-209.4	278.2	0.68	0.68	0.23
2,374.0	12.40	232.00	2,346.7	-188.7	-216.7	287.2	1.16	0.93	-3.26
2,418.0	13.00	231.50	2,389.6	-194.7	-224.2	296.9	1.39	1.36	-1.14
2,462.0	13.40	231.40	2,432.4	-200.9	-232.1	306.9	0.91	0.91	-0.23
2,505.0	13.00	231.40	2,474.3	-207.1	-239.8	316.7	0.93	-0.93	0.00
2,549.0	12.20	229.00	2,517.2	-213.2	-247.2	326.3	2.17	-1.82	-5.45
2,593.0	11.87	228.10	2,560.3	-219.3	-254.0	335.5	0.86	-0.75	-2.05
2,637.0	11.40	226.70	2,603.4	-225.3	-260.6	344.4	1.25	-1.07	-3.18
2,681.0	11.00	226.90	2,646.5	-231.1	-266.8	352.9	0.91	-0.91	0.45
2,725.0	10.60	227.00	2,689.7	-236.8	-272.8	361.2	0.91	-0.91	0.23
2,769.0	11.00	227.90	2,733.0	-242.3	-278.9	369.4	0.99	0.91	2.05
2,813.0	11.40	231.00	2,776.1	-247.9	-285.4	377.9	1.64	0.91	7.05
2,857.0	11.40	231.70	2,819.3	-253.3	-292.2	386.6	0.31	0.00	1.59
2,901.0	12.00	231.20	2,862.3	-258.9	-299.2	395.5	1.38	1.36	-1.14



Company:	NEWFIELD EXPLORATION	Local Co-ordinate Reference:	Well T-5-9-17
Project:	USGS Mylon SW (UT)	TVD Reference:	T-5-9-17 @ 5237.0ft (NDSI SS #2)
Site:	SECTION 4 T9S R17E	MD Reference:	T-5-9-17 @ 5237.0ft (NDSI SS #2)
Well:	T-5-9-17	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Actual	Database:	EDM 2003.21 Single User Db

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	N-S (ft)	E-W (ft)	Vertical Section (ft)	Dogleg Rate (%/100ft)	Build Rate (%/100ft)	Turn Rate (%/100ft)
2,944.0	11.40	229.00	2,904.5	-264.5	-305.8	404.2	1.74	-1.40	-5.12
2,988.0	11.80	225.30	2,947.6	-270.5	-312.3	413.1	1.92	0.91	-8.41
3,032.0	12.00	226.80	2,990.6	-276.8	-318.9	422.1	0.84	0.45	3.41
3,076.0	11.70	225.50	3,033.7	-283.0	-325.4	431.2	0.91	-0.68	-2.95
3,120.0	11.20	224.70	3,076.8	-289.2	-331.6	439.9	1.19	-1.14	-1.82
3,163.0	10.80	225.10	3,119.0	-295.0	-337.4	448.1	0.95	-0.93	0.93
3,207.0	11.20	226.70	3,162.2	-300.8	-343.4	456.5	1.14	0.91	3.64
3,251.0	11.70	229.50	3,205.3	-306.7	-349.9	465.2	1.70	1.14	6.36
3,295.0	11.80	229.10	3,248.4	-312.5	-356.7	474.2	0.29	0.23	-0.91
3,339.0	11.70	229.88	3,291.5	-318.3	-363.5	483.1	0.43	-0.23	1.77
3,382.0	11.70	229.90	3,333.6	-324.0	-370.2	491.8	0.01	0.00	0.05
3,426.0	12.00	228.40	3,376.6	-329.9	-377.0	500.9	0.98	0.68	-3.41
3,470.0	12.20	227.10	3,419.7	-336.1	-383.8	510.1	0.77	0.45	-2.95
3,514.0	12.20	227.50	3,462.7	-342.4	-390.7	519.4	0.19	0.00	0.91
3,558.0	11.90	227.20	3,505.7	-348.6	-397.4	528.6	0.70	-0.68	-0.68
3,601.0	12.00	228.60	3,547.8	-354.6	-404.0	537.5	0.71	0.23	3.26
3,645.0	11.40	228.00	3,590.9	-360.5	-410.7	546.4	1.39	-1.36	-1.36
3,689.0	12.10	229.00	3,633.9	-366.4	-417.4	555.4	1.66	1.59	2.27
3,733.0	12.50	230.00	3,676.9	-372.5	-424.5	564.7	1.03	0.91	2.27
3,777.0	11.70	229.80	3,719.9	-378.5	-431.6	574.0	1.82	-1.82	-0.45
3,820.0	11.80	228.10	3,762.0	-384.2	-438.2	582.7	0.84	0.23	-3.95
3,863.0	11.60	228.00	3,804.2	-390.0	-444.7	591.4	0.47	-0.47	-0.23
3,907.0	11.30	226.80	3,847.3	-396.0	-451.1	600.2	0.87	-0.68	-2.73
3,951.0	11.60	225.40	3,890.4	-402.0	-457.4	608.9	0.93	0.68	-3.18
3,995.0	12.30	225.40	3,933.5	-408.4	-463.9	618.0	1.59	1.59	0.00
4,039.0	12.00	225.70	3,976.5	-414.9	-470.5	627.2	0.70	-0.68	0.68
4,083.0	11.60	226.10	4,019.5	-421.2	-476.9	636.2	0.93	-0.91	0.91
4,126.0	11.10	227.30	4,061.7	-427.0	-483.1	644.7	1.29	-1.16	2.79
4,170.0	10.90	228.20	4,104.9	-432.6	-489.3	653.1	0.60	-0.45	2.05
4,214.0	11.30	227.20	4,148.1	-438.3	-495.6	661.6	1.01	0.91	-2.27
4,258.0	11.60	227.00	4,191.2	-444.3	-502.0	670.3	0.69	0.68	-0.45
4,302.0	11.40	225.80	4,234.3	-450.3	-508.3	679.1	0.71	-0.45	-2.73
4,346.0	11.10	223.90	4,277.5	-456.4	-514.4	687.6	1.08	-0.68	-4.32
4,389.0	11.10	223.50	4,319.7	-462.4	-520.1	695.9	0.18	0.00	-0.93
4,433.0	11.30	224.90	4,362.8	-468.5	-526.1	704.4	0.77	0.45	3.18
4,477.0	11.80	227.50	4,405.9	-474.6	-532.4	713.2	1.64	1.14	5.91
4,521.0	12.30	228.70	4,449.0	-480.7	-539.3	722.4	1.27	1.14	2.73
4,564.0	12.10	227.10	4,491.0	-486.8	-546.0	731.5	0.91	-0.47	-3.72
4,608.0	11.30	227.00	4,534.1	-492.9	-552.5	740.4	1.82	-1.82	-0.23
4,652.0	11.10	229.20	4,577.2	-498.6	-558.9	749.0	1.07	-0.45	5.00
4,696.0	11.20	230.70	4,620.4	-504.1	-565.4	757.5	0.70	0.23	3.41
4,740.0	11.30	228.10	4,663.6	-509.7	-571.9	766.0	1.17	0.23	-5.91
4,783.0	11.30	226.70	4,705.7	-515.4	-578.1	774.5	0.64	0.00	-3.26
4,827.0	11.20	225.00	4,748.9	-521.3	-584.3	783.0	0.79	-0.23	-3.86
4,871.0	10.90	224.70	4,792.1	-527.3	-590.2	791.5	0.69	-0.68	-0.68
4,915.0	10.59	225.10	4,835.3	-533.1	-596.0	799.7	0.72	-0.70	0.91
4,957.6	10.46	226.03	4,877.2	-538.6	-601.6	807.4	0.50	-0.30	2.18
T-5-9-17 TGT									
4,959.0	10.46	226.06	4,878.5	-538.8	-601.8	807.7	0.50	-0.29	2.21
5,002.0	10.50	227.64	4,920.8	-544.1	-607.5	815.5	0.67	0.09	3.67
5,046.0	10.63	226.85	4,964.1	-549.6	-613.4	823.6	0.44	0.30	-1.80
5,090.0	10.70	226.50	5,007.3	-555.2	-619.3	831.7	0.22	0.16	-0.80
5,134.0	11.03	228.03	5,050.5	-560.8	-625.4	840.0	1.00	0.75	3.48
5,177.0	11.07	231.00	5,092.7	-566.1	-631.7	848.2	1.33	0.09	6.91




Company:	NEWFIELD EXPLORATION	Local Co-ordinate Reference:	Well T-5-9-17
Project:	USGS Myton SW (UT)	VD Reference:	T-5-9-17 @ 5237.0ft (NDSI SS #2)
Site:	SECTION 4 T9S R17E	MD Reference:	T-5-9-17 @ 5237.0ft (NDSI SS #2)
Well:	T-5-9-17	North Reference:	True
Wellbore:	Wellbore #1	Survey Calculation Method:	Minimum Curvature
Design:	Actual	Database:	EDM 2003.21 Single User Db

Measured Depth (ft)	Inclination (°)	Azimuth (°)	Vertical Depth (ft)	+N/-S (ft)	+E/-W (ft)	Vertical Section (ft)	Dogleg Rate (°/100ft)	Build Rate (°/100ft)	Turn Rate (°/100ft)
5,221.0	10.50	232.50	5,136.0	-571.2	-638.1	856.5	1.44	-1.30	3.41
5,265.0	10.50	231.06	5,179.2	-576.2	-644.4	864.5	0.60	0.00	-3.27
5,309.0	10.50	229.30	5,222.5	-581.3	-650.6	872.5	0.73	0.00	-4.00
5,353.0	11.29	229.60	5,265.7	-586.7	-656.9	880.8	1.80	1.80	0.68
5,396.0	12.04	233.70	5,307.8	-592.1	-663.7	889.5	2.60	1.74	9.53
5,440.0	12.00	234.20	5,350.8	-597.5	-671.1	898.6	0.25	-0.09	1.14
5,484.0	12.66	233.20	5,393.8	-603.1	-678.7	907.9	1.58	1.50	-2.27
5,528.0	12.22	228.90	5,436.8	-609.0	-686.1	917.4	2.33	-1.00	-9.77
5,572.0	10.90	224.90	5,479.9	-615.0	-692.5	926.2	3.51	-3.00	-9.09
5,616.0	11.10	227.20	5,523.1	-620.9	-698.6	934.6	1.10	0.45	5.23
5,660.0	11.60	228.80	5,566.2	-626.7	-705.0	943.2	1.34	1.14	3.64
5,704.0	11.90	228.30	5,609.3	-632.6	-711.7	952.2	0.72	0.68	-1.14
5,748.0	12.10	225.40	5,652.4	-638.8	-718.4	961.3	1.44	0.45	-6.59
5,791.0	12.50	222.10	5,694.4	-645.5	-724.7	970.5	1.88	0.93	-7.67
5,835.0	12.50	222.90	5,737.3	-652.5	-731.2	979.9	0.39	0.00	1.82
5,879.0	11.80	222.50	5,780.3	-659.3	-737.4	989.2	1.60	-1.59	-0.91
5,923.0	11.20	222.30	5,823.5	-665.8	-743.4	997.9	1.37	-1.36	-0.45
5,967.0	10.68	223.55	5,866.7	-671.9	-749.0	1,006.2	1.30	-1.18	2.84
6,010.0	9.71	222.32	5,909.0	-677.5	-754.2	1,013.8	2.31	-2.26	-2.86
6,054.0	9.01	222.58	5,952.4	-682.7	-759.1	1,020.9	1.59	-1.59	0.59
6,098.0	8.75	221.48	5,995.9	-687.8	-763.6	1,027.7	0.71	-0.59	-2.50
6,142.0	8.17	221.48	6,039.4	-692.6	-767.9	1,034.1	1.32	-1.32	0.00
6,166.0	7.78	222.63	6,063.2	-695.1	-770.1	1,037.4	1.76	-1.63	4.79
6,220.0	6.90	225.22	6,116.7	-700.1	-774.9	1,044.3	1.74	-1.63	4.80




Checked By: _____ Approved By: _____ Date: _____

Project: USGS Myton SW (UT)
 Site: SECTION 4 T9S R17E
 Well: T-5-9-17
 Wellbore: Wellbore #1
 Design: Actual



Azimuths to True North
 Magnetic North: 11.19°
 Magnetic Field
 Strength: 52199.35nT
 Dip Angle: 65.79°
 Date: 4/30/2012
 Model: IGRF2010

Number: 43013514800000

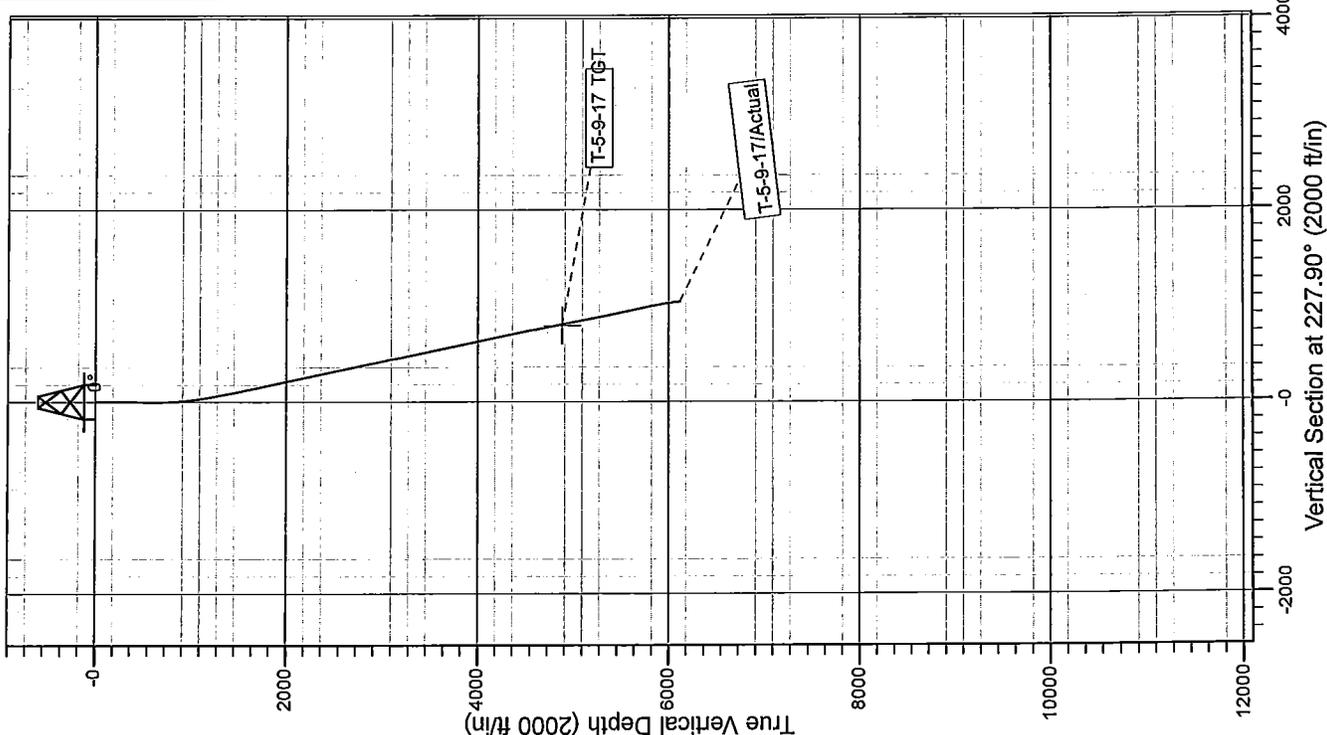

Design: Actual (T-5-9-17/Wellbore #1)
 Created By: Sarah Webb Date: 9:38, February 14 2012

THIS SURVEY IS CORRECT TO THE BEST OF MY KNOWLEDGE AND IS SUPPORTED BY ACTUAL FIELD DATA

RECEIVED: Jun. 28, 2013

Daily Activity Report**Format For Sundry****GMBU T-5-9-17****1/1/2013 To 5/30/2013****2/21/2013 Day: 1****Completion**

Rigless on 2/21/2013 - Run CBL, Cement top @ 552', Test Csg, BOPE, Frac valve & 2- outer gate valves (All good), Perf 1 st stg, CP5-4 Formation - RU The Perforators WLT, MU & RIH w/ 3 1/8" Disposable slick guns (16g, 0.34 EH, 21.00 pen) & perforate CP-5,4 formation @ 5890'-92', 5806'-10', 5797'-98', POOH w/ W/L, LD guns, All fired, RD W/L, Dump 10 gal of diesel down csg for freeze blanket, SWIFWE. RDMO B&C testers and The Perforators WLT. - B&C failed to show up on time. Wait on testers to show up and then wait on them to deliver 1000# chart recorder. - MIRU The Perforators WLT, MU & RIH w/ logging tools, Tag @ 6134", (PBSD @ 6162'), Log out of hole w/ 0 psi on well, Cement top @ 552', Log short jt @ 3505.5'-15.5', LD logging tools. - Safety Meeting, discussed location hazards, recent NFX incidents, job procedure, emergency plans, meeting point. - RU B&C Test unit, Dead head test unit, Test hyd. chambers on BOP (2800 psi on acc.), Test csg, Frac valve & inner gate valve to 250 psi 5-min low & 4,300 psi 30-min high, Shut BOP & lock rams w/ 1600 psi on acc. manifold. Bleed off & vent acc, Test BOP & outer gate valve to 250 psi 5-min low & 4,300 psi 10-min high, All tests good.

Daily Cost: \$0**Cumulative Cost:** \$31,962**2/22/2013 Day: 2****Completion**

Rigless on 2/22/2013 - Frac 5 stgs as detailed. Stage 5 screened out with 6# on perfs. Flowback well. - Held safety meeting with all parties involved. Topics of discussions: PPE, stop work authority, smoking area, muster area, evacuation plan, overhead loads & working around pressure. - Open well for immediate flowback @ approx 3 BPM. Well flowed for 3 hours & turned to oil. Recovered approx 500 bbls. SWIFN. - Stage #5, GB2 sands. 1477 psi on well. Frac GB2 sds w/ 41,940#'s of 20/40 sand in 233 bbls of Delta 140 fluid. Ave temp of frac fluid: 67? Broke @ 3378 psi @ 4.8 BPM. Treated w/ ave pressure of 2593 psi @ ave rate of 24.7 BPM. Screened out with 183 sks left in wellbore. - Stage #4, LODC sands. 1437 psi on well. Frac LODC sds w/ 99,510#'s of 20/40 sand in 566 bbls of Delta 140 fluid. Ave temp of frac fluid: 67? Broke @ 3378 psi @ 4.8 BPM. Treated w/ ave pressure of 2523 psi @ ave rate of 41.1 BPM. Pumped 500 gals of 15% HCL in flush for Stage #5. ISDP 2679 psi. FG=.95, 5 min SIP 1966 psi, 10 min SIP 1713 psi, 15 min SIP 1633 psi. Leave pressure on well. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 5K composite flow through frac plug & perf guns. Set plug @ 4260'. Perforate GB2 sds @ 4183-87' w/ 3 1/8" slick guns (16 gram .34" EH 21.00" pen) w/ 3 spf for total of 12 shots. 2564 total BWTR - Stage #1, CP5,4 sands. 0 psi on well. Frac CP5,4 sds w/ 90,220#'s of 20/40 sand in 520 bbls of Delta 140 fluid. Ave temp of frac fluid: 67? Broke @ 2973 psi @ 5.8 BPM. ISIP 1068 psi, FG=.63, 1 min SIP 818 psi, 4 min SIP 584 psi. Treated w/ ave pressure of 2533 psi @ ave rate of 38.6 BPM. Pumped 611 gals of 15% HCL in flush for Stage #2. ISDP 1656 psi. FG=.74, 5 min SIP 1392 psi, 10 min SIP 1353 psi, 15 min SIP 1327 psi. Leave pressure on well. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 5K composite flow through frac plug & perf guns. Set plug @ 5760'. Perforate CP3,2 sds @ 5716-18', 5713-14', 5673-75' w/ 3 1/8" slick guns (16 gram .34" EH 21.00" pen) w/ 3 spf for total of 21 shots. 782 total BWTR - Stage #3, LODC sands. 1221 psi on well. Frac LODC sds w/ 94,940#'s of 20/40 sand in 547 bbls of Delta 140 fluid. Ave temp of frac fluid: 67? Broke @ 3308 psi @ 4.8 BPM. Treated w/ ave pressure of 2153 psi @ ave rate of 40.4 BPM. Pumped 500 gals of 15% HCL in flush for Stage #4. ISDP 1850 psi. FG=.79, 5 min SIP 1696 psi, 10 min SIP 1639 psi, 15 min SIP 1586 psi. Leave pressure on well. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-

1/2" 5K composite flow through frac plug & perf guns. Set plug @ 5415'. Perforate LODC sds @ 5382-84', 5374-76', 5359-61', 5340-41' w/ 3 1/8" slick guns (16 gram .34" EH 21.00" pen) w/ 3 spf for total of 21 shots. 1856 total BWTR - Stage #2, CP3,2 sands. 1294 psi on well. Frac CP3,2 sds w/ 30,090#'s of 20/40 sand in 209 bbls of Delta 140 fluid. Ave temp of frac fluid: 67? Broke @ 3677 psi @ 4.9 BPM.. Treated w/ ave pressure of 3342 psi @ ave rate of 26.1 BPM. Pumped 500 gals of 15% HCL in flush for Stage #3. ISDP 2156 psi. FG=.83, 5 min SIP 1372 psi, 10 min SIP 1338 psi, 15 min SIP 1337 psi. Leave pressure on well. RU Perforators WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" 5K composite flow through frac plug & perf guns. Set plug @ 5560'. Perforate LODC sds @ 5497-5500', 5471-74', 5462-63' w/ 3 1/8" slick guns (16 gram .34" EH 21.00" pen) w/ 3 spf for total of 21 shots. 1151 total BWTR

Daily Cost: \$0

Cumulative Cost: \$40,693

3/1/2013 Day: 3

Completion

WWS #1 on 3/1/2013 - MOWOR. Set KP. ND Frac vlv, NU BOPs, test BOPs. - RU The Perforators WLT. RIH to set KP @ 4138'. POOH and RD WLT. - BD w/ steady stream of wtr while crew broke for lunch. - RU WFD test unit. Test hyd chambers w/ 2800 psi on the accumulator for five minutes each test. All tested good. Prep tally and drift tbg on rack. RU work floor and tbg equipment. Install tbg hanger with bleed nipple and TIW vlv. Tested BOP pipe rams 250 low for 5 min and 4500 for 10 min. No test. Uninstalled hanger and pulled out back pressure valve. Installed bull plug and reinstalled hanger. Retested pipe rams. Test TIW valve & 2-1/16" manual valves 250 low for 5 min and 4500 high for 10 min. -Good test. Uninstall hanger and remove bull plug. SWIFN - Held safety meeting with all parties involved. Topics of discussions: PPE, stop work authority, smoking area, muster area, evacuation plan, overhead loads & working around pressure. - ND Frac vlv, NU DO BOPs. Set pipe racks and unload tbg w/ fork lift. - Spot rig up on WH. SICP @ 700 psi. Open well up to the pit. RU WOR.

Daily Cost: \$0

Cumulative Cost: \$160,009

3/4/2013 Day: 4

Completion

WWS #1 on 3/4/2013 - RIH to DO/CO through last plg. EOT @ 5777'. - Safety Meeting, discussed location hazards, recent NFX incidents, job procedure, emergency plans, meeting point. - RIH w/ 4 3/4" chomp bit, 2 7/8" tbg off rack. W/ 40 jts in, RU pump and lines. Circ oil out if well w/ 40 bbls. Cont to PU pipe. - Tagged up on KP @ 4138' w/ 132 jts in. - RU nabors pwr swvl. - DO frac plg 1 in 19 min. Circ well cln and then hang back pwr swvl. Cont to PU pipe. Tag fill @ 5308' w/ jt 169. - RU pwr swvl and CO to frac plg 2 @ 5415' w/ jt 173. - DO frac plg 2 in 16 min. Circ well cln and swvl in pipe to tag fill @ 5480' w/ jt 175. - CO to Frac plg 3 @ 5580' w/ 178'. DO in 22 min. - Circ well cln and cont to RIH off swvl to tag frac plg 4 @ 5760'. Catch circ and DO frac plg 4 in 20 min. - Circ well cln, SWIFN, Drain pump and lines and SDFN. EOT @ 5777'. - Catch circ and DO KP in 32 min. Circ well clean, then swvl in pipe to tag frac plg 1 @ 4270' w/ jt 136.

Daily Cost: \$0

Cumulative Cost: \$167,574

3/5/2013 Day: 5

Completion

WWS #1 on 3/5/2013 - CO to PBTD. Circ cln and POOH. RBIH w/ production tbg and land tbg w/ 18K tension. NU WH and prep rods. - SICP @ 350 psi, SITP @ 300 psi. RU pump and and circ well w/60 bbls. - Safety Meeting, discussed location hazards, recent NFX incidents, job procedure, emergency plans, meeting point. - CO to PBTD @ 6162' w/ jt 197. - Circ well cln -

SD pump, LD pwr swvl. LD 8 jts. - POOH w/ 189 jts and 4 3/4" chomp bit. - TIH w/ NC, 2 jts, SN, 1 jt, 5.5" TAC w/ carbide slips, and 186 jts. - CSG flowing. RU pump and circ w/ 100 bbls. - SD pump and land tbg w/ hanger. RD floor, ND BOP stack. - PU an tbg and set TAC @ 5850' w/ 18,000# tension and land w/ tbg hanger. NU WH and X-over to rod equipment. Prep rod string.SWIFN. - Cont. to PU pipe to tag fill @ 6029'.

Daily Cost: \$0

Cumulative Cost: \$174,756

3/6/2013 Day: 6

Completion

WWS #1 on 3/6/2013 - Run pump and rods. Test pump. PWOP. - SICP @ 300 psi, SITP @ 200 psi. Flush tbg w/ 60 bbls. - PU and prime new Central Hyd 25-1.75-RHAC-20-4-21-24' pump, 28- 7/8" 8 pers, 134- 3/4" 4 pers, 72- 7/8" 4 pers, 1-4' X 7/8" pony, 1-2' X 7/8" pony. Seat pump w/ 1 1/2" X 30' polish rod. Load hole w/ wtr. Hang head. - Stroke test the tbg up to 800 psi - good test. RDMOWOR. PWOP 144' SL @ 5 SPM. - Safety Meeting, discussed location hazards, recent NFX incidents, job procedure, emergency plans, meeting point.

Daily Cost: \$0

Cumulative Cost: \$258,961

Pertinent Files: Go to File List
