

UTAH OIL AND GAS CONSERVATION COMMISSION

REMARKS: WELL LOG ELECTRIC LOGS X WATER SANDS LOCATION INSPECTED SUB. REPORT/abd.

DATE FILED JANUARY 12, 1996

LAND: FEE & PATENTED STATE LEASE NO. PUBLIC LEASE NO. U-67170 INDIAN

DRILLING APPROVED: FEBRUARY 13, 1996

SPUDDED IN: MARCH 18, 1996

COMPLETED: 4-23-96 PDW PUT TO PRODUCING: 4-23-96

INITIAL PRODUCTION: 149 BOPD; 94 MCF; 3 BOPD

GRAVITY A.P.I.

GOR: .63

PRODUCING ZONES: 5482-5485 (GRRV)

TOTAL DEPTH: 6250'

WELL ELEVATION: 5438' GR

DATE ABANDONED:

FIELD: MONUMENT BUTTE

UNIT:

COUNTY: DUCHESNE

WELL NO. MONUMENT BUTTE FEDERAL 3-25 API NO. 43-013-31605


LOCATION 756 FNE FT. FROM (N) (S) LINE. 1946 FWL FT. FROM (E) (W) LINE. NE NW 1/4 - 1/4 SEC. 25

TWP.	RGE.	SEC.	OPERATOR	TWP.	RGE.	SEC.	OPERATOR
8S	16E	25	INLAND PRODUCTION CO				

GEOLOGIC TOPS:

QUATERNARY	Star Point	Chinle	Molas
Alluvium	Wahweap	Shinarump	Manning Canyon
Lake beds	Masuk	Moenkopi	Mississippian
Pleistocene	Colorado	Sinbad	Humbug
Lake beds	Sego	PERMIAN	Brazer
TERTIARY	Buck Tongue	Kaibab	Pilot Shale
Pliocene	Castlegate	Coconino	Madison
Salt Lake	Mancos	Cutler	Leadville
Oligocene	Upper	Hoskinnini	Redwall
Norwood	Middle	DeChelly	DEVONIAN
Eocene	Lower	White Rim	Upper
Duchesne River	Emery	Organ Rock	Middle
Uinta	Blue Gate	Cedar Mesa	Lower
Bridger	Ferron	Halgaite Tongue	Ouray
Green River	Frontier	Phosphoria	Elbert
Garden Gulch Mkr 4404'	Dakota	Park City	McCracken
Point 3 Mkr 4410'	Burro Canyon	Rico (Goodridge)	Aneth
" " Mkr 4046'	Cedar Mountain	Supai	Simonson Dolomite
" " Mkr 4080'	Buckhorn	Wolfcamp	Sevy Dolomite
DOUGLAS CR Mkr 5100'	JURASSIC	CARBON I FEROUS	North Point
Big Arbonak Mkr 5320'	Morrison	Pennsylvanian	SILURIAN
Stone Cabin 5" Limestone Mkr 5500'	Salt Wash	Oquirrh	Laketown Dolomite
Wash Castle Peak 6024'	San Rafael Gr.	Weber	ORDOVICIAN
Flagstaff	Summerville	Morgan	Eureka Quartzite
North Horn	Bluff Sandstone	Hermosa	Pogonip Limestone
Almy	Curtis		CAMBRIAN
Paleocene	Entrada	Pardox	Lynch
Current Creek	Moab Tongue	Ismay	Bowman
North Horn	Carmel	Desert Creek	Tapeats
CRETACEOUS	Glen Canyon Gr.	Akah	Ophir
Montana	Navajo	Barker Creek	Tintic
Mesaverde	Kayenta		PRE - CAMBRIAN
Price River	Wingate	Cane Creek	
Blackhawk	TRIASSIC		

T8S, R16E, S.L.B.&M.

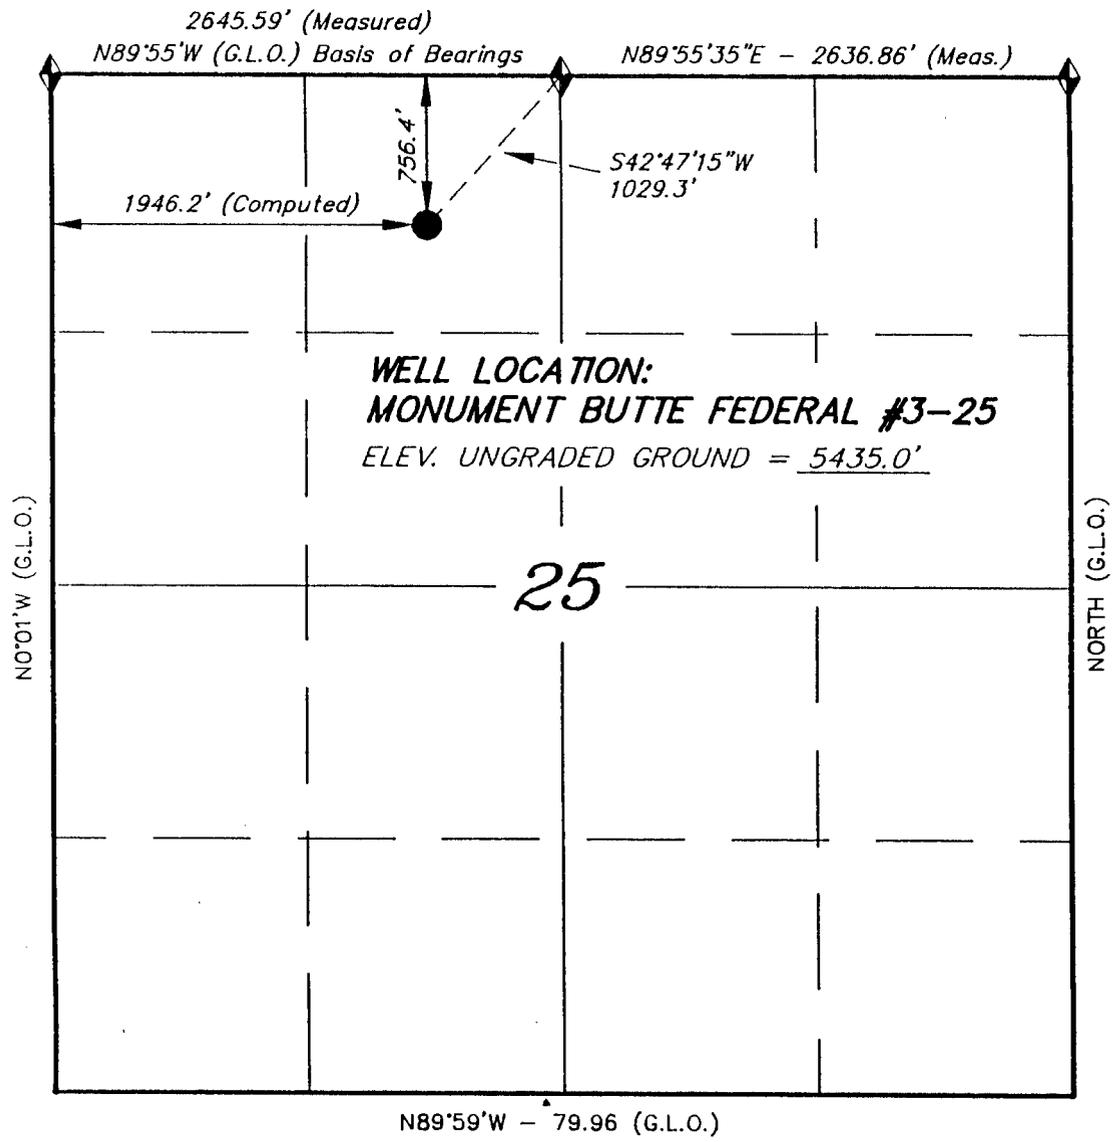

WELL LOCATION:
MONUMENT BUTTE FEDERAL #3-25
 ELEV. UNGRADED GROUND = 5435.0'


25

INLAND PRODUCTION COMPANY

WELL LOCATION, MONUMENT BUTTE FEDERAL #3-25, LOCATED AS SHOWN IN THE NE 1/4 NW 1/4 OF SECTION 25, T8S, R16E, S.L.B.&M. DUCHESNE COUNTY, UTAH.



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.



TRI STATE LAND SURVEYING & CONSULTING	
38 WEST 100 NORTH - VERNAL, UTAH 84078 (801) 781-2501	
SCALE: 1" = 1000'	SURVEYED BY: S.S. G.S.
DATE: 12-14-95	WEATHER: COLD
NOTES:	FILE #

◆ = SECTION CORNERS LOCATED
 BASIS OF ELEV; U.S.G.S. 7-1/2 min QUAD (MYTON SE)

**MONUMENT BUTTE FEDERAL #3-25
NE/NW SEC. 25, T8S, R16E
DUCHESNE COUNTY, UTAH
U-67170**

HAZARDOUS MATERIAL DECLARATION

INLAND PRODUCTION COMPANY guarantees that during the drilling & completion of the above referenced well, we will not use, produce, store, transport or dispose 10,000# annually of any of the hazardous chemicals contained in the Environmental Protection Agency's consolidated list of chemicals subject to reporting under Title III Superfund Amendments and Reauthorization Act (SARA) of 1986.

INLAND PRODUCTION COMPANY guarantees that during the drilling and completion of the above referenced well, we will use, produce, store, transport or dispose less than the threshold planning quantity (T.P.Q.) of any extremely hazardous substances as defined in 40 CFR 355.

**INLAND PRODUCTION COMPANY
MONUMENT BUTTE FEDERAL #3-25
NE/NW SECTION 25, T8S, R16E
DUCHESNE COUNTY, UTAH**

TEN POINT WELL PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta	0' - 3030'
Green River	3030'
Wasatch	6500'

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation 3030' - 6400' - Oil

4. PROPOSED CASING PROGRAM

8 5/8", J-55, 24# w/ ST&C collars; set at 300' (New)
5 1/2", J-55, 15.5# w/ LT&C collars; set at TD (New)

5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:

The operators minimum specifications for pressure control equipment are as follows:

A 8" Series 900 Hydril Bag type BOP and a 8" Double Ram Hydraulic unit with a closing unit will be utilized. Function test of BOPS's will be checked daily.

(See Exhibit F)

6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:

It is proposed that the hole be drilled with fresh water to the Green River Formation @ approximately 3030', and with mud thereafter. The mud system will be a water based gel-chemical, weighted to 10.0 ppg as necessary for gas control.

7. AUXILIARY SAFETY EQUIPMENT TO BE USED:

Auxiliary safety equipment will be a Kelly Cock, bit float, and a TIW valve with drill pipe threads.

8. TESTING, LOGGING AND CORING PROGRAMS:

No drill stem testing has been scheduled for this well. It is anticipated at this time that the logging will consist of a Dual Induction Laterolog, Compensated Neutron-Formation Density Log. Logs will run from TD to 3500'. The cement bond log will be run from PBTD to cement top. The use of mud loggers to be determined at a later date.

9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:

The anticipated bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered; nor that any other abnormal hazards such as H₂S will be encountered in this area.

10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:

It is anticipated that the drilling operations will commence in the 2nd Quarter, 1996 and take approximately eight days to drill.

**INLAND PRODUCTION COMPANY
MONUMENT BUTTE FEDERAL #3-25
NE/NW SECTION 25, T8S, R16E
DUCHESNE COUNTY, UTAH**

THIRTEEN POINT WELL PROGRAM

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Inland Production Company well location site Monument Butte Federal #3-25 located in the NE 1/4 NW 1/4 Section 25, T8S, R16E, S.L.B. & M. Duchesne County, Utah:

Proceed westerly out of Myton, Utah along Highway 40 - 1.5 miles \pm to the junction of this highway and Utah State Highway 53; proceed southerly along Utah State Highway 53 - 7.6 \pm miles to the beginning of the proposed access road for the Monument Butte Federal #1-25, and the Monument Butte Federal #2-25; proceed westerly .8 miles to the access road off of the Monument Butte Federal #3-25. If the Monument Butte Federal #1-25, and the #2-25 have not been drilled before the #3-25, the access road to the Monument Butte Federal #3-25 would be 1.6 miles. Leave Highway 53 in the NW/NW of Sec. 30. See Exhibit B.

The highways mentioned in the foregoing paragraph are bituminous surfaced roads to the point where the proposed access road exits to the west. The highways are maintained by Utah State road crews. All other roads are maintained by County Crews.

The aforementioned dirt oilfield service roads and other roads in the vicinity are constructed out of existing native materials that are prevalent to the existing area they are located in and range from clays to a sandy-clay shale material.

The roads required for access during the drilling, completion and production phase will be maintained at the standards required by the BLM or other controlling agencies. This maintenance will consist of some minor grader work for smoothing road surfaces and for snow removal.

2. PLANNED ACCESS ROAD

See Topographic Map "B".

The planned access road leaves the existing location described in Item #1 in the NW 1/4 NE 1/4 Section 25, T8S, R16E, S.L.B. & M., and proceeds in a westerly direction approximately .8 miles \pm , to the proposed location site.

The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is determined necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%.

There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road.

There are no fences encountered along this proposed road. There will no new gates or cattle guards required.

All construction material for this access road will be borrowed material accumulated during construction of the access road.

3. LOCATION OF EXISTING WELLS

There are seven (7) producing, Inland Production wells and one (1) unknown P&A well within a one (1) mile radius. See Exhibit "D".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

There are no existing facilities that will be used by this well.

It is anticipated that this well will be a producing oil well.

Upon construction of a tank battery the well pad will be surrounded by a dike of sufficient capacity to contain at minimum the entire contents of the largest tank within the facility battery.

Tank batteries will be built to BLM specification.

All permanent (on site for six (6) months or longer) structures constructed or installed (including pumping units) will be painted Desert Tan. All facilities will be painted within six months of installation.

5. LOCATION AND TYPE OF WATER SUPPLY

At the present time, it is anticipated that the water for this well will be transported through a temporary surface pipeline from our pre-approved Inland Production Company fresh water supply line located at the Monument Butte Federal #5-35 (SW/NW Sec. 35, T8S, R16E) location as indicated on Topographic Map - Exhibit "C".

In the event this water source is not used an alternate source will be used and all the necessary arrangements will be made with the proper authorities.

There will be no water well drilled at this site.

6. SOURCE OF CONSTRUCTION MATERIALS

See Location Layout Sheet - Exhibit "E".

All construction material for this location shall be borrowed material accumulated during construction of the location site and access road. (Pit lining material is referred to in Item #7.)

A mineral material application is not required for this location.

A mineral material application is not required for this location.

7. METHODS FOR HANDLING WASTE DISPOSAL

See Location Layout Sheet - Exhibit "E".

If the reserve pit is lined, it will be constructed and lined with a plastic nylon reinforced line so as not to leak, break, or allow discharge. It will be a minimum of 12 mil thickness with sufficient bedding (either straw or dirt) to cover any rocks. The line will overlap the pit wall and be covered with dirt and/or rocks to hold it in place. No trash, scrap pipe, etc., that could puncture the liner will be disposed on in the pit.

After first production, produced water will be confined to a pit or storage tank for a period not to exceed one hundred twenty (120) days. During the one hundred twenty (120) day period, in accordance with the onshore order #7, an application for approval of permanent disposal method and location, along with required water analysis, shall be submitted for the Authorized Officers approval.

A portable toilet will be provided for human waste.

A trash basket will be provided for garbage (trash) and hauled away to an approved disposal site at the completion of the drilling activities.

8. ANCILLARY FACILITIES

There are no ancillary facilities planned for at the present time and none foreseen in the near future.

9. WELL SITE LAYOUT

See attached Location Layout Sheet - Exhibit "E".

The reserve pit will be located on the south side between stakes 4 & 5.

There will be no flare pit on this location.

The stockpiled topsoil (first six (6) inches) will be stored near the west corner near stake #7.

Access to the well pad will be from the northeast corner between stakes 2 & 3.

The northeast corner will be rounded to avoid excess fill and drainage.

Fencing Requirements

All pits will be fenced according to the following minimum standards:

- b) The net wire shall be not more than two (2) inches above the ground. The barbed wire shall be three (3) inches above the net wire. Total height of the fence shall be at least forty-two (42) inches.
- c) Corner posts shall be cemented and/or braced in such a manner to keep tight at all times.
- d) Standard steel, wood or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than sixteen (16) feet.
- e) All wire shall be stretched, by using a stretching device, before it is attached to the corner posts.

The reserve pit fencing will be on three (3) sides during drilling operations and on the fourth side when the rig moves off location. Pits will be fenced and maintained until cleanup.

10. PLANS FOR RESTORATION OF SURFACE

a) *Producing Location*

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, material, trash and junk not required for production.

If a plastic nylon reinforced liner is used, it shall be torn and perforated before back filling of the reserve pit.

The reserve pit and that portion of the location not needed for production facilities/operations will be re contoured to the approximated natural contours. The reserve pit will be reclaimed within one hundred twenty (120) days from the date of well completion. Before any dirt work takes place, the reserve pit must have all fluids and hydrocarbons, all cans, barrels, pipe, etc., removed.

When the drilling and completion phase ends, reclamation of unused disturbed areas on the well pad/access road no longer needed for operations, such as cut slopes, and fill areas will be accomplished by grading, leveling and seeding as recommended by the Authorized Officer. The seed mixture will be per B.L.M. and stated in the conditions of approval.

b) *Dry Hole Abandoned Location*

At such time as the well is plugged and abandoned, the operator shall submit a subsequent report of abandonment and the B.L.M. will attach the appropriate surface rehabilitation conditions of approval.

11. SURFACE OWNERSHIP - Bureau Of Land Management

12. OTHER ADDITIONAL INFORMATION

- a) Inland Production Company is responsible for informing all persons in the area who are associated with this project that they will be subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, Inland is to immediately stop work that might further disturb such materials, and contact the Authorized Officer.
- b) Inland Production will control noxious weeds along rights-of-way for roads, pipelines, well sites, or other applicable facilities. On B.L.M. administered land it is required that a Pesticide Use Proposal shall be submitted, and given approval, prior to the application of herbicides or other possible hazardous chemicals.
- c) Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on Federal Lands after the conclusion of drilling operations or at any other time without B.L.M. authorization. However, if B.L.M. authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

The Cultural Resource Survey is attached.

Additional Surface Stipulations

All lease and/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws and regulations. Onshore Oil and Gas Orders, the approved plan of operations, and any applicable Notice to Lessees. Inland Production is fully responsible for the actions of its subcontractors. A copy of these conditions will be furnished to the field representative to insure compliance.

A complete copy of the approved APD, if applicable, shall be on location during the construction of the location and drilling activities.

Inland Production Company or a contractor employed by Inland Production shall contact the B.L.M. office at (801) 789-1362, 48 hours prior to construction activities.

The B.L.M. office shall be notified upon site completion prior to moving on the drilling rig.

13. LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION

Representative

Name: Brad Mecham
Address: P.O. Box 1446 Roosevelt, Utah 84066
Telephone: (801) 722-5103


Certification

Please be advised that INLAND PRODUCTION COMPANY is considered to be the operator of Well #3-25 NE/NW Section 25, Township 8S, Range 16E: Lease #U-67170 ; Duchesne County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by Hartford Accident #4488944.


I hereby certify that I, or persons under my direct supervision have inspected the proposed drill site and access route; that I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Inland Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

1-11-96

Date



Brad Mecham
Operations Manager

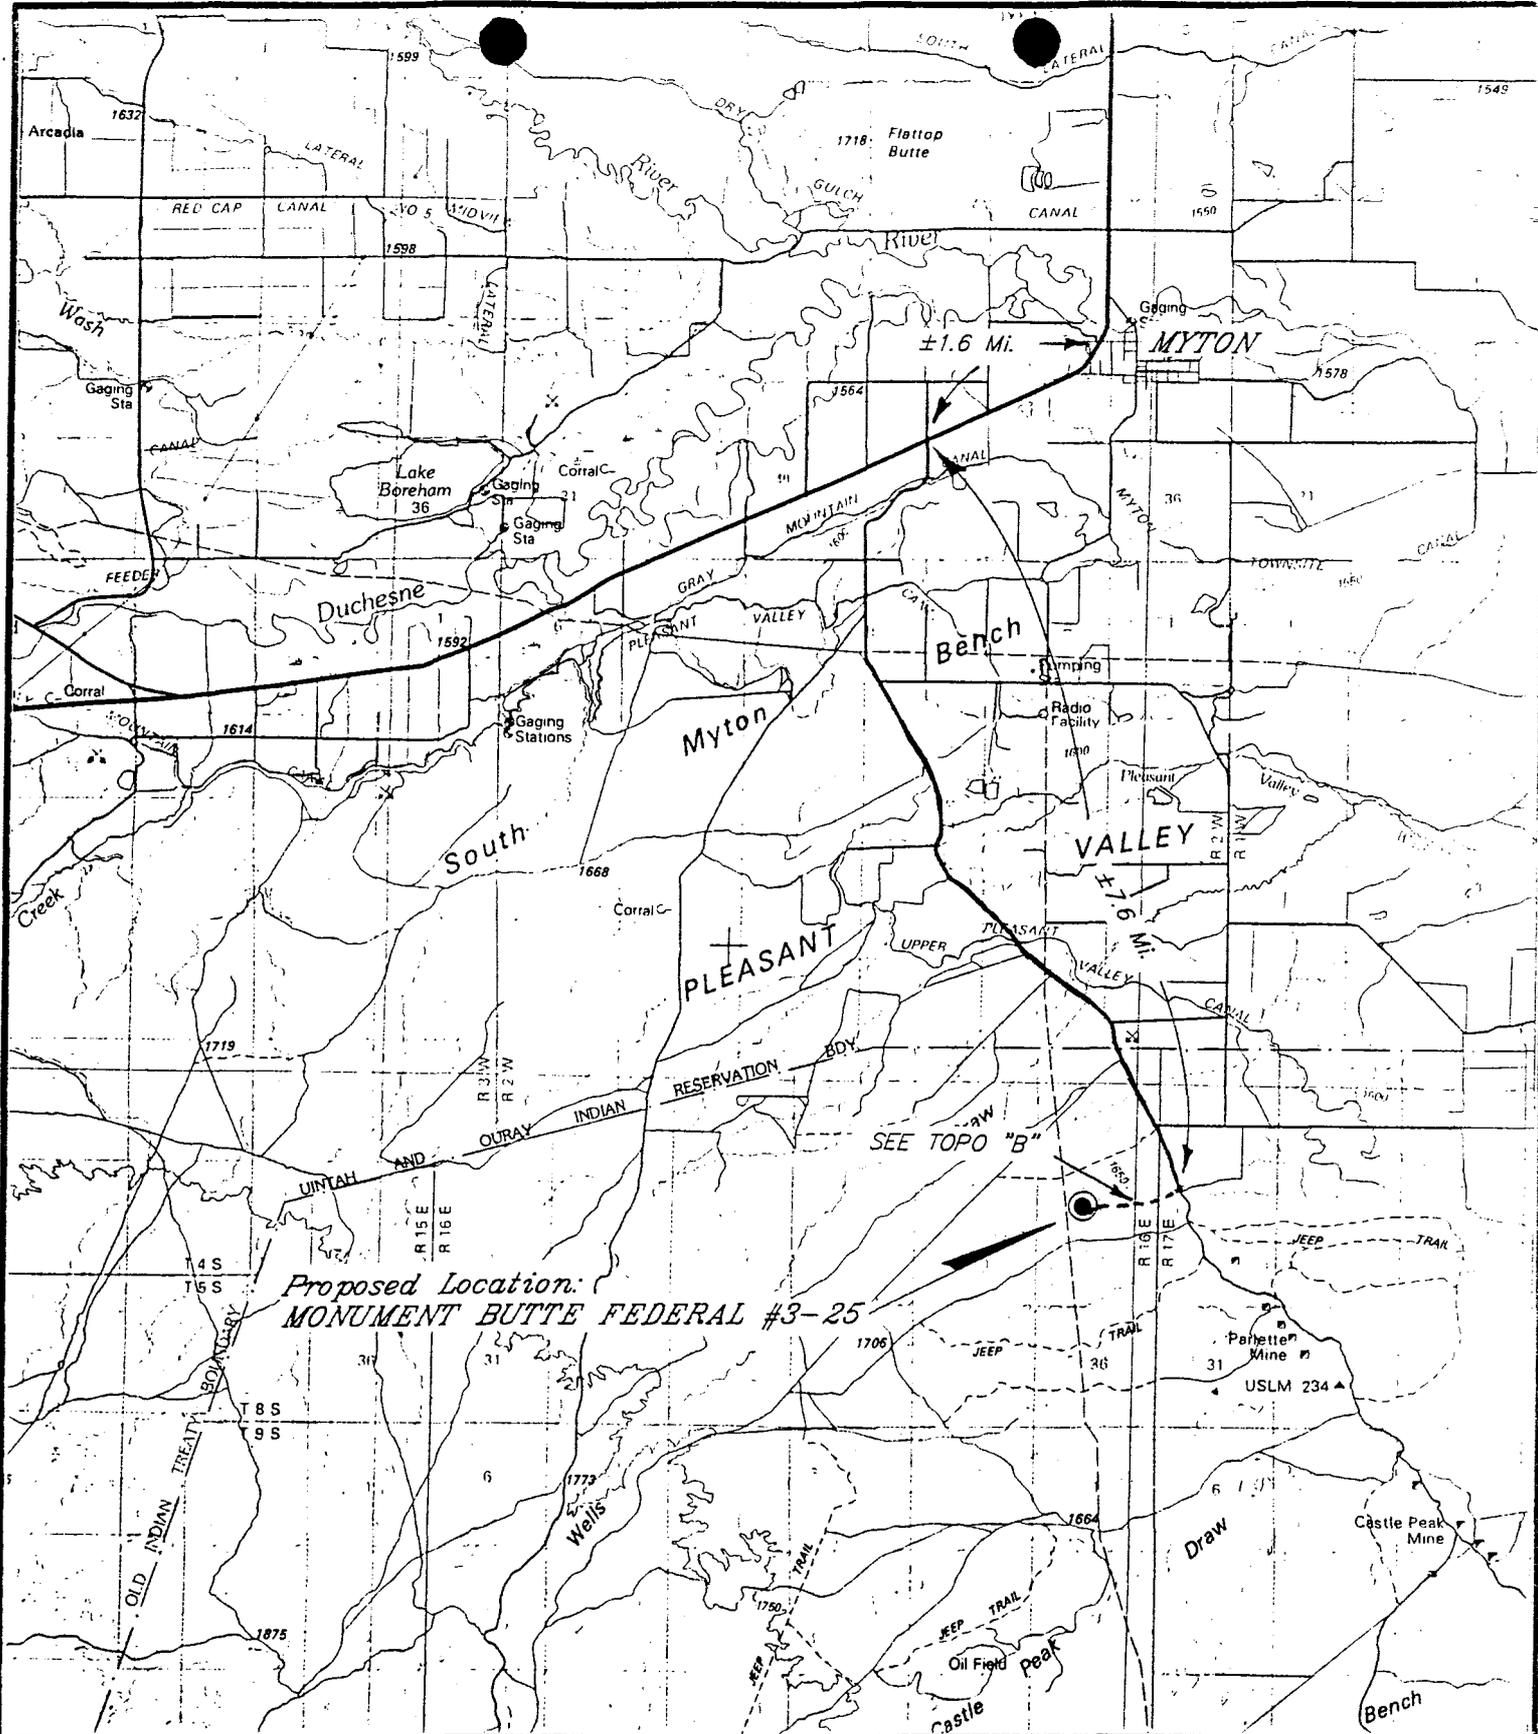


Proposed Location:
MONUMENT BUTTE FEDERAL #3-25

INLAND PRODUCTION COMPANY
 MONUMENT BUTTE FEDERAL #3-25
 SEC. 25, T8S, R16E, S.L.B.&M.
 TOPO "A"



Tri State
 Land Surveying, Inc.
 (801) 781-2501
 38 WEST 100 NORTH VERNAL, UTAH 84078

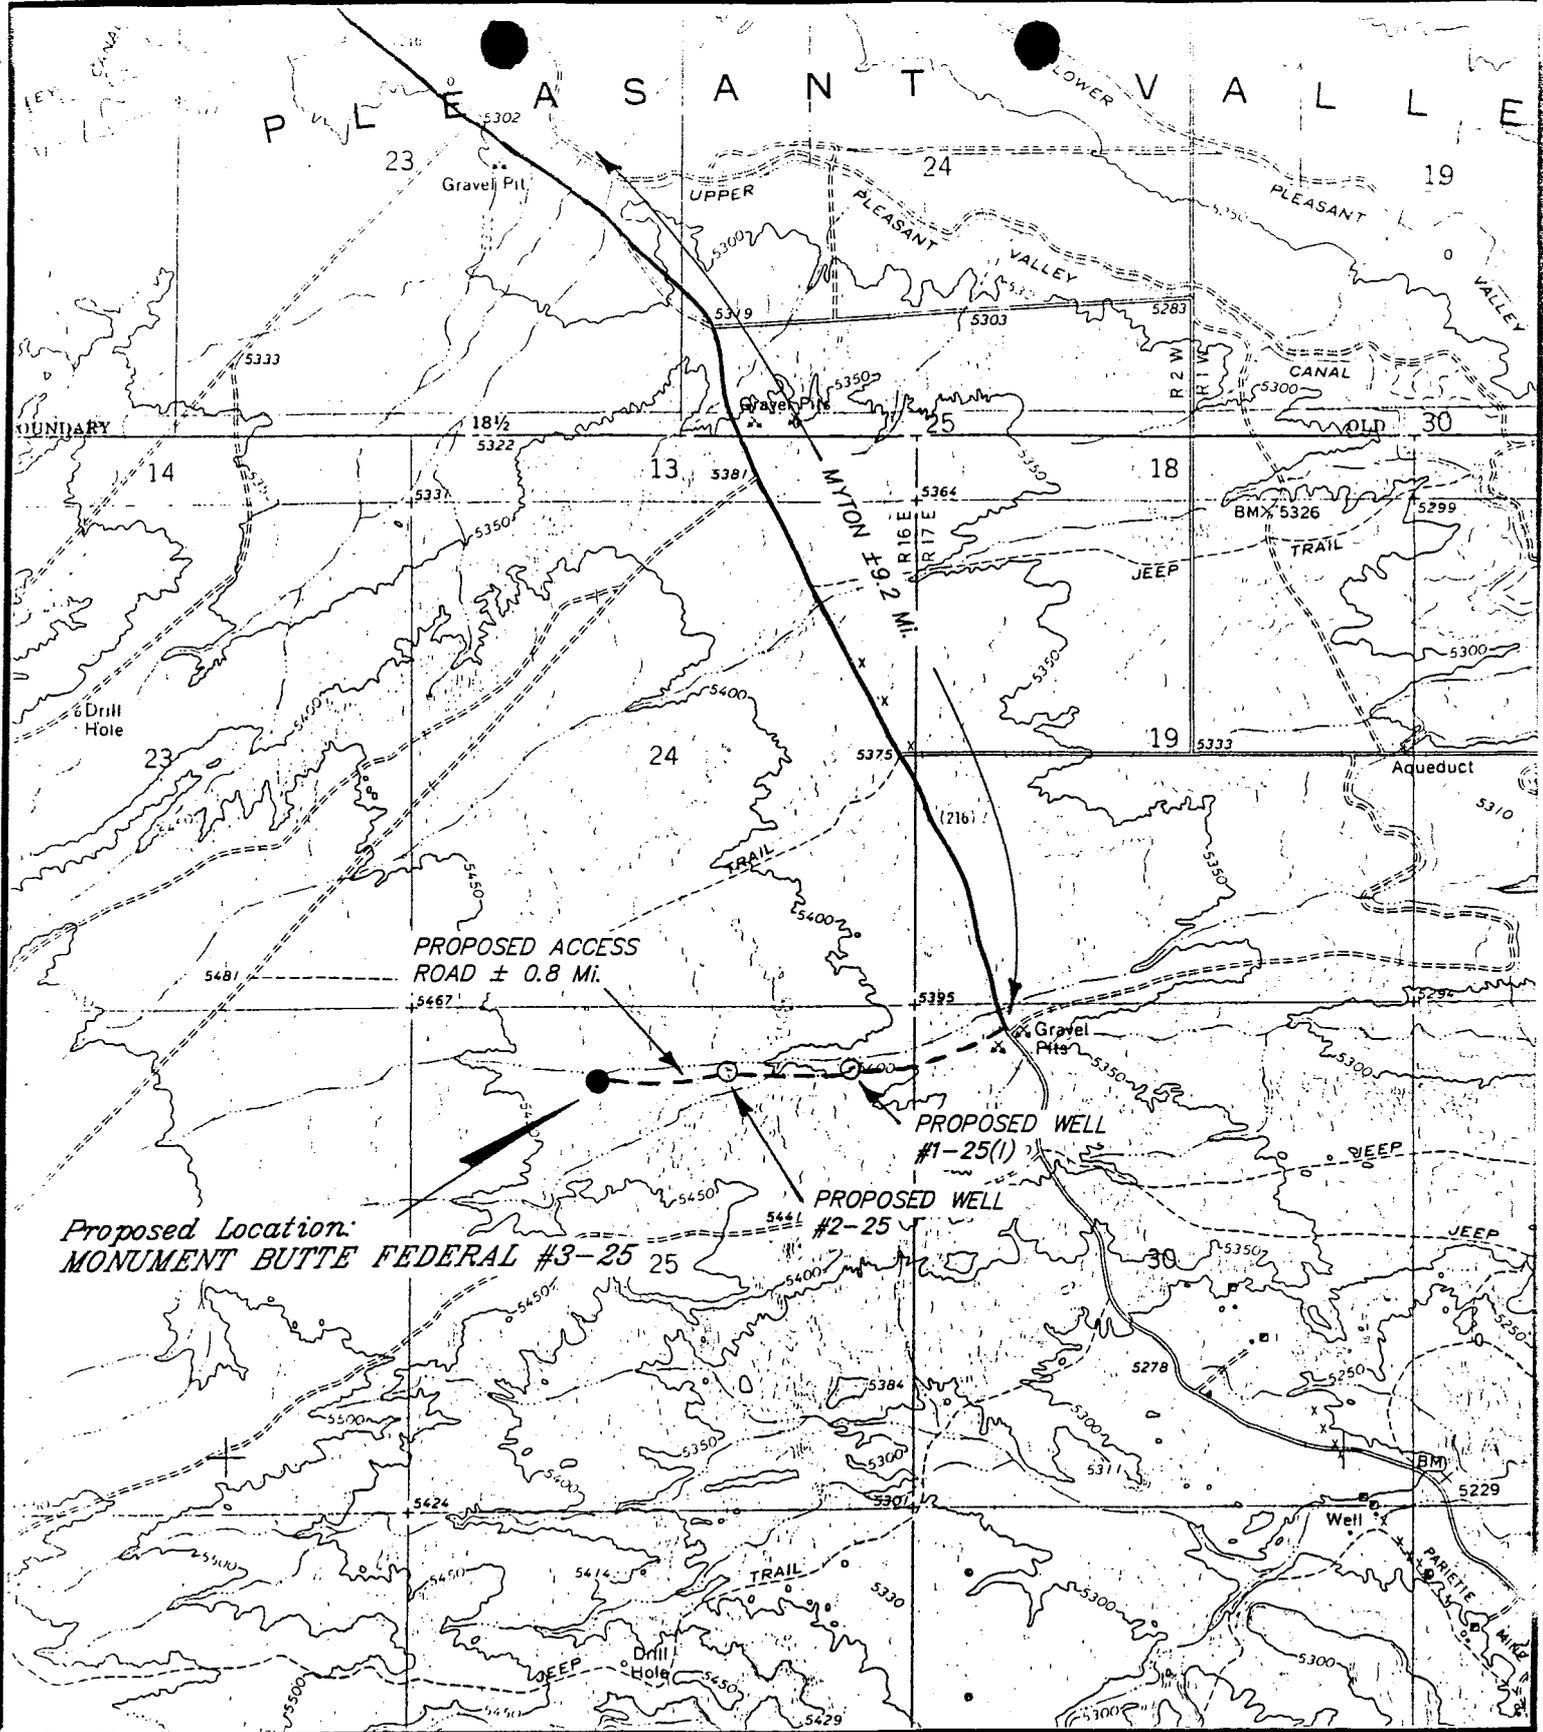

*Proposed Location:
MONUMENT BUTTE FEDERAL #3-25*

*PROPOSED ACCESS
ROAD ± 0.8 Mi.*

*PROPOSED WELL
#1-25(1)*

*PROPOSED WELL
#2-25*

INLAND PRODUCTION COMPANY

*MONUMENT BUTTE FEDERAL #3-25
SEC. 25, T8S, R16E, S.L.B.&M.
TOPO "B"*



SCALE: 1" = 2000'

Tri State
Land Surveying, Inc.
(801) 781-2501

38 WEST 100 NORTH VERNAL, UTAH 84078

POWER LINE

JOHNSON WATER LINE

R 2 W

WATER SOURCE

Lomax



RIGHT-OF-WAY and ACCESS
FOR FRESH WATER PIPELINE


DUCHESNE CO., UTAH

EXHIBIT C

SCALE 1:24,000

Date: 10/88 REVISED 3/89


BY: D. TAFF

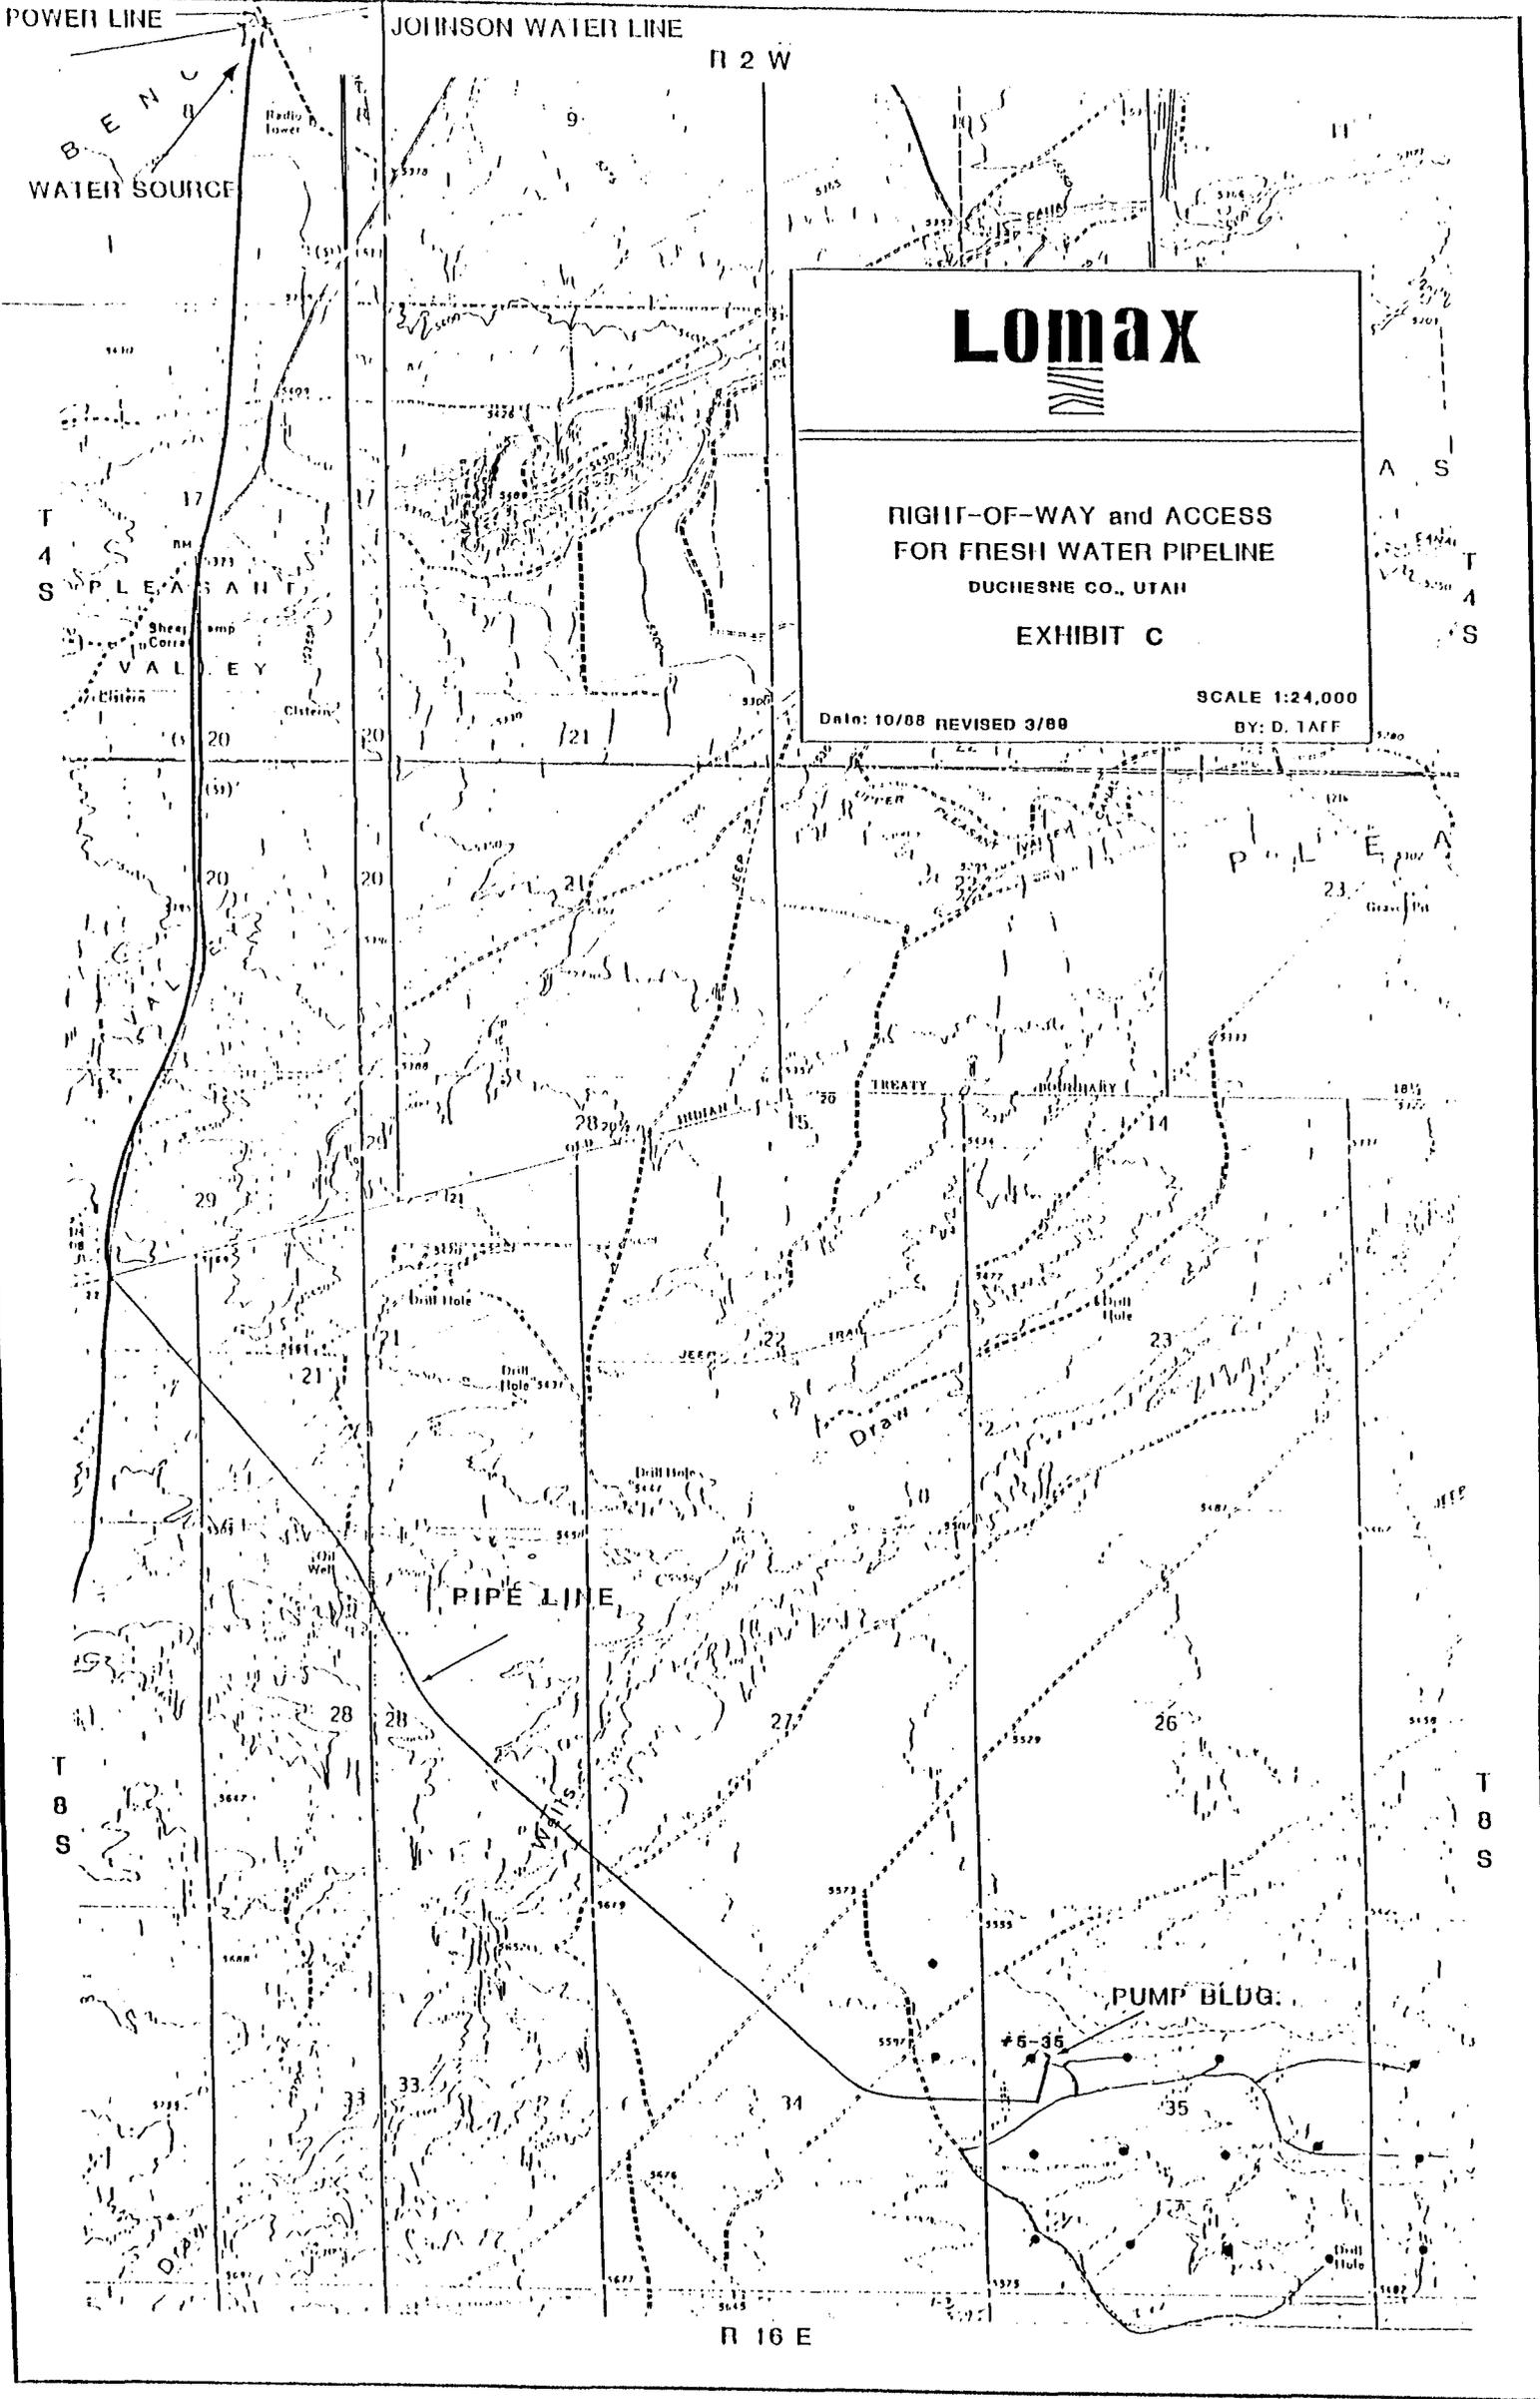

R 16 E

EXHIBIT "D"

Old Indian Treaty Boundary

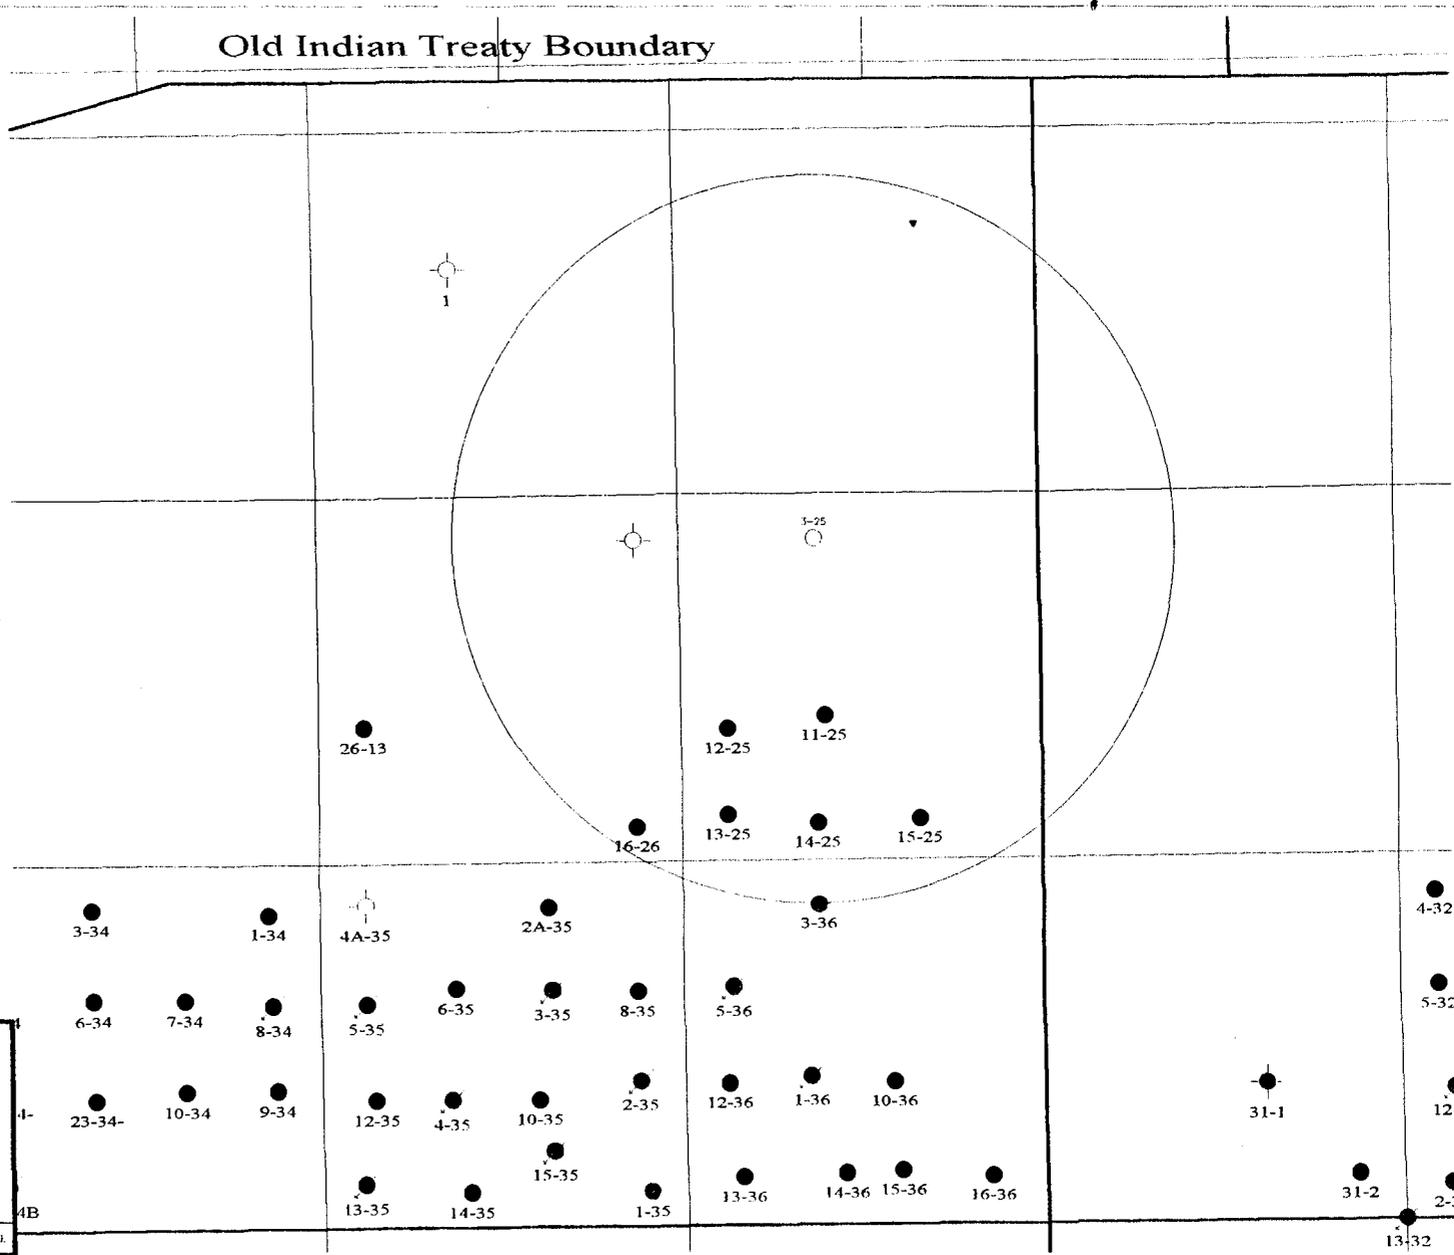

Inland
RESOURCES INC.




475 17th Street Suite 1500
Denver, Colorado 80202
Phone: (303)-292-0900

Monument Butte Fed. #3-25
One Mile Radius
Duchesne County, Utah

Date: 12-7-95 D.G.

INLAND PRODUCTION COMPANY

MONUMENT BUTTE FEDERAL #3-25
SEC. 25, T8S, R16E, S.L.B.&M.

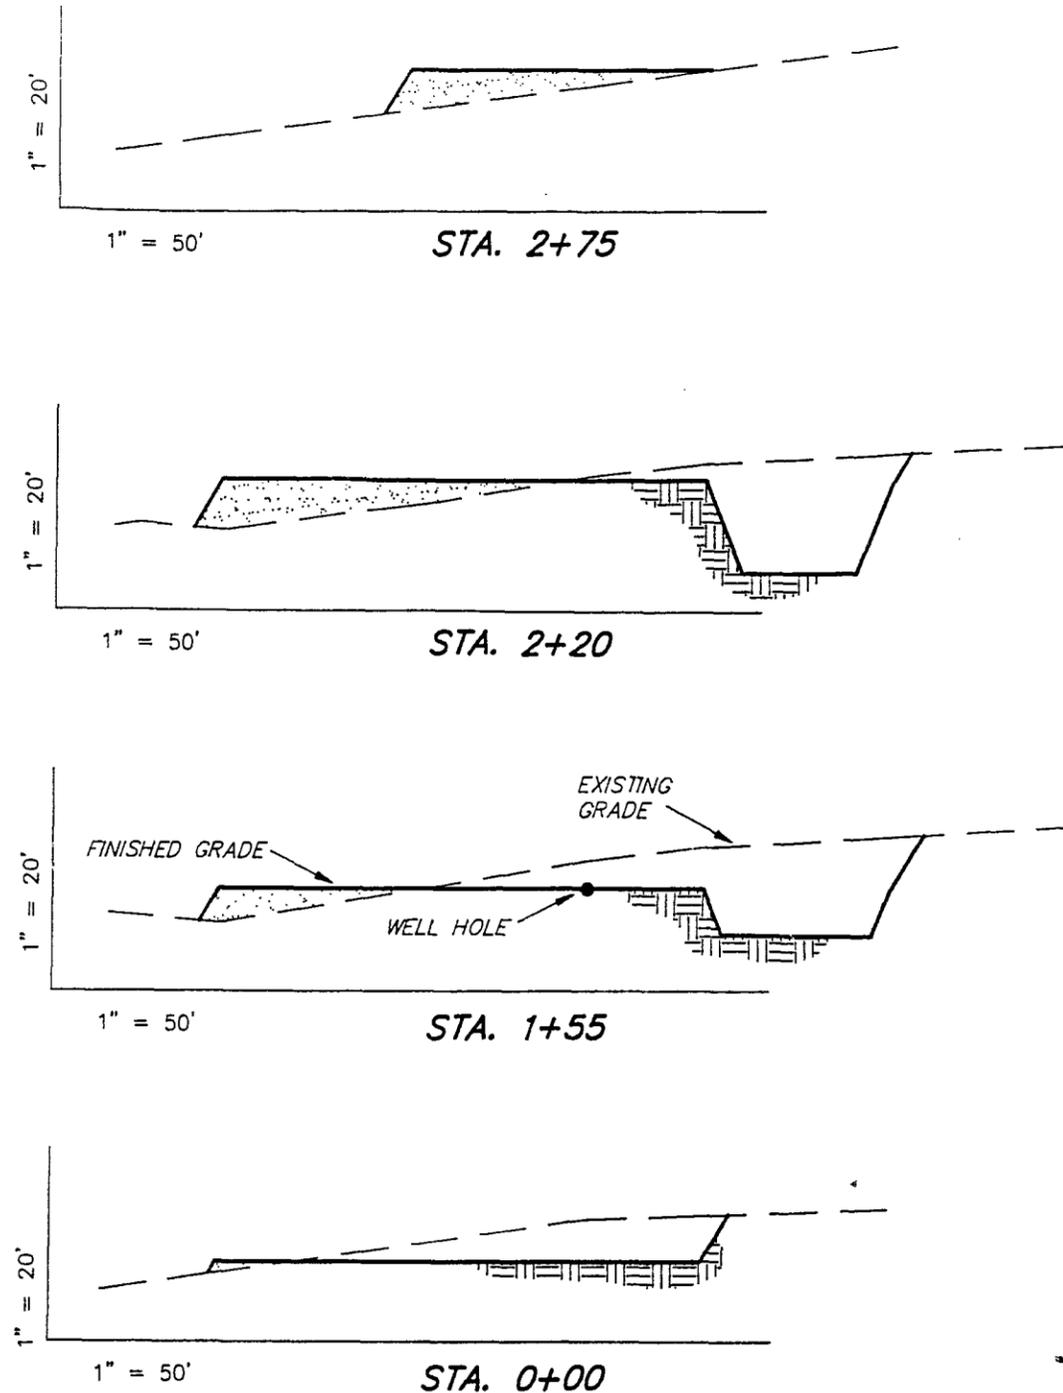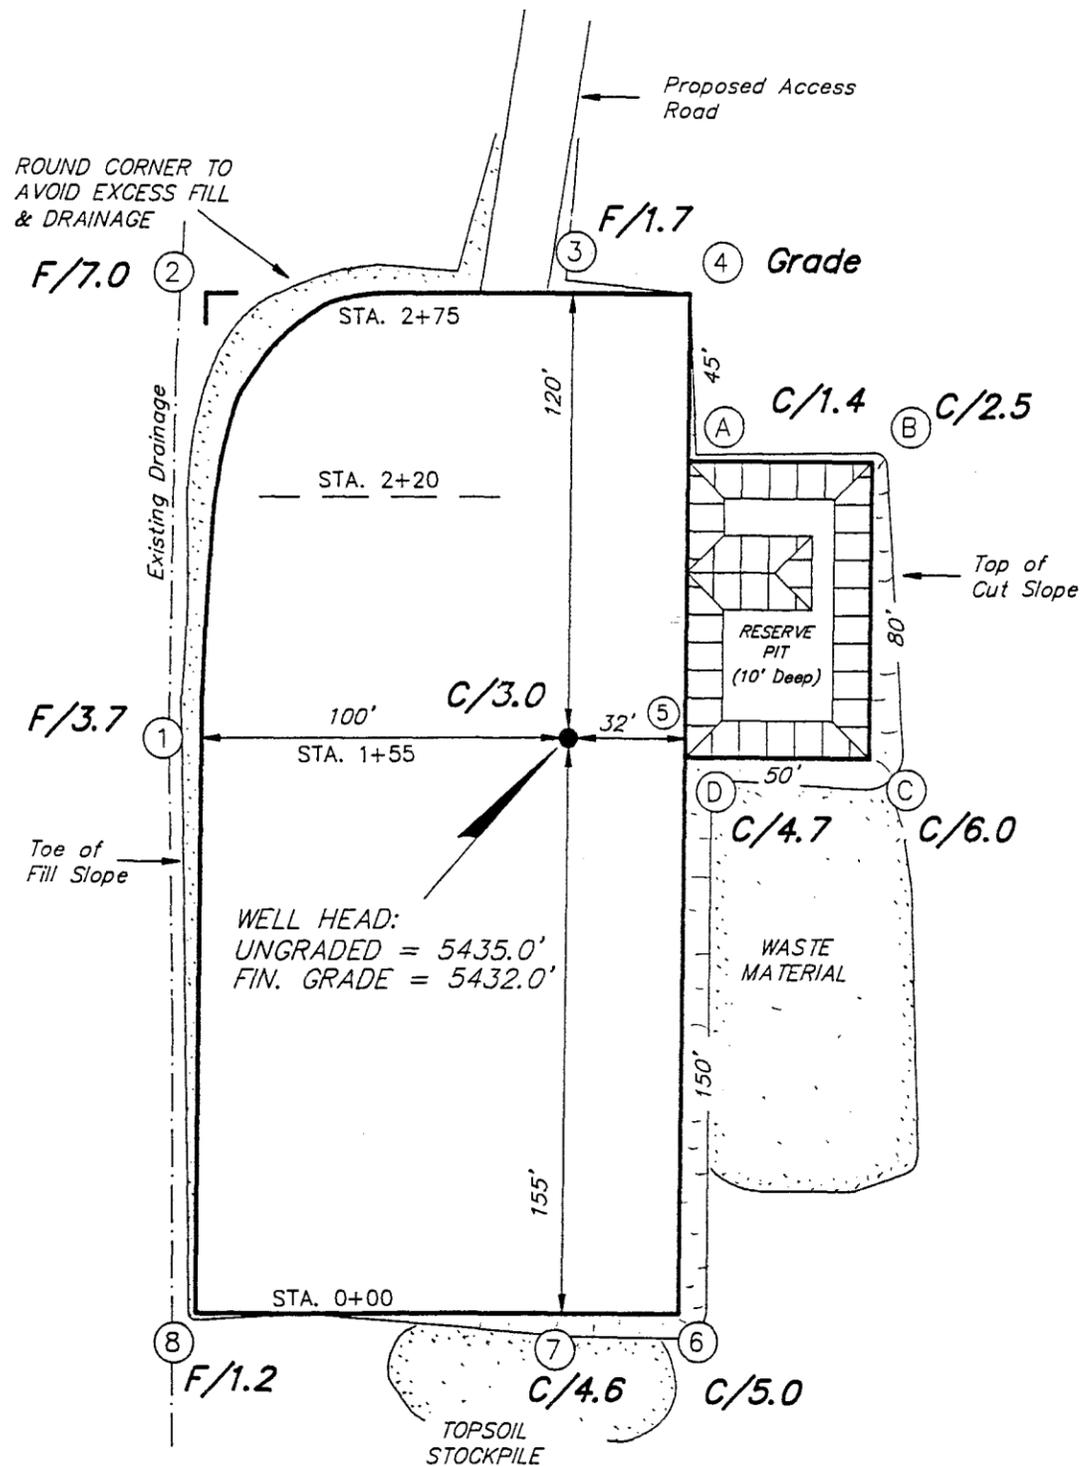

REFERENCE POINTS

- 150' NORTH = 5430.1'
- 200' NORTH = 5433.6'
- 200' WEST = 5438.0'
- 250' WEST = 5439.1'

APPROXIMATE YARDAGES

- CUT = 1,930 Cu. Yds.
- FILL = 1,930 Cu. Yds.
- PIT = 1,060 Cu. Yds.
- 6" TOPSOIL = 750 Cu. Yds.

SURVEYED BY: S.S. G.S.
DRAWN BY: J.R.S.
DATE: 12-14-95
SCALE: 1" = 50'
FILE:

Tri State
Land Surveying, Inc.
(801) 781-2501
38 WEST 100 NORTH VERNAL, UTAH 84078

2-M SYSTEM



EXHIBIT F

RAM TYPE B.O.P.

Make:

Size:

Model:

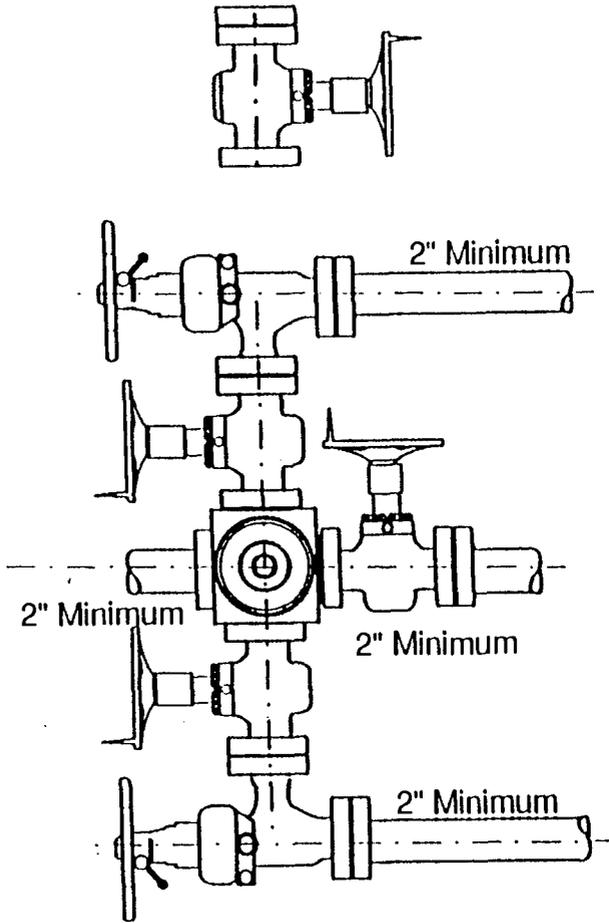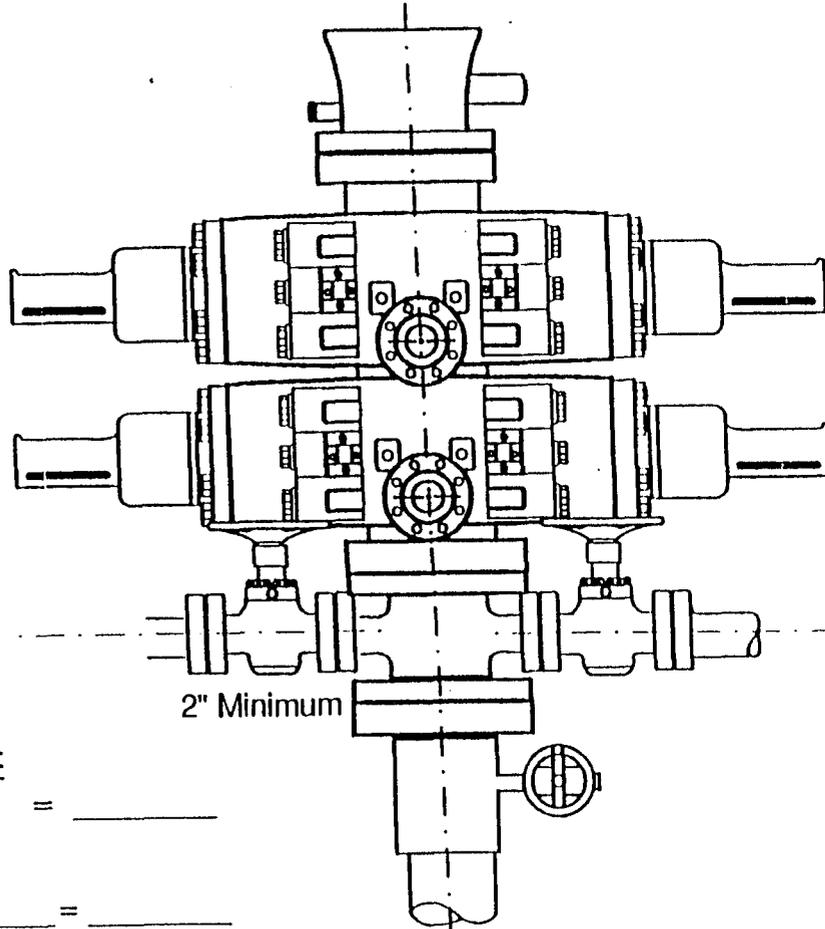

GAL TO CLOSE

Annular BOP = _____

Ramtype BOP

_____ Rams x _____ = _____

= _____ Gal.

_____ x 2 = _____ Total Gal.

Rounding off to the next higher
increment of 10 gal. would require

_____ Gal. (total fluid & nitro volume)

A CULTURAL AND PALEONTOLOGICAL RESOURCES
SURVEY OF MONUMENT BUTTE FEDERALWELLS

3-25, 6-25 AND 8-25 AND ACCESS ROADS,

DUCHESNE COUNTY, UTAH

by

Kathie A. Davies
Assistant Archaeologist

and

Heather M. Weymouth
Archaeologist

Prepared for:

Inland Production Company
P.O. Box 1446
Roosevelt, Utah 84066

Prepared by:

Sagebrush Archaeological Consultants, L.L.C.
3670 Quincy Avenue, Suite 203
Ogden, Utah 84403

Under Authority of Cultural Resources Use Permit No. 95UT54630

and

Under Authority of Utah State Antiquities Permit No. U-95-SJ-0699b

Archaeological Report No. 822-01

December 20, 1995

INTRODUCTION

In December 1995, Inland Production Company (Inland) of Roosevelt, Utah requested that Sagebrush Archaeological Consultants, L.L.C. (Sagebrush) conduct a cultural resources inventory of Inland's Monument Butte Federal wells #3-25 (756.4' FNL 1964.2' FWL), 6-25 (2137' FNL 2101' FWL) and 8-25 (1979' FNL 680' FEL) and their accompanying access roads located on Federal lands in Duchesne County, Utah (Figure 1).

The proposed wells are located in T. 8S., R. 16E., S. 25. The project area lies on USGS 7.5' Quadrangle Myton SE, Utah (1964). The project was carried out by Heather M. Weymouth and Leah K. Evans on the 11th, 12th, and 15th of December 1995 under authority of Utah State Antiquities Permit No. U-95-SJ-0699b and Cultural Resources Use Permit No. 95UT54630.

Previous surveys conducted in the project area reveal numerous projects. Martha Hayden, Paleontologist, with the Utah Geological Survey was consulted on December 18, 1995 concerning paleontological localities in the project area.

Due to the large number of projects conducted in this area, individual project descriptions will not be listed. A total of five individual sites and three paleontological localities have been previously recorded in the vicinity of the current project area. Following is a brief description of each of the five cultural resource sites and three paleontological localities previously recorded near the current project area:

Site 42Dc557. This site, located in a wide drainage at the base of a rock face, is a small historic trash scatter. This site was recommended NOT eligible to the NRHP.

Site 42Dc854. This site is a large prehistoric campsite located in a dunal area. This site consists primarily of a large (500-plus flakes) lithic scatter. Primary flakes are dominant with secondary common, tertiary flakes, shatter and cores present but rare. Fire-cracked rock (FCR) was scattered through the site in eroded areas. No particular FCR configurations were noted possibly due to the deflated nature of portions of the site. Seven crude bifaces and two possible groundstone fragments (one a possible mano fragment) were also located at this site. This site was recommended ELIGIBLE to the NRHP.

Site 42Dc908. This site consists of a large lithic scatter and is located on a gently sloping bench above a large drainage and below a small knoll. Tools located at the site include sixteen bifacially worked tools and two cores. No diagnostic tools or features were noted. This site was recommended ELIGIBLE to the NRHP.

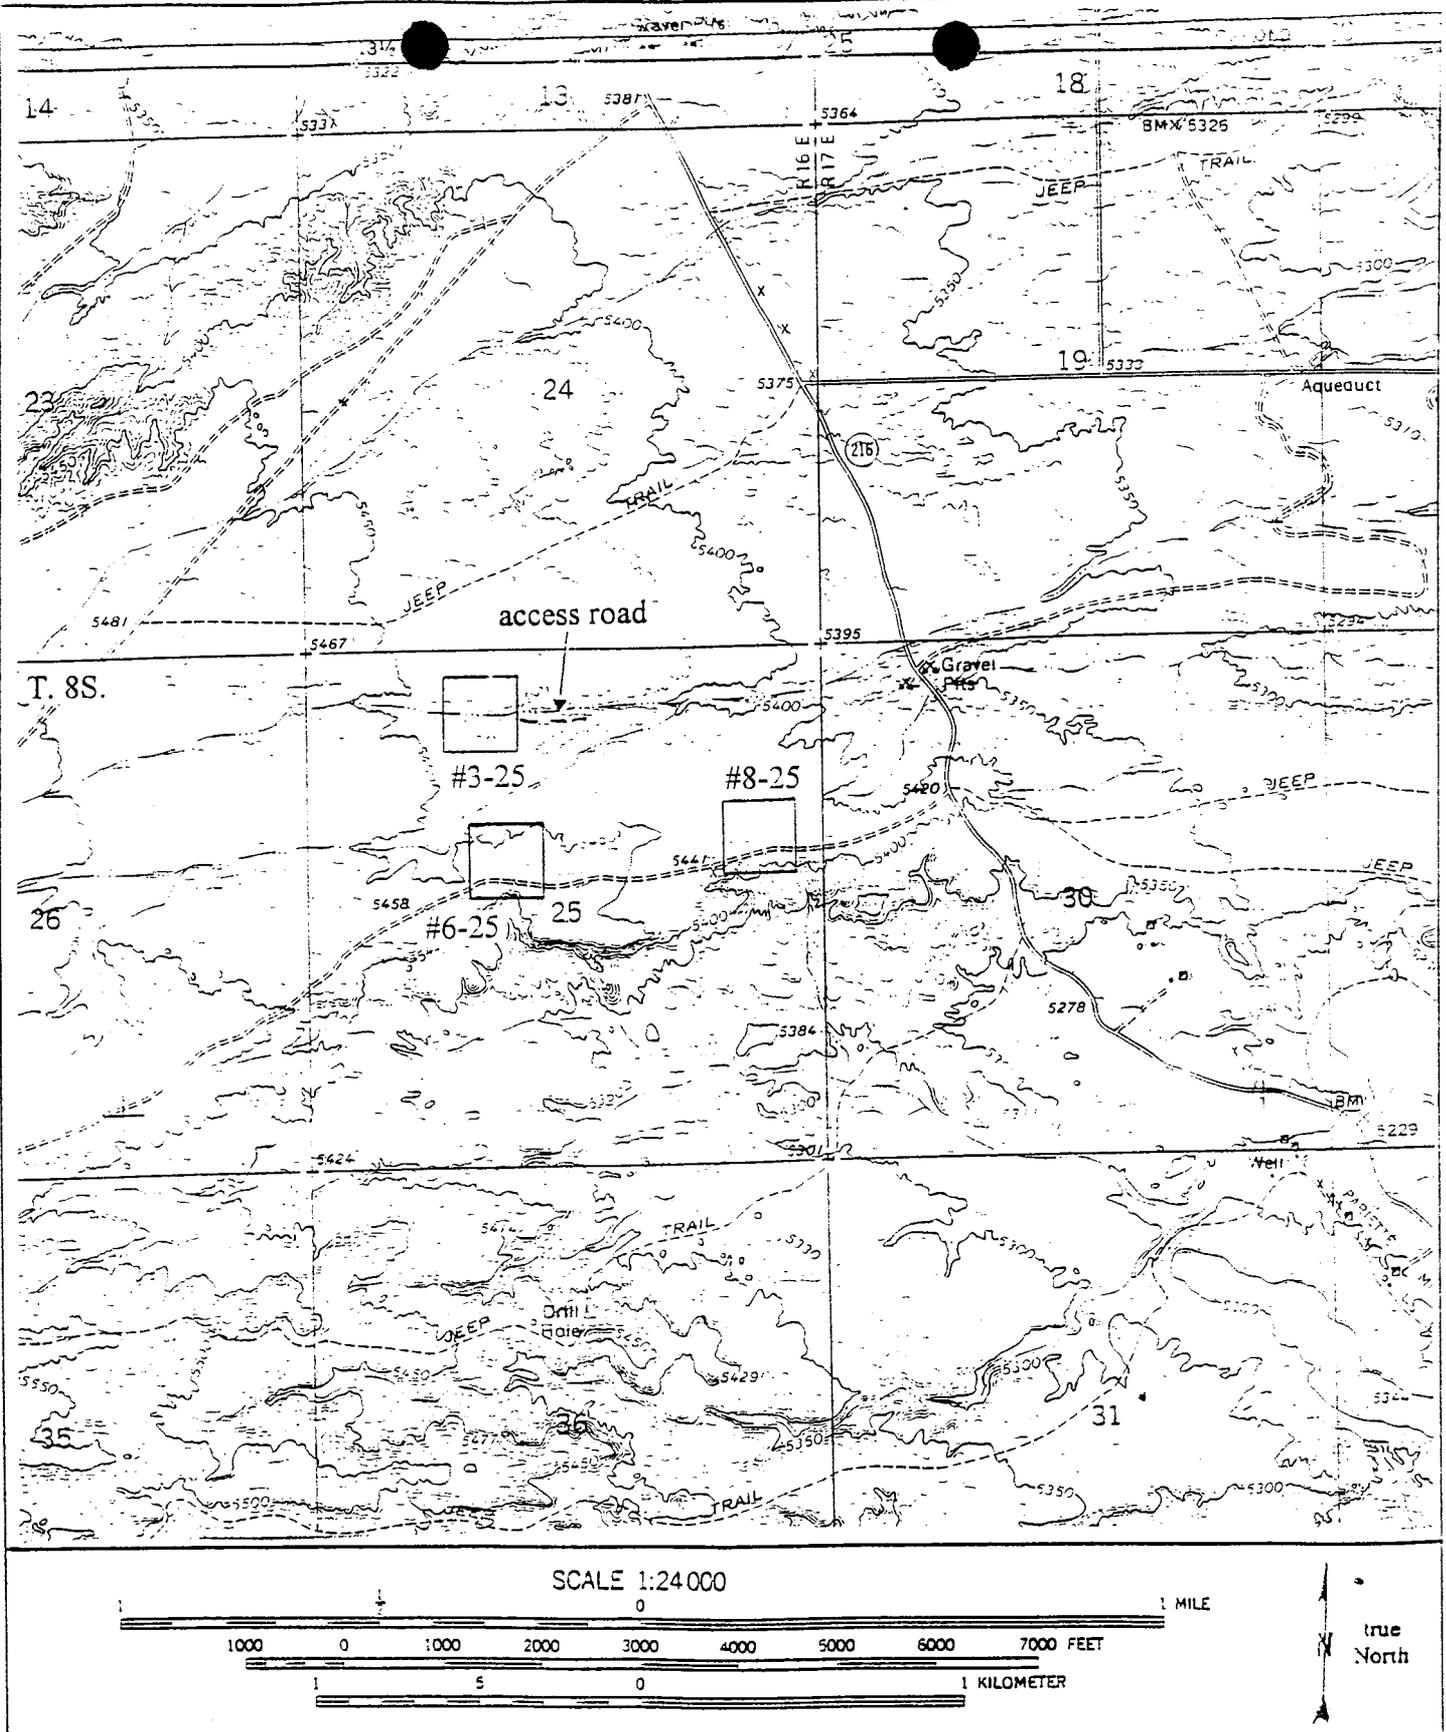


Figure 1. Location of Inland Production Company's Federal wells #3-25, 6-25 and 8-25. Taken from USGS 7.5' Quadrangle Myton SE, Utah (1964).

Site 42Dc909. This site, located on a sandy bluff flanked by three drainages, consists of a large and sparse lithic scatter. Artifacts noted include approximately 150 lithic flakes, three bifaces and a drill. No features and no diagnostic tools were noted. This site was recommended ELIGIBLE to the NRHP.

Site 42Dc937. This site, located at the terminus of a gravel-covered sand bar between two ephemeral stream channels, is a sparse lithic scatter of low grade chert. No diagnostic artifacts nor features are present at the site. This site was recommended NOT eligible to the NRHP.

Locality 42Dc103p. This locality, situated in the NW $\frac{1}{4}$ SE $\frac{1}{4}$ of Sec. 25, consists of plant specimens and a possible fish tail fossil found in an outcropping of sandstone in the Uinta Formation. This locality is considered IMPORTANT.

Locality 42Dc224v. This locality consists of several fossilized turtle shells eroding out of the portion of Uinta Formation exposed along the south side of well pad #15-36. Fragments of what appear to be "a small fossil lizard jaw". This locality is considered SIGNIFICANT.

Locality 42Dc225v. This locality consists of fragmented pieces of turtle shell scattered about the southwest portion of well #10-36. This material may have been transported by water action to this location from the outcrop immediately to the south. Additionally, a number of turtle shell fragments were found around the hill northeast of the well pad. This locality is considered IMPORTANT.

ENVIRONMENT

The project area lies in dissected tablelands south of Pleasant Valley. The elevation of the project area ranges from approximately 1615 to 1666 m (5300 to 5467 feet a.s.l.). Sediments consist of tan to light brown sandy loam with occasional sandstone outcroppings. Vegetation in the survey area consist of shadscale community species. Noted species include winterfat, cheat grass, four-wing salt brush, shadscale, sagebrush, prickly pear cactus, buckwheat, and bunch grass. There are no permanent water sources in the immediate project area. However, many seasonally flowing drainages and washes are present in the vicinity of the project area. These seasonal water sources were likely the primary sources of water in this area historically. Natural disturbance in the area is primarily in the form of aeolian movement of sand and some water erosion. Cultural disturbance includes grazing, and a 2-track road.

METHODOLOGY

The project area consists of three 40,469 m² (10 acre) parcels of land 201-by-201 m (660-by-660 ft) centered on the proposed well heads and access roads connecting the well locations to pre-existing access roads. The well pads were inventoried by Heather M. Weymouth and Leah K. Evans walking parallel transects spaced no more than 15 meters apart. The well pad access roads, which totaled 198 m (650 ft) in length, were walked in two parallel transects spaced 10 m (33 ft) apart to cover a corridor width of 30 m (100 ft) each. The area surveyed during this project (including all well pads and access roads) totaled 127,476 m² (31.5 acres).

RESULTS

No new cultural resources sites were located during this survey. Also, no new paleontological localities were noted.

RECOMMENDATIONS

Based on these findings cultural and paleontological clearance is recommended for the proposed project.

This investigation was conducted with techniques which are considered to be adequate for evaluating cultural and paleontological resources which could be adversely affected by the project. However, should such resources be discovered during construction, a report should be made immediately to Blaine Phillips, Archaeologist, at Bureau of Land Management in Vernal, Utah.

DEC 20 1995

JOHNSON WATER DISTRICT
R.R. 3 BOX 3188
ROOSEVELT, UT 84066
TELEPHONE (801) 722-2620


December 18, 1995

TO WHOM IT MAY CONCERN:

Inland Production Company has purchased a 3 inch water connection with Johnson Water District to supply Monument Butte oilfield.

Johnson Water District has given permission to Inland Production Company to use water from our system for the purpose of drilling and completing the Monument Butte Federal# 2-25, 1-251, and 3-25.

Sincerely,


Karen Ashby,
Secretary

JOHNSON WATER DISTRICT
JAN 12 1996

WORKSHEET
APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 01/12/96

API NO. ASSIGNED: 43-013-31605

WELL NAME: MON BUTTE FED 3-25
 OPERATOR: INLAND PRODUCTION CO (N5160)

PROPOSED LOCATION:
 NENW 25 - T08S - R16E
 SURFACE: 0756-FNL-1946-FWL
 BOTTOM: 0756-FNL-1946-FWL
 DUCHESNE COUNTY
 MONUMENT BUTTE FIELD (105)

INSPECT LOCATION BY: / /		
TECH REVIEW	Initials	Date
Engineering		
Geology		
Surface		

LEASE TYPE: FED
 LEASE NUMBER: U-67170

PROPOSED PRODUCING FORMATION: GRRV

RECEIVED AND/OR REVIEWED:

Plat

Bond: Federal State Fee
 (Number 4488944)

Potash (Y/N)

Oil shale (Y/N)

Water permit
 (Number 5-35 INJECTION WELL)

RDCC Review (Y/N)
 (Date: _____)

LOCATION AND SITING:

R649-2-3. Unit: _____

R649-3-2. General.

R649-3-3. Exception.

Drilling Unit.
 Board Cause no: _____
 Date: _____

COMMENTS: _____

STIPULATIONS: _____



State of Utah
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

Michael O. Leavitt
Governor

Ted Stewart
Executive Director

James W. Carter
Division Director

355 West North Temple
3 Triad Center, Suite 350
Salt Lake City, Utah 84180-1203
801-538-5340
801-359-3940 (Fax)
801-538-5319 (TDD)

February 13, 1996

Inland Production Company
P.O. Box 1446
Roosevelt, Utah 84066

Re: Monument Butte Federal #3-25 Well, 756' FNL, 1946' FWL, NE NW, Sec. 25,
T. 8 S., R. 16 E., Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. 40-6-1 et seq., Utah Administrative Code R649-3-1 et seq., and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-31605.

Sincerely,

A handwritten signature in black ink, appearing to read "R. J. Firth".

R. J. Firth
Associate Director

lwp

Enclosures

cc: Duchesne County Assessor
Bureau of Land Management, Vernal District Office
WAPD



Operator: Inland Production Company
Well Name & Number: Monument Butte Federal #3-25
API Number: 43-013-31605
Lease: U-67170
Location: NE NW Sec. 25 T. 8 S. R. 16 E.

Conditions of Approval

1. **General**
Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for Permit to Drill.

2. **Notification Requirements**
Notify the Division within 24 hours following spudding the well or commencing drilling operations. Contact Jimmie Thompson at (801)538-5340.

Notify the Division prior to commencing operations to plug and abandon the well. Contact Frank Matthews or Mike Hebertson at (801)538-5340.

3. **Reporting Requirements**
All required reports, forms and submittals shall be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

DOGMAH

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL, DEEPEN, OR PLUG BACK

1a. TYPE OF WORK
 DRILL DEEPEN PLUG BACK

b. TYPE OF WELL
 OIL WELL GAS WELL OTHER SINGLE ZONE MULTIPLE ZONE

2. NAME OF OPERATOR
 Inland Production Company

3. ADDRESS OF OPERATOR
 P.O. Box 1446 Roosevelt, UT 84066

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.)*
 At surface
 NE/NW
 At proposed prod. zone 756.4' FNL & 1946.2' FWL

14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*
 8.4 Miles south-of Myton, UT

15. DISTANCE FROM PROPOSED* LOCATION TO NEAREST PROPERTY OR LEASE LINE, FT. (Also to nearest drlg. unit line, if any)
 756.4'

16. NO. OF ACRES IN LEASE
 960

17. NO. OF ACRES ASSIGNED TO THIS WELL
 40

18. DISTANCE FROM PROPOSED LOCATION* TO NEAREST WELL, DRILLING, COMPLETED, OR APPLIED FOR, ON THIS LEASE, FT.
 1355.1'

19. PROPOSED DEPTH
 6500'

20. ROTARY OR CABLE TOOLS
 Rotary

21. ELEVATIONS (Show whether DF, RT, GR, etc.)
 5432' GR

22. APPROX. DATE WORK WILL START*
 2nd Quarter 1996

23. PROPOSED CASING AND CEMENTING PROGRAM

SIZE OF HOLE	SIZE OF CASING	WEIGHT PER FOOT	SETTING DEPTH	QUANTITY OF CEMENT
12 1/4	8 5/8	24#	300'	120 sx Class G+2% CaCl+2% Gel
7 7/8	5 1/2	15.5#	TD	400 sx Hilift followed by
				330 sx Class G w/ 10% CaCl

JAN 13 1996

IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen or plug back, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24. SIGNED Brad Mechem *Brad Mechem* TITLE Operations Manager DATE 1/9/96

(This space for Federal or State office use)

PERMIT NO. 42-012-31605

APPROVAL DATE
ASSISTANT DISTRICT MANAGER MINERALS DATE FEB 13 1996

APPROVED BY [Signature] TITLE _____
 CONDITIONS OF APPROVAL, IF ANY:

NOTICE OF APPROVAL

CONDITIONS OF APPROVAL ATTACHED TO OPERATOR'S COPY

*See Instructions On Reverse Side

44080-611-055

CONDITIONS OF APPROVAL
APPLICATION FOR PERMIT TO DRILL

Company/Operator: Inland Production Company

Well Name & Number: Monument Federal 3-25

API Number: 43-013-31605

Lease Number: U-67170

Location: NENW Sec. 25 T. 8S R. 16E

NOTIFICATION REQUIREMENTS

- Location Construction - at least forty-eight (48) hours prior to construction of location and access roads.
- Location Completion - prior to moving on the drilling rig.
- Spud Notice - at least twenty-four (24) hours prior to spudding the well.
- Casing String and Cementing - at least twenty-four (24) hours prior to running casing and cementing all casing strings.
- BOP and Related Equipment Tests - at least twenty-four (24) hours prior to initiating pressure tests.
- First Production Notice - within five (5) business days after new well begins, or production resumes after well has been off production for more than ninety (90) days.

For more specific details on notification requirements, please check the Conditions of Approval for Notice to Drill and Surface Use Program.

CONDITIONS OF APPROVAL FOR NOTICE TO DRILL

Approval of this application does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

All lease and/or unit operations will be conducted in such a manner that full compliance is made with applicable laws, regulations (43 CFR 3100), Onshore Oil and Gas Orders, and the approved plan of operations. The operator is fully responsible for the actions of his subcontractors. A copy of these conditions will be furnished to the field representative by the operator to insure compliance.

Be aware fire restrictions may be in effect when location is being constructed and/or when well is being drilled. Contact the appropriate Surface Management Agency for information.

A. DRILLING PROGRAM

1. Estimated Depth at Which Oil, Gas, Water, or Other Mineral Bearing Zones are Expected to be Encountered

Report ALL water shows and water-bearing sands to Tim Ingwell of this office. Copies of State of Utah form OGC-8-X are acceptable. If noticeable water flows are detected, submit samples to this office along with any water analyses conducted.

All usable water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling, will be recorded by depth and adequately protected. All oil and gas shows will be tested to determine commercial potential.

2. Pressure Control Equipment

The BOP and related equipment shall meet the minimum requirements of Onshore Oil and Gas Order No. 2 for equipment and testing requirements, procedures, etc., for a 2M system and individual components shall be operable as designed. Chart recorders shall be used for all pressure tests.

Test charts, with individual test results identified, shall be maintained on location while drilling and shall be made available to a BLM representative upon request.

If an air compressor is on location and is being utilized to provide air for the drilling medium while drilling, the special drilling requirements in Onshore Oil and Gas Order No. 2, regarding air or gas drilling shall be adhered to. If a mist system is being utilized then the requirement for a deduster shall be waived.

3. Casing Program and Auxiliary Equipment

Surface casing shall have centralizers on the bottom three joints, with a minimum of one centralizer per joint.

If conductor pipe is set it will be cemented to surface. If drive pipe is used it will be pulled prior to cementing surface casing.

As a minimum, the usable water and oil shale resources shall be isolated and/or protected by having a cement top for the production casing at least 200 ft. above the top of the Mahogany Oil Shale, identified at \pm 2739 ft. If gilsonite is encountered while drilling, it shall be isolated and/or protected via the cementing program.

4. Mud Program and Circulating Medium

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

No chromate additives will be used in the mud system on Federal and Indian lands without prior BLM approval to ensure adequate protection of fresh water aquifers.

5. Coring, Logging and Testing Program

Daily drilling and completion progress reports shall be submitted to this office on a weekly basis.

All Drill Stem tests (DST) shall be accomplished during daylight hours, unless specific approval to start during other hours is obtained from the AO. However, DSTs may be allowed to continue at night if the test was initiated during daylight hours and the rate of flow is stabilized and if adequate lighting is available (i.e., lighting which is adequate for visibility and vaporproof for safe operations). Packers can be released, but tripping should not begin before daylight unless prior approval is obtained from the AO.

The Gamma Ray and Induction Logs need to be pulled from TD to the Surface Shoe.

A cement bond log (CBL) will be run from the production casing shoe to \pm 2539 ft. and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.

Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (Form 3160-4) will be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3164. Two copies of all logs, core descriptions, core analyses, well-test data, geologic summaries, sample description, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, will be filed with Form 3160-4. Samples (cuttings, fluids, and/or gases) will be submitted when requested by the AO.

6. Notifications of Operations

No location will be constructed or moved, no well will be plugged, and no drilling or workover equipment will be removed from a well to be placed in a suspended status without prior approval of the AO. If operations are to be suspended, prior approval of the AO will be obtained and notification given before resumption of operations.

The Vernal District Office shall be notified, during regular work hours (7:45 a.m.-4:30 p.m., Monday through Friday except holidays), at least 24 hours prior to spudding the well.

Operator shall report production data to MMS pursuant to 30 CFR 216.5 using form MMS/3160.

Immediate Report: Spills, blowouts, fires, leaks, accidents, or any other unusual occurrences shall be promptly reported in accordance with the requirements of NTL-3A or its revision.

If a replacement rig is contemplated for completion operations, a "Sundry Notice" (Form 3160-5) to that effect will be filed, for prior approval of the AO, and all conditions of this approved plan are applicable during all operations conducted with the replacement rig.

The date on which production is commenced or resumed will be construed for oil wells as the date on which liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated or, the date on which liquid hydrocarbons are first produced into a permanent storage facility, whichever first occurs; and, for gas wells as the date on which associated liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated or, the date on which gas is first measured through permanent metering facilities, whichever first occurs.

Should the well be successfully completed for production, the AO will be notified when the well is placed in a producing status. Such notification will be sent by telegram or other written communication, not later than five (5) days following the date on which the well is placed on production.

Gas produced from this well may not be vented or flared beyond an initial authorized test period of 30 days or 50 MMCF following its completion, whichever occurs first, without the prior written approval of the Authorized Officer. Should gas be vented or flared without approval beyond the authorized test period, the operator may be directed to shut-in the well until the gas can be captured or approval to continue venting or flaring as uneconomic is granted and the operator shall be required to compensate the lessor for that portion of the gas vented or flared without approval which is determined to have been avoidably lost.

A schematic facilities diagram as required by 43 CFR 3162.7-5 (b.9. d.), and shall be submitted to the appropriate District Office within sixty (60) days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with 43 CFR 3162.7-5 (b. 4).

No well abandonment operations will be commenced without the prior approval of the AO. In the case of newly drilled dry holes or failures, and in emergency situations, oral approval will be obtained from the AO. A "Subsequent Report of Abandonment" Form 3160-5, will be filed with the AO within thirty (30) days following completion of the well for abandonment. This report will indicate where plugs were placed and the current status of surface restoration. Final abandonment will not be approved until the surface reclamation work required by the approved APD or approved abandonment notice has been completed to the satisfaction of the AO or his representative, or the appropriate Surface Managing Agency.

7. Other Information

All loading lines will be placed inside the berm surrounding the tank battery.

All off-lease storage, off-lease measurement, or commingling on-lease or off-lease will have prior written approval from the AO.

The oil and gas measurement facilities will be installed on the well location. The oil and gas meters will be calibrated in place prior to any deliveries. Tests for meter accuracy will be conducted following initial installation and at least quarterly thereafter. The AO will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports will be submitted to the Vernal District Office. All meter measurement facilities will conform with Onshore Oil & Gas Order No. 4 for liquid hydrocarbons and Onshore Oil & Gas Order No. 5 for natural gas measurement.

The use of materials under BLM jurisdiction will conform to 43 CFR 3610.2-3.

There will be no deviation from the proposed drilling and/or workover program without prior approval from the AO. Safe drilling and operating practices must be observed. All wells, whether drilling, producing, suspended, or abandoned will be identified in accordance with 43 CFR 3162.

"Sundry Notice and Report on Wells" (Form 3160-5) will be filed for approval for all changes of plans and other operations in accordance with 43 CFR 3162.3-2.

Section 102(b)(3) of the Federal Oil and Gas Royalty Management Act of 1982, as implemented by the applicable provisions of the operating regulations at Title 43 CFR 3162.4-1(c), requires that "not later than the 5th business day after any well begins production on which royalty is due anywhere on a lease site or allocated to a lease site, or resumes production in the case of a well which has been off production for more than 90 days, the operator shall notify the authorized officer by letter or sundry notice, Form 3160-5, or orally to be followed by a letter or sundry notice, of the date on which such production has begun or resumed."

If you fail to comply with this requirement in the manner and time allowed, you shall be liable for a civil penalty of up to \$10,000 per violation for each day such violation continues, not to exceed a maximum of 20 days. See Section 109(c)(3) of the Federal Oil and Gas Royalty Management Act of 1982 and the implementing regulations at Title 43 CFR 3162.4-1(b)(5)(ii).

APD approval is valid for a period of one (1) year from the signature date. An extension period may be granted, if requested, prior to the expiration of the original approval period.

In the event after-hours approval or notification is necessary, please contact one of the following individuals:

Wayne Bankert (801) 789-4170
Petroleum Engineer

Ed Forsman (801) 789-7077
Petroleum Engineer

Jerry Kenczka (801) 789-1190
Petroleum Engineer

BLM FAX Machine (801) 781-4410

EPA'S LIST OF NONEXEMPT EXPLORATION AND PRODUCTION WASTES

While the following wastes are nonexempt, they are not necessarily hazardous.

- Unused fracturing fluids or acids
- Gas plant cooling tower cleaning wastes
- Painting wastes
- Oil and gas service company wastes, such as empty drums, drum rinsate, vacuum truck rinsate, sandblast media, painting wastes, spent solvents, spilled chemicals, and waste acids
- Vacuum truck and drum rinsate from trucks and drums, transporting or containing nonexempt waste
- Refinery wastes
- Liquid and solid wastes generated by crude oil and tank bottom reclaimers
- Used equipment lubrication oils
- Waste compressor oil, filters, and blowdown
- Used hydraulic fluids
- Waste solvents
- Waste in transportation pipeline-related pits
- Caustic or acid cleaners
- Boiler cleaning wastes
- Boiler refractory bricks
- Incinerator ash
- Laboratory wastes
- Sanitary wastes
- Pesticide wastes
- Radioactive tracer wastes
- Drums, insulation and miscellaneous solids.

CONDITIONS OF APPROVAL
FOR THE SURFACE USE PROGRAM OF THE
APPLICATION FOR PERMIT TO DRILL

Company/Operator: Inland Production Company

API Number 43-013-31605

Well Name & Number: Monument Butte 3-25

Lease Number: U-67170

Location: NE NW Sec. 25 T.8 S. R.16 E.

Surface Ownership: BLM

Date NOS Received 1-8-96

Date APD Received 1-16-96

-Notification Requirements:

- * Location Construction- Forty-eight (48) hours prior to construction of location and access roads.
- * Location Completion- Prior to moving on the drilling rig.
- * Spud Notice- At least twenty-four (24) hours prior to spudding the well.
- * Casing String and Cementing- Twenty-four (24) hours prior to running casing and cementing all casing strings.
- * BOP and Related Equipment Tests- Twenty-four (24) hours prior to initiating pressure test.
- * First Production Notice- Within five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

-Access roads and surface disturbing activities will conform to standards outlined in the Bureau of Land Management and Forest Service publication: Surface Operating Standards for Oil and Gas Exploration and Development, (1989).

-All vehicle travel will be confined to existing access road rights-of-way.

-It is not anticipated that a liner will be required in the reserve pit, however, Byron Tolman with the BLM will be notified when the pit has been complete so an inspection can be made. If porous soils or fractured rock is encountered a liner may be required.

-After first production, produced waste water will be confined to a lined pit or storage tank for a period not to exceed ninety (90) days. During the 90 day period, in accordance with Onshore Order No. 7 an application for approval of a permanent disposal method and location, along with required water analysis, shall be submitted for the AO's approval. Failure to file an application within the time allowed will be considered an incident of noncompliance.

-One erosion dam would be constructed east of the 1-25 location which would service this well also. If the 3-25 location is constructed prior to the 1-25 location, the erosion dam would be constructed in conjunction with the 3-25 well.

-Topsoil should be windrowed on the west and south sides of the location instead of being piled on the west side as shown on the cut sheet.

-No construction, or drilling activities through the completion of the well, will be allowed between March 15 and August 15, in order to protect nesting plovers and burrowing owls. This restriction can be waived if required surveys indicate no plovers or owls are present.

3-28-96

Form 3160-5
(June 1990)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires: March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry to a different reservoir.
Use "APPLICATION FOR PERMIT—" for such proposals

5. Lease Designation and Serial No.

U-67170

6. If Indian, Allottee or Tribe Name

7. If Unit or CA, Agreement Designation

8. Well Name and No.

Mon. Butte Fed. #3-25

9. API Well No.

43-013-31605

10. Field and Pool, or Exploratory Area

Monument Butte

11. County or Parish, State

Duchesne County, Utah

SUBMIT IN TRIPLICATE

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator

Inland Production Company

3. Address and Telephone No.

P.O. Box 1446 Roosevelt, UT 84066 (801) 722-5103

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

**NE/NW 756.4' FNL & 1946.2' FWL
Sec. 25, T8S, R16E**

12. CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION

Notice of Intent
 Subsequent Report
 Final Abandonment Notice

TYPE OF ACTION

Abandonment
 Recompletion
 Plugging Back
 Casing Repair
 Altering Casing
 Other Spud Notification

Change of Plans
 New Construction
 Non-Routine Fracturing
 Water Shut-Off
 Conversion to Injection
 Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

Drilled 12 1/4" hole to 300' w/ Leon Ross Rathole Rig. Set 293.72' of 8 5/8" surface csg. Cement w/ 120 sx prem + 2% CaCl + 1/4#/sk flocele. Drilled Mouse & Rat hole.

SPUD @ 10:30 AM 3/19/96

RECEIVED
MAR 28 1996

14. I hereby certify that the foregoing is true and correct

Signed **Cheryl Cameron** Title **Regulatory Compliance Specialist** Date **3/25/96**

(This space for Federal or State office use)

Approved by _____ Title _____ Date _____
Conditions of approval, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*See Instruction on Reverse Side

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires: March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry to a different reservoir.
Use "APPLICATION FOR PERMIT—" for such proposals

5. Lease Designation and Serial No.

U-67170

6. If Indian, Allottee or Tribe Name

7. If Unit or CA, Agreement Designation

SUBMIT IN TRIPLICATE

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator

Inland Production Company

3. Address and Telephone No.

P.O. Box 1446 Roosevelt, UT 84066 (801) 722-5103

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

**NE/NW 756.4' FNL & 1946.2' FWL
Sec. 25, T8S, R16E**

8. Well Name and No.

Monument Butte Fed. #3-25

9. API Well No.

43-013-31605

10. Field and Pool, or Exploratory Area

Monument Butte

11. County or Parish, State

Duchesne County, Utah

12. CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION

- Notice of Intent
 Subsequent Report
 Final Abandonment Notice

TYPE OF ACTION

- Abandonment
 Recompletion
 Plugging Back
 Casing Repair
 Altering Casing
 Other **Weekly Status Report**
- Change of Plans
 New Construction
 Non-Routine Fracturing
 Water Shut-Off
 Conversion to Injection
 Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

WEEKLY STATUS REPORT FOR WEEK OF 3/19/96 - 4/1/96:

Drilled 7 7/8" hole from 302' - 6250' w/ Kenting Apollo, Rig #59. Run 6202.68' of 15.5# J-55 csg. Cmt w/ 275 sx Hifill followed by 350 sx Thixo w/ 10% CaCl.

W/O completion rig

APR - 9 1996

14. I hereby certify that the foregoing is true and correct

Signed **Cheryl Cameron** Title **Regulatory Compliance Specialist** Date **4/8/96**

(This space for Federal or State office use)

Approved by _____ Title _____ Date _____
Conditions of approval, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*See instruction on Reverse Side

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires: March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry to a different reservoir.
Use "APPLICATION FOR PERMIT—" for such proposals

5. Lease Designation and Serial No.

U-67170

6. If Indian, Allottee or Tribe Name

7. If Unit or CA, Agreement Designation

8. Well Name and No.

Monument Butte Fed. #3-25

9. API Well No.

43-013-31605

10. Field and Pool, or Exploratory Area

Monument Butte

11. County or Parish, State

Duchesne, Utah

SUBMIT IN TRIPLICATE

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator

Inland Production Company

3. Address and Telephone No.

P.O. BOX 1446 Roosevelt, Utah 84066 (801)722-5103

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

756.4' FNL & 1946.2' FWL

NE/NW Sec. 25, T8S, R16E

12. CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION

TYPE OF ACTION

Notice of Intent
 Subsequent Report
 Final Abandonment Notice

Abandonment
 Recompletion
 Plugging Back
 Casing Repair
 Altering Casing
 Other Weekly Status

Change of Plans
 New Construction
 Non-Routine Fracturing
 Water Shut-Off
 Conversion to Injection
 Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)


13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

Weekly Status Report for week of 4/12/96 - 4/17/96

Perf B sd @ 5420' - 5425' & 5375' - 5378'
Perf C sd @ 5310' - 5313'
Perf D sd @ 5142' - 5148' & 5150' - 5160'

TIH w/ production string

ON PRODUCTION 4/23/96



14. I hereby certify that the foregoing is true and correct.

Signed Cheryl Cameron

Title **Regulatory Compliance Specialist** Date **04/29/96**

(This space for Federal or State office use)

Approved by _____ Title _____ Date _____
Conditions of approval, if any:

INLAND PRODUCTION Co.

MBF # 3-25

SEC 25; T8S; R16E


POW 43-013-31605

U-67170

5/14/91

DAL

22-141 50 SHEETS
22-142 100 SHEETS
22-144 200 SHEETS

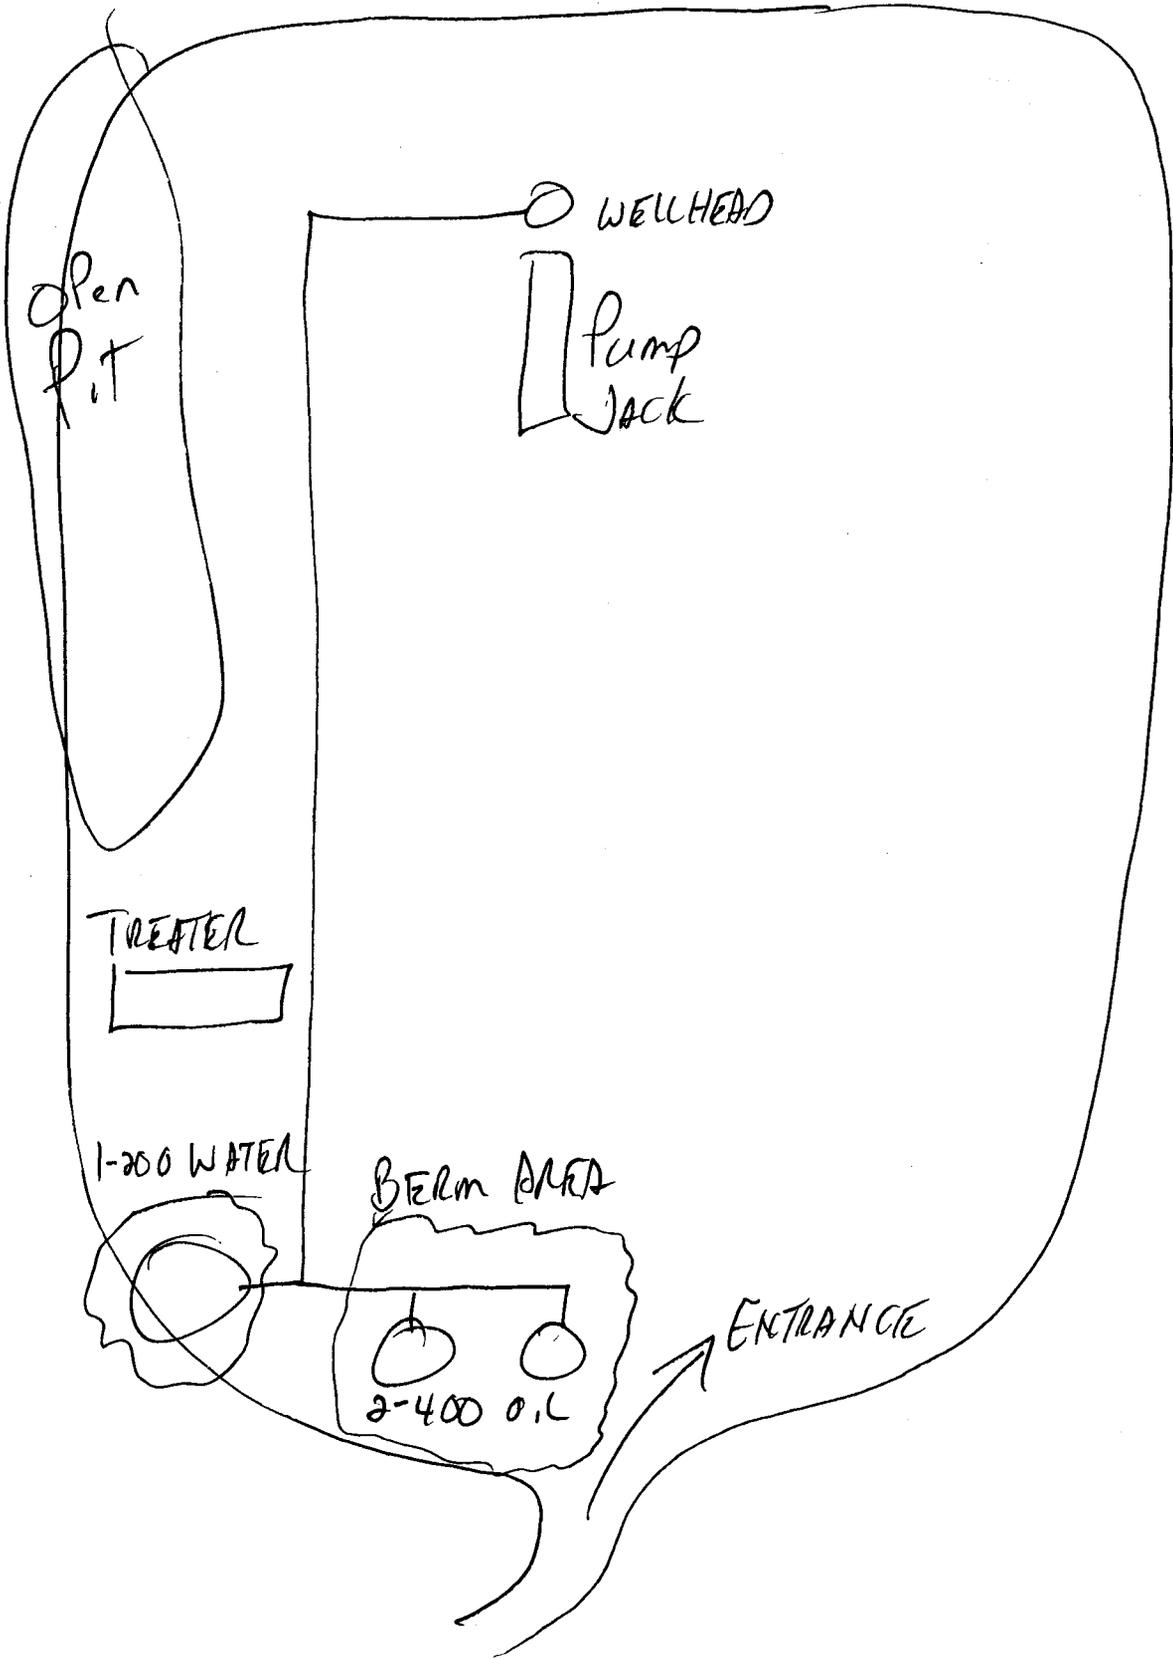

May 20, 96 15:53 No. 006 P. 02

TEL: 801-722-5103

INLAND PRODUCTION CO.

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING

ENTITY ACTION FORM - FORM 6

OPERATOR Inland Production Co

OPERATOR ACCT. NO. 5160

ADDRESS P.O. Box 1446

Roosevelt, UT 84066

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPED DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	11922	43-013-31605	Monument Butte Federal 3-25	NEWV	25	8S	16R	Duchesne	3/19/96	3/19/96
WELL 1 COMMENTS:											
B	99999	10835	43-013-31573	Monument Butte State 4-36	NWNW	36	8S	16E	Duchesne	3/22/96	3/22/96
WELL 2 COMMENTS:											
A	99999	11923	43-013-31623	Tar Sands Federal 3-28	NWNW	28	8S	17E	Duchesne	5/10/96	5/10/96
WELL 3 COMMENTS:											
B	99999	11924	43-013-31622	Boundary Federal 15-21	SWSE	21	8S	17E	Duchesne	5/16/96	5/16/96
WELL 4 COMMENTS:											
WELL 5 COMMENTS:											

ACTION CODES (See instructions on back of form)

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.

(3/89)


Cheryl Cameron
Signature

RCP 5/20/96
Title Date

Phone No. (801) 722-5103



May 16, 1996



*Bureau of Land Management
Vernal District Office
170 South 500 East
Vernal, Utah 84078*

ATTENTION: Wayne Bankert

**RE: Monument Butte Federal #3-25
NE/NW Sec. 25, T8S, R16E
Duchesne County, Utah
43 018 31605**

Dear Wayne,

Enclosed are the original and two copies of the Well Completion or Recompletion Report and Log, on the above referenced location. Included are the CBL, CNL and the DLL. Copies will also be submitted to the State of Utah.

If additional information is needed, please contact me at (801) 722-5103, in the Roosevelt office.

Sincerely,

*Cori Brown
Secretary*

**cc: Attn: Frank Matthews
State of Utah
Division of Oil, Gas & Mining
355 West North Temple
Salt Lake City, Utah 84180-1203**

*/cb
Enclosures*

**UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT**

SUBMIT IN DUPLICATE

(See other instructions on reverse side)

FORM APPROVED
OMB NO. 1004-0137
Expires: February 28, 1995

5. LEASE DESIGNATION AND SERIAL NO.

U-67170

6. IF INDIAN, ALLOTTEE OR TRIBE NAME

7. UNIT AGREEMENT NAME

8. FARM OR LEASE NAME, WELL NO.
Monument Butte Federal

9. API WELL NO.

3-25

10. FIELD AND POOL, OR WILDCAT

Monument Butte

11. SEC., T. R., M., OR BLOCK AND SURVEY OR AREA

Sec. 25, T8S, R16E

12. COUNTY OR PARISH

Duchesne

13. STATE

Utah

WELL COMPLETION OR RECOMPLETION REPORT AND LOG *

1a. TYPE OF WELL: OIL WELL GAS WELL DRY Other

b. TYPE OF COMPLETION: NEW WELL WORK OVER DEEP-EN PLUG BACK DIFF. RESRV. Other

2. NAME OF OPERATOR
Inland Production Company

3. ADDRESS AND TELEPHONE NO.
P.O. Box 1446 Roosevelt, Utah 84066 (801)722-5103

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements)*
At surface **NE/NW**

At top prod. interval reported below **756.4' FNL & 1946.2' FWL**

At total depth

14. PERMIT NO. **43-013-31605** DATE ISSUED **2-13-96**

15. DATE SPUDDED **3/19/96** 16. DATE T.D. REACHED **3/31/96** 17. DATE COMPL. (Ready to prod.) **4/23/96** 18. ELEVATIONS (DF, RKB, RT, GR, ETC.)* **5432' GR** 19. ELEV. CASINGHEAD **-**

20. TOTAL DEPTH, MD & TVD **6250'** 21. PLUG, BACK T.D., MD & TVD **6234' KB** 22. IF MULTIPLE COMPL., HOW MANY* **→** 23. INTERVALS DRILLED BY **→** ROTARY TOOLS **X** CABLE TOOLS

24. PRODUCING INTERVAL(S), OF THIS COMPLETION—TOP, BOTTOM, NAME (MD AND TVD)* **Green River** 25. WAS DIRECTIONAL SURVEY MADE
5420'-5425', 5375'-5378', 5310'-5313', 5142'-5148', 5150'-5160' **NO**

26. TYPE ELECTRIC AND OTHER LOGS RUN **CBL, CNL, DLL** 27. WAS WELL CORRED **NO**

28. CASING RECORD (Report all strings set in well)

CASING SIZE/GRADE	WEIGHT, LB./FT.	DEPTH SET (MD)	HOLE SIZE	TOP OF CEMENT, CEMENTING RECORD	AMOUNT PULLED
8 5/8	24#	290.52'	12 1/4	120 sx prem + w/2% Gel, 2% flocele	2000 CC & 1/4# /sk
5 1/2	15.5#	6250.31'	7 7/8	275 sx Hifill & 350 sx Thixo w/10% Calseal	

29. LINER RECORD

SIZE	TOP (MD)	BOTTOM (MD)	SACKS CEMENT*	SCREEN (MD)

30. TUBING RECORD

SIZE	DEPTH SET (MD)	PACKER SET (MD)

31. PERFORATION RECORD (Interval, size and number)

B sd 5420'-5425'
B Lime 5375'-5378'
C sd 5310'-5313'
D sd 5142'-5148' & 5150'-5160'

32. ACID, SHOT, FRACTURE, CEMENT SQUEEZE, ETC.

DEPTH INTERVAL (MD)	AMOUNT AND KIND OF MATERIAL USED
See back	

33.* PRODUCTION

DATE FIRST PRODUCTION 4/23/96		PRODUCTION METHOD (Flowing, gas lift, pumping—size and type of pump) Pumping 2 1/2" X 1 1/2" X 15' PHAC pump				WELL STATUS (Producing or shut-in) Producing	
DATE OF TEST 14 day average	HOURS TESTED	CHOKE SIZE N/A	PROD'N. FOR TEST PERIOD →	OIL—BBL. 149	GAS—MCF. 94	WATER—BBL. 3	GAS-OIL RATIO* .631
FLOW. TUBING PRESS.	CASING PRESSURE	CALCULATED 24-HOUR RATE →	OIL—BBL.	GAS—MCF.	WATER—BBL.	OIL GRAVITY-API (CORR.)	

34. DISPOSITION OF GAS (Sold, used for fuel, vented, etc.)

Sold & Used for fuel

TEST WITNESSED BY

35. LIST OF ATTACHMENTS

Logs in Item #26

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records

SIGNED **Cheryl Cameron**

TITLE **Regulatory Compliance Specialist** DATE **5/10/96**

*(See Instructions and Spaces for Additional Data on Reverse Side)

37. SUMMARY OF POROUS ZONES: (Show all important zones of porosity and contents thereof; cored intervals; and all drill-stem, tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures, and recoveries):

38.


GEOLOGIC MARKERS

FORMATION	TOP	BOTTOM	DESCRIPTION, CONTENTS, ETC.	NAME	TOP	
					MEAS. DEPTH	TRUE VERT. DEPTH
			#32			
Garden Gulch Mkr	4424'		Perf B sd 5420'-5425'			
Point 3 Marker	4710'		Perf B Lime 5375'-5378'			
X Marker	4946'		Perf C sd 5310'-5313'			
Y Marker	4980'		Frac w/93,600# 20/40 sd in 583 bbls gel			
Douglas Ck Mkr	5105'					
Bicarbonate Mkr	5372'		Perf D sd 5142'-5148' & 5150'-5160'			
B Limestone Mkr	5517'		Frac w/79,700# 20/40 sd in 471 bbls gel			
Castle Peak	6024'					

INLAND PRODUCTION COMPANY
APPLICATION FOR APPROVAL OF CLASS II INJECTION WELL
MONUMENT BUTTE FEDERAL #3-25

LEASE NO. U-67170

OCTOBER 21, 1996



APPLICATION FOR INJECTION WELL - UIC FORM 1

OPERATOR Inland Production Company
ADDRESS P.O. Box 790233 Vernal, UT 84079

Well name and number: Monument Butte Federal #3-25

Field or Unit name: Monument Butte Lease no. U-67170

Well location: QQ NENW section 25 township 8S range 16E county Duchesne

Is this application for expansion of an existing project? . Yes No

Will the proposed well be used for:

Enhanced Recovery?	Yes <input checked="" type="checkbox"/>	No <input type="checkbox"/>
Disposal?	Yes <input type="checkbox"/>	No <input checked="" type="checkbox"/>
Storage?	Yes <input type="checkbox"/>	No <input checked="" type="checkbox"/>

Is this application for a new well to be drilled? Yes No

If this application is for an existing well,
has a casing test been performed on the well? Yes No

Date of test: To be conducted @ time of conversion
API number: 43-013-31605

Proposed injection interval from 4300' to 6000'

Proposed maximum injection: rate 1000 BPD pressure 2000# psig

Proposed injection zone contains oil, gas, and/or fresh water within 1/2 mile of the well.

IMPORTANT: Additional information as required by R615-5-2 should accompany this form.

List of Attachments: Exhibits "A" through "F-1"

I certify that this report is true and complete to the best of my knowledge.

Name <u>Brad Mecham</u>	Signature <u><i>Brad Mecham</i></u>
Title <u>District Manager</u>	Date <u>10/21/96</u>
Phone No. <u>(801) 722-5103</u>	

(State use only)
Application approved by _____ Title _____
Approval Date _____

Comments:

REQUIREMENTS FOR INJECTION OF FLUIDS INTO RESERVOIRS
RULE R615-5-1

- 1) Operations to increase ultimate recovery, such as cycling of gas, the maintenance of pressure, the introduction of gas, water or other substances into a reservoir for the purpose of secondary or other enhanced recovery or for storage and the injection of water into any formation for the purpose of water disposal shall be permitted only by order of the Board after notice and hearing.
- 2) A request for agency action for authority for the injection of gas, liquefied petroleum gas, air, water or any other medium into any formation for any reason, including but not necessarily limited to the establishment of or the expansion of waterflood projects, enhanced recovery projects, and pressure maintenance projects shall contain:

2.1. *The name and address of the operator of the project;*

Answer: Inland Production Company
P.O. Box 1446
W. Poleline Road
Roosevelt, Utah 84066

2.2. *A plat showing the area involved and identifying all wells, including all proposed injection wells, in the project area and within one-half mile radius of the project area;*

Answer: Reference Exhibit "A".

2.3. *A full description of the particular operation for which approval is requested;*

Answer: To approve the conversion of the Monument Butte Federal #3-25 from a producing oil well to a water injection well in the Monument Butte field; and to approve the installation of an injection line from the Monument Butte Federal #1-25 to the Monument Butte Federal #3-25 with a 3" coated steel line approximately 3000' and buried 5' deep, in order to transfer water to the Monument Butte #3-25 from our existing water line at the Monument Butte Federal #1-25. Reference Exhibit "B".

2.4. *A description of the pools from which the identified wells are producing or have produced;*

Answer: The proposed injection well will inject into the Green River Formation.

2.5. *The names, description and depth of the pool or pools to be affected;*

Answer: The Green River Formation pool targeted for injection is the B, B-Lime, C and the D sands with a gamma ray derived top as follows: In the #3-25 "B" sand @ 5420', B-Lime @ 5375', "C" sand @ 5310', and the "D" sand @ 5142'. The injection zones are a porous and permeable lenticular calcareous sandstone. The porosity of the sandstone is intergranular. The confirming impermeable stratum directly above and below the injection zones are composed of tight, moderately calcareous lacustrine shale.

2.6. *A copy of a log of a representative well completed in the pool;*

Answer: Referenced log Monument Butte Federal #3-25 is currently on file with the Utah Division of Oil, Gas & Mining and the Bureau of Land Management.

2.7. *A statement as to the type of fluid to be used for injection, its source and the estimated amounts to be injected daily;*

Answer: Culinary water from Johnson Water District supply line.

Estimated Injection Rate: 200-400 BPD

2.8. *A list of all operators or owners and surface owners within a one-half mile radius of the proposed project;*

Answer: Reference Exhibit "C".

2.9. *An affidavit certifying that said operators or owners and surface owners within a one-half mile radius have been provided a copy of the petition for injection;*

Answer: Reference Exhibit "D".

2.10. *Any additional information the Board may determine is necessary to adequately review the petition.*

Answer: Inland will supply any additional information requested by the Bureau of Land Management, and the Utah Division of Oil, Gas and Mining.

4.0. *Establish recovery projects may be expanded and additional wells placed on injection only upon authority from the board after notice and hearing or by administrative approval.*

Answer: This proposed injection well is within the Monument Butte Field and the request is for administrative approval.

**REQUIREMENTS FOR CLASS II INJECTION WELLS INCLUDING WATER DISPOSAL, STORAGE
AND ENHANCED RECOVERY WELLS
SECTION V - RULE 615-5-2**

- 1) Injection well shall be completed, equipped, operated, and maintained in a manner that will prevent pollution and damage to any USDW, or other resources and will confine injected fluids to the interval approved.
- 2) The application for an injection well shall include a properly completed Form DOGM-UIC-1 and the following:

2.1. *A plat showing the location of the injection well, all abandoned or active wells within a one-half mile radius of the proposed wells, and the surface owner and the operator of any lands or producing leases, respectively, within a one-half mile radius of the proposed injection well;*

Answer: Reference Exhibits "A" and "C".

2.2. *Copies of electrical or radioactive logs, including gamma ray logs, for the proposed well run prior to the installation of casing and indicating resistivity, spontaneous potential, caliper and porosity;*

Answer: All logs have been filed with the Utah Division of Oil, Gas & Mining, and the Bureau of Land Management.

2.3. *A copy of a cement bond or comparable log run for the proposed injection well after casing was set and cemented;*

Answer: A copy of the cement bond log is on file with the Bureau of Land Management, and with the Utah Division of Oil, Gas & Mining

2.4. *Copies of log already on file with the Division should be referenced, but need not to be refiled.*

Answer: All copies are on file with the Bureau of Land Management, and the Utah Division of Oil, Gas & Mining.

2.5. *A description of the casing or proposed casing program of the injection well and of the proposed method for testing the casing before use of the well;*

Answer: The casing program 8-5/8" 24# J-55 surface casing run to 290.52', and 5 1/2" casing from surface to 6250.31'. A casing integrity test will be conducted @ time of conversion. Reference Exhibits "E-1" through "E-12".

2.6. *A statement as to the type of fluid to be used for injection, its source and estimated amounts to be injected daily.*

Answer: Culinary water from our pre approved Monument Butte supply line. Reference Exhibit "B".
Estimated Injection Rate: 200-400 BPD

2.7. *Standard laboratory analysis of the fluid to be injected, the fluid in the formation into which the fluid is being injected, and the compatibility of the fluids.*

Answer: Reference Exhibit "F" and "F-1" (Samples taken from the Monument Butte Federal #3-25, Johnson water, and the compatibility of both fluids).

2.8. *The proposed average and maximum injection pressures;*

Answer: Average Injection Pressure will be determined upon conversion by a Step Rate Test. Maximum injection pressure 2000#.

2.9. *Evidence and data to support a finding that the proposed injection well will not initiate fractures through the overlying strata or a confining interval that could enable the injected fluid or formation fluid to enter the fresh water strata;*

Answer: The frac gradients for the Monument Butte Federal #3-25 averages approximately .89 psig/ft. The maximum injection pressures will be kept below this gradient. A step rate test will be performed periodically to ensure we are below parting pressure.

2.10. *Appropriate geological data on the injection interval and confining beds, including the geologic name, lithologic description, thickness, depth, and lateral extent;*

Answer: The injection zone is from 4300' - 6000', found with the Green River Formation. The reservoirs are a very fine grain sandstone with minor interbedded shale streaks. The top of the "D" estimated at approximately 5142'. The estimated average porosity is 14%; the estimated fracture pressure is 2100# psi.

The porous and permeable lenticular sandstones vary in thickness from 0' to 40' and are confined to the Monument Butte Field by low porosity calcareous shale and carbonates.

The confining stratum directly above and below the injection zone is the Douglas Creek member of the Green River Formation. The strata confining the injection zone is composed of tight, moderately calcareous sandy lacustrine shale. All of the confining strata is impermeable and it will effectively seal off the oil, gas, and water of the injection zone from any strata directly above or below it. Maps and cross sections to the Boundary Unit are on file with the Division of Oil, Gas & Mining and also with the U. S. Bureau of Land Management.

2.11. *A review of the mechanical condition of each well within a one-half mile radius of the proposed injection well to assure that no conduit exists that could enable fluids to migrate up or down the wellbore and enter improper intervals;*

Answer: Exhibits "E-1" through "E-12".

The injection system will be equipped with high and low pressure shut-down devices which will automatically shut-in injection waters if a system blockage or leakage occurs. One way check valves will also insure proper flow management. Relief valves will also be utilized for high pressure relief.

2.12. *An affidavit certifying that a copy of the application has been provided to all operators or owners, and surface owners within a one-half mile radius of the proposed injection well;*

Answer: Exhibit "D".

2.13 *Any other additional information that the Board or Division may determine is necessary to adequately review the application.*

Answer: Inland Production Company will await review of this application and additional information will be submitted if required.

3) Applications for injection wells which are within a recovery project area will be considered for approval.

3.1. Pursuant to Rule 615-5-1-3

3.2. Subsequent to Board approval of a recovery project pursuant to Rule 615-5-1-3.

4) Approval of an injection well is subject to the requirements of Rule 615-5-4, if the proposed injection interval can be classified as an USDW.

5) In addition to the requirements of this section, the provisions of Rule 615-3-1, R615-3-4, R615-3-24, R615-3-32, R615-8-1 and R615-10 apply to all Class II injection wells.

INLAND PRODUCTION COMPANY

**Monument Butte Federal #3-25
Sec. 25, T8S, R16E
Duchesne County, Utah**

PLUGGING & ABANDONMENT PLAN

The plugging and abandonment plan consists of the following plugs:

- PLUG #1: Set 200' plug from 3650' - 3850' w/ 30 sx cmt**
- PLUG #2: Set 200' plug from 2400' - 2200' w/ 30 sx cmt**
- PLUG #3: Set 100' plug from 353' - 253' w/ 15 sx cmt**
- PLUG #4: Set 10 sx cmt plug from 50' - Surface**
- PLUG #5: Pump 75 sx cmt down 5 1/2" by 8 5/8" Annulus**

EXHIBIT "A"



Inland
RESOURCES INC.

475 17th Street Suite 1500
Denver, Colorado 80202
Phone: (303)-292-0900

One Half Mile Radius
Monument Butte #3-25
Duchesne County, Utah

Date: 9/17/96 J.A.

EXHIBIT "B"

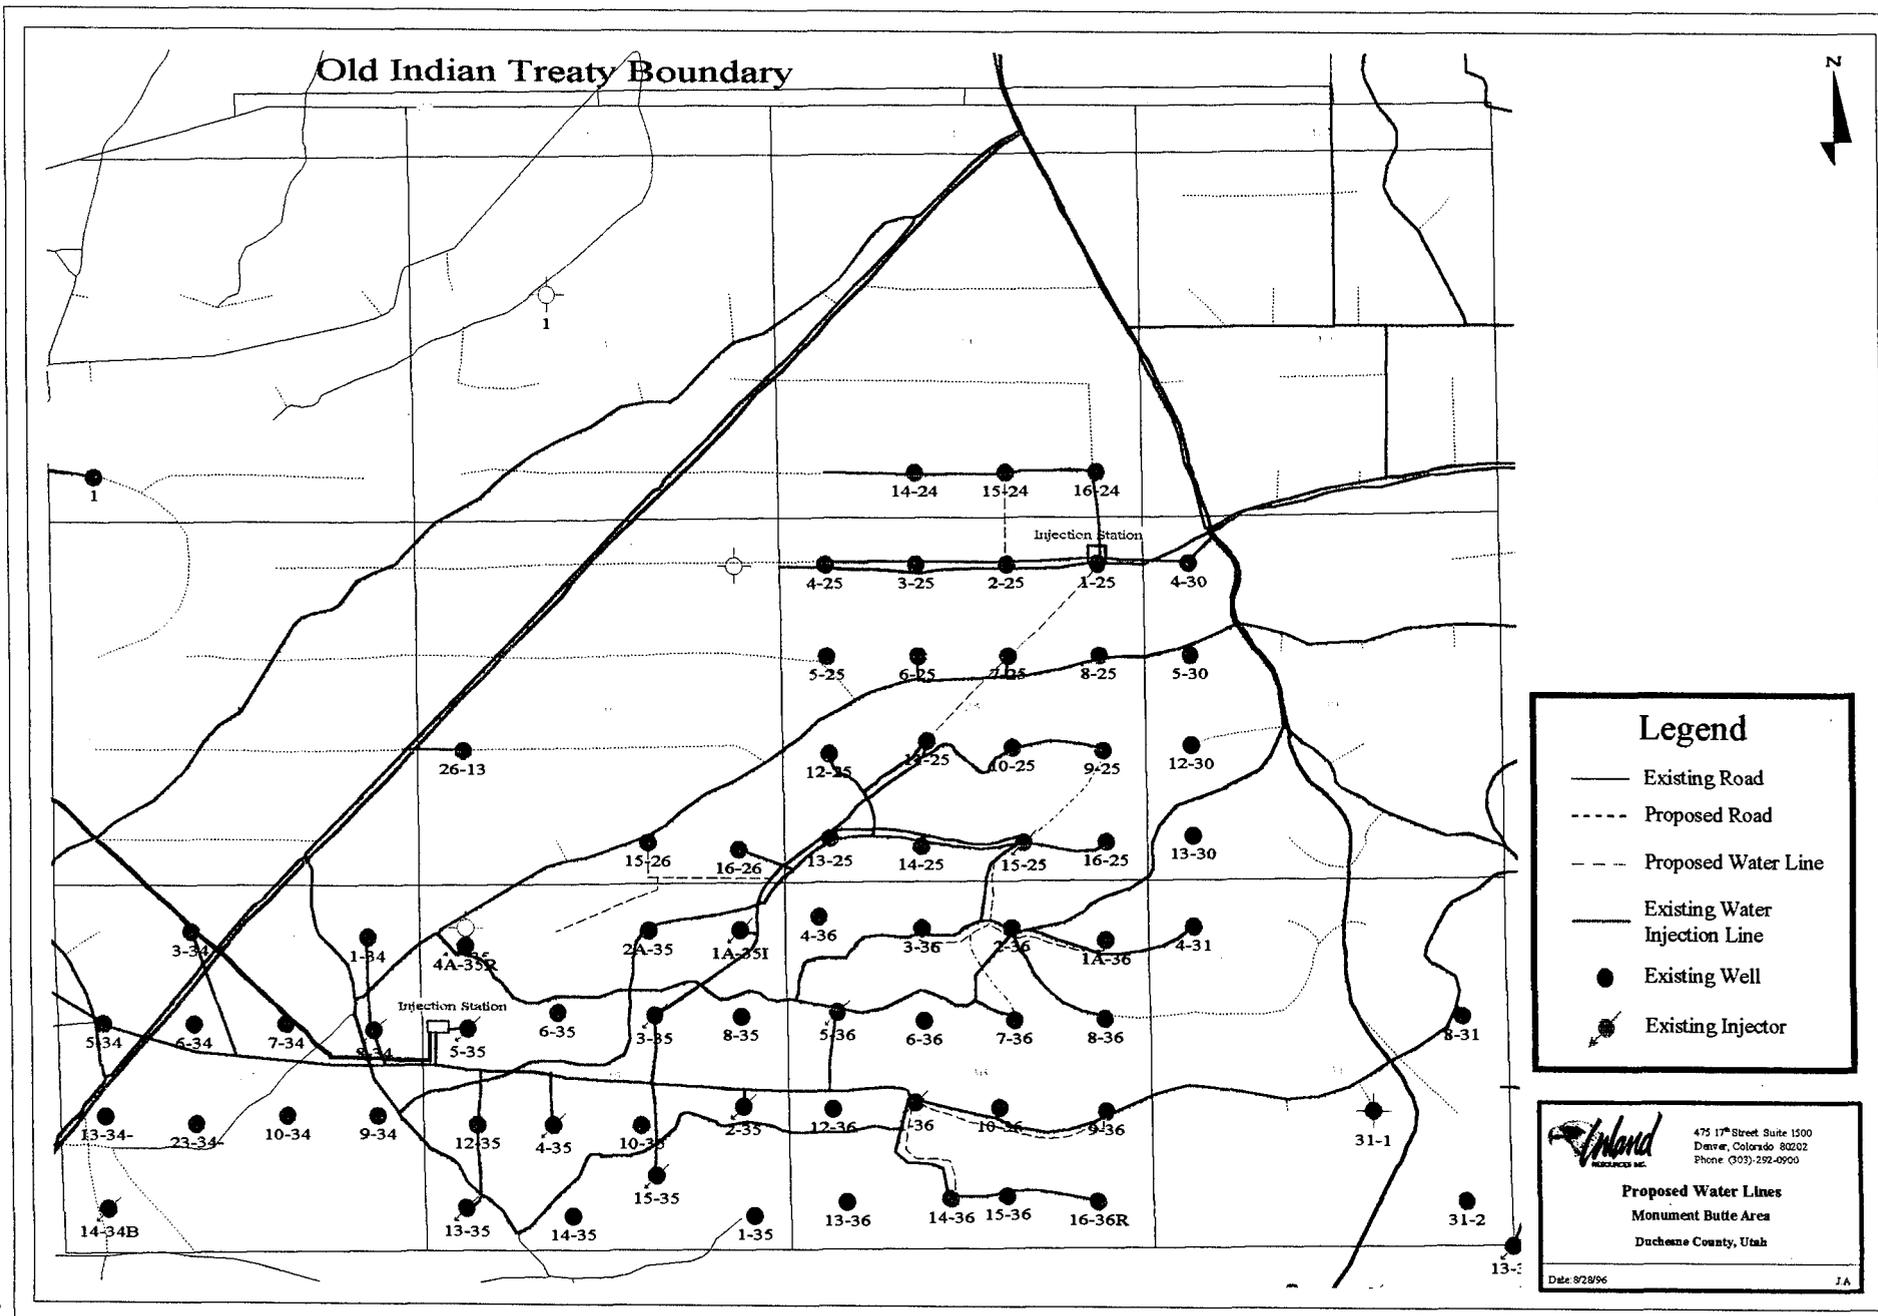


EXHIBIT "C"

**SURFACE OWNERS, OWNERS AND OPERATORS WITHIN A ONE-HALF MILE RADIUS OF THE
MONUMENT BUTTE FEDERAL #3-25**

Bureau of Land Management
Vernal District Office
170 South 500 East
Vernal, Utah 84078

EXHIBIT "D"

RE: Application for Approval of Class II Injection Well
Monument Butte Federal #3-25.

I certify that a copy of the application has been provided to all surface owners within a one-half mile radius of the proposed injection well.




INLAND PRODUCTION COMPANY
Brad Mecham
District Manager

Sworn to and subscribed before me this 29 day of October 1996.



Notary Public in and for the State of Utah



Monument Butte Federal #3-25

Spud Date: 3/27/96
 Put on Production: 4/23/96
 GL: 5432' KB: 5445'

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 293.72'
 DEPTH LANDED: 290.52'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 147 jts. (6247')
 DEPTH LANDED: 6250.31'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 275 sk Hyfill mixed & 350 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING

SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
 NO. OF JOINTS: 164 jts (?)
 TUBING ANCHOR: 5106'
 SEATING NIPPLE: 2-7/8" (1.10')
 TOTAL STRING LENGTH: ? (EOT @ 5486')
 SN LANDED AT: 5391'

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM
 SUCKER RODS: 4-3/4" scraped, 110-3/4" slick rods, 96-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 1-2-1/2" x 1-1/2" x 15" RHAC
 STROKE LENGTH: 74"
 PUMP SPEED, SPM: 7 SPM
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR


FRAC JOB

4/16/96 5425'-5310' Frac B-1, Bi-Carb and C sand as follows:
 93,600# of 20/40 sd in 583 bbls of Boragel. Breakdown @ 4000#. Pre-frac ISIP @ 1600 psi. Treated @ avg Rate 31 bpm, avg press 1800 psi. ISIP-1991 psi, 5-min 1923 psi. Flowback on 16/64" ck after 5 min SI @ 1.5 bpm.

4/21/96 5142'-5160' Frac D-1 sand as follows:
 79,000# 20/49 sd in 471 bbls Boragel. Breakdown @ 1266 psi, treated @ avg rate 30 bpm w/1550 psi avg. ISIP 1967 psi, 5-min 1622 psi. Flowback on 16/64" ck @ 1.3 bpm.

PERFORATION RECORD

4/15/96	5420'-5425'	4 JSPF	20 holes
4/15/96	5375'-5378'	4 JSPF	12 holes
4/15/96	5310'-5313'	4 JSPF	12 holes
4/17/96	5142'-5148'	4 JSPF	24 holes
4/17/96	5150'-5160'	4 JSPF	40 holes

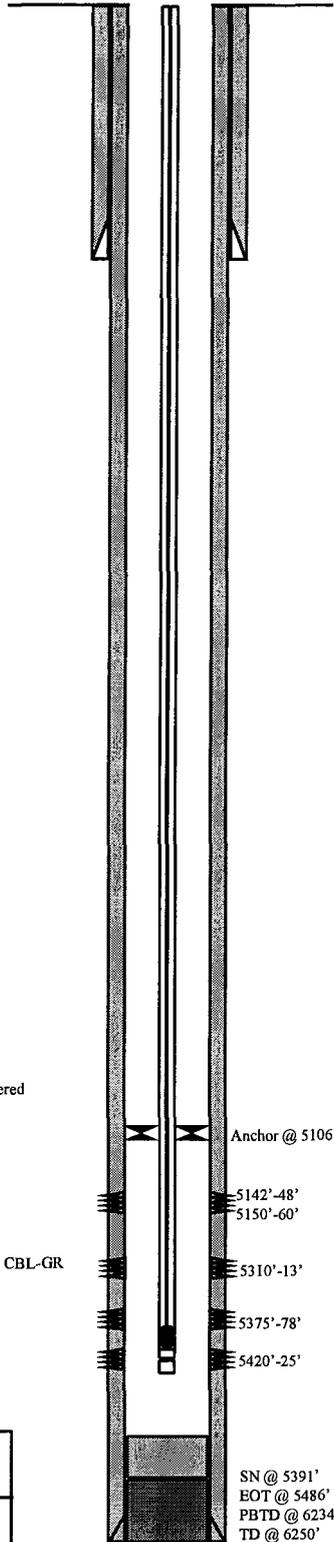

SN @ 5391'
 EOT @ 5486'
 PBDT @ 6234'
 TD @ 6250'



Inland Resources Inc.

Monument Butte Federal #3-25

756 FNL 1946 FEL

NENW Section 25-T8S-R16E

Duchesne Co, Utah

API #43-013-31605; Lease #U-67170

Monument Butte Federal #3-25

Spud Date: 3/27/96
 Put on Injection: --/--/--
 GL: 5432' KB: 5445'

Injection Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 293.72'
 DEPTH LANDED: 290.52'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt


PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 147 jts. (6247')
 DEPTH LANDED: 6250.31'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 275 sk Hyfill mixed & 350 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING

SIZE/GRADE/WT.: ?
 NO. OF JOINTS: ?
 PACKER: 5106'
 SEATING NIPPLE:
 TOTAL STRING LENGTH: ?
 SN LANDED AT:

SUCKER RODS

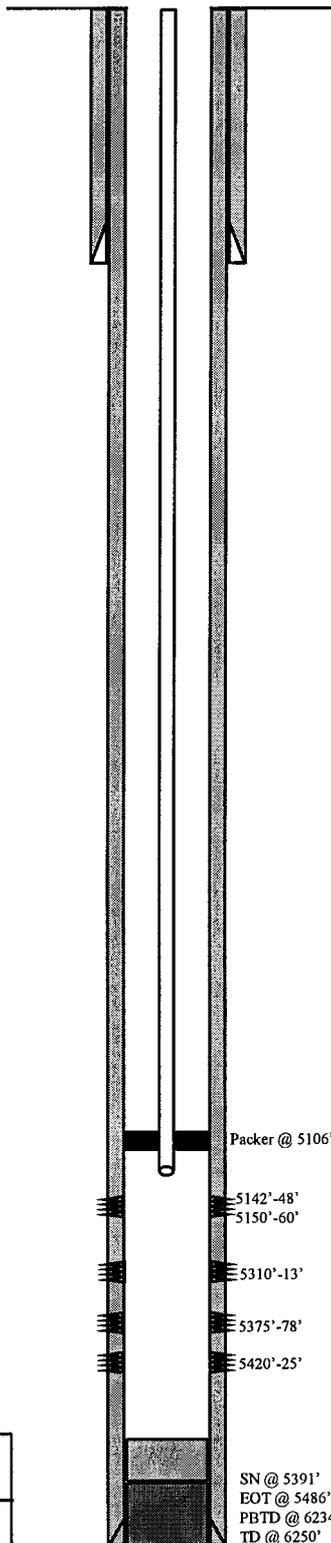

FRAC JOB

4/16/96 5425'-5310' Frac B-1, Bi-Carb and C sand as follows:
 93,600# of 20/40 sd in 583 bbls of
 Boragel. Breakdown @ 4000#. Pre-frac
 ISIP @ 1600 psi. Treated @ avg Rate 31
 bpm, avg press 1800 psi. ISIP-1991 psi,
 5-min 1923 psi. Flowback on 16/64" ck
 after 5 min SI @ 1.5 bpm.

4/21/96 5142'-5160' Frac D-1 sand as follows:
 79,000# 20/49 sd in 471 bbls Boragel.
 Breakdown @ 1266 psi, treated @ avg
 rate 30 bpm w/1550 psi avg. ISIP 1967
 psi, 5-min 1622 psi. Flowback on 16/64"
 ck @ 1.3 bpm.

PERFORATION RECORD

4/15/96	5420'-5425'	4 JSPF	20 holes
4/15/96	5375'-5378'	4 JSPF	12 holes
4/15/96	5310'-5313'	4 JSPF	12 holes
4/17/96	5142'-5148'	4 JSPF	24 holes
4/17/96	5150'-5160'	4 JSPF	40 holes

Packer @ 5106'

5142'-48'
 5150'-60'

5310'-13'

5375'-78'

5420'-25'

SN @ 5391'
 EOT @ 5486'
 PBTD @ 6234'
 TD @ 6250'



Inland Resources Inc.

Monument Butte Federal #3-25

756 FNL 1946 FEL

NENW Section 25-T8S-R16E

Duchesne Co, Utah

API #43-013-31605; Lease #U-67170

Monument Butte Federal #3-25

Spud Date: 3/27/96
 Plugged: --/--/--
 GL: 5432' KB: 5445'

Plugged Diagram

SURFACE CASING


CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 293.72'
 DEPTH LANDED: 290.52'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 147 jts. (6247')
 DEPTH LANDED: 6250.31'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 275 sk Hyfill mixed & 350 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING

SUCKER RODS

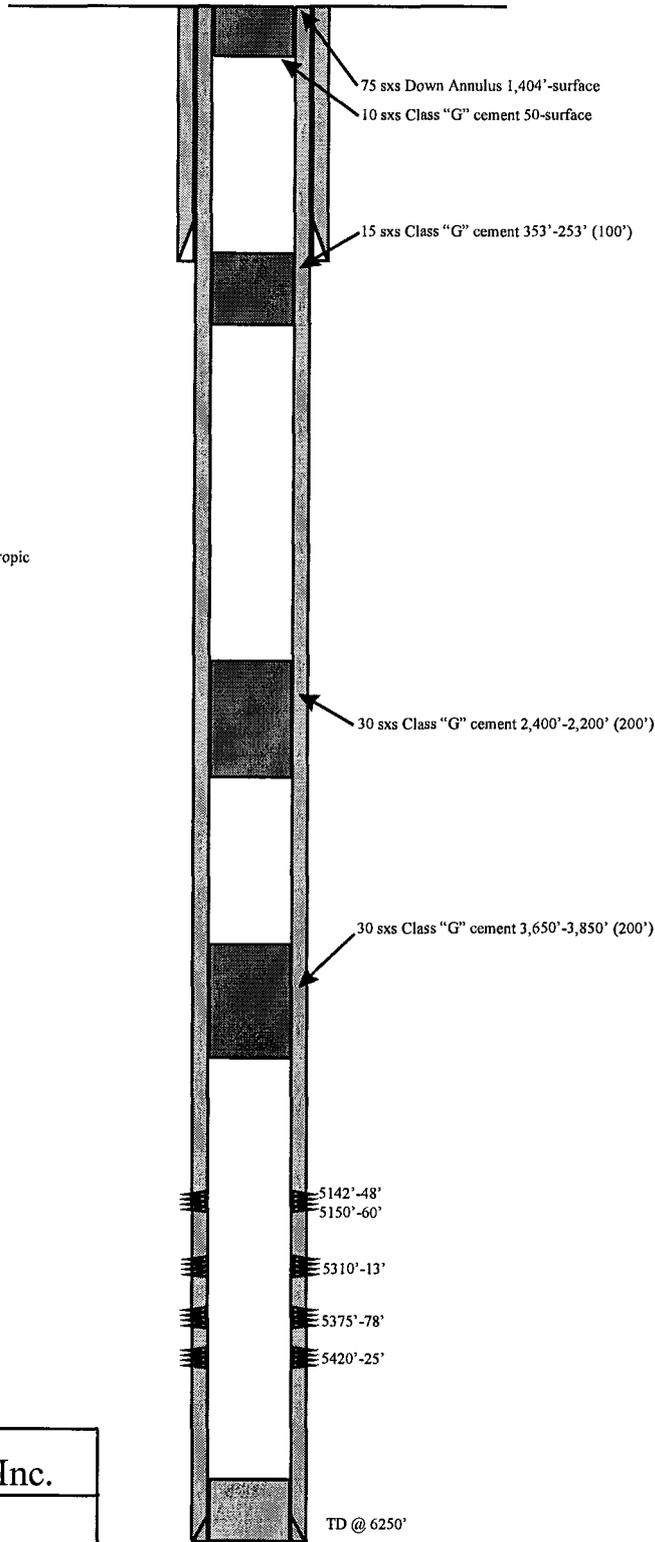

	Inland Resources Inc.
	Monument Butte Federal #3-25
	756 FNL 1946 FEL
	NENW Section 25-T8S-R16E
	Duchesne Co, Utah
API #43-013-31605; Lease #U-67170	

Monument Butte Federal #1-25

Spud Date: 4/17/96
 Put on Production: 5/10/96
 GL: 5398' KB: 5411'

Initial Production: 354 BOPD,
 458 MCFPD, 8 BWPD

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 304'
 DEPTH LANDED: 303'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt, est 5 bbls to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 146 jts.
 DEPTH LANDED: 6246.44'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 275 sk Hyfill mixed & 355 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING


SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
 NO. OF JOINTS: 199 jts
 TUBING ANCHOR: 5864'
 SEATING NIPPLE: 2-7/8" (1.10')
 TOTAL STRING LENGTH: ? (EOT @ 5999')
 SN LANDED AT: ?

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM
 SUCKER RODS: 4-3/4" scraped, 132-3/4" slick rods, 95-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 2-1/2" x 1-1/2" x 10 x 15 RHAC
 STROKE LENGTH: 86"
 PUMP SPEED, SPM: 7 SPM
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR

FRAC JOB

4/30/96	6091'-6184'	Frac CP-4 and CP-2 sand as follows: 83,400# 20/40 sd in 523 bbls Boragel. Breakdown @ 1801 psi. ISIP 1760 psi, 5-min 1631 psi. Flowback after 5 min SI on 16/64" ck @ 1.6 bpm.
5/2/96	5459'-5468'	Frac B-2 sand as follows: 50,000# of 20/40 sd in 353 bbls Boragel. Breakdown @ 1008 psi. Treated @ avg rate 16.8 bpm, avg press 1450#. ISIP-2256 psi, 5-min 2042 psi. Flowback on 16/64" ck @ 1 bpm.
5/4/96	5317'-5327'	Frac C sand as follows: 57,400# of 20/40 sd in 383 bbls of Boragel. Frmtn broke @ 1797#. Avg treating press 1450# @ 162 bpm. ISIP-1820 psi, 5-min 1698 psi. Start flowback on 16/64" ck @ 1.5 bpm.
5/7/96	5151'-5160'	Frac D-1 sand as follows: 56,400# of 20/40 sd in 379 bbls of Boragel. Breakdown @ 1794 psi, treat @ avg rate 18.5, avg press 1300 psi. ISIP-1843 psi, 5-min 1775 psi. Start flowback on 16/64" ck @ 1.7 bpm, flowed for 1-1/4 hours & died.

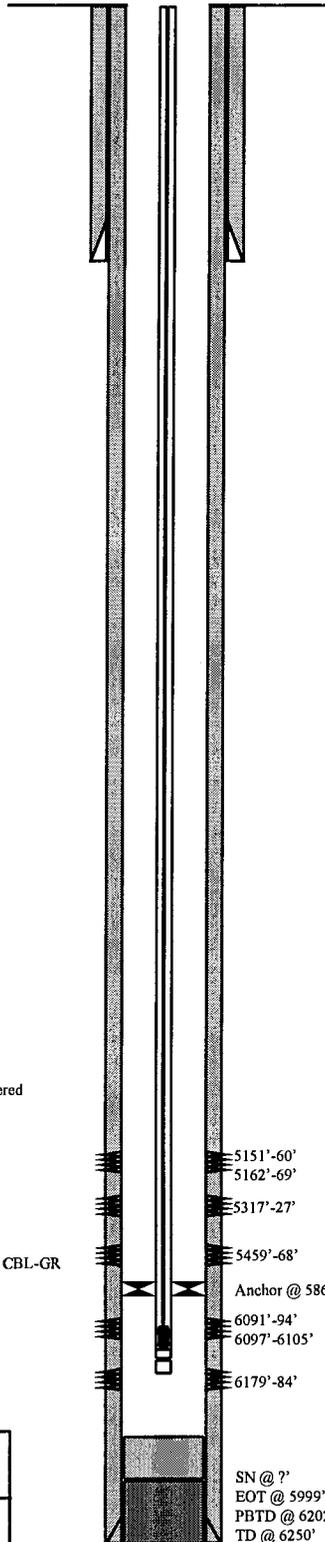

PERFORATION RECORD

4/25/96	6179'-6184'	4 JSPF	? holes
4/25/96	6091'-6094'	4 JSPF	? holes
4/25/96	6097'-6105'	4 JSPF	? holes
5/1/96	5459'-5468'	4 JSPF	36 holes
5/3/96	5317'-5327'	4 JSPF	40 holes
5/6/96	5151'-5160'	4 JSPF	36 holes
5/6/96	5162'-5169'	4 JSPF	28 holes

SN @ ?
 EOT @ 5999'
 PBTD @ 6202'
 TD @ 6250'



Inland Resources Inc.

Monument Butte Federal #1-25

660 FNL 660 FEL

NENE Section 25-T8S-R16E

Duchesne Co, Utah

API #43-013-31608; Lease #U-67170

Monument Butte Federal #2-25

Spud Date: 3/13/96
 Put on Production: 4/10/96
 GL: 5413' KB: 5426'

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: ? jts. (305')
 DEPTH LANDED: 302'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt, est 5 bbls cmt to surf

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: ? jts. (6605.03')
 DEPTH LANDED: 6583.60'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 340 sk Hyfill mixed & 450 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING


SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
 NO. OF JOINTS: 148 jts (?)
 TUBING ANCHOR: 4500'
 SEATING NIPPLE: 2-7/8" (1.10')
 TOTAL STRING LENGTH: ? (EOT @ 5535')
 SN LANDED AT: ?

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM
 SUCKER RODS: 4-3/4" scraped, 108-3/4" slick rods, 96-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 2-1/2" x 1-1/2" x 17' RHAC
 STROKE LENGTH: 100"
 PUMP SPEED, SPM: 8 SPM
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR

FRAC JOB

4/1/96	5316'-5324'	Frac C sand as follows: 77,770# of 20/40 sd w/ 456 bbls of Boragel. Breakdown @ 2168 psi, treated as follows: avg rate 18 bpm, avg press 2100 psi. ISIP-2267, 5-min 2242 psi. Flowback after 5 min. on 16/64" ck @ 1.5 bpm
4/3/96	5136'-5156'	Frac D sand as follows: 72,000# of 20/40 sd in 430 bbls of Boragel. Breakdown @ 1601# treated @ avg rate 23.3 bpm, avg press 1750 psi. ISIP-2152 psi, 5-min 2042 psi, Flowback after 5 min on 16/64" ck @ 1bpm.
4/6/96	5414'-5451'	Frac GB-4 sand as follows: 81,600# of 20/40 sd in 453 bbls of Boragel. Breakdown @ 2350, treated @ avg rate 27.5 bpm, avg press 1900 psi. ISIP 2346 psi, 5-min 2339 psi. Flowback after 5 min on 16/64" ch @ 2.1 bpm.

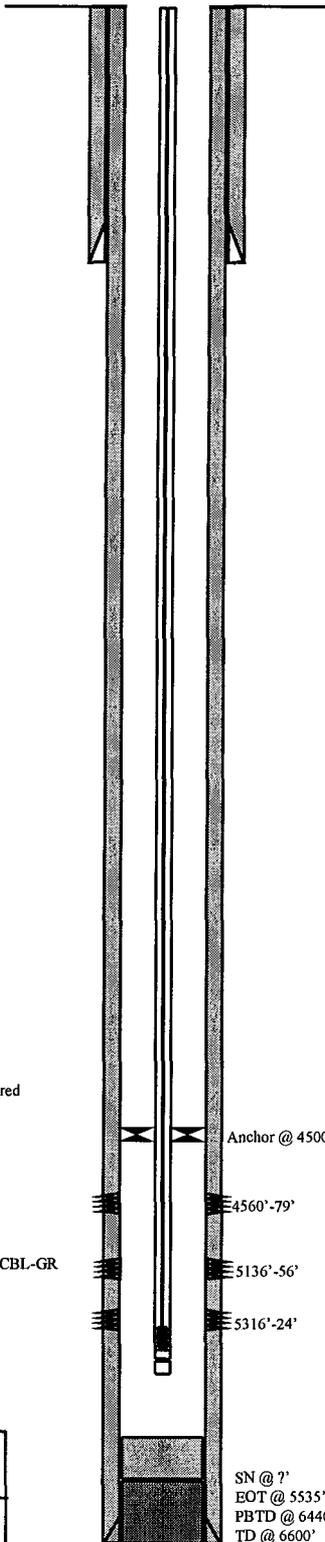

PERFORATION RECORD

3/30/96	5316'-5324'	4 JSPF	32 holes
4/2/96	5136'-5156'	? JSPF	? holes
4/4/96	4560'-4579'	4 JSPF	72 holes



Inland Resources Inc.
Monument Butte Federal #2-25
 679 FNL 1979 FEL
 NWNE Section 25-T8S-R16E
 Duchesne Co, Utah
 API #43-013-31604; Lease #U-67170

Monument Butte Federal #4-25

Spud Date: 7/16/96
 Put on Production: 8/14/96
 GL: 5454' KB: 5467'

Initial Production: 137 BOPD,
 141 MCFPD, 14 BWPD

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 283.00'(7 jts.)
 DEPTH LANDED: 281.40' GL
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt, est 3 bbls to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 151 jts. (6355.35')
 DEPTH LANDED: 6351.35'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 320 sk Hyfill mixed & 360 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING


SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
 NO. OF JOINTS: 202 jts (?)
 TUBING ANCHOR: 5999'
 SEATING NIPPLE: 2-7/8" (1.10')
 TOTAL STRING LENGTH: ? (EOT @ 6104')
 SN LANDED AT: 6034'

SUCKER RODS

POLISHED ROD: 1-1/2" x 22' polished
 SUCKER RODS: 8-1" scraped, 132-3/4" plain rods, 101-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 1-2-1/2" x 1-1/2" x 12 RHAC pump
 STROKE LENGTH: 86"
 PUMP SPEED, SPM: 8 SPM
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR

FRAC JOB

8/2/96	6285'-6290'	Frac CP-5 sand as follows: 68,000# of 20/40 sand in 438 bbls of Boragel. Breakdown @ 2763 psi. Treated @ avg rate of 20.8 w/avg press of 2200 psi. ISIP-2398 psi, 5-min 2156 psi. Flowback on 16/64" ck for 1-1/2 hrs and died.
8/5/96	5147'-5293'	Frac D-1, D-2 & D-3 sands as follows: 138,000# of 20/40 sand in 706 bbls of Boragel. Breakdown @ 1777psi. Treated @ avg rate of 32.5 bpm w/avg press of 1100 psi. ISIP-1900 psi, 5-min 1716 psi. Flowback on 16/64" ck for 2-1/2 hrs and died.
8/7/96	4853'-4864'	Frac PB-10 sand as follows: 61,300# of 20/40 sand in 369 bbls of Boragel. Breakdown @ 1803 psi. Treated @ avg rate of 16.3 bpm w/avg press of 1750 psi. ISIP-2456 psi, 5-min 2362 psi. Flowback on 16/64" ck for 2 hrs and died.
8/9/96	4710'-4717'	Frac GB-6 sand as follows: 68,700# of 209/40 sd in 385 bbls of Boragel. Breakdown @ 2010psi. Treated @ avg rate of 16 bpm w/avg press of 2100 psi. ISIP-2834 psi, 5-min 1763 psi. Flowback on 12/64" ck for 2 hrs and died.

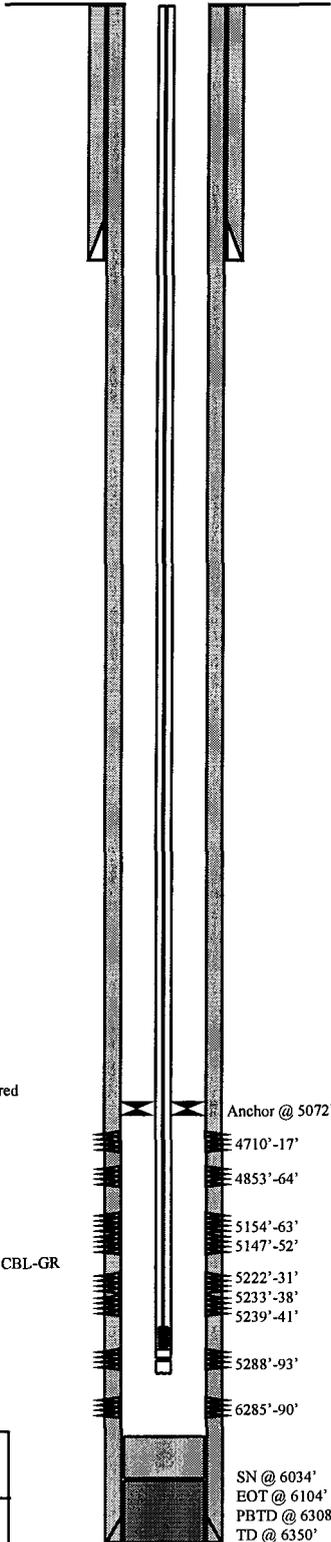

PERFORATION RECORD

Date	Depth Range	Tool Joint	Holes
8/1/96	6285'-6290'	4 JSPF	24 holes
8/3/96	5288'-5293'	4 JSPF	20 holes
8/3/96	5239'-5241'	4 JSPF	8 holes
8/3/96	5233'-5238'	4 JSPF	20 holes
8/3/96	5222'-5231'	4 JSPF	36 holes
8/3/96	5147'-5152'	2 JSPF	10 holes
8/3/96	5154'-5163'	2 JSPF	18 holes
8/6/96	4853'-4864'	4 JSPF	44 holes
8/9/96	4710'-4717'	4 JSPF	32 holes



Inland Resources Inc.

Monument Butte Federal #4-25

660 FWL 660 FNL

NWNW Section 25-T8S-R16E

Duchesne Co, Utah

API #43-013-31639; Lease #U-34346

SN @ 6034'
 EOT @ 6104'
 PBDT @ 6308'
 TD @ 6350'

Monument Butte Federal #5-25

Spud Date: 6/20/96
 Put on Production: 7/23/96
 GL: 5454' KB: 5467'

Initial Production: 23 BOPD,
 156 MCFPD, 5 BWPD

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 296.45'
 DEPTH LANDED: 294.85' GL
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt, est 4 bbls to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 148 jts. (6221.06')
 DEPTH LANDED: 6211.01'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 325 sk Hyfill mixed & 340 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING

SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
 NO. OF JOINTS: 200 jts (?)
 TUBING ANCHOR: 5072'
 SEATING NIPPLE: 2-7/8" (1.10')
 TOTAL STRING LENGTH: ? (EOT @ 5753')
 SN LANDED AT: 5597'


SUCKER RODS

POLISHED ROD: 1-1/2" x 22' SM
 SUCKER RODS: 4-3/4" scraped, 120-3/4" slick rods, 95-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 1-2-1/2" x 1-1/2" x 12 x 15 RHAC pump
 STROKE LENGTH: 81"
 PUMP SPEED, SPM: 6 SPM
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR

FRAC JOB

7/17/96 5613'-5654' **Frac A-3 sand as follows:**
 95,800# of 20/40 sand in 503 bbls of Boragel. Breakdown @ 1460 psi, treated @ avg rate of 24.5 bpm w/ avg press of 1350 psi. ISIP- 1620 psi, 5-min 1527 psi. Flowback on 16/64" ck for 2 hrs and died.

4/21/96 5142'-5160' **Frac D-1 and D-2 sand as follows:**
 83,900# of 20/40 sand in 470 bbls of Boragel. Breakdown @ 1330 psi. Treated @ avg rate of 26 bpm w/ avg press of 2250 psi. ISIP-2143 psi, 5-min 2073 psi. Flowback for 15 on 16/65" ck, rec 4 BW

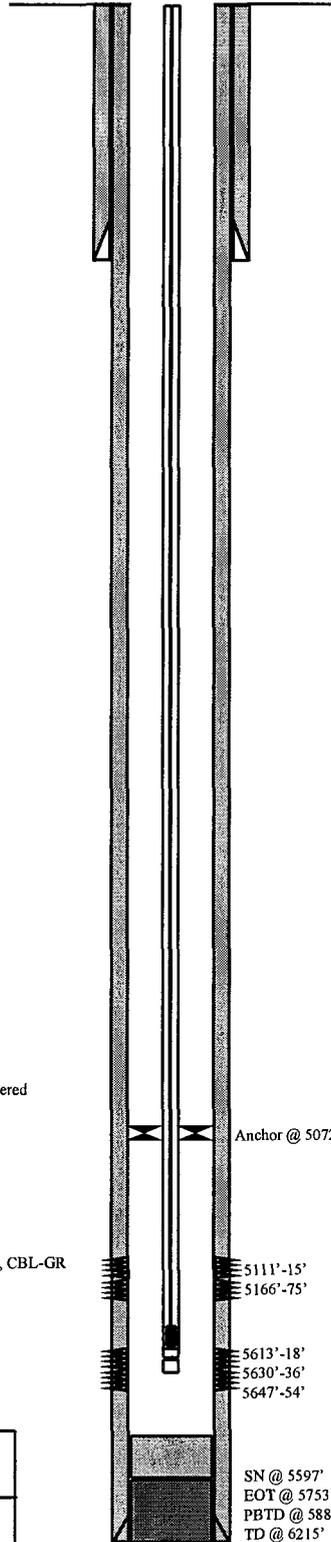

PERFORATION RECORD

Date	Interval	Number of Holes	Notes
7/16/96	5613'-5618'	4 JSPF	20 holes
7/16/96	5630'-5636'	4 JSPF	24 holes
7/16/96	5647'-5654'	4 JSPF	28 holes
7/18/96	5111'-5115'	4 JSPF	16 holes
7/18/96	5166'-5175'	4 JSPF	36 holes

Anchor @ 5072'

5111'-15'
 5166'-75'
 5613'-18'
 5630'-36'
 5647'-54'

SN @ 5597'
 EOT @ 5753'
 PBTB @ 5886'
 TD @ 6215'



Inland Resources Inc.

Monument Butte Federal #5-25

660 FWL 1860 FNL

SWNW Section 25-T8S-R16E

Duchesne Co, Utah

API #43-013-31638; Lease #U-34346

Monument Butte Federal #6-25

Spud Date: 3/6/96
 Put on Production: 3/28/96
 GL: 5467' KB: 5480'

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: ? jts. (305.15')
 DEPTH LANDED: ?'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt, return 6 bbls cmt to surf

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: ? jts. (6294')
 DEPTH LANDED: 6291'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 210 sk Hyfill mixed & 370 sxs thixotropic
 CEMENT TOP AT: 991' per CBL

TUBING

SIZE/GRADE/WT.: 2-7/8" / WC-50 / 6.5#
 NO. OF JOINTS: 193 jts (?)
 TUBING ANCHOR: 6043'
 SEATING NIPPLE: 2-7/8" (1.10')
 TOTAL STRING LENGTH: ? (EOT @ ?)
 SN LANDED AT: ?

SUCKER RODS


POLISHED ROD: 1-1/2" x 22' SM
 SUCKER RODS: 4-3/4" scraped, 138-3/4" slick rods, 95-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 2-1/2" x 1-1/2" x 15' RHAC
 STROKE LENGTH: ?"
 PUMP SPEED, SPM: ? SPM
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR

FRAC JOB

3/20/96 6090'-6098' **Frac CP-2 sand as follows:**
 54,700# 20/40 sd in 427 bbls Boragel.
 Breakdown @ 1586 psi. Prefrac ISIP *NA*.
 Treated @ avg rate 20.5 bpm avg press
 1750 psi, ISIP-2185 psi, 1-min 2113, 2-
 min 2000, 3-min 1986, 4-min 1950, 5-
 min 1941. Start flowback after 5 min. SI
 on 16/64" ck @ 1.8 bpm.

3/22/96 5308'-5316' **Frac C sand as follows:**
 71,400# of 20/40 sd in 452 bbls Boragel.
 Breakdown @ 2352'. Treated @ avg rate
 20 bpm, avg press 1500 psi. ISIP-1692
 psi, 5-min 1200 psi. Flowback after 5
 min on 16/64" ck @ 1.7 bpm.

3/25/96 5122'-5139' **Frac D-1 sand as follows:**
 69,000# 20/40 sd in 421 bbls Boragel.
 Breakdown @ 1525 psi. Treated @ avg
 rate 22 bpm, avg press 1200 psi. ISIP
 1982 psi, 2-min 1908. Flowback w
 16/64" ck @ 1.8 bpm.

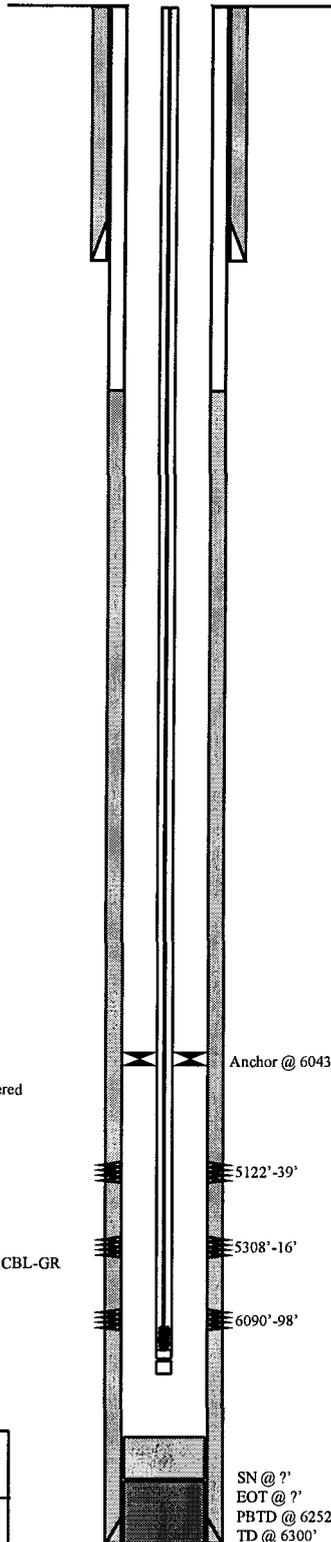

PERFORATION RECORD

3/19/96	6090'-6098'	4 JSPF	32 holes
3/21/96	5308'-5316'	4 JSPF	32 holes
3/23/96	5122'-5139'	4 JSPF	64 holes



Inland Resources Inc.

Monument Butte Federal #6-25

2137 FNL 2101 FWL

SENW Section 25-T8S-R16E

Duchesne Co, Utah

API #43-013-31596; Lease #U-67170

SN @ ?'
 EOT @ ?'
 PBD @ 6252'
 TD @ 6300'

Monument Butte Federal #7-25

Spud Date: 2/9/96
 Put on Production: 3/13/96
 GL: 5457' KB: 5468'

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: ? jts. (306.77')
 DEPTH LANDED: 305.24'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt, 3 bbls to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: ? jts. (6199.78')
 DEPTH LANDED: 6193'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 70 sk Hyfill mixed & 430 sxs thixotropic
 CEMENT TOP AT: 2948 per CBL

TUBING

SIZE/GRADE/WT.: 2-7/8" / WC-50 / 6.5#
 NO. OF JOINTS: 202 jts (6101')
 TUBING ANCHOR: 5891'
 SEATING NIPPLE: 2-7/8" (1.10')
 MUD ANCHOR:
 TOTAL STRING LENGTH: ? (EOT @ 5991')
 SN LANDED AT: 5927'

SUCKER RODS


POLISHED ROD: 1-1/4" x 22' SM
 SUCKER RODS: 4-3/4" scraped, 132-3/4" slick rods, 96-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 2-1/2" x 1-1/2" x 16"
 STROKE LENGTH: 74"
 PUMP SPEED, SPM: 8 SPM
 PUMPING UNIT SIZE: ?
 PRIME MOVER: ?
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR

FRAC JOB

2/28/96	6096'-6110'	Frac CP-2 sand as follows: 43,900# of 20/40 sd in 414 bbls of Boragel, avg rate 24.5, avg press 2100 psi. ISIP 2268 psi, 5-min 2139 psi, 10-min 2100 psi. Flowback @ 1 bpm on 12/64" ck.
3/1/96	5289'-5301'	Frac C sand as follows: 65,200# 20/40 sd in 460 bbls of Boragel brokedown @ 1920, pre-frac ISIP: 1438 psi. Treated @ avg rate 22 bpm @ 1900 psi, ISIP-1989 psi, 5-min 1971 psi, 10-min 1972. Flowback @ 1 bpm for 3 hours until dead.
3/4/96	5133'-5147'	Frac D-1 sand as follows: 72,500# 20/40 sd in 464 bbls of Boragel. Breakdown @ 2034, pre-frac ISIP @ 1105. Treated @ avg rate 20 bpm @ 1850 psi. ISIP 2277, 5-min 2187, 10-min 2154. Flowback @ 1 bpm on 12/64" ck.
3/6/96	4620'-4628'	Frac GB-6 zone as follows: 56,200# of 20/40 sd in 388 bbls of Boragel. Breakdown @ 2356, prefrac ISIP @ 1957 psi treated @ avg rate 20 bpm, avg press 2150. ISIP 2303 psi, 5-min 2276, 10-min 2255. Flowback 1 bom on 12/64" ck.

PERFORATION RECORD

2/27/96	6096'-6110'	4 JSPF	52 holes
2/29/96	5289'-5301'	4 JSPF	44 holes
3/2/96	5133'-5147'	4 JSPF	52 holes
3/5/96	4620'-4628'	4 JSPF	32 holes

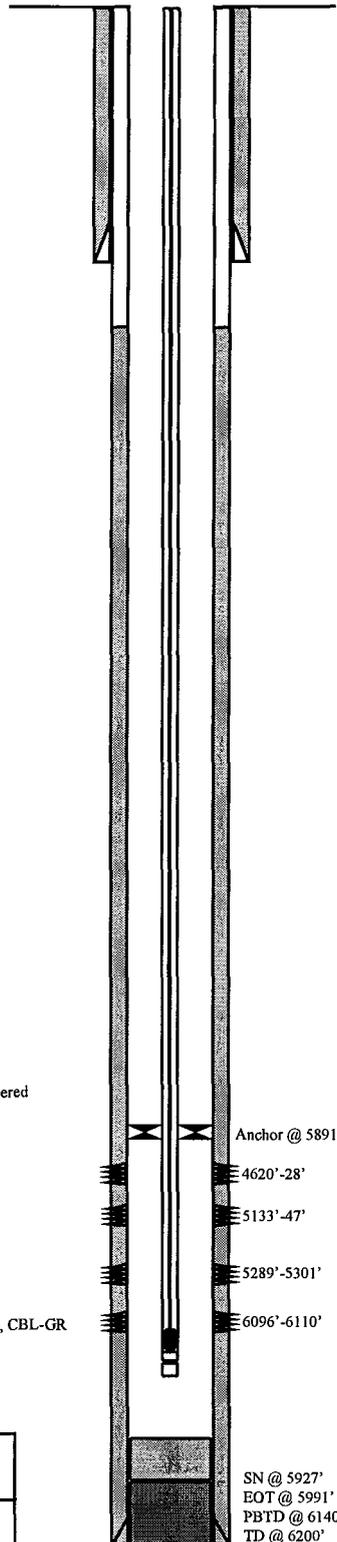



Inland Resources Inc.

Monument Butte Federal #7-25

1980 FNL 1950 FEL

NENE Section 25-T8S-R16E

Duchesne Co, Utah


API #43-013-31561; Lease #U-67170

Monument Butte Federal #11-25

Wellbore Diagram

Well History:

10-28-95	Spud Well
11-22-95	Perf 5,587'-5,599', 5,602'-5,623'
11-23-95	Frac LDC zone as follows: Totals 104,500# 20/40 sd, 29,967 gal Avg TP 2,600 @ 36 BPM ISIP 3,396, after 5 min 2,952
11-27-95	Perf 5,298'-5,305', 5,334'-5,341'
11-28-95	Frac B-1 and B-2 zones as follows: 73,500# 20/40 sd, 25,546 gal Avg TP 2,150 @ 38 BPM ISIP 2,128, after 5 min 2,040
11-29-95	Perf 4,998'-5,010', 5,017'-5,020', 5,023'-5,027', 5,080'-5,088'
11-30-95	Frac D zone as follows: 90,820# 20/40 sd, 29,200 gal Avg TP 1,980 @ 30 BPM ISIP 1,980, after 5 min. 1,920
12-3-95	Put On Production

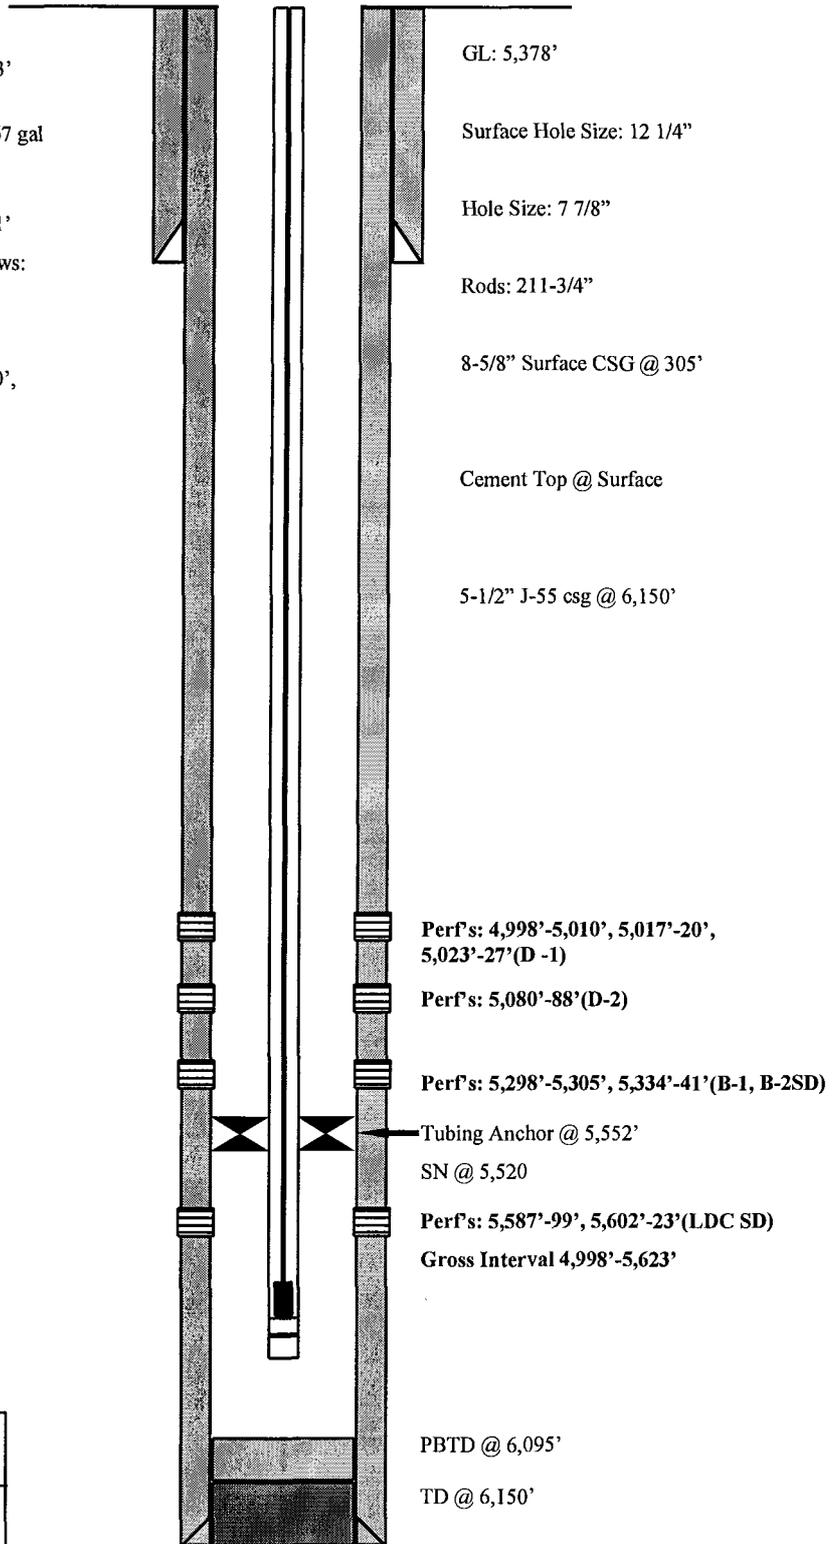

	<p>Inland Resources Inc.</p>
	<p>Monument Butte Federal #11-25 2092 FWL 2074 FSL NESW Section 25-T8S-R16E Duchesne Co, Utah API #43-013-31553; Lease #U-67170</p>

Monument Butte Federal #14-24

Spud Date: 5/29/96
 Put on Production: 8/3/96
 GL: 5430' KB: 5443'

Initial Production: 76 BOPD,
 96 MCFPD, 11 BWPD

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 7 jts.(307.10')
 DEPTH LANDED: 302.10'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt, est 7 bbls to surf.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 149 jts.(6294.61')
 DEPTH LANDED: 6288.61'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 330 sk Hyfill mixed & 390 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING

SIZE/GRADE/WT.: 2-7/8"/6.5#/LS tbg.
 NO. OF JOINTS: 198 jts.
 TUBING ANCHOR: 4667'
 SEATING NIPPLE: 2-7/8" (1.10')
 TOTAL STRING LENGTH: EOT @ 5489'
 SN LANDED AT: 5362'

SUCKER RODS


POLISHED ROD: 1-1/2" x 22' polished rod.
 SUCKER RODS: 4-3/4" scraped, 110-3/4" slick rods, 96-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 2-1/2" x 1-1/2" x 10' x 15' RHAC pump
 STROKE LENGTH: 86"
 PUMP SPEED, SPM: 6 SPM
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR

FRAC JOB

7/25/96 5202'-5392' Frac C, D-3 and D-1 sands as follows:
 138,400# of 20/40 sd in 688 bbls of Boragel. Breakdown @ 2900 psi. Treated @ avg rate of 36 bpm w/avg press of 1970 psi. ISIP-2039 psi., 5-min 1980 psi. Flowback on 16/64" ck for 5 hrs & died.

7/29/96 5072'-5080' Frac XY/DC sand as follows:
 72,900# of 20/40 sd in 401 bbls of Boragel. Breakdown @ 2174 psi. Treated @ avg rate of 20 bpm w/avg press of 2450 psi. ISIP- 2536 psi, 5-min 2409 psi. Flowback on 16/64" ck for 4 hrs until dead.

7/31/96 4711'-4728' Frac GB-6 sand as follows:
 85,300# of 20/40 sd in 401 bbls of Boragel. Breakdown @ 1510 psi. Treated @ avg rate of 20.5 bpm w/avg press of 2500 psi. ISIP-4371 psi, 5-min 3010 psi. Flowback on 16/64" ck. for 3-1/2 hrs until dead.

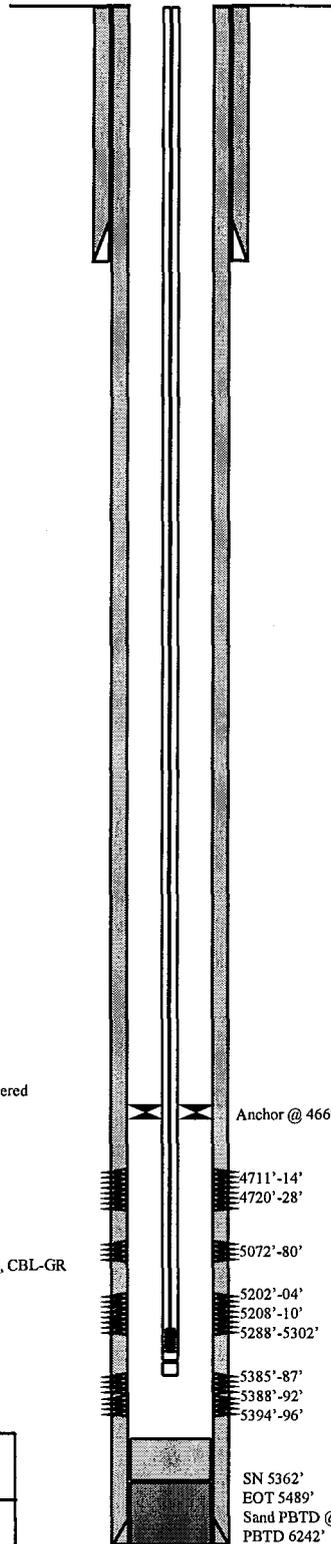

PERFORATION RECORD

7/24/96	5384'-5387'	2 JSFP	4 holes
7/24/96	5388'-5392'	2 JSFP	8 holes
7/24/96	5394'-5396'	2 JSFP	4 holes
7/24/96	5288'-5302'	4 JSFP	56 holes
7/24/96	5202'-5204'	2 JSFP	4 holes
7/24/96	5208'-5210'	2 JSFP	4 holes
7/27/96	5072'-5080'	4 JSFP	32 holes
7/30/96	4711'-4714'	4 JSFP	16 holes
7/30/96	4720'-4728'	4 JSFP	36 holes



Inland Resources Inc.

Monument Butte Federal #14-24

660 FSL 1980 FWL

SESW Section 24-T8S-R16E

Duchesne Co, Utah

API #43-013-31630; Lease #U-67170

Monument Butte Federal #15-24

Spud Date: 5/10/96
 Put on Production: 6/15/96
 GL: 5416' KB: 5429'

Initial Production: 9 BOPD,
 22 MCFPD, 20 BWPD

Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 7 jts.(293.68')
 DEPTH LANDED: 290'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt.

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 148 jts.(6302.63')
 DEPTH LANDED: 6300'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 330 sk Hyfill mixed & 355 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING

SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
 NO. OF JOINTS: 200 jts
 TUBING ANCHOR: 5175'
 SEATING NIPPLE: 2-7/8" (1.10')
 TOTAL STRING LENGTH: ? (EOT @ 6092')
 SN LANDED AT: 6026'


SUCKER RODS

POLISHED ROD: 1-1/2" x 22' polished rod.
 SUCKER RODS: 4-3/4" scraped, 138-3/4" slick rods, 93-3/4" scraped
 TOTAL ROD STRING LENGTH: ?
 PUMP NUMBER: ?
 PUMP SIZE: 2-1/2" x 1-1/2" x ?
 STROKE LENGTH: 86"
 PUMP SPEED, SPM: 7 SPM
 LOGS: Dual Laterlog, GR, SP, Spectral Density-Dual Spaced Neutron, CBL-GR

FRAC JOB

6/6/96 6105'-6173' **Frac CP-2 and CP-1 sands as follows:**
 77,700# 20/40 sd in 437 bbls of Boragel.
 Breakdown @ 1958 psi & treated @ avg
 1480 psi. ISIP-1802 psi, 5-min 1638 psi.
 Flowback on 16/64" ck @ 1.4 bpm 1.5
 hrs until dead.

6/8/96 5213'-5230' **Frac D-1 sand as follows:**
 57,500# 20/40 sd in 433 bbls Boragel.
 Breakdown @ 2113 psi & treated @ avg
 rate 16.5 bpm w/ avg press 1250 psi.
 ISIP-1846 psi, 5-min 1573 psi. Flowback
 on 16/64" ck. 1-1/2 hrs until dead.

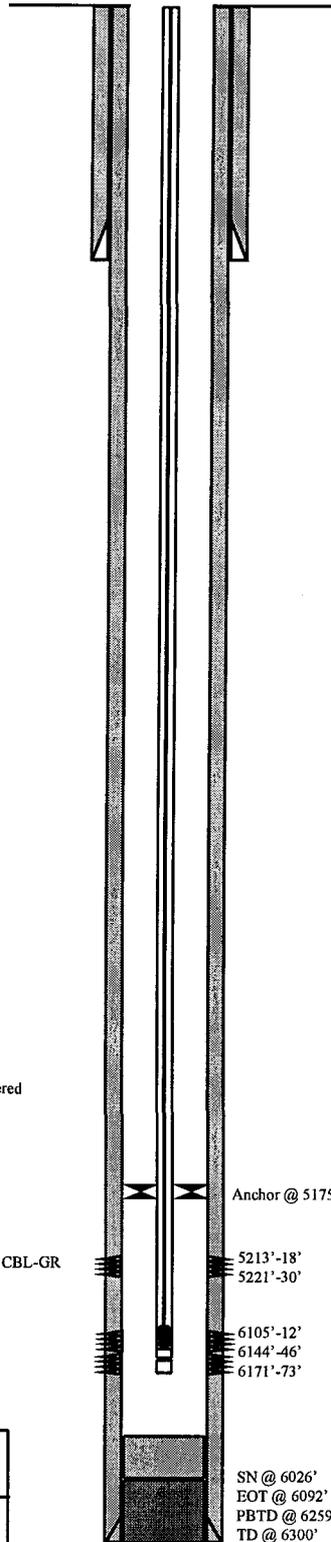

PERFORATION RECORD

6/5/96	6171'-6173'	4 JSPF	4 holes
6/5/96	6144'-6146'	4 JSPF	8 holes
6/5/96	6105'-6112'	4 JSPF	28 holes
6/7/96	5221'-2130'	4 JSPF	20 holes
6/7/96	5213'-5218'	4 JSPF	36 holes



Inland Resources Inc.

Monument Butte Federal #15-24

660 FSL 1980 FEL

SWSE Section 24-T8S-R16E

Duchesne Co, Utah

API #43-013-31628; Lease #U-67170

UNICHEM

A Division of BJ Services

Exhibit "F"

P.O. Box 217
Roosevelt, Utah 84066

Office (801) 722-5066
Fax (801) 722-5727


WATER ANALYSIS REPORT

Company INLAND Address _____ Date 10-22-96
Source 3-25 Date Sampled _____ Analysis No. _____

	Analysis	mg/l(ppm)	*Meg/l
1. PH	<u>8.9</u>		
2. H ₂ S (Qualitative)	<u>0.5</u>		
3. Specific Gravity	<u>1.014</u>		
4. Dissolved Solids		<u>25,359</u>	
5. Alkalinity (CaCO ₃)		<u>840</u>	
6. Bicarbonate (HCO ₃)		<u>2,600</u>	÷ 61 <u>43</u> HCO ₃
7. Chlorides (Cl)		<u>13,200</u>	÷ 35.5 <u>372</u> Cl
8. Sulfates (SO ₄)		<u>0</u>	÷ 48 <u>0</u> SO ₄
9. Calcium (Ca)		<u>6</u>	÷ 20 <u>0</u> Ca
10. Magnesium (Mg)		<u>0</u>	÷ 12.2 <u>0</u> Mg
11. Total Hardness (CaCO ₃)		<u>15</u>	
12. Total Iron (Fe)		<u>0.7</u>	
13. Manganese			
14. Barium (Qualitative)			
15. Phosphate Residuals			

*Milli equivalents per liter

PROBABLE MINERAL COMPOSITION



Compound	Equiv. Wt.	X	Meg/l	=	Mg/l
Ca(HCO ₃) ₂	81.04				
CaSO ₄	68.07				
CaCl ₂	55.50				
Mg(HCO ₃) ₂	73.17				
MgSO ₄	60.19				
MgCl ₂	47.62				
NaHCO ₃	84.00		<u>43</u>		<u>3,612</u>
Na ₂ SO ₄	71.03				
NaCl	58.46		<u>372</u>		<u>21,747</u>

Saturation Values	Distilled Water 20°C
CaCO ₃	13 Mg/l
CaSO ₄ · 2H ₂ O	2,090 Mg/l
MgCO ₃	103 Mg/l

REMARKS _____

Exhibit "F-1"

AQUAMIX SCALING PREDICTIONS

COMPANY: INLAND
 LOCATION:
 SYSTEM:

10-22-96

WATER DESCRIPTION:	5-35 TRIPLEX	3-25
P-ALK AS PPM CaCO3	100	840
M-ALK AS PPM CaCO3	610	2600
SULFATE AS PPM SO4	0	0
CHLORIDE AS PPM Cl	750	13200
HARDNESS AS PPM CaCO3	130	15
CALCIUM AS PPM CaCO3	16	6
MAGNESIUM AS PPM CaCO3	22	0
SODIUM AS PPM Na	644	9545
BARIUM AS PPM Ba	0	0
STRONTIUM AS PPM Sr	0	0
CONDUCTIVITY	0	0
TOTAL DISSOLVED SOLIDS	2043	25359
TEMP (DEG-F)	100	100
SYSTEM pH	7.8	8.9

WATER COMPATIBILITY CALCULATIONS
 5-35 TRIPLEX AND 3-25
 CONDITIONS: TEMP.=100 AND pH=8.4
 WATER ONE IS 5-35 TRIPLEX

o/o OF WATER # 1	STIFF DAVIS CaCO3 INDEX	lbs/1000 BBL EXCESS CaCO3	mg/l BaSO4 IN EXCESS OF SATURATION	mg/l SrO4 IN EXCESS OF SATURATION	mg/l Gypsum IN EXCESS OF SATURATION
100	.36	3	0	0	0
90	.33	2	0	0	0
80	.28	2	0	0	0
70	.20	1	0	0	0
60	.12	0	0	0	0
50	.05	0	0	0	0
40	0	0	0	0	0
30	-.05	0	0	0	0
20	-.12	0	0	0	0
10	-.19	0	0	0	0
0	-.28	0	0	0	0

DIVISION OF OIL, GAS AND MINING
UNDERGROUND INJECTION CONTROL PROGRAM

**PERMIT
STATEMENT OF BASIS**

Applicant: Inland Production company

Unit: Mon. Butte NE

Location: Secs. 22,25 & 26, T.8S., R.16 E.

Ownership Issues: The Monument Butte North East Unit was approved by the Board of Oil, Gas and Mining on March 5, 1996 (Cause No. 213-3). The Monument Butte North East Unit was approved for increased ultimate recovery of oil. Selected intervals in the Green River Formation will be perforated for water injection. The surface within the unit area and within a one-half mile around the unit is owned by the Federal Government (BLM) and the State School Trust(SITLA). Inland Production holds all of the leases in the unit area. There are numerous interest owners in the unit and on surrounding leases.

Well Integrity: Existing and proposed injection wells generally have surface casing set at approximately 300 feet and are cemented to surface. Production casing is generally set between 6000 feet and 6300 feet. Cement tops on production casing on existing wells varies and range from 3000 feet below surface to surface. It is the practice of the operator to use sufficient quantities of cement on newly drilled wells to bring cement to surface. A review of bond logs on existing wells shows concurrence with reported cement tops. On newly drilled wells cement tops are sometimes difficult to determine because the operator has been using a highlift light cement as a lead cement. This cement has low compressive strength and does not show up as good bond on a CBL. Cement tops at 3000 feet and above are adequate to insure mechanical integrity considering the injection zones are generally at 4000 feet and below. A 2 7/8 inch or 2 3/8 inch tubing shall be utilized. A retrievable packer will be placed approximately 50 feet above the uppermost perforation. A casing test will be performed at the time of conversion and a casing\tubing pressure test will be conducted prior to commencing injection. Subsequent pressure tests will be conducted at least every five years or any time a packer is pulled or there has been a loss of mechanical integrity.

Ground Water Protection: The base of moderately saline water is at a depth of approximately 1300 feet to 2000 feet in the Monument Butte North East Unit area. These water zones are found in sands in the Uinta Formation and upper sands of the Green River Formation and are generally discontinuous and not subject to direct recharge. Aquifers with high quality water are rarely encountered and are of limited

extent. A review of the records indicates that there are no water wells in the area of the project. Confining intervals above and below the proposed injection zone consists of tight lacustrine shales and limestones. An analysis was submitted for the water present in the injection zone. The total dissolved solids content was over 11,000 mg/l. The injection zone is not classified as an underground source of drinking water (USDW). The water to be injected comes from the Johnson Water Company and has a TDS of approximately 2500 mg/l. Injection of this water into the proposed injection zone will not degrade any aquifers.

Producing wells in the area of review generally have adequate casing and cement to protect and isolate water of differing quality. At the time an application is received for a proposed injection well, a review of all wells in a one-half mile radius will be conducted to determine if corrective action is needed .

Oil/Gas & Other Mineral Resources Protection: All correlative rights and mineral interests issues were addressed at the time the waterflood unit came before the board.


Bonding: Wells within the unit are on federal surface and are bonded with the BLM.

Actions Taken and Further Approvals Needed: A notice of agency action was sent to both the Salt Lake Tribune and the Uinta Basin Standard for the Monument Butte Federal North East Unit 15-24, 1-25, 3-25, 7-25, 9-25 and 15-26 wells. Applications for all of the above wells have been received. BLM approval of the wells will be required under applicable onshore orders. A final permit will be issued on wells after all conditions of approval and stipulations are met as outlined on the approval to convert letter. An individual statement of basis addendum will be prepared for each well subsequently approved for conversion.

Note: Applicable technical publications concerning water resources in the general vicinity of this project have been reviewed and taken into consideration during the permit review process.

Reviewer(s): D. Jarvis Date: 10/24/96

UBS 11/12/96

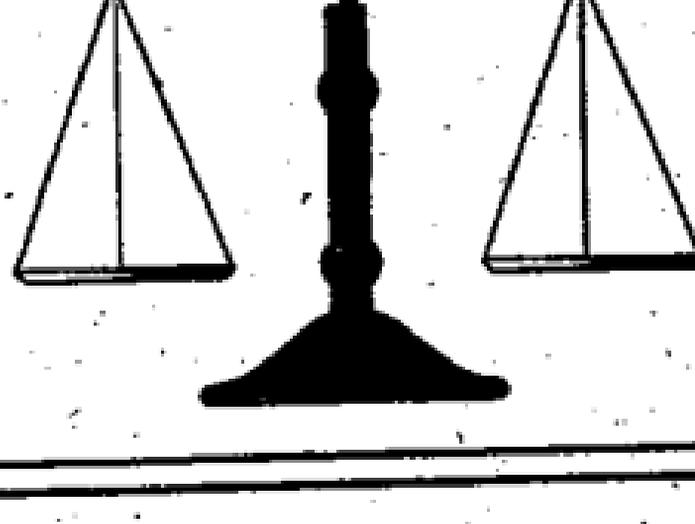

NOTICE OF AGENCY ACTION

**CAUSE NO. UIC-184
IN THE MATTER OF
THE APPLICATION OF
INLAND PRODUCTION
COMPANY FOR AD-
MINISTRATIVE AP-
PROVAL OF THE
MONUMENT BUTTE
FEDERAL 7-25 AND 3-
25 WELLS LOCATED IN
SECTION 25, TOWN-
SHIP 8 SOUTH, RANGE
16 EAST, S.L.M.,
DUCHESNE COUNTY,
UTAH, AS CLASS II IN-
JECTION WELLS**

**THE STATE OF UTAH
TO ALL PERSONS IN-
TERESTED IN THE
ABOVE ENTITLED
MATTER.**

Notice is hereby given that the Division of Oil, Gas and Mining (the "Division") is commencing an informal adjudicative proceeding to consider the application of Inland Production Company for administrative approval of the Monument Butte Federal 7-25 and 3-25 wells, located in Section 25, Township 8 South, Range 16 East, S.L.M., Duchesne County, Utah, for conversion to Class II injection wells. The proceeding will be conducted in accordance with Utah Admin. R.649-10, Administrative Procedures.

The interval from 4300 feet to 6000 feet (Green River Formation) will be selectively perforated for water injection. The maximum injection pressure will be limited to 2000 PSIG with a maximum rate of 1000 BWPD.

Any person desiring to object to the application or otherwise intervene in the proceeding,s must file a written protest or notice of intervention with the Division within fifteen

BEFORE THE DIVISION OF OIL, GAS AND MINING
DEPARTMENT OF NATURAL RESOURCES
STATE OF UTAH

---ooOoo---

IN THE MATTER OF THE	:	NOTICE OF AGENCY
APPLICATION OF INLAND	:	ACTION
PRODUCTION COMPANY FOR	:	
ADMINISTRATIVE APPROVAL OF	:	CAUSE NO. UIC-184
THE MONUMENT BUTTE FEDERAL	:	
7-25 AND 3-25 WELLS LOCATED IN	:	
SECTION 25, TOWNSHIP 8 SOUTH,	:	
RANGE 16 EAST, S.L.M.,	:	
DUCHESNE COUNTY, UTAH, AS	:	
CLASS II INJECTION WELLS	:	

---ooOoo---

THE STATE OF UTAH TO ALL PERSONS INTERESTED IN THE ABOVE ENTITLED MATTER.


Notice is hereby given that the Division of Oil, Gas and Mining (the "Division") is commencing an informal adjudicative proceeding to consider the application of Inland Production Company for administrative approval of the Monument Butte Federal 7-25 and 3-25 wells, located in Section 25, Township 8 South, Range 16 East, S.L.M., Duchesne County, Utah, for conversion to Class II injection wells. The proceeding will be conducted in accordance with Utah Admin. R.649-10, Administrative Procedures.

The interval from 4300 feet to 6000 feet (Green River Formation) will be selectively perforated for water injection. The maximum injection pressure will be limited to 2000 PSIG with a maximum rate of 1000 BWPD.

Any person desiring to object to the application or otherwise intervene in the proceeding, must file a written protest or notice of intervention with the Division within fifteen days following publication of this notice. If such a protest or notice of intervention is received, a hearing will be scheduled before the Board of Oil, Gas and Mining. Protestants and/or intervenors should be prepared to demonstrate at the hearing how this matter affects their interests.

Dated this 6th day of November 1996.

STATE OF UTAH
DIVISION OF OIL, GAS & MINING



R. J. Firth
Associate Director, Oil & Gas

Inland Production Company
Monument Butte Federal 7-25 and 3-25 Wells
Cause No. UIC-184

Publication Notices were sent to the following:

Inland Production Company
P. O. Box 1446
Roosevelt, Utah 84066

Newspaper Agency Corporation
Legal Advertising
Tribune Building, Front Counter
143 South Main
Salt Lake City, Utah 84111

Uintah Basin Standard
268 South 200 East
Roosevelt, Utah 84066

Vernal District Office
Bureau of Land Management
170 South 500 East
Vernal, Utah 84078

U.S. Environmental Protection Agency
Region VIII
Attn. Dan Jackson
999 18th Street
Denver, Colorado 80202-2466


Lorraine Platt
Secretary
November 6, 1996



State of Utah
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

Michael O. Leavitt
Governor
Ted Stewart
Executive Director
James W. Carter
Division Director

355 West North Temple
3 Triad Center, Suite 350
Salt Lake City, Utah 84180-1203
801-538-5340
801-359-3940 (Fax)
801-538-5319 (TDD)

November 6, 1996

Newspaper Agency Corporation
Legal Advertising
Tribune Building, Front Counter
143 South Main
Salt Lake City, Utah 84111

Re: Notice of Agency Action - Cause No. UIC-184

Gentlemen:

Enclosed is a copy of the referenced Notice of Agency Action. Please publish the Notice, once only, as soon as possible. Please send proof of publication and billing to the Division of Oil, Gas and Mining, 1594 West North Temple, Suite 1210, P.O. Box 145801, Salt Lake City, Utah 84114-5801.

Sincerely,

Lorraine Platt

Lorraine Platt
Secretary

Enclosure





State of Utah
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

Michael O. Leavitt
Governor
Ted Stewart
Executive Director
James W. Carter
Division Director

355 West North Temple
3 Triad Center, Suite 350
Salt Lake City, Utah 84180-1203
801-538-5340
801-359-3940 (Fax)
801-538-5319 (TDD)

November 6, 1996

Uintah Basin Standard
268 South 200 East
Roosevelt, Utah 84066

Re: Notice of Agency Action - Cause No. UIC-184

Gentlemen:

Enclosed is a copy of the referenced Notice of Agency Action. Please publish the Notice, once only, as soon as possible. Please send proof of publication and billing to the Division of Oil, Gas and Mining, 1594 West North Temple, Suite 1210, P.O. Box 145801, Salt Lake City, Utah 84114-5801.

Sincerely,

A handwritten signature in cursive script that reads "Lorraine Platt".

Lorraine Platt
Secretary

Enclosure



143 SOUTH MAIN ST.
 P. O. BOX 45838
 SALT LAKE CITY, UTAH 84145
 FED. TAX I. D. # 87-0217663

Newspaper Agency Corporation
 The Salt Lake Tribune  DESERET NEWS

CUSTOMER'S
 COPY

PROOF OF PUBLICATION

CUSTOMER NAME AND ADDRESS	ACCOUNT NUMBER	DATE
DIV OF OIL, GAS & MINING 1594 W NORTH TEMPLE STE # 1210 SALT LAKE CITY UT 84114	D5385340L-07	11/14/96

ACCOUNT NAME	
DIV OF OIL, GAS & MINING	
TELEPHONE	INVOICE NUMBER
801-538-5340	TLBB8200461
SCHEDULE	
START 11/14/96 END 11/14/96	
CUST. REF. NO.	
UIC-184	
CAPTION	
NOTICE OF AGENCY ACTION CAUSE N	
SIZE	
73 LINES 1.00 COLUMN	
TIMES	RATE
1	1.64
MISC. CHARGES	AD CHARGES
.00	119.72
TOTAL COST	
119.72	

OFFICE COPY

NOTICE OF AGENCY ACTION
 CAUSE NO. UIC-184
 BEFORE THE DIVISION OF OIL,
 GAS AND MINING
 DEPARTMENT OF NATURAL
 RESOURCES, STATE OF UTAH

IN THE MATTER OF THE APPLICATION OF INLAND PRODUCTION COMPANY FOR ADMINISTRATIVE APPROVAL OF THE MONUMENT BUTTE FEDERAL 7-25 AND 3-25 WELLS LOCATED IN SECTION 25, TOWNSHIP 8 SOUTH, RANGE 16 EAST, S.L.M., DUCHESNE COUNTY, UTAH, AS CLASS II INJECTION WELLS.

THE STATE OF UTAH TO ALL PERSONS INTERESTED IN THE ABOVE ENTITLED MATTER.

Notice is hereby given that the Division of Oil, Gas and Mining (the "Division") is commencing an informal adjudicative proceeding to consider the application of Inland Production Company for administrative approval of the Monument Butte Federal 7-25 and 3-25 wells, located in Section 25, Township 8 South, Range 16 East, S.L.M. Duchesne County, Utah, for conversion to Class II injection wells. The proceeding will be conducted in accordance with Utah Admin. R. 649-10, Administrative Procedures.

The interval from 4300 feet to 6000 feet (Green River Formation) will be selectively perforated for water injection. A maximum requested injection pressure will be limited to 2000 PSIG with a maximum rate of 1000 BWPD.

Any person desiring to object to the application or otherwise intervene in the proceeding, must file a written protest or notice of intervention with the Division within fifteen days following publication of this notice. If such a protest or notice of intervention is received, a hearing will be scheduled before the Board of Oil, Gas and Mining. Protestants and/or intervenors should be prepared to demonstrate at the hearing how this matter affects their interests.

DATED this 6th day of November, 1996.

STATE OF UTAH
 DIV. OF OIL, GAS AND MINING
 R. J. Fifth
 Associate Director, Oil & Gas
 BB820040

AFFIDAVIT OF PUBLICATION

AS NEWSPAPER AGENCY CORPORATION LEGAL BOOKKEEPER, I CERTIFY THAT ADVERTISEMENT OF NOTICE OF AGENCY ACTION CAUSE N DIV OF OIL, GAS & MINING WAS PUBLISHED BY THE NEWS CORPORATION, AGENT FOR THE SALT LAKE TRIBUNE AND DESERET NEWS, DA, PRINTED IN THE ENGLISH LANGUAGE WITH GENERAL CIRCULATION IN UTAH, IN SALT LAKE CITY, SALT LAKE COUNTY IN THE STATE OF UTAH.

PUBLISHED ON START 11/14/96 END 11/14/96

SIGNATURE *Joan Money*

DATE 11/14/96



THIS IS NOT A STATEMENT BUT A "PROOF OF PUBLICATION"
 PLEASE PAY FROM BILLING STATEMENT.



State of Utah
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

Michael O. Leavitt
Governor

Ted Stewart
Executive Director

James W. Carter
Division Director

355 West North Temple
3 Triad Center, Suite 350
Salt Lake City, Utah 84180-1203
801-538-5340
801-359-3940 (Fax)
801-538-5319 (TDD)

December 16, 1996

Inland Production Company
P. O. Box 1446
Roosevelt, Utah 84079

Re: Monument Butte Federal 7-25 and monument Butte Federal 3-25 wells, Section 25, Township 8 South, Range 16 East, Duchesne County, Utah


Gentlemen:

Pursuant to Utah Admin. Code R649-5-3-3, the Division of Oil, Gas and Mining (the "Division") issues its administrative approval for conversion of the referenced wells to Class II injection wells. Accordingly, the following stipulations shall apply for full compliance with this approval:

1. Compliance with all applicable requirements for the operation, maintenance and reporting for Underground Injection Control ("UIC") Class II injection wells pursuant to Utah Admin. Code R649-1 et seq.
2. Conformance with all conditions and requirements of the complete application submitted by Inland Production Company.

If you have any questions regarding this approval or the necessary requirements, please contact Dan Jarvis at this office.

Sincerely,


R.J. Firth
Associate Director

cc: Dan Jackson, Environmental Protection Agency
Bureau of Land Management, Vernal





State of Utah
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

Michael O. Leavitt
Governor

Ted Stewart
Executive Director

James W. Carter
Division Director

355 West North Temple
3 Triad Center, Suite 350
Salt Lake City, Utah 84180-1203
801-538-5340
801-359-3940 (Fax)
801-538-5319 (TDD)

UNDERGROUND INJECTION CONTROL PERMIT


Cause No. UIC-184

Operator: Inland Production Company
Wells: Monument Butte Federal 7-25 and Monument Butte
Federal 3-25
Location: Section 25, Township 8 South, Range 16 East,
County: Duchesne
API No.: 43-013-31561 and 43-013-31605
Well Type: Enhanced Recovery (waterflood)

Stipulations of Permit Approval

1. Approval for conversion to Injection Well issued on December 16, 1996
2. Maximum Allowable Injection Pressure: 2000 psig
3. Maximum Allowable Injection Rate: (restricted by pressure limitation)
4. Injection Interval: 4300 feet to 6000 feet (Green River Formation)

Approved by:



R.J. Firth
Associate Director, Oil and Gas



Date



UNITED STATES DEPARTMENT OF THE INTERIOR BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or deepen or reentry to a different reservoir. Use "APPLICATION FOR PERMIT -" for such proposals

5. Lease Designation and Serial No. U-67170
6. If Indian, Allottee or Tribe Name
7. If unit or CA, Agreement Designation
8. Well Name and No. Mon. Butte Fed. #3-25
9. API Well No. 43-013-31605
10. Field and Pool, or Exploratory Area Monument Butte
11. County or Parish, State Duchesne, UT

SUBMIT IN TRIPLICATE

1. Type of Well [X] Oil Well [] Gas well [] Other
2. Name of Operator Inland Production Company
3. Address and Telephone No. P.O. Box 790233 Vernal, UT 84079 Phone No. (801) 789-1866
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) NE/NW Sec. 25, T8S, R16E

12 CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA


Table with 2 columns: TYPE OF SUBMISSION and TYPE OF ACTION. Includes checkboxes for Notice of Intent, Subsequent Report, Final Abandonment Notice, Abandonment, Recompletion, Plugging Back, Casing repair, Altering Casing, Other, Change of Plans, New Construction, Non-Routine Fracturing, Water Shut-off, Conversion to Injection, and Dispose Water.

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work)

Weekly Status Report for week of 1/21/96 - 1/23/96:

Unseat pump. ND wellhead. On Injection 1/28/97

See attached csg integrity test.



14. I hereby certify that the foregoing is true and correct

Signed Cheryl Cameron Title Regulatory Compliance Specialist Date 1/30/97

(This space of Federal or State office use.)

Approved by Title Date
Conditions of approval, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly to make to any department of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*See Instruction on Reverse Side

NO tax credit 1/98

CASING INTEGRITY TEST

1/28/97

Monument Butte Federal #3-25

NE/NW Sec, 25, T8S, R16E

Duchesne County, Utah

API # 43-013-31605

0 MIN	1260 PSIG
10 MIN	1260 PSIG
20 MIN	1260 PSIG
30 MIN	1260 PSIG
40 MIN	1260 PSIG
50 MIN	1260 PSIG
60 MIN	1260 PSIG
70 MIN	1260 PSIG
80 MIN	1260 PSIG
90 MIN	1260 PSIG
100 MIN	1260 PSIG
120 MIN	1260 PSIG

TUBING PRESSURE 0 PSI

TEST CONDUCTED BY RODDIE BIRD/INLAND PRODUCTION COMPANY

UNITED STATES DEPARTMENT OF THE INTERIOR BUREAU OF LAND MANAGEMENT

FORM APPROVED

Budget Bureau No. 1004-0135

Expires March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or deepen or reentry to a different reservoir. Use "APPLICATION FOR PERMIT -" for such proposals

SUBMIT IN TRIPLICATE

1. Type of Well

[X] Oil Well [] Gas well [] Other

2. Name of Operator

Inland Production Company

3. Address and Telephone No.

P.O. Box 790233 Vernal, UT 84079 Phone No. (801) 789-1866

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

NE/NW Sec. 25, T8S, R16E

5. Lease Designation and Serial No.

U-67170

6. If Indian, Allottee or Tribe Name

7. If unit or CA, Agreement Designation

8. Well Name and No.

Mon. Butte Fed. #3-25

9. API Well No.

43-013-31605

10. Field and Pool, or Exploratory Area

Monument Butte

11. County or Parish, State

Duchesne, UT

12. CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION

TYPE OF ACTION

[X] Notice of Intent

[] Subsequent Report

[] Final Abandonment Notice

[] Abandonment

[] Recompletion

[] Plugging Back

[] Casing repair

[] Altering Casing

[] Other

[] Change of Plans

[] New Construction

[] Non-Routine Fracturing

[] Water Shut-off


[X] Conversion to Injection

[] Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work)

Inland Production Company requests authorization to convert the Monument Butte Federal 3-25 from a producing well to an injection well.



14. I hereby certify that the foregoing is true and correct

Signed Cheryl Cameron

Title Regulatory Compliance Specialist

Date 12/6/96

(This space of Federal or State office use.)

Approved by

Title

Date

Conditions of approval, if any:


Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly to make to any department of the United States any false, fictitious or fraudulent statements or representations as

to any matter within its jurisdiction.



February 27, 1997

Bureau of Land Management
Vernal District Office
170 South 500 East
Vernal, Utah 84078



**ATTENTION: Ed Forsman
Wayne Bankert**

Gentlemen,

Enclosed are the original's and two copies (each) of the following Sundry Notices and Reports on Wells: (copies will also be submitted to the State of Utah)

~~Monument Butte Federal 1-34~~
~~Monument Butte Federal 3-25~~
~~MBFNE 13-26~~
Tar Sands Federal 16-30

~~Monument Butte Federal 3A-35~~
~~MBFNE 11-26~~
~~MBFNE 7-26~~

Please contact me in the Vernal Branch office (801) 789-1866 (P.O. Box 790233, Vernal, UT, 84079,) if you have any questions, or need additional information.

Sincerely,
Cheryl Cameron
Cheryl Cameron
Regulatory Compliance Specialist

cc:

Mike Hebertson
State of Utah
Division of Oil, Gas & Mining
P.O. Box 145801
Salt Lake City, Utah 84114-5801

Enclosures

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires: March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry a different reservoir.
Use "APPLICATION FOR PERMIT -" for such proposals

5. Lease Designation and Serial No.
U-67170

6. If Indian, Allottee or Tribe Name
NA

7. If Unit or CA, Agreement Designation
NA

8. Well Name and No.
MONUMENT BUTTE FEDERAL 3-25

9. API Well No.
43-013-31605

10. Field and Pool, or Exploratory Area
MONUMENT BUTTE

11. County or Parish, State
DUCHESNE COUNTY, UTAH

SUBMIT IN TRIPLICATE

1. Type of Well

Oil Well Gas Well Other **Injector**

2. Name of Operator
INLAND PRODUCTION COMPANY

3. Address and Telephone No.
475 17TH STREET, SUITE 1500, DENVER, COLORADO 80202 (303) 292-0900

4. Location of Well (Footage, Sec., T., R., m., or Survey Description)
0756 FNL 1946 FWL NE/NW Section 25, T08S R16E


12. CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION
<input checked="" type="checkbox"/> Notice of Intent <input type="checkbox"/> Subsequent Report <input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Abandonment <input type="checkbox"/> Recompletion <input type="checkbox"/> Plugging Back <input type="checkbox"/> Casing Repair <input type="checkbox"/> Altering Casing <input checked="" type="checkbox"/> Other Injection Rate
	<input type="checkbox"/> Change of Plans <input type="checkbox"/> New Construction <input type="checkbox"/> Non-Routine Fracturing <input type="checkbox"/> Water Shut-Off <input type="checkbox"/> Conversion to Injection <input type="checkbox"/> Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

The Monument Butte Federal 3-25 has not pressured up, thus Inland Production Company is unable to conduct a Step Rate Test at this time. The well will be re-evaluated in six months. Inland will continue to use the existing maximum pressure.



14. I hereby certify that the foregoing is true and correct

Signed *Kenneth H. Adams* Title Engineering Technician Date 11/14/97

(This space for Federal or State office use)

Approved by _____ Title _____ Date _____

Conditions of approval, if any:
CC: UTAH DOGM

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS, AND MINING

1. SUNDRY NOTICES AND REPORTS ON WELLS		5. LEASE DESIGNATION AND SERIAL NO. U-67170	
(Do not use this form for proposals to drill or to deepen or plug back to a different reservoir. Use "APPLICATION FOR PERMIT--" for such proposals.)		6. IF INDIAN, ALLOTTEE OR TRIBAL NAME N/A	
		7. UNIT AGREEMENT NAME NA	
OIL WELL <input type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER <input checked="" type="checkbox"/> Injection		8. FARM OR LEASE NAME MON BUTTE FED 3-25-8-16	
2. NAME OF OPERATOR INLAND PRODUCTION COMPANY		9. WELL NO. MON BUTTE FED 3-25-8-16	
3. ADDRESS OF OPERATOR Rt. 3 Box 3630, Myton Utah 84052 435-646-3721		10. FIELD AND POOL, OR WILDCAT MONUMENT BUTTE	
4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.* See also space 17 below.) At surface NE/NW Section 25, T08S R16E 756 FNL 1946 FWL		11. SEC., T., R., M., OR BLK. AND SURVEY OR AREA NE/NW Section 25, T08S R16E	
		12. COUNTY OR PARISH DUCHESNE	13. STATE UT
14. API NUMBER 43-013-31605	15. ELEVATIONS (Show whether DF, RT, GR, etc.) 5432 GR		

16. Check Appropriate Box To Indicate Nature of Notice, Report, or Other Data

NOTICE OF INTENTION TO:		SUBSEQUENT REPORT OF:	
TEST WATER SHUT-OFF <input type="checkbox"/>	PULL OR ALTER CASING <input type="checkbox"/>	WATER SHUT-OFF <input type="checkbox"/>	REPAIRING WELL <input type="checkbox"/>
FRACTURE TREAT <input type="checkbox"/>	MULTIPLE COMPLETE <input type="checkbox"/>	FRACTURE TREATMENT <input type="checkbox"/>	ALTERING CASING <input type="checkbox"/>
SHOOT OR ACIDIZE <input type="checkbox"/>	ABANDON* <input type="checkbox"/>	SHOOTING OR ACIDIZING <input type="checkbox"/>	ABANDONMENT* <input type="checkbox"/>
REPAIR WELL <input type="checkbox"/>	<input type="checkbox"/>	(OTHER) <input checked="" type="checkbox"/> 5 Year MIT	
(OTHER) <input type="checkbox"/>	<input type="checkbox"/>	(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)	

17 DESCRIBE PROPOSED OR COMPLETED OPERATIONS. (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

A 5 year MIT was conducted on the subject well. On 12/7/01 Mr. Dennis Ingram W/ State DOGM was contacted and set up a time to conduct the MIT on the casing. On 12/12/01 the casing was pressured to 1150 psi w/ no pressure loss charted in the 1/2 hour test. No governmental agencies were able to witness the test.

COPY SENT TO OPERATOR
 Date: 12-19-01
 Initials: CR

**Accepted by the
Utah Division of
Oil, Gas and Mining**
 Date: 12-18-01
 By: [Signature]

RECEIVED
 DEC 14 2001
 DIVISION OF
OIL, GAS AND MINING

18 I hereby certify that the foregoing is true and correct

SIGNED Krishna Russell TITLE Production Clerk DATE 12/13/01
 Krishna Russell

cc: BLM
(This space for Federal or State office use)

APPROVED BY _____ TITLE _____ DATE _____
 CONDITIONS OF APPROVAL, IF ANY:

Mechanical Integrity Test Casing or Annulus Pressure Test

Inland Production Company

Rt. 3 Box 3630
Myton, UT 84052
435-646-3721

Witness: _____ Date 12/12/01 Time 10:00 am pm

Test Conducted by: BRET HEWIE

Others Present: _____

Well: <u>MONUMENT BUTTE FEDERAL 3-25-8-16</u>	Field: <u>HAWKEYE UNIT</u>
Well Location: <u>NE/NW SEC. 25-T8S-R16E</u>	API No: <u>43-013-31605</u>


<u>Time</u>	<u>Casing Pressure</u>	
0 min	<u>1150</u>	psig
5	<u>1150</u>	psig
10	<u>1145</u>	psig
15	<u>1145</u>	psig
20	<u>1145</u>	psig
25	<u>1145</u>	psig
30 min	<u>1145</u>	psig
35		psig
40		psig
45		psig
50		psig
55		psig
60 min		psig

Tubing pressure: 760 psig

Result: Pass Fail

Signature of Witness: _____

Signature of Person Conducting Test: Bret Hewie

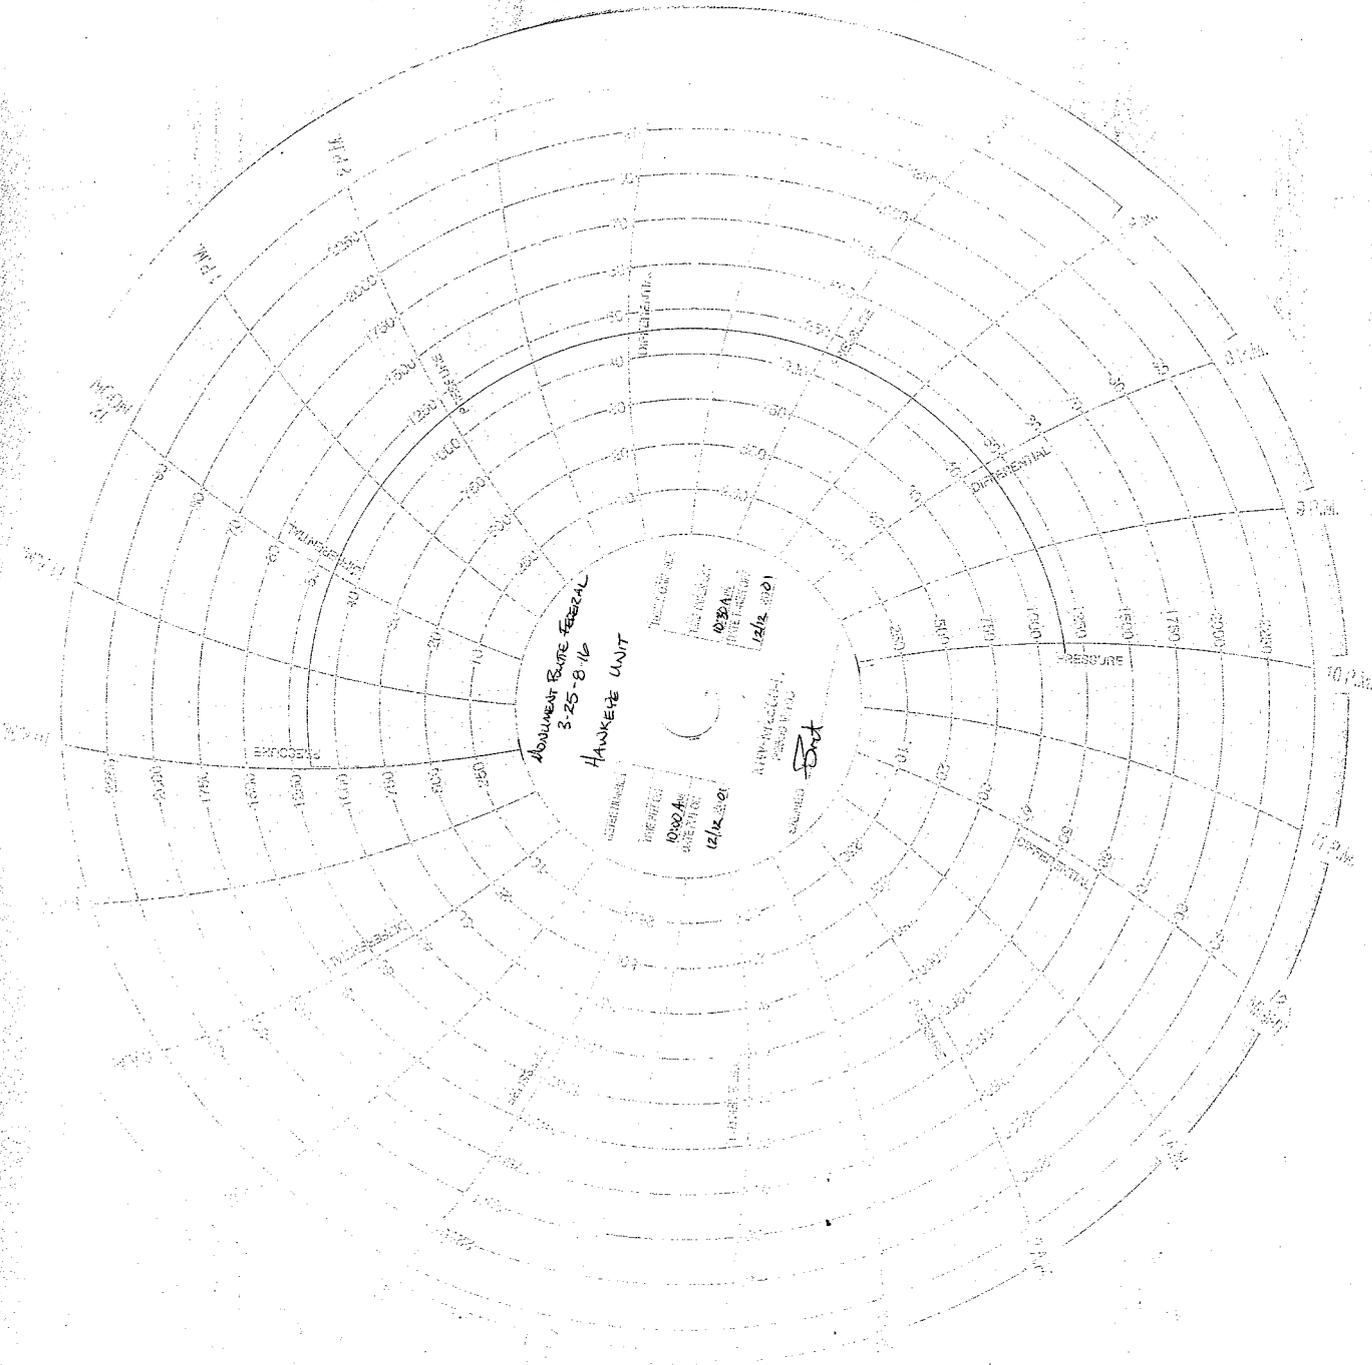

ADJUSTMENT EXPOSE FEDERAL
3-25-8-1/2
HAWKEYE UNIT

1000 PSI
1212 PSI
1212 PSI
1212 PSI

Bart

**DIVISION OF OIL, GAS AND MINING
UNDERGROUND INJECTION CONTROL PROGRAM
PERMIT
AMMENDED STATEMENT OF BASIS**

Applicant: Inland Production Company

<u>Well</u>	<u>API Number</u>	<u>Location</u>	<u>Unit</u>
Mon. Butte Fed. 3-25	43-013-31605	25-8S-16E	Mon. Butte NE
Mon. Butte Fed. 13-25	43-013-31513	25-8S-16E	Mon. Butte NE
State 14-32	43-013-31039	32-8S-16E	Wells Draw
Federal 44-33B	43-013-31240	33-8S-16E	Wells Draw
Mon. Butte 5-34	43-013-31499	34-8S-16E	Travis
Mon. Federal 9-34	43-013-31407	34-8S-16E	Monument Butte
Federal 23-34B	43-013-31241	34-8S-16E	Wells Draw
Mon. Federal 15-35	43-013-31264	35-8S-16E	Monument Butte
Mon. Federal 1A-35	43-013-31514	35-8S-16E	Monument Butte
MB 3-35-8-16	43-013-30608	35-8S-16E	Monument Butte
Federal 5-35	43-013-30686	35-8S-16E	Monument Butte
MB 13-35-8-16	43-013-30745	35-8S-16E	Monument Butte
MB 1-36-8-16	43-013-30592	36-8S-16E	Monument Butte
MB 13-36-8-16	43-013-30623	36-8S-16E	Monument Butte
State 5-36	43-013-30624	36-8S-16E	Monument Butte
Mon. Federal 12-25	43-047-32526	25-8S-17E	Humpback
Gilsonite St. 13-32	43-013-31403	32-8S-17E	Gilsonite
Odekirk 7-36-8-17	43-047-33078	36-8S-17E	Odekirk Spring
Mon. Federal 42-1J	43-013-31404	01-9S-16E	Jonah
Federal 41-5G	43-013-31205	05-9S-16E	Wells Draw
Castle Peak Fed. 43-5	43-013-30858	05-9S-16E	Wells Draw
Allen Fed. 1-5A	43-013-15780	05-9S-17E	Jonah
Mon. Fed. 24-6	43-013-31363	06-9S-17E	Jonah
Allen Fed. 1-6	43-013-15779	06-9S-17E	Jonah
Mon. Fed. 33-8	43-013-31427	08-9S-17E	Beluga

The wells listed above are all currently permitted Class II injection wells in the Monument Butte Secondary Recovery area. The wells are located in various secondary recovery units as shown above. Inland has requested approval to open additional perforations in these injection wells. Some of the requested perforations are above existing perforations, some are in the existing perforated interval and some are below the existing perforations. All requested perforations are within the Green River Formation which is the unitized interval for all of the Monument Butte area secondary recovery units. Cement Bond Logs were checked on all wells requesting additional perforations above the original permitted perforations. All wells have adequate

cement above the requested intervals. These requests by Inland are being treated as minor permit modifications and approval is recommended.

Reviewer(s): Brad Hill Date 03/20/2003



United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Utah State Office
P.O. Box 45155
Salt Lake City, UT 84145-0155
<http://www.blm.gov>



IN REPLY REFER TO:
3106
(UT-924)

September 16, 2004

Memorandum

To: Vernal Field Office
From: Acting Chief, Branch of Fluid Minerals
Subject: Merger Approval

Attached is an approved copy of the name change recognized by the Utah State Office. We have updated our records to reflect the merger from Inland Production Company into Newfield Production Company on September 2, 2004.

Michael Coulthard
Acting Chief, Branch of
Fluid Minerals

Enclosure

1. State of Texas Certificate of Registration

cc: MMS, Reference Data Branch, James Sykes, PO Box 25165, Denver CO 80225
State of Utah, DOGM, Attn: Earlene Russell, PO Box 145801, SLC UT 84114
Teresa Thompson
Joe Incardine
Connie Seare

UTSL-	15855	61052	73088	76561	
071572A	16535	62848	73089	76787	
065914	16539	63073B	73520A	76808	
	16544	63073D	74108	76813	
	17036	63073E	74805	76954	63073X
	17424	63073O	74806	76956	63098A
	18048	64917	74807	77233	68528A
UTU-	18399	64379	74808	77234	72086A
	19267	64380	74389	77235	72613A
02458	26026A	64381	74390	77337	73520X
03563	30096	64805	74391	77338	74477X
03563A	30103	64806	74392	77339	75023X
04493	31260	64917	74393	77357	76189X
05843	33992	65207	74398	77359	76331X
07978	34173	65210	74399	77365	76788X
09803	34346	65635	74400	77369	77098X
017439B	36442	65967	74404	77370	77107X
017985	36846	65969	74405	77546	77236X
017991	38411	65970	74406	77553	77376X
017992	38428	66184	74411	77554	78560X
018073	38429	66185	74805	78022	79485X
019222	38431	66191	74806	79013	79641X
020252	39713	67168	74826	79014	80207X
020252A	39714	67170	74827	79015	81307X
020254	40026	67208	74835	79016	
020255	40652	67549	74868	79017	
020309D	40894	67586	74869	79831	
022684A	41377	67845	74870	79832	
027345	44210	68105	74872	79833	
034217A	44426	68548	74970	79831	
035521	44430	68618	75036	79834	
035521A	45431	69060	75037	80450	
038797	47171	69061	75038	80915	
058149	49092	69744	75039	81000	
063597A	49430	70821	75075		
075174	49950	72103	75078		
096547	50376	72104	75089		
096550	50385	72105	75090		
	50376	72106	75234		
	50750	72107	75238		
10760	51081	72108	76239		
11385	52013	73086	76240		
13905	52018	73087	76241		
15392	58546	73807	76560		



Office of the Secretary of State

The undersigned, as Secretary of State of Texas, does hereby certify that the attached is a true and correct copy of each document on file in this office as described below:

Newfield Production Company
Filing Number: 41530400

Articles of Amendment

September 02, 2004

In testimony whereof, I have hereunto signed my name officially and caused to be impressed hereon the Seal of State at my office in Austin, Texas on September 10, 2004.



A handwritten signature in black ink, appearing to read "G. Connor".

Secretary of State

ARTICLES OF AMENDMENT
TO THE
ARTICLES OF INCORPORATION
OF
INLAND PRODUCTION COMPANY

FILED
In the Office of the
Secretary of State of Texas
SEP 02 2004
Corporations Section

Pursuant to the provisions of Article 4.04 of the Texas Business Corporation Act (the "TBCA"), the undersigned corporation adopts the following articles of amendment to the articles of incorporation:

ARTICLE 1 – Name

The name of the corporation is Inland Production Company.

ARTICLE 2 – Amended Name

The following amendment to the Articles of Incorporation was approved by the Board of Directors and adopted by the shareholders of the corporation on August 27, 2004.

The amendment alters or changes Article One of the Articles of Incorporation to change the name of the corporation so that, as amended, Article One shall read in its entirety as follows:

"ARTICLE ONE – The name of the corporation is Newfield Production Company."

ARTICLE 3 – Effective Date of Filing

This document will become effective upon filing.

The holder of all of the shares outstanding and entitled to vote on said amendment has signed a consent in writing pursuant to Article 9.10 of the TBCA, adopting said amendment, and any written notice required has been given.

IN WITNESS WHEREOF, the undersigned corporation has executed these Articles of Amendment as of the 1st day of September, 2004.

INLAND RESOURCES INC.

By: Susan G. Riggs
Susan G. Riggs, Treasurer

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

UIC FORM 5

TRANSFER OF AUTHORITY TO INJECT

Well Name and Number See Attached List		API Number
Location of Well		Field or Unit Name See Attached List
Footage :	County :	Lease Designation and Number
QQ, Section, Township, Range:	State : UTAH	

EFFECTIVE DATE OF TRANSFER: 9/1/2004

CURRENT OPERATOR

Company: <u>Inland Production Company</u>	Name: <u>Brian Harris</u>
Address: <u>1401 17th Street Suite 1000</u>	Signature: <u><i>Brian Harris</i></u>
<u>city Denver state Co zip 80202</u>	Title: <u>Engineering Tech.</u>
Phone: <u>(303) 893-0102</u>	Date: <u>9/15/2004</u>
Comments:	

NEW OPERATOR

Company: <u>Newfield Production Company</u>	Name: <u>Brian Harris</u>
Address: <u>1401 17th Street Suite 1000</u>	Signature: <u><i>Brian Harris</i></u>
<u>city Denver state Co zip 80202</u>	Title: <u>Engineering Tech.</u>
Phone: _____	Date: <u>9/15/2004</u>
Comments:	

(This space for State use only)

Transfer approved by: *A. Hunt*
Title: *Perk. Services Manager*

Approval Date: 9-20-04

Comments: Note: Indian Country wells will require EPA approval.

RECEIVED
SEP 20 2004

DIV. OF OIL, GAS & MINING

6a. (R649-9-2)Waste Management Plan has been received on: IN PLACE
6b. Inspections of LA PA state/fee well sites complete on: waived

7. **Federal and Indian Lease Wells:** The BLM and or the BIA has approved the merger, name change, or operator change for all wells listed on Federal or Indian leases on: BLM BIA

8. **Federal and Indian Units:**
The BLM or BIA has approved the successor of unit operator for wells listed on: n/a

9. **Federal and Indian Communization Agreements ("CA"):**
The BLM or BIA has approved the operator for all wells listed within a CA on: na/

10. **Underground Injection Control ("UIC")** The Division has approved UIC Form 5, **Transfer of Authority to Inject**, for the enhanced/secondary recovery unit/project for the water disposal well(s) listed on: 2/23/2005

DATA ENTRY:

1. Changes entered in the **Oil and Gas Database** on: 2/28/2005
2. Changes have been entered on the **Monthly Operator Change Spread Sheet** on: 2/28/2005
3. Bond information entered in RBDMS on: 2/28/2005
4. Fee/State wells attached to bond in RBDMS on: 2/28/2005
5. Injection Projects to new operator in RBDMS on: 2/28/2005
6. Receipt of Acceptance of Drilling Procedures for APD/New on: waived

FEDERAL WELL(S) BOND VERIFICATION:

1. Federal well(s) covered by Bond Number: UT 0056

INDIAN WELL(S) BOND VERIFICATION:

1. Indian well(s) covered by Bond Number: 61BSBDH2912

FEE & STATE WELL(S) BOND VERIFICATION:

1. (R649-3-1) The **NEW** operator of any fee well(s) listed covered by Bond Number 61BSBDH2919

2. The **FORMER** operator has requested a release of liability from their bond on: n/a*
The Division sent response by letter on: n/a

LEASE INTEREST OWNER NOTIFICATION:

3. (R649-2-10) The **FORMER** operator of the fee wells has been contacted and informed by a letter from the Division of their responsibility to notify all interest owners of this change on: n/a

COMMENTS:

*Bond rider changed operator name from Inland Production Company to Newfield Production Company - received 2/23/05

Mechanical Integrity Test Casing or Annulus Pressure Test

Inland Production Company

Rt. 3 Box 3630
Myton, UT 84052
435-646-3721

Witness: _____ Date 8/17/05 Time 11:00 am pm

Test Conducted by: Mike Hullinger

Others Present: _____

Well: Monument better Fed. 3-25-8-16

Field: _____

Well Location: NE/NW sec 25-T8S-R16E

API No: 43-013-31605

<u>Time</u>	<u>Casing Pressure</u>	
0 min	<u>1450</u>	psig
5	<u>1450</u>	psig
10	<u>1450</u>	psig
15	<u>1450</u>	psig
20	<u>1450</u>	psig
25	<u>1450</u>	psig
30 min	<u>1450</u>	psig
35	_____	psig
40	_____	psig
45	_____	psig
50	_____	psig
55	_____	psig
60 min	_____	psig

Tubing pressure: 970 psig

Result: Pass Fail

Signature of Witness: Lloyd Bartlett

Signature of Person Conducting Test: _____

INJECTION WELL - PRESSURE TEST

Well Name: <u>MB Fed. #3-25-8-16</u>	API Number: <u>43-013-31605</u>
Qtr/Qtr: <u>NE/NW</u> Section: <u>25</u>	Township: <u>8S</u> Range: <u>16E</u>
Company Name: <u>Newfield</u>	
Lease: State _____ Fee _____	Federal <u>U67107</u> Indian _____
Inspector: <u>Lloyd Bartlett</u>	Date: <u>8-17-05</u> <u>1053</u>

Initial Conditions:

Tubing - Rate: _____ Pressure: 970 psi
 Casing/Tubing Annulus - Pressure: _____ psi

Conditions During Test:

Time (Minutes)	Annulus Pressure	Tubing Pressure
0	<u>1450</u>	<u>970</u>
5	<u>1450</u>	<u>970</u>
10	<u>1450</u>	<u>970</u>
15	<u>1450</u>	<u>970</u>
20	<u>1450</u>	<u>970</u>
25	<u>1450</u>	<u>970</u>
30	<u>1450</u>	<u>970</u>

Results: Pass/Fail

Conditions After Test:

Tubing Pressure: 970 psi
 Casing/Tubing Annulus Pressure: 1450 psi

COMMENTS: Recompletion for perfs.

Michael Thullinger
 Operator Representative

RECEIVED
 AUG 24 2005
 DIV. OF OIL, GAS & MINING

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
UTU67170

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:
MON BUTTE NE

1. TYPE OF WELL: OIL WELL GAS WELL OTHER Injection well

8. WELL NAME and NUMBER:
MON BUTTE FED 3-25

2. NAME OF OPERATOR:
Newfield Production Company

9. API NUMBER:
4301331605

3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

10. FIELD AND POOL, OR WILDCAT:
Monument Butte

4. LOCATION OF WELL:
FOOTAGES AT SURFACE: 0756 FNL 1946 FWL

COUNTY: Duchesne

OTR/OTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: NE/NW, 25, T8S, R16E

STATE: Utah

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF ACTION SubDate

TYPE OF SUBMISSION	TYPE OF ACTION	TYPE OF ACTION
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 08/24/2005	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE
	<input type="checkbox"/> CONVERT WELL TYPE	<input checked="" type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION
		<input type="checkbox"/> REPERFORATE CURRENT FORMATION
		<input type="checkbox"/> SIDETRACK TO REPAIR WELL
		<input type="checkbox"/> TEMPORARITLY ABANDON
		<input type="checkbox"/> TUBING REPAIR
		<input type="checkbox"/> VENT OR FLAIR
		<input type="checkbox"/> WATER DISPOSAL
		<input type="checkbox"/> WATER SHUT-OFF
		<input type="checkbox"/> OTHER: -

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The subject well was recompleted in the Green River Formation. Six new intervals were perforated. The CP2 sds @ 6100-6114'; CP3 @ 6160-6166'; D3 sds @ 5232-5238'; D2 sds @ 5200-5206, D1 sds @ 5130-5134' and PB10 @ 4842-4856', all with 4 JSPF for a total of 160 shots. On 8-15-05 Dennis Ingram with the State of Utah DOGM ws contacted concerning the MIT on the above listed well. Permission was given at that time to perform the test on 8-17-05. On 8-17-05 the csg was pressured up to 1450 psig and charted for 30 minutes with no pressure loss. The well wsa not injecting during the test. The tbq pressure was 970 psig during the test. There was a State representative available to witness the test. Dennis Ingram.

Accepted by the
Utah Division of
Oil, Gas and Mining

Date: 08-31-05
By: *[Signature]*

NOTICE TO OPERATOR
DATE: 9-1-05
BY: CHD

NAME (PLEASE PRINT) Kathy Chapman

TITLE Office Manager


SIGNATURE *[Signature]*

DATE 08/24/2005

(This space for State use only)

RECEIVED
AUG
SEP 25 2005

DIV. OF OIL, GAS & MINING

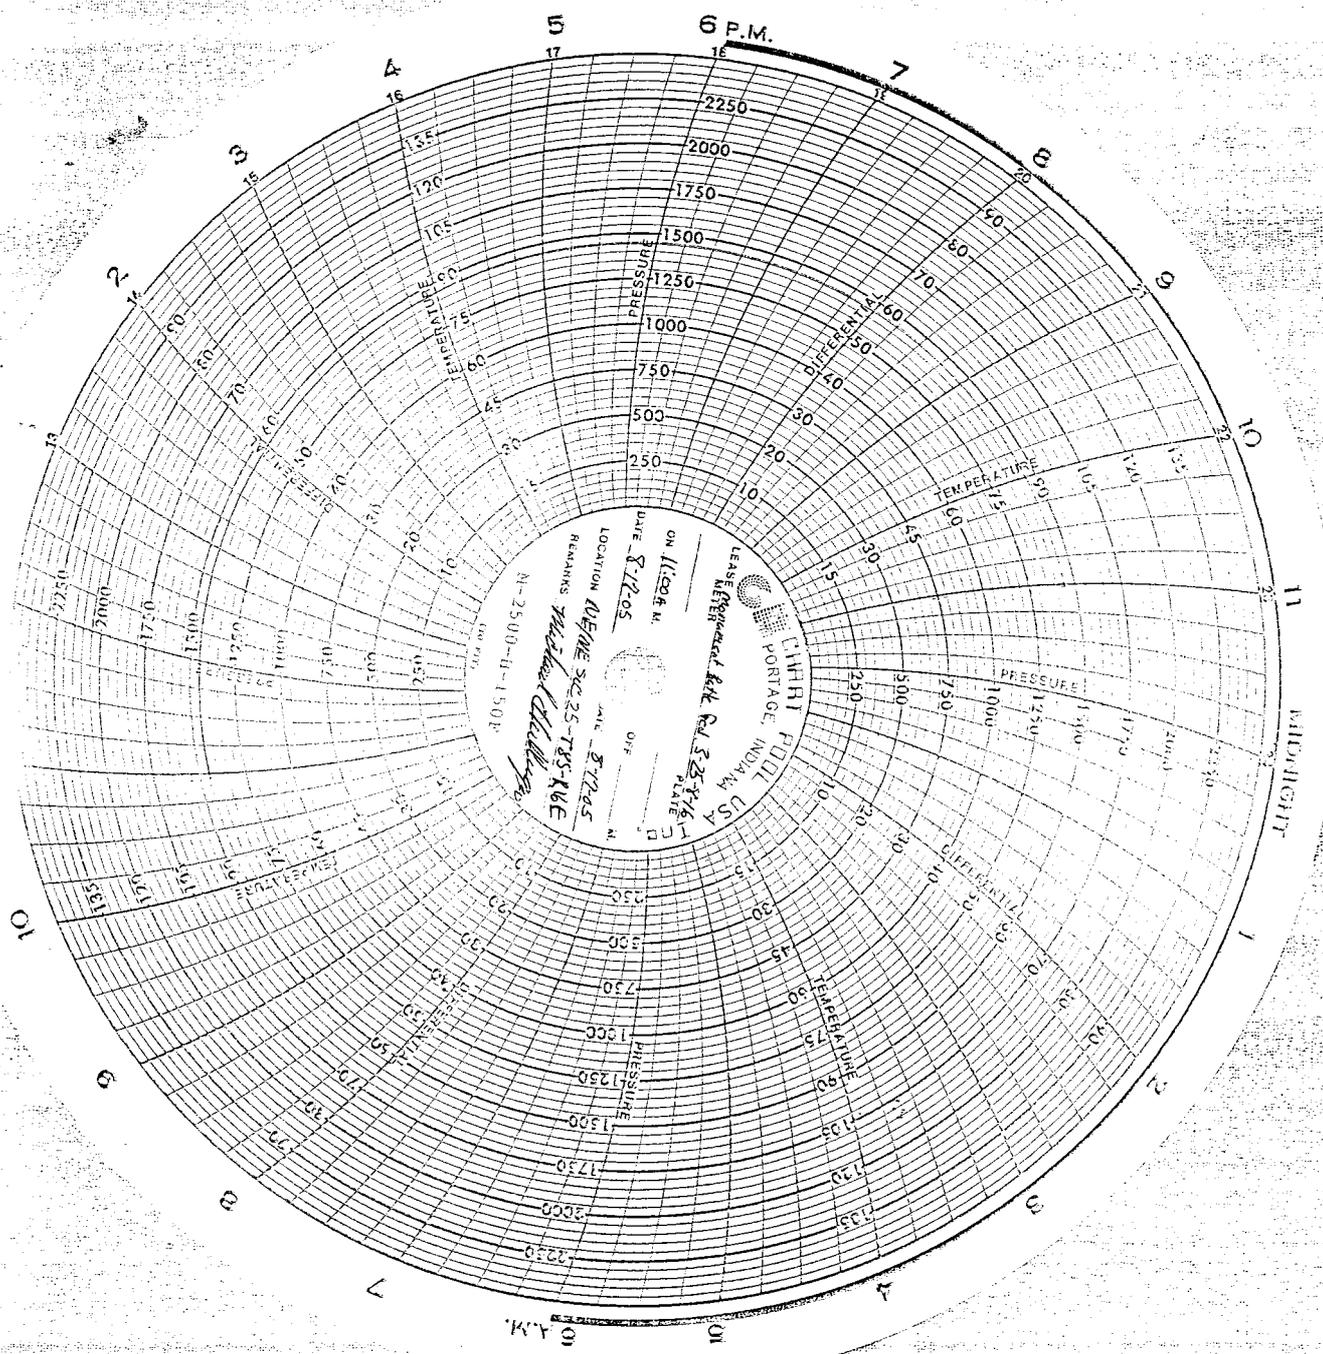

ON 11:00 A.M.
 DATE 8-12-05
 LOCATION OUENE SEC 25-T8S-R6E
 REMARKS *Water level 11:00 AM*
 N-2500-H-150R
 LEASE OPERATOR *Red 3-25-14-16*
 PORTAGE, INDIANA
 CHHRT POOL US
 OFF M

G.P.M.

PRESSURE

TEMPERATURE

PRESSURE

TEMPERATURE

DIFFERENTIAL

A.M.

NEWFIELD PRODUCTION COMPANY
 RT. 3 BOX 3630
 MYTON, UT 84052

ENTITY ACTION FORM
 DEPARTMENT OF NATURAL RESOURCES
 DIVISION OF OIL, GAS AND MINING

FORM 6

OPERATOR ACCT NO: N2695

ACTIN CODE	CRRNT ENTITY	NEW ENTITY	API NUMBER	WELL	QQ	SEC	TWN	RNG	REASON	EFFECTIVE
D	14648	15150	4301332359	FEDERAL 9-24-8-16	NENSE	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	99998	15150	4301331633	MONUMENT BUTTE FED NE 11-24	NESW	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	12293	15150	4301331990	MBFNE 11-24-8-16	NESW	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	14611	15150	4301332366	FEDERAL 10-24-8-16	NWSE	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	12244	15150	4301331923	MBFNE 12-24	NWSW	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	11907	15150	4301331629	MONUMENT BUTTE FED NE 16-24	SESE	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	11930	15150	4301331630	MONUMENT BUTTE FED 14-24	SESW	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	11912	15150	4301331628	MON BUTTE FED NE 15-24	SWSE	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	11984	15150	4301331653	MON BUTTE FED NE 13-24	SWSW	24	8S	16E	Monument Butte North East EOR	1/1/2006
D	11884	15150	4301331608	MON BUTTE FED 1-25(I)	NENE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11881	15150	4301331601	MONUMENT BUTTE FED 8-25	SENE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11887	15150	4301331604	MONUMENT BUTTE FED 2-25	NWNE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11873	15150	4301331561	MON BUTTE FED 7-25	SWNE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11882	15150	4301331596	MONUMENT BUTTE FED 6-25	SENE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11922	15150	4301331605	MON BUTTE FED 3-25	NENW	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11897	15150	4301331600	MON BUTTE FED 9-25	NESE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11874	15150	4301331562	MONUMENT BUTTE FED 10-25	NWSE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11899	15150	4301331597	MONUMENT BUTTE FED 16-25	SESE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11847	15150	4301331559	MON BUTTE FED 15-25	SWSE	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11840	15150	4301331554	MONUMENT BUTTE FED 12-25	NWSW	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11841	15150	4301331553	MON BUTTE FED 11-25	NESW	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11805	15150	4301331531	MONUMENT BUTTE FED 14-25	SESW	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11786	15150	4301331513	MON BUTTE FED 13-25	SWSW	25	8S	16E	Monument Butte North East EOR	1/1/2006
D	11900	15150	4301331502	MON BUTTE FED 15-26	SWSE	26	8S	16E	Monument Butte North East EOR	1/1/2006
D	11814	15150	4301331517	MONUMENT BUTTE FED 16-26	SESE	26	8S	16E	Monument Butte North East EOR	1/1/2006

*new entity assigned 1/31/06
 ER, DOGM*

RECEIVED
JAN 25 2006

KIM KETTLE
 PRODUCTION CLERK 1/25/2006

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER: USA UTU-67170
6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
7. UNIT or CA AGREEMENT NAME: GMBU
8. WELL NAME and NUMBER: MON BUTTE FED 3-25
9. API NUMBER: 4301331605
10. FIELD AND POOL, OR WILDCAT: GREATER MB UNIT
COUNTY: DUCHESNE
STATE: UT

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

4. LOCATION OF WELL:
FOOTAGES AT SURFACE: 756 FNL 1946 FWL

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NENW, 25, T8S, R16E

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 07/07/2010	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Five Year MIT
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On 07/06/2010 Dennis Ingram with the State of Utah DOGM was contacted concerning the 5 Year MIT on the above listed well. Permission was given at that time to perform the test on 07/06/2010. On 07/07/2010 the casing was pressured up to 1280 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tubing pressure was 1763 psig during the test. There was not a State representative available to witness the test.

API# 43-013-31605

NAME (PLEASE PRINT) Lucy Chavez-Naupoto TITLE Administrative Assistant

SIGNATURE *Lucy Chavez-Naupoto* DATE 07/08/2010

(This space for State use only)

RECEIVED
JUL 12 2010
DIV. OF OIL, GAS & MINING

Mechanical Integrity Test Casing or Annulus Pressure Test

Newfield Production Company
Rt. 3 Box 3630
Myton, UT 84052
435-646-3721

Witness: _____ Date 7/7/10 Time 11:30 (am) pm

Test Conducted by: NEWFIELD EXPLORATION

Others Present: _____

Well: MONUMENT BUTTE Federal 3-25-8-16	Field: MONUMENT BUTTE
Well Location: NE/NW, Sec 25, T8S, R16E	API No: 43-013-31605

<u>Time</u>	<u>Casing Pressure</u>	
0 min	<u>1780</u>	psig
5	<u>1780</u>	psig
10	<u>1780</u>	psig
15	<u>1780</u>	psig
20	<u>1780</u>	psig
25	<u>1780</u>	psig
30 min	<u>1780</u>	psig
35	_____	psig
40	_____	psig
45	_____	psig
50	_____	psig
55	_____	psig
60 min	_____	psig

Tubing pressure: 1763 psig

Result: Pass Fail

Signature of Witness: _____

Signature of Person Conducting Test: Bob Whitehead

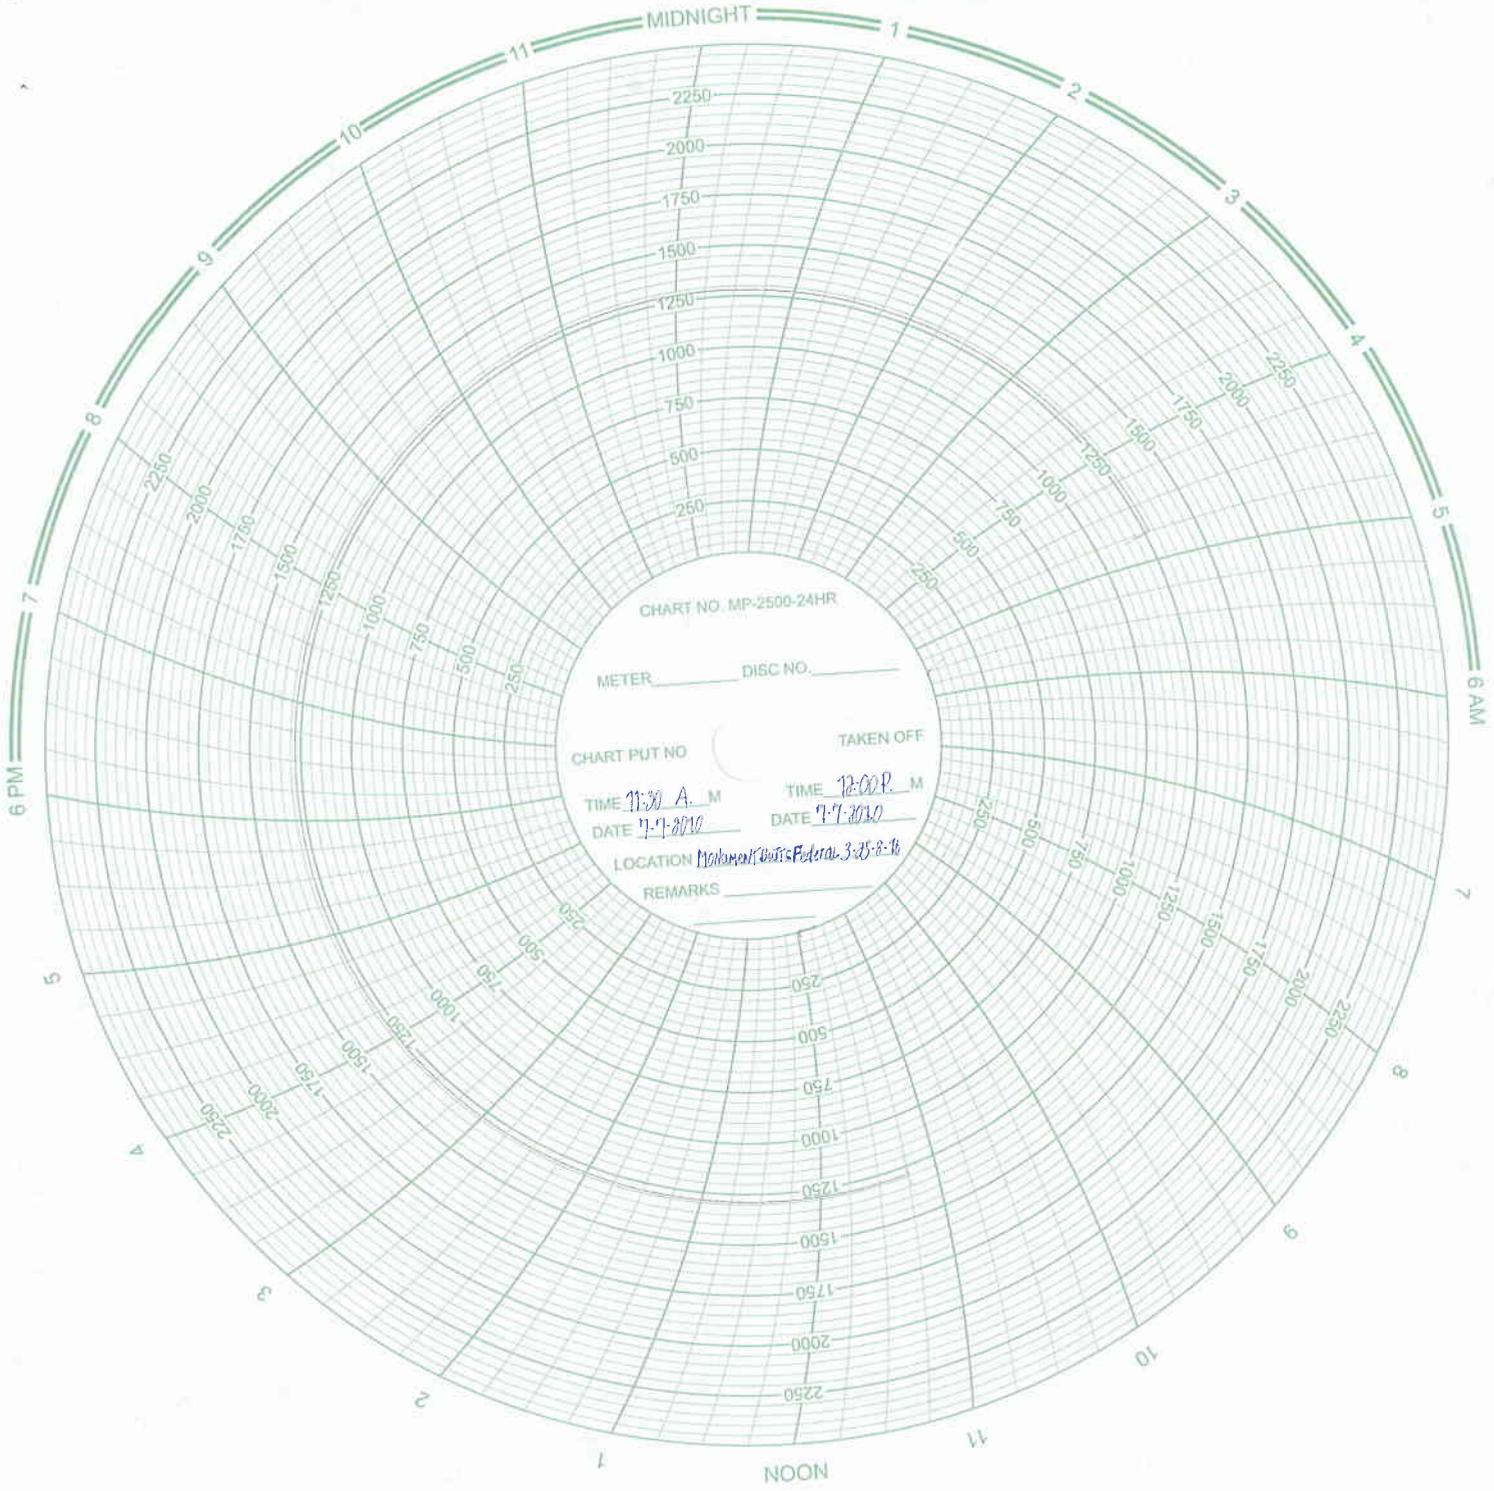


CHART NO. MP-2500-24HR

METER _____ DISC NO. _____

CHART PUT NO. _____ TAKEN OFF _____

TIME 11:30 A. M. TIME 12:00 P. M.

DATE 7-7-2010 DATE 7-7-2010

LOCATION Madhavpur Federal 3-25-8-16

REMARKS _____

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67170
Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
1. TYPE OF WELL Water Injection Well	8. WELL NAME and NUMBER: MON BUTTE FED 3-25	
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	9. API NUMBER: 43013316050000	
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	PHONE NUMBER: 435 646-4825 Ext	9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0756 FNL 1946 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENW Section: 25 Township: 08.0S Range: 16.0E Meridian: S	COUNTY: DUCHESNE	
		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input checked="" type="checkbox"/> NOTICE OF INTENT Approximate date work will start: 11/21/2011 <input type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: <input type="checkbox"/> SPUD REPORT Date of Spud: <input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input checked="" type="checkbox"/> CHANGE TUBING <input checked="" type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> DEEPEN <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> PLUG BACK <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> APD EXTENSION <input type="checkbox"/> WILDCAT WELL DETERMINATION <input type="checkbox"/> OTHER: <input style="width: 50px;" type="text"/>	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.		
<p>Newfield would like to modify the following injection well in order to more efficiently flood the productive sands in the offset producers. A concentric injection design is being proposed. This design will result in 2 unique injection profiles within this one well. Following the workover an updated schematic will be submitted with the workover report showing the split between Zone 1 and Zone 2. The split will be very similiar to that of the 2-25-8-16D which was completed in October. Newfield would also like to change the name of this well to Monument Butte Federal 3-25-8-16D.</p>		
		<p>Approved by the Utah Division of Oil, Gas and Mining</p> <p>Date: <u>11/23/2011</u></p> <p>By: <u></u></p>
NAME (PLEASE PRINT) Lucy Chavez-Naupoto	PHONE NUMBER 435 646-4874	TITLE Water Services Technician
SIGNATURE N/A	DATE 11/21/2011	

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING	FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.	5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67170
1. TYPE OF WELL Water Injection Well	6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY	7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052	8. WELL NAME and NUMBER: MON BUTTE FED 3-25-8-16D
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0756 FNL 1946 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENW Section: 25 Township: 08.0S Range: 16.0E Meridian: S	9. API NUMBER: 43013316050000
PHONE NUMBER: 435 646-4825 Ext	9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
STATE: UTAH	COUNTY: DUCHESNE

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 2/14/2012	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> OTHER	OTHER: <input type="text" value="W/O MIT/Dual INJ"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The Monument Butte Federal 3-25-8-16D had workover procedures performed - water isolation/concentric injection, attached is the schematic showing the updated information. On 02/13/2012 Chris Jensen with the State of Utah DOGM was contacted concerning the MIT on the above listed well. On 02/14/2012 the csg was pressured up to 1155 psig for 30 minutes with no pressure loss. The well was not injecting during the test. The tbg pressure for the 1.9 tbg was 890 psig and the tbg pressure for the 2-7/8" tbg was 495 psig during the test. There was not a State representative available to witness the test.

**Accepted by the
Utah Division of
Oil, Gas and Mining**

Date: March 05, 2012

By: 

NAME (PLEASE PRINT) Lucy Chavez-Naupoto	PHONE NUMBER 435 646-4874	TITLE Water Services Technician
SIGNATURE N/A	DATE 2/27/2012	

Mechanical Integrity Test Casing or Annulus Pressure Test

Newfield Production Company
Rt. 3 Box 3630
Myton, UT 84052
435-646-3721

Witness: _____ Date 2/14/12 Time 9:00 (am) pm

Test Conducted by: Troy Lazenby

Others Present: Jared Robison

Well: Monument Butte 3-25-8-16 Federal Field: Monument Butte
Well Location: NE/NW Sec 25-T85-R16E API No: 43-013-31605
Duchesne County, UT UTV87538X


<u>Time</u>	<u>Casing Pressure</u>	
0 min	<u>1155</u>	psig
5	<u>1155</u>	psig
10	<u>1155</u>	psig
15	<u>1155</u>	psig
20	<u>1155</u>	psig
25	<u>1155</u>	psig
30 min	<u>1155</u>	psig
35	_____	psig
40	_____	psig
45	_____	psig
50	_____	psig
55	_____	psig
60 min	_____	psig

Tubing pressure: 278-495 1.9 = 890 psig

Result: Pass Fail

Signature of Witness: _____

Signature of Person Conducting Test: Troy Lazenby

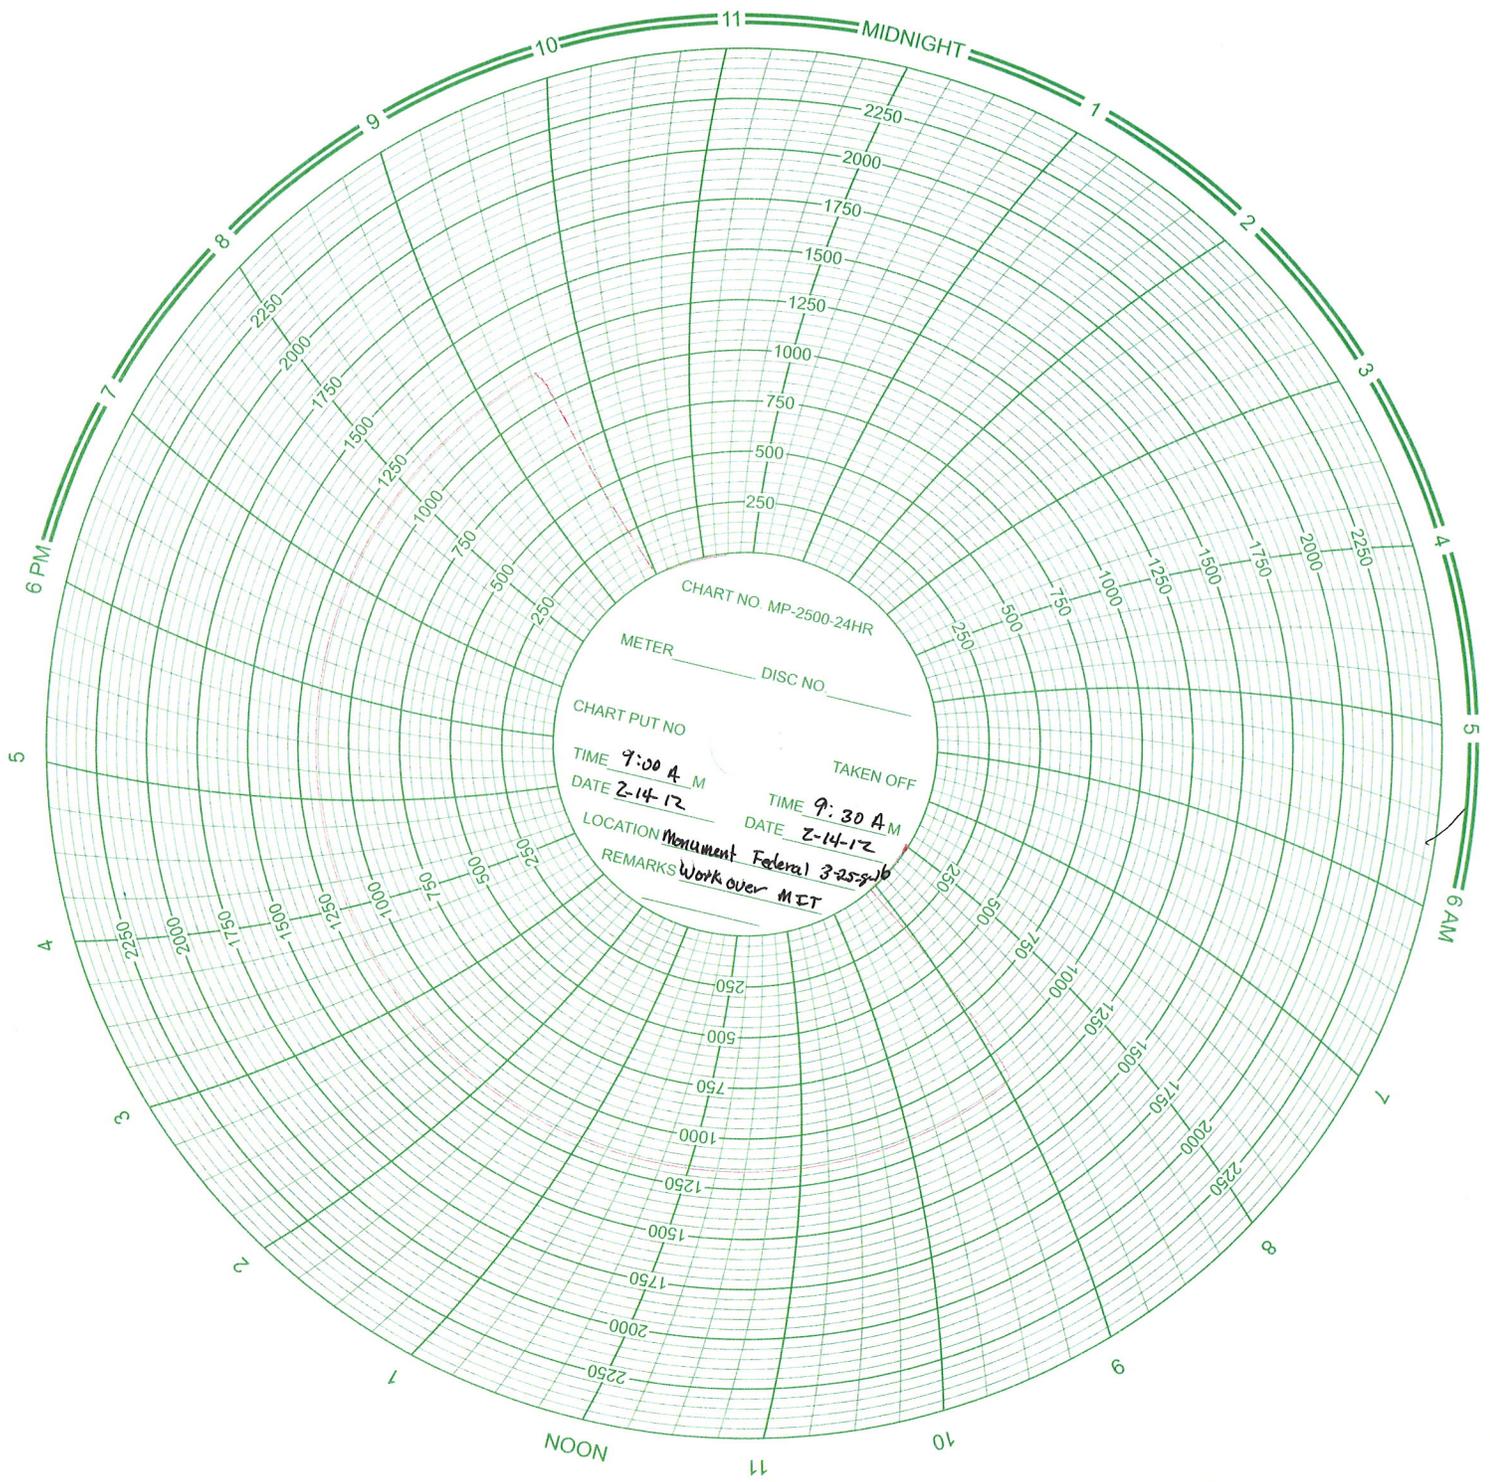

Spud Date: 3/27/96
 Put on Production: 4/23/96
 Put on Injection: 1/29/97
 GL: 5432' KB: 5445'

Monument Butte Federal 3-25-8-16

Initial Production: 149 BO,
 94 MCF, 3 BWPD

Injection Diagram

SURFACE CASING


CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 293.72'
 DEPTH LANDED: 290.52'
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 120 sxs Premium cmt

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 147 jts. (6247')
 DEPTH LANDED: 6250.31'
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 275 sk Hyfill mixed & 350 sxs thixotropic
 CEMENT TOP AT: Surface per CBL

TUBING

SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
 NO. OF JOINTS: 154 jts (4775.2')
 CE 5-1/2" @ 4791.54'
 SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
 NO. OF JOINTS: 15 jts (469.9')
 SEATING NIPPLE: 2-7/8" (1.10")
 SN LANDED AT: 5264.9'
 Perf Sub 2-7/8" / N-80 (6.2')
 PBR Seal Assembly: 2-7/8" @ 5272.2'
 CE @ 5280.33'
 W.L. reentry guide: 2-7/8" @ 5284.1'
 TOTAL STRING LENGTH: EOT @ 5285' KB

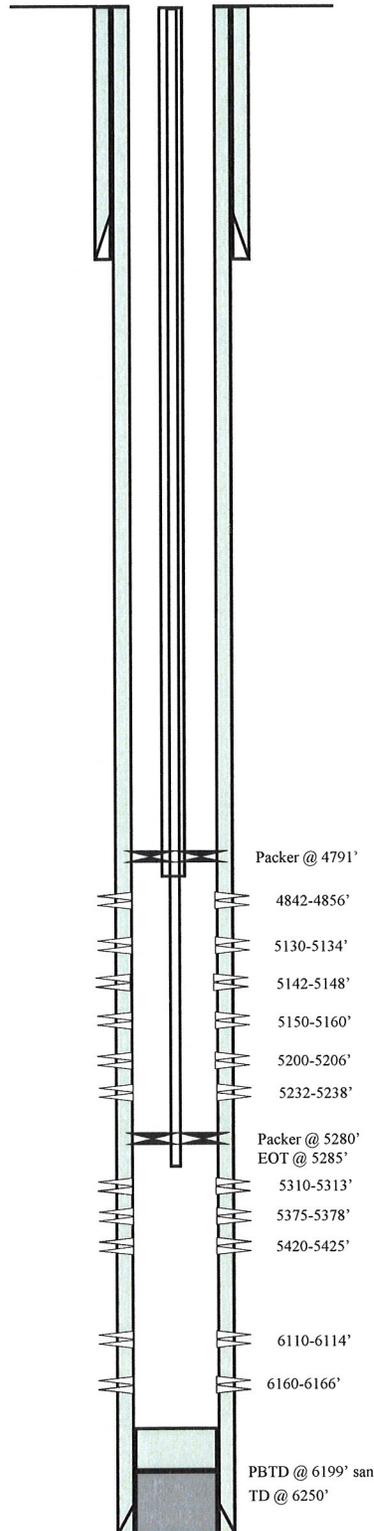

FRAC JOB

4/16/96 5425'-5310' **Frac B-1, Bi-Carb and C sand as follows:**
 93,600# of 20/40 sd in 583 bbls of Boragel.
 Treated @ avg Rate 31 bpm, avg press 1800 psi. ISIP-1991 psi. Calc. flush: 5420 gal. Actual flush: 5262 gal.

4/21/96 5142'-5160' **Frac D-1 sand as follows:**
 79,000# 20/49 sd in 471 bbls Boragel.
 Treated @ avg rate 30 bpm w/1550 psi avg. ISIP 1967 psi. Calc flush: 5142 gal. Actual flush: 5039 gal.

1/24/97 **Convert to injector.**

7-26-05 6110-6166' **Recompletion Frac CP2 & CP3 sand as follows:** 19,005#'s 20/40 sd in 198 bbls of Lightning 17 frac fluid. Treated @ avg pressure 3580 psi @ ave rate of 14 BPM. ISIP 2250 psi. Calc flush: 1616 gal. Actual flush: 1504 gal.

7-26-05 5200-5238' **Recompletion Frac D2 & D3 sands as follows:** 14,299#'s 20/40 sd in 158 bbls of Lightning 17 frac fluid. Treated @ avg pressure 3408 psi @ ave rate of 14.1 BPM. ISIP 2500 psi. Calc flush: 1313 gal. Actual flush: 1193 gal.

7-26-05 4842-4856' **Recompletion Frac PB10 sands as follows:** 22,023#'s 20/40 sd in 338 bbls of Lightning 17 frac fluid. Treated @ avg pressure 3015 psi @ ave rate of 14.1 BPM. ISIP 2100 psi. Calc flush: 1333 gal. Actual flush: 1155 gal.

8-17-05 **MIT completed**

7-7-10 **5 yr. MIT**

02/11/12 **Concentric Injection Procedure completed**
 - dual injection lines installed - 2 packers set.

02/14/12 **MIT Finalized** - tbg detail updated

PERFORATION RECORD

Date	Interval	Tool	Holes
4/15/96	5420'-5425'	4 JSPF	20 holes
4/15/96	5375'-5378'	4 JSPF	12 holes
4/15/96	5310'-5313'	4 JSPF	12 holes
4/17/96	5142'-5148'	4 JSPF	24 holes
4/17/96	5150'-5160'	4 JSPF	40 holes
7-25-05	6110-6114'	4 JSPF	16 holes
7-25-05	6160-6166'	4 JSPF	24 holes
7-25-05	5232-5238'	4 JSPF	24 holes
7-25-05	5200-5206'	4 JSPF	24 holes
7-25-05	5130-5134'	4 JSPF	16 holes
7-25-05	4842-4856'	4 JFPF	56 holes



Monument Butte Federal 3-25-8-16
 756 FNL 1946 FEL
 NENW Section 25-T8S-R16E
 Duchesne Co, Utah
 API #43-013-31605; Lease #U-67170

NEWFIELD  ROCKY MOUNTAINS		Daily Workover Report		Well Name: MON BT NE 3-25-8-16	
		MAJWKO		AFE: 26521	
				Report Date: 2/13/12	
				Operation: RU Total Safety. Circulate Biocide.	
Field:	GMBU CTB4	Rig Name:	WWS #5	Work Performed:	2/6/2012
Location:	S25 T8S R16E	Supervisor:	Gary Dietz	Day:	1
County:	DUCHESNE	Phone:	435- 823-4211	Daily Cost:	\$10,075
State:	UT	Email:	gdietz@newfield.com	Cum DWR:	\$10,075
Reason for Workover: Water Isolation					
24 Hr Summary:	MIRU Western rig #5. Well is flowing back W/ H2S in the stream. Leave well flowing back overnight W/ 2 man watchcrew.				
24 Hr Plan Forward:	RU H2S monitoring equipment & Cascade unit. Treat well W/ Biocide & Scavenger.				
Incidents:	None	Newfield Pers:	2	Contract Pers:	8
Conditions:					
Critical Comments					
Activity Summary					
0 Hr(s); P : MIRU Western rig #5. Well is flowing back W/ H2S in stream (160 ppm max). Setup flowback crew for overnight flowback operations. Release rig crew.					
0 Hr(s); P : Mixing Muliti-Chen Biocide and H2S Scavenger in all disposal loads.,					

NEWFIELD  ROCKY MOUNTAINS		Daily Workover Report		Well Name: MON BT NE 3-25-8-16	
		MAJWKO		AFE: 26521	
				Report Date: 2/13/12	
				Operation: TOH W/ packer. TIH W/ bit/scraper.	
Field:	GMBU CTB4	Rig Name:	WWS #5	Work Performed:	2/7/2012
Location:	S25 T8S R16E	Supervisor:	Gary Dietz	Day:	2
County:	DUCHESNE	Phone:	435- 823-4211	Daily Cost:	\$16,355
State:	UT	Email:	gdietz@newfield.com	Cum DWR:	\$26,430
Reason for Workover: Water Isolation					
24 Hr Summary:	RU Total Safety gas monitoring equipment. Perforate tbg & Circulate well W/ Biocide & Scavenger.				
24 Hr Plan Forward:	Circ well W/ 11 ppg CaCl2. TOH W/ injection packer. TIH W/ bit and scraper.				
Incidents:	None	Newfield Pers:	3	Contract Pers:	9
Conditions:					
Critical Comments					
Activity Summary					
0 Hr(s); P : MIRU Total Safety. Set up remote gas monitors & Work/escape masks. Certify personnel W/ FIT tests. RU Perforators WL truck, lubricator & grease head. RIH & perf 4 holes in tbg @ 4790' (3' above PSN). RU HO trk to annulus. Ensure circulation through holes (OK). RD WLT. Circulate annulus full of fresh water treated W/ Biocide and H2S Scavenger. Release well to NPC flowback crew and resume flowing back through night.					
0 Hr(s); P : Haul in 200 bbls of 11 ppg of CaCl2.					
0 Hr(s); P : Mixing Muliti-Chen Biocide and H2S Scavenger in all disposal loads.					

NEWFIELD**Daily Workover Report**Well Name: **MON BT NE 3-25-8-16**

AFE: 26521

Report Date: 2/13/12

MAJWKO

Operation: TOH W/ bit/scraper. TIH W/ packers.

Field:	GMBU CTB4	Rig Name:	WWS #5	Work Performed:	2/8/2012
Location:	S25 T8S R16E	Supervisor:	Gary Dietz	Day:	3
County:	DUCHESNE	Phone:	435-823-4211	Daily Cost:	\$23,200
State:	UT	Email:	gdietz@newfield.com	Cum DWR:	\$49,630

Reason for Workover: Water Isolation

24 Hr Summary: Circ well W/ 11 ppg CaCl2. Well static. TOH W/ injection packer, TIH W/ bit and scraper. Pressure test tbg.

24 Hr Plan Forward: TOH W/ bit and scraper. TIH W/ packers & land outer string.

Incidents:	None	Newfield Pers:	1	Contract Pers:	9	Conditions:
------------	------	----------------	---	----------------	---	-------------

Critical Comments

Activity Summary

0 Hr(s); P : RU & circulate 130 bbls 11 ppg CaCl2 dn tbg & out annulus. Well is dead. ND wellhead. NU BOP. Release packer @ 4802'. TOH and talley injection string--LD perforated jt & pkr. Trickled 15 bbls CaCl2 dn annulus while pulling. MU & TIH W/ 4 3/4" bit, 5 1/2" casing scraper and 153 jts of injection string. Talley, drift & PU 17 jts 2 7/8 8rd 6.5# YB J-55 tbg to clear packer seat (5291'). Well still static. Drop standing valve down tbg. RIH W/ sandline & push SV to SN. RU test "T" on tbg. Pressure test tbg to 3000 psi. Held solid for 30 minutes. Retrieve SV W/ overshot on sandline. TOH W/ 16 jts tbg. Break each collar, clean & inspect pins and apply Liquid O-ring to pins. SIFN W/ EOT @ 4785'.

0 Hr(s); P : Mixing Muliti-Chen Biocide and H2S Scavenger in all disposal loads.

NEWFIELD**Daily Workover Report**Well Name: **MON BT NE 3-25-8-16**

AFE: 26521

Report Date: 2/13/12

MAJWKO

Operation: PU & run inner injection string.

Field:	GMBU CTB4	Rig Name:	WWS #5	Work Performed:	2/9/2012
Location:	S25 T8S R16E	Supervisor:	Gary Dietz	Day:	4
County:	DUCHESNE	Phone:	435-823-4211	Daily Cost:	\$7,850
State:	UT	Email:	gdietz@newfield.com	Cum DWR:	\$57,480

Reason for Workover: Water Isolation

24 Hr Summary: TOH W/ bit and scraper. TIH W/ injection string and packers. Set btm packer & land tbg. Circ packer fluids. Drop standing valve & set upper packer. Pressure test tbg overnight.

24 Hr Plan Forward: Confirm tbg test & retrieve standing valve. PU & RIH W/ seal ass'y and 1.90" inner injection string.

Incidents:	None	Newfield Pers:	1	Contract Pers:	9	Conditions:
------------	------	----------------	---	----------------	---	-------------

Critical Comments

Activity Summary

0 Hr(s); P : Well has slight blow in both sides. TOH W/ tbg--LD bit & scraper. Trickled 15 bbls CaCl2 dn annulus while pulling. PU & run outer injection string as follows: 2 7/8 W.L. re-entry guide, Weatherford 5 1/2" Arrow-set 1X packer (RH release), 2 7/8 PBR (2.188" bore), 2 7/8 perf'd sub, 2 7/8 SN, 15 jts 2 7/8 tbg, Weatherford 5 1/2" HRP (hyd. Set pkr) & 154 jts 2 7/8 8rd 6.5# M-50 tbg. ND BOP. Set AS-1X packer @ 5280' W/ SN @ 5265', HRP pkr @ 4791' and EOT @ 5285'. Land tbg W/ 10,000# tension on Cameron tbg hanger. NU Cameron secondary injection spool on wellhead. Install tbg sub in 2 7/8 hanger. Mix 80 bbls fresh water W/ 15 gals Multi-Chem MC-6031 & 5 gals B-8850. Pump dn tbg @ 90°F. Displace packer fluids W/ 30 bbls CaCl2. Drop standing valve dn tbg & let fall. Pressure up on tbg & set HRP packer @ 2100 psi. Pressure test tbg to 3000 psi. Having slow leakoff. Keep bumping pressure back up. Leakoff getting slower. Leave 3000 psi on tbg overnight.

0 Hr(s); P : Mixing Muliti-Chen Biocide and H2S Scavenger in all disposal loads.

NEWFIELD ROCKY MOUNTAINS		Daily Workover Report		Well Name: MON BT NE 3-25-8-16	
		MAJWKO		AFE: 26521	
				Report Date: 2/13/12	
				Operation: Circ out drlg mud. Land inner string.	
Field:	GMBU CTB4	Rig Name:	WWS #5	Work Performed:	2/10/2012
Location:	S25 T8S R16E	Supervisor:	Gary Dietz	Day:	5
County:	DUCHESNE	Phone:	435-823-4211	Daily Cost:	\$68,188
State:	UT	Email:	gdietz@newfield.com	Cum DWR:	\$125,668
Reason for Workover: Water Isolation					
24 Hr Summary:	Well flowing. Bullhead 12 ppg drilling mud. PU & RIH W/ seal assembly and 1.90" inner injection string. Unable to circ mud out of hole.				
24 Hr Plan Forward:	TOH partway. Stage mud out of hole. Land inner string & RU wellhead.				
Incidents:	None	Newfield Pers:	1	Contract Pers:	9
Critical Comments					
Activity Summary					
0 Hr(s); P : Tbg pressure @ 2475 psi (annulus @ 0). RU HO trk & bump tbg pressure to 3000 psi. Held solid for 30 minutes. Retrieve standing valve W/ overshot on sandline. Well is flowing slightly (no H2S). NU BOP on secondary spool. Pump remainder of 11 ppg CaCl2 dn 2 7/8 (15 bbls @ 1000 psi). Well is flowing back. Order 12 ppg drilling mud. Bullhead 15 bbls mud down 2 7/8 tbg @ 1200 psi. Well static. Talley, drift, PU & TIH W/ Weatherford 1.90" Seal assembly and 163 jts 1.90" IJ 2.76# J-55 tbg. Sting in & space out W/ 1-10' & 1-4' tbg sub. RU to rev out mud. Unable to lift. SIFN.					
0 Hr(s); P : Mixing Multi-Chen Biocide and H2S Scavenger in all disposal loads.					

NEWFIELD ROCKY MOUNTAINS		Daily Workover Report		Well Name: MON BT NE 3-25-8-16	
		MAJWKO		AFE: 26521	
				Report Date: 2/13/12	
				Operation: Perform MIT	
Field:	GMBU CTB4	Rig Name:	WWS #5	Work Performed:	2/11/2012
Location:	S25 T8S R16E	Supervisor:	Gary Dietz	Day:	6
County:	DUCHESNE	Phone:	435-823-4211	Daily Cost:	\$40,040
State:	UT	Email:	gdietz@newfield.com	Cum DWR:	\$165,708
Reason for Workover: Water Isolation					
24 Hr Summary:	Stage drilling mud from 2 7/8 tbg. Land 1.9" inner string & NU wellhead. RDMOSU & remove associated equipment from location.				
24 Hr Plan Forward:	Perform MIT.				
Incidents:	None	Newfield Pers:	1	Contract Pers:	9
Critical Comments					
1.90" IJ inner string has 1.61" ID !! Need slip type elevators Must remove spool to pull 2 7/8					
Activity Summary					
0 Hr(s); P : Well static. TOH W/ 88 jts of 1.9" tbg. RU HO trk & circ mud out of hole (hole static). TIH W/ 88 jts of tbg. Circ out remainder of mud. Well flowing slightly. Install tbg hanger in string. Sting into PBR & land inner string W/ 5,000# compression. ND BOP. Install Cameron modified B-2 adapter flange & install new threaded gate valve. Shut well in. RDMOSU. RD Total Safety & release equipment. Empty tanks & remove equipment. Well ready for MIT.					



Final Daily Workover Report

Well Name: **MON BT NE 3-25-8-16**

AFE: 26521

Report Date: 2/21/12

MAJWKO

Operation: **MIT**

Field:	GMBU CTB4	Rig Name:	Rigless	Work Performed:	2/14/2012
Location:	S25 T8S R16E	Supervisor:	Alfredo Rios	Day:	7
County:	DUCHESNE	Phone:	435- 823-0173	Daily Cost:	\$41,852
State:	UT	Email:	arios@newfield.com	Cum DWR:	\$207,560

Reason for Workover: Water Isolation

24 Hr Summary: Conduct an MIT

24 Hr Plan Forward: Wait for approval to inject well

Incidents:	None	Newfield Pers:	1	Contract Pers:	0	Conditions:
------------	------	----------------	---	----------------	---	-------------

Critical Comments

1.90" IJ inner string has 1.61" ID !! Need slip type elevators Must remove spool to pull 2 7/8

Activity Summary

09:00 - 09:30; 0.5 Hr(s); P : On 02/13/2012 Chris Jensen with the State of Utah was contacted concerning the MIT on the above listed well. On 02/14/2012 the csg was pressured up to 1155 psig and charted for 30 minute with no pressure loss. The well was not injecting during the test. The tbg pressure for the 1.9 tubing was 890 psig and the tbg pressure for the 2-7/8 tubing was 495 psig during the test. There was not a State representative available to witness the test.

Failures

Failure Date	Failure 1	Failure 2	Failure 3

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67170
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Water Injection Well		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		8. WELL NAME and NUMBER: MON BUTTE FED 3-25-8-16D
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052		9. API NUMBER: 43013316050000
PHONE NUMBER: 435 646-4825 Ext		9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0756 FNL 1946 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENW Section: 25 Township: 08.0S Range: 16.0E Meridian: S		COUNTY: DUCHESNE
		STATE: UTAH

11.

CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA


TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 3/14/2012	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> OTHER	OTHER: <input type="text" value="Put On Injection"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above reference well was put on injection at 2:30 PM on 03/14/2012. The Monument Butte Federal 3-25-8-16 - 2-7/8" tbg has a 1/2" meter with seven digits and was put on at a rate of 250 BWIPD. The Monument Butte Federal 3-25-8-16D - 1.9" tbg has a 1/2" meter with seven digits and was put on at a rate of 200 BWIPD.

**Accepted by the
Utah Division of
Oil, Gas and Mining**

Date: March 26, 2012

By: 

NAME (PLEASE PRINT)

Lucy Chavez-Naupoto

PHONE NUMBER

435 646-4874

TITLE

Water Services Technician

SIGNATURE

N/A

DATE

3/14/2012

Revised
43 013 31605
Monument Butte Federal 3-25-8-16 D

Initial Production: 149 BO,
94 MCF, 3 BWPD

Spud Date: 3/27/96
Put on Production: 4/23/96
Put on Injection: 1/29/97
GL: 5432' KB: 5445'

Injection Diagram

SURFACE CASING


CSG SIZE: 8-5/8"
GRADE: J-55
WEIGHT: 24#
LENGTH: 293.72'
DEPTH LANDED: 290.52'
HOLE SIZE: 12-1/4"
CEMENT DATA: 120 sxs Premium cmt

PRODUCTION CASING

CSG SIZE: 5-1/2"
GRADE: J-55
WEIGHT: 15.5#
LENGTH: 147 jts. (6247')
DEPTH LANDED: 6250.31'
HOLE SIZE: 7-7/8"
CEMENT DATA: 275 sk Hyfill mixed & 350 sxs thixotropic
CEMENT TOP AT: Surface per CBL

TUBING

SIZE/GRADE/WT.: 2-7/8" / M-50 / 6.5#
NO. OF JOINTS: 154 jts (4775.2')
CE 5-1/2" @ 4791.54'
EOT @ 4795'
SIZE/GRADE/WT.: 1.90" IJ / J-55 / 2.76#
NO. OF JOINTS: 163 jts
SEATING NIPPLE: 2-7/8" (1.10')
SN LANDED AT: 5264.9'
Perf Sub 2-7/8" / N-80 (6.2')
PBR Seal Assembly: 2-7/8" @ 5272.2'
CE @ 5280.33'
W.L. reentry guide: 2-7/8" @ 5284.1'
TOTAL STRING LENGTH: EOT @ 5285' KB

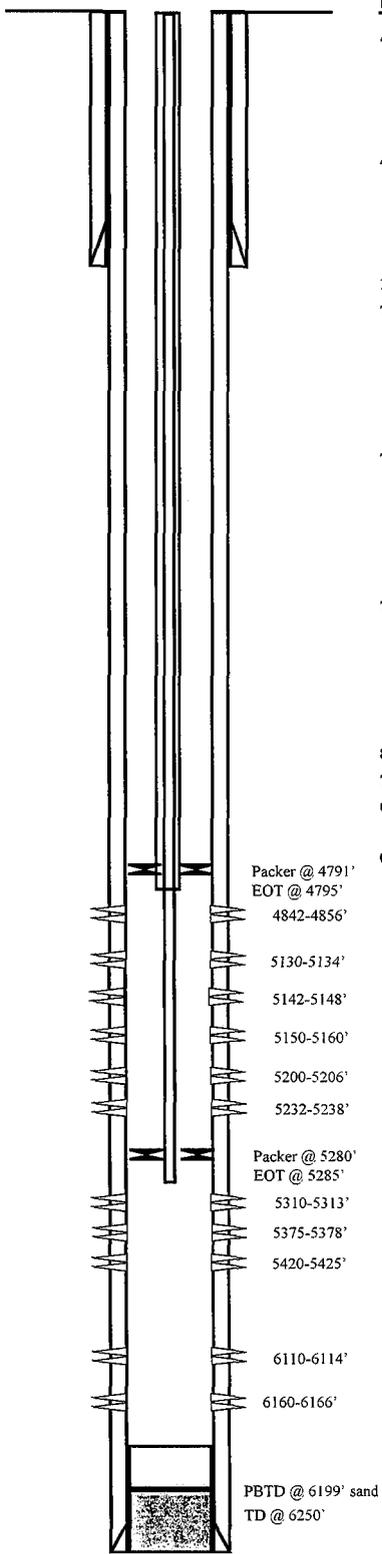

FRAC JOB

4/16/96 5425'-5310' **Frac B-1, Bi-Carb and C sand as follows:**
93,600# of 20/40 sd in 583 bbls of Boragel.
Treated @ avg Rate 31 bpm, avg press 1800
psi. ISIP-1991 psi. Calc. flush: 5420 gal.
Actual flush: 5262 gal.

4/21/96 5142'-5160' **Frac D-1 sand as follows:**
79,000# 20/49 sd in 471 bbls Boragel.
Treated @ avg rate 30 bpm w/1550 psi avg.
ISIP 1967 psi. Calc flush: 5142 gal. Actual
flush: 5039 gal.

1/24/97
7-26-05 6110-6166' **Convert to injector.**

7-26-05 5200-5238' **Recompletion Frac CP2 & CP3 sand as follows:**
19,005#'s 20/40 sd in 198 bbls of
Lightning 17 frac fluid. Treated @ avg
pressure 3580 psi @ ave rate of 14 BPM.
ISIP 2250 psi. Calc flush: 1616 gal. Actual
flush: 1504 gal.

7-26-05 5200-5238' **Recompletion Frac D2 & D3 sands as follows:**
14,299#'s 20/40 sd in 158 bbls of
Lightning 17 frac fluid. Treated @ avg
pressure 3408 psi @ ave rate of 14.1 BPM.
ISIP 2500 psi. Calc flush: 1313 gal. Actual
flush: 1193 gal.

7-26-05 4842-4856' **Recompletion Frac PB10 sands as follows:**
22,023#'s 20/40 sd in 338 bbls of
Lightning 17 frac fluid. Treated @ avg
pressure 3015 psi @ ave rate of 14.1 BPM.
ISIP 2100 psi. Calc flush: 1333 gal. Actual
flush: 1155 gal.

8-17-05 **MIT completed**
7-7-10 **5 yr. MIT**
02/11/12 **Concentric Injection Procedure completed**
- dual injection lines installed - 2 packers set.
02/14/12 **MIT Finalized** - tbg detail updated

PERFORATION RECORD

Date	Interval	Holes	Type	Count
4/15/96	5420'-5425'	4	JSPF	20 holes
4/15/96	5375'-5378'	4	JSPF	12 holes
4/15/96	5310'-5313'	4	JSPF	12 holes
4/17/96	5142'-5148'	4	JSPF	24 holes
4/17/96	5150'-5160'	4	JSPF	40 holes
7-25-05	6110-6114'	4	JSPF	16 holes
7-25-05	6160-6166'	4	JSPF	24 holes
7-25-05	5232-5238'	4	JSPF	24 holes
7-25-05	5200-5206'	4	JSPF	24 holes
7-25-05	5130-5134'	4	JSPF	16 holes
7-25-05	4842-4856'	4	JPPF	56 holes

NEWFIELD

Monument Butte Federal 3-25-8-16 D
756 FNL 1946 ~~FWL~~ FWL
NENW Section 25-T8S-R16E
Duchesne Co, Utah
API #43-013-31605; Lease #U-67170

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-67170
		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
1. TYPE OF WELL Water Injection Well		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		8. WELL NAME and NUMBER: MON BUTTE FED 3-25-8-16D
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052		9. API NUMBER: 43013316050000
PHONE NUMBER: 435 646-4825 Ext		9. FIELD and POOL or WILDCAT: MONUMENT BUTTE
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0756 FNL 1946 FWL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENW Section: 25 Township: 08.0S Range: 16.0E Meridian: S		COUNTY: DUCHESNE
		STATE: UTAH

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 1/12/2017	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input checked="" type="checkbox"/> OTHER	OTHER: <input type="text" value="5 YR MIT"/>

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On 01/09/2017 Amy Doebele with the State of Utah DOGM was contacted concerning the 5 Year MIT on the above listed well. On 01/12/2017 the casing was pressured up to 1125 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tbg pressure for the 1.9 tbg was 1265 psig and the tbg pressure for the 2-7/8" was 1609 psig during the test. There was a State representative available to witness the test - Amy Doebele.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
January 26, 2017**

NAME (PLEASE PRINT) Lucy Chavez-Naupoto	PHONE NUMBER 435 646-4874	TITLE Water Services Technician
SIGNATURE N/A	DATE 1/16/2017	

Mechanical Integrity Test Casing or Annulus Pressure Test

Newfield Production Company

Rt. 3 Box 3630
Myton, UT 84052
435-646-3721

Witness: Amy Doebele Date 1/12/17 Time 8:34 am pm
Test Conducted by: Kim Gides
Others Present: J.D Amy Doebele
5 yr.

Well: 3-25-8-16 Monument Butte Field: Monument Butte
Well Location: NE/1/4 Sec 25, T88 R16E API No: 43-013-31605
Duchesne County, UT

<u>Time</u>	<u>Casing Pressure</u>	
0 min	<u>1125</u>	psig
5	<u>1125</u>	psig
10	<u>1125</u>	psig
15	<u>1125</u>	psig
20		psig
25		psig
30 min		psig
35		psig
40		psig
45		psig
50		psig
55		psig
60 min		psig

Tubing pressure: 1265/1609 psig

Result: Pass Fail

Signature of Witness: Amy Doebele
Signature of Person Conducting Test: Kim Gides

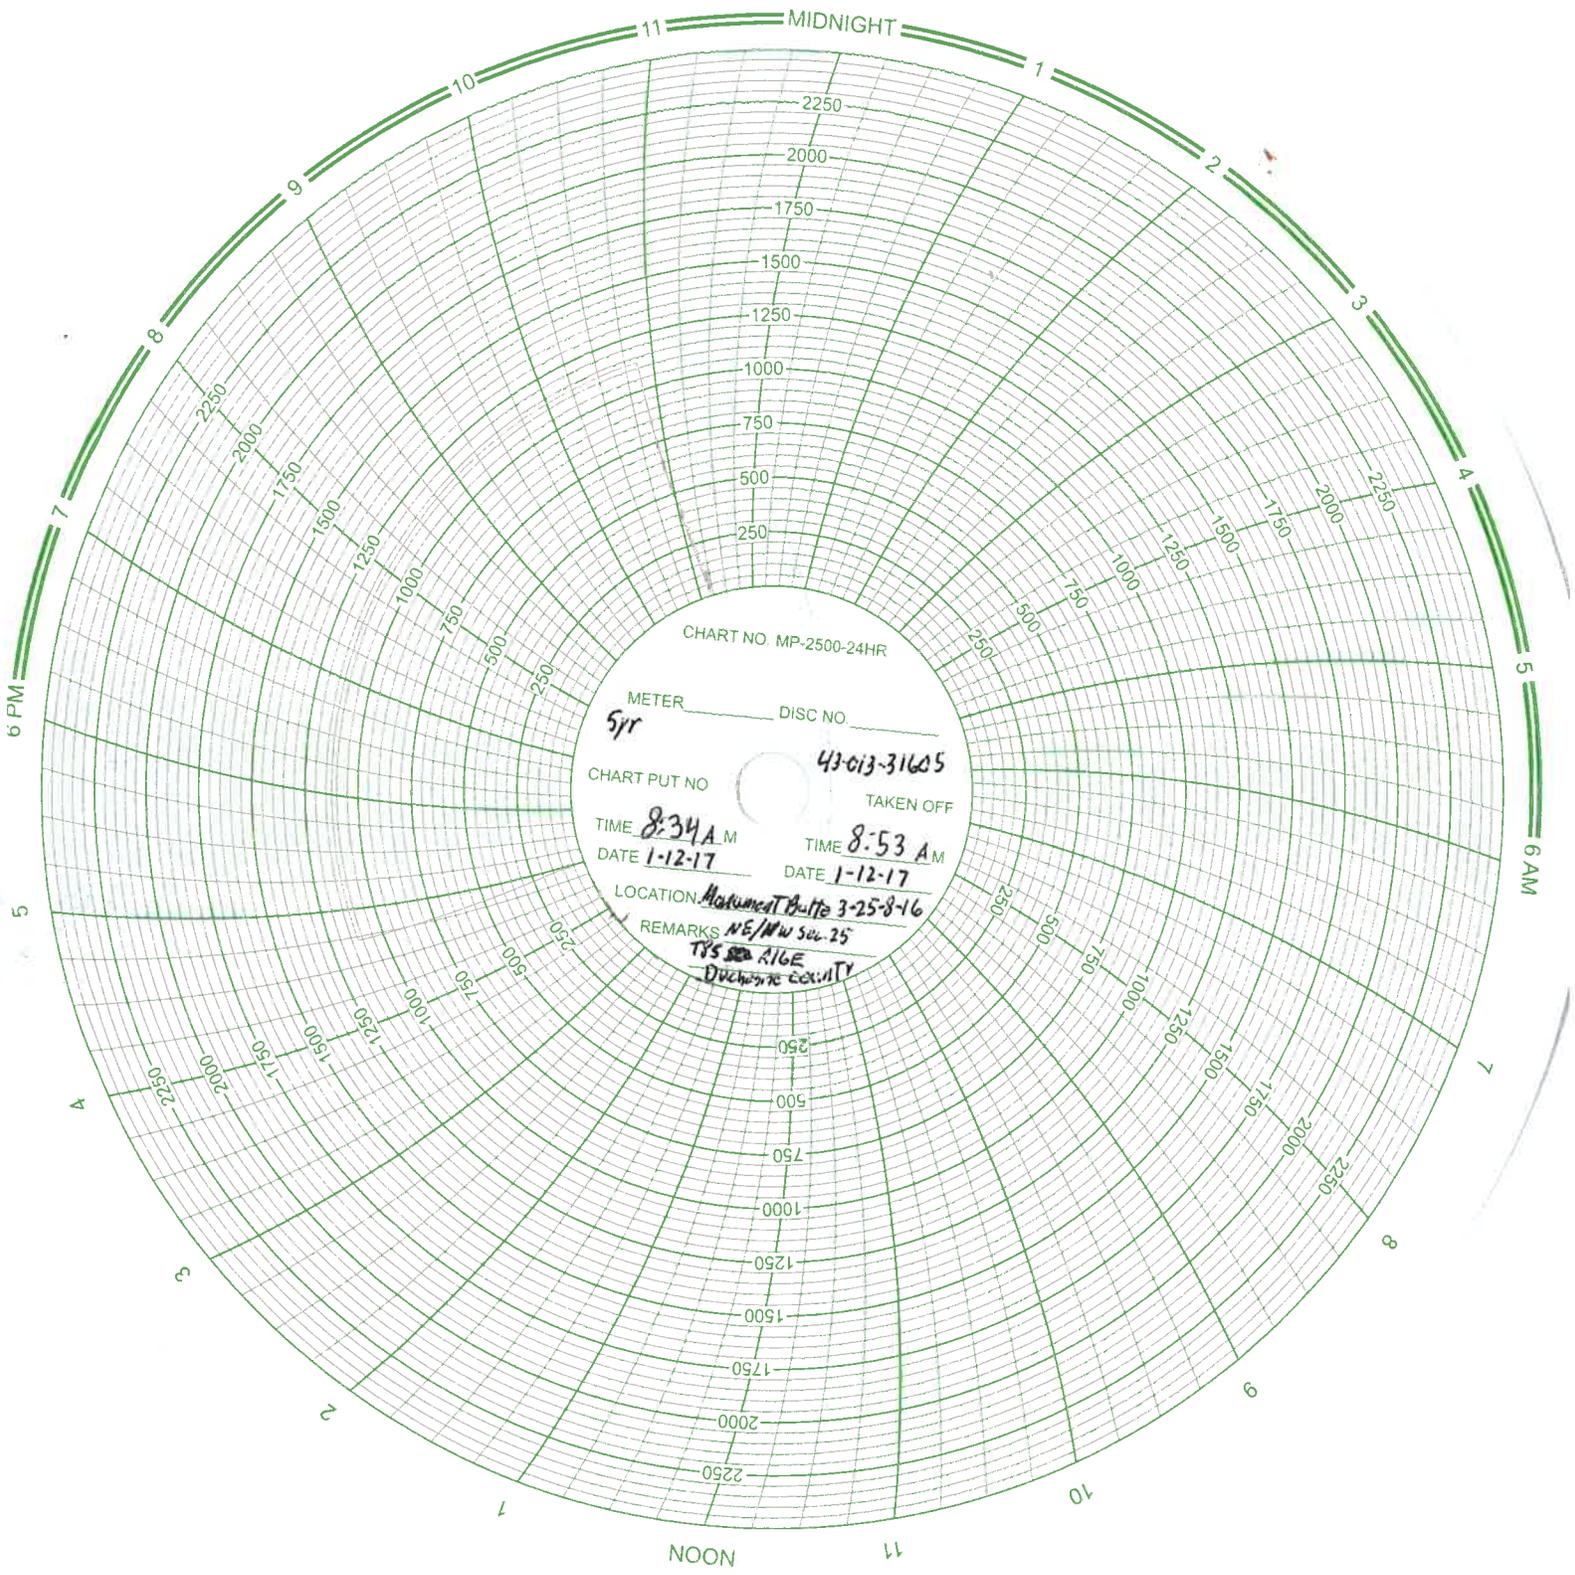


CHART NO MP-2500-24HR

METER 5yr DISC NO _____

CHART PUT NO _____ TAKEN OFF _____

TIME 8:34 A.M TIME 8:53 A.M
DATE 1-12-17 DATE 1-12-17

LOCATION Monument Butte 3-25-8-16

REMARKS NE/W/ Sec. 25
T&S RIG
Duchowicz County
