

UTAH OIL AND GAS CONSERVATION COMMISSION

REMARKS: WELL LOG ELECTRIC LOG FILE ☒ X WATER SANDS LOCATION INSPECTED SUB. REPORT/abd.

971107 Conf exp:

DATE FILED JULY 26, 1996

LAND: FEE & PATENTED

STATE LEASE NO.

PUBLIC LEASE NO.

INDIAN #

DRILLING APPROVED: SEPTEMBER 3, 1996

14-20-H62-3507

SPUDDED IN: SEPTEMBER 12, 1996

COMPLETED: 10.3.96 PDW PUT TO PRODUCING:

INITIAL PRODUCTION: 79 Bbl - 20 mcf - 29 Bbl

GRAVITY A.P.I.

GOR:

PRODUCING ZONES 4394 - 6232' GRV

TOTAL DEPTH: 6296'

WELL ELEVATION: 6029'

DATE ABANDONED:

FIELD: ANTELOPE CREEK

UNIT:

COUNTY: DUCHESNE

WELL NO. UTE TRIBAL 08-07

API NO. 43-013-31691

LOCATION 1700 FNL FT. FROM (N) (S) LINE, 2133 FEL

FT. FROM (E) (W) LINE. SW NW

1/4 - 1/4 SEC. 8

TWP. RGE. SEC. OPERATOR

TWP. RGE. SEC. OPERATOR

5S

3W

8


PETROGLYPH OPERATING

QUATERNARY	Star Point	Chinle	Molas
Alluvium	Wahweap	Shinarump	Manning Canyon
Lake beds	Masuk	Moenkopi	Mississippian
Pleistocene	Colorado	Sinbad	Humburg
Lake beds	Sego	PERMIAN	Brazer
TERTIARY	Buck Tongue	Kaibab	Pilot Shale
Pliocene	Castlegate	Coconino	Madison
Salt Lake	Mancos	Cutler	Leadville
Oligocene	Upper	Hoskinnini	Redwall
Norwood	Middle	DeChelly	DEVONIAN
Eocene	Lower	White Rim	Upper
Duchesne River	Emery	Organ Rock	Middle
Uinta	Blue Gate	Cedar Mesa	Lower
Bridger	Ferron	Haigaite Tongue	Ouray
Green River	Frontier	Phosphoria	Elbert
X MARKER	Dakota	Park City	McCracken
Downs Creek	Burro Canyon	Rico (Goodridge)	Aneth
B. Pine Stone	Cedar Mountain	Supai	Simonson Dolomite
Castle Peak	Buckhorn	Wolfcamp	Sevy Dolomite
Basal Camb	JURASSIC	CARBON I FEROUS	North Point
Wasatch	Morrison	Pennsylvanian	SILURIAN
Stone Cabin	Salt Wash	Oquirrh	Laketown Dolomite
Colton	San Rafael Gr.	Weber	ORDOVICIAN
Flagstaff	Summerville	Morgan	Eureka Quartzite
North Horn	Bluff Sandstone	Hermosa	Pogonip Limestone
Almy	Curtis		CAMBRIAN
Paleocene	Entrada	Pardox	Lynch
Current Creek	Moab Tongue	Ismay	Bowman
North Horn	Carmel	Desert Creek	Tapeats
CRETACEOUS	Glen Canyon Gr.	Akah	Ophir
Montana	Navajo	Barker Creek	Tintic
Mesaverde	Kayenta		PRE - CAMBRIAN
Price River	W. gate	Cane Creek	
Blackhawk	SSIC		

Petroglyph Operating Co., Inc.
P.O. Box 1839
Hutchinson, KS 67504-1839

July 19, 1996

Utah Division of Oil, Gas, & Mining
Attn: Mr. Frank Matthews, Petroleum Engineer
1594 West North Temple
Box 145801
Salt Lake City, UT 84114-5801



RE: APPLICATION FOR PERMIT TO DRILL
UTE TRIBAL # 08-07
SW/NE SEC. 8, T5S, R3W
DUCHESNE COUNTY, UTAH
LEASE NO. BIA 14-20-H62-3507
UTE TRIBAL LANDS

Dear Mr. Matthews:

Enclosed please find a copy of the Application for Permit to Drill and associated attachments for the referenced well.

Please address further communication regarding this matter (including approval) to:

Ed Trotter
P.O. Box 1910
Vernal, UT 84078
Phone # (801) 789-4120
Fax # (801) 789-1420

Sincerely,

Ed Trotter
Agent

Petroglyph Operating Co., Inc.

Attachments

/EHT/dmt

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL, DEEPEN, OR PLUG BACK

1a. TYPE OF WORK

DRILL ☒

DEEPEN ☐

PLUG BACK ☐

b. TYPE OF WELL

OIL
WELL ☒

GAS
WELL ☐

OTHER

SINGLE
ZONE ☐

MULTIPLE
ZONE ☐

2. NAME OF OPERATOR

PETROGLYPH OPERATING COMPANY INC.

3. ADDRESS OF OPERATOR

P.O. BOX 607 ROOSEVELT, UT 84066

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.*)

At surface

1700' FNL & 2133' FEL SW/4 NW/4

At proposed prod. zone

14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*

17.3 miles southwest of Myton, UT

15. DISTANCE FROM PROPOSED*

LOCATION TO NEAREST
PROPERTY OR LEASE LINE, FT.
(Also to nearest drig. unit line, if any)

1700'

16. NO. OF ACRES IN LEASE

640

17. NO. OF ACRES ASSIGNED
TO THIS WELL

40

18. DISTANCE FROM PROPOSED LOCATION*
TO NEAREST WELL, DRILLING, COMPLETED,
OR APPLIED FOR, ON THIS LEASE, FT.

19. PROPOSED DEPTH

6296'

20. ROTARY OR CABLE TOOLS

ROTARY

21. ELEVATIONS (Show whether DF, RT, GR, etc.)

6029' GRADED GROUND

22. APPROX. DATE WORK WILL START*

AUGUST, 1996

23.


PROPOSED CASING AND CEMENTING PROGRAM

SIZE OF HOLE	SIZE OF CASING	WEIGHT PER FOOT	SETTING DEPTH	QUANTITY OF CEMENT
12 1/4	8 5/8	24.0#	250'	135 sx class "G" + 2% CaCl ₂
7 7/8	5 1/2	15.5#	6296'	+ 1/4 #/sx celloflake.

50/50 POZMIX + 2% GEL + 10%
SALT TO 400' ABOVE ALL ZONES
OF INTEREST (+ 10% EXCESS).
LIGHT CEMENT (11 PPG +) +
LCM TO 200' ABOVE OIL SHALE
OR FRESH WATER INTERVALS
(+ 5% EXCESS).

PETROGLYPH OPERATING COMPANY INC. WILL BE THE DESIGNATED
OPERATOR OF THE SUBJECT WELL UNDER BOND # BO 4556.

pc: Utah Division of Oil, Gas and Mining
Bureau of Indian Affairs, Fort Duchesne, UT
Ute Tribe, Fort Duchesne, UT



IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen or plug back, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24.

SIGNED

TITLE AGENT FOR PETROGLYPH

DATE JULY 19, 1996

(This space for Federal or State office use)

PERMIT NO.

43-013-31691

APPROVAL DATE

APPROVED BY

TITLE

DATE

9/3/96

CONDITIONS OF APPROVAL, IF ANY:


*See Instructions On Reverse Side

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

T5S, R3W, U.S.B.&M.


PETROGLYPH OPERATING CO., INC.

Well Location, UTE TRIBAL #08-07, located as shown in SW 1/4 NE 1/4 of Section 8, T5S, R3W, U.S.B.&M. Duchesne County, Utah.

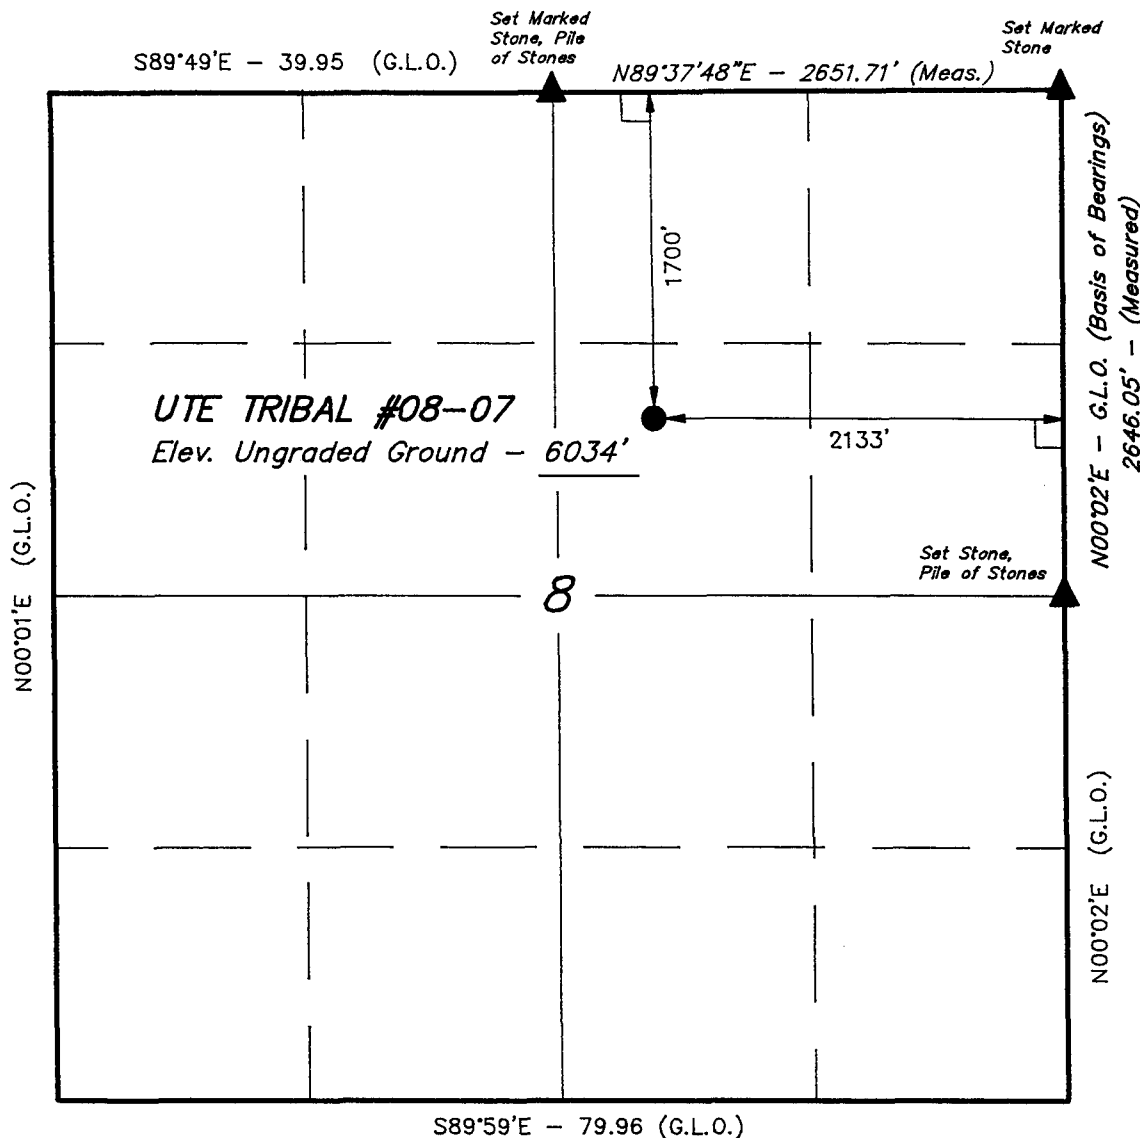

BASIS OF ELEVATION

SPOT ELEVATION AT THE NORTHEAST CORNER OF SECTION 8, T5S, R3W, U.S.B.&M. TAKEN FROM THE MYTON SW, QUADRANGLE, UTAH, DUCHESNE COUNTY, 7.5 MINUTE SERIES (TOPOGRAPHICAL MAP) PUBLISHED BY THE UNITED STATES DEPARTMENT OF THE INTERIOR, GEOLOGICAL SURVEY. SAID ELEVATION IS MARKED AS BEING 6060 FEET.

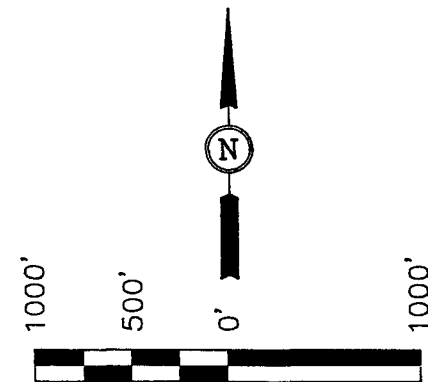

SCALE

CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME, OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

U. S. ROBERT L. FINE
REGISTERED LAND SURVEYOR
REGISTRATION NO. 161319
STATE OF UTAH

LEGEND:

- └─┘ = 90° SYMBOL
- = PROPOSED WELL HEAD.
- ▲ = SECTION CORNERS LOCATED.

UINTAH ENGINEERING & LAND SURVEYING

85 SOUTH 200 EAST - VERNAL, UTAH 84078

(801) 789-1017

SCALE 1" = 1000'	DATE SURVEYED: 7-1-96	DATE DRAWN: 7-2-96
PARTY D.A. H.M. L.T. G.S. C.T.	REFERENCES G.L.O. PLAT	
WEATHER HOT	FILE PETROGLYPH OPERATING CO., INC.	

EIGHT POINT PLAN

UTE TRIBAL #08-07
SW/NE SEC. 8, T5S R3W
DUCHESNE COUNTY, UTAH

1. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

FORMATIONS	DEPTH	SUBSEA
Mahogany Shale	2871.1	3168
'X' marker	4474.1	1565
Douglas Creek	4614.1	1425
"B" Limestone	5007.1	1032
B/Castle Peak Limestone	5561.1	478
Basal Carbonate Limestone	5966.1	73
Total Depth	6296.1	-257

Anticipated BHP 2700 psi

2. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS FORMATIONS:

<u>Substance</u>	<u>Formation</u>	<u>Depth</u>	<u>Subsea</u>
Oil/Gas	Douglas Creek	4614.1	1425
Oil/Gas	B/Castle Peak	5561.1	478
Other mineral zones	N/A		

3. PRESSURE CONTROL EQUIPMENT : BOP Schematic Diagram attached.

4. CASING PROGRAM :

						<u>MINIMUM SAFETY FACTOR</u>		
<u>HOLE SIZE</u>	<u>INTERVAL</u>	<u>LENGTH</u>	<u>SIZE</u>	<u>WEIGHT</u>	<u>GRADE</u>	<u>COLLAPSE</u>	<u>BURST</u>	<u>TENSILE</u>
12 1/4	0' - 250'	250'	8 5/8	24.0 #	J-55	1370 PSI	2950 PSI	263,000#
7 7/8	0' -6296.1'	6296.1'	5 1/2	15.5 #	M-50	4040 PSI	4810 PSI	202,000#

All casing will be new or inspected.

EIGHT POINT PLAN

UTE TRIBAL #08-07
SW/NE SEC. 8, T5S R3W
DUCHESNE COUNTY, UTAH

5. MUD PROGRAM

INTERVAL

0' - 250'
250' - 4000'
4000' - TD
TD

MUD TYPE

Air
Air/Mist & Aerated Water
Air/3% KCL water or KCL substitute
Gel/polyacrylamide polymer w/5-10% LCM

Sufficient mud inventory will be maintained on location during drilling to handle any adverse conditions that may arise.

6. VARIANCE REQUESTS:

- A. Petroglyph Operating Co., Inc. requests a variance to regulations requiring a straight run blooie line.
- B. Petroglyph Operating Co., Inc. requests a variance to regulations requiring an automatic ignitor or continuous pilot light on the blooie line.

7. EVALUATION PROGRAM:

Logs: Mud Logging	T.D. to base of surface csg.
Compensated Density-Compensated Neutron Log	T.D. to base of surface csg.
Dual Laterolog - Micro-SFL	T.D. to base of surface csg.
Numar (Magnetic Resonance Imaging Log)	@ Geologists discretion

Cores: None Programmed
DST': None Programmed

Completion: To be submitted at a later date.

8. ABNORMAL CONDITIONS:

None anticipated.

EIGHT POINT PLAN

UTE TRIBAL #08-07
SW/NE SEC. 8, T5S R3W
DUCHESNE COUNTY, UTAH

9. STANDARD REQUIRED EQUIPMENT:

- A. Choke Manifold
- B. Kelly Cock
- C. Stabbing Valve
- D. Visual Mud Monitoring

10. HAZARDOUS CHEMICALS:

No chemicals subject to reporting under SARA title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling of this well.

(Attachment: BOP Schematic Diagram)

2000 PSIG DIAGRAM


BOTH RAMS ARE 2000 PSIG RATED.

CASING FLANGE IS 9" 2000 PSIG RATED.

BOPE 9" 2000 PSIG

TESTING PROCEDURE:

1. BOPE 's will be tested with a professional tester to conform to Onshore Order #2 with retest every 14 days.
2. Blind rams will be tested to rated working pressure, 2000 psig
3. Casing will be tested to 0.22 psi/ft. or 1500 psig. Not to exceed 70% of burst strength, whichever is greater.
4. All lines subject to well pressure will be pressure tested to the same pressure as blind & pipe rams.
5. All BOPE specifications and configurations will meet Onshore Order #2 requirements for 2000 psig BOPE specifications.

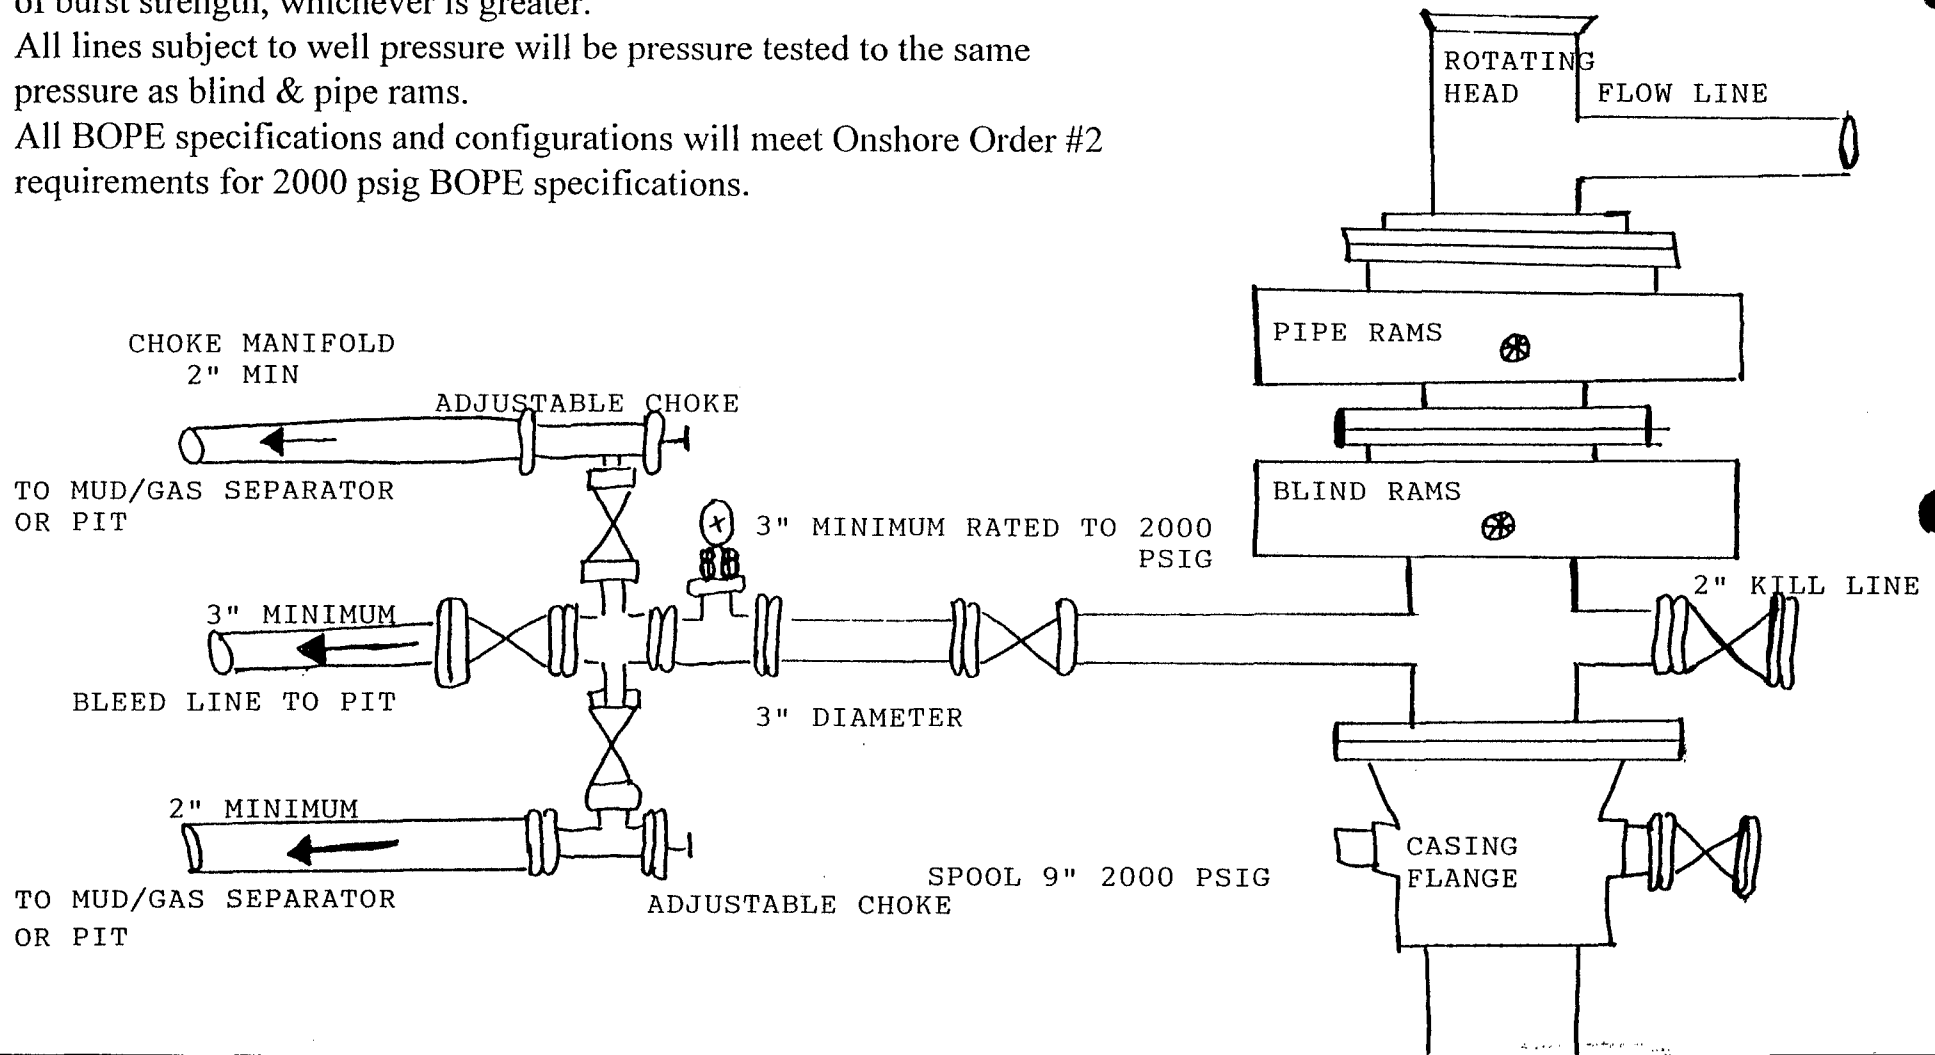

CONDITIONS OF APPROVAL
FOR THE SURFACE USE PROGRAM OF THE
APPLICATION FOR PERMIT TO DRILL

Company/Operator: Petroglyph Operating Co., Inc.
Well Name & Number: Ute Tribal #08-07
Lease Number: BIA 14-20-H62-3507
Location: 1700' FNL & 2133' FEL, SW/NE, Sec. 8, T5S R3W
U.S.B.&M., Duchesne County, Utah
Surface Ownership: Ute Indian Tribe

NOTIFICATION REQUIREMENTS

Location Construction - forty-eight (48) hours prior to construction of location and access roads.

Location Completion - prior to moving on the drilling rig.

Spud Notice - at least twenty-four (24) hours prior to spudding the well.

Casing String and Cementing - twenty-four (24) hours prior to running casing and cementing all casing strings.

BOP and related Equipment Tests - twenty-four (24) hours prior to running casing and tests.

First Production Notice - within five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

For more specific details on notification requirements, please check the Conditions of Approval for Notice To Drill and Surface Use Program.

THIRTEEN POINT SURFACE USE PROGRAM

1. EXISTING ROADS

- A. See attached Wellsite Plats showing directional reference stakes on location, and attached TOPO Map "B" showing access to location from existing road.
- B. The proposed well site is located approximately 17.3 miles southwest of Myton, Utah - See attached TOPO Map "A".
- C. Refer to attached Topographic Map "A" showing labeled access route to location.
- D. Existing roads will be maintained and repaired as necessary. No off lease Right-of-Way will be required.

2. PLANNED ACCESS ROAD

- A. The access road will be approximately 0.2 miles in length. See attached TOPO Map "B"
- B. The access road has a 30 foot ROW w/18 foot running surface.
- C. Maximum grade on access road will be 8%
- D. No turnouts will be required.
- E. Road drainage crossings shall be of the typical dry creek drainage crossing type.
- F. No culverts, bridges or major cuts & fills will be required.
- G. The access road will be dirt surface.
- H. No gates, cattleguards or fences will be required or encountered.

New or reconstructed roads will be centerlined - flagged at time of location staking.

All travel will be confined to existing access road Right-of-Way.

Access roads and surface disturbing activities will conform to standards outlined in the Bureau of Land Management and Forest Service Publication: Surface Operating Standards For Oil & Gas Exploration and Development, (1989).

The road shall be upgraded to meet the standards of the anticipated traffic flow and all-weather road requirements. Upgrading shall include ditching, drainage, graveling, crowning, and capping the

roadbed as necessary to provide a well-constructed safe road.

Prior to upgrading, the road shall be cleared of any snow cover and allowed to dry completely. Traveling off the 30 foot Right-of- Way will not be allowed.

Road drainage crossings shall be of the typical dry creek drainage crossing type. Crossings shall be designed so they will not cause siltation or accumulation of debris in the drainage crossings nor shall the drainages be blocked by the roadbed. Erosion of drainage ditches by run off water shall be prevented by diverting water off at frequent intervals by means of cutouts. Upgrading shall not be allowed during muddy conditions. Should mud holes develop, they shall be filled in and detours around them avoided.

As operator, Petroglyph Operating Co., Inc. shall be responsible for all maintenance on cattleguards, or gates associated with this oil and/or gas operation.

3. LOCATION OF EXISTING WELLS WITHIN A ONE MILE RADIUS OF PROPOSED WELL LOCATION

- A. Water wells - None
 - B. Abandoned wells - None
 - C. Temporarily abandoned wells - None.
 - D. Disposal wells - None.
 - E. Drilling wells - None.
 - F. Producing wells - 13*
 - G. Shut in wells - 1*
 - H. Injection wells - None
- (*See attached TOPO map "C" for location)

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

A. ON WELL PAD

- 1. Tank batteries - None
- 2. Production facilities-To be submitted later
- 3. Oil gathering lines - None

4. Gas gathering lines-None
5. Injection lines - None
6. Disposal lines - None
7. Surface pits - None

B. OFF WELL PAD

1. Proposed location of attendant off pad flowlines shall be flagged prior to archaeological clearance.
2. A 4 1/2" OD steel above ground gas sales pipeline will be laid approximately 1700' from proposed location to a point in the NE/NE of Section 8, T5S, R3W, where it will tie into Petroglyph Operating Co., Inc.'s existing pipeline.
Proposed pipeline crosses Ute Tribe lands, thus a Right-of-Way grant will be required. See attached TOPO Map D showing pipeline route.
3. Proposed pipeline will be a 4 1/2" OD steel, welded line laid on the surface.
4. Protective measures and devices for livestock and wildlife will be taken and/or installed where required.

If storage facilities/tank batteries are constructed on this lease, the facility/battery or the well pad shall be surrounded by a containment dike of sufficient capacity to contain, at a minimum, the entire contents of the largest tank within the facility/battery, unless more stringent protective requirements are deemed necessary by the authorized officer.

The production facilities will be placed on the West side of the location.

All permanent (on site for six months or longer) structures constructed or installed (including pumping units) will be painted a flat, non-reflective, earthtone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities required will be painted within 6 months of installation. Facilities required to comply with O.S.H.A.

(Occupational Safety and Health Act) will be excluded.
The required paint color is Desert Brown.

5. LOCATION & TYPE OF WATER SUPPLY

- A. Water supply will be from Target Trucking's Roosevelt Brine Storage and/or Target's water source in SE 1/4, Sec. 1, T 4S, R 5W Duchesne County, Utah (State water right #43-10152). All water will come from a non-depletable source.
- B. Water will be hauled by Target Trucking.
- C. No water well will be drilled on lease.

6. SOURCE OF CONSTRUCTION MATERIAL

- A. All construction material for this location and access road will be of native borrow and soil accumulated during the construction of location.
- B. All construction material will come from Ute Tribal Land.
- C. No mineral materials will be required.

7. METHODS OF HANDLING WASTE DISPOSAL

A. METHODS AND LOCATION

- 1. Cuttings will be confined in the reserve pit.
- 2. A portable toilet will be provided for human waste during the drilling and completion of the well. Disposal will be at the Vernal sewage disposal plant.
- 3. Burning will not be allowed. Trash and other waste material will be contained in a wire mesh cage and disposed of at an approved waste disposal facility.
- 4. Produced waste water will be confined to a lined pit or storage tank for a period not to exceed 90 days after initial production. During the 90 day period, an application for approval of a permanent disposal method and location, together with the required water analysis, will be submitted for the AO's approval.

5. All chemicals will be disposed of at an authorized disposal site. Drip pans and absorbent pads will be used on drilling rig to avoid leakage of oil to pit.

B. Water from drilling fluids and recovered during testing operations will be disposed of by either evaporating in reserve pit or be removed and disposed of at an authorized disposal site. Introduction of well bore hydrocarbons to reserve pit will be avoided by flaring them off in flare pit at time of recovery.

Burning of trash will not be allowed. All trash must be contained in a trash cage and hauled away to an approved disposal site at the completion of the drilling activities.

On BIA administered land:

All reserve pits will be lined with either native clay, commercial bentonite or plastic sufficient to prevent seepage. (If a plastic nylon reinforced liner is used, it shall be torn and perforated after the pit dries and before backfilling of the reserve pit).

A 12 mill liner shall be installed in the reserve pit.

___To protect the environment:

If the reserve pit is lined the operator will provide the BIA with a chemical analysis of the fluids in that pit no later than 90 days after the well completion to determine the method for final reclamation of the reserve pit. If the elemental concentrations shown by the chemical analysis exceeds the requirements described by part II, Standards of Quality for Waters of the State, Wastewater Disposal Regulations, State of Utah Division of Health, the contents and liner will be removed and disposed of at an authorized disposal site.

___To protect the environment (without a chemical analysis)
reserve pits will be constructed so as not to leak, break, or allow discharge of liquids.

___Storage tanks will be used if drill sites are located on tribal

irrigable land, flood plains, or on lands under crop production. After first production, produced waste water will be confined to a lined pit or storage tank for a period not to exceed ninety (90) days. During the 90 day period, in accordance with NTL-2B, an application for approval of a permanent disposal method and location, along with required water analysis, shall be submitted for the AO's approval. Failure to file an application within the time allowed will be considered an incident of noncompliance.

8. ANCILLARY FACILITIES

- A. No airstrips or camps are planned for this well.

9. WELL SITE LAYOUT

- A. Refer to attached well site plat for related topography cuts and fills & cross sections.
- B. Refer to attached well site plat for rig layout and soil material stockpile location as approved on On-site.
- C. Refer to attached well site plat for rig orientation parking areas, and access road.

The reserve pit will be located on the Southeast side of the location.

The flare pit will be located downwind of the prevailing wind direction on the Southeast side of the location, a minimum of 100 feet from the well head and 30 feet from the reserve pit fence.

The stockpiled topsoil will be stored on the Northwest side.

Access to the well pad will be from the Northeast.

N/A Diversion ditch(es) shall be constructed on the _____ side of the location (above/below) the cut slope, draining to the _____

N/A Soil compacted earthen berm(s) shall be placed on the _____ side(s) of the location between the _____

N/A The drainage(s) shall be diverted around the sides of the well pad location.

N/A The reserve pit and/or pad locations shall be constructed long and narrow for topographic reasons _____

X Corners No. 2, 6 & 8 will be rounded off to minimize excavation.

FENCING REQUIREMENTS

All pits will be fenced according to the following minimum standards:

- A. 39 inch net wire shall be used with at least one strand of barbed wire on top of the net wire. (barbed wire is not necessary if pipe or some type of reinforcement rod is attached to the top of the entire fence).
- B. The net wire shall be no more than 2 inches above the ground. The barbed wire strand shall be 3 inches above the net wire. Total height of the fence shall be at least 42 inches.
- C. Corner posts shall be cemented and/or braced in such a manner to keep the fence tight at all times.
- D. Standard steel, wood, or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than 16'.
- E. All wire shall be stretched by using a stretching device before it is attached to the corner posts.

The reserve pit fencing will be on the three sides during drilling operations and on the fourth side when the rig moves off the location. Pits will be fenced and maintained until clean-up.

Each existing fence to be crossed by the access road shall be braced and tied off before cutting so as to prevent slacking of the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BIA or SMA specifications. A cattleguard with an adjacent 16 foot gate shall be installed in any fence where a road is to be regularly travelled. If the well is a producer, the cattleguards (shall/ shall not) be permanently mounted on concrete bases. Prior to a new road, crossing any fence located on federal land, or any fence between federal land and private land, the operator will contact the BIA, who will in turn contact the grazing permittee or owner of said fence and offer him/her the opportunity to be present when the fence is cut in order to

satisfy himself/herself that the fence is adequately braced and tied off.

10. PLANS FOR RESTORATION OF SURFACE

A. PRODUCING LOCATION

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, materials, trash, and junk not required for production.

Immediately upon well completion, any hydrocarbons on the pit shall be removed in accordance with CFR 3162.7-1.

If a plastic nylon reinforced liner is used, it shall be torn and perforated before backfilling of the reserve pit.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximate natural contours. The reserve pit will be reclaimed within 120 days from the date of well completion (weather permitting). Before any dirt work takes place, the reserve pit will be completely dry and all cans, barrels, pipe, fluid, and hydrocarbons, will be removed.

Contact appropriate surface management agency for required seed mixture.

B. DRY HOLE/ABANDONED LOCATION

At such time as the well is plugged and abandoned, the operator will submit a subsequent report of abandonment and BIA will attach the appropriate surface rehabilitation conditions of approval.

ON BIA Administered lands:

Abandoned well sites, roads, or other disturbed areas will be restored to near their original condition. This procedure will include: (a) reestablishing irrigation systems where applicable, (b) reestablishing soil conditions in irrigated fields in such a way as to ensure cultivation and harvesting of crops and, (c) ensuring revegetation of the disturbed areas to the specifications of the Ute Indian Tribe or the BIA at the time of abandonment.

11. SURFACE OWNERSHIP

Access road: Ute Indian Tribe

Location: Ute Indian Tribe

12. OTHER INFORMATION

- A. Petroglyph Operating Co., Inc. will inform all persons in the area who are associated with this project that they are subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, the operator will immediately stop work that might further disturb such materials, and contact the AO. Within five working days the AO will inform the operator as to:
- whether the materials appear eligible for the National Register of historic Places;

the mitigation measures the operator will likely have to undertake before the site can be used.

-a time frame for the AO to complete an expedited review under 36 CFR 800.11 to confirm, through the State Historic Preservation Officer, that the findings of the AO are correct and that mitigation is appropriate.

If the operator wished, at any time, to relocate activities to avoid the expense of mitigation and/or the delays associated with this process, the AO will assume responsibility for whatever recordation and stabilization of the exposed materials that may be required. Otherwise, the operator will be responsible for mitigation costs. The AO will provide technical and procedural guidelines for the conduct of mitigation. Upon verification from the AO that required mitigation has been completed, the operator will then be allowed to resume construction.

- B. As operator, Petroglyph Operating Co., Inc. will control noxious weeds along Right-of-Ways for roads, pipelines, well sites, or other applicable facilities. A list of noxious weeds will be obtained from the BIA,

or the appropriate County Extension Office. On BIA administered land, a Pesticide Use proposal shall be submitted, and given approval, prior to the application of herbicides or other pesticides or possible hazardous chemicals.

- C. Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on Tribal Lands after the conclusion of drilling operations or at any other time without BIA authorization. However, if BIA authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

On BIA administered land:

Operator's employees, including subcontractors, will not gather firewood along roads constructed by operators. If wood cutting is required, a permit will be obtained from the Forestry Department of the BIA pursuant to 25 CFR 169.13 "Assessed Damages Incident to Right-of-Way authorization". All operators, subcontractors, vendors, and their employees or agents may not disturb saleable timber (including firewood) without a duly granted wood permit from the BIA Forester.

If the surface rights are owned by the Ute Indian Tribe and mineral rights are owned by another entity, an approved right-of-way will be obtained from the BIA before the operator begins any construction activities. If the surface is owned by another entity and the mineral rights are owned by the Ute Indian Tribe, rights-of-way will be obtained from the other entity.

All roads constructed by operators on the Uintah and Ouray Indian Reservation will have appropriate signs. Signs will be neat and of sound construction. They will state: (a) that the land is owned by the Ute Indian Tribe, (b) the name of the operator, (c) that firearms are prohibited to all non-Ute Tribal members (d) that permits must be obtained from the BIA before cutting firewood or other timber products, and (e) only authorized personnel permitted. All well site locations on the Uintah and Ouray Indian Reservation will have an appropriate sign indicating the name of the operator,

the lease serial number, the well name and number, the survey description of the well (either footage or the quarter-quarter section, the section, township, and range).

Additional Surface Stipulations

N/A No construction or drilling activities shall be conducted between

_____ and _____ because of _____

N/A No surface occupancy will be allowed within 1,000 feet of any sage grouse strutting ground.

N/A No construction or exploration activities are permitted within 1.5 mile radius of sage grouse strutting grounds from April 1 to June 30.

N/A There shall be no surface disturbance within 600 feet of live water (includes stock tanks, springs, and guzzlers).

N/A No cottonwood trees will be removed or damaged.

N/A Pond will be constructed according to BLM specifications approximately _____ ft. _____ of the location, as flagged on onsite.

LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION

PERMITTING

Ed Trotter

1620 West 750 North

Vernal UT 84078

Telephone # (801)789-4120

Fax # (801) 789-1420

OPERATIONS

Deanna Bell

P.O. Box 607

Roosevelt, UT 84066

(801) 722-2531

Fax # (801) 722-9145

All lease/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws, regulations, Onshore Oil and Gas Orders, the approval plan of operations, and any applicable Notice to Lessees. Petroglyph Operating Co., Inc. is fully responsible for the actions of their subcontractors. A copy of these conditions will be furnished to the field representative to insure compliance.

A copy of the approved APD and ROW grant, if applicable, shall be on location during construction of the location and drilling activities.

The BIA Office shall be notified upon site completion prior to moving on the drilling rig.

Certification:

I hereby certify that I, or persons under my direct supervision, have inspected the proposed drillsite and access route; that I am familiar with the conditions which presently exist; that the statements made in the Plan are to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed by Petroglyph Operating Co., Inc. and its contractors and sub-contractors in conformity with this Plan and the terms and conditions under which it is approved.

7-19-96



Date



PETROGLYPH OPERATING CO., INC.

LOCATION LAYOUT FOR

UTE TRIBAL #08-07
SECTION 8, T5S, R3W, U.S.B.&M.
1700' FNL 2133' FEL

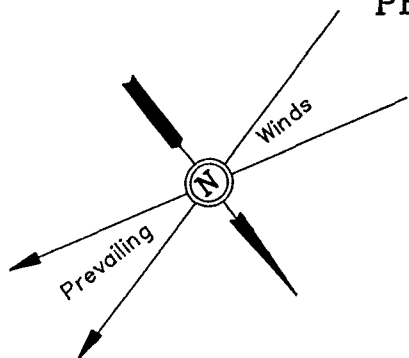

SCALE: 1" = 50'
DATE: 7-2-96
Drawn By: C.B.T.

NOTE:

Flare Pit is to be located a min. of 100' from the Well Head.

FLARE PIT



NOTE:
Pit Capacity W/2' of Freeboard is $\pm 4,600$ Bbls.

El. 34.3'
C-13.2' (btm. pit)

El. 41.9'
C-12.8'

Reserve Pit Backfill & Spoils Stockpile

RESERVE PITS (8' Deep)

Sta. 0+52

El. 48.2'
C-27.1' (btm. pit)

El. 46.1'
C-17.0'

Approx. Top of Cut Slope

El. 35.6'
C-6.5'

El. 26.1'
F-3.0'

El. 18.1'
F-11.0'

El. 23.9'
F-5.2'

Sta. 1+50

El. 07.6' Sta. 2+75
F-21.5'

Approx. Toe of Fill Slope

Topsoil Stockpile

Sta. 0+00

El. 11.8'
F-17.3'

El. 19.6'
F-9.5'

Existing Drainage

Existing Drainage

Round Corners as Needed

PIPE RACKS

CATWALK 125'

El. 34.3'
C-5.2'

40' RIG DOG HOUSE

100'

PUMP

MUD SHED

HOPPER

POWER

TOOLS

FUEL

STORAGE TANK

TRAILER

TOILET

FUEL

TRASH


40' 150'

Proposed Access Road

Elev. Ungraded Ground at Location Stake = 6034.3'

Elev. Graded Ground at Location Stake = 6029.1'

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East • Vernal, Utah 84078 • (801) 789-1017





PETROGLYPH OPERATING CO., INC.

TYPICAL CROSS SECTIONS FOR

UTE TRIBAL #08-07
SECTION 8, T5S, R3W, U.S.B.&M.
1700' FNL 2133' FEL

DATE: 7-2-96
Drawn By: C.B.T.

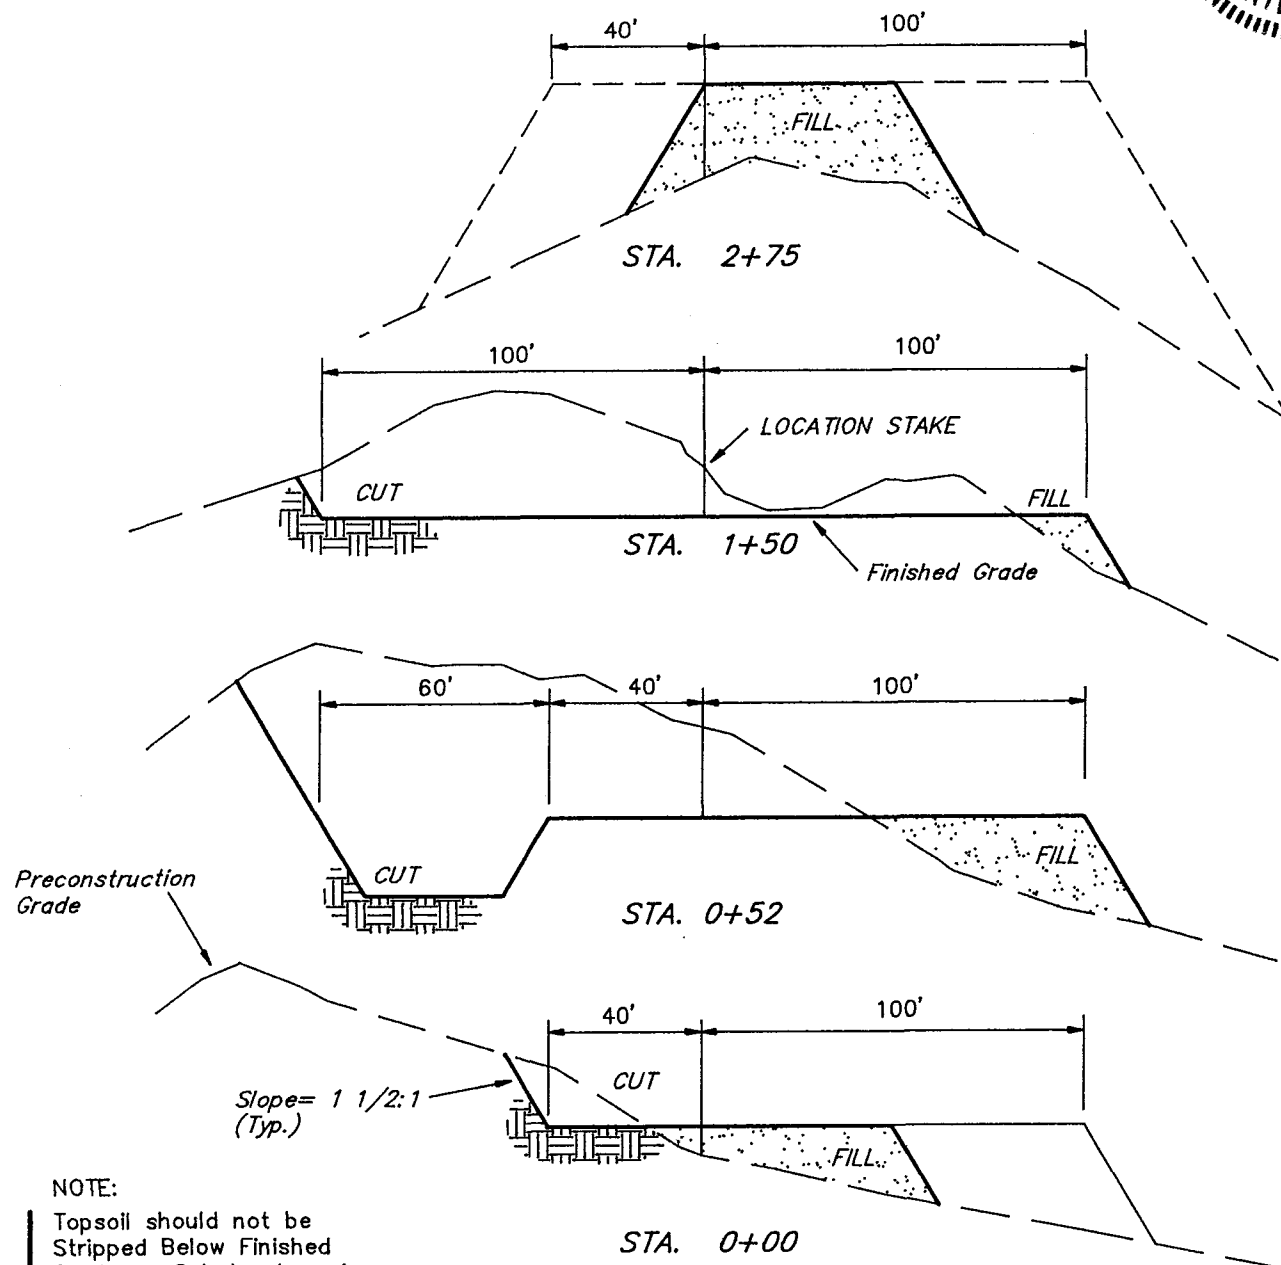

NOTE:


Topsoil should not be
Stripped Below Finished
Grade on Substructure Area.

APPROXIMATE YARDAGES

(12") Topsoil Stripping	= 1,670 Cu. Yds.
Remaining Location	= 10,510 Cu. Yds.
TOTAL CUT	= 12,180 CU.YDS.
FILL	= 9,320 CU.YDS.

EXCESS MATERIAL AFTER 5% COMPACTION	= 2,370 Cu. Yds.
Topsoil & Pit Backfill (1/2 Pit Vol.)	= 2,370 Cu. Yds.
EXCESS UNBALANCE (After Rehabilitation)	= 0 Cu. Yds.

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East * Vernal, Utah 84078 * (801) 789-1017

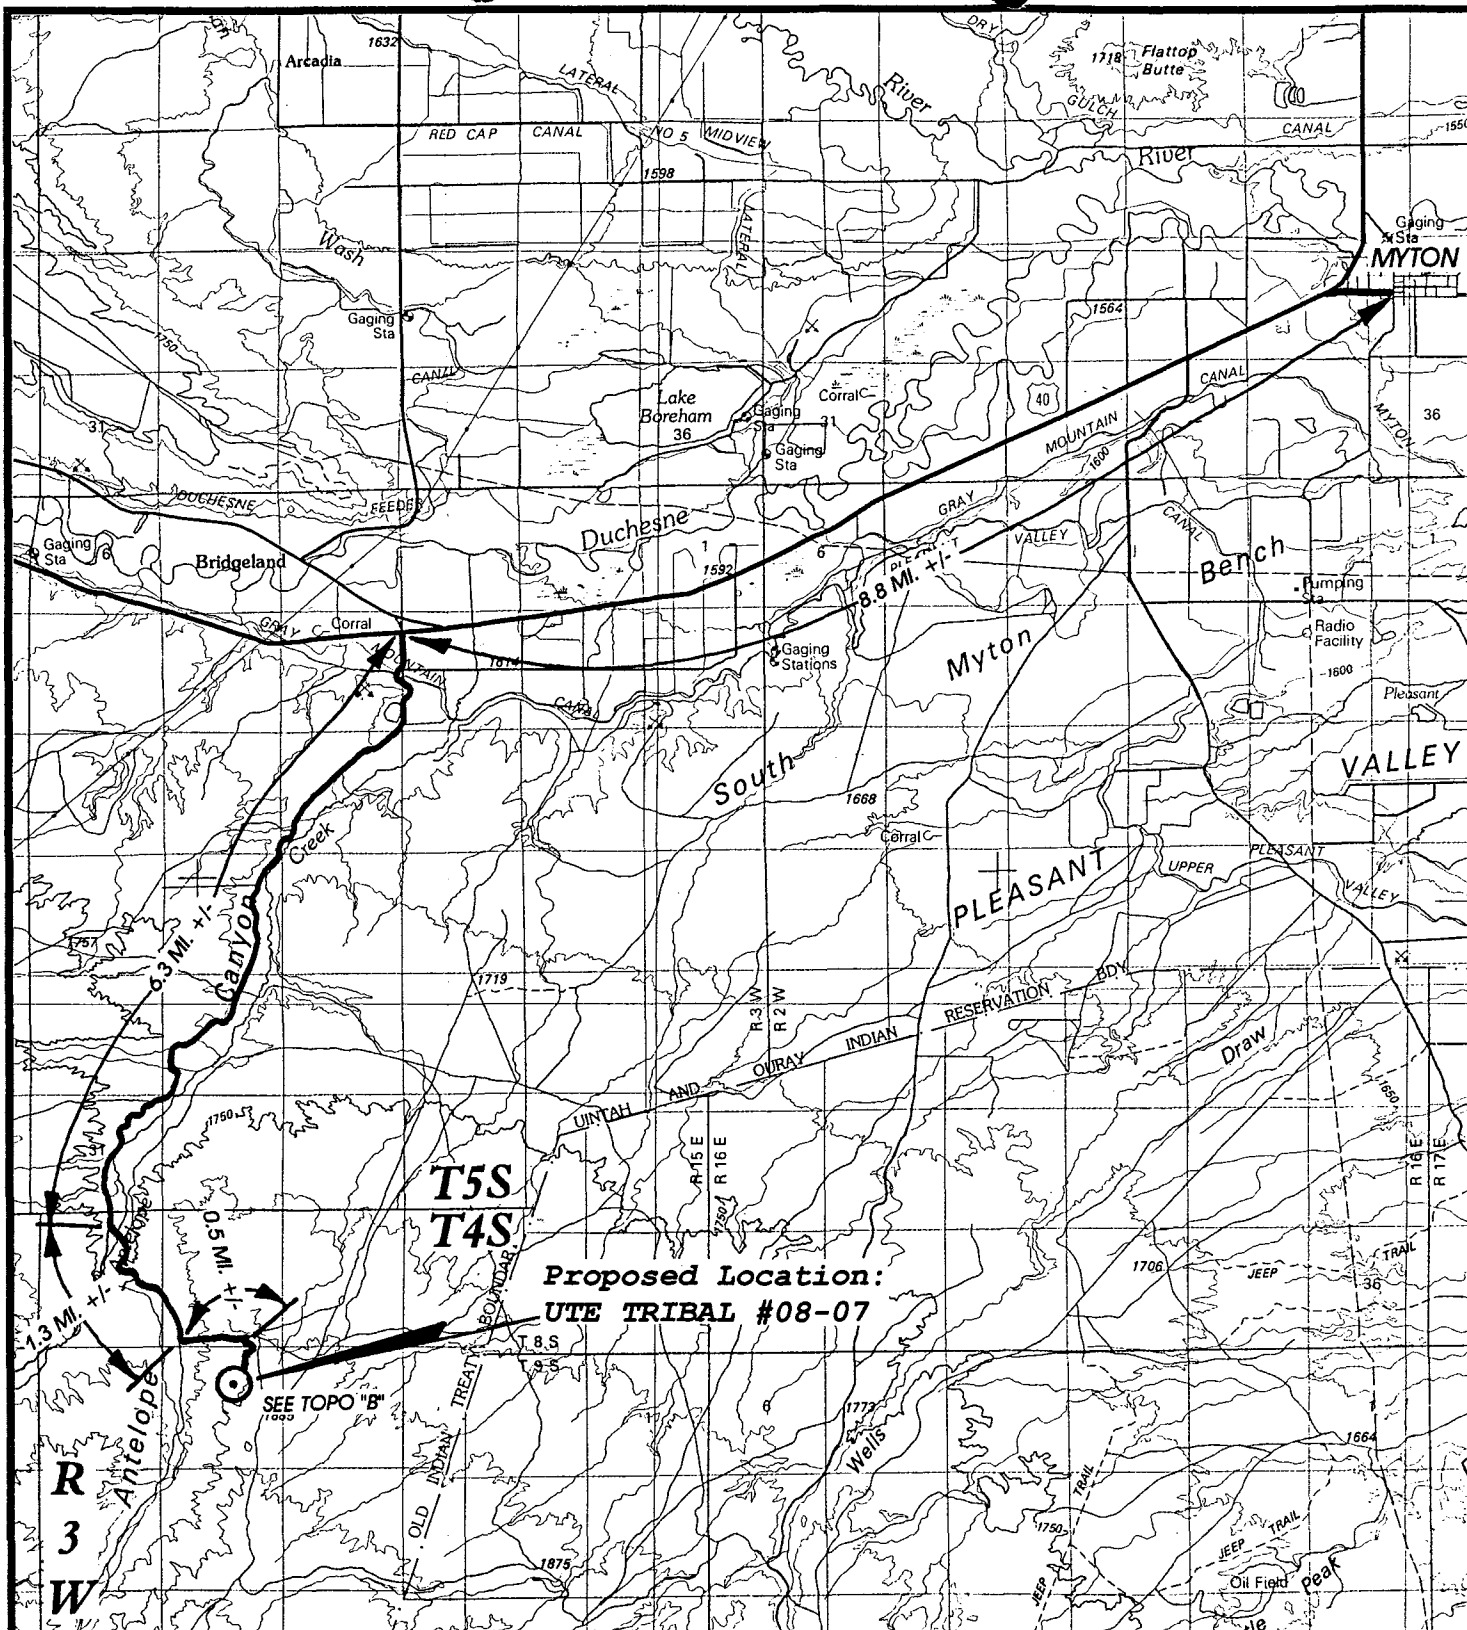

UELS

**TOPOGRAPHIC
MAP "A"**


DATE: 7-2-96
Drawn by: D.COX

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East • Vernal, Utah 84078 • (801) 789-1017



PETROGLYPH OPERATING CO., INC.

**UTE TRIBAL #08-07
SECTION 8, T5S, R3W, U.S.B.&M.
1700' FNL 2133' FEL**

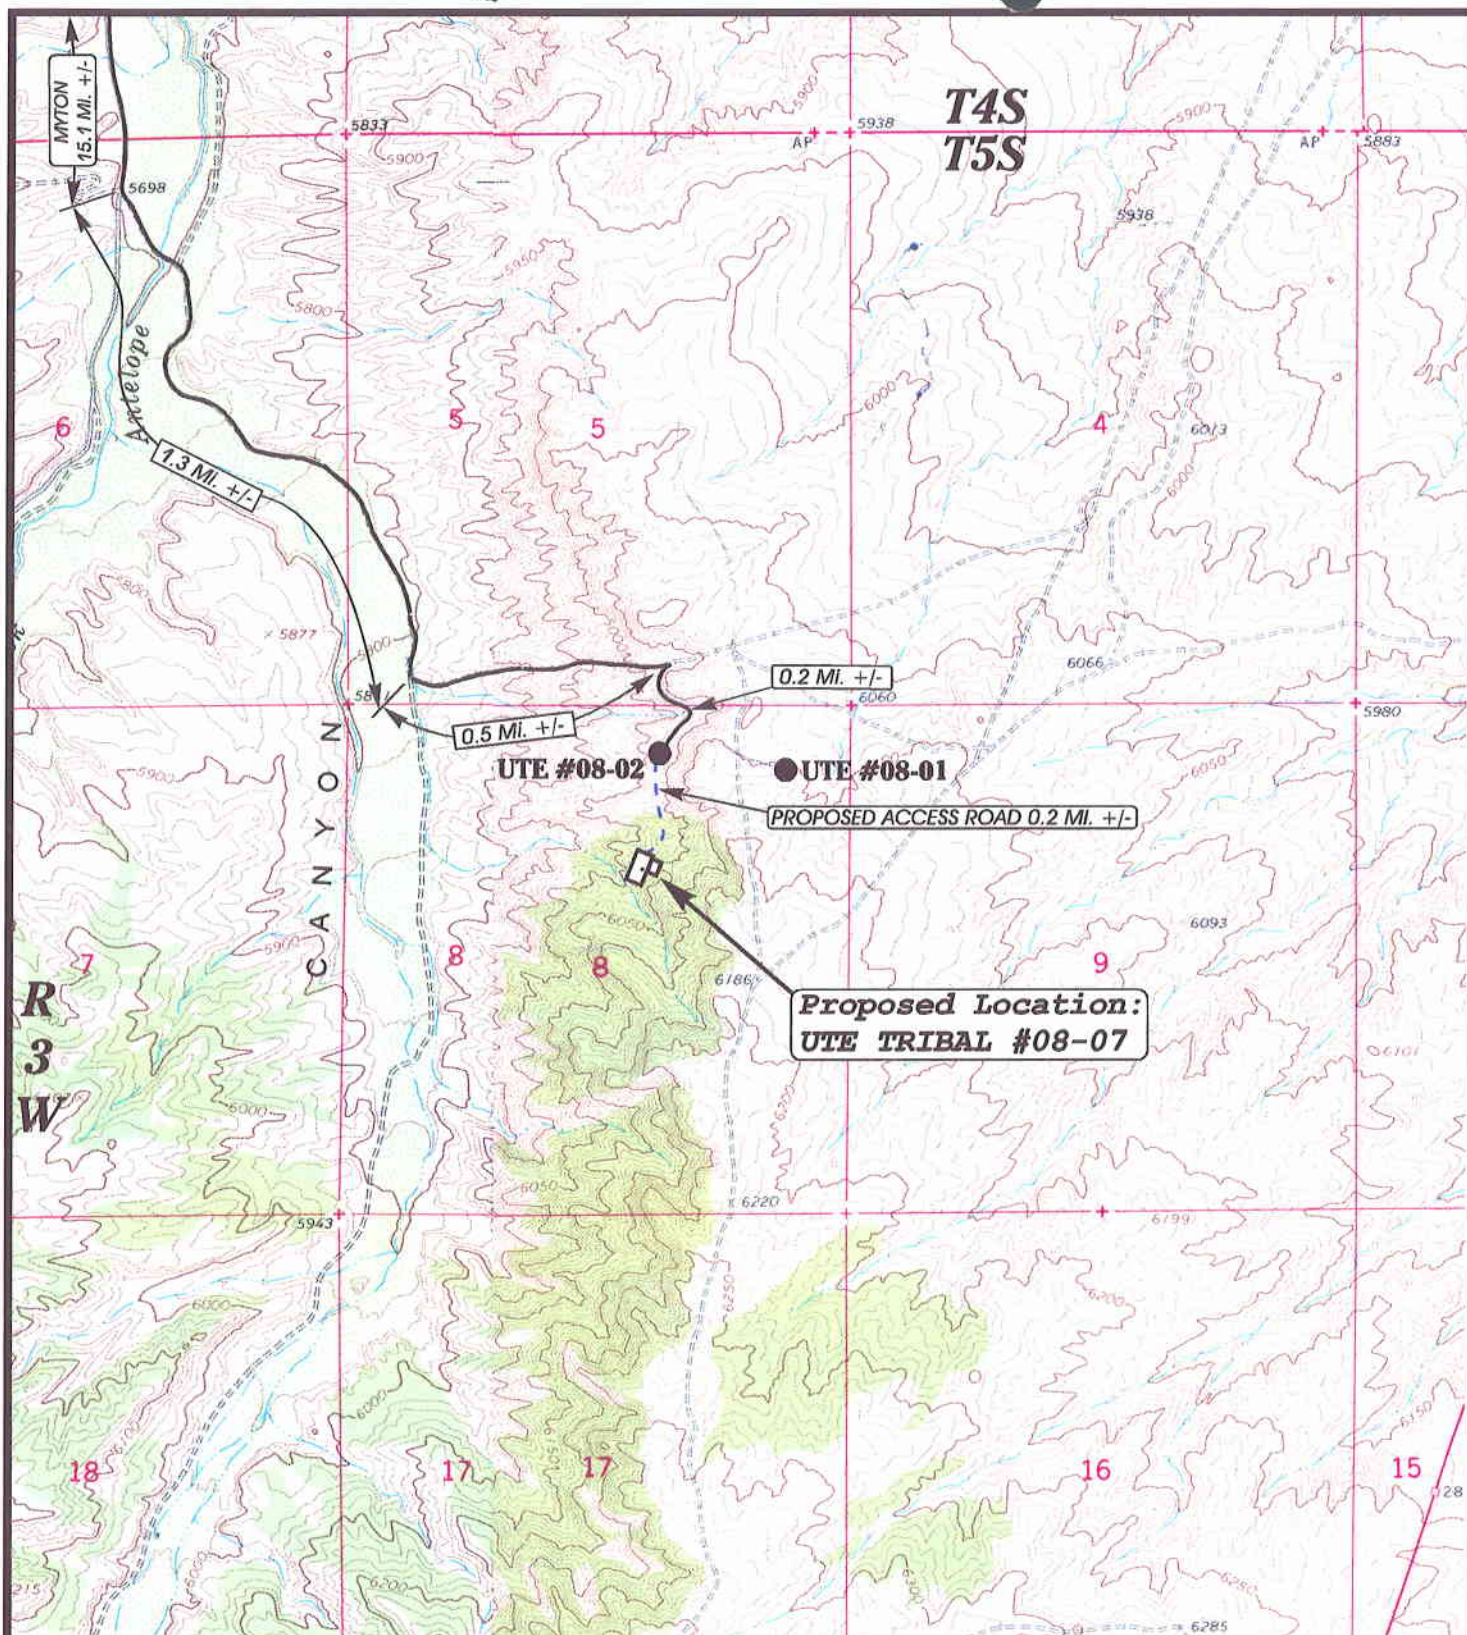

UTELs

TOPOGRAPHIC MAP "B"

DATE: 7-2-96
DRAWN BY: D.COX


UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East • Vernal, Utah 84078 • (801) 789-1017



SCALE: 1" = 2000'

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #08-07
SECTION 8, T5S, R3W, U.S.B.&M.
1700' FNL 2133' FEL

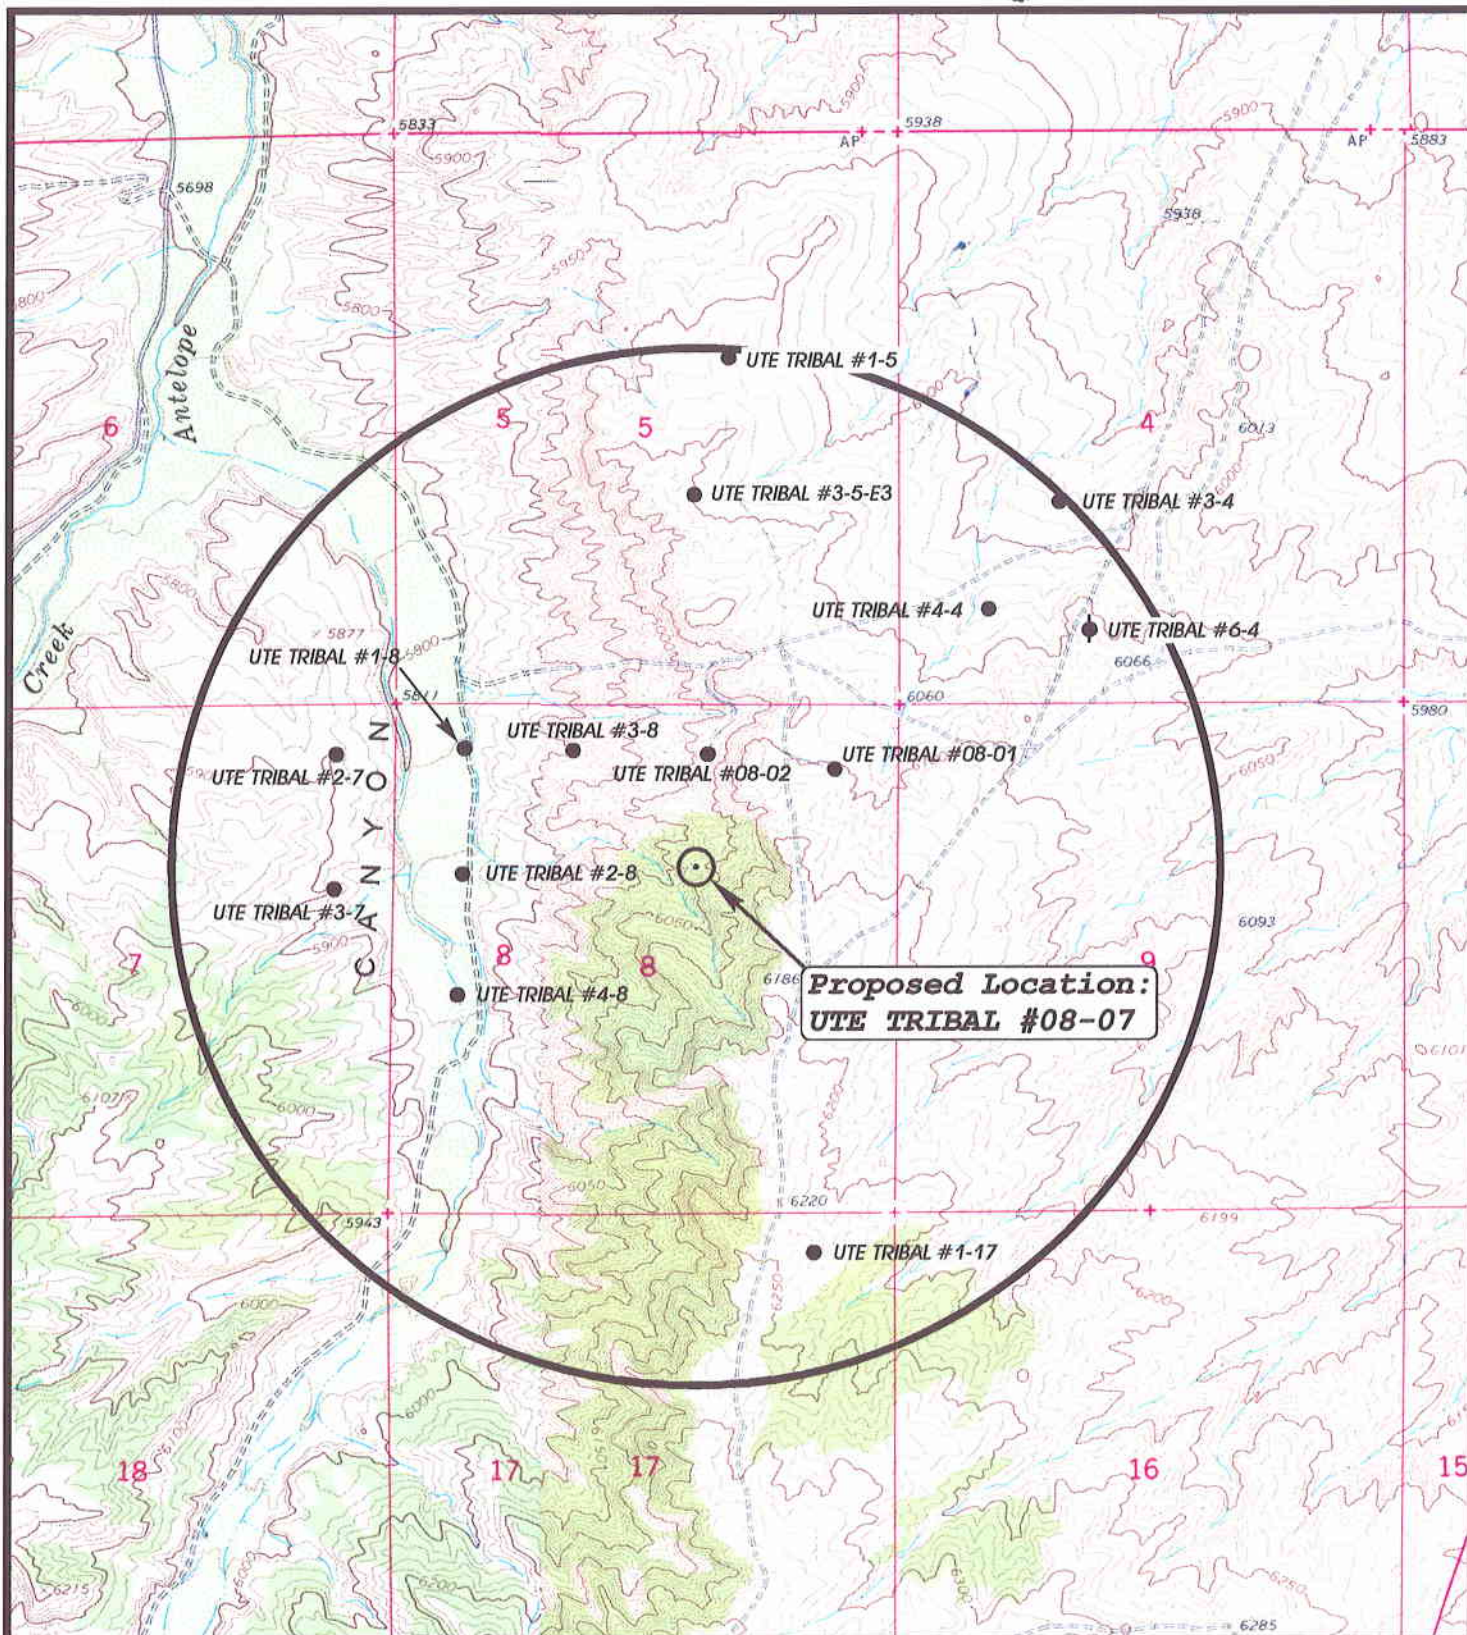

LEGEND

- Water Wells
- Abandoned Wells
- Temporarily Abandoned Wells
- Disposal Wells
- Drilling Wells
- Producing Wells
- Shut-In Wells

UETs

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East • Vernal, Utah 84078 • (801) 789-1017




SCALE: 1" = 2000'

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #08-07
SECTION 8, T5S, R3W, U.S.B.&M.
**TOPOGRAPHIC
MAP "C"**

DATE: 7-2-96
DRAWN BY: D.COX

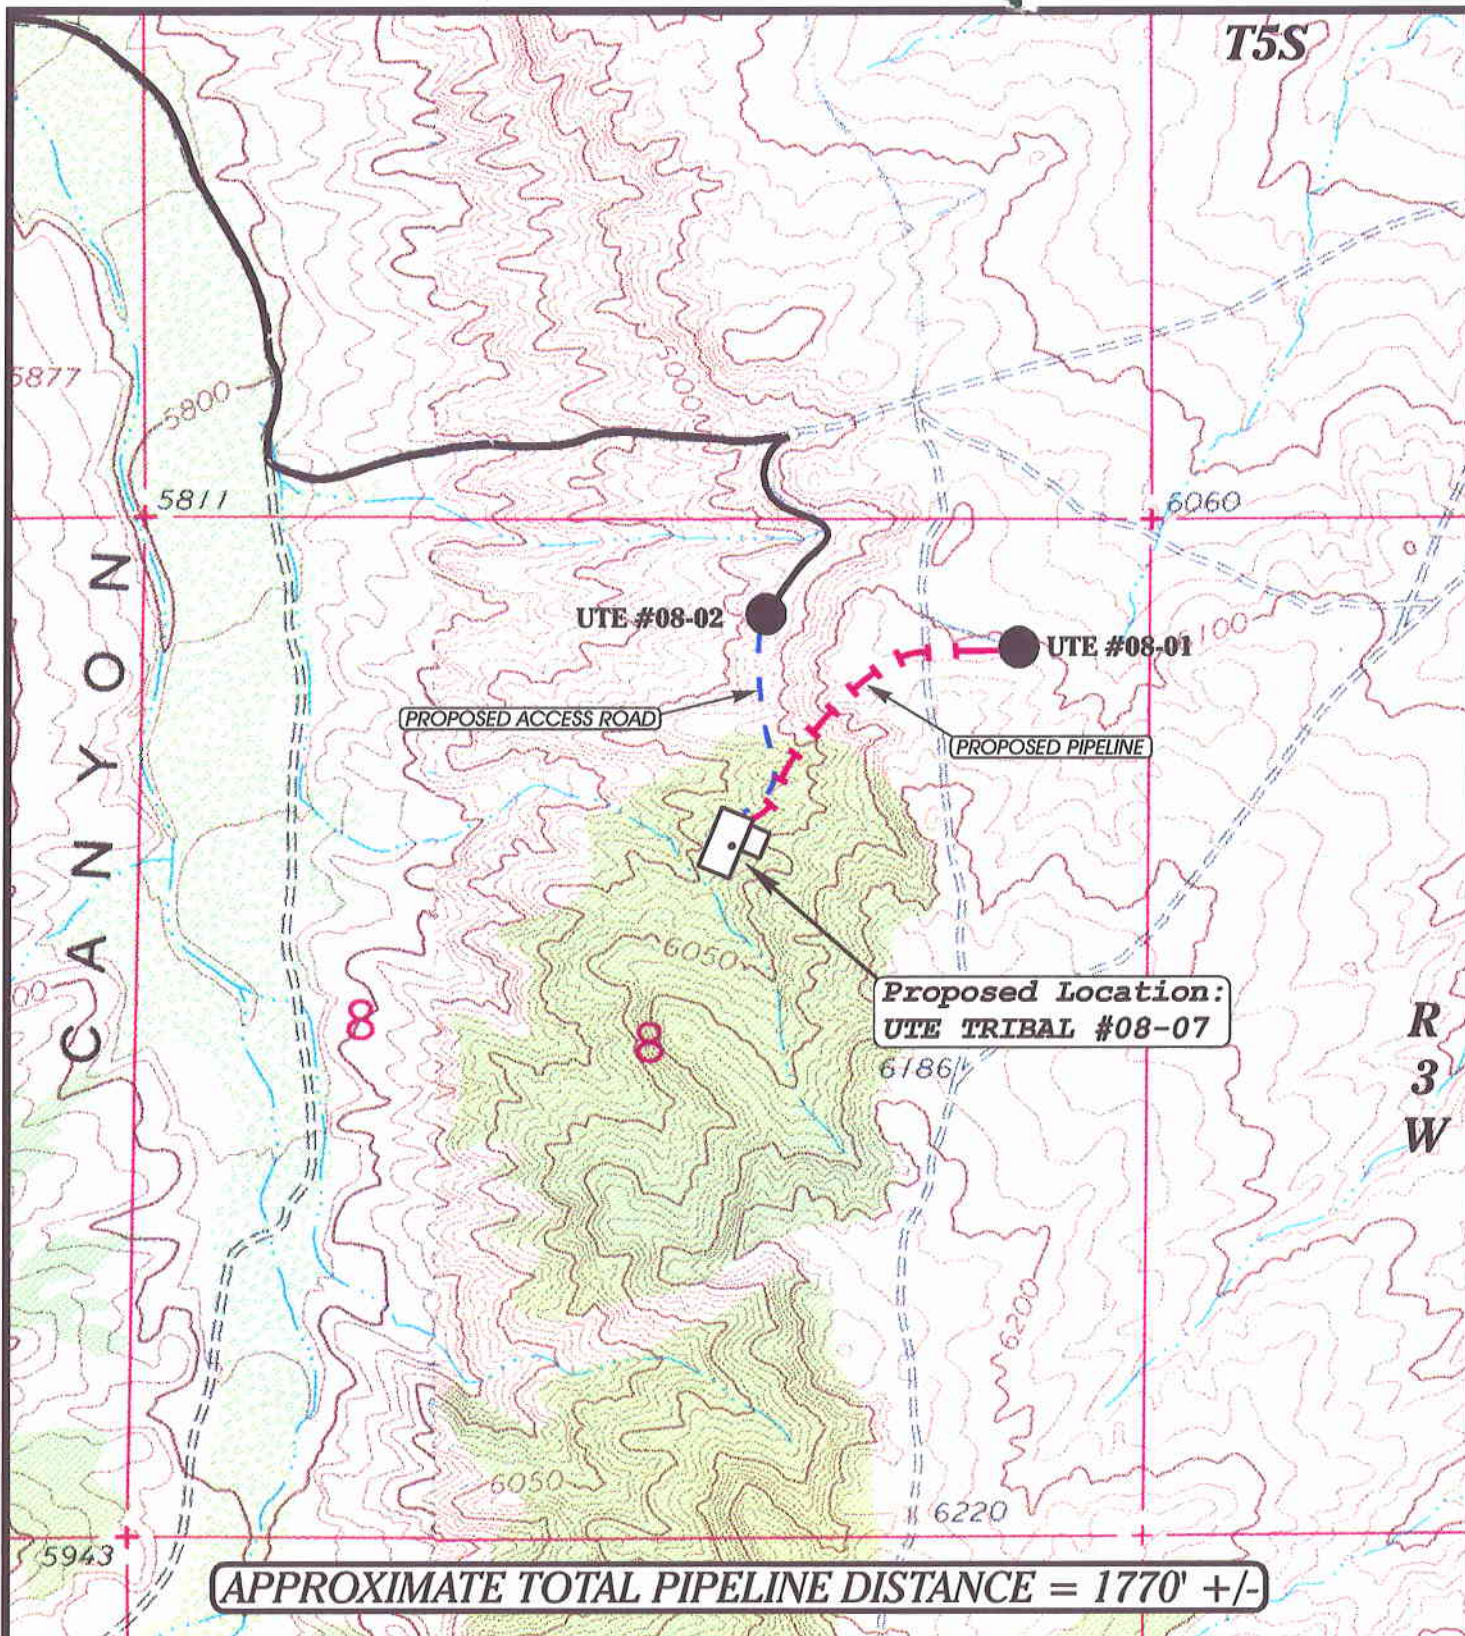

WORKSHEET
APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 07/26/96

API NO. ASSIGNED: 43-013-31691

WELL NAME: UTE TRIBAL 08-07
OPERATOR: PETROGLYPH OPERATING (N3800)

PROPOSED LOCATION:

SWNW 08 - T05S - R03W
SURFACE: 1700-FNL-2133-FEL
BOTTOM: 1700-FNL-2133-FEL
DUCHESNE COUNTY
ANTELOPE CREEK FIELD (060)

LEASE TYPE: IND
LEASE NUMBER: 14-20-H62-3507

PROPOSED PRODUCING FORMATION: GRRV

INSPECT LOCATION BY: / /

TECH REVIEW	Initials	Date
-------------	----------	------

Engineering		
-------------	--	--

Geology		
---------	--	--

Surface		
---------	--	--

RECEIVED AND/OR REVIEWED:

☒ Plat
☒ Bond: Federal ☒ State[] Fee[]
(Number 80 4556)
☒ Potash (Y/N)
☒ Oil shale (Y/N)
☒ Water permit
(Number 43-10152)
☒ RDCC Review (Y/N)
(Date: _____)


LOCATION AND SITING:

___ R649-2-3. Unit: _____
___ R649-3-2. General.
☒ R649-3-3. Exception.
___ Drilling Unit.
Board Cause no: _____
Date: _____

COMMENTS: _____

STIPULATIONS: _____

OPERATOR: PETROGLYPH OPERATING
FIELD: ANTELOPE CREEK (060)
SEC. TWP. RNG: SEC. 4 & 8, T5S, R3W
COUNTY: DUCHESNE
SPACING: UAC R649-3-3

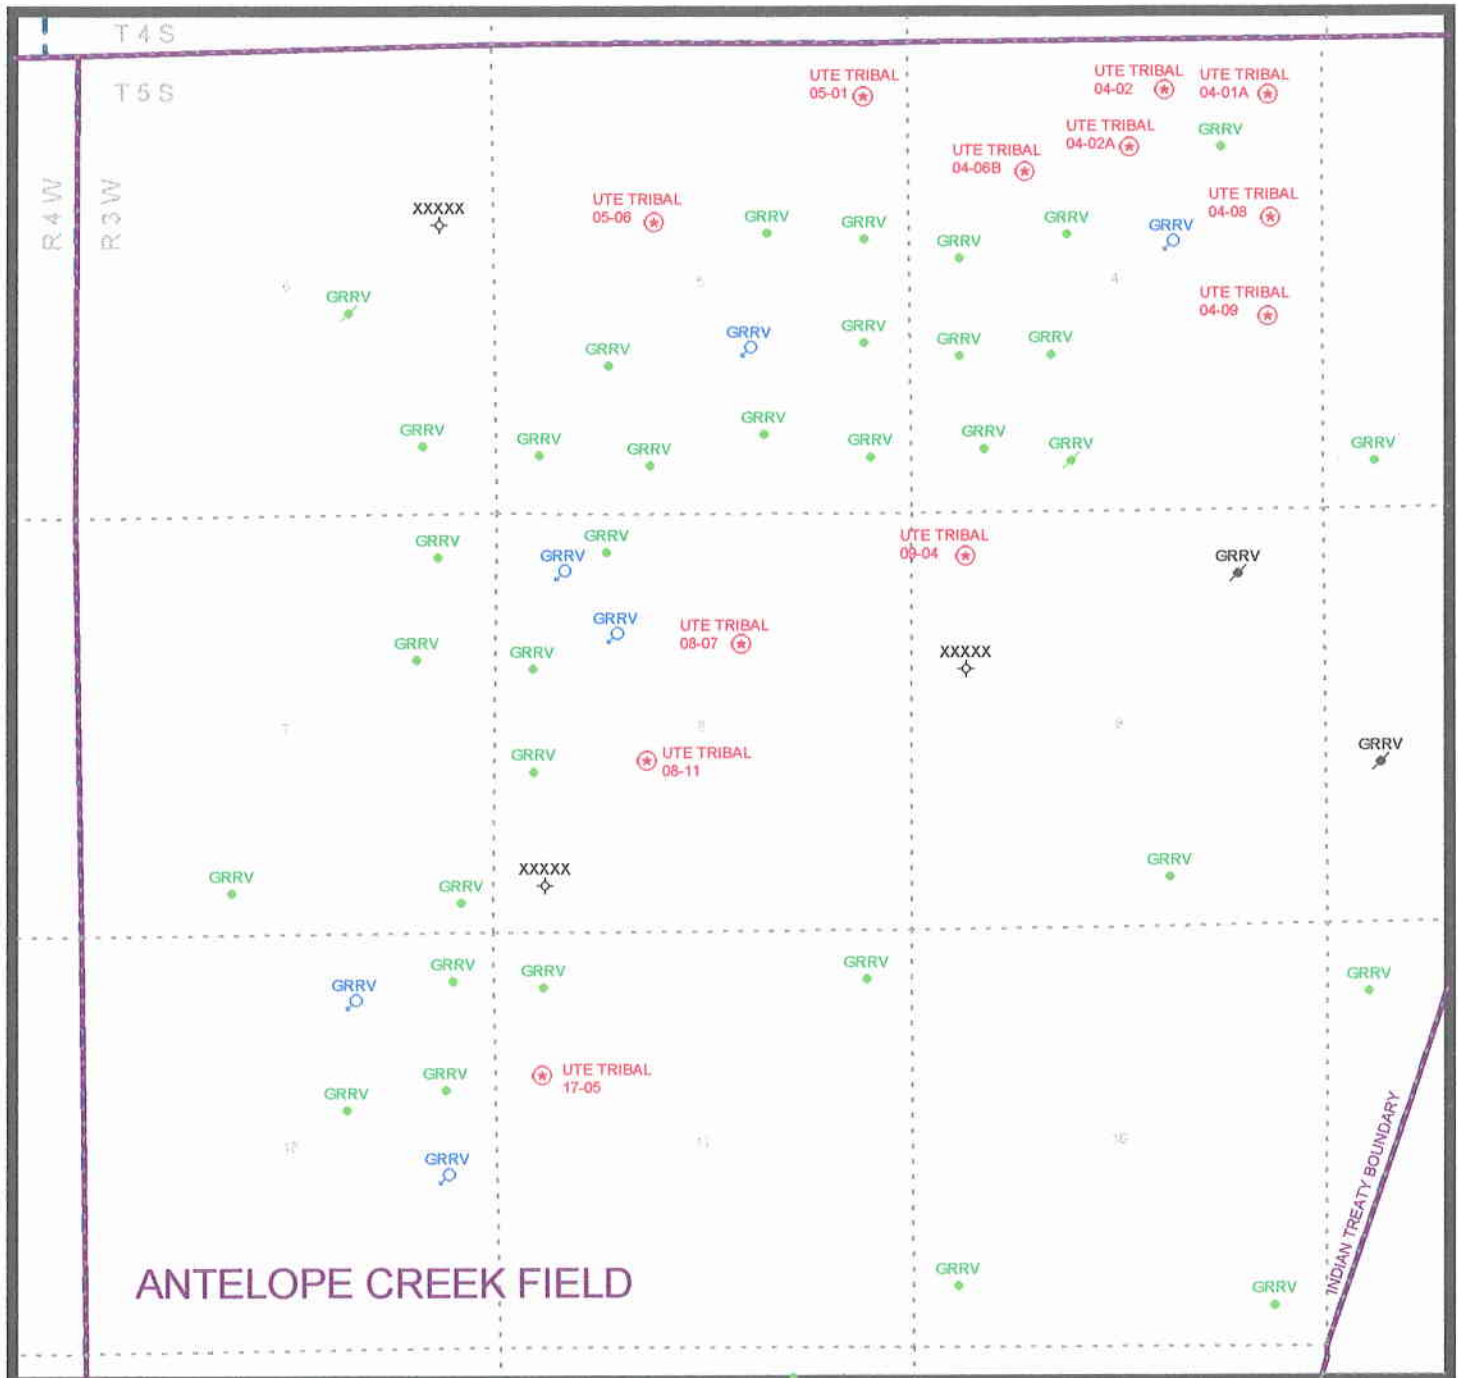

PREPARED:
DATE: 26-JULY-96

STATE OF UTAH, DIV OF OIL, GAS & MINERALS

Operator: PETROGLYPH OPERATING C	Well Name: UTE TRIBAL 08-07
Project ID: 43-013-31691	Location: SEC. 8 - T5S - R3W

Design Parameters:

Mud weight (8.80 ppg) : 0.457 psi/ft
 Shut in surface pressure : 2473 psi
 Internal gradient (burst) : 0.064 psi/ft
 Annular gradient (burst) : 0.000 psi/ft
 Tensile load is determined using air weight
 Service rating is "Sweet"

Design Factors:

Collapse : 1.125
 Burst : 1.00
 8 Round : 1.80 (J)
 Buttress : 1.60 (J)
 Other : 1.50 (J)
 Body Yield : 1.50 (B)

Length (feet)		Size (in.)	Weight (lb/ft)	Grade	Joint	Depth (feet)	Drift (in.)	Cost	
1	6,296	5.500	15.50	M-50	ST&C	6,296	4.820		
	Collapse Load Strgth S.F. (psi) (psi)			Burst Load (psi)	Min Int Strgth (psi)	Yield S.F.	Tension Load Strgth (kips) (kips)		S.F.
1	2878	3650	1.268	2878	4550	1.58	97.59	186	1.91 J

Prepared by : MATTHEWS, Salt Lake City, Utah
 Date : 09-03-1996
 Remarks :

GREEN RIVER

Minimum segment length for the 6,296 foot well is 1,500 feet.

SICP is based on the ideal gas law, a gas gravity of 0.75, and a mean gas temperature of 115°F (Surface 74°F , BHT 162°F & temp. gradient 1.400°/100 ft.)

String type: Production

The mud gradient and bottom hole pressures (for burst) are 0.457 psi/ft and 2,878 psi, respectively.

NOTE: The design factors used in this casing string design are as shown above. As a general guideline, Lone Star Steel recommends using minimum design factors of 1.125 - collapse (with evacuated casing), 1.0 - (uniaxial) burst, 1.8 - API 8rd tension, 1.6 - buttress tension, 1.5 - body yield tension, and 1.6 - EUE 8rd tension. Collapse strength under axial tension was calculated based on the Westcott, Dunlop and Kemler curve. Engineering responsibility for use of this design will be that of the purchaser.
 Costs for this design are based on a 1987 pricing model. (Version 1.07)



State of Utah
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

Michael O. Leavitt
Governor

Ted Stewart
Executive Director

James W. Carter
Division Director

355 West North Temple
3 Triad Center, Suite 350
Salt Lake City, Utah 84180-1203
801-538-5340
801-359-3940 (Fax)
801-538-5319 (TDD)

September 3, 1996

Petroglyph Operating Company, Inc.
P.O. Box 607
Roosevelt, Utah 84066

Re: Ute Tribal 08-07 Well, 1700' FNL, 2133' FEL, SW NW, Sec. 8,
T. 5 S., R. 3 W., Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. 40-6-1 et seq., Utah Administrative Code R649-3-1 et seq., and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-31691.

Sincerely,

R. J. Firth
Associate Director

lwp

Enclósures

cc: Duchesne County Assessor
Bureau of Land Management, Vernal District Office



Operator: Petroglyph Operating Company, Inc.
Well Name & Number: Ute Tribal 08-07
API Number: 43-013-31691
Lease: 14-20-H62-3507
Location: SW NW Sec. 8 T. 5 S. R. 3 W.

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for Permit to Drill.

2. Notification Requirements

Notify the Division within 24 hours following spudding the well or commencing drilling operations. Contact Jimmie Thompson at (801)538-5336.

Notify the Division prior to commencing operations to plug and abandon the well. Contact Frank Matthews at (801)538-5334 or Mike Hebertson at (801)538-5333.

3. Reporting Requirements

All required reports, forms and submittals shall be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

DOGMA

APPLICATION FOR PERMIT TO DRILL, DEEPEN, OR PLUG BACK

1a. TYPE OF WORK

DRILL ☒

DEEPEN ☐

PLUG BACK ☐

b. TYPE OF WELL

OIL
WELL ☒

GAS
WELL ☐

OTHER

SINGLE
ZONE ☐

MULTIPLE
ZONE ☐

2. NAME OF OPERATOR

PETROGLYPH OPERATING COMPANY INC.

3. ADDRESS OF OPERATOR

P.O. BOX 607 ROOSEVELT, UT 84066

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.*)

At surface

1700' FNL & 2133' FEL SW/4 NW/4

At proposed prod. zone

14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*

17.3 miles southwest of Myton, UT

15. DISTANCE FROM PROPOSED*

LOCATION TO NEAREST
PROPERTY OR LEASE LINE, FT.
(Also to nearest drlg. unit line, if any)

1700'

16. NO. OF ACRES IN LEASE

640

17. NO. OF ACRES ASSIGNED

TO THIS WELL 40

18. DISTANCE FROM PROPOSED LOCATION*
TO NEAREST WELL, DRILLING, COMPLETED,
OR APPLIED FOR, ON THIS LEASE, FT.

19. PROPOSED DEPTH

6296'

20. ROTARY OR CABLE TOOLS

ROTARY

21. ELEVATIONS (Show whether DF, RT, GR, etc.)

6029' GRADED GROUND


22. APPROX. DATE WORK WILL START*

AUGUST, 1996

23.

PROPOSED CASING AND CEMENTING PROGRAM

SIZE OF HOLE	SIZE OF CASING	WEIGHT PER FOOT	SETTING DEPTH	QUANTITY OF CEMENT
12 1/4	8 5/8	24.0#	250'	135 sx class "G" + 2% CaCl ₂
7 7/8	5 1/2	15.5#	6296'	+ 1/4 #/sx celloflake.



50/50 POZMIX + 2% GEL + 10%
SALT TO 400' ABOVE ALL ZONES
OF INTEREST (+ 10% EXCESS).
LIGHT CEMENT (11 PPG +) +
LCM TO 200' ABOVE OIL SHALE
OR FRESH WATER INTERVALS
(+ 5% EXCESS).

PETROGLYPH OPERATING COMPANY INC. WILL BE THE DESIGNATED
OPERATOR OF THE SUBJECT WELL UNDER BOND # BO 4556.

pc: Utah Division of Oil, Gas and Mining
Bureau of Indian Affairs, Fort Duchesne, UT
Ute Tribe, Fort Duchesne, UT

RECEIVED

IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen or plug back, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24.

SIGNED

TITLE AGENT FOR PETROGLYPH

DATE JULY 19, 1996

(This space for Federal or State office use)

NOTICE OF APPROVAL

PERMIT NO.

APPROVAL DATE

Assistant Field Manager

SEP 04 1996

APPROVED BY

TITLE

Mineral Resources

DATE

CONDITIONS OF APPROVAL, IF ANY:

CONDITIONS OF APPROVAL ATTACHED
TO OPERATOR'S COPY

U4080-6m-183

*See Instructions On Reverse Side

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

CONDITIONS OF APPROVAL
APPLICATION FOR PERMIT TO DRILL

Company/Operator: Petroglyph Operating Company

Well Name & Number: Ute Tribal 08-07

API Number: 43-013-31691

Lease Number: 14-20-H62-3507

Location: SWNE Sec. 08 T. 5S R. 3W

NOTIFICATION REQUIREMENTS

- | | | |
|---------------------------------|---|---|
| Location Construction | - | at least forty-eight (48) hours prior to construction of location and access roads. |
| Location Completion | - | prior to moving on the drilling rig. |
| Spud Notice | - | at least twenty-four (24) hours prior to spudding the well. |
| Casing String and Cementing | - | at least twenty-four (24) hours prior to running casing and cementing all casing strings. |
| BOP and Related Equipment Tests | - | at least twenty-four (24) hours prior to initiating pressure tests. |
| First Production Notice | - | within five (5) business days after new well begins, or production resumes after well has been off production for more than ninety (90) days. |

For more specific details on notification requirements, please check the Conditions of Approval for Notice to Drill and Surface Use Program.

CONDITIONS OF APPROVAL FOR NOTICE TO DRILL

Approval of this application does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

All lease and/or unit operations will be conducted in such a manner that full compliance is made with applicable laws, regulations (43 CFR 3100), Onshore Oil and Gas Orders, and the approved plan of operations. The operator is fully responsible for the actions of his subcontractors. A copy of these conditions will be furnished to the field representative by the operator to insure compliance.

Be aware fire restrictions may be in effect when location is being constructed and/or when well is being drilled. Contact the appropriate Surface Management Agency for information.

A. DRILLING PROGRAM

1. Estimated Depth at Which Oil, Gas, Water, or Other Mineral Bearing Zones are Expected to be Encountered

Report **ALL** water shows and water-bearing sands to Tim Ingwell of this office **prior to setting the next casing string or requesting plugging orders**. Faxed copies of State of Utah form OGC-8-X are acceptable. If noticeable water flows are detected, submit samples to this office along with any water analyses conducted.

All usable water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling, will be recorded by depth and adequately protected. All oil and gas shows will be tested to determine commercial potential.

2. Pressure Control Equipment

The BOP and related equipment shall meet the minimum requirements of Onshore Oil and Gas Order No. 2 for equipment and testing requirements, procedures, etc., for a **2M** system and individual components shall be operable as designed. Chart recorders shall be used for all pressure tests.

Test charts, with individual test results identified, shall be maintained on location while drilling and shall be made available to a BLM representative upon request.

If an air compressor is on location and is being utilized to provide air for the drilling medium while drilling, the special drilling requirements in Onshore Oil and Gas Order No. 2, regarding air or gas drilling shall be adhered to. If a mist system is being utilized then the requirement for a deduster shall be waived.

3. Casing Program and Auxiliary Equipment

Surface casing shall have centralizers on the bottom three joints, with a minimum of one centralizer per joint.

If conductor pipe is set it will be cemented to surface. If drive pipe is used it will be pulled prior to cementing surface casing.

As a minimum, the usable water and oil shale resources shall be isolated and/or protected by having a cement top for the production casing at least 200 ft. above the top of the usable water zone identified at ± 311 ft. or by setting the surface casing at ± 361 ft.. If gilsonite is encountered while drilling, it shall be isolated and/or protected via the cementing program.

4. Mud Program and Circulating Medium

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

No chromate additives will be used in the mud system on Federal and Indian lands without prior BLM approval to ensure adequate protection of fresh water aquifers.

5. Coring, Logging and Testing Program

Daily drilling and completion progress reports shall be submitted to this office on a weekly basis.

All Drill Stem tests (DST) shall be accomplished during daylight hours, unless specific approval to start during other hours is obtained from the AO. However, DSTs may be allowed to continue at night if the test was initiated during daylight hours and the rate of flow is stabilized and if adequate lighting is available (i.e., lighting which is adequate for visibility and vaporproof for safe operations). Packers can be released, but tripping should not begin before daylight unless prior approval is obtained from the AO.

A cement bond log (CBL) will be run from the production casing shoe to **TOP OF CEMENT** if the surface casing is set at ± 361 ft. or it will be run to **SURFACE** if the surface casing is set at ± 250 ft. and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.

Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (Form 3160-4) will be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3164. Two copies of all logs, core descriptions, core analyses, well-test data, geologic summaries, sample description, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, will be filed with Form 3160-4. Samples (cuttings, fluids, and/or gases) will be submitted when requested by the AO.

6. Notifications of Operations

No location will be constructed or moved, no well will be plugged, and no drilling or workover equipment will be removed from a well to be placed in a suspended status without prior approval of the AO. If operations are to be suspended, prior approval of the AO will be obtained and notification given before resumption of operations.

The Vernal District Office shall be notified, during regular work hours (7:45 a.m.-4:30 p.m., Monday through Friday except holidays), at least 24 hours prior to spudding the well.

Operator shall report production data to MMS pursuant to 30 CFR 216.5 using form MMS/3160.

Immediate Report: Spills, blowouts, fires, leaks, accidents, or any other unusual occurrences shall be promptly reported in accordance with the requirements of NTL-3A or its revision.

If a replacement rig is contemplated for completion operations, a "Sundry Notice" (Form 3160-5) to that effect will be filed, for prior approval of the AO, and all conditions of this approved plan are applicable during all operations conducted with the replacement rig.

The date on which production is commenced or resumed will be construed for oil wells as the date on which liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated or, the date on which liquid hydrocarbons are first produced into a permanent storage facility, whichever first occurs; and, for gas wells as the date on which associated liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated or, the date on which gas is first measured through permanent metering facilities, whichever first occurs.

Should the well be successfully completed for production, the AO will be notified when the well is placed in a producing status. Such notification will be sent by telegram or other written communication, not later than five (5) days following the date on which the well is placed on production.

Gas produced from this well may not be vented or flared beyond an initial authorized test period of 30 days or 50 MMCF following its completion, whichever occurs first, without the prior written approval of the Authorized Officer. Should gas be vented or flared without approval beyond the authorized test period, the operator may be directed to shut-in the well until the gas can be captured or approval to continue venting or flaring as uneconomic is granted and the operator shall be required to compensate the lessor for that portion of the gas vented or flared without approval which is determined to have been avoidably lost.

A schematic facilities diagram as required by 43 CFR 3162.7-5 (b.9. d.), and shall be submitted to the appropriate District Office within sixty (60) days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with 43 CFR 3162.7-5 (b. 4).

No well abandonment operations will be commenced without the prior approval of the AO. In the case of newly drilled dry holes or failures, and in emergency situations, oral approval will be obtained from the AO. A "Subsequent Report of Abandonment" Form 3160-5, will be filed with the AO within thirty (30) days following completion of the well for abandonment. This report will indicate where plugs were placed and the current status of surface restoration. Final abandonment will not be approved until the surface reclamation work required by the approved APD or approved abandonment notice has been completed to the satisfaction of the AO or his representative, or the appropriate Surface Managing Agency.

7. Other Information

All loading lines will be placed inside the berm surrounding the tank battery.

All off-lease storage, off-lease measurement, or commingling on-lease or off-lease will have prior written approval from the AO.

The oil and gas measurement facilities will be installed on the well location. The oil and gas meters will be calibrated in place prior to any deliveries. Tests for meter accuracy will be conducted following initial installation and at least quarterly thereafter. The AO will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports will be submitted to the Vernal District Office. All meter measurement facilities will conform with Onshore Oil & Gas Order No. 4 for liquid hydrocarbons and Onshore Oil & Gas Order No. 5 for natural gas measurement.

The use of materials under BLM jurisdiction will conform to 43 CFR 3610.2-3.

There will be no deviation from the proposed drilling and/or workover program without prior approval from the AO. Safe drilling and operating practices must be observed. All wells, whether drilling, producing, suspended, or abandoned will be identified in accordance with 43 CFR 3162.

"Sundry Notice and Report on Wells" (Form 3160-5) will be filed for approval for all changes of plans and other operations in accordance with 43 CFR 3162.3-2.

Section 102(b)(3) of the Federal Oil and Gas Royalty Management Act of 1982, as implemented by the applicable provisions of the operating regulations at Title 43 CFR 3162.4-1(c), requires that "not later than the 5th business day after any well begins production on which royalty is due anywhere on a lease site or allocated to a lease site, or resumes production in the case of a well which has been off production for more than 90 days, the operator shall notify the authorized officer by letter or sundry notice, Form 3160-5, or orally to be followed by a letter or sundry notice, of the date on which such production has begun or resumed."

If you fail to comply with this requirement in the manner and time allowed, you shall be liable for a civil penalty of up to \$10,000 per violation for each day such violation continues, not to exceed a maximum of 20 days. See Section 109(c)(3) of the Federal Oil and Gas Royalty Management Act of 1982 and the implementing regulations at Title 43 CFR 3162.4-1(b)(5)(ii).

APD approval is valid for a period of one (1) year from the signature date. An extension period may be granted, if requested, prior to the expiration of the original approval period.

In the event after-hours approval or notification is necessary, please contact one of the following individuals:

Wayne Bankert (801) 789-4170
Petroleum Engineer

Ed Forsman (801) 789-7077
Petroleum Engineer

Jerry Kenczka (801) 789-1190
Petroleum Engineer

BLM FAX Machine (801) 781-4410

EPA'S LIST OF NONEXEMPT EXPLORATION AND PRODUCTION WASTES

While the following wastes are nonexempt, they are not necessarily hazardous.

- Unused fracturing fluids or acids
- Gas plant cooling tower cleaning wastes
- Painting wastes
- Oil and gas service company wastes, such as empty drums, drum rinsate, vacuum truck rinsate, sandblast media, painting wastes, spent solvents, spilled chemicals, and waste acids
- Vacuum truck and drum rinsate from trucks and drums, transporting or containing nonexempt waste
- Refinery wastes
- Liquid and solid wastes generated by crude oil and tank bottom reclaimers
- Used equipment lubrication oils
- Waste compressor oil, filters, and blowdown
- Used hydraulic fluids
- Waste solvents
- Waste in transportation pipeline-related pits
- Caustic or acid cleaners
- Boiler cleaning wastes
- Boiler refractory bricks
- Incinerator ash
- Laboratory wastes
- Sanitary wastes
- Pesticide wastes
- Radioactive tracer wastes
- Drums, insulation and miscellaneous solids.

SURFACE USE PLAN OF OPERATION
Conditions of Approval (COA's)

1. The Ute Tribe Energy and Minerals Department is to be notified 48 hours prior to construction.
2. Petroglyph Operating Company will assure the Ute Tribe that any/all contractors/subcontractors have acquired a Tribal Business License and have an Access Permit prior to construction.
3. All vehicular traffic, personnel movement, construction and restoration operations should be confined to the areas examined, as referenced in report, and to the existing roadways and/or evaluated access routes.
4. All recommendations of the Bureau of Indian Affairs, combined site specific Environmental Analysis (EA) report shall be strictly adhered, during and after construction.
5. All personnel should refrain from collecting artifacts and from disturbing any significant cultural remains from subsurface deposits at are exposed or identified during construction.
6. The personnel from the Ute Tribe Energy & Minerals Department should be consulted, should cultural remains from subsurface deposits be exposed or identified during construction.
7. Upon completion of Application for Permit to Drill and Right-of-way, the Ute Tribe Energy & Minerals Resource Department will be notified by Petroglyph Operating Company so that a Tribal Technician can verify Affidavit of Completions.

Mitigation stipulations from the combined site specific Environmental Analysis.

1. Before the site is abandoned the company will be required to restore the well pad and access road to near their original state. The disturbed area will be reseeded with desirable perennial vegetation.
2. Noxious weeds will be controlled on all well sites and rights-of-way. If noxious weeds spread from the well sites or rights-of-way onto adjoining land, the company will also be responsible for their control.
3. The pipeline will be constructed to lay on the soil surface, and the right-of-way will not be bladed or cleared of vegetation.

Where pipelines are constructed parallel to roads they may be welded on the road and then lifted from the road onto the right-of-way.

Where pipelines do not parallel roads but cross country between stations, they shall be welded in place at wellsites or on access roads and then pulled between stations with a suitable piece of equipment. Traffic will be restricted along these areas so that the pipeline right-of-way will not be used as an access road.

4. An open drilling system shall be used. Reserve pits will be lined with impervious synthetic liners. Prior to backfilling the reserve pit all fluids will be pumped from the pit into trucks and hauled to approved disposal sites. When the reserve pits are backfilled the surplus oil and mud, etc will be buried a minimum of 3.0 feet below the surface of the soil.
5. A closed production system will be used. Production fluids will be contained in leak proof tanks. All production fluids will be disposed of at approved disposal sites. The indiscriminate dumping of production fluids on roads, well sites or other areas will not be allowed.
6. Although the access roads have a 30 foot right-of-way the bladed area of the road will be limited to 21 feet in all areas except where deep cuts and fills are required, sharp turns are required, or at the intersections with other roads.

DATE:

Superintendent, Uintah & Ouray Agency

TO: UT # 08-07, NE/4, Sec. 8, T5S, R3W, SLB&M.
UT # 04-06B, NW/4, Sec. 4, T5S, R3W, SLB&M

RECEIVED

AUG 28 1996

Based on available information received on 08/28/96 we cleared the proposed location in all areas of environmental impact.

COMMENTS: Based upon the reports submitted and the consensus of the on-site personnel, the Ute Tribe Energy and Minerals Department is requiring the following stipulations to apply:

1. The Ute Tribe Energy and Minerals Department is to be notified 48 hours prior to construction
2. Petroglyph Operating Company will assure the Ute Tribe that any/all contractor/subcontractors have acquired a tribal Business License and have an Access Permit prior to construction.
3. All vehicular traffic, personnel movement, construction and restoration operations should be confined to the areas examined, as referenced in report, and to the existing roadways and /or evaluated access routes.
4. All recommendations of the Bureau of Indian Affairs combined site specific Environmental Analysis report shall be strictly adhered, during and after construction.
5. All personnel should refrain from collecting artifacts and from disturbing any significant cultural remains from subsurface deposits be exposed or identified during construction.
6. The personnel from the Ute Tribe Energy & Minerals Department should be consulted should cultural remains from subsurface deposits be exposed or identified during construction.
7. Upon completion of Application for Permit to Drill and Right-of-way, the Ute Tribe Energy & Minerals Resource Department will be notified by Petroglyph Operating Company so that a Tribal Technician can verify Affidavit of Completions.

Wern A. Hartomey
Acting Superintendent

**SITE SPECIFIC
ENVIRONMENTAL ANALYSIS**

RECEIVED

AUG 28 1996

1.0 PROPOSED ACTION

Petroglyph Operating Co., Inc. is proposing to drill oil well 08-07, and construct 1770 feet of steel surface production pipeline, and 0.2 mile of access road..

2.0 ALTERNATIVE ACTIONS

- A. ALTERNATIVE CONSIDERED: The proposed action is the preferred alternative.
- B. NO ACTION: Under the no action alternative the proposed action would not be implemented.
- C. OTHER: NA

3.0 PERMITTEE/LOCATION

- A. Permittee- Petroglyph Operating Co., Inc.
- B. Date 7-10-96
- C. Well number 08-07
- D. Right-of-way-Pipeline R\W approx. 1770 feet, access road 0.2 miles.
- E. Site location- SWNE, Section 8, T5S, R3W, USB&M.

4.0 SITE SPECIFIC SURVEY

A. SITE DESCRIPTION

- 1. Elevation (feet) 6034
- 2. Annual precipitation (inches)- 12-14
- 3. Topography- rolling hills
- 4. Soil- The soil texture is (0 to 6") gravely shale loam with moderate permeability.

B. VEGETATION

- 1. Habitat type is upland pinion juniper.
- 2. Percent Ground Cover- estimated to be 40%.
- 3. Vegetation consists of approximately 13% grasses, 20% shrubs, 5% forbs, trees 62%. The main variety of grasses are squirrel tail, Indian ricegrass, poa, needle & thread, bluebunch wheat, and blue grama. Forbs are astragalus, mustard, lambs quarter, globemallow, buck wheat, & annuals. Shrubs consist of black sagebrush, prickly pear, shadscale. Trees are pinion pine, and Utah juniper.

4. Observed Threatened & Endangered species: None.
5. Potential For Threatened & Endangered species: Slight
7. Observed Noxious Weeds: None

8. AFFECTED ENVIRONMENTAL

1. There are no surface damages as a result of the initial survey.

4.1 WILDLIFE

A. POTENTIAL SITE UTILIZATION

1. Big Game-The area is used throughout the year by mule deer, elk, and antelope. During the winter it is used mainly by mule deer and elk.
2. Small Game-The area is used by cottontail rabbit.
3. Raptor- Various species of raptors use this area for habitat. Raptors which are observed using the area are Golden eagles, Redtail hawk, & Kestrel. Ferruginous hawk hunt in the area and there is an active nest located approximately 2.0 miles to the south of this project area in Section 20, T5S, R3W, USB&M.
5. Non-Game Wildlife- Animal species which have been observed using this area are black tail jack rabbit, coyote, fox, badger, and various species of reptiles, and song birds.
6. Threatened & Endangered Species: No T&E species are reported using the area of this project.

4.2 PRESENT SITE USE

A. USAGE

	<u>acres</u>
Rangeland	3.20
Irrigable land	0
Woodland	3.20
Non-Irrigable land	3.20
Commercial timber	0
Floodplain	0
Wetland	0
Riparian	0
Other:	0

4.3 CULTURAL RESOURCES

A. CULTURAL SURVEY

Cultural Resource Surveys were performed by James A. Truesdale, an Independent Archaeologist on June 3, 1996.

5.0 ENVIRONMENTAL IMPACTS

A. SURFACE ALTERATIONS

	<u>acres</u>
1. Access road	0.72
2. Well site	1.26
3. Pipeline right-of-way	1.22
4. Total area disturbed	3.20

B. VEGETATION/LANDSCAPE

1. Production loss (AUM's)/year: 0.21
2. Permanent scar on landscape: Yes x No
3. Potential impacts to Threatened & Endangered species:
Yes No X

C. SOIL/RANGE/WATERSHED

There will be an increase in soil erosion from wind and water. There will not be any possible point source of water pollution.

The area is presently used as rangeland. In recent years the area has been permitted for livestock grazing, but at the present time no permits have been issued for the area. This project will reduce livestock grazing by approximately 0.21 AUM/year.

The area is not used as irrigated cropland and a water right has not been designated for the area.

D. WILDLIFE/THREATENED & ENDANGERED SPECIES

There will be an insignificant reduction of wildlife habitat and grazing for livestock. There will also be an increase in wildlife disturbance and poaching resulting from the additional traffic and people using the area.

There are no known impacts to Threatened or Endangered species but is important habitat for the Ferruginous hawk. The area is important winter range for big game.

Ferruginous Hawks use this area for nesting and hunting. There is a nest approximately 2.0 miles south of the wellsite in Section 20 which has an active nesting history.

6.0 MITIGATION STIPULATIONS

A. VEGETATION/LANDSCAPE

1. Before the site is abandoned the company will be required to restore the well site and right-of-ways to near their original state. The disturbed area will be reseeded with desirable perennial vegetation.
2. Noxious weeds will be controlled on the well site and rights-of-way. If noxious weeds spread from the project area onto adjoining land, the company will also be responsible for their control.

B. SOILS/RANGE/WATERSHEDS

1. Soil erosion will be mitigated by reseeding all disturbed areas.
2. The pipeline will be constructed to lay on the soil surface, and the right-of-way will not be bladed or cleared of vegetation.

Where pipelines are constructed parallel to roads they may be welded on the road and then lifted from the road onto the right-of-way.

Where pipelines do not parallel roads but cross country between stations, they shall be welded in place at wellsites or on access roads and then pulled between stations with a suitable piece of equipment. Traffic will be restricted along these areas so that the pipeline right-of-way will not be used as an access road.

3. An open drilling system will be used. Reserve pits will be lined with impervious synthetic liners. Prior to backfilling the reserve pit all fluids will be pumped from the pit into trucks and hauled to approved disposal sites. When the reserve pits are backfilled the surplus oil and mud, etc will be buried a minimum of 3.0 feet below the surface of the soil.
4. A closed production system will be used. Production fluids will be contained in leak proof tanks. All production fluids will be disposed of at approved disposal sites. The indiscriminate dumping of production fluids on roads, wellsites or other areas will not be allowed.
5. Although the access roads have a 30 foot right-of-way the bladed area of the road will be limited to

21 feet in all areas except where deep cuts and fills are required, sharp turns are required, or at the intersections with other roads.

C. WILDLIFE/VEGETATION/THREATENED & ENDANGERED SPECIES

Because this project will not impact any sensitive or endangered species no stipulations have been developed for their protection.

D. CULTURAL RESOURCES

Cultural resource surveys were performed by James A. Truesdale. The consultant recommends clearance of the project as it is presently staked.

E. UTE TRIBAL REGULATIONS

(1). Prior to commencing surveys or construction on the U&O Indian Reservation the operator, and any of its sub-contractors, shall acquire access permits and business permits from the Ute Indian Tribe.

(2). Prior to the commencement of construction, the operator shall notify the Ute Tribal Department of Energy and Minerals of the date construction shall begin.

7.0 UNAVOIDABLE ADVERSE IMPACTS

A. SURFACE ALTERATIONS

None of the adverse impacts listed in 5.0 above can be avoided in a practical manner except those which are mitigated in item 6.0 above and those specified in BLM's 13 point surface use plan.

B. RELATIONSHIP BETWEEN SHORT-TERM USE OF THE ENVIRONMENT VS LONG TERM PRODUCTIVITY.

1. Short Term: (Estimated 20 years) A total loss of production on the land and the associated environmental impacts will continue to influence the surrounding area for the productive life of the well.
2. Long Term: Standard policies provide for rehabilitation of wellsite and rights-of-ways. After the land is rehabilitated, it is not expected to return to its original productive capability. Normally, there will be a permanent scar left on the landscape.

C. IRREVERSIBLE AND IRRETRIEVABLE COMMITMENT

Oil and Gas are non-renewable resources, once they have been removed they can never be replaced.

8.0 CUMULATIVE IMPACTS

A. FULL DEVELOPMENT

Each additional well drilled for development increases the soil erosion potential, reduces wildlife habitat and grazing, increases potential soil and geologic pollution resulting from salt loading, reduces the soil's potential to recover, and increases the potential of water pollution from produced waters and hydro-carbons. Therefore, strict conformance with the mitigation measures and recommendations in this document is emphasized to minimize the adverse environmental impacts.

9.0 NEPA COMPLIANCE

A. RESEARCH/DOCUMENTATION

Based on available information, 8-5-96, the proposed location in the following areas of environmental impacts has been cleared:

<u>X</u>	Yes	_____	No	Listed Threatened & Endangered species
<u>X</u>	Yes	_____	No	Critical wildlife habitat
<u>X</u>	Yes	_____	No	Historical and cultural resources

10.0 REMARKS

A. SURFACE PROTECTION/REHABILITATION

All essential surface protection and rehabilitation requirements are specified above.

11.0 RECOMMENDATIONS

A. APPROVAL/DISAPPROVAL

We recommend approval of the proposed action as outlined in item 1.0 above.

8-6-96

Date

Dale H. Sturges
Representative - BIA Land
Operations, Uintah and Ouray
Agency

12.0 DECLARATION

A. APPROVAL

It has been determined that the proposed action is not a federal action significantly affecting the quality of the environment as it would require the preparation of an environmental impact statement in accordance with Section 102 (2) (c) of the National Environmental Policy Act of 1969 (42 USC 4331) (2) (C).

8/7/96

Date

Acting Harry Orr
Superintendent,
Gintah and Ouray Agency

14.0 CONSULTATION

A. REPRESENTATIVES/ORGANIZATION

Dale Hanberg- BIA
Ed Trotter-Petroglyphs
Lonnie Nephi-UTEM

B:\EAPetro.80

DIVISION OF OIL, GAS AND MINING

CONFIDENTIAL

SPUDDING INFORMATION

Name of Company: PETROGLYPH OPERATING

Well Name: UTE TRIBAL 08-07

Api No. 43-013-31691

Section 8 Township 5S Range 3W County DUCHESNE

Drilling Contractor UNION

Rig #: 16

SPUDDED:

Date: 9/12/96

Time:

How: ROTARY

Drilling will commence:

Reported by: D. HACKFORD

Telephone #:

Date: 9/12/96 Signed: FRM

STATE OF OREGON
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM - FORM 6

OPERATOR Petroglyph Operating Co., Inc.
ADDRESS P.O. Box 1839
Hutchinson, KS 67504-1839

OPERATOR ACCT. NO. N3800


ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	11871	43-013-31691	Ute Tribal 08-07	SWNW	8	5S	3W	Duchesne	9-12-96	
WELL 1 COMMENTS: Ute Tribal 08-07 will tie into Ute Tribal 08-01 Battery <i>Entity added 10-22-96. Lc.</i>											
WELL 2 COMMENTS:											
WELL 3 COMMENTS:											
WELL 4 COMMENTS:											
WELL 5 COMMENTS:											

ACTION CODES (See instructions on back of form)

- A - Establish new entity for new well (single well only)
- B - Add new well to existing entity (group or unit well)
- C - Re-assign well from one existing entity to another existing entity
- D - Re-assign well from one existing entity to a new entity
- E - Other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.


(3/89)



Deanna K. Bell
Signature Deanna K. Bell
Operations Coordinator 9-16-96
Title Date
Phone No. (801) 722-2531

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING

REPORT OF WATER ENCOUNTERED DURING DRILLING



1. Well name and number: UTE TRIBAL 08-07

API number: 43-013-31691

2. Well Location: QQ SWNW Section 8 Township 5S Range 3W County Duchesne

3. Well operator: Petroglyph Petroglyph Operating Company, Inc.

Address: P.O. Box 1839
Hutchinson, KS 67504-1839 Phone: (316) 665-8500

4. Drilling contractor: Union

Address: P.O. Drawer
Buckhannon, WV 26201 Phone: (304) 472-4610

5. Water encountered (attach additional pages as needed):

DEPTH		VOLUME	QUALITY
FROM	TO	(FLOW RATE OR HEAD)	(FRESH OR SALTY)
375'		1 qt per 5 min.	FRESH
410	1250	Blow TEST 1qt per 5 min	FRESH
1250	3550	Blow TEST 1 1/2 qt per 5 min	FRESH
3550		1" TO 2" STREAM	FRESH

6. Formation tops:

If an analysis has been made of the water encountered, please attach a copy of the report to this form.

I hereby certify that this report is true and complete to the best of my knowledge.

Date:

Title

Name & Signature:

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUBMIT IN DUPLICATE*

(See other instructions on reverse side)

Form approved.
Budget Bureau No. 1004-0137
Expires August 31, 1985

WELL COMPLETION OR RECOMPLETION REPORT AND LOG*

1a. TYPE OF WELL: OIL WELL ☒ GAS WELL ☐ DRY ☐

b. TYPE OF COMPLETION: NEW WELL ☒ WORK OVER ☐ DEEP-EN ☐ PLUG BACK ☐ DIFF. RESVR. ☐

2. NAME OF OPERATOR
Petroglyph Operating Company, Inc.

3. ADDRESS OF OPERATOR
P.O. Box 1839 Hutchinson, KS 67504-1839

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.)
At surface

1700' FNL & 2133' FEL, SW NW

At top prod. interval reported below

At total depth 6296 RTD

14. PERMIT NO. 43-013-31691 DATE ISSUED

5. LEASE DESIGNATION AND SERIAL NO.
14-20-H62-3507

6. IF INDIAN, ALLOTTEE OR TRIBE NAME
Ute Indian Tribe

7. UNIT AGREEMENT NAME
14-20-H62-4650

8. FARM OR LEASE NAME
Ute Tribal

9. WELL NO.
08-07

10. FIELD AND POOL, OR WILDCAT
Antelope Creek

11. SEC., T., R., M., OR BLOCK AND SURVEY OR AREA

Sec 8-T5S-R3W

12. COUNTY OR PARISH
Duchesne

13. STATE
Utah

15. DATE SPUDDED 9-12-96 16. DATE T.D. REACHED 9-18-96 17. DATE COMPL. (Ready to prod.) 10-3-96 18. ELEVATIONS (DF, RKB, RT, GR, ETC.)* 6029'

20. TOTAL DEPTH, MD & TVD 6296' 21. PLUG BACK T.D., MD & TVD 6249' 22. IF MULTIPLE COMPL. HOW MANY* 23. INTERVALS DRILLED BY 24. PRODUCING INTERVAL(S), OF THIS COMPLETION—TOP, BOTTOM, NAME (MD AND TVD)*

Green River

26. TYPE ELECTRIC AND OTHER LOGS RUN
CNL, AIT 11-20-96

27. WAS WELL CORED

28. CASING RECORD (Report all strings set in well)

CASING SIZE	WEIGHT, LB./FT.	DEPTH SET (MD)	HOLE SIZE	CEMENTING RECORD	AMOUNT PULLED
8 5/8"	24#	252	12 1/4"	150 sx Class G	
5 1/2"	15.5#	6294	7 7/8"	90 sx Prem Lite Plus + 300 sx G	

29. LINER RECORD					30. TUBING RECORD	
SIZE	TOP (MD)	BOTTOM (MD)	SACKS CEMENT*	SCREEN (MD)	SIZE	DEPTH SET (MD)
					2 7/8"	5999'

31. PERFORATION RECORD (Interval, size and number)				32. ACID. SHOT. FRACTURE. CEMENT SQUEEZE, ETC.	
6228-32 (17 shots)	4843-45 (9 shots)			DEPTH INTERVAL (MD)	AMOUNT AND KIND OF MATERIAL USED
5248-54 (25 shots)	4394-4405 (45 shots)			6228-32	4000 gal fluid, 14700# prop
4978-82 (17 shots)				5248-54	4000 gal fluid, 14100# prop
4834-40 (25 shots)				4978-82	6859 gal fluid, 25200# prop
				4834-45	4000 gal fluid, 16700# prop
					6850 gal fluid, 26900# prop

33.* DATE FIRST PRODUCTION		PRODUCTION METHOD (Flowing, gas lift, pumping—size and type of pump)				WELL STATUS (Producing or shut-in)	
10-22-96		2 1/2" x 1 3/4" x 16' 40 ring pump				producing	
DATE OF TEST	HOURS TESTED	CHOKE SIZE	PROD'N. FOR TEST PERIOD	OIL—BBL.	GAS—MCF.	WATER—BBL.	GAS-OIL RATIO
10-26-96	24			79	20	29	
FLOW. TUBING PRESS.	CASINO PRESSURE	CALCULATED 24-HOUR RATE	OIL—BBL.	GAS—MCF.	WATER—BBL.	OIL GRAVITY-API (CORR.)	
	450						

34. DISPOSITION OF GAS (Sold, used for fuel, vented, etc.)
sold, used for fuel

TEST WITNESSED BY
Dave Schreiner

35. LIST OF ATTACHMENTS

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records

SIGNED

TITLE Administrative Operations Manager DATE 10-31-96


*(See Instructions and Spaces for Additional Data on Reverse Side)

37. SUMMARY OF POROUS ZONES: (Show all important zones of porosity and contents thereof; cored intervals; and all drill-stem, tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures, and recoveries):

FORMATION	TOP	BOTTOM	DESCRIPTION, CONTENTS, ETC.	38. GEOLOGIC MARKERS		
				NAME	MEAS. DEPTH	TRUE VERT. DEPTH
X Marker	4489					
Douglas Creek	4635					
B Limestone	5030					
Castle Peak	5560					
Basal Carbonate	5976					

VIA UPS

Vicky Dyson
State of Utah
Division of Oil, Gas & Mining
1594 W. North Temple, Ste. 1210
Salt Lake City, UT 84114



Ms. Dyson:

Enclosed please find the logs listed below for the wells located in Duchesne County, Utah.

<u>Well Name</u>	<u>Log</u>
Ute Tribal 03-04	CNL, AIT
Ute Tribal 03-12	CNL, AIT
Ute Tribal 04-02A	CNL/GR
Ute Tribal 04-08	CNL/GR, AIT
Ute Tribal 04-15	CNL, AIT
Ute Tribal 08-07	AIT - 43 013 31691
Ute Tribal 17-12	AIT
Ute Tribal 28-05A	CNL
Ute Tribal 30-01	CNL, AIT
Ute Tribal 30-08	CNL, AIT

CONFIDENTIAL

If you have any questions, please do not hesitate to contact me at (316) 665-8500.

Sincerely,

Angela R. Ely
Angela R. Ely
Administrative Operations Manager

ARE/ms

Enclosures

PETROGLYPH Operating Company, Inc.

6209 North Highway 61, Hutchinson, Kansas 67502 • P.O. Box 1839, Hutchinson, Kansas 67504-1839

November 26, 1996

Vicky Dyson
State of Utah
Division of Oil, Gas & Mining
1594 W. North Temple, Ste. 1210
Salt Lake City, UT 84114

Ms. Dyson:


Further to your letter dated November 18, 1996, enclosed please find the CNL listed below for the well located in Duchesne County, Utah. The AIT log was sent to your office November 15, 1996.

Well Name
Ute Tribal 08-07

Log
CNL (Porosity Log)

If you have any questions, please do not hesitate to contact me at (316) 665-8500.

Sincerely,



Glenna S. Balsick
Production Analyst

GSB/ae

Enclosures

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS


Do not use this form for proposals to drill or to deepen or reentry to a different reservoir.
Use "APPLICATION FOR PERMIT" for such proposals

SUBMIT IN TRIPLICATE

1. Type of Well <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other	5. Lease Designation and Serial No. 14-20-H62-3507
2. Name of Operator Petroglyph Operating Company, Inc.	6. If Indian, Allottee or Tribe Name Ute Indian Tribe
3. Address and Telephone No. P.O. Box 1839, Hutchinson, KS 67504-1839; (316) 665-8500	7. If Unit or CA, Agreement Designation 14-20-H62-4650
4. Location of Well (Footage, Sec., T., R., or Survey Description) 1700' FNL & 2133' FEL SW NW Sec. 8-T5S-R3W	8. Well Name and No. Ute Tribal 08-07
	9. API Well No. 43-013-31691
	10. Field and Pool, or Exploratory Area Antelope Creek
	11. County or Parish, State Duchesne County, UT

12. CHECK APPROPRIATE BOX(s) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Abandonment	<input type="checkbox"/> Change of Plans
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Recompletion	<input type="checkbox"/> New Construction
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Plugging Back	<input type="checkbox"/> Non-Routine Fracturing
	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> Water Shut-Off
	<input type="checkbox"/> Altering Casing	<input checked="" type="checkbox"/> Conversion to Injection
	<input type="checkbox"/> Other _____	<input type="checkbox"/> Dispose Water
(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)		

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*
Petroglyph Operating Company, Inc. has submitted an application for a UIC permit to convert the Ute Tribal 08-07 from a producing well to an injection well under the EPA Area Permit #UT2736-00000 within the Antelope Creek Waterflood Project Area located in Duchesne County, Utah.



14. I hereby certify that the foregoing is true and correct
Signed April Meyer Title Geo/Petro Engineering Tech Date May 6, 1997
(This space for Federal or State official use)
Approved by _____ Title _____ Date _____
Conditions of Approval, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter in its jurisdiction.

*See Instruction on Reverse Side

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry to a different reservoir.

Use "APPLICATION FOR PERMIT" for such proposals

SUBMIT IN TRIPLICATE

FORM APPROVED
Budget Bureau No. 1004-0135
Expires March 31, 1993

5. Lease Designation and Serial No.
14-20-H62-3507

6. If Indian, Allottee or Tribe Name
Ute Indian Tribe

7. If Unit or CA, Agreement Designation
14-20-H62-4650

8. Well Name and No.
Ute Tribal 08-07

9. API Well No.
43-013-31691

10. Field and Pool, or Exploratory Area
Antelope Creek

11. County or Parish, State
Duchesne County, UT

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

Petroglyph Operating Company, Inc.

3. Address and Telephone No.

P.O. Box 1839, Hutchinson, KS 67504-1839; (316) 665-8500

4. Location of Well (Footage, Sec., T., R., or Survey Description)

1700' FNL & 2133' FEL
SW NW Section 8-T5S-R3W

12. CHECK APPROPRIATE BOX(s) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION

☐ Notice of Intent
☒ Subsequent Report
☐ Final Abandonment Notice


TYPE OF ACTION

☐ Abandonment
☐ Recompletion
☐ Plugging Back
☐ Casing Repair
☐ Altering Casing
☒ Other Commence Injection
☐ Change of Plans
☐ New Construction
☐ Non-Routine Fracturing
☐ Water Shut-Off
☐ Conversion to Injection
☐ Dispose Water

(Note: Report results of multiple completion on Well
Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

Further to BLM & EPA approval (Permit #UT2736-04381), enclosed are copies of the MIT and Job Summary. Injection commenced on 12/2/97.



14. I hereby certify that the foregoing is true and correct

Signed Kathy Turner Title Petroleum Engineering Tech Date June 9, 1998

(This space for Federal or State official use)

Approved by _____ Title _____ Date _____

Conditions of Approval, if any:

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter in its jurisdiction.

*See Instruction on Reverse Side

Mechanical Integrity Test

Casing or Annulus Pressure Test for Well UT2736-04381

U.S. Environmental Protection Agency
Underground Injection Control Program, UIC Implementation Section, 8WM-DW
999 18th Street, Suite 500, Denver, CO 80202-2466
This form was printed on 05/21/1997.

EPA Witness: _____ Date 8/26/97

Test conducted by: Gene Searle

Others present: _____

UTE TRIBAL #08-07	2R UC as of / /
DUCHESNE	SWNW 08 05S 03W
Petroglyph Operating Company, Inc.,	Hutchinson, KS Op ID PTG01
Last MIT: No record / /	
Max Allowed Press psig	1996 Max Reported Press 0 psig


Is this a regularly scheduled test? ☐ Yes ☐ No
 Initial test for permit? ☒ Yes ☐ No
 Test after well rework? ☐ Yes ☐ No

Well injecting during test? ☒ NO ☐ YES _____ BPD

Initial casing/tubing annulus pressure 610 psig
 Does the annulus pressure build back up? ☐ Yes ☒ No

TUBING PRESSURE			
Initial	0 psig	psig	psig
End of Test	0 psig	psig	psig
CASING/TUBING ANNULUS PRESSURE			
Time	Test #1	Test #2	Test #3
0 min	610 psig	psig	psig
5	610		
10	610		
15 min	610		
20	610		
25	610		
30 min	610		
2 hrs	600		
Result (circle)	Pass Fail	Pass Fail	Pass Fail

PRINTED IN U.S.A.

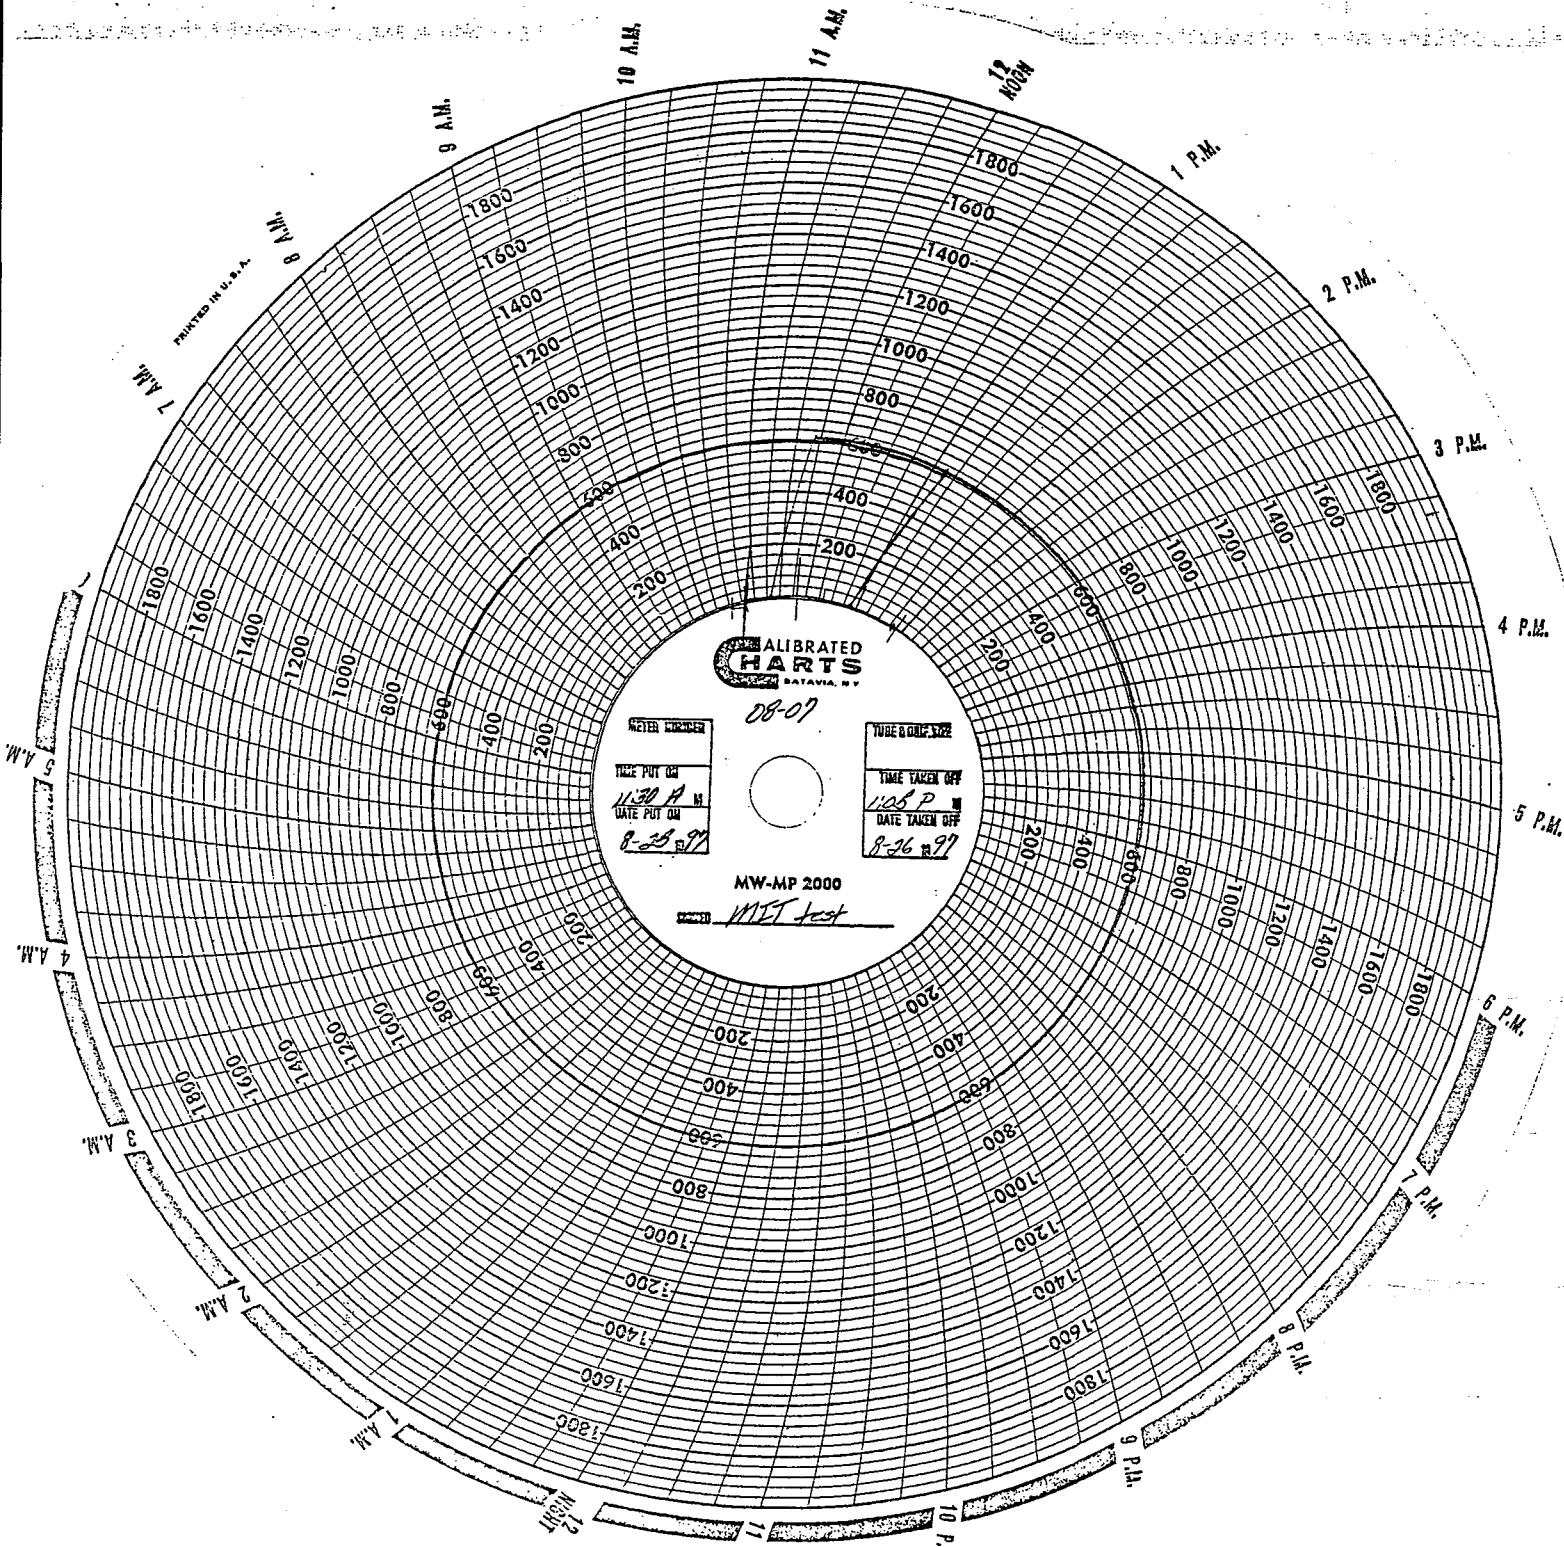

WORKOVER REPORT

5/14/98

Petroglyph Operating Co., Inc.

Operator: Petroglyph Operating Company, Inc.

Elevation: GL 6029

Lease: Ute Tribal 08-07

KB 6039

API #: 43-013-31691

Property: 11390

Location: 8 - 5 S - 3 W

AFE/EPE Number: 40037

County, St.: Duchesne UT

Event Type: convert to injector

Activity Date

Activity Description

8/23/97

Finish P.U. & RIH with 2 3/8" tubing to 4343'. N.D. BOP'S. Pump 100bbls. PKR fluid down casing. Drop standing valve. PKR would not set standing valve leaking. Fish standing valve & rebuild. Drop & set PKR. N.U. well head & fish standing valve. Fin. & test casing to 1000psi. Leave pressure on casing for MIT. SWIFN. FINAL REPORT.

Tubing Detail	KB	10.00	
	9' x 2 7/8" tubing sub.	4.00	
	2 3/8" x 2 7/8" x/o	.73	
	133jnts. 2 3/8" x 4.7# J-55 tubing	4319.24	
	2 3/8" x 2 7/8" x/o	.73	
	5 1/2" Hydro 1 PKR	7.67	4334.70
	"F" Nipple	1.05	
	EOT		4343.42

8/22/97

Flush tubing with 50bbls. hot prod. water. POOH & lay down rods & pump. Bleed down casing. N/D well head & N.U. BOP'S. Circulate well clean with 200bbls. hot prod. water. POOH & lay down 2 7/8" tubing (192jnts.). P.U. talley & RIH with 5 1/2" hydro & PKR & new 2 3/8" x 4.7# J-55 tubing. Breaking all collars & doping with teflon dope. (65jnts.)

8/21/97

PERFORATIONS:

6228-6232	Green River H (03)	4.3 SPF	17 shots
5248-5254	Green River D (05)	4.2 SPF	25 shots
4978-4982	Green River C (09)	4.3 SPF	17 shots
4843-4845	Green River C (06)	4.5 SPF	9 shots
4834-4840	Green River C (06)	4.2 SPF	25 shots
4394-4405	Green River B (10)	4.1 SPF	45 shots

MIRU service rig & equipment. Unseat pump & prep to flush rods. SWIFN.

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: INDIAN
1. TYPE OF WELL Water Injection Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: PETROGLYPH OPERATING CO		7. UNIT or CA AGREEMENT NAME: ANTELOPE CREEK
3. ADDRESS OF OPERATOR: 960 Broadway Avenue, Ste 500, Boise, ID, 83703		8. WELL NAME and NUMBER: UTE TRIBAL 08-07
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1700 FNL 2133 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: SWNW Section: 08 Township: 05.0S Range: 03.0W Meridian: U		9. API NUMBER: 43013316910000
9. FIELD and POOL or WILDCAT: ANTELOPE CREEK		COUNTY: DUCHESNE
STATE: UTAH		

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input checked="" type="checkbox"/> ACIDIZE	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> CASING REPAIR	
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 6/9/2014	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> CHANGE WELL NAME	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> CONVERT WELL TYPE	
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> NEW CONSTRUCTION	
	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> PLUG BACK	
	<input type="checkbox"/> PRODUCTION START OR RESUME	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION	
	<input type="checkbox"/> REPERFORATE CURRENT FORMATION	<input type="checkbox"/> SIDETRACK TO REPAIR WELL	<input type="checkbox"/> TEMPORARY ABANDON	
	<input type="checkbox"/> TUBING REPAIR	<input type="checkbox"/> VENT OR FLARE	<input type="checkbox"/> WATER DISPOSAL	
	<input type="checkbox"/> WATER SHUTOFF	<input type="checkbox"/> SI TA STATUS EXTENSION	<input type="checkbox"/> APD EXTENSION	
	<input type="checkbox"/> WILDCAT WELL DETERMINATION	<input type="checkbox"/> OTHER	OTHER: <input style="width: 100px;" type="text"/>	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

Please see attached.

Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY
 July 01, 2014

NAME (PLEASE PRINT) Rodrigo Jurado	PHONE NUMBER 435 722-5302	TITLE Regulatory & Compliance Spc
SIGNATURE N/A	DATE 6/30/2014	

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

FORM 9

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL OIL WELL <input type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER <u>Injection Well</u>		5. LEASE DESIGNATION AND SERIAL NUMBER: 14-20-H62-3507
2. NAME OF OPERATOR: Petroglyph Operating Company Inc.		6. IF INDIAN, ALLOTTEE OR TRIBE NAME: Ute Indian Tribe
3. ADDRESS OF OPERATOR: P.O. Box 607 CITY: <u>Roosevelt</u> STATE: <u>UT</u> ZIP: <u>84066</u>		7. UNIT or CA AGREEMENT NAME: 14-20-H62-4650
4. LOCATION OF WELL FOOTAGES AT SURFACE: 1700' FNL, 2133' FEL		8. WELL NAME and NUMBER: Ute Tribal 08-07
QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: <u>SWNW 8 5S 3W U</u>		9. API NUMBER: 4301331691
		10. FIELD AND POOL, OR WILDCAT: Antelope Creek
		COUNTY: <u>Duchesne</u>
		STATE: <u>UTAH</u>

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA			
TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will start: _____	<input checked="" type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLARE
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of work completion: <u>6/9/2014</u>	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/RESUME)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: _____
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

On 6/9/2014 Petroglyph Operating rigged up a coiled tubing unit on the well referenced above to acidize the well and improve the well's injection rates. The targeted treatment interval was 4,394'-5,254'. We ran in hole through the injection tubing, established an injection rate and slowly pulled back as we spotted acid over the referenced interval. We spotted 1,201 Gal of 15% Hcl, ran back in to the bottom of the interval and repeated spotting 798 Gal of Chlorine Dioxide, and ran back in again spotting in 1,113 Gal of 15% Hcl. The treatment was then flushed out into the formation with 672 Gallons of fresh water and the well was returned to injection.

NAME (PLEASE PRINT) <u>Rodrigo Jurado</u>	TITLE <u>Regulatory Compliance Specialist</u>
SIGNATURE 	DATE <u>6/30/2014</u>

(This space for State use only)
