

UTAH OIL AND GAS CONSERVATION COMMISSION

REMARKS: WELL LOG _____ ELECTRIC LOGS _____ **X** _____ WATER SANDS _____ LOCATION INSPECTED _____ SUB. REPORT/abd. _____DATE FILED **OCTOBER 30, 1997**

LAND: FEE & PATENTED

STATE LEASE NO.

PUBLIC LEASE NO.

INDIAN #

DRILLING APPROVED: **FEBRUARY 11, 1998****14-20-H62-3506**

SPUDDED IN:

COMPLETED: _____ PUT TO PRODUCING: _____

INITIAL PRODUCTION:

GRAVITY A.P.I.

GOR:

PRODUCING ZONES:

TOTAL DEPTH:

WELL ELEVATION:

DATE ABANDONED: **5-5-2000 LA'D**FIELD: **ANTELOPE CREEK**

UNIT:

COUNTY: **DUCHESNE**WELL NO. **UTE TRIBAL 07-05**API NO. **43-013-31977**LOCATION **1818 FNL** FT. FROM (N) (S) LINE, **480 FWL**FT. FROM (E) (W) LINE. **SW NW****1/4 - 1/4 SEC. 7**

TWP.

RGE.

SEC.

OPERATOR

TWP.


RGE.

SEC.

OPERATOR

5S**3W****7****PETROGLYPH OPERATING**

Petroglyph Operating Co., Inc.
P.O. Box 1839
Hutchinson, KS 67504-1839



October 15, 1997

Utah Division of Oil, Gas, & Mining
1594 West North Temple
Box 145801
Salt Lake City, UT 84114-5801

RE: APPLICATION FOR PERMIT TO DRILL
UTE TRIBAL #07-05
SW/NW SEC. 7, T5S, R3W
DUCHESNE COUNTY, UTAH
LEASE NO. BIA 14-20-H62-3506
UTE TRIBAL LANDS

Enclosed please find a copy of the Application for Permit to Drill and associated attachments for the referenced well.

Please address further communication regarding this matter (including approval) to:

Ed Trotter
P.O. Box 1910
Vernal, UT 84078
Phone # (801) 789-4120
Fax # (801) 789-1420

Sincerely,

A handwritten signature in dark ink, appearing to read "Ed Trotter". The signature is fluid and cursive, with a large loop at the end.

Ed Trotter
Agent

Petroglyph Operating Co., Inc.

Attachments

/EHT/dmt

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR DEEPEN


1a. TYPE OF WORK DRILL <input checked="" type="checkbox"/> DEEPEN <input type="checkbox"/>		5. LEASE DESIGNATION AND SERIAL NO. 14-20-H62-3506
b. TYPE OF WELL OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER <input type="checkbox"/> SINGLE ZONE <input type="checkbox"/> MULTIPLE ZONE <input type="checkbox"/>		6. IF INDIAN, ALLOTTEE OR TRIBE NAME UTE INDIAN TRIBE
2. NAME OF OPERATOR PETROGLYPH OPERATING COMPANY, INC.		7. UNIT AGREEMENT NAME
3. ADDRESS AND TELEPHONE NO. P.O. BOX 607, ROOSEVELT, UTAH 84066		8. FARM OR LEASE NAME, WELL NO. UTE TRIBAL
4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.)* At surface 1818' FNL & 480' FWL SW/NW At proposed prod. zone 146		9. API WELL NO. #07-05
14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE* 18.4 MILES SOUTHWEST OF MYTON, UTAH		10. FIELD AND POOL, OR WILDCAT ANTELOPE CREEK
15. DISTANCE FROM PROPOSED* LOCATION TO NEAREST PROPERTY OR LEASE LINE, FT. (Also to nearest drilg. unit line, if any) 480'±		11. SEC., T., R., M., OR BLK. AND SURVEY OR AREA SEC. 7, T5S, R3W
16. NO. OF ACRES IN LEASE 640		12. COUNTY OR PARISH DUCHESTER
17. NO. OF ACRES ASSIGNED TO THIS WELL 80		13. STATE UTAH
18. DISTANCE FROM PROPOSED LOCATION* TO NEAREST WELL, DRILLING, COMPLETED, OR APPLIED FOR, ON THIS LEASE, FT. 5808.8'		20. ROTARY OR CABLE TOOLS ROTARY
21. ELEVATIONS (Show whether DF, RT, GR, etc.) 5838.8' GRADED GROUND		22. APPROX. DATE WORK WILL START* OCTOBER 1997

CONFIDENTIAL

PROPOSED CASING AND CEMENTING PROGRAM

SIZE OF HOLE	GRADE SIZE OF CASING	WEIGHT PER FOOT	SETTING DEPTH	QUANTITY OF CEMENT
12 1/4	8 5/8	24.0#	250'	135 sx class "G" + 2% CaCl ₂
7 7/8	5 1/2	15.5#	5808.8'	+ 1/4 #/sx celloflake.
				50/50 POZMIX + 2% GEL + 10% SALT TO 400' ABOVE ALL ZONES OF INTEREST (+ 10% EXCESS). LIGHT CEMENT (11 PPG+) + LCM TO 200' ABOVE OIL SHALE OR FRESH WATER INTERVALS (+ 5% EXCESS).

CONFIDENTIAL

PETROGLYPH OPERATING COMPANY, INC. WILL BE THE DESIGNATED
OPERATOR OF THE SUBJECT WELL UNDER BOND #4556.pc: Utah Division of Oil, Gas, and Mining
Bureau of Indian Affairs, Fort Duchesne, Utah
Ute Tribe, Fort Duchesne, Utah

IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24. SIGNED [Signature] TITLE AGENT FOR PETROGLYPH DATE 10-23-97
(This space for Federal or State office use)

PERMIT NO. 43-013-31977

APPROVAL DATE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

CONDITIONS OF APPROVAL, IF ANY:

APPROVED BY

TITLE

DATE

*See Instructions On Reverse Side



T5S, R3W, U.S.B.&M.

PETROGLYPH OPERATING CO., INC.

Well Location, UTE TRIBAL #07-05, located is shown in the SW 1/4 NW 1/4 of Section 7, T5S, R3W, U.S.B.&M. Duchesne County, Utah.

BASIS OF ELEVATION

BRASS CAP SET IN CONCRETE BY SUNRISE ENGINEERING LOCATED IN THE SE 1/4 OF SECTION 8, T5S, R3W, U.S.B.&M. SAID ELEVATION IS MARKED AS BEING 6191.3 FEET.

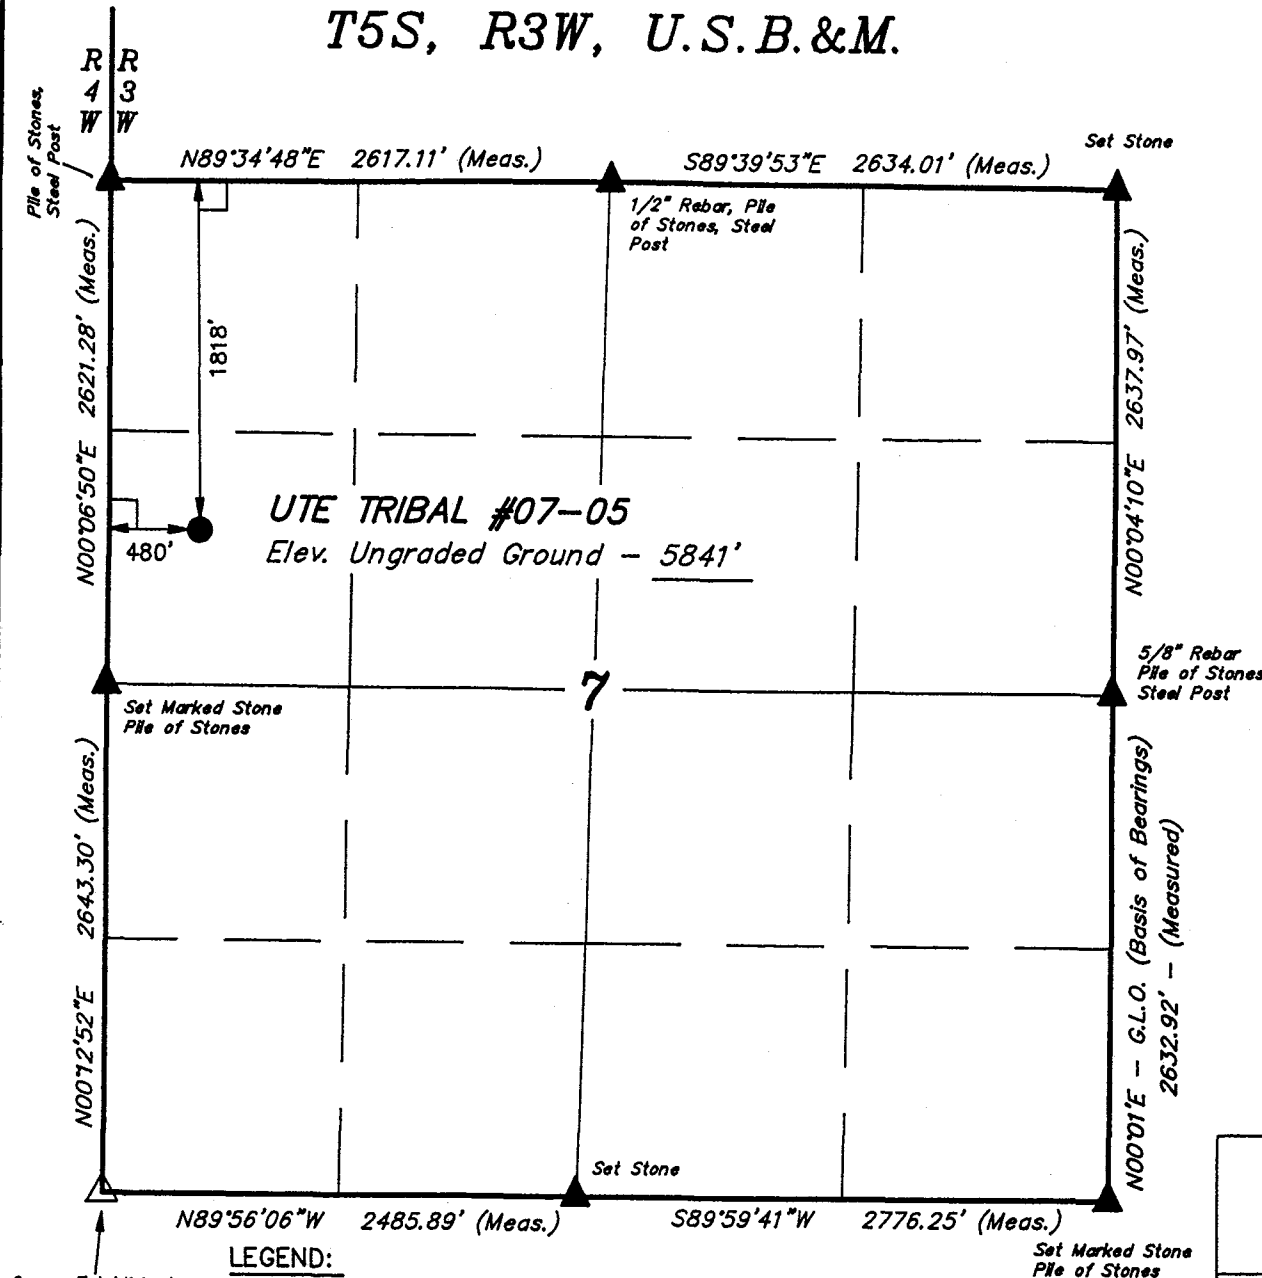

SCALE

CERTIFICATE

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

REGISTERED LAND SURVEYOR
REGISTRATION NO. 161319
STATE OF UTAH

UINTAH ENGINEERING & LAND SURVEYING
85 SOUTH 200 EAST - VERNAL, UTAH 84078
(801) 789-1017

LEGEND:

- └─┘ = 90° SYMBOL
- = PROPOSED WELL HEAD.
- ▲ = SECTION CORNERS LOCATED.
- △ = Section Corner Re-established by Bearing Tree Information. (Not Set on Ground)

Corner Established by Bearing Tree Information. (Not Set on Ground)

SCALE 1" = 1000'	DATE SURVEYED: 7-22-97	DATE DRAWN: 9-8-97
PARTY G.S. J.W. C.B.T.	REFERENCES G.L.O. PLAT	
WEATHER WARM	FILE PETROGLYPH OPERATING CO., INC.	

EIGHT POINT PLAN

UTE TRIBAL #07-05
SW/NW, SEC. 7, T5S R3W
DUCHESNE COUNTY, UTAH

1. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

FORMATIONS	DEPTH	SUBSEA
Mahogany Shale	2592.8	3256
"X" Marker	4198.8	1650
Douglas Creek	4344.8	1504
"B" Limestone	4737.8	1111
B/Castle Peak Limestone	5273.8	575
Basal Carbonate Limestone	5698.8	150
Total Depth	5808.8	40

Anticipated BHP 2000 psi

2. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS FORMATIONS:

<u>Substance</u>	<u>Formation</u>	<u>Depth</u>	<u>Subsea</u>
Oil/Gas	Douglas Creek	4344.8	1504
Oil/Gas	B/Castle Peak	5273.8	575
Other mineral zones	N/A		

3. PRESSURE CONTROL EQUIPMENT : BOP Schematic Diagram attached.

4. CASING PROGRAM :

						<u>MINIMUM SAFETY FACTOR</u>		
<u>HOLE SIZE</u>	<u>INTERVAL</u>	<u>LENGTH</u>	<u>SIZE</u>	<u>WEIGHT</u>	<u>GRADE</u>	<u>COLLAPSE</u>	<u>BURST</u>	<u>TENSILE</u>
12 1/4	0' - 250'	250'	8 5/8	24.0 #	J-55	1370 PSI	2950 PSI	263,000#
7 7/8	0' - 5808.8'	5808.8'	5 1/2	15.5 #	M-50	3650 PSI	4550 PSI	186,000#

All casing will be new or inspected.

EIGHT POINT PLAN

UTE TRIBAL #07-05
SW/NW, SEC. 7, T5S R3W
DUCHESNE COUNTY, UTAH

5. MUD PROGRAM

INTERVAL

0' - 250'
250' - 4000'
4000' - TD
TD

MUD TYPE

Air
Air/Mist & Aerated Water
Air/3% KCL water or KCL substitute
Gel/polyacrylamide polymer w/5-10% LCM

Sufficient mud inventory will be maintained on location during drilling to handle any adverse conditions that may arise.

6. VARIANCE REQUESTS:

- A. Petroglyph Operating Co., Inc. requests a variance to regulations requiring a straight run blooie line.
- B. Petroglyph Operating Co., Inc. requests a variance to regulations requiring an automatic ignitor or continuous pilot light on the blooie line.

7. EVALUATION PROGRAM:

Logs: Mud Logging
Compensated Density-Compensated Neutron Log
Dual Laterolog - Micro-SFL
Numar (Magnetic Resonance Imaging Log)

T.D. to base of surface csg.
T.D. to base of surface csg.
T.D. to base of surface csg.
@ Geologists discretion

Cores: None Programmed
DST: None Programmed

Completion: To be submitted at a later date.

8. ABNORMAL CONDITIONS:

None anticipated.

EIGHT POINT PLAN

UTE TRIBAL #07-05
SW/NW, SEC. 7, T5S R3W
DUCHESNE COUNTY, UTAH

9. STANDARD REQUIRED EQUIPMENT:

- A. Choke Manifold
- B. Kelly Cock
- C. Stabbing Valve
- D. Visual Mud Monitoring

10. HAZARDOUS CHEMICALS:

No chemicals subject to reporting under SARA title III in an amount equal to or greater than 10,000 pounds will be used, produced, stored, transported, or disposed of annually in association with the drilling of this well. Furthermore, no extremely hazardous substances, as defined in 40 CFR 355, in threshold planning quantities, will be used, produced, stored, transported, or disposed of in association with the drilling of this well.


(Attachment: BOP Schematic Diagram)

2000 PSIG DIAGRAM

BOTH RAMS ARE 2000 PSIG RATED.
CASING FLANGE IS 9" 2000 PSIG RATED.
BOPE 9" 2000 PSIG

TESTING PROCEDURE:

1. BOPE 's will be tested with a professional tester to conform to Onshore Order #2 with retest every 14 days.
2. Blind & Pipe rams will be tested to rated working pressure, 2000 psig
3. Casing will be tested to 0.22 psi/ft. or 1500 psig. Not to exceed 70% of burst strength, whichever is greater.
4. All lines subject to well pressure will be pressure tested to the same pressure as blind & pipe rams.
5. All BOPE specifications and configurations will meet Onshore Order #2 requirements for 2000 psig BOPE specifications.

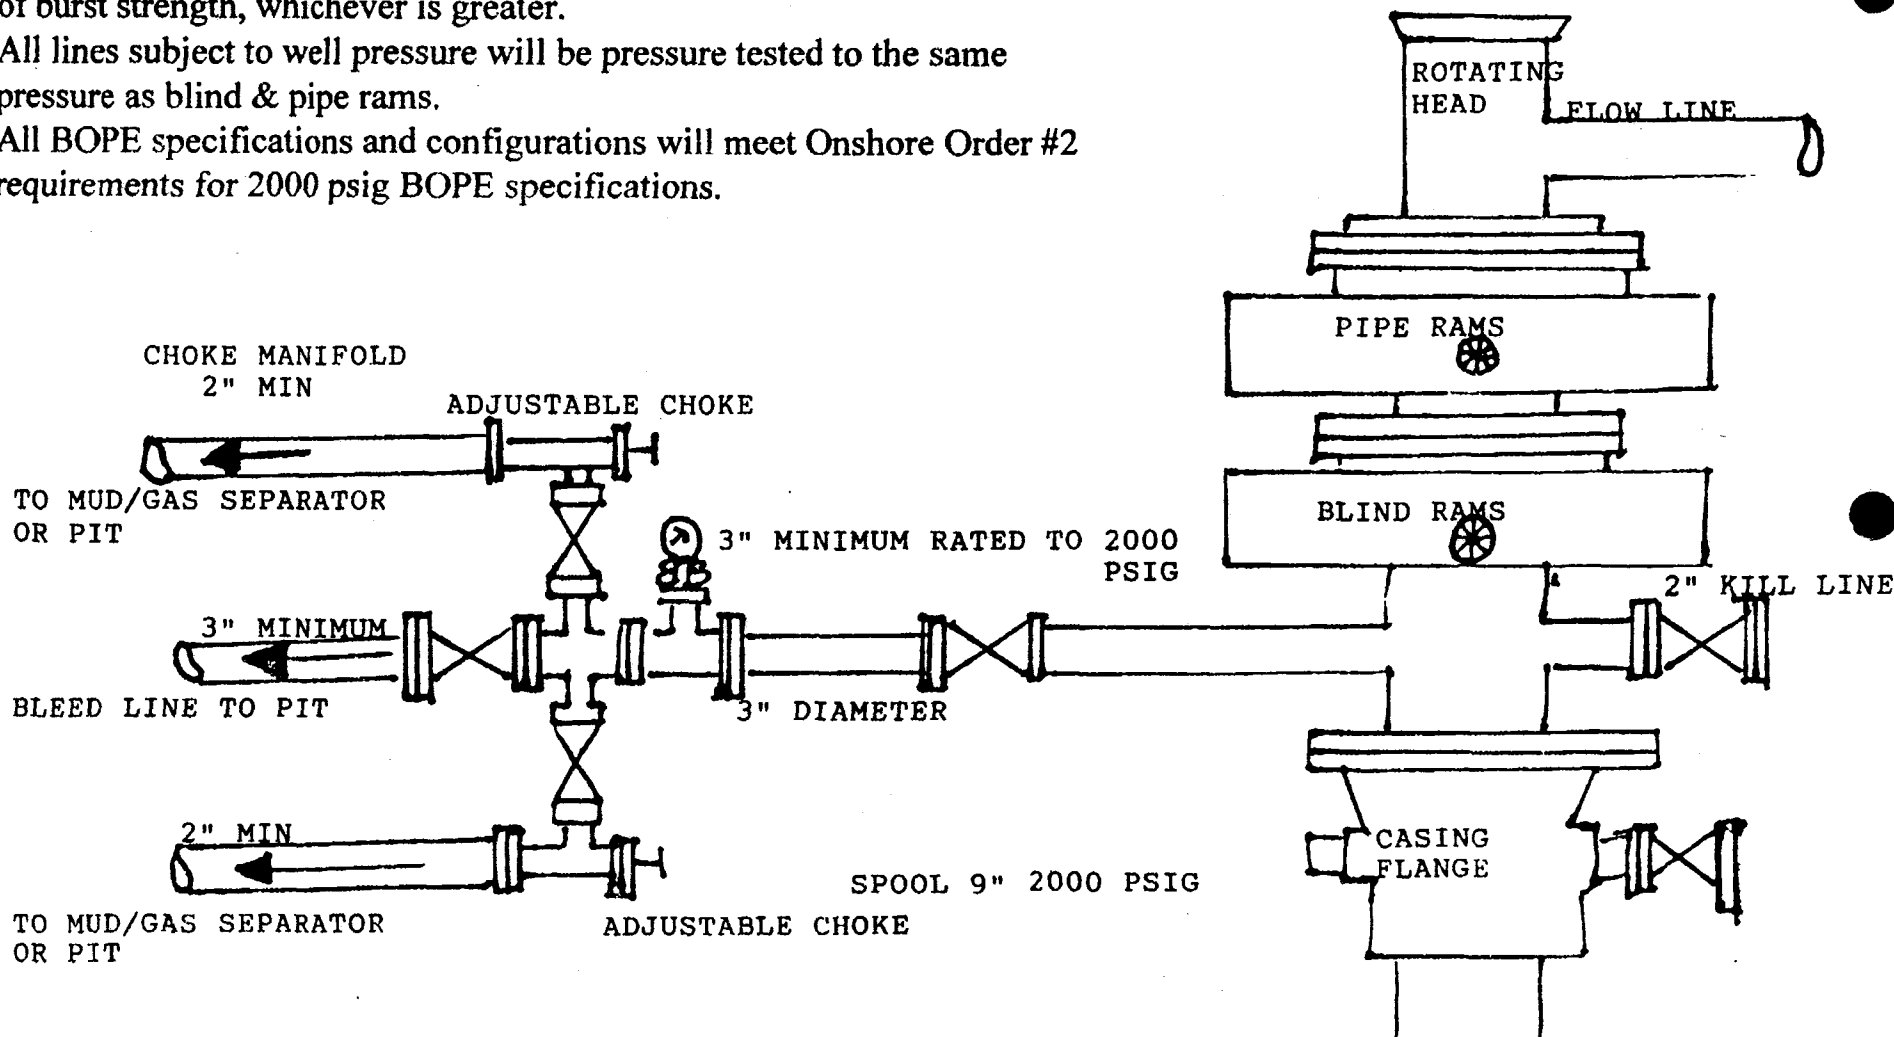

CONDITIONS OF APPROVAL
FOR THE SURFACE USE PROGRAM OF THE
APPLICATION FOR PERMIT TO DRILL

Company/Operator: Petroglyph Operating Co., Inc.
Well Name & Number: Ute Tribal #07-05
Lease Number: BIA 14-20-H62-3506
Location: 1818' FNL & 480' FWL, SW/NW, Sec. 7, T5S R3W
U.S.B.&M., Duchesne County, Utah
Surface Ownership: Ute Indian Tribe

NOTIFICATION REQUIREMENTS

Location Construction - forty-eight (48) hours prior to construction of location and access roads.

Location Completion - prior to moving on the drilling rig.

Spud Notice - at least twenty-four (24) hours prior to spudding the well.

Casing String and Cementing - twenty-four (24) hours prior to running casing and cementing all casing strings.

BOP and related Equipment Tests - twenty-four (24) hours prior to running casing and tests.

First Production Notice - within five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

For more specific details on notification requirements, please check the Conditions of Approval for Notice To Drill and Surface Use Program.

THIRTEEN POINT SURFACE USE PROGRAM

1. EXISTING ROADS

- A. See attached Wellsite Plats showing directional reference stakes on location, and attached TOPO Map "B" showing access to location from existing road.
- B. The proposed well site is located approximately 18.4 miles southwest of Myton, Utah - See attached TOPO Map "A".
- C. Refer to attached Topographic Map "A" showing labeled access route to location.
- D. Existing roads will be maintained and repaired as necessary. No off lease Right-of-Way will be required.

2. PLANNED ACCESS ROAD

- A. The access road will be approximately 0.1 miles in length. See attached TOPO Map "B".
- B. The access road has a 30 foot ROW w/18 foot running surface.
- C. Maximum grade on access road will be 8%
- D. No turnouts will be required.
- E. Road drainage crossings shall be of the typical dry creek drainage crossing type.
- F. No culverts, bridges or major cuts & fills will be required.
- G. The access road will be dirt surface.
- H. No gates, cattleguards or fences will be required or encountered.

New or reconstructed roads will be centerlined - flagged at time of location staking.

All travel will be confined to existing access road Right-of-Way.

Access roads and surface disturbing activities will conform to standards outlined in the Bureau of Land Management and Forest Service Publication: Surface Operating Standards For Oil & Gas Exploration and Development, (1989).

The road shall be upgraded to meet the standards of the anticipated traffic flow and all-weather road requirements. Upgrading shall include ditching, drainage, graveling, crowning, and capping the

roadbed as necessary to provide a well-constructed safe road.

Prior to upgrading, the road shall be cleared of any snow cover and allowed to dry completely. Traveling off the 30 foot Right-of- Way will not be allowed.

Road drainage crossings shall be of the typical dry creek drainage crossing type. Crossings shall be designed so they will not cause siltation or accumulation of debris in the drainage crossings nor shall the drainages be blocked by the roadbed. Erosion of drainage ditches by run off water shall be prevented by diverting water off at frequent intervals by means of cutouts. Upgrading shall not be allowed during muddy conditions. Should mud holes develop, they shall be filled in and detours around them avoided.

As operator, Petroglyph Operating Co., Inc. shall be responsible for all maintenance on cattleguards, or gates associated with this oil and/or gas operation.

3. LOCATION OF EXISTING WELLS WITHIN A ONE MILE RADIUS OF PROPOSED WELL LOCATION

- A. Water wells - None
- B. Abandoned wells - None
- C. Temporarily abandoned wells - None.
- D. Disposal wells - None.
- E. Drilling wells - None.
- F. Producing wells - 3*
- G. Shut in wells - 2*
- H. Injection wells - 1*

(*See attached TOPO map "C" for location)

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

A. ON WELL PAD

- 1. Tank batteries - None
- 2. Production facilities-To be submitted later
- 3. Oil gathering lines - None

4. Gas gathering lines-None
5. Injection lines - None
6. Disposal lines - None
7. Surface pits - None

B. OFF WELL PAD

1. Proposed location of attendant off pad flowlines shall be flagged prior to archaeological clearance.
2. A 4 1/2" OD steel above ground production pipeline will be laid approximately 570' from proposed location to a point in the NW/NW of Section 7, T5S, R3W, where it will tie into Petroglyph Operating Co., Inc.'s existing pipeline. Proposed pipeline crosses Ute Tribe lands, thus a Right-of-Way grant will be required. See attached TOPO Map D showing pipeline route.
3. Proposed pipeline will be a 4 1/2" OD steel, welded line laid on the surface.
4. Protective measures and devices for livestock and wildlife will be taken and/or installed where required.

If storage facilities/tank batteries are constructed on this lease, the facility/battery or the well pad shall be surrounded by a containment dike of sufficient capacity to contain, at a minimum, the entire contents of the largest tank within the facility/battery, unless more stringent protective requirements are deemed necessary by the authorized officer.

The production facilities will be placed on the West side of the location.

All permanent (on site for six months or longer) structures constructed or installed (including pumping units) will be painted a flat, non-reflective, earthtone color to match one of the standard environmental colors, as determined by the Rocky Mountain Five State Interagency Committee. All facilities required will be painted within 6 months of installation. Facilities required to comply with O.S.H.A.

(Occupational Safety and Health Act) will be excluded.
The required paint color is Desert Brown.

5. LOCATION & TYPE OF WATER SUPPLY

- A. Water supply will be from Target Trucking's Roosevelt Brine Storage and/or Target's water source in SE 1/4, Sec. 1, T 4S, R 5W Duchesne County, Utah (State water right #43-10152). All water will come from a non-depletable source.
- B. Water will be hauled by Target Trucking.
- C. No water well will be drilled on lease.

6. SOURCE OF CONSTRUCTION MATERIAL

- A. All construction material for this location and access road will be of native borrow and soil accumulated during the construction of location.
- B. All construction material will come from Ute Tribal Land.
- C. No mineral materials will be required.

7. METHODS OF HANDLING WASTE DISPOSAL

A. METHODS AND LOCATION

- 1. Cuttings will be confined in the reserve pit.
- 2. A portable toilet will be provided for human waste during the drilling and completion of the well. Disposal will be at the Vernal sewage disposal plant.
- 3. Burning will not be allowed. Trash and other waste material will be contained in a wire mesh cage and disposed of at an approved waste disposal facility.
- 4. Produced waste water will be confined to a lined pit or storage tank for a period not to exceed 90 days after initial production. During the 90 day period, an application for approval of a permanent disposal method and location, together with the required water analysis, will be submitted for the AO's approval.

5. All chemicals will be disposed of at an authorized disposal site. Drip pans and absorbent pads will be used on drilling rig to avoid leakage of oil to pit.

B. Water from drilling fluids and recovered during testing operations will be disposed of by either evaporating in reserve pit or be removed and disposed of at an authorized disposal site. Introduction of well bore hydrocarbons to reserve pit will be avoided by flaring them off in flare pit at time of recovery.

Burning of trash will not be allowed. All trash must be contained in a trash cage and hauled away to an approved disposal site at the completion of the drilling activities.

On BIA administered land:

All reserve pits will be lined with either native clay, commercial bentonite or plastic sufficient to prevent seepage. (If a plastic nylon reinforced liner is used, it shall be torn and perforated after the pit dries and before backfilling of the reserve pit).

A 12 mill liner shall be installed in the reserve pit.

To protect the environment:

If the reserve pit is lined the operator will provide the BIA with a chemical analysis of the fluids in that pit no later than 90 days after the well completion to determine the method for final reclamation of the reserve pit. If the elemental concentrations shown by the chemical analysis exceeds the requirements described by part II, Standards of Quality for Waters of the State, Wastewater Disposal Regulations, State of Utah Division of Health, the contents and liner will be removed and disposed of at an authorized disposal site.

To protect the environment (without a chemical analysis)
reserve pits will be constructed so as not to leak, break, or allow discharge of liquids.

Storage tanks will be used if drill sites are located on tribal

irrigable land, flood plains, or on lands under crop production. After first production, produced waste water will be confined to a lined pit or storage tank for a period not to exceed ninety (90) days. During the 90 day period, in accordance with NTL-2B, an application for approval of a permanent disposal method and location, along with required water analysis, shall be submitted for the AO's approval. Failure to file an application within the time allowed will be considered an incident of noncompliance.

8. ANCILLARY FACILITIES

- A. No airstrips or camps are planned for this well.

9. WELL SITE LAYOUT

- A. Refer to attached well site plat for related topography cuts and fills & cross sections.
- B. Refer to attached well site plat for rig layout and soil material stockpile location as approved on On-site.
- C. Refer to attached well site plat for rig orientation parking areas, and access road.

The reserve pit will be located on the Southeast side of the location.

The flare pit will be located downwind of the prevailing wind direction on the Southeast side of the location, a minimum of 100 feet from the well head and 30 feet from the reserve pit fence.

The stockpiled topsoil will be stored on the Southeast corner.

Access to the well pad will be from the North.

X A diversion ditch will be constructed on the North side of the access road at the junction of the access road to Ute Tribal #07-04 to divert the drainage to the North.

X A soil compacted berm with rip-rap will be constructed on the Southwest corner to divert the drainage around the location on the West side.

N/A The drainage(s) shall be diverted around the sides of the well pad location.

N/A The reserve pit and/or pad locations shall be constructed long and narrow for topographic reasons _____

X Corners No. 2, 6, & 8 will be rounded off to minimize excavation.

FENCING REQUIREMENTS

All pits will be fenced according to the following minimum standards:

- A. 39 inch net wire shall be used with at least one strand of barbed wire on top of the net wire. (barbed wire is not necessary if pipe or some type of reinforcement rod is attached to the top of the entire fence).
- B. The net wire shall be no more than 2 inches above the ground. The barbed wire strand shall be 3 inches above the net wire. Total height of the fence shall be at least 42 inches.
- C. Corner posts shall be cemented and/or braced in such a manner to keep the fence tight at all times.
- D. Standard steel, wood, or pipe posts shall be used between the corner braces. Maximum distance between any two posts shall be no greater than 16'.
- E. All wire shall be stretched by using a stretching device before it is attached to the corner posts.

The reserve pit fencing will be on the three sides during drilling operations and on the fourth side when the rig moves off the location. Pits will be fenced and maintained until clean-up.

Each existing fence to be crossed by the access road shall be braced and tied off before cutting so as to prevent slacking of the wire. The opening shall be closed temporarily as necessary during construction to prevent the escape of livestock, and upon completion of construction the fence shall be repaired to BIA or SMA specifications. A cattleguard with an adjacent 16 foot gate shall be installed in any fence where a road is to be regularly travelled. If the well is a producer, the cattleguards (shall/ shall not) be permanently mounted on concrete bases. Prior to a new road, crossing any fence located on federal land, or any fence between federal land and private land, the operator will contact the BIA, who will in turn contact the grazing permittee or owner of said fence and offer him/her the opportunity to be present when the fence is cut in order to

satisfy himself/herself that the fence is adequately braced and tied off.

10. PLANS FOR RESTORATION OF SURFACE

A. PRODUCING LOCATION

Immediately upon well completion, the location and surrounding area will be cleared of all unused tubing, equipment, debris, materials, trash, and junk not required for production.

Immediately upon well completion, any hydrocarbons on the pit shall be removed in accordance with CFR 3162.7-1.

If a plastic nylon reinforced liner is used, it shall be torn and perforated before backfilling of the reserve pit.

The reserve pit and that portion of the location not needed for production facilities/operations will be recontoured to the approximate natural contours. The reserve pit will be reclaimed within 120 days from the date of well completion (weather permitting). Before any dirt work takes place, the reserve pit will be completely dry and all cans, barrels, pipe, fluid, and hydrocarbons, will be removed.

Contact appropriate surface management agency for required seed mixture.

B. DRY HOLE/ABANDONED LOCATION

At such time as the well is plugged and abandoned, the operator will submit a subsequent report of abandonment and BIA will attach the appropriate surface rehabilitation conditions of approval.

ON BIA Administered lands:

Abandoned well sites, roads, or other disturbed areas will be restored to near their original condition. This procedure will include: (a) reestablishing irrigation systems where applicable, (b) reestablishing soil conditions in irrigated fields in such a way as to ensure cultivation and harvesting of crops and, (c) ensuring revegetation of the disturbed areas to the specifications of the Ute Indian Tribe or the BIA at the time of abandonment.

11. SURFACE OWNERSHIP

Access road: Ute Indian Tribe

Location: Ute Indian Tribe

12. OTHER INFORMATION

- A. Petroglyph Operating Co., Inc. will inform all persons in the area who are associated with this project that they are subject to prosecution for knowingly disturbing historic or archaeological sites, or for collecting artifacts. If historic or archaeological materials are uncovered during construction, the operator will immediately stop work that might further disturb such materials, and contact the AO. Within five working days the AO will inform the operator as to:
- whether the materials appear eligible for the National Register of historic Places;

the mitigation measures the operator will likely have to undertake before the site can be used.

-a time frame for the AO to complete an expedited review under 36 CFR 800.11 to confirm, through the State Historic Preservation Officer, that the findings of the AO are correct and that mitigation is appropriate.

If the operator wished, at any time, to relocate activities to avoid the expense of mitigation and/or the delays associated with this process, the AO will assume responsibility for whatever recordation and stabilization of the exposed materials that may be required. Otherwise, the operator will be responsible for mitigation costs. The AO will provide technical and procedural guidelines for the conduct of mitigation. Upon verification from the AO that required mitigation has been completed, the operator will then be allowed to resume construction.

- B. As operator, Petroglyph Operating Co., Inc. will control noxious weeds along Right-of-Ways for roads, pipelines, well sites, or other applicable facilities. A list of noxious weeds will be obtained from the BIA,

or the appropriate County Extension Office. On BIA administered land, a Pesticide Use proposal shall be submitted, and given approval, prior to the application of herbicides or other pesticides or possible hazardous chemicals.

- C. Drilling rigs and/or equipment used during drilling operations on this well site will not be stacked or stored on Tribal Lands after the conclusion of drilling operations or at any other time without BIA authorization. However, if BIA authorization is obtained, it is only a temporary measure to allow time to make arrangements for permanent storage on commercial facilities.

On BIA administered land:

Operator's employees, including subcontractors, will not gather firewood along roads constructed by operators. If wood cutting is required, a permit will be obtained from the Forestry Department of the BIA pursuant to 25 CFR 169.13 "Assessed Damages Incident to Right-of-Way authorization". All operators, subcontractors, vendors, and their employees or agents may not disturb saleable timber (including firewood) without a duly granted wood permit from the BIA Forester.

If the surface rights are owned by the Ute Indian Tribe and mineral rights are owned by another entity, an approved right-of-way will be obtained from the BIA before the operator begins any construction activities. If the surface is owned by another entity and the mineral rights are owned by the Ute Indian Tribe, rights-of-way will be obtained from the other entity.

All roads constructed by operators on the Uintah and Ouray Indian Reservation will have appropriate signs. Signs will be neat and of sound construction. They will state: (a) that the land is owned by the Ute Indian Tribe, (b) the name of the operator, (c) that firearms are prohibited to all non-Ute Tribal members (d) that permits must be obtained from the BIA before cutting firewood or other timber products, and (e) only authorized personnel permitted. All well site locations on the Uintah and Ouray Indian Reservation will have an appropriate sign indicating the name of the operator,

the lease serial number, the well name and number, the survey description of the well (either footage or the quarter-quarter section, the section, township, and range).

Additional Surface Stipulations

N/A No construction or drilling activities shall be conducted between

_____ and _____ because of _____

N/A No surface occupancy will be allowed within 1,000 feet of any sage grouse strutting ground.

N/A No construction or exploration activities are permitted within 1.5 mile radius of sage grouse strutting grounds from April 1 to June 30.

N/A There shall be no surface disturbance within 600 feet of live water (includes stock tanks, springs, and guzzlers).

N/A No cottonwood trees will be removed or damaged.

N/A Pond will be constructed according to BLM specifications approximately _____ ft. _____ of the location, as flagged on onsite.

LESSEE'S OR OPERATOR'S REPRESENTATIVE AND CERTIFICATION

PERMITTING

Ed Trotter

1620 West 750 North

Vernal UT 84078

Telephone # (801)789-4120

Fax # (801) 789-1420

OPERATIONS

Vince Guinn

P.O. Box 607

Roosevelt, UT 84066

(801) 722-2531

Fax # (801) 722-9145

All lease/or unit operations will be conducted in such a manner that full compliance is made with all applicable laws, regulations, Onshore Oil and Gas Orders, the approval plan of operations, and any applicable Notice to Lessees. Petroglyph Operating Co., Inc. is fully responsible for the actions of their subcontractors. A copy of these conditions will be furnished to the field representative to insure compliance.

A copy of the approved APD and ROW grant, if applicable, shall be on location during construction of the location and drilling activities.

The BIA Office shall be notified upon site completion prior to moving on the drilling rig.

Certification:

I hereby certify that I, or persons under my direct supervision, have inspected the proposed drillsite and access route; that I am familiar with the conditions which presently exist; that the statements made in the Plan are to the best of my knowledge, true and correct; and that the work associated with the operations proposed herein will be performed by Petroglyph Operating Co., Inc. and its contractors and sub-contractors in conformity with this Plan and the terms and conditions under which it is approved.

10-23-97



Date



PETROGLYPH OPERATING CO., INC.

LOCATION LAYOUT FOR

UTE TRIBAL #07-05
SECTION 7, T5S, R3W, U.S.B.&M.
1818' FNL 480' FWL

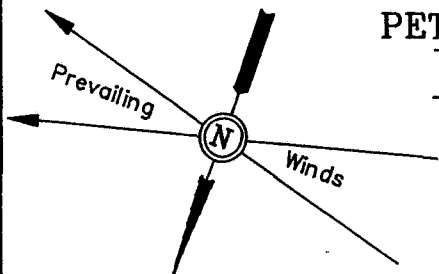

SCALE: 1" = 50'
DATE: 9-8-97
Drawn By: C.B.T.

NOTE:

Flare Pit is to be located a min. of 100' from the Well Head.

FLARE PIT




NOTE:
Pit Capacity W/2' of Freeboard is $\pm 4,600$ Bbls.

Approx. Top of Cut Slope

El. 46.5'
C-15.7'
(btm. pit)

C-1.9'
El. 40.7'



El. 36.2'
C-5.4'
(btm. pit)

El. 35.6'
F-3.2'

Reserve Pit Backfill & Spoils Stockpile

El. 33.6'
F-5.2'

F-6.7'
El. 32.1'

C-5.4'
El. 44.2'

Sta. 2+90

C-1.5'
El. 40.3'

Approx. Toe of Fill Slope

Sta. 0+00

F-9.1'
El. 29.7'

Proposed Access Road

Elev. Ungraded Ground at Location Stake = 5840.1'



Elev. Graded Ground at Location Stake = 5838.8'

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East • Vernal, Utah 84078 • (801) 789-1017





PETROGLYPH OPERATING CO., INC.

TYPICAL CROSS SECTIONS FOR

UTE TRIBAL #07-05
SECTION 7, T5S, R3W, U.S.B.&M.
1818' FNL 480' FWL



DATE: 9-8-97
Drawn By: C.B.T.

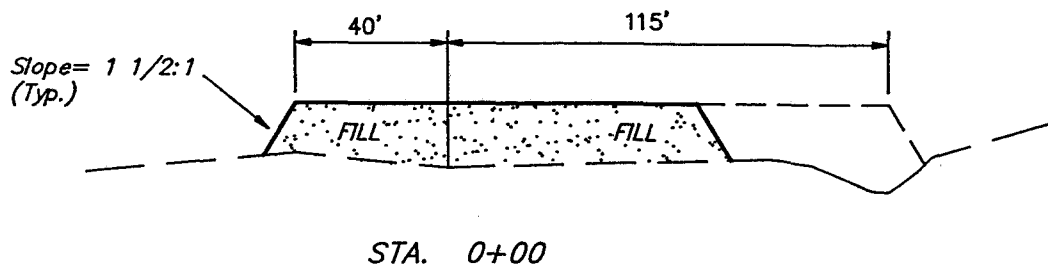

APPROXIMATE YARDAGES

(12") Topsoil Stripping	= 1,910 Cu. Yds.
Remaining Location	= 4,580 Cu. Yds.
TOTAL CUT	= 6,490 CU.YDS.
FILL	= 3,680 CU.YDS.

EXCESS MATERIAL AFTER 5% COMPACTION	= 2,620 Cu. Yds.
Topsoil & Pit Backfill (1/2 Pit Vol.)	= 2,610 Cu. Yds.
EXCESS UNBALANCE (After Rehabilitation)	= 10 Cu. Yds.

UINTAH ENGINEERING & LAND SURVEYING
85 So. 200 East • Vernal, Utah 84078 • (801) 789-1017

LEGEND:

⊙ PROPOSED LOCATION



Utah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(801) 789-1017 * FAX (801) 789-1018
Email: uels@easilink.com



PETROGLYPH OPERATING CO., INC.


**UTE TRIBAL #07-05
SECTION 7, T5S, R3W, U.S.B.&M.
1818' FNL 480' FWL**

**TOPOGRAPHIC
MAP**

8	27	97
MONTH	DAY	YEAR

SCALE: 1 : 100,000 DRAWN BY: D.COX REVISED: 00-00-00

A
TOPO

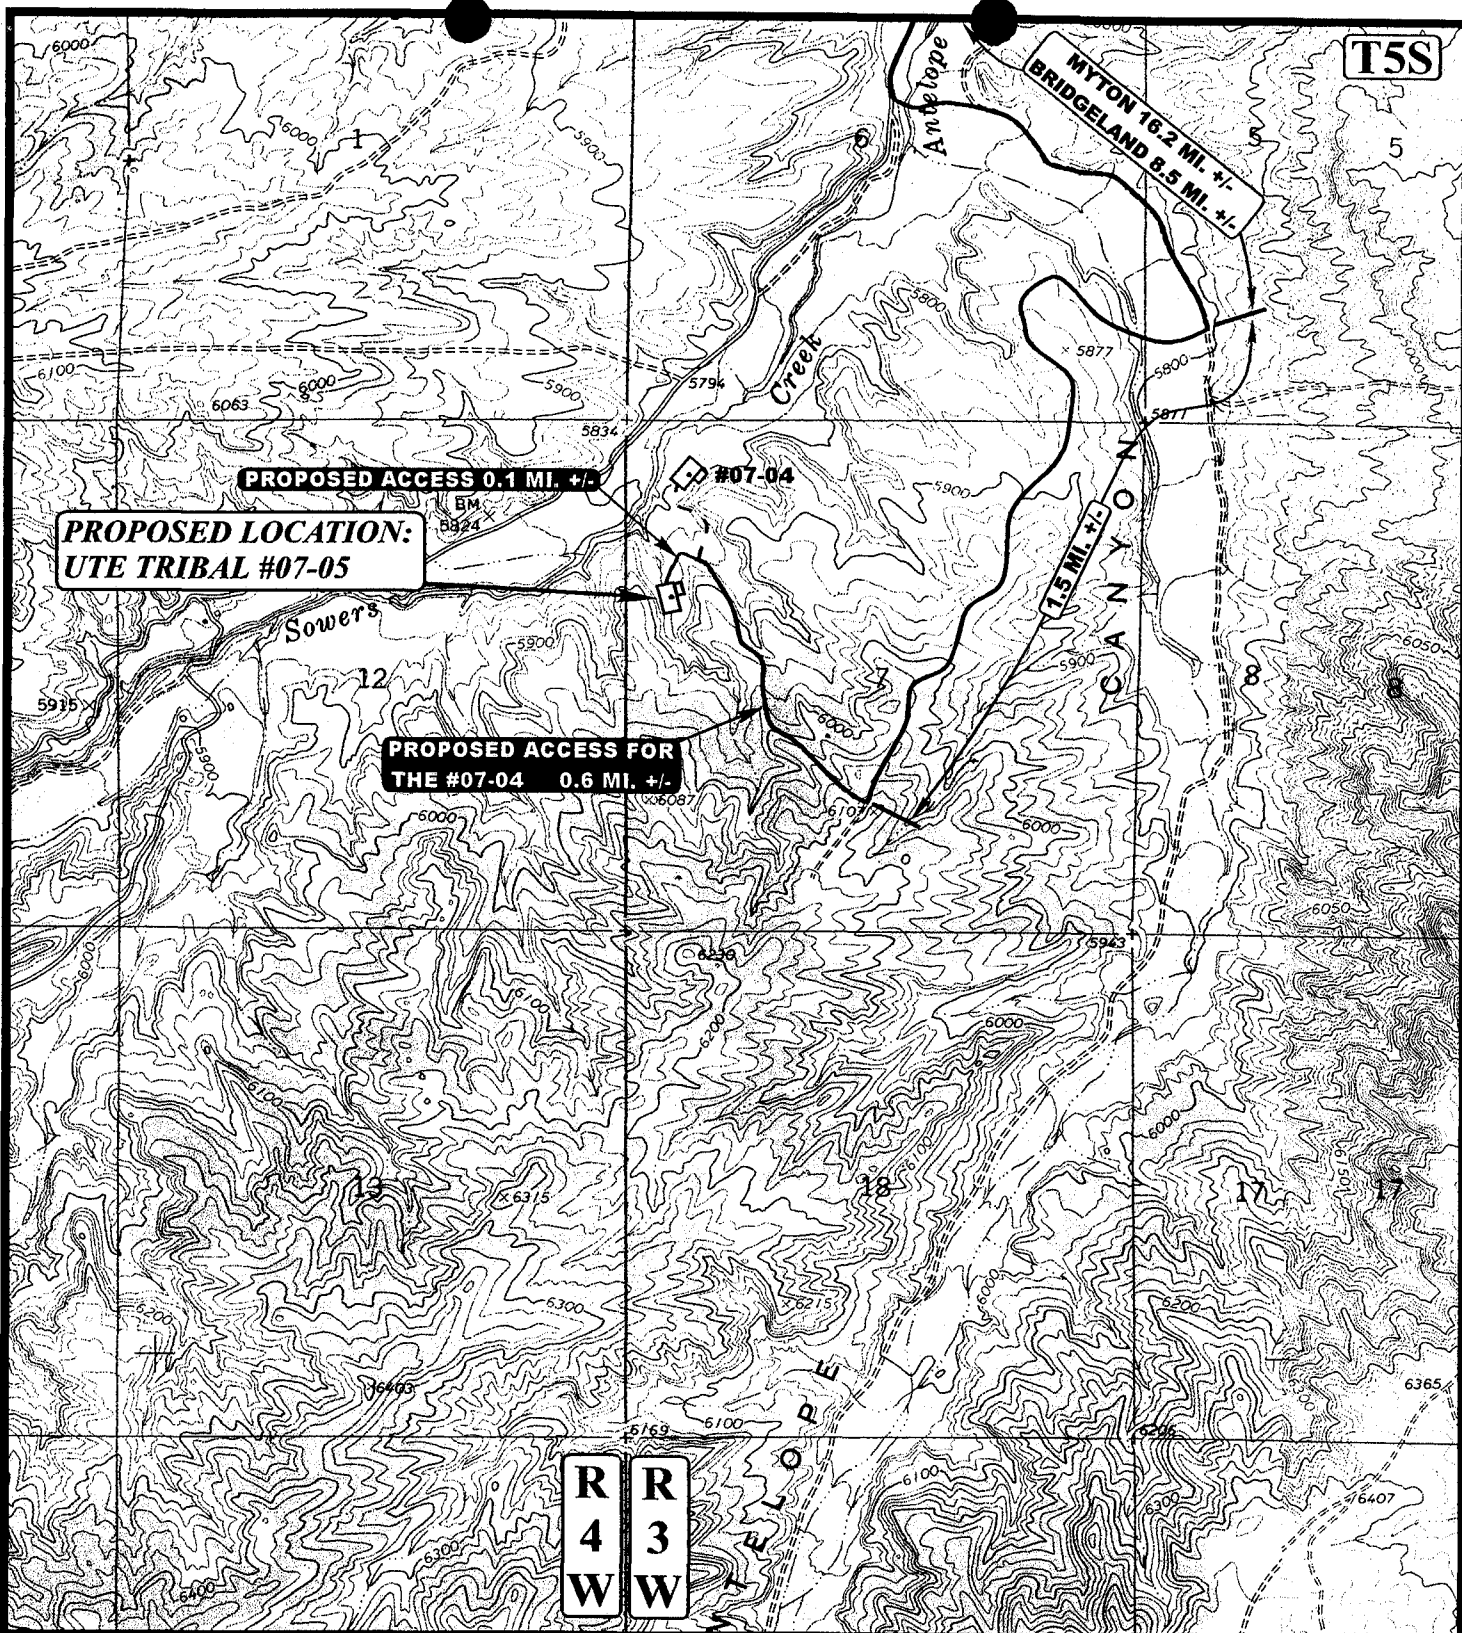

LEGEND:

--- PROPOSED ACCESS ROAD
— EXISTING ROAD

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #07-05
SECTION 7, T5S, R3W, U.S.B.&M.
1818' FNL 480' FWL



Uintah Engineering & Land Surveying
85 South 200 East Vernal, Utah 84078
(801) 789-1017 * FAX (801) 789-1018
Email: uels@easilink.com




TOPOGRAPHIC
MAP

8 **26** **97**
MONTH DAY YEAR

SCALE: 1" = 2000' DRAWN BY: D.COX REVISED: 9-25-97

B
TOPO

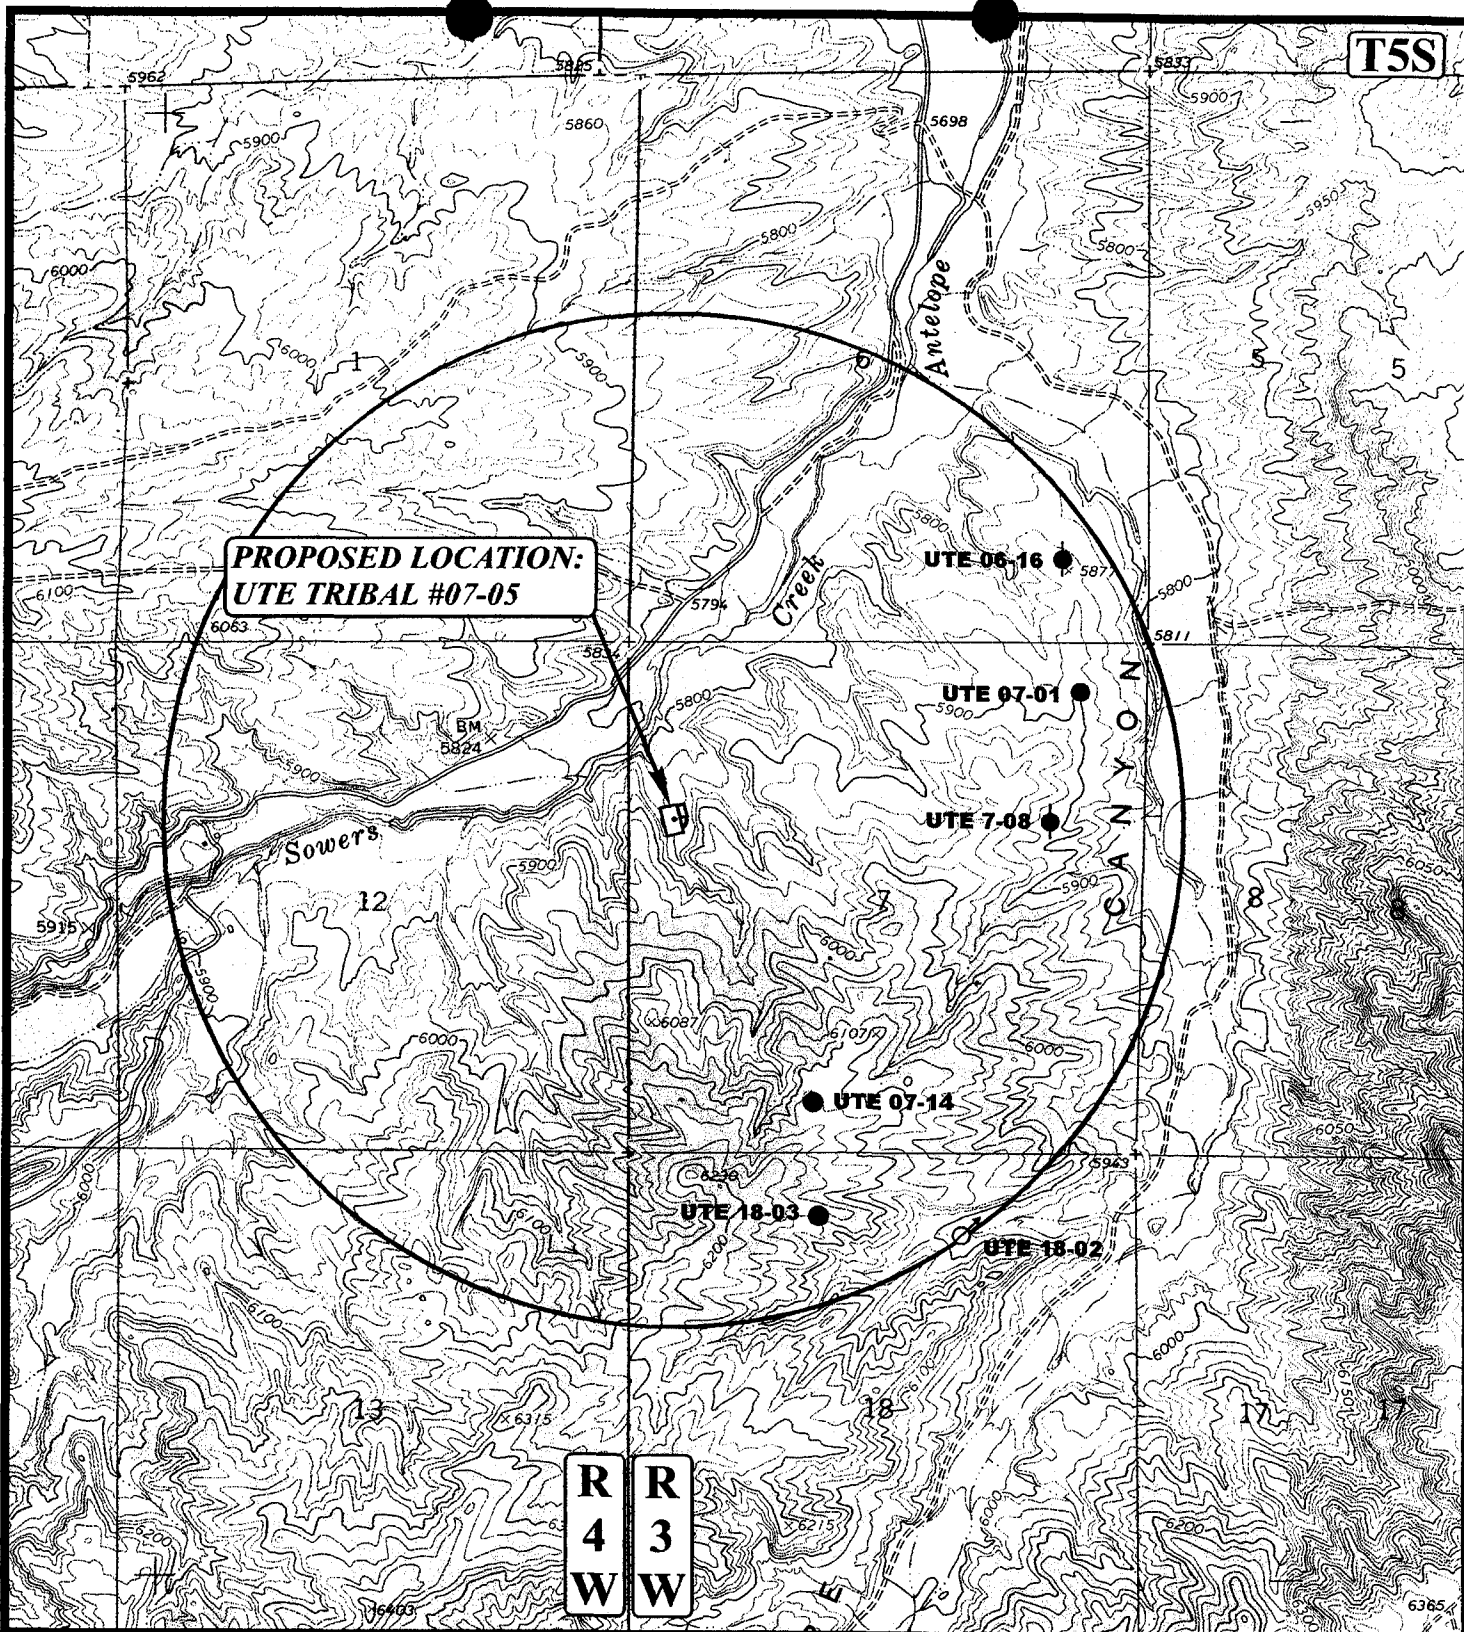

LEGEND:

- ⊗ DISPOSAL WELLS
- PRODUCING WELLS
- ⬮ SHUT IN WELLS
- ⊗ WATER WELLS
- ⬮ ABANDONED WELLS
- ⬮ TEMPORARILY ABANDONED

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #07-05
SECTION 7, T5S, R3W, U.S.B.&M.
1818' FNL 480' FWL



Uintah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 (801) 789-1017 * FAX (801) 789-1018
 Email: uels@easilink.com




TOPOGRAPHIC
MAP

8 **27** **97**
 MONTH DAY YEAR

SCALE: 1" = 2000' DRAWN BY: D.COX REVISED: 00-00-00



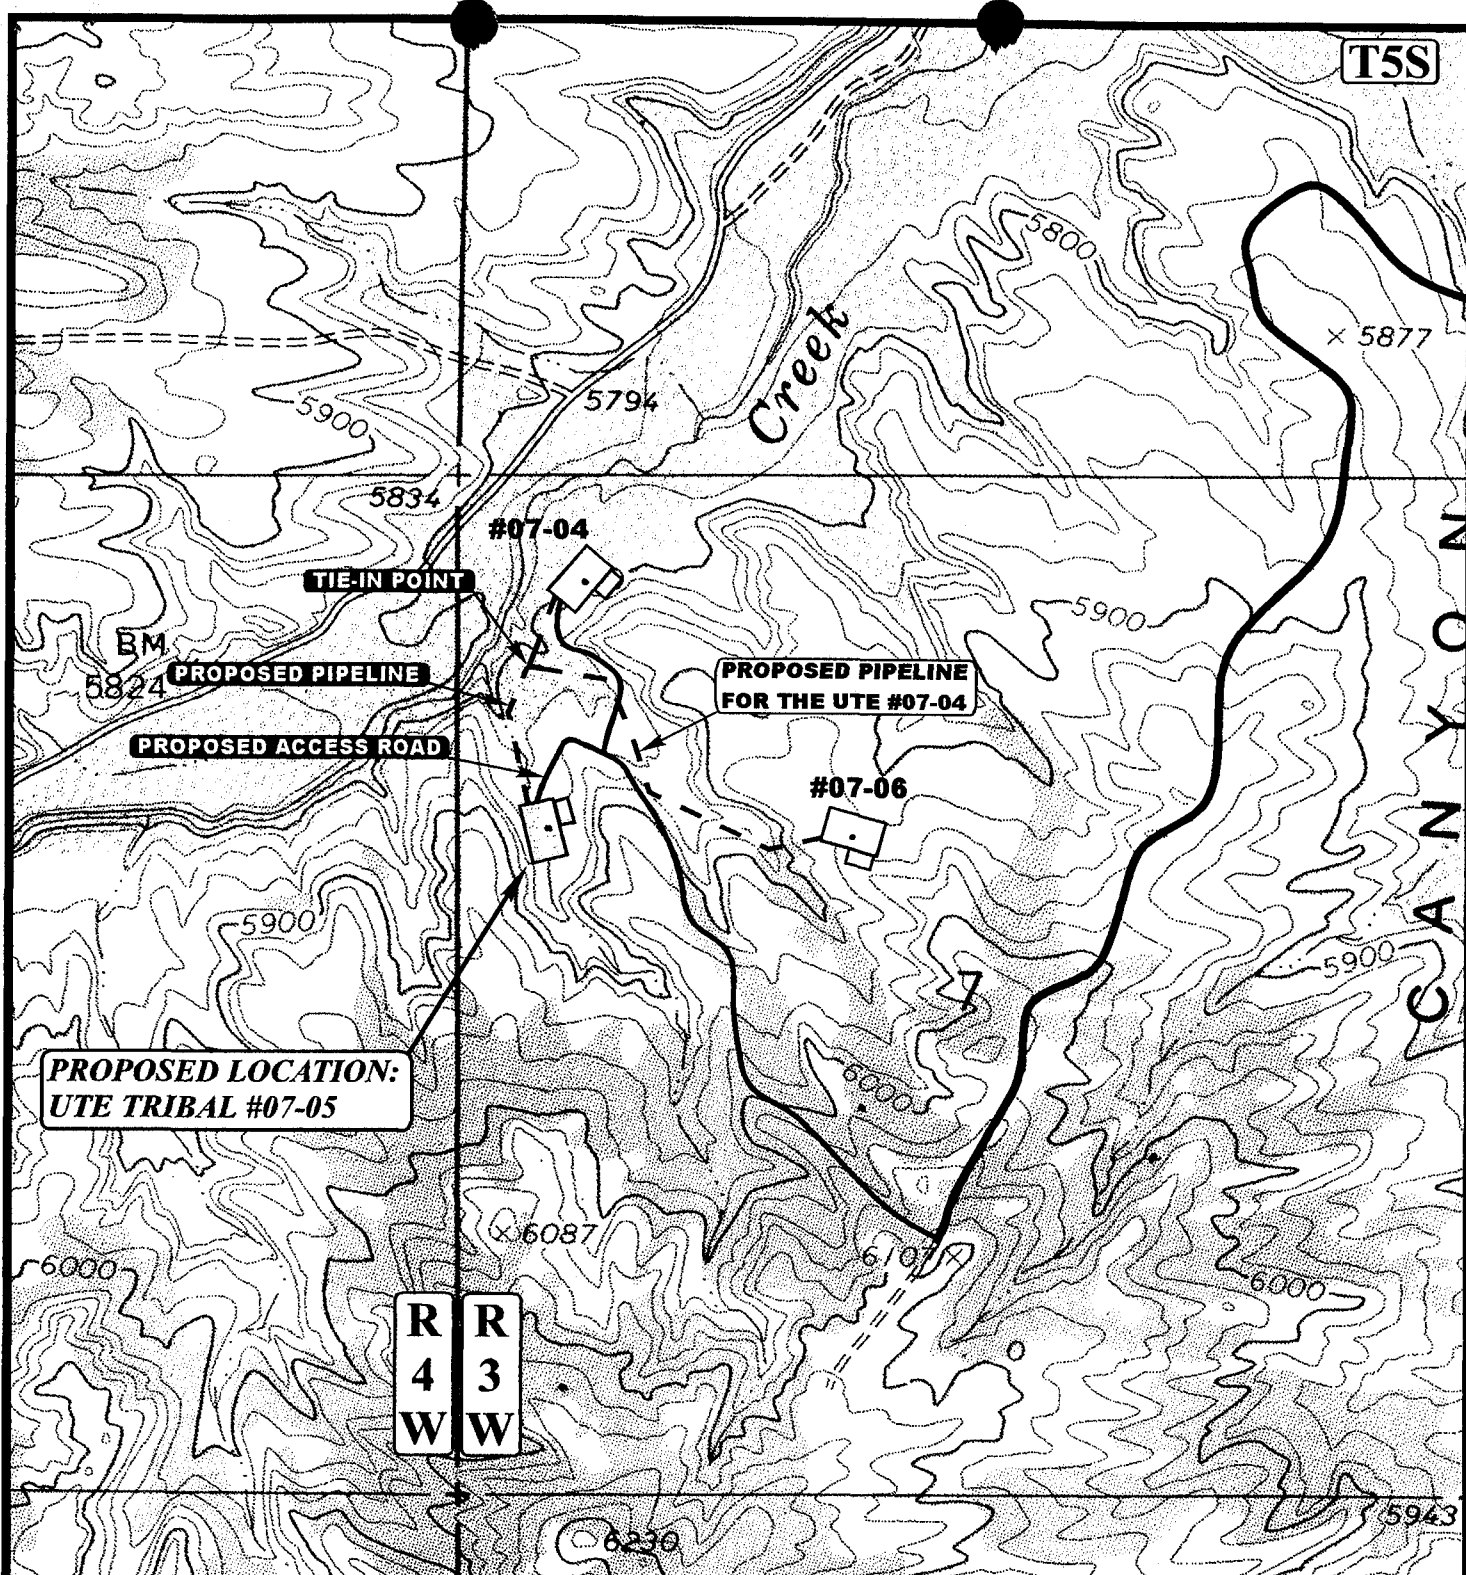

APPROXIMATE TOTAL PIPELINE DISTANCE = 570' +/-

LEGEND:

- — — — — EXISTING PIPELINE
- - - - - PROPOSED PIPELINE
- — — — — PROPOSED ACCESS

PETROGLYPH OPERATING CO., INC.

UTE TRIBAL #07-05
SECTION 7, T5S, R3W, U.S.B.&M.
1818' FNL 480' FWL



Uintah Engineering & Land Surveying
 85 South 200 East Vernal, Utah 84078
 (801) 789-1017 * FAX (801) 789-1813
 Email: uels@easilink.com



TOPOGRAPHIC
MAP

8 **27** **97**
 MONTH DAY YEAR

SCALE: 1" = 1000' DRAWN BY: D.COX REVISED: 9-25-97

D
TOPO

WORKSHEET
APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 10/30/97

API NO. ASSIGNED: 43-013-31977

WELL NAME: UTE TRIBAL 07-05
OPERATOR: PETROGLYPH OPERATING (N3800)

PROPOSED LOCATION:

SWNW 07 - T05S - R03W
SURFACE: 1818-FNL-0480-FWL
BOTTOM: 1818-FNL-0480-FWL
DUCHESNE COUNTY
ANTELOPE CREEK FIELD (060)

LEASE TYPE: IND
LEASE NUMBER: 14-20-H62-3506

PROPOSED PRODUCING FORMATION: GRRV

INSPECT LOCATION BY: / /

TECH REVIEW	Initials	Date
Engineering		
Geology		
Surface		

RECEIVED AND/OR REVIEWED:


☒ Plat
☒ Bond: Federal ☒ State[] Fee[]
(Number 4556)
☒ Potash (Y/N)
☒ Oil shale (Y/N)
☒ Water permit
(Number 43-10152)
☒ RDCC Review (Y/N)
(Date: _____)

LOCATION AND SITING:

____ R649-2-3. Unit: _____
☒ R649-3-2. General.
____ R649-3-3. Exception.
____ Drilling Unit.
____ Board Cause no: _____
____ Date: _____

COMMENTS:

STIPULATIONS:




DIVISION OF OIL, GAS & MINING

OPERATOR: PETROGLYPH OPERATING (N3800)

FIELD: ANTELOPE CREEK (060)

SEC. TWP, RNG: SEC. 7 & 20, T5S, R3W

COUNTY: DUCHESNE UAC: R649-3-2 & R649-3-3

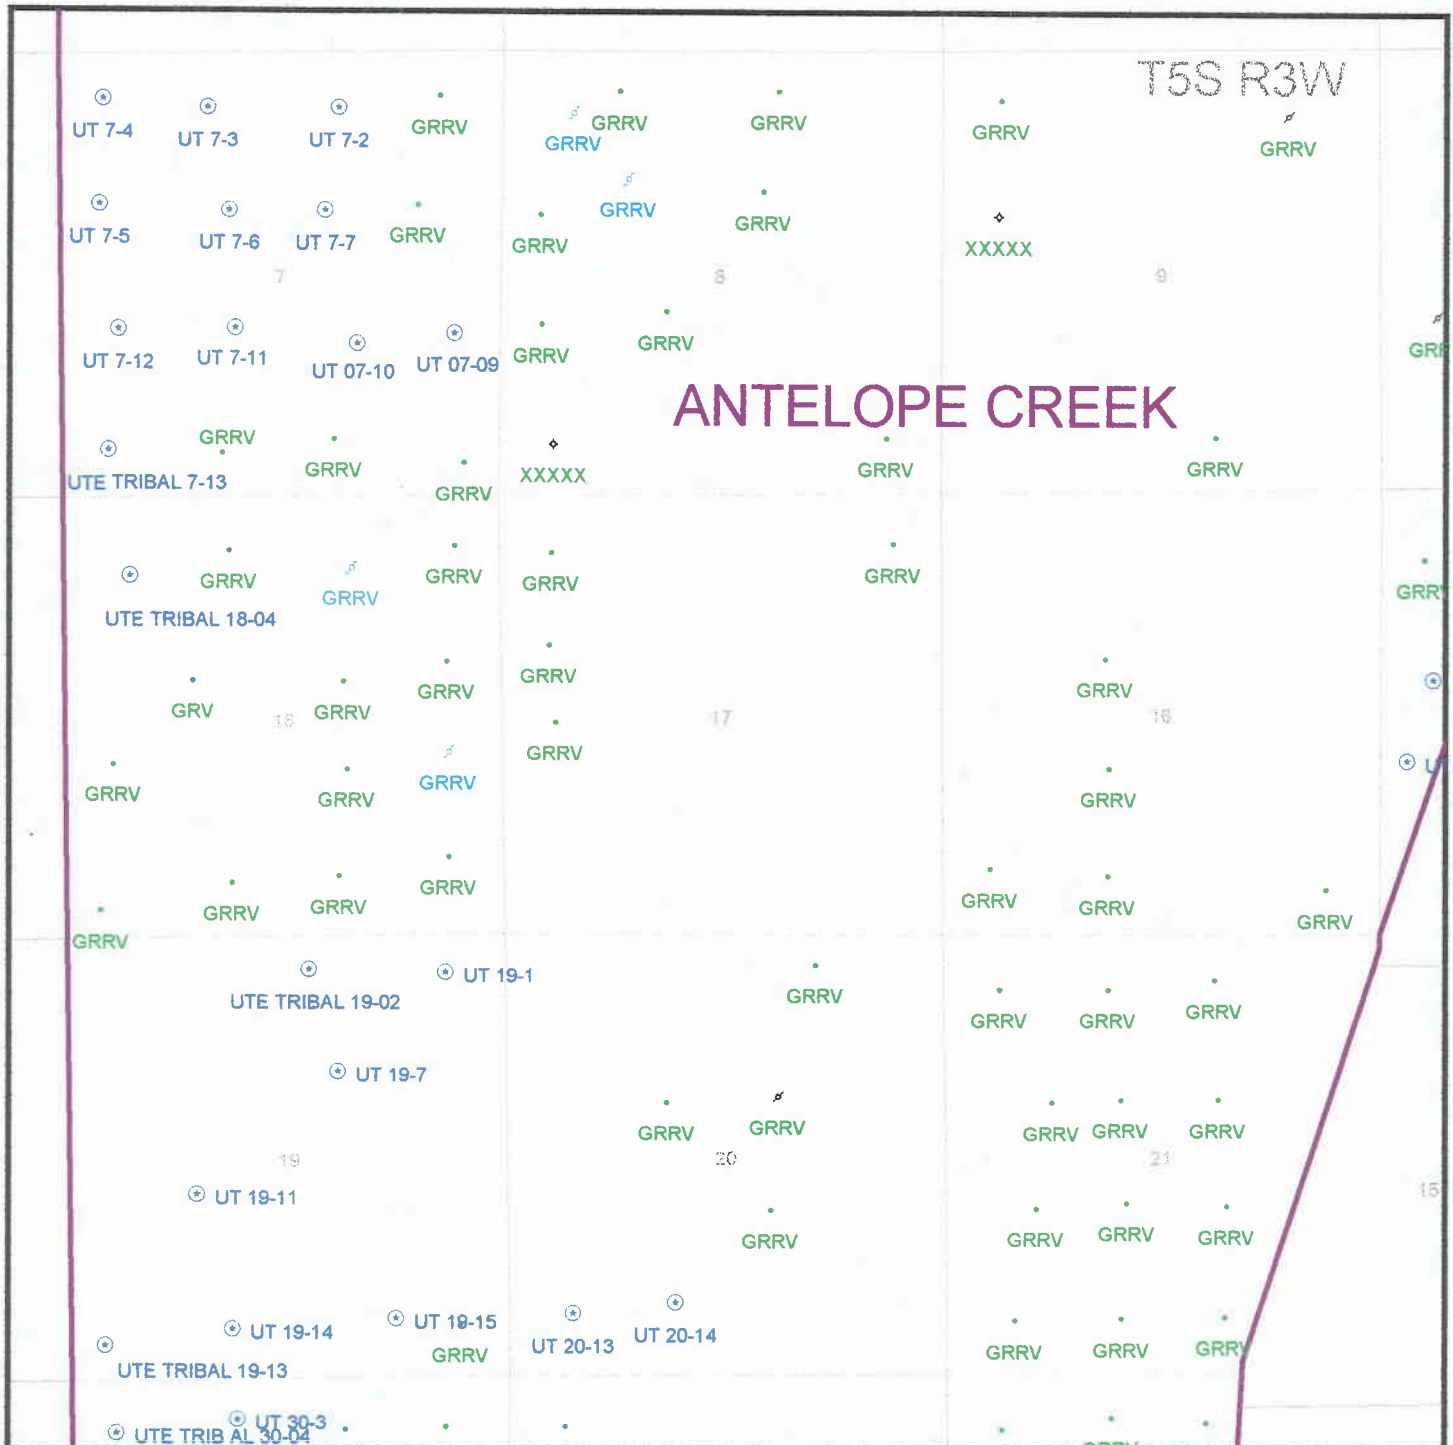

DATE PREPARED:
31-OCT-1997



State of Utah
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

Michael O. Leavitt
Governor

Ted Stewart
Executive Director

Lowell P. Braxton
Division Director

1594 West North Temple, Suite 1210
PO Box 145801
Salt Lake City, Utah 84114-5801
801-538-5340
801-359-3940 (Fax)
801-538-7223 (TDD)

February 11, 1998

Petroglyph Operating Company
P.O. Box 607
Roosevelt, Utah 84066


Re: Ute Tribal 07-05 Well, 1818' FNL, 480' FWL, SW NW, Sec. 7,
T. 5 S., R. 3 W., Duchesne County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. 40-6-1 et seq., Utah Administrative Code R649-3-1 et seq., and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-013-31977.

Sincerely,



John R. Baza
Associate Director

lwp

Enclosures

cc: Duchesne County Assessor
Bureau of Land Management, Vernal District Office

Operator: Petroglyph Operating Company
Well Name & Number: Ute Tribal 07-05
API Number: 43-013-31977
Lease: 14-20-H62-3506
Location: SW NW Sec. 7 T. 5 S. R. 3 W.

Conditions of Approval

1. General

Compliance with the requirements of Utah Admin. R. 649-1 et seq., the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for Permit to Drill.

2. Notification Requirements

Notify the Division within 24 hours following spudding the well or commencing drilling operations. Contact Jim Thompson at (801)538-5336.

Notify the Division prior to commencing operations to plug and abandon the well. Contact John R. Baza (801)538-5334.

3. Reporting Requirements

All required reports, forms and submittals shall be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR DEEPEN

1a. TYPE OF WORK

DRILL ☒DEEPEN ☐

b. TYPE OF WELL

OIL
WELL ☒GAS
WELL ☐

OTHER

SINGLE
ZONE ☐MULTIPLE
ZONE ☐

2. NAME OF OPERATOR

PETROGLYPH OPERATING COMPANY, INC.

3. ADDRESS AND TELEPHONE NO.

P.O. BOX 607, ROOSEVELT, UTAH 84066

4. LOCATION OF WELL (Report location clearly and in accordance with any State requirements.)*

At surface

1818' FNL & 480' FWL SW/NW

At proposed prod. zone

14. DISTANCE IN MILES AND DIRECTION FROM NEAREST TOWN OR POST OFFICE*

18.4 MILES SOUTHWEST OF MYTON, UTAH

15. DISTANCE FROM PROPOSED*

LOCATION TO NEAREST
PROPERTY OR LEASE LINE, FT.
(Also to nearest drig. unit line, if any)

480' ±

18. DISTANCE FROM PROPOSED LOCATION*
TO NEAREST WELL, DRILLING, COMPLETED,
OR APPLIED FOR, ON THIS LEASE, FT.

16. NO. OF ACRES IN LEASE

640

19. PROPOSED DEPTH

5808.8'

17. NO. OF ACRES ASSIGNED
TO THIS WELL

80

20. ROTARY OR CABLE TOOLS
ROTARY

21. ELEVATIONS (Show whether DF, RT, GR, etc.)

5838.8' GRADED GROUND

22. APPROX. DATE WORK WILL START*

OCTOBER 1997

23. PROPOSED CASING AND CEMENTING PROGRAM

SIZE OF HOLE	GRADE SIZE OF CASING	WEIGHT PER FOOT	SETTING DEPTH	QUANTITY OF CEMENT
12 1/4	8 5/8	24.0#	250'	135 sx class "G" + 2% CaCl ₂
7 7/8	5 1/2	15.5#	5808.8'	+ 1/4 #/sx celloflake.
<div data-bbox="365 1050 787 1291" data-label="Image"></div>				50/50 POZMIX + 2% GEL + 10% SALT TO 400' ABOVE ALL ZONES OF INTEREST (+ 10% EXCESS). LIGHT CEMENT (11 PPG+) + LCM TO 200' ABOVE OIL SHALE OR FRESH WATER INTERVALS (+ 5% EXCESS).

PETROGLYPH OPERATING COMPANY, INC. WILL BE THE DESIGNATED
OPERATOR OF THE SUBJECT WELL UNDER BOND #4556.pc: Utah Division of Oil, Gas, and Mining
Bureau of Indian Affairs, Fort Duchesne, Utah
Ute Tribe, Fort Duchesne, Utah

RECEIVED

OCT 28 1997

IN ABOVE SPACE DESCRIBE PROPOSED PROGRAM: If proposal is to deepen, give data on present productive zone and proposed new productive zone. If proposal is to drill or deepen directionally, give pertinent data on subsurface locations and measured and true vertical depths. Give blowout preventer program, if any.

24.

SIGNED

TITLE

AGENT FOR PETROGLYPH

DATE

10-23-97

(This space for Federal or State office use)

PERMIT NO.

VOICE OF APPROVAL

APPROVAL DATE

Application approval does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
CONDITIONS OF APPROVAL, IF ANY:

APPROVED BY

TITLE

Assistant Field Manager
Mineral Resources

DATE

FEB 10 1998

*See Instructions On Reverse Side

TO: Bureau of Land Management, Vernal District Office
Attention: Minerals and Mining Division

RECEIVED
FEB 02 1998

SECTION 07, TOWNSHIP 5 SOUTH RANGE 3 WEST, USB&M	
Ute Tribal 07-02, NWNE	Ute Tribal 07-06, SENW
Ute Tribal 07-03, NENW	Ute Tribal 07-07, SWNE
Ute Tribal 07-05, SWNW	

- 1) 75 foot corridor right of way to include the following:
 - a) One buried 3" steel oil pipeline.
 - b) One buried 3" poly water pipeline
 - c) One buried 3" poly gas pipeline
 - d) One buried 6" steel water pipeline
 - e) One surface 4 1/2" steel production pipeline
 - f) 4" production pipeline
- 2) 30 foot access road

YES x NO Listed threatened or endangered species
YES x NO Critical wildlife habitat
YES x NO Archaeological or cultural resources
YES NO Air quality aspects (to be used only if
Project is in or adjacent to a Class I area

1. The Ute Tribe Energy and Minerals Dept. is to be notified 48 hours prior to construction, as a Tribal Technician is to monitor construction.

2. 75 foot corridor rights of way shall be granted with the following:
 - a) Buried pipelines shall be a minimum of 3 feet below soil surface.
 - b) Surface pipelines shall be limited to 13 feet wide.
 - c) Buried pipelines shall be limited to 15 feet wide.
3. Pipelines adjacent to access roads shall be buried within 1.5 feet from the outside edge of the barrow ditch. Additional pipelines shall be parallel to each other, as safety requirements will allow.
4. Access roads shall be limited to 30 feet.
5. Petroglyph Operating Company will assure the Ute Tribe that any/all contractors and sub-contractors have acquired a Tribal Business License and have an access permits prior to construction.
6. All vehicular traffic, personnel movement, construction and restoration operations should be confined to the areas examined, as referenced in report, and to the existing roadways and/or evaluated access routes.
7. All personnel should refrain from collecting artifacts and from disturbing any significant cultural resources in the area.
8. The personnel from the Ute Energy and Minerals Department should be consulted if cultural remains from subsurface deposits be exposed or identified during construction.
9. All mitigative stipulations contained in the Bureau of Indian Affairs site specific Environmental Analysis (EA), will be strictly adhered.
10. Upon completion of Application of Right-of-way, the Ute Tribe Energy and Minerals Department, will be notified by Petroglyph Operating Company, so that a Tribal Technician can verify Affidavit of Completions.

If you have any questions in regards to the above, please feel free to contact us (801) 722-4310.

Richard L. Pitt

CONDITIONS OF APPROVAL
APPLICATION FOR PERMIT TO DRILL

Company/Operator: Petroglyph Operating Company Inc.

Well Name & Number: Ute Tribal 07-05

API Number: 43-013-31977

Lease Number: 14-20-H62-3506

Location: SWNW Sec. 07 T.5S R. 3W

NOTIFICATION REQUIREMENTS

- | | | |
|---------------------------------|---|-----------------------------------------------------------------------------------------------------------------------------------------------|
| Location Construction | - | at least forty-eight (48) hours prior to construction of location and access roads. |
| Location Completion | - | prior to moving on the drilling rig. |
| Spud Notice | - | at least twenty-four (24) hours prior to spudding the well. |
| Casing String and Cementing | - | at least twenty-four (24) hours prior to running casing and cementing all casing strings. |
| BOP and Related Equipment Tests | - | at least twenty-four (24) hours prior to initiating pressure tests. |
| First Production Notice | - | within five (5) business days after new well begins, or production resumes after well has been off production for more than ninety (90) days. |

For more specific details on notification requirements, please check the Conditions of Approval for Notice to Drill and Surface Use Program.

CONDITIONS OF APPROVAL FOR NOTICE TO DRILL

Approval of this application does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

All lease and/or unit operations will be conducted in such a manner that full compliance is made with applicable laws, regulations (43 CFR 3100), Onshore Oil and Gas Orders, and the approved plan of operations. The operator is fully responsible for the actions of his subcontractors. A copy of these conditions will be furnished the field representative to insure compliance.

Be aware fire restrictions may be in effect when location is being constructed and/or when well is being drilled. Contact the appropriate Surface Management Agency for information.

A. DRILLING PROGRAM

1. Estimated Depth at Which Oil, Gas, Water, or Other Mineral Bearing Zones are Expected to be Encountered

Report ALL water shows and water-bearing sands to Tim Ingwell of this office **prior to setting the next casing string or requesting plugging orders**. Faxed copies of State of Utah form OGC-8-X are acceptable. If noticeable water flows are detected, submit samples to this office along with any water analyses conducted.

All usable water and prospectively valuable minerals (as described by BLM at onsite) encountered during drilling, will be recorded by depth and adequately protected. All oil and gas shows will be tested to determine commercial potential.

2. Pressure Control Equipment

The BOP and related equipment shall meet the minimum requirements of Onshore Oil and Gas Order No. 2 for equipment and testing requirements, procedures, etc., for a **2M** system and individual components shall be operable as designed. Chart recorders shall be used for all pressure tests.

Test charts, with individual test results identified, shall be maintained on location while drilling and shall be made available to a BLM representative upon request.

If an air compressor is on location and is being utilized to provide air for the drilling medium while drilling, the special drilling requirements in Onshore Oil and Gas Order No. 2, regarding air or gas drilling shall be adhered to. If a mist system is being utilized then the requirement for a deduster shall be waived.

3. Casing Program and Auxiliary Equipment

Surface casing shall have centralizers on the bottom three joints, with a minimum of one centralizer per joint.

As a minimum, the usable water shall be isolated and/or protected by having a cement top for the production casing at least 200 ft. above the top of the shallowest potential productive zone. If gilsonite is encountered while drilling, it shall be isolated and/or protected via the cementing program.

4. Mud Program and Circulating Medium

Hazardous substances specifically listed by the EPA as a hazardous waste or demonstrating a characteristic of a hazardous waste will not be used in drilling, testing, or completion operations.

No chromate additives will be used in the mud system on Federal and Indian lands without prior BLM approval to ensure adequate protection of fresh water aquifers.

5. Coring, Logging and Testing Program

Daily drilling and completion progress reports shall be submitted to this office on a weekly basis.

All Drill Stem tests (DST) shall be accomplished during daylight hours, unless specific approval to start during other hours is obtained from the AO. However, DSTs may be allowed to continue at night if the test was initiated during daylight hours and the rate of flow is stabilized and if adequate lighting is available (i.e., lighting which is adequate for visibility and vaporproof for safe operations). Packers can be released, but tripping should not begin before daylight unless prior approval is obtained from the AO.

A cement bond log (CBL) will be run from the production casing shoe to the top of the cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.

Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (Form 3160-4) will be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3164. Two copies of all logs, core descriptions, core analyses, well-test data, geologic summaries, sample description, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, will be filed with Form 3160-4. Samples (cuttings, fluids, and/or gases) will be submitted when requested by the AO.

6. Notifications of Operations

No location will be constructed or moved, no well will be plugged, and no drilling or workover equipment will be removed from a well to be placed in a suspended status without prior approval of the AO. If operations are to be suspended, prior approval of the AO will be obtained and notification given before resumption of operations.

Operator shall report production data to MMS pursuant to 30 CFR 216.5 using form MMS/3160.

Immediate Report: Spills, blowouts, fires, leaks, accidents, or any other unusual occurrences shall be promptly reported in accordance with the requirements of NTL-3A or its revision.

If a replacement rig is contemplated for completion operations, a "Sundry Notice" (Form 3160-5) to that effect will be filed, for prior approval of the AO, and all conditions of this approved plan are applicable during all operations conducted with the replacement rig.

The date on which production is commenced or resumed will be construed for oil wells as the date on which liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated or, the date on which liquid hydrocarbons are first produced into a permanent storage facility, whichever first occurs; and, for gas wells as the date on which associated liquid hydrocarbons are first sold or shipped from a temporary storage facility, such as a test tank, and for which a run ticket is required to be generated or, the date on which gas is first measured through permanent metering facilities, whichever first occurs.

Should the well be successfully completed for production, the AO will be notified when the well is placed in a producing status. Such notification will be sent by telegram or other written communication, not later than five (5) days following the date on which the well is placed on production.

Gas produced from this well may not be vented or flared beyond an initial authorized test period of 30 days or 50 MMCF following its completion, whichever occurs first, without the prior written approval of the Authorized Officer. Should gas be vented or flared without approval beyond the authorized test period, the operator may be directed to shut-in the well until the gas can be captured or approval to continue venting or flaring as uneconomic is granted and the operator shall be required to compensate the lessor for that portion of the gas vented or flared without approval which is determined to have been avoidably lost.

A schematic facilities diagram as required by 43 CFR 3162.7-5(d) shall be submitted to the appropriate Field Office within 60 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with 43 CFR 3162.7-5 (1).

No well abandonment operations will be commenced without the prior approval of the AO. In the case of newly drilled dry holes or failures, and in emergency situations, oral approval will be obtained from the AO. A "Subsequent Report of Abandonment" Form 3160-5, will be filed with the AO within thirty (30) days following completion of the well for abandonment. This report will indicate where plugs were placed and the current status of surface restoration. Final abandonment will not be approved until the surface reclamation work required by the approved APD or approved abandonment notice has been completed to the satisfaction of the AO or his representative, or the appropriate Surface Managing Agency.

7. Other Information

All loading lines will be placed inside the berm surrounding the tank battery.

All off-lease storage, off-lease measurement, or commingling onlease or off-lease will have prior written approval from the AO.

The oil and gas measurement facilities will be installed on the well location. The oil and gas meters will be calibrated in place prior to any deliveries. Tests for meter accuracy will be conducted on initial meter installations and at least quarterly thereafter. The AO will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports will be submitted to the Vernal Field Office. All meter measurement facilities will conform with Onshore Oil & Gas Order No. 4 for liquid hydrocarbons and Onshore Oil & Gas Order No. 5 for natural gas measurement.

The use of materials under BLM jurisdiction will conform to 43 CFR 3610.2-3.

There will be no deviation from the proposed drilling and/or workover program without prior approval from the AO. Safe drilling and operating practices must be observed. All wells, whether drilling, producing, suspended, or abandoned will be identified in accordance with 43 CFR 3162.

"Sundry Notice and Report on Wells" (Form 3160-5) will be filed for approval for all changes of plans and other operations in accordance with 43 CFR 3162.3-2.

Section 102(b)(3) of the Federal Oil and Gas Royalty Management Act of 1982, as implemented by the applicable provisions of the operating regulations at Title 43 CFR 3162.4-1(c), requires that "not later than the 5th business day after any well begins production on which royalty is due anywhere on a lease site or allocated to a lease site, or resumes production in the case of a well which has been off production for more than 90 days, the operator shall notify the authorized officer by letter or sundry notice, Form 3160-5, or orally to be followed by a letter or sundry notice, of the date on which such production has begun or resumed."

If you fail to comply with this requirement in the manner and time allowed, you shall be liable for a civil penalty of up to \$10,000 per violation for each day such violation continues, not to exceed a maximum of 20 days. See Section 109(c)(3) of the Federal Oil and Gas Royalty Management Act of 1982 and the implementing regulations at Title 43 CFR 3162.4-1(b)(5)(ii).

APD approval is valid for a period of one (1) year from the signature date. An extension period may be granted, if requested, prior to the expiration of the original approval period.

In the event after-hours approvals are necessary, please contact one of the following individuals:

Ed Forsman (435) 789-7077
Petroleum Engineer

Wayne P. Bankert (435) 789-4170
Petroleum Engineer

Jerry Kencka (435) 781-1190
Petroleum Engineer

BLM FAX Machine (435) 781-4410

EPA'S LIST OF NONEXEMPT EXPLORATION AND PRODUCTION WASTES

While the following wastes are nonexempt, they are not necessarily hazardous.

Unused fracturing fluids or acids

Gas plant cooling tower cleaning wastes

Painting wastes

Oil and gas service company wastes, such as empty drums, drum rinsate, vacuum truck rinsate, sandblast media, painting wastes, spent solvents, spilled chemicals, and waste acids

Vacuum truck and drum rinsate from trucks and drums, transporting or containing nonexempt waste

Refinery wastes

Liquid and solid wastes generated by crude oil and tank bottom reclaimers

Used equipment lubrication oils

Waste compressor oil, filters, and blowdown

Used hydraulic fluids

Waste solvents

Waste in transportation pipeline-related pits

Caustic or acid cleaners

Boiler cleaning wastes

Boiler refractory bricks

Incinerator ash

Laboratory wastes

Sanitary wastes

Pesticide wastes

Radioactive tracer wastes

Drums, insulation and miscellaneous solids.

SURFACE USE PROGRAM

The Surface Use Conditions of Approval all come from the Bureau of Indian Affairs Concurrence Memorandum and Site Specific Environmental Analysis.

The Ute Tribe Energy and Mineral Department is to be notified 48 hours prior to construction. A Tribal Technician is to monitor construction.

Seventy-five (75) foot wide Rights-Of-Way (ROWs) corridor shall be granted for the following:

Access roads which shall have constructed travel width limited to 22 feet within a 30 foot allocation of the ROW, except as granted for sharp curves or intersections.

Surface pipelines shall be limited to 13 feet of the ROW. The pipeline will be constructed to lay on the soil surface, and the ROW for the pipeline will not be bladed or cleared of vegetation.

Where pipelines are constructed parallel to roads they may be welded on the road and then lifted from the road onto the ROW. Where pipelines cross country between stations, they shall be welded in place at wellsites or on roads and then pulled into place with suitable equipment. Traffic will be restricted along these areas so that the pipeline ROW will not be used as an access road.

Buried pipelines shall be buried a minimum of 3 feet below the soil surface within an area of disturbance limited to 15 feet wide, and construction will be monitored by a Tribal Technician.

Buried pipelines adjacent to access roads shall be buried within 1.5 feet from the outside edge of the barrow ditch. Any additional buried pipelines shall be parallel to the outer side of the first buried pipeline and shall be constructed as close to the first pipeline as safety requirements allow.

After construction of the buried pipeline is completed the disturbed area of the right-of-way shall be contoured to blend into the natural landscape and it shall be reseeded with desirable vegetation as recommended by the BIA. Between September 15 and November 1 of the year following pipeline construction all disturbed areas shall be reseeded with perennial vegetation according to BIA, or Ute Tribe specifications.

Petroglyph will assure the Ute Tribe that any/all contractors and subcontractors have acquired a Tribal Business License and have access permits prior to commencing surveys or construction.

All vehicular traffic, personnel movement, construction, and restoration activities shall be confined to the areas examined, as referenced in report, and to the existing roadways and/or evaluated access routes.

All personnel shall refrain from collecting artifacts and from disturbing any significant cultural resources in the area.

The Ute Tribe Energy & Mineral Department shall be consulted if cultural remains from subsurface deposits are exposed or identified during construction.

Before the site is abandoned, the company will be required to restore the well site and ROWs to near their original state. The disturbed areas will be reseeded with desirable perennial vegetation.

Noxious weeds will be controlled on the well site and rights-of-way. If noxious weeds spread from the project area onto adjoining land, the company will also be responsible for their control.

Reserve pits will be lined with impervious synthetic liners. Prior to backfilling the reserve pit all fluids will be pumped from the pit into trucks and hauled to approved disposal sites. When the reserve pits are backfilled the cuttings and mud, etc. left in them to be buried will be buried a minimum of three feet below the surface of the soil.

A closed production system will be used. Production fluids will be contained in leak proof tanks. All production fluids will be disposed of at approved disposal sites. The indiscriminate dumping of production fluids on roads, wellsites or other areas will not be allowed.

Firewood shall be stockpiled at convenient locations near the wellsite and along the access road.

A cattleguard shall be placed in the fenceline where the road to well 7-04 crosses through the fence. A gate shall be placed next to the cattleguard. The cattleguard shall be maintained for the life of the well. When the well is plugged and abandoned the cattleguard shall be removed by the operator and the fence shall be repaired in a satisfactory manner.

Keep the road to well 7-05 south of the fenceline and cattleguard rather than follow the proposed pipeline. The pipeline will follow the road.

Near the intersection with the road proceeding to well 7-04 existing drainages would be diverted into the east channel as agreed to at the onsite. North of the access road to 7-05, where the road to 7-04 crosses the diversion channel, the channel shall be excavated approximately two feet deeper than the channel bottom for the construction of a good low water crossing and large rocks shall be placed in the channel for the stability of the road and for erosion control. This would prevent an increase in erosion occurring in and near the low water crossing to well 7-04 which might also eventually affect the road to well 7-05.

Petroglyph, their employees, sub-contractors, and representatives shall not carry fire arms on their person or in their vehicles while working on Indian lands.

Upon completion of the project approved under this Application for Permit to Drill and Right-of-way, the Ute Tribe Energy & Minerals Resources Department will be notified by Petroglyph Operating Company so that a Tribal Technician can verify Affidavit of Completion's.



United States Department of the Interior

BUREAU OF LAND MANAGEMENT

Vernal Field Office
170 South 500 East
Vernal, Utah 84078-2799

<http://www.blm.gov/utah/vernal>

Phone: (435) 781-4400

Fax: (435) 781-4410

IN REPLY REFER TO:

3160

UT08300

May 3, 2000

Petroglyph Operating Co., Inc.
P. O. Box 607
Roosevelt, Utah 84066

Re: Notification of Expiration
Well No. Ute Tribal 07-05
SWNW, Section 7, T5S, R3W
Lease No. 14-20-H62-3506
Duchesne County, Utah

43-013-31977

Gentlemen:

The Application for Permit to Drill the above-referenced well was approved on February 10, 1998. Petroglyph Operating Company, Inc. requested an extension of the original APD approval for an additional year. The request was reviewed and the extension approved until February 10, 2000. According to our records, no known activity has transpired at the approved location. In view of the foregoing, this office is notifying you the approval of the referenced application has expired. If you intend to drill at this location at a future date, a new Application for Permit to Drill must be submitted.

This office requires a letter confirming that no surface disturbance has been made for this drill site. Any surface disturbance associated with the approved location of this well is to be rehabilitated. A schedule for this rehabilitation must be submitted to this office. Your cooperation in this matter is appreciated.

Sincerely,

Margie Herrmann

Margie Herrmann
Legal Instruments Examiner

cc: State Div. OG&M

RECEIVED

MAY 05 2000

DIVISION OF
OIL, GAS AND MINING

7-5S-3W
43-013-31974

Petroglyph Operating
Ute Tribal 7-5
7-5S-3W
43-013-31977

expires 2/10/2000

Petroglyph Operating
Ute Tribal 7-6
7-5S-3W
43-013-31978

expires 2/10/2000

Petroglyph Operating
Ute Tribal 7-7
7-5S-3W
43-013-31979

expires 2/10/2000

Petroglyph Operating
Ute Tribal 31-1
31-5S-3E
43-013-32033

expires 1/28/2000

Petroglyph Operating
Ute Tribal 31-10
31-5S-3W
43-013-32037

expired 1/28/99
letter being done

Petroglyph Operating
Ute Tribal 31-15
31-5S-3W
43-013-32040

expired 1/28/99
letter being done

Sego Resources
Sego Resources 3
23-11S-15E
43-013-31948

expires 9/29/99

Snyder Oil
Ute Tribal 25-F
25-4S-1E
43-047-32809

drilling

APD Approval
Extensions
per
Margie Herman
- BLM Vernal -
email 3/4/99

Well File
