


NEWFIELD



October 29, 2004

State of Utah
Division of Oil, Gas & Mining
Attn: Diana Whitney
1594 West North Temple - Suite 1210
P.O. Box 145801
Salt Lake City, Utah 84114-5801

RE: Applications for Permit to Drill: Federal 1-33-8-18 and 8-33-8-18.

Dear Diana:

Enclosed find APD's on the above referenced wells. The 1-33-8-18 is an Exception Location. The appropriate paperwork will be forthcoming. If you have any questions, feel free to give either Brad or myself a call.

Sincerely,

A handwritten signature in cursive script that reads "Mandie Crozier".

Mandie Crozier
Regulatory Specialist

mc
enclosures

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0136
Expires January 31, 2004

5. Lease Serial No.
UTU-74872

6. If Indian, Allottee or Tribe Name
N/A

7. If Unit or CA Agreement, Name and No.
N/A

8. Lease Name and Well No.
Federal 1-33-8-18

9. API Well No.
43-047-36036

10. Field and Pool, or Exploratory
Eight Mile Flat

11. Sec., T., R., M., or Blk. and Survey or Area
NE/NE Sec. 33, T8S R18E

12. County or Parish
Uintah

13. State
UT

1a. Type of Work: DRILL REENTER

1b. Type of Well: Oil Well Gas Well Other Single Zone Multiple Zone

2. Name of Operator
Newfield Production Company

3a. Address
Route #3 Box 3630, Myton UT 84052

3b. Phone No. (include area code)
(435) 646-3721

4. Location of Well (Report location clearly and in accordance with any State requirements.)*
At surface NE/NE 906' FNL 705' FEL 594570X 40.079314
At proposed prod. zone 4436928Y -109.890854

14. Distance in miles and direction from nearest town or post office*
Approximatley 23.1 miles south of Myton, Utah

15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 705' f/lse, NA f/unit
16. No. of Acres in lease
677.36

17. Spacing Unit dedicated to this well
40 Acres

18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1,141'
19. Proposed Depth
6270'

20. BLM/BIA Bond No. on file
UTU0056

21. Elevations (Show whether DF, KDB, RT, GL, etc.)
4869.0' GL

22. Approximate date work will start*
1st Quarter 2005

23. Estimated duration
Approximately seven (7) days from spud to rig release.

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature *Lana Nebeker* Name (Printed/Typed) Lana Nebeker Date 10-28-04
Title Production Clerk


Approved by (Signature) *Bradley G. Hill* Name (Printed/Typed) BRADLEY G. HILL Date 11-03-04
Title ENVIRONMENTAL SCIENTIST III

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.
Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on reverse)


Federal Approval of this
Action is Necessary



T8S, R18E, S.L.B.&M.

NEWFIELD PRODUCTION COMPANY

WELL LOCATION, FEDERAL 1-33-8-18,
LOCATED AS SHOWN IN THE NE 1/4 NE
1/4 OF SECTION 33, T8S, R18E,
S.L.B.&M. UTAH COUNTY, UTAH.

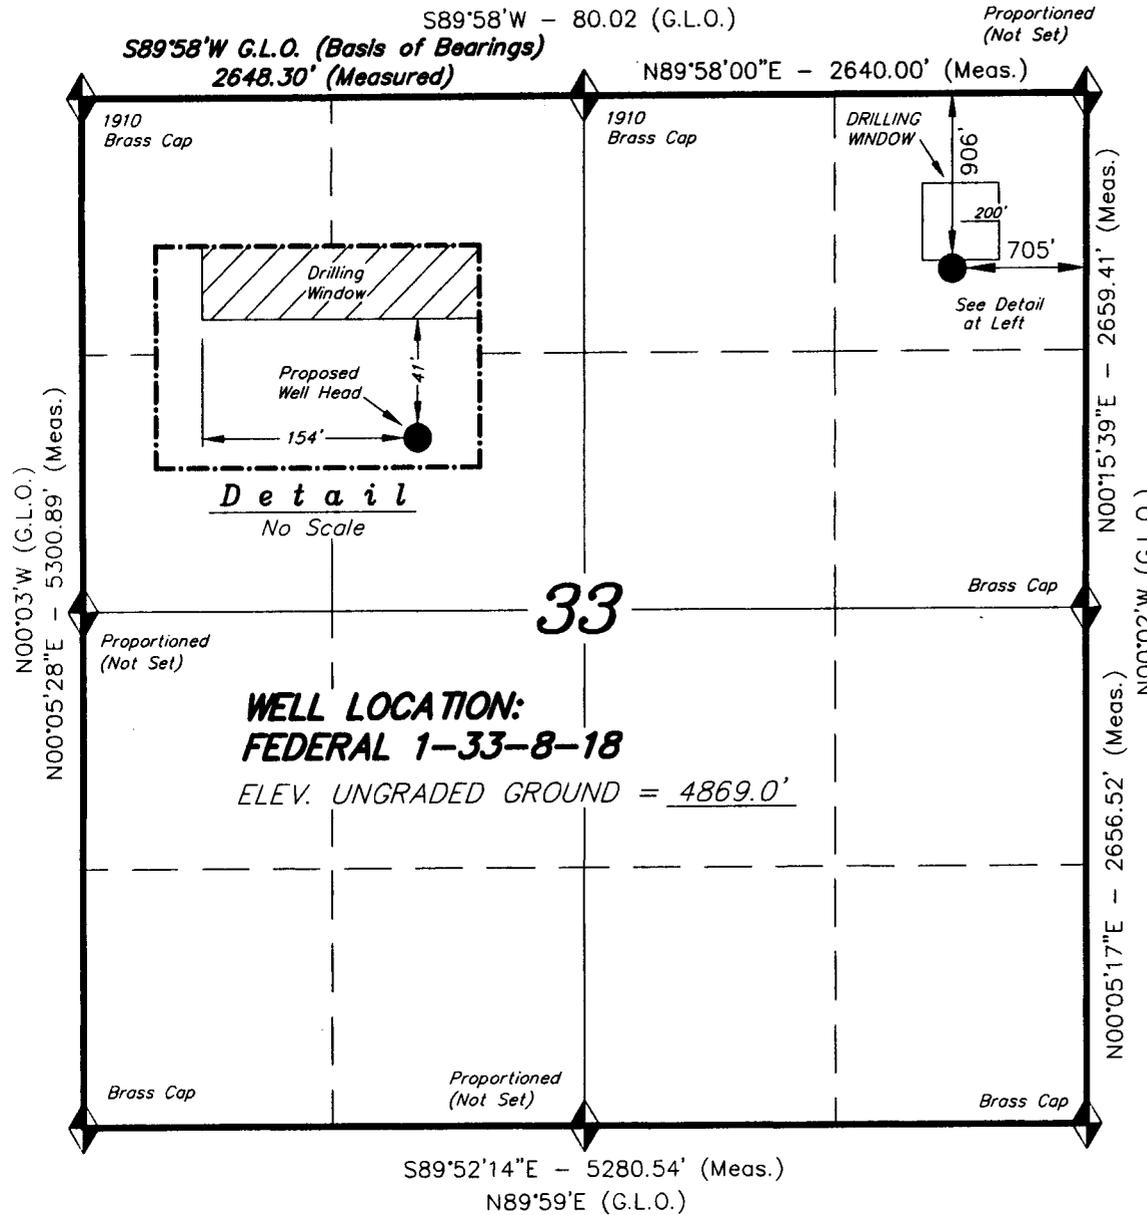

THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS MADE BY ME OR UNDER MY SUPERVISION AND THAT THE SAME ARE TRUE AND CORRECT TO THE BEST OF MY KNOWLEDGE AND BELIEF.

REGISTERED LAND SURVEYOR
 No. 189377
 STACY W. STEWART
 REGISTERED LAND SURVEYOR
 REGISTRATION No. 189377
 STATE OF UTAH

TRI STATE LAND SURVEYING & CONSULTING	
180 NORTH VERNAL AVE. - VERNAL, UTAH 84078 (435) 781-2501	
SCALE: 1" = 1000'	SURVEYED BY: C.M.
DATE: 9-21-04	DRAFTED BY: F.T.M.
NOTES:	FILE #

◆ = SECTION CORNERS LOCATED
 BASIS OF ELEV; U.S.G.S. 7-1/2 min QUAD (PARIETTE DRAW SW)

NEWFIELD PRODUCTION COMPANY
FEDERAL 1-33-8-18
NE/NE SECTION 33, T8S, R18E
UINTAH COUNTY, UTAH

ONSHORE ORDER NO. 1

DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta	0' – 1640'
Green River	2410'
Wasatch	6270'

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation 2410' – 6270' - Oil

4. PROPOSED CASING PROGRAM

Please refer to the Monument Butte Field Standard Operation Procedure (SOP).

5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:

Please refer to the Monument Butte Field SOP. See Exhibit "C".

6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:

Please refer to the Monument Butte Field SOP.

7. AUXILIARY SAFETY EQUIPMENT TO BE USED:

Please refer to the Monument Butte Field SOP.

8. TESTING, LOGGING AND CORING PROGRAMS:

Please refer to the Monument Butte Field SOP.

9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:

The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered.

10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:

Please refer to the Monument Butte Field SOP.

**NEWFIELD PRODUCTION COMPANY
FEDERAL #1-33-8-18
NE/NE SECTION 33, T8S, R18E
UINTAH COUNTY, UTAH**

ONSHORE ORDER NO. 1

MULTI-POINT SURFACE USE & OPERATIONS PLAN

1. EXISTING ROADS

See attached Topographic Map "A"

To reach Newfield Production Company well location site Federal #1-33-8-18 located in the NE 1/4 NE 1/4 Section 33, T8S, R18E, Uintah County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.6 miles \pm to the junction of this highway and UT State Hwy 53; proceed southeasterly along Hwy 53 - 13.8 miles \pm to it's junction with an existing dirt road to the north; proceed northerly \pm 0.1 miles \pm to it's junction with an existing road to the east; proceed northeasterly \pm 7.4 miles to it's junction with the beginning of the proposed access road; proceed northeasterly along the proposed access road - 5,280. \pm to the proposed well location.

2. PLANNED ACCESS ROAD

See Topographic Map "B" for the location of the proposed access road.

3. LOCATION OF EXISTING WELLS

Refer to Exhibit "B".

4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES

Please refer to the Monument Butte Field Standard Operating Procedure (SOP).

5. LOCATION AND TYPE OF WATER SUPPLY

Please refer to the Monument Butte Field SOP. See Exhibit "A".

6. SOURCE OF CONSTRUCTION MATERIALS

Please refer to the Monument Butte Field SOP.

7. METHODS FOR HANDLING WASTE DISPOSAL

Please refer to the Monument Butte Field SOP.

8. ANCILLARY FACILITIES

Please refer to the Monument Butte Field SOP.

9. **WELL SITE LAYOUT**

See attached Location Layout Diagram.

10. **PLANS FOR RESTORATION OF SURFACE**

Please refer to the Monument Butte Field SOP.

11. **SURFACE OWNERSHIP** - Bureau Of Land Management

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. MOAC Report #03-154, 02/3/04. Paleontological Resource Survey prepared by, Wade E. Miller, 5/12/04. See attached report cover pages, Exhibit "D".

For the Federal #1-33-8-18 Newfield Production Company requests a 555.' ROW be granted in Lease UTU-65969 and 1985' of disturbed area be granted in Lease UTU-74872 to allow for construction of the proposed access road. **Refer to Topographic Map "B"**. The proposed access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests a 1,750' ROW in Lease UTU-65969,, and 1990' of disturbed area be granted in Lease UTU-74872 to allow for construction of the proposed gas lines. It is proposed that the ROW and disturbed area will be 50' wide to allow for construction of a 3" gas gathering line, and a 2" poly fuel gas line. Both lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Newfield Production Company requests a 1,750' ROW in Lease UTU-65969, and 1,790' of disturbed area be granted in Lease UTU-74872 to allow for construction of the proposed water lines. It is proposed that the ROW and disturbed area will be 50' wide to allow for construction of a buried 3" steel water injection line and a 3" poly water return line. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Water Disposal

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Inland's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

Threatened, Endangered, And Other Sensitive Species

Possible Rapture nest site - Dixie Sadler to advise.

Reserve Pit Liner

A 12 mil liner with felt is required. Please refer to the Monument Butte Field SOP.

Reserve Pit Liner

Please refer to the Monument Butte Field SOP.

Location and Reserve Pit Reclamation

Please refer to the Monument Butte Field SOP.

The following seed mixture will be used on the topsoil stockpile, to the recontoured surface of the reserve pit, and for final reclamation: (All poundages are in pure live seed)

Gardeners Salt Bush	<i>AtriplexGardneri</i>	4 lbs/acre
Mat Saltbush	<i>Atriplex Corrugata</i>	4 lbs/acre
Crested Wheat Grass		4 lbs/acre

Details of the On-Site Inspection

The proposed Federal #1-33-8-18 was on-sited on 5/20/04. The following were present; Brad Mecham (NewfieldProduction), David Gerbig (Newfield Production), Byron Tolman (Bureau of Land Management). Weather conditions were clear.

13. LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION

Representative

Name: Brad Mecham

Address: Route #3 Box 3630
Myton, UT 84052


Telephone: (435) 646-3721

Certification

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #1-33-8-18 NE/NE Section 33, Township 8S, Range 18E: Lease UTU-74872 Uintah County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by Hartford Accident #4488944.

I hereby certify that the proposed drillsite and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Inland Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.


10-28-04
Date


Lana Nebeker
Production Clerk

NEWFIELD PRODUCTION COMPANY

FEDERAL 1-33-8-18

Section 33, T8S, R18E, S.L.B.&M.

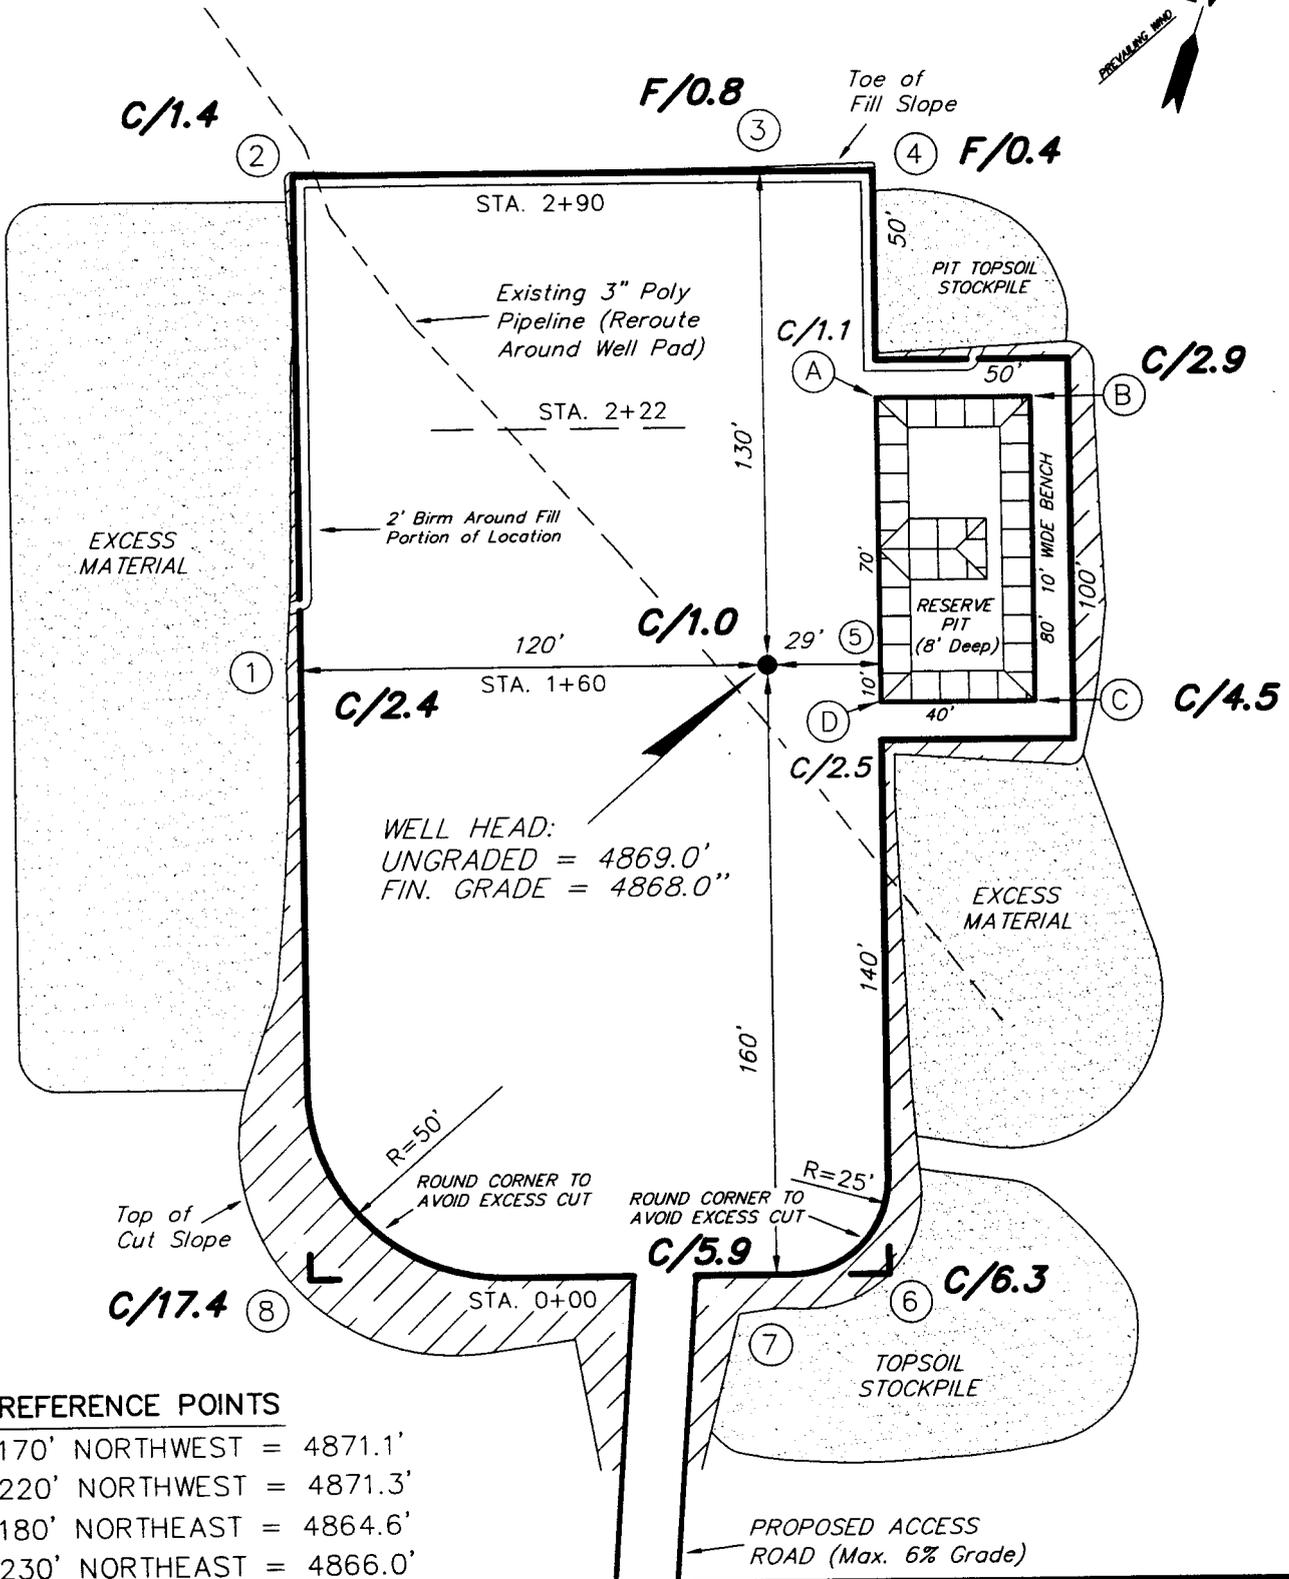

REFERENCE POINTS





- 170' NORTHWEST = 4871.1'
- 220' NORTHWEST = 4871.3'
- 180' NORTHEAST = 4864.6'
- 230' NORTHEAST = 4866.0'

SURVEYED BY: C.M.	SCALE: 1" = 50'
DRAWN BY: F.T.M.	DATE: 9-21-04

(435) 781-2501

Tri State
Land Surveying, Inc.
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

NEWFIELD PRODUCTION COMPANY
CROSS SECTIONS
FEDERAL 1-33-8-18

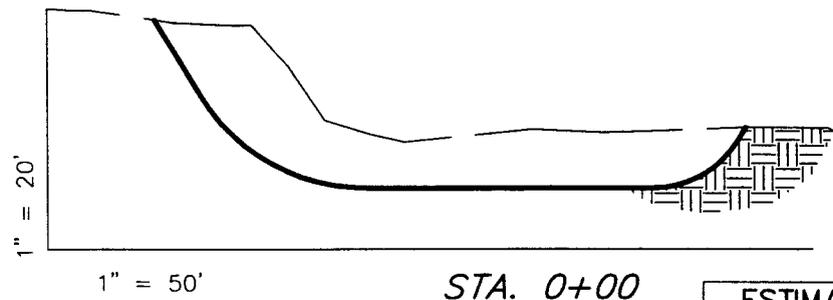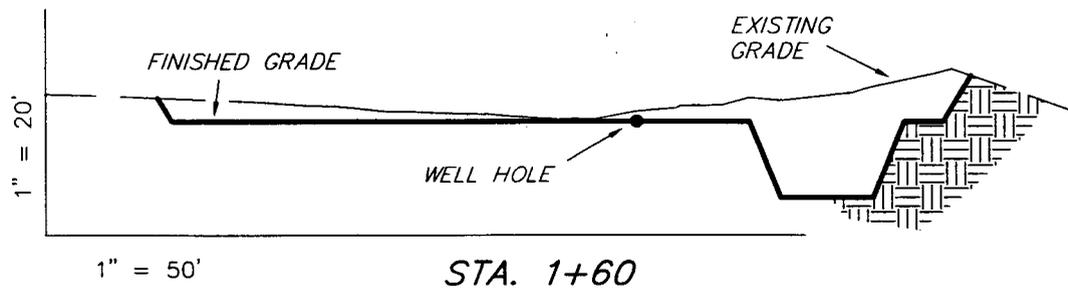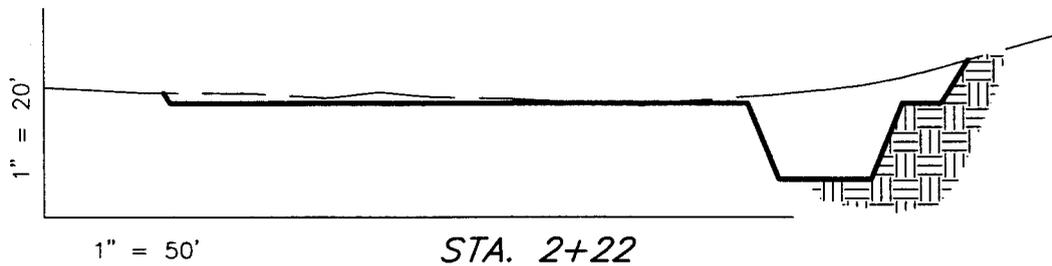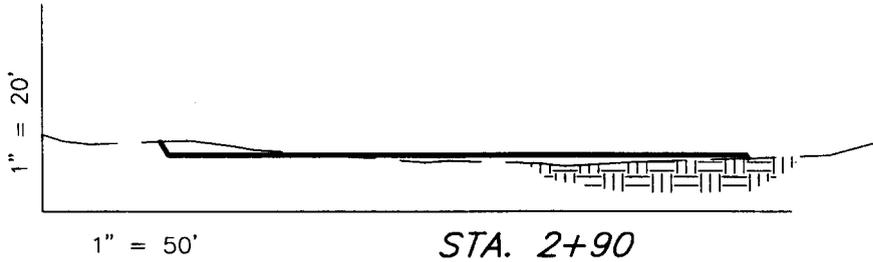

NOTE:
 UNLESS OTHERWISE NOTED
 ALL CUT/FILL SLOPES ARE
 AT 1.5:1

ESTIMATED EARTHWORK QUANTITIES
 (No Shrink or swell adjustments have been used)
 (Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	4,210	190	Topsoil is not included in Pad Cut	4,020
PIT	640	0		640
TOTALS	4,850	190	890	4,660

SURVEYED BY: C.M.


SCALE: 1" = 50'

DRAWN BY: F.T.M.

DATE: 9-21-04

Tri State
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078
 (435) 781-2501

NEWFIELD PRODUCTION COMPANY
TYPICAL RIG LAYOUT
FEDERAL 1-33-8-18

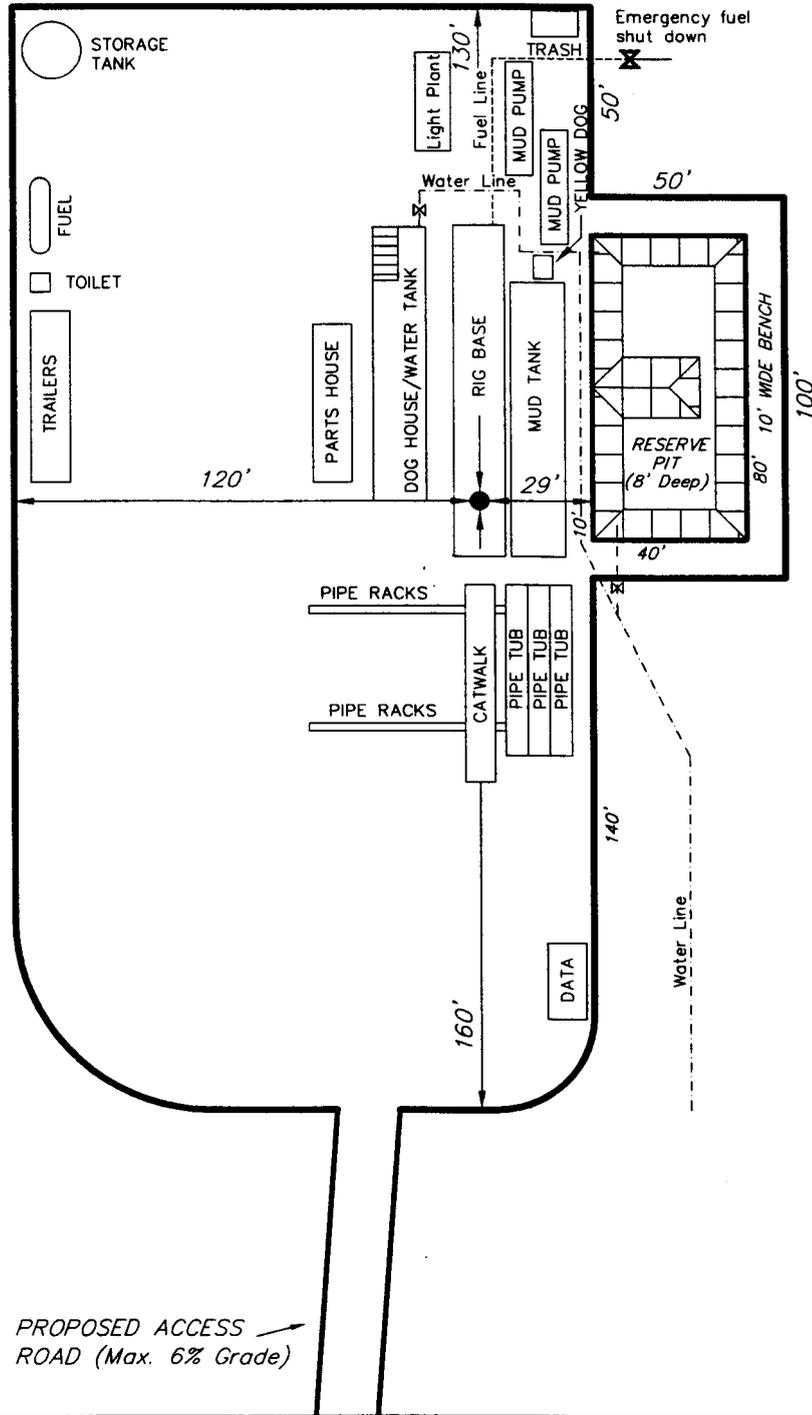

SURVEYED BY: C.M.

SCALE: 1" = 50'

DRAWN BY: F.T.M.

DATE: 9-21-04

Tri State (435) 781-2501
Land Surveying, Inc.
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078



Proposed Location
Federal 1-33

See Topo "B"

NEWFIELD
Exploration Company

Federal 1-33-8-18
SEC. 33, T8S, R18E, S.L.B.&M.



Tri-State
Land Surveying Inc.
(435) 781-2501
38 West 100 North Vernal, Utah 84078


SCALE: 1" = 100,000'
DRAWN BY: bgm
DATE: 10-05-2004

Legend

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP

"A"

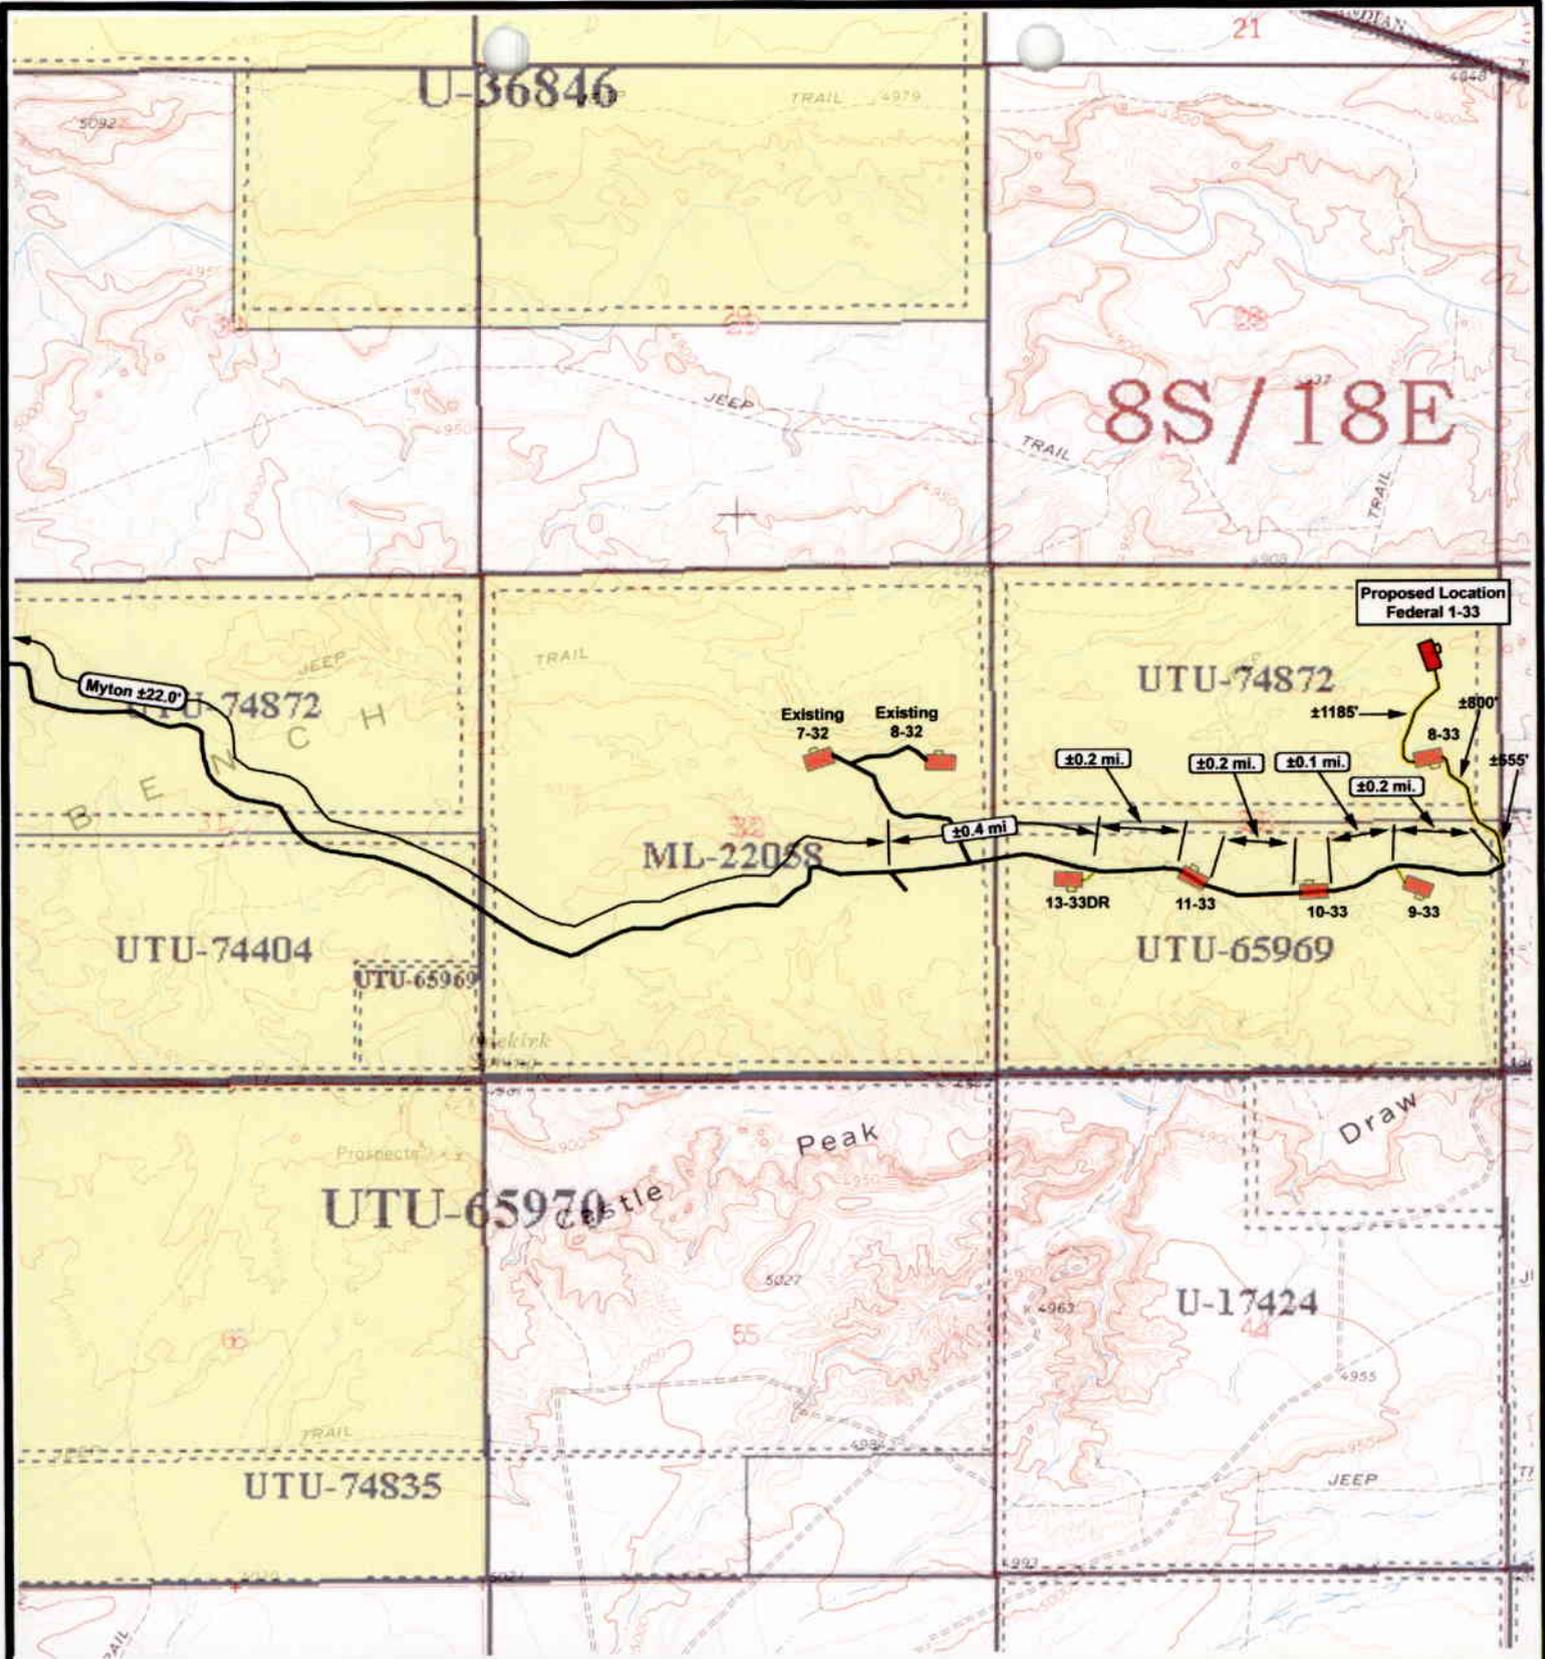

NEWFIELD
Exploration Company

Federal 1-33-8-18
SEC. 33, T8S, R18E, S.L.B.&M.




Tri-State
Land Surveying Inc.
(435) 781-2501
38 West 100 North Vernal, Utah 84078

SCALE: 1" = 2000'
DRAWN BY: bgm
DATE: 10-05-2004

Legend

- Existing Road
- Proposed Access

TOPOGRAPHIC MAP
"B"

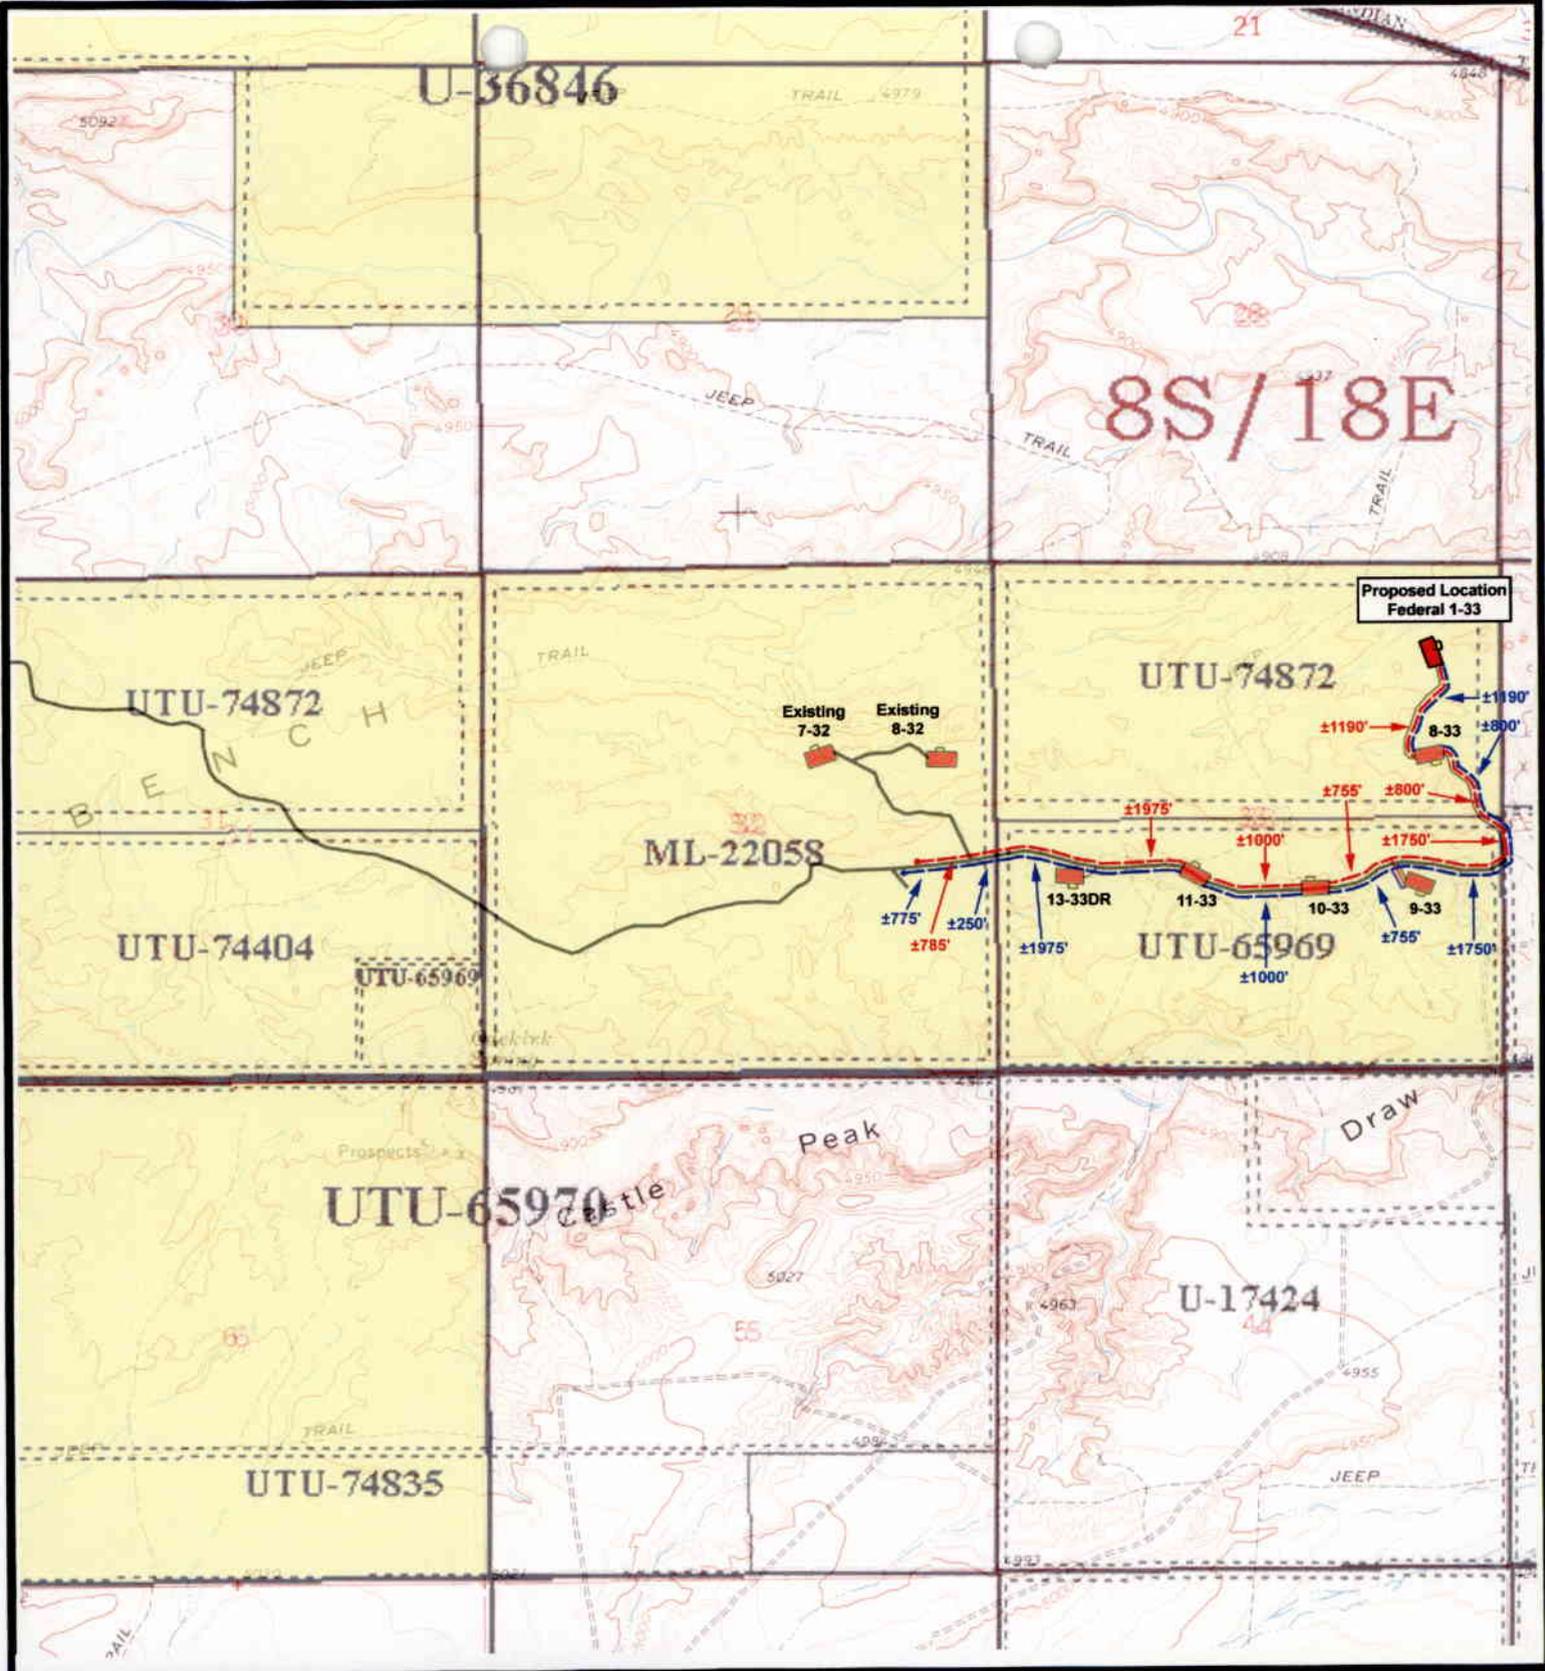

NEWFIELD
Exploration Company

Federal 1-33-8-18
SEC. 33, T8S, R18E, S.L.B.&M.




Tri-State
Land Surveying Inc.
(435) 781-2501
38 West 100 North Vernal, Utah 84078


SCALE: 1" = 2000'
DRAWN BY: bgm
DATE: 10-05-2004

Legend

- Existing Road
- Proposed Access
- Proposed Gas Line
- Proposed Water Line

TOPOGRAPHIC MAP
"C"

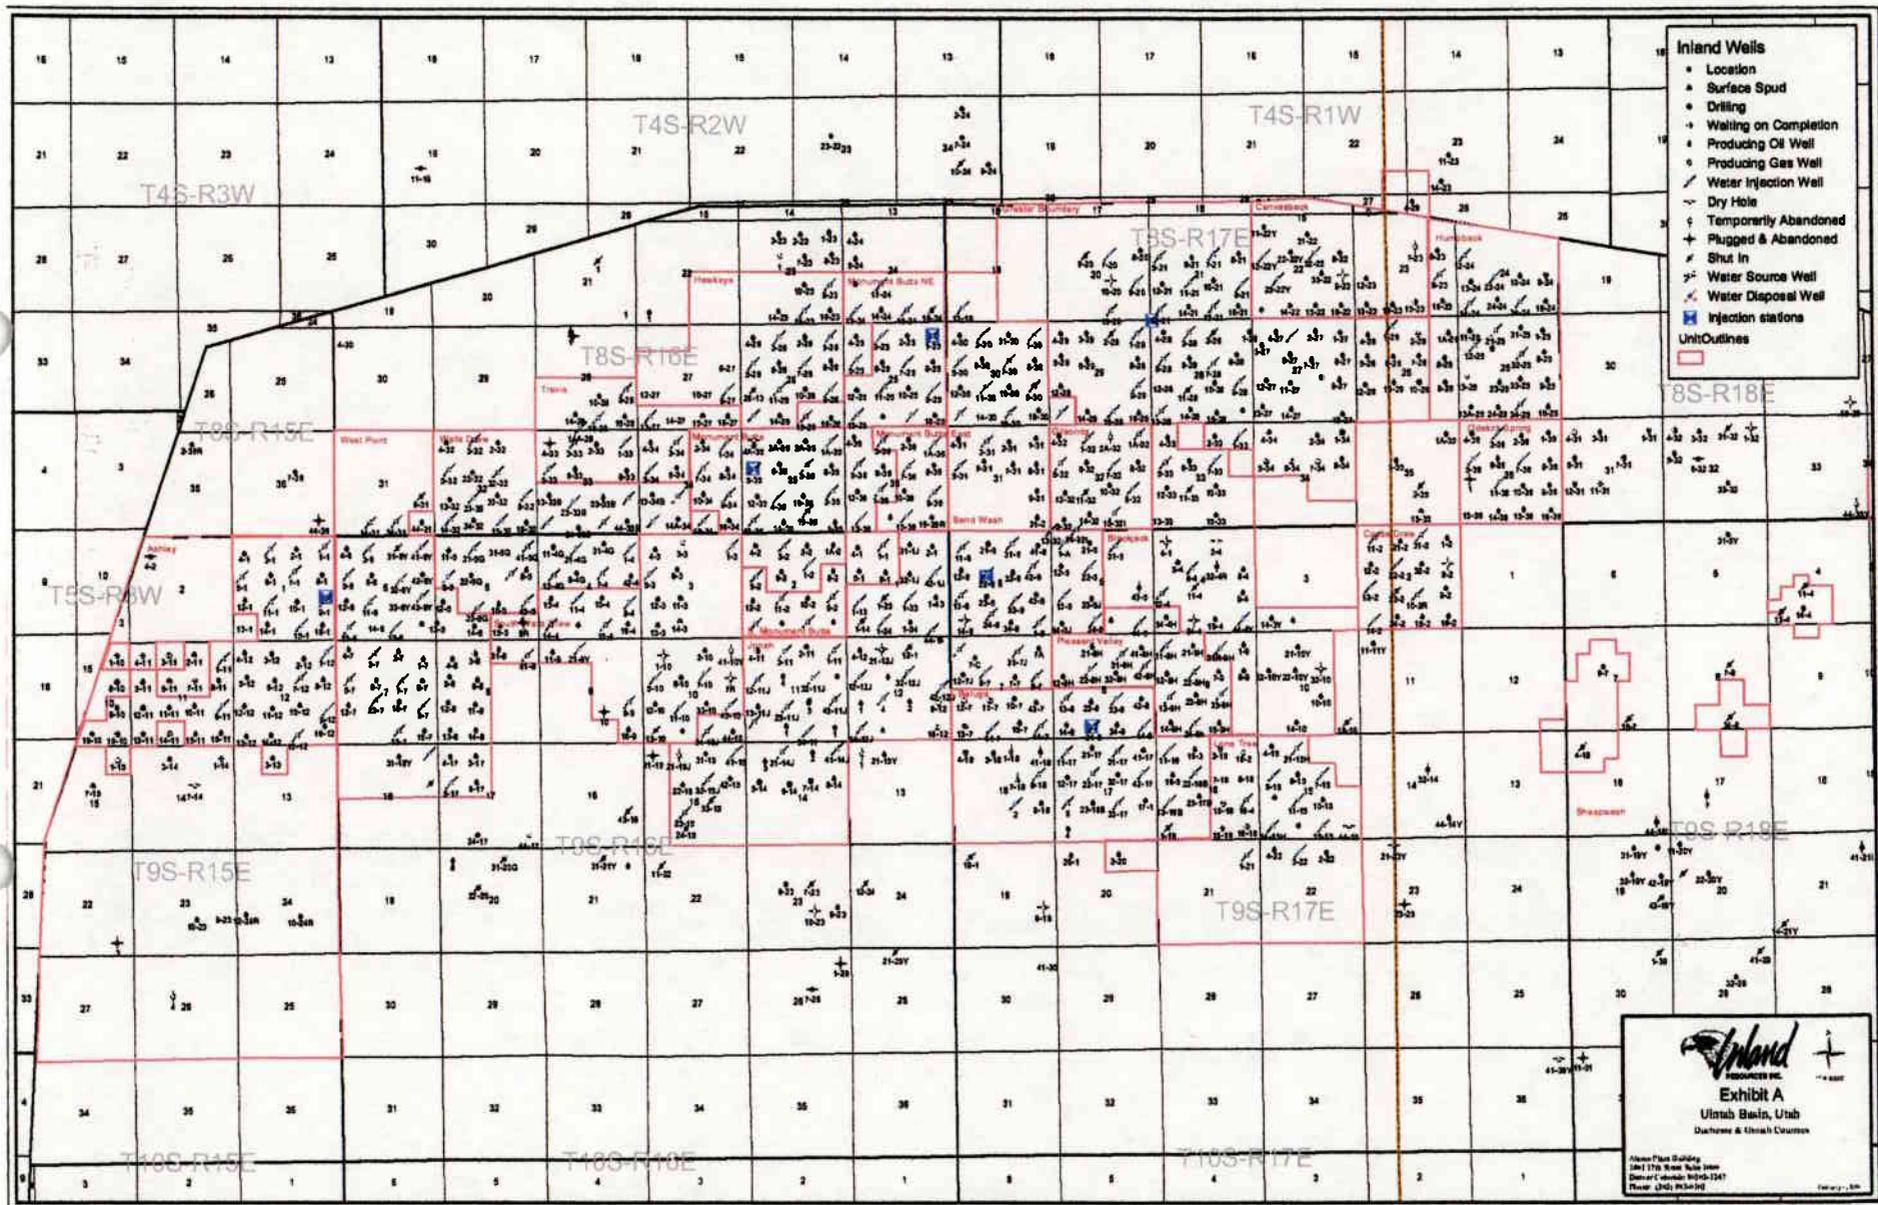

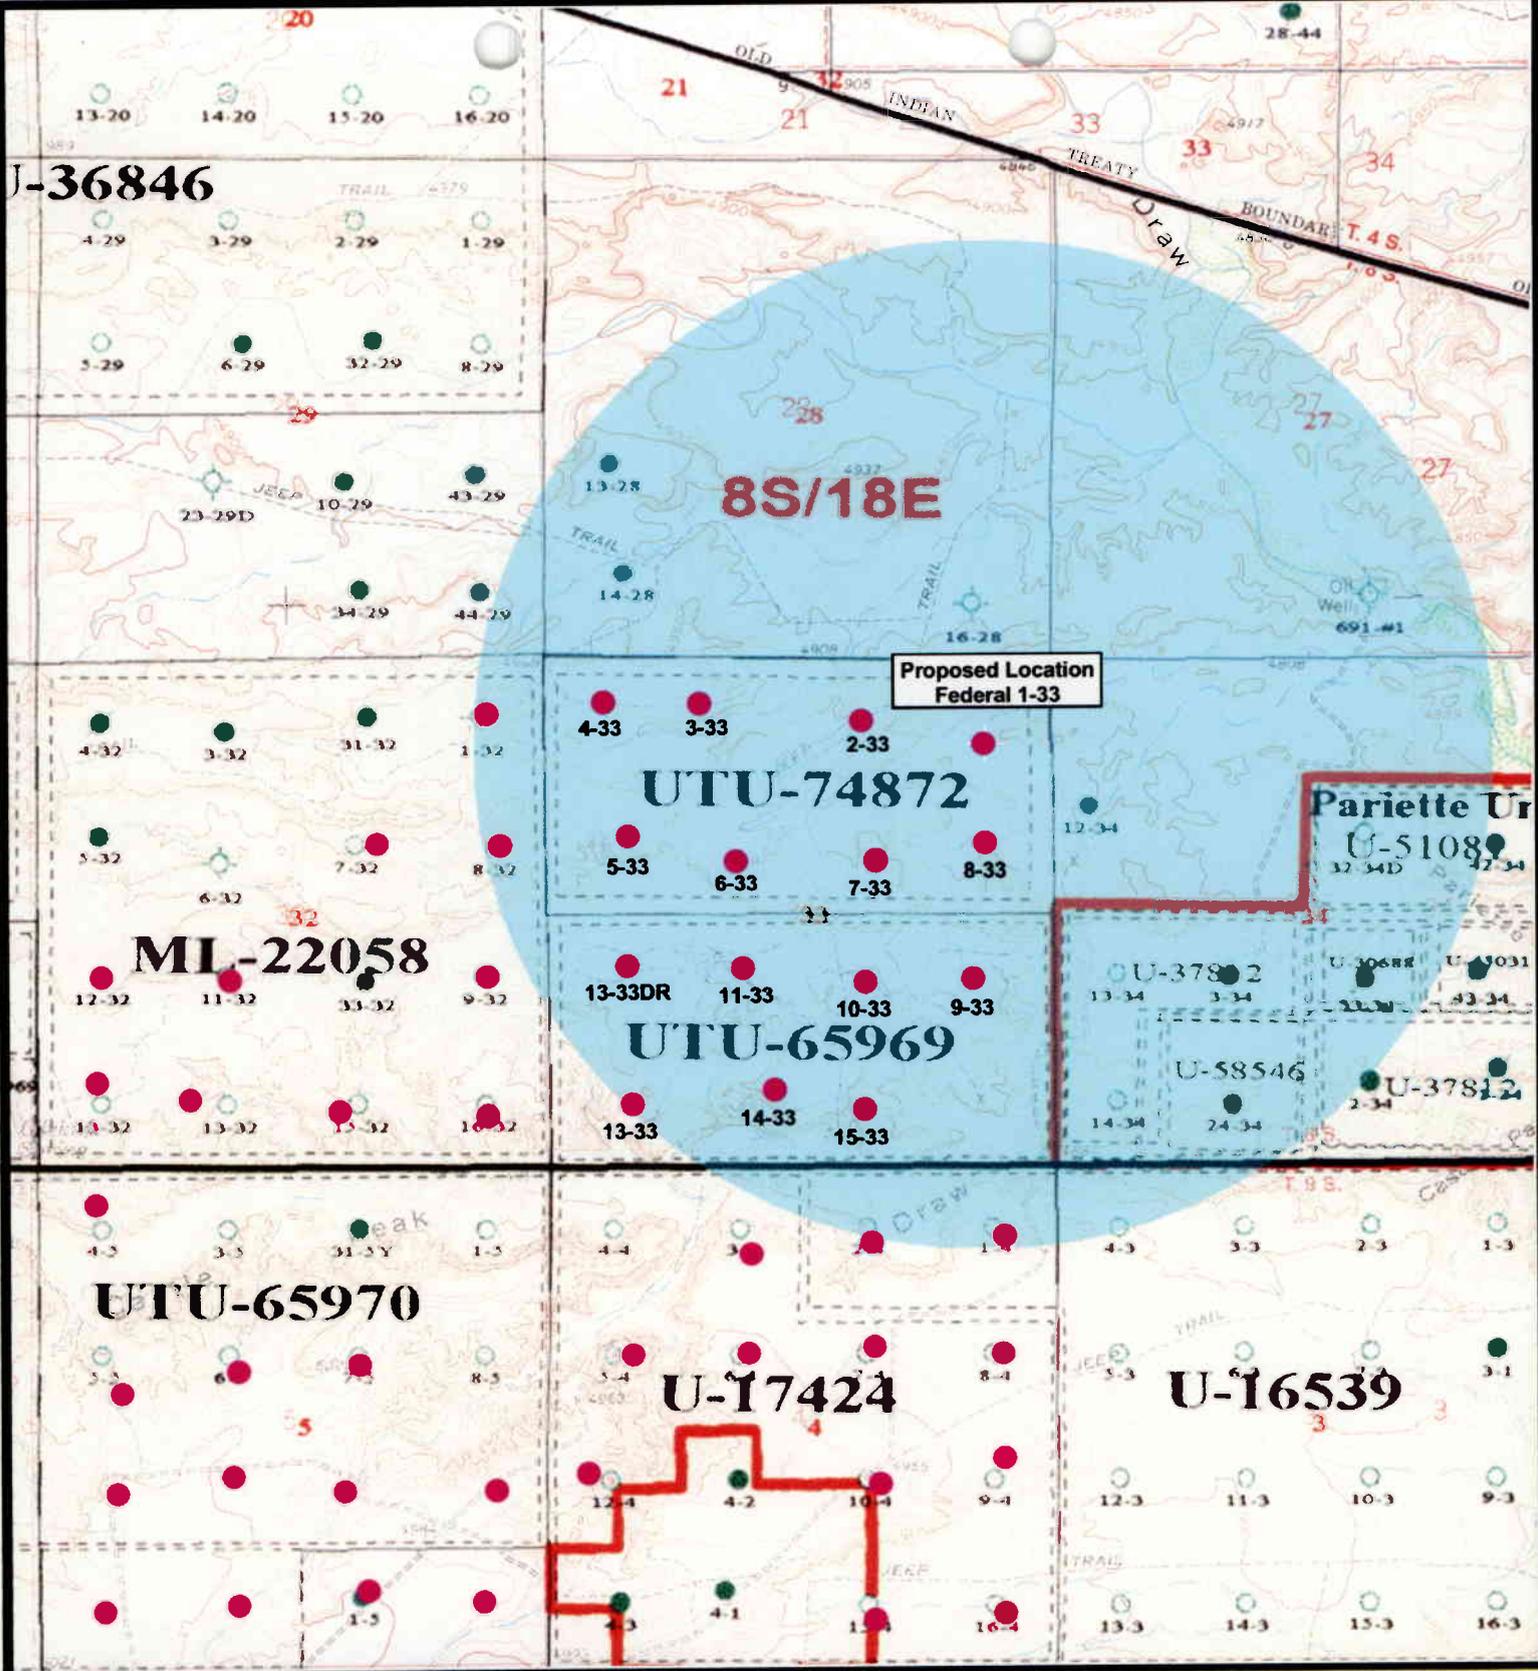

NEWFIELD
Exploration Company

Federal 1-33-8-18
SEC. 33, T8S, R18E, S.L.B.&M.



Tri-State
Land Surveying Inc.
(435) 781-2501
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'
DRAWN BY: bgm
DATE: 10-05-2004

Legend

- Well Locations
- One-Mile Radius

Exhibit "B"

2-M SYSTEM

Blowout Prevention Equipment Systems

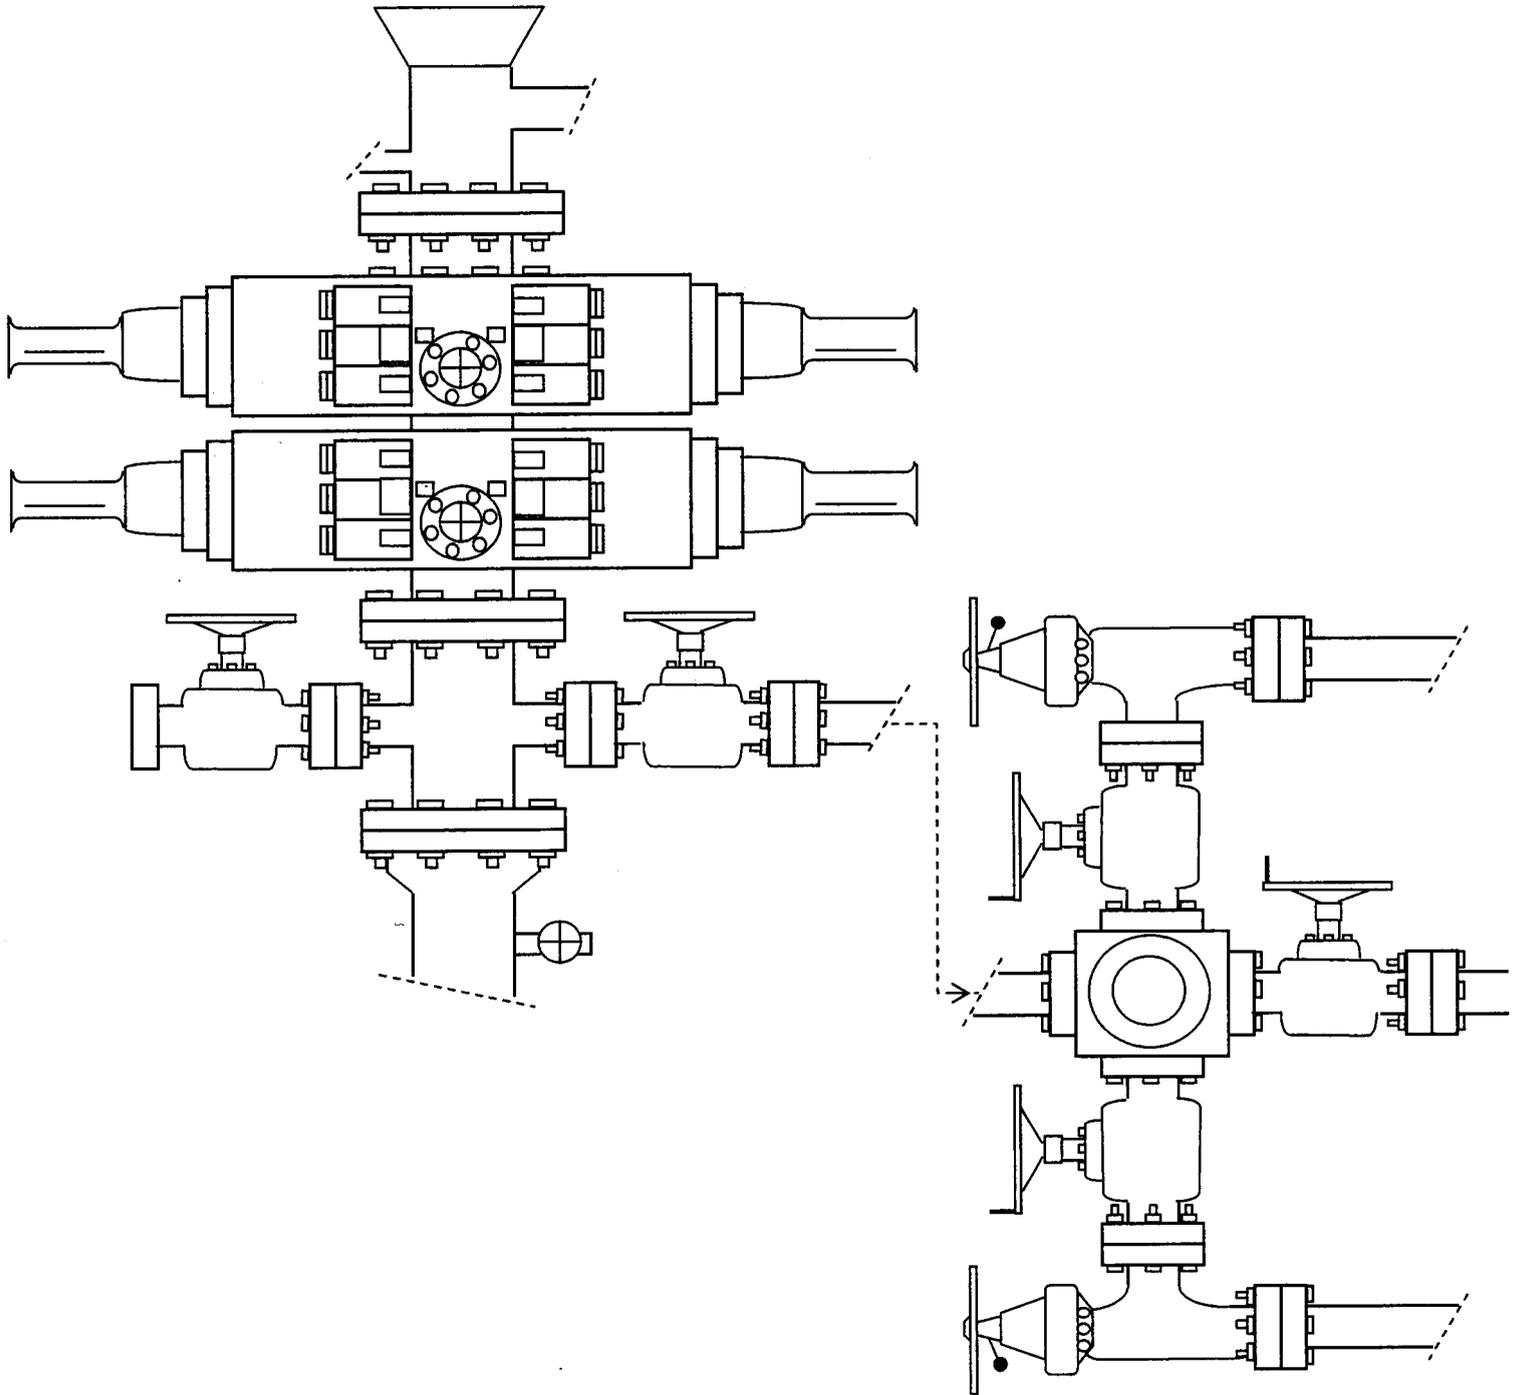


EXHIBIT C

CULTURAL RESOURCE INVENTORY OF
INLAND PRODUCTIONS PARCEL IN
T 8 S, R18 E, SEC. 33 AND
T 9 S, R 18 E, SEC. 3 & 4,
UINTAH COUNTIES, UTAH

BY:

Katie Simon
and
Keith R. Montgomery

Prepared For:

Bureau of Land Management
Vernal Field Office

Prepared Under Contract With:

Inland Production
Route 3, Box 3630
Myton, UT 84052

Prepared By:


Montgomery Archaeological Consultants
P.O. Box 147
Moab, Utah 84532

MOAC Report No. 03-154

February 3, 2004

United States Department of Interior (FLPMA)
Permit No. 03-UT-60122

State of Utah Antiquities Project (Survey)
Permit No. U-03-MQ-0799b

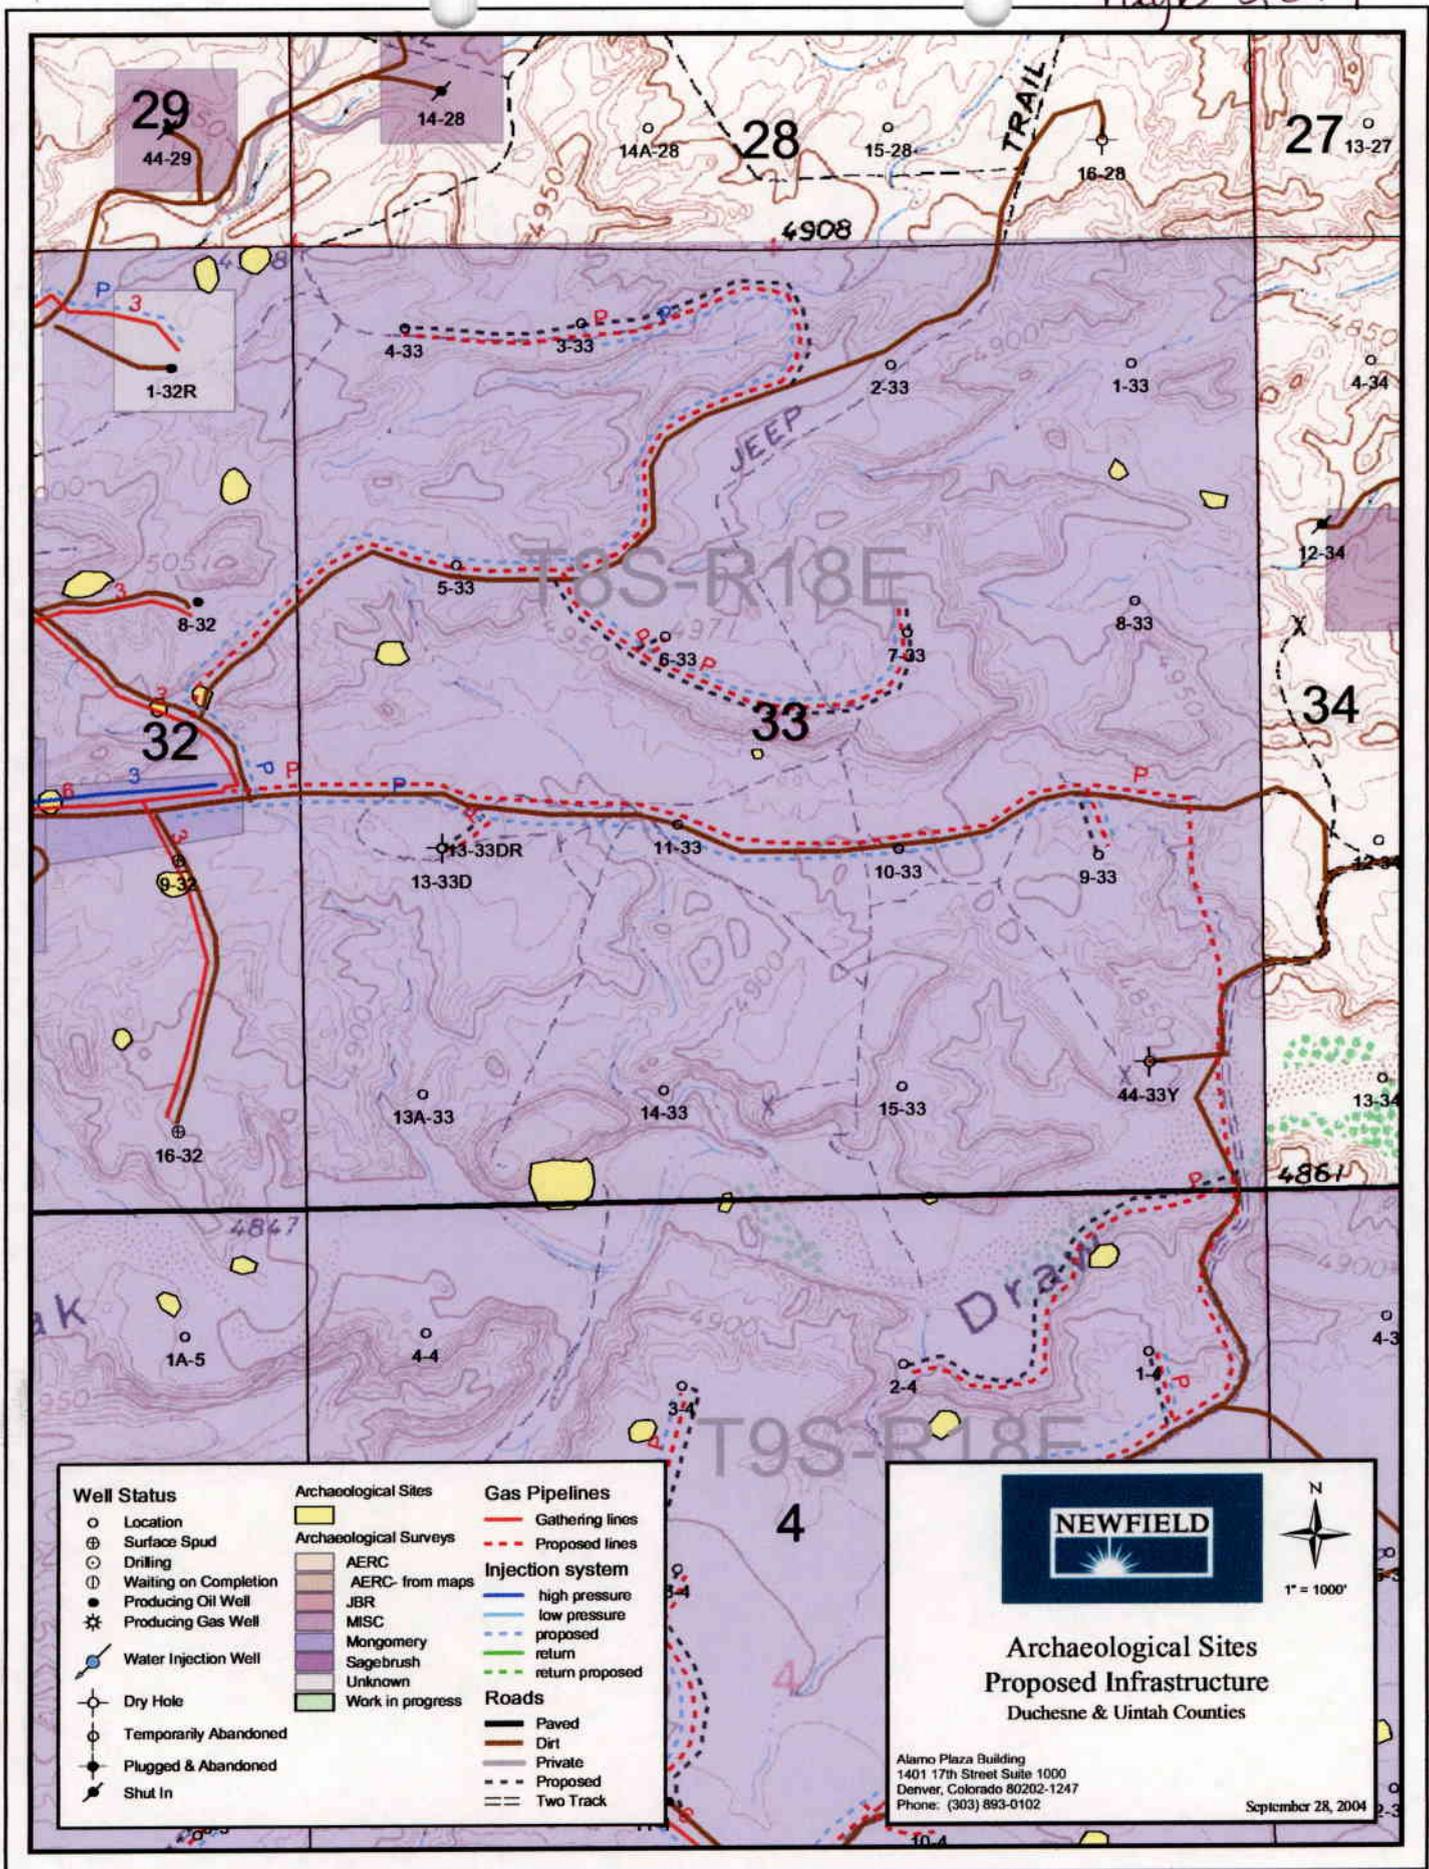

Well Status	Archaeological Sites	Gas Pipelines
○ Location	Archaeological Sites	— Gathering lines
⊕ Surface Spud	Archaeological Surveys	- - - Proposed lines
⊙ Drilling	AERC	— high pressure
⊙ Waiting on Completion	AERC from maps	— low pressure
● Producing Oil Well	JBR	- - - proposed
⊙ Producing Gas Well	MISC	— return
⊙ Water Injection Well	Mongomery	- - - return proposed
⊙ Dry Hole	Sagebrush	— Paved
⊙ Temporarily Abandoned	Unknown	— Dirt
⊙ Plugged & Abandoned	Work in progress	— Private
⊙ Shut In		- - - Proposed
		⊎ Two Track



**Archaeological Sites
Proposed Infrastructure**
Duchesne & Uintah Counties

Alamo Plaza Building
1401 17th Street Suite 1000
Denver, Colorado 80202-1247
Phone: (303) 893-0102

September 28, 2004

INLAND RESOURCES, INC.

**PALEONTOLOGICAL FIELD SURVEY OF PROPOSED
PRODUCTION DEVELOPMENT AREAS,
UINTAH COUNTY, UTAH**

(Section 33, T 8 S, R 18 E; & Section 6, T 9 S, R 19 E)

REPORT OF SURVEY

Prepared for:


Inland Resources, Inc.

Prepared by:

Wade E. Miller

Consulting Paleontologist

May 12, 2004

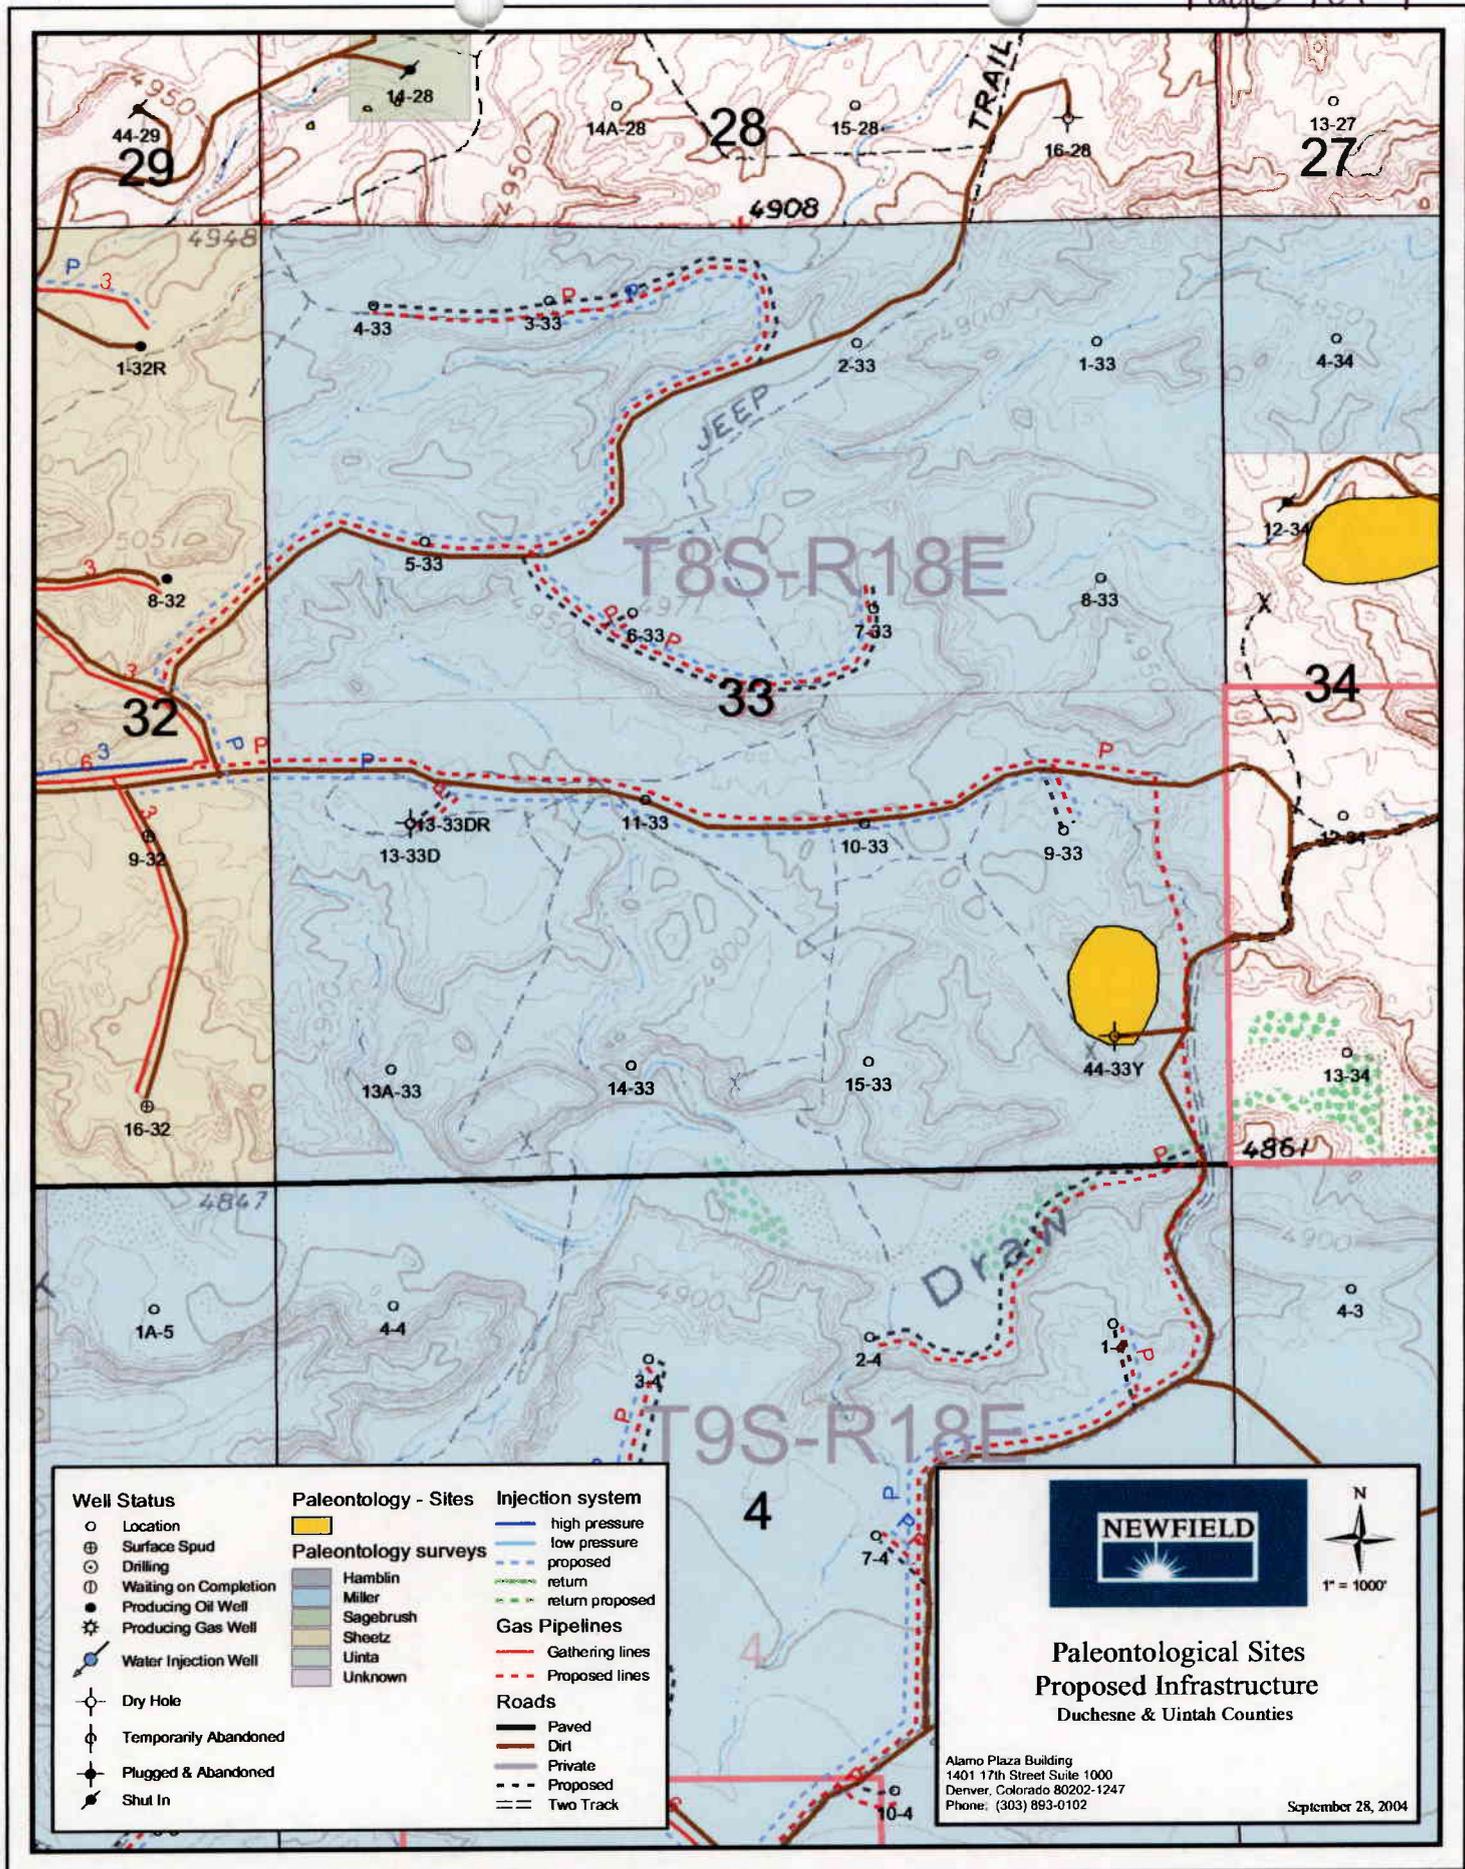

Well Status	Paleontology - Sites	Injection system
○ Location	Yellow box	Blue line: high pressure
⊕ Surface Spud	Paleontology surveys	Light blue line: low pressure
⊙ Drilling	Hamblin	Dashed blue line: proposed
⊖ Waiting on Completion	Miller	Green dashed line: return
● Producing Oil Well	Sagebrush	Green dashed line: return proposed
⊙ Producing Gas Well	Sheetz	Red dashed line: Gas Pipelines
⊙ Water Injection Well	Uinta	Red dashed line: Gathering lines
⊙ Dry Hole	Unknown	Red dashed line: Proposed lines
⊙ Temporarily Abandoned		Roads
⊙ Plugged & Abandoned		Black line: Paved
⊙ Shut In		Brown line: Dirt
		Grey line: Private
		Dashed grey line: Proposed
		Double line: Two Track



**Paleontological Sites
Proposed Infrastructure**
Duchesne & Uintah Counties

Alamo Plaza Building
1401 17th Street Suite 1000
Denver, Colorado 80202-1247
Phone: (303) 893-0102

September 28, 2004

WORKSHEET
APPLICATION FOR PERMIT TO DRILL

APD RECEIVED: 11/01/2004

API NO. ASSIGNED: 43-047-36036

WELL NAME: FEDERAL 1-33-8-18

OPERATOR: NEWFIELD PRODUCTION (N2695)

CONTACT: MANDIE CROZIER

PHONE NUMBER: 435-646-3721

PROPOSED LOCATION:

NENE 33 080S 180E
SURFACE: 0906 FNL 0705 FEL
BOTTOM: 0906 FNL 0705 FEL
UINTAH
8 MILE FLAT NORTH (590)

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-74872

SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: GRRV

COALBED METHANE WELL? NO

INSPECT LOCATN BY: / /		
Tech Review	Initials	Date
Engineering		
Geology		
Surface		

LATITUDE: 40.07921

LONGITUDE: -109.8909

RECEIVED AND/OR REVIEWED:

- Plat
- Bond: Fed[1] Ind[] Sta[] Fee[]
(No. UTU0056)
- Potash (Y/N)
- Oil Shale 190-5 (B) or 190-3 or 190-13
- Water Permit
(No. MUNICIPAL)
- RDCC Review (Y/N)
(Date: _____)
- Fee Surf Agreement (Y/N)

LOCATION AND SITING:


- _____ R649-2-3.
Unit _____
- _____ R649-3-2. General
Siting: 460 From Qtr/Qtr & 920' Between Wells
- R649-3-3. Exception
- _____ Drilling Unit
Board Cause No: _____
Eff Date: _____
Siting: _____
- _____ R649-3-11. Directional Drill

COMMENTS:

Sip, Separate file

STIPULATIONS:

*1- Federal Approval
2- Spacing Slip*

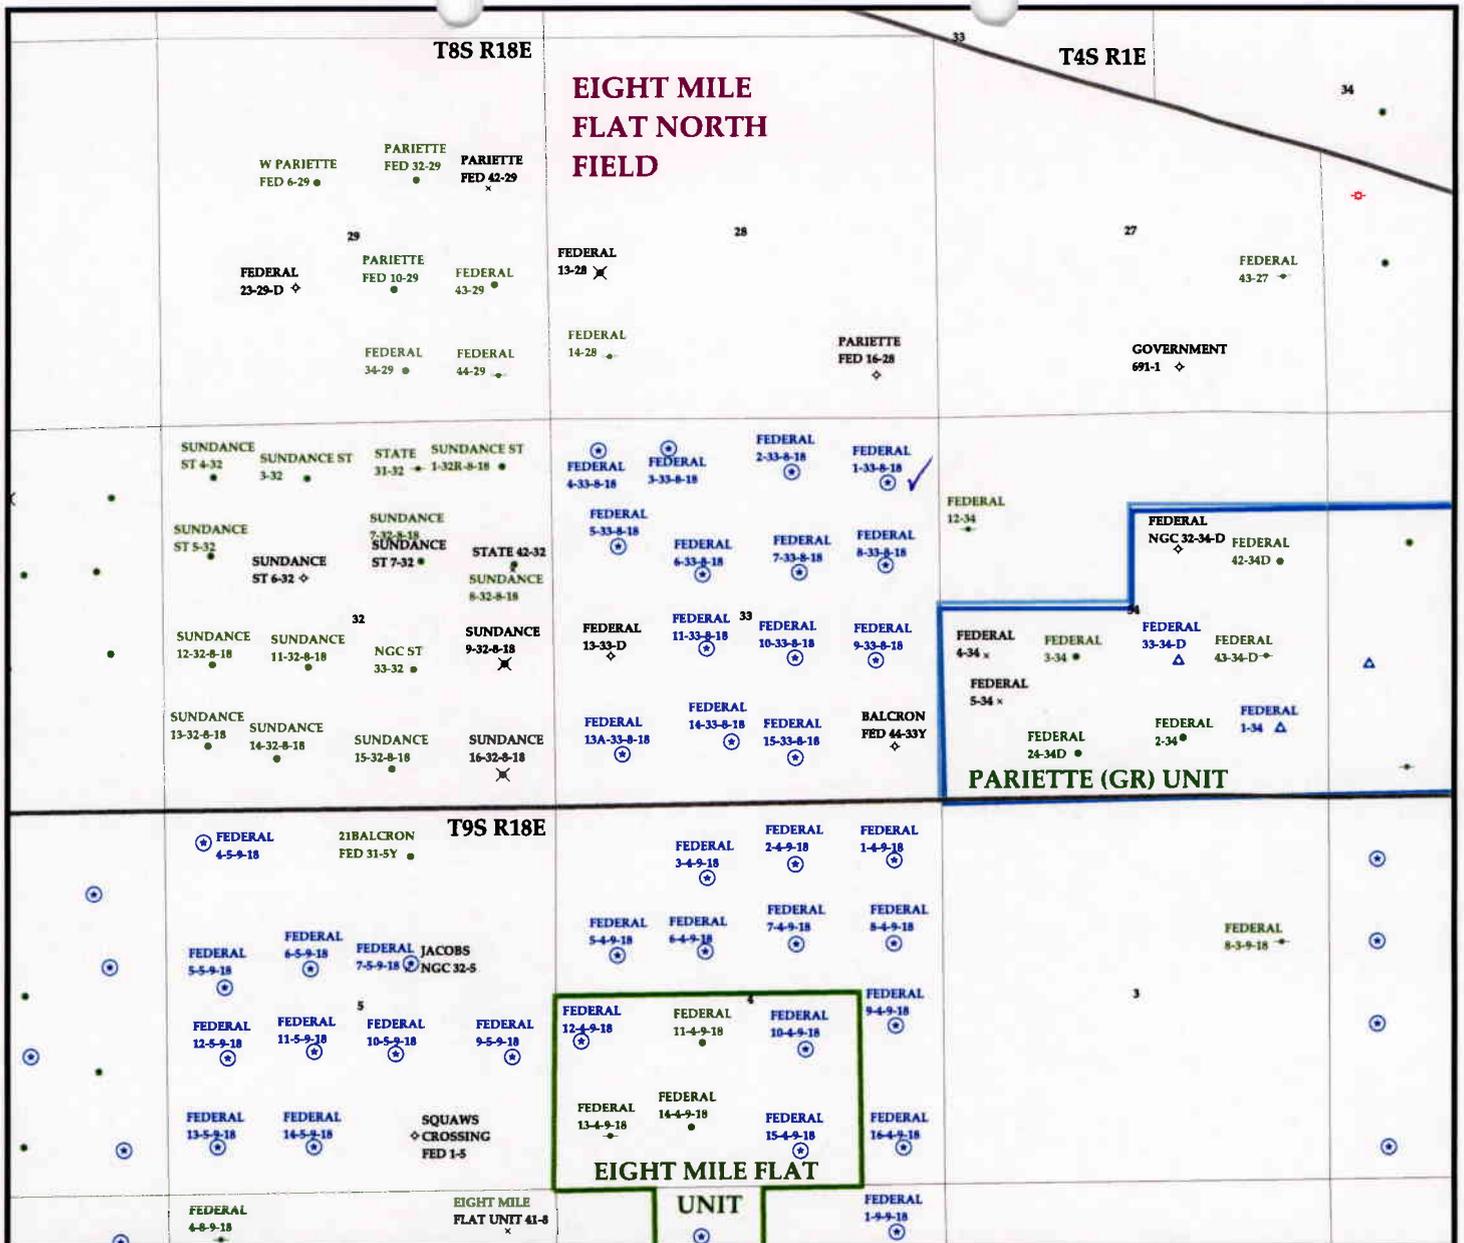


OPERATOR: NEWFIELD PROD CO (N2695)

SEC. 33 T.8S R.18E

FIELD: EIGHT MILE FLAT NORTH (590)

COUNTY: UINTAH

SPACING: R649-3-3 / EXCEPTION LOCATION



Utah Oil Gas and Mining

Wells	Units.shp	Fields.shp
⚡ GAS INJECTION	🟩 EXPLORATORY	⬜ ABANDONED
⚡ GAS STORAGE	🟪 GAS STORAGE	🟩 ACTIVE
✕ LOCATION ABANDONED	🟨 NF PP OIL	🟪 COMBINED
⊕ NEW LOCATION	🟩 NF SECONDARY	🟪 INACTIVE
⊕ PLUGGED & ABANDONED	🟩 PENDING	🟩 PROPOSED
⚡ PRODUCING GAS	🟩 PI OIL	🟩 STORAGE
● PRODUCING OIL	🟩 PP GAS	🟩 TERMINATED
⚡ SHUT-IN GAS	🟩 PP GEOTHERML	
⚡ SHUT-IN OIL	🟩 PP OIL	
✕ TEMP. ABANDONED	🟩 SECONDARY	
○ TEST WELL	🟩 TERMINATED	
⚡ WATER INJECTION		
⚡ WATER SUPPLY		
⚡ WATER DISPOSAL		



PREPARED BY: DIANA WHITNEY
DATE: 2-NOVEMBER-2004

002

NEWFIELD



November 1, 2004

Utah Division of Oil, Gas & Mining
P.O. Box 145801
Attn: Diana Whitney
Salt Lake City, Utah 84114-5801

Re: Exception Location: Federal 1-33-8-18
906' FNL, 705' FEL NENE Sec 33-T8S-18E
Uintah Cty., Utah; Lease UTU-74872

Dear Ms. Whitney:

Pursuant to Rule R649-3-3 of the Oil & Gas Rules and Regulations of the State of Utah, Newfield Production Company, Inc. hereby requests an exception location for the drilling of the captioned well. Rule R649-3-2 requires a well to be located in the center of a forty (40) acre quarter-quarter section, or a substantially equivalent lot or tract, with a tolerance of two hundred (200) feet in any direction from the center.

The above referenced location is an exception location under Rule 649-3-2, being 41' south of the drilling window tolerance for the NENE of Sec 33-T8S-R18E. The attached plat depicts the proposed drillsite location and illustrates the deviation from the drilling window, in accordance with Rule R649-3-2. The requested location has been selected to avoid a possible rapture nest.

RAPTOR

Please note the location is completely within Federal lease UTU-74872. The drillsite lease and all surrounding acreage within a four hundred sixty foot (460') radius of the proposed location is owned by Newfield Production Company.

If you have any questions or need additional information please contact me at (303)-382-4448. Thank you for your assistance in this matter.

Sincerely,
NEWFIELD PRODUCTION COMPANY

Laurie Deseau
Properties Administrator

RECEIVED

NOV 03 2004

DIV. OF OIL, GAS & MINING

005



State of Utah

Department of
Natural Resources

ROBERT L. MORGAN
Executive Director

Division of
Oil, Gas & Mining

LOWELL P. BRAXTON
Division Director

OLENE S. WALKER
Governor

GAYLE F. McKEACHNIE
Lieutenant Governor

November 3, 2004

Newfield Production Company
Rt. #3, Box 3630
Myton, UT 84052

Re: Federal 1-33-8-18 Well, 906' FNL, 705' FEL, NE NE, Sec. 33, T. 8 South,
R. 18 East, Uintah County, Utah


Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

Appropriate information has been submitted to DOGM and administrative approval of the requested exception location is hereby granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-047-36036.

Sincerely,



John R. Baza
Associate Director

pab
Enclosures

cc: Uintah County Assessor
Bureau of Land Management, Vernal District Office

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
Budget Bureau No. 1004-0135
Expires: March 31, 1993

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill or to deepen or reentry a different reservoir.
Use "APPLICATION FOR PERMIT -" for such proposals

5. Lease Designation and Serial No.

UTU-74872

6. If Indian, Allottee or Tribe Name

NA

7. If Unit or CA, Agreement Designation

SUNDANCE

8. Well Name and No.

FEDERAL 1-33-8-18

9. API Well No.

43-047-36036

10. Field and Pool, or Exploratory Area

8 MILE FLAT NORTH

11. County or Parish, State

UINTAH COUNTY, UT.

SUBMIT IN TRIPLICATE

1. Type of Well

Oil Well Gas Well Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3. Address and Telephone No.

Rt. 3 Box 3630, Myton Utah, 84052 435-646-3721

4. Location of Well (Footage, Sec., T., R., m., or Survey Description)

906 FNL 705 FEL NE/NE Section 33, T8S R18E

12. CHECK APPROPRIATE BOX(es) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION

Notice of Intent
 Subsequent Report
 Final Abandonment Notice

TYPE OF ACTION

Abandonment
 Recompletion
 Plugging Back
 Casing Repair
 Altering Casing
 Other Permit Extension

Change of Plans
 New Construction
 Non-Routine Fracturing
 Water Shut-Off
 Conversion to Injection
 Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)*

Newfield Production Company requests to extend the Permit to Drill this well for one year. The original approval date was 11/3/04 (expiration 11/3/05).

This APD has not been approved yet by the BLM.

Approved by the
Utah Division of
Oil, Gas and Mining

Date: 11-02-05
By: *[Signature]*

COPY SENT TO OPERATOR
Date: 11-8-05
Initials: CHD

14. I hereby certify that the foregoing is true and correct

Signed

[Signature]
Mandie Crozier

Regulatory Specialist

Date

10/27/2005

CC: UTAH DOGM

(This space for Federal or State office use)

Approved by

Title

Date

Conditions of approval, if any:

CC: Utah DOGM

RECEIVED

OCT 31 2005

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

DIV. OF OIL, GAS & MINING

**Application for Permit to Drill
Request for Permit Extension
Validation**

(this form should accompany the Sundry Notice requesting permit extension)

API: 43-047-36036
Well Name: Federal 1-33-8-18
Location: NE/NE Section 33, T8S R18E
Company Permit Issued to: Newfield Production Company
Date Original Permit Issued: 11/3/2004

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision.

Following is a checklist of some items related to the application, which should be verified.

If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes No NA

Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes No

Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes No

Have there been any changes to the access route including ownership, or right-of-way, which could affect the proposed location? Yes No

Has the approved source of water for drilling changed? Yes No

Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes No

Is bonding still in place, which covers this proposed well? Yes No

Mandi Cuzi
Signature

10/28/2005
Date

Title: Regulatory Specialist

Representing: Newfield Production Company

RECEIVED
OCT 31 2005
DIV. OF OIL, GAS & MINING

RECEIVED

NOV - 1 2004

BLM VERNAL, UTAH

Form 3160-3
(September 2001)

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

FORM APPROVED
OMB No. 1004-0136
Expires January 31, 2004

5. Lease Serial No. UTU-74872	
6. If Indian, Allottee or Tribe Name N/A	
7. If Unit or CA Agreement, Name and No. N/A	
8. Lease Name and Well No. Federal 1-33-8-18	
9. API Well No. 43-0A7-36036	
1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER	10. Field and Pool, or Exploratory Eight Mile Flat
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone	11. Sec., T., R., M., or Blk. and Survey or Area NE/NE Sec. 33, T8S R18E
2. Name of Operator Newfield Production Company	12. County or Parish Uintah
3a. Address Route #3 Box 3630, Myton UT 84052	13. State UT
3b. Phone No. (include area code) (435) 646-3721	14. Distance in miles and direction from nearest town or post office* Approximatley 23.1 miles south of Myton, Utah
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NE/NE 906' FNL 705' FEL At proposed prod. zone	15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 705' f/lse, NA f/unit
16. No. of Acres in lease 677.36	17. Spacing Unit dedicated to this well 40 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1,141'	19. Proposed Depth 6270'
20. BLM/BIA Bond No. on file UT 0056 - UTB000192	21. Elevations (Show whether DF, KDB, RT, GL, etc.) 4869.0' GL
22. Approximate date work will start* 1st Quarter 2005	23. Estimated duration Approximately seven (7) days from spud to rig release.

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- Well plat certified by a registered surveyor.
- A Drilling Plan.
- A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
- Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
- Operator certification.
- Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature <i>Lana Nebeker</i>	Name (Printed/Typed) Lana Nebeker	Date 10-28-04
Title Production Clerk		
Approved by (Signature) <i>Howard B. Cleavage</i>	Name (Printed/Typed)	Date 12/09/2005
Title Assistant Field Manager Mineral Resources	Office	

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

CONDITIONS OF APPROVAL ATTACHED

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

*(Instructions on reverse)

NOTICE OF APPROVAL RECEIVED

DEC 19 2005


DIV. OF OIL, GAS & MINING

UDOGM



UNITED STATES DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT
VERNAL FIELD OFFICE

170 South 500 East VERNAL, UT 84078 (435) 781-4400



**CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO
DRILL**

Company: Newfield Production Co.
Well No: Federal 1-33-8-18
API No: 43-047-36036

Location: NENE, Sec 33, T8S, R18E
Lease No: UTU-74872
Agreement: N/A

Petroleum Engineer:	Matt Baker	Office: 435-781-4490	Cell: 435-828-4470
Petroleum Engineer:	Michael Lee	Office: 435-781-4432	Cell: 435-828-7875
Supervisory Petroleum Technician:	Jamie Sparger	Office: 435-781-4502	Cell: 435-828-3913
Environmental Scientist:	Paul Buhler	Office: 435-781-4475	Cell: 435-828-4029
Environmental Scientist:	Karl Wright	Office: 435-781-4484	
Natural Resource Specialist:	Holly Villa	Office: 435-781-4404	
Natural Resource Specialist:	Melissa Hawk	Office: 435-781-4476	
After Hours Contact Number:	435-781-4513	Fax: 435-781-4410	

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations.

NOTIFICATION REQUIREMENTS

- | | | |
|--|---|--|
| Location Construction
(Notify Melissa Hawk) | - | Forty-Eight (48) hours prior to construction of location and access roads. |
| Location Completion
(Notify Melissa Hawk) | - | Prior to moving on the drilling rig. |
| Spud Notice
(Notify PE) | - | Twenty-Four (24) hours prior to spudding the well. |
| Casing String & Cementing
(Notify SPT) | - | Twenty-Four (24) hours prior to running casing and cementing all casing strings. |
| BOP & Related Equipment Tests
(Notify SPT) | - | Twenty-Four (24) hours prior to initiating pressure tests. |
| First Production Notice
(Notify PE) | - | Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days. |

***SURFACE USE PROGRAM
CONDITIONS OF APPROVAL (COAs)***

This well is being approved in accordance with Washington Instruction Memorandum 2005-247 and Section 390 (Category 3) of the Energy Policy Act which establishes statutory categorical exclusions (CX) under the National Environmental Policy Act (NEPA). Category 3 states that an oil or gas well can be drilled within a developed field for which an approved land use plan or any environmental document prepared pursuant to NEPA analyzed drilling as a reasonably foreseeable activity, so long as such plan or document was approved within five (5) years prior to the date of spudding the well. This well is covered under the *Final Environmental Impact Statement and Record of Decision Castle Peak and Eightmile Flat Oil and Gas Exploration Project Newfield Rocky Mountains Inc.*, signed November 21, 2005. If the well has not been spudded by November 21, 2010, a new environmental document will have to be prepared prior to the approval of the APD.

Due to the presence of Sclerocactus habitat in this area, a survey shall be conducted by a qualified botanist prior to construction to determine if Sclerocactus are present. If cactus plants are located in the areas proposed for disturbance, changes will need to be made to avoid cactus plants.

The construction of the access road and location shall be monitored by a certified paleontologist and a report of the findings provided to the Vernal Field Office of the Bureau of Land Management.

4 to 6 inches of topsoil shall be stripped from the location and placed where it can most easily be accessed for interim reclamation. Once the well has been converted to water injection, the fill slopes shall be recontoured and the topsoil shall be spread over the entire well location. The well location shall then be seeded with crested wheatgrass (Variety Hycrest) at a 12 lb/acre rate (pure live seed). After seeding has been completed, an access road loop to the well head can be established. The reserve pit will be allowed to stay open until interim reclamation is completed so the entire area can be seeded at the same time. The interim seeding of the well location and reserve pit shall be done by either drilling the seed or by broadcasting the seed and dragging it with a spike tooth harrow.

The pipeline trench shall be dug in the borrow ditch of the road and the trench material side cast into the existing vegetation. Both the water line and the gas line shall be buried in the same trench. When backfilling the trenches, care shall be taken to disturb as little of the vegetation as possible and thus allowing the existing plants to reestablish on their own, however, these disturbed areas shall also be seeded with crested wheatgrass at the 12 lb/acre rate to ensure vegetation establishment and to keep invasive weeds to a minimum. All seeding of the pipelines shall be completed using a seed drill.

The temporary gas lines used during the temporary production phase shall be laid on the surface, and then removed once the well is turned to water injection.

No pipeline construction will be allowed outside of already disturbed areas when soils are muddy and rutting of soils becomes apparent from the use of vehicles. If rutting occurs, operations must cease until soils are dry or frozen.

DOWNHOLE CONDITIONS OF APPROVAL

All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to. The following items are emphasized:

SITE SPECIFIC DOWNHOLE CONDITIONS OF APPROVAL

1. None.

DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS

1. There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well. Any changes in operation must have prior approval from the BLM, Vernal Field Office Petroleum Engineers.
2. The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
3. **Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.**
4. Blowout prevention equipment (BOPE) will remain in use until the well is completed or abandoned. Closing unit controls must remain unobstructed and readily accessible at all times. Choke manifolds must be located outside of the rig substructure.

All BOPE components will be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests must be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test must be reported in the driller's log.

BOP drills must be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.

Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.

No aggressive/fresh hard-banded drill pipe shall be used within casing.

5. All shows of fresh water and minerals will be reported and protected. A sample will be taken of any water flows and a water analysis furnished the BLM, Vernal Field Office. All oil and gas shows will be adequately tested for commercial possibilities, reported, and protected.

6. No location will be constructed or moved, no well will be plugged, and no drilling or workover equipment will be removed from a well to be placed in a suspended status without prior approval of the BLM, Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM, Vernal Field Office must be obtained and notification given before resumption of operations.
7. Chronologic drilling progress reports must be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.

Any change in the program must be approved by the BLM, Vernal Field Office. "Sundry Notices and Reports on Wells" (Form BLM 3160-5) must be filed for all changes of plans and other operations in accordance with 43 CFR 3162.3-2.

Emergency approval may be obtained orally, but such approval does not waive the written report requirement. Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, will require the filing of a suitable plan pursuant to Onshore Oil & Gas Order No. 1 of 43 CFR 3164.1 and prior approval by the BLM, Vernal Field Office.

In accordance with 43 CFR 3162.4-3, this well must be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.

8. Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) will be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, will be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) will be submitted only when requested by the BLM, Vernal Field Office.

Please submit an electronic copy of all logs run on this well in LAS format to UT_VN_Wellogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM. The cement bond log must be submitted in raster format (TIF, PDF other).

9. All off-lease storage, off-lease measurement, or commingling on-lease or off-lease will have prior written approval from the BLM, Vernal Field Office.

All measurement points shall be identified as point of sales or allocation for royalty determination prior to the installation of facilities.

10. Oil and gas meters will be calibrated in place prior to any deliveries. The Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports will be submitted to the BLM, Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement.
11. A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM, Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
12. This APD is approved subject to the requirement that, should the well be successfully completed for production, the BLM, Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
 - a. Operator name, address, and telephone number.
 - b. Well name and number.
 - c. Well location (¼¼, Sec., Twn, Rng, and P.M.).
 - d. Date well was placed in a producing status (date of first production for which royalty will be paid).
 - e. The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
 - f. The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
 - g. Unit agreement and / or participating area name and number, if applicable.
 - h. Communitization agreement number, if applicable.
13. Any venting or flaring of gas will be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from Field Office Petroleum Engineers.

14. All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events as defined in NTL3A, will be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production
15. Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.
16. Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

DIVISION OF OIL, GAS AND MINING

SPUDDING INFORMATION

Name of Company: NEWFIELD PRODUCTION COMPANY

Well Name: FEDERAL 1-33-8-18

Api No: 43-047-36036 Lease Type: FEDERAL

Section 33 Township 08S Range 18E County UINTAH

Drilling Contractor ROSS DRILLING RIG # 21

SPUDDED:

Date 04/04/06

Time 11:00 AM

How DRY

Drilling will Commence: _____

Reported by PERRY

Telephone # (435) 823-2072

Date 04/04/2006 Signed CHD

PAGE 02
INLAND
4356463031
04/06/2006 08:25

STATE OF UTAH
DIVISION OF OIL, GAS AND MINING
ENTITY ACTION FORM - FORM 6

OPERATOR: NEWFIELD PRODUCTION COMPANY
ADDRESS: RT. 3 BOX 3630
MYTON, UT 84052

OPERATOR ACCT. NO. N2895

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION					SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG	COUNTY		
A	99999	15293	4304735786	STATE 8-2-9-18	SE/NE	2	8S	18E	UINTAH	03/31/06	4/6/06
WELL 1 COMMENTS: <i>GRUV</i> — K											
A	99999	15294	4304736187	FEDERAL 9-19-9-18	NE/SE	19	8S	18E	UINTAH	3/30/06	4/6/06
WELL 2 COMMENTS: <i>GRUV</i> — K											
B	99999	14844	4304736037	FEDERAL 8-33-8-18	SE/NE	33	8S	18E	UINTAH	04/01/06	4/6/06
WELL 3 COMMENTS: <i>GRUV Sundance</i> — K											
B	99999	11486	4301333010	GILSONITE STATE H-32-8-17	SE/NE	12	8S	17E	DUCHESNE	04/03/06	4/6/06
WELL 4 COMMENTS: <i>GRUV</i> — K											
B	99999	14844	4304736036	FEDERAL 1-33-8-18	NE/NE	33	8S	18E	UINTAH	04/04/06	4/6/06
WELL 5 COMMENTS: <i>GRUV Sundance</i> — K											
B	99999	11486	4301333009	STATE G-32-8-18 17	SE/NE	32	8S	17E	DUCHESNE	04/04/06	4/6/06
WELL 6 COMMENTS: <i>GRUV</i> — K											

RECEIVED

APR 06 2006

DIVISION OF OIL, GAS & MINING

- ACTION CODES (See instructions on back of form)
- A - Establish new entity for new well (single well only)
 - B - Add interest to existing entity (group or unit well)
 - C - Re-assign well from one existing entity to another existing entity
 - D - Re-assign well from one existing entity to a new entity
 - E - Other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.


 Lana Nebeker
 Production Clerk
 April 6, 2006
 Title Date

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on reverse side

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
 NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
 Myton, UT 84052

3b. Phone No. (include are code)
 435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
 906 FNL 705 FEL
 NE/NE Section 33 T8S R18E

5. Lease Serial No.
 UTU74872

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or No.
 SUNDANCE UNIT

8. Well Name and No.
 FEDERAL 1-33-8-18

9. API Well No.
 4304736036

10. Field and Pool, or Exploratory Area
 Monument Butte

11. County or Parish, State
 Uintah, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input checked="" type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

Formation water is produced to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY**

I hereby certify that the foregoing is true and correct Name (Printed/ Typed) Mandie Crozier	Title Regulatory Specialist
Signature <i>Mandie Crozier</i>	Date 05/26/2006

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by	Title	Date
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED
MAY 30 2006
DIV. OF OIL, GAS & MINING

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

FORM APPROVED
OMB No. 1004-0135
Expires January 31, 2004

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an
abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on reverse side

1. Type of Well <input type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input checked="" type="checkbox"/> Other Unassigned		5. Lease Serial No. UTU74872
2. Name of Operator NEWFIELD PRODUCTION COMPANY		6. If Indian, Allottee or Tribe Name.
3a. Address Route 3 Box 3630 Myton, UT 84052	3b. Phone No. (include are code) 435.646.3721	7. If Unit or CA/Agreement, Name and/or No. SUNDANCE UNIT
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) 906 FNL 705 FEL NE/NE Section 33 T8S R18E		8. Well Name and No. FEDERAL 1-33-8-18
		9. API Well No. 4304736036
		10. Field and Pool, or Exploratory Area Monument Butte
		11. County or Parish, State Uintah, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 4/4/06 MIRU Ross # 24. Spud well @ 11:00am. Drill 310' of 12 1/4" hole with air mist. TIH W/ 7 Jt's 8 5/8" J-55 24 # csgn. Set @ 307.29 4/10/06 cement with 160 sks of class "G" w/ 3% CaCL2 + 1/4# sk Cello- Flake Mixed @ 15.8 ppg > 1.17 cf/ sk yeild. Returned 1.5 bbls cement to pit. WOC.

I hereby certify that the foregoing is true and correct Name (Printed/ Typed) Don Bastian	Title Drilling Foreman
Signature 	Date 04/11/2006

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____	Title _____	Date _____
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office _____	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED

APR 12 2006

DIV. OF OIL, GAS & MINING

NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

8 5/8 CASING SET AT 317.29

LAST CASING 8 5/8" set @ 317.29
 DATUM 12' KB
 DATUM TO CUT OFF CASING _____
 DATUM TO BRADENHEAD FLANGE _____
 TD DRILLER 310 LOGGER _____
 HOLE SIZE 12 1/4

OPERATOR Newfield Production Company
 WELL Federal 1-33-8-18
 FIELD/PROSPECT Monument Butte
 CONTRACTOR & RIG # Ross Rig #21

LOG OF CASING STRING:							
PIECES	OD	ITEM - MAKE - DESCRIPTION	WT / FT	GRD	THREAD	CONDT	LENGTH
		Shoe Joint 44.87'					
		WHI - 92 csg head			8rd	A	0.95
7	8 5/8"	Maverick ST&C csg	24#	J-55	8rd	A	305.44
		GUIDE shoe			8rd	A	0.9
CASING INVENTORY BAL.		FEET	JTS	TOTAL LENGTH OF STRING			307.29
TOTAL LENGTH OF STRING		307.29	7	LESS CUT OFF PIECE			2
LESS NON CSG. ITEMS		1.85		PLUS DATUM TO T/CUT OFF CSG			12
PLUS FULL JTS. LEFT OUT		0		CASING SET DEPTH			317.29
TOTAL		305.44	7	} COMPARE			
TOTAL CSG. DEL. (W/O THRDS)		305.44	7				
TIMING		1ST STAGE					
BEGIN RUN CSG.	Spud	4/4/2006	11:00am	GOOD CIRC THRU JOB <u>yes</u>			
CSG. IN HOLE		4/4/2006	5:12 PM	Bbls CMT CIRC TO SURFACE <u>1.5</u>			
BEGIN CIRC		4/10/2006	8:41am	RECIPROCATED PIPE FOR <u>N/A</u>			
BEGIN PUMP CMT		4/10/2006	8:48am				
BEGIN DSPL. CMT		4/10/2006	9:00am	BUMPED PLUG TO <u>537</u> PSI			
PLUG DOWN		4/10/2006	9:09am				
CEMENT USED		CEMENT COMPANY- B. J.					
STAGE	# SX	CEMENT TYPE & ADDITIVES					
1	160	Class "G" w/ 2% CaCL2 + 1/4#/sk Cello-Flake mixed @ 15.8 ppg 1.17 cf/sk yield					
CENTRALIZER & SCRATCHER PLACEMENT		SHOW MAKE & SPACING					
Centralizers - Middle first, top second & third for 3							

COMPANY REPRESENTATIVE Don Bastian DATE 4/10/2006

UNIT STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

5. Lease Serial No.
UTU74872

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or No.
SUNDANCE UNIT

8. Well Name and No.
FEDERAL 1-33-8-18

9. API Well No.
4304736036

10. Field and Pool, or Exploratory Area
Monument Butte

11. County or Parish, State
Uintah,UT

1. Type of Well
 Oil Well Gas Well Other Unassigned

2. Name of Operator
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
Myton, UT 84052

3b. Phone No. (include are code)
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
906 FNL 705 FEL
NE/NE Section 33 T8S R18E

12. CHECK APPROPRIATE BOX(ES) TO INIDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Weekly Status Report
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 4/20/06MIRU Union #14. Set all equipment. Pressure test Kelly, TIW, Choke manifold, & Bop's to 2,000 psi. Test 8.625 csgn to 1,500 psi. Vernal BLM field, & Roosevelt DOGM office was notified of test. PU BHA and tag cement @ 260'. Drill out cement & shoe. Drill a 7.875 hole with fresh water to a depth of 6205'. Lay down drill string & BHA. Open hole log w/ Dig/SP/GR log's TD to surface. PU & TIH with Guide shoe, shoe jt, float collar, 146jt's of 5.5 J-55, 15.5# csgn. Set @ 6189.19/ KB. Cement with 375 sks cement mixed @ 11.0 ppg & 3.43 yld. The 475 sks cement mixed @ 14.4 ppg & 1.24 yld. Returned 20 bbls of cement to reserve pit. Nipple down Bop's. Drop slips @ 106,000 #'s tension. Release rig @ 2:00 pm 4/25/06.

I hereby certify that the foregoing is true and correct Name (Printed/ Typed) Don Bastian	Title Drilling Foreman
Signature <i>Don Bastian</i>	Date 04/26/2006

APPROVED BY _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Approved by	Title	Date
	Office	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED

APR 28 2006

NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

5 1/2" CASING SET AT 6189.19

Flt cllr @ 6147.57'

LAST CASING 8 5/8" SET AT 317.29

OPERATOR Newfield Production Company

DATUM 12' KB

WELL Federal 1-33-8-18

DATUM TO CUT OFF CASING 12'

FIELD/PROSPECT / Monument Butte

DATUM TO BRADENHEAD FLANGE _____

CONTRACTOR & RIG # Union Rig #14

TD DRILLER 6150' Loggers TD 6205'

HOLE SIZE 7 7/8"

LOG OF CASING STRING:							
PIECES	OD	ITEM - MAKE - DESCRIPTION	WT / FT	GRD	THREAD	CONDT	LENGTH
		Landing Jt					14
	SHJT	5.90' @ 4363.10'					
145	5 1/2"	ETC LT & C casing	15.5#	J-55	8rd	A	6133.38
		Float collar					0.6
1	5 1/2"	ETC LT&C csg	15.5#	J-55	8rd	A	42.56
		GUIDE shoe			8rd	A	0.65
CASING INVENTORY BAL.		FEET	JTS	TOTAL LENGTH OF STRING			6191.19
TOTAL LENGTH OF STRING		6191.19	146	LESS CUT OFF PIECE			14
LESS NON CSG. ITEMS		15.25		PLUS DATUM TO T/CUT OFF CSG			12
PLUS FULL JTS. LEFT OUT		84.85	2	CASING SET DEPTH			6189.19
TOTAL		6260.79	148	} COMPARE			
TOTAL CSG. DEL. (W/O THRDS)		6260.79	148				
TIMING		1ST STAGE	2nd STAGE				
BEGIN RUN CSG.		1:30Am	4/25/2006	GOOD CIRC THRU JOB <u>Yes</u>			
CSG. IN HOLE		5:30AM	4/25/2006	Bbls CMT CIRC TO SURFACE <u>10</u>			
BEGIN CIRC		5:35Am	4/25/2006	RECIPROCATED PIPE FOR <u>THRUSTROKE</u>			
BEGIN PUMP CMT		7:58AM	4/25/2006	DID BACK PRES. VALVE HOLD ? <u>YES</u>			
BEGIN DSPL. CMT		8:57Am	4/25/06/	BUMPED PLUG TO <u>1640</u> PSI			
PLUG DOWN		9:20AM	4/25/2006				
CEMENT USED		CEMENT COMPANY- B. J.					
STAGE	# SX	CEMENT TYPE & ADDITIVES					
1	375	Premlite II w/ 10% gel + 3 % KCL, 5#s /sk CSE + 2# sk/kolseal + 1/2#s/sk Cello Flake					
		mixed @ 11.0 ppg W / 3.43 cf/sk yield					
2	475	50/50 poz W/ 2% Gel + 3% KCL, .5%EC1,1/4# sk C.F. 2% gel. 3% SM mixed @ 14.4 ppg W/ 1.24 YLD					
CENTRALIZER & SCRATCHER PLACEMENT			SHOW MAKE & SPACING				
Centralizers - Middle first, top second & third. Then every third collar for a total of 20.							

COMPANY REPRESENTATIVE Don Bastian

DATE 4/26/2006

(See other instructions on reverse side)

OMB NO. 1004-0137
Expires: February 28, 1995

**UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT**

WELL COMPLETION OR RECOMPLETION REPORT AND LOG*

1a. TYPE OF WORK
 OIL WELL GAS WELL DRY Other _____

1b. TYPE OF WELL
 NEW WELL WORK OVER DEEPEN PLUG BACK DIFF RESVR. Other _____

2. NAME OF OPERATOR
Newfield Exploration Company

3. ADDRESS AND TELEPHONE NO.
1401 17th St. Suite 1000 Denver, CO 80202

4. LOCATION OF WELL (Report locations clearly and in accordance with any State requirements.)*
 At Surface 906' FNL & 705' FEL (NE/NE) Sec. 33, T8S, R18E
 At top prod. Interval reported below

5. LEASE DESIGNATION AND SERIAL NO.
UTU-74872

6. IF INDIAN ALLOTTEE OR TRIBE NAME
NA

7. UNIT AGREEMENT NAME
Sundance Unit

8. FARM OR LEASE NAME, WELL NO.
Federal 1-33-8-18

9. WELL NO.
43-047-36036

10. FIELD AND POOL OR WILDCAT
Eight Mile Flat

11. SEC., T., R., M. OR BLOCK AND SURVEY OR AREA
Sec. 33, T8S, R18E

12. COUNTY OR PARISH
Uintah

13. STATE
UT

14. API NO. 43-047-36036 **DATE ISSUED** 11/3/04

15. DATE SPUDDED 4/4/06 **16. DATE T.D. REACHED** 4/24/06 **17. DATE COMPL. (Ready to prod.)** 5/23/06 **18. ELEVATIONS (DF, RKB, RT, GR, ETC.)*** 4869' GL 4879' KB **19. ELEV. CASINGHEAD**

20. TOTAL DEPTH, MD & TVD 6163' **21. PLUG BACK T.D., MD & TVD** 6170' **22. IF MULTIPLE COMPL. HOW MANY*** **23. INTERVALS DRILLED BY** -----> **ROTARY TOOLS** X **CABLE TOOLS**

24. PRODUCING INTERVAL(S) OF THIS COMPLETION--TOP, BOTTOM, NAME (MD AND TVD)*
Green River 4470'-6144'

25. WAS DIRECTIONAL SURVEY MADE
No

26. TYPE ELECTRIC AND OTHER LOGS RUN
Dual Induction Guard, SP, Compensated Density, Compensated Neutron, GR, Caliper, Cement Bond Log

27. WAS WELL CORED
No

CASING RECORD (Report all strings set in well)

CASING SIZE/GRADE	WEIGHT, LB./FT.	DEPTH SET (MD)	HOLE SIZE	TOP OF CEMENT, CEMENTING RECORD	AMOUNT PULLED
8-5/8" - J-55	24#	317'	12-1/4"	To surface with 160 sx Class "G" cmt	
5-1/2" - J-55	15.5#	6189'	7-7/8"	375 sx Premlite II and 475 sx 50/50 Poz	

LINER RECORD

SIZE	TOP (MD)	BOTTOM (MD)	SACKS CEMENT*	SCREEN (MD)

TUBING RECORD

SIZE	DEPTH SET (MD)	PACKER SET (MD)
2-7/8"	EOT @ 6091'	TA @ 5922'

31. PERFORATION RECORD (Interval, size and number)

INTERVAL	SIZE	SPF/NUMBER
(BSLS) 6060'-78', 6109'-16', 6120'-44'	.46"	4/196
(CP2) 5770'-77', 5798'-5812'	.43"	4/84
(D1&2) 4956'-61', 5022'-30'	.43"	4/52
(GB6) 4470'-4477'	.43"	4/28

32. ACID, SHOT, FRACTURE, CEMENT SQUEEZE, ETC.

DEPTH INTERVAL (MD)	AMOUNT AND KIND OF MATERIAL USED
6060'-6144'	Frac w/ 90.059# 20/40 sand in 824 bbls fluid
5770'-5812'	Frac w/ 90.362# 20/40 sand in 683 bbls fluid
4956'-5030'	Frac w/ 35.010# 20/40 sand in 383 bbls fluid
4470'-4477'	Frac w/ 32.182# 20/40 sand in 351 bbls fluid

33.* PRODUCTION

DATE FIRST PRODUCTION 5/23/06 **PRODUCTION METHOD** (Flowing, gas lift, pumping--size and type of pump) 2-1/2" x 1-1/2" x 14.5' RHAC SM Plunger Pump **WELL STATUS** (Producing or shut-in) PRODUCING

DATE OF TEST 30 day ave **HOURS TESTED** **CHOKE SIZE** **PROD'N. FOR TEST PERIOD** -----> **OIL--BBL.S.** 15 **GAS--MCF.** 5 **WATER--BBL.** 37 **GAS-OIL RATIO** 333

FLOW, TUBING PRESS. **CASING PRESSURE** **CALCULATED 24-HOUR RATE** -----> **OIL--BBL.** **GAS--MCF.** **WATER--BBL.** **OIL GRAVITY-API (CORR.)**

RECEIVED

34. DISPOSITION OF GAS (Sold, used for fuel, vented, etc.) Sold & Used for Fuel **TEST WITNESSED BY** JUL 03 2006

35. LIST OF ATTACHMENTS

36. I hereby certify that the foregoing and attached information is complete and correct as determined from all available records

SIGNED Mandie Crozier TITLE Regulatory Specialist DATE 6/26/2006

Mandie Crozier

DIV. OF OIL, GAS & MINING

*(See Instructions and Spaces for Additional Data on Reverse Side)

37. SUMMARY OF POROUS ZONES: (Show all important zones of porosity and contents thereof; cored intervals, and all drill-stem, tests, including depth interval tested, cushion used, time tool open, flowing and shut-in pressures, and recoveries);				38. GEOLOGIC MARKERS		
FORMATION	TOP	BOTTOM	DESCRIPTION, CONTENTS, ETC.	NAME	TOP	
					MEAS. DEPTH	TRUE VERT. DEPTH
			Well Name Federal 1-33-8-18	Garden Gulch Mkr	3892'	
				Garden Gulch 1	4113'	
				Garden Gulch 2	4232'	
				Point 3 Mkr	4505'	
				X Mkr	4721'	
				Y-Mkr	4756'	
				Douglas Creek Mkr	4897'	
				BiCarbonate Mkr	5172'	
				B Limestone Mkr	5320'	
				Castle Peak	5650'	
				Basal Carbonate	6060'	
				Total Depth (LOGGERS)	6205'	

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

1. Type of Well <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other		5. Lease Serial No. UTU74872
2. Name of Operator NEWFIELD PRODUCTION COMPANY		6. If Indian, Allottee or Tribe Name.
3a. Address Route 3 Box 3630 Myton, UT 84052	3b. Phone No. (include are code) 435.646.3721	7. If Unit or CA/Agreement, Name and/or No. SUNDANCE UNIT
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) 906 FNL 705 FEL NE/NE Section 33 T8S R18E		8. Well Name and No. FEDERAL 1-33-8-18
		9. API Well No. 4304736036
		10. Field and Pool, or Exploratory Area Monument Butte
		11. County or Parish, State Uintah, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Weekly Status Report
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

Status report for time period 05/16/06 - 05/23/06

Subject well had completion procedures initiated in the Green River formation on 05-16-06 without the use of a service rig over the well. A cement bond log was run and a total of four Green River intervals were perforated and hydraulically fracture treated with 20/40 mesh sand. Perforated intervals are as follows: Stage #1 (6120'-6144'),(6109'-6116'),(6060'-6078'); Stage #2 (5798'-5812'),(5770'-5777'); Stage #3 (5022'-5030'),(4956'-4961'); Stage #4 (4470'-4477'). All perforations, were 4 JSPF. Composite flow-through frac plugs were used between stages. Fracs were flowed back through chokes. A service rig was moved over the well on 05-18-2006. Bridge plugs were drilled out and well was cleaned to 6170'. Zones were swab tested for sand cleanup. A new 1 1/2" bore rod pump was run in well on sucker rods. Well was placed on production via rod pump on 05-23-2006.

I hereby certify that the foregoing is true and correct	Title
Name (Printed/ Typed) Lana Nebeker	Production Clerk
Signature 	Date 07/03/2006

Approved by	Title	Date
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on reverse)

RECEIVED
JUL 05 2006

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELLS
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on reverse side

1. Type of Well
 Oil Well Gas Well Other

2. Name of Operator
 NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630
 Myton, UT 84052

3b. Phone No. (include area code)
 435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)
 906 FNL 705 FEL
 NE/NE Section 33 T8S R18E

5. Lease Serial No.
 UTU74872

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or No.
 SUNDANCE UNIT

8. Well Name and No.
 FEDERAL 1-33-8-18

9. API Well No.
 4304736036

10. Field and Pool, or Exploratory Area
 Monument Butte

11. County or Parish, State
 Uintah, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input checked="" type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production(Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment Notice	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Variance _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation (clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomplete horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompletion in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

Newfield Production Company is requesting a variance from Onshore Order 43 CFR Part 3160 Section 4 requiring production tanks to be equipped with Enardo or equivalent vent line valves. Newfield operates wells that produce from the Green River formation, which are relatively low gas producers (20 mcfpd). The majority of the wells are equipped with a three phase separator to maximize gas separation and sales.

Newfield is requesting a variance for safety reasons. Crude oil production tanks equipped with back pressure devices will emit a surge of gas when the thief hatches are open. While gauging tanks, lease operators will be subject to breathing toxic gases as well as risk a fire hazard, under optimum conditions

*10/16/06
BM*

I hereby certify that the foregoing is true and correct Name (Printed/ Typed) Mandie Crozier	Title Regulatory Specialist
Signature <i>Mandie Crozier</i>	Date 05/26/2006

THIS SPACE FOR FEDERAL AGENCY USE **Accepted by the Utah Division of Oil, Gas and Mining** **Federal Approval Of This Action is Necessary**

Approved by _____ Date _____

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction.

Date: *6/12/06*
 By: *Josh K. Dert*

(Instructions on reverse)

RECEIVED
MAY 30 2006
 DIV. OF OIL, GAS & MINING



UNITED STATES ENVIRONMENTAL PROTECTION AGENCY

REGION 8
1595 WYNKOOP STREET
DENVER, CO 80202-1129
http://www.epa.gov/region8

NOV 20 2008

Ref: 8P-W-GW

CERTIFIED MAIL
RETURN RECEIPT REQUESTED

Eric Sundberg
Newfield Production Company
1001 Seventeenth Street, Suite 2000
Denver, CO 80202

Accepted by the
Utah Division of
Oil, Gas and Mining.
FOR RECORD ONLY

RECEIVED

DEC 02 2008

DIV. OF OIL, GAS & MINING

8S 18E 33
Re: Final Permit
EPA UIC Permit UT21100-07422
Federal 1-33-8-18
Uintah County, Utah
API No.: 43-047-36036

Dear Mr. Sundberg:

Enclosed is your copy of the FINAL Underground Injection Control (UIC) Permit for the proposed Federal 1-33-8-18 injection well. A Statement of Basis that discusses the conditions and requirements of this EPA UIC Permit, is also included.

The Public Comment period for this Permit ended on OCT 22 2008. No comments on the Draft Permit were received during the Public Notice period; therefore the Effective Date for this EPA UIC Permit is the date of issuance. All conditions set forth herein refer to Title 40 Parts 124, 144, 146, and 147 of the Code of Federal Regulations (CFR) and are regulations that are in effect as of the Effective Date of this Permit.

Please note that under the terms and conditions of this Final Permit you are authorized only to construct the proposed injection well. Prior to commencing injection, you first must fulfill all "Prior to Commencing Injection" requirements of the Final Permit, Part II Section C.1, and obtain written Authorization to Inject from the EPA. It is your responsibility to be familiar with and to comply with all provisions of your Final Permit. The EPA forms referenced in the permit are available at http://www.epa.gov/safewater/uic/reportingforms.html. Guidance documents for Cement Bond Logging, Radioactive Tracer testing, Step Rate testing, Mechanical Integrity demonstration, Procedure in the Event of a Mechanical Integrity Loss, and other UIC guidances, are available at http://www.epa.gov/region8/water/uic/deep_injection.html. Upon request, hard copies of the EPA forms and guidances can be provided.


This EPA UIC Permit is issued for the operating life of the well unless terminated (Part III, Section B). The EPA may review this Permit at least every five (5) years to determine whether any action is warranted pursuant to 40 CFR § 144.36(a).

If you have any questions on the enclosed Final Permit or Statement of Basis, please call Emmett Schmitz of my staff at (303) 312-6174, or toll-free at (800) 227-8917, ext. 312-6174.

NOV 10 2003

FOR RECORD ONLY

Sincerely,



Stephen S. Tuber
Assistant Regional Administrator
Office of Partnerships and Regulatory Assistance

enclosure: Final UIC Permit
Statement of Basis

cc: Letter only:

Uintah & Ouray Business Committee, Ute Indian Tribe:
Curtis Cesspooch, Chairman
Irene Cuch, Vice-Chairwoman
Frances Poowegup, Councilwoman
Ronald Groves, Councilman
Phillip Chimburas, Councilman
Steven Cesspooch, Councilman

Daniel Picard, Superintendent
Uintah & Ouray Indian Agency
U.S. Bureau of Indian Affairs

cc: all enclosures:

Michael Guinn
District Manager
Newfield Production Company
Myton, Utah

Larry Love
Director
Energy & Minerals Dept.
Ute Indian Tribe

Elaine Willie
Gap Coordinatorr
Ute Indian Tribe

Michelle Sabori
Acting Director
Land Use Dept.
Ute Indian Tribe

Gilbert Hunt
Assistant Director
State of Utah - Natural Resources

Fluid Minerals Engineering Dept.
U.S. Bureau of Land Management
Vernal, Utah





**UNDERGROUND INJECTION CONTROL PROGRAM
PERMIT**

PREPARED: November 2008

Permit No. UT21100-07422

Class II Enhanced Oil Recovery Injection Well

**Federal 1-33-8-18
Uintah County, UT**

Issued To

Newfield Production Company
1001 Seventeenth Street, Suite 2000
Denver, CO 80202

PART I. AUTHORIZATION TO CONSTRUCT AND OPERATE	2
PART II. SPECIFIC PERMIT CONDITIONS	3
Section A. WELL CONSTRUCTION REQUIREMENTS	3
1. Casing and Cement	3
2. Injection Tubing and Packer	3
3. Sampling and Monitoring Devices	3
4. Well Logging and Testing	4
5. Postponement of Construction or Conversion	4
6. Workovers and Alterations	4
Section B. MECHANICAL INTEGRITY	4
1. Demonstration of Mechanical Integrity (MI)	5
2. Mechanical Integrity Test Methods and Criteria	5
3. Notification Prior to Testing	5
4. Loss of Mechanical Integrity	5
Section C. WELL OPERATION	6
1. Requirements Prior to Commencing Injection	6
2. Injection Interval	6
3. Injection Pressure Limitation	6
4. Injection Volume Limitation	7
5. Injection Fluid Limitation	7
6. Tubing-Casing Annulus (TCA)	7
Section D. MONITORING, RECORDKEEPING, AND REPORTING OF RESULTS	7
1. Monitoring Parameters, Frequency, Records and Reports	7
2. Monitoring Methods	7
3. Records Retention	8
4. Annual Reports	8
Section E. PLUGGING AND ABANDONMENT	8
1. Notification of Well Abandonment, Conversion or Closure	9
2. Well Plugging Requirements	9
3. Approved Plugging and Abandonment Plan	9
4. Forty Five (45) Day Notice of Plugging and Abandonment	9
5. Plugging and Abandonment Report	9
6. Inactive Wells	9

PART III. CONDITIONS APPLICABLE TO ALL PERMITS	11
Section A. EFFECT OF PERMIT	11
Section B. CHANGES TO PERMIT CONDITIONS	11
1. Modification, Reissuance, or Termination	11
2. Conversions	11
3. Transfer of Permit	11
4. Permittee Change of Address	12
5. Construction Changes, Workovers, Logging and Testing Data	12
Section C. SEVERABILITY	12
Section D. CONFIDENTIALITY	12
Section E. GENERAL PERMIT REQUIREMENTS	12
1. Duty to Comply	12
2. Duty to Reapply	13
3. Need to Halt or Reduce Activity Not a Defense	13
4. Duty to Mitigate	13
5. Proper Operation and Maintenance	13
6. Permit Actions	13
7. Property Rights	13
8. Duty to Provide Information	13
9. Inspection and Entry	13
10. Signatory Requirements	14
11. Reporting requirements	14
Section F. FINANCIAL RESPONSIBILITY	15
1. Method of Providing Financial Responsibility	15
2. Insolvency	15
APPENDIX A - WELL CONSTRUCTION REQUIREMENTS	A-1
APPENDIX B - LOGGING AND TESTING REQUIREMENTS	B-1
APPENDIX C - OPERATING REQUIREMENTS	C-1
APPENDIX D - MONITORING AND REPORTING REQUIREMENTS	D-1
APPENDIX E - PLUGGING AND ABANDONMENT REQUIREMENTS	E-1
APPENDIX F - CORRECTIVE ACTION REQUIREMENTS	F-1

Part I. AUTHORIZATION TO CONSTRUCT AND OPERATE

Under the authority of the Safe Drinking Water Act and Underground Injection Control (UIC) Program regulations of the U. S. Environmental Protection Agency (EPA) codified at Title 40 of the Code of Federal Regulations (40 CFR) Parts 2, 124, 144, 146, and 147, and according to the terms of this Permit,

Newfield Production Company
1001 Seventeenth Street, Suite 2000
Denver, CO 80202

is authorized to construct and to operate the following Class II injection well or wells:

Federal 1-33-8-18
906' FNL & 705' FEL, NENE S33, T8S, R18E
Uintah County, UT

EPA regulates the injection of fluids into injection wells so that injection does not endanger underground sources of drinking water (USDWs). EPA UIC Permit conditions are based on authorities set forth at 40 CFR Parts 144 and 146, and address potential impacts to USDWs.

Under 40 CFR Part 144, Subpart D, certain conditions apply to all UIC Permits and may be incorporated either expressly or by reference. General permit conditions for which the content is mandatory and not subject to site-specific differences are not discussed in this document. Issuance of this Permit does not convey any property rights of any sort or any exclusive privilege, nor does it authorize injury to persons or property or invasion of other private rights, or any infringement of other Federal, State or local laws or regulations. (40 CFR §144.35) An EPA UIC Permit may be issued for the operating life of the injection well or project unless terminated for reasonable cause under 40 CFR §§144.39, 144.40 and 144.41, and may be reviewed at least once every five (5) years to determine if action is required under 40 CFR §144.36(a).

This Permit is issued for the life of the well(s) unless modified, revoked and reissued, or terminated under 40 CFR 144.39 or 144.40. This EPA Permit may be adopted, modified, revoked and reissued, or terminated if primary enforcement authority for a UIC Program is delegated to an Indian Tribe or State. Upon the effective date of delegation, reports, notifications, questions and other correspondence should be directed to the Indian Tribe or State Director.

Issue Date: NOV 20 2008

Effective Date NOV 20 2008



for Stephen S. Tuber
Assistant Regional Administrator*
Office of Partnerships and Regulatory Assistance

*NOTE: The person holding this title is referred to as the "Director" throughout this Permit.

PART II. SPECIFIC PERMIT CONDITIONS

Section A. WELL CONSTRUCTION REQUIREMENTS

These requirements represent the approved minimum construction standards for well casing and cement, injection tubing, and packer.

Details of the approved well construction plan are incorporated into this Permit as APPENDIX A. Changes to the approved plan that may occur during construction must be approved by the Director prior to being physically incorporated.

1. Casing and Cement.

The well or wells shall be cased and cemented to prevent the movement of fluids into or between underground sources of drinking water. The well casing and cement shall be designed for the life expectancy of the well and of the grade and size shown in APPENDIX A. Remedial cementing may be required if shown to be inadequate by cement bond log or other attempted demonstration of Part II (External) mechanical integrity.

2. Injection Tubing and Packer.

Injection tubing is required, and shall be run and set with a packer at or below the depth indicated in APPENDIX A. The packer setting depth may be changed provided it remains below the depth indicated in APPENDIX A and the Permittee provides notice and obtains the Director's approval for the change.

3. Sampling and Monitoring Devices.

The Permittee shall install and maintain in good operating condition:

- (a) a "tap" at a conveniently accessible location on the injection flow line between the pump house or storage tanks and the injection well, isolated by shut-off valves, for collection of representative samples of the injected fluid; and
- (b) one-half (1/2) inch female iron pipe fitting, isolated by shut-off valves and located at the wellhead at a conveniently accessible location, for the attachment of a pressure gauge capable of monitoring pressures ranging from normal operating pressures up to the Maximum Allowable Injection Pressure specified in APPENDIX C:
 - (i) on the injection tubing; and
 - (ii) on the tubing-casing annulus (TCA); and
- (c) a pressure actuated shut-off device attached to the injection flow line set to shut-off the injection pump when or before the Maximum Allowable Injection Pressure (MAIP) specified in APPENDIX C is reached at the wellhead; and
- (d) a non-resettable cumulative volume recorder attached to the injection line.

4. Well Logging and Testing

Well logging and testing requirements are found in APPENDIX B. The Permittee shall ensure the log and test requirements are performed within the time frames specified in APPENDIX B. Well logs and tests shall be performed according to current EPA-approved procedures. Well log and test results shall be submitted to the Director within sixty (60) days of completion of the logging or testing activity, and shall include a report describing the methods used during logging or testing and an interpretation of the test or log results.

5. Postponement of Construction or Conversion

The Permittee shall complete well construction within one year of the Effective Date of the Permit, or in the case of an Area Permit within one year of Authorization of the additional well. Authorization to construct and operate shall expire if the well has not been constructed within one year of the Effective Date of the Permit or Authorization and the Permit may be terminated under 40 CFR 144.40, unless the Permittee has notified the Director and requested an extension prior to expiration. Notification shall be in writing, and shall state the reasons for the delay and provide an estimated completion date. Once Authorization has expired under this part, the complete permit process including opportunity for public comment may be required before Authorization to construct and operate may be reissued.

6. Workovers and Alterations

Workovers and alterations shall meet all conditions of the Permit. Prior to beginning any addition or physical alteration to an injection well that may significantly affect the tubing, packer or casing, the Permittee shall give advance notice to the Director and obtain the Director's approval. The Permittee shall record all changes to well construction on a Well Rework Record (EPA Form 7520-12), and shall provide this and any other record of well workover, logging, or test data to EPA within sixty (60) days of completion of the activity.

A successful demonstration of Part I MI is required following the completion of any well workover or alteration which affects the casing, tubing, or packer. Injection operations shall not be resumed until the well has successfully demonstrated mechanical integrity and the Director has provided written approval to resume injection.

Section B. MECHANICAL INTEGRITY

The Permittee is required to ensure each injection well maintains mechanical integrity at all times. The Director, by written notice, may require the Permittee to comply with a schedule describing when mechanical integrity demonstrations shall be made.

An injection well has mechanical integrity if:

- (a) There is no significant leak in the casing, tubing, or packer (Part I); and
- (b) There is no significant fluid movement into an underground source of drinking water through vertical channels adjacent to the injection well bore (Part II).

1. Demonstration of Mechanical Integrity (MI).

The operator shall demonstrate MI prior to commencing injection and periodically thereafter. Well-specific conditions dictate the methods and the frequency for demonstrating MI and are discussed in the Statement of Basis. The logs and tests are designed to demonstrate both internal (Part I) and external (Part II) MI as described above. The conditions present at this well site warrant the methods and frequency required in Appendix B of this Permit.

In addition to these regularly scheduled demonstrations of MI, the operator shall demonstrate internal (Part I) MI after any workover which affects the tubing, packer or casing.

The Director may require additional or alternative tests if the results presented by the operator are not satisfactory to the Director to demonstrate there is no movement of fluid into or between USDWs resulting from injection activity. Results of MI tests shall be submitted to the Director as soon as possible but no later than sixty (60) days after the test is complete.

2. Mechanical Integrity Test Methods and Criteria

EPA-approved methods shall be used to demonstrate mechanical integrity. Ground Water Section Guidance No. 34 "Cement Bond Logging Techniques and Interpretation", Ground Water Section Guidance No. 37, "Demonstrating Part II (External) Mechanical Integrity for a Class II injection well permit", and Ground Water Section Guidance No. 39, "Pressure Testing Injection Wells for Part I (Internal) Mechanical Integrity" are available from EPA and will be provided upon request.

The Director may stipulate specific test methods and criteria best suited for a specific well construction and injection operation.

3. Notification Prior to Testing.

The Permittee shall notify the Director at least 30 days prior to any scheduled mechanical integrity test. The Director may allow a shorter notification period if it would be sufficient to enable EPA to witness the mechanical integrity test. Notification may be in the form of a yearly or quarterly schedule of planned mechanical integrity tests, or it may be on an individual basis.

4. Loss of Mechanical Integrity.

If the well fails to demonstrate mechanical integrity during a test, or a loss of mechanical integrity becomes evident during operation (such as presence of pressure in the TCA, water flowing at the surface, etc.), the Permittee shall notify the Director within 24 hours (see Part III Section E Paragraph 11(e) of this Permit) and the well shall be shut-in within 48 hours unless the Director requires immediate shut-in.

Within five days, the Permittee shall submit a follow-up written report that documents test results, repairs undertaken or a proposed remedial action plan.

Injection operations shall not be resumed until after the well has successfully been repaired and demonstrated mechanical integrity, and the Director has provided approval to resume injection.

Section C. WELL OPERATION

INJECTION BETWEEN THE OUTERMOST CASING PROTECTING UNDERGROUND SOURCES OF DRINKING WATER AND THE WELL BORE IS PROHIBITED.

Injection is approved under the following conditions:

1. Requirements Prior to Commencing Injection.

Well injection, including for new wells authorized by an Area Permit under 40 CFR 144.33 (c), may commence only after all well construction and pre-injection requirements herein have been met and approved. The Permittee may not commence injection until construction is complete, and

- (a) The Permittee has submitted to the Director a notice of completion of construction and a completed EPA Form 7520-10 or 7520-12; all applicable logging and testing requirements of this Permit (see APPENDIX B) have been fulfilled and the records submitted to the Director; mechanical integrity pursuant to 40 CFR 146.8 and Part II Section B of this Permit has been demonstrated; and
 - (i) The Director has inspected or otherwise reviewed the new injection well and finds it is in compliance with the conditions of the Permit; or
 - (ii) The Permittee has not received notice from the Director of his or her intent to inspect or otherwise review the new injection well within 13 days of the date of the notice in Paragraph 1a, in which case prior inspection or review is waived and the Permittee may commence injection.

2. Injection Interval.

Injection is permitted only within the approved injection interval, listed in APPENDIX C. Additional individual injection perforations may be added provided that they remain within the approved injection interval and the Permittee provides notice to the Director in accordance with Part II, Section A, Paragraph 6.

3. Injection Pressure Limitation

- (a) The permitted Maximum Allowable Injection Pressure (MAIP), measured at the wellhead, is found in APPENDIX C. Injection pressure shall not exceed the amount the Director determines is appropriate to ensure that injection does not initiate new fractures or propagate existing fractures in the confining zone adjacent to USDWs. In no case shall injection pressure cause the movement of injection or formation fluids into a USDW.
- (b) The Permittee may request a change of the MAIP, or the MAIP may be increased or decreased by the Director in order to ensure that the requirements in Paragraph (a) above are fulfilled. The Permittee may be required to conduct a step rate injection test or other suitable test to provide information for determining the fracture pressure of the injection zone. Change of the permitted MAIP by the Director shall be by modification of this Permit and APPENDIX C.

4. Injection Volume Limitation.

Injection volume is limited to the total volume specified in APPENDIX C.

5. Injection Fluid Limitation.

Injected fluids are limited to those identified in 40 CFR 144.6(b)(2) as fluids used for enhanced recovery of oil or natural gas, including those which are brought to the surface in connection with conventional oil or natural gas production that may be commingled with waste waters from gas plants which are an integral part of production operations unless those waters are classified as a hazardous waste at the time of injection, pursuant to 40 CFR 144.6(b). Non-exempt wastes, including unused fracturing fluids or acids, gas plant cooling tower cleaning wastes, service wastes and vacuum truck wastes, are NOT approved for injection. This well is NOT approved for commercial brine injection, industrial waste fluid disposal or injection of hazardous waste as defined by CFR 40 Part 261. The Permittee shall provide a listing of the sources of injected fluids in accordance with the reporting requirements in Part II Section D Paragraph 4 and APPENDIX D of this Permit.

6. Tubing-Casing Annulus (TCA)

The tubing-casing annulus (TCA) shall be filled with water treated with a corrosion inhibitor, or other fluid approved by the Director. The TCA valve shall remain closed during normal operating conditions and the TCA pressure shall be maintained at zero (0) psi.

If TCA pressure cannot be maintained at zero (0) psi, the Permittee shall follow the procedures in Ground Water Section Guidance No. 35 "Procedures to follow when excessive annular pressure is observed on a well."

Section D. MONITORING, RECORDKEEPING, AND REPORTING OF RESULTS

1. Monitoring Parameters, Frequency, Records and Reports.

Monitoring parameters are specified in APPENDIX D. Pressure monitoring recordings shall be taken at the wellhead. The listed parameters are to be monitored, recorded and reported at the frequency indicated in APPENDIX D even during periods when the well is not operating.

Monitoring records must include:

- (a) the date, time, exact place and the results of the observation, sampling, measurement, or analysis, and;
- (b) the name of the individual(s) who performed the observation, sampling, measurement, or analysis, and;
- (c) the analytical techniques or methods used for analysis.

2. Monitoring Methods.

- (a) Monitoring observations, measurements, samples, etc. taken for the purpose of complying with these requirements shall be representative of the activity or condition being monitored.

- (b) Methods used to monitor the nature of the injected fluids must comply with analytical methods cited and described in Table 1 of 40 CFR 136.3 or Appendix III of 40 CFR 261, or by other methods that have been approved in writing by the Director.
- (c) Injection pressure, annulus pressure, injection rate, and cumulative injected volumes shall be observed and recorded at the wellhead under normal operating conditions, and all parameters shall be observed simultaneously to provide a clear depiction of well operation.
- (d) Pressures are to be measured in pounds per square inch (psi).
- (e) Fluid volumes are to be measured in standard oil field barrels (bbl).
- (f) Fluid rates are to be measured in barrels per day (bbl/day).

3. Records Retention.

- (a) Records of calibration and maintenance, and all original strip chart recordings for continuous monitoring instrumentation, copies of all reports required by this permit, and records of all data used to complete the application for this permit shall be retained for a period of AT LEAST THREE (3) YEARS from the date of the sample, measurement, report, or application. This period may be extended anytime prior to its expiration by request of the Director.
- (b) Records of the nature and composition of all injected fluids must be retained until three (3) years after the completion of any plugging and abandonment (P&A) procedures specified under 40 CFR 144.52(a)(6) or under Part 146 Subpart G, as appropriate. The Director may require the Permittee to deliver the records to the Director at the conclusion of the retention period. The Permittee shall continue to retain the records after the three (3) year retention period unless the Permittee delivers the records to the Director or obtains written approval from the Director to discard the records.

4. Annual Reports.

Whether the well is operating or not, the Permittee shall submit an Annual Report to the Director that summarizes the results of the monitoring required by Part II Section D and APPENDIX D.

The first Annual Report shall cover the period from the effective date of the Permit through December 31 of that year. Subsequent Annual Reports shall cover the period from January 1 through December 31 of the reporting year. Annual Reports shall be submitted by February 15 of the year following data collection. EPA Form 7520-11 may be copied and shall be used to submit the Annual Report, however, the monitoring requirements specified in this Permit are mandatory even if EPA Form 7520-11 indicates otherwise.

Section E. PLUGGING AND ABANDONMENT

1. Notification of Well Abandonment, Conversion or Closure.

The Permittee shall notify the Director in writing at least forty-five (45) days prior to: 1) plugging and abandoning an injection well, 2) converting to a non-injection well, and 3) in the case of an Area Permit, before closure of the project.

2. Well Plugging Requirements

Prior to abandonment, the injection well shall be plugged with cement in a manner which isolates the injection zone and prevents the movement of fluids into or between underground sources of drinking water, and in accordance with 40 CFR 146.10 and other applicable Federal, State or local law or regulations. Tubing, packer and other downhole apparatus shall be removed. Cement with additives such as accelerators and retarders that control or enhance cement properties may be used for plugs; however, volume-extending additives and gel cements are not approved for plug use. Plug placement shall be verified by tagging. Plugging gel of at least 9.6 lb/gal shall be placed between all plugs. A minimum 50 ft surface plug shall be set inside and outside of the surface casing to seal pathways for fluid migration into the subsurface. The Plugging Record must be certified as accurate and complete by the person responsible for the plugging operation. Prior to placement of the cement plug(s) the well shall be in a state of static equilibrium with the mud weight equalized top to bottom, either by circulating the mud in the well at least once or by a comparable method prescribed by the Director.

3. Approved Plugging and Abandonment Plan.

The approved plugging and abandonment plan is incorporated into this Permit as APPENDIX E. Changes to the approved plugging and abandonment plan must be approved by the Director prior to beginning plugging operations. The Director also may require revision of the approved plugging and abandonment plan at any time prior to plugging the well.

4. Forty Five (45) Day Notice of Plugging and Abandonment.

The Permittee shall notify the Director at least forty-five (45) days prior to plugging and abandoning a well and provide notice of any anticipated change to the approved plugging and abandonment plan.

5. Plugging and Abandonment Report.

Within sixty (60) days after plugging a well, the Permittee shall submit a report (EPA Form 7520-13) to the Director. The plugging report shall be certified as accurate by the person who performed the plugging operation. Such report shall consist of either:

- (a) A statement that the well was plugged in accordance with the approved plugging and abandonment plan; or
- (b) Where actual plugging differed from the approved plugging and abandonment plan, an updated version of the plan, on the form supplied by the Director, specifying the differences.

6. Inactive Wells.

After any period of two years during which there is no injection the Permittee shall plug and abandon the well in accordance with Part II Section E Paragraph 2 of this Permit unless the Permittee:

- (a) Provides written notice to the Director;
- (b) Describes the actions or procedures the Permittee will take to ensure that the well will not endanger USDWs during the period of inactivity. These actions and procedures shall include compliance with mechanical integrity demonstration, Financial Responsibility and all other permit requirements designed to protect USDWs; and
- (c) Receives written notice by the Director temporarily waiving plugging and abandonment requirements.

PART III. CONDITIONS APPLICABLE TO ALL PERMITS

Section A. EFFECT OF PERMIT

The Permittee is allowed to engage in underground injection in accordance with the conditions of this Permit. The Permittee shall not construct, operate, maintain, convert, plug, abandon, or conduct any other activity in a manner that allows the movement of fluid containing any contaminant into underground sources of drinking water, if the presence of that contaminant may cause a violation of any primary drinking water regulation under 40 CFR 142 or may otherwise adversely affect the health of persons. Any underground injection activity not authorized by this Permit or by rule is prohibited. Issuance of this Permit does not convey property rights of any sort or any exclusive privilege; nor does it authorize any injury to persons or property, any invasion of other private rights, or any infringement of any other Federal, State or local law or regulations. Compliance with the terms of this Permit does not constitute a defense to any enforcement action brought under the provisions of Section 1431 of the Safe Drinking Water Act (SDWA) or any other law governing protection of public health or the environment, for any imminent and substantial endangerment to human health or the environment, nor does it serve as a shield to the Permittee's independent obligation to comply with all UIC regulations. Nothing in this Permit relieves the Permittee of any duties under applicable regulations.

Section B. CHANGES TO PERMIT CONDITIONS

1. Modification, Reissuance, or Termination.

The Director may, for cause or upon a request from the Permittee, modify, revoke and reissue, or terminate this Permit in accordance with 40 CFR 124.5, 144.12, 144.39, and 144.40. Also, this Permit is subject to minor modification for causes as specified in 40 CFR 144.41. The filing of a request for modification, revocation and reissuance, termination, or the notification of planned changes or anticipated noncompliance on the part of the Permittee does not stay the applicability or enforceability of any condition of this Permit.

2. Conversions.

The Director may, for cause or upon a written request from the Permittee, allow conversion of the well from a Class II injection well to a non-Class II well. Conversion may not proceed until the Permittee receives written approval from the Director. Conditions of such conversion may include but are not limited to, approval of the proposed well rework, follow up demonstration of mechanical integrity, well-specific monitoring and reporting following the conversion, and demonstration of practical use of the converted configuration.

3. Transfer of Permit.

Under 40 CFR 144.38, this Permit is transferable provided the current Permittee notifies the Director at least thirty (30) days in advance of the proposed transfer date (EPA Form 7520-7) and provides a written agreement between the existing and new Permittees containing a specific date for transfer of Permit responsibility, coverage and liability between them. The notice shall adequately demonstrate that the financial responsibility requirements of 40 CFR 144.52(a)(7) will be met by the new Permittee. The Director may require modification or revocation and reissuance of the Permit to change the name of the Permittee and incorporate such other requirements as may be necessary under the Safe Drinking Water Act; in some cases, modification or revocation and reissuance is mandatory.

4. Permittee Change of Address.

Upon the Permittee's change of address, or whenever the operator changes the address where monitoring records are kept, the Permittee must provide written notice to the Director within 30 days.

5. Construction Changes, Workovers, Logging and Testing Data

The Permittee shall give advance notice to the Director, and shall obtain the Director's written approval prior to any physical alterations or additions to the permitted facility. Alterations or workovers shall meet all conditions as set forth in this permit. The Permittee shall record any changes to the well construction on a Well Rework Record (EPA Form 7520-12), and shall provide this and any other record of well workovers, logging, or test data to EPA within sixty (60) days of completion of the activity.

Following the completion of any well workovers or alterations which affect the casing, tubing, or packer, a successful demonstration of mechanical integrity (Part III, Section F of this Permit) shall be made, and written authorization from the Director received, prior to resuming injection activities.

Section C. SEVERABILITY

The Provisions of this Permit are severable, and if any provision of this Permit or the application of any provision of this Permit to any circumstance, is held invalid, the application of such provision to other circumstances, and the remainder of this Permit shall not be affected thereby.

Section D. CONFIDENTIALITY

In accordance with 40 CFR Part 2 and 40 CFR 144.5, information submitted to EPA pursuant to this Permit may be claimed as confidential by the submitter. Any such claim must be asserted at the time of submission by stamping the words "confidential business information" on each page containing such information. If no claim is made at the time of submission, EPA may make the information available to the public without further notice. If a claim is asserted, the validity of the claim will be assessed in accordance with the procedures in 40 CFR Part 2 (Public Information). Claims of confidentiality for the following information will be denied:

- The name and address of the Permittee, and
- information which deals with the existence, absence or level of contaminants in drinking water.

Section E. GENERAL PERMIT REQUIREMENTS

1. Duty to Comply.

The Permittee must comply with all conditions of this Permit. Any noncompliance constitutes a violation of the Safe Drinking Water Act (SDWA) and is grounds for enforcement action; for Permit termination, revocation and reissuance, or modification; or for denial of a permit renewal application; except that the Permittee need not comply with the provisions of this Permit to the extent and for the duration such noncompliance is authorized in an emergency permit under 40 CFR 144.34. All violations of the SDWA may subject the Permittee to penalties and/or criminal prosecution as specified in Section 1423 of the SDWA.

2. Duty to Reapply.

If the Permittee wishes to continue an activity regulated by this Permit after the expiration date of this Permit, under 40 CFR 144.37 the Permittee must apply for a new permit prior to the expiration date.

3. Need to Halt or Reduce Activity Not a Defense.

It shall not be a defense for a Permittee in an enforcement action that it would have been necessary to halt or reduce the permitted activity in order to maintain compliance with the conditions of this Permit.

4. Duty to Mitigate.

The Permittee shall take all reasonable steps to minimize or correct any adverse impact on the environment resulting from noncompliance with this Permit.

5. Proper Operation and Maintenance.

The Permittee shall at all times properly operate and maintain all facilities and systems of treatment and control (and related appurtenances) which are installed or used by the Permittee to achieve compliance with the conditions of this Permit. Proper operation and maintenance includes effective performance, adequate funding, adequate operator staffing and training, and adequate laboratory and process controls, including appropriate quality assurance procedures. This provision requires the operation of back-up or auxiliary facilities or similar systems only when necessary to achieve compliance with the conditions of this Permit.

6. Permit Actions.

This Permit may be modified, revoked and reissued or terminated for cause. The filing of a request by the Permittee for a permit modification, revocation and reissuance, or termination, or a notification of planned changes or anticipated noncompliance, does not stay any permit condition.

7. Property Rights.

This Permit does not convey any property rights of any sort, or any exclusive privilege.

8. Duty to Provide Information.

The Permittee shall furnish to the Director, within a time specified, any information which the Director may request to determine whether cause exists for modifying, revoking and reissuing, or terminating this permit, or to determine compliance with this permit. The Permittee shall also furnish to the Director, upon request, copies of records required to be kept by this Permit. The Permittee is required to submit any information required by this Permit or by the Director to the mailing address designated in writing by the Director.

9. Inspection and Entry.

The Permittee shall allow the Director, or an authorized representative, upon the presentation of credentials and other documents as may be required by law, to:

- (a) Enter upon the Permittee's premises where a regulated facility or activity is located or conducted, or where records must be kept under the conditions of this Permit;

- (b) Have access to and copy, at reasonable times, any records that must be kept under the conditions of this Permit;
- (c) Inspect at reasonable times any facilities, equipment (including monitoring and control equipment), practices, or operations regulated or required under this Permit; and,
- (d) Sample or monitor at reasonable times, for the purpose of assuring permit compliance or as otherwise authorized by the SDWA, any substances or parameters at any location.

10. Signatory Requirements.

All applications, reports or other information submitted to the Director shall be signed and certified according to 40 CFR 144.32. This section explains the requirements for persons duly authorized to sign documents, and provides wording for required certification.

11. Reporting Requirements.

- (a) **Planned changes.** The Permittee shall give notice to the Director as soon as possible of any planned changes, physical alterations or additions to the permitted facility, and prior to commencing such changes.
- (b) **Anticipated noncompliance.** The Permittee shall give advance notice to the Director of any planned changes in the permitted facility or activity which may result in noncompliance with permit requirements.
- (c) **Monitoring Reports.** Monitoring results shall be reported at the intervals specified in this Permit.
- (d) **Compliance schedules.** Reports of compliance or noncompliance with, or any progress reports on, interim and final requirements contained in any compliance schedule of this Permit shall be submitted no later than 30 days following each schedule date.
- (e) **Twenty-four hour reporting.** The Permittee shall report to the Director any noncompliance which may endanger human health or the environment, including:
 - (i) Any monitoring or other information which indicates that any contaminant may cause endangerment to a USDW; or
 - (ii) Any noncompliance with a permit condition or malfunction of the injection system which may cause fluid migration into or between USDWs.

Information shall be provided, either directly or by leaving a message, within twenty-four (24) hours from the time the permittee becomes aware of the circumstances by telephoning (800) 227-8917 and requesting EPA Region VIII UIC Program Compliance and Technical Enforcement Director, or by contacting the EPA Region VIII Emergency Operations Center at (303) 293-1788.

In addition, a follow up written report shall be provided to the Director within five (5) days of the time the Permittee becomes aware of the circumstances. The written submission shall contain a description of the noncompliance and its cause, the period of noncompliance including exact dates and times, and if the noncompliance has not been corrected the anticipated time it is expected to continue; and the steps taken or planned to reduce, eliminate, and prevent recurrence of the noncompliance.

- (f) Oil Spill and Chemical Release Reporting: The Permittee shall comply with all reporting requirements related to the occurrence of oil spills and chemical releases by contacting the National Response Center (NRC) at (800) 424-8802, (202) 267-2675, or through the NRC website <http://www.nrc.uscg.mil/index.htm>.
- (g) Other Noncompliance. The Permittee shall report all instances of noncompliance not reported under paragraphs Part III, Section E Paragraph 11(b) or Section E, Paragraph 11(e) at the time the monitoring reports are submitted. The reports shall contain the information listed in Paragraph 11(e) of this Section.
- (h) Other information. Where the Permittee becomes aware that it failed to submit any relevant facts in the permit application, or submitted incorrect information in a permit application or in any report to the Director, the Permittee shall promptly submit such facts or information to the Director.

Section F. FINANCIAL RESPONSIBILITY

1. Method of Providing Financial Responsibility.

The Permittee shall maintain continuous compliance with the requirement to maintain financial responsibility and resources to close, plug, and abandon the underground injection well(s). No substitution of a demonstration of financial responsibility shall become effective until the Permittee receives written notification from the Director that the alternative demonstration of financial responsibility is acceptable. The Director may, on a periodic basis, require the holder of a permit to revise the estimate of the resources needed to plug and abandon the well to reflect changes in such costs and may require the Permittee to provide a revised demonstration of financial responsibility.

2. Insolvency.

In the event of:

- (a) the bankruptcy of the trustee or issuing institution of the financial mechanism; or
- (b) suspension or revocation of the authority of the trustee institution to act as trustee; or

- (c) the institution issuing the financial mechanism losing its authority to issue such an instrument

the Permittee must notify the Director in writing, within ten (10) business days, and the Permittee must establish other financial assurance or liability coverage acceptable to the Director within sixty (60) days after any event specified in (a), (b), or (c) above.

The Permittee must also notify the Director by certified mail of the commencement of voluntary or involuntary proceedings under Title 11 (Bankruptcy), U.S. Code naming the owner or operator as debtor, within ten (10) business days after the commencement of the proceeding. A guarantor, if named as debtor of a corporate guarantee, must make such a notification as required under the terms of the guarantee.

APPENDIX A

WELL CONSTRUCTION REQUIREMENTS

See diagram.

The Federal No. 1-33-8-18 was drilled to a total depth of 6205 feet (KB) in the Wasatch Formation.

Surface casing (8-5/8 inch) was set at a depth of 307 feet in a 12-1/4 inch hole using 160 sacks of Class "G" cement which was circulated to the surface.

Production casing (5-1/2 inch) was set at a depth of 6189 feet (KB) in a 7-7/8 inch hole with 375 sacks of Premium Lite II and 475 sacks of 50/50 poz mix. This well construction is considered adequate to protect USDWs.

The EPA calculates the top of cement as 654 feet from the surface. The Cement Bond Log (CBL) identifies top of cement at surface. CBL analysis does identify adequate 80% bond index cement bond within the Confining Zone.

The schematic diagram shows enhanced recovery injection perforations in the Douglas Creek Member of the Green River Formation. Additional perforations may be added at a later time between the depths of 3937 feet and the top of the Wasatch Formation (Estimated to be 6185 feet) provided the operator first notifies the Director and later submits an updated well completion report (EPA Form 7520-12) and schematic diagram.

The packer will be set no higher than 100 feet above the top perforation.

UT 21100-07422 Federal 1-33-8-18

Spud Date: 4/4/06
Put on Production: 5/23/06
K.B.: 4879' G.L.: 4869'

Initial Production: 15 BOPD,
5 MCFD, 37 BWPD

Proposed Injection Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
GRADE: J-55
WEIGHT: 24#
LENGTH: 7 jts (367.29') *Base USDWs 175'*
DEPTH LANDED: 317.29' KB
HOLE SIZE: 12-1/4"
CEMENT DATA: 160 sxs Class "G" cmt, est 1.5 bbbls cmt to surf.

Green River 1558'

PRODUCTION CASING

CSG SIZE: 5-1/2" *Tionz 3108'*
GRADE: J-55
WEIGHT: 15.5# *Mahogany B. 3144-65'*
LENGTH: 146 jts (6191.19')
DEPTH LANDED: 6189.19' KB
HOLE SIZE: 7-7/8"
CEMENT DATA: 375 sxs Prem Lite II mixed & 475 sxs 50/50 POZ.
CEMENT TOP AT: Surface

TUBING

SIZE/GRADE/WT: 2-7/8" / J-55 / 6.5#
NO. OF JOINTS: 187 jts (5912.17')
TUBING ANCHOR: 5922.17' KB
NO. OF JOINTS: 1 jt (31.63')
SEATING NIPPLE: 2-7/8" (1.10')
SN LANDED AT: 5956.60' KB
NO. OF JOINTS: 3 jts (94.93')
TOTAL STRING LENGTH: EOT @ 6091.13' w/10' KB

Castle Peak 5650'-5672'

Basal Carbonate 6050'

FRAC JOB

05/18/05	6060-6144'	Frac BLSL sands as follows: 90.059# 20/40 sand in 824 bbbls Lightning 17 frac fluid. Treated @ avg press of 2026 psi w/avg rate of 25.4 BPM. ISIP 2060 psi. Calc flush: ? gal. Actual flush: 5544 gal
05/18/06	5770-5812'	Frac CP2 sands as follows: 90.362# 20/40 sand in 683 bbbls Lightning 17 frac fluid. Treated @ avg press of 1280 psi w/avg rate of 25.5 BPM. ISIP 1500 psi. Calc flush: ? gal. Actual flush: 5208 gal
05/18/06	4956-5030'	Frac D1&2 sands as follows: 35.010# 20/40 sand 383 bbbls Lightning 17 frac fluid. Treated @ avg press of 1832 psi w/avg rate of 25.5 BPM. ISIP 1490 psi. Calc flush: ? gal. Actual flush: 4410 gal.
05/18/06	4470'-4477'	Frac GB6 sands as follows: 32,182# 20/40 sand in 351 bbbls Lightning 17 frac fluid. Treated @ avg press of 2089 psi w/avg rate of 25.4 BPM. ISIP 2025 psi. Calc flush: ? gal. Actual flush: 4368 gal

*3700'-4438' 86% Bond
3746'-3937' Confining Zone
3937' Garden Gully*

Packer @ 4435'
4470-4477'

4900' Douglas Creek

4956-4961'
5022-5030'

5770-5777'
5798-5812'

6060-6078'
6109-6116'
6120-6144'

PBTD @ 6170'
SHOE @ 6189'

TD @ 6205'

Est. N2S2222 6185'

PERFORATION RECORD

05/17/06	6120-6144'	4 JSPF	96 holes
05/17/06	6109-6116'	4 JSPF	28 holes
05/17/06	6060-6078'	4 JSPF	72 holes
05/18/06	5798-5812'	4 JSPF	56 holes
05/18/06	5770-5777'	4 JSPF	28 holes
05/18/06	5022-5030'	4 JSPF	32 holes
05/18/06	4956-4961'	4 JSPF	20 holes
05/18/06	4470-4477'	4 JSPF	72 holes

NEWFIELD

Federal 1-33-8-18

906' FNL & 705' FEL

NE/NE Section 33-T8S-R18E

Uintah Co, Utah

API #43-047-36036; Lease #UTU-74872

APPENDIX B

LOGGING AND TESTING REQUIREMENTS

Logs.

Logs will be conducted according to current UIC guidance. It is the responsibility of the Permittee to obtain and use guidance prior to conducting any well logging required as a condition of this permit.

NO LOGGING REQUIREMENTS

Tests.

Tests will be conducted according to current UIC guidance. It is the responsibility of the Permittee to obtain and use guidance prior to conducting any well test required as a condition of this permit.

WELL NAME: Federal 1-33-8-18	
TYPE OF TEST	DATE DUE
Step Rate Test	Within a 180-day period following commencement of injection
Standard Annulus Pressure	Prior to receiving authorization to inject and at least once within a five (5) year year period following the last successful test.
Pore Pressure	Prior to receiving authorization to inject

APPENDIX C

OPERATING REQUIREMENTS

MAXIMUM ALLOWABLE INJECTION PRESSURE:

Maximum Allowable Injection Pressure (MAIP) as measured at the surface shall not exceed the pressure(s) listed below.

WELL NAME	MAXIMUM ALLOWED INJECTION PRESSURE (psi)
	ZONE 1 (Upper)
Federal 1-33-8-18	1,115

INJECTION INTERVAL(S):

Injection is permitted only within the approved injection interval listed below. Injection perforations may be altered provided they remain within the approved injection interval and the Permittee provides notice to the Director in accordance with Part II, Section A, Paragraph 6. Specific injection perforations can be found in Appendix A.

WELL NAME: Federal 1-33-8-18	APPROVED INJECTION INTERVAL (KB, ft)		FRACTURE GRADIENT (psi/ft)
	TOP	BOTTOM	
FORMATION NAME			
Green River: Garden Gulch - Douglas Creek - Basal Carbonate Members	3,937.00	6,185.00	0.690

ANNULUS PRESSURE:

The annulus pressure shall be maintained at zero (0) psi as measured at the wellhead. If this pressure cannot be maintained, the Permittee shall follow the procedures listed under Part II, Section C. 6. of this permit.

MAXIMUM INJECTION VOLUME:

There is no limitation on the number of barrels per day (bbls/day) of water that shall be injected into this well, provided further that in no case shall injection pressure exceed that limit shown in Appendix C.

APPENDIX D

MONITORING AND REPORTING PARAMETERS

This is a listing of the parameters required to be observed, recorded, and reported. Refer to the permit Part II, Section D, for detailed requirements for observing, recording, and reporting these parameters.

OBSERVE MONTHLY AND RECORD AT LEAST ONCE EVERY THIRTY DAYS	
OBSERVE AND RECORD	Injection pressure (psig)
	Annulus pressure(s) (psig)
	Injection rate (bbl/day)
	Fluid volume injected since the well began injecting (bbls)

ANNUALLY	
ANALYZE	Injected fluid total dissolved solids (mg/l)
	Injected fluid specific gravity
	Injected fluid specific conductivity
	Injected fluid pH

ANNUALLY	
REPORT	Each month's maximum and averaged injection pressures (psig)
	Each month's maximum and minimum annulus pressure(s) (psig)
	Each month's injected volume (bbl)
	Fluid volume injected since the well began injecting (bbl)
	Written results of annual injected fluid analysis
	Sources of all fluids injected during the year

Records of all monitoring activities must be retained and made available for inspection at the following location:

Newfield Production Company
1001 Seventeenth Street - Suite 2000
Denver, CO 80202

APPENDIX E

PLUGGING AND ABANDONMENT REQUIREMENTS

See diagram.

The well shall be plugged in a manner that isolates the injection zone and prevents movement of fluid into or between USDWs and in accordance with other applicable Federal, State or local law or regulation. Tubing, packers, and any downhole apparatus shall be removed. Class A, C, G, and H cements, with additives such as accelerators and retarders that control or enhance cement properties, may be used for plugs. However, volume extending additives and gel cements are not approved for plug use. Plug placement shall be verified by tagging. Plugging gel of at least 9.2 lb/gal shall be placed between all plugs. Within sixty (60) days after plugging, the owner or operator shall submit Plugging Record (EPA Form 7520-13) to the Director. The Plugging Record must be certified as accurate and complete by the person responsible for the plugging operation. At a minimum, the following plugs are required:

PLUG NO. 1: Seal Injection Zone: Set a cast iron bridge plug (CIBP) no more than fifty (50) feet above the top injection perforation. Place at least twenty (20) feet of cement plug on top of the CIBP.

PLUG NO. 2: Seal Mahogany Shale and Trona intervals: Squeeze a cement plug on the backside of the 5-1/2 inch casing across the Trona Zone and the Mahogany Shale approximately 3050 feet to 3215 feet (unless pre-existing backside cement precludes cement-squeezing this interval) followed by a minimum 165-foot balanced cement plug inside the 5-1/2 inch casing across the Trona Zone and the Mahogany Shale, approximately 3050 feet to 3215 feet.

PLUG NO. 3: Seal USDWs: Squeeze a cement plug (1500 feet - 1600 feet) on the backside of the 5-1/2 inch casing across the base of the Uinta formation (unless pre-existing backside cement precludes cement-squeezing this interval), followed by a minimum 100-foot balanced cement plug inside the 5-1/2 inch casing across the base of the Uinta Formation, approximately 1500 feet to 1600 feet.

PLUG NO.4: Seal Surface: Set a Class "G" cement plug within the 5-1/2 inch casing to 367 feet and up the 5-1/2 inch by 8-5/8 inch casings annulus to the surface.

Federal 1-33-8-18

Spud Date: 4/4/06
 Put on Production: 5/23/06
 K.B.: 4879' G.L.: 4869'

Proposed P&A Wellbore Diagram

SURFACE CASING

CSG SIZE: 8-5/8"
 GRADE: J-55
 WEIGHT: 24#
 LENGTH: 7 jts. (307.29')
 DEPTH LANDED: 317.29' KB
 HOLE SIZE: 12-1/4"
 CEMENT DATA: 160 sxs Class "G" cmt, est 1.5 bbls cmt to surf.

Cement top @ Surface

Pump 43 sxs Class G Cement down 5 - 1/2" casing to 367'

Casing Shoe @ 317'

367'

Green River 1558'

1500'-1600' Cement Plug

PRODUCTION CASING

CSG SIZE: 5-1/2"
 GRADE: J-55
 WEIGHT: 15.5#
 LENGTH: 146 jts. (6191.19')
 DEPTH LANDED: 6189.19' KB
 HOLE SIZE: 7-7/8"
 CEMENT DATA: 375 sxs Prem. Lite II mixed & 475 sxs 50/50 POZ.
 CEMENT TOP AT: Surface

Cement Plug 3050'-3215'

3108' Tionz

3144' - 3163' Mahogany Bench

*20'+ Class G Cement plug on top of CIBP
 CIBP 50' above top perf-*

4470-4477'

4900' Douglas Creek

4956-4961'

5022-5030'

5770-5777'

5798-5812'

6050' Basal Carbonate

6060-6078'

6109-6116'

6120-6144'

PBTD @ 6170'

SHOE @ 6189'

Est. Wasatch 6185'

TD @ 6205'

 <p>NEWFIELD</p>
<p>Federal 1-33-8-18</p> <p>906' FNL & 705' FEL</p> <p>NE/NE Section 33-T8S-R18E</p> <p>Utah Co, Utah</p> <p>API #43-047-360.36; Lease #UTU-74872</p>


APPENDIX F

CORRECTIVE ACTION REQUIREMENTS

The surface of Area-of-Review (AOR) well Federal No. 12-34-8-18 will be monitored weekly for evidence of injectate fluid contamination.

Newfield Production Company (Newfield) developed a corrective action monitoring program, effective July 10, 2008, entitled "Procedure Related To Proposed Class II Enhanced Recovery Injection Wells Determined By The EPA To Have Specific Area-of-Review (AOR) Wells With Inadequate Cement Across The Confining Zone." (See Appendix F-2).

If possible fluid movement out of the Injection Zone is identified, either through the weekly surface monitoring, through Newfield's July 10, 2008 procedure described above, or through any other means or evidence of mechanical integrity failure, (i.e., increased bradenhead annulus pressure, tubing/casing pressure readings, etc.) the Permittee will immediately shut in the Federal No. 1-33-8-18 and notify the Director. No injection into Federal No. 1-33-8-18 will be permitted until the Permittee has notified the Director that the non-compliance has been resolved via submission of a Rework Record (EPA Form No. 7520-12), a schematic diagram, a chronological history of rework, and has received authorization from the Director to re-commence injection.



RE: Procedure related to proposed Class II Enhanced Oil Recovery Injection Wells determined by the EPA to have specific Area of Review (AOR) wells with inadequate cement across the confining zone

Effective July 10, 2008 Newfield Production Company will implement the following procedure to address concerns related to protection of Underground Sources of Drinking Water (USDW) in AOR wells where the interval of cement bond index across the confining zone behind pipe has been determined to be inadequate. The procedure is intended to meet the corrective action requirements found in the UIC Class II permit, as well as provide data that could be used to detect and prevent fluid movement out of the proposed injection zone.

- 1) Establish baseline production casing by surface casing annulus pressures prior to water injection in subject well with a calibrated gauge.
- 2) Record the baseline pressure, report findings to Newfield engineering group and keep on file so it is available upon request
- 3) Place injection well in service. Run packer integrity and radioactive tracer logs to verify wellbore integrity and determine zones taking water.
- 4) Construct a geologic cross section showing zones taking water and their geologic equivalent zones in the AOR wells.
- 5) Submit a report of the packer integrity log, radioactive tracer log, and geologic cross section to to the Newfield engineering staff for review and keep on file so it is available upon request
- 6) Weekly observations of the site will be made by Newfield during normal well operating activities. Any surface discharge of fluids will be reported immediately.
- 7) After injection well is placed in service, weekly observations of annulus pressure will be made and compared to baseline pressure and will be recorded once monthly. The recorded pressure information will be kept on file and be available upon request.
- 8) If pressure increases by more than 10% above baseline at any time in an AOR well with insufficient cement bond, Newfield will run a temperature survey log in subject well. This log, in concert with the geologic crosssection, will enable the determination of water movement in the open hole by production casing annulus through a shift in geothermal gradient.
- 9) If water movement is determined in annulus, Newfield will shut in the injection well and repair the production casing by open hole annulus or leave the injection well out of service.

STATEMENT OF BASIS

NEWFIELD PRODUCTION COMPANY
FEDERAL 1-33-8-18
UINTAH COUNTY, UT

EPA PERMIT NO. UT21100-07422

CONTACT: Emmett Schmitz
U. S. Environmental Protection Agency
Ground Water Program, 8P-W-GW
1595 Wynkoop Street
Denver, Colorado 80202-1129
Telephone: 1-800-227-8917 ext. 312-6174

This STATEMENT OF BASIS gives the derivation of site-specific UIC Permit conditions and reasons for them. Referenced sections and conditions correspond to sections and conditions in the Permit.

EPA UIC permits regulate the injection of fluids into underground injection wells so that the injection does not endanger underground sources of drinking water. EPA UIC permit conditions are based upon the authorities set forth in regulatory provisions at 40 CFR Parts 144 and 146, and address potential impacts to underground sources of drinking water. Under 40 CFR 144.35 Issuance of this permit does not convey any property rights of any sort or any exclusive privilege, nor authorize injury to persons or property or invasion of other private rights, or any infringement of other Federal, State or local laws or regulations. Under 40 CFR 144 Subpart D, certain conditions apply to all UIC Permits and may be incorporated either expressly or by reference. General Permit conditions for which the content is mandatory and not subject to site-specific differences (40 CFR Parts 144, 146 and 147) are not discussed in this document.

PART I. General Information and Description of Facility

Newfield Production Company
1001 Seventeenth Street, Suite 2000
Denver, CO 80202

on

September 19, 2006

submitted an application for an Underground Injection Control (UIC) Program Permit or Permit Modification for the following injection well or wells:

Federal 1-33-8-18
906' FNL & 705' FEL, NENE S33, T8S, R18E
Uintah County, UT

Regulations specific to Uintah-Ouray Indian Reservation injection wells are found at 40 CFR 147 Subpart TT.

The application, including the required information and data necessary to issue or modify a UIC Permit in accordance with 40 CFR Parts 144, 146 and 147, was reviewed and determined by EPA to be complete.

The Permit will expire upon delegation of primary enforcement responsibility (primacy) for applicable portions of the UIC Program to the Ute Indian Tribe or the State of Utah unless the delegated agency has the authority and chooses to adopt and enforce this Permit as a Tribal or State Permit.

TABLE 1.1 shows the status of the well or wells as "New", "Existing", or "Conversion" and for Existing shows the original date of injection operation. Well authorization "by rule" under 40 CFR Part 144 Subpart C expires automatically on the Effective Date of an issued UIC Permit.

The Federal No. 1-33-8-18 is currently an active Green River Formation (Garden Gulch and Douglas Creek Members) oil well. It is the initial intent of the applicant to use the current production perforations for Class II enhanced recovery injection. The Federal No. 1-33-8-18 has total depth in the Wasatch Formation.

TABLE 1.1
WELL STATUS / DATE OF OPERATION

NEW WELLS

Well Name	Well Status	Date of Operation
Federal 1-33-8-18	New	N/A

PART II. Permit Considerations (40 CFR 146.24)

Hydrogeologic Setting

Water wells for domestic supply in this area, when present, generally are completed into the shallow alluvium, the Duchesne River Formation, or the underlying Uinta Formation, and the water generally contains approximately 500 to 1,500 mg/l and higher total dissolved solids.

The Uinta-Animas aquifer in the Uinta Basin is present in water-yielding beds of sandstone, conglomerate, and siltstone of the Duchesne River and Uinta Formations, the Renegade Tongue of the Wasatch Formation, and the Douglas Creek Member of the Green River Formation. The Renegade Tongue of the Wasatch Formation and the Douglas Creek Member of the Green River Formation contain an aquifer along the southern and eastern margins of the basin where the rocks primarily consist of fluvial, massive, irregularly bedded sandstone and siltstone. Water-yielding units in the Uinta-Animas aquifer in the Uinta Basin commonly are separated from each other and from the underlying Mesaverde aquifer by units of low permeability composed of claystone, shale, marlstone, or limestone. In the Uinta Basin, for example, the part of the aquifer in the Duchesne River and Uinta Formations ranges in thickness from 0 feet at the southern margin of the aquifer to as much as 9,000 feet in the north-central part of the aquifer. Ground-water recharge to the Uinta-Animas aquifer generally occurs in the areas of higher altitude along the margins of the basin. Ground water is discharged mainly to streams, springs, and by transpiration from vegetation growing along stream valleys. The rate of ground-water withdrawal is small, and natural discharge is approximately equal to recharge. Recharge occurs near the southern margin of the aquifer, and discharge occurs near the White and Green Rivers (from USGS publication HA 730-C). Water samples from Mesaverde sands in the nearby Natural Buttes Unit yielded highly saline water.

Geologic Setting (TABLE 2.1)

The proposed enhanced oil recovery injection well is located in the Greater Monument Butte Field, T7-9S and R15-19E, which lies near the center of the broad, gently northward dipping south flank of the Uinta Basin. More than 450 million barrels of oil (63 MT) have been produced from sediments of the Uinta Basin. The Uinta Basin is a topographic and structural trough encompassing an area of more than 9300 square mi (14,900 km) in northeast Utah. The basin is sharply asymmetrical, with a steep north flank bounded by the east-west-trending Uinta Mountains, and a gently dipping south flank. The Uinta Basin was formed in Paleocene to Eocene time, creating a large area of internal drainage which was filled by the ancestral Lake Uinta. The lacustrine, or fresh water lake-formed, sediments deposited in and around Lake Uinta make up the Uintah and Green River Formations. The southern shore of Lake Uinta was very broad and flat, resulting in large cyclic shifts of the location of the shoreline during the many repeated transgressive and regressive cycles caused by the climatic and tectonic-induced rise and fall of water levels of the lake. Distributary-mouth bars, distributary channels, and near-shore bars are the primary oil producing sandstone reservoirs in the area. (Ref: "Reservoir Characterization of the Lower Green River Formation, Southwest Uinta Basin, Utah Biannual Technical Progress Report, 4/1/99-9/30/99", by C. D. Morgan, Program Manager, November 1999, Contract DE-AC26-98BC15103).

The Duchesne River Formation is absent in this area. Shale and siltstone of the Uintah Formation outcrop and compose the surface rock throughout the area. The lower 600 feet to 800 feet of the Uinta Formation, consisting generally of shale interbedded with occasionally water-bearing sandstone lenses between 5 feet to 20 feet thick, is underlain by the Green River Formation. The

Green River Formation is further subdivided into several Member and local marker units. The cyclic nature of Green River deposition in the southern shore area resulted in numerous stacked, intertonguing deltaic and near-shore sand and silt deposits. Red alluvial shale and siltstone deposits that intertongue with the Green River sediments are of the Colton and Wasatch Formations. Under the Wasatch Formation is the Mesaverde Formation, which consists primarily of continental-origin deposits of interbedded shale, sandstone, and coal.

The geologic dip is about 200 feet per mile, and there are no known surface faults in this area. Veins of gilsonite, a natural resinous hydrocarbon occasionally mined as a resource, occurs in the greater Uintah Basin though it is predominantly found on the eastern margin of the basin near the Colorado border. Vertical veins, generally between 2 ft to 6 ft wide but up to 28 ft wide, may extend many miles in length and occasionally extend as deep as 2000 ft. In this area within the Greater Monument Butte Field there is one known gilsonite vein. This vein is not considered to present a pathway for migration of fluid out of the injection zone because it terminates at depth of about 2000 ft, far above the protective confining layer and much deeper injection zone. Newfield and the owner of this former gilsonite mine have agreed to conditions for operation near this vein to ensure no potential for impact to this vein or to ground water from enhanced oil recovery operations.

TABLE 2.1
GEOLOGIC SETTING
Federal 1-33-8-18

Formation Name	Top (ft)	Base (ft)	TDS (mg/l)	Lithology
Uinta USDW: Publ. 92	0	175	< 10,000	Sand and shale
Uinta	175	1,558		Interbedded lacustrine sand, shale and carbonate with fluvial sand and shale.
Green River	1,538	3,937		Interbedded lacustrine sand, shale and carbonate with fluvial sand and shale.
Green River: Trona	3,108	3,144		Evaporite
Green River: Mahogany Bench	3,144	3,163		Oil shale
Green River: Garden Gulch Member	3,937	4,900	10,229	Interbedded lacustrine sand, shale and carbonate with fluvial sand and shale.
Green River: Douglas Creek Member	4,900	6,050	10,229	Interbedded lacustrine sand, shale and carbonate with fluvial sand and shale.
Green River: Basal Carbonate Member	6,050	6,185		Carbonate

Proposed Injection Zone(s) (TABLE 2.2)

An injection zone is a geological formation, group of formations, or part of a formation that receives fluids through a well. The proposed injection zones are listed in TABLE 2.2.

Injection will occur into an injection zone that is separated from USDWs by a confining zone which is free of known open faults or fractures within the Area of Review.

The EPA approved interval for Class II enhanced recovery injection in the Federal No. 1-33-8-18 is located between the top of the Garden Gulch Member (3937 feet) and the top of the Wasatch Formation estimated to be 6185 feet.

TABLE 2.2
INJECTION ZONES
Federal 1-33-8-18

Formation Name	Top (ft)	Base (ft)	TDS (mg/l)	Fracture Gradient (psi/ft)	Porosity	Exempted?*
Green River: Garden Gulch - Douglas Creek - Basal Carbonate Members	3,937	6,185	10,229	0.690		N/A

* **C - Currently Exempted**
E - Previously Exempted
P - Proposed Exemption
N/A - Not Applicable

Confining Zone(s) (TABLE 2.3)

A confining zone is a geological formation, part of a formation, or a group of formations that limits fluid movement above the injection zone. The confining zone or zones are listed in TABLE 2.3.

The 191-foot (3746 feet - 3937 feet) shale, and impervious and argillaceous silt/sand lenses Confining Zone directly overlies the top of the Garden Gulch Member.

TABLE 2.3
CONFINING ZONES
Federal 1-33-8-18

Formation Name	Formation Lithology	Top (ft)	Base (ft)
Green River: Confining Zone	Shale	3,746	3,937

Underground Sources of Drinking Water (USDWs) (TABLE 2.4)

Aquifers or the portions thereof which contain less than 10,000 mg/l total dissolved solids (TDS) and are being or could in the future be used as a source of drinking water are considered to be USDWs. The USDWs in the area of this facility are identified in TABLE 2.4.

Throughout the Greater Monument Butte Field area undergoing enhanced oil recovery operations, water analyses of the Green River Formation generally exhibit total dissolved solids (TDS) content well in excess of 10,000 mg/l. However, some recent water analyses from the field showed lower TDS values closer to 10,000 mg/l. While rain and surface water recharge into Green River Formation outcrops further south along the Book Cliffs/Roan Cliffs in effect "freshens" the Green River Formation water near those outcrops, in this area of the Monument Butte Field the observed occasional 'freshening' is ascribed to the effective dilution of the originally in-place high TDS water from injection of relatively fresh water for enhanced oil recovery operations. Water samples from deeper Mesaverde Formation sands in the nearby Natural Buttes Unit yield highly saline water.

The State of Utah "Water Wells and Springs" identifies no public water supply wells within the one-quarter (1/4) mile Area-of-Review (AOR) around the Federal No. 1-33-8-18.

Technical Publication No. 92: State of Utah, Department of Natural Resources, cites the base of Underground Sources of Drinking Water (USDW) in the Uinta Formation approximately 175 feet from the surface. However, absent definitive information relative to the water quality of the Uinta Formation, from the depth of 175 feet to the base of the Uinta Formation (1558 feet), the EPA will require, during plugging and abandonment, a cement plug at the base of the Uinta Formation to protect contamination of possible Uinta USDWs.

TABLE 2.4
UNDERGROUND SOURCES OF DRINKING WATER (USDW)
Federal 1-33-8-18

Formation Name	Formation Lithology	Top (ft)	Base (ft)	TDS (mg/l)
Uinta Formation	Publication 92 calculation of USDW. Sand and shale.	0	175	< 10,000
Uinta	Interbedded sand, shale and carbonate with fluvial sand and shale.	175	1,538	

PART III. Well Construction (40 CFR 146.22)

The Federal No. 1-33-8-18 was drilled to a total depth of 6205 feet (KB) in the Wasatch Formation.

Surface casing (8-5/8 inch) was set at a depth of 307 feet in a 12-1/4 inch hole using 160 sacks of Class "G" cement which was circulated to the surface.

Production casing (5-1/2 inch) was set at a depth of 6189 feet (KB) in a 7-7/8 inch hole with 375 sacks of Premium Lite II and 475 sacks of 50/50 poz mix. This well construction is considered adequate to protect USDWs.

The EPA calculates the top of cement as 654 feet from the surface. The Cement Bond Log (CBL) identifies top of cement at surface. CBL analysis does identify adequate 80% bond index cement bond within the Confining Zone.

The schematic diagram shows enhanced recovery injection perforations in the Douglas Creek Member of the Green River Formation. Additional perforations may be added at a later time between the depths of 3937 feet and the top of the Wasatch Formation (Estimated to be 6185 feet) provided the operator first notifies the Director and later submits an updated well completion report (EPA Form 7520-12) and schematic diagram.

The packer will be set no higher than 100 feet above the top perforation.

TABLE 3.1
WELL CONSTRUCTION REQUIREMENTS
Federal 1-33-8-18

Casing Type	Hole Size (in)	Casing Size (in)	Cased Interval (ft)	Cemented Interval (ft)
Production	7.88	5.50	0 - 6,189	0 - 6,170
Surface	12.25	8.63	0 - 307	0 - 307

The approved well completion plan will be incorporated into the Permit as APPENDIX A and will be binding on the Permittee. Modification of the approved plan is allowed under 40 CFR 144.52(a)(1) provided written approval is obtained from the Director prior to actual modification.

Casing and Cementing (TABLE 3.1)

The construction plan for the well or wells proposed for conversion to an injection well was evaluated and determined to be in conformance with standard practices and guidelines that ensure well injection does not result in the movement of fluids into USDWs. Well construction and conversion details for the well or wells are shown in TABLE 3.1.

Tubing and Packer

Injection tubing is required to be installed from a packer up to the surface inside the well casing. The packer will be set above the uppermost perforation. The tubing and packer are designed to prevent injection fluid from coming into contact with the outermost casing.

Tubing-Casing Annulus (TCA)

The TCA allows the casing, tubing and packer to be pressure-tested periodically for mechanical integrity, and will allow for detection of leaks. The TCA will be filled with fresh water treated with a corrosion inhibitor or other fluid approved by the Director.

The tubing/casing annulus must be kept closed at all times so that it can be monitored as required under condition of the Permit.

Monitoring Devices

The permittee will be required to install and maintain wellhead equipment that allows for monitoring pressures and providing access for sampling the injected fluid. Required equipment may include but is not limited to: 1) shut-off valves located at the wellhead on the injection tubing and on the TCA; 2) a flow meter that measures the cumulative volume of injected fluid; 3) fittings or pressure gauges attached to the injection tubing and the TCA for monitoring the injection and TCA pressure; and 4) a tap on the injection line, isolated by shut-off valves, for sampling the injected fluid.

All sampling and measurement taken for monitoring must be representative of the monitored activity.

PART IV. Area of Review, Corrective Action Plan (40 CFR 144.55)

**TABLE 4.1
AOR AND CORRECTIVE ACTION**

Well Name	Type	Status (Abandoned Y/N)	Total Depth (ft)	TOC Depth (ft)	CAP Required (Y/N)
Federal 12-34-8-18	Producer	No	5,920	2,275	Yes
Federal 2-33-8-18	Producer	No	6,200	585	No
Federal 8-33-8-18	Producer	No	6,150	86	No

TABLE 4.1 lists the wells in the Area of Review ("AOR") and shows the well type, operating status, depth, top of casing cement ("TOC") and whether a Corrective Action Plan ("CAP") is required for the well.

Area Of Review

Applicants for Class I, II (other than "existing" wells) or III injection well Permits are required to identify the location of all known wells within the injection well's Area of Review (AOR) which penetrate the injection zone, or in the case of Class II wells operating over the fracture pressure of the formation, all known wells within the area of review that penetrate formations which may be affected by increased pressure. Under 40 CFR 146.6 the AOR may be a fixed radius of not less than one quarter (1/4) mile or a calculated zone of endangering influence. For Area Permits, a fixed width of not less than one quarter (1/4) mile for the circumscribing area may be used.

Corrective Action Plan

For wells in the AOR which are improperly sealed, completed, or abandoned, the applicant shall develop a Corrective Action Plan (CAP) consisting of the steps or modifications that are necessary to prevent movement of fluid into USDWs.

The CAP will be incorporated into the Permit as APPENDIX F and become binding on the permittee.

TABLE 4.1 lists the wells in the AOR, and shows the well type, operating status, depth, top of casing cement and whether a CAP is required for this well.

PART V. Well Operation Requirements (40 CFR 146.23)

**TABLE 5.1
INJECTION ZONE PRESSURES
Federal 1-33-8-18**

Formation Name	Depth Used to Calculate MAIP (ft)	Fracture Gradient (psi/ft)	Initial MAIP (psi)
Green River: Garden Gulch - Douglas Creek - Basal Carbonate Members	4,470	0.690	1,115

Approved Injection Fluid

The approved injection fluid is limited to Class II injection well fluids pursuant to 40 CFR § 144.6(b). For disposal wells injecting water brought to the surface in connection with natural gas storage operations, or conventional oil or natural gas production, the fluid may be commingled and the well used to inject other Class II wastes such as drilling fluids and spent well completion, treatment and stimulation fluid. Injection of non-exempt wastes, including unused fracturing fluids or acids, gas plant cooling tower cleaning wastes, service wastes, and vacuum truck and drum rinsate from trucks and drums transporting or containing non-exempt waste, is prohibited.

The proposed injectate will be a blend of culinary-quality water from the Johnson Water District pipeline and/or water from the Green River pipeline, and produced Green River water from wells proximate to the Federal No. 1-33-8-18.

Injection Pressure Limitation

Injection pressure, measured at the wellhead, shall not exceed a maximum calculated to assure that the pressure used during injection does not initiate new fractures or propagate existing fractures in the confining zones adjacent to the USDWs.

The applicant submitted injection fluid density and injection zone data which was used to calculate a formation fracture pressure and to determine the maximum allowable injection pressure (MAIP), as measured at the surface, for this Permit.

TABLE 5.1 lists the fracture gradient for the injection zone and the approved MAIP, determined according to the following formula:

$$FP = [fg - (0.433 * sg)] * d$$

- FP = formation fracture pressure (measured at surface)
- fg = fracture gradient (from submitted data or tests)
- sg = specific gravity (of injected fluid)
- d = depth to top of injection zone (or top perforation)

Injection Volume Limitation

Cumulative injected fluid volume limits are set to assure that injected fluids remain within the boundary of the exempted area. Cumulative injected fluid volume is limited when injection occurs into an aquifer that has been exempted from protection as a USDW.

There will be no restrictions on the cumulative volume or daily volume of authorized Class II fluid to be injected into the approved Green River Formation interval. The permittee shall not exceed the authorized injection pressure.

Mechanical Integrity (40 CFR 146.8)

An injection well has mechanical integrity if:

1. there is no significant leak in the casing, tubing, or packer (Part I); and
2. there is no significant fluid movement into a USDW through vertical channels adjacent to the injection well bore (Part II).

The Permit prohibits injection into a well which lacks mechanical integrity.

The Permit requires that the well demonstrate mechanical integrity prior to injection and periodically thereafter. A demonstration of mechanical integrity includes both internal (Part I) and external (Part II). The methods and frequency for demonstrating Part I and Part II mechanical integrity are dependent upon well-specific conditions as explained below.

Well construction and site-specific conditions dictate the following requirements for Mechanical Integrity (MI) demonstrations:

PART I MI: Internal MI will be demonstrated prior to beginning injection. Since this well is constructed with a standard casing, tubing, and packer configuration, a successful mechanical integrity test (MIT) is required to take place at least once every five (5) years. A demonstration of Part I MI is also required prior to resuming injection following any workover operation that affects the casing, tubing or packer. Part I MI may be demonstrated by a standard tubing-casing annulus pressure test using the maximum permitted injection pressure or 1000 psi, which ever is less, with a ten (10) percent or less pressure loss over thirty (30) minutes.

PART VI. Monitoring, Recordkeeping and Reporting Requirements

Injection Well Monitoring Program

At least once a year the permittee must analyze a sample of the injected fluid for total dissolved solids (TDS), specific conductivity, pH, and specific gravity. This analysis shall be reported to EPA annually as part of the Annual Report to the Director. Any time a new source of injected fluid is added, a fluid analysis shall be made of the new source.

Instantaneous injection pressure, injection flow rate, cumulative fluid volume and TCA pressures must be observed on a weekly basis. A recording, at least once every thirty (30) days, must be made of the injection pressure, annulus pressure, monthly injection flow rate and cumulative fluid volume. This information is required to be reported annually as part of the Annual Report to the Director.

PART VII. Plugging and Abandonment Requirements (40 CFR 146.10)

Plugging and Abandonment Plan

Prior to abandonment, the well shall be plugged in a manner that isolates the injection zone and prevents movement of fluid into or between USDWs, and in accordance with any applicable Federal, State or local law or regulation. Tubing, packer and other downhole apparatus shall be removed. Cement with additives such as accelerators and retarders that control or enhance cement properties may be used for plugs; however, volume-extending additives and gel cements are not approved for plug use. Plug placement shall be verified by tagging. Plugging gel of at least 9.6 lb/gal shall be placed between all plugs. A minimum 50 ft surface plug shall be set inside and outside of the surface casing to seal pathways for fluid migration into the subsurface. Within sixty (60) days after plugging the owner or operator shall submit Plugging Record (EPA Form 7520 13) to the Director. The Plugging Record must be certified as accurate and complete by the person responsible for the plugging operation. The plugging and abandonment plan is described in Appendix E of the Permit.

The well shall be plugged in a manner that isolates the injection zone and prevents movement of fluid into or between USDWs and in accordance with other applicable Federal, State or local law or

regulation. Tubing, packers, and any downhole apparatus shall be removed. Class A, C, G, and H cements, with additives such as accelerators and retarders that control or enhance cement properties, may be used for plugs. However, volume extending additives and gel cements are not approved for plug use. Plug placement shall be verified by tagging. Plugging gel of at least 9.2 lb/gal shall be placed between all plugs. Within sixty (60) days after plugging, the owner or operator shall submit Plugging Record (EPA Form 7520-13) to the Director. The Plugging Record must be certified as accurate and complete by the person responsible for the plugging operation. At a minimum, the following plugs are required:

PLUG NO. 1: Seal Injection Zone: Set a cast iron bridge plug (CIBP) no more than fifty (50) feet above the top injection perforation. Place at least twenty (20) feet of cement plug on top of the CIBP.

PLUG NO. 2: Seal Mahogany Shale and Trona intervals: Squeeze a cement plug on the backside of the 5-1/2 inch casing across the Trona Zone and the Mahogany Shale approximately 3050 feet to 3215 feet (unless pre-existing backside cement precludes cement-squeezing this interval) followed by a minimum 165-foot balanced cement plug inside the 5-1/2 inch casing across the Trona Zone and the Mahogany Shale, approximately 3050 feet to 3215 feet.

PLUG NO. 3: Seal USDWs: Squeeze a cement plug (1500 feet - 1600 feet) on the backside of the 5-1/2 inch casing across the base of the Uinta formation (unless pre-existing backside cement precludes cement-squeezing this interval), followed by a minimum 100-foot balanced cement plug inside the 5-1/2 inch casing across the base of the Uinta Formation, approximately 1500 feet to 1600 feet.

PLUG NO.4: Seal Surface: Set a Class "G" cement plug within the 5-1/2 inch casing to 367 feet and up the 5-1/2 inch by 8-5/8 inch casings annulus to the surface.

PART VIII. Financial Responsibility (40 CFR 144.52)

Demonstration of Financial Responsibility

The permittee is required to maintain financial responsibility and resources to close, plug, and abandon the underground injection operation in a manner prescribed by the Director. The permittee shall show evidence of such financial responsibility to the Director by the submission of a surety bond, or other adequate assurance such as financial statements or other materials acceptable to the Director. The Regional Administrator may, on a periodic basis, require the holder of a lifetime permit to submit a revised estimate of the resources needed to plug and abandon the well to reflect inflation of such costs, and a revised demonstration of financial responsibility if necessary. Initially, the operator has chosen to demonstrate financial responsibility with:

Financial Statement that was reviewed and approved by the EPA February 22, 2008.

Financial Statement, received April 22, 2005

Evidence of continuing financial responsibility is required to be submitted to the Director annually.

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
USA UTU-74872

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:
SUNDANCE UNIT

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

8. WELL NAME and NUMBER:
FEDERAL 1-33-8-18

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

9. API NUMBER:
4304736036

3. ADDRESS OF OPERATOR:
Route 3 Box 3630 CITY Myton STATE UT ZIP 84052

PHONE NUMBER
435.646.3721

10. FIELD AND POOL, OR WILDCAT:
MONUMENT BUTTE

4. LOCATION OF WELL:
FOOTAGES AT SURFACE: 906 FNL 705 FEL

COUNTY: UINTAH

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NENE, 33, T8S, R18E

STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: <u>04/16/2009</u>	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input checked="" type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: -
	<input checked="" type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above listed well was converted from an oil well to an injection well on 4/16/09.

On 4/1/09 Margo Smith with the EPA was contacted concerning the initial MIT on the above listed well. Permission was given at that time to perform the test on 4/8/09. On 4/22/09 the csg was pressured up to 1320 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tbq pressure was 220 psig during the test. There was not an EPA representative available to witness the test.

EPA# UT21100-07422

API# 43-047-36036

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY**

NAME (PLEASE PRINT) Callie Ross

TITLE Production Clerk

SIGNATURE *Callie Ross*

DATE 04/24/2009

(This space for State use only)

RECEIVED
APR 27 2009
DIV. OF OIL, GAS & MINING

Mechanical Integrity Test

Casing or Annulus Pressure Mechanical Integrity Test

U.S. Environmental Protection Agency
Underground Injection Control Program
999 18th Street, Suite 500 Denver, CO 80202-2466

EPA Witness: _____ Date: 04/22/09
 Test conducted by: Dale Giles
 Others present: _____

Well Name: <u>Federal 1-33-B-18</u>	Type: ER SWD	Status: AC TA UC
Field: <u>Sundance Unit</u>		
Location: _____	Sec: <u>33 T 8 N 15 R 15 E</u> / W	County: <u>Uintah</u> State: <u>Wt.</u>
Operator: <u>Newfield Production Co.</u>		
Last MIT: <u>/ /</u>	Maximum Allowable Pressure: _____	PSIG

Is this a regularly scheduled test? Yes No
 Initial test for permit? Yes No
 Test after well rework? Yes No
 Well injecting during test? Yes No If Yes, rate: _____ bpd

Pre-test casing/tubing annulus pressure: 0 psig

MIT DATA TABLE	Test #1	Test #2	Test #3
TUBING PRESSURE			
Initial Pressure	<u>220</u> psig	psig	psig
End of test pressure	<u>220</u> psig	psig	psig
CASING / TUBING ANNULUS PRESSURE			
0 minutes	<u>1320</u> psig	psig	psig
5 minutes	<u>1320</u> psig	psig	psig
10 minutes	<u>1320</u> psig	psig	psig
15 minutes	<u>1320</u> psig	psig	psig
20 minutes	<u>1320</u> psig	psig	psig
25 minutes	<u>1320</u> psig	psig	psig
30 minutes	<u>1320</u> psig	psig	psig
_____ minutes	psig	psig	psig
_____ minutes	psig	psig	psig
RESULT	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail

Does the annulus pressure build back up after the test? Yes No

MECHANICAL INTEGRITY PRESSURE TEST

Additional comments for mechanical integrity pressure test, such as volume of fluid added to annulus and bled back at end of test, reason for failing test (casing head leak, tubing leak, other), etc.:

Signature of Witness: _____

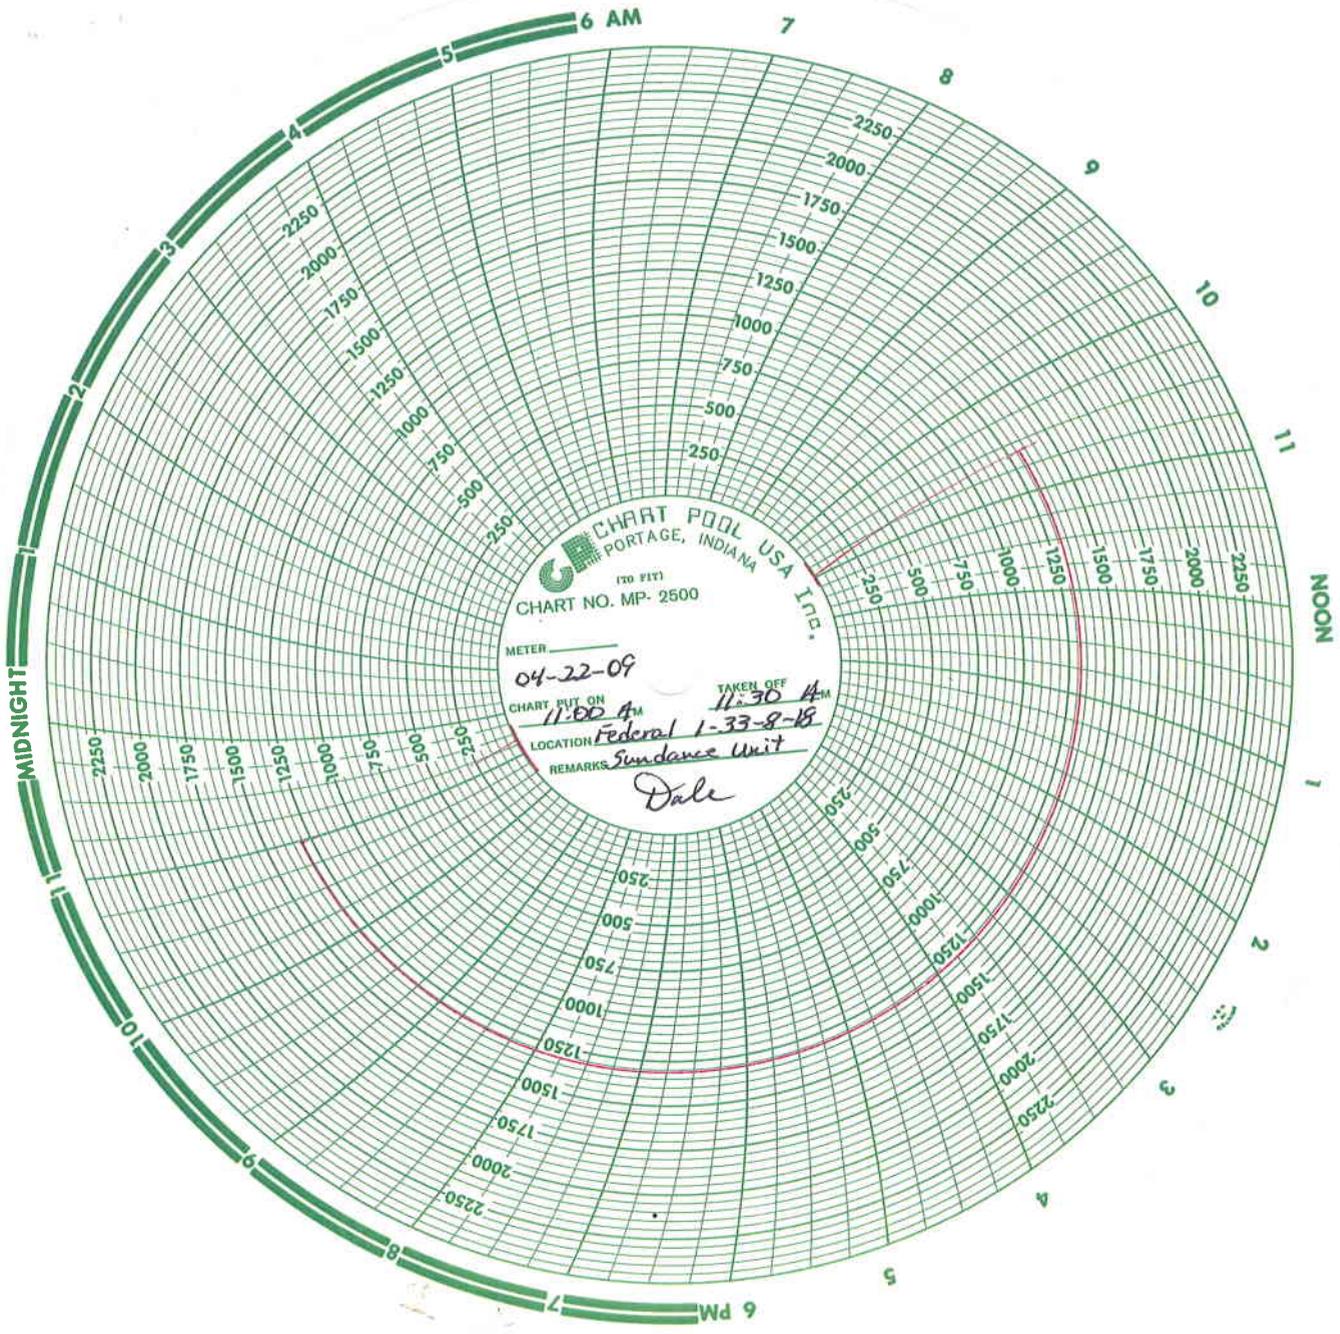


CHART POOL USA INC.
PORTAGE, INDIANA
170 FT
CHART NO. MP-2500

METER _____
04-22-09
CHART PUT ON 11:00 AM
TAKEN OFF 11:30 AM
LOCATION Federal 1-33-8-18
REMARKS Sundance Unit
Date



UNITED STATES ENVIRONMENTAL PROTECTION AGENCY
REGION 8

1595 Wynkoop Street
DENVER, CO 80202-1129
Phone 800-227-8917
<http://www.epa.gov/region08>

MAY 05 2009

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY**

Ref: 8P-W-GW

CERTIFIED MAIL
RETURN RECEIPT REQUESTED

Michael Guinn
District Manager
Newfield Production Company
Route 3 - Box 3630
Myton, UT 84052

RE: Authority to Commence Injection
EPA UIC Permit UT21100-07422
Federal No. 1-33-8-18
Uintah County, Utah
API #: 43-047-36036

85 18E 33

Dear Mr. Guinn:

Newfield Production Company (Newfield) has satisfactorily completed Environmental Protection Agency (EPA) Prior to Commencing Injection requirements for Final Permit, UT21100-07422, effective November 20, 2008. The Part I (Internal) Mechanical Integrity Test (MIT), Well Rework Record (EPA Form No. 7520-12), schematic diagram, and pore pressure, were reviewed and approved by EPA on April 28, 2009.

As of the date of this letter, Newfield is authorized to commence injection into Federal No. 1-33-8-18 at a maximum allowable injection pressure (MAIP) of 1,115 psig. Until such time as Permittee demonstrates through a Step Rate Test (SRT) that the Fracture Gradient (FG) is other than 0.690 psi/ft, Federal No.1-33-8-18 shall be operated at a MAIP no greater than 1,115 psig.

RECEIVED
MAY 11 2009
DIV. OF OIL, GAS & MINING

As of this approval, responsibility for permit compliance and enforcement is transferred to Region 8 UIC Technical Enforcement Program office. Therefore, please direct all monitoring and compliance correspondence to the following address, referencing your well name and UIC Permit number on all correspondence regarding this well to:

Mr. Nathan Wiser
Technical Enforcement Program – UIC
U.S. EPA Region 8: Mail Code 8ENF-UFO
1595 Wynkoop Street
Denver, CO 80202-1129

Or, you may contact Mr. Wiser by telephone at 303-312-6211, or 1 800-227-8927, ext. 312-6211.

Please remember that it is your responsibility to be aware of and to comply with all conditions of injection well Permit UT21100 -07422 .

If you have questions regarding the above action, please call Emmett Schmitz at 303-312-6174 or 1-800-227-8917, ext. 312-6174.

Sincerely,



Steven Pratt, P.E., CAPM (Inactive)
Director, Ground Water Program

cc: Uintah & Ouray Business Committee, Ute Indian Tribe
Curtis Cesspooch, Chairman
Irene Cuch, Vice-Chairwoman
Frances Poowegup, Councilwoman
Ronald Groves, Councilman
Phillip Chimburas, Councilman
Steven Cesspooch, Councilman

Daniel Picard, Superintendent
Uintah & Ouray Indian Agency
U.S. Bureau of Indian Affairs

Eric Sundberg
Newfield Production Company
Denver, CO

Larry Love
Director
Energy & Minerals Dept.
Ute Indian Tribe

Ferron Secakuku
Director
Natural Resources
Ute Indian Tribe

Gilbert Hunt
Associate Director
State of Utah – Division of Oil, Gas & Mining

Fluid Minerals Engineering Dept.
U.S. Bureau of Land Management
Vernal, Utah

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER:
USA UTU-74872

SUNDRY NOTICES AND REPORTS ON WELLS

6. IF INDIAN, ALLOTTEE OR TRIBE NAME:

7. UNIT or CA AGREEMENT NAME:
SUNDANCE UNIT

8. WELL NAME and NUMBER:
FEDERAL 1-33-8-18

9. API NUMBER:
4304736036

10. FIELD AND POOL, OR WILDCAT:
MONUMENT BUTTE

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

4. LOCATION OF WELL: FOOTAGES AT SURFACE: 906 FNL 705 FEL COUNTY: UINTAH

OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NENE, 33, T8S, R18E STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input checked="" type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will <u>07/07/2009</u>	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
<input type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: _____	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Change status, put well on injection.
	<input checked="" type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
The above reference well was put on injection at 10:00AM on 7-7-09.

UT 21100-07422

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY**

NAME (PLEASE PRINT) Kathy Chapman TITLE Office Manager
SIGNATURE *Kathy Chapman* DATE 07/08/2009

(This space for State use only)

RECEIVED
JUL 09 2009
DIV. OF OIL, GAS & MINING

STATE OF UTAH
DEPARTMENT OF NATURAL RESOURCES
DIVISION OF OIL, GAS AND MINING

5. LEASE DESIGNATION AND SERIAL NUMBER: USA UTU-74872
6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
7. UNIT or CA AGREEMENT NAME: SUNDANCE UNIT
8. WELL NAME and NUMBER: FEDERAL 1-33-8-18
9. API NUMBER: 4304736036
10. FIELD AND POOL, OR WILDCAT: MONUMENT BUTTE

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.

1. TYPE OF WELL: OIL WELL GAS WELL OTHER

2. NAME OF OPERATOR:
NEWFIELD PRODUCTION COMPANY

3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052 PHONE NUMBER 435.646.3721

4. LOCATION OF WELL:
FOOTAGES AT SURFACE: 906 FNL 705 FEL COUNTY: UINTAH
OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NENE, 33, T8S, R18E STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate) Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only) Date of Work Completion: 04/16/2009	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARILY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input checked="" type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input type="checkbox"/> OTHER: -
	<input checked="" type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.
The above listed well was converted from an oil well to an injection well on 4/16/09.
On 4/1/09 Margo Smith with the EPA was contacted concerning the initial MIT on the above listed well. Permission was given at that time to perform the test on 4/8/09. On 4/22/09 the csg was pressured up to 1320 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tbg pressure was 220 psig during the test. There was not an EPA representative available to witness the test.
EPA# UT21100-07422 API# 43-047-36036

RECEIVED

JUL 13 2009

DIV. OF OIL, GAS & MINING

NAME (PLEASE PRINT) Callie Ross TITLE Production Clerk
SIGNATURE _____ DATE 04/24/2009

(This space for State use only)

Daily Activity Report

Format For Sundry

FEDERAL 1-33-8-18**2/1/2009 To 6/30/2009****4/15/2009 Day: 1****Conversion**

Nabors #1111 on 4/14/2009 - MIRU Nabors #1111. RD pumping unit. Hot oiler had pumped 60 BW down csg @ 250°. Soft seat rods & pump. Pump 30 BW down tbg @ 250°, tbg did not fill. TOOH w/ rods as follows (LD on trailer): 1 1/2" X 22' polished rod, 2' X 3/4" pony rod, 100- 3/4" guided rods, 102- 3/4" plain rods, 30- 3/4" guided rods, 6- 1 1/2" weight rods & 2 1/2" X 1 1/2" X 10' X 14' RHAC rod pump. Flushed rods & tbg w/ additional 20 BW @ 250° during TOOH. X-over for tbg. ND wellhead. Release TA. NU BOPs. RU rig floor. SWIFN.

4/16/2009 Day: 2**Conversion**

Nabors #1111 on 4/15/2009 - TOOH w/ 187- jts 2 7/8" J-55 tbg (tallying, breaking collars & applying Liquid O-ring to threads) TA, 1- jt tbg, SN, 1- jt tbg, PBGA, 3 jts tbg, bull plug. LD 53- jts 2 7/8" tbg & BHA. Flushed tbg w/ 30 BW @ 250° during TOOH. PU & TIH w/ Weatherford Arrowset 1-X packer, SN & 139- jts 2 7/8" J-55 6.5# tbg. Flush tbg w/ 30 BW & drop standing valve. Pressure tbg to 3000 psi. Lost 200 psi in 15 min. Pressure tbg to 3000 psi. SW

4/17/2009 Day: 3**Conversion**

Nabors #1111 on 4/16/2009 - Tbg pressure had dropped to 2000 psi. Pressure tbg to 3000 psi. Held pressure for 30 min w/ 0psi loss. RU sandline. RIH w/ fishing tool on sandline & retrieve standing valve. RD rig floor. ND BOPs. NU wellhead. Pump 75 bbbls packer fluid down tbg-csg annulus. ND wellhead. Set Arrowset 1-X packer w/ CE @ 4409' w/ 15,000# tension. NU wellhead. Pressure test annulus to 1400 psi, held test for 30 min w/ 0 psi loss. RDMOSU. Ready for MIT!

4/23/2009 Day: 4**Conversion**

Rigless on 4/22/2009 - On 4/1/09 Margo Smith with the EPA was contacted concerning the initial MIT on the above listed well (Fed 1-33-8-18). Permission was given at that time to perform the test on 4/8/09. On 4/22/09 the csg was pressured up to 1320 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tbg pressure was 220 psig during the test. There was not an EPA representative available to witness the test. Final Report! EPA# UT21100-07422 API# 43-047-36036

UNITED STATES
DEPARTMENT OF THE INTERIOR
BUREAU OF LAND MANAGEMENT

SUNDRY NOTICES AND REPORTS ON WELL
Do not use this form for proposals to drill or to re-enter an abandoned well. Use Form 3160-3 (APD) for such proposals.

SUBMIT IN TRIPLICATE - Other Instructions on page 2

1. Type of Well <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other		5. Lease Serial No. USA UTU-74872
2. Name of Operator NEWFIELD PRODUCTION COMPANY		6. If Indian, Allottee or Tribe Name.
3a. Address Route 3 Box 3630 Myton, UT 84052	3b. Phone (include are code) 435.646.3721	7. If Unit or CA/Agreement, Name and/or SUNDANCE UNIT
4. Location of Well (Footage, Sec., T., R., M., or Survey Description) 906 FNL 705 FEL NENE Section 33 T8S R18E		8. Well Name and No. FEDERAL 1-33-8-18
		9. API Well No. 4304736036
		10. Field and Pool, or Exploratory Area MONUMENT BUTTE
		11. County or Parish, State UINTAH, UT

12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Step Rate Test _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	_____

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

A step rate test was conducted on the subject well on November 3, 2009. Results from the test indicate that the fracture gradient is .717 psi/ft. Therefore, Newfield is requesting that the maximum allowable injection pressure (MAIP) be changed to 1240 psi.

**Accepted by the
Utah Division of
Oil, Gas and Mining
FOR RECORD ONLY**

I hereby certify that the foregoing is true and correct <i>Printed/ Typed</i> Chevenne Bateman	Title Well Analyst Foreman
Signature 	Date 11/17/2009

THIS SPACE FOR FEDERAL OR STATE OFFICE USE

Approved by _____	Title _____	Date _____
Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.	Office _____	

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction


(Instructions on page 2)

RECEIVED

NOV 19 2009

DIV. OF OIL, GAS & MINING

Federal 1-33-8-18
Sundance Unit
Step Rate Test
November 3, 2009

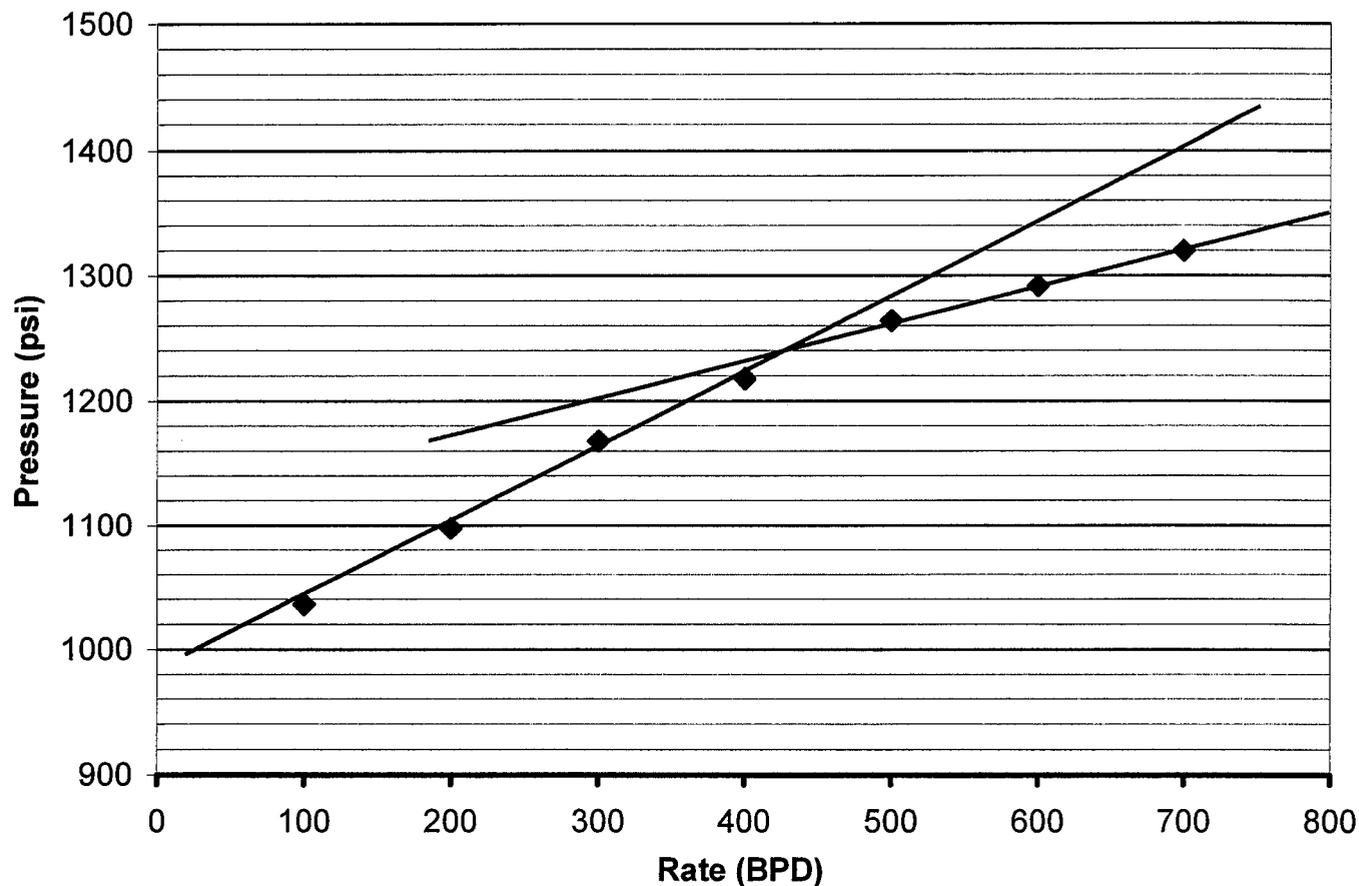

Start Pressure:

919 psi

Instantaneous Shut In Pressure (ISIP):

1272 psi

Top Perforation:

4470 feet


Fracture pressure (Pfp):

1240 psi

FG:

0.717 psi/ft

<u>Step</u>	<u>Rate(bpd)</u>	<u>Pressure(psi)</u>
1	100	1036
2	200	1098
3	300	1168
4	400	1218
5	500	1264
6	600	1292
7	700	1320

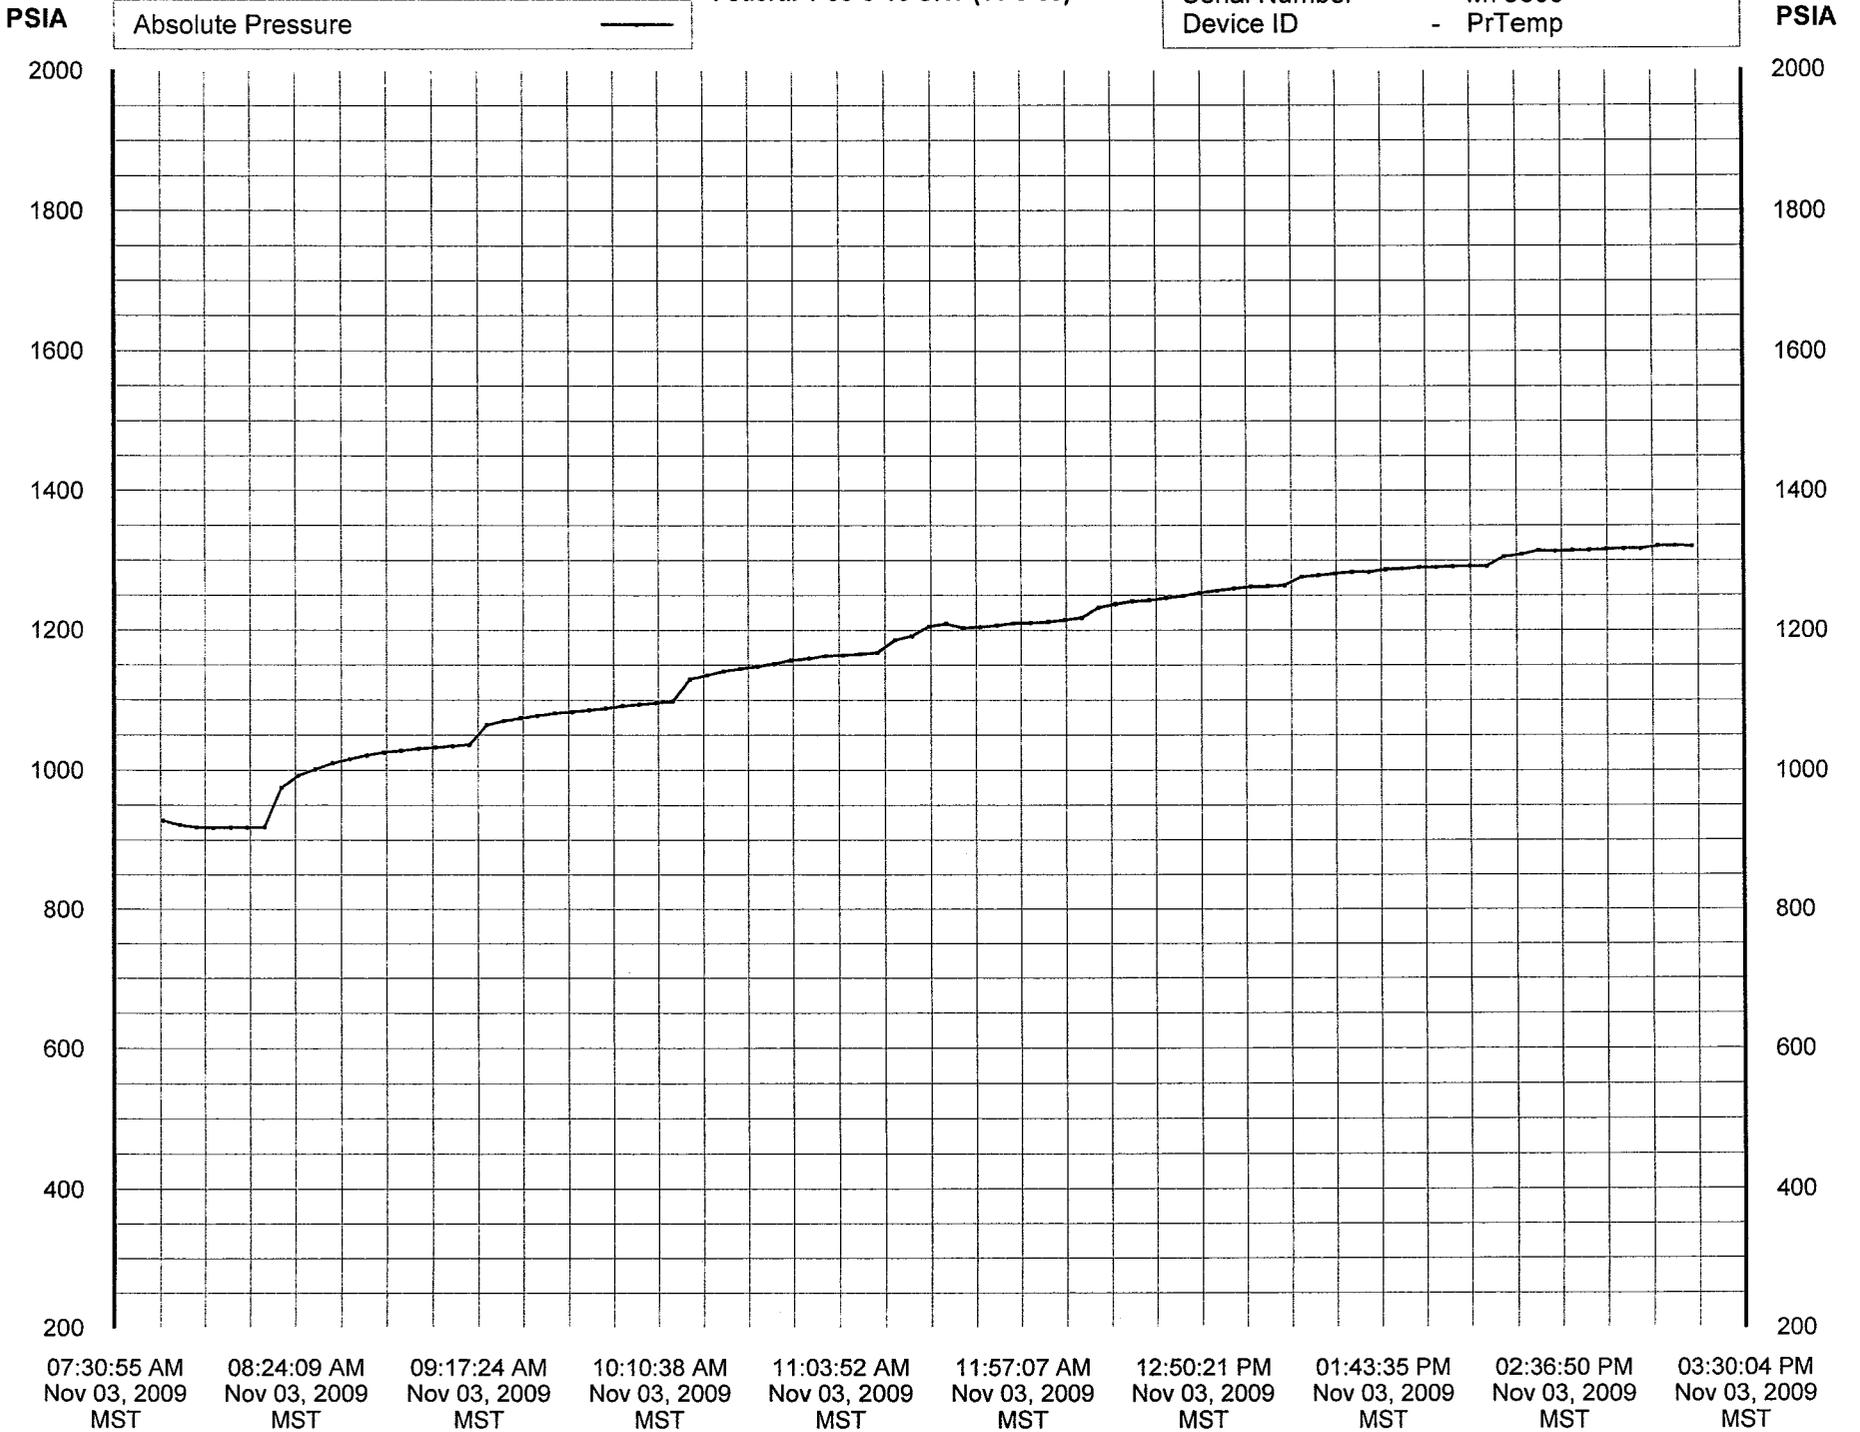

Report Name: PrTemp1000 Data Table
 Report Date: Nov 04, 2009 08:14:49 AM MST
 File Name: S:\Welinfo\PTC@ Instruments 2.00\Federal 1-33-8-18 SRT (11-3-09).csv
 Title: Federal 1-33-8-18 SRT (11-3-09)
 Device: PrTemp1000 - Temperature and Pressure Recorder
 Hardware Revision: REV2C (64K)
 Serial Number: M75866
 Device ID: PrTemp
 Data Start Date: Nov 03, 2009 07:45:00 AM MST
 Data End Date: Nov 03, 2009 03:14:59 PM MST
 Reading Rate: 2 Seconds
 Readings: 1 to 91 of 91
 Last Calibration Date: May 22, 2009
 Next Calibration Date: May 22, 2010

<u>Reading</u>	<u>Date and Time (MST)</u>	<u>Absolute Pressure</u>	<u>Annotation</u>
1	Nov 03, 2009 07:45:00 AM	928.400	PSIA
2	Nov 03, 2009 07:49:59 AM	922.200	PSIA
3	Nov 03, 2009 07:54:59 AM	918.800	PSIA
4	Nov 03, 2009 07:59:59 AM	917.800	PSIA
5	Nov 03, 2009 08:05:01 AM	918.200	PSIA
6	Nov 03, 2009 08:10:00 AM	918.200	PSIA
7	Nov 03, 2009 08:15:01 AM	919.000	PSIA
8	Nov 03, 2009 08:19:59 AM	975.000	PSIA
9	Nov 03, 2009 08:25:00 AM	991.800	PSIA
10	Nov 03, 2009 08:29:59 AM	1001.200	PSIA
11	Nov 03, 2009 08:35:00 AM	1009.800	PSIA
12	Nov 03, 2009 08:40:00 AM	1015.800	PSIA
13	Nov 03, 2009 08:45:00 AM	1021.200	PSIA
14	Nov 03, 2009 08:50:00 AM	1025.400	PSIA
15	Nov 03, 2009 08:55:00 AM	1027.800	PSIA
16	Nov 03, 2009 09:00:01 AM	1030.800	PSIA
17	Nov 03, 2009 09:04:59 AM	1032.400	PSIA
18	Nov 03, 2009 09:10:01 AM	1034.600	PSIA
19	Nov 03, 2009 09:14:59 AM	1036.200	PSIA
20	Nov 03, 2009 09:20:00 AM	1064.600	PSIA
21	Nov 03, 2009 09:25:00 AM	1070.000	PSIA
22	Nov 03, 2009 09:30:00 AM	1074.200	PSIA
23	Nov 03, 2009 09:35:00 AM	1077.600	PSIA
24	Nov 03, 2009 09:39:59 AM	1081.000	PSIA
25	Nov 03, 2009 09:45:00 AM	1083.200	PSIA
26	Nov 03, 2009 09:49:59 AM	1085.600	PSIA
27	Nov 03, 2009 09:55:00 AM	1088.000	PSIA
28	Nov 03, 2009 10:00:00 AM	1091.800	PSIA
29	Nov 03, 2009 10:04:59 AM	1093.400	PSIA
30	Nov 03, 2009 10:09:59 AM	1095.800	PSIA
31	Nov 03, 2009 10:15:00 AM	1098.000	PSIA
32	Nov 03, 2009 10:20:00 AM	1129.400	PSIA
33	Nov 03, 2009 10:25:00 AM	1135.200	PSIA
34	Nov 03, 2009 10:30:01 AM	1141.000	PSIA
35	Nov 03, 2009 10:35:00 AM	1144.600	PSIA
36	Nov 03, 2009 10:40:01 AM	1147.800	PSIA
37	Nov 03, 2009 10:45:00 AM	1151.600	PSIA
38	Nov 03, 2009 10:50:00 AM	1156.600	PSIA
39	Nov 03, 2009 10:55:00 AM	1159.200	PSIA
40	Nov 03, 2009 11:00:00 AM	1163.200	PSIA
41	Nov 03, 2009 11:05:01 AM	1164.000	PSIA
42	Nov 03, 2009 11:09:59 AM	1165.600	PSIA
43	Nov 03, 2009 11:15:01 AM	1167.800	PSIA
44	Nov 03, 2009 11:20:00 AM	1185.800	PSIA
45	Nov 03, 2009 11:25:01 AM	1191.400	PSIA
46	Nov 03, 2009 11:30:00 AM	1205.200	PSIA
47	Nov 03, 2009 11:35:00 AM	1209.200	PSIA
48	Nov 03, 2009 11:40:01 AM	1203.000	PSIA
49	Nov 03, 2009 11:45:00 AM	1204.400	PSIA
50	Nov 03, 2009 11:50:01 AM	1207.000	PSIA
51	Nov 03, 2009 11:54:59 AM	1210.000	PSIA
52	Nov 03, 2009 12:00:01 PM	1210.600	PSIA
53	Nov 03, 2009 12:05:00 PM	1212.000	PSIA
54	Nov 03, 2009 12:10:01 PM	1214.800	PSIA
55	Nov 03, 2009 12:15:00 PM	1217.600	PSIA
56	Nov 03, 2009 12:20:00 PM	1232.400	PSIA
57	Nov 03, 2009 12:25:00 PM	1237.800	PSIA
58	Nov 03, 2009 12:30:00 PM	1241.400	PSIA
59	Nov 03, 2009 12:35:01 PM	1242.800	PSIA
60	Nov 03, 2009 12:40:00 PM	1246.000	PSIA

61	Nov 03, 2009 12:45:01 PM	1249.000	PSIA
62	Nov 03, 2009 12:50:01 PM	1253.400	PSIA
63	Nov 03, 2009 12:55:02 PM	1256.800	PSIA
64	Nov 03, 2009 01:00:00 PM	1259.800	PSIA
65	Nov 03, 2009 01:05:00 PM	1262.400	PSIA
66	Nov 03, 2009 01:10:00 PM	1263.000	PSIA
67	Nov 03, 2009 01:15:00 PM	1264.200	PSIA
68	Nov 03, 2009 01:20:01 PM	1276.400	PSIA
69	Nov 03, 2009 01:25:00 PM	1278.600	PSIA
70	Nov 03, 2009 01:30:01 PM	1281.000	PSIA
71	Nov 03, 2009 01:35:00 PM	1283.400	PSIA
72	Nov 03, 2009 01:40:01 PM	1283.400	PSIA
73	Nov 03, 2009 01:45:00 PM	1287.200	PSIA
74	Nov 03, 2009 01:50:00 PM	1288.200	PSIA
75	Nov 03, 2009 01:55:00 PM	1290.000	PSIA
76	Nov 03, 2009 02:00:00 PM	1290.400	PSIA
77	Nov 03, 2009 02:05:01 PM	1291.200	PSIA
78	Nov 03, 2009 02:10:00 PM	1292.000	PSIA
79	Nov 03, 2009 02:15:01 PM	1291.800	PSIA
80	Nov 03, 2009 02:20:00 PM	1305.200	PSIA
81	Nov 03, 2009 02:25:01 PM	1309.000	PSIA
82	Nov 03, 2009 02:30:00 PM	1314.600	PSIA
83	Nov 03, 2009 02:34:59 PM	1313.400	PSIA
84	Nov 03, 2009 02:39:59 PM	1314.600	PSIA
85	Nov 03, 2009 02:45:00 PM	1315.000	PSIA
86	Nov 03, 2009 02:50:00 PM	1316.200	PSIA
87	Nov 03, 2009 02:55:00 PM	1317.000	PSIA
88	Nov 03, 2009 03:00:00 PM	1317.000	PSIA
89	Nov 03, 2009 03:04:59 PM	1320.800	PSIA
90	Nov 03, 2009 03:10:00 PM	1321.400	PSIA
91	Nov 03, 2009 03:14:59 PM	1320.400	PSIA


PSIA

Absolute Pressure

Federal 1-33-8-18 ISIP (11-3-09)

Device - PrTemp1000
Serial Number - M75866
Device ID - PrTemp

PSIA

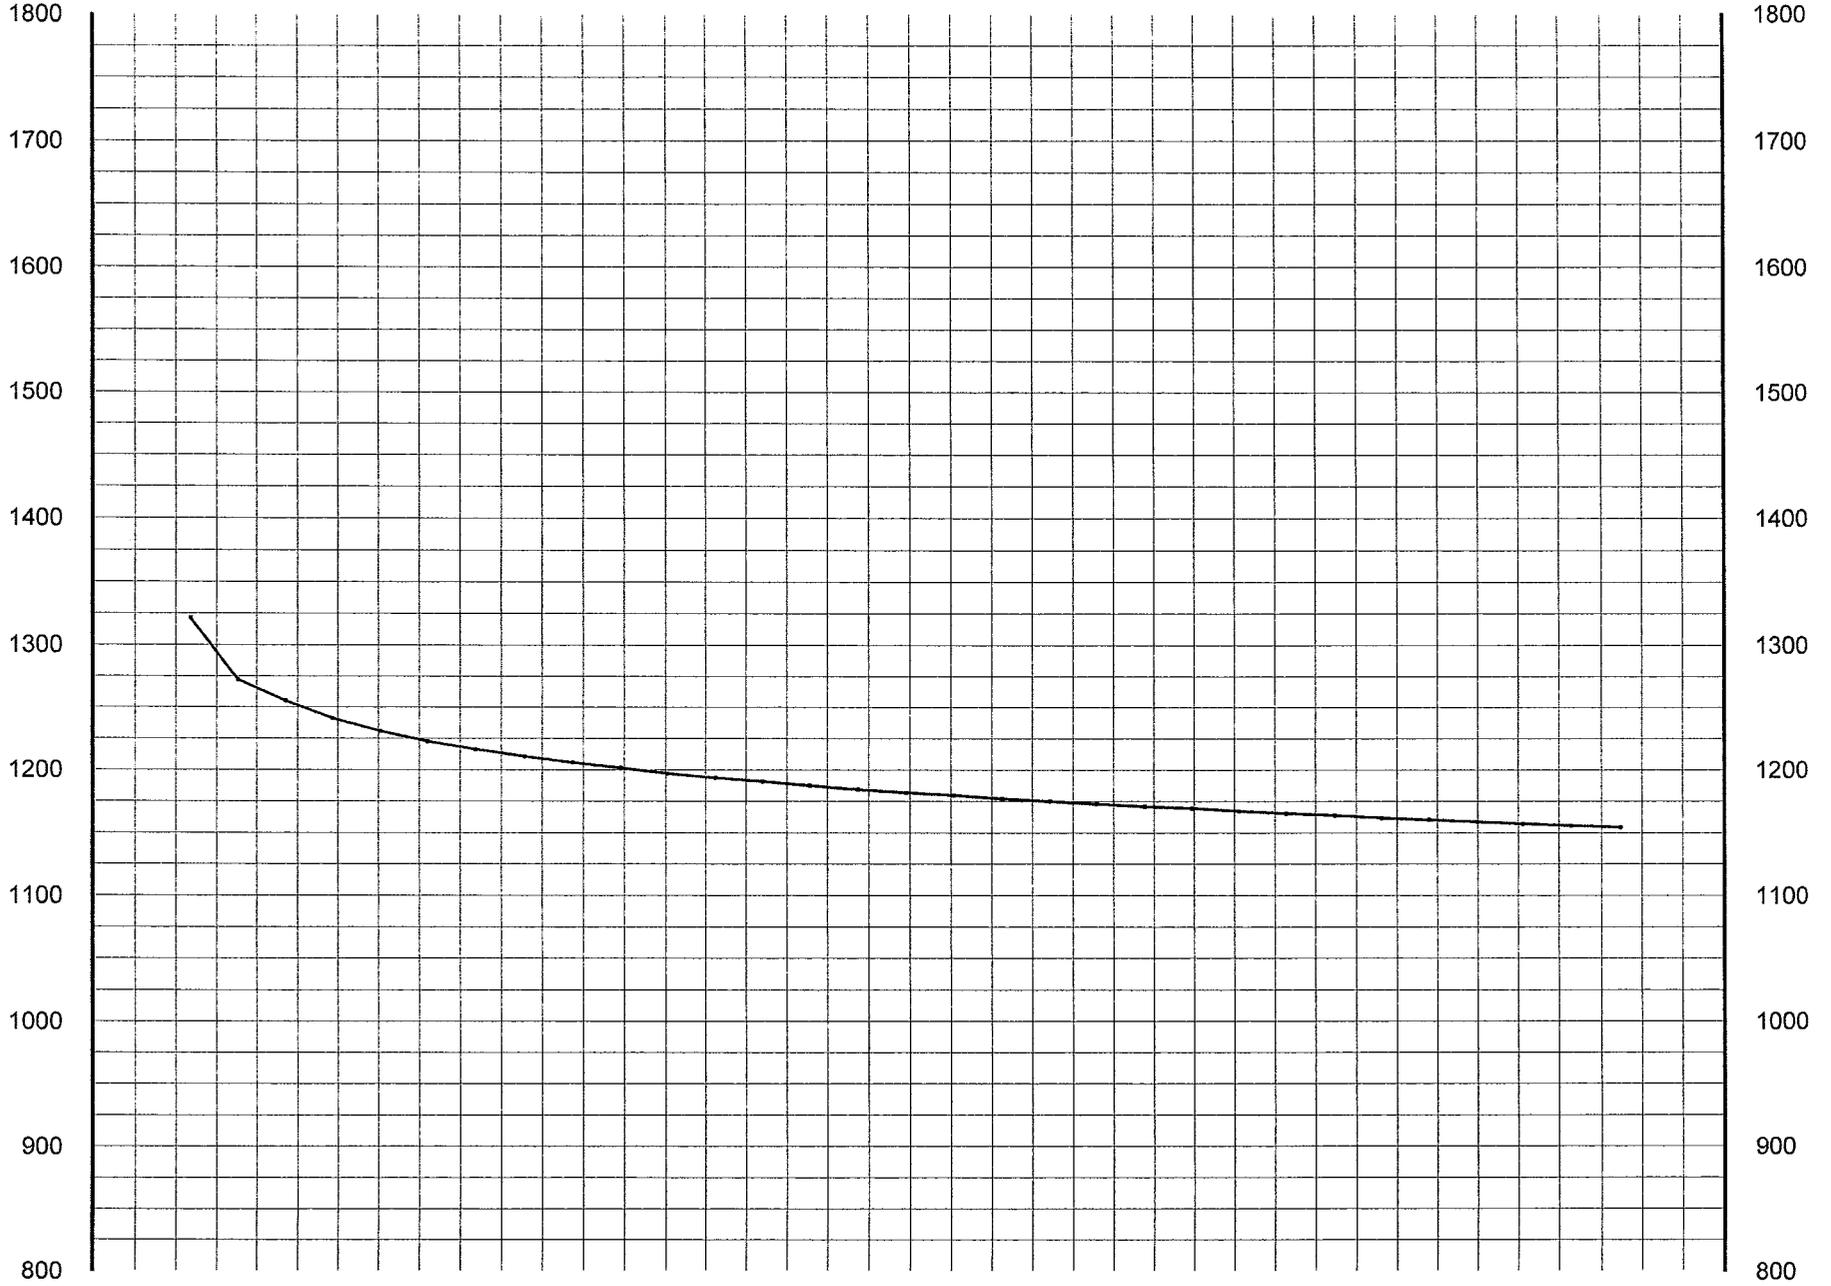

03:13:10 PM Nov 03, 2009 MST
03:16:35 PM Nov 03, 2009 MST
03:20:00 PM Nov 03, 2009 MST
03:23:25 PM Nov 03, 2009 MST
03:26:50 PM Nov 03, 2009 MST
03:30:15 PM Nov 03, 2009 MST
03:33:40 PM Nov 03, 2009 MST
03:37:05 PM Nov 03, 2009 MST
03:40:30 PM Nov 03, 2009 MST
03:43:55 PM Nov 03, 2009 MST
03:47:20 PM Nov 03, 2009 MST

Report Name: PrTemp1000 Data Table
 Report Date: Nov 04, 2009 08:14:39 AM MST
 File Name: S:\Welinfo\PTC@ Instruments 2.00\Federal 1-33-8-18 ISIP (11-3-09).csv
 Title: Federal 1-33-8-18 ISIP (11-3-09)
 Device: PrTemp1000 - Temperature and Pressure Recorder
 Hardware Revision: REV2C (64K)
 Serial Number: M75866
 Device ID: PrTemp
 Data Start Date: Nov 03, 2009 03:15:11 PM MST
 Data End Date: Nov 03, 2009 03:45:11 PM MST
 Reading Rate: 2 Seconds
 Readings: 1 to 31 of 31
 Last Calibration Date: May 22, 2009
 Next Calibration Date: May 22, 2010

<u>Reading</u>	<u>Date and Time (MST)</u>	<u>Absolute Pressure</u>	<u>Annotation</u>
1	Nov 03, 2009 03:15:11 PM	1321.200	PSIA
2	Nov 03, 2009 03:16:11 PM	1272.200	PSIA
3	Nov 03, 2009 03:17:11 PM	1255.400	PSIA
4	Nov 03, 2009 03:18:10 PM	1241.400	PSIA
5	Nov 03, 2009 03:19:11 PM	1231.000	PSIA
6	Nov 03, 2009 03:20:10 PM	1222.800	PSIA
7	Nov 03, 2009 03:21:10 PM	1216.400	PSIA
8	Nov 03, 2009 03:22:12 PM	1210.800	PSIA
9	Nov 03, 2009 03:23:12 PM	1205.800	PSIA
10	Nov 03, 2009 03:24:12 PM	1201.400	PSIA
11	Nov 03, 2009 03:25:10 PM	1197.000	PSIA
12	Nov 03, 2009 03:26:12 PM	1193.600	PSIA
13	Nov 03, 2009 03:27:11 PM	1190.600	PSIA
14	Nov 03, 2009 03:28:10 PM	1187.400	PSIA
15	Nov 03, 2009 03:29:11 PM	1184.400	PSIA
16	Nov 03, 2009 03:30:11 PM	1181.800	PSIA
17	Nov 03, 2009 03:31:10 PM	1179.600	PSIA
18	Nov 03, 2009 03:32:11 PM	1177.000	PSIA
19	Nov 03, 2009 03:33:11 PM	1175.000	PSIA
20	Nov 03, 2009 03:34:10 PM	1172.800	PSIA
21	Nov 03, 2009 03:35:11 PM	1170.800	PSIA
22	Nov 03, 2009 03:36:11 PM	1169.400	PSIA
23	Nov 03, 2009 03:37:11 PM	1167.200	PSIA
24	Nov 03, 2009 03:38:11 PM	1165.400	PSIA
25	Nov 03, 2009 03:39:12 PM	1163.800	PSIA
26	Nov 03, 2009 03:40:11 PM	1161.800	PSIA
27	Nov 03, 2009 03:41:11 PM	1160.400	PSIA
28	Nov 03, 2009 03:42:12 PM	1158.800	PSIA
29	Nov 03, 2009 03:43:10 PM	1157.200	PSIA
30	Nov 03, 2009 03:44:10 PM	1155.600	PSIA
31	Nov 03, 2009 03:45:11 PM	1154.400	PSIA

STATE OF UTAH DEPARTMENT OF NATURAL RESOURCES DIVISION OF OIL, GAS, AND MINING		FORM 9
SUNDRY NOTICES AND REPORTS ON WELLS Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.		5. LEASE DESIGNATION AND SERIAL NUMBER: UTU-74872
1. TYPE OF WELL Water Injection Well		6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY		7. UNIT or CA AGREEMENT NAME: GMBU (GRRV)
3. ADDRESS OF OPERATOR: Rt 3 Box 3630 , Myton, UT, 84052		8. WELL NAME and NUMBER: FEDERAL 1-33-8-18
4. LOCATION OF WELL FOOTAGES AT SURFACE: 0906 FNL 0705 FEL QTR/QTR, SECTION, TOWNSHIP, RANGE, MERIDIAN: Qtr/Qtr: NENE Section: 33 Township: 08.0S Range: 18.0E Meridian: S		9. API NUMBER: 43047360360000
PHONE NUMBER: 435 646-4825 Ext		9. FIELD and POOL or WILDCAT: 8 MILE FLAT NORTH
COUNTY: UINTAH		STATE: UTAH
11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA		
TYPE OF SUBMISSION	TYPE OF ACTION	
<input type="checkbox"/> NOTICE OF INTENT Approximate date work will start:	<input type="checkbox"/> ACIDIZE <input type="checkbox"/> ALTER CASING <input type="checkbox"/> CASING REPAIR <input type="checkbox"/> CHANGE TO PREVIOUS PLANS <input type="checkbox"/> CHANGE TUBING <input type="checkbox"/> CHANGE WELL NAME <input type="checkbox"/> CHANGE WELL STATUS <input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS <input type="checkbox"/> CONVERT WELL TYPE <input type="checkbox"/> DEEPEN <input type="checkbox"/> FRACTURE TREAT <input type="checkbox"/> NEW CONSTRUCTION <input type="checkbox"/> OPERATOR CHANGE <input type="checkbox"/> PLUG AND ABANDON <input type="checkbox"/> PLUG BACK <input type="checkbox"/> PRODUCTION START OR RESUME <input type="checkbox"/> RECLAMATION OF WELL SITE <input type="checkbox"/> RECOMPLETE DIFFERENT FORMATION <input type="checkbox"/> REPERFORATE CURRENT FORMATION <input type="checkbox"/> SIDETRACK TO REPAIR WELL <input type="checkbox"/> TEMPORARY ABANDON <input type="checkbox"/> TUBING REPAIR <input type="checkbox"/> VENT OR FLARE <input type="checkbox"/> WATER DISPOSAL <input type="checkbox"/> WATER SHUTOFF <input type="checkbox"/> SI TA STATUS EXTENSION <input type="checkbox"/> WILDCAT WELL DETERMINATION <input checked="" type="checkbox"/> OTHER	
<input checked="" type="checkbox"/> SUBSEQUENT REPORT Date of Work Completion: 3/17/2014	<input type="checkbox"/> OTHER: <input style="width: 50px;" type="text" value="5 YR MIT"/>	
<input type="checkbox"/> SPUD REPORT Date of Spud:	<input type="checkbox"/> APD EXTENSION	
<input type="checkbox"/> DRILLING REPORT Report Date:	<input type="checkbox"/> WATER SHUTOFF	
12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc. 5 YR MIT performed on the above listed well. On 03/17/2014 the casing was pressured up to 1602 psig and charted for 30 minutes with no pressure loss. The well was not injecting during the test. The tbg pressure was 952 psig during the test. There was not an EPA representative available to witness the test. EPA #UT22197-07422		
Accepted by the Utah Division of Oil, Gas and Mining FOR RECORD ONLY April 02, 2014		
NAME (PLEASE PRINT) Lucy Chavez-Naupoto	PHONE NUMBER 435 646-4874	TITLE Water Services Technician
SIGNATURE N/A	DATE 3/31/2014	

Mechanical Integrity Test

Casing or Annulus Pressure Mechanical Integrity Test

U.S. Environmental Protection Agency
Underground Injection Control Program
999 18th Street, Suite 500 Denver, CO 80202-2466

EPA Witness: _____ Date: 3/17/14

Test conducted by: Chris Walters

Others present: _____

Well Name: <u>1-33-8-18 Fed</u>	Type: ER SWD	Status: AC TA UC
Field: <u>Mon. Butte</u>		
Location: <u>NE/NE Sec: 33 T 8 N 18 R 18 E</u>	County: <u>Uintah</u>	State: <u>UT</u>
Operator: <u>Newfield</u>		
Last MIT: <u>1 1</u>	Maximum Allowable Pressure: _____	PSIG

Is this a regularly scheduled test? Yes No
 Initial test for permit? Yes No
 Test after well rework? Yes No
 Well injecting during test? Yes No If Yes, rate: 34 bpd

Pre-test casing/tubing annulus pressure: 1604 psig

MIT DATA TABLE	Test #1	Test #2	Test #3
TUBING PRESSURE			
Initial Pressure	<u>864</u> psig	psig	psig
End of test pressure	<u>952</u> psig	psig	psig
CASING / TUBING ANNULUS PRESSURE			
0 minutes	<u>1604</u> psig	psig	psig
5 minutes	<u>1607</u> psig	psig	psig
10 minutes	<u>1607</u> psig	psig	psig
15 minutes	<u>1605</u> psig	psig	psig
20 minutes	<u>1606</u> psig	psig	psig
25 minutes	<u>1605</u> psig	psig	psig
30 minutes	<u>1602</u> psig	psig	psig
_____ minutes	psig	psig	psig
_____ minutes	psig	psig	psig
RESULT	<input checked="" type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail	<input type="checkbox"/> Pass <input type="checkbox"/> Fail


Does the annulus pressure build back up after the test? Yes No

MECHANICAL INTEGRITY PRESSURE TEST

Additional comments for mechanical integrity pressure test, such as volume of fluid added to annulus and bled back at end of test, reason for failing test (casing head leak, tubing leak, other), etc.:

Signature of Witness: _____

1-33-8-18 Fed MIT 3-17-14
3/17/2014 8:34:04 AM

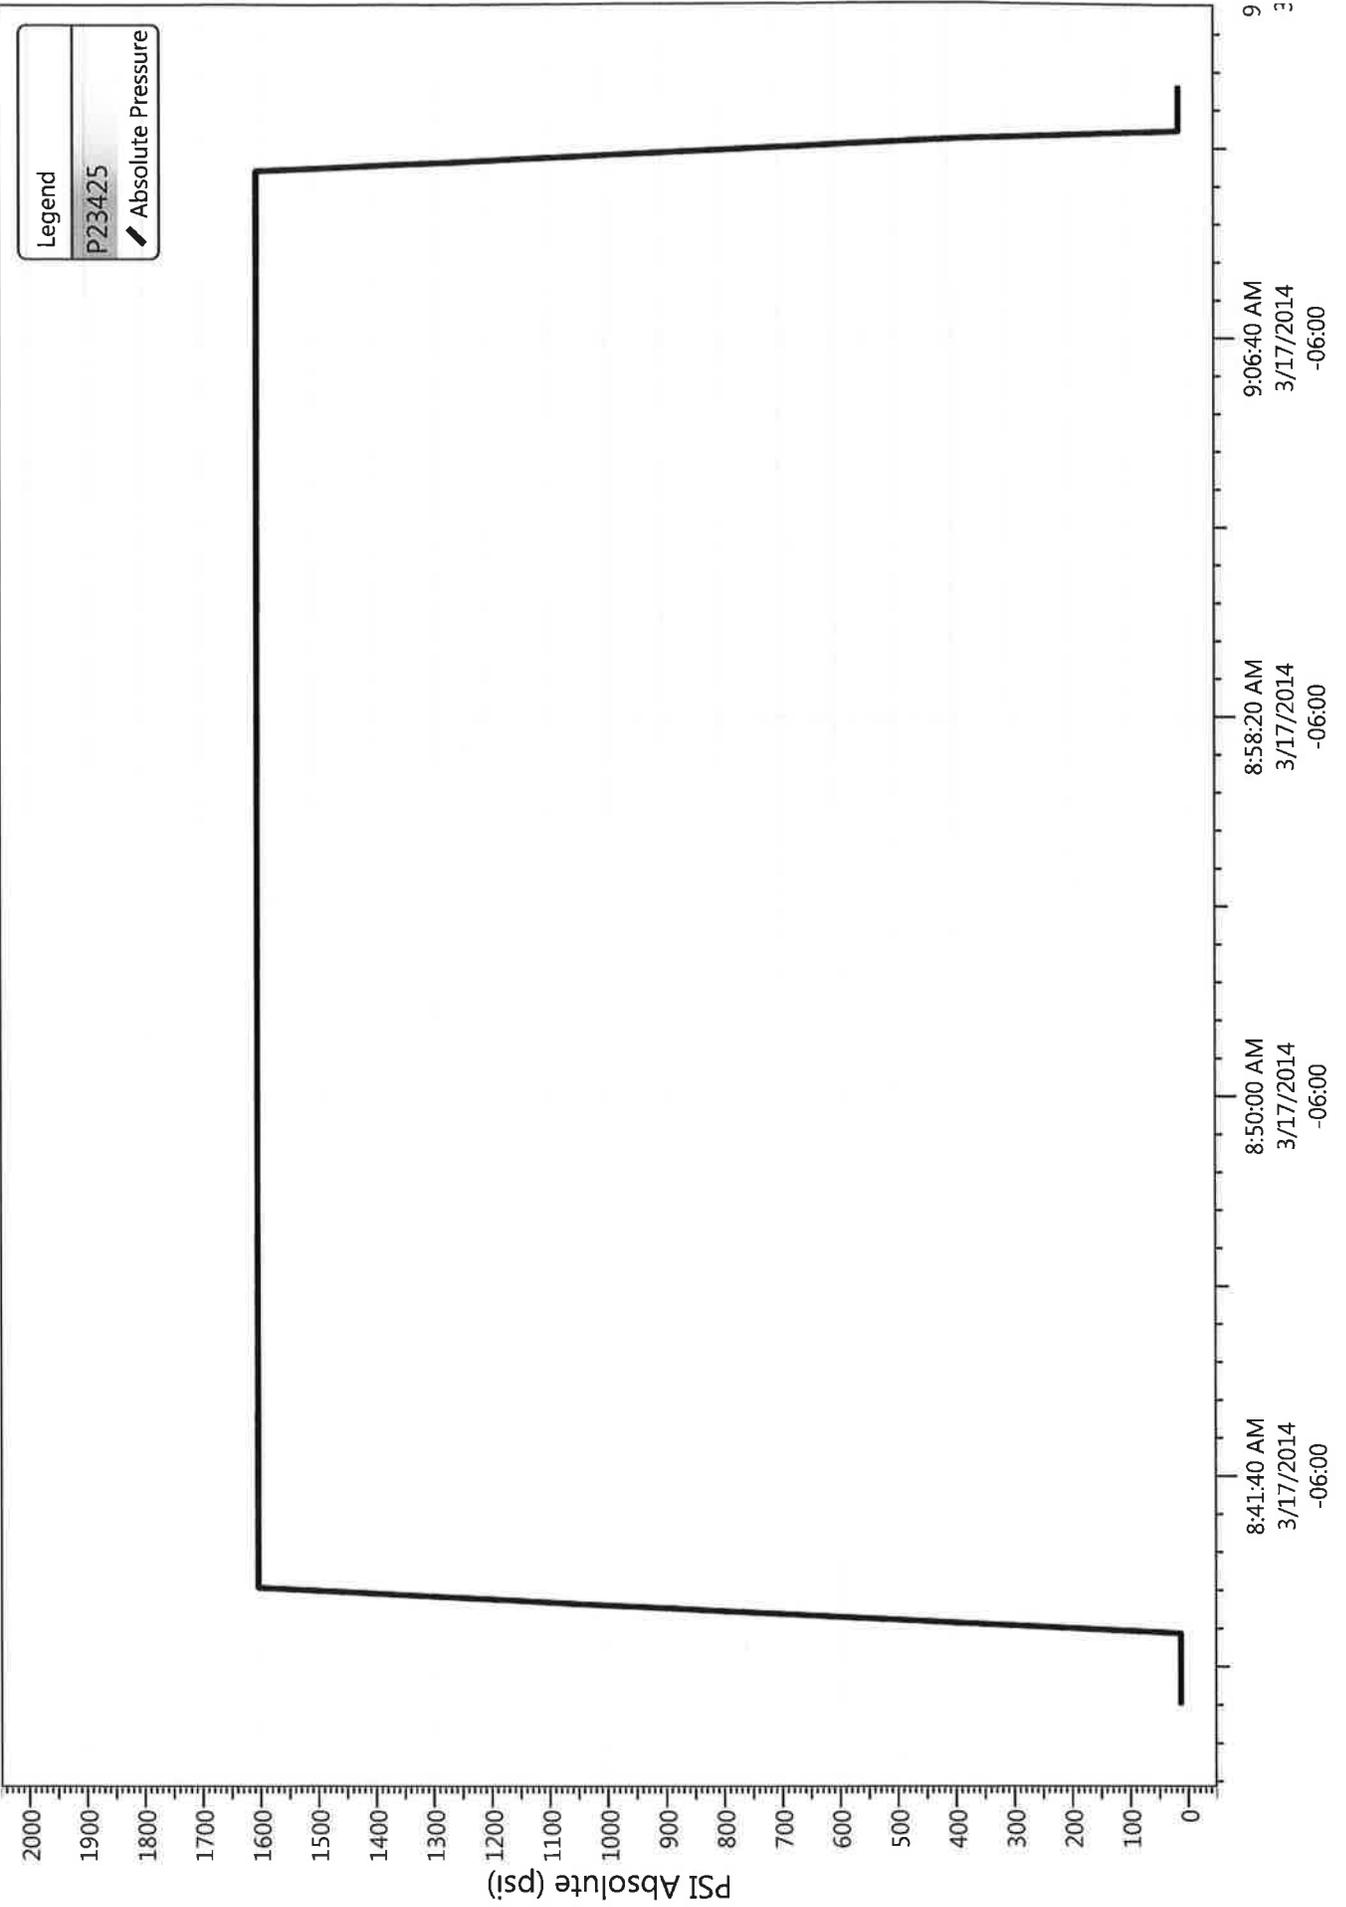


43-047-36036

Well Name: Federal 1-33-8-18

Surface Legal Location 33-8S-18E		API/UWI 43047360360000	Well RC 500160484	Lease	State/Province Utah	Field Name GMBU CTB9	County Uintah
Spud Date	Rig Release Date	On Production Date 5/23/2006	Original KB Elevation (ft) 4,881	Ground Elevation (ft) 4,869	Total Depth All (TVD) (ftKB)	PBTD (All) (ftKB) Original Hole - 6,170.0	

Most Recent Job				
Job Category Testing	Primary Job Type	Secondary Job Type N/A	Job Start Date 3/17/2014	Job End Date 3/17/2014

TD: 6,205.0 Vertical - Original Hole, 9/15/2015 1:25:20 PM

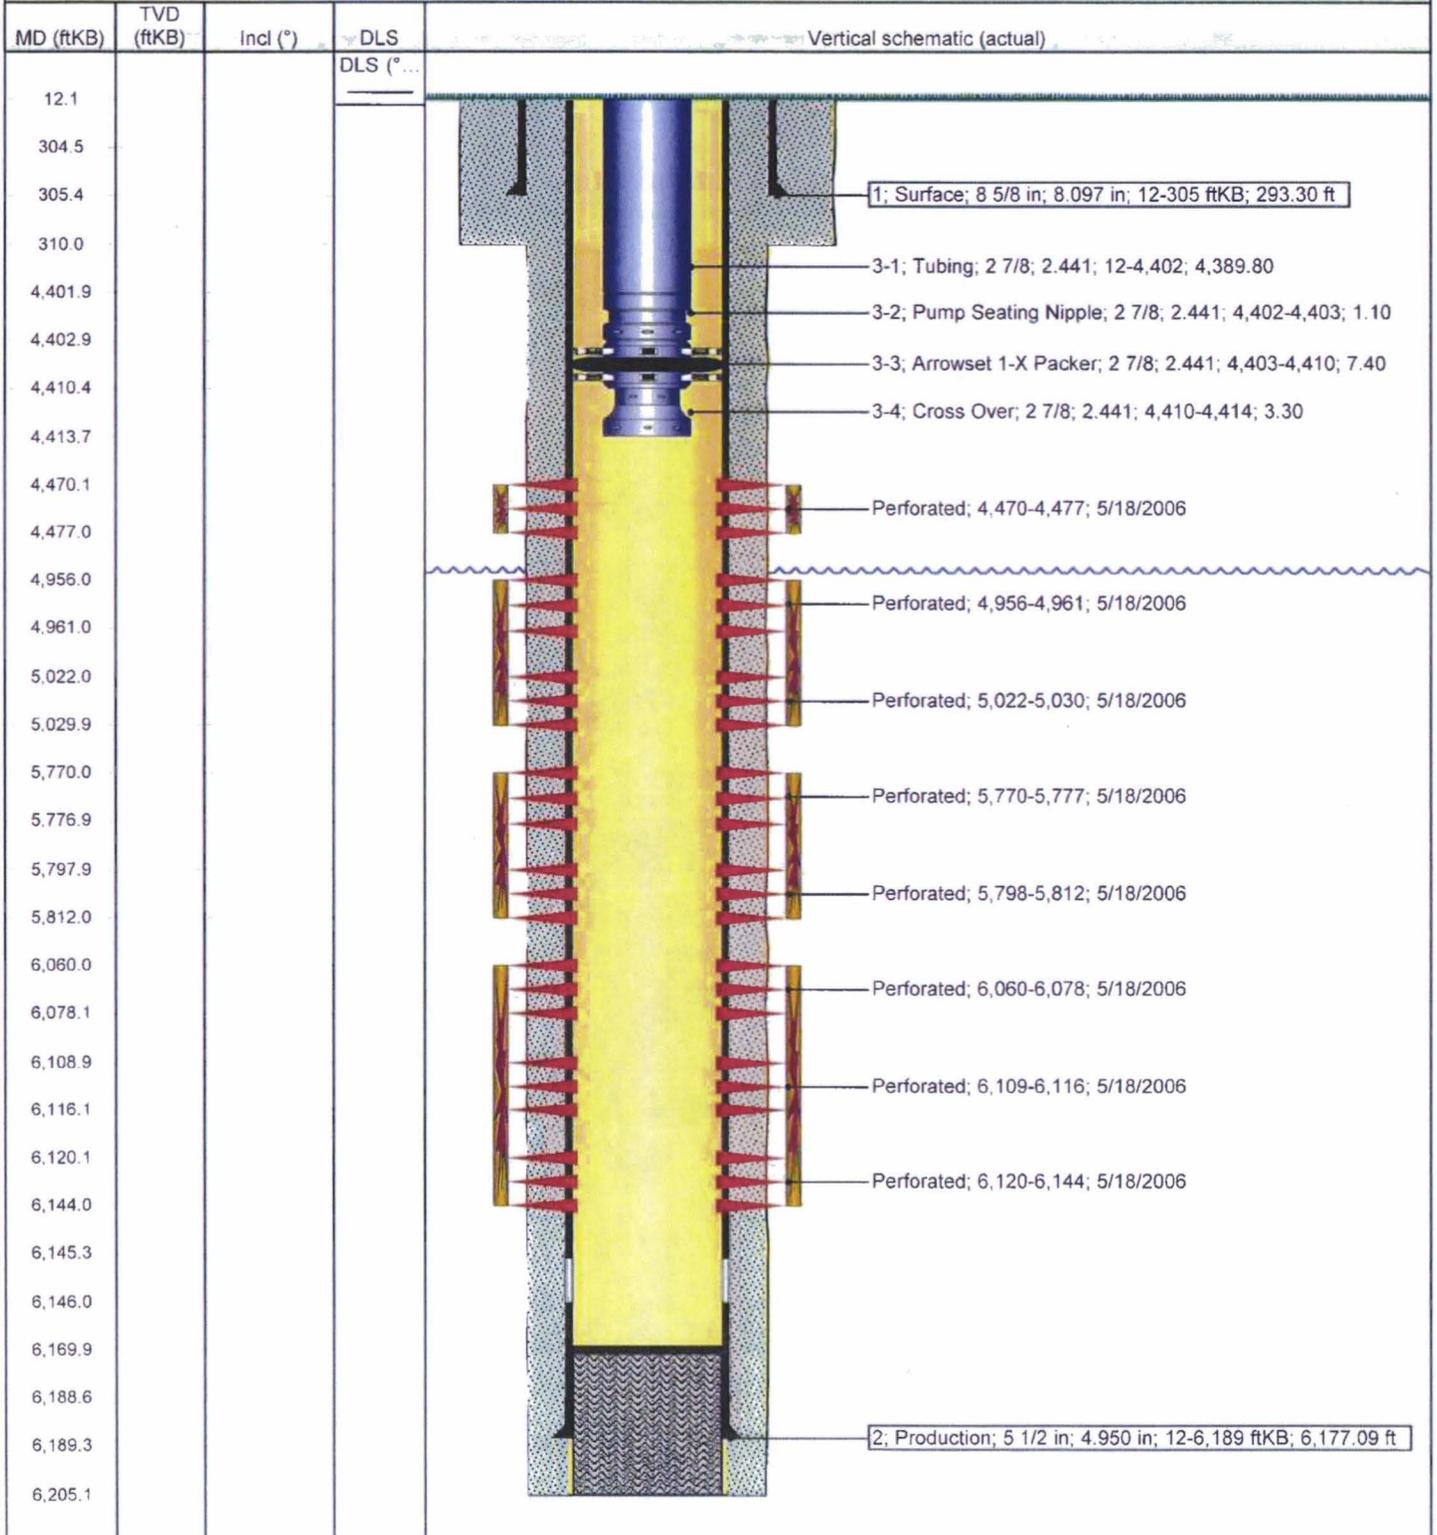

NEWFIELD



Newfield Wellbore Diagram Data Federal 1-33-8-18

Surface Legal Location 33-8S-18E		API/UWI 43047360360000		Lease	
County Uintah		State/Province Utah		Basin	
Well Start Date 4/4/2006		Spud Date		Final Rig Release Date	
Original KB Elevation (ft) 4,881		Ground Elevation (ft) 4,869		Total Depth (ftKB) 6,205.0	
				Total Depth All (TVD) (ftKB)	
				PBTD (All) (ftKB) Original Hole - 6,170.0	

Casing Strings

Csg Des	Run Date	OD (in)	ID (in)	Wt/Len (lb/ft)	Grade	Set Depth (ftKB)
Surface	4/4/2006	8 5/8	8.097	24.00	J-55	305
Production	4/25/2006	5 1/2	4.950	15.50	J-55	6,189

Cement

String: Surface, 305ftKB 4/10/2006

Cementing Company		Top Depth (ftKB) 12.0	Bottom Depth (ftKB) 310.0	Full Return?	Vol Cement Ret (bbl)
Fluid Description 2% CaCL2 + 1/4#/sk Cello-Flake mixed		Fluid Type Lead	Amount (sacks) 160	Class G	Estimated Top (ftKB) 12.0

String: Production, 6,189ftKB 4/25/2006

Cementing Company		Top Depth (ftKB) 12.0	Bottom Depth (ftKB) 6,205.0	Full Return?	Vol Cement Ret (bbl)
Fluid Description		Fluid Type Lead	Amount (sacks) 375	Class Premlite II	Estimated Top (ftKB) 12.0
Fluid Description		Fluid Type Tail	Amount (sacks) 475	Class 50/50 poz	Estimated Top (ftKB) 3,000.0

Tubing Strings

Tubing Description		Run Date			Set Depth (ftKB)			
Tubing		4/22/2009			4,413.6			
Item Des	Jts	OD (in)	ID (in)	Wt (lb/ft)	Grade	Len (ft)	Top (ftKB)	Btm (ftKB)
Tubing	139	2 7/8	2.441	6.50	J-55	4,389.80	12.0	4,401.8
Pump Sealing Nipple	1	2 7/8	2.441			1.10	4,401.8	4,402.9
Arrowset 1-X Packer	1	2 7/8	2.441			7.40	4,402.9	4,410.3
Cross Over	1	2 7/8	2.441			3.30	4,410.3	4,413.6

Rod Strings

Rod Description		Run Date			Set Depth (ftKB)		
Item Des	Jts	OD (in)	Wt (lb/ft)	Grade	Len (ft)	Top (ftKB)	Btm (ftKB)

Perforation Intervals

Stage#	Zone	Top (ftKB)	Btm (ftKB)	Shot Dens (shots/ft)	Phasing (°)	Nom Hole Dia (in)	Date
4	GB6, Original Hole	4,470	4,477	4			5/18/2006
3	D1 & D2, Original Hole	4,956	4,961	4			5/18/2006
3	D1 & D2, Original Hole	5,022	5,030	4			5/18/2006
2	CP2, Original Hole	5,770	5,777	4			5/18/2006
2	CP2, Original Hole	5,798	5,812	4			5/18/2006
1	BSLS, Original Hole	6,060	6,078	4			5/18/2006
1	BSLS, Original Hole	6,109	6,116	4			5/18/2006
1	BSLS, Original Hole	6,120	6,144	4			5/18/2006

Stimulations & Treatments

Stage#	ISIP (psi)	Frac Gradient (psi/ft)	Max Rate (bbl/min)	Max PSI (psi)	Total Clean Vol (bbl)	Total Slurry Vol (bbl)	Vol Recov (bbl)
1	2,060	0.77	25.6	2,436			
4	2,025	0.89	25.6	2,328			
3	1,490	0.73	25.6	2,059			
2	1,500	0.69	25.7	1,673			

Proppant

Stage#	Total Prop Vol Pumped (lb)	Total Add Amount
1		Proppant White Sand 90059 lb
4		Proppant White Sand 32182 lb
3		Proppant White Sand 35010 lb
2		Proppant White Sand 90362 lb
