

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER



FORM APPROVED  
OMB No. 1004-0136  
Expires January 31, 2004

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU-65635
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name N/A
2. Name of Operator Newfield Production Company		7. If Unit or CA Agreement, Name and No. N/A
3a. Address Route #3 Box 3630, Myton UT 84052		8. Lease Name and Well No. Federal 11-19-9-18
3b. Phone No. (include area code) (435) 646-3721		9. API Well No. 43047-393A7
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NE/SW 1976' FSL 1916' FWL 590631 X 40. 014577 At proposed prod. zone 4429705Y -109.938058		10. Field and Pool, or Exploratory Eight Mile Flat
11. Sec., T., R., M., or Blk. and Survey or Area NE/SW Sec. 19, T9S R18E		12. County or Parish Uintah
13. State UT		14. Distance in miles and direction from nearest town or post office* Approximatley 18.8 miles southeast of Myton, Utah
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 1916' f/lse, NA' f/unit	16. No. of Acres in lease 638.08	17. Spacing Unit dedicated to this well 40 Acres
18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1267'	19. Proposed Depth 5565'	20. BLM/BIA Bond No. on file UTB000192
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5179' GL	22. Approximate date work will start* 4th Quarter 2007	23. Estimated duration Approximately seven (7) days from spud to rig release.

24. Attachments

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

1. Well plat certified by a registered surveyor.
2. A Drilling Plan.
3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office).
4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).
5. Operator certification.
6. Such other site specific information and/or plans as may be required by the authorized officer.

25. Signature 	Name (Printed/Typed) Mandie Crozier	Date 6/7/07
Title Regulatory Specialist		
Approved by (Signature) 	Name (Printed/Typed) BRADLEY G. HILL	Date 06-18-07
Title ENVIRONMENTAL MANAGER		

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached.

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

\*(Instructions on reverse)

Federal Approval of this  
Action is Necessary

RECEIVED

JUN 11 2007

DIV. OF OIL, GAS & MINING

*NEWFIELD PRODUCTION COMPANY*



THIS IS TO CERTIFY THAT THE ABOVE PLAT WAS  
PREPARED FROM FIELD NOTES OF ACTUAL SURVEYS  
MADE BY ME OR UNDER MY SUPERVISION AND THAT  
THE SAME ARE TRUE AND CORRECT TO THE BEST OF  
MY KNOWLEDGE AND BELIEF. No. 189377


STACY W.  
STEWART  
REGISTERED LAND SURVEYOR  
REGISTRATION No. 100377  
STATE OF UTAH

180 NORTH VERNAL AVE. - VERNAL, UTAH 84078  
(435) 781-2501

SURVEYED BY: C.M.

DRAWN BY: T.C.J.

SCALE: 1" = 1000'

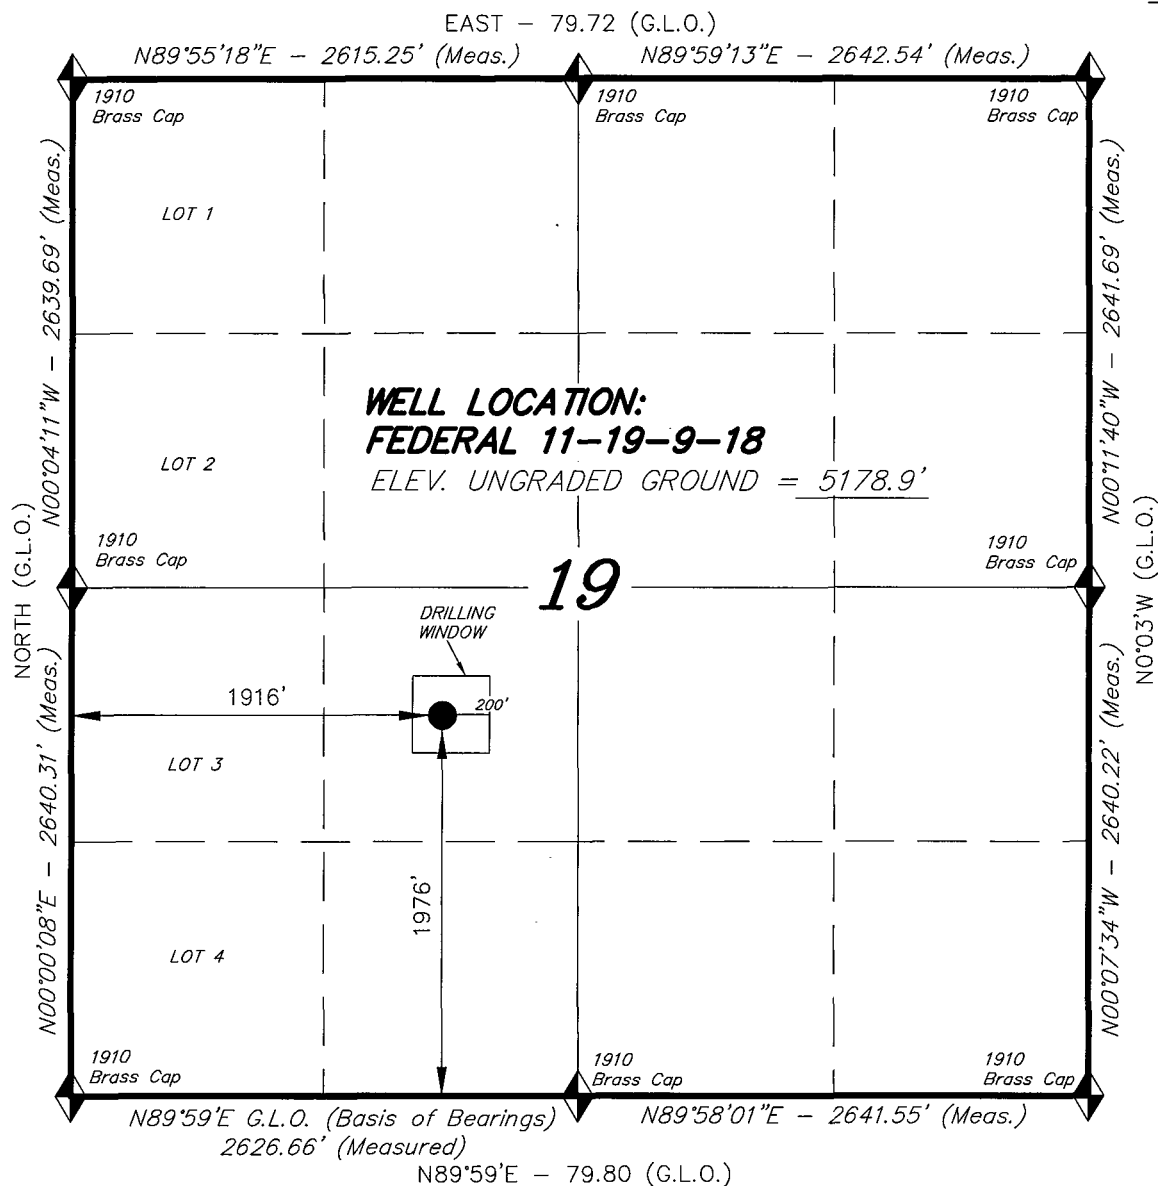

 = SECTION CORNERS LOCATED

BASIS OF ELEV;

U.S.G.S. 7-1/2 min QUAD (PARIETTE DRAW SW)

FEDERAL 11-19-9-18  
(Surface Location) NAD 83  
LATITUDE = 40° 00' 52.50"  
LONGITUDE = 109° 56' 19.47"

NEWFIELD PRODUCTION COMPANY  
FEDERAL #11-19-9-18  
NE/SW SECTION 19, T9S, R18E  
UINTAH COUNTY, UTAH

ONSHORE ORDER NO. 1

DRILLING PROGRAM

1. GEOLOGIC SURFACE FORMATION:

Uinta formation of Upper Eocene Age

2. ESTIMATED TOPS OF IMPORTANT GEOLOGIC MARKERS:

Uinta	0' – 1015'
Green River	1015'
Wasatch	5565'

3. ESTIMATED DEPTHS OF ANTICIPATED WATER, OIL, GAS OR MINERALS:

Green River Formation 1015' – 5565' - Oil

4. PROPOSED CASING PROGRAM

Please refer to the Monument Butte Field Standard Operation Procedure (SOP).

5. MINIMUM SPECIFICATIONS FOR PRESSURE CONTROL:

Please refer to the Monument Butte Field SOP. See Exhibit "C".

6. TYPE AND CHARACTERISTICS OF THE PROPOSED CIRCULATION MUDS:

Please refer to the Monument Butte Field SOP.

7. AUXILIARY SAFETY EQUIPMENT TO BE USED:

Please refer to the Monument Butte Field SOP.

8. TESTING, LOGGING AND CORING PROGRAMS:

Please refer to the Monument Butte Field SOP.

9. ANTICIPATED ABNORMAL PRESSURE OR TEMPERATURE:

The anticipated maximum bottom hole pressure is 1800 psi. It is not anticipated that abnormal temperatures will be encountered.

10. ANTICIPATED STARTING DATE AND DURATION OF THE OPERATIONS:

Please refer to the Monument Butte Field SOP.

**NEWFIELD PRODUCTION COMPANY  
FEDERAL #11-19-9-18  
NE/SW SECTION 19, T9S, R18E  
UINTAH COUNTY, UTAH**

**ONSHORE ORDER NO. 1**

**MULTI-POINT SURFACE USE & OPERATIONS PLAN**

**1. EXISTING ROADS**

See attached Topographic Map "A"

To reach Newfield Production Company well location site Federal #11-19-9-18 located in the NE 1/4 SW 1/4 Section 19, T9S, R18E, Uintah County, Utah:

Proceed southwesterly out of Myton, Utah along Highway 40 - 1.6 miles  $\pm$  to the junction of this highway and UT State Hwy 53; proceed southeasterly along Hwy 53 - 15.3 miles  $\pm$  to it's junction with an existing dirt road to the southeast; proceed southeasterly - 1.8 miles  $\pm$  to it's junction with the beginning of the proposed access road to the southwest; proceed southwesterly along the proposed access road - 390'  $\pm$ ; continue in a southeasterly direction - 200'  $\pm$  to the proposed well location.

**2. PLANNED ACCESS ROAD**

See Topographic Map "B" for the location of the proposed access road.

**3. LOCATION OF EXISTING WELLS**

Refer to Exhibit "B".

**4. LOCATION OF EXISTING AND/OR PROPOSED FACILITIES**

All permanent surface equipment will be painted Carlsbad Canyon.  
Please refer to the Monument Butte Field Standard Operating Procedure (SOP).

**5. LOCATION AND TYPE OF WATER SUPPLY**

Newfield Production will transport water by truck for drilling purposes from the following water sources:

Johnson Water District  
Water Right: 43-10136

Neil Moon Pond  
Water Right: 43-11787

Maurice Harvey Pond  
Water Right: 47-1358

Newfield Collector Well  
Water Right: 41-3530 (A30414DV, contracted with the Duchesne County Conservancy District).

Please refer to the Monument Butte Field SOP. See Exhibit "A".

6. **SOURCE OF CONSTRUCTION MATERIALS**

Please refer to the Monument Butte Field SOP.

7. **METHODS FOR HANDLING WASTE DISPOSAL**

Please refer to the Monument Butte Field SOP.

8. **ANCILLARY FACILITIES**

Please refer to the Monument Butte Field SOP.

9. **WELL SITE LAYOUT**

See attached Location Layout Diagram.

10. **PLANS FOR RESTORATION OF SURFACE**

Please refer to the Monument Butte Field SOP.

11. **SURFACE OWNERSHIP** - Bureau Of Land Management (Proposed location and access roads leading to).

12. **OTHER ADDITIONAL INFORMATION**

The Archaeological Resource Survey and Paleontological Resource Survey for this area are attached. MOAC Report #03-82, 01/12/04. Paleontological Resource Survey prepared by, Wade E. Miller, 07/28/03. See attached report cover pages, Exhibit "D".

Newfield Production Company requests 590' of disturbed area be granted in Lease UTU-65635 to allow for construction of the planned access road. **Refer to Topographic Map "B"**. For the planned access road a temporary width of 60' will be needed for construction purposes with a permanent width of 30' and a running surface of 18'. The construction phase of the planned access road will last approximately (5) days. The planned access road will be an 18' crown road (9' either side of the centerline) with drainage ditches along either side of the proposed road whether it is deemed necessary in order to handle any run-off from normal meteorological conditions that are prevalent to this area. The maximum grade will be less than 8%. There will be no culverts required along this access road. There will be barrow ditches and turnouts as needed along this road. There are no fences encountered along this proposed road. There will be no new gates or cattle guards required. All construction material for this access road will be borrowed material accumulated during construction of the access road.

Newfield Production Company requests a 90' ROW be granted in Lease UTU-79013 and 4,070' of disturbed area be granted in Lease UTU-65635 to allow for construction of the proposed surface gas lines. It is proposed that the ROW and disturbed area will temporarily be 50' wide to allow for construction of a 6" gas gathering line, and a 3" poly fuel gas line and 30' wide upon completion of the proposed gas lines. Both lines will tie in to the existing pipeline infrastructure. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

Newfield Production Company requests a 90' ROW be granted in Lease UTU-79013 and 4,070' of disturbed area be granted in Lease UTU-65635 to allow for construction of the proposed water lines. It is proposed that the ROW and disturbed area will temporarily be 50' wide to allow for construction of a buried 3" steel water injection line and a buried 3" poly water return line and 30' wide upon completion of the proposed water lines. **Refer to Topographic Map "C."** For a ROW plan of development, please refer to the Monument Butte Field SOP.

### **Water Disposal**

Immediately upon first production, all produced water will be confined to a steel storage tank. If the production water meets quality guidelines, it is transported to the Ashley, Monument Butte, Jonah, and Beluga water injection facilities by company or contract trucks. Subsequently, the produced water is injected into approved Class II wells to enhance Newfield's secondary recovery project.

Water not meeting quality criteria, is disposed at Newfield's Pariette #4 disposal well (Sec. 7, T9S R19E) or at State of Utah approved surface disposal facilities.

### **Threatened, Endangered, And Other Sensitive Species**

**Mountain Plover:** If new construction or surface disturbing activities are scheduled to occur between May 1 and June 15, detailed surveys of the area within 0.5 mile of the proposed location and within 300 feet of proposed access routes must be conducted to detect the presence of mountain plovers. All surveys must be conducted in accordance with the survey protocols outlined in the most recent USFWS Survey Protocol. Surveys must be completed prior to initiating new construction or surface disturbing activities. No new construction or surface disturbing activities will be allowed between March 15 and August 15 within a 0.5 mile radius of any documented mountain plover nest site.

**Burrowing Owl:** Due to the proximity of the location to active prairie dog towns, there is the potential to encounter nesting burrowing owls between April 1 and August 15. If new construction or surface disturbing activities are scheduled between April 1 and August 15, pre-construction surveys will be conducted to detect the presence of nesting burrowing owls within 0.5 mile of any new construction or surface disturbing activity (see Vernal BLM Field Office Protocol). No new construction or surface disturbing activities will be allowed between April 1 and August 15 within a 0.5 mile radius of any active burrowing owl nest.

### **Reserve Pit Liner**

A 16 mil liner with felt is required. Please refer to the Monument Butte Field SOP.

### **Location and Reserve Pit Reclamation**

Please refer to the Monument Butte Field SOP.

The following seed mixture will be used on the topsoil stockpile, to the recontoured surface of the reserve pit, and for final reclamation: (All poundages are in pure live seed)

Shadscale	<i>Atriplex Confertifolia</i>	6 lbs/acre
Galletta Grass	<i>Hilaria Jamesii</i>	6 lbs/acre

### **Details of the On-Site Inspection**

The proposed Federal #11-19-9-18 was on-sited on 5/11/07. The following were present; Dave Allred (Newfield Production), Chuck MacDonald (Bureau of Land Management), and Brandon McDonald (Bureau of Land Management). Weather conditions were clear and ground cover was 100% open.

## **13. LESSEE'S OR OPERATORS REPRESENTATIVE AND CERTIFICATION**

### **Representative**

Name: Dave Allred  
Address: Route #3 Box 3630  
Myton, UT 84052  
Telephone: (435) 646-3721


### **Certification**

Please be advised that NEWFIELD PRODUCTION COMPANY is considered to be the operator of well #11-19-9-18 NE/SW Section 19, Township 9S, Range 18E: Lease UTU-65635 Uintah County, Utah: and is responsible under the terms and conditions of the lease for the operations conducted upon the leased lands. Bond coverage is provided by US Specialty Insurance #B001832.

I hereby certify that the proposed drill site and access route have been inspected, and I am familiar with the conditions which currently exist; that the statements made in this plan are true and correct to the best of my knowledge; and that the work associated with the operations proposed here will be performed by Newfield Production Company and its contractors and subcontractors in conformity with this plan and the terms and conditions under which it is approved. This statement is subject to the provisions of 18 U.S.C. 1001 for the filing of a false statement.

6/7/07

Date



Mandie Crozier



Regulatory Specialist

Newfield Production Company

# NEWFIELD PRODUCTION COMPANY

FEDERAL 11-19-9-18

Section 19, T9S, R18E, S.L.B.&M.

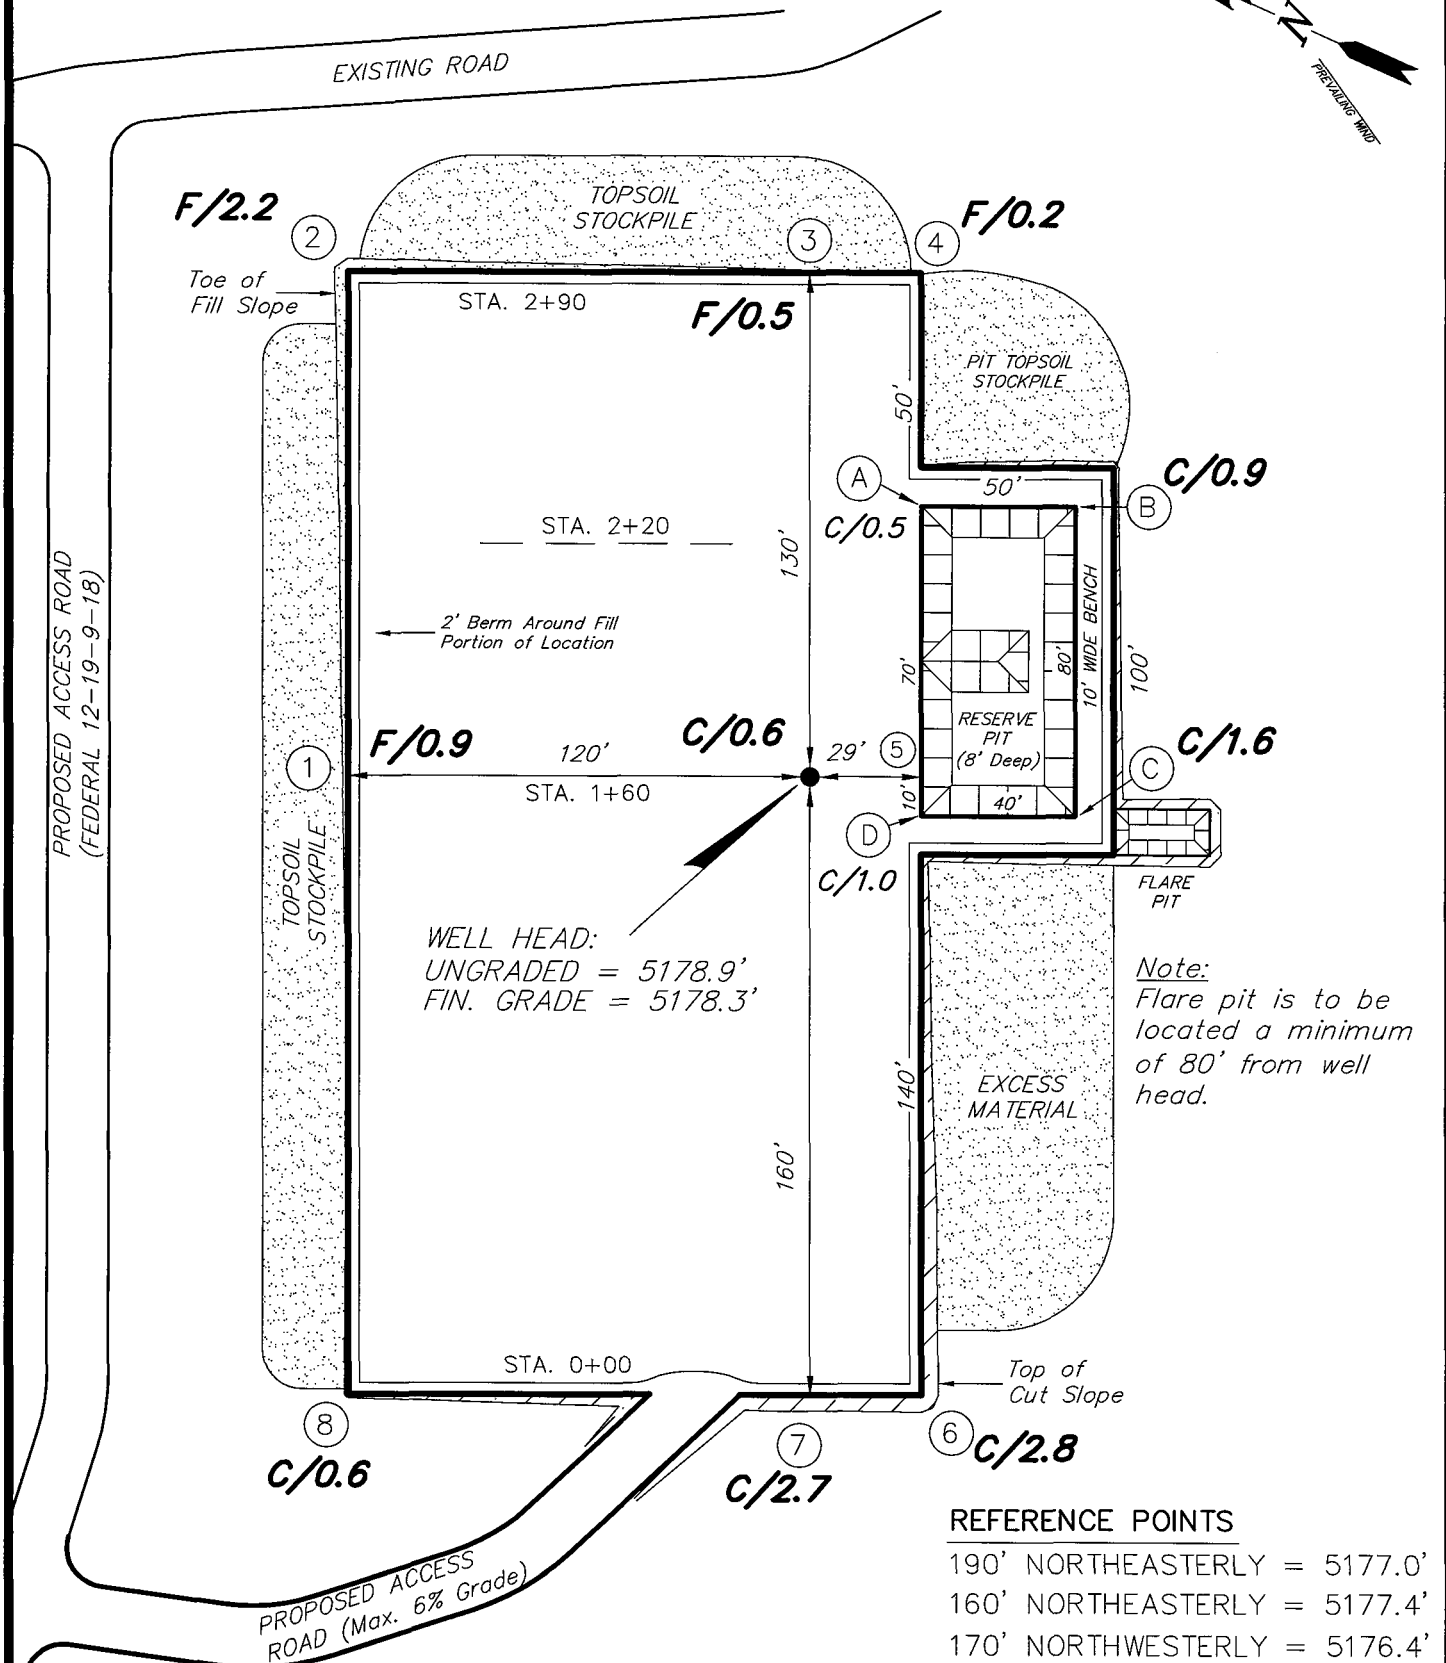

SURVEYED BY: C.M.

SCALE: 1" = 50'

DRAWN BY: T.C.J.

DATE: 02-28-07





**Tri State**  
Land Surveying, Inc.

(435) 781-2501

180 NORTH VERNAL AVE. VERNAL, UTAH 84078

# NEWFIELD PRODUCTION COMPANY

## CROSS SECTIONS FEDERAL 11-19-9-18

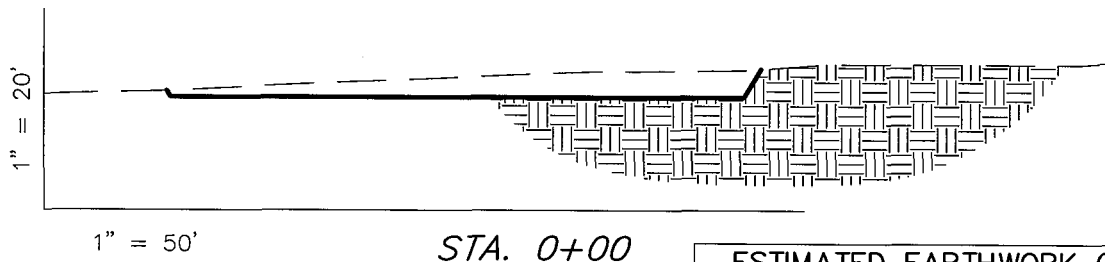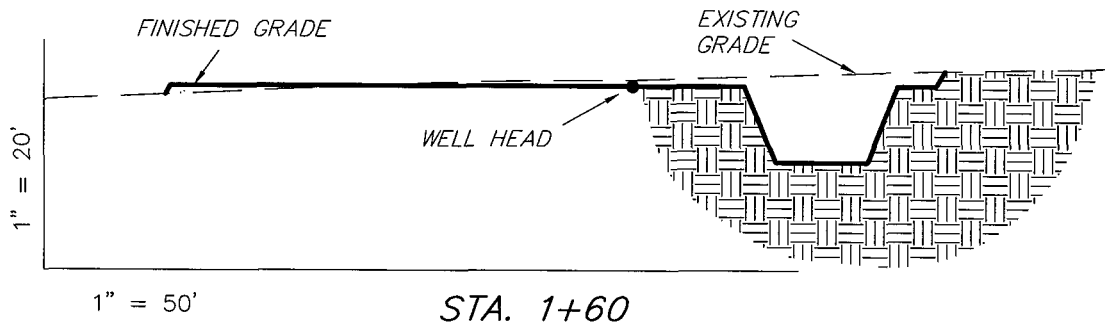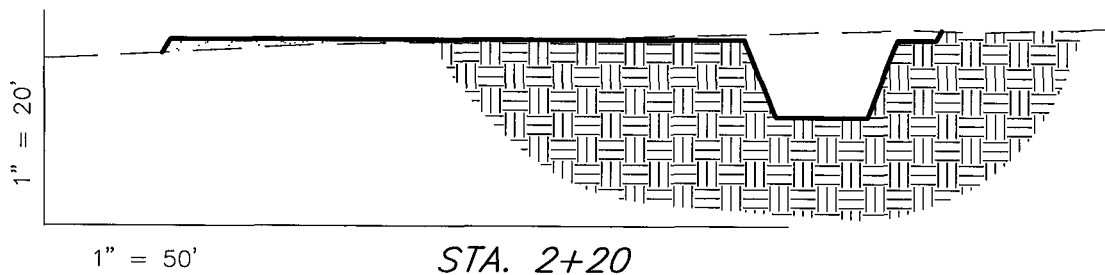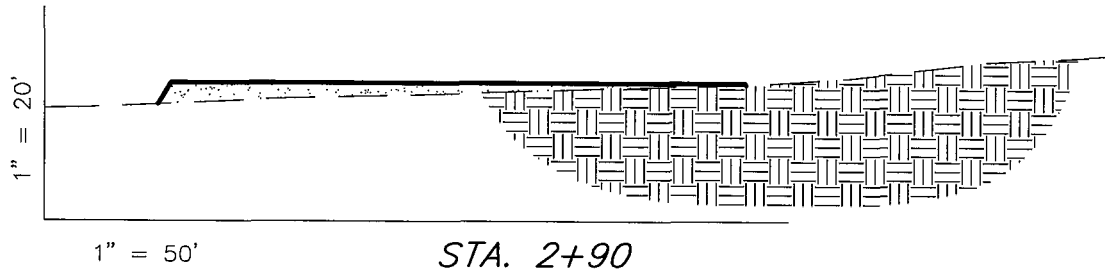

NOTE:  
UNLESS OTHERWISE NOTED  
ALL CUT/FILL SLOPES ARE  
AT 1.5:1

### ESTIMATED EARTHWORK QUANTITIES (No Shrink or swell adjustments have been used) (Expressed in Cubic Yards)

ITEM	CUT	FILL	6" TOPSOIL	EXCESS
PAD	760	760	Topsoil is not included in Pad Cut	0
PIT	640	0		640
TOTALS	1,400	760	940	640

SURVEYED BY: C.M.

SCALE: 1" = 50'

DRAWN BY: T.C.J.

DATE: 02-28-07


**Tri State**  
Land Surveying, Inc.  
180 NORTH VERNAL AVE. VERNAL, UTAH 84078

(435) 781-2501

# NEWFIELD PRODUCTION COMPANY

## TYPICAL RIG LAYOUT

### FEDERAL 11-19-9-18

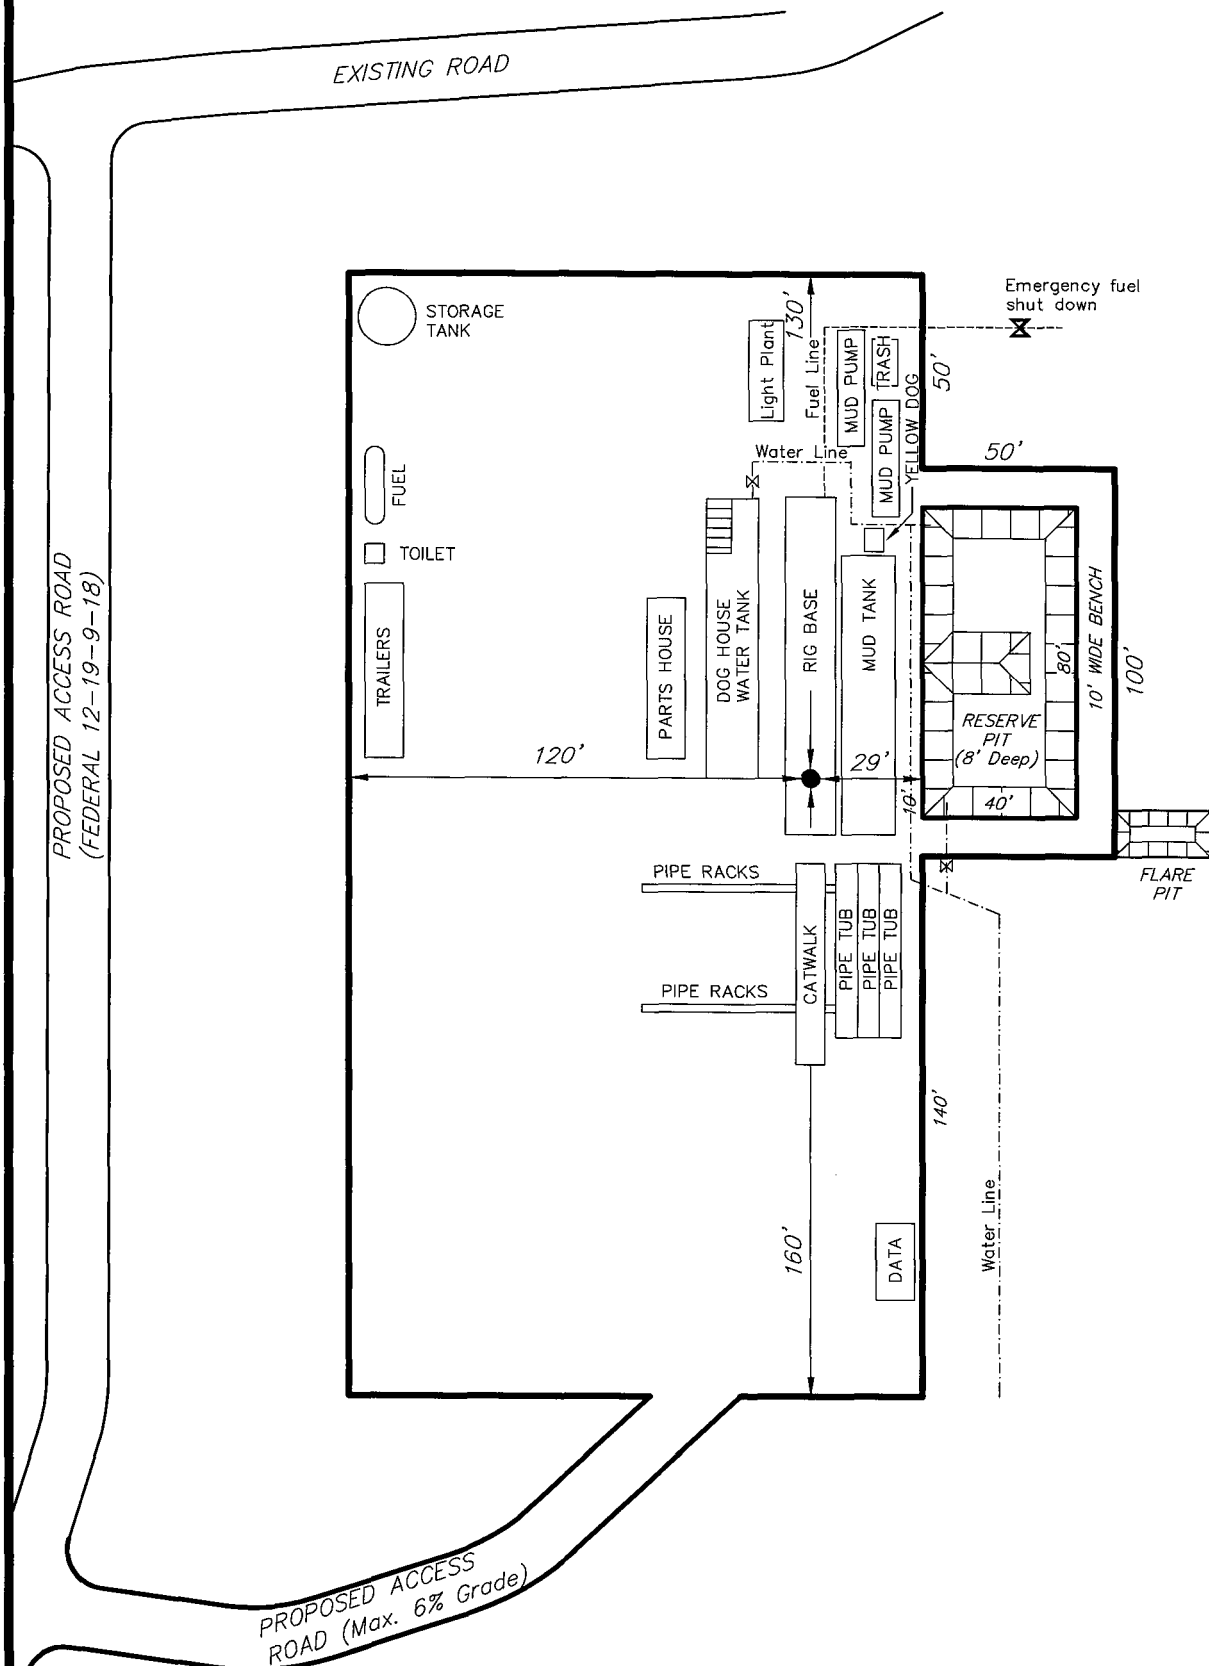

SURVEYED BY: C.M.

SCALE: 1" = 50'

DRAWN BY: T.C.J.

DATE: 02-28-07

**Tri State** (435) 781-2501  
**Land Surveying, Inc.**  
 180 NORTH VERNAL AVE. VERNAL, UTAH 84078


# Newfield Production Company Proposed Site Facility Diagram

Federal 11-19-9-18

NE/SW Sec. 19, T9S, R18E

Uintah County, Utah

UTU-65635

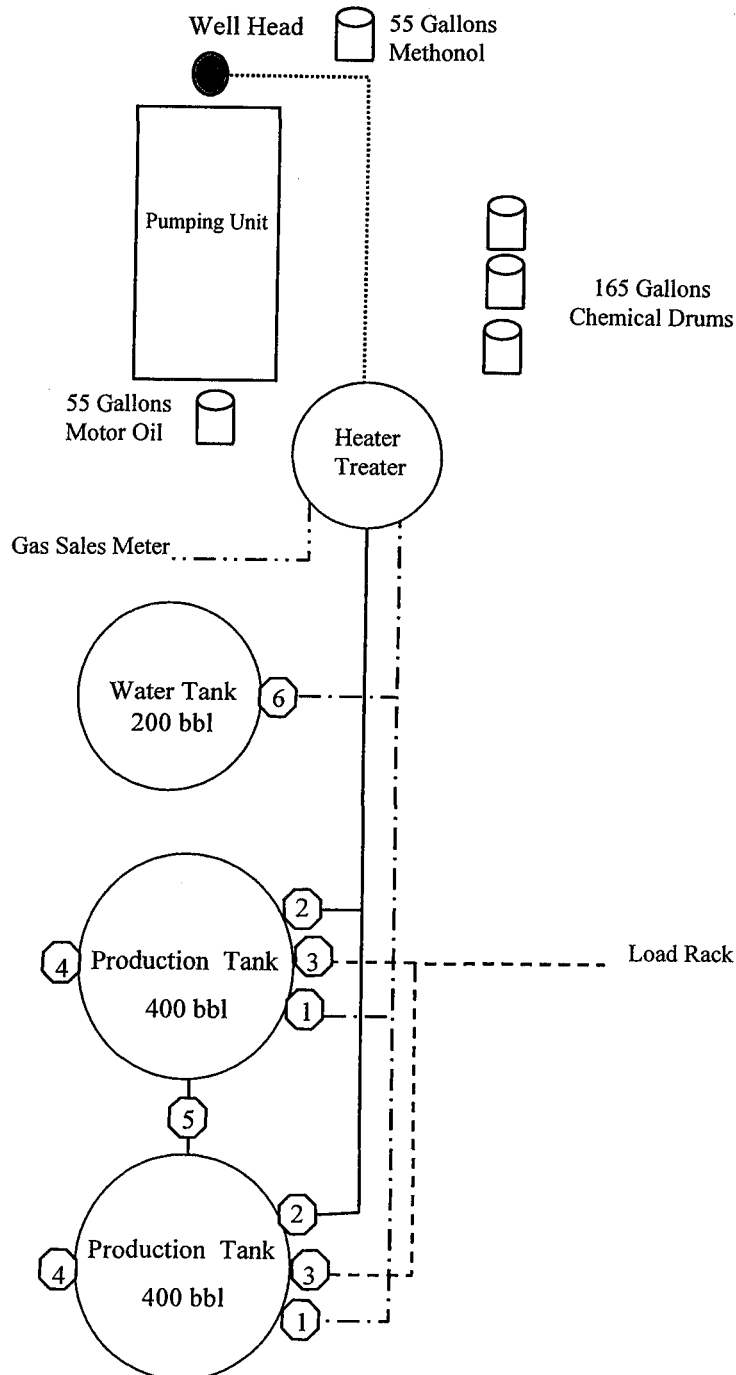

## Legend

Emulsion Line	.....
Load Rack	-----
Water Line	-.-.-.-.
Gas Sales	.....
Oil Line	————

## Production Phase:


- 1) Valves 1, 3, and 4 sealed closed
- 2) Valves 2, 5, and 6 sealed open


## Sales Phase:

- 1) Valves 1, 2, 4, 5, and 6 sealed closed
- 2) Valve 3 open

## Draining Phase:

- 1) Valves 1 and 6 open



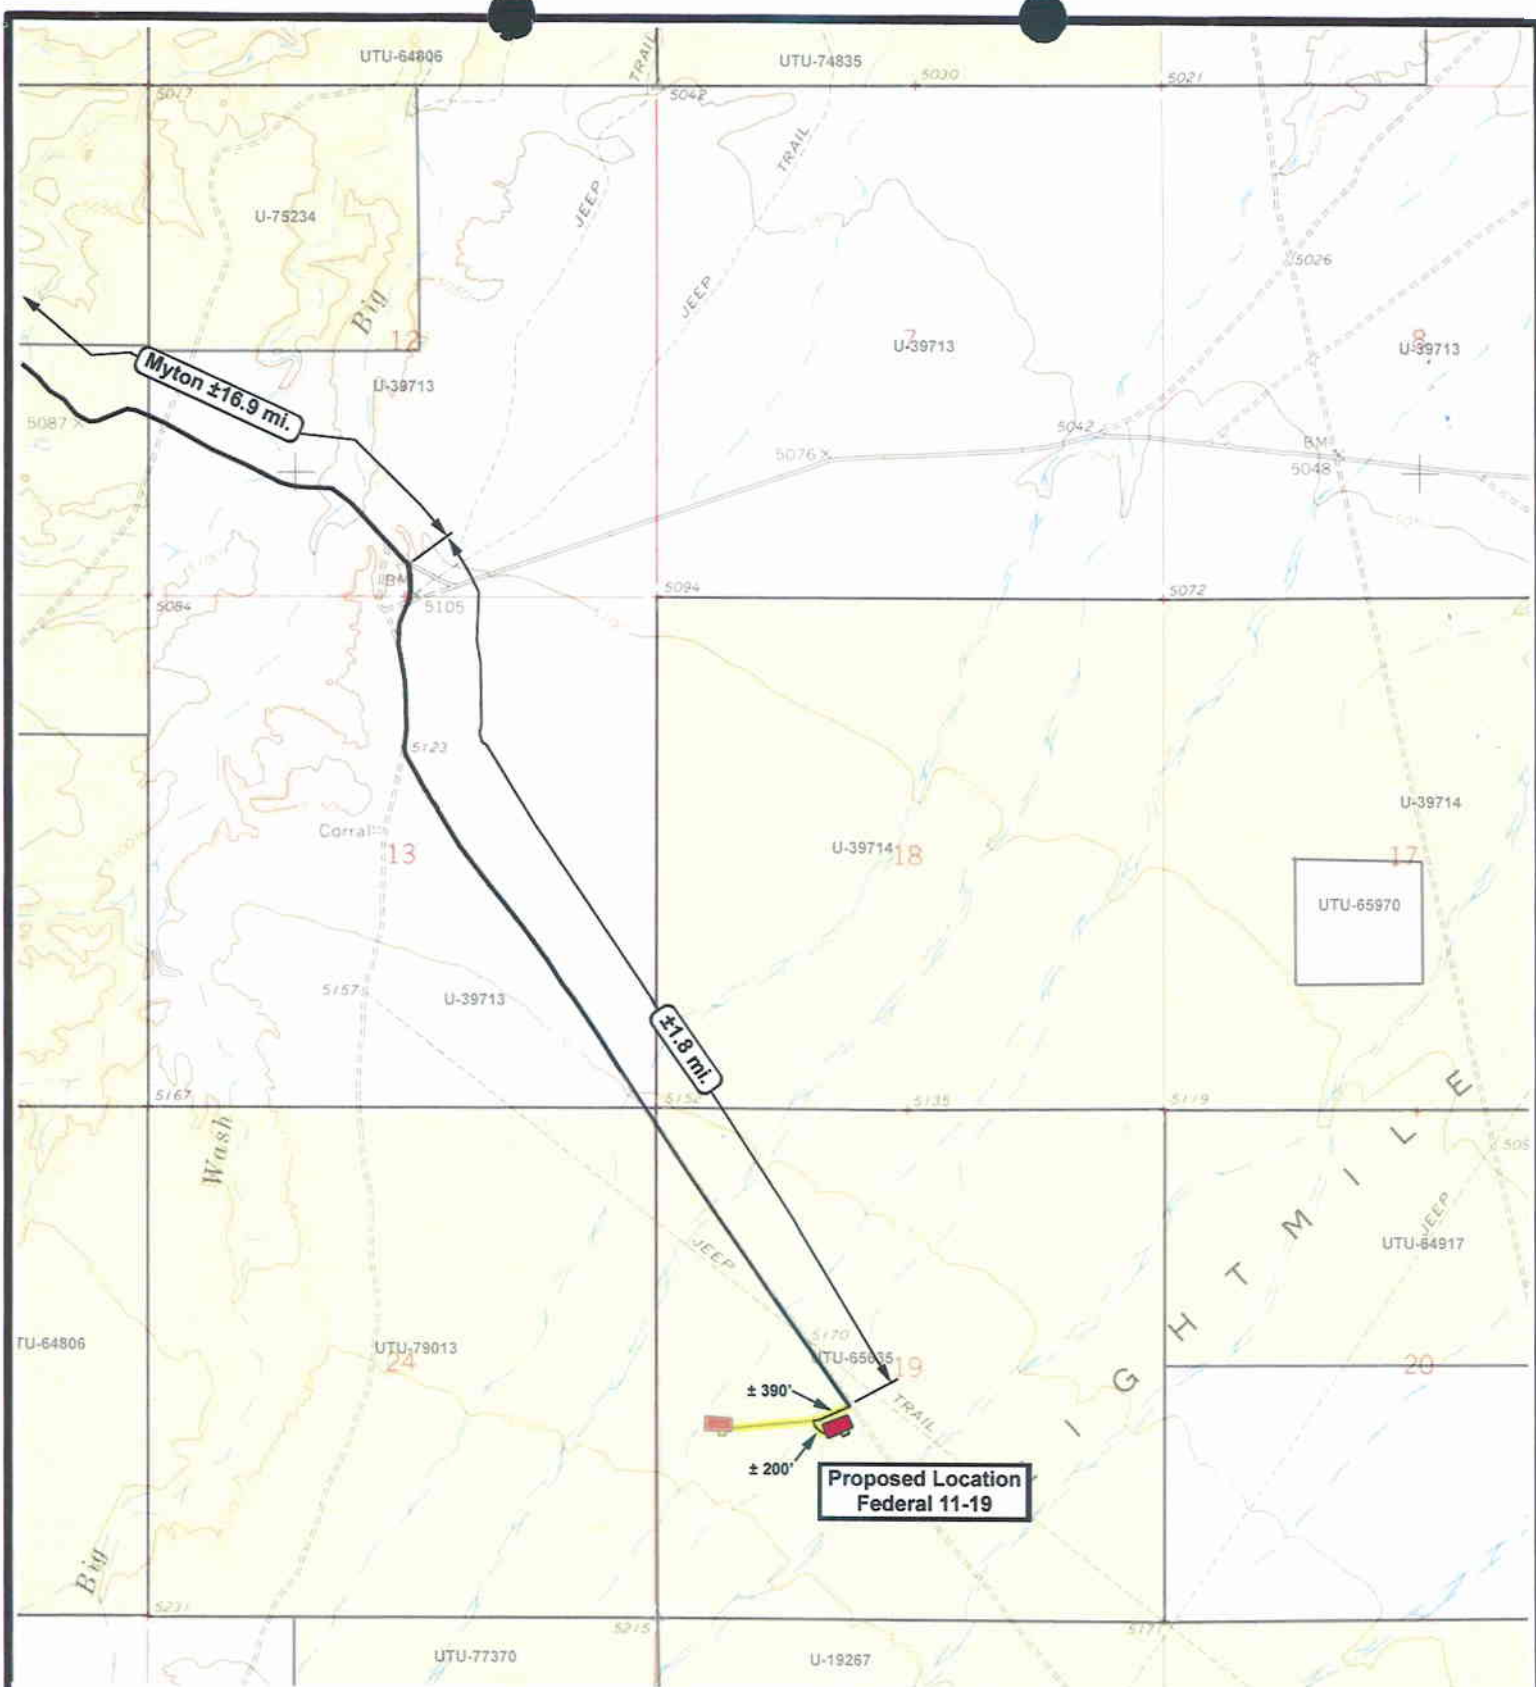

**NEWFIELD**  
Exploration Company

**Federal 11-19-9-18**  
**SEC. 19, T9S, R18E, S.L.B.&M.**



**Tri-State**  
Land Surveying Inc.  
(435) 781-2501

180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'

DRAWN BY: mw


DATE: 03-05-2007


**Legend**

Existing Road  
 Proposed Access

**TOPOGRAPHIC MAP**

**"B"**

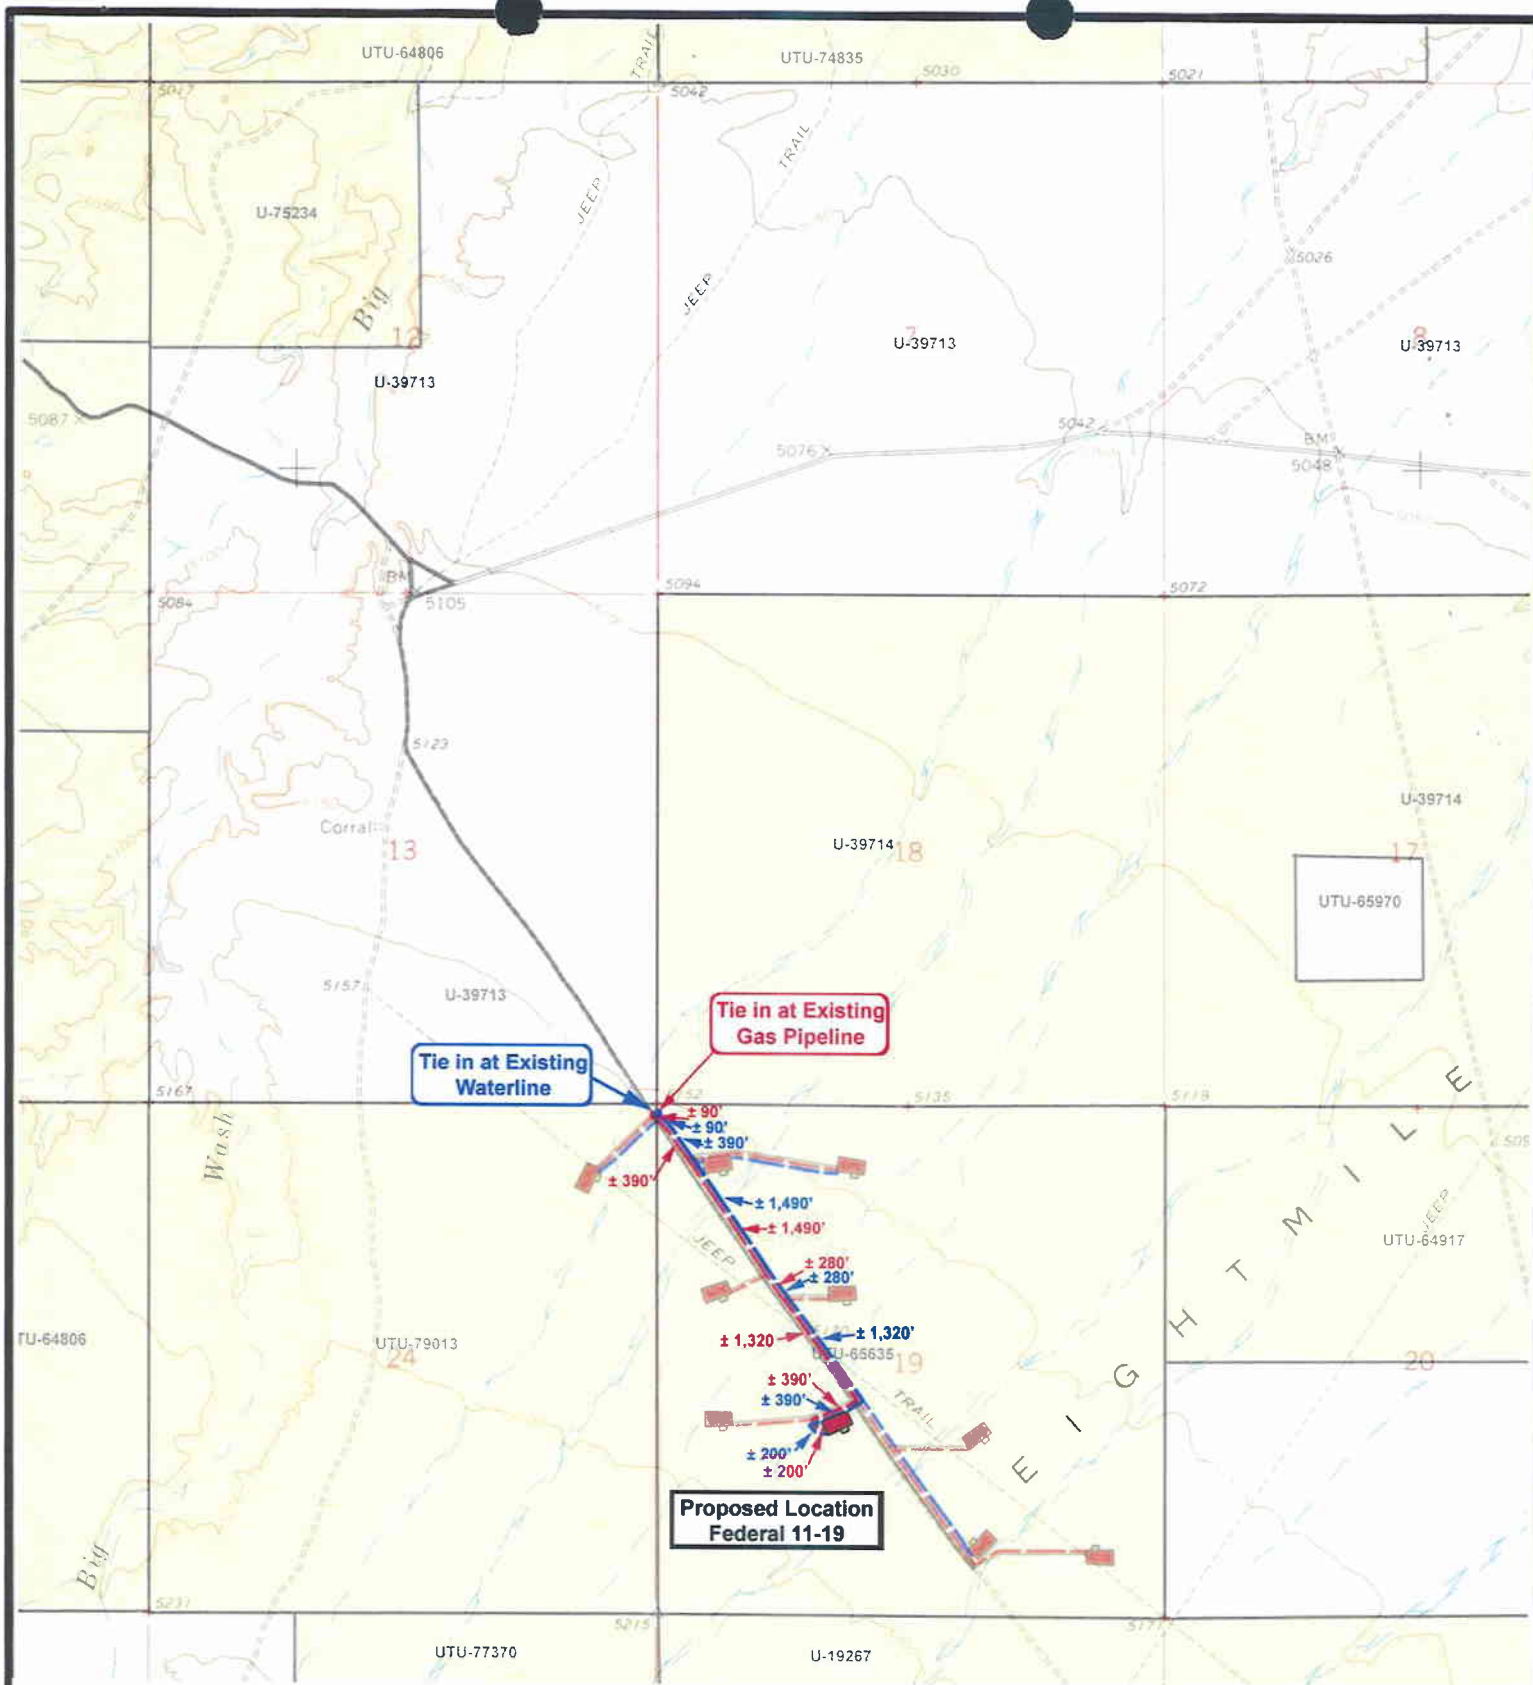



**NEWFIELD**  
Exploration Company

**Federal 11-19-9-18**  
**SEC. 19, T9S, R18E, S.L.B.&M.**





**Tri-State**  
*Land Surveying Inc.*  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'

DRAWN BY: mw


DATE: 03-05-2007


**Legend**

	Roads
	Proposed Gas Line
	Proposed Water Line


**TOPOGRAPHIC MAP**

**"C"**

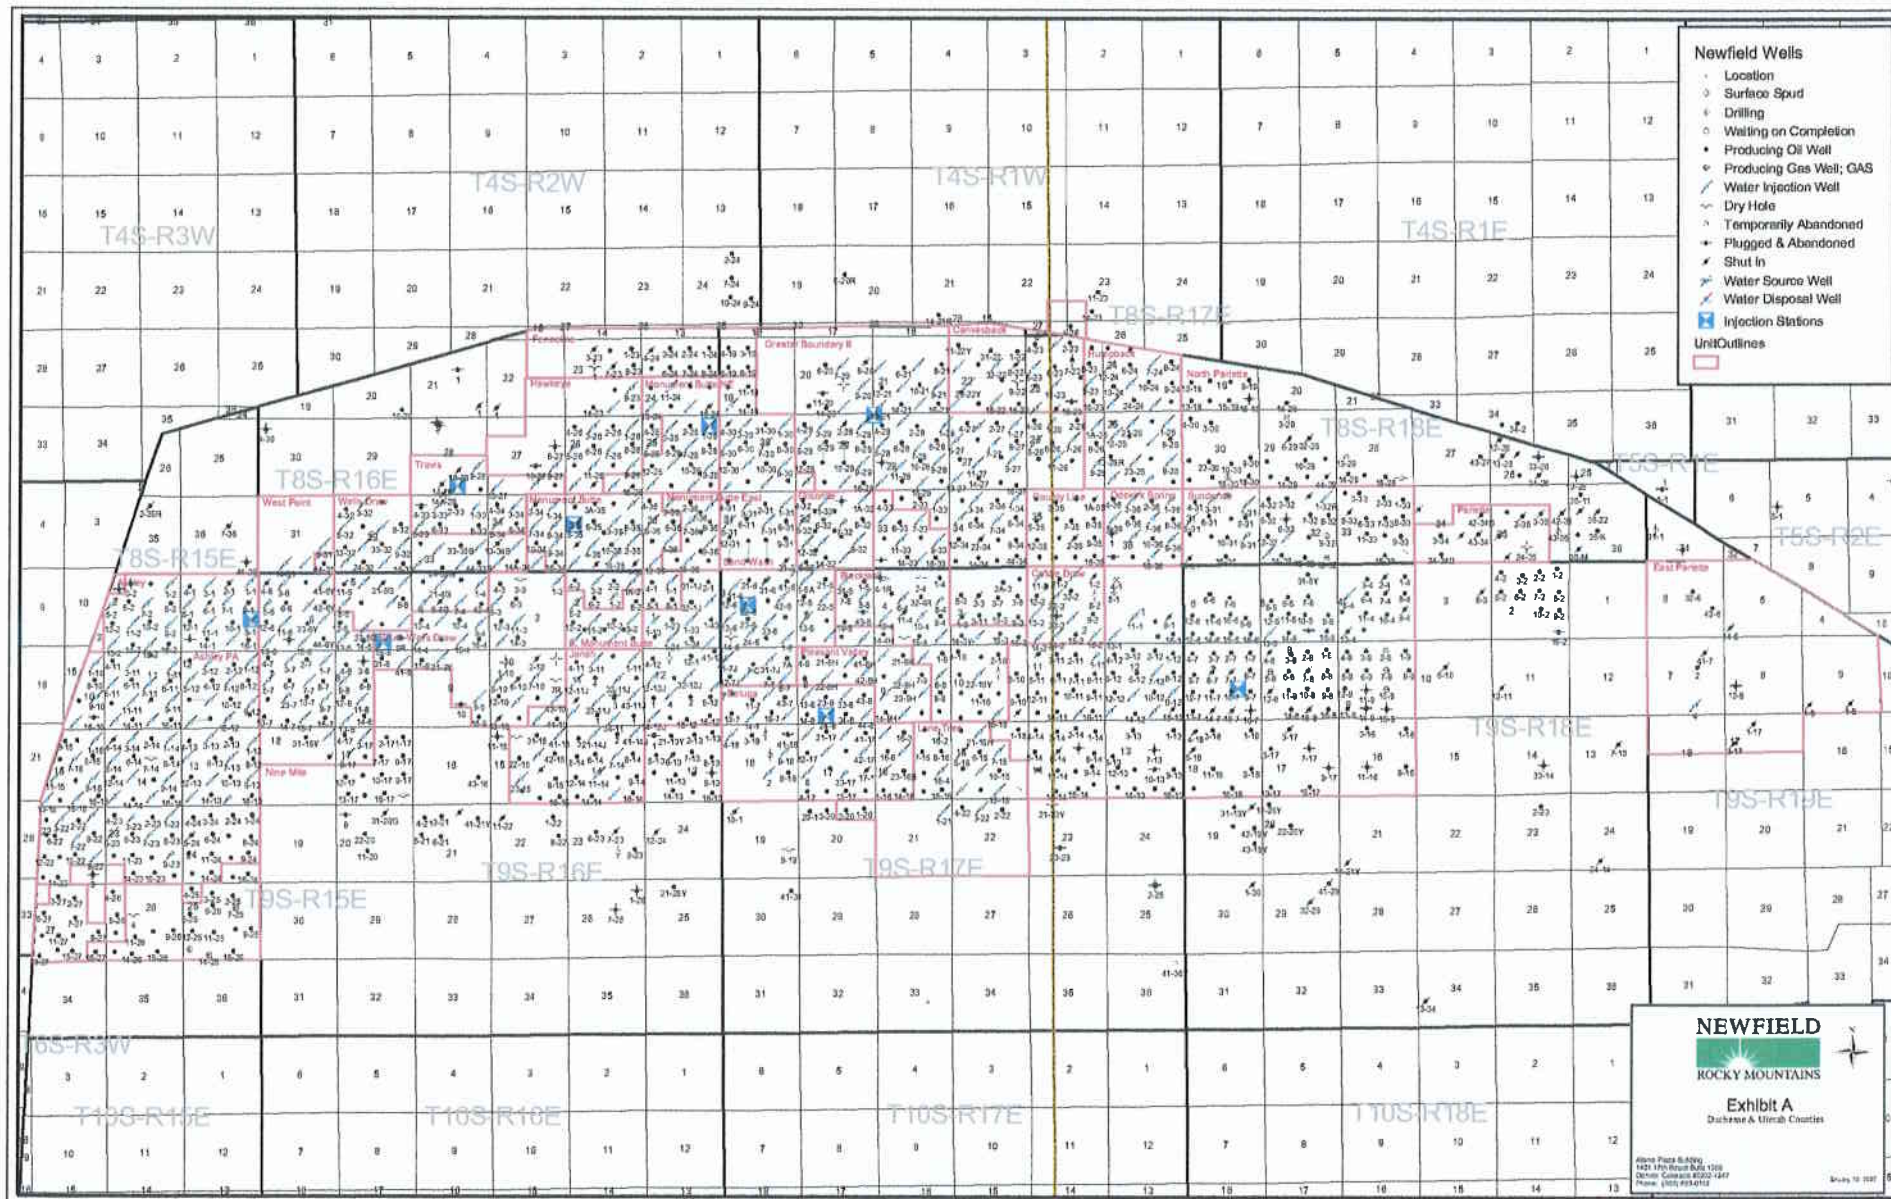

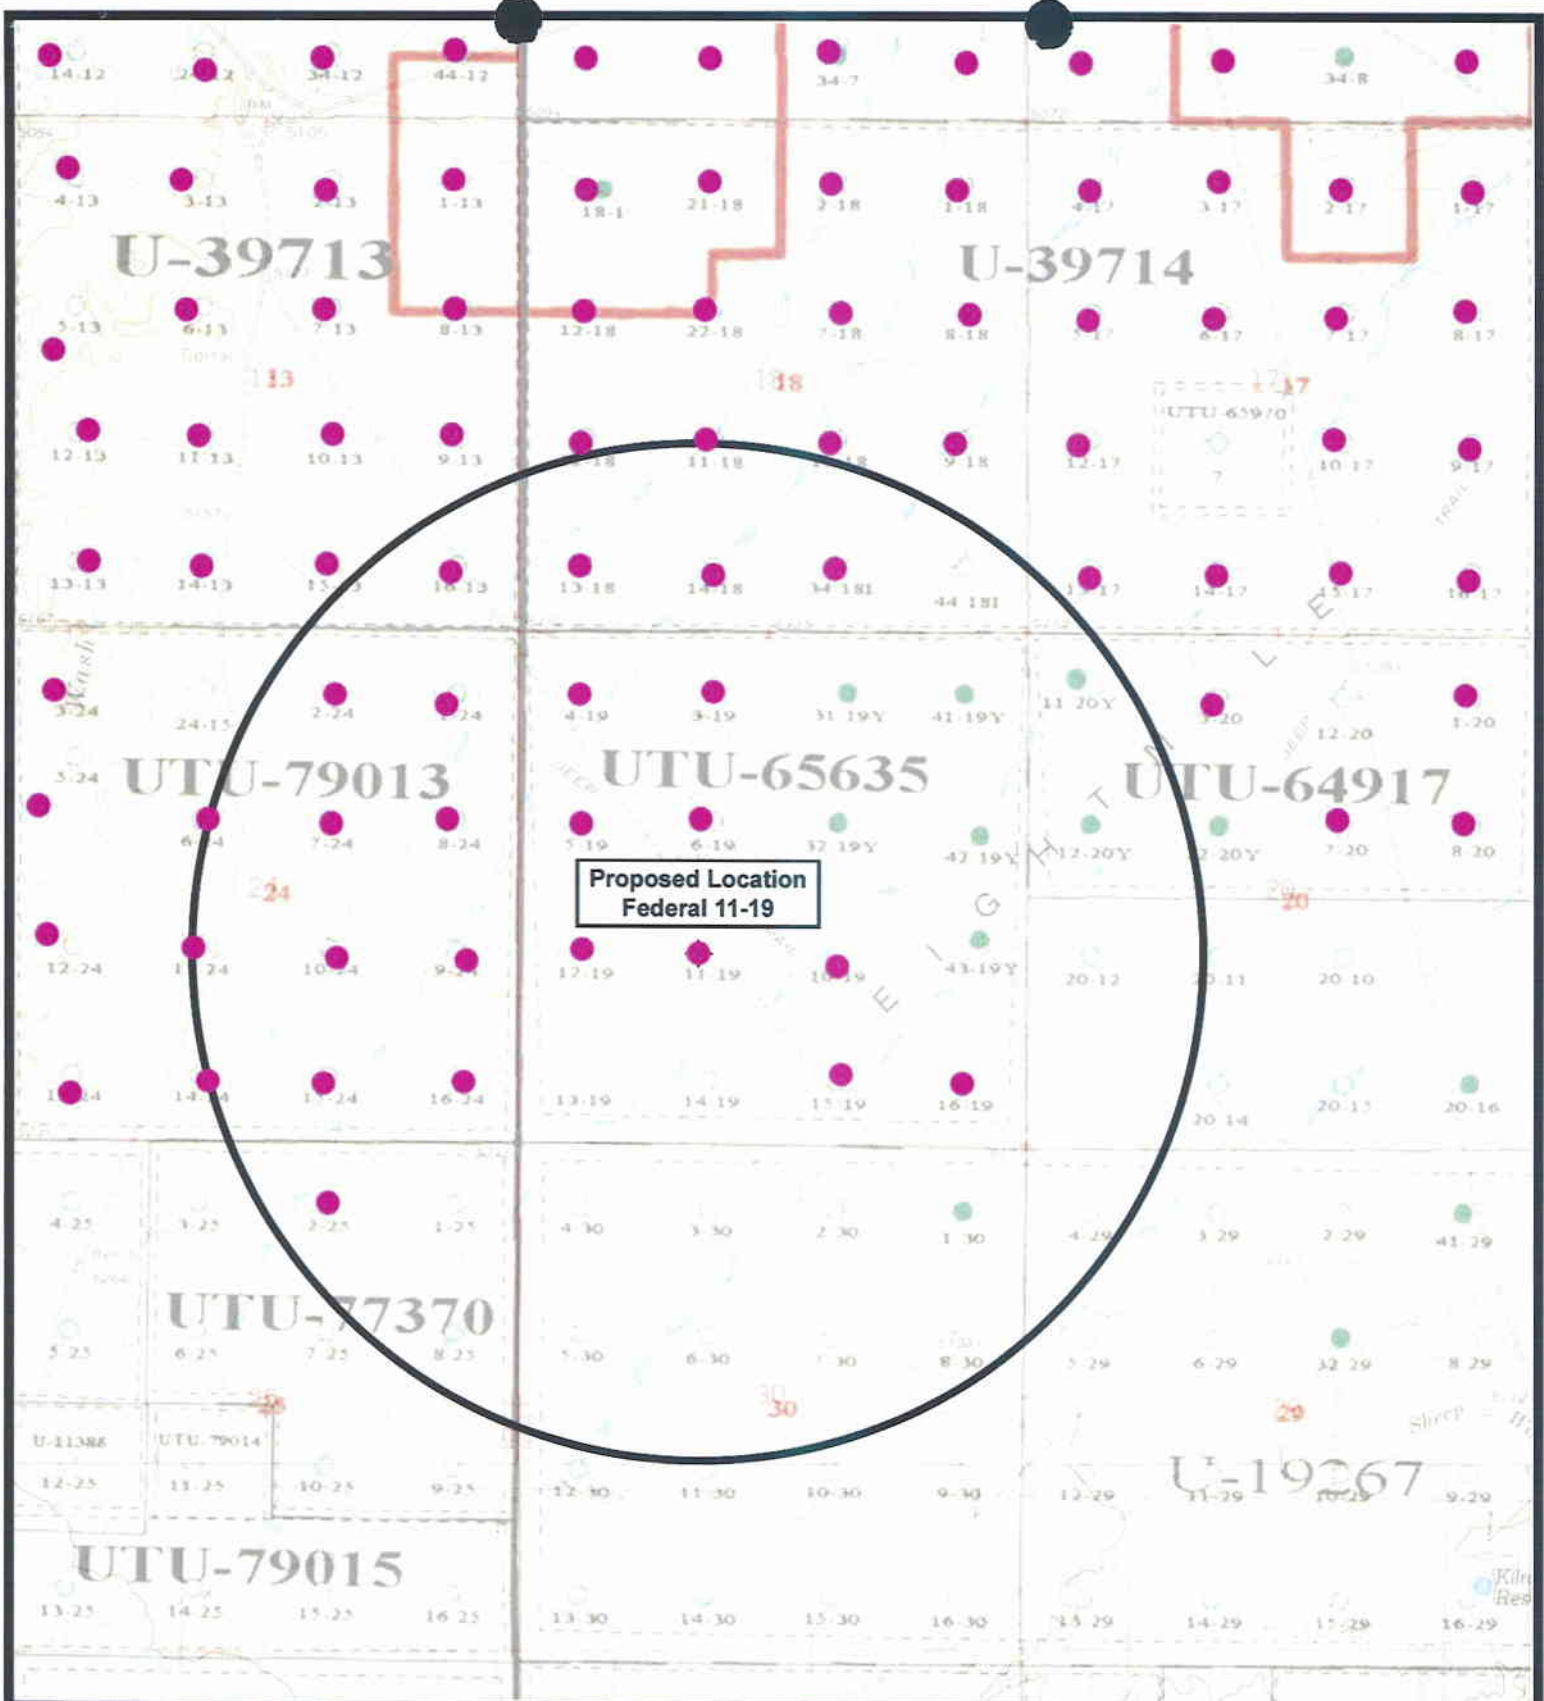

Proposed Location  
Federal 11-19



**NEWFIELD**  
Exploration Company

**Federal 11-19-9-18**  
**SEC. 19, T9S, R18E, S.L.B.&M.**





**Tri-State**  
Land Surveying Inc.  
(435) 781-2501  
180 North Vernal Ave. Vernal, Utah 84078

SCALE: 1" = 2,000'

DRAWN BY: mw

DATE: 03-05-2007

**Legend**

● Location

○ One-Mile Radius

**Exhibit "B"**

## 2-M SYSTEM

Blowout Prevention Equipment Systems

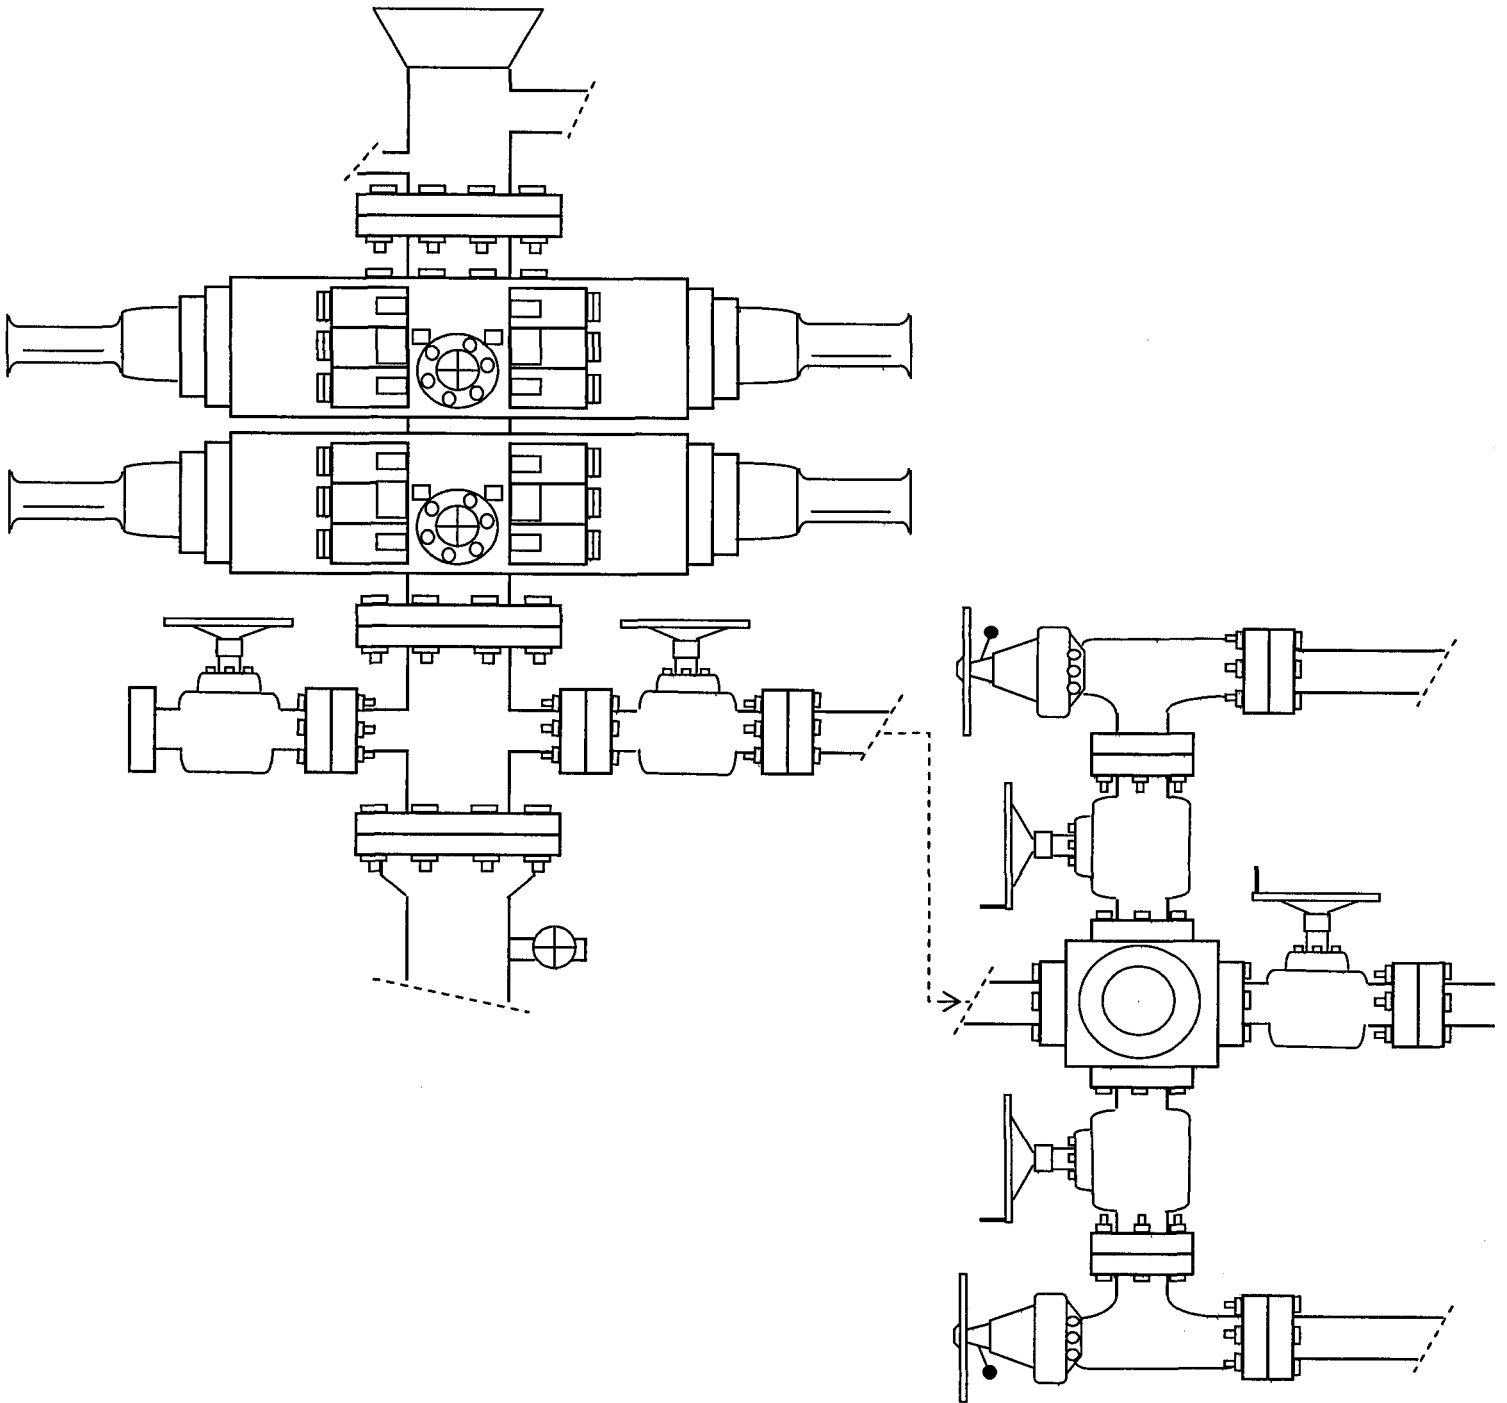


EXHIBIT C

CULTURAL RESOURCE INVENTORY OF  
INLAND PRODUCTIONS' PARCEL IN  
T 9 S, R17 E, SEC. 13, 14, 15, 23, & 24  
AND T 9 S, R 18 E, SEC. 18 & 19,  
DUCHESNE AND UINTAH COUNTIES, UTAH

Exhibit "D"  
1 of 2

BY:

Katie Simon  
and  
Keith R. Montgomery

Prepared For:

Bureau of Land Management  
Vernal Field Office

Prepared Under Contract With:

Inland Production  
2507 Flintridge Place  
Fort Collins, CO 80521

Prepared By:

Montgomery Archaeological Consultants  
P.O. Box 147  
Moab, Utah 84532

MOAC Report No. 03-82

January 12, 2004

United States Department of Interior (FLPMA)  
Permit No. 03-UT-60122

State of Utah Antiquities Project (Survey)  
Permit No. U-03-MQ-0750b

2 of 2

**INLAND RESOURCES, INC.**

**PALEONTOLOGICAL FIELD SURVEY OF PROPOSED  
PRODUCTION DEVELOPMENT AREAS,  
DUCHESNE AND UTAH COUNTIES, UTAH**

(Section 35, T 8 S, R 17 E; Sections 13, 14, 23, 24, T 9 S, R 17 E; NE 1/4, NE 1/4,  
Section 15, T 9 S, R 17 E; Sections 18, 19, T 9 S, R 18 E; Sections  
2, 3, 10 and western half of Section 11, T 9 S, R 15 E)

**REPORT OF SURVEY**

Prepared for:

**Inland Resources, Inc.**

Prepared by:

Wade E. Miller  
Consulting Paleontologist  
July 28, 2003

**WORKSHEET**  
**APPLICATION FOR PERMIT TO DRILL**

APD RECEIVED: 06/11/2007

API NO. ASSIGNED: 43-047-39397

WELL NAME: FEDERAL 11-19-9-18

OPERATOR: NEWFIELD PRODUCTION ( N2695 )

PHONE NUMBER: 435-646-3721

CONTACT: MANDIE CROZIER

PROPOSED LOCATION:

NESW 19 090S 180E

SURFACE: 1976 FSL 1916 FWL

BOTTOM: 1976 FSL 1916 FWL

COUNTY: UINTAH

LATITUDE: 40.01458 LONGITUDE: -109.9381

UTM SURF EASTINGS: 590631 NORTHINGS: 4429705

FIELD NAME: 8 MILE FLAT NORTH ( 590 )

INSPECT LOCATN BY: / /

**Tech Review**

**Initials**

**Date**

Engineering

Geology

Surface

LEASE TYPE: 1 - Federal

LEASE NUMBER: UTU-65635

SURFACE OWNER: 1 - Federal

PROPOSED FORMATION: GRRV

COALBED METHANE WELL? NO

RECEIVED AND/OR REVIEWED:

☒ Plat

☒ Bond: Fed[1] Ind[] Sta[] Fee[]  
(No. UTB000192 )

☒ Potash (Y/N)

☒ Oil Shale 190-5 (B) or 190-3 or 190-13

☒ Water Permit

(No. 43-10136 )

☒ RDCC Review (Y/N)

(Date: )

☒ Fee Surf Agreement (Y/N)

☒ Intent to Commingle (Y/N)

LOCATION AND SITING:

\_\_\_ R649-2-3.

Unit: \_\_\_\_\_

\_\_\_ R649-3-2. General

Siting: 460 From Qtr/Qtr & 920' Between Wells

\_\_\_ R649-3-3. Exception

\_\_\_ Drilling Unit

Board Cause No: \_\_\_\_\_

Eff Date: \_\_\_\_\_

Siting: \_\_\_\_\_

\_\_\_ R649-3-11. Directional Drill

COMMENTS: \_\_\_\_\_

STIPULATIONS: \_\_\_\_\_



## EIGHT MILE FLAT NORTH FIELD

OPERATOR: NEWFIELD PROD CO (N2695)

SEC: 18 T.9S R. 22E

FIELD: EIGHT MILE NORTH (590)

COUNTY: UINTAH

SPACING: R649-3-2 / GENERAL SITING

**Field Status**


- ABANDONED
- ACTIVE
- COMBINED
- INACTIVE
- PROPOSED
- STORAGE
- TERMINATED

**Unit Status**


- EXPLORATORY
- GAS STORAGE
- NF PP OIL
- NF SECONDARY
- PENDING
- PI OIL
- PP GAS
- PP GEOTHERML
- PP OIL
- SECONDARY
- TERMINATED

### Wells Status

- GAS INJECTION
- GAS STORAGE
- LOCATION ABANDONED
- NEW LOCATION
- PLUGGED & ABANDONED
- PRODUCING GAS
- PRODUCING OIL
- SHUT-IN GAS
- SHUT-IN OIL
- TEMP. ABANDONED
- TEST WELL
- WATER INJECTION
- WATER SUPPLY
- WATER DISPOSAL
- DRILLING



Utah Oil Gas and Mining



PREPARED BY: DIANA MASON  
DATE: 14-JUNE-2007



JON M. HUNTSMAN, JR.  
Governor

GARY R. HERBERT  
Lieutenant Governor

# State of Utah

## DEPARTMENT OF NATURAL RESOURCES

MICHAEL R. STYLER  
Executive Director

### Division of Oil Gas and Mining

JOHN R. BAZA  
Division Director

June 18, 2007

Newfield Production Company  
Rt. #3, Box 3630  
Myton, UT 84052

Re: Federal 11-19-9-18 Well, 1976' FSL, 1916' FWL, NE SW, Sec. 19, T. 9 South,  
R. 18 East, Uintah County, Utah

Gentlemen:

Pursuant to the provisions and requirements of Utah Code Ann. § 40-6-1 *et seq.*, Utah Administrative Code R649-3-1 *et seq.*, and the attached Conditions of Approval, approval to drill the referenced well is granted.

This approval shall expire one year from the above date unless substantial and continuous operation is underway, or a request for extension is made prior to the expiration date. The API identification number assigned to this well is 43-047-39397.

Sincerely,

Gil Hunt  
Associate Director

pab  
Enclosures

cc: Uintah County Assessor  
Bureau of Land Management, Vernal Office

**Operator:** Newfield Production Company  
**Well Name & Number** Federal 11-19-9-18  
**API Number:** 43-047-39397  
**Lease:** UTU-65635

**Location:** NE SW                      **Sec.** 19                      **T.** 9 South                      **R.** 18 East

### **Conditions of Approval**

**1. General**

Compliance with the requirements of Utah Admin. R. 649-1 *et seq.*, the Oil and Gas Conservation General Rules, and the applicable terms and provisions of the approved Application for permit to drill.

**2. Notification Requirements**

Notify the Division with 24 hours of spudding the well.

- Contact Carol Daniels at (801) 538-5284.

Notify the Division prior to commencing operations to plug and abandon the well.

- Contact Dustin Doucet at (801) 538-5281 office      (801) 733-0983 home

**3. Reporting Requirements**

All required reports, forms and submittals will be promptly filed with the Division, including but not limited to the Entity Action Form (Form 6), Report of Water Encountered During Drilling (Form 7), Weekly Progress Reports for drilling and completion operations, and Sundry Notices and Reports on Wells requesting approval of change of plans or other operational actions.

**4. State approval of this well does not supersede the required federal approval, which must be obtained prior to drilling.**

**5. This proposed well is located in an area for which drilling units (well spacing patterns) have not been established through an order of the Board of Oil, Gas and Mining (the "Board"). In order to avoid the possibility of waste or injury to correlative rights, the operator is requested, once the well has been drilled, completed, and has produced, to analyze geological and engineering data generated therefrom, as well as any similar data from surrounding areas if available. As soon as is practicable after completion of its analysis, and if the analysis suggests an area larger than the quarter-quarter section upon which the well is located is being drained, the operator is requested to seek an appropriate order from the Board establishing drilling and spacing units in conformance with such analysis by filing a Request for Agency Action with the Board.**

RECEIVED  
VERNAL FIELD OFFICE

2007 JUN 11 PM 2:47

Form 3160-3  
(September 2001)

FORM APPROVED  
OMB No. 1004-0136  
Expires January 31, 2004

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

DEPT. OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

APPLICATION FOR PERMIT TO DRILL OR REENTER

1a. Type of Work: <input checked="" type="checkbox"/> DRILL <input type="checkbox"/> REENTER		5. Lease Serial No. UTU-65635
1b. Type of Well: <input checked="" type="checkbox"/> Oil Well <input type="checkbox"/> Gas Well <input type="checkbox"/> Other <input checked="" type="checkbox"/> Single Zone <input type="checkbox"/> Multiple Zone		6. If Indian, Allottee or Tribe Name N/A
2. Name of Operator Newfield Production Company		7. If Unit or CA Agreement, Name and No. N/A
3a. Address Route #3 Box 3630, Myton UT 84052	3b. Phone No. (include area code) (435) 646-3721	8. Lease Name and Well No. Federal 11-19-9-18
4. Location of Well (Report location clearly and in accordance with any State requirements. *) At surface NE/SW 1976' FSL 1916' FWL At proposed prod. zone		9. API Well No. 43 047 39397
14. Distance in miles and direction from nearest town or post office* Approximatley 18.8 miles southeast of Myton, Utah		10. Field and Pool, or Exploratory Eight Mile Flat
15. Distance from proposed* location to nearest property or lease line, ft. (Also to nearest drig. unit line, if any) Approx. 1916' f/lse, NA' f/unit	16. No. of Acres in lease 638.08	11. Sec., T., R., M., or Blk. and Survey or Area NE/SW Sec. 19, T9S R18E
17. Spacing Unit dedicated to this well 40 Acres	18. Distance from proposed location* to nearest well, drilling, completed, applied for, on this lease, ft. Approx. 1267'	12. County or Parish Uintah
19. Proposed Depth 5565'	20. BLM/BIA Bond No. on file UTB000192 WYB000493	13. State UT
21. Elevations (Show whether DF, KDB, RT, GL, etc.) 5179' GL	22. Approximate date work will start* 4th Quarter 2007	23. Estimated duration Approximately seven (7) days from spud to rig release.
24. Attachments		

The following, completed in accordance with the requirements of Onshore Oil and Gas Order No.1, shall be attached to this form:

- |   |  |
|---|--|
| 1. Well plat certified by a registered surveyor.  | 4. Bond to cover the operations unless covered by an existing bond on file (see Item 20 above).    |
| 2. A Drilling Plan.   | 5. Operator certification.   |
| 3. A Surface Use Plan (if the location is on National Forest System Lands, the SUPO shall be filed with the appropriate Forest Service Office). | 6. Such other site specific information and/or plans as may be required by the authorized officer. |

25. Signature 	Name (Printed/Typed) Mandie Crozier	Date 6/7/07
Title Regulatory Specialist		
Approved by (Signature) 	Name (Printed/Typed) JERRY KENCZKA	Date 3-18-2008
Title Assistant Field Manager Lands & Mineral Resources		
Office VERNAL FIELD OFFICE		

Application approval does not warrant or certify the the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Conditions of approval, if any, are attached

**CONDITIONS OF APPROVAL ATTACHED**

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

\*(Instructions on reverse)

UDOGM

NOTICE OF APPROVAL

RECEIVED

MAR 24 2008

DIV. OF OIL, GAS & MINING

NOS 3/23/07  
07 PP 1651A



UNITED STATES DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT  
VERNAL FIELD OFFICE

170 South 500 East

VERNAL, UT 84078

(435) 781-4400



**CONDITIONS OF APPROVAL FOR APPLICATION FOR PERMIT TO DRILL**

Company: Newfield Production Company  
Well No: Federal 11-19-9-18  
API No: 43-047-39397

Location: NESW, Sec. 19, T 9S, R18E  
Lease No: UTU-65635  
Agreement: N/A

Title	Name	Office Phone Number	Cell Phone Number
Petroleum Engineer:	Matt Baker	(435) 781-4490	(435) 828-4470
Petroleum Engineer:	Michael Lee	(435) 781-4432	(435) 828-7875
Petroleum Engineer:	James Ashley	(435) 781-4470	(435) 828-7874
Petroleum Engineer:	Ryan Angus	(435) 781-4430	(435) 828-7368
Supervisory Petroleum Technician:	Jamie Sparger	(435) 781-4502	(435) 828-3913
NRS/Enviro Scientist:		(435) 781-4475	(435) 828-4029
Supervisory NRS/Enviro Scientist:	Karl Wright	(435) 781-4484	(435) 828-7381
NRS/Enviro Scientist:	Holly Villa	(435) 781-4404	(435) 828-3544
NRS/Enviro Scientist:		(435) 781-4476	
NRS/Enviro Scientist:	Chuck Macdonald	(435) 781-4441	(435) 828-7482
NRS/Enviro Scientist:		(435) 781-3400	(435) 828-3544
NRS/Enviro Scientist:	Michael Cutler	(435) 781-3401	(435) 828-3546
NRS/Enviro Scientist:	Anna Figueroa	(435) 781-3407	(435) 828-3548
NRS/Enviro Scientist:	Verlyn Pindell	(435) 781-3402	(435) 828-3547
NRS/Enviro Scientist:	Darren Williams	(435) 781-4447	(435) 828-4029
NRS/Enviro Scientist:	Nathan Packer	(435) 781-3405	(435) 828-3545

Fax: (435) 781-3420

**A COPY OF THESE CONDITIONS SHALL BE FURNISHED TO YOUR  
FIELD REPRESENTATIVE TO INSURE COMPLIANCE**

All lease and/or unit operations are to be conducted in such a manner that full compliance is made with the applicable laws, regulations (43 CFR Part 3160), and this approved Application for Permit to Drill including Surface and Downhole Conditions of Approval. The operator is considered fully responsible for the actions of his subcontractors. A copy of the approved APD must be on location during construction, drilling, and completion operations. **This permit is approved for a two (2) year period, or until lease expiration, whichever occurs first. An additional extension, up to two (2) years, may be applied for by sundry notice prior to expiration.**

**NOTIFICATION REQUIREMENTS**

Location Construction (Notify Environmental Scientist)	-	Forty-Eight (48) hours prior to construction of location and access roads.
Location Completion (Notify Environmental Scientist)	-	Prior to moving on the drilling rig.
Spud Notice (Notify Petroleum Engineer)	-	Twenty-Four (24) hours prior to spudding the well.
Casing String & Cementing (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to running casing and cementing all casing strings.
BOP & Related Equipment Tests (Notify Supv. Petroleum Tech.)	-	Twenty-Four (24) hours prior to initiating pressure tests.
First Production Notice (Notify Petroleum Engineer)	-	Within Five (5) business days after new well begins or production resumes after well has been off production for more than ninety (90) days.

***SURFACE USE PROGRAM  
CONDITIONS OF APPROVAL (COAs)***

- If there is an active Gilsonite mining operation within 2 miles of the well location, operator shall notify the Gilsonite operator at least 48 hours prior to any blasting during construction.
- If paleontological materials are uncovered during construction, the operator is to immediately stop work and contact the Authorized Officer (AO). A determination will be made by the AO as to what mitigation may be necessary for the discovered paleontologic material before construction can continue.

**STIPULATIONS:**

- The proposed area contains Mountain plover habitat. With this occurrence there will be a timing restriction during project activity (construction and drilling) to minimize disturbance to Mountain plover nesting from May 15 – June 15.
- An active colony of prairie dogs and their burrows (burrowing owl habitat) were observed on and around the proposed site. With this occurrence there will be a timing restriction during project activity (construction and drilling) to minimize disturbance during Burrowing Owl nesting from April 1 – August 31.
- Lease Notices from RMP: None
- Comments:
  1. If it is anticipated that construction or drilling will occur during the given timing restrictions for any wildlife, a BLM or qualified biologist shall be notified so surveys can be conducted. Depending upon the results of the surveys, permission to proceed may or may not be recommended or granted (depending on the species being surveyed and the condition of the habitat).

**Follow-up Actions and/or Recommendations:**

Based on the previous field exam and existing data, and if all timing restrictions are adhered to then, it is my opinion that a no effect situation exists for Special Status Wildlife Species with the construction and drilling of this proposed drill site. Therefore, this site is cleared from a Special Status Wildlife Species perspective.

**CONDITIONS OF APPROVAL:**

- All traffic related to this action will be restricted to approved routes. Cross-country vehicle travel will not be allowed.
- All pipelines (surface and buried) will be laid within one 50' wide construction ROW, on one side of the road, and will reduce down to a 30' wide permanent ROW on lease.
- A temporary road ROW will not be granted. The road ROW will be 30 foot for construction and will reduce to an 18 foot running surface.

- The access road will be crowned and ditched. Flat-bladed roads are not allowed. All roads will have an 18', crowned (2 to 3% minimum), running surface. All roads will have drainage ditches along both sides of road.
- No vehicle travel, construction or routine maintenance activities shall be performed during periods when the soil is too wet to adequately support vehicles and/or construction equipment. If such equipment creates ruts in excess of three inches deep, the soil shall be deemed too wet to adequately support construction equipment.
- If additional erosion occurs during the life of this project, more culverts, low water crossings, berms, wing ditches or etc. will be needed to control the erosion.
- Low-water crossings will be appropriately constructed to avoid sedimentation of drainage ways and other water resources.
- Pipelines will be buried at all major drainage crossings.
- Prevent fill and stock piles from entering drainages.
- To insure impermeability, the reserve pit will be lined with a 16 ml or greater liner and felt prior to spudding.
- The liner is to be cut 5 feet below ground surface or at the level of the cuttings, whichever is deeper, and the excess liner material is to be disposed of at an authorized disposal site.
- When the reserve pit contains fluids or toxic substances, the operator must ensure animals do not ingest or become entrapped in pit fluids.
- Any hydrocarbons in the reserve pit will be removed **immediately** upon well completion; in accordance with 43 CFR 3162.7-1. Pits must be free of oil and other liquid and solid wastes prior to filling.
- Monument Butte SOP, Section 9.2 - Pit Fencing Minimum Standards - will be strictly adhered to. To include 9.2.2.3 - Corner posts will be cemented and/or braced in such a manner as to keep fence tight at all times.
- If Uinta Basin hookless cactus or other special status plants are found, construction will cease and the AO will be notified to determine the appropriate mitigation.

- **Interim Reclamation:**

The topsoil from the reserve pit shall be stripped and piled separately near the reserve pit. When the reserve pit is closed, it shall be re-contoured and the topsoil re-spread, and the area shall be **seeded using a rangeland drill**. Seeding depth as per AO, or seed distributor. If portions of the site are too steep (>40%), or rocky, that portion may be broadcast seeded. If broadcasting seed, the seed shall be walked into the soil with a dozer immediately after the seeding is completed, or covered by soil using a drag chain. Seeding shall occur in the fall (August 1<sup>st</sup> until snow or ground is frozen) with the following seed mix:

Seed mix:

Common name	Latin name	lbs/acre	Recommended seed planting depth
Squirreltail grass	<i>Elymus elymoides</i>	3.0	1/4 - 1/2"
Siberian wheatgrass	<i>Agropyron fragile</i>	1.0	1/2"
Shadscale saltbush	<i>Atriplex confertifolia</i>	0.50	1/2"
Four-wing saltbush	<i>Atriplex canescens</i>	0.50	1/2"
Gardner's saltbush	<i>Atriplex gardneri</i>	0.50	1/2"
Scarlet globemallow	<i>Sphaeralcea coccinea</i>	0.10	1/8 - 1/4"

- All pounds are pure live seed.
- All seed and mulch will be certified weed free.
- Rates are set for drill seeding; double rate if broadcasting.
- Reseeding may be required if initial seeding is not successful.

- **Final reclamation:**

- Once the location is plugged and abandoned, the well location, access, and any disturbed areas shall be recontoured to natural topography, topsoil shall be respread, and the entire location shall be seeded following guidelines in the seed mix bullet statement above. Final seed mix: same as interim.
- Noxious and/or invasive weeds will be controlled along access roads, pipelines, well sites, and all other applicable facilities. Any noxious and/or invasive weeds outbreak, directly attributed to the activities of the Operator, will be the responsibility of the Operator to control. On BLM administered land, a Pesticide Use Proposal (PUP) must be submitted and approved prior to the application of herbicides, pesticides, or other possibly hazardous chemicals.
- The topsoil from the reserve pit shall be stripped and piled separately near the reserve pit. When the reserve pit is closed, it shall be recontoured and the topsoil respread, and the area shall be seeded in the same manner as the location topsoil.
- Once the location is plugged and abandoned, it shall be recontoured to natural topology, topsoil shall be respread, and the entire location shall be seeded with a seed mix recommended by the AO (see above). Seed application will follow all guidelines in the interim seed mix bullet statement above. If reclamation seeding should take place using the broadcast method, the seed at a minimum will be walked into the soil with a dozer immediately after the seeding is completed.

- The authorized officer may prohibit surface disturbing activities during severe winter conditions to minimize watershed damage. This limitation does not apply to operation and maintenance of producing wells.
- The authorized officer may prohibit surface disturbing activities during wet or muddy conditions to minimize watershed damage. This limitation does not apply to operation and maintenance of producing wells.
- All well facilities not regulated by OSHA will be painted Carlsbad Canyon.
- All boulders with a length or diameter greater than 3 feet, that are found showing at the surface, will be stockpiled for use during final reclamation.
- Notify the Authorized Officer 48 hours prior to surface disturbing activities.

**DOWNHOLE PROGRAM  
CONDITIONS OF APPROVAL (COAs)**

**SITE SPECIFIC DOWNHOLE COAs:**

- Production casing cement shall be brought up and into the surface.
- Logging: Run gamma ray and electric logs from TD to surface casing.

**All provisions outlined in Onshore Oil & Gas Order #2 Drilling Operations shall be strictly adhered to.** The following items are emphasized:

**DRILLING/COMPLETION/PRODUCING OPERATING STANDARDS**

- The spud date and time shall be reported orally to Vernal Field Office within 24 hours of spudding.
- Notify Vernal Field Office Supervisory Petroleum Engineering Technician at least 24 hours in advance of casing cementing operations and BOPE & casing pressure tests.
- All requirements listed in Onshore Order #2 III. E. Special Drilling Operations are applicable for air drilling of surface hole.
- Blowout prevention equipment (BOPE) shall remain in use until the well is completed or abandoned. Closing unit controls shall remain unobstructed and readily accessible at all times. Choke manifolds shall be located outside of the rig substructure.
- All BOPE components shall be inspected daily and those inspections shall be recorded in the daily drilling report. Components shall be operated and tested as required by Onshore Oil & Gas Order No. 2 to insure good mechanical working order. All BOPE pressure tests shall be performed by a test pump with a chart recorder and **NOT** by the rig pumps. Test shall be reported in the driller's log.
- BOP drills shall be initially conducted by each drilling crew within 24 hours of drilling out from under the surface casing and weekly thereafter as specified in Onshore Oil & Gas Order No. 2.
- Casing pressure tests are required before drilling out from under all casing strings set and cemented in place.
- No aggressive/fresh hard-banded drill pipe shall be used within casing.
- **Cement baskets shall not be run on surface casing.**
- The operator must report all shows of water or water-bearing sands to the BLM. If flowing water is encountered it must be sampled, analyzed, and a copy of the analyses submitted to the BLM Vernal Field Office.

- The operator must report encounters of all non oil & gas mineral resources (such as Gilsonite, tar sands, oil shale, trona, etc.) to the Vernal Field Office, in writing, within 5 working days of each encounter. Each report shall include the well name/number, well location, date and depth (from KB or GL) of encounter, vertical footage of the encounter and, the name of the person making the report (along with a telephone number) should the BLM need to obtain additional information.
- A complete set of angular deviation and directional surveys of a directional well will be submitted to the Vernal BLM office engineer within 30 days of the completion of the well.
- While actively drilling, chronologic drilling progress reports shall be filed directly with the BLM, Vernal Field Office on a weekly basis in sundry, letter format or e-mail to the Petroleum Engineers until the well is completed.
- A cement bond log (CBL) will be run from the production casing shoe to the top of cement and shall be utilized to determine the bond quality for the production casing. Submit a field copy of the CBL to this office.
- **Please submit an electronic copy of all other logs run on this well in LAS format to UT\_VN\_Welllogs@BLM.gov. This submission will supersede the requirement for submittal of paper logs to the BLM.**
- There shall be no deviation from the proposed drilling, completion, and/or workover program as approved. Safe drilling and operating practices must be observed. Any changes in operation must have prior approval from the BLM Vernal Field Office.

## **OPERATING REQUIREMENT REMINDERS:**

- All wells, whether drilling, producing, suspended, or abandoned, shall be identified in accordance with 43 CFR 3162.6. There shall be a sign or marker with the name of the operator, lease serial number, well number, and surveyed description of the well.
- In accordance with 43 CFR 3162.4-3, this well shall be reported on the "Monthly Report of Operations" (Oil and Gas Operations Report ((OGOR)) starting with the month in which operations commence and continue each month until the well is physically plugged and abandoned. This report shall be filed in duplicate, directly with the Minerals Management Service, P.O. Box 17110, Denver, Colorado 80217-0110, or call 1-800-525-7922 (303) 231-3650 for reporting information.
- Should the well be successfully completed for production, the BLM Vernal Field office must be notified when it is placed in a producing status. Such notification will be by written communication and must be received in this office by not later than the fifth business day following the date on which the well is placed on production. The notification shall provide, as a minimum, the following informational items:
  - Operator name, address, and telephone number.
  - Well name and number.
  - Well location ( $\frac{1}{4}$  Sec., Twn, Rng, and P.M.).
  - Date well was placed in a producing status (date of first production for which royalty will be paid).
  - The nature of the well's production, (i.e., crude oil, or crude oil and casing head gas, or natural gas and entrained liquid hydrocarbons).
  - The Federal or Indian lease prefix and number on which the well is located; otherwise the non-Federal or non-Indian land category, i.e., State or private.
  - Unit agreement and/or participating area name and number, if applicable.
  - Communitization agreement number, if applicable.
- Any venting or flaring of gas shall be done in accordance with Notice to Lessees (NTL) 4A and needs prior approval from the BLM Vernal Field Office.
- All undesirable events (fires, accidents, blowouts, spills, discharges) as specified in NTL 3A will be reported to the BLM, Vernal Field Office. Major events, as defined in NTL3A, shall be reported verbally within 24 hours, followed by a written report within 15 days. "Other than Major Events" will be reported in writing within 15 days. "Minor Events" will be reported on the Monthly Report of Operations and Production.

- Whether the well is completed as a dry hole or as a producer, "Well Completion and Recompletion Report and Log" (BLM Form 3160-4) shall be submitted not later than 30 days after completion of the well or after completion of operations being performed, in accordance with 43 CFR 3162.4-1. Two copies of all logs run, core descriptions, and all other surveys or data obtained and compiled during the drilling, workover, and/or completion operations, shall be filed on BLM Form 3160-4. Submit with the well completion report a geologic report including, at a minimum, formation tops, and a summary and conclusions. Also include deviation surveys, sample descriptions, strip logs, core data, drill stem test data, and results of production tests if performed. Samples (cuttings, fluid, and/or gas) shall be submitted only when requested by the BLM, Vernal Field Office.
- All off-lease storage, off-lease measurement, or commingling on-lease or off-lease, shall have prior written approval from the BLM Vernal Field Office.
- Oil and gas meters shall be calibrated in place prior to any deliveries. The BLM Vernal Field Office Petroleum Engineers will be provided with a date and time for the initial meter calibration and all future meter proving schedules. A copy of the meter calibration reports shall be submitted to the BLM Vernal Field Office. All measurement facilities will conform to the API standards for liquid hydrocarbons and the AGA standards for natural gas measurement. All measurement points shall be identified as the point of sale or allocation for royalty purposes.
- A schematic facilities diagram as required by Onshore Oil & Gas Order No. 3 shall be submitted to the BLM Vernal Field Office within 30 days of installation or first production, whichever occurs first. All site security regulations as specified in Onshore Oil & Gas Order No. 3 shall be adhered to. All product lines entering and leaving hydrocarbon storage tanks will be effectively sealed in accordance with Onshore Oil & Gas Order No. 3.
- Any additional construction, reconstruction, or alterations of facilities, including roads, gathering lines, batteries, etc., which will result in the disturbance of new ground, shall require the filing of a suitable plan and need prior approval of the BLM Vernal Field Office. Emergency approval may be obtained orally, but such approval does not waive the written report requirement.
- No location shall be constructed or moved, no well shall be plugged, and no drilling or workover equipment shall be removed from a well to be placed in a suspended status without prior approval of the BLM Vernal Field Office. If operations are to be suspended for more than 30 days, prior approval of the BLM Vernal Field Office shall be obtained and notification given before resumption of operations.
- Pursuant to Onshore Oil & Gas Order No. 7, this is authorization for pit disposal of water produced from this well for a period of 90 days from the date of initial production. A permanent disposal method must be approved by this office and in operation prior to the end of this 90-day period. In order to meet this deadline, an application for the proposed permanent disposal method shall be submitted along with any necessary water analyses, as soon as possible, but no later than 45 days after the date of first production. Any method of disposal which has not been approved prior to the end of the authorized 90-day period will be considered as an Incident of Noncompliance and will be grounds for issuing a shut-in order until an acceptable manner for disposing of said water is provided and approved by this office.

- Unless the plugging is to take place immediately upon receipt of oral approval, the Field Office Petroleum Engineers must be notified at least 24 hours in advance of the plugging of the well, in order that a representative may witness plugging operations. If a well is suspended or abandoned, all pits must be fenced immediately until they are backfilled. The "Subsequent Report of Abandonment" (Form BLM 3160-5) must be submitted within 30 days after the actual plugging of the well bore, showing location of plugs, amount of cement in each, and amount of casing left in hole, and the current status of the surface restoration.

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

FORM APPROVED  
Budget Bureau No. 1004-0135  
Expires: March 31, 1993

**SUNDRY NOTICES AND REPORTS ON WELLS**

Do not use this form for proposals to drill or to deepen or reentry a different reservoir.  
Use "APPLICATION FOR PERMIT -" for such proposals

**SUBMIT IN TRIPLICATE**

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

**NEWFIELD PRODUCTION COMPANY**

3. Address and Telephone No.

**Rt. 3 Box 3630, Myton Utah, 84052 435-646-3721**

4. Location of Well (Footage, Sec., T., R., m., or Survey Description)

**1976 FSL 1916 FWL NE/SW Section 19, T9S R18E**

5. Lease Designation and Serial No.

**UTU-65635**

6. If Indian, Allottee or Tribe Name

**NA**

7. If Unit or CA, Agreement Designation

**NA**

8. Well Name and No.

**FEDERAL 11-19-9-18**

9. API Well No.

**43-047-39397**

10. Field and Pool, or Exploratory Area

**8 MILE FLAT**

11. County or Parish, State

**UINTAH COUNTY, UT.**

12. **CHECK APPROPRIATE BOX(S) TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA**

**TYPE OF SUBMISSION**

☒ Notice of Intent  
☐ Subsequent Report  
☐ Final Abandonment Notice

**TYPE OF ACTION**

☐ Abandonment  
☐ Recompletion  
☐ Plugging Back  
☐ Casing Repair  
☐ Altering Casing  
☒ Other **Permit Extension**

☐ Change of Plans  
☐ New Construction  
☐ Non-Routine Fracturing  
☐ Water Shut-Off  
☐ Conversion to Injection  
☐ Dispose Water

(Note: Report results of multiple completion on Well Completion or Recompletion Report and Log form.)

13. Describe Proposed or Completed Operations (Clearly state all pertinent details, and give pertinent dates, including estimated date of starting any proposed work. If well is directionally drilled, give subsurface locations and measured and true vertical depths for all markers and zones pertinent to this work.)\*

Newfield Production Company requests to extend the Permit to Drill this well for one year. The original approval date was 6/18/07.

This APDis not yet due to expire with the BLM.

Approved by the  
Utah Division of  
Oil, Gas and Mining

**COPY SENT TO OPERATOR**

Date: **6.2.2008**

Initials: **KS**

Date: **05-28-08**

By: **[Signature]**

**RECEIVED**

**MAY 28 2008**

**DEPT. OF OIL, GAS & MINING**

14. I hereby certify that the foregoing is true and correct

Signed

**Mandie Crozier**

Title

**Regulatory Specialist**

Date

**5/27/2008**

CC: UTAH DOGM

(This space for Federal or State office use)

Approved by

Title

Date

Conditions of approval, if any:

CC: Utah DOGM

Title 18 U.S.C. Section 1001, makes it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious or fraudulent statements or representations as to any matter within its jurisdiction.

RESET

**Application for Permit to Drill  
Request for Permit Extension  
Validation**

(this form should accompany the Sundry Notice requesting permit extension)

**API:** 43-047-39397  
**Well Name:** Federal 11-19-9-18  
**Location:** NE/SW Section 19,T9S R18E  
**Company Permit Issued to:** Newfield Production Company  
**Date Original Permit Issued:** 6/18/2007

The undersigned as owner with legal rights to drill on the property as permitted above, hereby verifies that the information as submitted in the previously approved application to drill, remains valid and does not require revision.

Following is a checklist of some items related to the application, which should be verified.

If located on private land, has the ownership changed, if so, has the surface agreement been updated? Yes ☐ No ☒ NA

Have any wells been drilled in the vicinity of the proposed well which would affect the spacing or siting requirements for this location? Yes ☐ No ☒

Has there been any unit or other agreements put in place that could affect the permitting or operation of this proposed well? Yes ☐ No ☒

Have there been any changes to the access route including ownership, or right-of-way, which could affect the proposed location? Yes ☐ No ☒

Has the approved source of water for drilling changed? Yes ☐ No ☒

Have there been any physical changes to the surface location or access route which will require a change in plans from what was discussed at the onsite evaluation? Yes ☐ No ☒

Is bonding still in place, which covers this proposed well? Yes ☒ No ☐

  
Signature

5/27/2008

Date

**Title:** Regulatory Specialist

**Representing:** Newfield Production Company

RECEIVED  
MAY 28 2008  
DIV. OF OIL, GAS & MINING

## DIVISION OF OIL, GAS AND MINING

### **SPUDDING INFORMATION**

Name of Company: NEWFIELD PRODUCTION COMPANY

Well Name: FEDERAL 11-19-9-18

Api No: 43-047-39397 Lease Type: FEDERAL

Section 19 Township 09S Range 18E County UINTAH

Drilling Contractor ROSS DRILLING RIG # 24

### **SPUDDED:**

Date 07/08/08

Time 10:30 AM

How DRY

**Drilling will Commence:** \_\_\_\_\_

Reported by TROY ZUFEIT

Telephone # (435) 823-6313

Date 07/08//08 Signed CHD

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

RECEIVED  
JUL 14 2008  
DIV. OF OIL, GAS & MINING

FORM APPROVED  
OMB No. 1004-0137  
Expires: July 31, 2010

**SUNDRY NOTICES AND REPORTS ON WELLS**  
Do not use this form for proposals to drill or to re-enter an  
abandoned well. Use Form 3160-3 (APD) for such proposals.

**SUBMIT IN TRIPLICATE - Other Instructions on page 2**

1. Type of Well  
☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator  
NEWFIELD PRODUCTION COMPANY

3a. Address Route 3 Box 3630  
Myton, UT 84052

3b. Phone (include area code)  
435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)  
1976 FSL 1916 FWL  
NESW Section 19 T9S R18E

5. Lease Serial No.

UTU-65635

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.

FEDERAL 11-19-9-18

9. API Well No.

4304739397

10. Field and Pool, or Exploratory Area

MONUMENT BUTTE

11. County or Parish, State

UINTAH, UT

**12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Spud Notice _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recompleat horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recompleat in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 7/8/08 MIRU Ross #24. Spud well @ 10:30am. Drill 320' of 121/4" hole with air mist. TIH w/7 jt's 85/8" j-55 24# csgn. set @ 324.38KB On 7/10/08 cement with 160 sks of class "G" w/ 3% CaCl<sub>2</sub> + 1/4# sk Cello-Flake mixed @15.8 ppg>1.17 cf/sk yeild. Returned 1 bbls cement to pit. Woc.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Jay Burton

Signature

Title

Drilling Foreman

Date

07/10/2008

**THIS SPACE FOR FEDERAL OR STATE OFFICE USE**

Approved by

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Title

Date

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

# NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

8 5/8 CASING SET AT 324.38

LAST CASING 8 5/8" SET # 324.38  
 DATUM 12' KB  
 DATUM TO CUT OFF CASING \_\_\_\_\_  
 DATUM TO BRADENHEAD FLANGE \_\_\_\_\_  
 TD DRILLER 320 LOGGER \_\_\_\_\_  
 HOLE SIZE 12 1/4

OPERATOR Newfield Production Company  
 WELL Federal 11-19-9-18  
 FIELD/PROSPECT Monument Butte  
 CONTRACTOR & RIG # Ross Rig # 24

## LOG OF CASING STRING:

PIECES	OD	ITEM - MAKE - DESCRIPTION	WT / FT	GRD	THREAD	CONDT	LENGTH
		Shoe Joint 45.92'					
		WHI - 92 csg head			8rd	A	0.95
7	8 5/8"	Maverick ST&C csg	24#	J-55	8rd	A	312.53
		<b>GUIDE</b> shoe			8rd	A	0.9
CASING INVENTORY BAL.		FEET	JTS	TOTAL LENGTH OF STRING			314.38
TOTAL LENGTH OF STRING		314.38	7	LESS CUT OFF PIECE			2
LESS NON CSG. ITEMS		1.85		PLUS DATUM TO T/CUT OFF CSG			12
PLUS FULL JTS. LEFT OUT		0		CASING SET DEPTH			<b>324.38</b>
TOTAL		312.53	7	} COMPARE			
TOTAL CSG. DEL. (W/O THRDS)		312.53	7				
TIMING		1ST STAGE					
BEGIN RUN CSG.		Spud 7/8/2008	10:30am	GOOD CIRC THRU JOB			Yes
CSG. IN HOLE		7/9/2008	4:00pm	Bbls CMT CIRC TO SURFACE			1
BEGIN CIRC		7/10/2008	11:36 AM	RECIPROCATED PIPE FOR			N/A
BEGIN PUMP CMT		7/10/2008	11:42am				
BEGIN DSPL. CMT		7/10/2008	11:53am	BUMPED PLUG TO			115 PSI Left on Csg. PSI
PLUG DOWN		7/10/2008	12:00 PM				

CEMENT USED		CEMENT COMPANY- <b>B. J.</b>	
STAGE	# SX	CEMENT TYPE & ADDITIVES	
1	160	Class "G" w/ 2% CaCL2 + 1/4#/sk Cello-Flake mixed @ 15.8 ppg 1.17 cf/sk yield	
CENTRALIZER & SCRATCHER PLACEMENT		SHOW MAKE & SPACING	
Centralizers - Middle first, top second & third for 3			

COMPANY REPRESENTATIVE Jay Burton DATE 7/10/2008

STATE OF UTAH  
DIVISION OF OIL, GAS AND MINING  
ENTITY ACTION FORM - FORM 6

OPERATOR: **NEWFIELD PRODUCTION COMPANY**  
ADDRESS: **RT. 3 BOX 3630**  
**MYTON, UT 84052**

OPERATOR ACCT. NO. **N2695**

ACTION CODE	CURRENT ENTITY NO.	NEW ENTITY NO.	API NUMBER	WELL NAME	WELL LOCATION				COUNTY	SPUD DATE	EFFECTIVE DATE
					QQ	SC	TP	RG			
B	99999	14844 ✓	4304736025	FEDERAL 14-33-8-18	SESW	33	8S	18E	UINTAH	7/10/2008	7/31/08
WELL 1 COMMENTS: GRRV											
B	99999	10835 ✓	4301333862	MONUMENT BUTTE STATE F-36-8-16	NWNW	36	8S	16E	DUCHESNE	7/11/2008	7/31/08
GRRV BHL = NWNW											
A	99999	16990	4304739397	FEDERAL 11-19-9-18	NESW	19	9S	18E	UINTAH	7/8/2008	7/31/08
GRRV											
B	99999	11486 ✓	4301333864	GILSONITE STATE L-32-8-17	SENE	32	8S	17E	DUCHESNE	7/14/2008	7/31/08
GRRV BHL = NWSE											
A	99999	16991	4304739395	FEDERAL 6-19-9-18	SESW	19	9S	18E	UINTAH	7/14/2008	7/31/08
WELL 5 COMMENTS: GRRV											
A	99999	16992	4301333851	STATE 11-16-9-16	NESW	16	9S	16E	DUCHESNE	7/16/2008	7/31/08
WELL 5 COMMENTS: GRRV											

ACTION CODES (See instructions on back of form)

- A - new entity for new well (single well only)
- B - well to existing entity (group or unit well)
- C - from one existing entity to another existing entity
- D - well from one existing entity to a new entity
- E - other (explain in comments section)

NOTE: Use COMMENT section to explain why each Action Code was selected.

RECEIVED

JUL 16 2008

DIV. OF OIL, GAS & MINING

Signature

Production Clerk

Jenri Park

07/16/08

Date

UNITED STATES  
DEPARTMENT OF THE INTERIOR  
BUREAU OF LAND MANAGEMENT

**SUNDRY NOTICES AND REPORTS ON WELLS**  
Do not use this form for proposals to drill or to re-enter an  
abandoned well. Use Form 3160-3 (APD) for such proposals.

FORM APPROVED  
OMB No. 1004-0137  
Expires: July 31, 2010

**SUBMIT IN TRIPLICATE - Other Instructions on page 2**

1. Type of Well

☒ Oil Well ☐ Gas Well ☐ Other

2. Name of Operator

NEWFIELD PRODUCTION COMPANY

3a. Address

Route 3 Box 3630  
Myton, UT 84052

3b. Phone (include area code)

435.646.3721

4. Location of Well (Footage, Sec., T., R., M., or Survey Description)

1976 FSL 1916 FWL

NESW Section 19 T9S R18E

5. Lease Serial No.

UTU-65635

6. If Indian, Allottee or Tribe Name.

7. If Unit or CA/Agreement, Name and/or

8. Well Name and No.

FEDERAL 11-19-9-18

9. API Well No.

4304739397

10. Field and Pool, or Exploratory Area

MONUMENT BUTTE

11. County or Parish, State

UINTAH, UT

**12. CHECK APPROPRIATE BOX(ES) TO INDICATE NATURE OF NOTICE, OR OTHER DATA**

TYPE OF SUBMISSION	TYPE OF ACTION			
<input type="checkbox"/> Notice of Intent	<input type="checkbox"/> Acidize	<input type="checkbox"/> Deepen	<input type="checkbox"/> Production (Start/Resume)	<input type="checkbox"/> Water Shut-Off
<input checked="" type="checkbox"/> Subsequent Report	<input type="checkbox"/> Alter Casing	<input type="checkbox"/> Fracture Treat	<input type="checkbox"/> Reclamation	<input type="checkbox"/> Well Integrity
<input type="checkbox"/> Final Abandonment	<input type="checkbox"/> Casing Repair	<input type="checkbox"/> New Construction	<input type="checkbox"/> Recomplete	<input checked="" type="checkbox"/> Other _____
	<input type="checkbox"/> Change Plans	<input type="checkbox"/> Plug & Abandon	<input type="checkbox"/> Temporarily Abandon	Weekly Status Report _____
	<input type="checkbox"/> Convert to Injector	<input type="checkbox"/> Plug Back	<input type="checkbox"/> Water Disposal	

13. Describe Proposed or Completed Operation: (Clearly state all pertinent details, including estimated starting date of any proposed work and approximate duration thereof. If the proposal is to deepen directionally or recomple horizontally, give subsurface locations and measured and true vertical depths of all pertinent markers and zones. Attach the Bond under which the work will be performed or provide the Bond No. on file with BLM/BIA. Required subsequent reports shall be filed within 30 days following completion of the involved operations. If the operation results in a multiple completion or recomple in a new interval, a Form 3160-4 shall be filed once testing has been completed. Final Abandonment Notices shall be filed only after all requirements, including reclamation, have been completed, and the operator has determined that the site is ready for final inspection.)

On 7/16/08 MIRU Patterson # 52. Set all equipment. Pressure test Kelly, TIW, Choke manifold, & Bop's to 2,000 psi. Test 8.625 csgn to 1,500 psi. Vernal BLM field, & Roosevelt DOGM office was notified of test. PU BHA and tag cement @ 278'. Drill out cement & shoe. Drill a 7.875 hole with fresh water to a depth of 5560'. Lay down drill string & BHA. Open hole log w/ Dig/SP/GR log's TD to surface. PU & TIH with Guide shoe, shoe jt, float collar, 130 jt's of 5.5 J-55, 15.5# csgn. Set @ 5559.94' KB. Cement with 275 sks cement mixed @ 11.0 ppg & 3.43 yld. The 400 sks cement mixed @ 14.4 ppg & 1.24 yld. Returned 35 bbls of cement to reserve pit. Nipple down Bop's. Drop slips @ 100,000 #'s tension. Release rig @ 6:00am on 7/22/08.

I hereby certify that the foregoing is true and correct (Printed/ Typed)

Title

Drilling Foreman

Jay Burton

Signature

Date

07/22/2008

**THIS SPACE FOR FEDERAL OR STATE OFFICE USE**

Approved by

Title

Date

Conditions of approval, if any, are attached. Approval of this notice does not warrant or certify that the applicant holds legal or equitable title to those rights in the subject lease which would entitle the applicant to conduct operations thereon.

Office

Title 18 U.S.C. Section 1001 and Title 43 U.S.C. Section 1212, make it a crime for any person knowingly and willfully to make to any department or agency of the United States any false, fictitious and fraudulent statements or representations as to any matter within its jurisdiction

(Instructions on page 2)

**RECEIVED**

**JUL 29 2008**

**DIV. OF OIL, GAS & MINING**

# NEWFIELD PRODUCTION COMPANY - CASING & CEMENT REPORT

<p style="text-align: center;"><u>5 1/2"</u> CASING SET AT <u>5559.94</u></p> <p>LAST CASING <u>8 5/8"</u> SET # <u>324</u></p> <p>DATUM <u>12' KB</u></p> <p>DATUM TO CUT OFF CASING <u>12'</u></p> <p>DATUM TO BRADENHEAD FLANGE _____</p> <p>TD DRILLER <u>5560</u> Loggers _____</p> <p>HOLE SIZE <u>7 7/8"</u></p>	<p>Flt cllr @ <u>5532.69</u></p> <p>OPERATOR <u>Newfield Production Company</u></p> <p>WELL <u>Federal 11-19-9-18</u></p> <p>FIELD/PROSPECT <u>Monument Butte</u></p> <p>CONTRACTOR &amp; RIG # <u>Patterson #52</u></p>
---	--

LOG OF CASING STRING:							
PIECES	OD	ITEM - MAKE - DESCRIPTION	WT / FT	GRD	THREAD	CONDT	LENGTH
		Landing Jt					14
		<b>Short jt</b> 3635' (6.66)					
<b>129</b>	<b>5 1/2"</b>	ETC LT & C casing	<b>15.5#</b>	<b>J-55</b>	<b>8rd</b>	<b>A</b>	5520.69
		Float collar					0.6
<b>1</b>	<b>5 1/2"</b>	ETC LT&C csg	<b>15.5#</b>	<b>J-55</b>	<b>8rd</b>	<b>A</b>	26
		<b>GUIDE</b> shoe			<b>8rd</b>	<b>A</b>	0.65
CASING INVENTORY BAL.		FEET	JTS	TOTAL LENGTH OF STRING			5561.94
TOTAL LENGTH OF STRING		5561.94	129	LESS CUT OFF PIECE			14
LESS NON CSG. ITEMS		15.25		PLUS DATUM TO T/CUT OFF CSG			12
PLUS FULL JTS. LEFT OUT		255.7	6	CASING SET DEPTH			<b>5559.94</b>
TOTAL		<b>5802.39</b>	136	} COMPARE			
TOTAL CSG. DEL. (W/O THRDS)		5816.39	136				
TIMING		1ST STAGE	2nd STAGE				
BEGIN RUN CSG.		7/21/2008	7:00pm	GOOD CIRC THRU JOB <u>yes</u>			
CSG. IN HOLE		7/21/2008	10:00pm	Bbls CMT CIRC TO SURFACE			
BEGIN CIRC		7/21/2008	10:30pm	RECIPROCATED PIPE FOR <u>THRUSTROKE</u> NA			
BEGIN PUMP CMT		7/22/2008	1:11am	DID BACK PRES. VALVE HOLD ? <u>yes</u>			
BEGIN DSPL. CMT		7/22/2008	1:53am	BUMPED PLUG TO <u>1380</u> PSI			
PLUG DOWN		7/22/2008	2:17am				
CEMENT USED		CEMENT COMPANY- <b>B. J.</b>					
STAGE	# SX	CEMENT TYPE & ADDITIVES					
<b>1</b>	<b>275</b>	Premilite II w/ 10% gel + 3 % KCL, 3#s /sk CSE + 2# sk/kolseal + 1/2#s/sk Cello Flake					
		mixed @ 11.0 ppg W / 3.43 cf/sk yield					
<b>2</b>	<b>400</b>	50/50 poz W/ 2% Gel + 3% KCL, .5%EC1, 1/4# sk C.F. 2% gel. 3% SM mixed @ 14.4 ppg W/ 1.24 YLD					
CENTRALIZER & SCRATCHER PLACEMENT			SHOW MAKE & SPACING				
Centralizers - Middle first, top second & third. Then every third collar for a total of 20.							

COMPANY REPRESENTATIVE Jay Burton DATE 7/22/2008

RECEIVED

JUL 29 2008

DIV. OF OIL, GAS & MINING

STATE OF UTAH  
DEPARTMENT OF NATURAL RESOURCES  
DIVISION OF OIL, GAS AND MINING

SUNDRY NOTICES AND REPORTS ON WELLS

Do not use this form for proposals to drill new wells, significantly deepen existing wells below current bottom-hole depth, reenter plugged wells, or to drill horizontal laterals. Use APPLICATION FOR PERMIT TO DRILL form for such proposals.


1. TYPE OF WELL:		OIL WELL <input checked="" type="checkbox"/> GAS WELL <input type="checkbox"/> OTHER <input type="checkbox"/>		5. LEASE DESIGNATION AND SERIAL NUMBER: USA UTU-65635
2. NAME OF OPERATOR: NEWFIELD PRODUCTION COMPANY				6. IF INDIAN, ALLOTTEE OR TRIBE NAME:
3. ADDRESS OF OPERATOR: Route 3 Box 3630 CITY Myton STATE UT ZIP 84052		PHONE NUMBER 435.646.3721	7. UNIT or CA AGREEMENT NAME:	
4. LOCATION OF WELL: FOOTAGES AT SURFACE: 1976 FSL 1916 FWL				8. WELL NAME and NUMBER: FEDERAL 11-19-9-18
OTR/OTR. SECTION. TOWNSHIP. RANGE. MERIDIAN: NESW, 19, T9S, R18E				9. API NUMBER: 4304739397
				10. FIELD AND POOL, OR WILDCAT: MONUMENT BUTTE
				COUNTY: UINTAH
				STATE: UT

11. CHECK APPROPRIATE BOXES TO INDICATE NATURE OF NOTICE, REPORT, OR OTHER DATA

TYPE OF SUBMISSION	TYPE OF ACTION		
<input type="checkbox"/> NOTICE OF INTENT (Submit in Duplicate)  Approximate date work will _____	<input type="checkbox"/> ACIDIZE	<input type="checkbox"/> DEEPEN	<input type="checkbox"/> REPERFORATE CURRENT FORMATION
	<input type="checkbox"/> ALTER CASING	<input type="checkbox"/> FRACTURE TREAT	<input type="checkbox"/> SIDETRACK TO REPAIR WELL
	<input type="checkbox"/> CASING REPAIR	<input type="checkbox"/> NEW CONSTRUCTION	<input type="checkbox"/> TEMPORARITLY ABANDON
	<input type="checkbox"/> CHANGE TO PREVIOUS PLANS	<input type="checkbox"/> OPERATOR CHANGE	<input type="checkbox"/> TUBING REPAIR
	<input type="checkbox"/> CHANGE TUBING	<input type="checkbox"/> PLUG AND ABANDON	<input type="checkbox"/> VENT OR FLAIR
<input checked="" type="checkbox"/> SUBSEQUENT REPORT (Submit Original Form Only)  Date of Work Completion: 08/29/2008	<input type="checkbox"/> CHANGE WELL NAME	<input type="checkbox"/> PLUG BACK	<input type="checkbox"/> WATER DISPOSAL
	<input type="checkbox"/> CHANGE WELL STATUS	<input type="checkbox"/> PRODUCTION (START/STOP)	<input type="checkbox"/> WATER SHUT-OFF
	<input type="checkbox"/> COMMINGLE PRODUCING FORMATIONS	<input type="checkbox"/> RECLAMATION OF WELL SITE	<input checked="" type="checkbox"/> OTHER: - Weekly Status Report
	<input type="checkbox"/> CONVERT WELL TYPE	<input type="checkbox"/> RECOMPLETE - DIFFERENT FORMATION	

12. DESCRIBE PROPOSED OR COMPLETED OPERATIONS. Clearly show all pertinent details including dates, depths, volumes, etc.

The above subject well was completed on 08-13-08, attached is a daily completion status report.

NAME (PLEASE PRINT) Jentri Park	TITLE Production Clerk
SIGNATURE 	DATE 08/29/2008

(This space for State use only)

RECEIVED

SEP 02 2008

DIV. OF OIL, GAS & MINING

## Daily Activity Report

Format For Sundry

**FEDERAL 11-19-9-18****6/1/2008 To 10/30/2008****7/30/2008 Day: 1****Completion**

Rigless on 7/29/2008 - Instal 5K frac head. NU 6" 5K Cameron BOP. RU H/O truck & pressure test casing, blind rams, frac head, csg & casing valves to 4500 psi. RU Perforators LLC WLT w/ mast & run CBL under pressure. WLTD @ 5470' & cement top @ 130'. Perforate stage #1, CP4 sds @ 5252-66' w/ 3-1/8" Slick Guns (19 gram, .49"HE, 120°) w/ 4 spf for total of 56 shots. 131 bbls EWTR. SIFN.

**8/8/2008 Day: 2****Completion**

Rigless on 8/7/2008 - RU BJ Services "Ram Head" frac flange. RU BJ & frac CP4 sds, stage #1 down casing w/ 75,408#'s of 20/40 sand w/ 611 bbls of Lightning 17 frac fluid. Open well w/ 0 psi on casing. Perfs broke down @ 2707 psi. Pump 30 gals of Techna Hib chemical. Treated @ ave pressure of 1789 w/ ave rate of 22.9 bpm w/ 8 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 2099. 742 bbls EWTR. Leave pressure on well. RU PSI WLT, crane & lubricator. RIH w/ Weatherford 5-1/2" (6K) composite flow through frac plug & 8', 10' perf guns. Set plug @ 5190'. Perforate CP2 sds @ 5136-44' & CP1 sds @ 5086-96' w/ 3-1/8" Slick Guns (23 gram, .37"HE, 120°) w/ 4 spf for total of 72 shots. RU BJ & frac stage #2 w/ 75,466#'s of 20/40 sand in 601 bbls of Lightning 17 frac fluid. Open well w/ 1840 psi on casing. Perfs broke down @ 4236 psi. Pump 30 gals of Techna Hib chemical. Treated @ ave pressure of 1956 w/ ave rate of 23.1 bpm w/ 8 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 1966. 1343 bbls EWTR. Leave pressure on well. RU WLT. RIH w/ frac plug & 12' perf gun. Set plug @ 4790'. Perforate A1 sds @ 4678-90' w/ 4 spf for total of 48 shots. RU BJ & frac stage #3 w/ 74,502#'s of 20/40 sand in 590 bbls of Lightning 17 frac fluid. Open well w/ 1570 psi on casing. Perfs broke down @ 2731 psi. Pump 30 gals of Techna Hib chemical. Treated @ ave pressure of 1825 w/ ave rate of 23.1 bpm w/ 8 ppg of sand. Spot 12 bbls of 15% HCL acid in flush for next stage. ISIP was 2099. 1343 bbls EWTR. Leave pressure on well. RU WLT. RIH w/ frac plug & 8' perf gun. Set plug @ 4610'. Perforate B2 sds @ 4550-58' w/ 4 spf for total of 32 shots. RU BJ & frac stage #4 w/ 39,058#'s of 20/40 sand in 411 bbls of Lightning 17 frac fluid. Open well w/ 1630 psi on casing. Perfs broke down @ 3427 psi. Pump 30 gals of Techna Hib chemical. Treated @ ave pressure of 1842 w/ ave rate of 23.1 bpm w/ 6 ppg of sand. ISIP was 1668. 2344 bbls EWTR. RD BJ & WLT. Flow well back. Well flowed for 5 hours & died w/ 700 bbls rec'd. SIFN.

**8/9/2008 Day: 3****Completion**

Leed #712 on 8/8/2008 - MIRUSU. Open well w/ 100 psi on casing. RD Cameron BOP's & frac head. Instal production tbg head & Schaffer BOP's. RU 4-3/4" Chomp mill & x-over sub. Tally & TIH w/ new J-55, 2-7/8", 6.5# tbg to 150 jts. RU swivel, pump & tanks. TIH to plug @ 4610'. Drlg out plug #1. TIH w/ tbg to tag sand @ 4678'. C/O to plug @ 4790'. SIFN.

**8/12/2008 Day: 4****Completion**

Leed #712 on 8/11/2008 - No pressure on well. Con't C/O sd & drill out composite bridge plugs as follows (using conventional circulation): sd @ 4709', plug @ 4790' in 35 minutes; no sd, plug @ 5190' in 22 minutes. Con't swivelling jts in hole. Tag fill @

5335'. Drill plug remains & sd to PBTD @ 5528'. Circ hole clean W/ no fluid loss. RD swivel. Pull EOT to 5462'. RU swab equipment. IFL @ sfc. Made 4 swb runs rec 32 BW. FL @ 600'. SIFN W/ est 1602 BWTR.

8/13/2008 Day: 5

Completion

Leed #712 on 8/12/2008 - No pressure on well. Con't swabbing well for cleanup. IFL @ sfc. Made 13 swb runs rec 155 BTF W/ light gas, sm tr oil & no sd. FFL @ 1100'. TIH W/ tbg & tag PBTD @ 5528' (no new fill). Circ hole clean. Lost est 30 BW & rec tr oil. LD excess tbg. TOH W/ tbg--LD bit. TIH W/ BHA & production tbg as follows: 2 7/8 NC, 2 jts tbg, SN, 1 jt tbg, new 5 1/2" TA (45K) & 170 jts 2 7/8 8rd 6.5# J-55 tbg. ND BOP. Set TA @ 5238' W/ SN @ 5272' & EOT @ 5335'. Land tbg W/ 16,000# tension. NU wellhead. RU & pump 60 BW dn tbg (returned same amount). PU & TIH W/ pump and "A" grade rod string to 1900'. PU polished rod & SIFN. Est 1476 BWTR.

8/14/2008 Day: 6

Completion

Leed #712 on 8/13/2008 - No pressure on well. Con't PU & TIH W/ pump and rod string f/ 1900' (complete as follows): new CDI 2 1/2" X 1 1/2" X 18' RHAC pump, 6-1 1/2" weight rods, 20-3/4" scraped rods, 85-3/4" plain rods, 96-3/4" scraped rods and 1 1/2" X 26' polished rod. Seat pump & RU pumping unit. Fill tbg W/ 2 BW. Pressure test tbg & pump to 200 psi. Stroke pump up W/ unit to 800 psi. Good pump action. RDMOSU. Est 1478 BWTR. Place well on production @ 3:30 PM 8/13/2008 W/ 72" SL @ 6 SPM. FINAL REPORT!!

Pertinent Files: Go to File List
